

**314th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
December, 2011**



New International Terminal Building (Goa)



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for December 2011 contains information on the status of the 561 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During December 2011, 26 projects (1 project each of Mines, Shipping and Power, 2 projects of Petroleum, 5 projects of Road Transport & Highways, 16 projects of Telecommunication Sectors) have reported completion.

The online reporting of the implementation status of the ongoing projects from the project authorities has improved considerably with majority of project authorities reporting online during the current month. During December 2011, 102 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 49 months, in respect of projects relating to Railways, Coal, Petroleum, Power, Road Transport and Highways, Steel, Fertilizer, Civil Aviation and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	132	10
2.	ROAD TRANSPORT & HIGHWAYS	131	55
3.	POWER	94	16
4.	PETROLEUM	69	10
5.	COAL	51	2
6.	TELECOMMUNICATION	22	0
7.	SHIPPING & PORTS	24	0
8.	STEEL	16	3
9.	FERTILISERS	6	3
10.	CIVIL AVIATION	5	2
11.	ATOMIC ENERGY	5	1
12.	URBAN DEVELOPMENT	4	0
13.	WATER RESOURCES	1	0
14.	PETROCHEMICALS	1	0
Total		561	102

3. The total original cost of implementation of the 561 projects was about ₹ 7, 16,175.48 Crores and their anticipated completion cost is likely to be ₹ 8, 36,734.26 Crores, which reflects an overall cost overrun of 16.8 %. The expenditure incurred on these projects till December, 2011 is ₹ 3, 50,107.85 Crores, which is 41.8 % of the revised cost of the projects.

4. Out of the 561 projects, 6 projects are ahead of schedule, 170 are on schedule, 242 projects are delayed and 82 projects have been sanctioned without any commissioning schedule/date Further, in case of 61 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized.

5. During the month under reference 242 projects are reporting delay which is same as that of November'2011. Out of 242 delayed projects, 50 projects had overall delay in the range of 1 to 12 months, 52 projects had a delay in the range of 13 to 24 months, 104 projects had a delay in the range of 25 to 60 months and 36 projects had a delay of 61 months and above.

6. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

7. The brief reasons for time overruns as reported by various projects implementing agencies are inadequate mobilization by the contractors, law and order problems, delays in engineering designs, change of scope delays in pre-project activity, Maoist problems and forest and environment clearances etc. Brief reasons for cost overruns are mainly due to inflation, fluctuation of exchange rate, higher tender value, change of scope etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

The Sector-wise details of additional delays are as under:-

i) In the **Coal sector**, Two projects have reported additional delays. Barsingsar TPS (125 mw), Neyveli Lignite Corp. Ltd, Rajasthan has reported an additional delay of 1 month (overall delay 31 months) due to delay in commissioning and Bina Extension project, Northern Coalfields Ltd has reported an additional delays of 4 months, however the project authorities have not reported any specific reason of it .

ii) In the **Fertilizer sector**, 3 projects have reported additional delays in the range of 1 -5 months. Thal Ammonia Revamp Project, RCF, Haryana has reported an additional delay of 5 months due to delay in issue of equity documents by PDIL, Capacity Enhancement of Ammonia & Urea Plant, NFL and Capacity Enhancement of Vijaypur Plant, NFL have reported additional delay of 1 month and 4 months respectively. However, no reasons have been reported by the project authorities for both the projects.

iii) In the **Petroleum Sector**, 10 projects have reported additional delays in the range of 1-40 months. Karanpur Moradabad-Kashipur-Rudrapur Pipeline Project, GAIL, has reported an additional delay of 1 months as the land owners are demanding for high compensation, Compressor Stations Kailaras and Chainsa, GAIL has an additional delay of 3 months due to delay in delivery of critical equipments, Heera Reconstruction, ONGC has an additional delay of 3 months due to delay in revamping jobs and installation of revamped equipments, Neelam Reconstruction, ONGC has an additional delay of 3 months due to contractual problems, Development of C- Series Fields, ONGC has an additional delay of 4 months due to delay in drilling of development wells, North Tapti Gas Field Development, ONGC has an additional delay of 9 months due to increased facility costs, Offshore Grid Interconnectivity Project in Mumbai High, ONGC has an additional delay of 12 months due to contractual problems, Jagdishpur- Haldia Pipeline project, Phase-I, GAIL has an additional delay of 40 months as the project is to be synchronized with the revival of Fertilizer plants at Haldia, Diesel Hydrotreator project at Mumbai Refinery, HPCL and Wind Power Project, ONGC have additional delay of 8 months and 10 months respectively, however; no reason has been reported by the project authorities.

iv) In the **Power Sector**, 16 projects have reported additional delays in the range of 1-10 months. Three projects have reported an additional delay of 1 month each, five projects have reported an additional delay of 2 months each and three projects have reported an additional delay of 3 months each for which no reasons have been reported by the project authority. The project, Teesta Low Dam Stage III, NHPC, Western Region Strengthening Scheme –II, PGCIL and Teesta Low Dam HEP, Stage-IV, NHPC have reported an additional delay of 4, 4 and 6 months respectively due to massive earth quake in the region in September, 2011. Parbati HEP, Stage-III, NHPC has reported an additional delay of 7 months due to frequent strike / workstoppage by locals and Kishanganga HEP, NHPC has reported an additional delay of 10 months, for which no reason has been reported by the project authority .

v) In the **Atomic Energy Sector**, Kudankulam APP, NPCIL has reported an additional delay of 1 month (overall delay of 50 months) due to agitation by the local public/ bodies .

vi) In **Steel sector**, 3 projects have reported additional delays in the range of 1-3 months. The project, Rebuilding of Coke Oven Battery No. 1 and 2, SAIL, has reported an additional delay of one month due to initial delay in design and engineering, 700 TPD ARI Separation Unit-4 at Oxygen Plant- II Bhilai, SAIL has reported an additional delay of 2 months (overall delay of 9 months) due to delay in detailed Engineering. Drawings, Expansion of Bokaro Steel plant, SAIL has reported an additional delay of 3 months due to delay in approval of various packages at different times.

vii) In the **Road Transport and Highways Sector**, 55 projects have reported additional delays in the range of 1-29 months. 6 projects have reported additional delay of 1 month each, 7 projects have reported an additional delay of 2 months each, 11 projects have reported an additional delay of 3 months each, 2 projects have an additional delay of 4 months each, 4 projects have reported an additional delay of 5 months each, 11 projects have an additional delay of 6 months each, 5 projects have an additional delay of 9 months each, Thanjaur- Trichy, NH-67, NHAI has an additional delay of 11 months and Chennai – Tada (six lane), NHAI has reported an additional delay of 29 months, 4 projects have an additional delay of 12 months each and 2 projects have an additional delay of 15 months each .However, no reason has been reported by the project authority (for all projects).

viii) In **Civil Aviation Sector**, two projects have reported additional delay. Kamraj Domestic Terminal, Phase-II and Expansion Anna International, AAI has reported an additional delay of 2 months due to land dispute with Min. of Defense, New Airport at Pakyong (Sikkim) Air port, AAI has reported an additional delay of 6 months due to delay in handing over sites .

ix) In Railways sector, 10 projects have reported additional delay in the range of 3-49 months. Lanjigarh Junction, East Coast Railways, Nandyas Yerraguntla (NL), South Central Railways, Khurda Road – Bolangir (NL), Katakhal to Bhairabi, North East Frontier Railways have reported an additional delay of 3 months each due to delay in land acquisitions, Howrah- Amta- Champadanga NL, South Eastern Railways has reported an additional delay of 21 months due to delay in land acquisition and shortage of staff, Bankura – Damodar (GC), South Eastern Railways has reported an additional delay of 39 months due to delay in land acquisition, Rajatgarh- Barang, Rail Vikash Nigam Ltd, Khurda Road –Barang, Rail Vikash Nigam Ltd, have reported an additional delay of 28 months each Tamluk Digha, line Doubling, SER and Panspura – Kharagpur 3D line, Rail Vikash Nigam Ltd have reported an additional delay of 39 and 49 months respectively, however the project authorities have not reported any reasons for delay.

The status as on 31.12.2011 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.



(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	132	10
2	Road Transport & Highways	131	55
3	Power	94	16
4	Petroleum	69	10
5	Coal	51	2
6	Shipping & Ports	24	0
7	Telecommunications	22	0
8	Steel	16	3
9	Fertilisers	6	3
10	Atomic Energy	5	1
11	Civil Aviation	5	2
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	561	102

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC AND MAITHON RB(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
<u>Road Transport & Highways</u>				
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
June,2011				
<u>Petroleum</u>				
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
<u>Power</u>				
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
<u>Railways</u>				
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
<u>Road Transport & Highways</u>				
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00
July,2011				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Steel</u>				
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
<u>Petroleum</u>				
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
August,2011				
<u>Power</u>				
30	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]	262.10	09/2010	164.00
<u>Railways</u>				
31	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]	262.00	-	548.54
<u>Road Transport & Highways</u>				
32	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]	193.00	10/2008	338.70
33	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256]	359.00	03/2009	870.60
<u>Telecommunications</u>				
34	NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]	312.86	02/2008	204.43
<u>Urban Development</u>				
35	DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]	8,676.00	06/2010	18,304.30

September,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Petroleum</u>				
36	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF(INDIAN OIL CORPORATION LIMITED) - [N16000040]	293.60	12/2009	234.81
<u>Railways</u>				
37	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN(WESTERN RAILWAY) - [220100116]	112.53	03/1996	509.57
38	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves(NORTH WESTERN RAILWAY) - [N22000106]	643.36	03/2011	786.54
<u>Road Transport & Highways</u>				
39	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106225]	217.00	10/2008	352.26
October,2011				
<u>Power</u>				
40	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000043]	204.07	06/2011	129.60
November,2011				
41	WESTERN REGION STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000050]	230.89	01/2011	98.20
<u>Road Transport & Highways</u>				
42	RINGBUNDS TO JHAJHANPUR (BR-6)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000030]	340.00	06/2008	570.00
43	THRISSUR TO ANGAMALI (NH-47)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000037]	312.50	03/2009	604.40
December,2011				
<u>Mines</u>				
44	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [100100054]	4,091.51	12/2008	4,183.00
<u>Petroleum</u>				
45	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000024]	2,305.30	06/2010	1,266.47
46	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)(GAS AUTHORITY OF INDIA LIMITED) - [N16000052]	4,429.38	10/2010	2,325.60
<u>Power</u>				
47	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000023]	238.25	05/2011	220.82

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
48	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106246]	227.00	10/2008	403.60
49	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106276]	629.00	11/2010	910.00
50	LALITPUR TO SAGAR, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106299]	198.00	11/2008	187.30
51	JHANSI TO LALITPUR, NH-26(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000097]	276.09	09/2009	295.40
52	PONDICHERY - TINDIVANAU NH-66(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000100]	285.00	07/2010	359.40
<u>Shipping & Ports</u>				
53	Construction & License out the OPERATION, MANAG. &(PORT TRUST) - [N25000038]	230.00	12/2010	219.00
<u>Telecommunications</u>				
54	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000039]	601.49	12/2008	496.20
55	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1(BHARAT SANCHAR NIGAM LIMITED) - [N26000040]	192.48	03/2009	119.45
56	Procurement of 2.5G DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000066]	424.00	03/2009	.00
57	Procurement of 10G (40 chl) DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000067]	590.10	03/2009	.00
58	Procurement of 10G 40 CHL (12 chl equipped) DWDM(BHARAT SANCHAR NIGAM LIMITED) - [N26000068]	545.50	03/2010	.00
59	Procurement of STM-1 SDH equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000069]	154.03	03/2010	.00
60	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000070]	355.92	03/2010	.00
61	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000071]	477.00	03/2010	.00
62	Procurement of DXC equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000074]	229.00	03/2010	.00
63	GSM equipment of 900000Lines (2G) PunjabPhase V.2(BHARAT SANCHAR NIGAM LIMITED) - [N26000081]	241.49	09/2009	123.76
64	GSM equipment of 975000Lines (2G) 325000 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000083]	625.53	02/2010	.00
65	GSM equipment of 1100000Lines (2G) UP East Phase(BHARAT SANCHAR NIGAM LIMITED) - [N26000084]	624.75	09/2010	.00
66	GSM equipment of 375000Lines (2G) 75000lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000085]	170.23	06/2009	.00
67	GSM equipment of 849862Lines (2G) 150138 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000087]	584.33	02/2009	403.71
68	GSM equipment of 1900000Lines (2G) 401700 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000091]	760.20	-	819.57
69	GSM equipment of 1700000Lines (2G) 234100 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000092]	677.75	10/2009	461.56

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
	May,2011			
	<u>Civil Aviation</u>			
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97


Summary of projects in the Flash Report for the month of December, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	584
Number of Projects completed/dropped/frozen in Previous Month	3
Number of Projects completed/dropped/frozen in Current Month	26
Number of Projects Added in Current Month	6
Number of Projects in Current Month	561


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 561 projects, 6 projects are ahead of schedule, 169 projects are on schedule and 242 projects are delayed. Of the balance, 82 projects do not have fixed dates of commissioning while 61 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

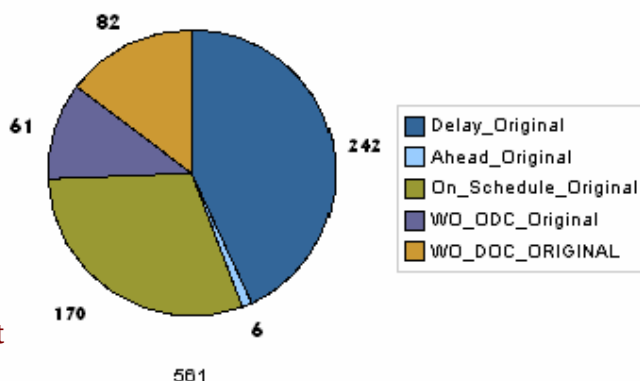

III. Investment Scenario

The Total Original cost of implementation of 561 projects when sanctioned, was of the order of Rs. 716175.48 crore but this was subsequently revised to Rs. 836734.26 crore implying a cost overrun of 16.8%. The expenditure incurred on these projects till December, 2011 is Rs. 350107.85 crore, which is 41.8% of the revised cost of the projects.

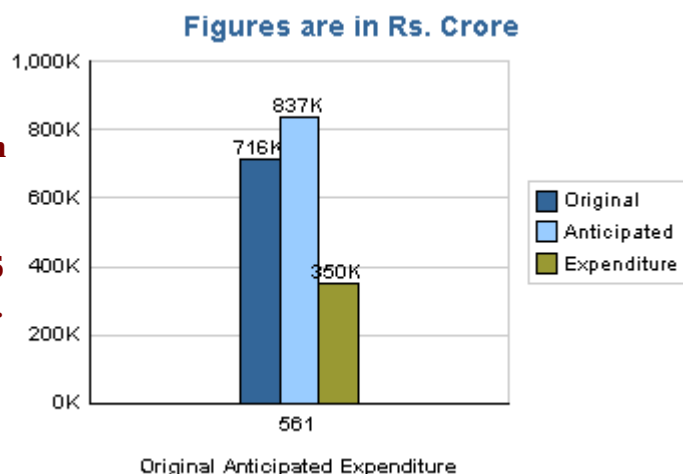

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	584
No of Projects Completed/Dropped/Frozen in Previous Month	3
No of Projects Completed/Dropped/Frozen in Current Month	26
No of Projects added in Current Month	6
No of Projects in Current Month	561

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	242	6	170	61	82	561	43.14
Latest Approved (Date)	246	9	218	34	54	561	43.85

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	439	572,090.72	615,074.16	223,420.41	36.30	42,983.44	7.50
Latest Approved (RCE)	122	197,293.76	221,660.10	126,687.44	57.20	24,366.34	12.40
Total (RCE)	561	769,384.48	836,734.26	350,107.85	41.84	67349.78	8.75
Original Cost of All Projects							
Original Cost	561	716,175.48	836,734.26	350,107.85	41.80	120,558.78	16.80

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	242	357,480.70	434,511.11	235,981.86	54.30	77,030.41	21.50
Latest Approved (RCE)	246	352,566.72	399,975.83	216,981.11	54.20	47,409.11	13.40

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	102	111,223.38	123,417.97	80,972.18	65.60	12,194.59	11.00

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	51	34,718.7	38,348.4	10.5	12	13,742.8	17,970.2	30.8
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	65,244.8	71,412.4	9.5	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	69	149,804.8	158,021.2	5.5	16	49,968.0	65,969.0	32.0
8	Power	94	195,705.4	211,046.4	7.8	18	33,538.6	48,944.4	45.9
9	Railways	132	65,054.7	134,133.5	106.2	102	37,373.6	106,509.2	185.0
10	Road Transport & Highways	131	73,894.7	75,983.8	2.8	15	4,435.6	7,093.7	59.9
11	Shipping & Ports	24	17,822.2	18,838.3	5.7	10	6,294.5	7,511.6	19.3
12	Telecommunications	22	11,794.1	12,010.6	1.8	4	1,593.2	1,892.4	18.8
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		561	716,175.5	836,734.3	16.8	191	203,901.3	333,837.0	63.7

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	16 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 23
3	Coal	51	34,718.7	38,348.4	10.5	17	11,824.7	14,994.8	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 9
5	Steel	16	65,244.8	71,412.4	9.5	5	46,957.9	52,521.9	3 - 36
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	149,804.8	158,021.2	5.5	33	81,100.0	89,549.8	2 - 120
8	Power	94	195,705.4	211,046.4	7.8	47	122,641.4	137,571.7	2 - 90
9	Railways	132	65,054.7	134,133.5	106.2	28	22,295.6	52,619.5	2 - 213
10	Road Transport & Highways	131	73,894.7	75,983.8	2.8	83	29,531.8	31,814.4	2 - 101
11	Shipping & Ports	24	17,822.2	18,838.3	5.7	9	7,849.0	8,674.1	2 - 93
12	Telecommunications	22	11,794.1	12,010.6	1.8	9	5,042.3	5,241.3	13 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		561	716,175.5	836,734.3	16.8	242	357,480.7	434,511.1	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	4	29,228.3	34,066.3	0 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 23
3	Coal	51	34,718.7	38,348.4	10.5	17	11,824.7	14,994.8	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 9
5	Steel	16	65,244.8	71,412.4	9.5	8	39,531.8	41,991.7	0 - 9
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	149,804.8	158,021.2	5.5	21	56,890.7	60,524.0	0 - 73
8	Power	94	195,705.4	211,046.4	7.8	41	116,770.2	129,631.3	2 - 83
9	Railways	132	65,054.7	134,133.5	106.2	36	15,437.2	49,483.2	0 - 213
10	Road Transport & Highways	131	73,894.7	75,983.8	2.8	84	29,728.3	32,177.4	0 - 101
11	Shipping & Ports	24	17,822.2	18,838.3	5.7	10	8,051.2	8,989.8	2 - 93
12	Telecommunications	22	11,794.1	12,010.6	1.8	16	7,815.2	8,094.8	7 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		561	716,175.5	836,734.3	16.8	246	328,852.7	399,975.8	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	51	36,435.7	38,348.4	5.2	7	6,587.2	8,967.6	36.1
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	71,120.1	71,412.4	0.4	3	598.0	910.3	52.2
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	69	163,049.4	158,021.2	-3.1	3	32,036.9	32,844.0	2.5
8	Power	94	201,502.2	211,046.4	4.7	11	26,449.9	36,059.0	36.3
9	Railways	132	87,302.6	134,133.5	53.6	81	42,884.8	90,007.5	109.9
10	Road Transport & Highways	131	74,061.2	75,983.8	2.6	14	4,239.1	6,730.7	58.8
11	Shipping & Ports	24	18,254.0	18,838.3	3.2	8	6,321.3	7,007.1	10.8
12	Telecommunications	22	11,798.0	12,010.6	1.8	2	527.3	803.1	52.3
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		561	769,384.5	836,734.3	8.8	134	145,188.0	219,951.2	51.5

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	0	0.00	0.00	0- 0
3	Coal	51	34,718.73	38,348.38	10.45	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	1	8,692.00	12,291.00	36- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	149,804.77	158,021.15	5.48	13	18,756.72	32,734.21	6- 120
8	Power	94	195,705.41	211,046.35	7.84	5	11,736.15	14,216.06	0- 90
9	Railways	132	65,054.74	134,133.50	106.19	8	3,606.22	11,184.08	0- 141
10	Road Transport & Highways	131	73,894.67	75,983.76	2.83	0	0.00	0.00	0- 0
11	Shipping & Ports	24	17,822.23	18,838.27	5.70	3	813.55	955.25	5- 22
12	Telecommunications	22	11,794.14	12,010.64	1.84	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		561	716175.48	836734.26	16.83	31	44074.42	72087	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	2	16,663.00	21,501.00	16- 51
2	Civil Aviation	5	5,021.58	5,611.07	11.74	2	3,750.51	4,340.00	10- 13
3	Coal	51	34,718.73	38,348.38	10.45	7	6,813.24	10,581.09	9- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	2	23,135.00	28,699.00	3- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	149,804.77	158,021.15	5.48	14	48,918.96	63,843.01	6- 120
8	Power	94	195,705.41	211,046.35	7.84	17	32,942.16	47,937.25	7- 90
9	Railways	132	65,054.74	134,133.50	106.19	25	11,576.60	43,338.19	12- 213
10	Road Transport & Highways	131	73,894.67	75,983.76	2.83	14	4,239.06	6,730.74	7- 99
11	Shipping & Ports	24	17,822.23	18,838.27	5.70	6	3,498.52	4,553.72	7- 93
12	Telecommunications	22	11,794.14	12,010.64	1.84	4	1,593.19	1,892.37	13- 72
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	24- 24
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		561	716175.48	836734.26	16.83	95	160068.14	246212.37	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Mines</u>						
SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE	10/2004	4,091.51	12/2008	4,401.76	06/2011	4,183.00
<u>Road Transport & Highways</u>						
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	12/2003	227.00	10/2008	227.00	12/2011	403.60
MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	03/2005	629.00	11/2010	629.00	12/2011	910.00
LALITPUR TO SAGAR, NH-26 (NHAI)	12/2003	198.00	11/2008	198.00	12/2011	187.30
<u>Petroleum</u>						
HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	09/2006	2,305.30	06/2010	2,305.30	11/2011	1,266.47
<u>Power</u>						
TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II	10/2006	238.25	05/2011	238.25	12/2011	220.82
<u>Road Transport & Highways</u>						
JHANSI TO LALITPUR, NH-26	12/2003	276.09	09/2009	276.09	12/2011	295.40
PONDICHERY - TINDIVANAU NH-66	03/2005	285.00	07/2010	285.00	12/2011	359.40
<u>Telecommunications</u>						
GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)	06/2007	601.49	12/2008	601.49	03/2011	496.20
GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1	01/2008	192.48	03/2009	192.48	02/2011	119.45
Procurement of STM-1 SDH equipment	02/2007	154.03	03/2010	154.03	N.A.	.00
GSM equipment of 1700000Lines (2G) 234100 lines 3G	10/2008	677.75	10/2009	719.90	03/2011	461.56
Procurement of STM-16 MADM equipment	03/2008	355.92	03/2010	355.92	N.A.	.00
GSM equipment of 900000Lines (2G) PunjabPhase V.2	09/2008	241.49	09/2009	241.49	03/2011	123.76
GSM equipment of 1100000Lines (2G) UP East Phase	09/2009	624.75	09/2010	624.75	N.A.	.00
GSM equipment of 975000Lines (2G) 325000 lines 3G	02/2009	625.53	02/2010	625.53	N.A.	.00
GSM equipment of 849862Lines (2G) 150138 lines 3G	02/2008	584.33	02/2009	584.33	03/2011	403.71
Procurement of 10G (40 chl) DWDM equipment	08/2006	590.10	03/2009	590.10	N.A.	.00

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Petroleum</u>						
DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)	11/2007	4,429.38	10/2010	2,370.00	N.A.	2,325.60
<u>Telecommunications</u>						
Procurement of 10G 40 CHL (12 chi equipped) DWDM	12/2007	545.50	03/2010	545.50	N.A.	.00
Procurement of DXC equipment	02/2008	229.00	03/2010	229.00	N.A.	.00
<u>Shipping & Ports</u>						
Construction & License out the OPERATION, MANAG. &	06/2006	230.00	12/2010	230.00	06/2011	219.00
<u>Telecommunications</u>						
GSM equipment of 375000Lines (2G) 75000lines 3(G)	06/2008	170.23	06/2009	170.23	N.A.	.00
GSM equipment of 1900000Lines (2G) 401700 lines 3(	01/2009	760.20	N.A.	1,100.00	02/2011	819.57
Procurement of STM-16 ADM equipment	02/2007	477.00	03/2010	477.00	N.A.	.00
Procurement of 2.5G DWDM equipment	08/2006	424.00	03/2009	424.00	N.A.	.00

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Atomic Energy</u>					
RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW)	10/2009	12,320.00	-	12,320.00	12/2016
<u>Coal</u>					
Muraidih UG	2/2011	339.88	4/2014	339.88	4/2014
<u>Power</u>					
TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W	12/2011	2,422.66	8/2014	2,422.66	8/2014
TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT	12/2011	552.44	2/2014	552.44	2/2014
SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	297.33	8/2014	297.33	8/2014
SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJEC	12/2011	1,746.65	8/2014	1,746.65	8/2011

VII. Milestones (Cumulative due & achieved)

Total	2182
Achieved up to month	964

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	15,824.00	12/2008	02/2013	03/2013	1
<u>Civil Aviation</u>						
D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. AAI	1,808.00	2,015.00	01/2011	12/2011	02/2012	2
C/o new Airport at Pakyong(Sikkim) Airport AAI	309.46	309.46	01/2011	06/2012	12/2012	6
<u>Coal</u>						
BARSINGSAR TPS (2 125MW) (NLC) NLC	1,114.18	1,868.71	06/2009	12/2011	01/2012	1
BINA EXTN. PROJ(6.0 Mtpa) NCL	168.97	168.97	03/2014	11/2013	03/2014	4
<u>Fertilisers</u>						
CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ NFL	438.00	438.00	07/2011	03/2012	04/2012	1
CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS NFL	325.00	325.00	07/2011	11/2011	03/2012	4
THAL AMMONIA REVAMP PROJECT RCF	488.75	488.75	N.A.	11/2011	04/2012	5
<u>Steel</u>						
Rebuilding of coke oven battery No.1 and 2 (Bokar SAIL	500.90	500.90	N.A.	12/2011	01/2012	1
700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT- II, BHILLAI SAIL	232.93	232.93	05/2011	12/2011	02/2012	2
EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	12/2011	03/2012	3
<u>Petroleum</u>						
KARANPUR MORADABAD- KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- GAIL	238.68	204.00	01/2012	03/2012	04/2012	1
COMPRESSOR STATIONS (KAILARAS AND CHAINSA) GAIL	1,167.00	798.00	04/2011	12/2011	03/2012	3
HEERA RECONSTRUCTION ONGC	706.70	706.70	04/2010	12/2011	03/2012	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NEELAM RECONSTRUCTION ONGC	305.08	305.08	04/2011	12/2011	03/2012	3
DEVELOPMENT OF C- SERIES FIELDS ONGC	3,195.16	2,800.00	N.A.	11/2011	03/2012	4
DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY HPCL	3,284.00	2,174.00	09/2011	09/2011	05/2012	8
North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	06/2011	03/2012	9
Wind Power Project ONGC	1,106.00	1,106.00	06/2012	06/2012	04/2013	10
OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2012	03/2013	12
JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I GAIL	7,596.18	7,596.18	01/2013	03/2012	07/2015	40
Power						
CHAMERA, STAGE-III (NHPC) NHPC	1,405.63	2,084.00	08/2010	02/2012	03/2012	1
BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,692.97	12/2009	09/2014	10/2014	1
EASTERN REGION STRENGTHENING SCHEME- II PGCIL	227.52	227.52	06/2010	12/2011	01/2012	1
URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	1,794.00	11/2009	04/2012	06/2012	2
NIMOO BAZGO HYDROELECTRIC PROJECT NHPC	611.01	936.00	08/2010	11/2012	01/2013	2
CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.26	913.25	02/2011	03/2012	05/2012	2
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCL	2,491.58	3,422.44	07/2014	07/2016	09/2016	2
MOUDA STPP (NTPC) NTPC	5,459.28	6,010.89	08/2012	01/2013	03/2013	2
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) PGCIL	3,779.46	3,779.46	09/2009	03/2012	06/2012	3
VINDHYACHAL STTP STAGE-IV (NTPC) NTPC	5,915.00	5,915.00	10/2012	12/2012	03/2013	3
RIHAND STTP STAGE-III (2X500MW) (NTPC) NTPC	6,230.81	6,230.81	10/2012	12/2012	03/2013	3
TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE NHPC	768.92	1,628.39	03/2007	05/2012	09/2012	4
WESTERN REGION STRENGTHENING SCHEME- II PGCIL	5,221.23	5,221.23	07/2010	02/2012	06/2012	4

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	12/2012	06/2013	6
PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.56	2,716.00	10/2010	06/2012	01/2013	7
KISHANGANGA HEP NHPC	2,238.67	3,642.00	01/2016	01/2016	11/2016	10
<u>Railways</u>						
LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	12/2011	03/2012	3
NANDYAL- YERRAGUNTLA(NL),SCR SCR	155.74	840.32	02/2009	12/2011	03/2012	3
KHURDA ROAD- BOLANGIR(NL)ECOR ECOR	355.38	1,100.00	N.A.	12/2011	03/2012	3
Katakhal to Bhairabi NEFR	227.90	223.01	12/2012	12/2013	03/2014	3
HOWRAH-AMTA- CHAMPADANGA NL (SER) SER	31.42	499.16	03/2007	06/2012	03/2014	21
RAJATGARH- BARANG(LD),ECOR RVNL	166.16	243.40	N.A.	12/2010	04/2013	28
KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) RVNL	133.41	225.00	N.A.	12/2010	04/2013	28
BANKURA - DAMODAR (GC) (SER) SER	111.90	1,211.22	03/2005	12/2012	03/2016	39
TAMLUK DIGHA,LINE DOUBLING (SER) SER	293.97	723.27	06/2005	03/2012	06/2015	39
PANSPURA-KHARAGPUR 3D LINE RVNL	252.50	529.23	02/2010	11/2011	12/2015	49
<u>Road Transport & Highways</u>						
HALDIA PORT (PORT CONNECTIVITY) (NH-41) NHAI	273.00	522.00	03/2005	12/2011	01/2012	1
MAIBANG TO LUNDING (AS- 26), KM.60.500 TO KM.83.400, NH-54 NHAI	167.64	167.64	11/2008	12/2013	01/2014	1
KASIA TO GORAKHPUR (NH- 28)(NHAI) NHAI	242.00	242.00	12/2008	12/2011	01/2012	1
SITAPUR-LUCKNOW NHAI	322.00	322.00	06/2009	12/2011	01/2012	1
KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN NHAI	418.04	418.04	03/2010	12/2011	01/2012	1
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	12/2011	01/2012	1
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	12/2011	02/2012	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 NHAI	412.78	479.54	11/2007	12/2011	02/2012	2
ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	01/2012	03/2012	2
GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	03/2012	05/2012	2
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	07/2010	12/2011	02/2012	2
Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) NHAI	572.30	572.30	10/2011	08/2012	10/2012	2
Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	02/2012	04/2012	2
SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 NHAI	157.47	154.57	09/2007	03/2012	06/2012	3
HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	12/2011	03/2012	3
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 NHAI	193.09	166.30	03/2008	12/2011	03/2012	3
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 NHAI	166.27	193.10	03/2008	12/2011	03/2012	3
AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	12/2011	03/2012	3
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) NHAI	227.00	227.00	12/2008	12/2011	03/2012	3
JHAJHARPUR TO DARBANGA (BR-7) NHAI	340.00	340.00	09/2008	12/2011	03/2012	3
NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	363.00	N.A.	12/2011	03/2012	3
ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) NHAI	295.00	295.00	08/2010	12/2011	03/2012	3
END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER NHAI	464.00	464.00	01/2011	12/2011	03/2012	3
Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	12/2011	03/2012	3
SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	03/2012	07/2012	4
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) NHAI	225.00	225.00	10/2008	12/2011	04/2012	4
SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) NHAI	151.30	151.30	10/2008	12/2011	05/2012	5
SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	12/2011	05/2012	5


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NAGPUR-KONDHALI,NH-6(NHAI) NHAI	168.00	168.00	12/2008	01/2012	06/2012	5
PATHANKOT BHOGPUR NH-1A NHAI	229.00	284.00	05/2010	12/2011	05/2012	5
AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) NHAI	367.49	367.49	03/2005	12/2011	06/2012	6
GARH Mukteshwar-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 NHAI	275.00	275.00	09/2007	12/2011	06/2012	6
HAPUR-GARH Mukteshwar (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	12/2011	06/2012	6
BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) NHAI	195.00	195.00	06/2008	12/2011	06/2012	6
NALBARI TO BIJNI (AS-8) NHAI	200.00	200.00	06/2008	12/2011	06/2012	6
NAGAON TO DHARAMTUL (AS-2) NHAI	264.72	264.72	06/2008	12/2011	06/2012	6
NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	12/2011	06/2012	6
DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	12/2011	06/2012	6
DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	12/2011	06/2012	6
GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID NHAI	600.24	600.24	10/2009	12/2011	06/2012	6
DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE NHAI	232.45	232.45	09/2010	06/2012	12/2012	6
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	12/2011	07/2012	7
KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	12/2011	09/2012	9
SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI) NHAI	203.43	203.43	10/2008	03/2012	12/2012	9
GUWHATI TO NALBARI (AS-4) NHAI	175.96	175.96	04/2008	03/2012	12/2012	9
GUWAHATI TO NALBARI (AS-5) NHAI	198.16	198.16	04/2008	03/2012	12/2012	9
BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	217.61	04/2010	03/2012	12/2012	9
THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	12/2011	11/2012	11


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
BIJNI TO ASSAM /WB.BORDER (NH- 31.C)(2)(NHAI) NHAI	237.80	237.80	06/2008	12/2011	12/2012	12
NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	12/2011	12/2012	12
TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	03/2012	03/2013	12
DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	12/2011	12/2012	12
HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	280.00	280.00	02/2009	12/2011	03/2013	15
MAIBANG TO LUNDING (AS- 27), KM.40.000 TO KM.60.500 NHAI	200.00	200.00	04/2009	12/2011	03/2013	15
Chennai-Tada(Six lane) NHAI	353.37	353.37	10/2011	10/2011	03/2014	29
Number of projects reporting additional delay = 102						

Trend and Graphical Analysis of All Projects

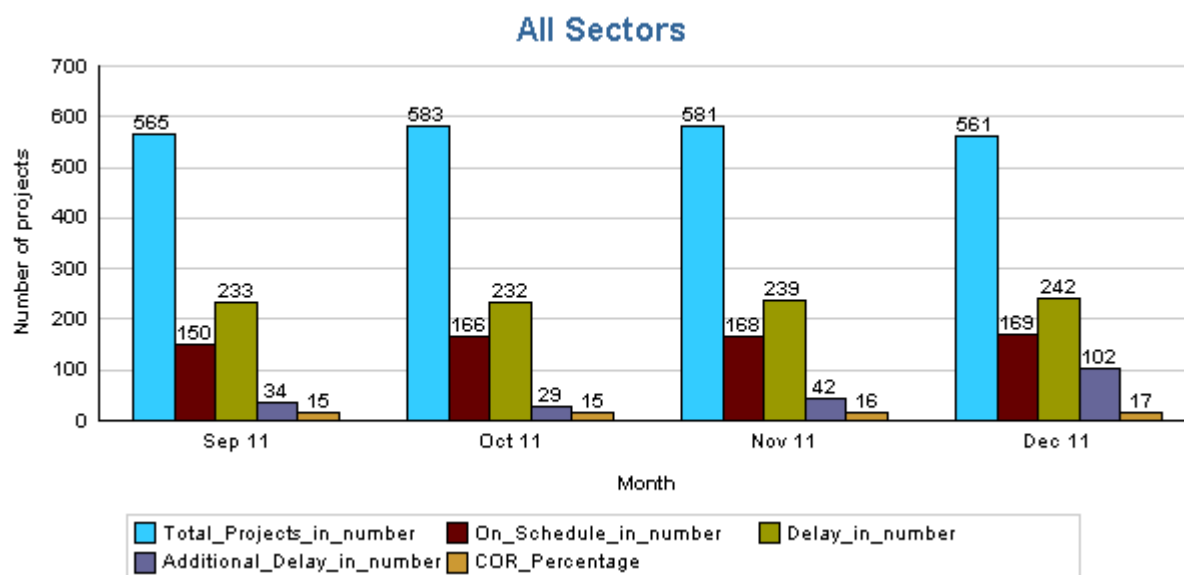


All Sectors Break-up of 242 Delayed projects in December 2011

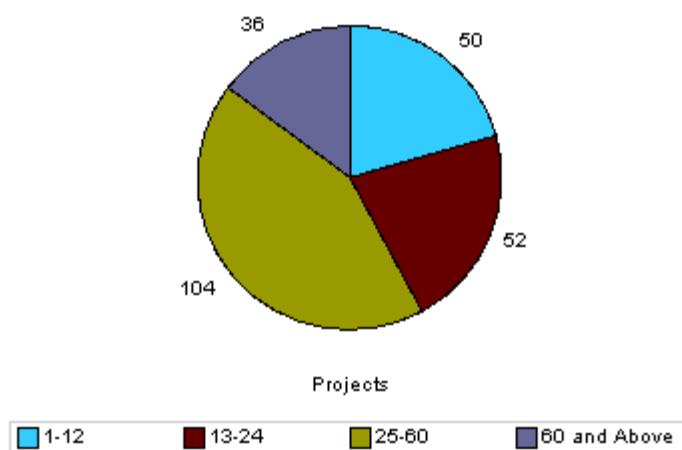


Trend and Graphical Analysis


Urban Development Sector

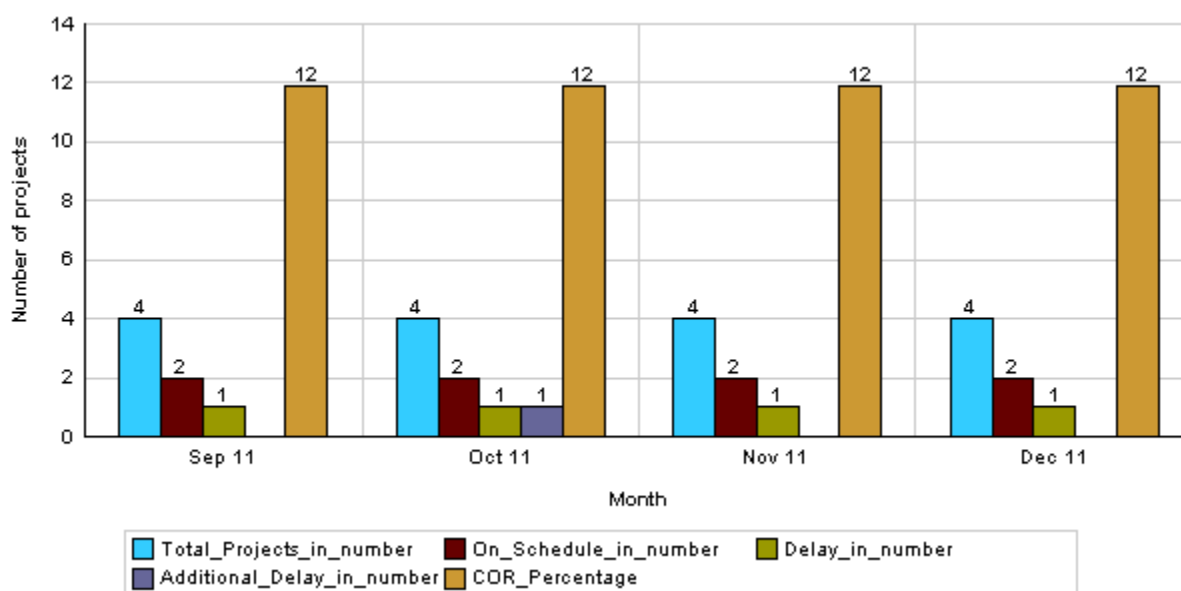


Urban Development Sector Break-up of 1 Delayed projects in December 2011

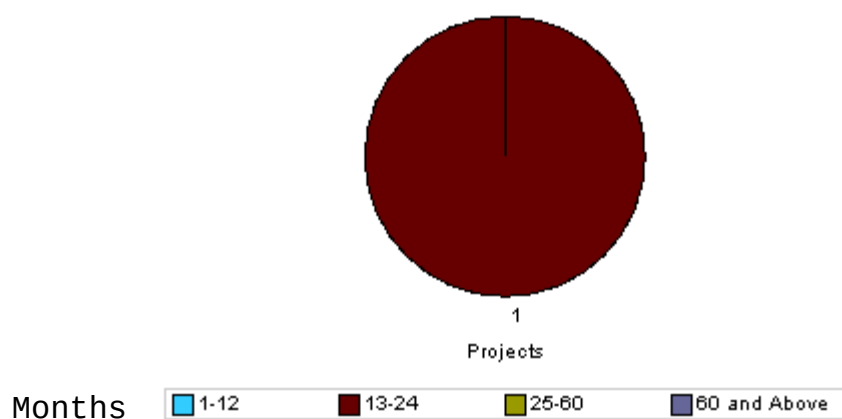


Trend and Graphical Analysis Telecommunications Sector

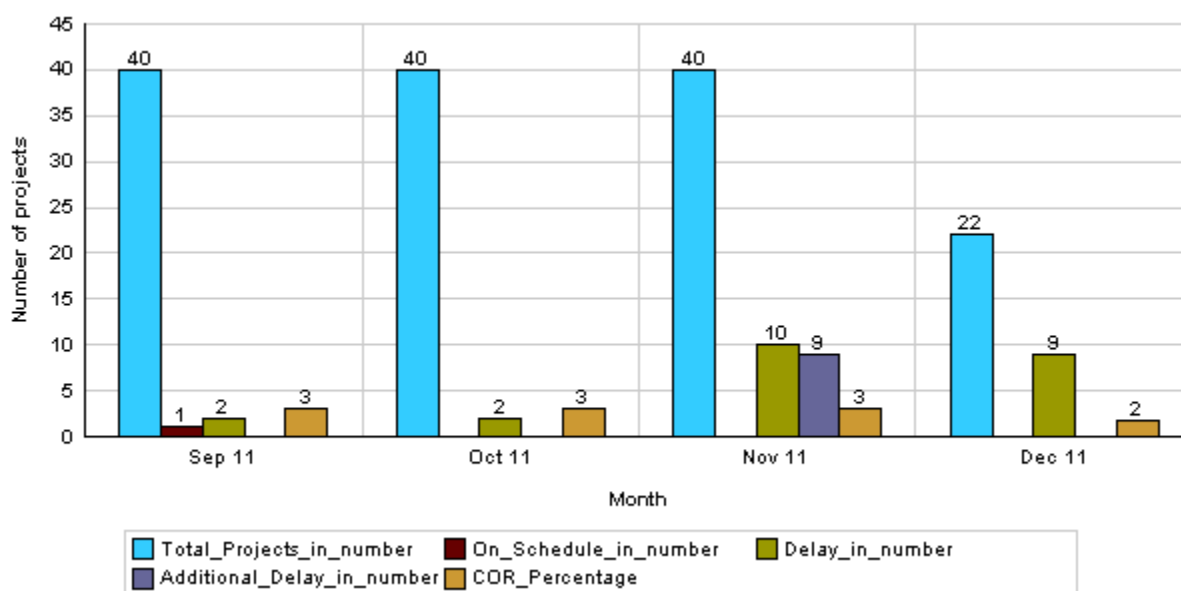


Telecommunications Sector Break-up of 9 Delayed projects in December 2011

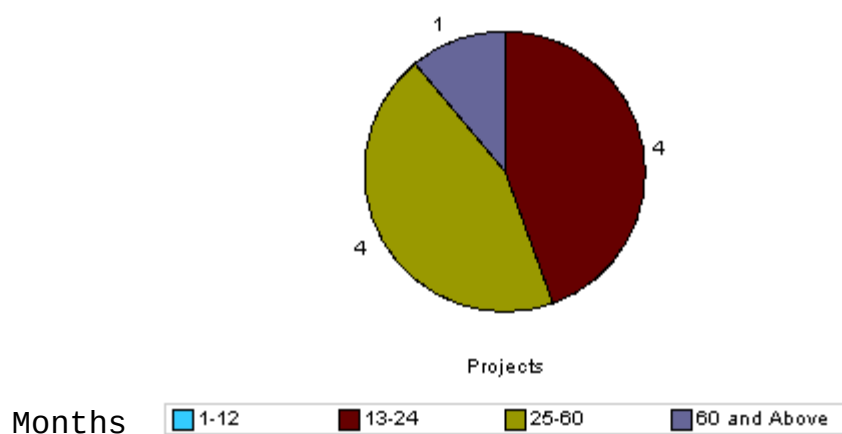


Trend and Graphical Analysis Shipping and Ports Sector

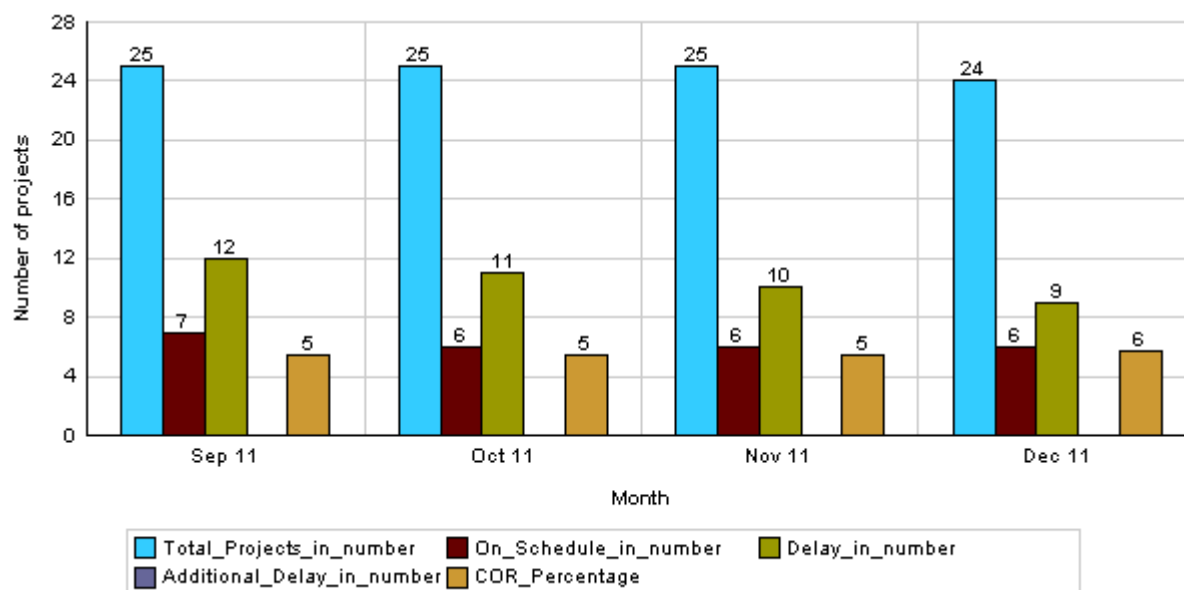


Sector Break-up of 9 Delayed projects in December 2011

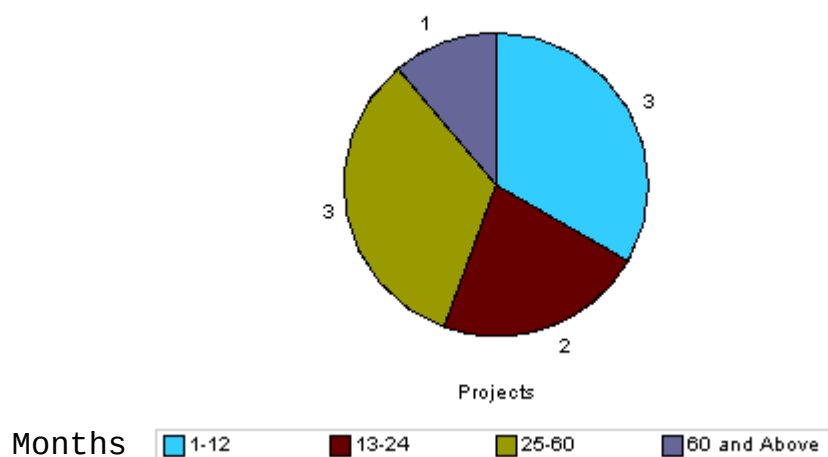

Trend and Graphical Analysis Road Transport and Highways Sector

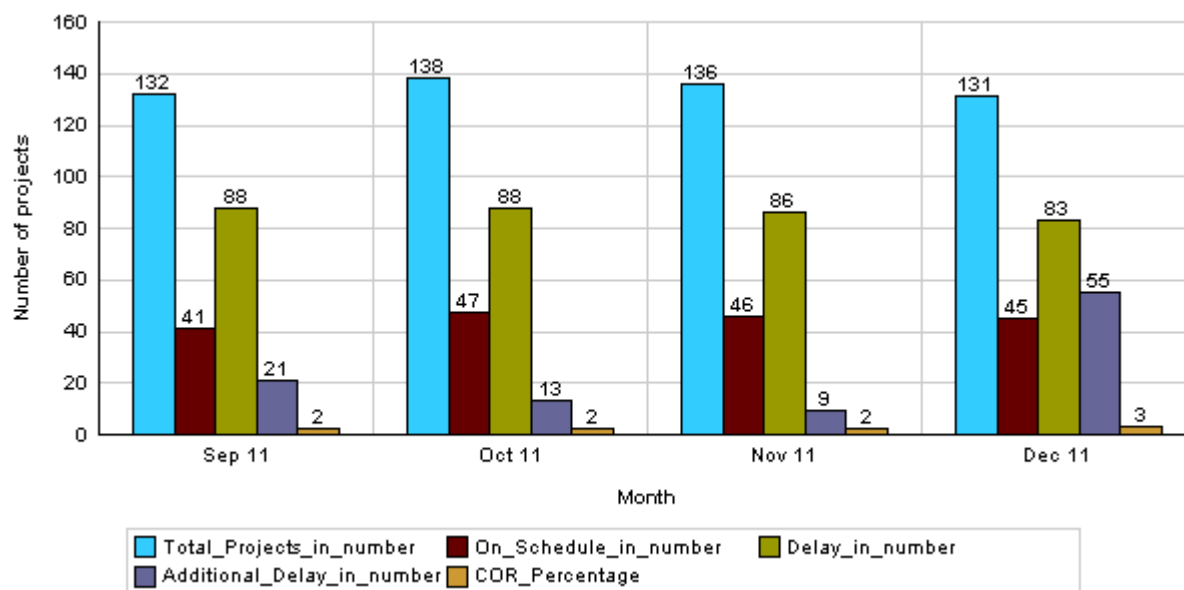


Sector Break-up of 83 Delayed projects in December 2011

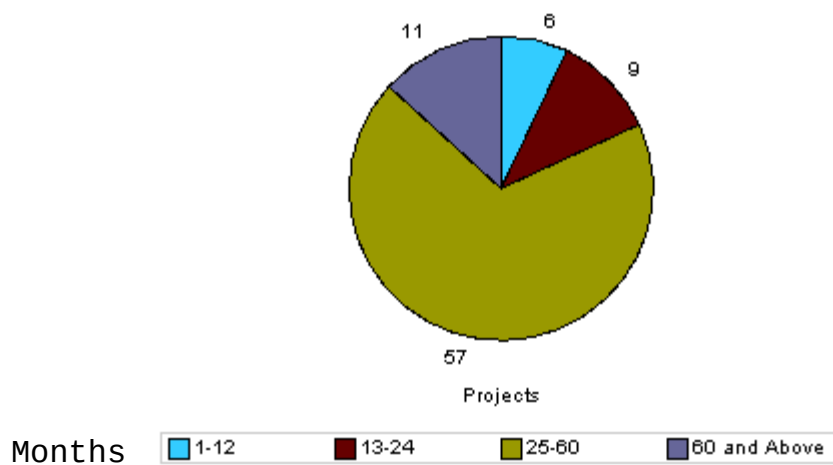


Trend and Graphical Analysis

Railways Sector

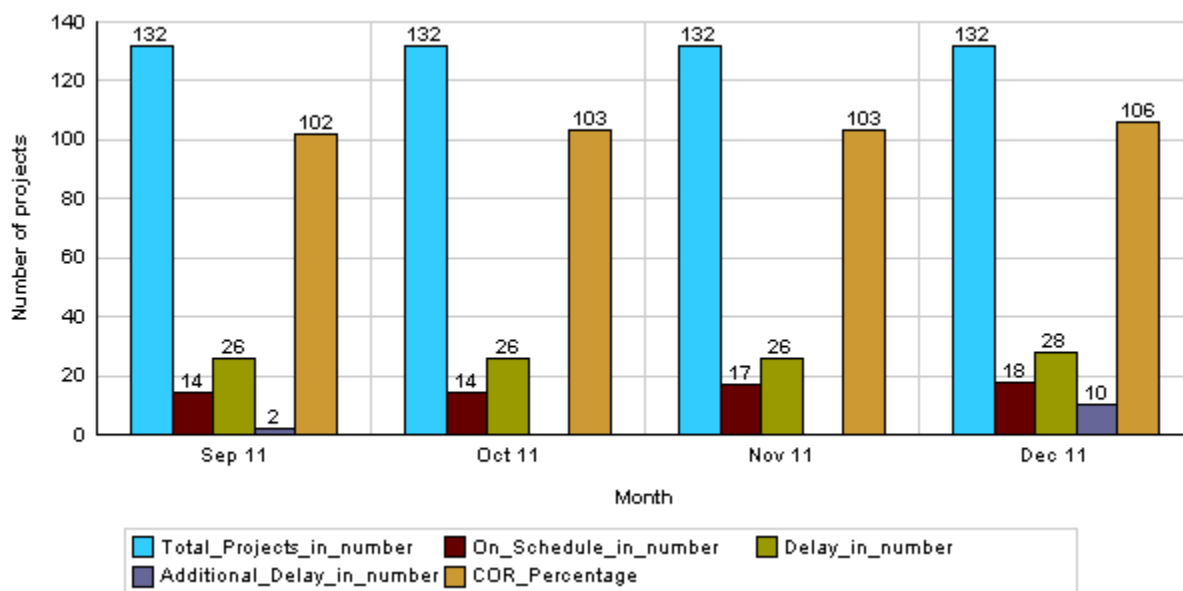


Railways Sector Sector Break-up of 28 Delayed projects in December 2011

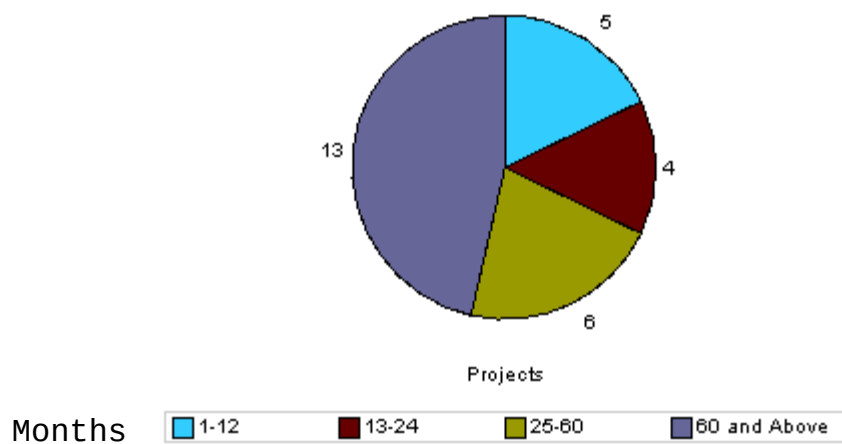


Trend and Graphical Analysis


Power Sector

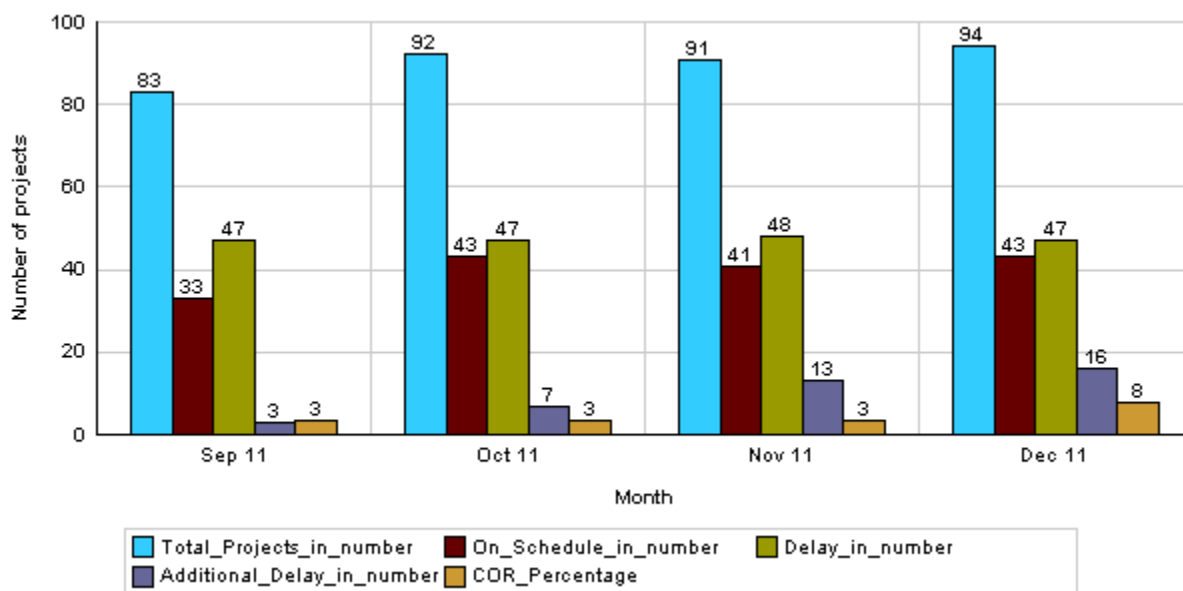


Power Sector Sector Break-up of 47 Delayed projects in December 2011

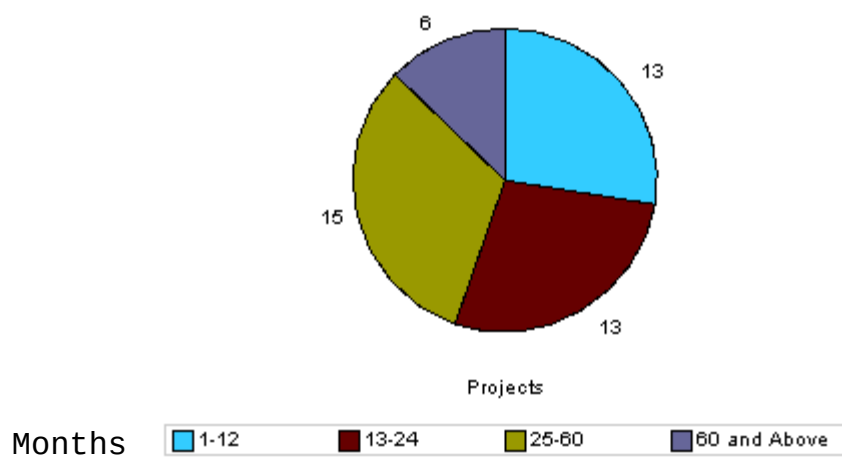

Trend and Graphical Analysis Petroleum Sector

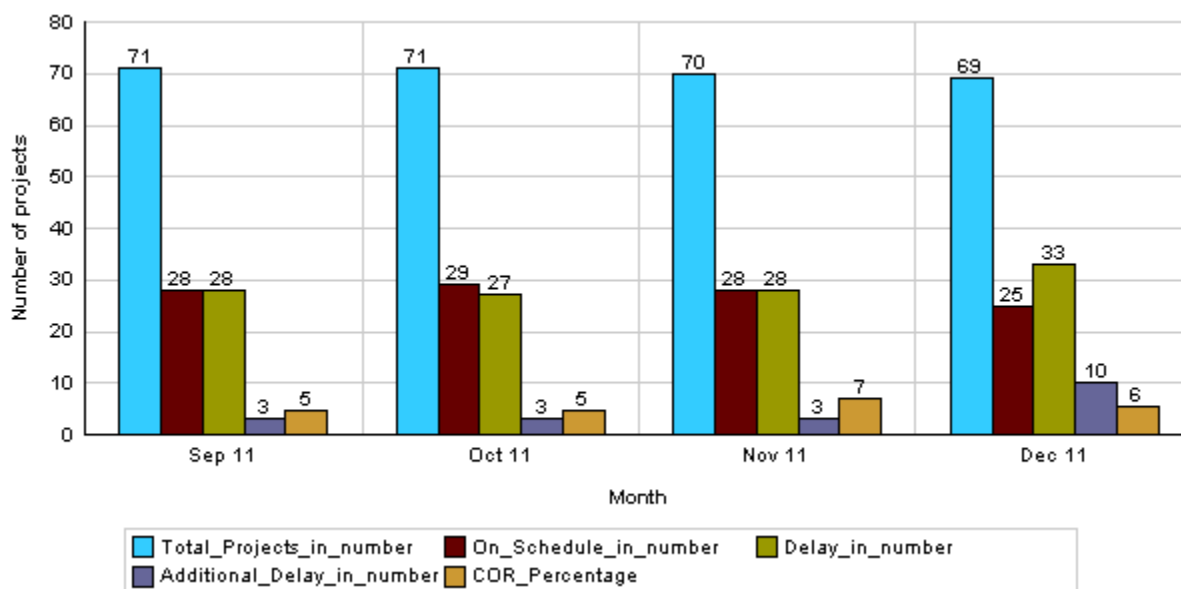


Petroleum Sector Sector Break-up of 33 Delayed projects in December 2011

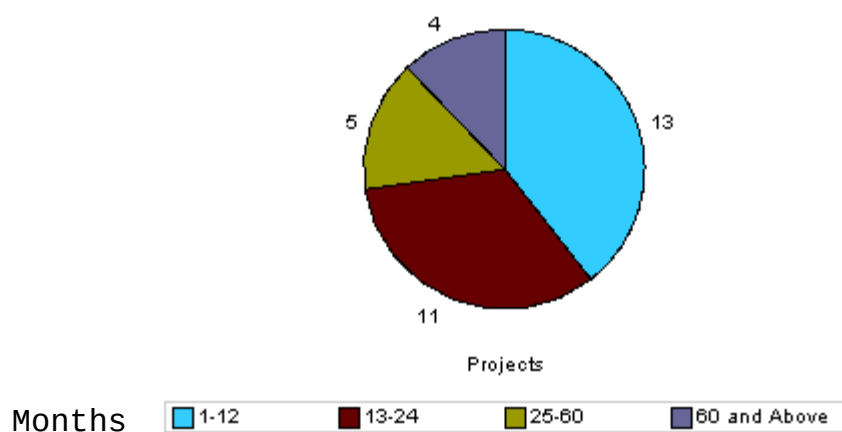


Trend and Graphical Analysis

Steel Sector

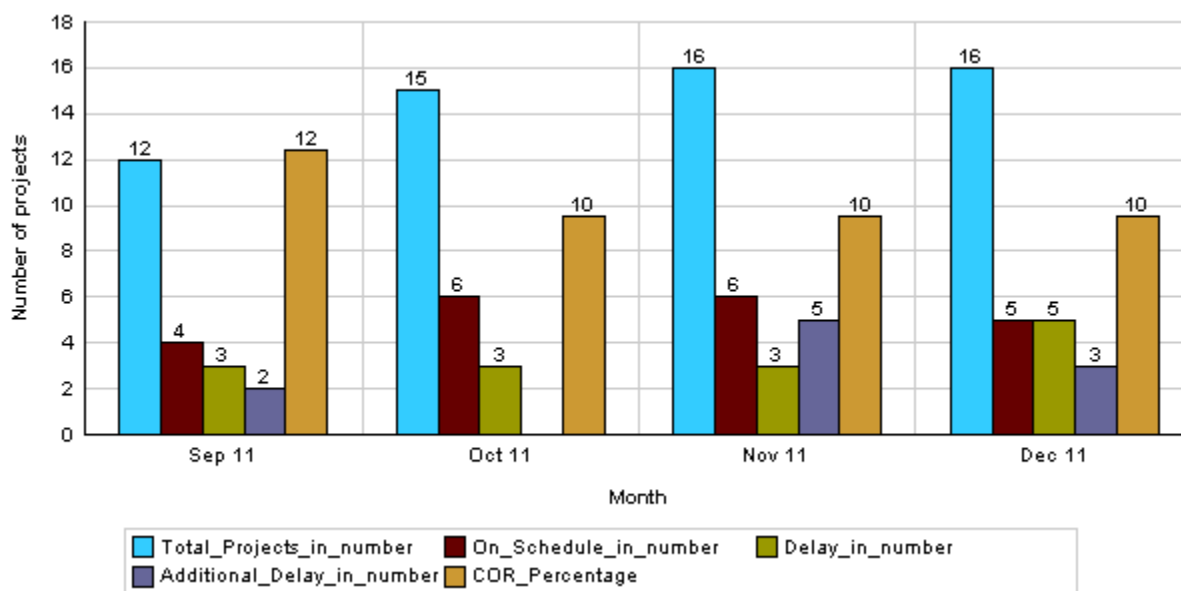


Steel Sector Sector Break-up of 5 Delayed projects in December 2011

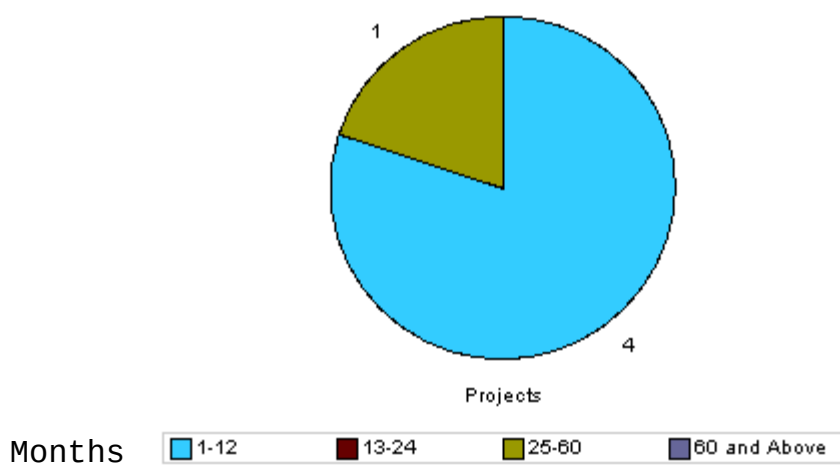


Trend and Graphical Analysis

Fertilisers Sector

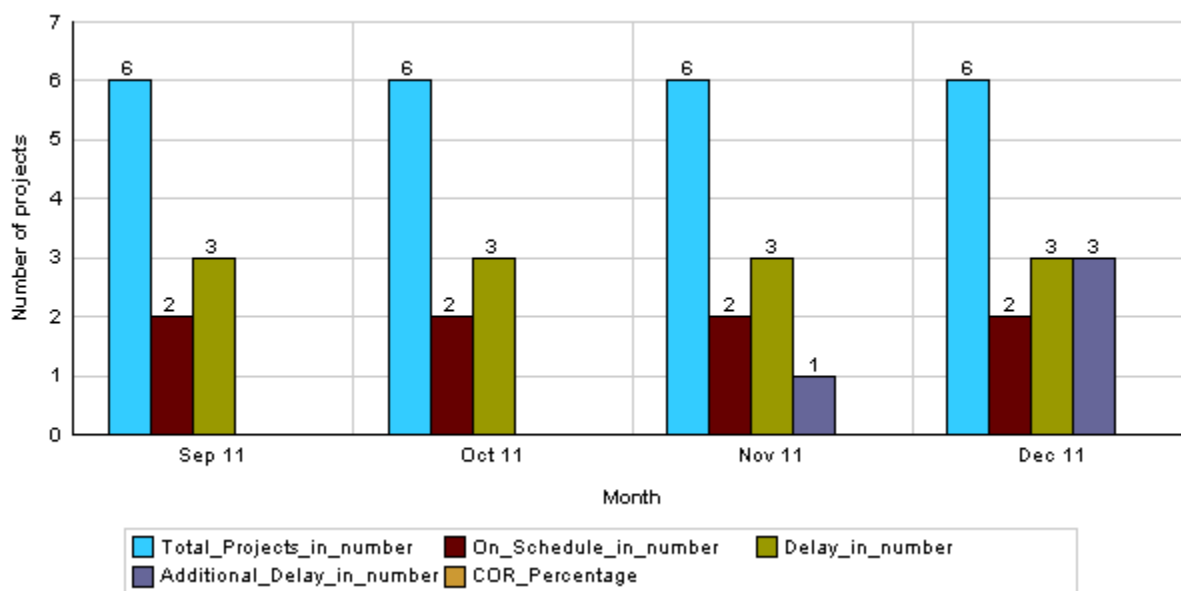


Fertilisers Sector Sector Break-up of 3 Delayed projects in December 2011

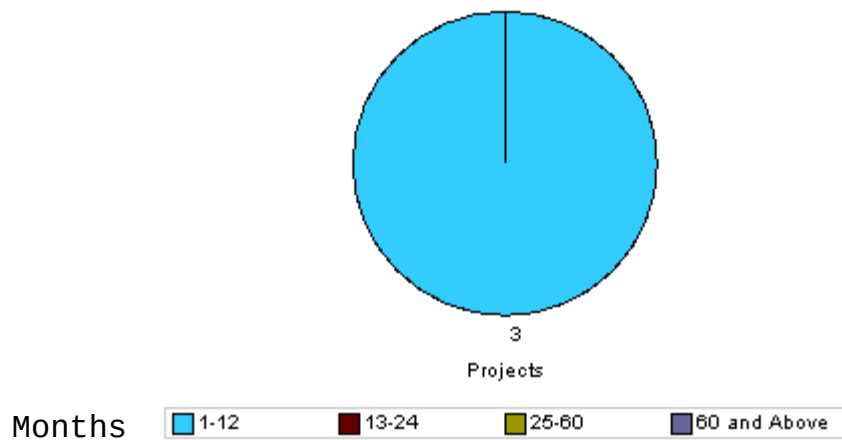


Trend and Graphical Analysis

Coal Sector

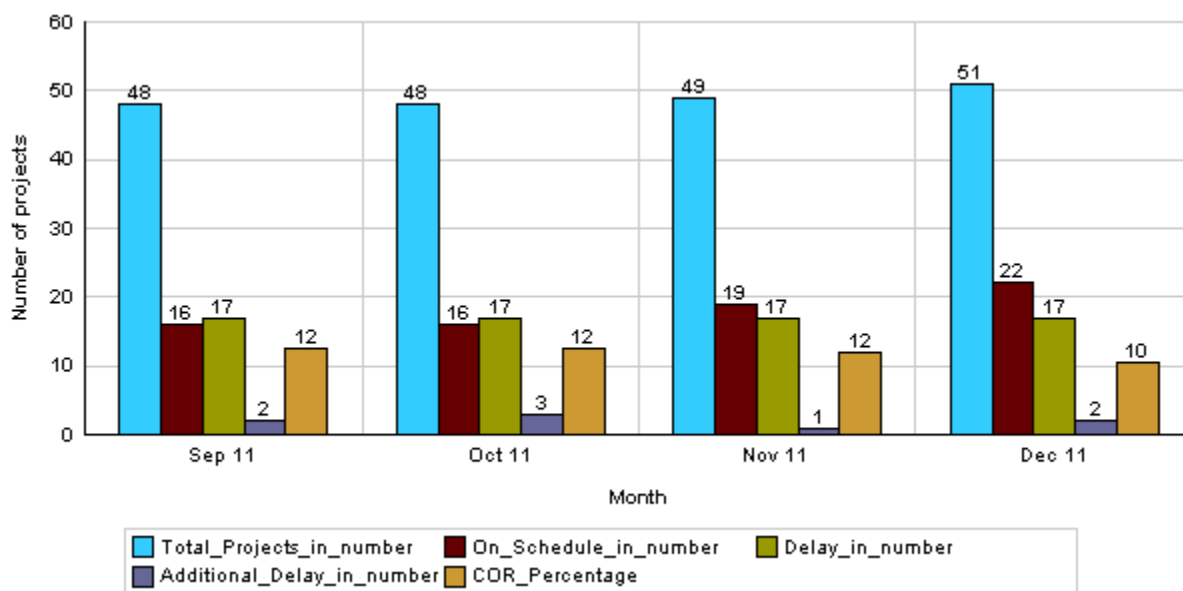


Coal Sector Sector Break-up of 17 Delayed projects in December 2011

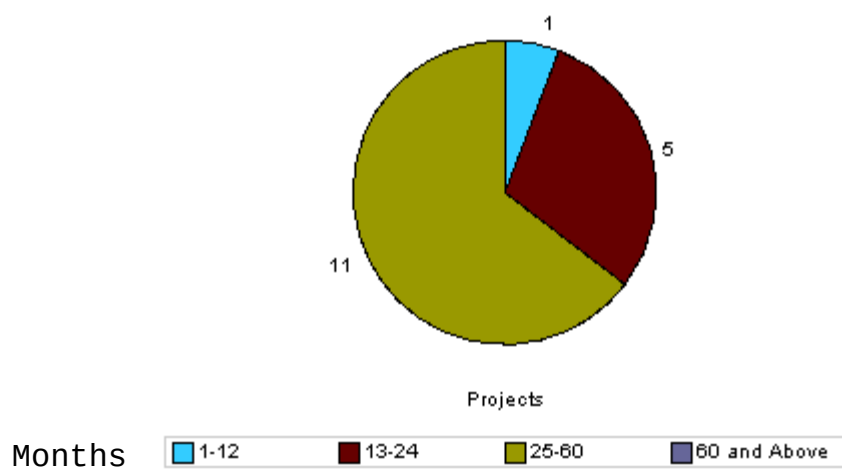


Trend and Graphical Analysis

Civil Aviation Sector

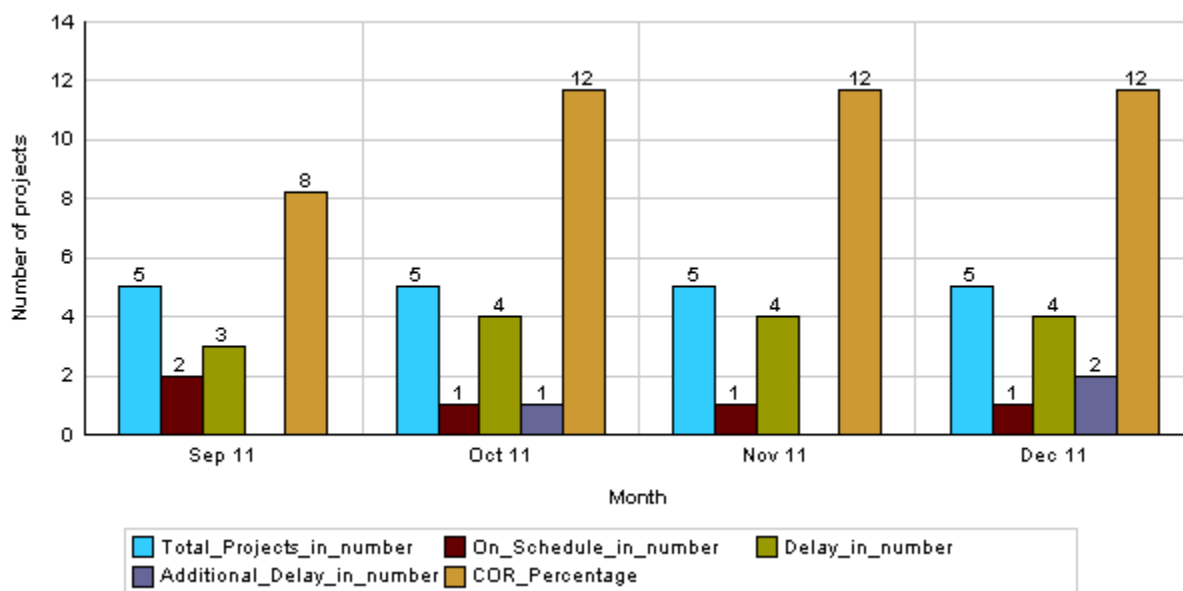


Civil Aviation Sector Break-up of 4 Delayed projects in December 2011

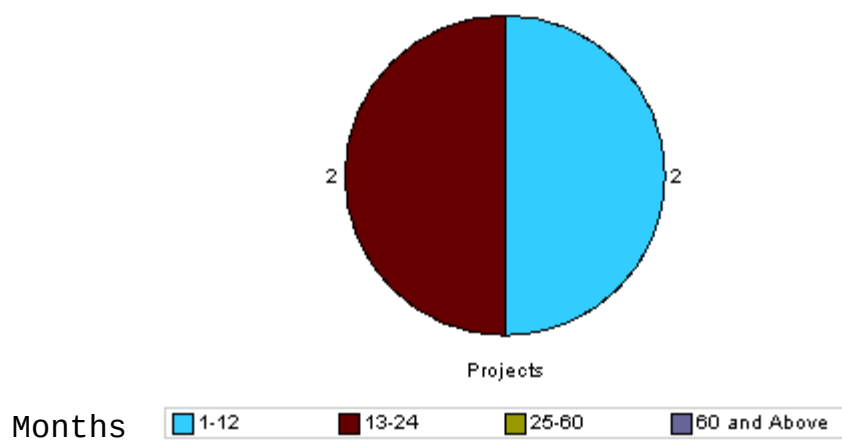

Trend and Graphical Analysis

Atomic Energy Sector

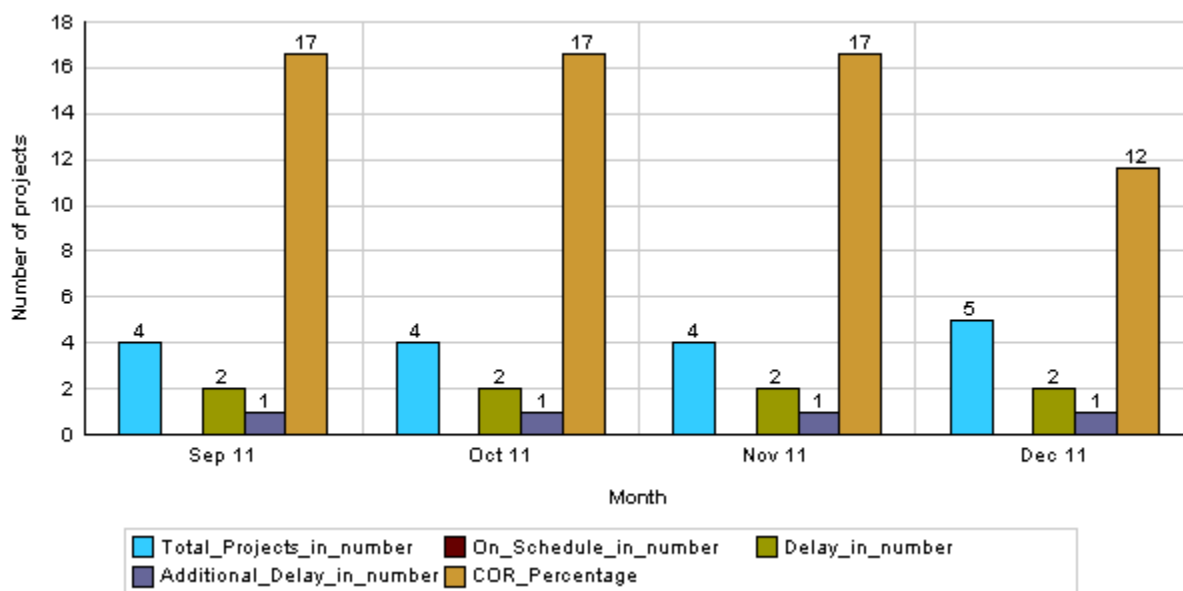

Atomic Energy Sector Sector Break-up of 2 Delayed projects in December 2011



Months



Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	41,548.29	41,548.29	46,386.29
Civil Aviation	5	5,021.58	5,228.58	5,611.07
Coal	51	34,718.73	36,435.68	38,348.38
Fertilisers	6	5,317.41	5,317.41	5,317.41
Steel	16	65,244.82	71,120.10	71,412.36
Petrochemicals	1	5,460.61	8,920.00	8,920.00
Petroleum	69	149,804.77	163,049.42	158,021.15
Power	94	195,705.41	201,502.24	211,046.35
Railways	132	65,054.74	87,302.55	134,133.50
Road Transport & Highways	131	73,894.67	74,061.17	75,983.76
Shipping & Ports	24	17,822.23	18,254.04	18,838.27
Telecommunications	22	11,794.14	11,798.02	12,010.64
Urban Development	4	44,245.18	44,304.08	49,518.08
Water Resources	1	542.90	542.90	1,187.00
Grand total	561	716,175.48	769,384.48	836,734.26

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,376.91	09/2010	01/2012	16(O)	5/80
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/0
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,212.00	12/2008	03/2013	51(O)	39/106
4	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,261.00	- 05/2016	11/2016	6(R1)	0/0
5	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,	10/2009	12,320.00	12,320.00	823.00	- -	12/2016	-	0/16
	Total		41,548.29	46,386.29	20,673.61				44/202
<u>Civil Aviation</u>									
6	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,574.69	01/2011	02/2012	13(O)	0/0
7	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,679.95	05/2011	03/2012	10(O)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	57.03	05/2012	08/2012	3(O)	0/0
9	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	166.54	01/2011	12/2012	23(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	326.92	06/2013	06/2013	0(O)	0/0
	Total		5,021.58	5,611.07	3,805.13				0/0
<u>Coal</u>									
11	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015	03/2015	0(O)	0/0
12	BARSINGSAR TPS (2 125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,868.71	1,697.55	06/2009	01/2012	31(O)	26/26
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	87.57	03/2010	03/2012	24(O)	9/11

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	43.06	03/2012 03/2012	03/2012	0(R3)	11/42
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhy Pradesh	10/2007	259.40 -	259.40	1.51	03/2012 -	03/2012	0(O)	0/1
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	96.75	- -	03/2012	-	4/4
17	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	71.46	- -	03/2012	-	5/7
18	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	79.01	03/2012 -	03/2012	0(O)	21/27
19	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	26.39	03/2012 03/2012	03/2012	0(R3)	8/34
20	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,316.04	06/2009 -	07/2012	37(O)	19/24
21	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,362.39	- -	02/2013	-	0/39
22	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	105.51	03/2011 03/2012	03/2013	12(R3)	0/2
23	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhy Pradesh	05/2006	789.88 -	741.62	289.22	03/2010 -	03/2013	36(O)	2/2
24	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	576.38	- -	03/2013	-	0/8
25	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	12.31	03/2013 03/2013	03/2013	0(R3)	3/83
26	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	115.80	- -	03/2013	-	6/11
27	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	85.28	- -	03/2013	-	5/7
28	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	31.39	03/2013 -	03/2013	0(O)	0/2
29	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	219.22	03/2013 09/2012	12/2013	15(R3)	5/22
30	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,281.50	03/2010 -	03/2014	48(O)	0/15
31	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,136.49	03/2010 -	03/2014	48(O)	0/13
32	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	40.35	03/2014 -	03/2014	0(O)	1/2
33	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	261.05	- -	03/2014	-	0/4
34	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.96	03/2011 -	03/2014	36(O)	0/3
35	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	203.27	-	03/2014	-	0/5
37	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	33.66	03/2011 03/2012	03/2014	24(R3)	1/2
38	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	61.08	03/2012 03/2012	03/2014	24(R3)	0/2
39	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	89.01	03/2012 03/2013	03/2014	12(R3)	0/2
40	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	30.97	03/2014	03/2014	0(O)	0/0
41	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	339.88	-	04/2014	04/2014	0(O)	0/0
42	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77	339.77	0.65	-	10/2014	-	0/1
43	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	140.46	03/2012	03/2015	36(O)	2/2
44	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	1/5
45	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	58.80	-	03/2015	-	2/12
46	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
47	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	71.02	12/2012	03/2015	27(O)	7/44
48	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
49	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	1/1
50	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	19.87	03/2015 03/2015	03/2015	0(R3)	4/31
51	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
52	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.17	03/2015	03/2015	0(O)	0/0
53	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	1,230.27	-	04/2015	04/2015	0(O)	0/0
54	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	6.25	12/2015	12/2015	0(O)	0/0
55	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	236.02	03/2014	03/2016	24(O)	2/2
56	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	18.16	07/2012 03/2014	03/2016	24(R3)	1/2
57	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	34.28	-	03/2016	-	1/12
58	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	90.98	03/2016	03/2016	0(O)	0/1
59	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	282.99	03/2016	03/2016	0(O)	1/2

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
60	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL, Orissa	12/2007	490.00 -	490.10	101.17	- -	03/2017	-	6/12
61	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA, 6MT - [N06000091]NCL, Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 -	03/2018	0(O)	0/0
	Total		34,718.73 -	38,348.38	12,436.00				154/558
<u>Fertilisers</u>									
62	CAPACITY ENHANCEMENT OF VIJAI PUR-I PLANTS - [N08000007]NFL, Madhya Pradesh	09/2008	325.00 -	325.00	150.34	07/2011 -	03/2012	8(O)	0/0
63	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF, Haryana	01/2009	488.75 -	488.75	214.81	- 04/2012	04/2012	0(R3)	6/22
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL, Madhya Pradesh	09/2008	438.00 -	438.00	150.34	07/2011 -	04/2012	9(O)	0/0
65	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL, Haryana	01/2010	1,292.84 -	1,292.84	269.37	01/2013 -	01/2013	0(O)	0/5
66	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL, Punjab	01/2010	1,294.19 -	1,294.19	265.54	01/2013 -	01/2013	0(O)	0/5
67	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL, Punjab	01/2010	1,478.63 -	1,478.63	375.78	12/2012 -	01/2013	1(O)	8/8
	Total		5,317.41 -	5,317.41	1,426.18				14/40
<u>Steel</u>									
68	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL, Jharkhandd	10/2007	500.90 -	500.90	340.61	- -	01/2012	-	3/3
69	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Chhatisgarh	07/2007	232.93 -	232.93	178.90	05/2011 -	02/2012	9(O)	1/1
70	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	313.84	- 12/2011	03/2012	3(R3)	15/21
71	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	12,417.12	12/2011 -	03/2012	3(O)	13/14
72	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhandd	01/2008	6,325.00 -	6,325.00	2,305.64	12/2011 -	03/2012	3(O)	10/11
73	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	230.10	- 08/2010	03/2012	19(R3)	0/1
74	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	236.27	- 02/2011	04/2012	14(R3)	2/3

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
75	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,050.03	10/2009 10/2012	10/2012	0(R3)	57/59
76	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	56.61	- 10/2012	10/2012	0(R3)	3/4
77	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	460.00	165.56	- 05/2012	12/2012	7(R3)	1/2
78	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, Chhatisgarh	06/2009	2,875.00 -	2,875.00	443.66	12/2012 -	12/2012	0(O)	4/6
79	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Chhatisgarh	09/2008	11,812.00 11,812.00	11,812.00	5,883.40	03/2013 -	03/2013	0(O)	5/8
80	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
81	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC, Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
82	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00 -	17,265.00	4,139.18	03/2013 -	06/2013	3(O)	17/20
83	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55 -	254.55	1.11	11/2013 -	11/2013	0(O)	0/0
Total			65,244.82 -	71,412.36	35,762.03				131/153
<u>Petrochemicals</u>									
84	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	3,637.35	- 12/2013	12/2013	0(R3)	9/30
Total			5,460.61 -	8,920.00	3,637.35				9/30
<u>Petroleum</u>									
85	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL, Maharashtra	06/2008	304.40 -	304.40	259.52	09/2010 -	09/2010	0(O)	10/61
86	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
87	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]BRPL, Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
88	EURO-IV DHDH - [N16000109]CPCL, Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,754.80	- -	12/2011	-	0/116
89	MNW-NF BRIDGE PROJECT - [N16000045]ONGC, Maharashtra	05/2008	175.21 -	162.12	124.45	03/2009 02/2012	01/2012	-1(R3)	0/0
90	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL, Gujarat	02/2009	250.00 349.00	250.00	219.18	03/2013 03/2013	01/2012	-14(R1)	0/0
91	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 12,160.26	12,160.26	7,552.41	01/2012 -	01/2012	0(O)	0/0
92	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	- 12/2008	03/2012	39(R3)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	0(R3)	0/0
94	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL, Multi State	11/2007	1,816.07 -	1,385.00	1,035.30	10/2010 12/2011	03/2012	3(R3)	0/1
95	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	674.74	04/2011 12/2011	03/2012	3(R3)	2/2
96	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 898.00	898.00	779.06	09/2011 03/2012	03/2012	0(R3)	0/0
97	HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70 -	706.70	668.00	04/2010 -	03/2012	23(O)	0/0
98	NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08 -	305.08	279.30	04/2011 -	03/2012	11(O)	0/0
99	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	934.05	09/2011 03/2012	03/2012	0(R3)	0/0
100	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL, Multi State	06/2009	348.00 -	261.00	178.09	03/2012 08/2012	03/2012	-5(R3)	1/4
101	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	177.19	06/2011 03/2012	03/2012	0(R3)	9/9
102	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	530.44	03/2011 05/2011	03/2012	10(R3)	0/0
103	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL, Gujarat	02/2009	267.00 -	267.00	185.70	09/2012 09/2012	03/2012	-6(R3)	0/0
104	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL, Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
105	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 252.37	204.00	153.70	01/2012 -	04/2012	3(O)	3/8
106	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
107	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,185.96	05/2010 05/2012	05/2012	0(R3)	0/0
108	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	113.49	05/2010 04/2012	05/2012	1(R3)	0/0
109	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	353.92	07/2010 05/2012	05/2012	0(R3)	0/0
110	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	715.36	09/2011 05/2012	05/2012	0(R3)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
111	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	79.60	- -	05/2012	-	21/36
112	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	2,050.63	08/2010 03/2012	06/2012	3(R3)	0/0
113	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	612.54	06/2012 -	06/2012	0(O)	0/0
114	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,300.00	911.98	06/2012 06/2012	06/2012	0(R3)	6/8
115	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	120.24	04/2011 -	07/2012	15(O)	0/0
116	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	170.50	06/2011 07/2012	07/2012	0(R2)	9/9
117	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	503.58	07/2012 -	07/2012	0(O)	0/0
118	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,480.98	03/2012 08/2012	08/2012	0(R3)	0/3
119	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	131.65	08/2012 -	08/2012	0(O)	0/0
120	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,743.40	09/2012 -	09/2012	0(O)	0/0
121	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,400.00	524.32	09/2012 09/2012	09/2012	0(R3)	0/11
122	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	23.44	09/2012 -	09/2012	0(O)	0/0
123	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.71	09/2011 -	12/2012	15(O)	0/0
124	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	400.34	10/2012 12/2012	12/2012	0(R3)	0/0
125	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	98.77	12/2011 -	01/2013	13(O)	0/0
126	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	50.90	01/2013 01/2013	01/2013	0(R3)	14/18
127	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2(O)	0/0
128	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	36.72	02/2013 02/2013	02/2013	0(R3)	22/42
129	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	258.24	03/2006 03/2013	03/2013	0(R3)	6/6

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
130	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2013	12(R1)	0/0
131	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,788.99	05/2010 03/2013	03/2013	0(R3)	0/0
132	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	398.22	03/2013 -	03/2013	0(O)	0/0
133	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
134	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	1.50	03/2013 -	03/2013	0(O)	0/0
135	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0
136	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	342.69	- 04/2013	04/2013	0(R3)	0/167
137	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	04/2013	10(O)	0/0
138	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	861.79	-	05/2013 -	05/2013	0(O)	0/0
139	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	12,266.00	11/2012 11/2012	06/2013	7(R3)	47/100
140	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
141	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	20.01	12/2013 12/2013	12/2013	0(R3)	0/0
142	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
143	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	-	01/2014 -	01/2014	0(O)	0/0
144	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	452.61	02/2014 -	02/2014	0(O)	0/0
145	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	595.83	03/2007 03/2014	03/2014	0(R3)	3/3
146	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.30	10/2010 -	12/2014	50(O)	0/0
147	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	-	12/2014 -	12/2014	0(O)	0/0
148	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014	0(O)	0/0
149	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	-	04/2015 -	04/2015	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
150	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	1.63	01/2013	07/2015	30(O)	0/0
151	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,413.90	03/2007 03/2017	03/2017	0(R3)	6/6
152	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	246.67	02/2011 08/2011	08/2011	0(R3)	0/0
153	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	6.93	-	-	-	0/0
Total			149,804.77	158,021.15	61,434.94				159/610
Power									
154	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJEC - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	-	08/2014	08/2011	-36(O)	0/0
155	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	137.90	06/2010 06/2010	01/2012	19(R3)	0/0
156	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	333.30	02/2012	02/2012	0(O)	0/0
157	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	68.20	02/2012 02/2012	02/2012	0(R3)	0/0
158	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	166.00	08/2011	02/2012	6(O)	0/0
159	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	215.80	07/2010 02/2012	02/2012	0(R3)	0/0
160	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	104.70	07/2011	02/2012	7(O)	0/0
161	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 2,283.68	2,283.69	2,559.40	04/2005	03/2012	83(O)	9/11
162	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,532.00	12/2009	03/2012	27(O)	50/60
163	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	2,084.00	1,713.78	08/2010 08/2011	03/2012	7(R3)	0/3
164	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.66	712.30	10/2009	03/2012	29(O)	20/20
165	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.83	4,262.00	05/2011 05/2011	03/2012	10(R3)	2/6
166	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	306.13	07/2011	03/2012	8(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	215.86	131.90	06/2012 -	03/2012	-3(O)	0/0
168	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	123.10	04/2012 -	04/2012	0(O)	0/0
169	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.25	713.40	02/2011 08/2011	05/2012	9(R3)	1/4
170	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	387.90	05/2012 -	05/2012	0(O)	0/0
171	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	1,794.00	1,630.92	11/2009 11/2011	06/2012	7(R3)	0/4
172	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,779.29	1,758.98	09/2008 -	06/2012	45(O)	3/38
173	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,779.46	3,514.40	09/2009 -	06/2012	33(O)	11/30
174	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	512.20	01/2010 01/2010	06/2012	29(R3)	0/22
175	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,010.70	07/2010 -	06/2012	23(O)	20/20
176	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	119.30	11/2011 11/2011	06/2012	7(R3)	0/0
177	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	942.30	02/2012 -	06/2012	4(O)	0/0
178	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	520.10	06/2012 -	06/2012	0(O)	0/0
179	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	37.88	06/2012 -	06/2012	0(O)	0/0
180	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,758.20	08/2012 -	08/2012	0(O)	0/0
181	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	4,329.70	08/2012 -	08/2012	0(O)	0/0
182	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	537.70	08/2012 -	08/2012	0(O)	0/0
183	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.39	1,418.05	03/2007 -	09/2012	66(O)	25/25
184	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,278.40	10/2012 -	10/2012	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
185	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	199.20	10/2012	10/2012	0(O)	0/0
186	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	15.00	10/2012	10/2012	0(O)	0/0
187	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	505.00	11/2012	11/2012	0(O)	0/0
188	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	291.30	11/2012	11/2012	0(O)	0/0
189	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	137.90	11/2012	11/2012	0(O)	0/0
190	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	685.00	11/2011	12/2012	13(O)	6/34
191	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	2,856.50	12/2012	12/2012	0(O)	0/0
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	251.30	11/2011	12/2012	13(O)	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	304.20	11/2011	12/2012	13(O)	0/0
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	149.50	02/2012	12/2012	10(O)	0/0
195	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	488.80	12/2012	12/2012	0(O)	0/0
196	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,716.00	1,639.06	10/2010 12/2011	01/2013	13(R3)	0/1
197	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	702.55	08/2010 09/2011	01/2013	16(R3)	0/3
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	26.80	01/2013	01/2013	0(O)	0/0
199	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	29.90	01/2013	01/2013	0(O)	0/0
200	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,967.00	04/2009	03/2013	47(O)	0/9
201	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	382.80	09/2010	03/2013	30(O)	0/0
202	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	3,215.00	08/2012	03/2013	7(O)	6/16
203	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	2,531.00	10/2012	03/2013	5(O)	3/15

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
204	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,364.00	10/2012 -	03/2013	5(O)	5/16
205	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	257.50	03/2013 -	03/2013	0(O)	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	158.60	04/2013 -	04/2013	0(O)	0/0
207	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	11.10	04/2013 -	04/2013	0(O)	0/0
208	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,059.04	09/2009 -	06/2013	45(O)	0/0
209	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	89.84	01/2012 07/2013	07/2013	0(R3)	0/0
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	98.50	07/2013 -	07/2013	0(O)	0/0
211	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0
212	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0
213	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	262.14	08/2012 08/2013	08/2013	0(R3)	8/18
214	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	156.30	08/2013 -	08/2013	0(O)	0/0
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	20.60	08/2013 -	08/2013	0(O)	0/0
216	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	178.50	08/2013 -	08/2013	0(O)	0/0
217	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,462.50	01/2012 -	09/2013	20(O)	0/0
218	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	137.00	11/2011 -	09/2013	22(O)	0/0
219	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,598.00	06/2011 -	10/2013	28(O)	1/29
220	BARH STTP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,211.00	08/2013 08/2013	10/2013	2(R3)	5/18
221	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	-	10/2013 -	10/2013	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	117.20	11/2013	11/2013	0(O)	0/0
223	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26	558.26	-	11/2013	11/2013	0(O)	0/0
224	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	-	12/2013	11/2013	-1(O)	0/0
225	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	207.60	12/2013	12/2013	0(O)	0/0
226	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34	1,366.34	-	12/2013	12/2013	0(O)	0/0
227	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	-	12/2013	12/2013	0(O)	0/0
228	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72	913.63	293.42	07/2006	01/2014	0(R3)	5/5
229	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44	552.44	-	02/2014	02/2014	0(O)	0/0
230	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	72.90	03/2014	03/2014	0(O)	0/0
231	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	31.00	05/2014	05/2014	0(O)	0/0
232	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,246.00	03/2013	06/2014	15(O)	2/13
233	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	-	06/2014	06/2014	0(O)	0/0
234	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	-	08/2014	08/2014	0(O)	0/0
235	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	-	08/2014	08/2014	0(O)	0/0
236	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	-	08/2014	08/2014	0(O)	0/0
237	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	3,239.10	08/2013	09/2014	13(O)	0/0
238	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	-	09/2014	09/2014	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
239	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 8,693.00	8,692.97	6,324.00	12/2009 11/2010	10/2014	47(R3)	45/70
240	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,434.73	09/2009 07/2014	12/2014	5(R3)	1/20
241	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	-	01/2015 -	01/2015	0(O)	0/0
242	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,290.06	09/2010 08/2014	12/2015	16(R3)	11/11
243	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	278.27	07/2010 02/2016	02/2016	0(R3)	0/10
244	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,697.46	05/2013 06/2016	06/2016	0(R3)	2/22
245	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 3,422.44	3,422.44	233.48	07/2014 -	09/2016	26(O)	4/7
246	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,083.48	01/2016 01/2016	11/2016	10(R3)	0/2
247	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	814.90	12/2007 12/2009	-	-	0/18
Total			195,705.41 -	211,046.35	96,642.67				245/580
<u>Railways</u>									
248	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	58.22	02/2015 -	02/2015	0(O)	0/0
249	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	-	- -	12/2010	-	0/0
250	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	88.49	12/2012 -	12/2012	0(O)	0/0
251	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	176.57	03/1998 08/2005	08/2005	0(R1)	0/0
252	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 227.52	227.52	258.80	03/2008 03/2009	10/2010	19(R1)	0/0
253	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	176.98	12/2007 03/2010	12/2010	9(R1)	0/0
254	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	297.37	03/2009 12/2008	12/2010	24(R1)	0/0
255	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	475.12	06/1999 03/2011	03/2011	0(R3)	0/0
256	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	331.25	- -	03/2011	-	0/0
257	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	242.59	- 03/2011	03/2011	0(R3)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
258	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	273.00	304.39	- 03/2009	03/2011	24(R1)	0/0
259	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 -	329.70	267.79	03/2009 12/2009	03/2011	15(R1)	0/0
260	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 -	435.87	365.15	- 03/2011	03/2011	0(R3)	0/0
261	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP, Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,228.31	- 06/2011	06/2011	0(R3)	1/1
262	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O)	0/0
263	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 -	735.10	199.78	- 09/2009	12/2011	27(R1)	0/0
264	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	254.35	03/2013 -	12/2011	-15(O)	0/0
265	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	596.33	- -	02/2012	-	0/0
266	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,206.84	- -	02/2012	-	0/0
267	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 762.33	762.33	439.42	- 12/2009	02/2012	26(R1)	0/0
268	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER, West Bengal	04/2009	259.51 -	259.51	71.20	12/2011 02/2012	02/2012	0(R3)	0/0
269	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 634.13	634.13	544.82	03/1995 -	03/2012	204(O)	0/0
270	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 407.78	820.32	532.41	- -	03/2012	-	0/0
271	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, Orissa	04/1993	100.00 142.98	227.94	190.08	03/2002 -	03/2012	120(O)	0/0
272	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, Jharkhand	04/1995	184.00 254.07	675.00	482.31	- 12/2011	03/2012	3(R3)	0/0
273	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL), (SWR) - [220100190]SWR, Karnataka	04/1996	157.00 262.82	262.82	212.77	- 03/2012	03/2012	0(R3)	0/0
274	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 164.36	840.32	516.14	02/2009 -	03/2012	37(O)	0/0
275	MUZAFFARPUR-SITAMARHI(NL), ECR - [220100194]ECR, Bihar	04/1997	100.00 483.62	411.22	426.86	- 03/2012	03/2012	0(R3)	0/0
276	MUNEERABAD-MAHABOONAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	537.47	95.27	- -	03/2012	-	0/0
277	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 501.69	903.56	577.49	- 03/2012	03/2012	0(R3)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
278	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	242.14	- 02/2011	03/2012	13(R3)	0/0
279	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	181.53	- -	03/2012	-	0/0
280	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	427.89	349.47	- 03/2012	03/2012	0(R3)	0/0
281	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	197.98	- -	03/2012	-	0/0
282	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	944.25	- -	03/2012	-	0/0
283	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	194.01	03/2010 -	03/2012	24(O)	0/0
284	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	219.79	- -	03/2012	-	0/0
285	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	0(O)	0/0
286	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12(O)	0/0
287	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	183.88	03/2011 -	03/2012	12(O)	0/0
288	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	36.31	03/2012 -	03/2012	0(O)	0/0
289	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	51.65	03/2012 -	03/2012	0(O)	0/0
290	Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	5.98	03/2012 -	03/2012	0(O)	0/0
291	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	332.01	- 07/2012	07/2012	0(R3)	0/0
292	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	293.16	06/2004 -	12/2012	102(O)	0/0
293	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	817.73	12/2012 -	12/2012	0(O)	0/0
294	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	353.59	- 03/2012	12/2012	9(R3)	0/0
295	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	246.11	- 03/2012	12/2012	9(R3)	0/0
296	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	592.94	03/2009 12/2012	12/2012	0(R3)	0/0
297	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,101.12	10/2007 12/2012	12/2012	0(R3)	0/0
298	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	452.38	03/2010 -	12/2012	33(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
299	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	110.37	12/2012 -	12/2012	0(O)	0/0
300	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	160.18	- -	03/2013	-	0/0
301	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	708.55	- -	03/2013	-	0/0
302	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	876.10	- -	03/2013	-	0/0
303	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	87.46	- -	03/2013	-	0/0
304	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.14	0.49	03/2013 -	03/2013	0(O)	0/0
305	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	236.08	- 02/2009	04/2013	50(R1)	0/0
306	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	189.84	- 03/2009	04/2013	49(R1)	0/0
307	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	147.46	- 06/2013	06/2013	0(R3)	0/0
308	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	75.30	12/2011 11/2013	11/2013	0(R3)	0/0
309	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	180.24	- -	12/2013	-	0/0
310	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	283.10	36.90	02/2006 -	12/2013	94(O)	0/0
311	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,885.61	03/2009 -	12/2013	57(O)	0/0
312	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	151.23	03/2007 03/2007	03/2014	84(R1)	0/0
313	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	991.07	12/2008 -	03/2014	63(O)	0/0
314	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.75	267.62	03/2014 -	03/2014	0(O)	0/0
315	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.49	3.79	04/2014 -	03/2014	-1(O)	0/0
316	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	52.83	03/2014 -	03/2014	0(O)	0/0
317	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	118.00	03/2014 -	03/2014	0(O)	0/0
318	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	203.78	03/2014 -	03/2014	0(O)	0/0
319	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	84.11	12/2012 -	03/2014	15(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
320	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	112.33	03/2010 06/2014	06/2014	0(R3)	0/0
321	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,279.87	04/2008 03/2014	12/2014	9(R3)	0/0
322	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	721.53	- 12/2010	03/2015	51(R3)	0/0
323	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	170.11	- -	03/2015	-	0/0
324	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	0(R3)	0/0
325	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
326	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
327	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	723.27	387.27	06/2005 07/2011	06/2015	47(R3)	0/0
328	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	208.25	02/2010 -	12/2015	70(O)	0/0
329	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.63	12/2015 -	12/2015	0(O)	0/0
330	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	1,211.22	411.62	03/2005 12/2008	03/2016	87(R1)	0/0
331	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	554.31	03/2011 03/2014	03/2016	24(R3)	0/0
332	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	4.01	03/2014 03/2016	03/2016	0(R3)	0/0
333	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	14.28	03/2016 -	03/2016	0(O)	0/0
334	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	71.47	03/2016 -	03/2016	0(O)	0/0
335	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	8.17	03/2016 -	06/2016	3(O)	0/0
336	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	7,340.14	03/2001 -	12/2017	201(O)	0/0
337	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	148.45	- 03/2010	-	-	0/0
338	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	235.30	- -	-	-	0/0
339	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	114.26	- -	-	-	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
340	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	483.14	- -	-	-	0/0
341	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	570.21	03/1998 -	-	-	0/0
342	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	945.73	646.16	- -	-	-	0/0
343	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.17	- -	-	-	0/0
344	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	458.26	0.35	07/2008 -	-	-	0/0
345	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,145.69	07/2005 -	-	-	0/0
346	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	71.02	- -	-	-	0/0
347	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	284.74	- 05/2009	-	-	0/0
348	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	88.18	- -	-	-	0/0
349	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	821.93	06/2007 -	-	-	0/0
350	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	313.40	04/2003 03/2010	-	-	0/0
351	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	486.74	- -	-	-	0/0
352	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
353	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	351.76	- 12/2012	-	-	0/0
354	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
355	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	80.36	- -	-	-	0/0
356	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	209.71	- -	-	-	0/0
357	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
358	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	389.08	03/2008 06/2008	-	-	0/0
359	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	218.59	- -	-	-	0/0
360	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	461.11	- -	-	-	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
361	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	33.42	- -	-	-	0/0
362	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	582.83	93.28	- -	-	-	0/0
363	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	529.88	37.89	- -	-	-	0/0
364	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
365	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	175.70	03/2011 -	-	-	0/0
366	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,413.07	172.18	03/2004 12/2010	-	-	0/0
367	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
368	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,302.12	1,302.12	608.97	- 06/2012	12/2012	6(R3)	0/0
369	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
370	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	863.23	451.29	- -	-	-	0/0
371	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	460.51	- -	-	-	1/1
372	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,225.00	12/2006 08/2010	-	-	0/0
373	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	478.76	02/2010 02/2011	-	-	0/0
374	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	381.90	- -	-	-	0/0
375	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	141.98	- -	-	-	0/0
376	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	135.47	- -	-	-	0/0
377	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	80.65	- -	-	-	0/0
378	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	180.42	12/2010 03/2011	-	-	0/0
379	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	132.78	- 12/2010	-	-	0/0
Total			65,054.74 -	134,133.50	56,395.52				2/2

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Road Transport & Highways								
380	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	212.54	06/2005	12/2011	78(O)	0/0
381	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	475.60	03/2005	01/2012	82(O)	0/0
382	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00	242.00	434.10	12/2008	01/2012	37(O)	0/0
383	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	01/2012	31(O)	0/0
384	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	343.30	03/2010	01/2012	22(O)	0/0
385	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	661.40	07/2010	01/2012	18(O)	0/0
386	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	173.32	08/2004	02/2012	90(O)	0/0
387	GAGODHAR-GARAMORE(PK-IV, NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78	479.54	437.40	11/2007	02/2012	51(O)	0/0
388	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	315.90	09/2009	02/2012	29(O)	0/0
389	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	946.63	07/2010	02/2012	19(O)	0/0
390	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	166.36	08/2004 07/2010	03/2012	20(R3)	0/0
391	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09	166.30	184.50	03/2008	03/2012	48(O)	0/0
392	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27	193.10	155.10	03/2008	03/2012	48(O)	0/0
393	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	285.60	10/2008	03/2012	41(O)	0/0
394	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	360.90	03/2008	03/2012	48(O)	0/0
395	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	03/2012	38(O)	0/0
396	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	262.60	06/2008	03/2012	45(O)	0/0
397	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	375.50	12/2008	03/2012	39(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
398	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	318.40	09/2008	03/2012	42(O)	0/0
399	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	464.70	09/2008	03/2012	42(O)	0/0
400	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,	04/2000	196.50	363.00	239.50	-	03/2012	9(R3)	0/0
401	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	252.70	11/2008	03/2012	40(O)	0/0
402	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	03/2012	14(O)	0/0
403	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	660.00	08/2010	03/2012	19(O)	0/0
404	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	420.00	01/2011	03/2012	14(O)	0/0
405	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,607.00	08/2011	03/2012	7(O)	0/0
406	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	257.50	10/2008	04/2012	42(O)	0/0
407	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	549.70	02/2012	04/2012	2(O)	0/0
408	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	174.00	10/2008	05/2012	43(O)	0/0
409	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	489.20	03/2008	05/2012	50(O)	0/0
410	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	258.92	02/2004	05/2012	99(O)	0/0
411	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
412	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00	284.00	346.80	05/2010	05/2012	24(O)	0/0
413	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.00	05/2012	05/2012	0(O)	0/0
414	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	863.70	05/2012	05/2012	0(O)	0/0
415	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	408.50	05/2012	05/2012	0(O)	0/0
416	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	185.00	09/2007	06/2012	57(O)	0/0
417	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	06/2012	87(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
418	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	298.70	09/2007	06/2012	57(O)	0/0
419	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	257.30	09/2007	06/2012	57(O)	0/0
420	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	94.14	09/2008	06/2012	45(O)	0/0
421	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.20	10/2008	06/2012	44(O)	0/0
422	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	178.50	06/2008	06/2012	48(O)	0/0
423	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	264.40	06/2008	06/2012	48(O)	0/0
424	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	261.29	06/2008	06/2012	48(O)	0/0
425	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	184.20	06/2008	06/2012	48(O)	0/0
426	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	130.40	05/2008	06/2012	49(O)	0/0
427	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	199.40	06/2008	06/2012	48(O)	0/0
428	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	454.00	12/2008	06/2012	42(O)	0/0
429	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	738.20	10/2009	06/2012	32(O)	0/0
430	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.60	10/2009	06/2012	32(O)	0/0
431	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.90	12/2009	06/2012	30(O)	0/0
432	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	396.80	06/2012	06/2012	0(O)	0/0
433	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,538.00	10/2011	06/2012	8(O)	0/0
434	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,736.00	11/2011	06/2012	7(O)	0/0
435	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	86.89	04/2004	07/2012	99(O)	0/0
436	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	173.06	02/2004	07/2012	101(O)	0/0
437	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	330.60	07/2012	07/2012	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
438	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	150.70	05/2008 -	08/2012	51(O)	0/0
439	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	277.50	10/2008 -	09/2012	47(O)	0/0
440	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	231.30	10/2008 -	09/2012	47(O)	0/0
441	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,098.00	09/2012 -	09/2012	0(O)	0/0
442	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	184.60	06/2010 -	10/2012	28(O)	0/0
443	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.40	09/2009 -	10/2012	37(O)	0/0
444	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16(O)	0/0
445	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	576.90	10/2011 -	10/2012	12(O)	0/0
446	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,266.00	10/2012 -	10/2012	0(O)	0/0
447	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	11/2012	41(O)	0/0
448	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	29.04	11/2012 -	11/2012	0(O)	0/0
449	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	11/2012 -	11/2012	0(O)	0/0
450	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	212.50	06/2008 -	12/2012	54(O)	0/0
451	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	214.50	10/2008 -	12/2012	50(O)	0/0
452	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	284.30	10/2008 -	12/2012	50(O)	0/0
453	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	177.40	07/2008 -	12/2012	53(O)	0/0
454	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	126.90	04/2008 -	12/2012	56(O)	0/0
455	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	189.20	04/2008 -	12/2012	56(O)	0/0
456	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	229.80	04/2008 -	12/2012	56(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
457	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	161.30	04/2010	12/2012	32(O)	0/0
458	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	173.60	09/2010	12/2012	27(O)	0/0
459	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	558.60	05/2010	12/2012	31(O)	0/0
460	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	784.40	12/2012	12/2012	0(O)	0/0
461	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	666.00	01/2013	01/2013	0(O)	0/0
462	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	117.20	02/2013	02/2013	0(O)	0/0
463	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	232.00	02/2009	03/2013	49(O)	0/0
464	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	86.27	04/2009	03/2013	47(O)	0/0
465	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	03/2013	32(O)	0/0
466	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	1,214.00	-	03/2013	-	0/0
467	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	813.90	03/2013	03/2013	0(O)	0/0
468	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	390.40	03/2013	03/2013	0(O)	0/0
469	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
470	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	107.60	03/2013	03/2013	0(O)	0/0
471	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	11.71	03/2013	03/2013	0(O)	0/0
472	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
473	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	533.30	05/2013	05/2013	0(O)	0/0
474	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	157.10	05/2013	05/2013	0(O)	0/0
475	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
476	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	351.54	3.91	05/2013	05/2013	0(O)	0/0
477	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	374.00	33.88	05/2013	05/2013	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
478	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	118.00	09/2007	06/2013	69(O)	0/0
479	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7(O)	0/0
480	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
481	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	97.76	06/2013	06/2013	0(O)	0/0
482	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	758.70	06/2013	06/2013	0(O)	0/0
483	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
484	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	34.80	04/2009	07/2013	51(O)	0/0
485	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	57.78	11/2008	07/2013	56(O)	0/0
486	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41(O)	0/0
487	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	73.26	07/2013	07/2013	0(O)	0/0
488	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	07/2013	0(O)	0/0
489	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	22.53	07/2013	07/2013	0(O)	0/0
490	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,	03/2011	839.00	839.00	-	-	08/2013	-	0/1
491	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	339.30	08/2013	08/2013	0(O)	0/0
492	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	182.50	08/2013	08/2013	0(O)	0/0
493	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	-	08/2013	08/2013	0(O)	0/0
494	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	5.59	09/2013	09/2013	0(O)	0/0
495	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	12.84	09/2013	09/2013	0(O)	0/0
496	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
497	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
498	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	358.40	11/2013	11/2013	0(O)	0/0
499	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	-	11/2013	11/2013	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
500	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
501	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
502	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
503	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	2.12	11/2008	01/2014	62(O)	0/0
504	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	200.80	10/2011	03/2014	29(O)	0/0
505	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	1.79	09/2007	04/2014	79(O)	0/0
506	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	0.36	07/2009	04/2014	57(O)	0/0
507	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	34.56	08/2014	08/2014	0(O)	0/0
508	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	456.00	10/2014	10/2014	0(O)	0/0
509	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
510	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
	Total		73,894.67	75,983.76	46,591.07				0/1
Shipping & Ports									
511	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67 298.17	373.22	336.25	04/2009 11/2009	02/2011	15(R3)	0/0
512	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK, Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
513	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP., Kerala	12/2010	241.50	241.50	157.81	09/2011	09/2011	0(O)	0/0
514	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00 165.00	165.00	125.00	12/2005 01/2008	10/2011	45(R3)	0/0
515	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	359.44	358.79	04/2011 06/2011	11/2011	5(R3)	0/0
516	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP., Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
517	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP., Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	884.48	03/2012	03/2012	0(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
518	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
519	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
520	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 05/2012	05/2012	0(R3)	0/0
521	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	652.40	12/2010 -	09/2012	21(O)	0/0
522	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	284.43	09/2012 -	09/2012	0(O)	0/0
523	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
524	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	106.93	12/2012 -	12/2012	0(O)	0/0
525	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
526	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O)	0/0
527	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
528	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0
529	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	12/2013	0(O)	0/0
530	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O)	0/0
531	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
532	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
533	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
534	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.85	10/2008 -	-	-	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		17,822.23	18,838.27	4,749.63				0/0
	<u>Telecommunications</u>								
535	Implementation of FTTH, the state of the art access, upon eq - [N26000072]BSNL, Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
536	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94	373.94	211.35	12/2008	02/2011	26(O)	0/0
537	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL, Orissa	11/2007	277.34	377.54	308.13	03/2009	02/2011	23(O)	0/0
538	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL, Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
539	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
540	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00	229.41	66.20	02/2007	08/2011	54(O)	0/0
541	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
542	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL, Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
543	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL, Multi State	11/2003	250.00	425.51	161.31	12/2005	12/2011	72(O)	0/0
544	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL, Uttaranchal	01/2009	149.15	158.72	76.55	06/2009	12/2011	30(O)	0/0
545	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81	336.81	155.71	01/2009	12/2011	35(O)	0/0
546	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL, Bihar	10/2007	366.00	366.00	227.39	10/2008	12/2011	38(O)	0/0
547	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL, Gujarat	08/2008	868.00	868.00	362.62	08/2009	12/2011	28(O)	0/0
548	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL, Madhya pradesh	11/2009	916.70	930.60	757.02	11/2010	12/2011	13(O)	0/0
549	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL, Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	12/2011	23(O)	0/0
550	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL, Kerala	01/2009	848.70	848.70	712.86	01/2010	12/2011	23(O)	0/0

Sector Wise Details

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
551	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	21.80	10/2010 03/2012	07/2012	4(R3)	0/0
552	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
553	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL, Maharashtra	09/2008	1,799.94 -	1,799.94	308.43	09/2009 -	-	-	0/0
554	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
555	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL, Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
556	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL, Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	-	-	0/0
	Total		11,794.14 -	12,010.64	4,178.00				0/0
Urban Development									
557	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24(O)	6/6
558	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	2,494.00	-	09/2014 -	09/2014	0(O)	0/0
559	DELHI MRTS PHASE-III - [N28000056]DMRC, Delhi	09/2011	35,242.00 -	35,242.00	72.66	03/2016 -	03/2016	0(O)	0/0
560	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
	Total		44,245.18 -	49,518.08	2,340.23				6/6
Water Resources									
561	PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			716,175.48	836,734.26	350,107.85				764/2182

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

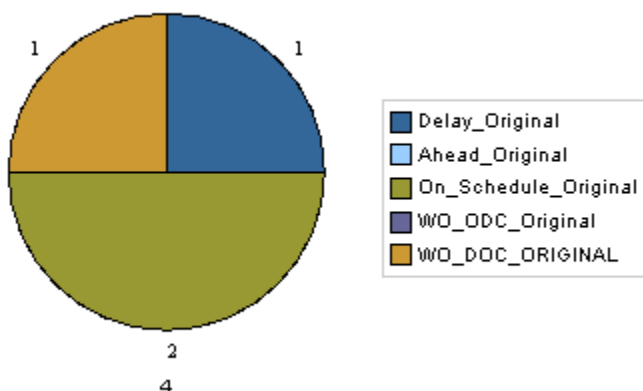

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till December, 2011 is Rs. 2340.23 crore, which is 4.7% of the revised cost of the projects.

Figures are in Rs. Crore

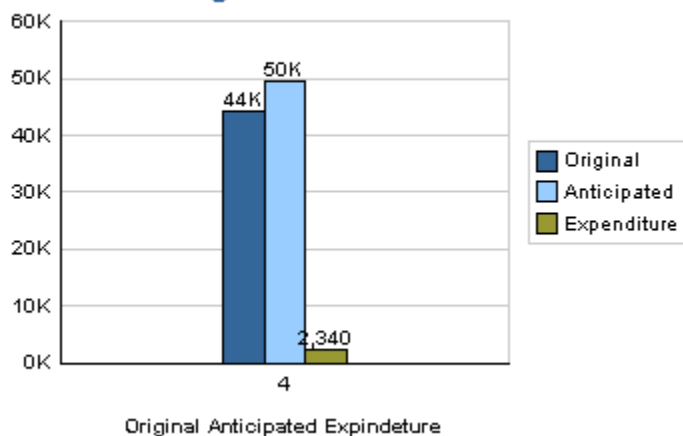

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects 22

Number of Projects Delayed 9

Number of Projects Without Date Of Commissioning 13

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 22 projects, 9 projects are delayed .13 projects do not have fixed dates of commissioning.

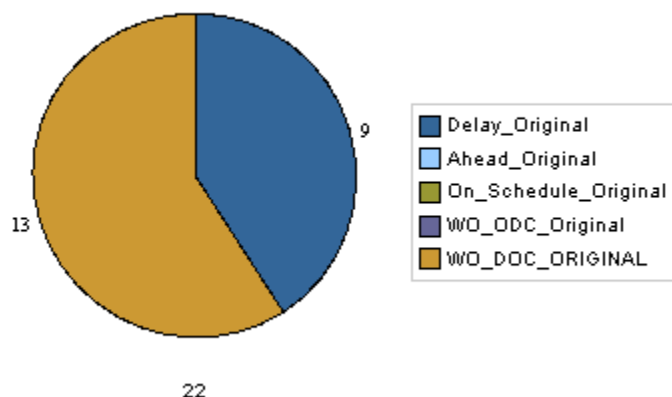

III. Investment Scenario

The Total Original cost of implementation of 22 projects when sanctioned, was of the order of Rs. 11794.14 crore but this was subsequently revised to Rs. 12010.64 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till December, 2011 is Rs. 4178 crore, which is 34.8% of the revised cost of the projects.

Figures are in Rs. Crore

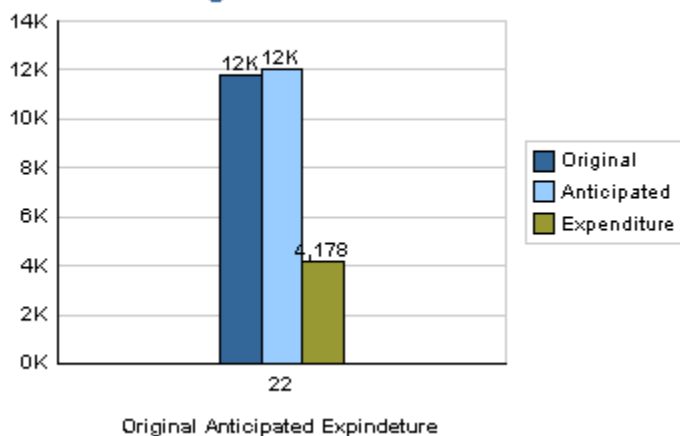

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	24
Number of Projects On Schedule	6
Number of Projects Delayed	9

Number of Projects Without Date Of Commissioning	9
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 24 projects, 6 projects are on schedule and 9 projects are delayed .9 projects do not have fixed dates of commissioning.

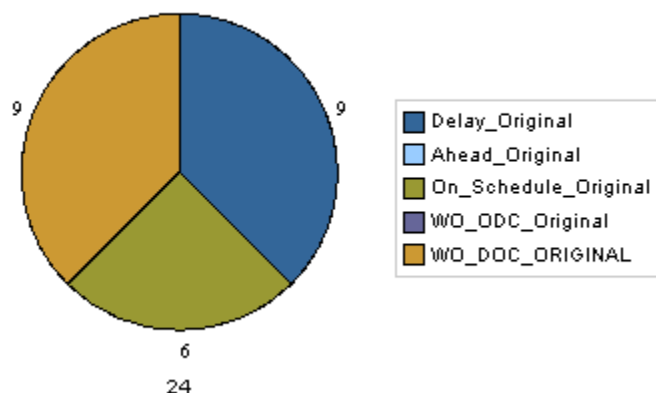

III. Investment Scenario

The Total Original cost of implementation of 24 projects when sanctioned, was of the order of Rs. 17822.23 crore but this was subsequently revised to Rs. 18838.27 crore implying a cost overrun of 5.7%. The expenditure incurred on these projects till December, 2011 is Rs. 4749.63 crore, which is 25.2% of the revised cost of the projects.

Figures are in Rs. Crore

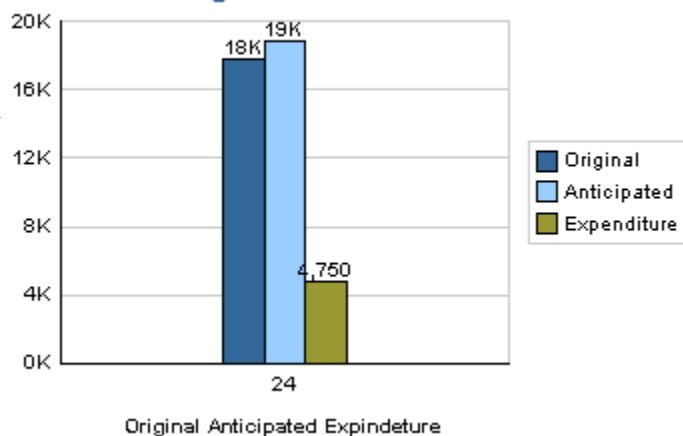

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	131
Number of Projects On Schedule	45
Number of Projects Delayed	83

Number of Projects Without Original Date of Commissioning	3
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 131 projects, 45 projects are on schedule and 83 projects are delayed .3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

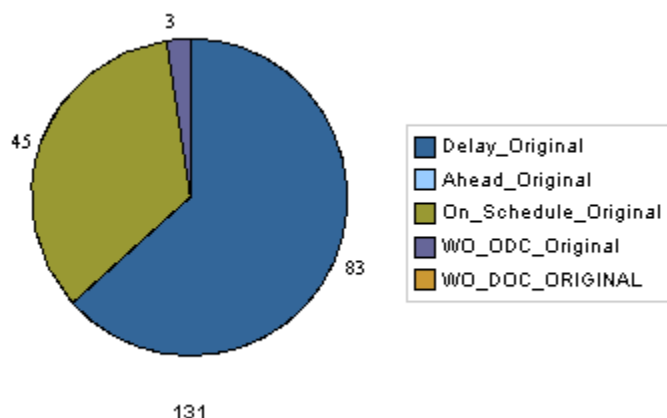

III. Investment Scenario

The Total Original cost of implementation of 131 projects when sanctioned, was of the order of Rs. 73894.67 crore but this was subsequently revised to Rs. 75983.76 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till December, 2011 is Rs. 46591.07 crore, which is 61.3% of the revised cost of the projects.

Figures are in Rs. Crore

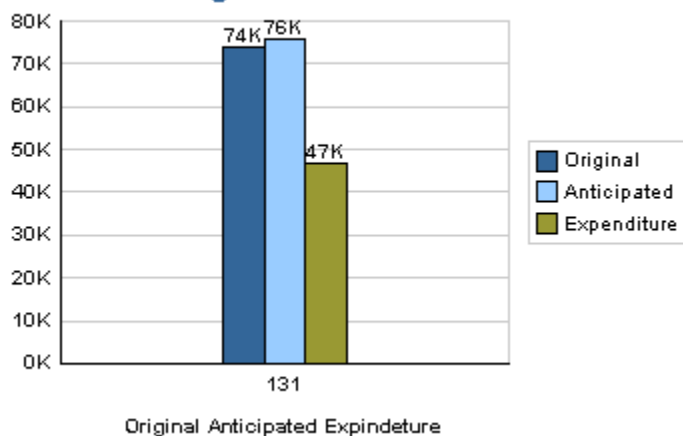

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	132
Number of Projects On Schedule	18
Number of Projects Delayed	28
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	31
Number of Projects Without Date Of Commissioning	53

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 132 projects, 2 projects are ahead of schedule, 18 projects are on schedule and 28 projects are delayed. 53 projects do not have fixed dates of commissioning. 31 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

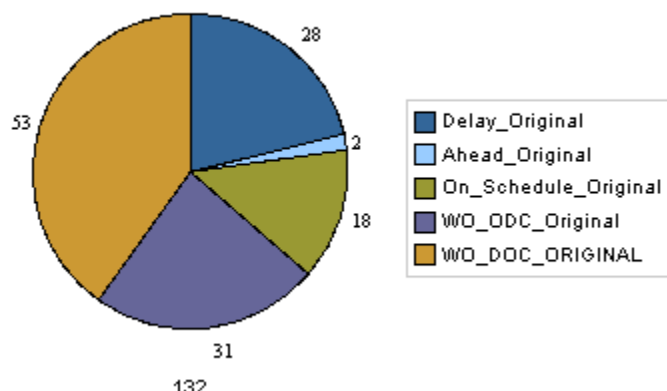

III. Investment Scenario

The Total Original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 65054.74 crore but this was subsequently revised to Rs. 134133.5 crore implying a cost overrun of 106.2%. The expenditure incurred on these projects till December, 2011 is Rs. 56395.52 crore, which is 42% of the revised cost of the projects.

Figures are in Rs. Crore

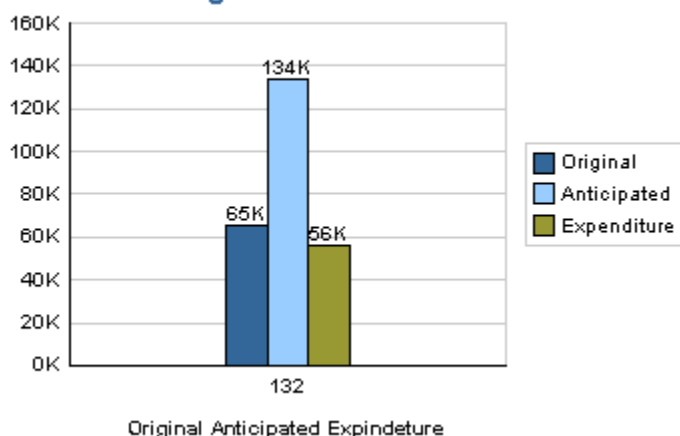

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	94
Number of Projects On Schedule	43
Number of Projects Delayed	47
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 94 projects, 2 projects are ahead of schedule, 43 projects are on schedule and 47 projects are delayed .2 projects do not have fixed dates of commissioning.

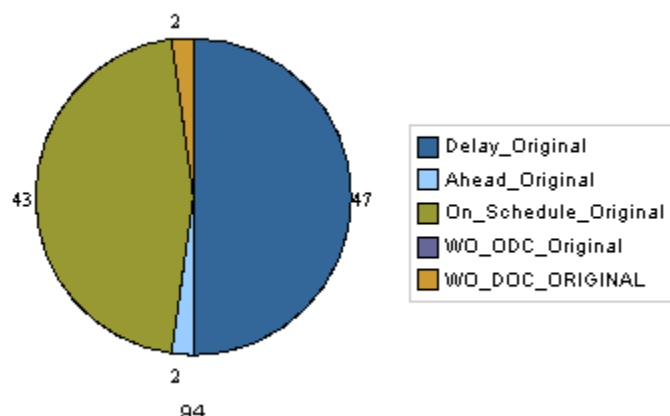

III. Investment Scenario

The Total Original cost of implementation of 94 projects when sanctioned, was of the order of Rs. 195705.41 crore but this was subsequently revised to Rs. 211046.35 crore implying a cost overrun of 7.8%. The expenditure incurred on these projects till December, 2011 is Rs. 96642.67 crore, which is 45.8% of the revised cost of the projects.

Figures are in Rs. Crore

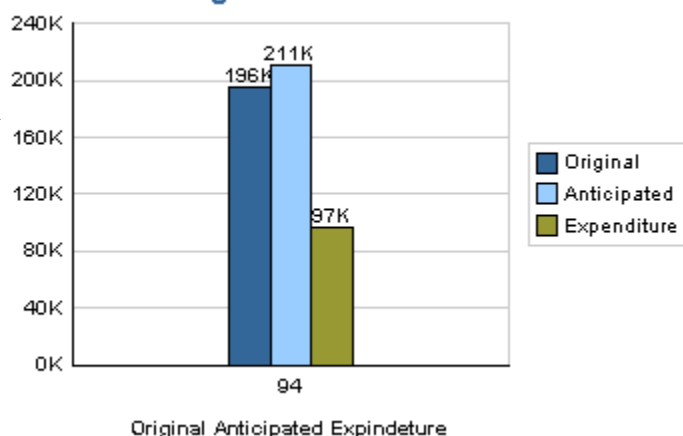

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	69
Number of Projects On Schedule	25
Number of Projects Delayed	33
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	4
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 69 projects, 2 projects are ahead of schedule, 25 projects are on schedule and 33 projects are delayed. 5 projects do not have fixed dates of commissioning. 4 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

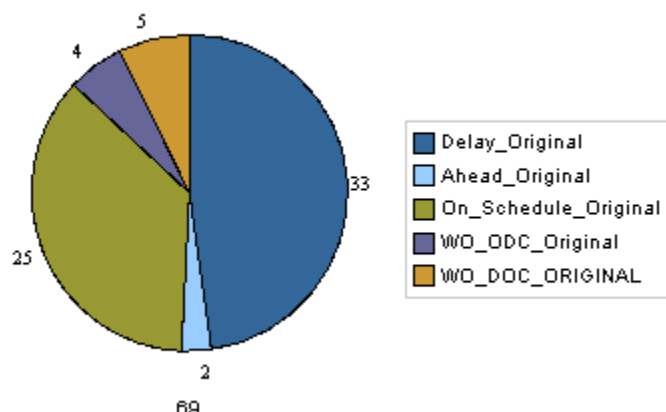

III. Investment Scenario

The Total Original cost of implementation of 69 projects when sanctioned, was of the order of Rs. 149804.77 crore but this was subsequently revised to Rs. 158021.15 crore implying a cost overrun of 5.5%. The expenditure incurred on these projects till December, 2011 is Rs. 61434.94 crore, which is 38.9% of the revised cost of the projects.

Figures are in Rs. Crore

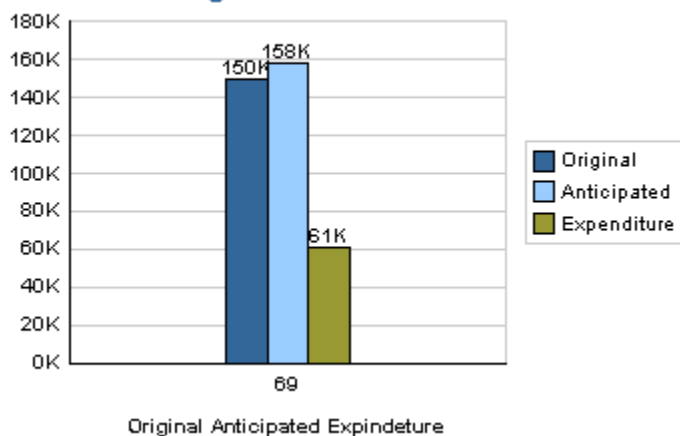

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	16
Number of Projects On Schedule	5
Number of Projects Delayed	5

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 5 projects are on schedule and 5 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

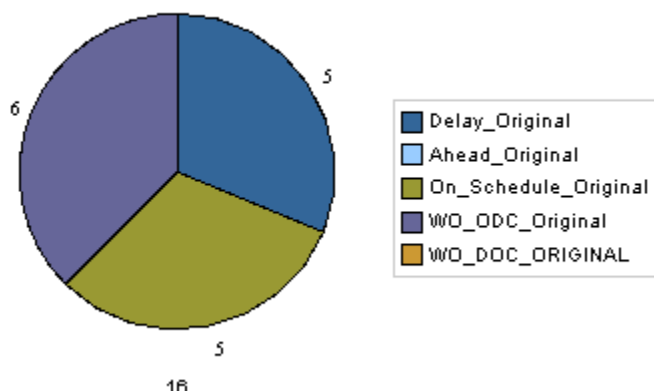

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 65244.82 crore but this was subsequently revised to Rs. 71412.36 crore implying a cost overrun of 9.5%. The expenditure incurred on these projects till December, 2011 is Rs. 35762.03 crore, which is 50.1% of the revised cost of the projects.

Figures are in Rs. Crore

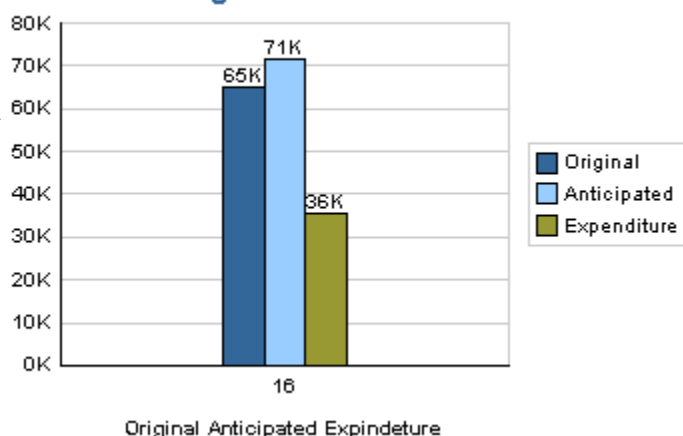

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Original Date of Commissioning	1
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

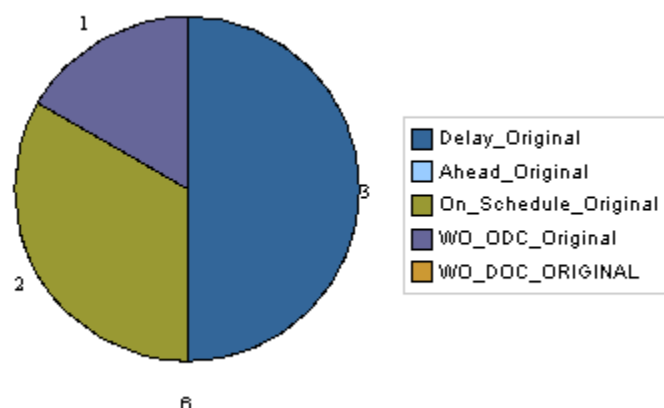

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till December, 2011 is Rs. 1426.18 crore, which is 26.8% of the revised cost of the projects.

Figures are in Rs. Crore

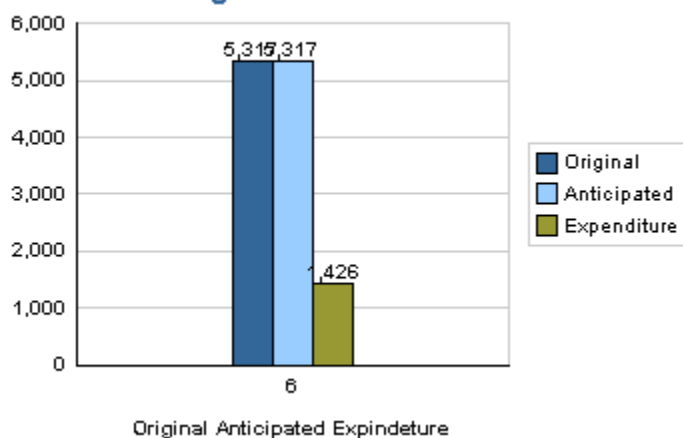

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	22
Number of Projects Delayed	17

Number of Projects Without Original Date of Commissioning	12
---	----

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 22 projects are on schedule and 17 projects are delayed .12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

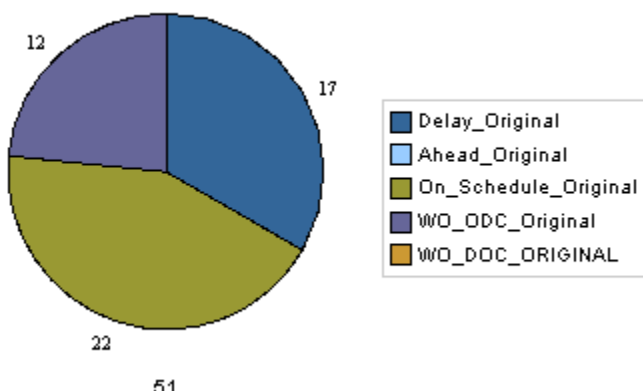

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 34718.73 crore but this was subsequently revised to Rs. 38348.38 crore implying a cost overrun of 10.5%. The expenditure incurred on these projects till December, 2011 is Rs. 12436 crore, which is 32.4% of the revised cost of the projects.

Figures are in Rs. Crore

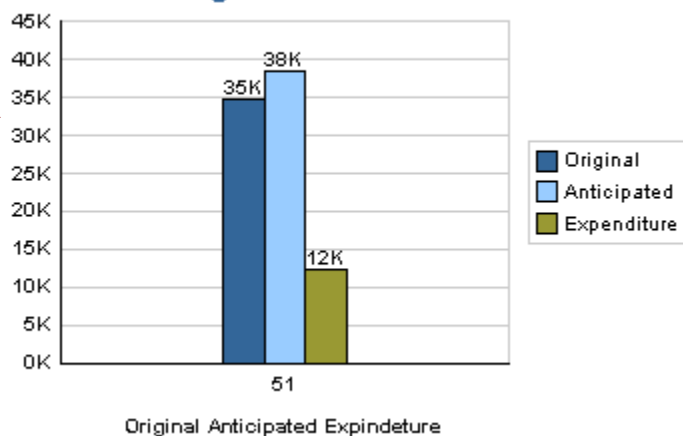

Sector wise current status of projects on theFlash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 4 projects are delayed .

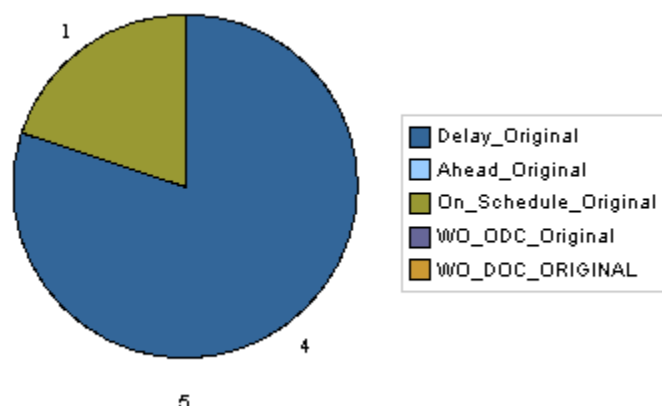

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till December, 2011 is Rs. 3805.13 crore, which is 67.8% of the revised cost of the projects.

Figures are in Rs. Crore

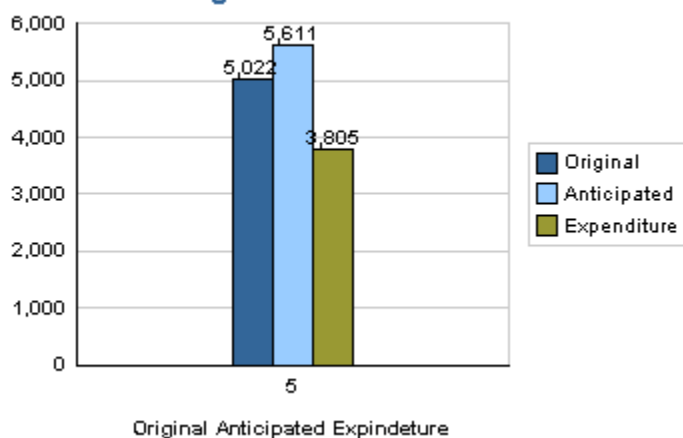

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	5
Number of Projects Delayed	2
Number of Projects Without Original Date of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed .3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

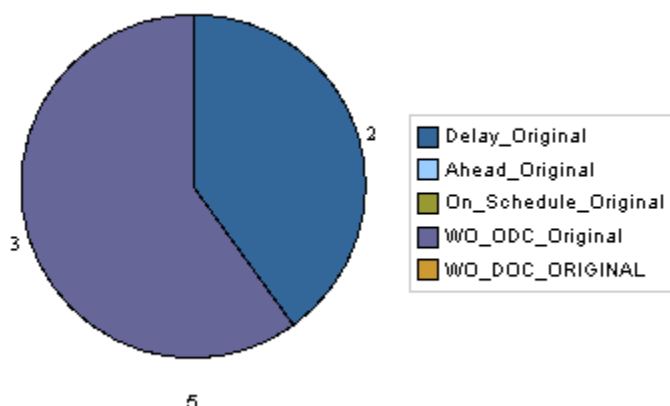

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 46386.29 crore implying a cost overrun of 11.6%. The expenditure incurred on these projects till December, 2011 is Rs. 20673.61 crore, which is 44.6% of the revised cost of the projects.

Figures are in Rs. Crore

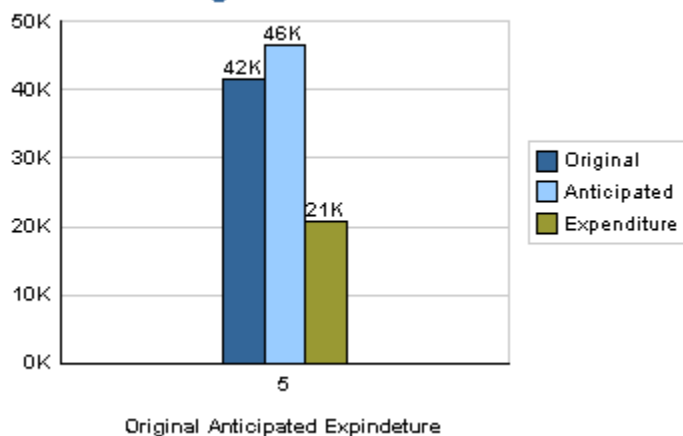

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	33	32855.21	39238.54	22706.11
2	Arunachal Pr.	4	9512.22	13992.18	7469.45
3	Assam	37	23895.78	35572.29	19742.14
4	Bihar	28	28362.95	33110.20	21445.92
5	Chhatisgarh	24	54493.92	57725.27	23484.04
6	Delhi	3	37985.00	37965.41	138.86
7	Goa	1	335.61	335.61	57.03
8	Gujarat	27	32264.42	32871.57	6012.65
9	Haryana	10	5795.35	7512.27	5107.15
10	Himachal Pr.	6	14761.20	17455.42	12729.27
11	J and K	10	14019.35	33604.41	11810.09
12	Jharkhandd	22	14396.48	15999.88	6586.23
13	Karnataka	25	30657.64	39102.46	16768.78
14	Kerala	8	6934.87	7623.92	2363.34
15	Madhya pradesh	24	17335.55	17581.76	7127.49
16	Maharashtra	51	70165.50	83689.80	39525.06
17	Manipur	1	727.56	3056.85	554.31
18	Mizoram	2	988.06	3307.12	297.21
19	Multi State	97	125418.36	130674.34	44469.70
20	Nagaland	1	850.00	850.00	8.44
21	Orissa	27	42805.18	46076.37	16442.51
22	Punjab	7	4613.20	5599.16	3014.40
23	Rajasthan	15	25357.18	26106.33	8448.91
24	Sikkim	2	1648.94	3690.03	219.17
25	Tamil Nadu	35	52418.20	60937.00	35108.56
26	Tripura	3	1522.39	2053.23	489.11
27	Uttar Pradesh	27	18443.94	22048.24	9955.67
28	Uttaranchal	6	10025.65	11948.21	4820.30
29	West Bengal	25	37585.77	47006.39	23205.95
TOTAL		561	716175.48	836734.26	350107.85

LIST OF PROJECTS IN WHICH EXPENDITURE MORE THAN COST

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	14212.00
2	BARSINGSAR TPS (2 125MW) (NLC)	Coal	NLC	1114.18	1626.09	1697.55
3	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	HPCL	613.54	0.00	671.52
4	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1418.05
5	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.01	0.00	702.55
6	CHAMERA,STAGE-III (NHPC)	Power	NHPC	1405.63	0.00	1713.78
7	KOTESHWAR HEP(THDC)	Power	THDCL	1301.56	2283.68	2559.40
8	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	PGCIL	297.37	297.91	306.13
9	CHUTAK HYDRO-ELECTRIC PROJECT	Power	NHPC	621.26	0.00	713.40
10	GUNA-ETAWAH(NCR), NL	Railways	NCR	158.77	432.46	558.07
11	CALICUT-MANGALORE (DL) (SR)	Railways	SR	240.00	0.00	596.33
12	KARUR-SALEM(NL),SR	Railways	SR	155.55	229.88	646.16
13	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	ECR	491.19	1099.20	1145.69
14	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	248.44	576.27	817.73
15	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	721.53
16	BILASPUR-URKURA (DL)	Railways	RVNL	151.52	0.00	304.39
17	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	RVNL	136.62	0.00	176.98
18	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	0.00	365.15
19	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	NEFR	733.00	0.00	991.07
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	250.82
21	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	233.00	501.69	577.49
22	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	NEFR	1000.00	1500.00	2279.87
23	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	ER	184.00	254.07	482.31
24	KODERMA GIRIDH (NL), ECR	Railways	ECR	371.36	0.00	381.90
25	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	100.00	142.98	190.08
26	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	114.01	332.92	349.47
27	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	227.48
28	RENIGUNTA-GUNTAKAL(RE)	Railways	RVNL	168.34	0.00	313.40
29	RAJATGARH-BARANG(LD),ECOR	Railways	RVNL	166.16	0.00	236.08
30	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	478.76
31	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	(NR)	409.00	625.30	821.93
32	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	460.51
33	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	NER	395.00	1062.36	1206.84
34	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	2885.61

SN	PROJ TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
35	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	219.79
36	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	475.12
37	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	407.78	532.41
38	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	SR	100.00	0.00	486.74
39	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	SWR	295.00	412.91	483.14
40	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	302.23	331.25
41	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	293.16
42	GONDIA-JABALPUR(GC),(SECR)	Railways	SECR	386.30	0.00	570.21
43	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	164.36	516.14
44	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	461.11
45	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	RVNL	240.00	0.00	267.79
46	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	Railways	WR	148.61	227.52	258.80
47	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	NER	381.17	0.00	451.29
48	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	MRTTP	907.69	1032.76	3225.00
49	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	228.09	242.14
50	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	353.59
51	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Road Transport & Highways	NHAI	412.78	0.00	437.40
52	SITAPUR-LUCKNOW	Road Transport & Highways	NHAI	322.00	0.00	553.70
53	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	594.20
54	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	NHAI	280.00	0.00	581.50
55	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
56	TRICHY - DINDIGUAL NH-45	Road Transport & Highways	NHAI	576.00	0.00	661.40
57	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	846.50

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
58	Pune-sholapur,pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1802.00
59	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	NHAI	441.00	0.00	946.63
60	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	666.00
61	Bijapur-Hungund Section	Road Transport & Highways	NHAI	748.00	0.00	1214.00
62	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.90
63	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	NHAI	572.30	0.00	576.90
64	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2607.00
65	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	NHAI	295.00	0.00	660.00
66	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	227.00
67	Armur to kadloor yellareddy	Road Transport & Highways	NHAI	390.56	0.00	549.70
68	RAJMARG CHORAHHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	NHAI	229.91	0.00	231.30
69	SAGAR - RAJMARG CHORAHHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	214.50
70	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	174.00

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
71	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	2736.00
72	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	863.70
73	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	388.00	0.00	408.50
74	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	NHAI	168.00	0.00	454.00
75	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	NHAI	600.24	0.00	738.20
76	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	284.30
77	KASIA TO GORAKHPUR (NH-28)(NHAI)	Road Transport & Highways	NHAI	242.00	0.00	434.10
78	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	NHAI	227.00	0.00	375.50
79	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	262.60
80	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	558.60
81	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	NHAI	225.00	0.00	257.50
82	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	277.50
83	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	360.90

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
84	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	464.70
85	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	252.70
86	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	264.40
87	NALBARI T BIJNI (AS-7)	Road Transport & Highways	NHAI	208.00	0.00	229.80
88	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	489.20
89	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	257.30
90	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	185.00
91	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
92	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	NHAI	229.00	0.00	346.80
93	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	298.70
94	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	NHAI	273.00	0.00	475.60
95	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	285.60
96	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	RVNL	245.67	298.17	336.25
97	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	RINL	230.00	0.00	236.27

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMUL ATIVE EXPENDIT URE
98	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	Telecomm unications	BSNL	277.34	0.00	308.13

List of project Without Original Date of Commissioning

(Dec,2011)

			Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
<u>Atomic Energy</u>					
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	- 04/2011	04/2012
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	- 05/2016	11/2016
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,	10/2009	12,320.00 -	- -	12/2016
	Total		24,885.29 -		
<u>Coal</u>					
4	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	- -	03/2012
5	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	- -	03/2012
6	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	- -	02/2013
7	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	- -	03/2013
8	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	- -	03/2013
9	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	- -	03/2013
10	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	- -	03/2014
11	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	- -	03/2014
12	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77 -	- -	10/2014
13	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	- -	03/2015
14	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72 -	- -	03/2016
15	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	- -	03/2017
	Total		9,412.38 -		
<u>Fertilisers</u>					
16	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	- 04/2012	04/2012
	Total		488.75 -		
<u>Steel</u>					
17	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90 -	- -	01/2012

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
18	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	- 12/2011	03/2012
19	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	- 08/2010	03/2012
20	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	- 02/2011	04/2012
21	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	- 10/2012	10/2012
22	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	- 05/2012	12/2012
	Total		1,874.79 -		
Petrochemicals					
23	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	- 12/2013	12/2013
	Total		5,460.61 -		
Petroleum					
24	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	- -	12/2011
25	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	- 12/2008	03/2012
26	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	- -	05/2012
27	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	- 04/2013	04/2013
	Total		6,969.84 -		
Railways					
28	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	12/2011
29	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
30	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012
31	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	- 12/2009	02/2012
32	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	- -	03/2012
33	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	- 12/2011	03/2012
34	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	- 03/2012	03/2012
35	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	- 03/2012	03/2012

		Date of		Date of	
		Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
36	MUNEERABAD- MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
37	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	- 03/2012	03/2012
38	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	- 02/2011	03/2012
39	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012
40	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	- 03/2012	03/2012
41	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
42	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
43	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012
44	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	- 07/2012	07/2012
45	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	- 03/2012	12/2012
46	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	- 03/2012	12/2012
47	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013
48	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
49	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2013
50	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013
51	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	- 02/2009	04/2013
52	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	- 03/2009	04/2013
53	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	- 06/2013	06/2013
54	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013
55	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	- 12/2010	03/2015
56	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015
57	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	- 12/2012	-
58	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,302.12	- 06/2012	12/2012

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning	
				Original / Revised	Anticipated
1	2	3	4	7	8
Total			8,039.95	-	
<u>Road Transport & Highways</u>					
59	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,	04/2000	196.50	-	03/2012
			363.00	06/2011	
60	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	-	03/2013
			-	-	
61	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,	03/2011	839.00	-	08/2013
			-	-	
Total			1,783.50	-	
Grand Total			58,915.11		

List of project Without Date of Commissioning

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning	
				Original / Revised	Anticipated
1	2	3	4	5	6
<u>Petroleum</u>					
1	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	09/2010 -	09/2010
2	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	12/2010 -	06/2011
3	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	09/2009 -	08/2011
4	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	02/2011 08/2011	08/2011
5	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00 -	- -	-
	Total		4,157.85 -		
<u>Power</u>					
6	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		596.45 -		
<u>Railways</u>					
7	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	12/2010
8	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
9	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 227.52	03/2008 03/2009	10/2010
10	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
11	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010
12	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
13	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011
14	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	- 03/2011	03/2011
15	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
16	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
17	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	- 03/2011	03/2011
18	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	- 06/2011	06/2011
19	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-

List of project Without Date of Commissioning

(Dec,2011)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Antici- pated
1	2	3	4	5	6
20	New BG line Rly line from Eklakhi-Balughat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	-
21	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	- -	-
22	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	-
23	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	03/1998 -	-
24	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-
25	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
26	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	-
27	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	07/2005 -	-
28	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
29	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	-
30	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
31	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	-
32	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
33	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-
34	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	- -	-
35	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-
36	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
37	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
38	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
39	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
40	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-
41	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-
42	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-
43	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
44	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-
45	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	-

List of project Without Date of Commissioning

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning	
				Original / Revised	Anticipated
1	2	3	4	5	6
46	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
47	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	-
48	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
49	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	-
50	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-
51	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	- -	-
52	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	12/2006 08/2010	-
53	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	-
54	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	- -	-
55	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-
56	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-
57	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	-
58	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	12/2010 03/2011	-
59	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	- 12/2010	-
Total			18,057.85 -		
Shipping & Ports					
60	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
61	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	06/2006 09/2011	09/2011
62	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	09/2011 -	09/2011
63	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	12/2005 01/2008	10/2011
64	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 06/2011	11/2011
65	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	-
66	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	12/2007 01/2009	-
67	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-
68	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-
Total			4,960.10 -		

List of project Without Date of Commissioning

(Dec,2011)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Telecommunications</u>					
69	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010
70	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	02/2011
71	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	03/2009 -	02/2011
72	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	03/2009 -	03/2011
73	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
74	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 -	08/2011
75	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 -	08/2011
76	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	09/2011 -	09/2011
77	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
78	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	09/2009 -	-
79	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
80	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
81	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	-
	Total		6,751.87 -		
<u>Urban Development</u>					
82	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Grand Total			34,638.30		

List of Delay Project w.r.to Original

Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
<u>Atomic Energy</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,376.91	09/2010 -	01/2012	16
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	14,212.00	12/2008 -	03/2013	51
Total			16,663.00 -	21,501.00	17,588.91			
<u>Civil Aviation</u>								
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,574.69	01/2011 -	02/2012	13
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,679.95	05/2011 -	03/2012	10
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	57.03	05/2012 -	08/2012	3
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	166.54	01/2011 -	12/2012	23
Total			4,395.58 -	4,985.07	3,478.21			
<u>Coal</u>								
7	BARSINGSAR TPS (2 125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,868.71	1,697.55	06/2009 -	01/2012	31
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	87.57	03/2010 -	03/2012	24
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,316.04	06/2009 -	07/2012	37
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	105.51	03/2011 03/2012	03/2013	24
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 -	741.62	289.22	03/2010 -	03/2013	36
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	219.22	03/2013 09/2012	12/2013	9
13	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,281.50	03/2010 -	03/2014	48
14	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,136.49	03/2010 -	03/2014	48
15	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.96	03/2011 -	03/2014	36
16	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.66	03/2011 03/2012	03/2014	36
17	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	61.08	03/2012 03/2012	03/2014	24
18	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	89.01	03/2012 03/2013	03/2014	24

List of Delay Project w.r.to Original

Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
19	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	140.46	03/2012	03/2015	36
20	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48
21	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	71.02	12/2012	03/2015	27
22	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	236.02	03/2014	03/2016	24
23	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	18.16	07/2012	03/2016	44
	Total		11,824.69	14,994.80	7,802.47			
	Fertilisers							
24	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	150.34	07/2011	03/2012	8
25	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	150.34	07/2011	04/2012	9
26	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	375.78	12/2012	01/2013	1
	Total		2,241.63	2,241.63	676.46			
	Steel							
27	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93	232.93	178.90	05/2011	02/2012	9
28	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	12,417.12	12/2011	03/2012	3
29	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	6,325.00	6,325.00	2,305.64	12/2011	03/2012	3
30	EXPANSION OF RINL/VSP FROM 3 MTPY- 6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	9,050.03	10/2009	10/2012	36
31	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	4,139.18	03/2013	06/2013	3
	Total		46,957.93	52,521.93	28,090.87			
	Petroleum							
32	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	124.45	03/2009	01/2012	34
33	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	2,920.82	1,173.84	09/2010	03/2012	18
34	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07	1,385.00	1,035.30	10/2010	03/2012	17
35	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	798.00	674.74	04/2011	03/2012	11

List of Delay Project w.r.to Original

Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
36	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	779.06	09/2011 03/2012	03/2012	6
37	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	668.00	04/2010 -	03/2012	23
38	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	279.30	04/2011 -	03/2012	11
39	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	934.05	09/2011 03/2012	03/2012	6
40	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	177.19	06/2011 03/2012	03/2012	9
41	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	530.44	03/2011 05/2011	03/2012	12
42	KARANPUR MORADABAD-KASHIPUR- RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 252.37	204.00	153.70	01/2012 -	04/2012	3
43	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	73
44	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,185.96	05/2010 05/2012	05/2012	24
45	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	113.49	05/2010 04/2012	05/2012	24
46	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	353.92	07/2010 05/2012	05/2012	22
47	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	715.36	09/2011 05/2012	05/2012	8
48	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	2,050.63	08/2010 03/2012	06/2012	22
49	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	120.24	04/2011 -	07/2012	15
50	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	170.50	06/2011 07/2012	07/2012	13
51	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,480.98	03/2012 08/2012	08/2012	5
52	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.71	09/2011 -	12/2012	15
53	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	400.34	10/2012 12/2012	12/2012	2
54	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	98.77	12/2011 -	01/2013	13
55	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2
56	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	258.24	03/2006 03/2013	03/2013	84

List of Delay Project w.r.to Original

Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
57	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2013	36
58	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,788.99	05/2010 03/2013	03/2013	34
59	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	04/2013	10
60	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	12,266.00	11/2012 11/2012	06/2013	7
61	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	595.83	03/2007 03/2014	03/2014	84
62	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.30	10/2010 -	12/2014	50
63	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	1.63	01/2013 -	07/2015	30
64	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,413.90	03/2007 03/2017	03/2017	120
	Total		81,099.95 -	89,549.75	39,409.25			
Power								
65	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	137.90	06/2010 06/2010	01/2012	19
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	166.00	08/2011 -	02/2012	6
67	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	215.80	07/2010 02/2012	02/2012	19
68	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	104.70	07/2011 -	02/2012	7
69	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 2,283.68	2,283.69	2,559.40	04/2005 -	03/2012	83
70	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	7,532.00	12/2009 -	03/2012	27
71	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	2,084.00	1,713.78	08/2010 08/2011	03/2012	19
72	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.66	712.30	10/2009 -	03/2012	29
73	SIMHADRI STPP STAGE - II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,262.00	05/2011 05/2011	03/2012	10
74	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	306.13	07/2011 -	03/2012	8
75	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.25	713.40	02/2011 08/2011	05/2012	15
76	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	1,794.00	1,630.92	11/2009 11/2011	06/2012	31
77	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,779.29	1,758.98	09/2008 -	06/2012	45

List of Delay Project w.r.to Original

Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
78	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,779.46	3,514.40	09/2009 -	06/2012	33
79	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	512.20	01/2010 01/2010	06/2012	29
80	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,010.70	07/2010 -	06/2012	23
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	119.30	11/2011 11/2011	06/2012	7
82	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	942.30	02/2012 -	06/2012	4
83	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.39	1,418.05	03/2007 -	09/2012	66
84	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	685.00	11/2011 -	12/2012	13
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	251.30	11/2011 -	12/2012	13
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	304.20	11/2011 -	12/2012	13
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	149.50	02/2012 -	12/2012	10
88	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,639.06	10/2010 12/2011	01/2013	27
89	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	702.55	08/2010 09/2011	01/2013	29
90	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	3,967.00	04/2009 -	03/2013	47
91	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	382.80	09/2010 -	03/2013	30
92	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	3,215.00	08/2012 -	03/2013	7
93	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	2,531.00	10/2012 -	03/2013	5
94	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,364.00	10/2012 -	03/2013	5
95	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,059.04	09/2009 -	06/2013	45
96	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	89.84	01/2012 07/2013	07/2013	18
97	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	262.14	08/2012 08/2013	08/2013	12
98	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,462.50	01/2012 -	09/2013	20

List of Delay Project w.r.to Original

Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
99	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19 -	184.19	137.00	11/2011 -	09/2013	22
100	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, Assam	01/2008	4,375.35 -	4,375.35	2,598.00	06/2011 -	10/2013	28
101	BARH STPP STAGE -II - [N18000047]NTPC, Bihar	02/2008	7,341.04 -	7,341.04	3,211.00	08/2013 08/2013	10/2013	2
102	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72 913.63	913.63	293.42	07/2006 01/2014	01/2014	90
103	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttaranchal	11/2006	2,978.48 -	2,978.48	1,246.00	03/2013 -	06/2014	15
104	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19 -	11,130.19	3,239.10	08/2013 -	09/2014	13
105	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97 8,693.00	8,692.97	6,324.00	12/2009 11/2010	10/2014	58
106	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,434.73	09/2009 07/2014	12/2014	63
107	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,290.06	09/2010 08/2014	12/2015	63
108	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	278.27	07/2010 02/2016	02/2016	67
109	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,697.46	05/2013 06/2016	06/2016	37
110	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttaranchal	08/2008	2,491.58 3,422.44	3,422.44	233.48	07/2014 -	09/2016	26
111	KISHANGANGA HEP - [N18000031]NHPC, J and K	07/2007	2,238.67 3,642.04	3,642.00	1,083.48	01/2016 01/2016	11/2016	10
	Total		122,641.43 -	137,571.66	79,461.19			
<u>Railways</u>								
112	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213
113	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER, West Bengal	04/2009	259.51 -	259.51	71.20	12/2011 02/2012	02/2012	2
114	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 634.13	634.13	544.82	03/1995 -	03/2012	204
115	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, Orissa	04/1993	100.00 142.98	227.94	190.08	03/2002 -	03/2012	120
116	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 164.36	840.32	516.14	02/2009 -	03/2012	37
117	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	324.90	194.01	03/2010 -	03/2012	24
118	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE, Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12
119	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat	04/2006	196.97 -	196.97	183.88	03/2011 -	03/2012	12

List of Delay Project w.r.to Original

Dec,2011)

						Date of Commissioning		Delay w.r.t. Original (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
120	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	293.16	06/2004 -	12/2012	102
121	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	592.94	03/2009 12/2012	12/2012	45
122	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,101.12	10/2007 12/2012	12/2012	62
123	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	452.38	03/2010 -	12/2012	33
124	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	75.30	12/2011 11/2013	11/2013	23
125	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	283.10	36.90	02/2006 -	12/2013	94
126	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,885.61	03/2009 -	12/2013	57
127	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	151.23	03/2007 03/2007	03/2014	84
128	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	991.07	12/2008 -	03/2014	63
129	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	84.11	12/2012 -	03/2014	15
130	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	112.33	03/2010 06/2014	06/2014	51
131	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,279.87	04/2008 03/2014	12/2014	80
132	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	12
133	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	723.27	387.27	06/2005 07/2011	06/2015	120
134	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	208.25	02/2010 -	12/2015	70
135	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	1,211.22	411.62	03/2005 12/2008	03/2016	132
136	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	554.31	03/2011 03/2014	03/2016	60
137	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	4.01	03/2014 03/2016	03/2016	24
138	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	8.17	03/2016 -	06/2016	3
139	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	7,340.14	03/2001 -	12/2017	201
Total			22,295.57 -	52,619.53	20,853.00			
Road Transport & Highways								
140	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	212.54	06/2005 -	12/2011	78

List of Delay Project w.r.to Original

Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
141	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	475.60	03/2005	01/2012	82
142	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00	242.00	434.10	12/2008	01/2012	37
143	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	01/2012	31
144	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	343.30	03/2010	01/2012	22
145	TRICHY - DINDIGUL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	661.40	07/2010	01/2012	18
146	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	173.32	08/2004	02/2012	90
147	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78	479.54	437.40	11/2007	02/2012	51
148	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	315.90	09/2009	02/2012	29
149	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	946.63	07/2010	02/2012	19
150	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	166.36	08/2004 07/2010	03/2012	91
151	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09	166.30	184.50	03/2008	03/2012	48
152	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27	193.10	155.10	03/2008	03/2012	48
153	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	285.60	10/2008	03/2012	41
154	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	360.90	03/2008	03/2012	48
155	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	03/2012	38
156	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	262.60	06/2008	03/2012	45
157	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	375.50	12/2008	03/2012	39
158	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	332.94	318.40	09/2008	03/2012	42
159	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	464.70	09/2008	03/2012	42
160	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	252.70	11/2008	03/2012	40
161	SALEM - U / UNDRUPET(BOT -1/TN-06) NH - 68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	03/2012	14
162	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	660.00	08/2010	03/2012	19

List of Delay Project w.r.to Original

Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
163	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	420.00	01/2011 -	03/2012	14
164	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,607.00	08/2011 -	03/2012	7
165	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00 -	225.00	257.50	10/2008 -	04/2012	42
166	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	549.70	02/2012 -	04/2012	2
167	SAGAR BY PASS, KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30	174.00	10/2008 -	05/2012	43
168	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	489.20	03/2008 -	05/2012	50
169	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	263.27	258.92	02/2004 -	05/2012	99
170	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.90	02/2010 -	05/2012	27
171	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00 -	284.00	346.80	05/2010 -	05/2012	24
172	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	185.00	09/2007 -	06/2012	57
173	AGRA-SHIKOHABAD (GQ) KM.199.66- KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	06/2012	87
174	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	275.00	298.70	09/2007 -	06/2012	57
175	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	257.30	09/2007 -	06/2012	57
176	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	94.14	09/2008 -	06/2012	45
177	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	170.20	10/2008 -	06/2012	44
178	BIJNI TO ASSAM WB BORDER (NH- 31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	178.50	06/2008 -	06/2012	48
179	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	264.40	06/2008 -	06/2012	48
180	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	261.29	06/2008 -	06/2012	48
181	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	184.20	06/2008 -	06/2012	48
182	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	130.40	05/2008 -	06/2012	49
183	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	199.40	06/2008 -	06/2012	48
184	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	454.00	12/2008 -	06/2012	42

List of Delay Project w.r.to Original

Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
185	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	738.20	10/2009 -	06/2012	32
186	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	294.60	10/2009 -	06/2012	32
187	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	412.90	12/2009 -	06/2012	30
188	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	1,538.00	10/2011 -	06/2012	8
189	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	2,736.00	11/2011 -	06/2012	7
190	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	86.89	04/2004 -	07/2012	99
191	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	173.06	02/2004 -	07/2012	101
192	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	150.70	05/2008 -	08/2012	51
193	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	277.50	10/2008 -	09/2012	47
194	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	231.30	10/2008 -	09/2012	47
195	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	184.60	06/2010 -	10/2012	28
196	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.40	09/2009 -	10/2012	37
197	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16
198	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	576.90	10/2011 -	10/2012	12
199	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	11/2012	41
200	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	212.50	06/2008 -	12/2012	54
201	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	214.50	10/2008 -	12/2012	50
202	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	284.30	10/2008 -	12/2012	50
203	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	177.40	07/2008 -	12/2012	53
204	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	126.90	04/2008 -	12/2012	56
205	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	189.20	04/2008 -	12/2012	56
206	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	229.80	04/2008 -	12/2012	56
207	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	161.30	04/2010 -	12/2012	32

List of Delay Project w.r.to Original

Dec,2011)

						Date of Commissioning		Delay w.r.t. Original (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
208	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	173.60	09/2010 -	12/2012	27
209	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	558.60	05/2010 -	12/2012	31
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	232.00	02/2009 -	03/2013	49
211	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	86.27	04/2009 -	03/2013	47
212	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	594.20	07/2010 -	03/2013	32
213	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	118.00	09/2007 -	06/2013	69
214	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	846.50	11/2012 -	06/2013	7
215	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	34.80	04/2009 -	07/2013	51
216	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	57.78	11/2008 -	07/2013	56
217	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.20	02/2010 -	07/2013	41
218	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	10/2013	14
219	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	2.12	11/2008 -	01/2014	62
220	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	200.80	10/2011 -	03/2014	29
221	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	1.79	09/2007 -	04/2014	79
222	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	0.36	07/2009 -	04/2014	57
Total			29,531.77 -	31,814.36	32,389.86			
Shipping & Ports								
223	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	7
224	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2
225	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 05/2012	05/2012	5
226	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	652.40	12/2010 -	09/2012	21
227	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29

List of Delay Project w.r.to Original

Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
228	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25
229	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24
230	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52
231	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93
Total			7,848.98 -	8,674.13	1,106.42			
<u>Telecommunications</u>								
232	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	161.31	12/2005 -	12/2011	72
233	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	12/2011	30
234	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	12/2011	35
235	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	366.00	227.39	10/2008 -	12/2011	38
236	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	362.62	08/2009 -	12/2011	28
237	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	757.02	11/2010 -	12/2011	13
238	GSM equipment of 1500000Lines (2G) 264700lines 3(G - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	346.90	01/2010 -	12/2011	23
239	GSM equipment of 1900000Lines (2G) 335500lines 3(G - [N26000094]BSNL,Kerala	01/2009	848.70 -	848.70	712.86	01/2010 -	12/2011	23
240	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.80	10/2010 03/2012	07/2012	21
Total			5,042.27 -	5,241.25	2,822.16			
<u>Urban Development</u>								
241	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24
Total			6,395.00 -	11,609.00	2,267.57			
<u>Water Resources</u>								
242	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60
Total			542.90 -	1,187.00	35.49			
Grand Total				357,480.70	434,511.11	235,981.86		

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	- 04/2011	04/2012	0/0
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	- 05/2016	11/2016	0/0
	Total		12,565.29 -			0/0
<u>Civil Aviation</u>						
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 -	02/2012	0/0
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2012	0/0
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	08/2012	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 -	12/2012	0/0
7	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
	Total		5,021.58 -			0/0
<u>Coal</u>						
8	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	03/2015 -	03/2015	0/0
9	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	03/2014 -	03/2014	0/0
10	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	04/2014 -	04/2014	0/0
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	03/2015 -	03/2015	0/0
12	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
13	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	12/2015 -	12/2015	0/0
14	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 -	03/2018	0/0
	Total		9,380.82 -			0/0
<u>Fertilisers</u>						
15	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	03/2012	0/0
16	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	04/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
	Total		763.00			0/0
			-			
	<u>Steel</u>					
17	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	04/2013	04/2013	0/0
			-	-		
18	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	05/2013	05/2013	0/0
			-	-		
19	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55	11/2013	11/2013	0/0
			-	-		
	Total		1,725.10			0/0
			-			
	<u>Petroleum</u>					
20	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	12/2010	06/2011	0/0
			-	-		
21	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	09/2009	08/2011	0/0
			1,646.39	-		
22	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	03/2009	01/2012	0/0
			-	02/2012		
23	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00	03/2013	01/2012	0/0
			349.00	03/2013		
24	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	01/2012	01/2012	0/0
			12,160.26	-		
25	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	-	03/2012	0/0
			-	12/2008		
26	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	09/2010	03/2012	0/0
			2,920.82	03/2012		
27	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	09/2011	03/2012	0/0
			898.00	03/2012		
28	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70	04/2010	03/2012	0/0
			-	-		
29	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08	04/2011	03/2012	0/0
			-	-		
30	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	09/2011	03/2012	0/0
			2,730.00	03/2012		
31	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70	03/2011	03/2012	0/0
			755.76	05/2011		
32	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00	09/2012	03/2012	0/0
			-	09/2012		
33	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00	03/2012	03/2012	0/0
			-	-		
34	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	04/2006	05/2012	0/0
			2,218.01	05/2011		
35	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29	05/2010	05/2012	0/0
			6,326.40	05/2012		
36	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40	05/2010	05/2012	0/0
			837.54	04/2012		

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
37	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2012	0/0
38	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	09/2011 05/2012	05/2012	0/0
39	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	06/2012	0/0
40	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2012	0/0
41	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	07/2012	0/0
42	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	07/2012 -	07/2012	0/0
43	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	08/2012	0/0
44	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2012	0/0
45	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2012	0/0
46	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2012	0/0
47	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	10/2012 12/2012	12/2012	0/0
48	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
49	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	01/2013	0/0
50	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	03/2013	0/0
51	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
52	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2013	0/0
53	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	03/2013	0/0
54	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	03/2013	0/0
55	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	03/2013	0/0
56	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	04/2013	0/0
57	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
58	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	08/2013	0/0
59	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
60	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
61	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0

List of Projects Without Milestones

(Dec,2011)

		<u>Date of</u> <u>Commissioning</u>				Milestones Achieved/ Total
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Antici- pated	
1	2	3	4	7	8	10
62	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
63	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
64	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
65	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
66	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
67	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0
68	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 299.00	02/2011 08/2011	08/2011	0/0
69	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	- -	-	0/0
Total			101,355.35 -			0/0
<u>Power</u>						
70	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJEC - [N18000116]PGCIL, Chhatisgarh	12/2011	1,746.65 -	08/2014 -	08/2011	0/0
71	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL, Multi State	12/2007	227.52 -	06/2010 06/2010	01/2012	0/0
72	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL, Multi State	02/2009	664.96 -	02/2012 -	02/2012	0/0
73	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL, Multi State	02/2009	409.50 -	02/2012 02/2012	02/2012	0/0
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL, Rajasthan	02/2009	210.79 -	08/2011 -	02/2012	0/0
75	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL, Multi State	02/2009	353.57 -	07/2010 02/2012	02/2012	0/0
76	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL, Multi State	03/2009	196.10 -	07/2011 -	02/2012	0/0
77	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL, Multi State	04/2008	297.37 297.91	07/2011 -	03/2012	0/0
78	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL, Bihar	02/2010	215.86 -	06/2012 -	03/2012	0/0
79	System Strengthening -X of SR - [N18000086]PGCIL, Multi State	12/2009	276.61 -	04/2012 -	04/2012	0/0
80	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL, Multi State	11/2009	1,075.12 -	05/2012 -	05/2012	0/0
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL, Multi State	02/2009	317.69 -	11/2011 11/2011	06/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
82	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	02/2012 -	06/2012	0/0
83	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	06/2012 -	06/2012	0/0
84	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	06/2012 -	06/2012	0/0
85	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	08/2012 -	08/2012	0/0
86	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	08/2012 -	08/2012	0/0
87	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	08/2012 -	08/2012	0/0
88	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	10/2012 -	10/2012	0/0
89	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	10/2012 -	10/2012	0/0
90	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	10/2012 -	10/2012	0/0
91	TRANSMISSION SYSTEM OF VINDHYACHAL- IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	11/2012 -	11/2012	0/0
92	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	11/2012 -	11/2012	0/0
93	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	11/2012 -	11/2012	0/0
94	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	12/2012 -	12/2012	0/0
95	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	11/2011 -	12/2012	0/0
96	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	11/2011 -	12/2012	0/0
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	02/2012 -	12/2012	0/0
98	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	12/2012 -	12/2012	0/0
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	01/2013 -	01/2013	0/0
100	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	01/2013 -	01/2013	0/0
101	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	03/2013	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
102	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	03/2013 -	03/2013	0/0
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	04/2013 -	04/2013	0/0
104	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	04/2013 -	04/2013	0/0
105	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 -	06/2013	0/0
106	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	01/2012 07/2013	07/2013	0/0
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	07/2013 -	07/2013	0/0
108	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
109	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	07/2013 -	07/2013	0/0
110	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	08/2013 -	08/2013	0/0
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	08/2013 -	08/2013	0/0
112	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	08/2013 -	08/2013	0/0
113	RAMPUR HEP(412 MW) - [N18000024]JSVNL,Himachal Pr.	01/2007	2,047.03 -	01/2012 -	09/2013	0/0
114	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	11/2011 -	09/2013	0/0
115	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	10/2013 -	10/2013	0/0
116	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	11/2013 -	11/2013	0/0
117	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26 -	11/2013 -	11/2013	0/0
118	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL,Multi State	08/2011	1,391.97 -	12/2013 -	11/2013	0/0
119	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	12/2013 -	12/2013	0/0
120	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	12/2013 -	12/2013	0/0
121	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	12/2013 -	12/2013	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
122	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	02/2014 -	02/2014	0/0
123	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	03/2014 -	03/2014	0/0
124	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	05/2014 -	05/2014	0/0
125	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	06/2014 -	06/2014	0/0
126	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	08/2014 -	08/2014	0/0
127	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
128	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	08/2014 -	08/2014	0/0
129	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	08/2013 -	09/2014	0/0
130	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	09/2014 -	09/2014	0/0
131	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	01/2015 -	01/2015	0/0
Total			92,179.81 -			0/0
<u>Railways</u>						
132	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	02/2015	0/0
133	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	12/2010	0/0
134	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	12/2012	0/0
135	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
136	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 227.52	03/2008 03/2009	10/2010	0/0
137	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
138	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010	0/0
139	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
140	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
141	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	- 03/2011	03/2011	0/0
142	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0

List of Projects Without Milestones

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
143	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
144	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	- 03/2011	03/2011	0/0
145	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
146	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	12/2011	0/0
147	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	12/2011	0/0
148	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
149	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012	0/0
150	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	- 12/2009	02/2012	0/0
151	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	12/2011 02/2012	02/2012	0/0
152	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2012	0/0
153	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	- -	03/2012	0/0
154	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2012	0/0
155	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	- 12/2011	03/2012	0/0
156	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	- 03/2012	03/2012	0/0
157	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	02/2009 -	03/2012	0/0
158	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	- 03/2012	03/2012	0/0
159	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
160	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	- 03/2012	03/2012	0/0
161	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	- 02/2011	03/2012	0/0
162	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012	0/0
163	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	- 03/2012	03/2012	0/0
164	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
165	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
166	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
167	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012	0/0
168	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
169	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
170	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	03/2012	0/0
171	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	03/2012 -	03/2012	0/0
172	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	03/2012 -	03/2012	0/0
173	Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012	0/0
174	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	- 07/2012	07/2012	0/0
175	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	06/2004 -	12/2012	0/0
176	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 -	12/2012	0/0
177	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	- 03/2012	12/2012	0/0
178	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	- 03/2012	12/2012	0/0
179	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	03/2009 12/2012	12/2012	0/0
180	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	10/2007 12/2012	12/2012	0/0
181	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
182	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	12/2012 -	12/2012	0/0
183	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
184	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013	0/0
185	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2013	0/0
186	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
187	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	03/2013 -	03/2013	0/0
188	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	- 02/2009	04/2013	0/0
189	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	- 03/2009	04/2013	0/0
190	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	- 06/2013	06/2013	0/0
191	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	12/2011 11/2013	11/2013	0/0

List of Projects Without Milestones

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
192	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya Pradesh	04/2005	383.79 -	- -	12/2013	0/0
193	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	02/2006 -	12/2013	0/0
194	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	03/2009 -	12/2013	0/0
195	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	03/2007 03/2007	03/2014	0/0
196	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	12/2008 -	03/2014	0/0
197	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	03/2014 -	03/2014	0/0
198	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2014	0/0
199	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	03/2014 -	03/2014	0/0
200	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	03/2014 -	03/2014	0/0
201	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
202	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	12/2012 -	03/2014	0/0
203	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014	0/0
204	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2014	0/0
205	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	- 12/2010	03/2015	0/0
206	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015	0/0
207	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2015	03/2015	0/0
208	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	03/2015 -	03/2015	0/0
209	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	03/2015 -	03/2015	0/0
210	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	06/2005 07/2011	06/2015	0/0
211	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	12/2015	0/0
212	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
213	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	03/2005 12/2008	03/2016	0/0
214	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	03/2011 03/2014	03/2016	0/0
215	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
216	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0

List of Projects Without Milestones

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
217	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
218	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
219	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 8,000.00	03/2001 -	12/2017	0/0
220	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
221	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	04/1983	36.80 274.41	- -	-	0/0
222	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	- -	-	0/0
223	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 412.91	- -	-	0/0
224	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 -	03/1998 -	-	0/0
225	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 229.88	- -	-	0/0
226	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00 -	- -	-	0/0
227	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	-	0/0
228	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 1,099.20	07/2005 -	-	0/0
229	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	- -	-	0/0
230	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	-	0/0
231	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, Bihar	04/1997	78.23 162.87	- -	-	0/0
232	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00 625.30	06/2007 -	-	0/0
233	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
234	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 -	- -	-	0/0
235	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 -	- -	-	0/0
236	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, Multi State	04/2000	138.00 519.67	- 12/2012	-	0/0
237	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 -	- -	-	0/0
238	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-	0/0
239	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	- -	-	0/0
240	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
241	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
242	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-	0/0
243	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-	0/0
244	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-	0/0
245	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-	0/0
246	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-	0/0
247	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	-	0/0
248	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
249	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	-	0/0
250	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
251	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,302.12	- 06/2012	12/2012	0/0
252	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	-	0/0
253	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-	0/0
254	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	12/2006 08/2010	-	0/0
255	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	-	0/0
256	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	- -	-	0/0
257	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-	0/0
258	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-	0/0
259	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	-	0/0
260	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	12/2010 03/2011	-	0/0
261	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	- 12/2010	-	0/0
Total			61,606.14 -			0/0

Road Transport & Highways

262	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	12/2011	0/0
263	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	03/2005 -	01/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
264	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00 -	12/2008 -	01/2012	0/0
265	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00 -	06/2009 -	01/2012	0/0
266	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04 -	03/2010 -	01/2012	0/0
267	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	07/2010 -	01/2012	0/0
268	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	02/2012	0/0
269	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	11/2007 -	02/2012	0/0
270	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	02/2012	0/0
271	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00 -	07/2010 -	02/2012	0/0
272	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	03/2012	0/0
273	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	03/2008 -	03/2012	0/0
274	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	03/2012	0/0
275	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2012	0/0
276	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	03/2012	0/0
277	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	03/2012	0/0
278	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	06/2008 -	03/2012	0/0
279	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	12/2008 -	03/2012	0/0
280	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	03/2012	0/0
281	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	03/2012	0/0
282	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,	04/2000	196.50 363.00	- 06/2011	03/2012	0/0
283	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	03/2012	0/0
284	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	03/2012	0/0
285	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00 -	08/2010 -	03/2012	0/0
286	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	01/2011 -	03/2012	0/0
287	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	03/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
288	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya Pradesh	12/2003	225.00 -	10/2008 -	04/2012	0/0
289	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	04/2012	0/0
290	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	10/2008 -	05/2012	0/0
291	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	05/2012	0/0
292	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	05/2012	0/0
293	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	05/2012	0/0
294	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00 -	05/2010 -	05/2012	0/0
295	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	05/2012	0/0
296	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	05/2012	0/0
297	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	05/2012 -	05/2012	0/0
298	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	06/2012	0/0
299	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	06/2012	0/0
300	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	09/2007 -	06/2012	0/0
301	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	06/2012	0/0
302	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	06/2012	0/0
303	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2012	0/0
304	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	06/2012	0/0
305	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	06/2012	0/0
306	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	06/2012	0/0
307	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	06/2012	0/0
308	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	06/2012	0/0
309	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	06/2012	0/0
310	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2012	0/0
311	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	10/2009 -	06/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
312	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	06/2012	0/0
313	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	06/2012	0/0
314	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	06/2012	0/0
315	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	06/2012	0/0
316	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	06/2012	0/0
317	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	07/2012	0/0
318	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	07/2012	0/0
319	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	07/2012	0/0
320	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	08/2012	0/0
321	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2012	0/0
322	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	09/2012	0/0
323	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	09/2012	0/0
324	LAKHNADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012	0/0
325	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	10/2012	0/0
326	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
327	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	10/2012	0/0
328	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
329	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
330	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
331	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	11/2012 -	11/2012	0/0
332	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
333	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
334	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
335	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
336	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
337	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
338	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
339	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
340	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0
341	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
342	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
343	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	01/2013 -	01/2013	0/0
344	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
345	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	02/2009 -	03/2013	0/0
346	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
347	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
348	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00 -	- -	03/2013	0/0
349	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00 -	03/2013 -	03/2013	0/0
350	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
351	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00 -	03/2013 -	03/2013	0/0
352	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
353	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
354	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
355	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
356	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00 -	05/2013 -	05/2013	0/0
357	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	05/2013 -	05/2013	0/0
358	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	05/2013 -	05/2013	0/0
359	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
360	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	06/2013	0/0
361	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
362	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
363	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	06/2013 -	06/2013	0/0
364	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
365	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
366	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
367	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
368	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2013	0/0
369	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0
370	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	07/2013	0/0
371	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0
372	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
373	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
374	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
375	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
376	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	09/2013	0/0
377	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	10/2013	0/0
378	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
379	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
380	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
381	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
382	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
383	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
384	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	01/2014	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
385	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
386	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
387	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
388	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
389	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
390	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
391	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
	Total		73,055.67 -			0/0
<u>Shipping & Ports</u>						
392	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
393	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	06/2006 09/2011	09/2011	0/0
394	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	09/2011 -	09/2011	0/0
395	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	12/2005 01/2008	10/2011	0/0
396	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 06/2011	11/2011	0/0
397	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	06/2011 01/2012	01/2012	0/0
398	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	03/2012 -	03/2012	0/0
399	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	01/2012 -	03/2012	0/0
400	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
401	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	12/2011 05/2012	05/2012	0/0
402	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	12/2010 -	09/2012	0/0
403	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 -	09/2012	0/0
404	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
405	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 -	12/2012	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
406	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	03/2013	0/0
407	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
408	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	01/2009 -	05/2013	0/0
409	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	03/2006 -	12/2013	0/0
410	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013	0/0
411	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
412	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	-	0/0
413	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	12/2007 01/2009	-	0/0
414	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-	0/0
415	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		17,822.23 -			0/0
Telecommunications						
416	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010	0/0
417	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	02/2011	0/0
418	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	03/2009 -	02/2011	0/0
419	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	03/2009 -	03/2011	0/0
420	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
421	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 -	08/2011	0/0
422	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 -	08/2011	0/0
423	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	09/2011 -	09/2011	0/0
424	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 -	12/2011	0/0
425	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	12/2011	0/0
426	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	12/2011	0/0
427	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	10/2008 -	12/2011	0/0

List of Projects Without Milestones

(Dec,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	7	8	10
428	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N260000089]BSNL,Gujarat	08/2008	868.00 -	08/2009 -	12/2011	0/0
429	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N260000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	12/2011	0/0
430	GSM equipment of 1500000Lines (2G) 264700lines 3(G - [N260000093]BSNL,Andhra Pradesh	01/2009	922.91 -	01/2010 -	12/2011	0/0
431	GSM equipment of 1900000Lines (2G) 335500lines 3(G - [N260000094]BSNL,Kerala	01/2009	848.70 -	01/2010 -	12/2011	0/0
432	ERP implementation in BSNL on Turnkey basis - [N260000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	07/2012	0/0
433	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N260000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
434	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N260000043]BSNL,Maharashtra	09/2008	1,799.94 -	09/2009 -	-	0/0
435	Execution of telecom network requirement of defence - [N260000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
436	Implementation of FTTH, the state of the art Acces - [N260000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
437	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N260000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	-	0/0
	Total		11,794.14 -			0/0
<u>Urban Development</u>						
438	FARIDABAD EXTENSION - [N280000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
439	DELHI MRTS PHASE-III - [N280000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
440	C/o office building for IDBI at bandra Kurla Compl - [N280000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
<u>Water Resources</u>						
441	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			425,662.21			0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
