

**326th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
December, 2012**



NHAI - JHANSI TO LALITPUR, NH-25,26



**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

दिसंबर, 2012 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 566 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। दिसंबर, 2012 के दौरान 9 परियोजनाओं (सड़क परिवहन तथा राजमार्ग क्षेत्र की 4 परियोजनाओं, ऊर्वरक क्षेत्र की 2 परियोजनाओं तथा विद्युत, रेलवे और पोत परिवहन एवं बंदरगाह क्षेत्र की प्रत्येक की 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 566 परियोजनाओं में से 258 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 82 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 82 परियोजनाओं में से, 25 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। इस्पात, पोत परिवहन तथा बंदरगाह, कोयला, रेलवे, पेट्रोलियम, विद्युत तथा सड़क परिवहन एवं राजमार्ग क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 51 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	126	35	9	5
2.	सड़क परिवहन एवं राजमार्ग	146	85	35	3
3.	विद्युत	99	52	20	12
4.	पेट्रोलियम	73	34	9	3
5.	कोयला	51	21	3	1
6.	दूरसंचार	14	8	0	0
7.	पोत परिवहन एवं पत्तन	20	6	3	1
8.	इस्पात	17	10	3	0
9.	ऊर्वरक	3	0	0	0
10.	नागर विमानन	6	2	0	0
11.	परमाणु ऊर्जा	5	3	0	0
12.	शहरी विकास	4	1	0	0
13.	जल संसाधन	1	1	0	0
14.	पेट्रोरसायन	1	0	0	0
कुल		566	258	82	25

3. 566 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,85,633.54 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,27,454.45 करोड़ रुपए होने की संभावना है जो 1,41,820.91 करोड़ रुपए (मूल लागत का 18.10%) की समग्र लागत वृद्धि को दर्शाता है। दिसंबर, 2012 तक इन परियोजनाओं पर किया गया व्यय 4,34,000.60 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 46.80% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.12.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	499.16	1488.67
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1412.74	1162.50
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. 566 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 184 समय पर तथा 258 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या 276 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है। इसके अलावा, 30 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 89 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया गया है। 258 विलंबित परियोजनाओं में से, 70 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 57 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 91 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 40 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.12.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2013	216
2	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
3	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	06/2016	135
4	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	06/2005	06/2016	132
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	01/2013	132

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की समीक्षा करेंगे ।

5. विभिन्न परियोजना कार्यान्वयनकर्ता एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, वन संबंधी स्वीकृति में विलंब, मेसर्स बीएचईएल द्वारा सामग्री की आपूर्ति में विलंब, कुशल जनशक्ति की कमी, ठेकेदार द्वारा अपर्याप्त संग्रहण, निधि व्यय, उपकरणों को संस्थापित करने में विलंब, कार्यक्षेत्र में बदलाव, उपकरणों की आपूर्ति में विलंब, कानून और व्यवस्था की समस्या आदि शामिल हैं ।

6. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाओं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दिए गए हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.12.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	499.16	169.68	03/2007	03/2015	0
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	730	352.01	07/2012	ऊ.न.	0
3	इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.17	242.39	ऊ.न.	03/2015	0
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	0
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1086.41	427.98	06/2005	06/2016	0

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

7. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.12.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)
				मूल	अनुमानित	
1	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	रेलवे	04/1985	158.77	432.46	558.07
2	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	205.16
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	538.10
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	590.02
5	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8521.82

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.12.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	उ.न.	उ.न.
2	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	रेलवे	04/1985	03/1994	उ.न.	12/2011
3	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	उ.न.	03/2010	उ.न.
4	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
5	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल		12/1994	उ.न.	उ.न.	03/2012

	(एससीआर)	रेलवे				
--	----------	-------	--	--	--	--

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

8. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है :-

(i) **इस्पात क्षेत्र में**, 17 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं । माह के दौरान 3 परियोजनाओं के संबंध में 1-2 माह तक के अतिरिक्त विलंब की सूचना दी है । '330 टीपीएच बायलर-6 और सहायक प्रणाली, आरआईएनएल' एवं '67.5 मे.वा. टीजी-5 सहायक प्रणाली आपात विद्युत मांग, आरआईएनएल' परियोजनाओं के संबंध में मेसर्स बीएचईएल द्वारा सामग्री की आपूर्ति में विलंब के कारण क्रमशः 1 तथा 2 माह के अतिरिक्त विलंब की सूचना दी है । 'बेलाडिला लौह अयस्क परियोजना डिपोजिट-11बी, एनएमडीसी के संबंध में 2 माह के अतिरिक्त विलंब की सूचना दी है । तथापि, इस परियोजना के संबंध में परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है ।

(ii) **पोत परिवहन तथा पत्तन क्षेत्र में**, 20 परियोजनाओं में से 6 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 1-5 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से एक बड़ी परियोजना है । '120 बी.पी. (एएच03 टाइप) एएचटीएस के दो जहाजों का अधिग्रहण, पोत परिवहन,' 'पुथु में एलएनजी पुनःगैसीकरण टर्मिनल को स्थापित करना, पोर्ट ट्रस्ट' तथा 82000 डीडब्ल्यूटी कामसावमैक्स 4 बल्क कैरिअरों का अधिग्रहण, पोत परिवहन' परियोजना के संबंध में क्रमशः 1, 1 और 5 माह के अतिरिक्त विलंब की सूचना दी है । तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष सूचना नहीं दी है ।

(iii) **कोयला क्षेत्र में**, 51 परियोजनाओं में से 21 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 6-24 माह के अतिरिक्त विलंब की सूचना दी है जिनमें से 1 बड़ी परियोजना है । 'टीपीएस-II विस्तार (1470 मे.वा. से 1970 मे.वा.), एनएलसी' परियोजना के संबंध में उपस्कर स्थापन में विलंब तथा ठेकेदार द्वारा अपर्याप्त सेवा प्रदान करने के कारण 6 माह के अतिरिक्त विलंब की सूचना दी है ('रामगंडम ओसी-II विस्तार,एससीसीएल' तथा 'चुर्चा आरओयूजी (1.35 एमटीवाई), एसईसीएल' के संबंध में वन अनुमति में विलंब के कारण 12 से 24 माह के अतिरिक्त विलंब की सूचना दी है ।

(iv) **रेलवे क्षेत्र में**, 126 परियोजनाओं में से 35 परियोजनाएं विलंबित हैं । माह के दौरान, 9 परियोजनाओं के संबंध में प्रत्येक में 6-51 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 5 बड़ी परियोजनाएं हैं । 9 परियोजनाओं में से, 1 परियोजना के संबंध में 6 माह के अतिरिक्त विलंब की सूचना दी गई है तथा 3 परियोजनाओं के संबंध में प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना दी गई है ।

(V) **पेट्रोलियम क्षेत्र** में, 99 परियोजनाओं में से 52 परियोजनाएं विलंबित हैं। माह के दौरान, 20 परियोजनाओं के संबंध में 1-11 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 12 बड़ी परियोजनाएं हैं। इन 20 परियोजनाओं में से, 3 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'कम्प्रेसर स्टेशन्स (कैलारास तथा चेन्सा) गेल' परियोजना ने ठेकेदार द्वारा धीमी प्रगति के कारण 2 महीने अतिरिक्त विलंब की सूचना दी है। 'कोची-कूटांड बंगलोर मंगलोर पाइप लाइन परियोजना गेल' ने आरओयू समस्या के कारण 3 महीने अतिरिक्त विलंब की सूचना दी है।

(VI) **विद्युत क्षेत्र** में, 99 परियोजनाओं में से 51 परियोजनाएं विलंबित हैं। माह के दौरान 9 परियोजनाओं के संबंध में 1-6 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 5 परियोजनाएं बड़ी परियोजनाएं हैं। इन 9 परियोजनाओं में से 3 परियोजना के संबंध में क्रमशः प्रत्येक में 1 माह के विलंब की सूचना प्राप्त हुई है तथा 3 परियोजनाओं के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। '765 केवी सिस्टम फॉर सेंट्रल पार्ट ऑफ नार्दर्न ग्रिड पार, पीजीसीआईएल' परियोजना ने आरओयू समस्या के कारण 3 महीने अतिरिक्त विलंब की सूचना दी है। डीवीसी, पीजीसीआईएल से संबद्ध पूरक पारेषण तथा कोलडैम एचईपी,एनटीपीसी' परियोजनाओं ने क्रमशः वन संबंधी स्वीकृति तथा मुख्य बांध में सीपेज समस्या के कारण प्रत्येक में अतिरिक्त 6 महीने विलंब की सूचना दी है।

(VII) **सड़क परिवहन एवं राजमार्ग क्षेत्र** में, 146 परियोजनाओं में से 86 परियोजनाएं विलंबित हैं। माह के दौरान 10 परियोजनाओं के संबंध में 1-13 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 3 परियोजनाएं बड़ी परियोजनाएं हैं। इन 10 परियोजनाओं में से 8 परियोजनाओं के संबंध में प्रत्येक में एक माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। राजमार्ग चौराहा से लखनानन्दन (297 से 351 कि.मी.), एनएच 26, एनएचएआई तथा वाडनेर-देवधारी (एनएस-60/एमएच) (94-123 कि.मी.), एनएचएआई' ने क्रमशः 6 तथा 13 महीने अतिरिक्त विलंब की सूचना दी है। परियोजना कार्यान्वयनकर्ता एजेंसी ने इन परियोजनाओं के विलंब के लिए किसी विशेष कारण का उल्लेख नहीं किया है। तथापि, इन परियोजनाओं में विलंब के कारणों में भूमि अधिग्रहण, वन तथा पर्यावरण संबंधी अनुमति में विलंब, जनसुविधा स्थानांतरित करने की समस्या, ठेकेदार का खराब कार्य निष्पादन आदि शामिल हैं।

9. दिनांक 30.11.2012 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपये तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

10. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for December 2012 contains information on the status of the 566 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During December 2012, 9 projects (4 projects in Road Transport & Highways, 2 projects in Fertilizers, 1 project each in Power, Railways and Shipping & Ports Sector) have reported completion.

2. During the reference month, out of 566 projects, 258 projects are delayed with respect to latest schedule and 82 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 82 projects, 25 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 51 months in respect of projects relating to Steel, Shipping & Ports, Coal, Railways, Petroleum, Power and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	126	35	9	5
2.	ROAD TRANSPORT & HIGHWAYS	146	85	35	3
3.	POWER	99	52	20	12
4.	PETROLEUM	73	34	9	3
5.	COAL	51	21	3	1
6.	TELECOMMUNICATION	14	8	0	0
7.	SHIPPING & PORTS	20	6	3	1
8.	STEEL	17	10	3	0
9.	FERTILISERS	3	0	0	0
10.	CIVIL AVIATION	6	2	0	0
11.	ATOMIC ENERGY	5	3	0	0
12.	URBAN DEVELOPMENT	4	1	0	0
13.	WATER RESOURCES	1	1	0	0
14.	PETROCHEMICALS	1	0	0	0
Total		566	258	82	25

3. Total original cost of implementation of the 566 projects was about ₹ 7,85,633.54 crore and their anticipated completion cost is likely to be ₹ 9,27,454.45 crore, which reflects an overall cost overruns of ₹ 1,41,820.91 crore (18.10 % of original cost). The expenditure incurred on these projects till December 2012 is ₹ 4,34,009.60 crore, which is 46.80 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-12-2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	499.16	1488.67
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1412.74	1162.50
5	RUPSA-BANGRIPOSI (GC)(SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. Out of the 566 projects, 5 projects are ahead of schedule, 184 are on schedule and 258 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 276 if delay is calculated on the basis of original schedule of completion. Further, 30 projects have been sanctioned without any commissioning schedule/date and for 89 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 258 delayed projects, 70 projects have overall delay in the range of 1 to 12 months, 57 projects have a delay in the range of 13 to 24 months, 91 projects have a delay in the range of 25 to 60 months and 40 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-12-2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
3	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
4	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	06/2005	06/2016	132
5	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

5. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of material by M/s BHEL, shortage of skilled manpower, inadequate mobilization by the contractor, fund constraints, delay in equipment erection, change in scope of work, delay in supply of equipment, law & order problem, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31.12.2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ crore)		EXPENDITURE CUMULATIVE (₹ crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	499.16	169.68	03/2007	03/2015	0
2	NANGALDAMTALWARA (NL), NR	Railways	03/1981	37.68	730.00	352.01	07/2012	N.A.	0
3	NEW BGRLY LINE FROM EKLAKHI-BALURGHA T (NEFR)	Railways	04/1983	36.80	703.17	242.39	N.A.	03/2015	0
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	0
5	TAMLUK DIGHA, LINE DOUBLING (SER)	Railways	03/1984	293.97	1086.41	427.98	06/2005	06/2016	0

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

7. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31.12.2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		EXPENDITURE CUMMULATIVE (₹ ; crore)
				ORIGINAL	REVISED	
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	04/1985	158.77	432.46	558.07
2	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	205.16
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	538.10
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	590.02
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8521.82

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.12.2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.A.	N.A.
2	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	04/1985	03/1994	N.A.	12/2011
3	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.A.	03/2010	N.A.
4	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
5	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.A.	N.A.	03/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

8. The Sector-wise details of delays/additional delays are as under:-

i) In the **Steel Sector**, out of 17 projects, 10 projects are delayed. During the month 3 projects have reported additional delays in the range of 1-2 months. The projects '330 TPH Boiler-6 and Auxiliary System, RINL' and '67.5 MW TG-5 Auxiliary System Emergency Power Requirement, RINL' have reported additional delay of 1 and 2 months respectively due to delay in supply of materials by M/s BHEL. The project 'Bailadila Iron Ore Project Deposit- 11B, NMDC' has reported additional delay of 2 months. However, no specific reasons have been reported by the project authorities for delay in this project.

ii) In the **Shipping & Ports Sector**, out of 20 projects, 6 projects are delayed. During the month 3 projects have reported additional delays in the range of 1-5 months, out of which 1 is a Mega project. The projects 'Acquisition of two nos. of 120 B.P (AH03 Type) AHTS Vessels, Shipping', 'Setting up of LNG Regasification Terminal at Puthu, Port Trust' and 'Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers, Shipping' have reported additional delay of 1, 1 and 5 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

iii) In the **Coal Sector**, out of 51 projects, 21 projects are delayed. During the month 3 projects have reported additional delays in the range of 6-24 months, out of which 1 is a Mega project. The project 'TPS-II Expansion (1470 MW TO 1970 MW), NLC' has reported additional delay of 6 months due to delay in equipment erection and inadequate mobilization by the contractor. The projects 'Ramagundam OC-II Extension, SCCL' and 'Churcha ROUG (1.35MTY), SECL' have reported additional delay of 12 and 24 months respectively due to delay in forest clearance.

iv) In the **Railways Sector**, out of 126 projects, 35 projects are delayed. During the month 9 projects have reported additional delays in the range of 6-51 months, out of which 5 are Mega project. Of these 9 projects, 1 project has reported additional delay of 6 months and 3 projects have reported additional delay of 12 months each. The project 'Agartala Sabroom, NL, NEFR' has reported additional delay of 21 months due to fund constraints. The projects 'New B.G. Line from Tetelia to Byrnihat (National Project), NEFR' and 'Bhairabi Sairong, NL, NEFR' have reported additional delay of 24 months

each due to delay in forest clearance. The projects 'New Line from Dimapur to Zubza (Kohima) (National Project), NEFR' and 'Sevok Rangpo, NEFR' have reported additional delay of 24 and 51 months respectively due to change in scope of work.

v) In the Petroleum Sector, out of 73 projects, 34 projects are delayed. During the month 9 projects have reported additional delays in the range of 1-6 months, out of which 3 are Mega projects. Of these 9 projects, 3 projects have reported additional delay of 1 month each and 2 projects have reported additional delay of 2 months each. The project 'Construction of 12 Offshore Supply Vessels (OSV), ONGC' has reported additional delay of 4 months due to shortage of skilled manpower and '102 MW Wind Power Project, ONGC' has reported additional delay of 5 months due to change in scope of work. The projects 'Diesel Hydrotreater Project at Mumbai Refinery, HPCL' and 'Conversion of RIG Sagar Samrat to Mobile Offshore, ONGC' have reported additional delay of 5 and 6 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

vi) In the Power Sector, out of 99 projects, 52 projects are delayed. During the month 20 projects have reported additional delays in the range of 1-11 months, out of which 12 are Mega projects. Of these 20 projects, 3 projects have reported additional delay of 1 month each, 2 projects have reported additional delay of 2 months each and 8 projects have reported additional delay of 3 months each. The projects 'Transmission System Associated with Sasan Ultra ME, PGCIL', 'Rampur HEP (412 MW), SJVNL' and '765 KV Pooling Station and Network with DVC and MA, PGCIL' have reported additional delay of 4, 5 and 9 months respectively due to delay in forest clearance. The project 'Rihand STTP Stage-III (2X500MW), NTPC' has reported additional delay of 6 months due to delay in supply of equipment. The projects 'Transmission System of Vindhyachal-IV & Rihand-I, PGCIL' and 'Northern Region Transmission Strengthening Scheme, PGCIL' have reported additional delay of 9 months each due to delay in land acquisition. The project 'Bongaigaon Thermal Power Project, NTPC' has reported additional delay of 11 months due to law & order problem.

vii) In the Road Transport & Highways Sector, out of 146 projects, 85 are delayed. During the month 35 projects have reported additional delays in the range of 1-15 months, out of which 3 are Mega Projects. Of these 35 projects, 13 projects have reported additional delay of 1 month each, 3 projects have reported additional delay of 2 months each, 8 projects have reported additional delay of 3 months each, 1 project has reported

additional delay of 5 months and 4 projects have reported additional delay of 6 months each. The projects 'Bijni to Assam/W.B. Border (NH-31.C) (2), NHAI', 'Nalbari to Bijni (AS-8), NHAI' and 'Six Lanning of Vadakkancherry Thrissuresection, NHAI' have reported additional delay of 12 months each. The projects 'Guwhati to Nalbari (AS-4), NHAI', 'Guwahati to Nalbari (AS-5), NHAI' and 'Brahmputra Bridge, NH NO-31, NHAI' have reported additional delay of 15 months each. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

9. The status as on 31.12.2012 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

10. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	146	35
2	Railways	126	9
3	Power	99	20
4	Petroleum	73	10
5	Coal	51	5
6	Shipping & Ports	20	3
7	Steel	17	3
8	Telecommunications	14	0
9	Civil Aviation	6	0
10	Atomic Energy	5	0
11	Urban Development	4	0
12	Fertilisers	3	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	566	85

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	1438
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
<u>Railways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
<u>Road Transport & Highways</u>				
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
<u>Shipping & Ports</u>				
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
June,2012				
<u>Steel</u>				
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
<u>Power</u>				
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	3779.46
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
<u>Railways</u>				
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
<u>Road Transport & Highways</u>				
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9
July,2012				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Power</u>				
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
<u>Railways</u>				
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096]	196.97	03/2011	218.66
August,2012				
<u>Steel</u>				
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
<u>Power</u>				
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
<u>Road Transport & Highways</u>				
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235]	193.09	03/2008	189.15
September,2012				
<u>Petroleum</u>				
34	REVAMPING OF WIN PLATFORM AT MH ASSET(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000044]	333.40	05/2010	680.85
<u>Telecommunications</u>				
35	PROJ.III OF NIB-II OF MESSAGING STORAGE(BHARAT SANCHAR NIGAM LIMITED) - [260100099]	250.00	12/2005	80.47
36	NIB Project Capacity Expansion(BHARAT SANCHAR NIGAM LIMITED) - [N26000098]	175.52	12/2008	60.84
October,2012				
<u>Road Transport & Highways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
37	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106204]	275.00	09/2007	306.65
38	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106301]	151.30	10/2008	190.61
November,2012				
<u>Petroleum</u>				
39	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC(GAS AUTHORITY OF INDIA LIMITED) - [N16000071]	348.00	03/2012	203.31
December,2012				
<u>Fertilisers</u>				
40	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS(NATIONAL FERTILISER LIMITED) - [N08000007]	325.00	07/2011	185.1
41	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ(NATIONAL FERTILISER LIMITED) - [N08000008]	438.00	07/2011	239.93
<u>Power</u>				
42	WESTERN REGION STRENGTHENING SCHEME-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000022]	5,221.23	07/2010	3175.3
<u>Railways</u>				
43	MUMBAI URBAN TRANSPORT PROJECT PHASE-I(METROPOLITAN RAPID TRANSPORT PROJECTS) - [N22000093]	3,125.20	06/2011	4334
<u>Road Transport & Highways</u>				
44	DAKOPA TO NAGAON (NH-36)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106288]	225.00	06/2008	285.2
45	JHAJHARPUR TO DARBANGA (BR-7)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000031]	340.00	09/2008	575.32
46	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000118]	464.00	01/2011	535.62
47	Hyderabad-yadgiri N.H no-202(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000142]	388.00	05/2012	537.91
<u>Shipping & Ports</u>				
48	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA(SHIPPING crp. of india) - [N25000031]	1,066.91	09/2012	1027.12


Summary of projects in the Flash Report for the month of December, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	567
Number of Projects completed/dropped/frozen in Previous Month	1
Number of Projects completed/dropped/frozen in Current Month	9
Number of Projects are not Reported in Current Month	2
Number of Projects Added in Current Month	11
Number of Projects in Current Month	566


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 566 projects, 4 projects are ahead of schedule, 167 projects are on schedule and 276 projects are delayed. Of the balance, 89 projects do not have fixed dates of commissioning while 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

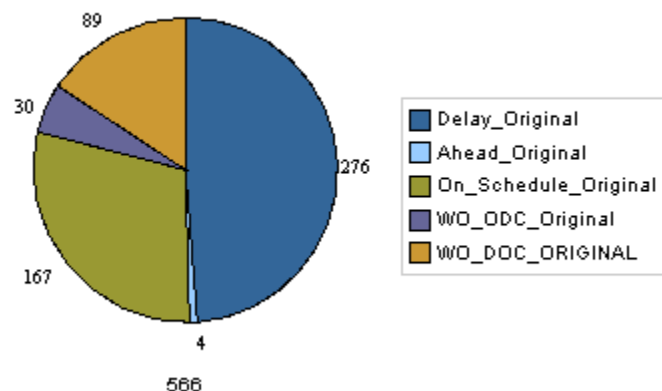

III. Investment Scenario

The Total Original cost of implementation of 566 projects when sanctioned, was of the order of Rs. 785633.54 crore but this was subsequently revised to Rs. 927454.45 crore implying a cost overrun of 18.1%. The expenditure incurred on these projects till December, 2012 is Rs. 434009.6 crore, which is 46.8% of the revised cost of the projects.

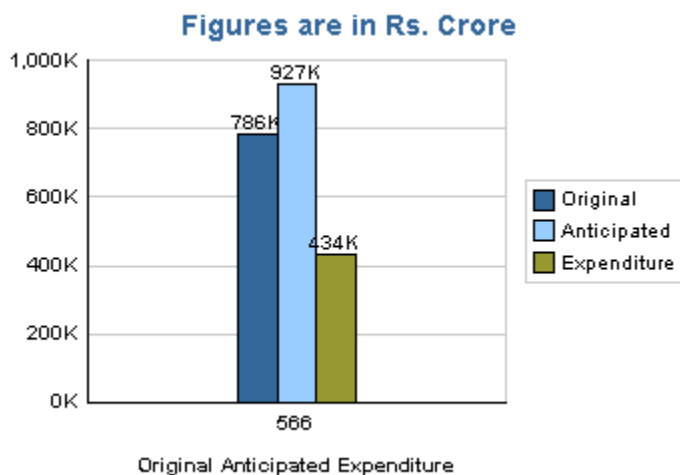

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	567
No of Projects Completed/Dropped/Frozen in Previous Month	1
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects are not reported in Current Month	2
No of Projects added in Current Month	11
No of Projects in Current Month	566

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	276	4	167	30	89	566	48.76
Latest Approved (Date)	258	5	184	30	89	566	45.58

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	415	658,015.73	693,039.76	298,299.24	43.00	35,024.03	5.30
Latest Approved (RCE)	151	186,730.20	234,414.69	135,710.36	57.90	47,684.49	25.50
Total (RCE)	566	844,745.93	927,454.45	434,009.60	46.80	82708.52	9.79
Original Cost of All Projects							
Original Cost	566	785,633.54	927,454.45	434,009.60	46.80	141,820.91	18.10

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	276	441,244.73	543,104.56	321,498.08	59.20	101,859.83	23.10
Latest Approved (RCE)	258	439,144.45	501,467.32	297,437.14	59.30	62,322.87	14.20

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	82	123,683.98	138,329.67	99,442.03	71.90	14,645.69	11.80

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	36,056.5	37,510.5	4.0	7	8,579.5	10,631.3	23.9
4	Fertilisers	3	4,065.7	4,065.7	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	73	177,447.7	188,692.3	6.3	16	54,264.0	73,426.2	35.3
8	Power	99	227,823.1	243,653.3	6.9	19	46,019.4	61,849.6	34.4
9	Railways	126	61,393.5	148,131.7	141.3	108	42,365.2	129,150.0	204.8
10	Road Transport & Highways	146	94,417.9	96,356.5	2.1	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	20	15,908.0	18,174.9	14.3	9	8,629.0	11,218.5	30.0
12	Telecommunications	14	5,964.9	5,905.7	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	785,633.5	927,454.5	18.1	186	221,202.1	372,202.5	68.3

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,097.3	38,721.1	24.5	14	12,420.0	20,910.9	68.4
2	Arunachal Pr.	4	9,512.2	14,144.3	48.7	2	6,441.3	11,073.4	71.9
3	Assam	34	22,035.9	35,405.4	60.7	12	10,491.8	23,955.3	128.3
4	Bihar	30	26,917.6	34,673.4	28.8	13	12,343.6	20,099.4	62.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	10	5,496.6	7,636.7	38.9	3	1,448.2	3,588.3	147.8
8	Himachal Pr.	5	13,355.6	17,246.7	29.1	4	11,308.5	15,199.7	34.4
9	J and K	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	26	46,344.4	55,830.8	20.5	9	8,598.8	18,491.8	115.1
11	Kerala	7	20,376.7	21,818.2	7.1	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	22	18,978.9	19,273.4	1.6	3	2,027.6	2,741.5	35.2
13	Maharashtra	52	93,207.4	108,066.8	15.9	15	28,256.2	45,605.8	61.4
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	31	57,664.0	62,099.1	7.7	12	32,671.6	37,106.7	13.6
19	Punjab	7	4,836.2	5,778.0	19.5	2	532.4	1,474.2	176.9
20	Rajasthan	13	20,962.9	20,917.1	-0.2	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	23	18,822.9	22,659.7	20.4	8	3,498.5	7,383.5	111.0
25	West Bengal	27	42,286.1	54,884.3	29.8	17	25,617.0	38,215.2	49.2
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	24	46,583.8	47,866.9	2.8	6	1,548.3	2,831.4	82.9
28	Jharkhandd	23	14,447.4	18,429.0	27.6	6	1,897.3	6,050.7	218.9
29	Uttaranchal	4	6,097.2	7,037.6	15.4	2	2,640.7	3,581.2	35.6
30	Multi State	108	143,702.1	153,168.6	6.6	22	10,740.0	24,254.3	125.8
Total		566	785,633.5	927,454.5	18.1	186	221,202.1	372,202.5	68.3

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	10 - 27
3	Coal	51	36,056.5	37,510.5	4.0	21	18,020.0	19,893.5	16 - 60
4	Fertilisers	3	4,065.7	4,065.7	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	3 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	73	177,447.7	188,692.3	6.3	39	107,659.6	121,546.0	1 - 120
8	Power	99	227,823.1	243,653.3	6.9	52	131,109.8	146,326.9	1 - 102
9	Railways	126	61,393.5	148,131.7	141.3	44	29,131.4	76,631.5	1 - 216
10	Road Transport & Highways	146	94,417.9	96,356.5	2.1	86	42,151.6	44,090.3	2 - 107
11	Shipping & Ports	20	15,908.0	18,174.9	14.3	7	7,295.2	8,778.8	5 - 87
12	Telecommunications	14	5,964.9	5,905.7	-1.0	8	2,967.1	2,971.0	11 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	785,633.5	927,454.5	18.1	276	441,244.7	543,104.6	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,097.3	38,721.1	24.5	12	16,856.0	20,665.4	5 - 41
2	Arunachal Pr.	4	9,512.2	14,144.3	48.7	3	9,356.2	13,737.9	25 - 78
3	Assam	34	22,035.9	35,405.4	60.7	32	21,259.3	34,443.6	12 - 120
4	Bihar	30	26,917.6	34,673.4	28.8	13	20,238.4	26,111.2	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	10 - 10
6	Gujarat	22	31,111.6	31,313.5	0.6	6	15,224.5	15,394.7	6 - 24
7	Haryana	10	5,496.6	7,636.7	38.9	5	2,407.4	4,094.1	1 - 50
8	Himachal Pr.	5	13,355.6	17,246.7	29.1	5	13,355.6	17,246.7	25 - 102
9	J and K	10	14,927.0	34,825.6	133.3	9	13,826.3	33,724.9	10 - 201
10	Karnataka	26	46,344.4	55,830.8	20.5	9	21,604.1	26,588.7	9 - 101
11	Kerala	7	20,376.7	21,818.2	7.1	4	5,356.0	6,006.0	5 - 58
12	Madhya pradesh	22	18,978.9	19,273.4	1.6	13	10,571.4	10,585.3	5 - 60
13	Maharashtra	52	93,207.4	108,066.8	15.9	24	50,822.7	60,375.3	6 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 35
17	Nagaland	1	850.0	850.0	0.0	1	850.0	850.0	24 - 24
18	Orissa	31	57,664.0	62,099.1	7.7	11	33,068.2	34,030.5	9 - 132
19	Punjab	7	4,836.2	5,778.0	19.5	4	1,611.4	2,553.2	1 - 58
20	Rajasthan	13	20,962.9	20,917.1	-0.2	6	15,563.1	15,258.8	3 - 52
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	27 - 51
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	11	30,528.8	36,459.4	9 - 87
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,101.4	1,395.4	9 - 21
24	Uttar Pradesh	23	18,822.9	22,659.7	20.4	11	11,635.1	13,615.4	5 - 94
25	West Bengal	27	42,286.1	54,884.3	29.8	16	27,379.4	34,514.0	3 - 135
26	Delhi	4	38,214.4	38,194.8	-0.1	2	478.4	458.8	11 - 72
27	Chhatisgarh	24	46,583.8	47,866.9	2.8	6	18,544.1	18,855.4	6 - 48
28	Jharkhandd	23	14,447.4	18,429.0	27.6	11	8,935.4	10,095.1	11 - 102
29	Uttaranchal	4	6,097.2	7,037.6	15.4	4	6,097.2	7,037.6	5 - 45
30	Multi State	108	143,702.1	153,168.6	6.6	50	80,329.5	87,230.6	1 - 216
Total		566	785,633.5	927,454.5	18.1	276	441,244.7	543,104.6	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	2,278.1	2,660.6	10 - 22
3	Coal	51	36,056.5	37,510.5	4.0	21	18,020.0	19,893.5	16 - 60
4	Fertilisers	3	4,065.7	4,065.7	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	3 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	73	177,447.7	188,692.3	6.3	34	97,902.4	106,265.6	1 - 86
8	Power	99	227,823.1	243,653.3	6.9	52	131,109.8	146,326.9	1 - 102
9	Railways	126	61,393.5	148,131.7	141.3	35	19,015.5	60,384.2	2 - 216
10	Road Transport & Highways	146	94,417.9	96,356.5	2.1	85	41,871.6	43,810.3	2 - 107
11	Shipping & Ports	20	15,908.0	18,174.9	14.3	6	7,145.2	8,178.8	5 - 34
12	Telecommunications	14	5,964.9	5,905.7	-1.0	8	2,967.1	2,971.0	11 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	785,633.5	927,454.5	18.1	258	415,171.5	501,467.3	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	37,022.5	37,510.5	1.3	6	7,115.6	7,603.7	6.9
4	Fertilisers	3	4,065.7	4,065.7	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	73	194,077.5	188,692.3	-2.8	2	30,602.0	32,253.0	5.4
8	Power	99	231,630.2	243,653.3	5.2	13	39,029.6	51,052.7	30.8
9	Railways	126	91,157.4	148,131.7	62.5	81	46,557.8	104,218.2	123.8
10	Road Transport & Highways	146	94,584.4	96,356.5	1.9	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	20	17,661.9	18,174.9	2.9	6	3,312.5	4,036.9	21.9
12	Telecommunications	14	5,988.4	5,905.7	-1.4	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	844,745.9	927,454.5	9.8	128	164,775.1	255,879.0	55.3

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	51	36,056.46	37,510.52	4.03	0	0.00	0.00	0- 0
4	Fertilisers	3	4,065.66	4,065.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	15- 15
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	73	177,447.66	188,692.30	6.34	11	20,638.48	35,088.71	24- 120
8	Power	99	227,823.09	243,653.33	6.95	2	2,253.45	3,986.02	0- 76
9	Railways	126	61,393.48	148,131.67	141.28	17	6,309.80	23,226.43	1- 141
10	Road Transport & Highways	146	94,417.90	96,356.52	2.05	0	0.00	0.00	0- 0
11	Shipping & Ports	20	15,907.97	18,174.92	14.25	5	5,400.70	6,860.25	10- 87
12	Telecommunications	14	5,964.89	5,905.68	-0.99	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		566	785633.54	927454.45	18.05	38	42166.93	80703.58	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	22- 22
3	Coal	51	36,056.46	37,510.52	4.03	4	7,617.44	9,621.06	16- 51
4	Fertilisers	3	4,065.66	4,065.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	5- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	73	177,447.66	188,692.30	6.34	13	52,458.98	70,307.15	10- 120
8	Power	99	227,823.09	243,653.33	6.95	17	45,001.89	60,218.99	7- 102
9	Railways	126	61,393.48	148,131.67	141.28	35	18,194.53	65,699.55	1- 216
10	Road Transport & Highways	146	94,417.90	96,356.52	2.05	11	3,324.28	5,445.20	21- 105
11	Shipping & Ports	20	15,907.97	18,174.92	14.25	5	6,462.00	8,025.50	13- 87
12	Telecommunications	14	5,964.89	5,905.68	-0.99	2	1,065.85	1,089.32	25- 45
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	21- 21
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		566	785633.54	927454.45	18.05	98	185665.88	291934.2	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

S.no	Project	DOA	Original		Now anticipated		Final
			Cost	DOC	Cost	DOC	Expenditure
	<u>Fertilisers</u>						
1	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS	09/2008	325.00	07/2011	325.00	12/2012	185.10
2	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ	09/2008	438.00	07/2011	438.00	12/2012	239.93
	<u>Power</u>						
3	WESTERN REGION STRENGTHENING SCHEME-II	07/2006	5,221.23	07/2010	5,221.23	12/2012	3,175.30
	<u>Railways</u>						
4	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	04/2003	3,125.20	06/2011	4,501.80	03/2012	4,334.00
	<u>Road Transport & Highways</u>						
5	DAKOPA TO NAGAON (NH-36)(NHAI)	12/2003	225.00	06/2008	225.00	12/2012	285.20
6	JHAJHARPUR TO DARBANGA (BR-7)	12/2003	340.00	09/2008	340.00	12/2012	575.32
7	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER	01/2008	464.00	01/2011	464.00	12/2012	535.62
8	Hyderabad-yadgiri N.H no-202	08/2010	388.00	05/2012	388.00	12/2012	537.91
	<u>Shipping & Ports</u>						
9	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA	08/2008	1,066.91	09/2012	968.35	12/2012	1,027.12

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
<u>Petroleum</u>						
1	SINGLE POINT MOORING FACILITY(SMP) PROJECT	7/2010	1,043.57	4/2012	1,043.57	1/2013
<u>Power</u>						
2	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT	7/2011	181.93	7/2013	181.93	7/2013
3	AUGMENTION OF TRANSFORMERS IN NORTHEN REGION - PART A	12/2012	156.04	10/2014	156.04	10/2014
4	COMMON TRANSMISSION SCHEME WITH ISSG	1/2013	182.80	10/2014	182.80	10/2014
<u>Road Transport & Highways</u>						
5	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	7/2012	356.40	7/2014	356.40	7/2014
6	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	11/2011	478.00	10/2013	478.00	3/2014
7	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	4/2012	624.00	4/2014	624.00	4/2014
8	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	4/2011	682.00	10/2013	682.00	3/2014
<u>Shipping & Ports</u>						
9	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER	7/2011	220.49	1/2013	220.49	6/2013
10	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL	1/2012	511.87	3/2014	511.87	-
<u>Telecommunications</u>						
11	DELHI CONVERGENT BILLING AND CRM PE-5834	2/2006	229.41	3/2012	229.41	2/2013

VII. Milestones (Cumulative due & achieved)

Total	3404
Achieved up to month	1274

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Coal</u>						
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,027.59	06/2009	03/2013	09/2013	6
2	RAMAGUNDAM OC-II EXTENSION SCCL	418.97	418.97	03/2012	03/2014	03/2015	12
3	CHURCHA ROUG (1.35MTY) SECL	462.35	462.35	03/2014	03/2014	03/2016	24
	<u>Steel</u>						
4	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	12/2012	01/2013	1
5	Bailadila Iron Ore Project Deposit- 11B (NMDC) NMDC	295.89	607.17	12/2011	01/2013	03/2013	2
6	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2011	01/2013	03/2013	2
	<u>Petroleum</u>						
7	CONSTRUCTION OF NEW PROCESS COMPLEX MHN ONGC	2,853.29	6,326.40	05/2010	12/2012	01/2013	1
8	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT IOCL	341.50	341.50	02/2013	02/2013	03/2013	1
9	EURO-IV DHDT CPCL	2,615.69	2,615.69	N.A.	12/2012	01/2013	1
10	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA ONGC	370.11	370.11	04/2011	11/2012	01/2013	2
11	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	253.66	08/2012	03/2013	05/2013	2
12	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	08/2013	12/2013	4
13	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY HPCL	3,284.00	2,174.00	09/2011	09/2012	02/2013	5
14	102 MW WIND POWER PROJECT ONGC	1,106.00	820.00	06/2012	10/2013	03/2014	5
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE ONGC	861.79	756.65	05/2013	05/2013	11/2013	6
	<u>Power</u>						
16	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.26	913.00	02/2011	12/2012	01/2013	1
17	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	386.32	07/2011	12/2012	01/2013	1
18	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	04/2015	04/2015	05/2015	1

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
19	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA PGCIL	1,347.32	1,347.32	02/2012	01/2013	03/2013	2
20	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX PGCIL	182.68	182.68	01/2013	01/2013	03/2013	2
21	PARBATI HEP (NHPC) II NHPC	3,919.59	5,366.00	09/2009	12/2017	03/2018	3
22	NIMOO BAZGO HYDROELECTRIC PROJECT NHPC	611.01	936.00	08/2010	03/2013	06/2013	3
23	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	09/2013	12/2013	3
24	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND PGCIL	2,360.95	2,360.95	08/2012	09/2013	12/2013	3
25	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G PGCIL	1,736.36	1,736.36	06/2012	12/2012	03/2013	3
26	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR PGCIL	1,075.12	1,075.12	05/2012	03/2013	06/2013	3
27	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	12/2012	03/2013	3
28	System Strengthening -X of SR PGCIL	276.61	276.61	04/2012	12/2012	03/2013	3
29	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME PGCIL	7,031.88	7,031.88	12/2012	02/2013	06/2013	4
30	RAMPUR HEP(412 MW) SJVNL	2,047.03	2,047.03	01/2012	09/2013	02/2014	5
31	RIHAND STTP STAGE-III (2X500MW) (NTPC) NTPC	6,230.81	6,230.81	10/2012	05/2013	11/2013	6
32	765 KV POOLING STATION AND NETWORK WITH DVC AND MA PGCIL	7,075.33	7,075.33	08/2012	03/2013	12/2013	9
33	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I PGCIL	4,672.99	4,672.99	11/2012	06/2013	03/2014	9
34	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	03/2013	12/2013	9
35	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	07/2011	11/2014	10/2015	11
<u>Railways</u>							
36	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR NEFR	156.00	406.40	N.A.	12/2012	06/2013	6
37	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER NEFR	915.70	1,717.29	N.A.	03/2013	03/2014	12
38	Katakhal to Bhairabi NEFR	227.90	223.01	12/2012	03/2014	03/2015	12
39	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg NEFR	1,676.31	4,255.37	03/2009	12/2013	12/2014	12
40	AGARTALA SABROOM, NL, NEFR NEFR	813.34	1,141.75	03/2014	03/2014	12/2015	21
41	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P NEFR	200.00	385.20	N.A.	03/2014	03/2016	24
42	BHAIRABI SAIRONG, NL, NEFR NEFR	619.34	2,393.48	04/2014	03/2015	03/2017	24
43	New Line from Dimapur to Zubza(Kohima) national pr NEFR	850.00	850.00	03/2015	03/2015	03/2017	24
44	SEVOK RANGPO, NEFR NEFR	1,339.48	3,380.58	12/2015	12/2015	03/2020	51

Road Transport & Highways


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
45	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	12/2012	01/2013	1
46	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	12/2012	01/2013	1
47	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	12/2012	01/2013	1
48	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) NHAI	367.49	367.49	03/2005	12/2012	01/2013	1
49	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 NHAI	166.27	193.10	03/2008	12/2012	01/2013	1
50	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	12/2012	01/2013	1
51	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) NHAI	229.91	229.91	10/2008	12/2012	01/2013	1
52	NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2011	12/2012	01/2013	1
53	THANJAUR-TRICHY, NH-67 (NHAI) NHAI	280.00	280.00	06/2009	12/2012	01/2013	1
54	GANJAM-ICCHAPURUM, NH-5 (NHAI) NHAI	263.27	263.27	02/2004	12/2012	01/2013	1
55	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	12/2012	01/2013	1
56	Surat- Dahisar (Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	12/2012	01/2013	1
57	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	12/2012	01/2013	1
58	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) NHAI	203.43	203.43	10/2008	12/2012	02/2013	2
59	GWALIOR BYPASS, NH-75, 3 NHAI	300.93	300.93	10/2009	12/2012	02/2013	2
60	Kishangarh-Ajmer-Beawer NHAI	795.00	795.00	05/2012	12/2012	02/2013	2
61	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	12/2012	03/2013	3
62	SILIGURI TO ISLAMPUR (WB-7) NHAI	225.00	225.00	07/2008	12/2012	03/2013	3
63	DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	12/2012	03/2013	3
64	MP/Maharashtra Border-Dhula NHAI	835.00	835.00	06/2012	12/2012	03/2013	3
65	Hyderabad-Vijaywada Km. 40 to 221.50 Km NHAI	1,740.00	1,740.00	10/2012	12/2012	03/2013	3
66	Jaipur-Tonk-Deoli NHAI	792.06	792.06	12/2012	12/2012	03/2013	3
67	FORBESGANJ TO SIMRAHI (NH-57) (NHAI) NHAI	332.94	332.94	09/2008	12/2012	05/2013	5
68	NAGPUR-KONDHALI, NH-6 (NHAI) NHAI	168.00	168.00	12/2008	12/2012	06/2013	6
69	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NHAI	232.45	232.45	09/2010	12/2012	06/2013	6
70	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) NHAI	940.00	940.00	07/2012	12/2012	06/2013	6
71	Gurgaon-Kotputli Km 42.70 to 54.4 Km NHAI	1,673.70	1,673.70	10/2011	12/2012	06/2013	6
72	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2) (NHAI) NHAI	237.80	237.80	06/2008	12/2012	12/2013	12
73	NALBARI TO BIJNI (AS-8) NHAI	200.00	200.00	06/2008	12/2012	12/2013	12


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
74	ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	12/2012	3/2013	3
75	NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	12/2012	3/2013	3
76	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION NHAI	617.00	617.00	08/2012	03/2014	03/2015	12
77	GUWHATI TO NALBARI (AS-4) NHAI	175.96	175.96	04/2008	12/2012	03/2014	15
78	GUWAHATI TO NALBARI (AS-5) NHAI	198.16	198.16	04/2008	12/2012	03/2014	15
79	BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	217.61	04/2010	12/2012	03/2014	15
<u>Shipping & Ports</u>							
80	Acquisition of two nos. of 120 B.P BY 079& 080 SHIPP.	290.85	272.50	06/2011	09/2012	10/2012	1
81	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	01/2013	02/2013	1
82	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers SHIPP.	612.72	532.83	12/2012	05/2013	10/2013	5

Trend and Graphical Analysis of All Projects (w.r.t. Original Schedule)

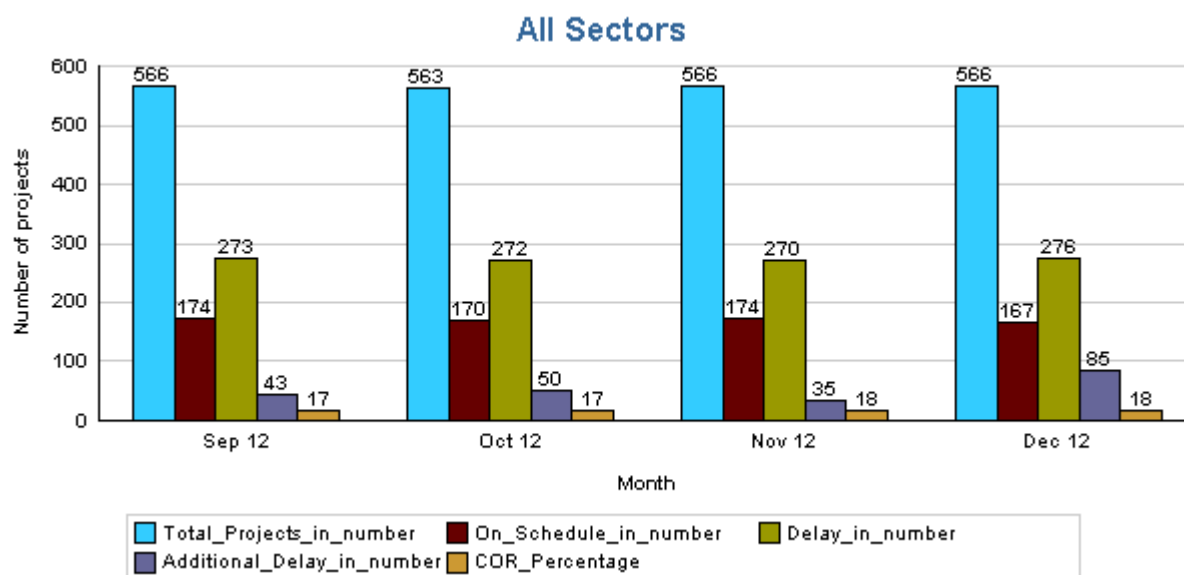


All Sectors Break-up of 276 Delayed projects in December 2012

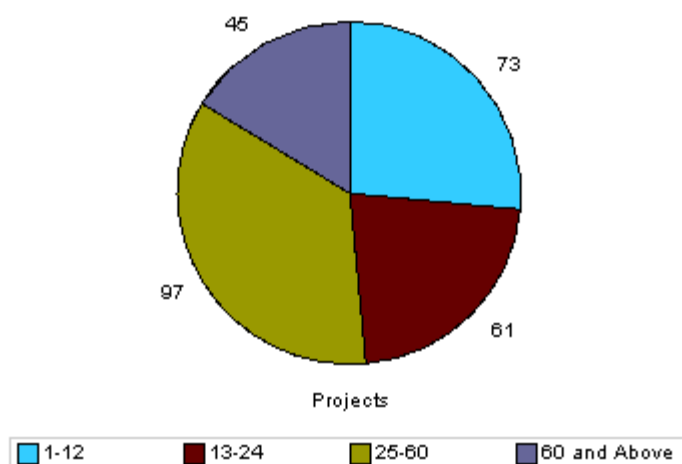


Trend and Graphical Analysis

Urban Development Sector

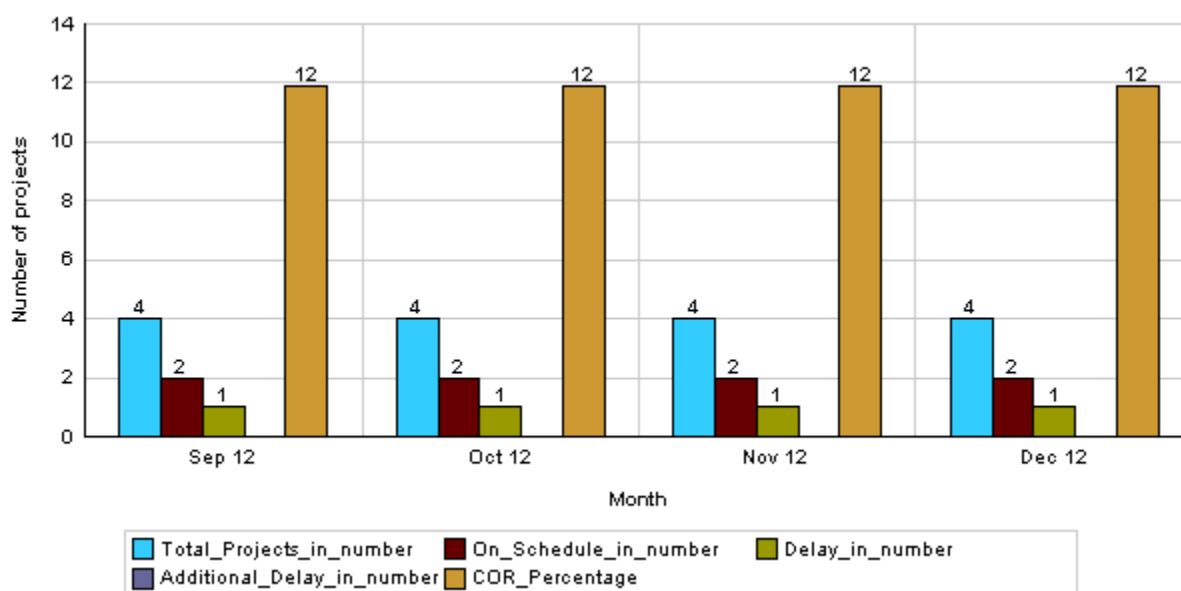


Urban Development Sector Break-up of 1 Delayed projects in December 2012

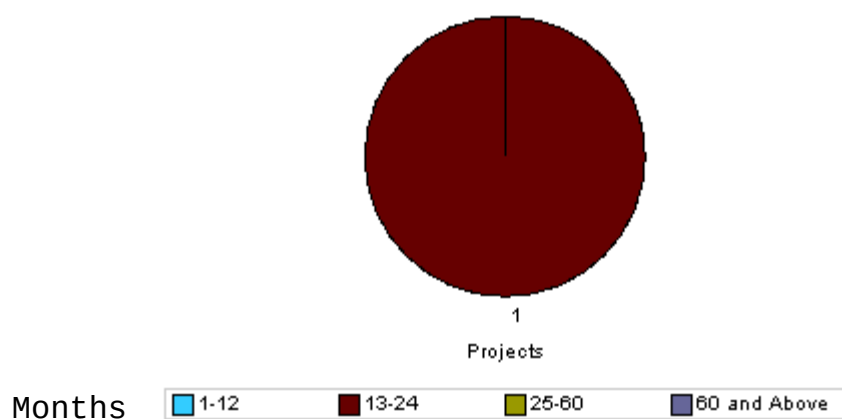


Trend and Graphical Analysis


Telecommunications Sector

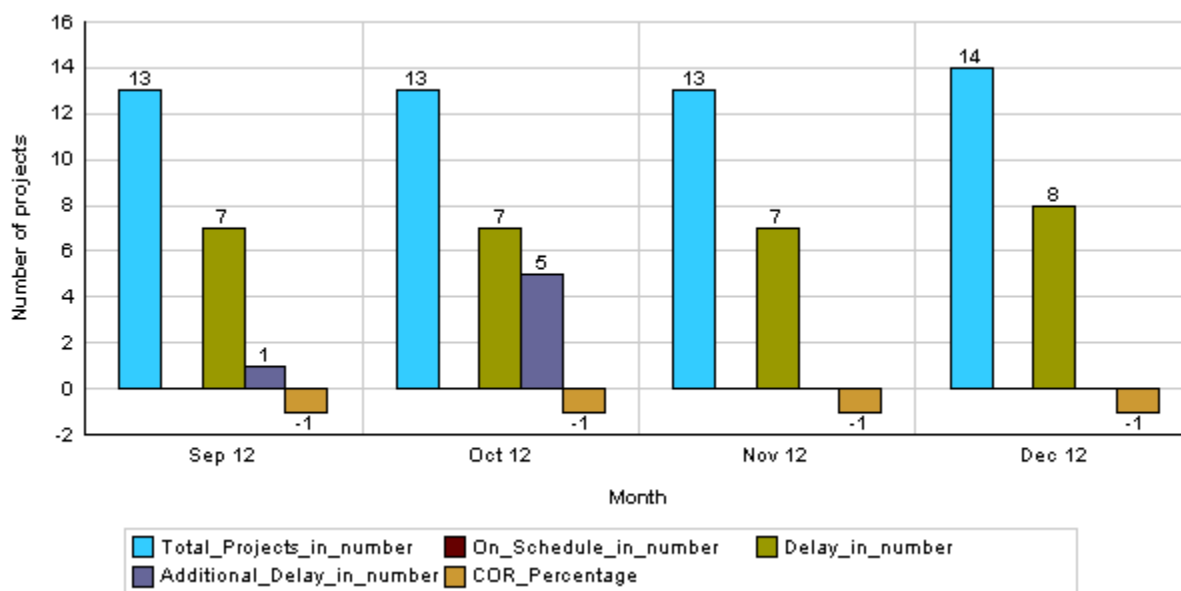


Telecommunications Sector Break-up of 8 Delayed projects in December 2012

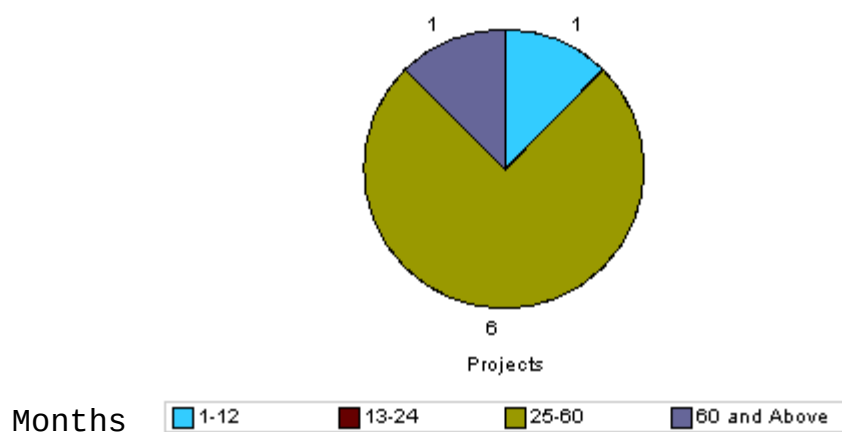

Trend and Graphical Analysis Shipping and Ports Sector

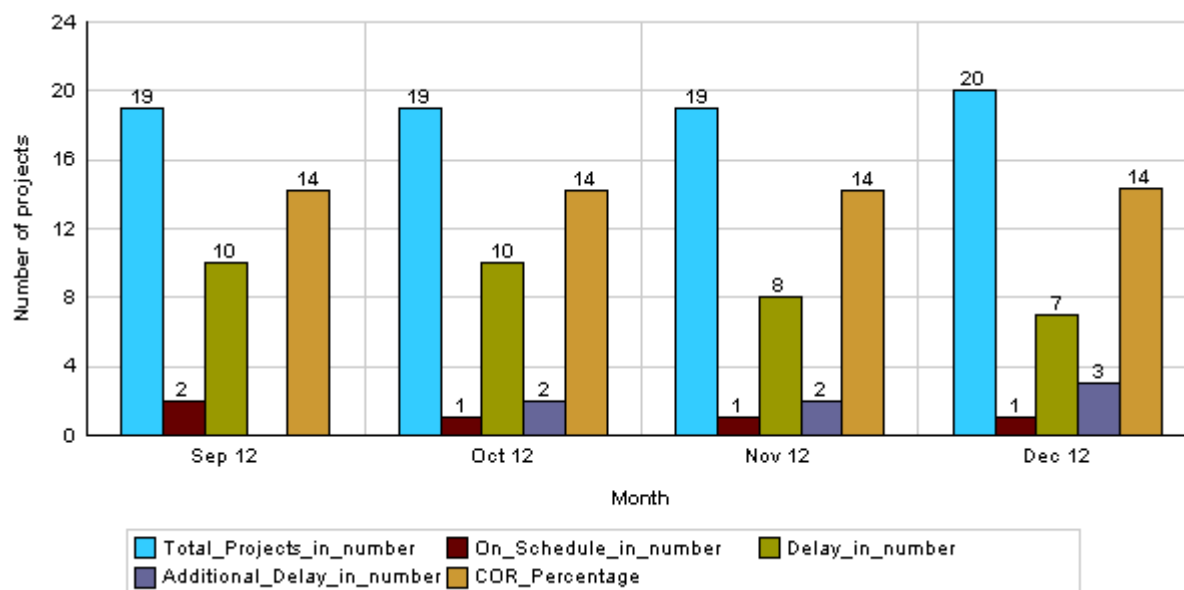


Sector Break-up of 7 Delayed projects in December 2012

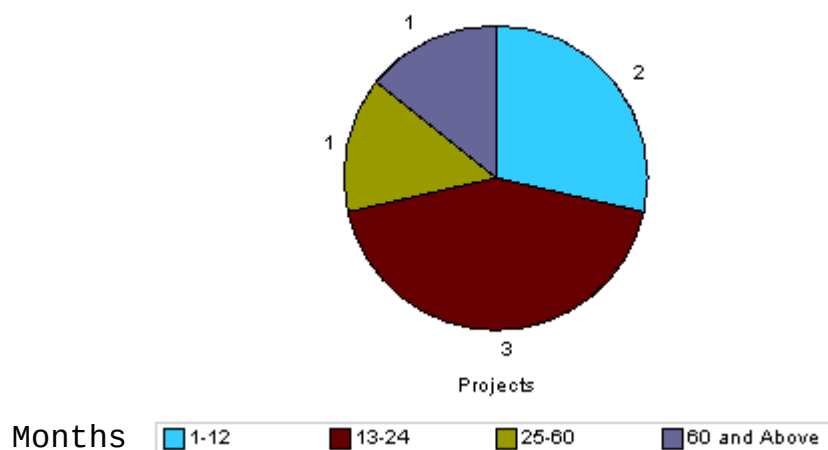


Trend and Graphical Analysis

Road Transport and Highways Sector

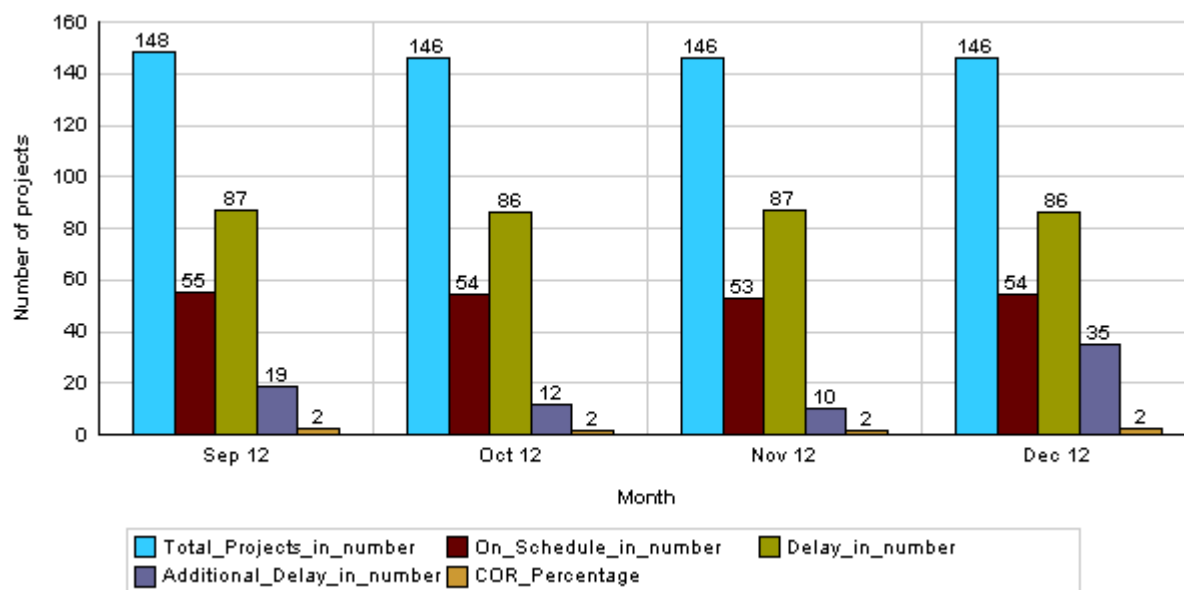


Sector Break-up of 86 Delayed projects in December 2012

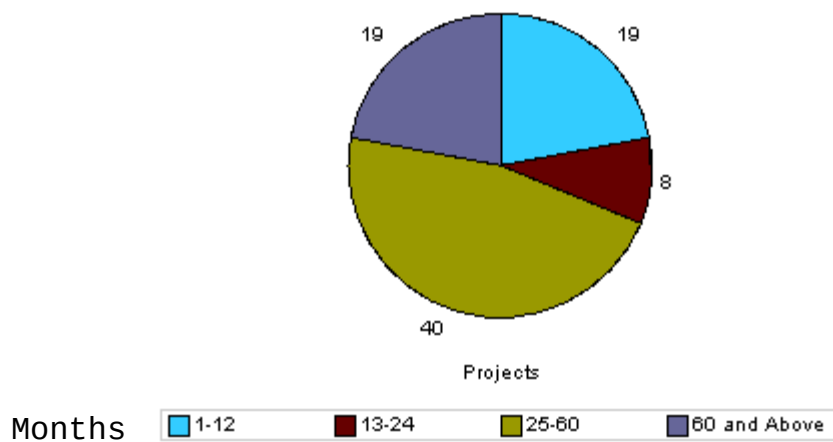


Trend and Graphical Analysis

Railways Sector

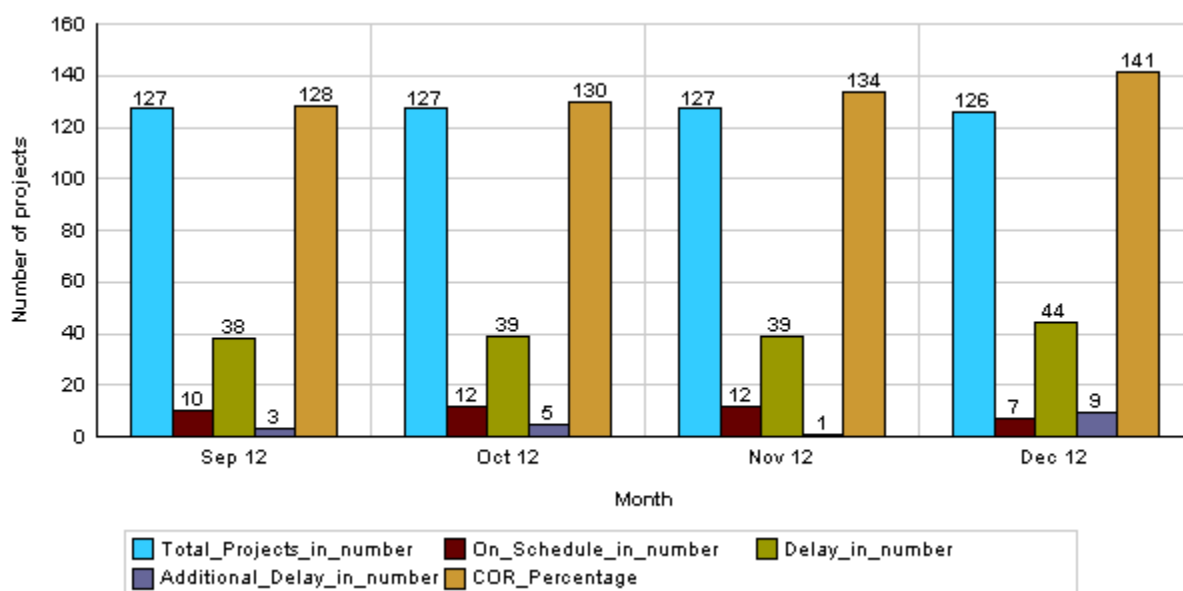


Railways Sector Sector Break-up of 44 Delayed projects in December 2012

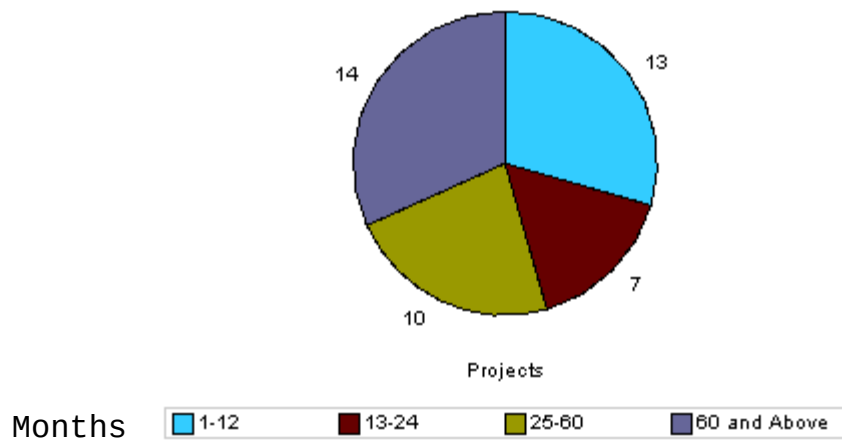


Trend and Graphical Analysis

Power Sector

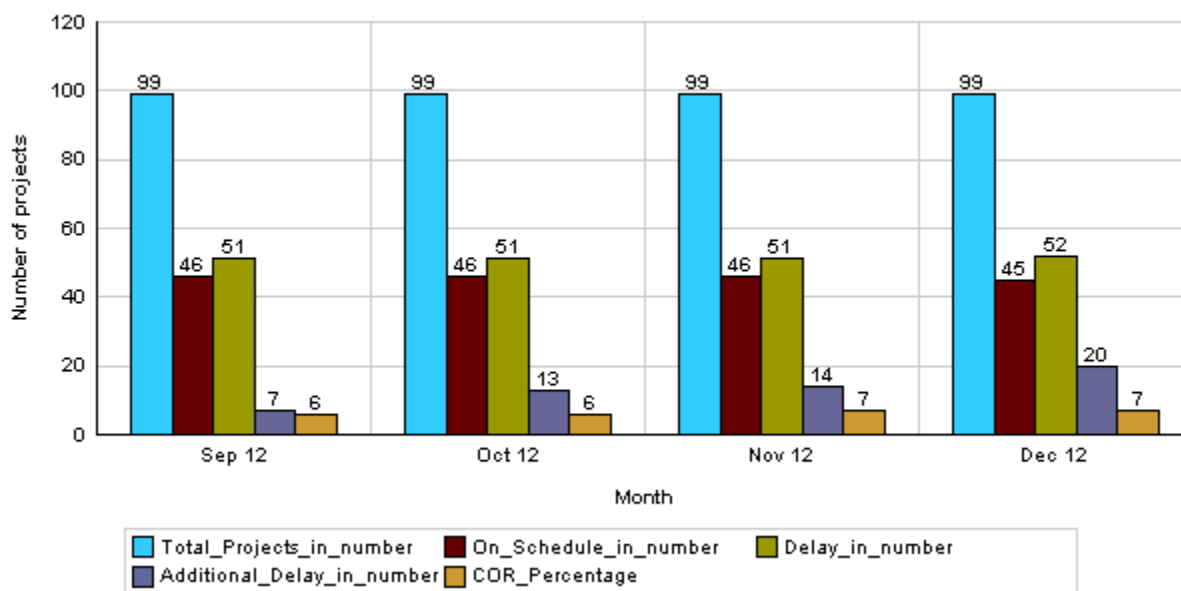


Power Sector Break-up of 52 Delayed projects in December 2012

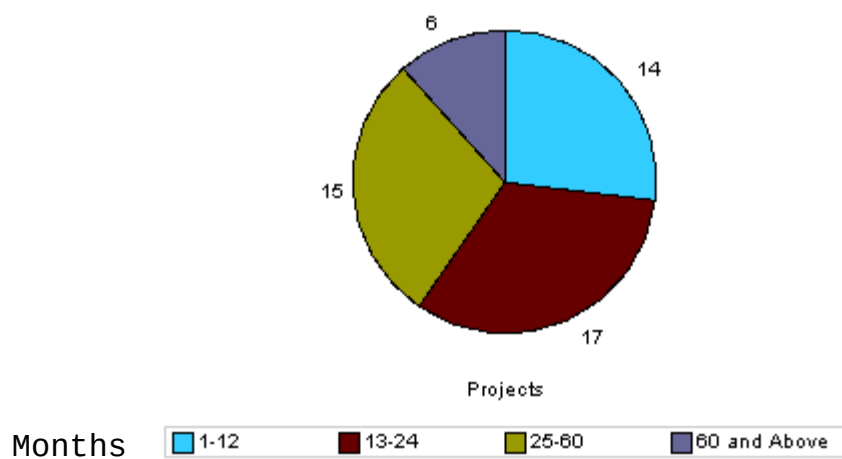


Trend and Graphical Analysis

Petroleum Sector

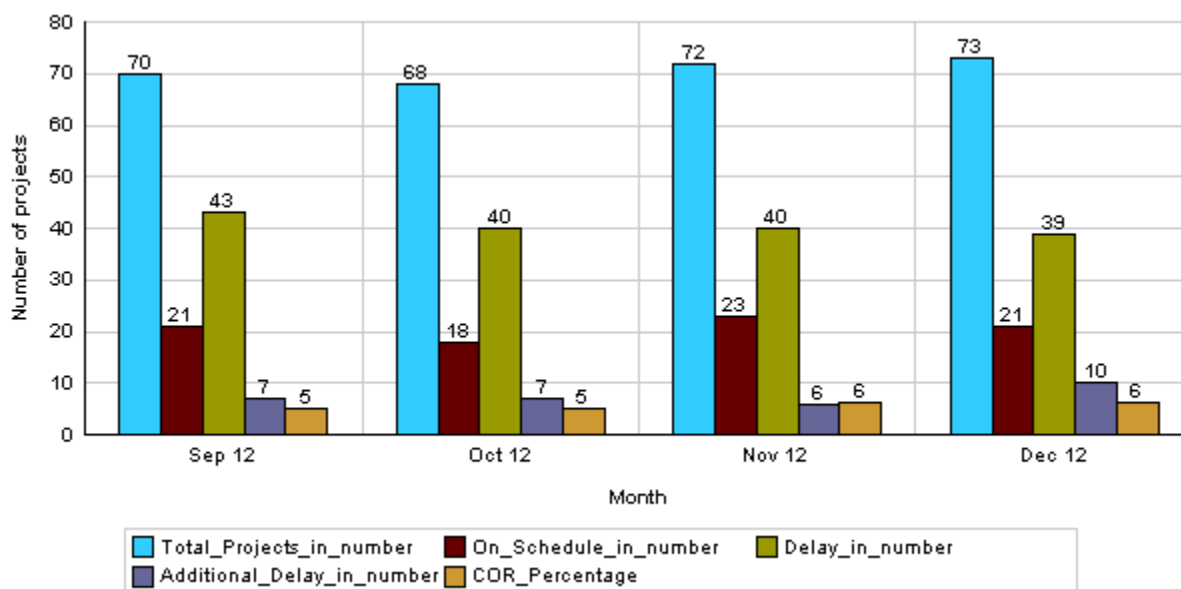


Petroleum Sector Sector Break-up of 39 Delayed projects in December 2012

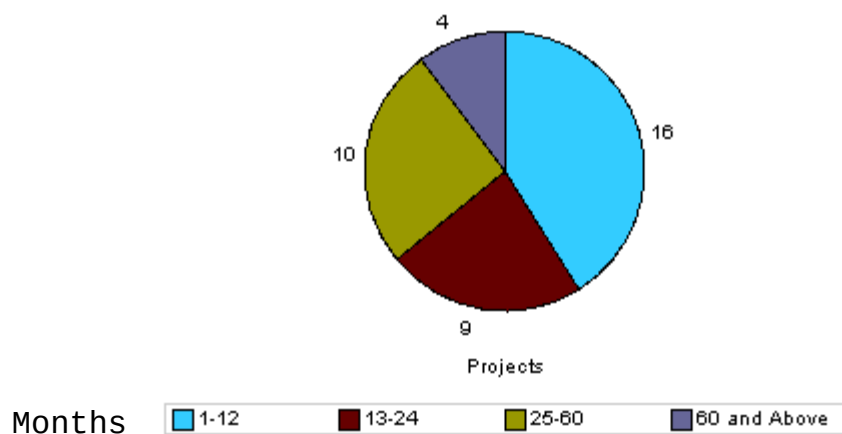


Trend and Graphical Analysis

Steel Sector

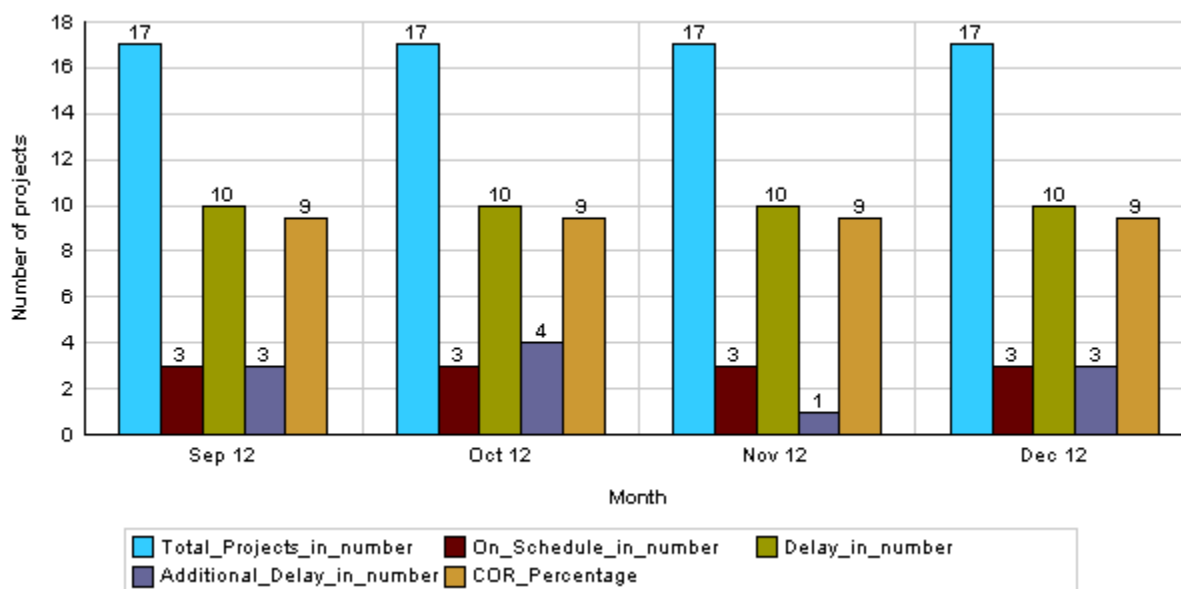


Steel Sector Sector Break-up of 10 Delayed projects in December 2012

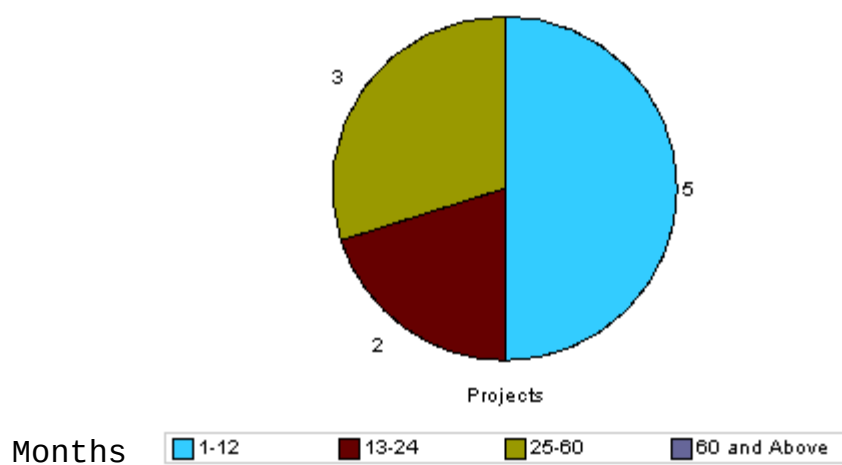


Trend and Graphical Analysis

Fertilisers Sector

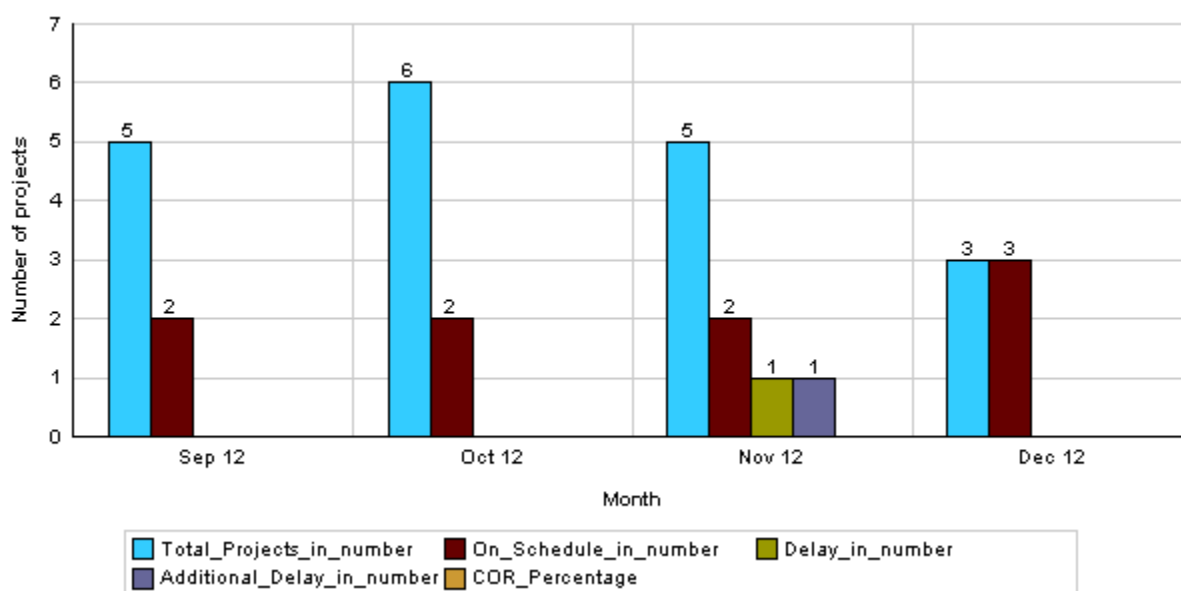


Fertilisers Sector Break-up of 0 Delayed projects in December 2012




Trend and Graphical Analysis

Coal Sector

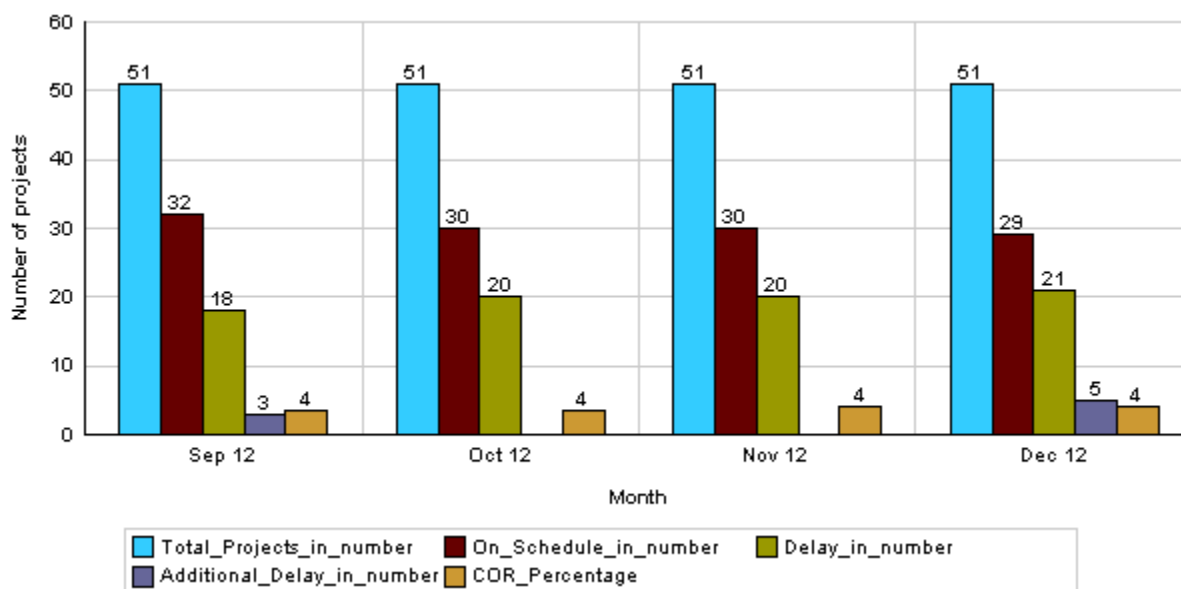


Coal Sector Sector Break-up of 21 Delayed projects in December 2012

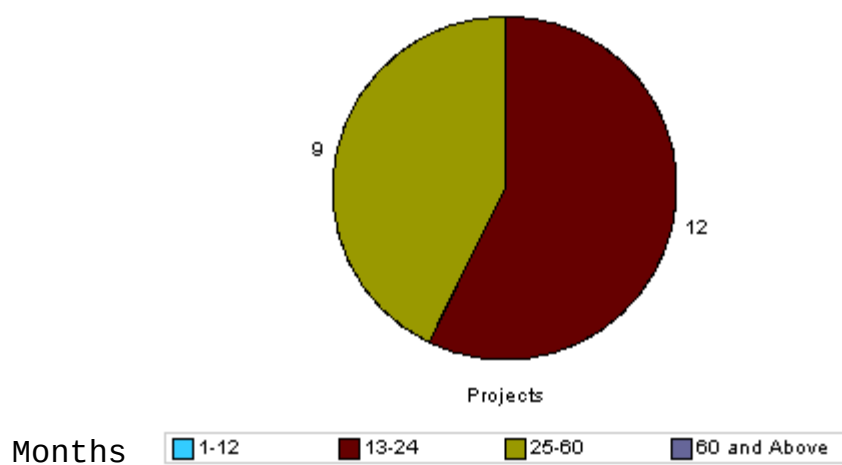


Trend and Graphical Analysis

Civil Aviation Sector

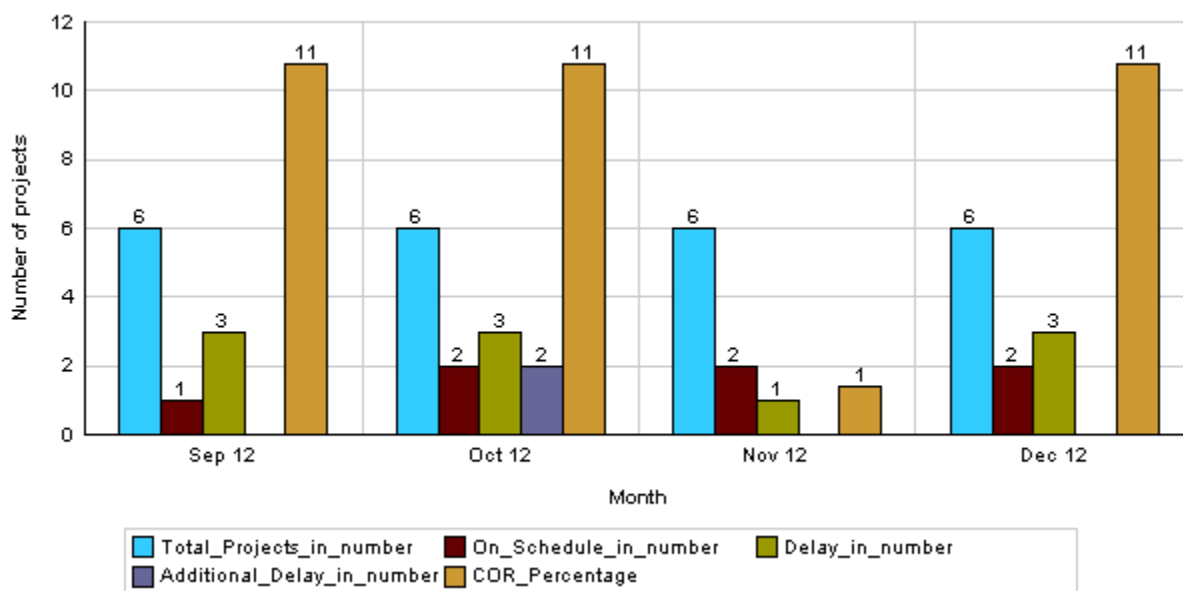


Civil Aviation Sector Break-up of 3 Delayed projects in December 2012

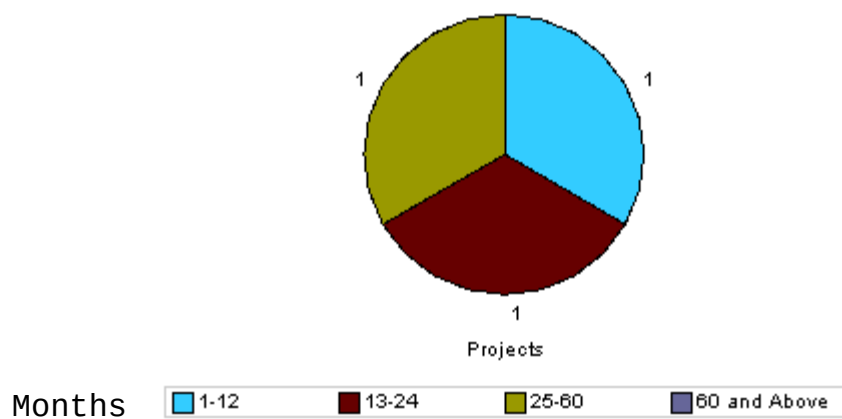


Trend and Graphical Analysis

Atomic Energy Sector

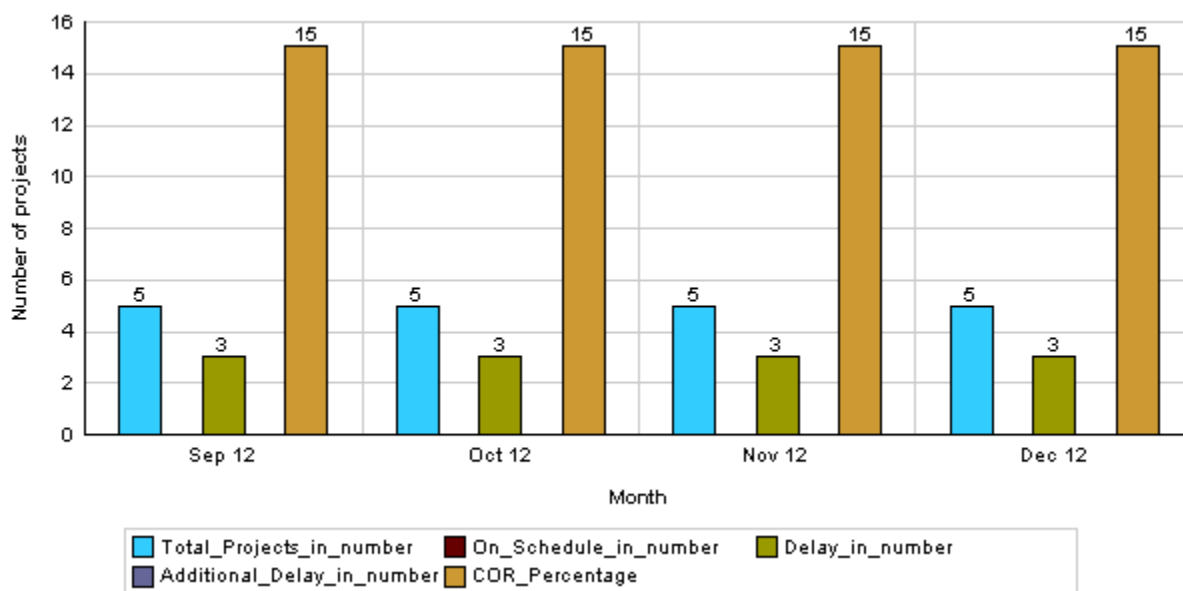

Atomic Energy Sector Sector Break-up of 3 Delayed projects in December 2012

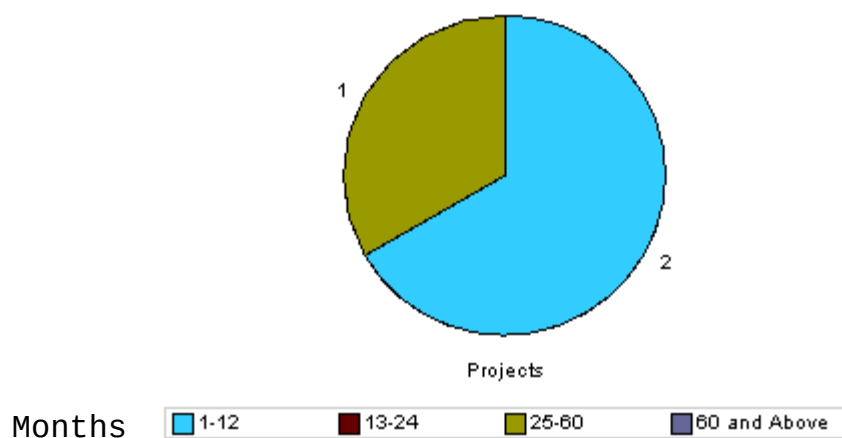

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	24,058.57
Civil Aviation	6	5,473.58	5,680.58	6,063.07	4,735.60
Coal	51	36,056.46	37,022.46	37,510.52	13,463.30
Fertilisers	3	4,065.66	4,065.66	4,065.66	946.00
Steel	17	65,285.87	67,562.15	71,443.41	45,840.84
Petrochemicals	1	5,460.61	8,920.00	8,920.00	5,981.96
Petroleum	73	177,447.66	194,077.53	188,692.30	86,213.52
Power	99	227,823.09	231,630.19	243,653.33	109,048.30
Railways	126	61,393.48	91,157.40	148,131.67	61,217.00
Road Transport & Highways	146	94,417.90	94,584.40	96,356.52	68,989.47
Shipping & Ports	20	15,907.97	17,661.93	18,174.92	8,042.54
Telecommunications	14	5,964.89	5,988.36	5,905.68	1,728.20
Urban Development	4	44,245.18	44,304.08	49,518.08	3,708.81
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	566	785,633.54	844,745.93	927,454.45	434,009.60

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Atomic Energy									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,241.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	15,276.00	12/2008 -	03/2013	51(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,960.33	09/2010 -	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,497.00	12/2016 -	03/2017	3(O) -	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,084.24	04/2011 -	-	-	0/0
Total			41,548.29 -	47,832.29	24,058.57				47/327
Civil Aviation									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,199.24	05/2011 -	03/2013	22(O) -	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	198.22	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	169.33	05/2012 -	03/2013	10(O) -	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,742.12	01/2011 02/2012	02/2012	-	0/0
10	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	452.00	49.73	03/2015 -	03/2015	0(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	376.96	06/2013 -	06/2013	0(O) -	0/0
Total			5,473.58 -	6,063.07	4,735.60				0/0
Coal									
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	424.32	03/2013 09/2012	07/2014	16(O) 22(R)	7/22
13	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	94.86	03/2016 -	03/2016	0(O) -	2/5

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	391.28	03/2016 03/2016	03/2016	0(O) 0(R)	2/2
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	100.37	03/2012 -	03/2014	24(O) -	5/9
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	12/2007	471.66 341.63	341.63	143.73	03/2011 -	03/2013	24(O) -	0/2
17	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	119.24	03/2010 -	03/2015	60(O) -	4/5
18	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	39.81	03/2016 -	03/2016	0(O) -	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	117.63	03/2017 -	03/2017	0(O) -	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.95	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	535.10	165.15	03/2015 03/2015	03/2015	0(O) 0(R)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	264.84	03/2014 -	03/2016	24(O) -	2/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	08/2007	163.51 -	163.51	34.68	03/2011 -	03/2014	36(O) -	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,243.76	03/2014 -	03/2014	0(O) -	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,396.85	03/2014 -	03/2014	0(O) -	10/15
27	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	71.37	03/2015 -	03/2015	0(O) -	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.63 -	479.63	114.38	03/2013 -	03/2013	0(O) -	5/10
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48(O) -	0/1
33	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	80.86	12/2012 -	03/2015	27(O) -	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	112.76	03/2013 -	03/2013	0(O) -	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	30.89	03/2014 -	03/2014	0(O) -	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/6

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KHADIA EXPANSION OPENCASE PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	3.87	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	334.67	03/2013 -	03/2013	0(O) -	2/2
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	108.50	03/2010 -	03/2014	48(O) -	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	675.55	03/2013 -	03/2013	0(O) -	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44(O) -	1/2
43	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	204.96	03/2014 -	03/2014	0(O) -	1/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.34	03/2012 -	03/2014	24(O) -	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	25.06	12/2015 -	08/2017	20(O) -	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	2.07	03/2012 -	03/2015	36(O) -	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	60.74	03/2012 -	03/2014	24(O) -	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.88	03/2014 -	03/2016	24(O) -	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	91.35	03/2013 -	03/2013	0(O) -	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	09/2009	153.82 -	153.82	24.39	03/2014 -	03/2014	0(O) -	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	122.89	03/2012 -	03/2015	36(O) -	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	29.45	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016	0(O) -	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	49.63	03/2012 -	-	-	11/42

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	44.23	03/2016	03/2016	0(O)	0/10
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,536.19	06/2009	09/2013	51(O)	19/24
61	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,709.61	03/2012	03/2014	24(O)	0/39
62	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	108.35	03/2012	03/2014	24(O)	0/2
	Total		36,056.46	37,510.52	13,463.30				165/637
	Fertilisers								
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	-	01/2013	01/2013	0(O)	5/5
64	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	-	01/2013	01/2013	0(O)	0/8
65	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	946.00	01/2013	01/2013	0(O)	0/5
	Total		4,065.66	4,065.66	946.00				5/18
	Steel								
66	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	226.72	-	04/2013	-	13/19
67	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	250.59	08/2010	01/2013	29(O)	0/1
68	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	254.09	02/2011	03/2013	25(O)	2/3
69	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	148.58	-	11/2013	-	11/21
70	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	226.41	05/2012	06/2013	13(O)	1/2
71	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	343.48	12/2011 03/2012	03/2013	15(O) 12(R)	16/21
72	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	118.28	10/2012	03/2013	5(O)	3/4
73	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	332.65	11.43	08/2014	08/2014	0(O)	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
74	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL, Orissa	11/2011	254.55 -	254.55	12.02	11/2013 -	11/2013	0(O) -	1/1
75	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00 -	17,265.00	7,353.31	03/2013 -	09/2013	6(O) -	22/27
76	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00 -	6,325.00	3,189.32	12/2011 -	12/2012	12(O) -	11/16
77	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	1,282.41	12/2012 -	03/2013	3(O) -	10/12
78	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	14,002.26	12/2011 -	12/2012	12(O) -	19/19
79	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	9,958.76	10/2009 -	03/2013	41(O) -	62/64
80	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Orissa	09/2008	11,812.00 11,812.00	11,812.00	8,450.87	11/2013 -	03/2013	-8(O) -	8/14
81	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL, Maharashtra	12/2011	187.33 -	187.33	12.05	- -	12/2013	- -	0/1
82	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL, Orissa	01/2012	254.90 -	254.90	0.26	12/2014 -	12/2014	0(O) -	0/0
Total			65,285.87 -	71,443.41	45,840.84				179/225
<u>Petrochemicals</u>									
83	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	5,981.96	04/2012 12/2013	12/2013	20(O) 0(R)	18/29
Total			5,460.61 -	8,920.00	5,981.96				18/29
<u>Petroleum</u>									
84	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	03/2014	21(O) -	0/0
85	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	1,147.97	06/2012 -	06/2013	12(O) -	0/0
86	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	271.67	04/2011 -	01/2013	21(O) -	0/0
87	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	629.62	12/2011 -	01/2013	13(O) -	0/0
88	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	1,175.96	03/2013 -	03/2014	12(O) -	0/0
89	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00 -	586.00	4.26	07/2015 -	07/2015	0(O) -	0/0
90	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	711.28	12/2014 -	12/2014	0(O) -	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
91	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	4.84	12/2014	12/2014	0(O)	0/0
92	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	460.70	204.60	07/2012	-	-	0/17
93	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	145.56	02/2013	03/2013	1(O)	38/42
94	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00	190.00	21.38	03/2014	03/2014	0(O)	0/0
95	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	225.78	-	10/2012	-	36/36
96	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	798.00	710.76	04/2011	-	-	2/2
97	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	344.48	09/2011	12/2013	27(O)	0/0
98	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29	6,326.40	5,583.21	05/2010	01/2013	32(O)	0/0
99	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	394.00	377.13	-	-	-	21/22
100	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	756.65	80.91	05/2013	11/2013	6(O)	0/0
101	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	27.13	08/2013	01/2014	5(O)	0/0
102	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	240.95	47.51	09/2012	09/2013	12(O)	0/0
103	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
104	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	267.00	220.44	09/2012	09/2012	-	0/0
105	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43	2,300.00	1,684.05	03/2012	-	-	0/21
106	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00	486.00	34.88	09/2013	09/2013	0(O)	0/0
107	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	159.73	-	-	-	0/0
108	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	2,735.65	2,184.00	04/2006	06/2013	86(O)	0/0
109	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	5,633.44	3,919.55	08/2010	12/2013	40(O)	0/0

Sector Wise Details

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
112	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
113	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	2,174.00	1,249.87	09/2011 -	02/2013	17(O) -	0/76
114	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,480.21	09/2011 03/2012	03/2013	18(O) 12(R)	0/0
115	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	115.70	03/2013 -	04/2013	1(O) -	0/0
116	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
117	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	676.54	03/2013 -	04/2014	13(O) -	0/0
118	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	72.36	11/2012 -	10/2013	11(O) -	0/0
119	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	406.26	01/2014 -	01/2014	0(O) -	0/0
120	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
121	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,975.77	- -	01/2013	- -	115/116
122	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	351.23	01/2013 -	06/2013	5(O) -	18/18
123	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,124.47	04/2013 -	04/2013	0(O) -	0/167
124	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	26.42	05/2015 -	05/2015	0(O) -	0/0
125	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,170.37	06/2012 -	03/2013	9(O) -	8/8
126	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.00	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
127	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	634.47	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
128	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	03/2014	0(O) -	0/0
129	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	277.79	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
130	IROP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	9.21	12/2015 -	12/2015	0(O) -	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	2,059.63	-	03/2015	03/2015	0(O)	0/0
132	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.54	01/2013	07/2015	30(O)	0/0
133	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	4.49	10/2010	12/2014	50(O)	0/0
134	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 312.00	312.00	276.60	01/2012 01/2012	01/2013	12(O) 12(R)	0/1
135	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	1,126.97	12/2012 12/2012	03/2014	15(O) 15(R)	0/21
136	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00	666.00	-	11/2015	11/2015	0(O)	0/0
137	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	12,160.26	8,570.48	01/2012	03/2013	14(O)	0/108
138	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	4,524.89	09/2012	09/2013	12(O)	0/0
139	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,154.13	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
140	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	701.81	04/2015	04/2015	0(O)	0/0
141	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24(O) 22(R)	0/0
142	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	566.23	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
143	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00	913.00	21.50	07/2015	07/2015	0(O)	0/0
144	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	19,629.00	11/2012	09/2013	10(O)	60/100
145	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	726.16	09/2012	09/2012	-	0/11
146	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	2,760.15	02/2014	02/2014	0(O)	0/0
147	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	246.81	184.00	04/2012	-	-	0/0
148	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	1,417.00	74.11	05/2014	05/2014	0(O)	0/0
149	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	553.91	07/2012	-	-	0/31

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
150	RESITEMENT OF MARKETING INSTALLATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	909.00	- -	-	-	51/53
151	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	03/2012	1,210.64 -	1,210.64	-	03/2015 -	03/2015	0(O) -	0/0
152	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014	0(O) -	0/0
153	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	1,043.57	997.72	04/2012 -	01/2013	9(O) -	0/0
154	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	165.66	08/2012 -	05/2013	9(O) -	0/0
155	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	199.91	03/2012 -	-	-	13/20
156	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	89.68	12/2013 -	12/2013	0(O) -	0/0
Total			177,447.66 -	188,692.30	86,213.52				377/885
Power									
157	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,515.00	08/2012 -	12/2013	16(O) -	0/11
158	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,149.50	02/2012 -	03/2013	13(O) -	0/7
159	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	696.50	05/2012 -	06/2013	13(O) -	0/11
160	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,093.40	06/2012 -	03/2013	9(O) -	0/4
161	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	0/0
162	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,861.00	08/2013 -	09/2014	13(O) -	7/19
163	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,722.00	12/2009 -	03/2016	75(O) -	26/47
164	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,494.00	07/2011 -	10/2015	51(O) -	4/28
165	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.00	775.29	02/2011 10/2012	01/2013	23(O) 3(R)	2/4
166	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	367.00	08/2014 -	08/2014	0(O) -	0/20

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	33.70	06/2014 -	06/2014	0(O) -	0/20
168	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	475.30	09/2014 -	09/2014	0(O) -	8/19
169	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	868.00	10/2009 -	03/2013	41(O) -	20/20
170	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	479.40	11/2012 -	03/2014	16(O) -	3/11
171	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
172	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	528.60	05/2014 -	05/2014	0(O) -	0/16
173	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	764.20	08/2013 -	08/2013	0(O) -	0/14
174	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	82.30	08/2014 -	08/2014	0(O) -	0/21
175	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	631.70	12/2013 -	12/2013	0(O) -	0/13
176	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	57.90	10/2012 -	03/2013	5(O) -	0/15
177	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	864.13	12/2007 12/2009	-	-	0/10
178	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	2,063.68	05/2013 06/2016	03/2017	46(O) 9(R)	5/22
179	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,935.69	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
180	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	6,358.91	4,669.00	04/2009 -	09/2014	65(O) -	0/9
181	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,116.00	12/2016 -	12/2016	0(O) -	0/5
182	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,843.11	09/2008 -	03/2013	54(O) -	17/37
183	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,626.00	08/2012 -	03/2013	7(O) -	11/16
184	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	634.00	09/2016 -	09/2016	0(O) -	0/12

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
185	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	814.50	08/2010 01/2013	06/2013	34(O) 5(R)	0/3
186	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,326.50	08/2013 -	09/2014	13(O) -	0/17
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	248.30	02/2012 -	12/2013	22(O) -	0/14
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	335.30	11/2011 -	12/2013	25(O) -	0/11
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	348.20	11/2011 -	12/2013	25(O) -	0/14
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	81.30	01/2013 -	03/2013	2(O) -	0/7
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	225.00	07/2013 -	07/2013	0(O) -	0/12
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	642.50	04/2013 -	10/2013	6(O) -	0/12
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	106.90	08/2013 -	08/2013	0(O) -	0/16
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	60.20	11/2014 -	11/2014	0(O) -	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	-	03/2015 -	03/2015	0(O) -	0/0
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	14.90	04/2015 -	05/2015	1(O) -	0/0
197	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	478.50	11/2012 -	12/2013	13(O) -	0/10
198	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,996.58	10/2010 01/2013	09/2013	35(O) 8(R)	0/6
199	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,694.37	09/2009 07/2014	03/2018	102(O) 44(R)	1/20
200	PARE HYDRO ELECTRIC PROJECT (110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	450.04	08/2012 08/2013	09/2014	25(O) 13(R)	15/21
201	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pr.	01/2007	2,047.03 -	2,047.03	2,113.01	01/2012 -	02/2014	25(O) -	0/2
202	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,814.00	10/2012 -	11/2013	13(O) -	11/16
203	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	1,137.00	11/2016 -	11/2016	0(O) -	0/11

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
204	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	10,667.00	5,872.26	09/2010 08/2014	03/2017	78(O) 31(R)	11/11
205	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	58.10	04/2013	04/2013	0(O)	0/15
206	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,994.10	08/2012	12/2013	16(O)	0/7
207	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	1,508.74	-	06/2016	06/2016	0(O)	0/0
208	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	1,935.35	-	12/2014	12/2014	0(O)	0/0
209	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/0
210	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	57.30	08/2014	08/2014	0(O)	0/20
211	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	123.80	02/2015	02/2015	0(O)	0/0
212	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	1,263.26	183.60	11/2014	11/2014	0(O)	0/0
213	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	134.40	01/2015	01/2015	0(O)	0/19
214	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	38.80	08/2014	08/2014	0(O)	0/20
215	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	71.90	06/2014	06/2014	0(O)	0/19
216	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	167.80	04/2012	03/2013	11(O)	0/0
217	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	131.78	06/2012	03/2013	9(O)	0/9
218	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	806.70	08/2012	12/2013	16(O)	0/11
219	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,640.00	03/2013	09/2015	30(O)	2/14
220	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,252.08	09/2009 06/2013	12/2013	51(O) 6(R)	0/0
221	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,638.44	03/2007 09/2012	02/2013	71(O) 5(R)	25/25

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	435.00	07/2010 02/2016	11/2016	76(O) 9(R)	1/10
223	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	41.30	01/2014 -	01/2014	0(O) -	0/17
224	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	114.00	08/2014 -	08/2014	0(O) -	0/0
225	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	135.60	10/2014 -	10/2014	0(O) -	0/21
226	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	333.83	07/2011 -	01/2013	18(O) -	0/5
227	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,124.70	10/2012 -	12/2013	14(O) -	0/12
228	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	337.60	01/2015 -	01/2015	0(O) -	0/20
229	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	937.00	03/2014 -	03/2014	0(O) -	0/15
230	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	670.20	08/2013 -	08/2013	0(O) -	0/14
231	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	2.20	08/2014 -	08/2014	0(O) -	0/20
232	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	50.70	10/2014 -	10/2014	0(O) -	0/20
233	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	595.50	01/2010 -	02/2013	37(O) -	0/22
234	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	155.70	11/2011 -	09/2013	22(O) -	0/7
235	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,158.70	12/2012 -	06/2013	6(O) -	0/11
236	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	116.50	02/2014 -	02/2014	0(O) -	0/20
237	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	158.30	10/2013 -	10/2013	0(O) -	0/18

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	65.40	07/2013 -	07/2013	0(O) -	0/0
239	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	336.10	12/2013 -	12/2013	0(O) -	0/18
240	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	84.50	11/2013 -	11/2013	0(O) -	0/20
241	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	772.70	03/2013 -	03/2013	0(O) -	0/14
242	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	1,090.50	12/2013 -	12/2013	0(O) -	0/13
243	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,891.70	11/2012 -	03/2014	16(O) -	0/15
244	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	310.30	07/2014 -	07/2014	0(O) -	0/19
245	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	413.08	- -	07/2013	- -	6/29
246	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	374.97	07/2014 -	02/2015	7(O) -	0/16
247	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,063.60	12/2012 -	12/2013	12(O) -	0/11
248	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	621.00	11/2013 -	11/2013	0(O) -	0/15
249	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	58.40	01/2013 -	11/2013	10(O) -	0/16
250	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,081.00	1,860.84	11/2009 02/2013	03/2013	40(O) 1(R)	0/4
251	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	150.00	08/2015 -	08/2015	0(O) -	0/5
252	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	4,051.00	10/2012 -	03/2013	5(O) -	11/15
253	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 -	3,422.44	331.12	07/2014 -	05/2016	22(O) -	1/3
254	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	420.80	09/2010 -	03/2013	30(O) -	0/9

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
255	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76	9,569.76	380.90	06/2015	06/2015	0(O)	0/24
	Total		227,823.09	243,653.33	109,048.30				187/1255
	<u>Railways</u>								
256	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	1,141.75	449.26	03/2014	12/2015	21(O)	0/0
			813.34			-		-	
257	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00	227.42	250.82	12/2009	03/2011	-	0/0
			214.09			03/2011			
258	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08	2,820.00	188.66	-	03/2013	-	0/0
			1,010.00			-		-	
259	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00	453.04	396.45	03/2011	03/2011	-	0/0
			170.00			03/2011			
260	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90	548.95	543.08	06/1999	03/2011	-	0/0
			284.27			03/2011			
261	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	1,214.00	96.96	-	-	-	0/0
			-			-			
262	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14	404.39	3.77	03/2013	03/2013	0(O)	0/0
			385.60			-		-	
263	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
			901.62			-			
264	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	1,412.74	461.37	03/2005	06/2016	135(O)	0/0
			1,028.05			12/2008		90(R)	
265	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15	1,106.62	211.94	12/2010	03/2011	-	0/0
			1,106.62			03/2011			
266	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81	1,512.86	206.15	03/2004	03/2014	120(O)	0/0
			495.44			12/2010		39(R)	
267	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	2,393.48	31.46	04/2014	03/2017	35(O)	0/0
			619.34			-		-	
268	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	682.45	03/2010	12/2012	33(O)	0/0
			-			-		-	
269	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	350.00	330.65	-	03/2011	-	0/0
			-			03/2009			
270	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00	5,016.00	2,590.05	04/2008	12/2015	92(O)	0/0
			1,500.00			03/2014		21(R)	
271	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52	207.52	149.41	12/2012	12/2013	12(O)	0/0
			207.52			-		-	
272	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36	196.95	194.04	03/2011	-	-	0/0
			196.95			-			
273	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24	468.62	1.00	03/2012	-	-	0/0
			-			-			

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
274	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
275	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	914.71	12/2012 01/2013	01/2013	1(O) 0(R)	0/0
276	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
277	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
278	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2013	06/2013	0(O) 0(R)	0/0
279	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	406.40	280.75	- -	06/2013	- -	0/0
280	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	118.37	12/2012 -	-	-	0/0
281	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	85.55	- -	-	-	0/0
282	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	206.46	- -	03/2013	- -	0/0
283	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	458.91	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
284	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	571.48	- -	12/2012	- -	0/0
285	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	93.41	12/2011 02/2012	02/2012	-	0/0
286	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0
287	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
288	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	177.00	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
289	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
290	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	266.03	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
291	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	105.70	02/2006 -	12/2013	94(O) -	0/0
292	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	621.56	- -	03/2012	-	0/0
293	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
294	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	357.95	- 05/2009	05/2009	-	0/0
295	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	119.21	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
296	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	182.69	- -	-	-	0/0
297	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.64	735.10	222.32	- 09/2009	-	-	0/0
298	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
299	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	560.17	- -	01/2013	- -	0/0
300	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	141.66	- -	03/2014	- -	0/0
301	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	173.17	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
302	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	71.39	- -	-	-	0/0
303	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	9.04	03/2015 -	03/2015	0(O) -	0/0
304	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	835.57	06/2007 -	06/2007	-	0/0
305	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	685.77	03/2012 08/2012	02/2013	11(O) 6(R)	0/0
306	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	697.50	439.54	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
307	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	1,079.17	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
308	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	215.07	03/2014 -	03/2014	0(O) -	0/0
309	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	261.43	03/2012 03/2012	03/2013	12(O) 12(R)	0/0
310	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,401.22	- -	03/2013	- -	0/0
311	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	503.06	- -	03/2014	- -	1/1
312	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	758.81	- -	10/2012	-	0/0
313	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	735.14	12/2010 12/2010	03/2015	51(O) 51(R)	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
314	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	100.02	- -	03/2013	- -	0/0
315	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	228.88	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
316	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,995.25	238.06	- -	03/2013	- -	0/0
317	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
318	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	768.87	441.27	- 03/2010	03/2010	-	0/0
319	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	2,957.21	1,352.41	07/2005 -	-	-	0/0
320	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	126.63	- -	-	-	0/0
321	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	279.69	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
322	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
323	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	342.57	- -	12/2012	- -	0/0
324	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	116.35	12/2012 -	03/2015	27(O) -	0/0
325	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	345.63	05/2008 03/2011	03/2011	-	0/0
326	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	-	0/0
327	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	207.83	03/2002 -	03/2013	132(O) -	0/0
328	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,291.16	03/2009 -	12/2014	69(O) -	0/0
329	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
330	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.51	- -	02/2013	- -	0/0
331	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	638.03	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
332	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
333	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	406.58	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
334	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	900.00	289.01	- -	-	-	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
335	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	923.12	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
336	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	145.26	- -	03/2012	-	0/0
337	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	634.87	02/2009 -	03/2012	-	0/0
338	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	352.10	07/2012 -	-	-	0/0
339	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	42.31	- -	-	-	0/0
340	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	117.93	- -	03/2016	- -	0/0
341	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,329.90	12/2008 -	03/2014	63(O) -	0/0
342	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	247.13	- -	03/2015	- -	0/0
343	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24(O) -	0/0
344	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,913.51	207.96	03/2016 -	03/2016	0(O) -	0/0
345	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	40.20	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
346	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	43.80	03/2016 -	03/2016	0(O) -	0/0
347	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	33.08	03/2016 -	06/2016	3(O) -	0/0
348	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	429.24	03/2008 06/2008	-	-	0/0
349	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	355.00	378.12	03/2009 11/2012	03/2011	-	0/0
350	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	246.13	02/2010 11/2012	12/2015	70(O) 37(R)	0/0
351	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,604.67	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
352	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	589.19	- -	03/2012	-	0/0
353	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	132.81	12/2010 12/2010	12/2010	-	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
354	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	778.38	- -	03/2013	- -	0/6
355	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	243.30	12/2007 03/2010	12/2010	-	0/0
356	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	884.81	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
357	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	258.82	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
358	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13 727.13	1,225.00	225.75	- -	-	-	0/0
359	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	309.91	06/2004 -	12/2012	102(O) -	0/0
360	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,583.58	- -	03/2014	- -	0/0
361	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	344.50	04/2003 03/2010	-	-	0/0
362	REWARI-ROHTAK (NL),NR - [220100279]NR,Haryana	01/2004	149.38 330.23	602.78	503.47	02/2010 02/2011	02/2011	-	0/0
363	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	175.03	03/1998 08/2005	08/2005	-	0/0
364	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	416.20	03/2013 -	03/2014	12(O) -	0/0
365	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya Pradesh	04/2008	603.04 603.04	603.04	118.66	03/2012 -	03/2013	12(O) -	0/0
366	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	229.47	03/2010 -	03/2012	-	0/0
367	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	57.12	12/2015 -	03/2020	51(O) -	0/0
368	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	818.29	76.45	02/2015 -	-	-	0/0
369	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	312.64	03/2014 -	03/2014	0(O) -	0/0
370	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	138.67	- -	03/2013	- -	0/0
371	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	431.61	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
372	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	571.70	- 12/2009	02/2012	-	0/0
373	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	139.83	- -	-	-	0/0
374	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	40.35	- -	-	-	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
375	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	548.96	525.48	- -	-	-	0/0
376	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,240.22	12/2006 08/2010	08/2010	-	0/0
377	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	167.73	63.02	03/2012 -	02/2013	11(O) -	0/0
378	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,J and K	03/1995	2,500.00 2,500.00	20,000.00	8,549.43	03/2001 -	12/2017	201(O) -	0/0
379	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	819.40	170.80	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
380	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	415.66	03/2014 -	03/2013	-12(O) -	0/0
381	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	174.30	- 03/2010	-	-	0/0
Total			61,393.48 -	148,131.67	61,217.00				1/7
Road Transport & Highways									
382	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	391.73	05/2013 -	03/2014	10(O) -	0/0
383	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	274.81	11/2013 -	11/2013	0(O) -	0/0
384	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	624.00	-	04/2014 -	04/2014	0(O) -	0/0
385	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
386	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	11.32	01/2014 -	01/2014	0(O) -	0/0
387	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	266.79	02/2014 -	02/2014	0(O) -	0/0
388	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	292.53	02/2014 -	04/2014	2(O) -	0/0
389	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	45.59	04/2014 -	04/2014	0(O) -	0/0
390	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	131.68	05/2014 -	05/2014	0(O) -	0/0
391	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	992.49	08/2014 -	08/2014	0(O) -	0/0
392	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,110.70	06/2013 -	06/2013	0(O) -	0/0
393	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	34.97	09/2013 -	07/2014	10(O) -	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
394	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	646.53	08/2013	08/2013	0(O)	0/0
395	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	575.00	480.07	07/2013	07/2013	0(O)	0/0
396	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00	398.00	303.40	02/2014	02/2014	0(O)	0/0
397	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	998.79	107.47	08/2013	08/2013	0(O)	0/0
398	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	849.93	08/2013	08/2013	0(O)	0/0
399	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
400	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18	1,396.18	529.67	09/2014	09/2014	0(O)	0/0
401	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	194.93	09/2007	03/2014	78(O)	0/0
402	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	01/2013	94(O)	0/0
403	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,205.00	11/2012	06/2013	7(O)	0/0
404	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	296.81	11/2008	12/2013	61(O)	0/0
405	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	260.71	01/2009	01/2013	48(O)	0/0
406	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	01/2013	11(O)	0/0
407	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	194.51	02/2004	01/2013	107(O)	0/0
408	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	218.98	09/2013	09/2013	0(O)	0/0
409	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	597.32	06/2014	06/2014	0(O)	0/0
410	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	420.01	-	10/2013	-	2/2
411	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.82	01/2013	10/2013	9(O)	0/0
412	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	500.29	449.35	08/2013	08/2013	0(O)	0/0
413	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	256.64	06/2008	12/2013	66(O)	0/0
414	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	217.01	06/2008	03/2013	57(O)	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	230.62	06/2005 -	03/2013	93(O) -	0/0
416	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	234.82	04/2010 -	03/2014	47(O) -	0/0
417	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46(O) -	0/0
418	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	770.65	03/2013 -	03/2013	0(O) -	0/0
419	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	474.73	- -	12/2013	- -	0/1
420	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	05/2013	0(O) -	0/0
421	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	382.26	10/2011 -	03/2014	29(O) -	0/0
422	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	721.45	10/2011 -	06/2013	20(O) -	0/0
423	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	175.59	10/2008 -	01/2014	63(O) -	0/0
424	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	637.97	05/2010 -	03/2013	34(O) -	0/0
425	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	441.00	07/2013 -	07/2013	0(O) -	0/0
426	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.82	06/2013 -	06/2013	0(O) -	0/0
427	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	424.37	- -	06/2013	- -	1/1
428	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	238.37	06/2008 -	03/2013	57(O) -	0/0
429	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	191.01	05/2008 -	03/2013	58(O) -	0/0
430	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	274.33	09/2010 -	06/2013	33(O) -	0/0
431	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	213.01	08/2013 -	08/2013	0(O) -	0/0
432	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	417.69	09/2008 -	05/2013	56(O) -	0/0
433	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	-	10/2013 -	03/2014	5(O) -	0/0
434	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30(O) -	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
435	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	136.31	09/2008 -	03/2013	54(O) -	0/0
436	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	272.12	02/2004 -	01/2013	107(O) -	0/0
437	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	722.53	08/2013 -	08/2013	0(O) -	0/0
438	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	213.71	04/2008 -	03/2014	71(O) -	0/0
439	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	157.34	04/2008 -	03/2014	71(O) -	0/0
440	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	02/2013	40(O) -	0/0
441	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.30	12/2009 -	07/2013	43(O) -	0/0
442	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,909.50	09/2012 -	03/2013	6(O) -	0/0
443	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,737.60	10/2011 -	06/2013	20(O) -	0/0
444	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	281.08	09/2007 -	03/2013	66(O) -	0/0
445	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	283.67	02/2009 03/2014	03/2013	49(O) -12(R)	0/0
446	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	72.50	07/2009 -	04/2014	57(O) -	0/0
447	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014	79(O) -	0/0
448	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttaranchal	11/2011	478.00 -	478.00	229.22	10/2013 -	03/2014	5(O) -	0/0
449	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	189.74	08/2004 -	01/2013	101(O) -	0/0
450	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	187.62	08/2004 07/2010	01/2013	101(O) 30(R)	0/0
451	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	876.70	01/2013 -	01/2013	0(O) -	0/0
452	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	- -	3/3
453	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,935.90	10/2012 -	03/2013	5(O) -	0/0
454	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	419.12	05/2013 -	02/2014	9(O) -	0/0
455	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013	0(O) -	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
456	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	267.81	557.22	02/2013	02/2013	0(O)	0/0
457	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
458	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	500.28	09/2009	03/2013	42(O)	0/0
459	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	536.00	418.50	01/2014	01/2014	0(O)	0/0
460	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	1,591.80	12/2012	03/2013	3(O)	0/0
461	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.68	10/2008	02/2013	52(O)	0/0
462	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	294.44	10/2008	03/2013	53(O)	0/0
463	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16	702.16	199.69	07/2014	07/2014	0(O)	0/0
464	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
465	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,055.70	05/2012	02/2013	9(O)	0/0
466	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	186.07	06/2010	12/2013	42(O)	0/0
467	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
468	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24(O)	0/0
469	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	100.53	11/2008	07/2013	56(O)	0/0
470	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	68.37	04/2009	07/2013	51(O)	0/0
471	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	26.83	11/2008	01/2014	62(O)	0/0
472	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	124.50	04/2009	03/2013	47(O)	0/0
473	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	03/2013	9(O)	0/0
474	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	1,264.30	06/2013	06/2013	0(O)	0/0
475	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00	754.00	482.60	03/2013	03/2014	12(O)	0/0
476	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	269.32	11/2013	11/2013	0(O)	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
477	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	295.86	06/2008	03/2013	57(O)	0/0
478	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2013	54(O)	0/0
479	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19	484.19	31.33	10/2014	10/2014	0(O)	0/0
480	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	277.51	04/2008	12/2013	68(O)	0/0
481	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	252.98	06/2008	03/2013	57(O)	0/0
482	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	278.20	06/2008	12/2013	66(O)	0/0
483	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
484	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	257.43	06/2011	01/2013	19(O)	0/2
485	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.92	02/2010	12/2014	58(O)	0/0
486	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00	586.00	237.55	01/2014	01/2014	0(O)	0/0
487	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	465.86	09/2013	09/2013	0(O)	0/0
488	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	392.37	03/2008	03/2013	60(O)	0/0
489	PANIKHOLI-RIMOLI - [N24000197]NHAI, Orissa	03/2012	1,410.00	1,410.00	152.77	09/2014	09/2014	0(O)	0/0
490	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	995.04	10/2014	10/2014	0(O)	0/0
491	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	249.18	05/2008	03/2013	58(O)	0/0
492	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	574.00	472.14	03/2014	03/2014	0(O)	0/0
493	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	599.37	02/2013	02/2013	0(O)	0/0
494	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,221.90	07/2012	06/2013	11(O)	0/0
495	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	1,043.20	03/2013	03/2013	0(O)	0/0
496	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00	835.00	112.67	01/2014	01/2014	0(O)	0/0
497	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	3,465.50	11/2011	08/2013	21(O)	0/0
498	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17(O)	0/0
499	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00	1,987.00	-	07/2015	06/2016	11(O)	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
500	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	314.73	10/2008 -	06/2013	56(O) -	0/0
501	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya Pradesh	12/2003	229.91 -	229.91	275.64	10/2008 -	01/2013	51(O) -	0/0
502	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00 -	650.00	811.74	11/2013 -	11/2013	0(O) -	0/0
503	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	203.43	244.46	10/2008 -	02/2013	52(O) -	0/0
504	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25(O) -	0/0
505	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	805.39	393.68	03/2013 -	03/2013	0(O) -	0/0
506	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Orissa	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014	0(O) -	0/0
507	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	214.65	09/2007 -	03/2013	66(O) -	0/0
508	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	187.10	07/2008 -	03/2013	56(O) -	0/0
509	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0
510	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013	0(O) -	0/0
511	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014	0(O) -	0/0
512	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31(O) -	0/0
513	SNG toBANL - [N24000189]NHAI, J and K	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0
514	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60(O) -	0/0
515	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00 -	241.53	148.22	04/2004 -	01/2013	105(O) -	0/0
516	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,675.10	08/2011 -	01/2013	17(O) -	0/0
517	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	01/2013	43(O) -	0/0
518	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32(O) -	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
519	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	817.67	11/2013	11/2013	0(O)	0/0
520	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
521	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	83.75	05/2013	05/2013	0(O)	0/0
522	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	177.82	-	04/2013	-	2/2
523	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	697.74	03/2014	03/2014	0(O)	0/0
524	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	163.43	03/2008	01/2013	58(O)	0/0
525	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	37.68	11/2012	12/2013	13(O)	0/0
526	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	459.93	07/2013	07/2013	0(O)	0/0
527	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	149.40	06/2014	06/2014	0(O)	0/0
	Total		94,417.90	96,356.52	68,989.47				10/14
Shipping & Ports									
528	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011	11/2012	-	0/0
529	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49	220.49	98.31	01/2013	06/2013	5(O)	0/0
530	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87	511.87	107.56	03/2014	-	-	0/0
531	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	532.83	337.00	12/2012	10/2013	10(O) 10(R)	0/0
532	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03	277.03	294.87	12/2011	10/2012	-	0/0
533	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	272.50	194.14	06/2011	10/2012	-	0/0
534	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	248.23	02/2014	02/2014	0(O)	0/0
535	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10	1,012.23	371.96	12/2013	10/2013	-2(O) -2(R)	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
536	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	894.93	12/2010 09/2012	10/2013	34(O) 13(R)	0/0
537	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0
538	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0
539	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	10/2008	-	0/0
540	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1
541	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
542	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
543	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
544	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0
545	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	830.49	10/2008 11/2010	-	-	0/0
546	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,644.30	01/2012 09/2012	02/2013	13(O) 5(R)	0/0
547	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
	Total		15,907.97 -	18,174.92	8,042.54				0/1
<u>Telecommunications</u>									
548	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53(O) -	0/0
549	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.90	02/2007 12/2010	-	-	0/0
550	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	67.21	02/2007 03/2012	02/2013	72(O) 11(R)	0/0

Sector Wise Details

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
551	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL, Delhi	02/2006	229.41 -	229.41	67.19	03/2012 -	02/2013	11(O) -	0/0
552	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	06/2013	32(O) 15(R)	0/0
553	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
554	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
555	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttaranchal	01/2009	149.15 158.72	158.72	80.05	06/2009 -	03/2013	45(O) -	0/0
556	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	03/2013	51(O) -	0/0
557	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL, Madhya pradesh	11/2009	916.70 930.60	930.60	818.09	11/2010 -	12/2012	25(O) -	0/0
558	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	-	0/0
559	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL, Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	03/2013	48(O) -	0/0
560	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL, Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
561	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
Total			5,964.89 -	5,905.68	1,728.20				0/0
<u>Urban Development</u>									
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21(O) -	6/6
563	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
564	DELHI MRTS PHASE-III - [N28000056]DMRC, Delhi	09/2011	35,242.00 -	35,242.00	1,300.35	03/2016 -	03/2016	0(O) -	0/0
565	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	2,494.00	140.89	09/2014 -	09/2014	0(O) -	0/0
Total			44,245.18 -	49,518.08	3,708.81				6/6
<u>Water Resources</u>									

Sector Wise Details

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
566	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
			-			-		-	
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			785,633.54	927,454.45	434,009.60				995/3404

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

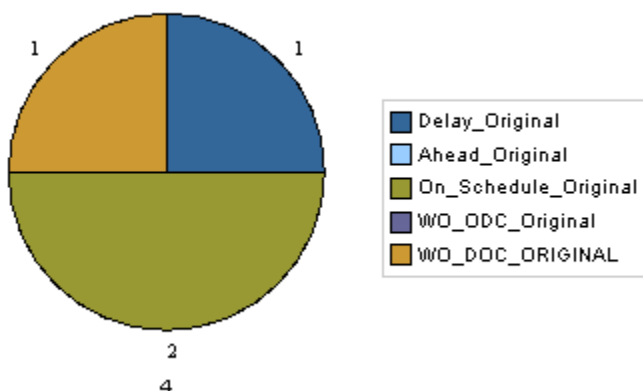

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till December, 2012 is Rs. 3708.81 crore, which is 7.5% of the revised cost of the projects.

Figures are in Rs. Crore

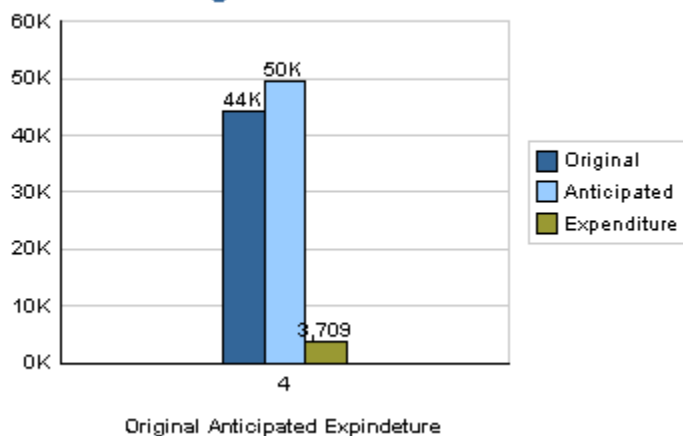

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **14**

Number of Projects Delayed **8**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 14 projects, 8 projects are delayed .6 projects do not have fixed dates of commissioning.

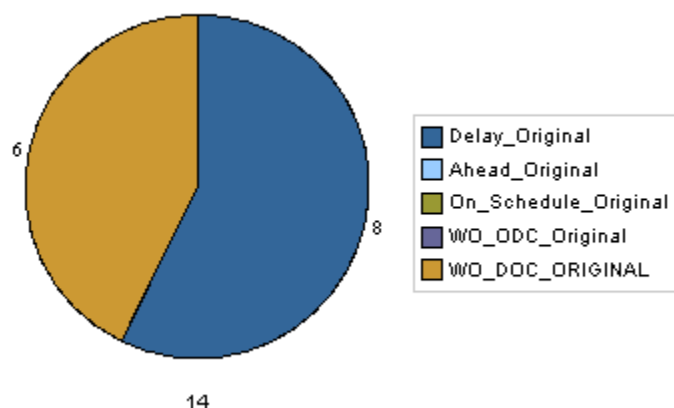

III. Investment Scenario

The Total Original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 5964.89 crore but this was subsequently revised to Rs. 5905.68 crore implying a cost overrun of -1%. The expenditure incurred on these projects till December, 2012 is Rs. 1728.2 crore, which is 29.3% of the revised cost of the projects.

Figures are in Rs. Crore

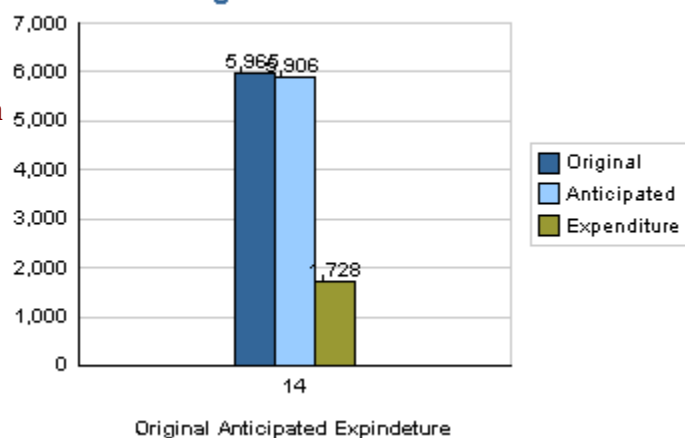

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	20
Number of Projects On Schedule	1
Number of Projects Delayed	7
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	10

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 2 projects are ahead of schedule, 1 project are on schedule and 7 projects are delayed .10 projects do not have fixed dates of commissioning.

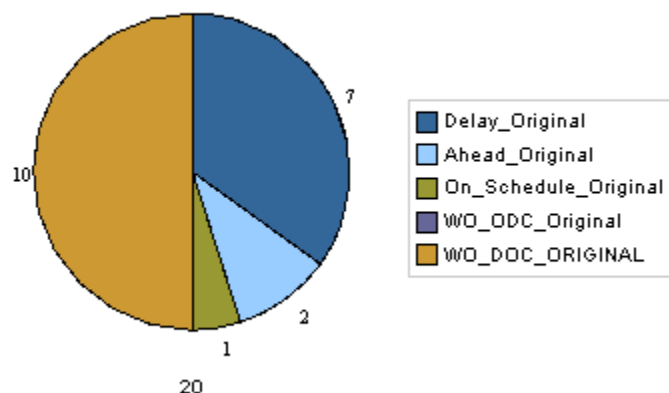

III. Investment Scenario

The Total Original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 15907.97 crore but this was subsequently revised to Rs. 18174.92 crore implying a cost overrun of 14.3%. The expenditure incurred on these projects till December, 2012 is Rs. 8042.54 crore, which is 44.3% of the revised cost of the projects.

Figures are in Rs. Crore

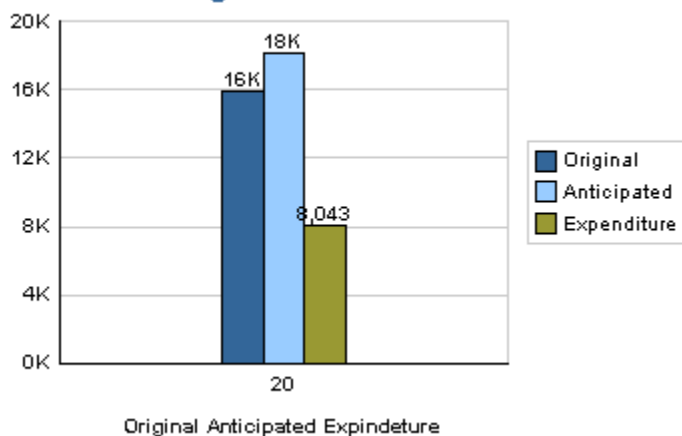

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	146
Number of Projects On Schedule	54
Number of Projects Delayed	86

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 146 projects, 54 projects are on schedule and 86 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

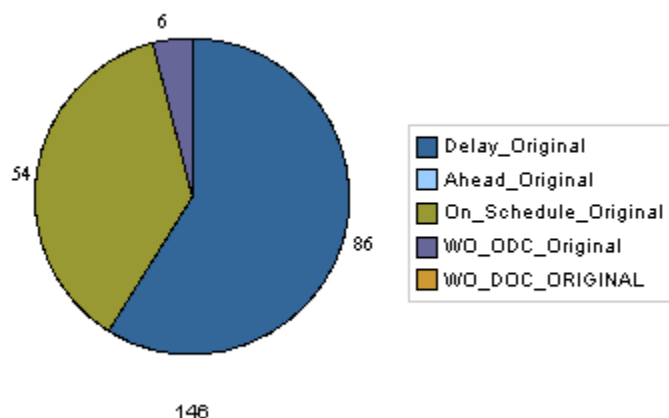

III. Investment Scenario

The Total Original cost of implementation of 146 projects when sanctioned, was of the order of Rs. 94417.9 crore but this was subsequently revised to Rs. 96356.52 crore implying a cost overrun of 2.1%. The expenditure incurred on these projects till December, 2012 is Rs. 68989.47 crore, which is 71.6% of the revised cost of the projects.

Figures are in Rs. Crore

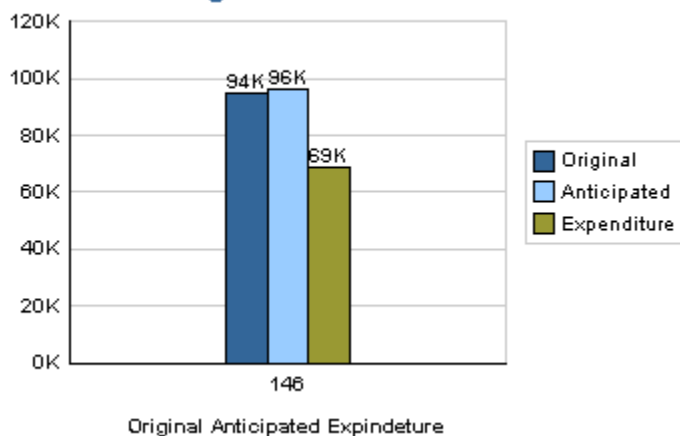

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	126
Number of Projects On Schedule	7
Number of Projects Delayed	44
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	19
Number of Projects Without Date Of Commissioning	55

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 126 projects, 1 project are ahead of schedule, 7 projects are on schedule and 44 projects are delayed .55 projects do not have fixed dates of commissioning.19 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

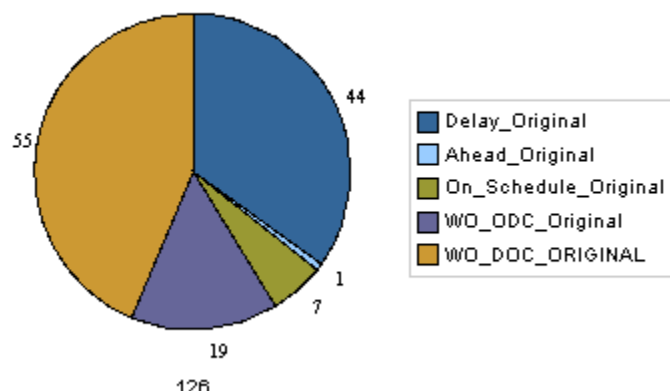

III. Investment Scenario

The Total Original cost of implementation of 126 projects when sanctioned, was of the order of Rs. 61393.48 crore but this was subsequently revised to Rs. 148131.67 crore implying a cost overrun of 141.3%. The expenditure incurred on these projects till December, 2012 is Rs. 61217 crore, which is 41.3% of the revised cost of the projects.

Figures are in Rs. Crore

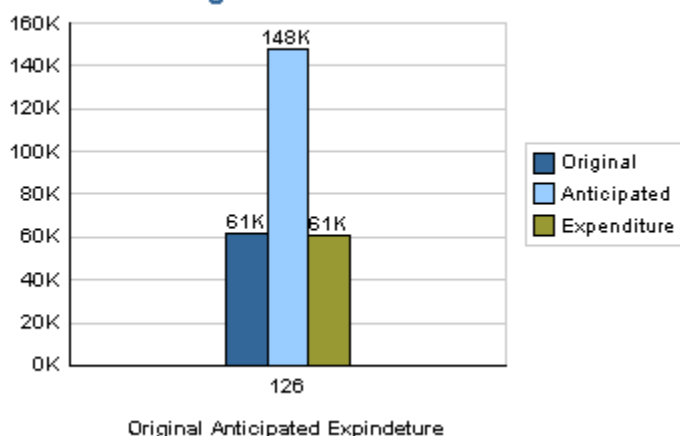

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	99
Number of Projects On Schedule	45
Number of Projects Delayed	52

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 99 projects, 45 projects are on schedule and 52 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

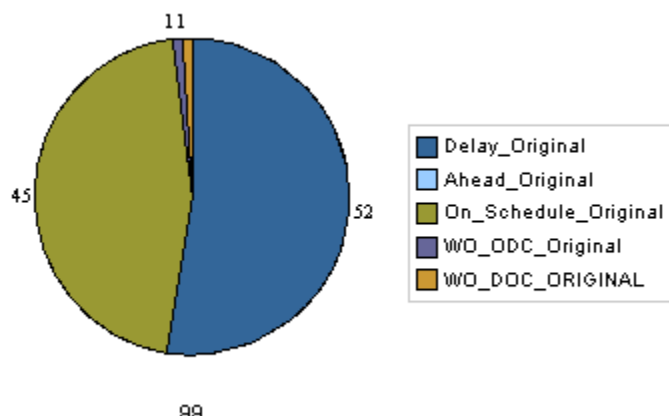

III. Investment Scenario

The Total Original cost of implementation of 99 projects when sanctioned, was of the order of Rs. 227823.09 crore but this was subsequently revised to Rs. 243653.33 crore implying a cost overrun of 6.9%. The expenditure incurred on these projects till December, 2012 is Rs. 109048.3 crore, which is 44.8% of the revised cost of the projects.

Figures are in Rs. Crore

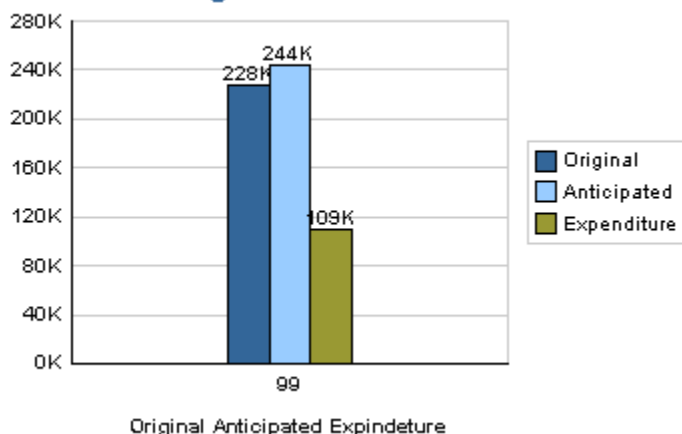

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	73
Number of Projects On Schedule	21
Number of Projects Delayed	39

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	12

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 73 projects, 21 projects are on schedule and 39 projects are delayed .12 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

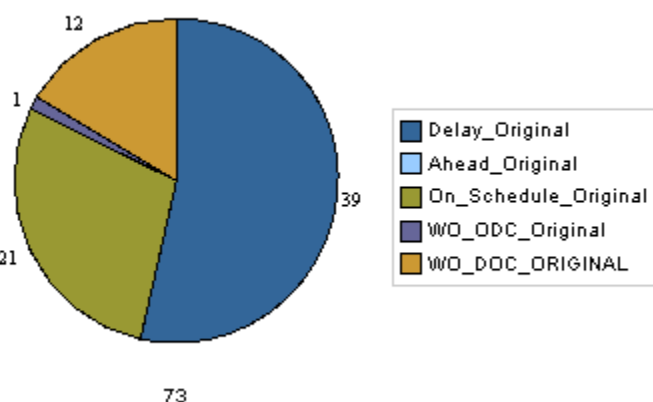

III. Investment Scenario

The Total Original cost of implementation of 73 projects when sanctioned, was of the order of Rs. 177447.66 crore but this was subsequently revised to Rs. 188692.3 crore implying a cost overrun of 6.3%. The expenditure incurred on these projects till December, 2012 is Rs. 86213.52 crore, which is 45.7% of the revised cost of the projects.

Figures are in Rs. Crore

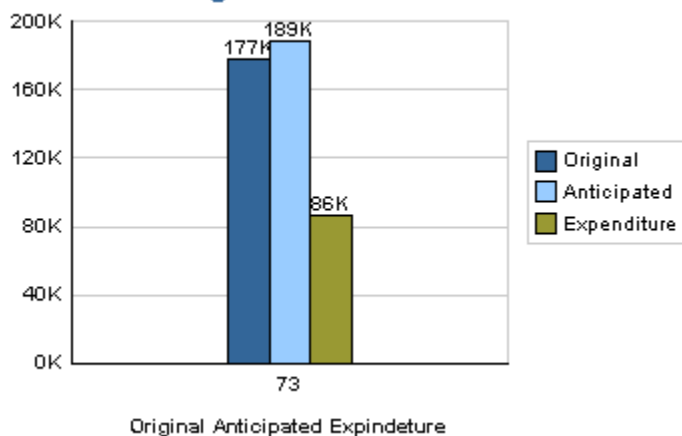

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 1 project are ahead of schedule, 3 projects are on schedule and 10 projects are delayed .3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

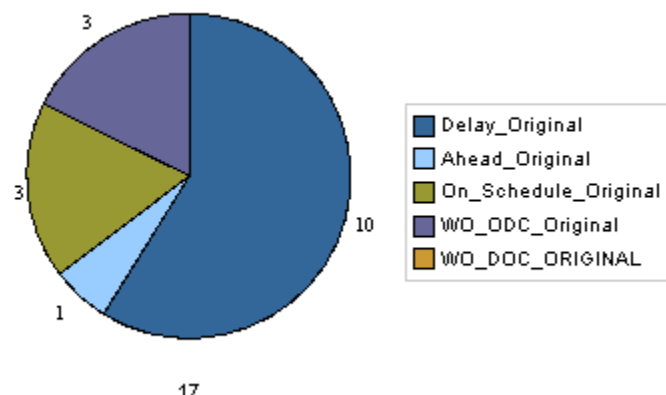

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till December, 2012 is Rs. 45840.84 crore, which is 64.2% of the revised cost of the projects.

Figures are in Rs. Crore

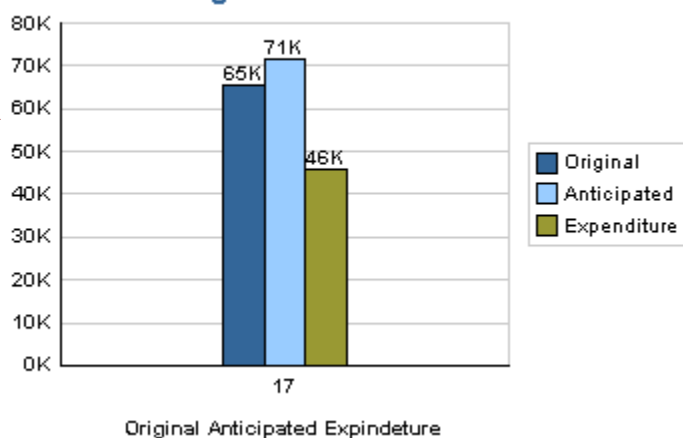

Sector wise current status of projects on theFlash Report


Fertilisers

I. Current Status:

Number of Projects	3
Number of Projects On Schedule	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are on schedule and



III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 4065.66 crore but this was subsequently revised to Rs. 4065.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till December, 2012 is Rs. 946 crore, which is 23.3% of the revised cost of the projects.

Figures are in Rs. Crore

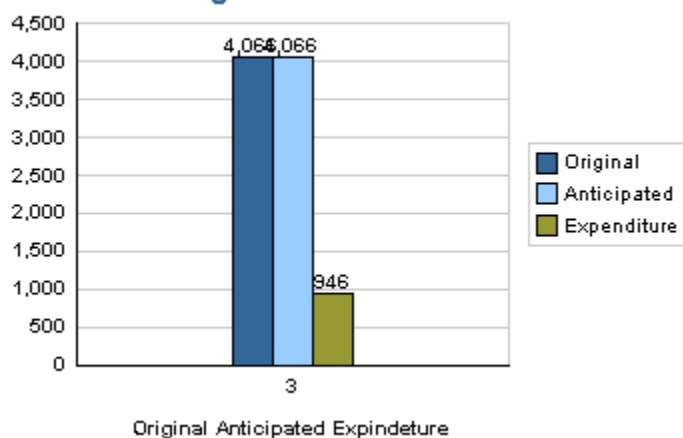

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	29
Number of Projects Delayed	21

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 29 projects are on schedule and 21 projects are delayed .1 project do not have fixed dates of commissioning.

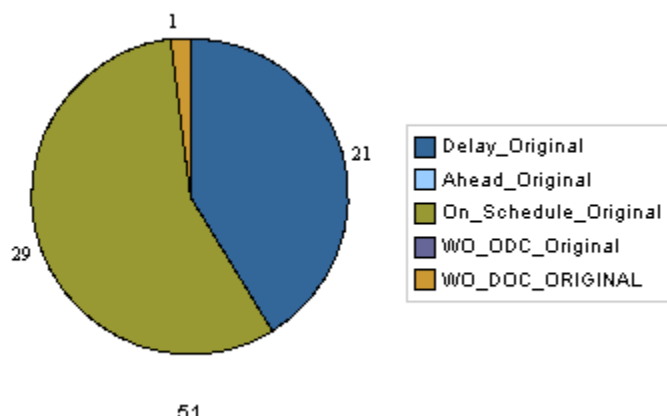

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37510.52 crore implying a cost overrun of 4%. The expenditure incurred on these projects till December, 2012 is Rs. 13463.3 crore, which is 35.9% of the revised cost of the projects.

Figures are in Rs. Crore

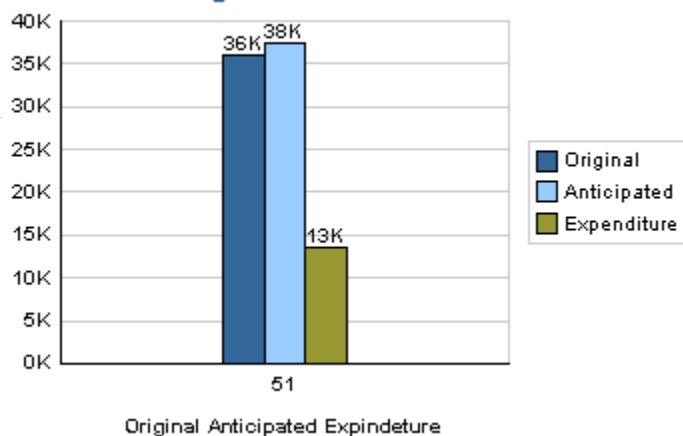

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

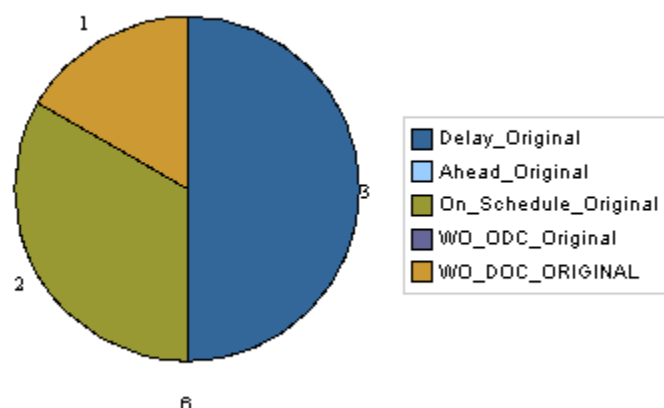

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till December, 2012 is Rs. 4735.6 crore, which is 78.1% of the revised cost of the projects.

Figures are in Rs. Crore

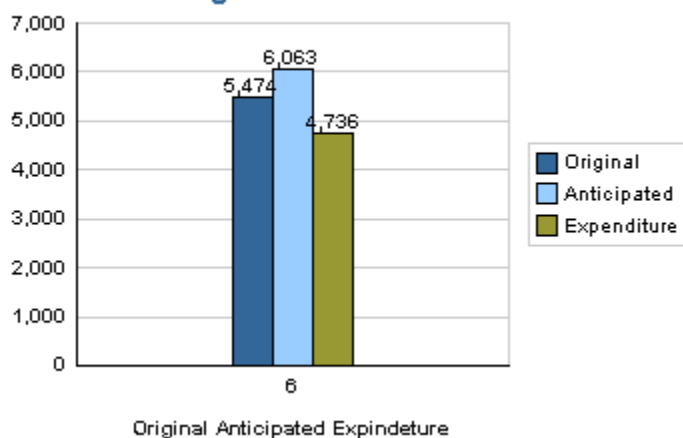

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

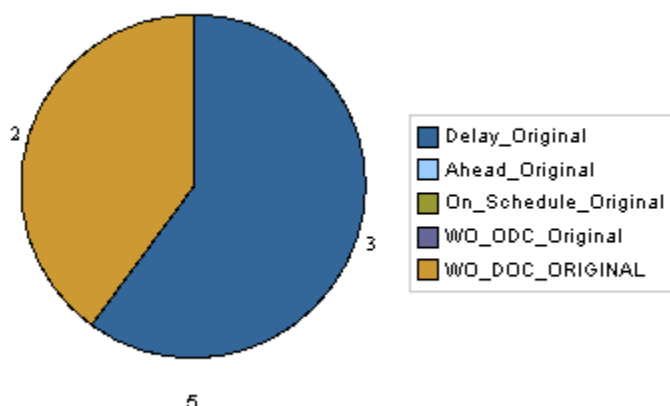

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till December, 2012 is Rs. 24058.57 crore, which is 50.3% of the revised cost of the projects.

Figures are in Rs. Crore

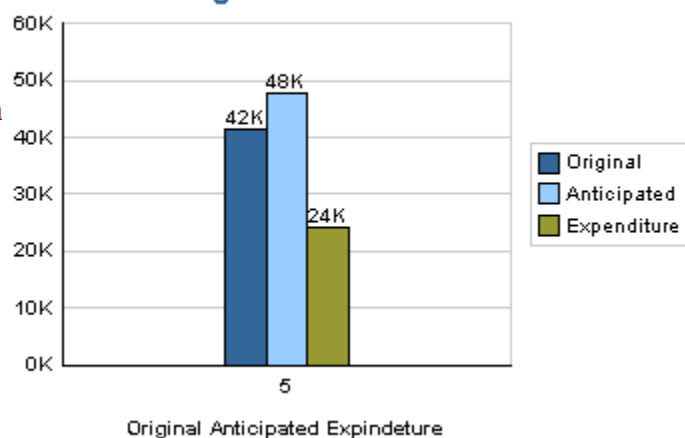

ANNEXURES

CENTAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	36	31097.25	38721.12	23261.58
2	Arunachal Pr.	4	9512.22	14144.29	8666.73
3	Assam	34	22035.93	35405.41	23773.36
4	Bihar	30	26917.64	34673.44	22917.38
5	Chhatisgarh	24	46583.84	47866.92	15375.45
6	Delhi	4	38214.41	38194.82	1575.64
7	Goa	1	335.61	335.61	169.33
8	Gujarat	22	31111.55	31313.49	9711.30
9	Haryana	10	5496.60	7636.69	7970.69
10	Himachal Pr.	5	13355.57	17246.69	13068.46
11	J and K	10	14926.96	34825.56	14099.18
12	Jharkhandd	23	14447.40	18428.98	8437.83
13	Karnataka	26	46344.40	55830.82	21053.74
14	Kerala	7	20376.67	21818.22	5161.99
15	Madhya pradesh	22	18978.92	19273.39	9076.96
16	Maharashtra	52	93207.43	108066.84	49324.68
17	Manipur	1	727.56	4444.00	1079.17
18	Meghalaya	2	762.00	762.00	685.29
19	Mizoram	2	1532.97	3307.11	406.43
20	Multi State	108	143702.08	153168.57	68142.38
21	Nagaland	1	850.00	850.00	8.45
22	Orissa	31	57663.96	62099.12	35758.83
23	Punjab	7	4836.20	5777.97	2650.62
24	Rajasthan	13	20962.87	20917.08	6942.16
25	Sikkim	2	1648.94	3690.04	255.34
26	Tamil Nadu	32	51275.95	62055.82	40835.24
27	Tripura	3	1522.39	2018.85	1028.00
28	Uttar Pradesh	23	18822.90	22659.67	11963.73
29	Uttaranchal	4	6097.21	7037.64	2280.39
30	West Bengal	27	42286.11	54884.29	28329.27
TOTAL		566	785633.54	927454.45	434009.60

LIST OF PROJECT MORE THAN COST

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	Atomic Energy	09/2003	3492.00	0.00	3960.33
2	KUDANKULAM APP (NPCIL)	NPCIL	Atomic Energy	12/2001	13171.00	0.00	15276.00
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	AAI	Civil Aviation	08/2008	1942.51	0.00	2199.24
4	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	BPCL	Petroleum	04/2008	825.00	0.00	1124.47
5	RESITMENT OF MARKETING INSTALATION AT VISAKH	HPCL	Petroleum	01/2009	756.00	898.00	909.00
6	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	NHPC	Power	10/2003	768.92	0.00	1638.44
7	URI H.E.P STAGE -II (NHPC)	NHPC	Power	08/2005	1729.29	0.00	1860.84
8	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	NHPC	Power	09/2005	1061.38	0.00	1252.08
9	CHUTAK HYDRO-ELECTRIC PROJECT	NHPC	Power	08/2006	621.26	0.00	775.29
10	NIMOO BAZGO HYDROELECTRIC PROJECT	NHPC	Power	08/2006	611.01	0.00	814.50
11	KOLDAM HEP (NTPC)	NTPC	Power	10/2002	4527.15	0.00	4669.00
12	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	PGCIL	Power	07/2006	557.24	0.00	595.50
13	RAMPUR HEP(412 MW)	SJVNL	Power	01/2007	2047.03	0.00	2113.01
14	AMRAVATI-NARKHER NL(CR)	CR	Railways	06/1994	120.90	284.27	543.08
15	LANJHIGARH-JUNAGARH NL(ECOR)	ECOR	Railways	04/1993	100.00	142.98	207.83
16	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	Railways	04/1996	114.01	332.92	406.58
17	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	Railways	04/1997	233.00	501.69	685.77
18	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	MRTPT	Railways	03/2000	907.69	3156.32	3240.22
19	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	NCR	Railways	04/1985	158.77	432.46	558.07
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	Railways	04/1999	108.00	214.09	250.82
21	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	NEFR	Railways	04/1996	1676.31	1676.31	3291.16
22	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	NEFR	Railways	09/1996	156.00	156.00	280.75
23	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	NEFR	Railways	09/1997	1000.00	1500.00	2590.05
24	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NEFR	Railways	04/2000	733.00	733.00	1329.90

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
25	KATIHAR - JOGBANI (GC)(NEFR)	NEFR	Railways	09/2001	100.00	492.98	735.14
26	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NEFR	Railways	04/2003	727.56	727.53	1079.17
27	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NEFR	Railways	01/2004	915.70	915.70	1583.58
28	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NEFR	Railways	12/2006	170.00	170.00	396.45
29	KANPUR-KASGANJ-MATHURA(GC),NER	NER	Railways	03/1997	395.00	1062.36	1401.22
30	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	Railways	04/1999	323.40	323.40	503.06
31	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	NER	Railways	03/2002	381.17	381.17	621.56
32	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	Railways	03/1995	2500.00	2500.00	8549.43
33	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	NR	Railways	07/1998	248.44	576.27	914.71
34	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	Railways	03/2002	409.00	625.30	835.57
35	JIND-SONEPAT (NL),NR	NR	Railways	01/2004	190.81	238.56	439.54
36	REWARI-ROHTAK (NL),NR	NR	Railways	01/2004	149.38	330.23	503.47
37	ELECTRIFICATION OF MORADABAD-ROZA	RE	Railways	12/2004	129.17	0.00	227.48
38	BILASPUR-URKURA (DL)	RVNL	Railways	04/1997	151.52	0.00	330.65
39	RAJATGARH-BARANG(LD),ECOR	RVNL	Railways	04/1999	166.16	0.00	258.82
40	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	Railways	04/2000	133.41	207.00	228.88
41	RENIGUNTA-GUNTAKAL(RE)	RVNL	Railways	06/2000	168.34	0.00	344.50
42	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	Railways	04/2003	136.62	0.00	243.30
43	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	Railways	12/1994	124.43	495.68	589.19
44	NANDYAL-YERRAGUNTLA(NL),SCR	SCR	Railways	03/1996	155.74	429.49	634.87
45	GADWAL - RAICHUR (NL), SCR	SCR	Railways	04/1998	92.63	228.09	266.03
46	RANCHI-LOHARDAGA(GC),SER	SER	Railways	04/1997	194.07	194.07	309.91
47	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	Railways	09/1995	100.00	100.00	525.48
48	CALICUT-MANGALORE (DL) (SR)	SR	Railways	02/1996	240.00	0.00	600.41
49	KARUR-SALEM(NL),SR	SR	Railways	02/1997	155.55	155.00	758.81
50	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	Railways	09/2006	343.17	343.17	571.48
51	KOTTUR-HARIHAR(NL),(SWR)	SWR	Railways	04/1995	65.94	302.23	342.57
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	Railways	02/1997	295.00	412.91	560.17
53	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	NHAI	Road Transport & Highways	04/2000	367.49	0.00	453.68

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
54	GANJAM-ICCHAPURUM,NH-5(NHAI)	NHAI	Road Transport & Highways	04/2000	263.27	0.00	272.12
55	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	NHAI	Road Transport & Highways	12/2003	221.82	0.00	296.81
56	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	Road Transport & Highways	12/2003	237.80	0.00	256.64
57	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	NHAI	Road Transport & Highways	12/2003	195.00	0.00	217.01
58	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	Road Transport & Highways	12/2003	230.00	0.00	230.62
59	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	Road Transport & Highways	12/2003	217.61	0.00	234.82
60	DHARAMTUL TO SONAPUR (AS-19)	NHAI	Road Transport & Highways	12/2003	200.00	0.00	238.37
61	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	NHAI	Road Transport & Highways	12/2003	160.00	0.00	191.01
62	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	Road Transport & Highways	12/2003	232.45	0.00	274.33
63	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	NHAI	Road Transport & Highways	12/2003	332.94	0.00	417.69

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
64	GUWAHATI TO NALBARI (AS-5)	NHAI	Road Transport & Highways	12/2003	198.16	0.00	213.71
65	GWALIOR BYPASS, NH-75,3	NHAI	Road Transport & Highways	12/2003	300.93	0.00	303.02
66	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	Road Transport & Highways	12/2003	280.00	0.00	283.67
67	JHANSI TO LALITPUR, NH-25,26	NHAI	Road Transport & Highways	12/2003	355.06	0.00	500.28
68	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	Road Transport & Highways	12/2003	275.00	0.00	279.68
69	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	NHAI	Road Transport & Highways	12/2003	240.00	0.00	294.44
70	NAGAON TO DHARAMTUL (AS-2)	NHAI	Road Transport & Highways	12/2003	264.72	0.00	295.86
71	NALBARI T BIJNI (AS-7)	NHAI	Road Transport & Highways	12/2003	208.00	0.00	277.51
72	NALBARI TO BIJNI (AS-6)	NHAI	Road Transport & Highways	12/2003	225.00	0.00	252.98
73	NALBARI TO BIJNI (AS-8)	NHAI	Road Transport & Highways	12/2003	200.00	0.00	278.20

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
74	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	NHAI	Road Transport & Highways	12/2003	340.68	0.00	392.37
75	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	NHAI	Road Transport & Highways	12/2003	251.03	0.00	314.73
76	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	NHAI	Road Transport & Highways	12/2003	229.91	0.00	275.64
77	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	NHAI	Road Transport & Highways	12/2003	203.43	0.00	244.46
78	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	NHAI	Road Transport & Highways	12/2003	157.47	0.00	214.65
79	SONAPUR TO GUWAHTI (AS-3)	NHAI	Road Transport & Highways	12/2003	245.00	0.00	491.21
80	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	NHAI	Road Transport & Highways	03/2005	190.00	0.00	260.71
81	HAPUR-GARH Mukteswar (Others) KM.58-93, NH-24	NHAI	Road Transport & Highways	03/2005	220.00	0.00	281.08
82	NAGPUR-KONDHALI,NH-6(NHAI)	NHAI	Road Transport & Highways	03/2005	168.00	0.00	457.30
83	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	NHAI	Road Transport & Highways	03/2005	557.00	0.00	930.92

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
84	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	Road Transport & Highways	03/2005	940.00	0.00	1221.90
85	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	NHAI	Road Transport & Highways	03/2005	941.00	0.00	1901.00
86	THANJAUR-TRICHY,NH-67(NHAI)	NHAI	Road Transport & Highways	03/2005	280.00	0.00	581.49
87	TRICHY - KORUR NH-67	NHAI	Road Transport & Highways	03/2005	516.00	0.00	760.07
88	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	Road Transport & Highways	04/2007	486.00	0.00	637.97
89	Surat- Dahisar(Six Lane) Km 263 to Km 502	NHAI	Road Transport & Highways	02/2009	1693.75	0.00	2675.10
90	Chennai-Tada(Six lane)	NHAI	Road Transport & Highways	04/2009	353.37	0.00	382.26
91	Gurgaon-Kotputli Km 42.70 to 54.4 Km	NHAI	Road Transport & Highways	04/2009	1673.70	0.00	2737.60
92	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	NHAI	Road Transport & Highways	05/2009	572.30	0.00	721.45
93	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	NHAI	Road Transport & Highways	05/2009	1108.00	0.00	3465.50

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
94	Kishangarh-Ajmer-Beawer	NHAI	Road Transport & Highways	11/2009	795.00	0.00	1055.70
95	Pune-sholapur, pkg1	NHAI	Road Transport & Highways	11/2009	1110.00	0.00	1802.10
96	Talegaon-amravati	NHAI	Road Transport & Highways	11/2009	567.00	0.00	817.67
97	MP/Maharashtra Border-Dhula	NHAI	Road Transport & Highways	12/2009	835.00	0.00	1068.70
98	Armur to kadloor yellareddy	NHAI	Road Transport & Highways	02/2010	390.56	0.00	631.65
99	Gujarat/Maharashtra Border Surat-Hazira Port Section	NHAI	Road Transport & Highways	03/2010	1509.10	0.00	1909.50
100	Hyderabad-Vijaywada Km. 40 to 221.50 Km	NHAI	Road Transport & Highways	04/2010	1740.00	0.00	1935.90
101	AMRITSAR-PATHANKOT	NHAI	Road Transport & Highways	05/2010	705.00	0.00	1205.00
102	Jaipur-Tonk-Deoli	NHAI	Road Transport & Highways	06/2010	792.06	0.00	1591.80
103	Hazaribagh-Ranchi	NHAI	Road Transport & Highways	08/2010	625.07	0.00	876.70

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
104	JAIPUR-REENGUS	NHAI	Road Transport & Highways	08/2010	267.81	0.00	557.22
105	Hungund-Surathkal and Mangalore-Knt/Kerala Border	NHAI	Road Transport & Highways	09/2010	946.00	0.00	1394.40
106	KUNDUPUR-SURATHKAL & MANGLORE	NHAI	Road Transport & Highways	09/2010	671.00	0.00	737.54
107	INDORE-DEWAS(NH-3)	NHAI	Road Transport & Highways	11/2010	325.00	0.00	419.12
108	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	Road Transport & Highways	12/2010	1008.50	0.00	1110.70
109	2-LANNING OF SHILONG BYPASS	NHAI	Road Transport & Highways	02/2011	226.00	0.00	266.79
110	PANIPAT-ROHTAK	NHAI	Road Transport & Highways	04/2011	807.00	0.00	995.04
111	2 LANNING OF MOKAMA-MUNGER	NHAI	Road Transport & Highways	05/2011	351.54	0.00	391.73
112	ROHTAK-BAWAL	NHAI	Road Transport & Highways	05/2011	650.00	0.00	811.74
113	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	Shipping & Ports	03/2007	245.67	298.17	326.08
114	Acquisition of Two nos. of 3060 DWT	SHIPP.	Shipping & Ports	04/2009	277.03	280.00	294.87
115	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	Steel	10/2005	8692.00	0.00	9958.76

SN	PROJ_TITLE	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
116	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT	RINL	Steel	07/2007	230.00	0.00	254.09
117	COKE OVEN BATTERY NO. 4 PHASE-II	RINL	Steel	08/2007	108.00	0.00	118.28

List of Projects Ahead of Schedule

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Steel</u>						
1	Expansion of Rourkela Steel Plant - [N12000056	9/2008	11,812.00 11,812.00	11,812.00	8,450.87	11/2013 -	03/2013
	Total		11,812.00 -	11,812.00	8,450.87		
	<u>Railways</u>						
2	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	415.66	03/2014 -	03/2013
	Total		1,389.62 -	1,389.62	415.66		
	<u>Shipping & Ports</u>						
3	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	371.96	12/2013 12/2013	10/2013
4	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060	2/2011	830.00 -	621.53	-	05/2013 -	03/2013
	Total		1,858.10 -	1,633.76	371.96		
	Grand Total		15,059.72	14,835.38	9,238.49		

Sectorwise Summary of Project Without Original Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Petroleum	1	2,615.69	.00	2,615.69	1,975.77
Power	1	421.01	623.44	623.44	413.08
Railways	19	5,791.43	8,427.61	16,309.18	7,761.44
Road Transport & Highways	6	4,069.00	.00	4,069.00	3,628.87
Steel	3	1,657.88	.00	1,657.88	387.35
Grand total	30	14,555.01	9,051.05	25,275.19	14,166.51

List of project Without Original Date of Commissioning

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Steel</u>								
1	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	226.72	-	04/2013	-	13/19
2	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	148.58	-	11/2013	-	17/21
3	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33	187.33	12.05	-	12/2013	-	0/1
	Total		1,657.88	1,657.88	387.35				30/41
	<u>Petroleum</u>								
4	EURO-IV DHD T - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,975.77	-	01/2013	-	117/116
	Total		2,615.69	2,615.69	1,975.77				117/116
	<u>Power</u>								
5	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	413.08	-	07/2013	-	6/29
	Total		421.01	623.44	413.08				6/29
	<u>Railways</u>								
6	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	342.57	-	12/2012	-	0/0
7	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	571.48	-	12/2012	-	0/0
8	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	560.17	-	01/2013	-	0/0
9	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.51	-	02/2013	-	0/0
10	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,820.00	188.66	-	03/2013	-	0/0
11	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	206.46	-	03/2013	-	0/0
12	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,401.22	-	03/2013	-	0/0
13	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	100.02	-	03/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	778.38	- -	03/2013	-	0/6
15	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,995.25	238.06	- -	03/2013	-	0/0
16	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	138.67	- -	03/2013	-	0/0
17	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	406.40	280.75	- -	06/2013	-	0/0
18	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
19	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	503.06	- -	03/2014	-	0/1
20	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,583.58	- -	03/2014	-	0/0
21	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	141.66	- -	03/2014	-	0/0
22	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	247.13	- -	03/2015	-	0/0
23	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
24	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	117.93	- -	03/2016	-	0/0
Total			5,791.43 -	16,309.18	7,761.44				0/7
Road Transport & Highways									
25	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
26	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3
27	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	177.82	- -	04/2013	-	2/2
28	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	424.37	- -	06/2013	-	1/1
29	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	420.01	- -	10/2013	-	2/2
30	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	474.73	- -	12/2013	-	0/1
Total			4,069.00 -	4,069.00	3,628.87				10/12
Grand Total			14,555.01	25,275.19	14,166.51				163/205

Sectorwise Summary Without Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	2	4,598.29	.00	6,783.29	5,044.57
Civil Aviation	1	1,808.00	2,015.00	2,015.00	1,742.12
Coal	1	249.03	.00	249.03	49.63
Petroleum	12	13,723.25	5,800.38	11,209.75	6,155.47
Power	1	596.45	1,007.16	1,007.16	864.13
Railways	55	15,462.91	27,164.16	43,229.93	20,483.00
Shipping & Ports	10	5,788.20	2,422.27	6,767.52	2,117.88
Telecommunications	6	2,997.75	.00	2,934.67	111.65
Urban Development	1	114.18	173.08	173.08	0.00
Grand total	89	45,338.06	38,582.05	74,369.43	36,568.45

List of project Without Date of Commissioning

Date of Commissioning					
S.No Project		Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00	09/2010	-
			-	-	
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	-
			-	-	
	Total		4,598.29		
			-		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
			2,015.00	02/2012	
	Total		1,808.00		
			-		
<u>Coal</u>					
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	-
			-	-	
	Total		249.03		
			-		
<u>Petroleum</u>					
5	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	09/2012	09/2012
			-	-	
6	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	09/2012	09/2012
			-	-	
7	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	-	10/2012
			-	-	
8	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	04/2011	-
			-	-	
9	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	-	-
			898.00	-	
10	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	-	-
			394.00	-	
11	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43	03/2012	-
			4,508.38	-	
12	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
			-	-	
13	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	03/2012	-
			-	-	
14	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	07/2012	-
			-	07/2012	
15	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	07/2012	-
			-	-	
16	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	04/2012	-
			-	-	
	Total		13,723.25		
			-		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Power</u>				
17	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		596.45 -		
	<u>Railways</u>				
18	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
19	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	03/2011
20	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
21	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
22	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
23	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
24	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
25	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
26	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRT,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
27	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
28	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
29	REWARI-ROHTAK (NL),NR - [220100279]NR,Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
30	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
31	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
32	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
33	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
34	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
35	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
36	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
37	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
38	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
39	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
40	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
41	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
42	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
43	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
44	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
45	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
46	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
47	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
48	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
49	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
50	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
51	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
52	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.64	- 09/2009	-
53	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
54	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-
55	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
56	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
57	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
58	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
59	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	-
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
61	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
62	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
63	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
64	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
65	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
66	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
67	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
68	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
69	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
70	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
71	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
72	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		15,462.91 -		
Shipping & Ports					
73	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
74	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	- 01/2009	01/2009
75	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
76	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
77	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 272.50	06/2011 -	10/2012
78	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
79	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012
80	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
81	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	-
82	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		5,788.20 -		
Telecommunications					
83	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
84	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
85	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
86	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
87	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
88	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
	Total		2,997.75 -		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Urban Development</u>				
89	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Grand Total			45,338.06		

List of Delay Project w.r.t Original and Revised

(Dec,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	15,276.00	12/2008 -	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,241.00	12/2015 -	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,497.00	12/2016 -	03/2017	3	-
Total			36,950.00 -	41,049.00	19,014.00				
<u>Civil Aviation</u>									
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,199.24	05/2011 -	03/2013	22	-
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	169.33	05/2012 -	03/2013	10	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	198.22	01/2011 04/2013	04/2013	27	0
Total			2,587.58 -	2,970.07	2,566.79				
<u>Coal</u>									
7	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	143.73	03/2011 -	03/2013	24	-
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,536.19	06/2009 -	09/2013	51	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	108.50	03/2010 -	03/2014	48	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	3,709.61	03/2012 -	03/2014	24	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	100.37	03/2012 -	03/2014	24	-
12	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.34	03/2012 -	03/2014	24	-
13	Churi Benti UG - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	34.68	03/2011 -	03/2014	36	-
14	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	60.74	03/2012 -	03/2014	24	-
15	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	108.35	03/2012 -	03/2014	24	-
16	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	424.32	03/2013 09/2012	07/2014	16	22
17	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48	-
18	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	2.07	03/2012 -	03/2015	36	-
19	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	119.24	03/2010 -	03/2015	60	-
20	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	80.86	12/2012 -	03/2015	27	-
21	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	122.89	03/2012 -	03/2015	36	-
22	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44	-
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	264.84	03/2014 -	03/2016	24	-
24	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.88	03/2014 -	03/2016	24	-
25	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
26	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
27	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	25.06	12/2015 -	08/2017	20	-
	Total		18,019.95 -	19,893.53	7,901.72				
<u>Steel</u>									
28	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	14,002.26	12/2011 -	12/2012	12	-
29	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,189.32	12/2011 -	12/2012	12	-
30	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	250.59	08/2010 -	01/2013	29	-
31	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 -	12,291.00	9,958.76	10/2009 -	03/2013	41	-
32	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	343.48	12/2011 03/2012	03/2013	15	12
33	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	118.28	10/2012 -	03/2013	5	-
34	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	254.09	02/2011 -	03/2013	25	-
35	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,282.41	12/2012 -	03/2013	3	-
36	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	226.41	05/2012 -	06/2013	13	-
37	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	7,353.31	03/2013 -	09/2013	6	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
Total			50,973.89	57,131.43	36,978.91				
<u>Petrochemicals</u>									
38	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	5,981.96	04/2012 12/2013	12/2013	20	0
Total			5,460.61	8,920.00	5,981.96				
<u>Petroleum</u>									
39	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,583.21	05/2010 05/2012	01/2013	32	8
40	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	977.00	629.62	12/2011	01/2013	13	-
41	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	271.67	04/2011	01/2013	21	-
42	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 312.00	312.00	276.60	01/2012 01/2012	01/2013	12	12
43	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57	1,043.57	997.72	04/2012	01/2013	9	-
44	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	2,174.00	1,249.87	09/2011	02/2013	17	-
45	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	277.79	03/2006 03/2013	03/2013	84	0
46	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,154.13	05/2010 03/2013	03/2013	34	0
47	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,480.21	09/2011 03/2012	03/2013	18	12

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
48	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL, Orissa	12/2009	1,492.33	1,492.33	1,170.37	06/2012	03/2013	9	-
49	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24	22
50	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50	341.50	145.56	02/2013	03/2013	1	-
51	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00	12,160.26	8,570.48	01/2012	03/2013	14	-
52	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
53	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
54	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11	372.11	115.70	03/2013	04/2013	1	-
55	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02	740.02	566.23	03/2010 03/2012	05/2013	38	14
56	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34	12
57	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	253.66	165.66	08/2012	05/2013	9	-
58	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86	12
59	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64	2,163.64	1,147.97	06/2012	06/2013	12	-
60	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL, Uttar Pradesh	07/2010	1,000.00	1,000.00	351.23	01/2013	06/2013	5	-
61	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00	30,426.00	19,629.00	11/2012	09/2013	10	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
62	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	4,524.89	09/2012	09/2013	12	-
63	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	240.95	47.51	09/2012	09/2013	12	-
64	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	72.36	11/2012	10/2013	11	-
65	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8	-
66	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	756.65	80.91	05/2013	11/2013	6	-
67	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,919.55	08/2010 03/2012	12/2013	40	21
68	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	344.48	09/2011	12/2013	27	-
69	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	27.13	08/2013	01/2014	5	-
70	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	634.47	03/2007 03/2014	03/2014	84	0
71	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	1,175.96	03/2013	03/2014	12	-
72	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	820.00	-	06/2012	03/2014	21	-
73	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	1,126.97	12/2012 12/2012	03/2014	15	15
74	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	676.54	03/2013	04/2014	13	-
75	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	4.49	10/2010	12/2014	50	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
76	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.54	01/2013	07/2015	30	-
77	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.00	03/2007 03/2017	03/2017	120	0
	Total		107,659.63	121,546.03	72,090.96				
			-	-					
	Power								
78	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	775.29	02/2011 10/2012	01/2013	23	3
79	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	333.83	07/2011	01/2013	18	-
80	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,638.44	03/2007 09/2012	02/2013	71	5
81	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	758.75	595.50	01/2010	02/2013	37	-
82	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29	2,081.00	1,860.84	11/2009 02/2013	03/2013	40	1
83	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,843.11	09/2008	03/2013	54	-
84	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	868.00	10/2009	03/2013	41	-
85	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	420.80	09/2010	03/2013	30	-
86	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,626.00	08/2012	03/2013	7	-
87	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,149.50	02/2012	03/2013	13	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
88	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	4,051.00	10/2012 -	03/2013	5	-
89	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,093.40	06/2012 -	03/2013	9	-
90	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	131.78	06/2012 -	03/2013	9	-
91	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	167.80	04/2012 -	03/2013	11	-
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	81.30	01/2013 -	03/2013	2	-
93	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	57.90	10/2012 -	03/2013	5	-
94	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	814.50	08/2010 01/2013	06/2013	34	5
95	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,158.70	12/2012 -	06/2013	6	-
96	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	696.50	05/2012 -	06/2013	13	-
97	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,996.58	10/2010 01/2013	09/2013	35	8
98	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	155.70	11/2011 -	09/2013	22	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	642.50	04/2013 -	10/2013	6	-
100	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,814.00	10/2012 -	11/2013	13	-
101	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	58.40	01/2013 -	11/2013	10	-
102	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,252.08	09/2009 06/2013	12/2013	51	6
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	335.30	11/2011 -	12/2013	25	-
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	348.20	11/2011 -	12/2013	25	-
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	248.30	02/2012 -	12/2013	22	-
106	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,124.70	10/2012 -	12/2013	14	-
107	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,994.10	08/2012 -	12/2013	16	-
108	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,515.00	08/2012 -	12/2013	16	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
109	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,063.60	12/2012 -	12/2013	12	-
110	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	806.70	08/2012 -	12/2013	16	-
111	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	478.50	11/2012 -	12/2013	13	-
112	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	2,113.01	01/2012 -	02/2014	25	-
113	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,891.70	11/2012 -	03/2014	16	-
114	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	479.40	11/2012 -	03/2014	16	-
115	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.	10/2002	4,527.15 -	6,358.91	4,669.00	04/2009 -	09/2014	65	-
116	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO, Arunachal Pr.	12/2008	573.99 -	573.99	450.04	08/2012 08/2013	09/2014	25	13
117	BARH STPP STAGE -II - [N18000047]NTPC, Bihar	02/2008	7,341.04 -	7,341.04	4,861.00	08/2013 -	09/2014	13	-
118	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,326.50	08/2013 -	09/2014	13	-
119	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, Mizoram	01/2011	913.63 913.63	913.63	374.97	07/2014 -	02/2015	7	-
120	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	14.90	04/2015 -	05/2015	1	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
121	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,640.00	03/2013 -	09/2015	30	-
122	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,494.00	07/2011 -	10/2015	51	-
123	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,722.00	12/2009 -	03/2016	75	-
124	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 -	3,422.44	331.12	07/2014 -	05/2016	22	-
125	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	435.00	07/2010 02/2016	11/2016	76	9
126	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,935.69	01/2016 01/2016	11/2016	10	10
127	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,872.26	09/2010 08/2014	03/2017	78	31
128	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	2,063.68	05/2013 06/2016	03/2017	46	9
129	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,694.37	09/2009 07/2014	03/2018	102	44
Total			131,109.81	146,326.91	94,566.49				
<u>Railways</u>									
130	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya Pradesh	09/2007	687.20 -	687.20	682.45	03/2010 -	12/2012	33	-
131	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	309.91	06/2004 -	12/2012	102	-
132	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	697.50	439.54	03/2012 03/2012	12/2012	9	9
133	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	884.81	03/2009 12/2012	12/2012	45	0
134	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,604.67	10/2007 12/2012	12/2012	62	0

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
135	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	914.71	12/2012 01/2013	01/2013	1	0
136	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	685.77	03/2012 08/2012	02/2013	11	6
137	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	266.03	02/2011 02/2011	02/2013	24	24
138	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	458.91	12/2012 12/2012	02/2013	2	2
139	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	167.73	63.02	03/2012 -	02/2013	11	-
140	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-
141	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	207.83	03/2002 -	03/2013	132	-
142	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	638.03	12/2011 12/2011	03/2013	15	15
143	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	261.43	03/2012 03/2012	03/2013	12	12
144	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	279.69	03/2012 03/2013	03/2013	12	0
145	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	406.58	03/2012 03/2013	03/2013	12	0
146	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	118.66	03/2012 -	03/2013	12	-
147	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	258.82	02/2009 02/2009	04/2013	50	50
148	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	228.88	03/2009 03/2009	04/2013	49	49
149	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	119.21	12/2011 11/2013	11/2013	23	0
150	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	105.70	02/2006 -	12/2013	94	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
151	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	149.41	12/2012 -	12/2013	12	-
152	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	206.15	03/2004 12/2010	03/2014	120	39
153	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,329.90	12/2008 -	03/2014	63	-
154	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	177.00	06/2013 06/2013	03/2014	9	9
155	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	416.20	03/2013 -	03/2014	12	-
156	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	819.40	170.80	03/2010 06/2014	06/2014	51	0
157	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,291.16	03/2009 -	12/2014	69	-
158	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	173.17	03/2007 03/2007	03/2015	96	96
159	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	735.14	12/2010 12/2010	03/2015	51	51
160	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	116.35	12/2012 -	03/2015	27	-
161	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	5,016.00	2,590.05	04/2008 03/2014	12/2015	92	21
162	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	246.13	02/2010 11/2012	12/2015	70	37
163	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	449.26	03/2014 -	12/2015	21	-
164	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	1,079.17	03/2011 03/2014	03/2016	60	24

List of Delay Project w.r.t Original and Revised

(Dec,2012)

						Date of Commissioning			
S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	
165	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	923.12	03/2014 03/2016	03/2016	24	0
166	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	40.20	03/2014 03/2016	03/2016	24	0
167	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	461.37	03/2005 12/2008	06/2016	135	90
168	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	431.61	06/2005 07/2011	06/2016	132	59
169	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	33.08	03/2016 -	06/2016	3	-
170	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	31.46	04/2014 -	03/2017	35	-
171	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24	-
172	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,J and K	03/1995	2,500.00 2,500.00	20,000.00	8,549.43	03/2001 -	12/2017	201	-
173	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	57.12	12/2015 -	03/2020	51	-
Total			29,131.38 -	76,631.51	31,155.65				
<u>Road Transport & Highways</u>									
174	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	187.62	08/2004 07/2010	01/2013	101	30
175	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	189.74	08/2004 -	01/2013	101	-
176	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	148.22	04/2004 -	01/2013	105	-
177	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	01/2013	94	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
178	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	163.43	03/2008 -	01/2013	58	-
179	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	260.71	01/2009 -	01/2013	48	-
180	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	275.64	10/2008 -	01/2013	51	-
181	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	257.43	06/2011 06/2011	01/2013	19	19
182	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	01/2013	43	-
183	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	272.12	02/2004 -	01/2013	107	-
184	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	194.51	02/2004 -	01/2013	107	-
185	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,675.10	08/2011 -	01/2013	17	-
186	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	01/2013	11	-
187	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.68	10/2008 -	02/2013	52	-
188	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	244.46	10/2008 -	02/2013	52	-
189	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	02/2013	40	-
190	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25	-
191	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,055.70	05/2012 -	02/2013	9	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
192	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	214.65	09/2007 -	03/2013	66	-
193	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	281.08	09/2007 -	03/2013	66	-
194	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	136.31	09/2008 -	03/2013	54	-
195	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	230.62	06/2005 -	03/2013	93	-
196	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	249.18	05/2008 -	03/2013	58	-
197	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.44	10/2008 -	03/2013	53	-
198	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	392.37	03/2008 -	03/2013	60	-
199	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	283.67	02/2009 03/2014	03/2013	49	-12
200	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	124.50	04/2009 -	03/2013	47	-
201	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	217.01	06/2008 -	03/2013	57	-
202	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	187.10	07/2008 -	03/2013	56	-
203	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	295.86	06/2008 -	03/2013	57	-
204	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60	-
205	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	252.98	06/2008 -	03/2013	57	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
206	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	191.01	05/2008 -	03/2013	58	-
207	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	238.37	06/2008 -	03/2013	57	-
208	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	500.28	09/2009 -	03/2013	42	-
209	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32	-
210	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	637.97	05/2010 -	03/2013	34	-
211	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,909.50	09/2012 -	03/2013	6	-
212	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	03/2013	9	-
213	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,935.90	10/2012 -	03/2013	5	-
214	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,591.80	12/2012 -	03/2013	3	-
215	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	417.69	09/2008 -	05/2013	56	-
216	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	314.73	10/2008 -	06/2013	56	-
217	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54	-
218	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	274.33	09/2010 -	06/2013	33	-
219	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,221.90	07/2012 -	06/2013	11	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
220	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,737.60	10/2011 -	06/2013	20	-
221	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	721.45	10/2011 -	06/2013	20	-
222	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	1,205.00	11/2012 -	06/2013	7	-
223	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	68.37	04/2009 -	07/2013	51	-
224	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	100.53	11/2008 -	07/2013	56	-
225	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	495.30	12/2009 -	07/2013	43	-
226	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,465.50	11/2011 -	08/2013	21	-
227	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-
228	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	209.00	3.82	01/2013 -	10/2013	9	-
229	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	256.64	06/2008 -	12/2013	66	-
230	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	278.20	06/2008 -	12/2013	66	-
231	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	296.81	11/2008 -	12/2013	61	-
232	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	277.51	04/2008 -	12/2013	68	-
233	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-
234	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60 -	407.60	186.07	06/2010 -	12/2013	42	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
235	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
236	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	193.45	37.68	11/2012 -	12/2013	13	-
237	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	175.59	10/2008 -	01/2014	63	-
238	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	26.83	11/2008 -	01/2014	62	-
239	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	325.00	419.12	05/2013 -	02/2014	9	-
240	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	157.34	04/2008 -	03/2014	71	-
241	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	213.71	04/2008 -	03/2014	71	-
242	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	234.82	04/2010 -	03/2014	47	-
243	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	194.93	09/2007 -	03/2014	78	-
244	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	382.26	10/2011 -	03/2014	29	-
245	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	391.73	05/2013 -	03/2014	10	-
246	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	482.60	03/2013 -	03/2014	12	-
247	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttaranchal	11/2011	478.00 -	478.00	229.22	10/2013 -	03/2014	5	-
248	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	-	10/2013 -	03/2014	5	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
249	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014	79	-
250	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	72.50	07/2009 -	04/2014	57	-
251	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	292.53	02/2014 -	04/2014	2	-
252	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
253	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	34.97	09/2013 -	07/2014	10	-
254	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90 -	635.90	-	07/2012 -	07/2014	24	-
255	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
256	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
257	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31	-
258	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
259	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
Total			42,151.63 -	44,090.25	42,017.52				
Shipping & Ports									
260	Construction of berthing and allied facilities off - [N25000037]PORT TRUST, Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
261	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,644.30	01/2012 09/2012	02/2013	13	5

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
262	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
263	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87	0
264	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 -	06/2013	5	-
265	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	894.93	12/2010 09/2012	10/2013	34	13
266	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	337.00	12/2012 12/2012	10/2013	10	10
Total			7,295.21 -	8,778.82	5,304.47				
Telecommunications									
267	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	818.09	11/2010 -	12/2012	25	-
268	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	67.21	02/2007 03/2012	02/2013	72	11
269	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	229.41	67.19	03/2012 -	02/2013	11	-
270	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	03/2013	51	-
271	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	80.05	06/2009 -	03/2013	45	-
272	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	03/2013	48	-

List of Delay Project w.r.t Original and Revised

(Dec,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
273	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53	-
274	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	06/2013	32	15
Total			2,967.14 -	2,971.01	1,616.55				
<u>Urban Development</u>									
275	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21	-
Total			6,395.00 -	11,609.00	2,267.57				
<u>Water Resources</u>									
276	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-
Total			542.90 -	1,187.00	35.49				
Grand Total			441,244.73	543,104.56	321,498.08				

Sectorwise Summary On Schedule

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Civil Aviation	2	1,078.00	.00	1,078.00	426.69
Coal	29	17,787.48	.00	17,367.96	5,511.95
Fertilisers	3	4,065.66	.00	4,065.66	946.00
Petroleum	21	53,449.09	.00	53,320.83	5,991.32
Power	45	95,695.82	.00	95,695.82	13,204.60
Railways	7	9,618.14	654.51	10,571.43	1,401.25
Road Transport & Highways	54	48,197.27	.00	48,197.27	23,343.08
Shipping & Ports	1	966.46	.00	994.82	248.23
Steel	3	842.10	.00	842.10	23.71
Urban Development	2	37,736.00	.00	37,736.00	1,441.24
Grand total	167	269,436.02	654.51	269,869.89	52,538.07

List of On schedule Projects

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	376.96	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070	2/2011	452.00 -	452.00	49.73	03/2015 -	03/2015
	Total		1,078.00 -	1,078.00	426.69		
	<u>Coal</u>						
3	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093	6/2010	2,675.67 -	2,675.67	1,396.85	03/2014 -	03/2014
4	KRISHNASHILA (NCL) (4MTY) - [N06000007	6/2011	789.88 -	741.62	334.67	03/2013 -	03/2013
5	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	165.15	03/2015 03/2015	03/2015
6	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.95	03/2014 03/2014	03/2014
7	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	117.63	03/2017 -	03/2017
8	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	71.37	03/2015 -	03/2015
9	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
10	KARMA OCP - [N06000088	6/2009	162.46 -	162.46	30.89	03/2014 -	03/2014
11	Rajrappa RCE OCP - [N06000087	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016
12	Purnadih OCP - [N06000085	7/2008	210.98 -	210.98	91.35	03/2013 -	03/2013
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	94.86	03/2016 -	03/2016
14	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	204.96	03/2014 -	03/2014
15	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	29.45	03/2015 -	03/2015
16	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.63 -	479.63	114.38	03/2013 -	03/2013
17	RAJMAHAL OC EXP. - [N06000056	9/2009	153.82 -	153.82	24.39	03/2014 -	03/2014
18	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	39.81	03/2016 -	03/2016
20	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
21	Muraidih UG Turn-key Project - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
22	JALAGAM VENGALA RAO OCP - [N06000094	7/2011	447.06 -	447.06	-	03/2015 -	03/2015
23	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
24	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	3.87	03/2018 03/2018	03/2018
25	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
26	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	44.23	03/2016 -	03/2016
27	KANIHA OCP, MCL, (10.0 Mty) - [N06000035	12/2007	457.77 -	457.77	112.76	03/2013 -	03/2013
28	JALLARAM SHAFT PROJECT - [N06000025	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
29	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	391.28	03/2016 03/2016	03/2016
30	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008	6/2008	1,188.31 -	1,188.31	675.55	03/2013 -	03/2013
31	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094	12/2009	1,943.66 -	1,943.66	1,243.76	03/2014 -	03/2014
	Total		17,787.48 -	17,367.96	5,511.95		
Fertilisers							
32	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJECT - [N08000004	1/2010	1,292.84 -	1,292.84	946.00	01/2013 -	01/2013
33	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJECT - [N08000005	1/2010	1,294.19 -	1,294.19	-	01/2013 -	01/2013
34	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT [N08000006	1/2010	1,478.63 -	1,478.63	-	01/2013 -	01/2013
	Total		4,065.66 -	4,065.66	946.00		
Petroleum							
35	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	4/2008	825.00 -	1,827.00	1,124.47	04/2013 -	04/2013
36	Development of WO-16 Cluster Fields - [N16000105	6/2010	2,523.00 -	2,523.00	406.26	01/2014 -	01/2014
37	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA [N16000112	8/2010	8,140.00 -	8,140.00	2,760.15	02/2014 -	02/2014
38	Wax Project - [N16000101	6/2010	576.60 -	576.60	89.68	12/2013 -	12/2013
39	Ahmedabad Redevelopment - [N16000120	11/2010	1,916.10 -	1,916.10	711.28	12/2014 -	12/2014

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	4.84	12/2014 -	12/2014
41	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	26.42	05/2015 -	05/2015
42	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
43	DABHOL BANGALORE PIPELINE PROJECT PHASE-II [N16000147	6/2009	486.00 -	486.00	34.88	09/2013 -	09/2013
44	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	666.00	-	11/2015 -	11/2015
45	REWARI KANPUR PIPELINE PROJECT - [N16000145	3/2012	1,210.64 -	1,210.64	-	03/2015 -	03/2015
46	Integrated Refinery Expansion Project - [N16000143	1/1999	14,225.00 -	14,225.00	9.21	12/2015 -	12/2015
47	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014
48	IOR of B-173A Field - [N16000140	1/2012	352.49 -	352.49	-	03/2014 -	03/2014
49	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	21.38	03/2014 -	03/2014
50	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	74.11	05/2014 -	05/2014
51	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
52	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE [N16000149	8/2011	586.00 -	586.00	4.26	07/2015 -	07/2015
53	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	913.00	21.50	07/2015 -	07/2015
54	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015
55	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
	Total		53,449.09 -	53,320.83	5,991.32		
Power							
56	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144	9/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016
57	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	9/2010	2,074.86 -	2,074.86	772.70	03/2013 -	03/2013
58	Northern Region system strengthening scheme-XXII - [N18000091	12/2010	209.78 -	209.78	106.90	08/2013 -	08/2013
59	Transmission system for phase-I generation projects in orissa-part B - [N18000093	12/2010	2,743.19 -	2,743.19	1,090.50	12/2013 -	12/2013
60	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV [N18000115	12/2011	297.33 -	297.33	38.80	08/2014 -	08/2014

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
61	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	116.50	02/2014 -	02/2014
62	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2 - [N18000113	12/2011	2,422.66 -	2,422.66	114.00	08/2014 -	08/2014
63	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112	11/2011	2,127.51 -	2,127.51	310.30	07/2014 -	07/2014
64	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111	8/2011	1,637.34 -	1,637.34	367.00	08/2014 -	08/2014
65	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	71.90	06/2014 -	06/2014
66	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107	8/2011	1,391.97 -	1,391.97	631.70	12/2013 -	12/2013
67	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED [N18000106	8/2011	425.51 -	425.51	158.30	10/2013 -	10/2013
68	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	336.10	12/2013 -	12/2013
69	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	380.90	06/2015 -	06/2015
70	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
71	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
72	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122	2/2012	1,927.16 -	1,927.16	50.70	10/2014 -	10/2014
73	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121	2/2012	324.33 -	324.33	2.20	08/2014 -	08/2014
74	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120	2/2012	1,310.85 -	1,310.85	123.80	02/2015 -	02/2015
75	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118	1/2012	259.28 -	259.28	41.30	01/2014 -	01/2014
76	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117	1/2012	1,422.85 -	1,422.85	134.40	01/2015 -	01/2015
77	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	1,746.65	57.30	08/2014 -	08/2014
78	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A [N18000138	12/2012	156.04 -	156.04	-	10/2014 -	10/2014

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID [N18000137]	9/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014
80	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI [N18000136]	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
81	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	150.00	08/2015 -	08/2015
82	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,137.00	11/2016 -	11/2016
83	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	634.00	09/2016 -	09/2016
84	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	1,116.00	12/2016 -	12/2016
85	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID [N18000130]	6/2012	1,263.26 -	1,263.26	183.60	11/2014 -	11/2014
86	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B [N18000129]	2/2012	3,201.44 -	3,201.44	135.60	10/2014 -	10/2014
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV [N18000128]	11/2011	723.63 -	723.63	60.20	11/2014 -	11/2014
88	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	82.30	08/2014 -	08/2014
89	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	33.70	06/2014 -	06/2014
90	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]	10/2011	558.26 -	558.26	84.50	11/2013 -	11/2013
91	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	475.30	09/2014 -	09/2014
92	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]	7/2011	181.93 -	181.93	65.40	07/2013 -	07/2013
93	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	528.60	05/2014 -	05/2014
94	Transmission system for transfer of power from Gen.proj in sikkim to NRWR part-B [N18000099]	3/2011	1,585.12 -	1,585.12	621.00	11/2013 -	11/2013
95	Supplementary transmission associated with vellur TPS - [N18000097]	8/2010	170.36 -	170.36	58.10	04/2013 -	04/2013
96	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]	3/2011	2,569.25 -	2,569.25	937.00	03/2014 -	03/2014
97	Northern region system strengthening scheme XVI - [N18000094]	7/2010	752.64 -	752.64	225.00	07/2013 -	07/2013
98	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]	12/2010	1,719.52 -	1,719.52	764.20	08/2013 -	08/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	Transmission system associated with krishnapatnam- Part-A - [N18000090	12/2010	779.21 -	779.21	670.20	08/2013 -	08/2013
100	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077	4/2010	4,404.57 -	4,404.57	337.60	01/2015 -	01/2015
	Total		95,695.82 -	95,695.82	13,204.60		
<u>Railways</u>							
101	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	7/1996	653.84 654.51	1,302.12	608.97	06/2013 06/2013	06/2013
102	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111	4/2010	2,619.02 -	2,913.51	207.96	03/2016 -	03/2016
103	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113	4/2008	653.19 -	653.46	215.07	03/2014 -	03/2014
104	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	4/2008	394.14 -	404.39	3.77	03/2013 -	03/2013
105	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114	4/2008	516.23 -	516.23	312.64	03/2014 -	03/2014
106	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112	4/2008	829.74 -	829.74	9.04	03/2015 -	03/2015
107	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	43.80	03/2016 -	03/2016
	Total		9,618.14 -	10,571.43	1,401.25		
<u>Road Transport & Highways</u>							
108	Indore-Jhabua-Gujrat/MP - [N24000136	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
109	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139	9/2010	1,655.00 -	1,655.00	465.86	09/2013 -	09/2013
110	Hazaribagh-Ranchi - [N24000141	8/2010	625.07 -	625.07	876.70	01/2013 -	01/2013
111	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	05/2013
112	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	995.04	10/2014 -	10/2014
113	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	992.49	08/2014 -	08/2014
114	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	31.33	10/2014 -	10/2014
115	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	199.69	07/2014 -	07/2014
116	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	11.32	01/2014 -	01/2014

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
117	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	529.67	09/2014 -	09/2014
118	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	149.40	06/2014 -	06/2014
119	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
120	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	107.47	08/2013 -	08/2013
121	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	849.93	08/2013 -	08/2013
122	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	218.98	09/2013 -	09/2013
123	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213	4/2012	624.00 -	624.00	-	04/2014 -	04/2014
124	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
125	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	597.32	06/2014 -	06/2014
126	JAIPUR-REENGUS - [N24000198	8/2010	267.81 -	267.81	557.22	02/2013 -	02/2013
127	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	152.77	09/2014 -	09/2014
128	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
129	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	449.35	08/2013 -	08/2013
130	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.55	01/2014 -	01/2014
131	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	112.67	01/2014 -	01/2014
132	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.82	06/2013 -	06/2013
133	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013
134	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
135	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	722.53	08/2013 -	08/2013
136	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	811.74	11/2013 -	11/2013
137	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	646.53	08/2013 -	08/2013
138	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,110.70	06/2013 -	06/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
139	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	599.37	02/2013 -	02/2013
140	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	1,043.20	03/2013 -	03/2013
141	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	303.40	02/2014 -	02/2014
142	2laning with PS Gopalganj- Chappra - [N24000190	12/2011	325.00 -	325.00	131.68	05/2014 -	05/2014
143	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
144	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	274.81	11/2013 -	11/2013
145	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	480.07	07/2013 -	07/2013
146	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	45.59	04/2014 -	04/2014
147	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	472.14	03/2014 -	03/2014
148	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
149	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	697.74	03/2014 -	03/2014
150	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	266.79	02/2014 -	02/2014
151	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	418.50	01/2014 -	01/2014
152	SAMAIKHALI - GANDHIDHAM - [N24000179	9/2010	805.39 -	805.39	393.68	03/2013 -	03/2013
153	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
154	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	213.01	08/2013 -	08/2013
155	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	83.75	05/2013 -	05/2013
156	Kandla - Mundra port - [N24000175	1/2011	953.88 -	953.88	459.93	07/2013 -	07/2013
157	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
158	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013
159	DEOLI-KOTA - [N24000148	1/2011	593.00 -	593.00	441.00	07/2013 -	07/2013
160	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM [N24000144	9/2010	852.00 -	852.00	770.65	03/2013 -	03/2013
161	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	817.67	11/2013 -	11/2013
	Total		48,197.27 -	48,197.27	23,343.08		

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Shipping & Ports</u>						
162	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
	Total		966.46 -	994.82	248.23		
	<u>Steel</u>						
163	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075	11/2011	254.55 -	254.55	12.02	11/2013 -	11/2013
164	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	11.43	08/2014 -	08/2014
165	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	0.26	12/2014 -	12/2014
	Total		842.10 -	842.10	23.71		
	<u>Urban Development</u>						
166	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	1,300.35	03/2016 -	03/2016
167	FARIDABAD EXTENSION - [N28000057	9/2011	2,494.00 -	2,494.00	140.89	09/2014 -	09/2014
	Total		37,736.00 -	37,736.00	1,441.24		
	Grand Total		269,436.02	269,869.89	52,538.07		

Sectorwise Summary of Project Without Milestone

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	1	1,106.29	.00	1,106.29	1,084.24
Civil Aviation	6	5,473.58	2,015.00	6,063.07	4,735.60
Coal	6	3,868.49	1,666.38	3,657.55	239.72
Petroleum	51	110,071.93	41,267.50	121,539.93	42,533.64
Power	14	12,580.60	.00	13,020.97	1,981.78
Railways	124	60,790.08	64,554.51	146,351.78	59,935.56
Road Transport & Highways	139	90,152.40	.00	92,091.02	65,103.17
Shipping & Ports	19	15,753.13	9,886.33	17,921.56	8,042.54
Steel	2	587.55	.00	587.55	11.69
Telecommunications	14	5,964.89	1,089.32	5,905.68	1,728.20
Urban Development	3	37,850.18	173.08	37,909.08	1,441.24
Water Resources	1	542.90	.00	1,187.00	35.49
Grand total	380	344,742.02	120,652.12	447,341.48	186,872.87

List of Projects Without Milestones

(Dec,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	-	0/0
			-	-		
	Total		1,106.29			0/0
			-			
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012	0/0
			2,015.00	02/2012		
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011	03/2013	0/0
			-	-		
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	05/2012	03/2013	0/0
			-	-		
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011	04/2013	0/0
			-	04/2013		
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013	0/0
			-	-		
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	03/2015	03/2015	0/0
			-	-		
	Total		5,473.58			0/0
			-			
<u>Coal</u>						
8	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	03/2014	03/2014	0/0
			-	-		
9	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	04/2014	04/2014	0/0
			-	-		
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04	03/2015	03/2015	0/0
			535.10	03/2015		
11	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	04/2015	04/2015	0/0
			-	-		
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	03/2016	03/2016	0/0
			-	-		
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	03/2018	03/2018	0/0
			1,131.28	03/2018		
	Total		3,868.49			0/0
			-			
<u>Steel</u>						
14	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	08/2014	08/2014	0/0
			-	-		
15	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Orissa	01/2012	254.90	12/2014	12/2014	0/0
			-	-		
	Total		587.55			0/0
			-			
<u>Petroleum</u>						

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
16	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 -	09/2012	0/0
17	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	01/2013	0/0
18	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
19	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	01/2013	0/0
20	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	01/2013	0/0
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
22	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	03/2013	0/0
23	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	03/2013	0/0
24	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
25	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
26	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
27	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
28	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
29	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	05/2013	0/0
30	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
31	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
32	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
33	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
34	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	09/2013	0/0
35	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
36	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
37	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	11/2013	0/0
38	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
39	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2013	0/0
40	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0
41	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
42	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
43	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
44	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
45	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	03/2014	0/0
46	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00 -	03/2014 -	03/2014	0/0
47	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	03/2014	0/0
48	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	03/2013 -	04/2014	0/0
49	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
50	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
51	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
52	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
53	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
54	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
55	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
56	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
57	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	03/2012	1,210.64 -	03/2015 -	03/2015	0/0
58	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
59	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
60	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0
61	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
62	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	07/2015 -	07/2015	0/0
63	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
64	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	12/2015	0/0
65	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
66	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	04/2012 -	-	0/0
Total			110,071.93 -			0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
Power						
67	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	03/2013	0/0
			-	-		
68	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	07/2013	07/2013	0/0
			-	-		
69	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	09/2009	12/2013	0/0
			-	06/2013		
70	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	03/2014	03/2014	0/0
			-	-		
71	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	08/2014	08/2014	0/0
			-	-		
72	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	09/2014	09/2014	0/0
			-	-		
73	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04	10/2014	10/2014	0/0
			-	-		
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63	11/2014	11/2014	0/0
			-	-		
75	SYSTEM STRENGTHENING-XXVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	11/2014	11/2014	0/0
			-	-		
76	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	12/2014	12/2014	0/0
			-	-		
77	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	02/2015	02/2015	0/0
			-	-		
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34	03/2015	03/2015	0/0
			-	-		
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40	04/2015	05/2015	0/0
			-	-		
80	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	06/2016	06/2016	0/0
			-	-		
Total			12,580.60			0/0
			-			
Railways						
81	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	-	03/2011	0/0
			-	03/2009		
82	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00	03/2009	03/2011	0/0
			380.00	11/2012		
83	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	03/2010	03/2012	0/0
			-	-		
84	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	03/2010	12/2012	0/0
			-	-		
85	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	03/1998	08/2005	0/0
			604.04	08/2005		
86	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00	06/2007	06/2007	0/0
			625.30	-		
87	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00	07/2008	07/2008	0/0
			363.26	-		
88	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42	-	05/2009	0/0
			369.70	05/2009		
89	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36	-	03/2010	0/0
			768.87	03/2010		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
90	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
91	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
92	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
93	REWARI-ROHTAK (NL), NR - [220100279]NR, Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
94	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
95	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
96	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
97	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
98	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
99	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR, Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
100	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012	0/0
101	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
102	Dakshin-barasat-lakshmikanthapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
103	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
104	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
105	MUNEERABAD-MAHABOONNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
106	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
107	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
108	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
109	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE, Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
110	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE, Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
111	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
112	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR, Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
113	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
114	JIND-SONEPAT (NL), NR - [220100280]NR, Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
115	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
116	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2012	0/0
117	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
118	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
119	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0
120	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	02/2013	0/0
121	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
122	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
123	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
124	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
125	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
126	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2013	0/0
127	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
128	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	03/2013	0/0
129	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
130	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
131	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2013	0/0
132	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
133	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2013	0/0
134	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
135	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
136	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
137	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya Pradesh	04/2008	603.04 603.04	03/2012 -	03/2013	0/0
138	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
139	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
140	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
141	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
142	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2013	06/2013	0/0
143	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	- -	06/2013	0/0
144	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
145	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
146	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	12/2013	0/0
147	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
148	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
149	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
150	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
151	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
152	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
153	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
154	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
155	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
156	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 06/2014	06/2014	0/0
157	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2014	0/0
158	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
159	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
160	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
161	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
162	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
163	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0
164	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
165	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 11/2012	12/2015	0/0
166	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
167	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2016	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
168	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2016	0/0
169	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
170	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
171	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
172	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
173	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
174	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
175	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
176	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	04/2014 -	03/2017	0/0
177	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,J and K	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
179	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
180	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
181	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
182	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
183	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
184	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.64	- 09/2009	-	0/0
185	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-	0/0
186	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-	0/0
187	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
188	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
189	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
190	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
191	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	-	0/0
192	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
193	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
194	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
195	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
196	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
197	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
198	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
199	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
200	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
201	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
202	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
203	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
204	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		60,790.08 -			0/0
Road Transport & Highways						
205	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	01/2013	0/0
206	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	01/2013	0/0
207	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	01/2013	0/0
208	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	01/2013	0/0
209	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	01/2013	0/0
210	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	01/2013	0/0
211	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	01/2013	0/0
212	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	01/2013	0/0
213	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	01/2013	0/0
214	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	01/2013	0/0
215	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	01/2013	0/0
216	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07 -	01/2013 -	01/2013	0/0
217	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	01/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
218	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	02/2013	0/0
219	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	02/2013	0/0
220	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	02/2013	0/0
221	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	02/2013	0/0
222	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	02/2013	0/0
223	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
224	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
225	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2013	0/0
226	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	03/2013	0/0
227	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
228	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2013	0/0
229	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	03/2013	0/0
230	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2013	0/0
231	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	03/2013	0/0
232	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	03/2013	0/0
233	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
234	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2013	0/0
235	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
236	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	03/2013	0/0
237	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	03/2013	0/0
238	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	03/2013	0/0
239	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	03/2013	0/0
240	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	03/2013	0/0
241	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	03/2013	0/0
242	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
243	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
244	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	03/2013	0/0
245	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	03/2013	0/0
246	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	03/2013	0/0
247	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	03/2013	0/0
248	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
249	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
250	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
251	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
252	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	05/2013	0/0
253	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
254	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
255	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	06/2013	0/0
256	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2013	0/0
257	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	06/2013	0/0
258	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	06/2013	0/0
259	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	06/2013	0/0
260	Chilkalripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
261	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
262	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
263	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
264	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
265	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
266	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
267	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	07/2013	0/0
268	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	07/2013 -	07/2013	0/0
269	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
270	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	07/2013	07/2013	0/0
271	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	11/2011	08/2013	0/0
272	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	08/2013	08/2013	0/0
273	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
274	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	08/2013	08/2013	0/0
275	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	08/2013	08/2013	0/0
276	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
277	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	08/2013	08/2013	0/0
278	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	08/2013	08/2013	0/0
279	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
280	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
281	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	05/2012	10/2013	0/0
282	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
283	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	01/2013	10/2013	0/0
284	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
285	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
286	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
287	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
288	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	06/2008	12/2013	0/0
289	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	06/2008	12/2013	0/0
290	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	11/2008	12/2013	0/0
291	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	04/2008	12/2013	0/0
292	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	02/2010	12/2013	0/0
293	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	06/2010	12/2013	0/0
294	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	06/2011	12/2013	0/0
295	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	11/2012	12/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
296	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
297	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
298	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	01/2014	0/0
299	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	01/2014	0/0
300	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
301	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
302	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00 -	01/2014 -	01/2014	0/0
303	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
304	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
305	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
306	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhandd	02/2012	398.00 -	02/2014 -	02/2014	0/0
307	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
308	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
309	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	03/2014	0/0
310	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
311	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
312	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
313	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
314	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
315	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
316	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttaranchal	11/2011	478.00 -	10/2013 -	03/2014	0/0
317	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	03/2014	0/0
318	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
319	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
320	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
321	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
322	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
323	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
324	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
325	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
326	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
327	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
328	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
329	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
330	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
331	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
332	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
333	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
334	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
335	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
336	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
337	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
338	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
339	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
340	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
341	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
342	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
343	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		90,152.40 -			0/0
Shipping & Ports						
344	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008	0/0
345	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
346	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
347	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 272.50	06/2011 -	10/2012	0/0
348	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
349	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012	0/0
350	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
351	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
352	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	02/2013	0/0
353	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
354	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0
355	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
356	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 -	06/2013	0/0
357	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2013	0/0
358	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 12/2012	10/2013	0/0
359	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 12/2013	10/2013	0/0
360	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	-	0/0
361	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
362	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
	Total		15,753.13 -			0/0
Telecommunications						
363	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
364	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	12/2012	0/0
365	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
366	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	02/2013	0/0
367	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	03/2013	0/0
368	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	03/2013	0/0
369	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
370	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2013	0/0
371	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	06/2013	0/0
372	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
373	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
374	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
375	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
376	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
	Total		5,964.89 -			0/0
Urban Development						
377	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
378	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
379	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
380	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			344,742.02			0/0

List of ongoing projects having cost overrun w.r.to original

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	15,276.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	3,960.33	09/2010 -	-
	Total		16,663.00 -	22,947.00	19,236.33		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,199.24	05/2011 -	03/2013
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) [N04000038]	08/2008	1,808.00 -	2,015.00	1,742.12	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	23,177.69		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,536.19	06/2009 -	09/2013
6	MAGADH OC (CCL) - [N06000015]	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	424.32	03/2013 -	07/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	117.63	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	4,909.54	3,709.61	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	204.96	03/2014 -	03/2014
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	94.86	03/2016 -	03/2016
	Total		8,579.45 -	37,918.25	30,284.49		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	5,981.96	04/2012 -	12/2013
	Total		5,460.61 -	46,838.25	36,266.45		
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	634.47	03/2007 -	03/2014

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.00	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	277.79	03/2006 -	03/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
18	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,583.21	05/2010 -	01/2013
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	3,919.55	08/2010 03/2012	12/2013
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,154.13	05/2010 -	03/2013
22	RESITMENT OF MARKETING INSTALATION AT VISAKH [N16000057	01/2009	756.00 -	898.00	909.00	- -	-
23	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	19,629.00	11/2012 -	09/2013
24	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI [N16000066	01/2008	224.00 -	394.00	377.13	- -	-
25	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	276.60	01/2012 -	01/2013
26	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	1,124.47	04/2013 -	04/2013
27	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
28	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	676.54	03/2013 -	04/2014
	Total		54,263.98 -	120,264.40	85,625.66		
<u>Power</u>							
29	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,694.37	09/2009 -	03/2018
30	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,669.00	04/2009 -	09/2014
31	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,872.26	09/2010 -	03/2017
32	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,638.44	03/2007 -	02/2013
33	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,722.00	12/2009 -	03/2016
34	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,252.08	09/2009 -	12/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	864.13	12/2007 -	-
36	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,996.58	10/2010 -	09/2013
37	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,860.84	11/2009 -	03/2013
38	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,843.11	09/2008 -	03/2013
39	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	814.50	08/2010 -	06/2013
40	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	775.29	02/2011 -	01/2013
41	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	435.00	07/2010 -	11/2016
42	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	595.50	01/2010 -	02/2013
43	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,935.69	01/2016 -	11/2016
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	331.12	07/2014 -	05/2016
45	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,626.00	08/2012 -	03/2013
46	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.32	333.83	07/2011 -	01/2013
47	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	413.08	- -	07/2013
	Total		46,019.35 -	182,113.99	127,298.48		
<u>Railways</u>							
48	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007	04/1985	158.77 274.56	540.96	558.07	03/1994 -	12/2011
49	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
50	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	174.30	- 03/2010	-
51	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	589.19	- -	03/2012
52	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	548.95	543.08	06/1999 -	03/2011
53	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,549.43	03/2001 -	12/2017
54	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	247.13	- -	03/2015
55	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	207.83	03/2002 -	03/2013
56	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	118.37	12/2012 -	-

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	600.41	- -	02/2012
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	206.15	03/2004 -	03/2014
59	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	638.03	12/2011 12/2010	03/2013
60	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	188.66	- -	03/2013
61	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	560.17	- -	01/2013
62	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	206.46	- -	03/2013
63	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
64	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	352.10	07/2012 -	-
65	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	261.43	03/2012 -	03/2013
66	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	712.00	758.81	- -	10/2012
67	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	634.87	02/2009 -	03/2012
68	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	71.39	- -	-
69	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,577.46	1,401.22	- -	03/2013
70	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	5,016.00	2,590.05	04/2008 12/2011	12/2015
71	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	145.26	- -	03/2012
72	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	173.17	03/2007 03/2007	03/2015
73	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	342.57	- -	12/2012
74	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	309.91	06/2004 -	12/2012
75	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.35	07/2008 -	07/2008
76	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,352.41	07/2005 -	-
77	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	345.63	05/2008 -	03/2011
78	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	07/1996	653.84 654.51	1,302.12	608.97	06/2013 -	06/2013
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	685.77	03/2012 -	02/2013
80	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	914.71	12/2012 -	01/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	227.42	250.82	12/2009 -	03/2011
82	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	735.14	12/2010 -	03/2015
83	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,214.00	96.96	- -	-
84	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	357.95	- 05/2009	05/2009
85	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	621.56	- -	03/2012
86	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	503.06	- -	03/2014
87	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	100.02	- -	03/2013
88	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	835.57	06/2007 -	06/2007
89	RENIGUNTA-GUNTAKAL(RE) - [220100260	06/2000	168.34 -	370.00	344.50	04/2003 03/2010	-
90	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	548.96	525.48	- -	-
91	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.00	778.38	- -	03/2013
92	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
93	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,329.90	12/2008 -	03/2014
94	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,240.22	12/2006 -	08/2010
95	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	266.03	02/2011 -	02/2013
96	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	571.70	- 12/2009	02/2012
97	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	458.91	12/2012 12/2012	02/2013
98	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.29	- -	-
99	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	461.37	03/2005 12/2008	06/2016
100	REWARI-ROHTAK (NL),NR - [220100279	01/2004	149.38 -	602.78	503.47	02/2010 -	02/2011
101	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	697.50	439.54	03/2012 -	12/2012
102	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	238.06	- -	03/2013
103	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	735.10	222.32	- 09/2009	-
104	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	258.82	02/2009 02/2009	04/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	1,079.17	03/2011 -	03/2016
106	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	279.69	03/2012 -	03/2013
107	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	441.27	- -	03/2010
108	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	884.81	03/2009 -	12/2012
109	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,604.67	10/2007 -	12/2012
110	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	85.55	- -	-
111	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	225.75	- -	-
112	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	1,717.29	1,583.58	- -	03/2014
113	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	330.65	- 03/2009	-
114	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	175.03	03/1998 08/2005	08/2005
115	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
116	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	76.45	02/2015 -	-
117	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	228.88	03/2009 03/2009	04/2013
118	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	138.67	- -	03/2013
119	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	243.30	12/2007 03/2010	12/2010
120	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	406.58	03/2012 -	03/2013
121	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N220000027	04/2005	240.00 -	355.00	378.12	03/2009 12/2009	-
122	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.60	0.76	- -	-
123	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	105.70	02/2006 -	12/2013
124	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	429.24	03/2008 06/2008	-
125	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU - [N220000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
126	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N220000053	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
127	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	229.47	03/2010 -	-
128	PANSPURA-KHARAGPUR 3D LINE - [N220000076	09/2007	252.50 -	529.23	246.13	02/2010 -	12/2015

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
129	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	900.00	289.01	- -	-
130	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N22000080]	09/2006	343.17 -	900.00	571.48	- -	12/2012
131	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR [N22000082]	12/2006	170.00 -	453.04	396.45	03/2011 -	03/2011
132	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR [N22000083]	09/1996	156.00 -	406.40	280.75	- -	06/2013
133	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) [N22000084]	09/2006	125.00 -	227.40	40.35	- -	-
134	TIDIVANAM-NAGARI (NL) [N22000085]	09/2006	456.00 -	582.83	139.83	- -	-
135	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	200.00 -	385.20	117.93	- -	03/2016
136	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	42.31	- -	-
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) [N22000088]	04/2006	325.00 -	819.40	170.80	03/2010 -	06/2014
138	BARDHAMAN-KATWA (GC) [N22000091]	04/2007	245.15 -	1,106.62	211.94	12/2010 -	03/2011
139	ELECTRIFICATION OF MORADABAD-ROZA [N22000095]	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012
140	TAMLUK DIGHA, LINE DOUBLING (SER) [N22000097]	03/1984	293.97 -	1,086.41	431.61	06/2005 -	06/2016
141	AGARTALA SABROOM, NL, NEFR [N22000099]	04/2008	813.34 -	1,141.75	449.26	03/2014 -	12/2015
142	BHAIRABI SAIRONG, NL, NEFR [N22000100]	04/2008	619.34 -	2,393.48	31.46	04/2014 -	03/2017
143	KISHANGANJ JALALGARH, NL, NEFR [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
144	SEVOK RANGPO, NEFR [N22000102]	04/2008	1,339.48 -	3,380.58	57.12	12/2015 -	03/2020
145	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) [N22000107]	04/2007	482.00 -	482.70	416.20	03/2013 -	03/2014
146	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) [N22000109]	04/2010	2,069.60 -	2,298.42	40.20	03/2014 -	03/2016
147	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. [N22000111]	04/2010	2,619.02 -	2,913.51	207.96	03/2016 -	03/2016
148	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) [N22000113]	04/2008	653.19 -	653.46	215.07	03/2014 -	03/2014
149	Dakshin-barasal-lakshmikantapur [N22000116]	04/2009	259.51 -	533.38	93.41	12/2011 -	02/2012
150	Ghutiasharif-Canning (ER) [N22000117]	04/2009	189.97 -	611.03	119.21	12/2011 -	11/2013
151	Pandabeswar-Chinpai doubling (ER) [N22000118]	04/2004	225.68 -	293.74	132.81	12/2010 -	12/2010

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	04/2008	394.14 -	404.39	3.77	03/2013 -	03/2013
153	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123	04/2008	318.24 -	468.62	1.00	03/2012 -	-
154	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125	04/2006	117.36 196.95	196.95	194.04	03/2011 -	-
155	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project [N22000127	04/1996	1,676.31 -	4,255.37	3,291.16	03/2009 -	12/2014
	Total		42,365.17 -	311,263.98	184,704.76		
Road Transport & Highways							
156	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	148.22	04/2004 -	01/2013
157	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221	12/2003	155.00 -	201.66	136.31	09/2008 -	03/2013
158	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.43	03/2008 -	01/2013
159	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	249.18	05/2008 -	03/2013
160	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	68.37	04/2009 -	07/2013
161	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	100.53	11/2008 -	07/2013
162	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014
163	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	72.50	07/2009 -	04/2014
164	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
165	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	194.93	09/2007 -	03/2014
166	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,465.50	11/2011 -	08/2013
	Total		3,324.28 -	316,709.18	189,511.17		
Shipping & Ports							
167	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,571.60	5.75	10/2008 -	10/2008
168	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
169	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	1,460.00	894.93	12/2010 -	10/2013
170	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
171	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
172	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
173	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00 -	4,150.00	3,644.30	01/2012 -	02/2013
174	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	248.23	02/2014 -	-
175	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	326.08	04/2009 -	02/2011
	Total		8,628.97 -	327,927.68	194,960.39		
<u>Steel</u>							
176	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	9,958.76	10/2009 -	03/2013
177	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	343.48	12/2011 06/2010	03/2013
178	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68	118.28	10/2012 -	03/2013
179	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00	14,002.26	12/2011 -	12/2012
180	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	230.00 -	343.58	254.09	02/2011 -	03/2013
181	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00 -	350.00	250.59	08/2010 -	01/2013
	Total		24,028.89 -	358,144.11	219,887.85		
<u>Telecommunications</u>							
182	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013
183	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70 -	930.60	818.09	11/2010 -	12/2012
	Total		1,065.85 -	359,233.43	220,785.99		
<u>Urban Development</u>							
184	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013
185	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048	11/2006	114.18 173.08	173.08	-	04/2009 -	-

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		6,509.18	371,015.51	223,053.56		
			-				
	<u>Water Resources</u>						
186	PAGLADIYA DAM PROJECT	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	- [300100001		-			-	
	Total		542.90	372,202.51	223,089.05		
			-				
	Grand Total		221,202.14	2,853,865.29	1,777,881.87		

List of ongoing projects having time and cost overrun w.r.to original

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	17,270.00	15,276.00	12/2008 -	03/2013
	Total		13,171.00 -	17,270.00	15,276.00		
	<u>Civil Aviation</u>						
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037	08/2008	1,942.51 -	2,325.00	2,199.24	05/2011 -	03/2013
	Total		1,942.51 -	19,595.00	17,475.24		
	<u>Coal</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087	10/2004	2,030.78 -	3,027.59	2,536.19	06/2009 -	09/2013
4	MAGADH OC (CCL) - [N06000015	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016	12/2009	212.34 -	977.53	424.32	03/2013 -	07/2014
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047	05/2008	4,904.54 -	4,909.54	3,709.61	03/2012 -	03/2014
	Total		7,617.44 -	29,216.06	24,164.59		
	<u>Petrochemicals</u>						
7	Assam gas Cracker project - [N16000106	04/2006	5,460.61 -	8,920.00	5,981.96	04/2012 -	12/2013
	Total		5,460.61 -	38,136.06	30,146.55		
	<u>Petroleum</u>						
8	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	663.69	634.47	03/2007 -	03/2014
9	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.00	03/2007 -	03/2017
10	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	277.79	03/2006 -	03/2013
11	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
12	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
13	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,583.21	05/2010 -	01/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
15	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	3,919.55	08/2010 03/2012	12/2013
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,154.13	05/2010 -	03/2013
17	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	19,629.00	11/2012 -	09/2013
18	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	276.60	01/2012 -	01/2013
19	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
20	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	676.54	03/2013 -	04/2014
	Total		52,458.98 -	108,443.21	77,095.16		
<u>Power</u>							
21	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,694.37	09/2009 -	03/2018
22	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,669.00	04/2009 -	09/2014
23	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,872.26	09/2010 -	03/2017
24	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,638.44	03/2007 -	02/2013
25	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,722.00	12/2009 -	03/2016
26	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,252.08	09/2009 -	12/2013
27	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,996.58	10/2010 -	09/2013
28	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,860.84	11/2009 -	03/2013
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,843.11	09/2008 -	03/2013
30	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	814.50	08/2010 -	06/2013
31	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	775.29	02/2011 -	01/2013
32	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	435.00	07/2010 -	11/2016
33	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	595.50	01/2010 -	02/2013
34	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,935.69	01/2016 -	11/2016
35	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	331.12	07/2014 -	05/2016

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,626.00	08/2012 -	03/2013
37	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.32	333.83	07/2011 -	01/2013
	Total		45,001.89 -	168,662.20	117,490.77		
<u>Railways</u>							
38	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
39	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,549.43	03/2001 -	12/2017
40	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	207.83	03/2002 -	03/2013
41	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	206.15	03/2004 -	03/2014
42	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	638.03	12/2011 12/2010	03/2013
43	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	261.43	03/2012 -	03/2013
44	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	5,016.00	2,590.05	04/2008 12/2011	12/2015
45	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	173.17	03/2007 03/2007	03/2015
46	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	309.91	06/2004 -	12/2012
47	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	685.77	03/2012 -	02/2013
48	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	914.71	12/2012 -	01/2013
49	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	735.14	12/2010 -	03/2015
50	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,329.90	12/2008 -	03/2014
51	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	266.03	02/2011 -	02/2013
52	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	458.91	12/2012 12/2012	02/2013
53	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	461.37	03/2005 12/2008	06/2016
54	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	697.50	439.54	03/2012 -	12/2012
55	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	258.82	02/2009 02/2009	04/2013
56	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	1,079.17	03/2011 -	03/2016
57	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	279.69	03/2012 -	03/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	884.81	03/2009 -	12/2012
59	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,604.67	10/2007 -	12/2012
60	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	228.88	03/2009 03/2009	04/2013
61	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	406.58	03/2012 -	03/2013
62	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	105.70	02/2006 -	12/2013
63	PANSPURA-KHARAGPUR 3D LINE - [N220000076	09/2007	252.50 -	529.23	246.13	02/2010 -	12/2015
64	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088	04/2006	325.00 -	819.40	170.80	03/2010 -	06/2014
65	TAMLUK DIGHA,LINE DOUBLING (SER) - [N220000097	03/1984	293.97 -	1,086.41	431.61	06/2005 -	06/2016
66	AGARTALA SABROOM, NL, NEFR - [N220000099	04/2008	813.34 -	1,141.75	449.26	03/2014 -	12/2015
67	BHAIRABI SAIRONG, NL, NEFR - [N220000100	04/2008	619.34 -	2,393.48	31.46	04/2014 -	03/2017
68	SEVOK RANGPO, NEFR - [N220000102	04/2008	1,339.48 -	3,380.58	57.12	12/2015 -	03/2020
69	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N220000107	04/2007	482.00 -	482.70	416.20	03/2013 -	03/2014
70	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N220000109	04/2010	2,069.60 -	2,298.42	40.20	03/2014 -	03/2016
71	Ghutiasharif-Canning (ER) - [N220000117	04/2009	189.97 -	611.03	119.21	12/2011 -	11/2013
72	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N220000127	04/1996	1,676.31 -	4,255.37	3,291.16	03/2009 -	12/2014
	Total		18,194.53 -	234,361.75	146,374.88		
Road Transport & Highways							
73	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	148.22	04/2004 -	01/2013
74	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	136.31	09/2008 -	03/2013
75	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.43	03/2008 -	01/2013
76	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	249.18	05/2008 -	03/2013
77	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	68.37	04/2009 -	07/2013
78	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	100.53	11/2008 -	07/2013
79	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N240000061	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
80	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	72.50	07/2009 -	04/2014
81	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
82	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	194.93	09/2007 -	03/2014
83	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,465.50	11/2011 -	08/2013
	Total		3,324.28 -	239,806.95	151,181.29		
<u>Shipping & Ports</u>							
84	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	1,460.00	894.93	12/2010 -	10/2013
85	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013
86	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
87	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
88	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048	03/2009	3,500.00 -	4,150.00	3,644.30	01/2012 -	02/2013
	Total		6,462.00 -	247,832.45	156,050.45		
<u>Steel</u>							
89	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	9,958.76	10/2009 -	03/2013
90	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	343.48	12/2011 06/2010	03/2013
91	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68	118.28	10/2012 -	03/2013
92	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00	14,002.26	12/2011 -	12/2012
93	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068	07/2007	230.00 -	343.58	254.09	02/2011 -	03/2013
94	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00 -	350.00	250.59	08/2010 -	01/2013
	Total		24,028.89 -	278,048.88	180,977.91		
<u>Telecommunications</u>							
95	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013

(Dec,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
96	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70	930.60	818.09	11/2010	12/2012
	Total		1,065.85	279,138.20	181,876.05		
			-				
	<u>Urban Development</u>						
97	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00	11,609.00	2,267.57	06/2011	03/2013
	Total		6,395.00	290,747.20	184,143.62		
			-				
	<u>Water Resources</u>						
98	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	Total		542.90	291,934.20	184,179.11		
			-				
	Grand Total		185,665.88	2,243,192.16	1,466,431.62		
