

**302th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
December, 2010**



FLUE GAS COOLER

HPCL - Madurai Refinery



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -7
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	8-12
List of Delete Projects	13-13
Summary of Projects	14-22
Sector wise Trend and Graphicalf Analysis	23-31
Sector wise analysis of projects	32-61
Graph	62-72
List of All Ongoing Projects	73-73
List of Abbreviations	74-75

EXECUTIVE SUMMARY

The Flash Report for December' 2010 (the 302nd Flash Report) contains information on the status of 567 projects in the Central Sector, each costing ` 150 Crores and above. During December' 2010, 8 projects reported completion (which have now been dropped from the monitor of this Ministry) and two new projects have been added.

The online submission of the implementation Status Report of the ongoing projects has been improving. In December, 2010 nearly 83% projects are reported online. Out of 567 ongoing projects on the monitor of this Ministry, 472 projects were updated online by the concerned project agencies. Sector-wise number of ongoing projects along with status of online reporting is given below:

S. No.	Sector	Projects on monitor	Reported Online	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	121	118	25
2.	RAILWAYS	147	83	2
3.	POWER	83	75	12
4.	PETROLEUM	67	66	8
5.	COAL	45	44	1
6.	TELECOMMUNICATION	40	40	22
7.	STEEL	19	6	1
8.	SHIPPING & PORTS	23	23	8
9.	CIVIL AVIATION	8	8	0
10.	FERTILISERS	6	5	1
11.	ATOMIC ENERGY	4	2	0
12.	URBAN DEVELOPMENT	2	1	0
13.	MINES	1	1	0
15.	WATER RESOURCES	1	0	0
Total		567	472	80

2. During December' 2010, eighty (80) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 72 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Telecommunications, Shipping & Ports and Fertilizers Sectors.

3. Out of 567 projects, 8 projects are ahead of schedule, 125 are on schedule and 295 projects are delayed. Of the balance, 80 projects do not have fixed dates of commissioning i.e. neither the year of commissioning nor the tentative gestation period of the projects have been reported. A large number of projects (59) have been sanctioned without any commissioning schedule/date. The concerned ministries have been asked to fix the date of commissioning at the earliest

4. The total original cost of implementation of the 567 projects was of the order of ` 5,92,535.30 Crores and their anticipated completion cost was ` 7,16,353.74 Crores, which reflects a cost overrun of 20.90%. The expenditure incurred on these projects till December, 2010 is ` 3,10,965.82 Crores.

5. Out of 567 projects, presently on the monitor at the end of December 2010, 8 projects were ahead of schedule, 125 projects were on schedule (22%), 295 projects were delayed (51%) (this excludes the 80 projects without date of commissioning and those that have not reported during the month). During the month, 80 projects have reported additional delays in the range of 1-72 months. The analysis of pictorial presentation shows that during current month, the project reporting delays have marginally increased to 295 from 291 reported in November'2010. The overall cost overrun has been somewhat constant since September 2010. It may be seen that out of 295 delayed projects, at the end of December, 2010, 69 projects had overall delay in the range of 1 to 12 months, 80 projects had delay in the range of 13 to 24 months, 112 projects had delay in the range of 25 to 60 months and 34 projects had time overrun of 61 months and above.

6. In the **Coal sector**, the Barsingsar TPS Project has reported additional delay of one month due to delay in releasing of funds.

7. In the **Steel Sector**, 330 TPH Boiler-6 and Auxiliary system project of RINL has reported an additional delay of 10 months due to delay in design and erection of equipments.

8. In the **Petroleum Sector**, 8 projects have reported additional delays in the range of 1-72 months. Installation of FCCV at Mumbai Refinery HPCL has reported additional delay of one month, as the commissioning is awaited. Sultanpur Neemrana Pipe line Project (GAIL) and Bawana Nangal Pipe line Project (GAIL) have reported additional delays of 2 months in view of the farmers demanding higher land compensation. VKPL Upgradation and Laying of Spur line (to Bhilwara and Chittorgarh) GAIL has reported on additional delay of 2 months due to delay in survey report. BNPL Superlines (Uttanchal & Punjab) GAIL has reported additional delay of 4 months due to synchronization with customer readiness. “Improved Oil Recovery, Rudrasagar ONGC”, “Improved Oil Recovery, Lakwa-Lakhmani ONGC” and “Improved Oil Recovery, Geleki ONGC” have additional delays of 24 months, 36 months and 72 months due to law and order problem in the North East Region.

9. In the **Power Sector**, 12 projects have reported additional delays in the range of 1-12 months. Transmission System associated with Barh Generation Project has reported additional delay of 3 months due to synchronization is the generation project anticipated. Transmission System for startup Power to DVC & Maithon RB G, PGCIL has reported additional delay of 1 month due to delay in Forest Clearance for about 13 hectare in Koderma – Bihar Shariff. The Establishment of 400/220 KV GIS Pooling Station Near Chamera, Transmission, System Associated with Chamera III HEP PGCIL have reported additional delay of 1 month and 2 months respectively, for which however, no specific reasons have been given by the project authorities. East – West Transmission corridor Strengthening Scheme PGCIL has reported additional delay of 2 months as final clearance for Rourkela-Raigarh is awaited. Eastern Region Strengthening Scheme II PGCIL has reported additional delay of 2 months due to Right of Way problem in West Bengal. Kundankulam-Atomic Power Plant Transmission System (PGCIL) has reported additional delay of 3 months due to severe Right of Way problem in Kerala. Western Region Transmission Strengthening Scheme II PGCIL has reported additional delay of 3 months due to delay in Right of Way problem, Forest Clearance and heavy rains. Western Region Strengthening Scheme V PGCIL has reported additional delay of 3 months due to delay in Right of Way problems. Tapovan – Vishnugad HEP NTPC has reported additional delay of 11 months due to Internal Audit for intake works and Award of balance works is anticipated by June’2011. Vishnugad Pipalkoti Hydro Electric Project THDCL has reported an additional delay of 12 months due to delay in diversion of forest land. PARE Hydro Electric Project (110MW) NEEPCO has reported additional delay of 12 months. However, no specific reason has been given by the project authority.

10. In the **Road Transport and Highways Sector**, 25 projects have reported additional delay in the range of 1-22 months. 18 projects have reported additional delay in 1-3 months due to slow progress of work by the contractor. Nagaon Bypass (NH-37) NHAI has reported additional delay of 4 months due to delay in Land acquisition, cutting of trees, shifting of utilities and poor law & order problems. Vijayapur to Pathankot (J&K), Assam/West Bengal Border to Gairkatta NHAI have reported additional delay of 6 months and 8 months due to delay in poor mobilization of the resources by the contractors & delay in land acquisition. Siliguri to Islampur NHAI has reported additional delay of 8 months due to delay in acquisition of land and prolonged monsoon period. Dholpur – Morena has reported additional delay of 9 months due to delay in obtaining Wildlife Clearance. Lakhnaadon to MP/MH Border NH7, NHAI has reported additional delay of 22 months due to delay in diversion of forest land. Four Lanning from MP/Maharashtra Border to Nagpur, NHAI has reported additional delay of 12 months. However, the project authorities have not mentioned any specific reason for such additional delays.

11. In the **Fertilizer Sector**, NANGAL- Ammonia Plant Feedstock project NFL Project has reported additional delay of one month, for which no specific reasons have been given by the project authorities.

12. In the **Railway Sector**, 2 projects have shown additional delays namely, the “Kosi Bridge (NL) ECR” and “Utratia-Zafrabad NR” have reported additional delay of 9 months and 18 months respectively. The project authorities have however not mentioned any specific reason for such additional delays.

13. In the **Telecommunication Sector**, 22 projects have shown additional delays in the range of 1-5 months. [GSM Equipment of 216650 Lines (2G) PH-V.1 BSNL, GSM Equipment of 390K Lines (2G) and 130K lines (3G) BSNL, GSM Equipment of 945000 Lines (2G) and 225000 lines (3G) BSNL, GSM Equipment of 1500000 Lines (2G) and 264700 lines (3G) BSNL, GSM Equipment of 900K Lines (2G) and 300K lines (3G) BSNL, GSM Equipment of 480K Lines (2G) and 220K lines (3G) BSNL, GSM Equipment of 900000 Lines (2G) Punjab Phase V.2 BSNL, GSM Equipment of 200000

Lines (2G) UP (West) Phase V BSNL and GSM Equipment of 849862 Lines (2G) 150138 lines (3G) BSNL have reported additional delays of 2 months, 2 months, 2 months, 2 months, 3 months, 3 months, 4 months, 4 months and 5 months], respectively due to slow progress by the contractor. GSM Equipment of 375000 Lines (2G) and 75000 lines (3G) BSNL has reported additional delay of one month due to delay in installation. Uttaranchal Telecom Circle Phase-VI (2G & 3G) BSNL has reported additional delay of 2 months due to delay in land acquisition problem. GSM Equipment of 1900000 lines (2G) 401700 lines (3G) BSNL and GSM Equipment of 614000 lines (2G) 150000 lines (3G) BSNL has reported additional delay of 2 months each due to shortage of technical people required for implementing the project. Assam Telecom Circle Phase-V.I, 2G & 3G BSNL has reported additional delay of 3 months due to delay in shifting of 79 BTS by Ericsson Company Ltd. GSM Equipment of 975000 lines (2G) 325000 lines (3G) BSNL has reported additional delay of 3 months due to delay in finalization of BTS sites. GSM Equipment of 1100000 lines (2G) UP East Phase V.2 BSNL and GSM Equipment of 799000 lines (2G) 101000 lines (3G) BSNL have reported additional delay of 3 months and 3 months due to delay in finalization of OFC media. GSM Equipment of 1867000 lines (2G) 383000 lines (3G) BSNL has reported additional delay of 3 months due to delay in supply by M/S ALCATEL & M/S ITI. GSM Equipment of 1700000 lines (2G) 234100 lines (3G) BSNL has reported additional delay of 3 months due to vendor problem. GSM Equipment of 1900000 lines (2G) 335500 lines (3G) BSNL has reported additional delay of 3 months due to delay in acquisition of site by the vendor. GSM Equipment of 700K lines (2G) 150K lines (3G) BSNL has reported additional delay of 4 months due to delay in 3 phase supply and site acquisition of BTS sites. GSM Equipment of 849862 lines (2G) 150138 lines (3G) BSNL and GSM Equipment of 1625000 lines (2G) 325000 lines (3G) BSNL has reported additional delay of 3 months and 4 months due to delay in installation by M/S ALCATEL.

14. In the **Shipping & Ports Sector**, 8 projects have shown additional delays in the range of 1-36 months. Construction of 13 & 14 Cargo Berth at Kandla Port Trust has reported additional delay of 24 months due to less royalty quoted by BOT Operators and retendering is in process. Construction of Berthing and Allied Facilities off Tekra Kandla Port Trust has reported additional delay of 25 months due to delay in fixation of capacity for the terminal the Tarrif Authority Major Port (TAMP) Office. Modification and Strengthening of Existing Berth No. 1 to 6 Kandla Port Trust has reported additional delay of 36 months due to change in scope of design of existing cargo berth, since it has outlived life of 50 years. Rail Connectivity to ICTT at Vallarpadam Port Trust, Acquisition of 6 57000 DWT

Handymax Bulk Cargo Ships, Setting up of LNG Regasification Terminal at Puthu Port Trust have reported additional delays of 2 months each, Deepening of Channel at Paradip Port Trust, Construction and Development of 2 Offshore Container Berths and Terminal, Mumbai Port Trust have reported additional delays of 3 months & 24 months respectively due to poor performance by the contractor.

The status as on 01.01.2011 in respect of completion of projects costing ` 150 Crores and above in different sectors during 2010-11 is indicated in the Report.



(Pankaj Jain)

**Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation**

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	147	2
2	Road Transport & Highways	121	25
3	Power	83	12
4	Petroleum	67	8
5	Coal	45	1
6	Telecommunications	40	22
7	Shipping & Ports	23	8
8	Steel	19	1
9	Civil Aviation	8	0
10	Fertilisers	6	1
11	Atomic Energy	4	0
12	Urban Development	2	0
13	Mines	1	0
14	Water Resources	1	0
	Total	567	80

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	168.33	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93
September,2010				
<u>Coal</u>				
8	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)(NEYVELI LIGNITE CORPORATION) - [060100090]	254.07	06/2009	1,687.78
<u>Steel</u>				
9	REBUILDING OF COKE OVEN BATTERY-10(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000016]	416.50	09/2009	305.14
<u>Petroleum</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
10	PANIPAT NAPHTA CRACKER PROJECT(INDIAN OIL CORPORATION LIMITED) - [160100292]	12,138.00	09/2009	12,054.37
11	DADRI- PANIPAT R-LNG SPUR PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000018]	250.66	06/2008	350.96
12	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000026]	638.90	04/2009	796.21
13	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE(INDIAN OIL CORPORATION LIMITED) - [N16000034]	348.00	12/2009	186.58
14	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000035]	1,131.00	12/2009	750.71
15	CHAINS- JHAJJAR PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000047]	967.77	09/2009	416.90
16	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000067]	643.46	-	726.45
17	Construction of Tank and Blending Facility at Vadi(INDIAN OIL CORPORATION LIMITED) - [N16000075]	267.00	-	72.99
18	BINA DESPATCH TERMINAL(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000078]	490.71	12/2009	590.52
<u>Railways</u>				
19	HOSPET-GUNTAKAL(LD),SCR(RAIL VIKAS NIGAM LTD.) - [220100195]	105.22	12/1999	283.49
20	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100224]	536.85	03/2003	1,005.50
21	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)(RAIL VIKAS NIGAM LTD.) - [220100244]	223.00	-	586.85
22	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000033]	352.00	03/2008	616.44
23	ABOHAR- FAZILKA, NR, NL(NORTHERN RAILWAY) - [N22000055]	86.44	03/2009	201.79
<u>Road Transport & Highways</u>				
24	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100203]	440.93	12/2006	641.40
25	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100204]	534.39	05/2007	716.15
26	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101178]	372.40	07/2004	406.05
27	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101181]	467.93	03/2005	453.64
28	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101187]	399.75	03/2005	424.96
29	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106227]	276.00	04/2008	360.00
30	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106228]	310.00	04/2008	392.26
31	MADURAI - KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106241]	507.49	03/2008	342.80
32	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106257]	556.00	03/2009	568.50

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
33	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106273]	469.80	12/2008	665.80
34	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106285]	261.00	08/2008	286.30
35	TOVARAMKURCHI-MADURAI,NH45B (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000054]	263.00	08/2008	317.74
36	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000060]	402.80	03/2009	453.70
37	PADALUR-TRICHY, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000083]	320.00	05/2009	636.10
38	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000093]	360.42	11/2009	478.40
39	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000105]	450.00	07/2008	876.61
40	ISLAM NAGAR TO KADTAL(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000109]	546.83	03/2010	667.80
41	WAINGANGA BRIDGE -CHHATISGARH-MAHARASHTRA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000120]	424.00	09/2010	298.40
Shipping & Ports				
42	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS(SHIPPING corp. of india) - [N25000013]	411.32	03/2010	406.28
43	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA(PORT TRUST) - [N25000046]	2,118.00	11/2004	.00
Telecommunications				
44	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I(DEPARTMENT OF TELECOMMUNICATION) - [260100051]	279.97	12/2004	136.24
45	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA(BHARAT SANCHAR NIGAM LIMITED) - [260100095]	1,174.75	03/2006	371.41
46	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000026]	741.77	10/2007	151.37
47	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-(BHARAT SANCHAR NIGAM LIMITED) - [N26000028]	364.52	-	51.44
48	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000042]	409.21	12/2008	470.24
49	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000061]	180.53	12/2009	25.97
October,2010				
Health & Family Welfare				
50	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS(HEALTH & FAMILY WELFARE) - [210100001]	71.18	03/1999	547.78
Railways				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
51	DHARMAVARAM-PAKALA (GC), SCR(SOUTH CENTRAL RAILWAY) - [220100282]	200.00	-	567.49
Road Transport & Highways				
52	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106268]	263.00	02/2009	420.80
53	AMRITSAR-WAGHA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000121]	205.88	06/2010	214.90
Shipping & Ports				
54	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE(SHIPPING crp. of india) - [N25000029]	1,658.59	07/2010	1,657.45
Telecommunications				
55	GSM BASED NETWORK EXPANSION PLAN PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000034]	239.19	04/2008	96.97
56	Provision of data network for CWG delhi(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000076]	488.76	10/2010	198.65
57	Expn of existing 2G & 3G GSM N/W by 750k(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000077]	180.53	06/2010	40.92
58	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph(BHARAT SANCHAR NIGAM LIMITED) - [N26000079]	577.35	09/2010	40.76
November,2010				
Petroleum				
59	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL)(INDIAN OIL CORPORATION LIMITED) - [160100289]	1,876.00	04/2009	2,747.34
60	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA(INDIAN OIL CORPORATION LIMITED) - [N16000017]	806.00	03/2008	840.06
Power				
61	SEWA- II H.E.P (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100220]	665.46	09/2007	982.76
62	NORTHERN REGION SYSTEM STRENGTHENING-XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000034]	417.76	12/2010	266.87
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000036]	408.36	12/2010	304.83
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000039]	261.55	11/2010	143.36
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000055]	525.14	07/2011	354.99
Railways				
66	RAJGIR-TILAIYA (NL), ECR(EAST CENTRAL RAILWAYS) - [220100312]	180.82	03/2006	272.46

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
67	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000079]	205.92	08/2009	204.50
68	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000080]	243.64	08/2009	256.40
<u>Telecommunications</u>				
69	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M(BHARAT SANCHAR NIGAM LIMITED) - [N26000051]	908.30	08/2009	211.83
70	CENTRALISED TRANSMISSION NMS(BHARAT SANCHAR NIGAM LIMITED) - [N26000064]	300.00	-	.00
December,2010				
<u>Petroleum</u>				
71	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000036]	372.00	-	229.04
72	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000037]	356.00	-	222.69
73	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000038]	1,492.00	04/2010	1,113.09
<u>Road Transport & Highways</u>				
74	SAGAR - RAJMARG CHORAH,KM 255-297, NH-26 (NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106302]	206.96	10/2008	281.90
75	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000078]	243.38	09/2008	286.40
76	BANGALORE-NEELAMANGLALA NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000104]	445.00	07/2010	803.40
<u>Shipping & Ports</u>				
77	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS(SHIPPING crp. of india) - [N25000030]	586.58	11/2010	634.09
<u>Telecommunications</u>				
78	KOLKATA TELECOM DISTRICT PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000036]	208.50	09/2008	146.00

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
September,2010				
<u>Road Transport & Highways</u>				
1	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N16000082]	300.00	10/2008	.00
November,2010				
<u>Civil Aviation</u>				
2	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N12000021]	535.00	06/2010	331.80


Summary of projects on the Flash Report for the month of Dec, 2010

I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 150 Cr. & above) Previous Month	585
Number of Projects Completed and Dropped Cost (Rs. 150 Cr. & above) in Previous Month	13
Number of Projects Completed and Dropped Cost (Rs. 150 Cr. & above) in Current month	8
No. of projects with Cost Anticipated greater than Rs. 150 Cr in Current Mont	1
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	2
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	567

II. Brief Analysis


a) Project Status w.r.t Original Schedule: Out of 567 projects, 8 projects are ahead of schedule, 125 projects are on schedule and 295 projects are delayed. Of the balance, 80 projects do not have fixed dates of commissioning while 59 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

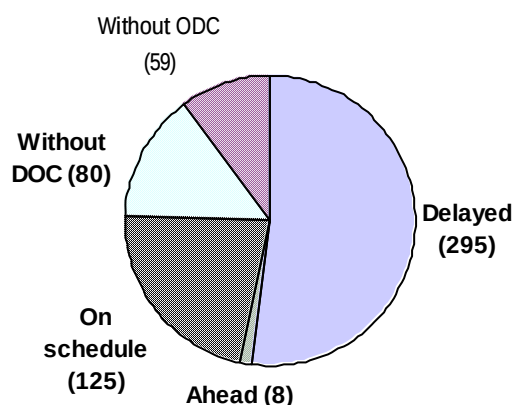

III. Investment Scenario

Figures are in Rs. Crore

The total Original cost of implementation of 567 projects when sanctioned, was of the order of Rs. 592535.30 crore but this was subsequently revised to Rs. 716353.74 crore implying a cost overrun of 20.90%. The expenditure incurred on these projects till Dec, 2010 is Rs. 310965.82 crore, which is 43.40% of the revised cost of the projects.

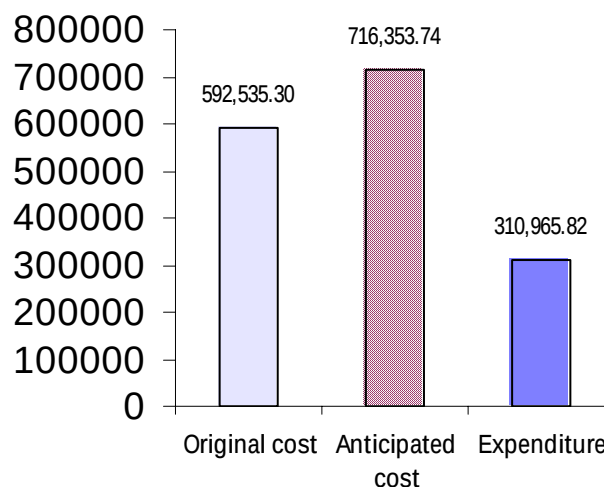

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	585
No of Projects Completed and Dropped in Previous Month	13
No of Projects Completed and Dropped in Current Month	8
No of Projects added in Current Month	2
No. of projects with Cost Anticipated greater than Rs. 150 Cr in Current Months	1
No of Projects in Current Month	567

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original (Date)	295	8	125	59	80	567	52.03
Latest Approved (Date)	295	12	150	42	70	567	52.03

III. (A) Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	477	492,846.11	532,858.59	215,726.84	40.50	40,012.48	8.10
Latest Approved (RCE)	90	147,127.99	183,495.15	95,238.98	51.90	36,367.16	24.70
Total (RCE)	567	639,974.10	716,353.74	310,965.82	43.41	76379.64	11.93
Original Cost of All Projects							
Original Cost	567	592,535.30	716,353.74	310,965.82	43.40	123,818.44	20.90

III. (B) Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	295	310,195.11	384,921.64	218,009.94	56.60	74,726.53	24.10
Latest Approved (RCE)	295	307,104.62	359,196.57	207,896.46	57.90	52,091.95	17.00

IV. Additional Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	81	56,409.25	59,205.46	31,446.04	53.10	2,796.21	5.00

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Road Transport & Highways</u>						
SAGAR - RAJMARG CHORAHA,KM 255-297, NH-26 (NHAI)	12/2003	206.96	10/2008	206.96	12/2010	281.90
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376	12/2003	243.38	09/2008	243.38	12/2010	286.40
BANGALORE-NEELAMANGLALA NH-4	03/2005	445.00	07/2010	445.00	12/2010	803.40
<u>Shipping & Ports</u>						
ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS	08/2007	586.58	11/2010	586.58	03/2011	634.09
<u>Telecommunications</u>						
KOLKATA TELECOM DISTRICT PH-4	09/2006	208.50	09/2008	208.50	02/2011	146.00
<u>Petroleum</u>						
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY	04/2008	356.00	N.A.	251.00	12/2010	222.69
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY	04/2008	372.00	N.A.	276.00	12/2010	229.04
MSQ UPGRADATION PROJECT AT BARAUNI REFINERY	04/2008	1,492.00	04/2010	1,525.00	12/2010	1,113.09

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Shipping & Ports</u>					
Acquisition of three(3) nos of 6500TEU Cellular container	10/2010	1,028.10	12/2013	1,028.10	12/2013
Acquisition of two(2) Nos. of 317000 DWT very large crude	10/2010	966.46	2/2014	966.46	2/2014

VII. Milestones (Cumulative due & achieved)

Total	2085
Achieved up to month	854

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Coal</u>						
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	12/2010	01/2011	1
<u>Fertilisers</u>						
NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT NFL	1,478.63	1,478.63	12/2012	12/2012	01/2013	1
<u>Steel</u>						
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	08/2010	06/2011	10
<u>Petroleum</u>						
INSTALLATION OF FCCV AT MUMBAI REFINERY HPCL	900.47	900.47	09/2009	11/2010	12/2010	1
SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) GAIL	396.13	396.13	10/2009	11/2010	01/2011	2
BAWANA NANGAL PIPE LINE PROJECT GAIL	1,816.07	1,400.00	N.A.	04/2011	06/2011	2
VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	375.00	06/2011	06/2011	08/2011	2
BNPL superlines(Uttranchal & Punjab) GAIL	540.92	540.92	05/2011	06/2011	10/2011	4
IOR, RUDRASAGAR (ONGCL) ONGC	113.90	438.85	03/2006	03/2011	03/2013	24
IOR LAKWA - LAKHMANI (ONGCL) ONGC	345.10	663.69	03/2007	03/2011	03/2014	36
IOR GELEKI (ONGCL) ONGC	390.09	1,674.11	03/2007	03/2011	03/2017	72
<u>Power</u>						
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G PGCIL	290.49	299.08	04/2010	01/2011	02/2011	1
EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER PGCIL	262.10	262.10	09/2010	12/2010	01/2011	1
EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME PGCIL	803.70	803.76	06/2009	12/2010	02/2011	2
EASTERN REGION STRENGTHENING SCHEME- II PGCIL	227.52	227.52	06/2010	12/2010	02/2011	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	297.37	07/2011	12/2010	02/2011	2
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) PGCIL	1,779.29	1,946.85	11/2008	03/2011	06/2011	3
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) PGCIL	3,779.46	3,725.13	09/2009	03/2011	06/2011	3
WESTERN REGION STRENGTHENING SCHEME- II PGCIL	5,221.23	4,978.56	07/2010	03/2011	06/2011	3
WESTERN REGION STRENGTHENING SCHEME- V PGCIL	477.69	477.69	09/2010	03/2011	06/2011	3
Tapovan-Vishnugad HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	03/2013	03/2013	02/2014	11
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCL	2,491.58	2,491.58	07/2014	03/2015	03/2016	12
PARE HYDRO ELECTRIC PROJECT(110 MW) NEEPCO	573.99	573.99	08/2012	08/2012	08/2013	12
<u>Railways</u>						
KOSI BRIDGE (NL), ECR ECR	323.41	341.41	N.A.	03/2012	12/2012	9
UTRATIA-ZAFRABAD, NR (LINE DOUBLING) (NR)	325.00	369.90	03/2010	12/2012	06/2014	18
<u>Road Transport & Highways</u>						
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 NHAI	480.00	480.00	11/2007	12/2010	01/2011	1
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS NHAI	210.00	210.00	04/2007	12/2010	01/2011	1
DARBHANGA- MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) NHAI	291.80	291.80	06/2008	12/2010	01/2011	1
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	12/2010	01/2011	1
THANJAUR-TRICHY,NH- 67(NHAI) NHAI	280.00	280.00	06/2009	12/2010	01/2011	1
NALBARI TO BIJNI (AS-8) NHAI	200.00	200.00	06/2008	01/2011	03/2011	2
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	01/2011	03/2011	2
HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	12/2010	03/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	12/2010	03/2011	3
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 NHAI	205.73	205.73	07/2004	12/2010	03/2011	3
GARHMUKTESHWAR- MURADABAD (NHAI) OTHERS KM.93-149.25, NH- 24 NHAI	275.00	275.00	09/2007	12/2010	03/2011	3
GAGODHAR- GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 NHAI	412.78	479.54	11/2007	12/2010	03/2011	3
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH- 7,KM.80 TO KM.120 NHAI	323.36	323.36	03/2008	12/2010	03/2011	3
AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	12/2010	03/2011	3
NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2008	12/2010	03/2011	3
NAGPUR-KONDHALI,NH- 6(NHAI) NHAI	168.00	168.00	12/2008	12/2010	03/2011	3
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	12/2010	03/2011	3
END OF DURG BYPASS- CHHATISGARH/MAHARASHT RA BORDER NHAI	464.00	464.00	01/2011	01/2011	04/2011	3
NAGAON BYPASS (NH- 37)(NHAI) NHAI	230.00	230.00	06/2008	12/2010	04/2011	4
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 NHAI	193.09	166.30	03/2008	12/2010	06/2011	6
SILIGURI TO ISLAMPUR (WB-7) NHAI	225.00	225.00	07/2008	12/2010	08/2011	8
ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	12/2010	08/2011	8
DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE NHAI	232.45	232.45	09/2010	03/2011	12/2011	9
Four Lanning from MP/Maharashtra Border to nagpur NHAI	1,170.52	1,170.52	06/2011	10/2011	10/2012	12
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS- 1/BOT/MP-2),NH7 NHAI	407.60	407.60	06/2010	12/2010	10/2012	22

Shipping & Ports

VIII. List of projects reporting additional delays



Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM PORT TRUST	245.67	298.17	04/2009	12/2010	02/2011	2
ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C SHIPP.	1,061.96	1,061.96	03/2012	01/2012	03/2012	2
SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	3,500.00	01/2012	01/2012	03/2012	2
DEEPENING OF CHEENEL AT PARADIP PORT TRUST	154.84	253.36	06/2007	12/2010	03/2011	3
CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER MUMBAI PORT TRU	1,228.00	1,460.00	12/2010	12/2010	12/2012	24
CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA PORT TRUST	702.00	755.50	03/2011	03/2011	03/2013	24
C/O Berthing and Allied Facilities off tekra near PORT TRUST	882.00	1,060.00	02/2011	02/2011	03/2013	25
Modification & Strengthening of Existing Berth No. 1 to 6 PORT TRUST	277.00	277.00	03/2012	03/2012	03/2015	36
Telecommunications						
GSM equipment of 375000Lines (2G) 75000lines 3(G) BSNL	170.23	170.23	06/2009	12/2010	01/2011	1
GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 BSNL	192.48	192.48	03/2009	12/2010	02/2011	2
GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) BSNL	373.94	373.94	12/2008	12/2010	02/2011	2
UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) BSNL	149.15	158.72	06/2009	12/2010	02/2011	2
GSM equipment of 945000Lines (2G) 225000lines 3(G) BSNL	366.00	529.32	10/2008	12/2010	02/2011	2
GSM equipment of 1900000Lines (2G) 401700 lines 3(BSNL	760.20	810.37	01/2010	12/2010	02/2011	2
GSM equipment of 1500000Lines (2G) 264700lines 3(G BSNL	922.91	922.91	01/2010	12/2010	02/2011	2
GSM equipment of 614000Lines (2G) 150000lines 3(G) BSNL	315.19	315.19	01/2010	12/2010	02/2011	2



VIII. List of projects reporting additional delays



Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) BSNL	601.49	601.49	12/2008	12/2010	03/2011	3
GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN BSNL	335.91	335.91	03/2009	12/2010	03/2011	3
Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	11/2010	02/2011	3
GSM equipment of 975000Lines (2G) 325000 lines 3(G BSNL	625.53	625.53	02/2010	11/2010	02/2011	3
GSM equipment of 1100000Lines (2G) UP East Phase BSNL	624.75	624.75	09/2010	12/2010	03/2011	3
GSM equipment of 799000Lines (2G) 101000 lines 3(G BSNL	328.13	392.44	03/2009	10/2010	01/2011	3
GSM equipment of 1867000Lines (2G) 383000 lines 3(BSNL	868.00	868.00	08/2009	12/2010	03/2011	3
GSM equipment of 1700000Lines (2G) 234100 lines 3(BSNL	677.75	719.70	10/2009	12/2010	03/2011	3
GSM equipment of 1900000Lines (2G) 335500lines 3(G BSNL	848.70	848.70	01/2010	11/2010	02/2011	3
GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) BSNL	277.34	277.34	03/2009	10/2010	02/2011	4
GSM equipment of 900000Lines (2G) PunjabPhase V.2 BSNL	241.49	241.49	09/2009	11/2010	03/2011	4
GSM equipment of 200000Lines (2G) UP(West)Phase V. BSNL	336.84	336.84	10/2009	11/2010	03/2011	4
GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	916.70	11/2010	11/2010	03/2011	4
GSM equipment of 849862Lines (2G) 150138 lines 3(G BSNL	584.33	584.33	02/2009	10/2010	03/2011	5



Number of projects reporting additional delay = 80



Sector wise Trend and Graphical Analysis (Sep'10,Oct'10,Nov'10,Dec'10)

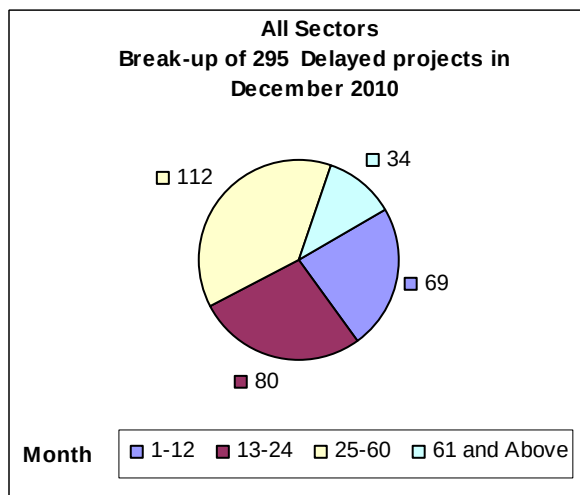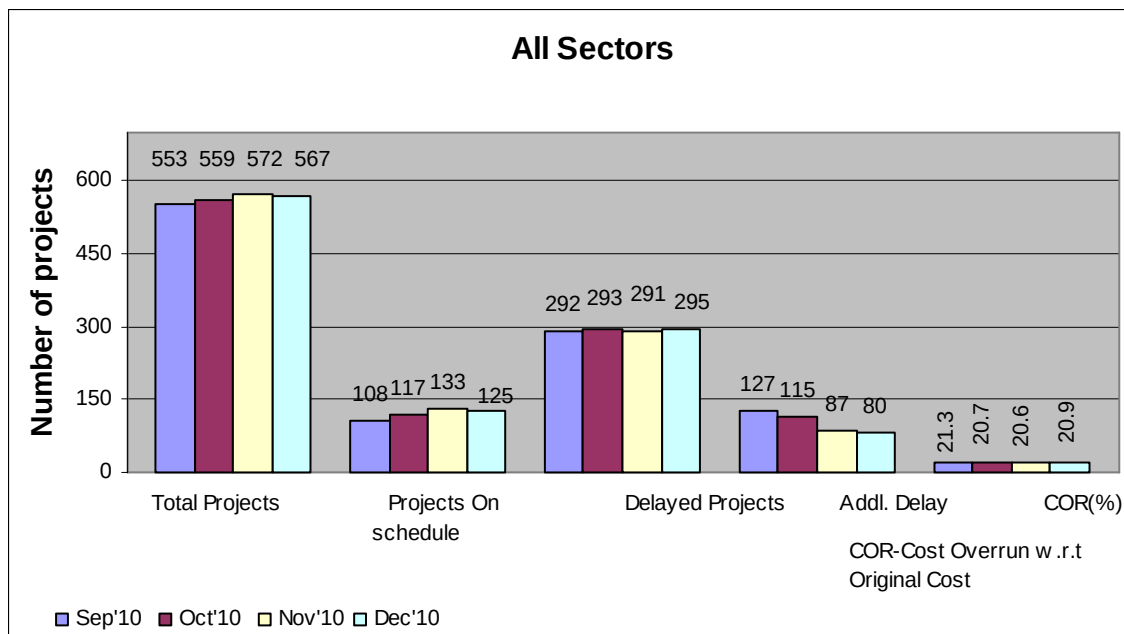

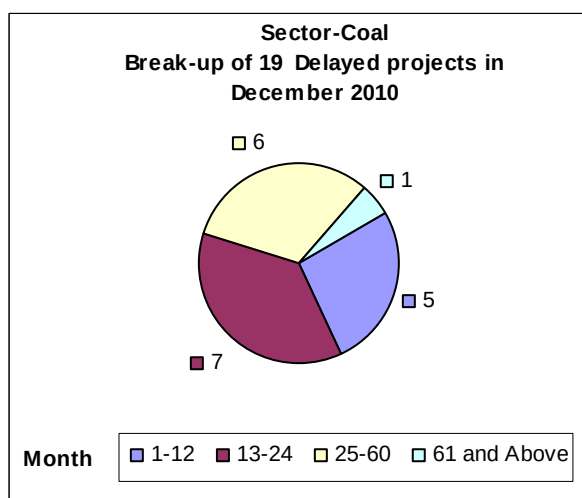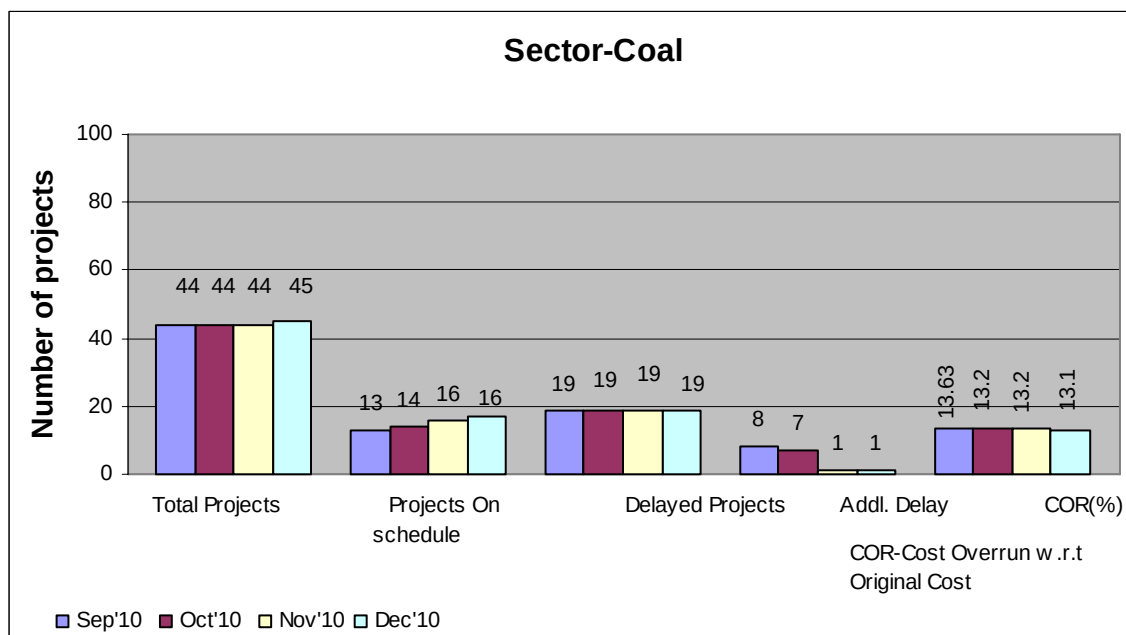


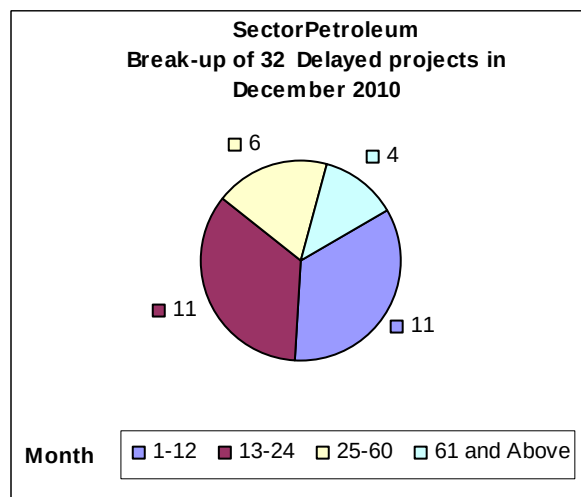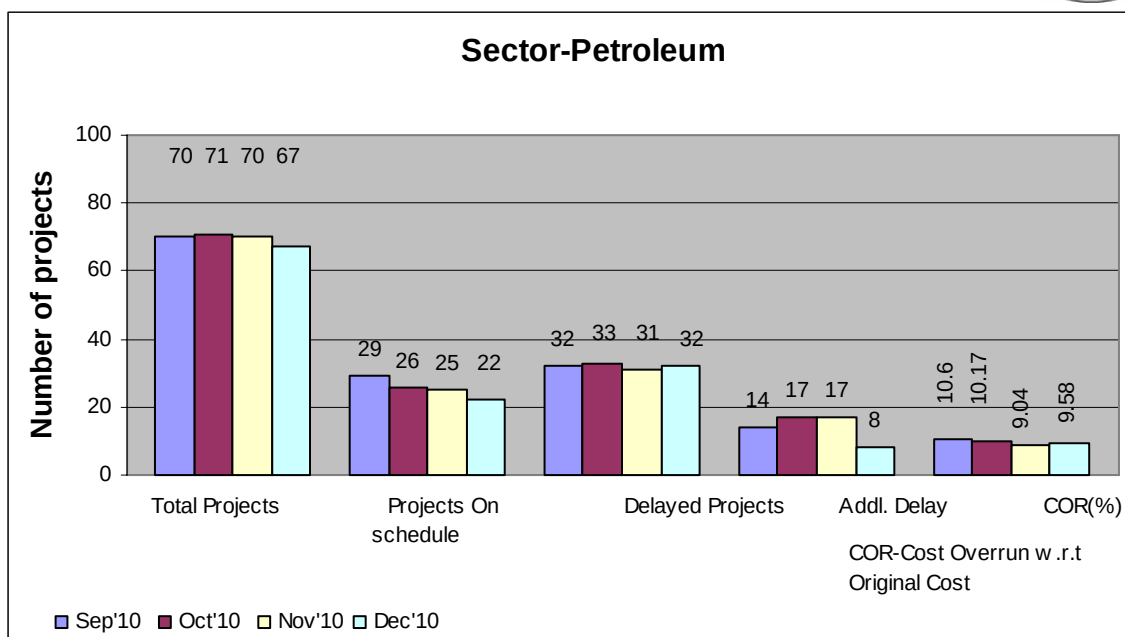

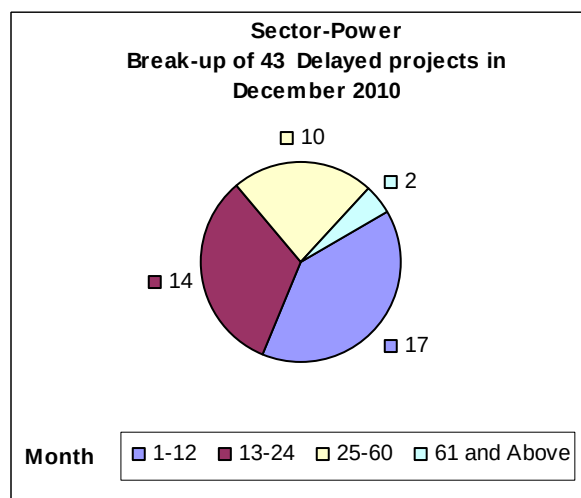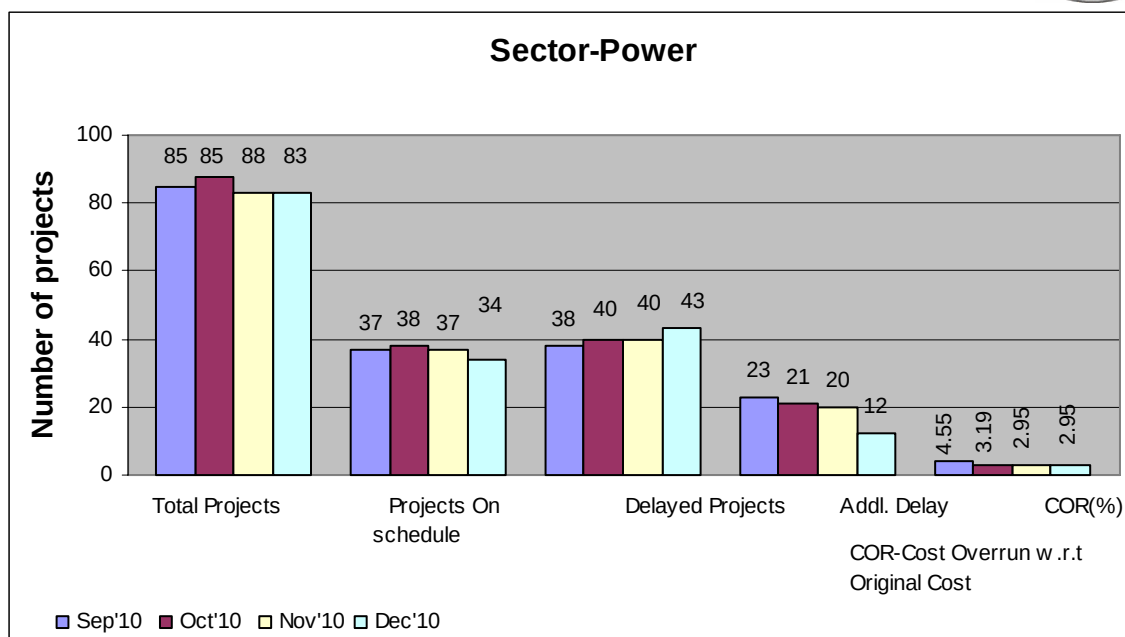


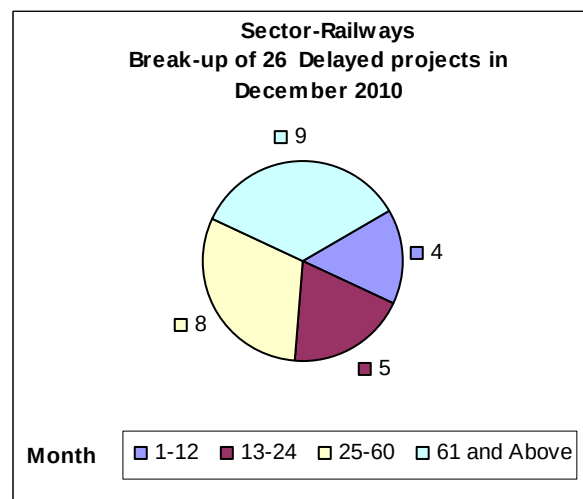
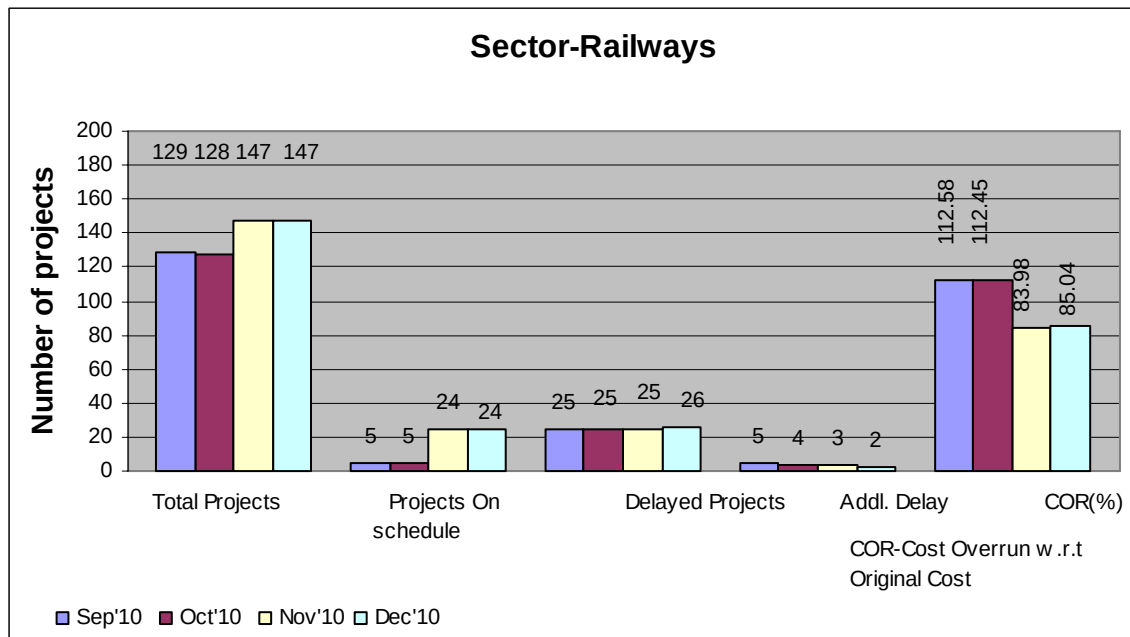




Sector-Road Transport & Highways


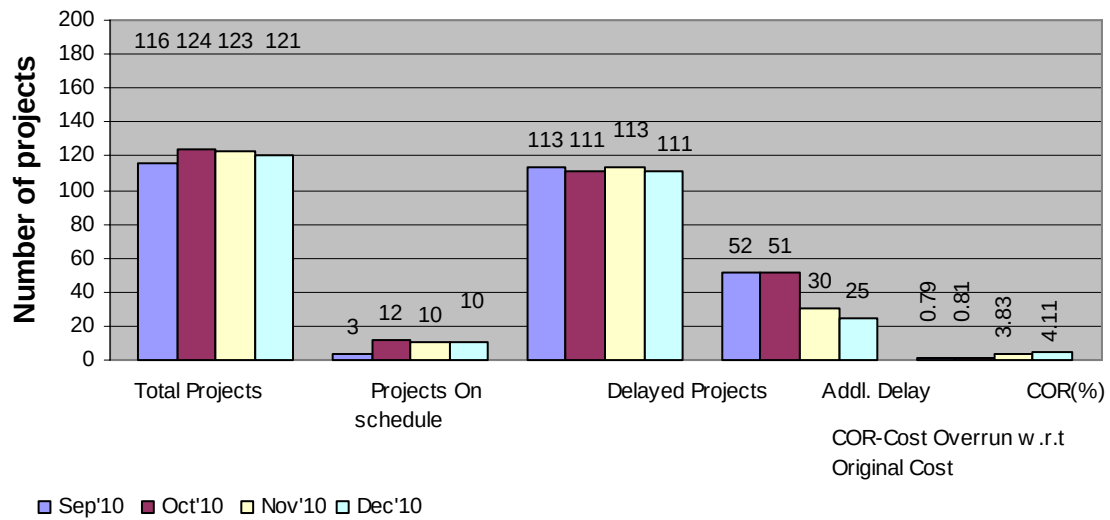


Sector-Road Transport and Highways Break-up of 111 Delayed projects in December 2010

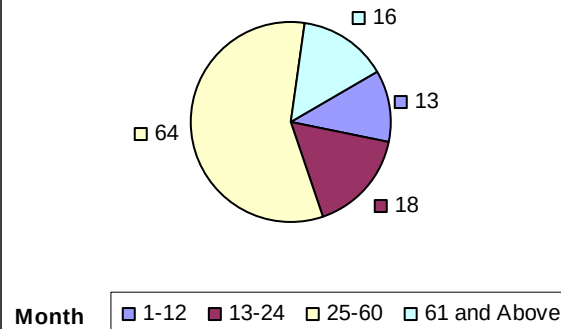

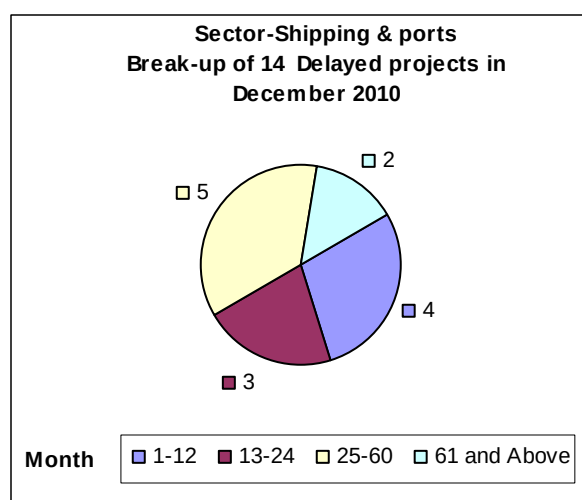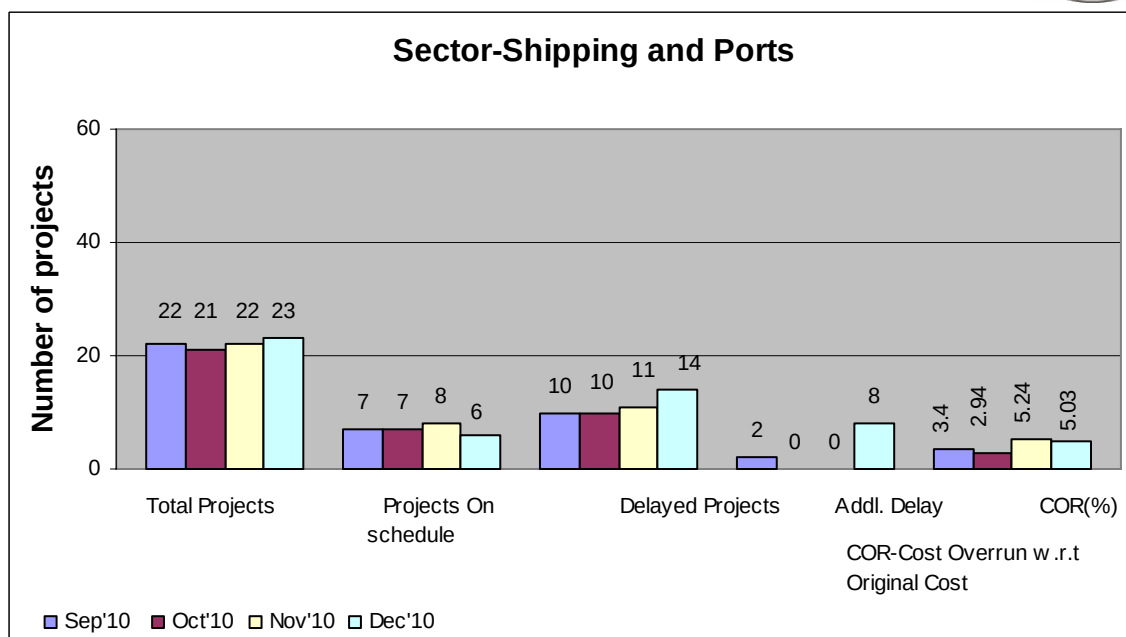

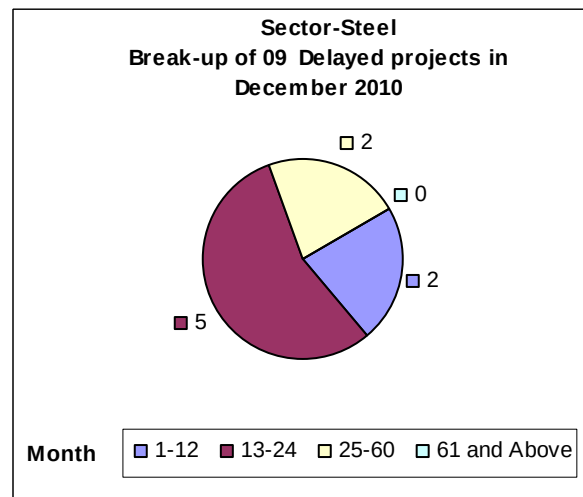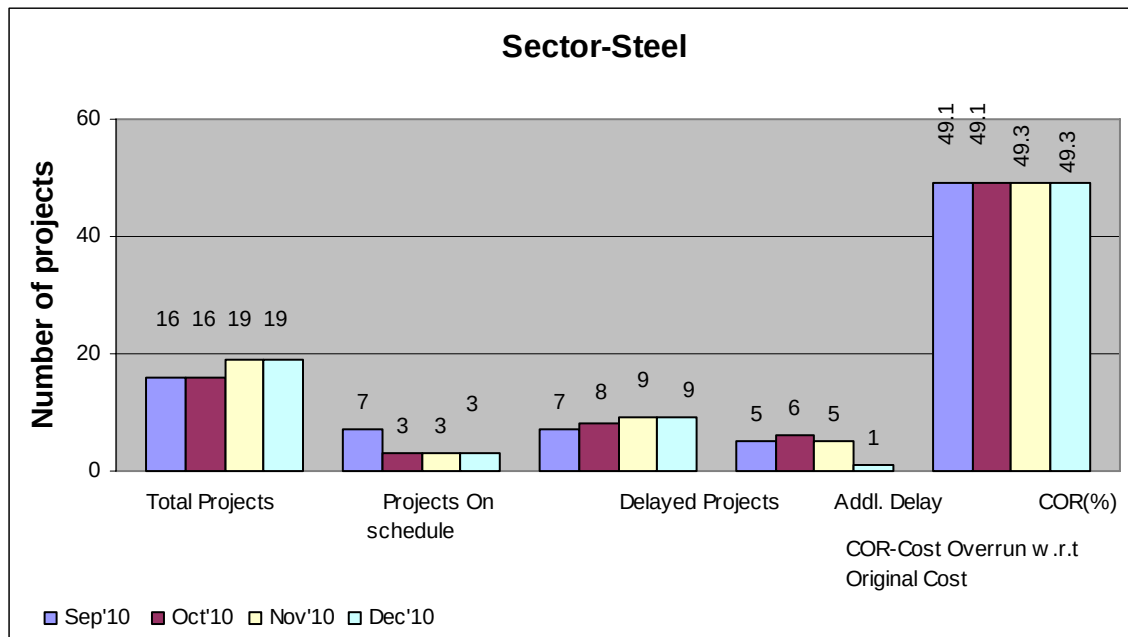

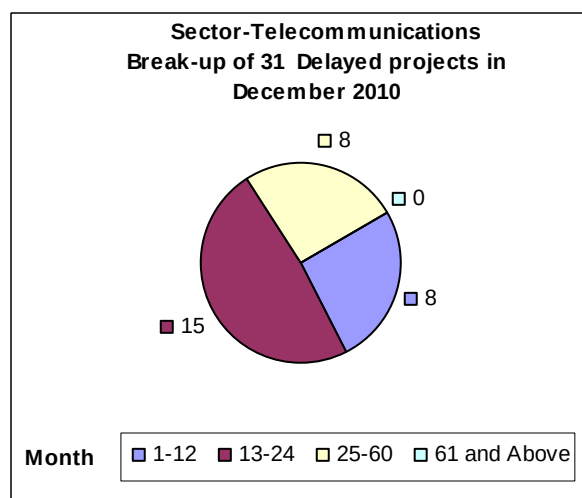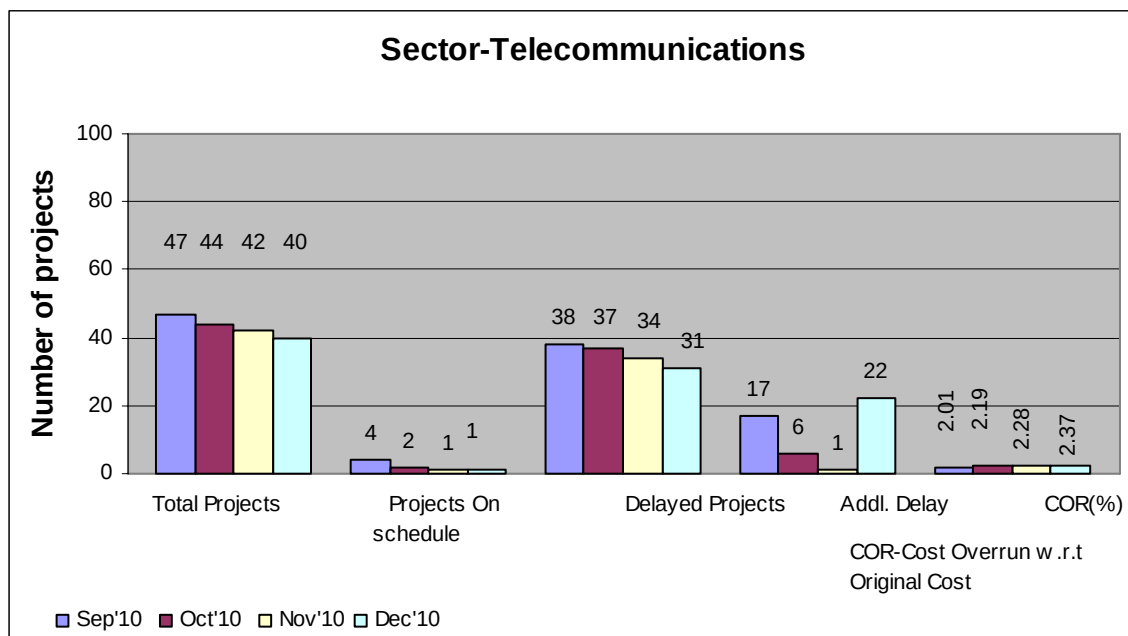

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	24,167.29
Civil Aviation	8	4,812.40	4,812.40	4,812.40
Coal	45	25,452.49	29,050.13	28,789.58
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	19	43,780.53	59,104.76	65,379.56
Petroleum	67	140,110.59	160,721.94	153,534.21
Power	83	179,759.57	180,170.28	185,077.10
Railways	147	68,578.35	81,651.69	126,901.43
Road Transport & Highways	121	45,247.77	45,247.77	47,108.09
Shipping & Ports	23	18,352.60	18,953.62	19,276.36
Telecommunications	40	19,435.89	19,408.79	19,898.19
Urban Development	2	15,071.00	8,608.36	30,503.36
Water Resources	1	542.90	542.90	1,187.00
Grand total	567	592,535.30	639,974.10	716,353.74

(Dec,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]NPCIL,Karnataka	05/2001	4,213.00	4,213.00	2,610.00	10/2009 09/2007	12/2010	39(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	486.37	-	04/2011	-	0/1
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	2,592.29	09/2010	09/2011	12(O)	8/80
4	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	13,171.00	13,398.00	12/2008	12/2011	36(O)	61/119
Total			21,982.29	24,167.29	19,086.66				140/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]AAI,Gujarat	02/2007	290.92	290.92	259.35	-	01/2011	-	1/24
6	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00	1,273.00	659.13	01/2011	01/2011	0(O)	0/0
7	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00	230.00	220.64	01/2011	01/2011	0(O)	0/0
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35	213.35	207.18	09/2010	02/2011	5(O)	0/0
9	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	1,942.51	867.54	05/2011	08/2011	3(O)	0/0
10	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73	204.73	21.65	05/2012	05/2012	0(O)	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60	393.60	205.95	06/2013	06/2013	0(O)	0/0
12	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29	264.29	85.64	01/2011	-	-	0/0
Total			4,812.40	4,812.40	2,527.08				1/24
<u>Coal</u>									
13	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18	1,626.09	1,525.84	06/2009	01/2011	19(O)	59/26
14	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08	172.08	156.09	03/2009 03/2011	03/2011	0(R3)	0/2
15	Churi Benti UG - [N06000083]JCL,Jharkhand	06/2007	163.51	163.51	33.46	03/2011	03/2011	0(O)	0/2
16	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78	2,453.57	2,063.64	06/2009	10/2011	28(O)	41/24

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	65.72	03/2010 -	03/2012	24(O)	0/4
18	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	102.68	03/2011 03/2012	03/2012	0(R3)	0/2
19	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	38.85	03/2012 -	03/2012	0(O)	8/42
20	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.13	03/2012 03/2012	03/2012	0(R3)	0/1
21	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	58.70	03/2012 -	03/2012	0(O)	0/0
22	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.57 418.97	418.97	71.60	- -	03/2012	-	7/7
23	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.91 -	181.19	0.90	- -	03/2012	-	2/8
24	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	68.37	03/2012 -	03/2012	0(O)	0/2
25	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	78.66	03/2012 -	03/2012	0(O)	0/2
26	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	1,318.00	08/2012 -	08/2012	0(O)	0/3
27	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.56	741.56	137.06	03/2010 03/2013	03/2013	0(R3)	0/2
28	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 1,188.31	1,188.31	556.01	03/2011 -	03/2013	24(O)	0/4
29	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.23	07/2012 03/2013	03/2013	0(R3)	0/2
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	11.42	03/2013 -	03/2013	0(O)	0/83
31	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	52.04	- -	03/2013	-	0/2
32	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	26.41	03/2013 -	03/2013	0(O)	0/2
33	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	22.83	03/2013 -	03/2013	0(O)	0/2
34	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	133.88	03/2013 07/2012	06/2013	11(R3)	2/22
35	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 2,675.67	2,675.67	1,022.08	03/2010 03/2014	03/2014	0(R3)	3/10
36	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 1,943.66	1,943.66	907.85	03/2010 03/2014	03/2014	0(R3)	2/8
37	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	140.85	03/2014 03/2014	03/2014	0(R3)	1/1
38	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	254.44	06/2014 -	03/2014	-3(O)	0/0
39	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	02/2006	50.08 153.82	153.82	15.29	- 03/2014	03/2014	0(R3)	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
40	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77	339.77	0.05	03/2014	03/2014	0(O)	0/2
41	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
42	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	213.57	03/2013	03/2014	12(O)	0/0
43	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	437.34	136.96	03/2012 03/2015	03/2015	0(R3)	0/1
44	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	11/2009	03/2015	64(O)	0/0
45	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	24.33	03/2013	03/2015	24(O)	0/3
46	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2012 03/2015	03/2015	0(R3)	0/0
47	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	54.49	- 12/2012	03/2015	27(R3)	7/44
48	Batura OC - [N06000049]BCCL,Madhya pradesh	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
49	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
50	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	201.58 209.78	209.78	14.89	- -	03/2015	-	0/8
51	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	44.47	03/2014 03/2016	03/2016	0(R3)	1/2
52	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	6.04	03/2015	03/2016	12(O)	0/2
53	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	158.59	198.59	92.09	03/2016	03/2016	0(O)	0/0
54	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	290.99	03/2016	03/2016	0(O)	0/2
55	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2016	03/2016	0(O)	0/0
56	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.00	490.10	59.35	- -	03/2017	-	0/1
57	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	-	- -	-	-	0/0
Total			25,452.49	28,789.58	9,817.26				133/329
Fertilisers									
58	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	18.28	07/2011	07/2011	0(O)	0/0
59	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	33.62	07/2011	07/2011	0(O)	0/0
60	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	29.87	- 11/2011	11/2011	0(R3)	2/22
61	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	71.49	01/2013	01/2013	0(O)	0/5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	61.56	01/2013	01/2013	0(O)	0/5
63	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	43.21	12/2012	01/2013	1(O)	0/8
	Total		5,317.41	5,317.41	258.03				2/40
	Mines								
64	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51	4,401.76	3,908.29	12/2008	03/2011	2(R3)	116/110
	Total		4,091.51	4,401.76	3,908.29				116/110
	Steel								
65	EXPANSION OF SALEM STEEL PLANT - [N12000050]SAIL,Tamil Nadu	01/2008	1,902.00	1,902.00	1,754.78	06/2011	09/2010	-9(O)	2/6
66	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]SAIL,Orissa	07/2007	302.70	302.70	244.97	06/2009	10/2010	16(O)	0/0
67	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]SAIL,Orissa	01/2008	197.66	197.66	130.32	11/2009	10/2010	11(O)	0/0
68	AIR SEPARATION PLANT (ASU-4) - [N12000060]RINL,Andhra Pradesh	03/2008	96.00	170.00	73.03	06/2010	12/2010	6(O)	0/0
69	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,499.00	7,446.00	10/2009	02/2011	16(O)	4/16
70	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL,Jharkhandd	07/2008	172.78	172.78	119.05	01/2010	02/2011	13(O)	0/1
71	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Madhya pradesh	07/2007	111.28	232.93	102.58	05/2011	05/2011	0(O)	0/1
72	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2003	295.89	607.17	31.05	-	06/2011	-	2/21
73	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	190.59	-	06/2011	10(R3)	0/1
74	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	235.68	04/2010	08/2011	16(O)	0/2
75	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	193.10	02/2010	08/2011	6(R3)	0/0
76	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	14,443.00	9,904.98	06/2011	12/2011	0(R3)	0/6
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00	6,325.00	1,608.60	12/2011	12/2011	0(R3)	0/7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
78	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Andhra Pradesh	05/2008	480.00 -	480.84	52.58	09/2010 -	05/2012	20(O)	0/0
79	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	25.19	10/2009 -	10/2012	36(O)	0/0
80	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	6,133.00 -	8,128.00	2,506.34	02/2011 -	03/2013	25(O)	0/0
81	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	1,782.09	03/2013 03/2013	03/2013	0(R3)	0/8
82	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]SAIL, Jharkhand	10/2007	892.32 -	892.32	616.57	08/2009 -	-	-	2/1
83	POWER PLANT-I - [N12000039]RINL, Andhra Pradesh	09/2007	462.00 -	350.00	84.40	12/2009 -	-	-	0/0
	Total		43,780.53 -	65,379.56	27,101.90				10/70
Petroleum									
84	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL, Maharashtra	03/2007	900.47 -	900.47	183.15	09/2009 -	12/2010	15(O)	0/0
85	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL, Punjab	01/2009	605.40 605.40	510.00	354.56	12/2010 12/2010	12/2010	0(R3)	17/17
86	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL, Kerala	09/2009	2,591.80 3,941.41	3,941.41	3,194.99	12/2009 -	12/2010	12(O)	0/0
87	RESIDUE UPGRADEATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL, Gujarat	01/2007	5,693.00 6,898.00	6,898.00	5,868.67	- 06/2010	01/2011	7(R3)	57/42
88	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]GAIL, Multi State	11/2007	5,595.31 4,316.00	3,700.00	3,326.01	11/2009 04/2010	01/2011	9(R3)	0/0
89	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL, Multi State	11/2007	396.13 -	396.13	185.56	10/2009 -	01/2011	15(O)	0/0
90	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar	06/2009	613.54 -	727.88	261.36	12/2010 -	01/2011	1(O)	0/0
91	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC, Gujarat	12/2003	900.92 1,493.49	976.08	738.32	06/2006 07/2010	02/2011	7(R3)	0/2
92	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 -	224.00	152.06	12/2010 02/2011	02/2011	0(R3)	0/0
93	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]BRPL, Assam	06/2006	1,431.91 1,646.39	1,687.00	1,484.16	09/2009 -	03/2011	18(O)	0/0
94	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.63	12/2008 12/2008	03/2011	27(R3)	0/0
95	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC, Maharashtra	09/2006	2,305.30 -	2,305.30	2,061.15	06/2010 06/2010	03/2011	9(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
96	MSQ IMPROVMENT PROJECT - [N16000040]IOCL, Assam	04/2008	293.60	294.00	200.45	12/2009	03/2011	15(O)	0/0
97	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL, Maharashtra	06/2008	304.40	304.40	181.21	12/2010	03/2011	3(O)	0/0
98	DAHEJ-VIJAYPUR PIPE LINE PROJECT (PHASE-II) - [N16000052]GAIL, Multi State	11/2007	4,429.38 4,403.00	2,500.00	1,887.54	10/2011 04/2011	04/2011	0(R3)	0/2
99	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL, Madhya Pradesh	11/2007	1,512.00 1,434.00	1,434.00	810.72	- 04/2011	04/2011	0(R3)	0/3
100	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 1,167.00	810.00	235.40	04/2011 04/2011	04/2011	0(R3)	0/2
101	HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70	706.70	515.98	04/2010	04/2011	12(O)	0/0
102	NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08	305.08	95.92	04/2011	04/2011	0(O)	0/0
103	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	03/2005 05/2011	05/2011	0(R3)	0/0
104	MNW-NF BRIDGE PROJECT - [N16000045]ONGC, Maharashtra	05/2008	175.21	162.12	58.26	03/2009	05/2011	26(O)	0/0
105	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	01/2010	589.70 755.76	755.76	139.20	03/2011 05/2011	05/2011	0(R3)	0/0
106	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL, Multi State	07/2011	1,816.07 1,816.07	1,400.00	558.61	- 04/2011	06/2011	2(R3)	0/1
107	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	540.92	1.35	06/2011	06/2011	0(O)	7/9
108	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32	375.00	0.13	06/2011	08/2011	2(O)	3/9
109	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00	3,597.00	112.64	09/2011	09/2011	0(O)	0/0
110	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00	3,284.00	80.01	09/2011	09/2011	0(O)	0/0
111	BNPL superlines (Uttanchal & Punjab) - [N16000091]GAIL, Multi State	12/2009	540.92	540.92	1.35	05/2011	10/2011	5(O)	0/0
112	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00	756.00	527.87	12/2011	12/2011	0(O)	0/0
113	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL, Gujarat	02/2009	349.00	349.00	132.83	08/2011	12/2011	4(O)	0/0
114	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL, Multi State	06/2009	348.00	348.00	-	03/2012	12/2011	-3(O)	6/12
115	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL, Maharashtra	02/2008	825.00	825.00	97.27	-	12/2011	-	0/203

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	180.09	12/2011 -	12/2011	0(O)	0/0
117	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	110.39	12/2011 -	12/2011	0(O)	0/0
118	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	34.39	- -	12/2011	-	0/116
119	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	411.41	03/2010 03/2012	03/2012	0(R1)	0/0
120	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,600.00	49.60	03/2012 -	03/2012	0(O)	11/10
121	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	19.99	- -	03/2012	-	5/36
122	Assam gas Cracker project - [N16000106]BCPL,Assam	04/2006	5,460.61 -	5,460.61	1,391.19	- -	04/2012	-	0/2
123	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	1,803.99	05/2010 05/2012	05/2012	0(R3)	0/0
124	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	1,552.63 2,920.82	2,920.82	356.64	02/2009 03/2012	05/2012	2(R3)	0/0
125	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 -	330.40	3.01	05/2010 -	05/2012	24(O)	0/0
126	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	-	07/2010 05/2012	05/2012	0(R3)	0/0
127	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	241.41	03/2010 03/2012	06/2012	3(R3)	0/0
128	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	214.05	06/2012 -	06/2012	0(O)	0/0
129	Additional Development of D-1 Field - [N16000097]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	214.37	12/2011 06/2012	06/2012	0(R3)	0/0
130	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	17.75	04/2011 -	07/2012	15(O)	0/0
131	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	10.50	08/2012 -	08/2012	0(O)	0/0
132	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	6,855.93 -	6,855.93	1,134.29	09/2012 -	09/2012	0(O)	0/0
133	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	22.94	- -	09/2012	-	0/15
134	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
135	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	29,777.00	5,029.55	- -	11/2012	-	58/103

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
136	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	1,797.35	9.78	12/2011	01/2013	13(O)	0/0
137	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	0.65	01/2013	01/2013	0(O)	0/0
138	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	7.93	01/2013	01/2013	0(O)	0/0
139	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	-	02/2013	02/2013	0(O)	0/0
140	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90	438.85	198.22	03/2006 03/2013	03/2013	0(R3)	6/6
141	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	06/2007	1,252.75	8,813.41	5,528.52	06/2009 03/2013	03/2013	0(R3)	0/0
142	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	263.44	03/2013	03/2013	0(O)	0/0
143	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
144	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
145	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
146	Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	6.48	02/2014	02/2014	0(O)	0/0
147	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	552.27	03/2007 03/2014	03/2014	0(R3)	3/3
148	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,138.77	03/2007 03/2017	03/2017	0(R3)	6/6
149	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	2.20	10/2010	-	-	0/0
150	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	1.60	-	-	-	0/0
Total			140,110.59	153,534.21	46,160.39				179/599
Power									
151	KORBA STPP STAGE-III - [N18000011]NTPC,Madhya pradesh	08/2006	2,448.50	2,448.49	2,119.00	02/2010	12/2010	10(O)	5/24
152	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]PGCIL,Gujarat	02/2008	340.72	340.72	160.15	11/2010	12/2010	1(O)	0/0
153	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	142.68	09/2010	01/2011	4(O)	0/0
154	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL,Multi State	12/2008	328.97	328.97	161.47	09/2011	01/2011	-8(O)	0/0
155	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34	241.27	158.18	06/2008	02/2011	32(O)	8/20

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70 -	803.76	628.94	06/2009 -	02/2011	20(O)	1/20
157	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44 -	2,570.44	1,818.00	08/2010 -	02/2011	6(O)	13/26
158	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	117.55	06/2010 -	02/2011	8(O)	0/0
159	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49 -	299.08	310.85	04/2010 -	02/2011	10(O)	0/0
160	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.37	251.84	07/2011 -	02/2011	-5(O)	0/0
161	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Uttar Pradesh	10/2006	975.96 -	894.26	629.93	10/2009 -	03/2011	17(O)	2/20
162	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89 -	230.89	58.41	01/2011 -	03/2011	2(O)	0/0
163	Transmission system associated with Uri-II HEP - [N18000023]PGCIL,J & K	10/2006	238.25 -	227.03	199.03	- -	05/2011	-	0/0
164	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,103.39	3,493.00	05/2011 -	05/2011	0(O)	0/0
165	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,946.85	1,636.77	11/2008 -	06/2011	31(O)	25/38
166	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,725.13	3,430.00	09/2009 -	06/2011	21(O)	15/30
167	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	639.52	412.16	01/2010 -	06/2011	17(O)	0/22
168	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	4,978.56	2,704.79	07/2010 -	06/2011	11(O)	3/20
169	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	325.00	09/2010 -	06/2011	9(O)	0/0
170	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07 -	204.07	92.74	06/2011 -	06/2011	0(O)	0/0
171	TRANSMISSION SYSTEM ASSOCIATED WITH CORBA III GENE - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61 -	276.61	172.46	06/2011 -	06/2011	0(O)	0/0
172	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	27.36	07/2011 -	07/2011	0(O)	0/0
173	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,394.55	08/2010 -	08/2011	12(O)	0/0
174	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.26 -	621.28	577.70	02/2011 -	08/2011	6(O)	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
175	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	107.07	08/2011	08/2011	0(O)	0/0
176	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC,J & K	08/2006	611.01	611.02	573.06	08/2010	09/2011	13(O)	0/0
177	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,729.29	1,724.79	1,290.19	11/2009	11/2011	24(O)	0/0
178	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	211.24	11/2011	11/2011	0(O)	0/0
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	165.93	11/2011	11/2011	0(O)	0/0
180	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	17.39	11/2011	11/2011	0(O)	0/0
181	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	91.24	11/2011	11/2011	0(O)	0/0
182	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,233.10	03/2007	12/2011	57(O)	1/25
183	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	6,691.00	12/2009	12/2011	24(O)	33/56
184	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,304.52	1,240.45	10/2010	12/2011	14(O)	0/0
185	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	59.13	01/2012	01/2012	0(O)	0/0
186	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	104.11	02/2012	02/2012	0(O)	0/0
187	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	12.80	02/2012	02/2012	0(O)	0/0
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	108.13	02/2012	02/2012	0(O)	0/0
189	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	166.25	07/2010	02/2012	19(O)	0/0
190	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	545.03	02/2012	02/2012	0(O)	0/0
191	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,153.17	04/2005	03/2012	83(O)	2/1
192	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	16.75	04/2012	04/2012	0(O)	0/0
193	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	114.09	05/2012	05/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
194	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	-	06/2012	06/2012	0(O)	0/0
195	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	46.13	06/2012	06/2012	0(O)	0/0
196	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	4.85	06/2012	06/2012	0(O)	0/0
197	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	854.30	09/2009	08/2012	35(O)	0/0
198	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,424.84	08/2012	08/2012	0(O)	0/0
199	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	2,818.03	08/2012	08/2012	0(O)	0/0
200	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	128.75	08/2012	08/2012	0(O)	0/0
201	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	1,599.00	07/2011	10/2012	15(O)	0/0
202	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	1,669.00	02/2012 08/2012	10/2012	2(R3)	0/0
203	TRANSMISSION SYSTEM ASSOCIATED WITH MUNDRA ULTRA M - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,144.97	10/2012	10/2012	0(O)	0/0
204	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	19.71	10/2012	10/2012	0(O)	0/0
205	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF I - [N18000089]PGCIL,Multi State	10/2012	160.32	160.32	-	10/2012	10/2012	0(O)	0/0
206	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	13.61	11/2012	11/2012	0(O)	0/0
207	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2012	965.58	965.58	95.60	11/2012	11/2012	0(O)	0/0
208	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42	358.42	9.25	12/2008 09/2010	12/2012	27(R1)	0/15
209	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
210	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	1,582.46	12/2012	12/2012	0(O)	0/0
211	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	1,296.00	11/2012	12/2012	1(O)	0/0
212	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	1,161.00	11/2012	12/2012	1(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
213	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	96.15	12/2012	12/2012	0(O)	0/0
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	-	01/2013	01/2013	0(O)	0/0
215	Transmission System for phase-1 generation project - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	-	02/2013	02/2013	0(O)	0/0
216	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,394.00	04/2009	03/2013	47(O)	19/41
217	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,319.72	05/2013 05/2013	05/2013	0(R3)	77/22
218	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	139.39	08/2012	08/2013	12(O)	4/13
219	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	1,663.60	08/2013	08/2013	0(O)	0/0
220	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,032.59	01/2012	09/2013	20(O)	2/10
221	BARH STPP STAGE -II (NTPC) - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	1,429.00	08/2013	10/2013	2(O)	0/0
222	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	6,285.33	4,323.47	09/2010	12/2013	39(O)	2/11
223	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72	913.63	218.16	07/2006	01/2014	90(O)	2/5
224	Tapovan-Vishnugad HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	946.00	03/2013	02/2014	11(O)	5/31
225	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	3,007.20	09/2009	07/2014	58(O)	1/20
226	BARH STPP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	5,136.00	11/2010	09/2014	46(O)	15/51
227	Transm System for development of Pooling str. in N - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
228	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00	2,978.86	250.70	07/2010	03/2015	56(O)	0/0
229	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	506.90	07/2014	01/2016	18(O)	0/0
230	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	2,491.58	137.40	07/2014	03/2016	20(O)	0/8
231	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,Manipur	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
232	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	780.75	12/2007	-	-	14/18
233	National Capital Thermal Power Project Stage-II - [N18000013]NTPC,Uttar Pradesh	10/2006	5,135.33	5,135.33	4,000.00	10/2010	-	-	12/40

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			179,759.57	185,077.10	78,751.88				267/622
<u>Railways</u>									
234	VALLAPARPADM-IDAPALLY, (NL) (RVNL) - [N22000048] RVNL, Kerala	07/2006	246.50 246.50	246.50	323.67	03/2009 03/2009	11/2009	8(R3)	0/0
235	KOTTUR-HARIHAR (NL), (SWR) - [220100212] SWR, Karnataka	04/1995	65.94 -	281.20	312.68	- -	09/2010	-	0/0
236	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322] WR, Gujarat	04/2005	148.61 -	227.52	246.10	03/2008 03/2009	10/2010	19(R1)	0/0
237	AJMER-UDAIPUR-CHITTAURGARH (GC), NWR - [220100185] NWR, Rajasthan	09/1996	262.00 456.00	567.23	546.55	- 03/2000	11/2010	128(R1)	0/0
238	KATIHAR - JOGBANI (GC) (NEFR) - [220100247] NEFR, Multi State	09/2001	100.00 492.98	724.31	700.29	- -	12/2010	-	0/0
239	RAJATGARH-BARANG (LD), ECOR - [220100286] RVNL, Orissa	04/1999	166.16 -	243.40	215.04	- 02/2009	12/2010	22(R1)	0/0
240	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327] RVNL, Orissa	04/2000	133.41 207.00	211.90	166.15	- 03/2009	12/2010	21(R1)	0/0
241	RAICHUR-GUNTAKAL (DL) (SCR) - [220100329] RVNL, Andhra Pradesh	04/2003	136.62 -	221.90	134.12	12/2007 03/2010	12/2010	9(R1)	0/0
242	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034] RVNL, Uttar Pradesh	04/2003	230.73 399.73	399.50	283.09	03/2009 12/2008	12/2010	24(R1)	0/0
243	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081] RVNL, Gujarat	09/2005	200.80 -	200.80	195.35	- -	12/2010	-	0/0
244	Pandabeswar-Chinai doubling (ER) - [N22000118] ER, West Bengal	04/2004	225.68 -	225.68	112.81	12/2010 -	12/2010	0(O)	0/0
245	DEOGHAR-DUMKA NEW BG LINE (DOUBL.) (ER) - [220100264] ER, Jharkhand	02/1999	180.73 -	358.00	330.78	12/2006 12/2008	02/2011	26(R1)	0/0
246	REWARI-ROHTAK (NL), NR - [220100279] (NR), Haryana	01/2004	149.38 330.23	475.16	431.86	02/2010 -	02/2011	12(O)	0/0
247	TALCHER-BIMALAGARH (NL) (ECOR) - [220100328] ECOR, Orissa	04/2005	726.96 -	810.78	70.80	- -	02/2011	-	0/0
248	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056] SWR, Karnataka	12/1992	46.00 -	218.00	227.16	- -	02/2011	-	0/0
249	AMRAVATI-NARKHER NL (CR) - [220100118] CR, Maharashtra	06/1994	120.90 284.27	488.76	357.49	06/1999 -	03/2011	141(O)	0/0
250	LANJHIGARH-JUNAGARH NL (ECOR) - [220100148] ECR, Orissa	04/1993	100.00 119.29	170.00	157.86	03/2002 -	03/2011	108(O)	0/0
251	MUZAFFARPUR-SITAMARHI (NL), ECR - [220100194] ECR, Bihar	03/1997	100.00 -	322.29	380.92	- -	03/2011	-	0/0
252	RANCHI-LOHARDAGA (GC), SER - [220100214] SER, Jharkhand	04/1997	193.78 -	456.45	247.29	06/2004 -	03/2011	81(O)	0/0
253	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] NCR, Multi State	09/1998	925.00 -	925.00	482.60	05/2008 -	03/2011	34(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
254	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 -	214.09	176.20	12/2009 -	03/2011	15(O)	0/0
255	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]SCR,Andhra Pradesh	05/2002	304.50 -	306.00	341.81	- -	03/2011	-	0/0
256	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	5,573.82	2,884.45	12/2006 08/2010	03/2011	7(R3)	0/0
257	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECR,Orissa	04/1994	355.38 -	700.00	110.49	- -	03/2011	-	0/0
258	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/1997	143.92 -	258.60	194.60	- -	03/2011	-	0/0
259	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	200.73 -	230.03	132.16	- -	03/2011	-	0/0
260	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0
261	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	348.78	319.58	- -	03/2011	-	0/0
262	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
263	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 255.96	272.11	223.40	- -	03/2011	-	0/0
264	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	77.36	12/2010 -	03/2011	3(O)	0/0
265	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
266	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	03/2006	258.35 -	258.35	9.38	03/2011 -	03/2011	0(O)	0/0
267	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	128.59	03/2011 -	03/2011	0(O)	0/0
268	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	726.31	03/2011 -	03/2011	0(O)	0/0
269	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	145.69	03/2011 -	03/2011	0(O)	0/0
270	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,078.00	- 12/2010	06/2011	6(R3)	0/1
271	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	118.55	02/2010 -	11/2011	21(O)	0/0
272	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	188.15	- 09/2009	12/2011	27(R1)	0/0
273	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	32.27	12/2011 -	12/2011	0(O)	0/0
274	Ghutarisharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	32.69	12/2011 -	12/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	727.52	488.20	- -	03/2012	-	0/0
276	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	415.59 -	495.74	97.19	- -	03/2012	-	0/0
277	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	140.88	03/2010 -	03/2012	24(O)	0/0
278	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	160.48	109.40	- -	03/2012	-	0/0
279	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	27.38	03/2012 -	03/2012	0(O)	0/0
280	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	34.03	03/2012 -	03/2012	0(O)	0/0
281	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]ER,Gujarat	04/2008	318.24 -	318.24	-	03/2012 -	03/2012	0(O)	0/0
282	TAMLUK DIGHA - [N22000097]LD,West Bengal	03/1984	293.97 -	293.97	313.13	06/2005 -	04/2012	82(O)	0/0
283	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	296.79	- -	07/2012	-	0/0
284	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	510.60	03/1994 -	12/2012	225(O)	0/0
285	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	2,100.00	529.22	- -	12/2012	-	0/0
286	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1997	248.44 576.27	1,103.47	726.64	- -	12/2012	-	0/0
287	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	383.15 -	863.23	346.38	- -	12/2012	-	0/0
288	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	234.45	170.23	- 03/2012	12/2012	9(R3)	0/0
289	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	193.51	- -	12/2012	-	0/0
290	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	422.96	03/2009 -	12/2012	45(O)	0/0
291	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.00	763.12	10/2007 -	12/2012	62(O)	0/0
292	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	232.32	03/2010 -	12/2012	33(O)	0/0
293	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	93.22	12/2012 -	12/2012	0(O)	0/0
294	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 -	410.08	115.41	- -	03/2013	-	0/0
295	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	608.40	- -	03/2013	-	0/0
296	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	912.70 912.70	1,556.23	382.30	- -	03/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
297	Ramanagram-Musore doubling with deiltification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.00	139.15	03/2013 -	03/2013	0(O)	0/0
298	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.13	0.03	03/2013 -	03/2013	0(O)	0/0
299	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	139.81	- -	12/2013	-	0/0
300	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	04/1996	1,000.00 1,500.00	3,230.02	2,001.81	04/2008 12/2011	03/2014	27(R1)	0/0
301	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	02/2000	733.00 -	1,655.80	607.72	12/2008 -	03/2014	63(O)	0/0
302	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	117.77	03/2014 -	03/2014	0(O)	0/0
303	BHAIRABI SAIRONG, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	1.61	04/2014 -	03/2014	-1(O)	0/0
304	New Work for Construction of Metro railway from Bu - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	-	03/2014 -	03/2014	0(O)	0/0
305	Jaipur - Ringus - Churu and Sikar - Lohatu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	2.89	03/2014 -	03/2014	0(O)	0/0
306	Suratpura - Hanumangarh - Sriganganagar Guage Canv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	1.70	03/2014 -	03/2014	0(O)	0/0
307	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	61.97	03/2014 -	03/2014	0(O)	0/0
308	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	88.60	03/2010 -	06/2014	51(O)	0/0
309	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	137.87	- -	03/2015	-	0/0
310	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	167.24	03/2014 -	03/2015	12(O)	0/0
311	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.90	12/2015 -	03/2015	-9(O)	0/0
312	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
313	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	5.46	03/2015 -	03/2015	0(O)	0/0
314	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,123.52	274.88	03/2011 -	03/2016	60(O)	0/0
315	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	3,447.41 -	5,573.83	-	03/2016 -	03/2016	0(O)	0/0
316	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	-	03/2016 -	03/2016	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
317	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	2,619.02	-	03/2016 -	03/2016	0(O)	0/0
318	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J & K	03/1995	2,500.00 8,000.00	11,270.00	6,641.78	03/2001 -	12/2017	201(O)	0/0
319	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 422.79	634.13	556.48	03/1995 -	-	-	0/0
320	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 -	617.63	386.41	- -	-	-	0/0
321	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR, Gujarat	04/1992	112.53 320.66	464.50	498.96	03/1996 06/2009	-	-	0/0
322	HOTGI-GADAG(GC), SWR - [220100125]SWR, Multi State	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
323	AMBALA-MORADABAD(RE) - [220100131]RE, Multi State	03/1993	152.21 157.76	265.00	265.33	03/1998 -	-	-	0/0
324	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	01/1986	36.80 274.41	285.93	232.31	- -	-	-	0/0
325	DALLIRAJHARA-JAGDALPUR, NL, SECR - [220100149]SECR, Chhatisgarh	04/1995	369.00 968.60	1,317.24	50.08	- -	-	-	0/0
326	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	581.69	- -	-	-	0/0
327	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, Jharkhand	04/1995	184.00 -	675.00	361.41	- 12/2011	-	-	0/0
328	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	1,010.00	68.06	- -	-	-	0/0
329	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 -	412.91	473.63	- -	-	-	0/0
330	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	356.00 -	1,038.00	491.58	03/1998 -	-	-	0/0
331	KADUR-CHIKMAGALUR-SAKLESHPU (NL),(SWR) - [220100190]SWR, Karnataka	04/1996	157.00 -	157.00	125.45	- 03/2012	-	-	0/0
332	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 -	712.00	432.80	- -	-	-	0/0
333	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1997	155.74 164.36	429.49	363.58	02/2009 -	-	-	0/0
334	HUBLI-AKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00 -	997.58	54.94	- -	-	-	0/0
335	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 1,062.36	1,548.95	1,117.42	- -	-	-	0/0
336	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1996	377.32 236.41	497.47	82.45	- -	-	-	0/0
337	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 154.30	154.30	106.79	03/2007 03/2007	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
338	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
339	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 -	1,099.20	875.46	07/2005 -	-	-	0/0
340	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR,Kerala	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0
341	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00 -	513.16	520.42	- -	-	-	0/0
342	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	65.39	- -	-	-	0/0
343	PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
344	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1999	242.42 369.70	369.70	151.69	- 05/2009	-	-	0/0
345	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	09/2001	320.10 -	522.56	315.75	- -	-	-	0/1
346	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	03/1997	78.23 -	162.87	79.22	- -	-	-	0/0
347	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 408.76	639.54	788.83	06/2007 -	-	-	0/0
348	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	274.05	04/2003 03/2010	-	-	0/0
349	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	432.28	- -	-	-	0/0
350	KOTLPALI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
351	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 -	228.09	198.33	- -	-	-	0/0
352	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 240.59	607.09	253.60	- 12/2012	-	-	0/0
353	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
354	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	325.17	311.98	03/2005 12/2008	-	-	0/0
355	BHILDI-SAMDARI (GC) - [220100291]RVNL,Gujarat	04/1999	244.74 479.00	479.00	476.85	- 03/2009	-	-	0/0
356	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	64.64	- -	-	-	0/0
357	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	156.16	- -	-	-	0/0
358	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	104.10 -	218.19	74.13	- -	-	-	0/0
359	KICHHA-KHATIMA (NL) - NER - [220100317]NER,Uttaranchal	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
360	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
361	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh	04/1992	458.45	573.12	555.49	-	-	-	0/0
362	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56	671.82	1.05	-	-	-	0/0
363	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1998	186.92	261.70	0.08	02/2006	-	-	0/0
364	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	241.98	03/2008 06/2008	-	-	0/0
365	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74	224.51	41.39	-	-	-	0/0
366	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09	881.19	86.35	-	-	-	0/0
367	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	98.25	-	-	-	0/0
368	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	284.20	-	-	-	0/0
369	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	17.44	-	-	-	0/0
370	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	42.02	-	-	-	0/0
371	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	29.04	-	-	-	0/0
372	KISHANGANJ JALALGARH, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	333.76	0.71	-	-	-	0/0
373	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]GC,Assam	04/1993	100.41	949.22	15.65	12/2009	-	-	0/0
374	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	132.55	-	03/2011	-24(R3)	0/0
375	MIRAJ-LATUR ROAD(GC),CR - [220100162]CR,Maharashtra	04/1993	225.00 360.63	816.40	829.77	03/2001 03/2010	-	-	0/0
376	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81	495.44	156.77	03/2004	12/2010	81(O)	0/0
377	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40	563.25	540.90	03/2004 03/2010	-	-	0/0
378	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96	762.33	313.01	-	12/2010	12(R1)	0/0
379	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36	452.35	302.42	-	03/2011	-	0/0
380	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00	390.00	0.93	-	03/2014	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			68,578.35	126,901.43	49,039.13				0/2
<u>Road Transport & Highways</u>									
381	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00	217.00	333.80	10/2008	12/2010	26(O)	0/0
382	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI,Uttar Pradesh	12/2003	205.00	205.00	324.40	10/2008	12/2010	26(O)	0/0
383	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI,Uttar Pradesh	12/2003	212.00	212.00	367.60	10/2008	12/2010	26(O)	0/0
384	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]NHAI,Kerala	04/2000	106.00	193.00	141.70	08/2006	01/2011	53(O)	0/0
385	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]NHAI,Tamil Nadu	12/2003	480.00	480.00	846.20	11/2007	01/2011	38(O)	0/0
386	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00	210.00	662.10	04/2007	01/2011	45(O)	0/0
387	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra	03/2005	579.00	579.00	728.90	04/2009	01/2011	21(O)	0/0
388	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	909.10	11/2010	01/2011	2(O)	0/0
389	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]NHAI,Bihar	12/2003	291.80	291.80	439.90	06/2008	01/2011	31(O)	0/0
390	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	575.20	03/2009	01/2011	22(O)	0/0
391	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	577.70	06/2009	01/2011	19(O)	0/0
392	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]NHAI,Andhra Pradesh	12/2003	208.46	208.46	197.80	08/2009	01/2011	17(O)	0/0
393	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]NHAI,Andhra Pradesh	12/2003	239.19	239.19	224.80	09/2009	01/2011	16(O)	0/0
394	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]NHAI,Andhra Pradesh	12/2003	194.80	194.80	179.70	08/2009	01/2011	17(O)	0/0
395	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka	03/2005	565.00	565.00	954.80	07/2010	01/2011	6(O)	0/0
396	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]NHAI,Uttar Pradesh	12/2003	239.00	239.00	396.20	10/2008	02/2011	28(O)	0/0
397	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	265.90	10/2008	02/2011	28(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
398	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	146.90	09/2007 -	03/2011	42(O)	0/0
399	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	102.51	08/2004 -	03/2011	79(O)	0/0
400	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	112.45	08/2004 -	03/2011	79(O)	0/0
401	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	03/2011	72(O)	0/0
402	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73 -	205.73	247.20	07/2004 -	03/2011	80(O)	0/0
403	GARHMUKTESHVAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	286.80	09/2007 -	03/2011	42(O)	0/0
404	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	425.10	11/2007 -	03/2011	40(O)	0/0
405	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]NHAI,Uttar Pradesh	12/2003	158.06 -	158.06	163.40	08/2005 -	03/2011	67(O)	0/0
406	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	307.20	10/2008 -	03/2011	29(O)	0/0
407	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00 -	239.00	287.10	07/2005 -	03/2011	68(O)	0/0
408	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]NHAI,Bihar	12/2003	275.00 -	275.00	316.40	07/2005 -	03/2011	68(O)	0/0
409	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36 -	323.36	189.90	03/2008 -	03/2011	36(O)	0/0
410	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	219.70	10/2008 -	03/2011	29(O)	0/0
411	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]NHAI,Uttar Pradesh	12/2003	451.97 -	451.97	526.20	04/2008 -	03/2011	35(O)	0/0
412	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	313.50	03/2008 -	03/2011	36(O)	0/0
413	MEERUT-MUZZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	659.80	03/2009 -	03/2011	24(O)	0/0
414	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	03/2011	26(O)	0/0
415	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI,Assam	12/2003	225.00 -	225.00	212.40	06/2008 -	03/2011	33(O)	0/0
416	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00 -	198.00	152.20	11/2008 -	03/2011	28(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
417	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya Pradesh	12/2003	225.00	225.00	219.30	10/2008	03/2011	29(O)	0/0
418	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI, Bihar	12/2003	340.00	340.00	504.50	06/2008	03/2011	33(O)	0/0
419	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	199.40	06/2008	03/2011	33(O)	0/0
420	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	537.20	06/2009	03/2011	21(O)	0/0
421	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	211.50	06/2008	03/2011	33(O)	0/0
422	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	386.30	12/2008	03/2011	27(O)	0/0
423	BARA TO ORAI, NH-2, 25 - [N24000069]NHAI, Uttar Pradesh	12/2003	465.00	465.00	607.80	04/2009	03/2011	23(O)	0/0
424	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI, Punjab	03/2005	309.00	309.00	549.60	06/2010	03/2011	9(O)	0/0
425	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	285.50	10/2009	03/2011	17(O)	0/0
426	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	294.10	09/2009	03/2011	18(O)	0/0
427	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09	276.09	294.60	09/2009	03/2011	18(O)	0/0
428	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	544.30	07/2010	03/2011	8(O)	0/0
429	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	285.00	332.50	07/2010	03/2011	8(O)	0/0
430	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	674.60	07/2010	03/2011	8(O)	0/0
431	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	121.06	02/2004	03/2011	85(O)	0/0
432	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI, Assam	12/2003	230.00	230.00	299.50	06/2008	04/2011	34(O)	0/0
433	GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	231.50	02/2004	04/2011	86(O)	0/0
434	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	411.40	01/2011	04/2011	3(O)	0/0
435	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00	242.00	338.60	12/2008	05/2011	29(O)	0/0
436	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	610.20	08/2010	05/2011	9(O)	0/0
437	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI, Madhya Pradesh	11/2008	549.00	549.00	697.00	05/2010	05/2011	12(O)	0/0
438	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	453.50	05/2010	05/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
439	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	347.80	03/2005	06/2011	75(O)	0/0
440	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	183.50	09/2007	06/2011	45(O)	0/0
441	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	201.66	71.02	09/2008	06/2011	33(O)	0/0
442	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K	12/2003	193.09	166.30	153.70	03/2008	06/2011	39(O)	0/0
443	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K	12/2003	166.27	193.10	120.90	03/2008	06/2011	39(O)	0/0
444	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00	227.00	295.20	10/2008	06/2011	32(O)	0/0
445	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	328.20	12/2008	06/2011	30(O)	0/0
446	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	332.94	234.90	09/2008	06/2011	33(O)	0/0
447	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	205.60	10/2008	06/2011	32(O)	0/0
448	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91	229.91	150.30	10/2008	06/2011	32(O)	0/0
449	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	579.90	10/2009	06/2011	20(O)	0/0
450	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	395.60	12/2009	06/2011	18(O)	0/0
451	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	260.00	03/2010	06/2011	15(O)	0/0
452	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	518.00	07/2010	06/2011	11(O)	0/0
453	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,764.00	01/2011	06/2011	5(O)	0/0
454	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	172.90	07/2008	08/2011	37(O)	0/0
455	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	195.10	11/2008	08/2011	33(O)	0/0
456	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	1,701.00	08/2011	08/2011	0(O)	0/0
457	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	35.45	04/2004	10/2011	90(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	223.00	06/2008	10/2011	40(O)	0/0
459	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	167.60	10/2011	10/2011	0(O)	0/0
460	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,368.00	10/2011	10/2011	0(O)	0/0
461	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	184.70	10/2011	10/2011	0(O)	0/0
462	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI,Bihar	12/2003	305.00	305.00	481.30	06/2008	11/2011	41(O)	0/0
463	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	141.00	10/2008	11/2011	37(O)	0/0
464	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	1,990.00	11/2011	11/2011	0(O)	0/0
465	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	150.80	06/2005	12/2011	78(O)	0/0
466	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	188.70	02/2009	12/2011	34(O)	0/0
467	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	68.81	04/2009	12/2011	32(O)	0/0
468	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	126.80	06/2008	12/2011	42(O)	0/0
469	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	135.00	06/2008	12/2011	42(O)	0/0
470	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	159.50	10/2008	12/2011	38(O)	0/0
471	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	367.10	09/2008	12/2011	39(O)	0/0
472	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	203.20	06/2008	12/2011	42(O)	0/0
473	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	269.80	03/2008	12/2011	45(O)	0/0
474	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	154.40	06/2008	12/2011	42(O)	0/0
475	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	173.60	04/2008	12/2011	44(O)	0/0
476	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	90.58	05/2008	12/2011	43(O)	0/0
477	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	159.30	06/2008	12/2011	42(O)	0/0
478	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	140.20	09/2010	12/2011	15(O)	0/0
479	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	99.39	04/2008	03/2012	47(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
480	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	148.50	04/2008	03/2012	47(O)	0/0
481	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	77.58	04/2010	03/2012	23(O)	0/0
482	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	178.00	02/2010	03/2012	25(O)	0/0
483	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	926.10	02/2010	05/2012	27(O)	0/0
484	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	372.50	05/2012	05/2012	0(O)	0/0
485	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	491.80	05/2012	05/2012	0(O)	0/0
486	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	135.60	10/2008	06/2012	44(O)	0/0
487	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	216.90	06/2012	06/2012	0(O)	0/0
488	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	246.60	07/2012	07/2012	0(O)	0/0
489	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	63.81	05/2008	08/2012	51(O)	0/0
490	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	359.00	63.81	05/2010	08/2012	27(O)	0/0
491	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	182.30	06/2010	10/2012	28(O)	0/0
492	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	232.40	09/2009	10/2012	37(O)	0/0
493	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
494	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	468.50	09/2012	10/2012	1(O)	0/0
495	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	393.30	10/2012	10/2012	0(O)	0/0
496	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	109.40	09/2007	06/2013	69(O)	0/0
497	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	29.51	04/2009	12/2013	56(O)	0/0
498	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.68	11/2008	12/2013	61(O)	0/0
499	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	155.04	29.09	11/2008	12/2013	61(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
500	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	38.03	09/2007	12/2013	75(O)	0/0
501	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	27.54	07/2009	12/2013	53(O)	0/0
	Total		45,247.77	47,108.09	41,511.41				0/0
	Shipping & Ports								
502	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]PORT TRUST, Karnataka	06/2006	230.00	230.00	219.00	12/2010	12/2010	0(O)	0/0
503	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40	2,427.40	819.64	10/2008	11/2010	25(O)	0/0
504	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00	165.00	108.79	12/2005 01/2008	01/2011	36(R3)	0/0
505	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]PORT TRUST, Kerala	03/2007	245.67 298.17	298.17	299.01	04/2009 11/2009	02/2011	15(R3)	0/0
506	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84 253.36	253.36	223.20	06/2007 07/2009	03/2011	20(R3)	0/0
507	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	359.44	344.58	04/2011	04/2011	0(O)	0/0
508	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST, Maharashtra	04/2009	290.85	290.85	72.59	03/2011	06/2011	3(O)	0/0
509	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP., Maharashtra	08/2008	1,108.12	1,168.42	760.34	04/2011	12/2011	8(O)	0/0
510	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST, Maharashtra	04/2009	277.03	277.03	55.40	09/2011	12/2011	3(O)	0/0
511	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP., Maharashtra	11/2007	1,061.96	1,061.96	219.98	03/2012	03/2012	0(O)	0/0
512	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP., Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	09/2005	03/2012	78(O)	0/0
513	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00	3,500.00	1,687.00	01/2012 01/2012	03/2012	2(R3)	0/0
514	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP., Maharashtra	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
515	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
516	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00	1,460.00	145.19	12/2010	12/2012	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
517	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	612.72	61.31	12/2012	12/2012	0(O)	0/0
518	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.16	02/2011	03/2013	25(O)	0/0
519	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	0.73	03/2011	03/2013	24(O)	0/0
520	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00	272.50	-	01/2009	05/2013	52(O)	0/0
521	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10	1,028.10	-	12/2013	12/2013	0(O)	0/0
522	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	966.46	-	02/2014	02/2014	0(O)	0/0
523	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.04	03/2012	03/2015	36(O)	0/0
524	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.22	10/2008	-	-	0/0
	Total		18,352.60	19,276.36	5,312.09				0/0
	Telecommunications								
525	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	216.14	09/2009	02/2010	5(O)	0/0
526	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	109.31	12/2005	10/2010	58(O)	0/0
527	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
528	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
529	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
530	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	73.73	02/2007 03/2010	12/2010	9(R3)	0/0
531	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86 234.24	353.00	234.24	02/2008	12/2010	34(O)	0/0
532	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
533	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
534	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
535	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
536	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
537	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	127.42	06/2009	01/2011	19(O)	0/0
538	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13	392.44	164.58	03/2009	01/2011	22(O)	0/0
539	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.88	03/2009	02/2011	23(O)	0/0
540	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	176.33	12/2008	02/2011	26(O)	0/0
541	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	308.13	03/2009	02/2011	23(O)	0/0
542	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	88.17	06/2009	02/2011	20(O)	0/0
543	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	02/2011	25(O)	0/0
544	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	02/2011	12(O)	0/0
545	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	219.08	10/2008	02/2011	28(O)	0/0
546	GSM equipment of 1900000Lines (2G) 401700 lines 3(G) - [N26000091]BSNL,Tamil Nadu	01/2009	760.20	810.37	748.30	01/2010 03/2011	02/2011	-1(R3)	0/0
547	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.88	01/2010	02/2011	13(O)	0/0
548	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	441.28	01/2010	02/2011	13(O)	0/0
549	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	110.54	01/2010	02/2011	13(O)	0/0
550	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007 11/2009	03/2011	16(R3)	0/0
551	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	477.44	12/2008	03/2011	27(O)	0/0
552	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	169.43	03/2009	03/2011	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	90.50	09/2009	03/2011	18(O)	0/0
554	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	31.15	10/2009	03/2011	17(O)	0/0
555	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	74.65	09/2010	03/2011	6(O)	0/0
556	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	395.77	02/2009	03/2011	25(O)	0/0
557	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	274.30	08/2009	03/2011	19(O)	0/0
558	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	211.83	11/2010	03/2011	4(O)	0/0
559	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.70	719.70	395.06	10/2009	03/2011	17(O)	0/0
560	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	138.65	10/2010	04/2011	6(O)	0/0
561	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	2.13	09/2011	09/2011	0(O)	0/0
562	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
563	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
564	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	-	-	0/0
Total			19,435.89	19,898.19	7,084.97				0/0
<u>Urban Development</u>									
565	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00 8,605.36	18,894.36	16,847.69	06/2010	12/2010	6(O)	0/8
566	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 3.00	11,609.00	3,523.55	12/2011	03/2013	15(O)	6/6
Total			15,071.00	30,503.36	20,371.24				6/14
<u>Water Resources</u>									
567	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
Total			542.90	1,187.00	35.49				0/0
Grand Total			592,535.30	716,353.74	310,965.82				854/2085


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

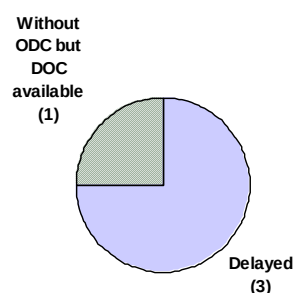

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs. 19086.66 Crores.

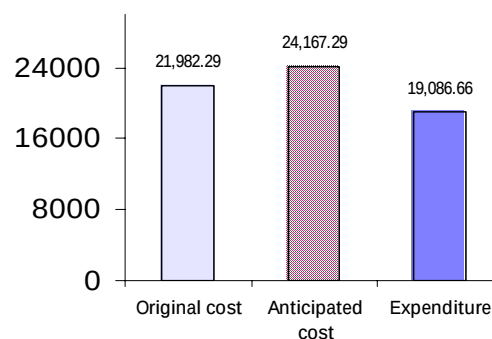


2. Sector: - Civil Aviation

Number of Projects	8
Number of Projects on schedule	4
Number of Projects Delayed	2
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule, 2 projects are delayed and 1 projects are original date of commissioning and 1 projects are Wo_Odc_Original.

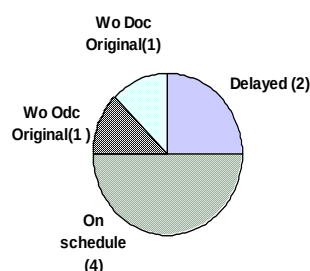

Investment Scenario

The total cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4812.40 Crores but this was subsequently revised to Rs. 4812.40 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs 2527.08 Crores.

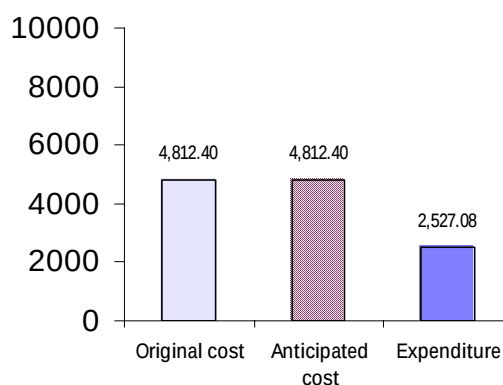


3. Sector: - Coal

Number of Projects	45
Number of Projects on schedule	17
Number of Projects Delayed	19
Number of Projects Ahead	1
Number of Projects Wo_ODC_Original	7
Number of Projects Wo_DOC_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 45 projects, 17 projects are on schedule, 19 projects are delayed and 1 projects are ahead and 7 Project W_Odc_Original and 1 Project W_Odc_Original .

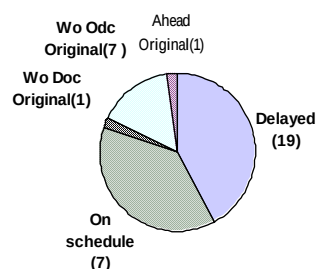

Investment Scenario

The total cost of implementation of 45 projects when sanctioned, was of the order of Rs. 25452.49 Crores but this was subsequently revised to Rs. 28789.58 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs 9817.26 Crores

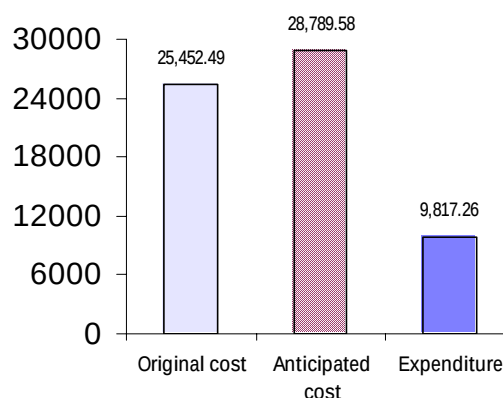


4. Sector: - Petroleum

Number of Projects	67
Number of Projects on schedule	22
Number of Projects Delayed	32
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	2
Number of Projects Without original date of commissioning	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 67 projects, 22 projects are on schedule, 32 projects are delayed and 2 projects are ahead and 2 projects is without date of commissioning and 9 Project is Without original date of commissioning.

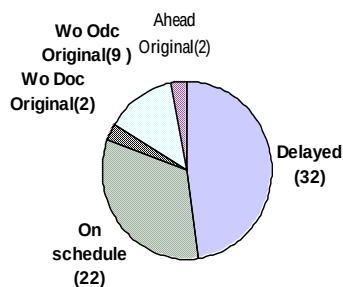

Investment Scenario

The total cost of implementation of 67 projects when sanctioned, was of the order of Rs. 140110.59 Crores but this was subsequently revised to Rs. 153534.21 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs. 46160.39 Crores.

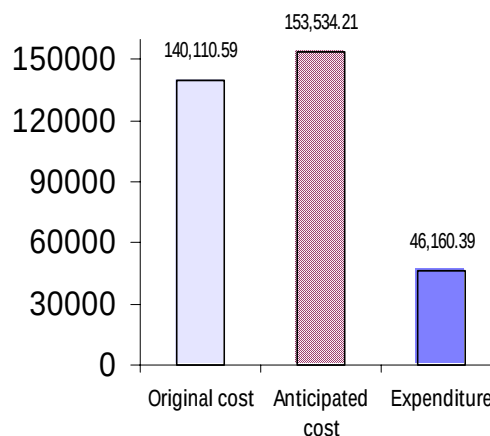


5. Sector: - Power


Number of Projects	83
Number of Projects on schedule	34
Number of Projects Delayed	43
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 83 projects, 34 projects are on schedule, 43 projects are delayed, and 2 Projects are Ahead, 3 projects are without date of commissioning and 1 project is without original date of commissioning

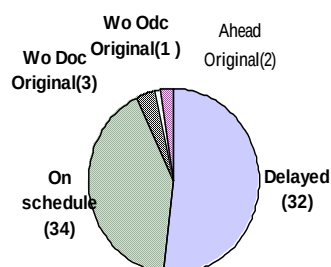

Investment Scenario

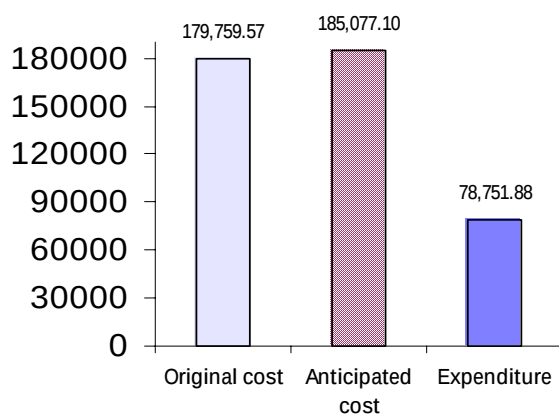


The total cost of implementation of 83 projects when sanctioned, was of the order of Rs. 179759.57 Crores but this was subsequently revised to Rs. 185077.10 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs. 78751.88 Crores.

6. Sector: - Railways

Number of Projects	147
Number of Projects on schedule	24
Number of Projects Delayed	26
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	58
Number of Projects Wo_Odc_Original	37


Brief Analysis

Project Status with out respect Original Schedule: Out of 147 projects, 24 projects are on schedule, 26 projects are delayed, 2 projects is ahead. 58 projects are Without date of commissioning and 37 projects are without original date of commissioning.

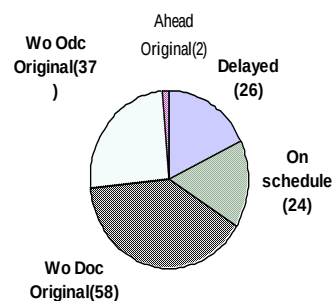

Investment Scenario

The total cost of implementation of 147 projects when sanctioned, was of the order of Rs. 68578.35 Crores but this was subsequently revised to Rs. 126901.43 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs. 49039.13 Crores.

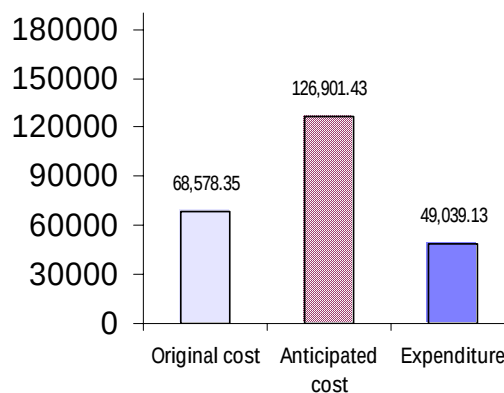


7. Sector: - Road Transport and Highways

Number of Projects	121
Number of Projects on schedule	10
Number of Projects Delayed	111


Brief Analysis

Project Status with respect to Original Schedule: Out of 121 projects, 10 projects are on schedule, 111 projects are delayed.



Investment Scenario

The total cost of implementation of 121 projects when sanctioned, was of the order of Rs 45247.77 Crores but this was subsequently revised to Rs. 47108.09 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs. 41511.41 Crores.

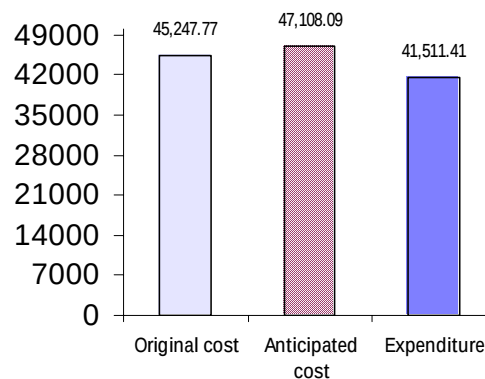


8. Sector: - Shipping and Ports


Number of Projects	23
Number of Projects on schedule	6
Number of Projects Delayed	14
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 23 projects, 6 projects are on schedule, 14 projects are delayed, 1 projects are ahead and 2 projects are without date of commissioning.

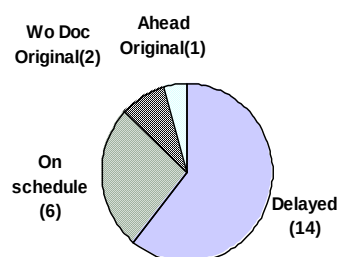

Investment Scenario

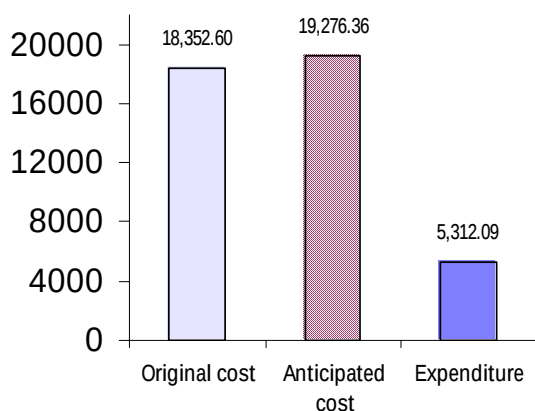


The total cost of implementation of 23 projects when sanctioned, was of the order of Rs.18352.60 Crores but this was subsequently revised to Rs. 19276.36 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs. 5312.09 Crores.

9. Sector: - Steel

Number of Projects	19
Number of Projects On schedule	3
Number of Projects Delayed	9
Number of Projects Wo_Doc_Original	5
Number of Projects Wo_Odc_Original	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 9 projects are delayed and 3 projects are on Schedule and 5 projects are Wo_Doc_Original and 2 Project is Wo_Odc_Original.

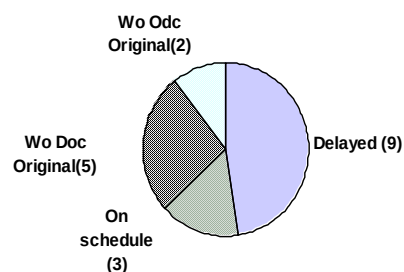

Investment Scenario

The total cost of implementation of 19 projects when sanctioned, was of the order of Rs.43780.53 Crores but this was subsequently revised to Rs. 65379.56 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs. 27101.90 Crores.

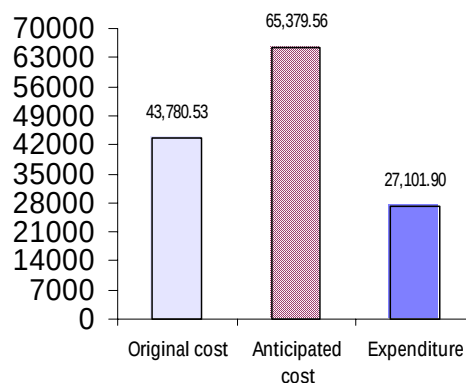


10. Sector: - Telecommunications

Number of Projects	40
Number of Projects Delayed	31
Number of Projects on Schedule	1
Number of Projects Wo_Doc_Original	8


Brief Analysis

Project Status with respect to Original Schedule: Out of 40 projects, 31 projects are delayed and 8 projects are with out date of commissioning, and 1 projects are on schedule.

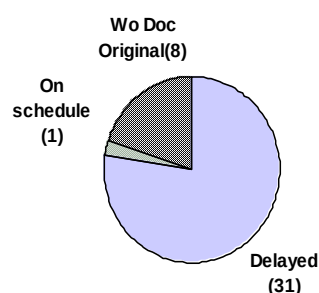

Investment Scenario

The total cost of implementation of 40 projects when sanctioned, was of the order of Rs 19435.89 Crores but this was subsequently revised to Rs. 19898.19 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs 7084.97 Crores.

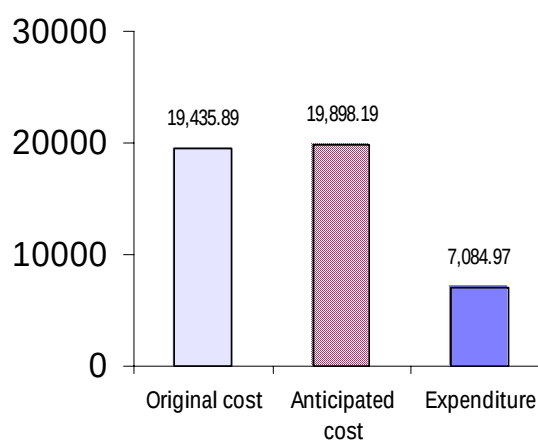


11. Sector: - Fertilisers

Number of Projects	6
Number of Projects Delayed	1
Number of Projects on Schedule	4
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 1 projects are Wo_Odc_Original, and 4 projects are on schedule and 1 project are delay.

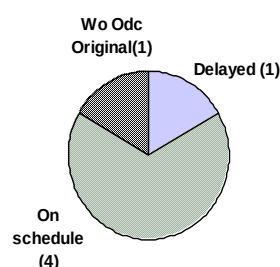

Investment Scenario

The total cost of implementation of 6 projects when sanctioned, was of the order of Rs 5317.41 Crores but this was subsequently revised to Rs. 5317.41 Crores. The expenditure incurred on these projects till Dec, 2010 is Rs 258.03 Crores.

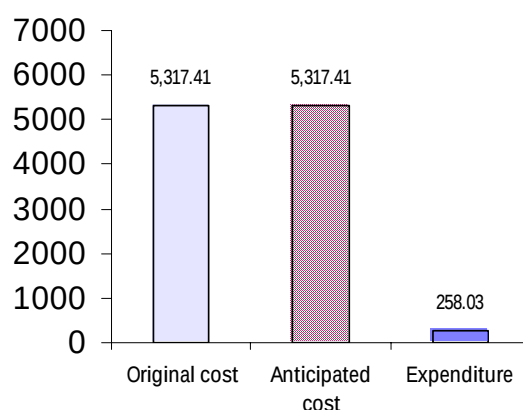

STATE WISE SUMMARY (AS ON 31.12.2010)

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	EXPENDITURE CUMM
1	Andhra Pradesh	35	30248.77	36880.05	16776.82
2	Arunachal Pr.	4	9512.22	9516.70	5891.98
3	Assam	38	22637.64	28829.75	12285.53
4	Bihar	30	28271.01	31304.80	17032.27
5	Chhatisgarh	17	20698.98	36333.97	12379.54
6	Delhi	2	8925.00	19123.77	16913.89
7	Goa	1	204.73	204.73	21.65
8	Gujarat	24	16555.73	19004.73	10749.13
9	Haryana	10	4821.32	6379.33	3570.88
10	Himachal Pr.	8	15381.72	15463.96	10632.88
11	J & K	8	8297.84	18455.56	10063.26
12	Jharkhandd	22	9929.62	14866.24	5582.45
13	Karnataka	18	15527.06	23146.38	11069.21
14	Kerala	11	9511.93	10939.72	7844.83
15	Madhya pradesh	26	20323.50	20501.63	7930.53
16	Maharashtra	51	66359.98	86599.99	28190.89
17	Manipur	1	578.62	578.62	28.33
18	Mizoram	2	988.06	3343.04	219.77
19	Multi State	95	112956.43	116930.00	34344.80
20	Nagaland	1	850.00	850.00	5.46
21	Orissa	26	49676.83	53643.33	14257.99
22	Punjab	9	5064.09	6028.72	2130.02
23	Rajasthan	14	11692.97	12782.09	7338.30
24	Sikkim	2	1603.77	3644.86	138.54
25	Tamil Nadu	34	42590.66	48576.77	34238.35
26	Tripura	3	1522.39	2053.24	187.40
27	Uttar Pradesh	38	23743.51	25662.26	16294.65
28	Uttaranchal	9	12100.46	14517.85	4300.99
29	West Bengal	28	41960.46	50191.65	20545.48
TOTAL		567	592535.30	716353.74	310965.82

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministrial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
