


**338th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
December 2013**



THDCL-TEHRI PUMPED STORAGE PLANT

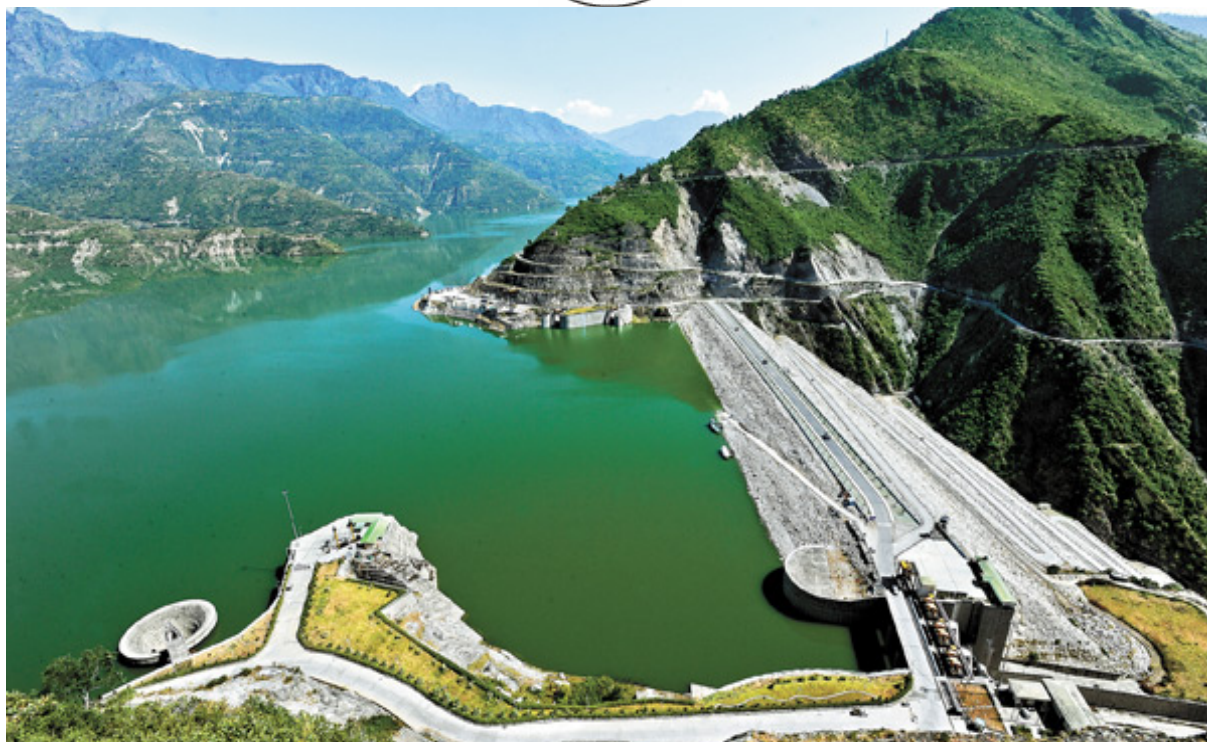

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-70
Sector wise Graph	71-81
ANNEXURE	82-82
Central Sector Projects	83-83
List of Projects Having Expenditure More than cost	84-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-106
List of On schedule Projects Original Schedule	107-113
List of Delayed Projects w.r.t Original Schedule	114-127
List of Projects Having Time and cost overrun w.r.t original	128-132
List of Projects Having cost overrun w.r.t original	133-144
List of Projects without Milestones	145-166
List of On schedule Projects w.r.t. Latest Schedule	167-174
List of Projects Ahead of Schedule w.r.t Latest Schedule	175-175
List of Delayed Projects w.r.t Latest Schedule	176-189

कार्यकारी सारांश

दिसंबर, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 741 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। दिसंबर, 2013 के दौरान 5 परियोजनाओं (4 परियोजनाएं पेट्रोलियम में तथा 1 परियोजना रेलवे क्षेत्र में) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 741 परियोजनाओं में से 198 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 40 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 40 परियोजनाओं में से, 16 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। नागर विमानन, इस्पात, सड़क, पोत परिवहन तथा पत्तन, विद्युत, रेलवे तथा पेट्रोलियम क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 12 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	285	36	2	0
2.	सड़क परिवहन एवं राजमार्ग	152	11	6	0
3.	विद्युत	100	50	9	6
4.	पेट्रोलियम	82	52	12	5
5.	कोयला	55	27	0	0
6.	इस्पात	20	10	9	5
7.	पोत परिवहन एवं पत्तन	19	1	1	0
8.	दूरसंचार	10	4	0	0
9.	नागर विमानन	8	2	1	0
10.	परमाणु ऊर्जा	4	4	0	0
11.	शहरी विकास	4	1	0	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		741	198	40	16

3. 741 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ₹9,12,557.61 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹10,92,632.33 करोड़ रुपए होने की संभावना है जो ₹1,80,074.72 करोड़ (मूल लागत का 19.70%) की समग्र लागत वृद्धि को दर्शाता है। दिसंबर, 2013 तक इन परियोजनाओं पर किया गया व्यय ₹5,16,627.39 करोड़ है जो परियोजनाओं की अनुमानित लागत का 47.30% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.12.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (31.12.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
3	सुबानश्री लोअर एचईपी (एनएचपीसी)	विद्युत	09/2003	6285.33	10667.00	4381.67
4	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00
5	बोगीबिल एंड लिंक लाईन पर ब्रह्मपुत्र पुल एनईएफआर	रेलवे	09/1997	1000.00	4996.65	3996.65

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 741 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 162 समय पर तथा 198 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 223 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 24 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 352 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 198 विलंबित परियोजनाओं में से, 45 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 52 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 62 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 39 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.12.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
2	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	09/2013	138

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, कार्य-क्षेत्र में बदलाव, माओवादी गतिविधियां, संविदा संबंधी मुद्दों, कार्यों को प्रदान करने में विलंब, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी

परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.12.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		संचयी व्यय (रु. करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.12.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.12.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012

	(एससीआर)					
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

i) **पोत परिवहन तथा पत्तन क्षेत्र** में, 19 परियोजनाओं में से 1 परियोजना विलंबित है । परियोजना 'एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्स व्हीकल (एसपीवी), चेन्नई पोर्ट ट्रस्ट' में भूमि अधिग्रहण में विलंब के कारण 6 माह के अतिरिक्त विलंब की सूचना दी गई है ।

ii) **नागर विमानन क्षेत्र** में, 8 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं । परियोजना '10 विमानपत्तनों पर एयरपोर्ट ऑपरेशंस नियंत्रण केन्द्रों की स्थापना, एएआई' में उपकरणों की आपूर्ति में विलंब के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

iii) **रेलवे क्षेत्र** में, 285 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं। माह के दौरान 2 परियोजनाओं के संबंध में क्रमशः 1 तथा 3 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'लांझीगढ़-जूनागढ़, नई लाइन, ईसीओआर' परियोजना के संबंध में निधि की कमियों के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा परियोजना 'हरमाटी-ईटानगर/नरहरियागन से नई लाइन का निर्माण, एनईएफआर' में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इस परियोजना में विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी विशेष कारणों की सूचना नहीं दी गई है) ।

iv) **सड़क क्षेत्र** में, 152 परियोजनाओं में से 11 परियोजनाएं विलंबित हैं । माह के दौरान 6 परियोजनाओं के संबंध में 1-9 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'नालबारी से बिजनी (एएस-6), एनएचआई' तथा 'धरमतुल से सोनपुर, 205-183 कि.मी. (एएस-20), एनएचएआई' में क्रमशः 1 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'नालबारी से बिजनी (एएस-7) एनएचएआई' तथा 'ब्रह्मपुत्र ब्रिज, एनएच सं.-31, एनएचआई' में क्रमशः 6 तथा 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'सोनपुर से गुवाहाटी (एएस-3)' एनएचएआई तथा 'गुवाहाटी से नालबारी (एएस-5), एनएचएआई' में प्रत्येक में 9 माह के अतिरिक्त

विलंब की सूचना प्राप्त हुई है (तथापि, इस परियोजना में विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी विशेष कारणों की सूचना नहीं दी गई है) ।

(V) इस्पात क्षेत्र में, 20 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं । माह के दौरान 9 परियोजनाओं के संबंध में 3-10 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है । जिनमें से 5 मेगा परियोजनाएं हैं । परियोजना 'बेलाडिला आइरन ओर परियोजना डिपोजिट-11बी, एनडीएमसी' में माओवादी गतिविधियों के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 7.0 एमटीपीए कुमारस्वामी लौह अयस्क खान परियोजना एनएमडीसी' में फिर से निविदा जारी करने संबंधी गतिविधियों के कारण 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ; परियोजनाएं 'कोक ओवन बैटरी सं. 4 फेज-II, आरआईएनएल' तथा 'बोकारों स्टील प्लांट का विस्तार, सेल' में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'इसको स्टील प्लांट का विस्तार, सेल', 'भिलाई स्टील प्लांट का विस्तार, सेल' तथा '1.2 एमटीपीए पीलेट संयंत्र परियोजना डोनीमलाई, एनडीएमसी' में प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'राउरकेल स्टील प्लांट का विस्तार, सेल' तथा 'दुर्गापुर स्टील प्लांट का विस्तार, सेल' में प्रत्येक में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; (तथापि, इस परियोजना में विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी विशेष कारणों की सूचना नहीं दी गई है) ।

(vi) विद्युत क्षेत्र में, 100 परियोजनाओं में से 50 परियोजनाएं विलंबित हैं । माह के दौरान 9 परियोजनाओं के संबंध में 1-10 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 6 परियोजनाएं मेगा परियोजनाएं हैं । परियोजना 'यूआरआई एच.ई.पी. स्टेज-II, एनएचपीसी' में आकस्मिक बाढ़ की घटना के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पूर्वी क्षेत्रों को सुदृढ़ करने की योजना-I, पीजीसीआईएल' में उपकरणों की आपूर्ति में हुए विलंब के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'उत्तरी क्षेत्रों की व्यवस्था को सुदृढ़ करने की योजना-X/ पीजीसीआईएल' तथा 'झारखंड तथा पश्चिम बंगाल भाग-बी में चरण-I की परियोजना हेतु पारेषण प्रणाली, पीजीसीआईएल' में भूमि अधिग्रहण में विलंब के कारण क्रमशः 3 तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'एसआर ग्रिड के XII व्यवस्था को सुदृढ़ करना, पीजीसीआईएल' में आरओडब्ल्यू समस्याओं के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'छत्तीसगढ़ में आईपीपीएस जेनेरेशन परियोजनाओं हेतु डब्ल्यूआर के पश्चिमी भाग के पारेषण प्रणाली को सुदृढ़ करना, पीजीसीआईएल,' 'मुंदरा अल्ट्रा मेगा पावर, परियोजना से जुड़े हुए पारेषण प्रणाली, पीजीसीआईएल' तथा 'ओडिसा भाग-सी में चरण-I जेनेरेशन परियोजना हेतु पारेषण प्रणाली, पीजीसीआईएल' में वन विभाग से मंजूरी मिलने में हुए विलंब के कारण क्रमशः 5, 9 तथा 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'छत्तीसगढ़ में आईपीपी परियोजनाओं हेतु

डब्ल्यूआ-एनआर एचवीडीसी इंटरकनेक्टर, पीजीसीआईएल' में तार कसने के लिए कॉरिडोर की अन-उपलब्धता के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(vi) **पेट्रोलियम क्षेत्र** में, 82 परियोजनाओं में से 52 परियोजनाएं विलंबित हैं । माह के दौरान 12 परियोजनाओं के संबंध में 1-12 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 5 परियोजनाएं बड़ी परियोजनाएं हैं । परियोजना 'हाइड्रोक्रैकर रिवैम्प तथा मुम्बई रिफाइनरी में नए सीसीआर की स्थापना करना, बीपीसीएल' तथा 'विजयपुर तथा पाटा में पेट्रोकेमिकल कॉम्प्लेक्स-II, गेल' में क्रमशः खराब सामग्रियों के अस्वीकृत होने तथा खराब मौसम की स्थिति के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'आईओआर, रुद्रसागर, ओएनजीसीएल' तथा 'मुंबई हाई में ऑफशोर ग्रिड इंटरकनेक्टिविटी परियोजना, ओएनजीसी' में क्रमशः कार्य के क्षेत्र में परिवर्तन तथा कार्य शुरू करने में हुए विलंब के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'कोनबन जीजीएस का उन्नयन तथा त्रिपुरा में पाइपलाइन ग्रिड परियोजना, ओएनजीसी' तथा 'बीएचई तथा बीएच-35 क्षेत्र का विकास, ओएनजीसी' में क्रमशः आरओयू समस्याओं तथा वेल प्लेटफॉर्म व पाइपलाइन के संस्थापन में हुए विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'मुंबई रिफाइनरी में डीजल हाइड्रोड्रेटर परियोजना, एचपीसीएल' तथा '2000 एचपी ड्रिलिंग आरआईजी के 2 सं. की खरीद, ऑयल' में क्रमशः उपकरणों की आपूर्ति में विलंब तथा कानूनी समस्याओं के कारण प्रत्येक में 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'यूरान चकन/शिकरापुर एलपीजी पाइपलाइन, एचपीसीएल' में वन संबंधी मंजूरी मिलने में हुए विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'एमआरपीएल फेज-III विस्तार, मंगलौर रिफाइनरी' तथा 'पारादीप हलदिया बरौनी पाइपलाइन का संवर्धन, आईओसीएल' में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'सी-26 कलस्टर क्षेत्रों का विकास, ओएनजीसी' में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इस परियोजना में विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी विशेष कारणों की सूचना नहीं दी गई है) ।

10. दिनांक 31.12.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपए तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।

11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for December 2013 contains information on the status of the 741 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During December 2013, 5 projects (4 projects in Petroleum and 1 project in Railway Sector) have reported completion.

2. During the reference month, out of 741 projects, 198 projects are delayed with respect to latest schedule and 40 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 40 projects, 16 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 12 months in respect of projects relating to Civil Aviation, Steel, Road, Shipping & Ports, Power, Railways and Petroleum Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	285	36	2	0
2.	ROAD TRANSPORT AND HIGHWAYS	152	11	6	0
3.	POWER	100	50	9	6
4.	PETROLEUM	82	52	12	5
5.	COAL	55	27	0	0
6.	STEEL	20	10	9	5
7.	SHIPPING AND PORTS	19	1	1	0
8.	TELECOMMUNICATIONS	10	4	0	0
9.	CIVIL AVIATION	8	2	1	0
10.	ATOMIC ENERGY	4	4	0	0
11.	URBAN DEVELOPMENT	4	1	0	0
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		741	198	40	16

3. Total original cost of implementation of the 741 projects was about ₹ 9,12,557.61 crore and their anticipated completion cost is likely to be ₹ 10,92,632.33 crore, which reflects overall cost overruns of ₹ 1,80,074.72 crore (19.70 % of original cost). The expenditure incurred on these projects till December 2013 is ₹ 5,16,627.39 crore, which is 47.30 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-12 -2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-12-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	11609.00	5214.00
3	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
4	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00
5	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	4996.65	3996.65

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 741 projects, 5 projects are ahead of schedule, 162 are on schedule and 198 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 223 if delay is calculated on the basis of original schedule of completion. Further, 24 projects have been sanctioned without any commissioning schedule/date and for 352 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 198 delayed projects, 45 projects have overall delay in the range of 1 to 12 months, 52 projects have a delay in the range of 13 to 24 months, 62 projects have a delay in the range of 25 to 60 months and 39 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-12-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2015	240
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	141
5	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	09/2013	138

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipment, fund constraints, geological surprises, change in scope of work, maoist activities, contractual issue, delay in award of works, ROU/ROW problems, law and order situation, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-12-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-12-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.12.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. The Sector-wise details of delays/additional delays are as under:-

- i) In the **Shipping & Ports Sector**, out of 19 projects, 1 project is delayed. The project 'Ennore Manali Express Way, F/O Special Purpose Vehicle (SPV), Chennai Port Trust' has reported additional delay of 6 months due to delay in land acquisition.

ii) In the **Civil Aviation Sector**, out of 8 projects, 2 projects are delayed. The project 'Establishment of Airport Operations Control Centres at 10 Airports, AAI' has reported additional delay of 4 months due to delay in supply of equipments.

iii) In the **Railways Sector**, out of 285 projects, 36 projects are delayed. During the month 2 projects have reported additional delays of 1 and 3 months respectively. The project 'Lanjhigarh-Junagarh, New Line, ECOR' has reported additional delay of 1 month due to fund constraints; and the project 'Construction of New Line from Harmati-Itanagar/Narhariagun, NEFR' has reported additional delay of 3 months (however, no specific reasons have been reported by the project authority for the delay in this project).

iv) In the **Road Sector**, out of 152 projects, 11 projects are delayed. During the month 6 projects have reported additional delays in the range of 1-9 months. The projects 'Nalbari to Bijni (AS-6), NHAI' and 'Dharamtul to Sonapur, KM 205-183 (AS-20), NHAI' have reported additional delays of 1 and 3 months respectively; the projects 'Nalbari to Bijni (AS-7), NHAI' and 'Brahmputra Bridge, NH NO-31, NHAI' have reported additional delays of 6 and 8 months respectively; and the projects 'Sonapur to Guwahati (AS-3), NHAI' and 'Guwahati to Nalbari (AS-5), NHAI' have reported additional delays of 9 months each (however, no specific reasons have been reported by the project authority for the delay in these projects).

v) In the **Steel Sector**, out of 20 projects, 10 projects are delayed. During the month 9 projects have reported additional delays in the range of 3-10 months, out of which 5 are Mega projects. The project 'Bailadila Iron ORE Project Deposit- 11B, NMDC' has reported additional delay of 6 months due to Maoist activities; the project '7.0 MTPA Kumaraswamy Iron ORE Mine Project, NMDC' has reported additional delay of 10 months due to re-tendering activities; the projects 'Coke Oven Battery No. 4 Phase-II, RINL' and 'Expansion of Bokaro Steel Plant, SAIL' have reported additional delays of 3 months each; the projects 'Expansion of IISCO Steel Plant, SAIL' , 'Expansion of Bhilai Steel Plant, SAIL' and '1.2 MTPA Pellet Plant Project Donimalai, NMDC' have reported additional delays of 6 months each; and the projects 'Expansion of Rourkela Steel Plant, SAIL' and 'Expansion of Durgapur Steel Plant, SAIL' have reported additional delays of 9 months each (however, no specific reasons have been reported by the project authorities for the delay in these projects).

vi) In the **Power Sector**, out of 100 projects, 50 projects are delayed. During the month 9 projects have reported additional delays in the range of 1-10 months, out of which 6 are Mega projects. The project 'URI H.E.P Stage-II, NHPC' has reported additional delay of 1 month due to occurrence of flash flood; the project 'Eastern Region Strengthening Scheme-I, PGCIL' has reported additional delay of 2 months due to delay in supply of equipments; the projects 'Northern Region System Strengthening Scheme-XV, PGCIL' and 'Transmission System for Phase-I Project in Jharkhand and West Bengal PART-B, PGCIL' have reported additional delays of 3 and 9 months respectively due to delay in land acquisition; the project 'System Strengthening XIII of SR Grid, PGCIL' has reported additional delay of 3 months due to ROW problems; the projects 'Transmission System Strengthening in Western Part of WR for IPPS Generation Projects in Chhattisgarh, PGCIL', 'Transmission System Associated with Mundra Ultra Mega Power Project, PGCIL' and 'Transmission System for Phase-I Generation Project in Orissa Part-C, PGCIL' have reported additional delays of 5, 9 and 10 months respectively due to delay in forest clearance; and the project 'WR-NR HVDC Interconnector for IPP Projects in Chhattisgarh, PGCIL' has reported additional delay of 6 months due to non-availability of stringing corridor.

vii) In the **Petroleum Sector**, out of 82 projects, 52 projects are delayed. During the month 12 projects have reported additional delays in the range of 1-12 months., out of which 5 are Mega projects. The projects 'Hydrocracker Revamp and Setting up a New CCR at Mumbai Refinery, BPCL' and 'Petrochemical Complex-II at Vijaypur and Pata, GAIL' have reported additional delays of 1 month each due to rejection of faulty materials and bad weather condition respectively; the projects 'IOR, Rudrasagar, ONGCL' and 'Offshore Grid Interconnectivity Project in Mumbai High, ONGC' have reported additional delays of 2 months each due to change in scope of work and delay in commissioning work respectively; the project 'Up-Gradation of Konaban GGS and Pipeline Grid Project at Tripura, ONGC' and 'Development of BHE and BH-35 area, ONGC' have reported additional delays of 3 months each due to ROU problems and delay in installation well platform & pipeline respectively; the projects 'Diesel Hydrotreater Project at Mumbai Refinery, HPCL' and 'Purchase of 2 Nos. of 2000 HP Drilling RIG, OIL' have reported additional delays of 8 months each due to delay in supply of equipments and legal issues respectively; the project 'Uran Chakan/Shikrapur LPG Pipeline, HPCL' has reported additional delay of 12 months due to delay in forest clearance; the projects 'MRPL Phase-III Expansion, Mangalore refinery' and

‘Augmentation of Paradip Haldia Barauni Pipeline, IOCL’ have reported additional delays of 1 months each; and the projects ‘Development of C-26 Cluster Fields, ONGC’ has reported additional delay of 12 months (however, no specific reasons have been reported by the project authorities for the delay in these projects).


10. The status as on 31.12.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	285	2
2	ROAD TRANSPORT AND HIGHWAYS	152	6
3	POWER	100	9
4	PETROLEUM	82	12
5	COAL	55	0
6	STEEL	20	9
7	SHIPPING AND PORTS	19	1
8	TELECOMMUNICATIONS	10	0
9	CIVIL AVIATION	8	1
10	ATOMIC ENERGY	4	0
11	URBAN DEVELOPMENT	4	0
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	741	40

Sectoral break up of on-going infrastructure projects.

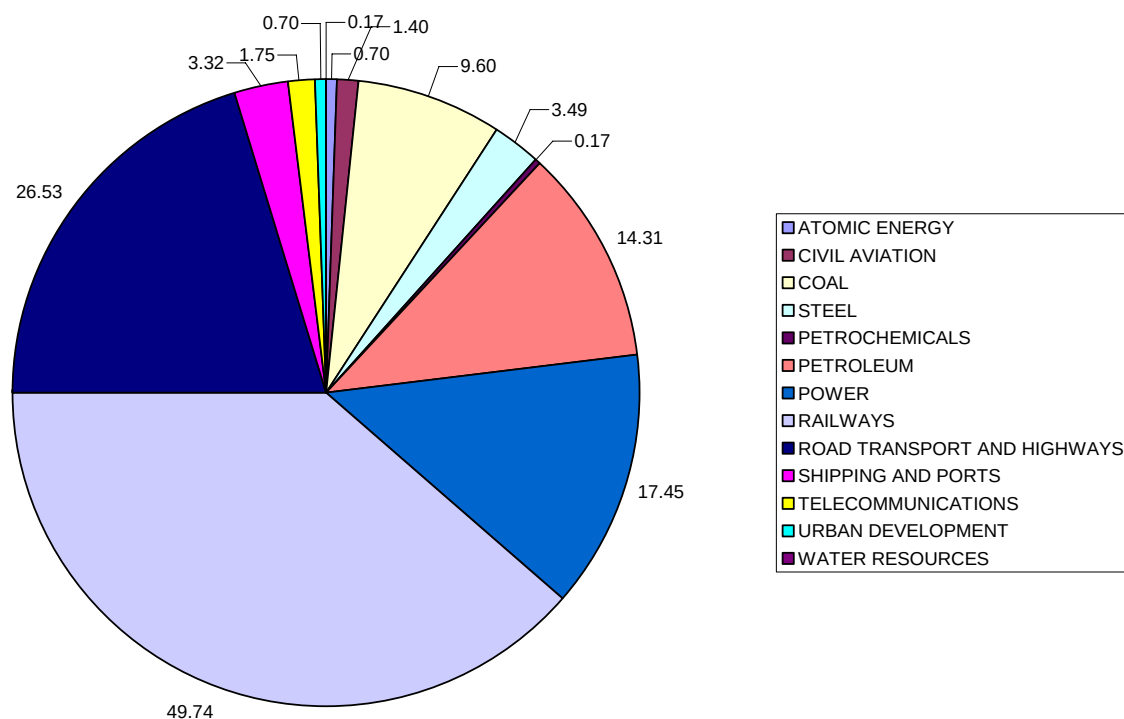

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>POWER</u>			
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>RAILWAYS</u>			
2	RENIGUNTA-GUNTAKAL(RE) (RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL) (RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>FERTILISERS</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT (NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>POWER</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-II (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56
	June,2013			
	<u>RAILWAYS</u>			
8	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000027]	240.00	03/2009	334.59
9	PANSPURA-KHARAGPUR 3D LINE (RAIL VIKAS NIGAM LTD.) - [N22000076]	252.50	02/2010	249.36
	July,2013			
	<u>PETROLEUM</u>			
10	NORTH TAPTI GAS FIELD DEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000096]	589.70	03/2011	912.53

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2013-2014

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100222]	768.92	03/2007	1467.53
12	CHUTAK HYDRO-ELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000007]	621.26	02/2011	731.93
	August,2013			
13	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND BANGLADESH -INDIAN PORTION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000089]	160.32	10/2012	87.63
	<u>RAILWAYS</u>			
14	MADURAI-RAMESWARAM-GC (SOUTHERN RAILWAY) - [N22000200]	240.00	-	367.21
15	KRISHNANAGAR-BETHUA DAHRI DOUBLING (EASTERN RAILWAYS) - [N22000226]	151.65	03/2015	90.21
16	DHARMAVARAM-PAKALA GC (SAUTH COST RAILWAY) - [N22000284]	294.99	-	658.53
	September,2013			
	<u>PETROLEUM</u>			
17	BUTADIENE EXTRACTION UNIT(BDEU) AT PANIPAT (INDIAN OIL CORPORATION LIMITED) - [N16000108]	341.50	02/2013	198.81
	<u>POWER</u>			
18	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000046]	7,031.88	12/2012	4591.9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
19	GWALIOR BYPASS, NH-75,3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000088]	300.93	10/2009	302.7
	October,2013			
	<u>POWER</u>			
20	NIMOO BAZGO HYDROELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000006]	611.01	08/2010	883.85
21	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000018]	557.24	01/2010	648.43
	<u>RAILWAYS</u>			
22	CHANDIGARH-LUDHIANA(NEW BG LINE),NR (NORTHERN RAILWAY) - [220100241]	248.44	12/2012	972.91
23	RUPSA-BANGRIPOSI (GC)(SER) (SOUTH EASTERN RAILWAY) - [220100323]	57.94	03/1998	176.14

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2013-2014

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>TELECOMMUNICATIONS</u>			
24	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06 (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000029]	231.38	10/2007	86.11
	November,2013			
	<u>RAILWAYS</u>			
25	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) (SOUTH WESTERN RAILWAY) - [220100190]	157.00	03/2012	330.38
	December,2013			
	<u>PETROLEUM</u>			
26	RESITMENT OF MARKETING INSTALATION AT VISAKH (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000057]	756.00	-	913.72
27	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000066]	224.00	-	312.61
28	FLUIDIZED CATALYTIC CRACKING UNIT(FCCU) REVAMP AT MATHURA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000107]	1,000.00	01/2013	755.25
29	CAPACITY AUGMENTATION OF KOTA PIYALA SECTION OF MMBPL PIPELINE (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000153]	152.89	06/2013	128.53
	<u>RAILWAYS</u>			
30	KOLAR-CHICKBALAPUR GC (SOUTH WESTERN RAILWAY) - [N22000275]	287.99	01/1999	434.57


Summary of projects in the Flash Report for the month of December, 2013

Project Implementation - Current Status:

Number of Projects in Previous Month	739
Number of Projects completed/dropped/frozen in Current Month	5
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	6
Number of Projects in Current Month	741

Brief Analysis


Project Status with respect to Original Schedule: Out of 741 projects, 4 projects are ahead of schedule, 138 projects are on schedule and 223 projects are delayed. Of the balance, 352 projects do not have fixed dates of commissioning while 24 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

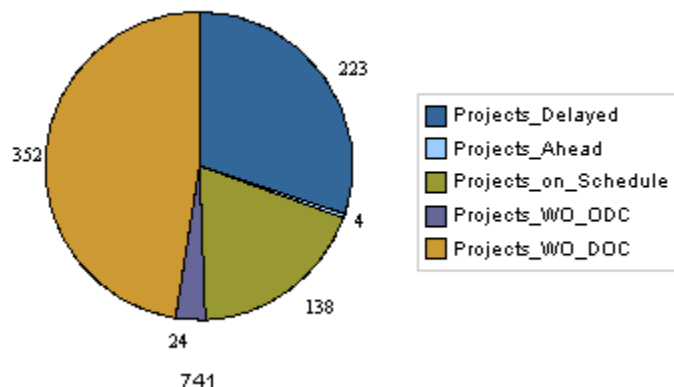

Investment Scenario

The Total Original cost of implementation of 741 projects when sanctioned, was of the order of Rs. 912557.61 crore but this was subsequently revised to Rs. 1092632.33 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till December, 2013 is Rs. 516627.39 crore, which is 47.3% of the revised cost of the projects.

Figures are in Rs. Crore

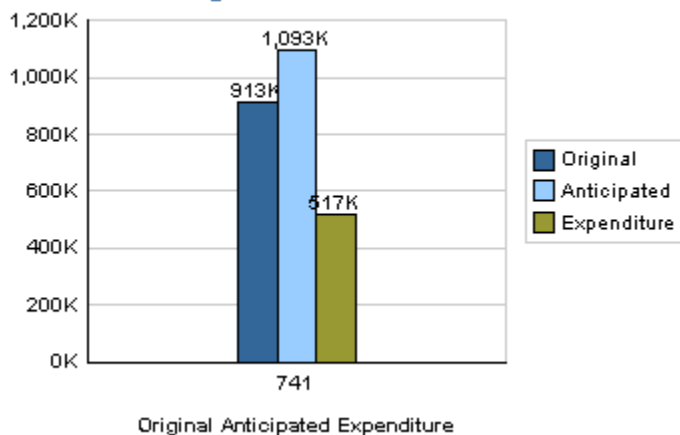

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	739
No of Projects Completed/Dropped/Frozen in current Month	5
No of Projects elevated to status of Major Project during the current months	1
No of Projects added in current Month	6
No of projects in current Month	741

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	223	4	138	24	352	741	30.09
Latest Approved (Date)	198	5	162	24	352	741	26.72

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	580	7,87,169.28	8,41,464.79	3,73,026.36	44.30	54,295.51	6.90
Latest Approved (RCE)	161	1,91,155.18	2,51,167.54	1,43,601.03	57.20	60,012.36	31.40
Total (RCE)	741	9,78,324.46	10,92,632.33	5,16,627.39	47.28	114307.87	11.68
Original Cost of All Projects							
Original Cost	741	9,12,557.61	10,92,632.33	5,16,627.39	47.30	1,80,074.72	19.70

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	223	452,841.33	557,881.66	330,439.51	59.20	105,040.33	23.20
Latest Approved (RCE)	198	463,297.28	529,960.67	315,366.57	59.50	66,663.39	14.40

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	40	112,536.84	116,167.37	82,910.70	71.40	3,630.53	3.20

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	4,086.1	4,996.7	22.3
3	COAL	55	38,127.1	41,525.2	8.9	7	8,579.5	12,575.3	46.6
4	STEEL	20	65,959.3	72,162.3	9.4	7	24,238.0	30,471.0	25.7
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	82	183,103.4	197,993.7	8.1	24	58,765.5	79,786.2	35.8
7	POWER	100	249,166.4	267,559.8	7.4	18	51,573.9	69,967.3	35.7
8	RAILWAYS	285	149,113.5	265,521.6	78.1	150	64,474.5	180,976.7	180.7
9	ROAD TRANSPORT AND HIGHWAYS	152	106,312.4	108,365.2	1.9	15	4,189.5	6,421.7	53.3
10	SHIPPING AND PORTS	19	15,617.1	17,871.5	14.4	9	8,629.0	11,187.6	29.7
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	4	47,598.2	52,871.1	11.1	2	6,509.2	11,782.1	81.0
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		741	912,557.6	1,092,632.3	19.7	242	255,105.6	442,700.0	73.5

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	46	36,933.8	45,110.4	22.1	14	12,772.4	21,816.0	70.8
2	ARUNACHAL PRADESH	4	9,512.2	17,331.9	82.2	4	9,512.2	17,331.9	82.2
3	ASSAM	41	24,155.5	39,221.8	62.4	21	12,677.8	27,830.4	119.5
4	BIHAR	46	32,579.0	41,000.0	25.8	17	13,347.2	21,784.5	63.2
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	15.8
6	GUJARAT	33	38,022.7	39,924.3	5.0	8	3,415.2	5,628.7	64.8
7	HARYANA	9	4,399.9	6,104.1	38.7	2	1,298.8	3,028.0	133.1
8	HIMACHAL PRADESH	5	13,845.2	19,510.6	40.9	4	11,798.2	17,463.6	48.0
9	JAMMU AND KASHMIR	8	13,694.7	32,976.6	140.8	4	6,634.2	25,916.1	290.6
10	KARNATAKA	36	53,708.6	65,661.8	22.3	14	11,651.4	24,097.7	106.8
11	KERALA	11	22,003.6	24,528.4	11.5	5	5,480.4	8,005.2	46.1
12	MADHYA PRADESH	21	31,448.2	32,674.6	3.9	5	3,317.9	4,963.7	49.6
13	MAHARASHTRA	56	97,971.1	111,407.9	13.7	19	33,512.3	49,352.8	47.3
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	724.1
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	MIZORAM	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	187.8
18	ODISHA	32	56,606.0	63,334.6	11.9	13	33,000.6	39,729.2	20.4
19	PUNJAB	6	2,360.2	2,435.2	3.2	1	284.0	359.0	26.4
20	RAJASTHAN	25	25,380.5	25,805.9	1.7	6	2,489.1	3,400.6	36.6
21	SIKKIM	2	1,648.9	3,684.9	123.5	1	1,339.5	3,375.4	152.0
22	TAMIL NADU	41	53,479.7	69,711.4	30.4	20	30,997.2	47,228.9	52.4
23	TRIPURA	6	2,966.3	4,409.2	48.6	3	2,129.4	3,606.7	69.4
24	UTTAR PRADESH	30	21,932.9	26,529.1	21.0	11	4,111.1	8,755.6	113.0
25	WEST BENGAL	36	49,851.1	61,412.4	23.2	15	22,672.9	34,234.2	51.0
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	DELHI	4	41,543.9	41,541.3	-0.0	0	0.0	0.0	0.0
28	CHHATISGARH	24	58,278.3	59,362.9	1.9	5	1,396.8	2,481.4	77.6
29	JHARKHAND	27	16,118.8	20,384.1	26.5	8	2,534.9	6,971.9	175.0
30	UTTARAKHAND	6	7,844.0	9,876.6	25.9	4	5,839.0	7,871.6	34.8
31	MULTI STATE	176	183,255.3	206,983.1	12.9	34	20,360.6	46,242.5	127.1
Total		741	912,557.6	1,092,632.3	19.7	242	255,105.6	442,700.0	73.5

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 66
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	2	653.7	653.7	7 - 50
3	COAL	55	38,127.1	41,525.2	8.9	27	24,452.6	28,222.1	12 - 72
4	STEEL	20	65,959.3	72,162.3	9.4	13	64,208.3	70,162.3	10 - 66
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
6	PETROLEUM	82	183,103.4	197,993.7	8.1	56	144,241.7	160,147.1	1 - 120
7	POWER	100	249,166.4	267,559.8	7.4	51	132,188.7	149,240.0	1 - 106
8	RAILWAYS	285	149,113.5	265,521.6	78.1	37	26,362.7	77,658.7	3 - 240
9	ROAD TRANSPORT AND HIGHWAYS	152	106,312.4	108,365.2	1.9	24	8,428.9	9,272.8	2 - 82
10	SHIPPING AND PORTS	19	15,617.1	17,871.5	14.4	3	1,889.9	2,541.0	5 - 99
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	31 - 59
12	URBAN DEVELOPMENT	4	47,598.2	52,871.1	11.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		741	912,557.6	1,092,632.3	19.7	223	452,841.3	557,881.7	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	46	36,933.8	45,110.4	22.1	7	14,367.7	18,774.3	19 - 66
2	ARUNACHAL PRADESH	4	9,512.2	17,331.9	82.2	3	9,356.2	16,923.9	13 - 93
3	ASSAM	41	24,155.5	39,221.8	62.4	33	21,991.6	36,065.5	3 - 120
4	BIHAR	46	32,579.0	41,000.0	25.8	5	17,679.5	22,340.7	13 - 98
5	GOA	1	335.6	388.5	15.8	0	0.0	0.0	-
6	GUJARAT	33	38,022.7	39,924.3	5.0	6	19,949.3	19,888.0	11 - 24
7	HARYANA	9	4,399.9	6,104.1	38.7	3	1,417.1	1,417.1	2 - 50
8	HIMACHAL PRADESH	5	13,845.2	19,510.6	40.9	3	10,751.3	14,496.6	41 - 106
9	JAMMU AND KASHMIR	8	13,694.7	32,976.6	140.8	3	6,468.0	25,723.0	10 - 181
10	KARNATAKA	36	53,708.6	65,661.8	22.3	8	18,302.9	18,460.4	10 - 48
11	KERALA	11	22,003.6	24,528.4	11.5	3	15,900.0	16,600.0	5 - 45
12	MADHYA PRADESH	21	31,448.2	32,674.6	3.9	2	946.6	1,059.4	36 - 69
13	MAHARASHTRA	56	97,971.1	111,407.9	13.7	20	42,206.5	49,740.5	6 - 129
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	108 - 108
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	-
16	MIZORAM	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	35 - 103
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	24 - 24
18	ODISHA	32	56,606.0	63,334.6	11.9	14	48,830.8	52,183.6	5 - 142
19	PUNJAB	6	2,360.2	2,435.2	3.2	0	0.0	0.0	-
20	RAJASTHAN	25	25,380.5	25,805.9	1.7	2	13,426.0	12,998.0	3 - 21
21	SIKKIM	2	1,648.9	3,684.9	123.5	2	1,648.9	3,684.9	15 - 50
22	TAMIL NADU	41	53,479.7	69,711.4	30.4	7	30,151.2	39,580.2	9 - 99
23	TRIPURA	6	2,966.3	4,409.2	48.6	4	2,417.4	3,860.4	10 - 120
24	UTTAR PRADESH	30	21,932.9	26,529.1	21.0	7	4,312.0	6,902.6	10 - 84
25	WEST BENGAL	36	49,851.1	61,412.4	23.2	11	26,260.6	31,286.6	3 - 141
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	-
27	DELHI	4	41,543.9	41,541.3	-0.0	1	2,494.0	2,494.0	8 - 8
28	CHHATISGARH	24	58,278.3	59,362.9	1.9	12	38,458.3	38,769.7	4 - 33
29	JHARKHAND	27	16,118.8	20,384.1	26.5	10	8,991.6	9,501.1	10 - 126
30	UTTARAKHAND	6	7,844.0	9,876.6	25.9	4	6,097.2	7,905.5	5 - 54
31	MULTI STATE	176	183,255.3	206,983.1	12.9	49	87,306.3	95,476.3	1 - 240
Total		741	912,557.6	1,092,632.3	19.7	223	452,841.3	557,881.7	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 66
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	2	653.7	653.7	7 - 50
3	COAL	55	38,127.1	41,525.2	8.9	27	24,452.6	28,222.1	12 - 72
4	STEEL	20	65,959.3	72,162.3	9.4	10	62,441.9	68,084.6	10 - 66
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	82	183,103.4	197,993.7	8.1	52	139,403.7	150,322.4	1 - 95
7	POWER	100	249,166.4	267,559.8	7.4	50	131,275.1	148,326.4	1 - 106
8	RAILWAYS	285	149,113.5	265,521.6	78.1	36	26,037.7	76,542.2	3 - 240
9	ROAD TRANSPORT AND HIGHWAYS	152	106,312.4	108,365.2	1.9	11	4,978.2	5,316.3	2 - 80
10	SHIPPING AND PORTS	19	15,617.1	17,871.5	14.4	1	1,228.0	1,429.1	51 - 51
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	31 - 59
12	URBAN DEVELOPMENT	4	47,598.2	52,871.1	11.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		741	912,557.6	1,092,632.3	19.7	198	435,425.1	529,960.7	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,625.0	6,946.0	4.8	2	2,660.6	2,981.7	12.1
3	COAL	55	41,499.6	41,525.2	0.1	4	1,431.8	1,716.6	19.9
4	STEEL	20	70,209.4	72,162.3	2.8	2	14,680.1	16,662.9	13.5
5	PETROCHEMICALS	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
6	PETROLEUM	82	197,726.1	197,993.7	0.1	11	33,581.4	38,023.2	13.2
7	POWER	100	252,902.1	267,559.8	5.8	13	42,941.5	57,599.3	34.1
8	RAILWAYS	285	182,049.2	265,521.6	45.9	117	65,493.8	149,020.5	127.5
9	ROAD TRANSPORT AND HIGHWAYS	152	107,183.9	108,365.2	1.1	8	2,627.0	3,987.7	51.8
10	SHIPPING AND PORTS	19	17,488.0	17,871.5	2.2	5	3,157.6	3,783.5	19.8
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	4	47,657.1	52,871.1	10.9	1	6,395.0	11,609.0	81.5
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		741	978,324.5	1,092,632.3	11.7	169	191,568.8	310,999.8	62.3

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	1	1,808.00	2,015.00	13- 13
3	COAL	55	38,127.05	41,525.17	8.91	0	0.00	0.00	0- 0
4	STEEL	20	65,959.26	72,162.25	9.40	5	9,557.89	13,808.07	33- 66
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	PETROLEUM	82	183,103.40	197,993.73	8.13	10	20,436.52	34,772.95	20- 120
7	POWER	100	249,166.39	267,559.81	7.38	2	2,253.45	3,986.02	0- 79
8	RAILWAYS	285	149,113.53	265,521.61	78.07	14	5,590.58	21,220.25	0- 141
9	ROAD TRANSPORT AND HIGHWAYS	152	106,312.42	108,365.22	1.93	6	1,288.26	1,831.07	0- 73
10	SHIPPING AND PORTS	19	15,617.12	17,871.52	14.44	5	5,400.70	6,829.35	10- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	4	47,598.18	52,871.08	11.08	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		741	912557.61	1092632.33	19.73	44	51796.01	93382.71	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 66
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	0	0.00	0.00	0- 0
3	COAL	55	38,127.05	41,525.17	8.91	5	7,938.86	11,886.62	19- 57
4	STEEL	20	65,959.26	72,162.25	9.40	4	23,538.89	29,522.85	30- 66
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	PETROLEUM	82	183,103.40	197,993.73	8.13	20	55,566.37	75,789.89	3- 120
7	POWER	100	249,166.39	267,559.81	7.38	15	43,738.85	60,790.17	10- 106
8	RAILWAYS	285	149,113.53	265,521.61	78.07	34	23,261.74	74,557.73	9- 240
9	ROAD TRANSPORT AND HIGHWAYS	152	106,312.42	108,365.22	1.93	8	1,628.10	2,471.98	57- 80
10	SHIPPING AND PORTS	19	15,617.12	17,871.52	14.44	2	1,378.00	2,029.10	51- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	1	149.15	158.72	54- 54
12	URBAN DEVELOPMENT	4	47,598.18	52,871.08	11.08	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		741	912557.61	1092632.33	19.73	92	179323.57	289074.06	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	RESITMENT OF MARKETING INSTALATION AT VISAKH	01/2009	756.00	N.A.	898.00	08/2013	913.72
2	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	01/2008	224.00	N.A.	394.00	03/2013	312.61
3	FLUIDIZED CATALYTIC CRACKING UNIT(FCCU) REVAMP AT MATHURA REFINERY	07/2010	1,000.00	01/2013	1,000.00	01/2014	755.25
4	CAPACITY AUGMENTATION OF KOTA PIYALA SECTION OF MMBPL PIPELINE	04/2011	152.89	06/2013	152.89	07/2013	128.53
	<u>RAILWAYS</u>						
5	KOLAR-CHICKBALAPUR GC	04/2006	287.99	01/1999	287.99	12/2013	434.57

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	KOTA JOBNER PIPELINE PROJECT	4/2011	276.26	3/2015	276.26	3/2015
	<u>POWER</u>					
2	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW)	7/2012	296.87	/	296.87	-
3	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	374.63	4/2016	374.63	4/2016
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
4	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	1,348.20	/	1,348.20	-
	<u>STEEL</u>					
5	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	10/2012	160.48	9/2017	160.48	9/2014
6	REBUILDING OF COB-7 AT BSL	10/2013	245.67	5/2016	245.67	5/2016

Milestones (Cumulative due & achieved)		
Total	3636	
Achieved up to month	1379	

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS AAI	344.28	344.28	03/2014	06/2014	10/2014	4
	<u>STEEL</u>						
2	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	09/2008	12/2013	03/2014	3
3	EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	12/2013	03/2014	3
4	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) NMDC	295.89	607.17	12/2011	03/2014	09/2014	6
5	EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	12/2011	12/2013	06/2014	6
6	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	09/2014	03/2015	6
7	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) NMDC	572.00	572.00	04/2013	03/2014	09/2014	6
8	EXPANSION OF ROURKELA STEEL PLANT SAIL	11,812.00	11,812.00	03/2013	12/2013	09/2014	9
9	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	03/2014	12/2014	9
10	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) NMDC	898.55	898.55	05/2013	03/2014	01/2015	10
	<u>PETROLEUM</u>						
11	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY BPCL	825.00	1,827.00	04/2013	11/2013	12/2013	1
12	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA GAIL	8,140.00	8,140.00	02/2014	02/2014	03/2014	1
13	MRPL PHASE-III EXPANSION MANGALORE REFIN	12,412.00	12,160.26	01/2012	12/2013	01/2014	1
14	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	586.00	586.00	08/2015	07/2015	08/2015	1
15	IOR, RUDRASAGAR (ONGCL) ONGC	113.90	480.00	03/2006	12/2013	02/2014	2
16	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	12/2013	02/2014	2


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
17	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA ONGC	288.04	253.66	08/2012	03/2014	06/2014	3
18	DEVELOPMENT OF BHE AND BH-35 AREA. ONGC	372.11	372.11	03/2013	12/2013	03/2014	3
19	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY HPCL	3,284.00	2,174.00	09/2011	09/2013	05/2014	8
20	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG OIL	270.00	270.00	12/2014	12/2014	08/2015	8
21	DEVELOPMENT OF C-26 CLUSTER FIELDS ONGC	2,592.17	2,592.17	05/2014	05/2014	05/2015	12
22	URAN CHAKAN/SHIKRAPUR LPG PIPELINE HPCL	309.81	309.82	10/2014	10/2014	10/2015	12
	<u>POWER</u>						
23	URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	2,081.00	11/2009	12/2013	01/2014	1
24	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	03/2014	05/2014	2
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV PGCIL	520.48	520.48	11/2011	09/2014	12/2014	3
26	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	06/2014	09/2014	3
27	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH PGCIL	2,127.51	2,127.51	07/2014	07/2014	12/2014	5
28	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	9,569.76	9,569.76	06/2015	06/2015	12/2015	6
29	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	06/2014	03/2015	9
30	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B PGCIL	3,201.44	3,201.44	10/2014	09/2014	06/2015	9
31	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C PGCIL	2,569.25	2,569.25	03/2014	05/2014	03/2015	10
	<u>RAILWAYS</u>						
32	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	12/2013	01/2014	1
33	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR NEFR	156.00	407.98	N.A.	12/2013	03/2014	3


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
34	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	04/2014	05/2014	1
35	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	04/2014	07/2014	3
36	NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	07/2014	01/2015	6
37	BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	309.56	04/2010	01/2015	09/2015	8
38	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	04/2014	01/2015	9
39	GUWAHATI TO NALBARI (AS-5) NHAI	198.16	198.16	04/2008	04/2014	01/2015	9
	<u>SHIPPING AND PORTS</u>						
40	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) PORT TRUST	150.00	600.00	03/2006	12/2013	06/2014	6
40							

Graphical Presentation of All Projects w.r.t. Original Schedule

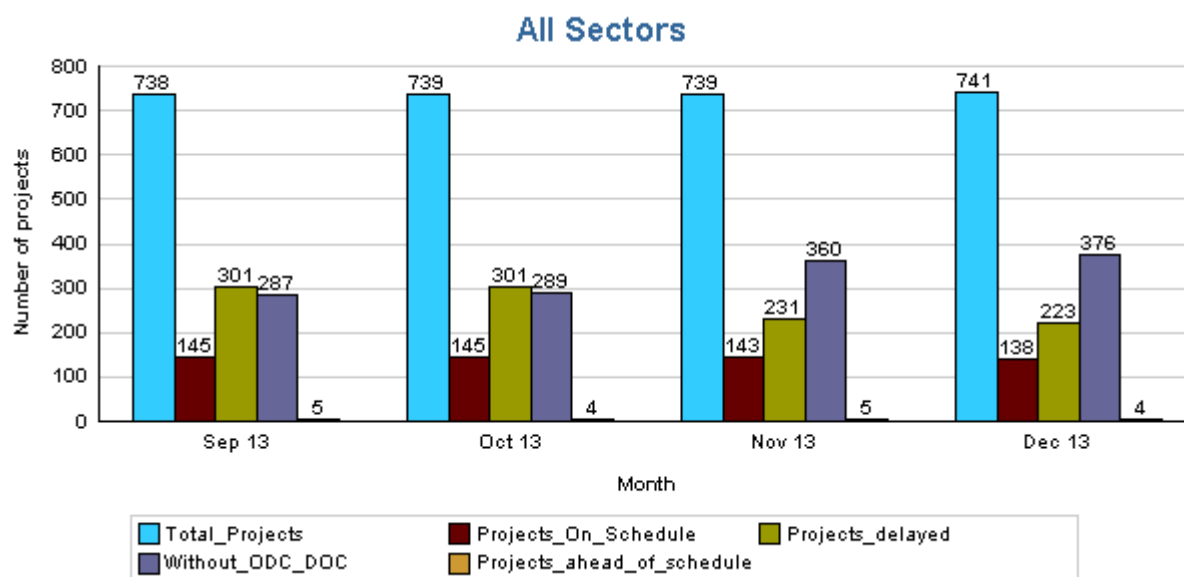


Break-up of 223 Delayed projects in December 2013

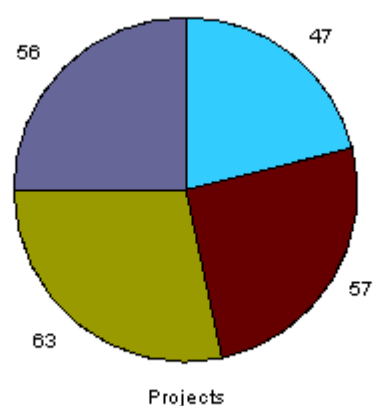


Delay in Months



Graphical Presentation of All Projects w.r.t. Revised Schedule

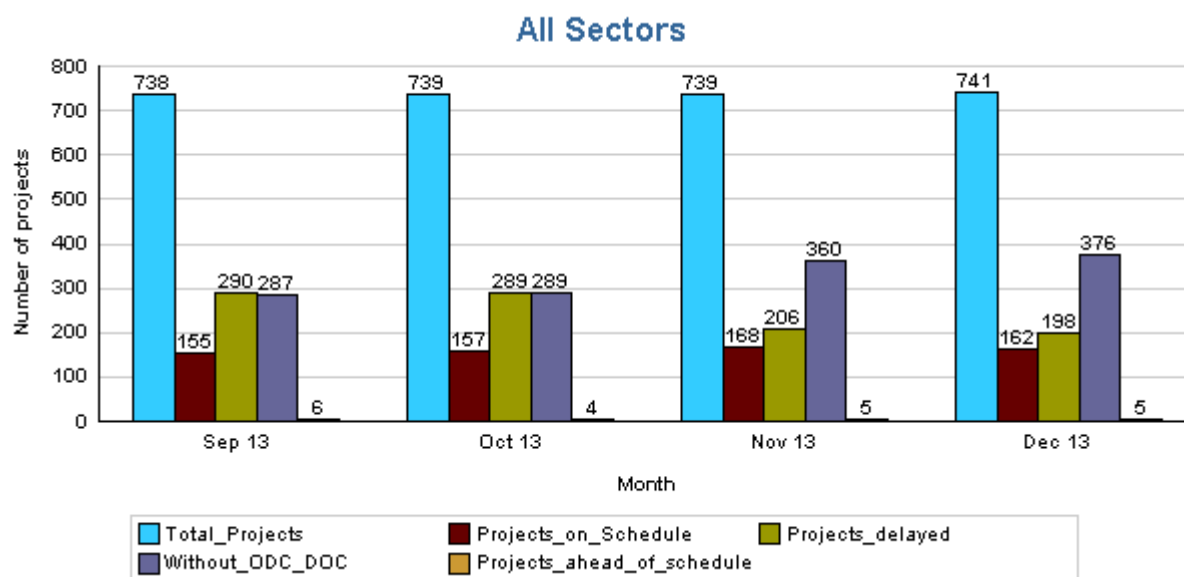


Break-up of 198 Delayed projects in December 2013

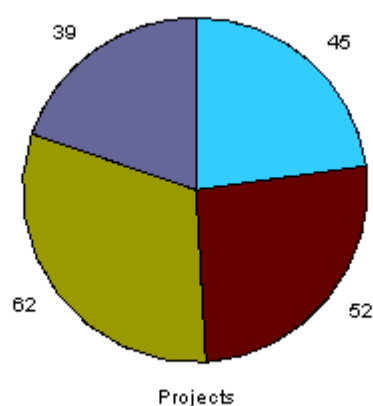


Delay in Months



Graphical Presentation of URBAN DEVELOPMENT Sector

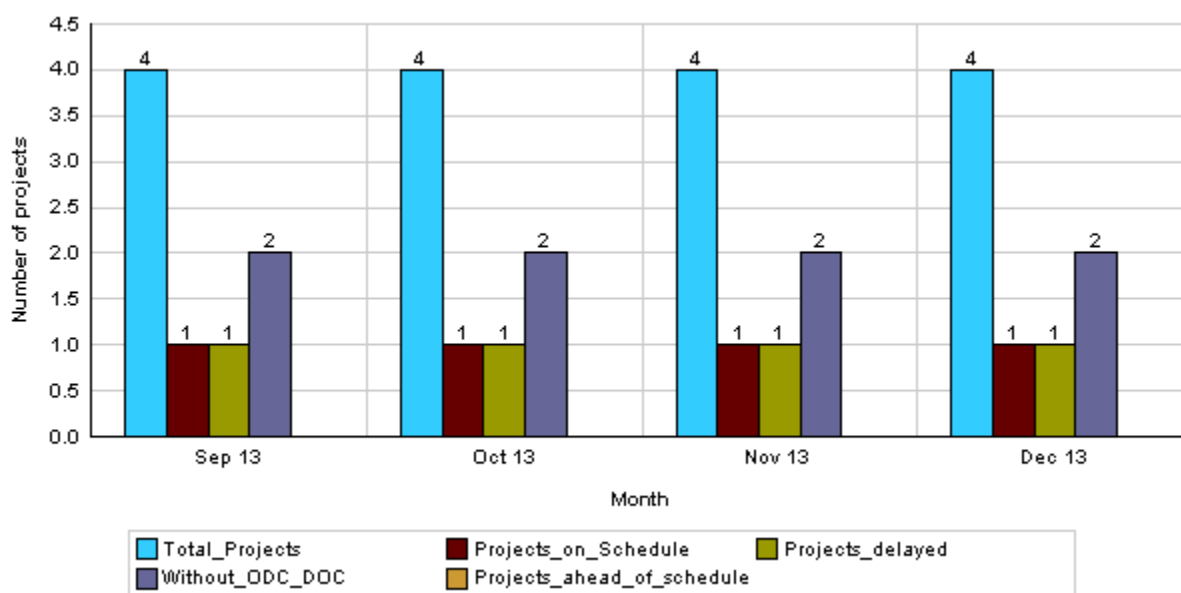


Break-up of 1 Delayed projects in December 2013




Delay in Months



Graphical Presentation of TELECOMMUNICATIONS Sector

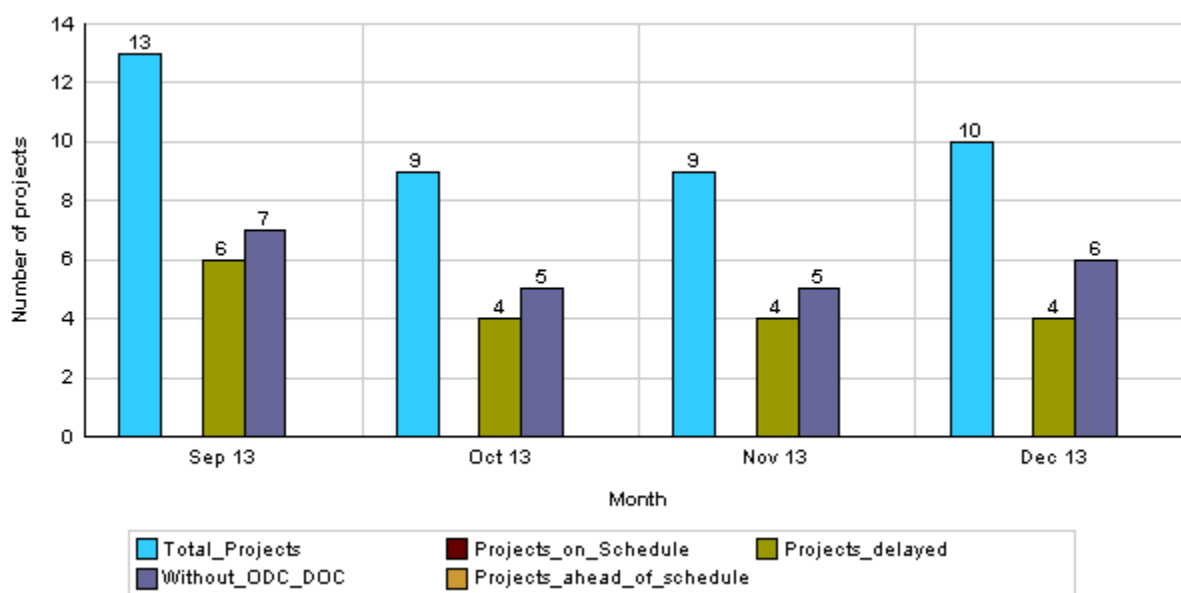


Break-up of 4 Delayed projects in December 2013

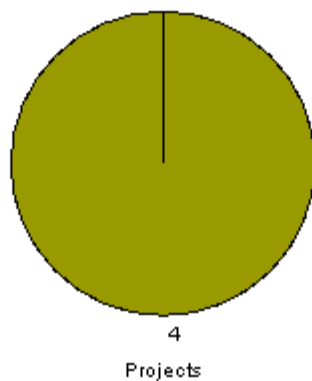


Delay in Months

Graphical Presentation of SHIPPING AND PORTS Sector

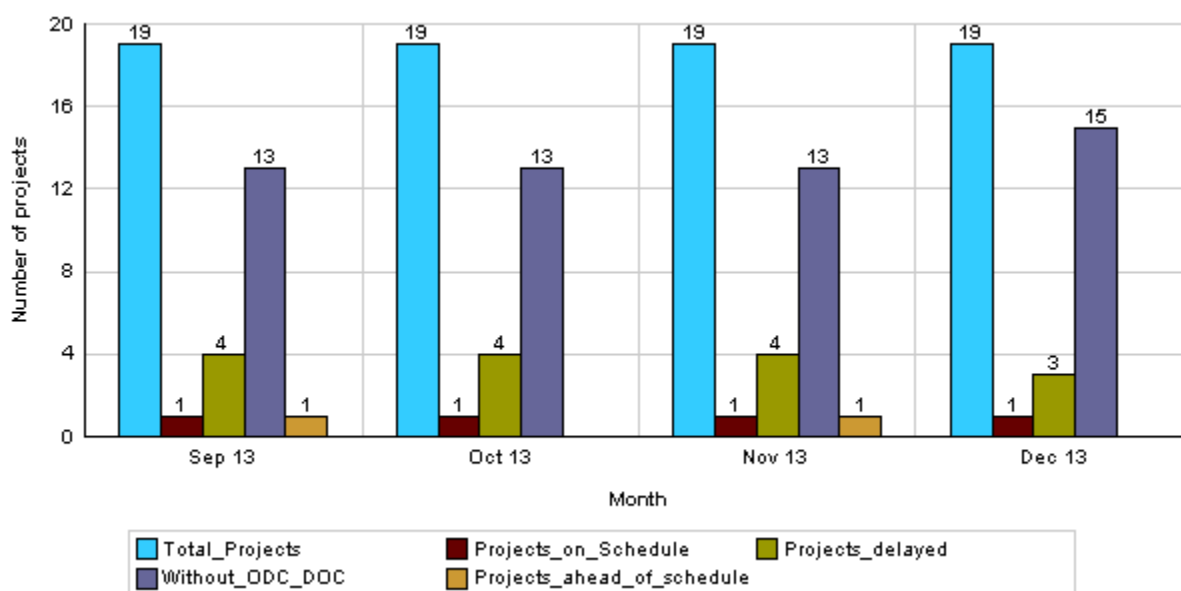


Break-up of 3 Delayed projects in December 2013

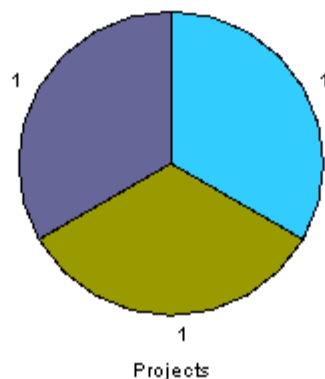


Delay in Months



Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

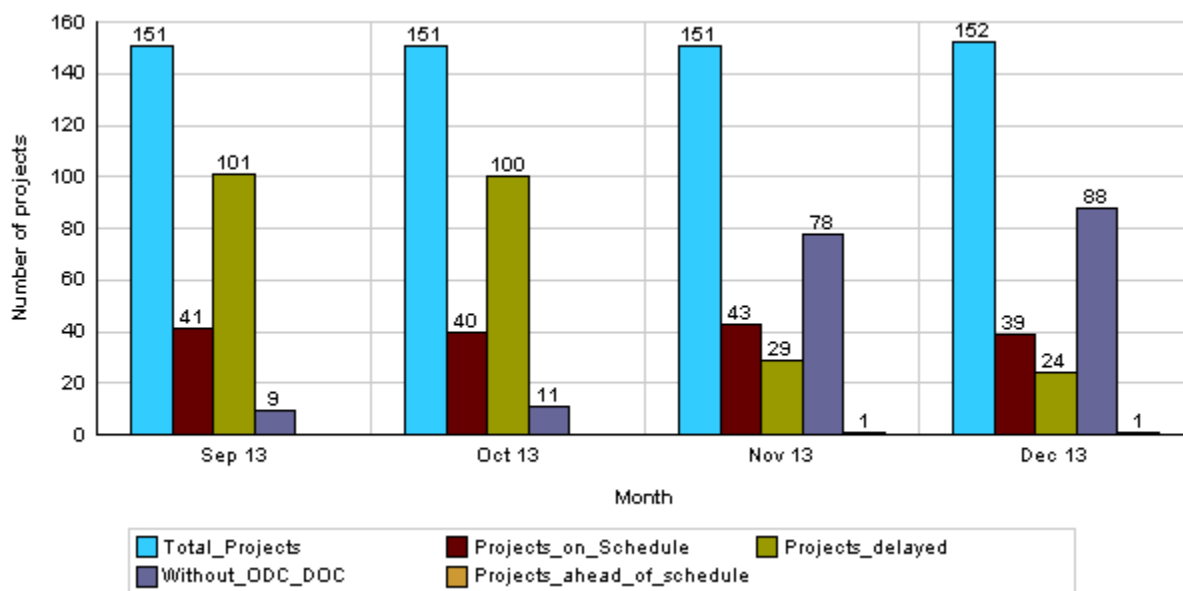


Break-up of 24 Delayed projects in December 2013

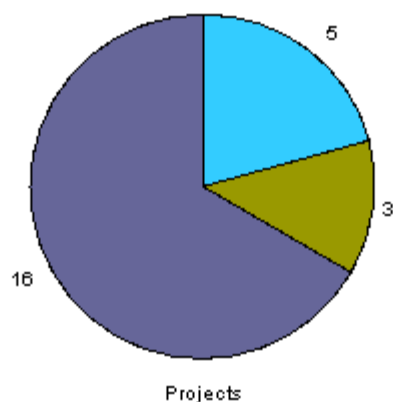


Delay in Months



Graphical Presentation of RAILWAYS Sector

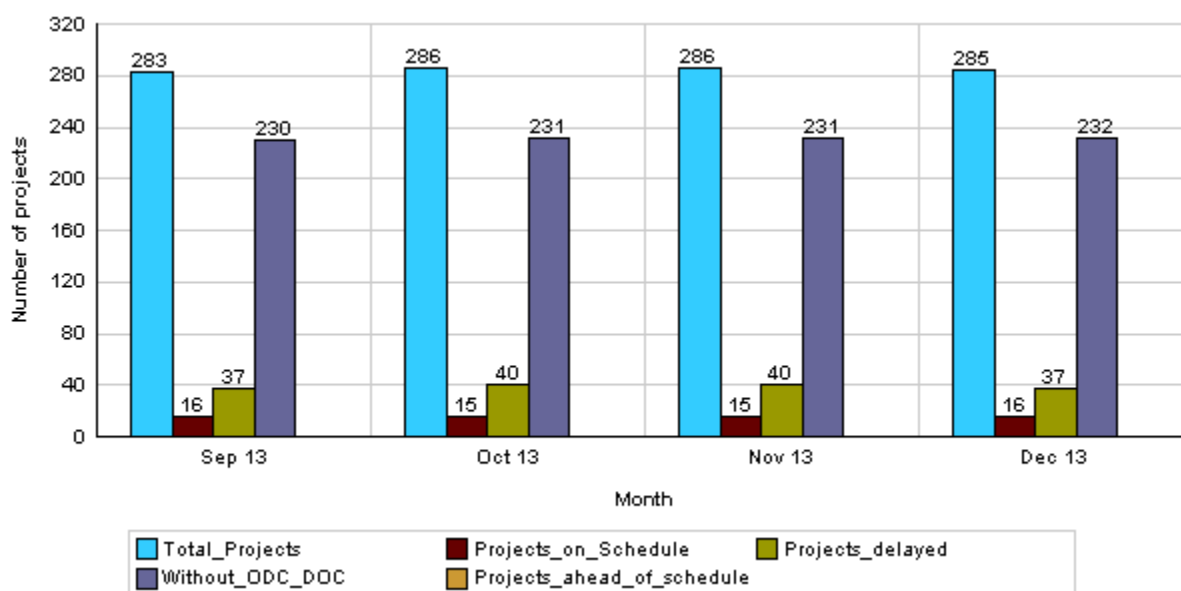


Break-up of 37 Delayed projects in December 2013

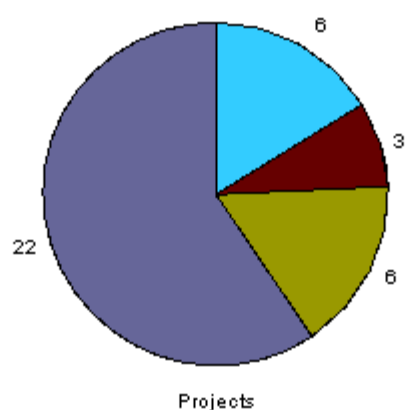


Delay in Months



Graphical Presentation of POWER Sector

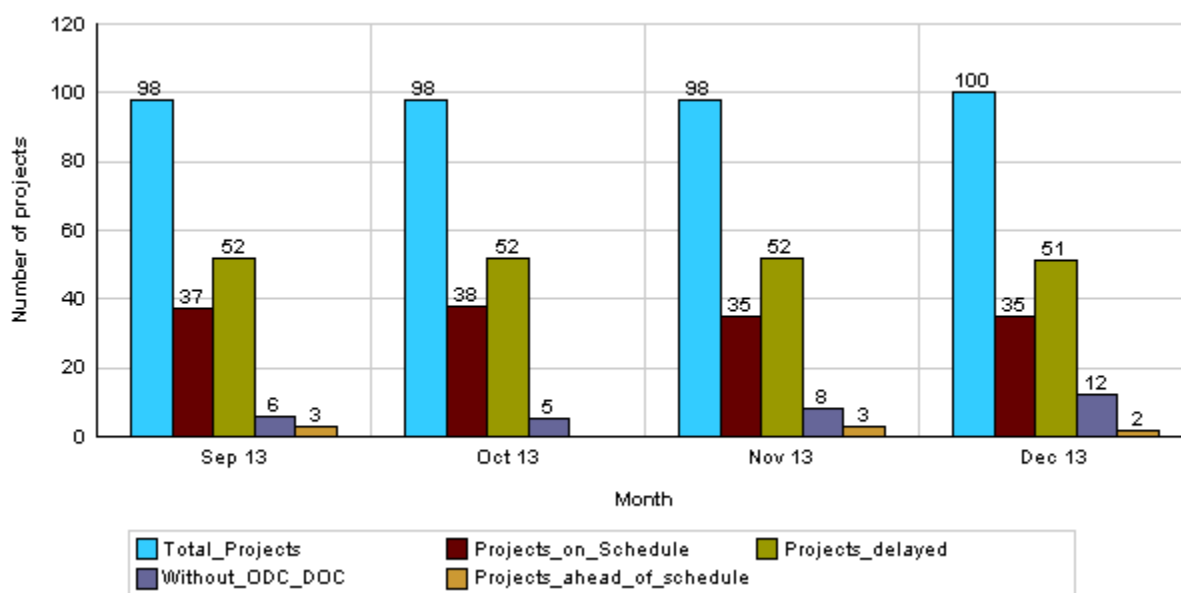


Break-up of 51 Delayed projects in December 2013

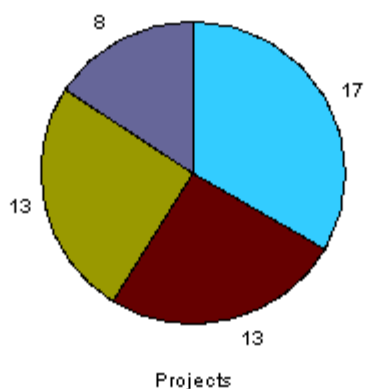


Delay in Months



Graphical Presentation of PETROLEUM Sector

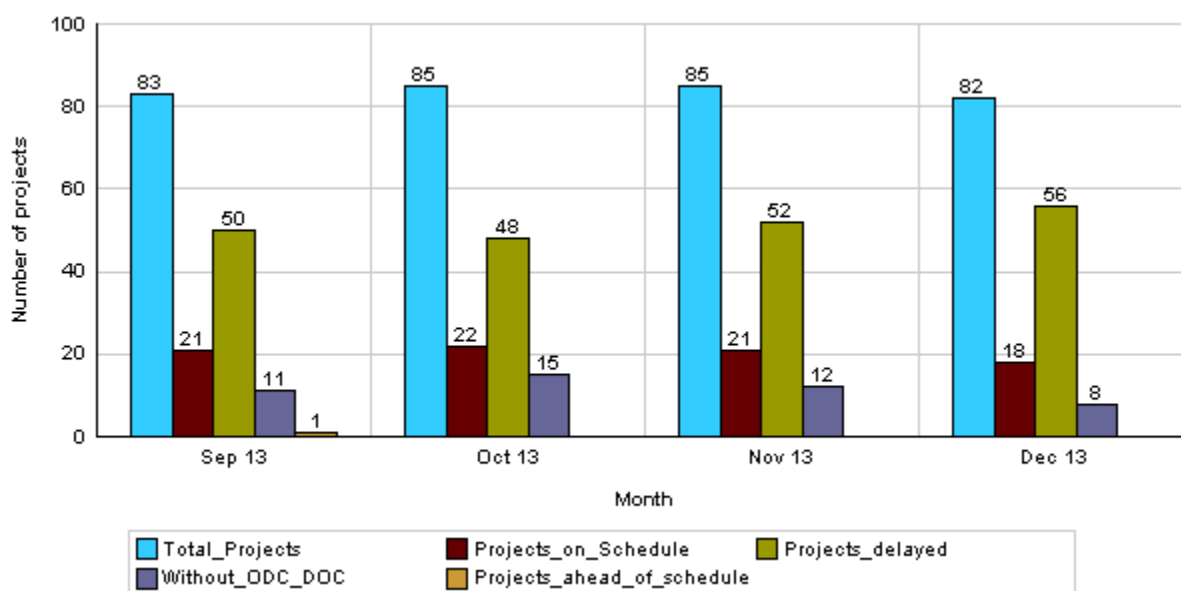


Break-up of 56 Delayed projects in December 2013

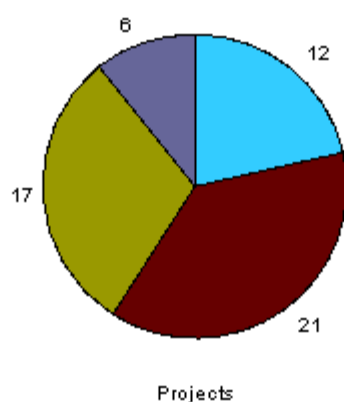


Delay in Months



Graphical Presentation of STEEL Sector

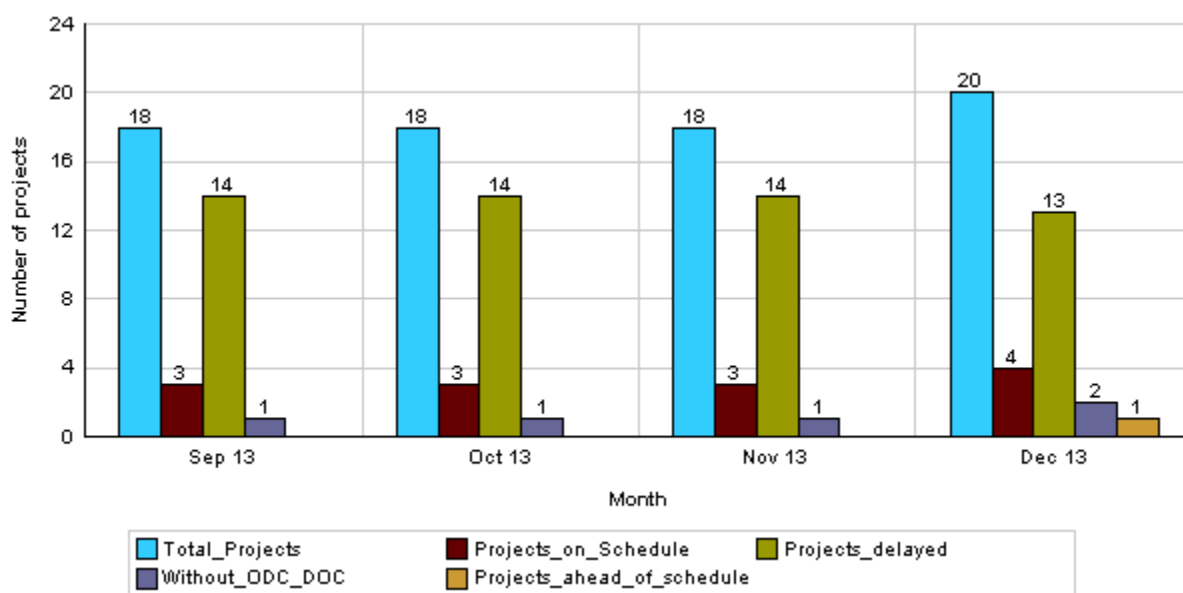


Break-up of 13 Delayed projects in December 2013

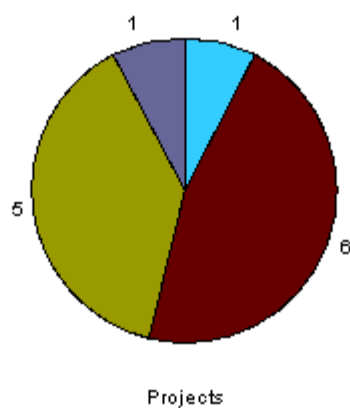


Delay in Months



Graphical Presentation of COAL Sector

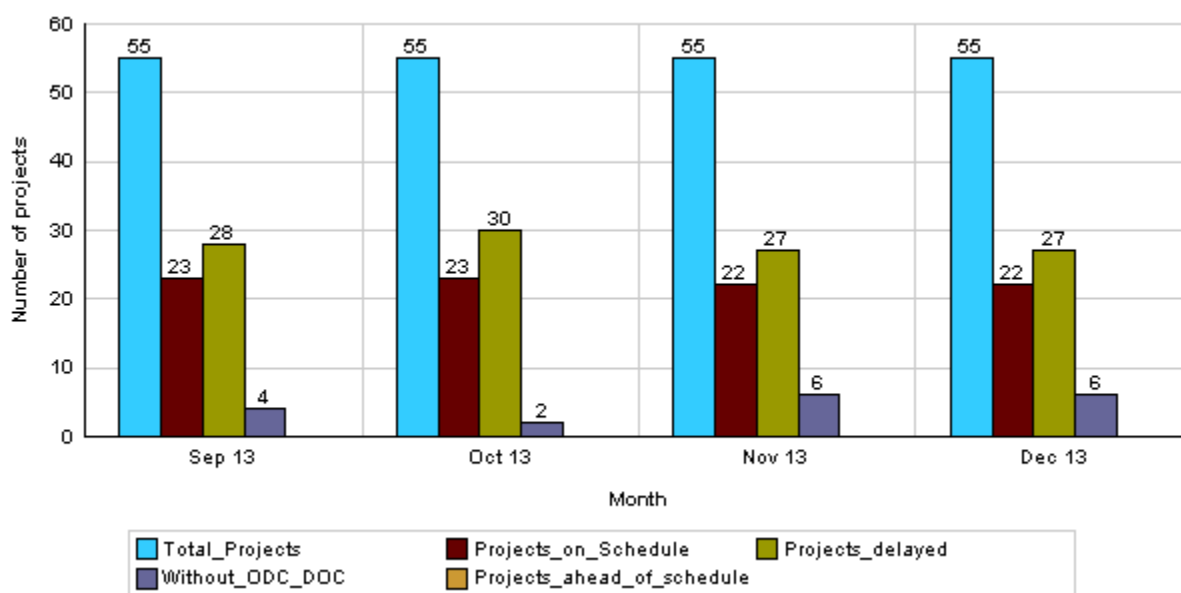


Break-up of 27 Delayed projects in December 2013

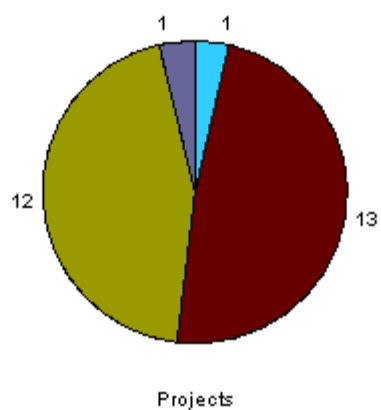


Delay in Months



Graphical Presentation of CIVIL AVIATION Sector

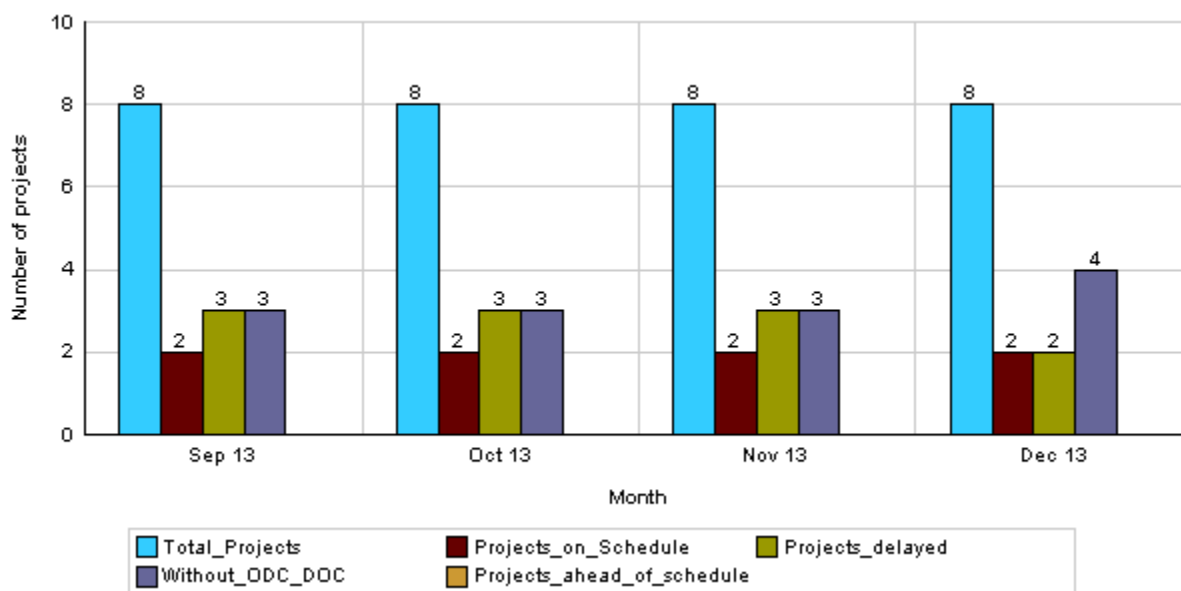


Break-up of 2 Delayed projects in December 2013

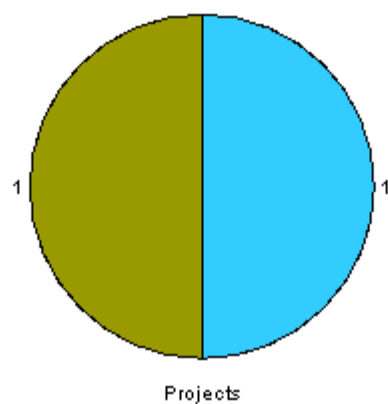


Delay in Months



Graphical Presentation of ATOMIC ENERGY Sector

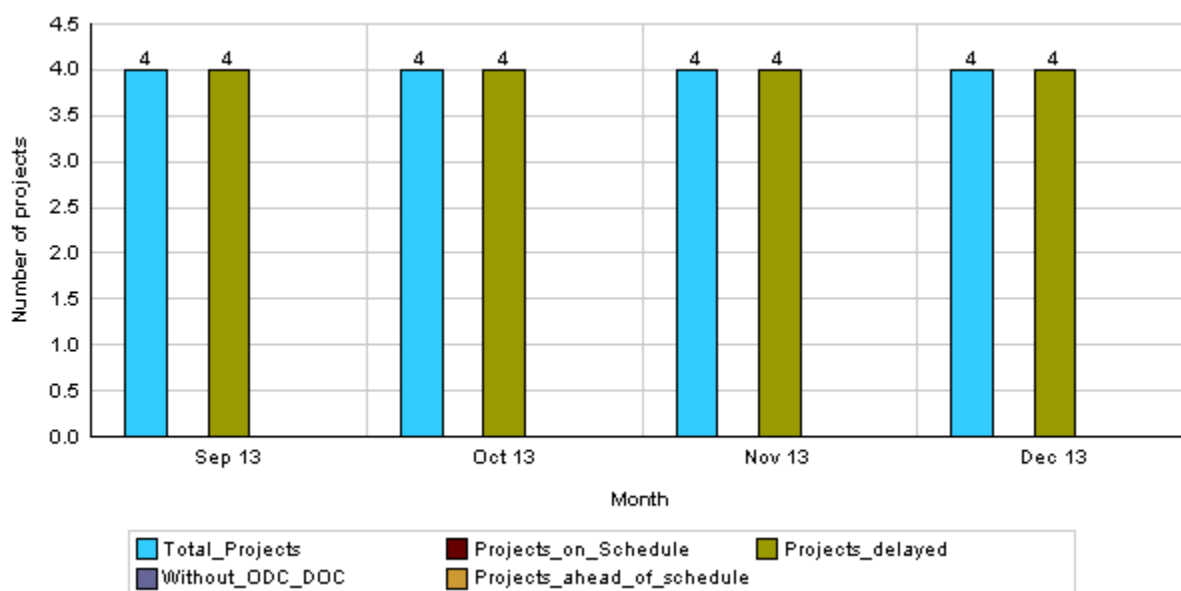

Break-up of 4 Delayed projects in December 2013

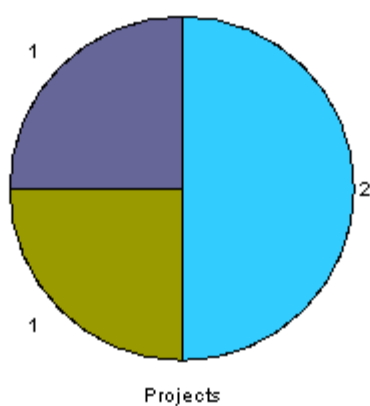

Delay in Months



Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	40,442.00	46,726.00	26,358.16
CIVIL AVIATION	8	6,035.46	6,624.95	6,946.00	5,541.80
COAL	55	38,127.05	41,499.58	41,525.17	16,992.15
STEEL	20	65,959.26	70,209.44	72,162.25	56,685.80
PETROCHEMICALS	1	5,460.61	8,920.00	8,920.00	4,510.51
PETROLEUM	82	183,103.40	197,726.12	197,993.73	100,971.49
POWER	100	249,166.39	252,902.06	267,559.81	122,983.17
RAILWAYS	285	149,113.53	182,049.15	265,521.61	77,081.07
ROAD TRANSPORT AND HIGHWAYS	152	106,312.42	107,183.94	108,365.22	86,173.46
SHIPPING AND PORTS	19	15,617.12	17,487.95	17,871.52	8,722.60
TELECOMMUNICATIONS	10	5,079.29	5,079.29	4,982.94	1,751.97
URBAN DEVELOPMENT	4	47,598.18	47,657.08	52,871.08	8,819.72
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	741	912,557.61	978,324.46	1,092,632.33	516,627.39

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(Dec,2013)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	3,088.00	12/2015 -	11/2016	11(O) -	2/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	16,485.00	12/2008 -	06/2014	66(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,666.16	09/2010 -	03/2015	54(O) -	9/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	2,119.00	12/2016 -	03/2017	3(O) -	0/69
	Total		40,442.00 -	46,726.00	26,358.16				50/327
	<u>CIVIL AVIATION</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI, WEST BENGAL	08/2008	1,942.51 2,325.00	2,593.13	2,476.01	05/2011 -	03/2013	-	0/0
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	244.66	01/2011 04/2013	03/2015	50(O) 23(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	260.78	05/2012 -	11/2013	-	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	2,015.00	1,908.47	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	190.30	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	461.56	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,946.00	5,541.80				0/0
	<u>COAL</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,143.43	03/2013 09/2012	10/2014	19(O) 25(R)	18/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	90.42	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	613.44	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	49.66	03/2020 -	03/2020	0(O) -	0/3
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	122.60	03/2012 -	03/2014	24(O) -	5/6

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	118.26	03/2011 -	03/2014	36(O) -	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	130.05	03/2010 -	03/2015	60(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	53.49	03/2016 -	03/2016	0(O) -	0/6
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	158.33	03/2017 -	03/2017	0(O) -	4/12
23	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]NCL,MULTI STATE	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014	0(O) -	0/2
24	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	162.91	03/2015 -	03/2015	0(O) -	0/3
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	269.16	03/2014 -	03/2016	24(O) -	2/8
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.28	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,300.67	03/2014 -	03/2016	24(O) -	6/12
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,586.15	03/2014 -	03/2016	24(O) -	10/15
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	74.32	03/2015 -	03/2015	0(O) -	1/13
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	113.94	03/2013 -	03/2015	24(O) -	3/8
31	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,ANDHRA PRADESH	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2015	0(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,ANDHRA PRADESH	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72(O) -	0/2
35	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	100.52	12/2012 -	03/2015	27(O) -	10/44
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,ANDHRA PRADESH	07/2012	417.33 -	417.33	0.15	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	113.61	03/2013 -	03/2015	24(O) -	5/10
38	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	49.77	03/2014 -	03/2014	0(O) -	0/2
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
40	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018	0(O) -	0/4
41	KISTARAM OCP - [N06000089]SCCL,ANDHRA PRADESH	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	381.07	03/2013 -	03/2014	12(O) -	0/2
43	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	116.51	03/2010 -	03/2014	48(O) -	9/10

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
44	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	1,188.31	746.30	03/2013 -	-	-	0/9
45	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	27.80	07/2012 -	03/2016	44(O) -	0/3
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.16	03/2014 -	03/2016	24(O) -	1/6
47	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	181.19	35.07	03/2012 -	-	-	4/6
48	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
49	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
50	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	246.90	12/2015 -	04/2018	28(O) -	2/33
51	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36(O) -	0/2
52	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	62.43	03/2012 -	03/2017	60(O) -	0/2
53	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
54	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.38	03/2014 -	03/2016	24(O) -	0/1
55	PUKNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	97.31	03/2013 -	03/2015	24(O) -	0/3
56	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	29.40	03/2014 -	03/2016	24(O) -	0/2
57	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016	0(O) -	0/2
58	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	418.97	242.96	03/2012 -	-	-	24/27
59	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,ANDHRA PRADESH	07/2011	162.76 -	162.76	2.56	03/2015 -	03/2015	0(O) -	4/29
60	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,ANDHRA PRADESH	11/2012	430.14 -	430.14	59.07	03/2016 -	-	-	4/48
61	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,ANDHRA PRADESH	06/2012	365.01 -	365.01	3.62	06/2015 -	06/2015	0(O) -	2/51
62	RKP OCP PHASE-I - [N06000079]SCCL,ANDHRA PRADESH	03/2010	209.78 -	209.78	54.43	03/2015 -	03/2015	0(O) -	8/31
63	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,ANDHRA PRADESH	10/2006	249.03 -	249.03	58.03	03/2012 -	-	-	16/42
64	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	48.56	03/2016 -	03/2016	0(O) -	0/12
65	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	140.55	03/2012 -	03/2016	48(O) -	0/2
66	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,833.94	06/2009 -	03/2014	57(O) -	19/23
67	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	4,940.31	03/2012 -	05/2014	26(O) -	19/38
	Total		38,127.05 -	41,525.17	16,992.15				198/777
	STEEL								

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	352.49	04/2013 09/2014	09/2014	17(O) 0(R)	17/18
69	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016	0(O) -	0/0
70	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	349.64	257.79	12/2009 08/2010	06/2013	-	1/1
71	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	343.58	288.95	01/2010 02/2011	11/2013	-	3/3
72	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	251.55	05/2013 01/2015	01/2015	20(O) 0(R)	13/20
73	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	296.11	09/2009 05/2012	06/2014	57(O) 25(R)	1/1
74	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	361.53	12/2011 09/2014	09/2014	33(O) 0(R)	15/20
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	159.67	09/2008 12/2013	03/2014	66(O) 3(R)	3/4
76	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	90.51	08/2014 -	08/2014	0(O) -	1/2
77	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	96.38	11/2013 -	06/2015	19(O) -	1/3
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	11,718.09	03/2013 -	03/2015	24(O) -	23/32
79	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,191.41	12/2011 -	03/2014	27(O) -	18/21
80	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	1,944.74	12/2012 -	12/2014	24(O) -	12/16
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,451.60	12/2011 -	06/2014	30(O) -	21/23
82	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,654.93	10/2009 10/2012	03/2014	53(O) 17(R)	66/67
83	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,400.65	03/2013 -	09/2014	18(O) -	15/19
84	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	108.67	10/2013 -	08/2014	10(O) -	0/3
85	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	-	09/2017 -	09/2014	-36(O) -	0/0
86	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	313.05	39.54	06/2015 -	06/2015	0(O) -	0/0
87	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	254.90	14.28	12/2014 -	12/2014	0(O) -	0/1
	Total		65,959.26 -	72,162.25	56,685.80				210/254
	<u>PETROCHEMICALS</u>								
88	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20(O) 0(R)	19/29

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		5,460.61 -	8,920.00	4,510.51				19/29
	<u>PETROLEUM</u>								
89	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	52.67	06/2012 -	03/2014	21(O) -	0/4
90	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23(O) -	0/0
91	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,MAHARASHTRA	10/2008	1,797.35 -	977.00	841.98	12/2011 -	12/2013	24(O) -	0/5
92	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.08	12/2014 -	12/2016	24(O) -	0/0
93	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.43	12/2014 -	12/2016	24(O) -	0/0
94	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24(O) 12(R)	0/5
95	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	105.13	08/2015 -	08/2015	0(O) -	0/0
96	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	540.92	334.22	07/2012 07/2012	-	-	6/7
97	BUTENE-1 PROJECT AT PANIPAT - [N16000139]IOCL,HARYANA	02/2012	190.00 -	165.00	107.60	03/2014 -	03/2014	0(O) -	23/24
98	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	142.87	06/2012 -	03/2014	21(O) -	0/0
99	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	445.92	09/2011 -	12/2014	39(O) -	0/0
100	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,ASSAM	08/2008	126.18 -	159.54	62.95	06/2012 -	03/2014	21(O) -	0/0
101	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	104.65	08/2013 -	03/2014	7(O) -	0/5
102	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	99.40	09/2012 -	03/2014	18(O) -	0/0
103	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12(O) -	0/5
104	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014	0(O) -	0/5
105	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
106	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	-	0/5
107	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2014	0(O) -	0/5
108	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	434.72	05/2013 06/2014	06/2014	13(O) 0(R)	0/5
109	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	10/2016	49(O) -	0/0
110	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	73.65	09/2013 -	09/2013	-	0/1

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
111	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	549.85	- -	-	-	0/0
112	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94(O) 20(R)	0/0
113	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.46	08/2010 03/2012	05/2014	45(O) 26(R)	0/10
114	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
115	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44(O) 22(R)	0/0
116	DEVELOPMENT OF BHE AND BH-35 AREA. - [N16000118]ONGC,MULTI STATE	08/2010	372.11 -	372.11	234.31	03/2013 -	03/2014	12(O) -	0/5
117	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	107.61	05/2014 -	05/2015	12(O) -	0/9
118	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63(O) 11(R)	0/0
119	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
120	DEVELOPMENT OF SB-14 FIELD - [N16000116]ONGC,MULTI STATE	01/2011	410.44 -	410.44	229.63	11/2012 -	02/2014	15(O) -	0/9
121	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	146.70	12/2014 -	12/2014	0(O) -	0/8
122	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	990.56	01/2014 -	12/2015	23(O) -	0/9
123	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,848.86	09/2011 05/2012	05/2014	32(O) 24(R)	6/76
124	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	1,975.56	09/2011 03/2012	03/2014	30(O) 24(R)	56/59
125	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	1.75	- -	-	-	0/0
126	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26(O) -	0/9
127	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	1,697.89	05/2015 -	05/2015	0(O) -	0/17
128	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,MAHARASHTRA	04/2008	825.00 -	1,827.00	1,488.84	04/2013 -	12/2013	8(O) -	0/167
129	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	400.85	03/2015 -	03/2015	0(O) -	0/12
130	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0
131	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	991.96	12/2015 -	05/2016	5(O) -	0/0
132	IOR GELEKI (ONGCL) - [160100216]ONGC,ASSAM	09/2001	390.09 1,674.11	1,674.11	1,759.52	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
133	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,ASSAM	09/2001	345.10 663.69	750.00	743.72	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
134	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	32.51	03/2014 -	12/2014	9(O) -	0/5
135	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,ASSAM	09/2001	113.90 438.85	480.00	452.91	03/2006 03/2013	02/2014	95(O) 11(R)	6/6
136	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
137	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0
138	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	-	0/1
139	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,264.75	12/2012 -	-	-	0/10
140	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.26	-	03/2015 -	03/2015	0(O) -	0/0
141	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	11/2012	666.00 701.00	701.00	172.24	11/2015 -	11/2015	0(O) -	14/29
142	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	93.57	06/2014 -	06/2014	0(O) -	0/0
143	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23(O) -	0/0
144	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	283.87	12/2014 -	12/2014	0(O) -	0/0
145	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	10,921.92	01/2012 -	01/2014	24(O) -	0/108
146	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,543.40	09/2012 -	03/2014	18(O) -	0/0
147	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	03/2014	46(O) 12(R)	0/0
148	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,MAHARASHTRA	01/2007	740.02 -	740.02	731.38	03/2010 03/2012	02/2014	47(O) 23(R)	0/0
149	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	48.55	07/2015 -	07/2015	0(O) -	0/0
150	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	24,112.00	11/2012 -	09/2014	22(O) -	60/100
151	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	918.75	09/2012 -	08/2015	35(O) -	5/11
152	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	5,979.82	02/2014 -	03/2014	1(O) -	0/0
153	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	19.63	04/2012 -	03/2014	23(O) -	0/0
154	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	-	07/2016 -	07/2016	0(O) -	0/5
155	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	749.95	05/2014 -	05/2014	0(O) -	0/5
156	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	770.44	07/2012 -	03/2014	20(O) -	0/31
157	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	08/2015	8(O) -	0/0
158	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015	0(O) -	0/0
159	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	267.86	12/2014 -	12/2014	0(O) -	0/0
160	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	414.82	11/2015 -	11/2015	0(O) -	9/25
161	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20(O) -	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
162	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	771.02	10/2011 -	10/2015	48(O) -	0/0
163	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KERALA	01/2006	993.00 1,693.00	1,693.00	1,054.78	01/2012 -	10/2015	45(O) -	0/0
164	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPR,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	925.99	10/2011 -	06/2014	32(O) -	0/0
165	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	0.04	- -	04/2015	- -	0/0
166	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	204.57	08/2012 -	06/2014	22(O) -	0/5
167	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	6.91	03/2015 -	06/2015	3(O) -	0/5
168	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.47	10/2014 -	10/2015	12(O) -	0/0
169	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	266.21	03/2012 -	03/2015	36(O) -	13/20
170	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	400.99	12/2013 -	03/2014	3(O) -	0/0
	Total		183,103.40 -	197,993.73	100,971.49				207/851
	<u>POWER</u>								
171	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,110.13	08/2012 -	03/2014	19(O) -	0/11
172	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-III - [N18000079]PGCIL,MULTI STATE	11/2009	1,075.12 -	1,075.12	-	05/2012 -	12/2013	19(O) -	5/8
173	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	-	- -	-	-	0/17
174	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	6.15	10/2014 -	10/2014	0(O) -	0/7
175	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,621.00	08/2013 -	09/2014	13(O) -	13/19
176	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	8,976.00	12/2009 -	03/2017	87(O) -	24/49
177	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,216.00	07/2011 -	06/2016	59(O) -	5/28
178	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015	0(O) -	2/20
179	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,151.72	09/2014 -	09/2014	0(O) -	7/20
180	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,ANDHRA PRADESH	06/2012	1,909.24 -	1,909.24	313.73	06/2015 -	06/2015	0(O) -	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
181	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,ANDHRA PRADESH	08/2011	1,637.34 -	1,637.34	1,123.83	08/2014 -	08/2014	0(O) -	7/20
182	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	42.36	06/2014 -	06/2014	0(O) -	0/20
183	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
184	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	4.84	10/2014 -	10/2014	0(O) -	2/2
185	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,MULTI STATE	10/2006	975.96 -	975.96	887.66	10/2009 -	05/2014	55(O) -	5/15
186	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016	0(O) -	0/0
187	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	771.27	11/2012 -	03/2015	28(O) -	2/13
188	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
189	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	-	05/2014 -	05/2014	0(O) -	2/11
190	ESTABLISHMENT OF POOLING STATIONS AT RAJGARH AND RAIPUR FOR IPP GENERATION PROJECTS IN CHATTISGARH - [N18000092]PGCIL,CHHATISGARH	12/2010	1,719.52 -	1,719.52	-	08/2013 -	12/2013	4(O) -	1/12
191	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	911.00	09/2017 -	09/2017	0(O) -	4/41
192	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	514.53	08/2014 -	08/2014	0(O) -	1/16
193	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	-	12/2013 -	12/2013	0(O) -	3/12
194	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016	0(O) -	0/0
195	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 1,007.16	1,007.16	913.41	12/2007 12/2009	-	-	2/11
196	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	5,139.00	2,624.41	12/2009 06/2016	03/2017	87(O) 9(R)	11/26
197	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,016.95	01/2016 -	11/2016	10(O) -	4/6
198	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	6,414.56	5,285.00	04/2009 -	09/2014	65(O) -	1/9
199	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	2,450.00	12/2016 -	12/2016	0(O) -	15/21
200	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,872.07	09/2008 -	03/2013	-	15/23

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
201	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,216.00	05/2017 -	05/2017	0(O) -	7/41
202	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017	0(O) -	1/9
203	MOUDA STPP - [N18000048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
204	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	1,408.00	09/2016 -	09/2016	0(O) -	16/17
205	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,218.89	08/2013 -	06/2015	22(O) -	0/17
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	-	07/2013 -	03/2014	8(O) -	2/11
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	267.38	02/2012 -	12/2013	22(O) -	1/13
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,MULTI STATE	02/2009	520.48 -	520.48	370.39	11/2011 -	12/2014	37(O) -	0/11
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	392.52	11/2011 -	12/2013	25(O) -	1/14
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,MULTI STATE	10/2010	182.68 -	182.68	-	01/2013 -	-	-	4/6
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	953.10	04/2013 -	03/2015	23(O) -	0/11
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	260.51	11/2014 -	11/2014	0(O) -	2/12
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	-	03/2016 -	03/2016	0(O) -	0/0
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	-	03/2015 -	03/2015	0(O) -	4/15
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	72.00	04/2015 -	05/2015	1(O) -	0/16
216	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	620.75	11/2012 -	03/2014	16(O) -	0/11
217	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,247.55	10/2010 -	03/2014	41(O) -	0/2
218	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,187.29	09/2009 -	07/2018	106(O) -	3/6
219	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,117.92	776.95	08/2013 -	09/2014	13(O) -	17/26
220	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	-	01/2012 -	-	-	14/28
221	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	6,230.81	4,544.00	10/2012 -	10/2013	-	16/16
222	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	1,823.00	11/2016 -	11/2016	0(O) -	16/17
223	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,454.75	09/2010 -	06/2018	93(O) -	0/0
224	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS - [N18000097]PGCIL,MULTI STATE	08/2010	170.36 -	170.36	-	04/2013 -	12/2013	8(O) -	6/15
225	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,084.04	08/2012 -	03/2014	19(O) -	0/5

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
226	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	-	06/2016 -	04/2015	-14(O) -	0/20
227	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	-	06/2012 -	-	-	0/3
228	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	470.32	12/2014 -	11/2014	-1(O) -	2/2
229	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	24.20	03/2014 -	03/2014	0(O) -	2/7
230	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	226.33	08/2014 -	05/2015	9(O) -	2/19
231	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	937.92	08/2012 -	12/2014	28(O) -	0/11
232	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	571.22	02/2015 -	02/2015	0(O) -	0/14
233	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	484.37	11/2014 -	11/2014	0(O) -	0/16
234	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	-	01/2015 -	01/2015	0(O) -	4/19
235	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	178.53	08/2014 -	08/2014	0(O) -	7/20
236	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	241.34	06/2014 -	09/2014	3(O) -	7/20
237	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	1,949.00	03/2013 -	03/2017	48(O) -	0/13
238	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,424.82	09/2009 -	04/2015	67(O) -	0/4
239	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	557.11	07/2010 02/2016	02/2017	79(O) 12(R)	1/10
240	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	115.07	01/2014 -	03/2015	14(O) -	3/18
241	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	664.72	08/2014 -	06/2015	10(O) -	2/19
242	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,198.22	10/2014 -	06/2015	8(O) -	3/18
243	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,611.92	10/2012 -	03/2015	29(O) -	0/11
244	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	-	11/2011 -	-	-	0/4
245	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,506.60	12/2012 -	03/2015	27(O) -	0/11
246	TRANS. SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	424.04	01/2015 -	12/2015	11(O) -	2/20
247	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,ANDHRA PRADESH	02/2012	324.33 -	324.33	19.51	08/2014 -	08/2014	0(O) -	9/20

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
248	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,ANDHRA PRADESH	02/2012	1,927.16 -	1,927.16	464.64	10/2014 -	10/2014	0(O) -	3/16
249	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016	0(O) -	0/0
250	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	355.82	02/2014 -	02/2014	0(O) -	4/17
251	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	-	10/2013 -	-	-	2/13
252	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,MAHARASHTRA	07/2011	181.93 -	181.93	141.37	07/2013 -	01/2014	6(O) -	0/13
253	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	-	12/2013 -	12/2013	0(O) -	3/13
254	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	214.68	11/2013 -	09/2014	10(O) -	7/20
255	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,340.45	03/2013 -	05/2014	14(O) -	4/15
256	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,162.88	03/2014 -	03/2015	12(O) -	4/15
257	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	1,873.82	12/2013 -	05/2014	5(O) -	0/13
258	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	62.98	01/2013 -	06/2015	29(O) -	5/18
259	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,117.87	11/2013 -	06/2015	19(O) -	5/16
260	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,835.50	11/2012 -	03/2015	28(O) -	0/15
261	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,473.44	07/2014 -	12/2014	5(O) -	2/14
262	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	623.44	691.11	07/2013 -	05/2014	10(O) -	18/25
263	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	913.63 -	913.63	501.56	07/2006 02/2015	02/2015	103(O) 0(R)	1/14
264	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
265	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,JAMMU AND KASHMIR	08/2005	1,729.29 -	2,081.00	2,096.81	11/2009 -	01/2014	50(O) -	1/2
266	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	679.00	08/2015 -	08/2015	0(O) -	13/14
267	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
268	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,422.44	379.49	07/2014 -	05/2016	22(O) -	1/1
269	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	462.22	09/2010 -	-	-	0/5
270	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,245.08	06/2015 -	12/2015	6(O) -	3/28
	Total		249,166.39 -	267,559.81	122,983.17				392/1373
	<u>RAILWAYS</u>								
271	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	184.06	1.85	- -	-	-	0/0
272	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	518.45	03/2014 -	03/2019	60(O) -	0/0
273	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
274	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	394.86	12/2009 03/2011	03/2014	51(O) 36(R)	0/0
275	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	0.17	- -	-	-	0/0
276	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 385.60	1,215.30	40.61	03/2013 -	03/2013	-	0/0
277	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	2,820.00	272.85	- -	-	-	0/0
278	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	17.01	- -	-	-	0/0
279	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
280	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	153.00	-	- -	-	-	0/0
281	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	2,000.00	24.27	- -	-	-	0/0
282	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	485.00	414.94	03/2011 03/2011	03/2011	-	0/0
283	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
284	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	86.14	- -	-	-	0/0
285	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	57.32	- -	03/2017	- -	0/0
286	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.10	725.00	558.06	06/1999 03/2011	03/2011	-	0/0
287	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.67	- -	-	-	0/0
288	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
289	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	123.10	- -	-	-	0/0
290	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
291	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
292	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.94	- -	-	-	0/0
293	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	199.75	31.95	- -	-	-	0/0
294	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	20.40	- -	-	-	0/0
295	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	4.25	- -	-	-	0/0
296	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	187.34	12/2012 -	12/2013	12(O) -	0/0
297	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	901.62	0.61	- -	-	-	0/0
298	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	0.97	- -	-	-	0/0
299	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	483.68	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
300	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	245.15 1,106.62	1,106.62	225.60	12/2010 03/2011	03/2011	-	0/0
301	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	9.99	- -	-	-	0/0
302	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
303	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,512.86	331.31	03/2004 12/2010	12/2014	129(O) 48(R)	0/0
304	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	337.49	0.12	- -	-	-	0/0
305	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	923.23	-	- -	-	-	0/0
306	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
307	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	111.36	04/2014 -	03/2017	35(O) -	0/0
308	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	38.11	- -	-	-	0/0
309	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	193.77	03/2011 -	-	-	0/0
310	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	70.01	- -	-	-	0/0
311	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	739.35	03/2010 -	12/2015	69(O) -	0/0
312	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	484.61	1.89	03/2012 -	-	-	0/0
313	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.67	- -	-	-	0/0
314	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.04	- -	-	-	0/0
315	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	267.37	33.96	- -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
316	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	2,942.62	04/2008 03/2014	12/2017	116(O) 45(R)	0/0
317	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
318	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	44.91	03/2015 -	12/2015	9(O) -	0/0
319	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	2.32	- -	-	-	0/0
320	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	59.62	- -	-	-	0/0
321	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	527.31	- -	-	-	0/0
322	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	92.44	- -	-	-	0/0
323	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	459.92	- -	-	-	0/0
324	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	1.91	- -	-	-	0/0
325	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	494.92	0.18	- -	-	-	0/0
326	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	103.76	- -	-	-	0/0
327	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
328	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
329	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.08	- -	-	-	0/0
330	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	- -	-	-	0/0
331	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	558.00	-	- -	-	-	0/0
332	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	88.77	- -	-	-	0/0
333	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	139.84	- -	-	-	0/0
334	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
335	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	407.98	379.31	- -	03/2014	- -	0/0
336	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	945.82	03/2007 -	03/2017	120(O) -	0/0
337	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	266.48	- -	-	-	0/0
338	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0

Sector Wise Details (Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
339	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	153.80	- -	-	-	0/0
340	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	533.38	101.36	12/2011 02/2012	02/2012	-	0/0
341	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	968.60	132.13	12/2012 -	-	-	0/0
342	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	388.67	56.07	12/2015 -	12/2015	0(O) -	0/0
343	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	406.92	136.18	- -	-	-	0/0
344	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	3.67	- -	-	-	0/0
345	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	366.73	4.20	- -	-	-	0/0
346	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	410.08	235.39	- -	03/2014	- -	0/0
347	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
348	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	142.05	- -	-	-	0/0
349	DEOGHAR - SULTANGANJ (NL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	607.09	516.05	12/2012 12/2012	02/2013	-	0/0
350	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	0.17	- -	-	-	0/0
351	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	1.39	02/2019 -	02/2019	0(O) -	0/0
352	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	651.17	7.08	- -	-	-	0/0
353	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
354	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	914.98	716.15	- -	12/2012	-	0/0
355	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
356	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
357	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	2.06	- -	-	-	0/0
358	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
359	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	224.00	12/2008 -	09/2014	69(O) -	0/0
360	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	259.09	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
361	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
362	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240(O) -	0/0
363	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,117.00	-	- -	-	-	0/0
364	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.09	270.00	287.43	02/2011 02/2011	03/2013	-	0/0
365	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.88	- -	-	-	0/0
366	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	0.94	- -	-	-	0/0
367	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	189.97 611.03	611.03	134.13	12/2011 11/2013	11/2013	-	0/0
368	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	261.70	72.78	02/2006 -	-	-	0/0
369	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	863.23	756.91	- -	03/2012	-	0/0
370	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
371	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	156.65	50.02	- -	-	-	0/0
372	GUDUR-DURGARA JAPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0
373	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	832.00	377.28	- 05/2009	05/2009	-	0/0
374	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 580.83	580.83	578.31	03/1994 -	01/2014	238(O) -	0/0
375	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	2.87	- -	-	-	0/0
376	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.80	02/2020 -	02/2020	0(O) -	0/0
377	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.34	- -	-	-	0/0
378	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	213.01	-	- -	-	-	0/0
379	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	528.65	193.34	- -	-	-	0/0
380	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	0.87	- -	-	-	0/0
381	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	4.34	- -	-	-	0/0
382	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	242.91	- 09/2009	-	-	0/0
383	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	444.18	-	- -	-	-	0/0
384	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
385	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 412.91	412.91	776.70	- -	01/2013	-	0/0
386	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	148.47	- -	03/2014	-	0/0
387	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 829.74	829.74	42.25	03/2015 -	03/2015	0(O) -	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
388	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
389	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	47.34	- -	-	-	0/0
390	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	40.48	- -	-	-	0/0
391	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	31.42 393.46	535.40	179.02	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
392	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
393	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	110.07	- -	-	-	0/0
394	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	0.59	04/2012 -	03/2016	47(O) -	0/0
395	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	313.24	162.82	01/1999 -	-	-	0/0
396	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	653.47	249.80	03/2014 -	03/2014	0(O) -	0/0
397	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	165.65	133.84	- -	-	-	0/0
398	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	847.75	836.79	06/2007 -	06/2007	-	0/0
399	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	1,043.56	722.28	03/2012 08/2012	-	-	0/0
400	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	34.32	- -	-	-	0/0
401	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	740.00	502.36	03/2012 03/2012	12/2012	-	0/0
402	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	1,770.51	03/2011 03/2014	03/2020	108(O) 72(R)	0/0
403	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	2,050.00	92.27	- -	-	-	0/0
404	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	235.05	- -	-	-	0/0
405	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	48.56	- -	-	-	0/0
406	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	2.15	- -	-	-	0/0
407	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	1,708.41	1,524.75	- -	03/2013	-	0/0
408	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
409	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	511.92	- -	03/2014	- -	1/1

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
410	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	800.00	765.59	- -	10/2012	-	0/0
411	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	128.11	12/2012 -	03/2018	63(O) -	0/0
412	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	1,022.64	742.18	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
413	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	146.24	03/2017 -	03/2017	0(O) -	0/0
414	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	1,054.35	0.35	- -	-	-	0/0
415	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	162.87	124.60	- -	-	-	0/0
416	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	262.21	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
417	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	1,995.25	279.43	- -	12/2014	- -	0/0
418	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
419	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	768.87	506.98	- 03/2010	03/2010	-	0/0
420	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	2,957.21	1,700.76	07/2005 -	-	-	0/0
421	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	418.17	187.76	- -	-	-	0/0
422	KONDAPALLI-KOTHAGUDEM - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	723.00	-	- -	-	-	0/0
423	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	341.41	289.97	03/2012 03/2013	03/2013	-	0/0
424	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
425	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,KARNATAKA	04/1995	65.94 302.23	302.23	361.29	- -	12/2012	-	0/0
426	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
427	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
428	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	8.35	- -	-	-	0/0
429	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	406.99	138.80	- -	-	-	0/0
430	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	1,630.97	404.71	05/2008 03/2011	-	-	0/0
431	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,ODISHA	04/1993	100.00 142.98	227.94	231.83	03/2002 -	01/2014	142(O) -	0/0
432	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	32.19	03/2014 -	03/2014	0(O) -	0/0
433	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	364.06	0.11	- -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
434	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,185.44	3,822.52	03/2009 -	03/2017	96(O) -	0/0
435	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,ANDHRA PRADESH	07/1998	125.00 363.26	480.00	0.86	07/2008 -	07/2008	-	0/0
436	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	11.31	- -	-	-	0/0
437	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.15	- -	-	-	0/0
438	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]JER,MULTI STATE	04/2009	493.96 -	493.96	116.77	- -	-	-	0/0
439	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	472.00	185.60	- -	02/2013	-	0/0
440	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]JER,JHARKHAND	04/1995	184.00 900.05	900.05	749.93	12/2011 12/2011	03/2013	-	0/0
441	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,ANDHRA PRADESH	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0
442	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	0.61	- -	03/2016	-	0/0
443	MANSA BHATINDA INCLUDING MM RAMAMNADI-MAURMANDI VIA TALWANDI SABOO NL - [N22000312]NR,PUNJAB	04/2009	396.04 -	396.04	80.52	- -	-	-	0/0
444	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	396.04	80.52	- -	-	-	0/0
445	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	114.01 332.92	477.88	444.46	03/2012 03/2013	03/2013	-	0/0
446	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
447	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	0.08	01/1999 -	-	-	0/0
448	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	965.16	558.08	- -	-	-	0/0
449	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	1,383.45	382.93	- -	-	-	0/0
450	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	377.44	0.33	- -	-	-	0/0
451	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.70	- -	-	-	0/0
452	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	466.48	0.25	01/1999 -	-	-	0/0
453	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
454	MONIGRAM- NIMTITA - [N22000301]JER,MULTI STATE	04/2012	250.93 -	250.93	-	- -	-	-	0/0
455	MOTIHARI-SITAMARHI (NL) - [N22000174]JECR,BIHAR	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
456	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	390.60	1.37	- -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
457	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,220.15	1,413.35	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
458	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	217.40	- -	03/2014	- -	0/0
459	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	194.64	- -	-	-	0/0
460	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	545.64	0.25	- -	-	-	0/0
461	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
462	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.29	- -	-	-	0/0
463	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	169.82	32.10	- -	-	-	0/0
464	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	0.52	- -	-	-	0/0
465	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	883.00	669.19	02/2009 -	03/2012	-	0/0
466	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	1,036.78	358.26	07/2012 -	-	-	0/0
467	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
468	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.92	- -	-	-	0/0
469	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	532.87	42.67	- -	-	-	0/0
470	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	150.86	- -	03/2017	- -	0/0
471	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	242.22	39.52	- -	-	-	0/0
472	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	4,083.02	2.84	- -	-	-	0/0
473	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	168.60	- -	03/2014	- -	0/0
474	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	98.33	- -	03/2016	- -	0/0
475	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	221.42	21.83	- -	-	-	0/0
476	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.17	250.35	- -	03/2015	- -	0/0
477	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
478	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	32.14	- -	03/2017	- -	0/0
479	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	0.51	- -	03/2015	- -	0/0
480	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	1,418.21	1,033.04	- -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
481	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	8.94	03/2015 -	03/2017	24(O) -	0/0
482	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,485.28	12/2008 -	03/2018	111(O) -	0/0
483	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	62.22	03/2014 -	03/2014	0(O) -	0/0
484	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,619.02 -	2,913.51	366.80	03/2016 -	03/2016	0(O) -	0/0
485	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	65.16	03/2016 -	06/2016	3(O) -	0/0
486	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,951.98	225.70	03/2016 -	03/2016	0(O) -	0/0
487	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
488	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
489	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	293.74	139.45	12/2010 12/2010	12/2010	-	0/0
490	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	191.00 -	191.00	198.31	- -	01/2014	- -	0/0
491	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 2,921.00	2,921.00	1,953.38	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
492	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, ANDHRA PRADESH	12/1994	124.43 495.68	925.30	639.35	- -	02/2014	- -	0/0
493	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	203.00 -	203.00	164.54	- -	03/2014	- -	0/0
494	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	15.18	- -	-	-	0/0
495	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
496	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	8.96	03/2015 -	03/2015	0(O) -	0/0
497	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.26	03/2017 -	03/2017	0(O) -	0/0
498	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
499	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
500	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	791.40	01/1999 -	-	-	0/0
501	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 842.35	1,122.00	823.85	- -	03/2013	-	0/6
502	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	264.93	12/2007 03/2010	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
503	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,229.17	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
504	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	287.33	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
505	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	913.48	461.76	- -	-	-	0/0
506	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	567.66	03/2013 -	03/2014	12(O) -	0/0
507	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	1,225.90	225.81	- -	-	-	0/0
508	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.90	355.23	06/2004 -	12/2014	126(O) -	0/0
509	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	3,019.17	2,415.63	- -	03/2015	- -	0/0
510	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	-	- -	-	-	0/0
511	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	784.34	- -	-	-	0/0
512	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	13.07	- -	-	-	0/0
513	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 603.04	1,421.25	282.18	03/2012 -	-	-	0/0
514	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	970.34	234.39	- -	-	-	0/0
515	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	287.00	1.01	- -	-	-	0/0
516	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	6.83	- 12/2017	12/2017	- 0(R)	0/0
517	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	14.04	- -	-	-	0/0
518	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	233.40	- -	-	-	0/0
519	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	365.77	- -	-	-	0/0
520	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
521	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.83	- -	-	-	0/0
522	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	64.07	12/2015 -	03/2017	15(O) -	0/0
523	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	562.74	0.58	- -	-	-	0/0
524	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	15.85	- -	-	-	0/0
525	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.81	- -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
526	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	40.63	- -	-	-	0/0
527	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	296.00	-	- -	-	-	0/0
528	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	839.00	0.01	- -	-	-	0/0
529	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	-	02/2015 -	02/2015	0(O) -	0/0
530	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.97	- -	-	-	0/0
531	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 516.23	516.23	446.14	03/2014 -	03/2014	0(O) -	0/0
532	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	810.78	128.52	- -	-	-	0/0
533	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.47	448.82	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
534	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	126.82	06/2013 -	06/2014	12(O) -	0/0
535	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.39	- -	-	-	0/0
536	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	157.96 1,188.91	1,188.91	647.53	- 12/2009	02/2012	-	0/0
537	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	236.93	-	- -	-	-	0/0
538	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	820.00	183.93	- -	-	-	0/0
539	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	420.00	59.66	- -	-	-	0/0
540	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	167.73	62.89	03/2012 -	02/2013	-	0/0
541	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	900.00	556.59	- -	-	-	0/0
542	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRT, WEST BENGAL	03/2000	907.69 3,156.32	3,176.10	3,468.31	12/2006 08/2010	08/2010	-	0/0
543	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	0.52	- -	-	-	0/0
544	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181(O) -	0/0
545	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	707.00	03/2014 -	03/2014	0(O) -	0/0
546	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	0.36	- -	-	-	0/0
547	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 325.00	1,116.53	245.54	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
548	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
549	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 356.87	548.01	200.24	- 03/2010	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
550	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	31.12	-	-	-	0/0
551	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	121.85	-	04/2014	-	0/0
552	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	1,604.00	46.18	-	-	-	0/0
553	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	2.38	-	-	-	0/0
554	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.27	-	-	-	0/0
555	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	-	-	-	0/0
	Total		149,113.53 -	265,521.61	77,081.07				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
556	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	329.89	08/2013 -	-	-	0/0
557	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
558	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	268.96	10/2014 -	10/2014	0(O) -	0/0
559	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	42.12	07/2014 -	07/2014	0(O) -	0/0
560	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	394.61	05/2013 -	-	-	0/0
561	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	647.94	11/2013 -	-	-	0/0
562	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	407.92	04/2014 -	04/2014	0(O) -	0/0
563	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	908.44	10/2014 -	10/2014	0(O) -	0/0
564	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	3.26	07/2014 -	07/2014	0(O) -	0/0
565	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	100.21	01/2014 -	01/2014	0(O) -	0/0
566	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	332.50	02/2014 -	02/2014	0(O) -	0/0
567	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	611.24	02/2014 -	02/2014	0(O) -	0/0
568	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014	0(O) -	0/0
569	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	161.49	05/2014 -	05/2014	0(O) -	0/0
570	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	558.46	09/2014 -	09/2014	0(O) -	0/0
571	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,424.72	08/2014 -	08/2014	0(O) -	0/0
572	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	-	06/2013 -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
573	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.40	09/2013 -	07/2014	10(O) -	0/0
574	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	-	08/2013 -	-	-	0/0
575	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	454.33	02/2014 -	02/2014	0(O) -	0/0
576	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,324.51	08/2013 -	-	-	0/0
577	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,388.00	08/2013 -	-	-	0/0
578	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	301.97	08/2013 -	-	-	0/0
579	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	714.59	07/2013 -	-	-	0/0
580	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,113.79	09/2014 -	09/2014	0(O) -	0/0
581	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	385.15	259.40	09/2007 07/2011	-	-	0/0
582	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015	0(O) -	0/0
583	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,161.40	11/2012 -	-	-	0/0
584	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	-	0/0
585	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,CHHATISGARH	03/2005	190.00 -	190.00	264.65	01/2009 -	-	-	0/0
586	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,ODISHA	04/2000	228.70 -	228.70	194.51	02/2004 -	11/2013	-	0/0
587	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	361.07	09/2013 -	-	-	0/0
588	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.56	02/2015 -	02/2015	0(O) -	0/0
589	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	1,725.30	06/2014 -	06/2014	0(O) -	0/0
590	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	597.22	-	-	-	2/2
591	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	36.47	01/2013 -	-	-	0/0
592	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	528.15	08/2013 -	-	-	0/0
593	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	291.11	06/2008 -	-	-	0/0
594	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	260.88	06/2008 -	-	-	0/0
595	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	239.93	06/2005 -	-	-	0/0
596	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	306.32	04/2010 09/2015	09/2015	65(O) 0(R)	0/0
597	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.06	02/2010 -	-	-	0/0
598	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	856.01	03/2013 -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
599	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.24	10/2011 -	-	-	0/0
600	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.91	10/2011 -	-	-	0/0
601	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,KARNATAKA	03/2011	839.00 -	839.00	825.42	- -	-	-	0/1
602	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	-	-	0/0
603	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	181.32	10/2008 -	-	-	0/0
604	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	334.61	04/2015 -	04/2015	0(O) -	0/0
605	DELHI HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.01	05/2010 -	03/2014	46(O) -	0/0
606	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	621.67	07/2013 -	-	-	0/0
607	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	294.35	06/2013 -	-	-	0/0
608	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	723.34	- -	-	-	1/1
609	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	-	06/2008 -	03/2014	69(O) -	0/0
610	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	209.92	05/2008 07/2014	07/2014	74(O) 0(R)	0/0
611	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	308.77	09/2010 -	-	-	0/0
612	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	20.71	09/2015 -	09/2015	0(O) -	0/0
613	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	487.69	09/2008 -	-	-	0/0
614	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015	0(O) -	0/0
615	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR, NAGPUR BYPASS - [N24000124]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30(O) -	0/0
616	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	226.29	10/2013 -	03/2014	5(O) -	0/0
617	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	150.62	09/2008 -	-	-	0/0
618	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,ODISHA	04/2000	263.27 -	263.27	276.46	02/2004 -	09/2013	-	0/0
619	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	1,294.08	08/2013 06/2014	06/2014	10(O) 0(R)	0/0
620	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,229.79	09/2012 -	-	-	0/0
621	GURGAON-KOTPUTLI KM 42.70 TO 54.4 KM - [N24000130]NHAI,MULTI STATE	04/2009	1,673.70 -	1,673.70	2,866.54	10/2011 -	-	-	0/0
622	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	306.31	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
623	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	249.37	04/2008 03/2014	03/2014	71(O) 0(R)	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
624	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	-	-	0/0
625	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,UTTAR PRADESH	03/2005	220.00 -	220.00	-	09/2007 -	11/2013	-	0/0
626	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	339.45	02/2009 -	05/2014	63(O) -	0/0
627	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57(O) -	0/0
628	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	73.71	09/2007 -	05/2014	80(O) -	0/0
629	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	308.49	10/2013 -	03/2014	5(O) -	0/0
630	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,KARNATAKA	04/2000	318.00 -	207.56	196.57	08/2004 -	10/2013	-	0/0
631	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,KARNATAKA	04/2000	241.00 -	196.65	-	08/2004 -	10/2013	-	0/0
632	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	948.41	01/2013 -	-	-	0/0
633	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	1,842.77	- -	-	-	3/3
634	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	548.40	05/2013 -	-	-	0/0
635	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	-	-	0/0
636	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	683.48	02/2013 -	-	-	0/0
637	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,979.78	12/2012 -	-	-	0/0
638	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	822.18	07/2013 -	-	-	0/0
639	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,UTTAR PRADESH	12/2003	355.06 -	355.06	507.99	09/2009 -	-	-	0/0
640	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	554.09	01/2014 -	01/2014	0(O) -	0/0
641	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	711.11	07/2013 -	-	-	0/0
642	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,127.12	05/2012 -	-	-	0/0
643	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	281.66	10/2008 -	-	-	0/0
644	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,BIHAR	12/2003	240.00 -	240.00	295.42	10/2008 -	-	-	0/0
645	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	588.54	07/2014 -	07/2014	0(O) -	0/0
646	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	938.40	- -	06/2014	-	2/3
647	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,MADHYA PRADESH	12/2003	407.60 -	407.60	186.77	06/2010 -	-	-	0/0
648	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,MADHYA PRADESH	12/2003	263.17 -	263.17	235.19	09/2009 -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
649	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	320.70	07/2012 -	-	-	0/0
650	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	241.28	146.70	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
651	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 382.02	382.02	101.21	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
652	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 265.53	265.63	87.03	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
653	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 247.43	247.43	177.70	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
654	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	1,936.00	06/2013 -	-	-	0/0
655	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	517.00	03/2013 -	-	-	0/0
656	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	03/2014	69(O) -	0/0
657	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,MAHARASHTRA	03/2005	168.00 -	168.00	457.30	12/2008 -	-	-	0/0
658	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	283.09	10/2014 -	10/2014	0(O) -	0/0
659	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	313.93	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
660	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	269.79	06/2008 05/2014	05/2014	71(O) 0(R)	0/0
661	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	308.16	06/2008 -	-	-	0/0
662	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	240.31	06/2015 -	06/2015	0(O) -	0/0
663	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	524.67	09/2013 -	-	-	0/0
664	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,KARNATAKA	04/2000	196.50 -	196.50	290.41	06/2011 -	-	-	0/2
665	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,129.29	02/2010 -	-	-	0/0
666	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	01/2014	0(O) -	0/0
667	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	153.76	09/2014 -	09/2014	0(O) -	0/0
668	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	-	-	0/0
669	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,325.75	10/2014 -	12/2013	-10(O) -	0/0
670	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	263.68	06/2014 -	06/2014	0(O) -	0/0
671	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,PUNJAB	12/2003	284.00 -	359.00	350.70	05/2008 -	-	-	0/0
672	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	662.29	03/2014 -	03/2014	0(O) -	0/0
673	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	-	-	0/0
674	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,333.25	07/2012 -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
675	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,206.67	03/2013 -	-	-	0/0
676	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	394.31	01/2014 -	01/2014	0(O) -	0/0
677	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	-	-	0/0
678	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,004.65	07/2015 -	07/2015	0(O) -	0/0
679	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	345.30	10/2008 -	-	-	0/0
680	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	248.77	06/2015 -	06/2015	0(O) -	0/0
681	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	256.68	09/2014 -	09/2014	0(O) -	0/0
682	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,153.77	11/2013 -	01/2014	2(O) -	0/0
683	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,TAMIL NADU	03/2005	941.00 -	941.00	-	01/2011 -	09/2013	-	0/0
684	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	778.50	03/2013 -	-	-	0/0
685	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	958.69	05/2014 -	05/2014	0(O) -	0/0
686	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 148.22	157.47	260.30	09/2007 03/2014	12/2013	75(O) -3(R)	0/0
687	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.45	07/2008 -	-	-	0/0
688	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	233.48	06/2014 -	06/2014	0(O) -	0/0
689	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	12/2013	0(O) -	0/0
690	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,117.37	12/2013 -	12/2013	0(O) -	0/0
691	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014	0(O) -	0/0
692	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	154.50	08/2012 -	-	-	0/0
693	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015	82(O) 0(R)	0/0
694	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	-	-	0/0
695	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,ODISHA	04/2000	225.00 -	241.53	-	04/2004 -	10/2013	-	0/0
696	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,760.57	08/2011 -	-	-	0/0
697	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,260.86	11/2013 -	-	-	0/0
698	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,TAMIL NADU	03/2005	280.00 -	280.00	581.50	06/2009 -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
699	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	571.00	-	10/2013 -	-	-	0/0
700	TRICHY - KORUR NH-67 - [N24000101]NHAI,TAMIL NADU	03/2005	516.00 -	516.00	866.86	07/2010 -	-	-	0/0
701	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	124.73	05/2013 -	-	-	0/0
702	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	366.60	-	-	-	2/2
703	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	930.16	03/2014 -	03/2014	0(O) -	0/0
704	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	193.10	198.80	03/2008 -	-	-	0/0
705	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	56.65	11/2012 -	-	-	0/0
706	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	0(O) -	0/0
707	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	-	-	-	0/0
	Total		106,312.42 -	108,365.22	86,173.46				10/14
	<u>SHIPPING AND PORTS</u>								
708	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	358.78	04/2011 11/2011	11/2011	-	0/0
709	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
710	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	-	0/0
711	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
712	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
713	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	363.20	02/2014 02/2014	02/2014	0(O) 0(R)	0/0
714	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0
715	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	1,429.10	984.19	12/2010 09/2012	03/2015	51(O) 30(R)	0/0
716	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
717	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
718	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
719	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
720	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99(O) 0(R)	0/0
721	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
722	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
723	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
724	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	832.04	10/2008 11/2010	-	-	0/0
725	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0
726	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	17,871.52	8,722.60				0/1
	TELECOMMUNICATIONS								
727	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	170.57	01/2009 -	12/2013	59(O) -	0/0
728	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41(O) 24(R)	0/0
729	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	-	0/0
730	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	336.84	-	10/2009 -	-	-	0/0
731	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.48	06/2009 -	12/2013	54(O) -	0/0
732	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
733	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
734	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEAPON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0

Sector Wise Details

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
735	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
736	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	246.51	05/2011 -	12/2013	31(O) -	0/0
	Total		5,079.29 -	4,982.94	1,751.97				0/0
	<u>URBAN DEVELOPMENT</u>								
737	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
738	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
739	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,595.00 -	38,595.00	6,061.33	03/2016 -	03/2016	0(O) -	0/0
740	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	490.82	09/2014 -	05/2015	8(O) -	0/0
	Total		47,598.18 -	52,871.08	8,819.72				3/3
	<u>WATER RESOURCES</u>								
741	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		912,557.61	1,092,632.33	516,627.39				1090/3636

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

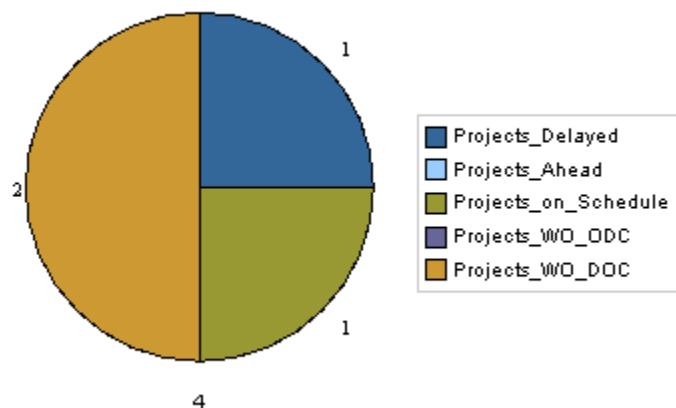

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 47598.18 crore but this was subsequently revised to Rs. 52871.08 crore implying a cost overrun of 11.1%. The expenditure incurred on these projects till December, 2013 is Rs. 8819.72 crore, which is 16.7% of the revised cost of the projects.

Figures are in Rs. Crore

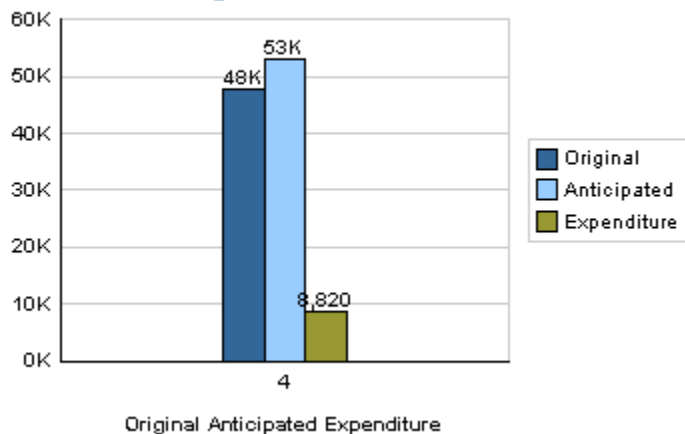

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	10
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	6

Brief Analysis


Project Status with respect to Original Schedule: Out of 10 projects, 4 projects are delayed .6 projects do not have fixed dates of commissioning.

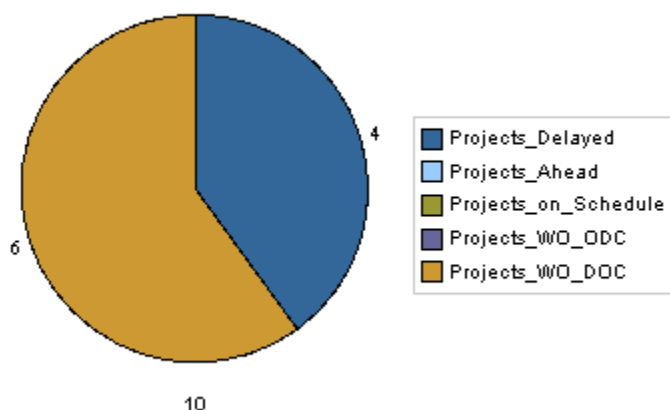

Investment Scenario

The Total Original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 5079.29 crore but this was subsequently revised to Rs. 4982.94 crore implying a cost overrun of -1.9%. The expenditure incurred on these projects till December, 2013 is Rs. 1751.97 crore, which is 35.2% of the revised cost of the projects.

Figures are in Rs. Crore

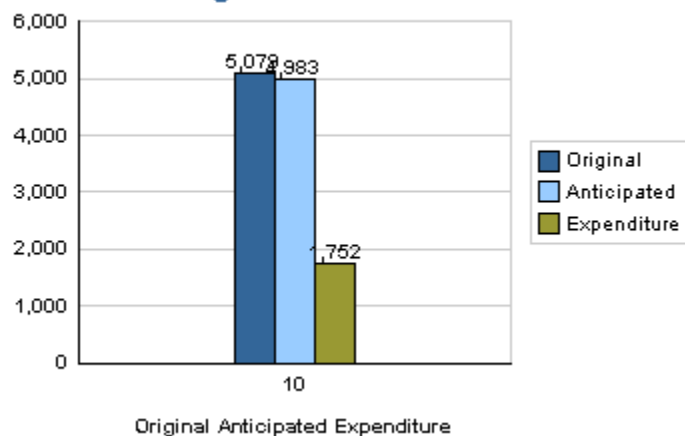

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning 15

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are on schedule and 3 projects are delayed .15 projects do not have fixed dates of commissioning.

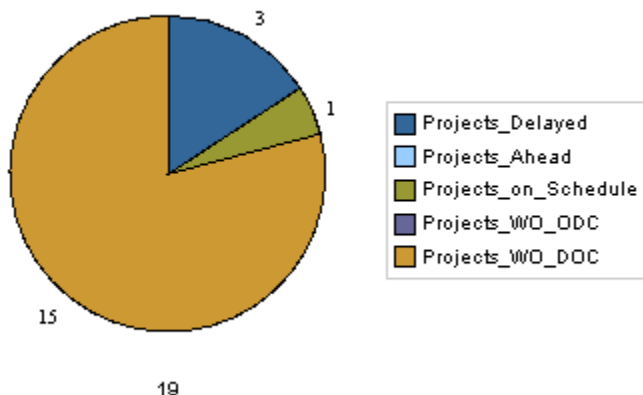

Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17871.52 crore implying a cost overrun of 14.4%. The expenditure incurred on these projects till December, 2013 is Rs. 8722.6 crore, which is 48.8% of the revised cost of the projects.

Figures are in Rs. Crore

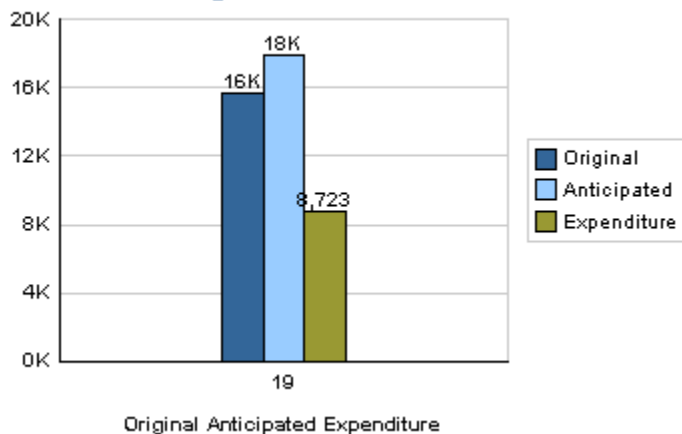

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHW

Current Status:

Number of Projects	152
Number of Projects On Schedule	39
Number of Projects Delayed	24
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	87

Brief Analysis


Project Status with respect to Original Schedule: Out of 152 projects, 1 project are ahead of schedule, 39 projects are on schedule and 24 projects are delayed .87 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

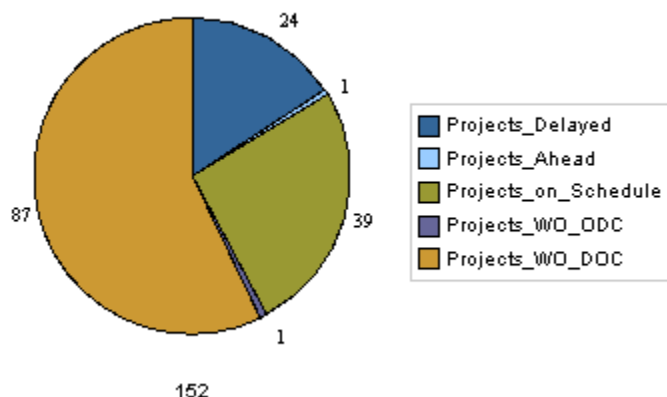

Investment Scenario

The Total Original cost of implementation of 152 projects when sanctioned, was of the order of Rs. 106312.42 crore but this was subsequently revised to Rs. 108365.22 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till December, 2013 is Rs. 86173.46 crore, which is 79.5% of the revised cost of the projects.

Figures are in Rs. Crore

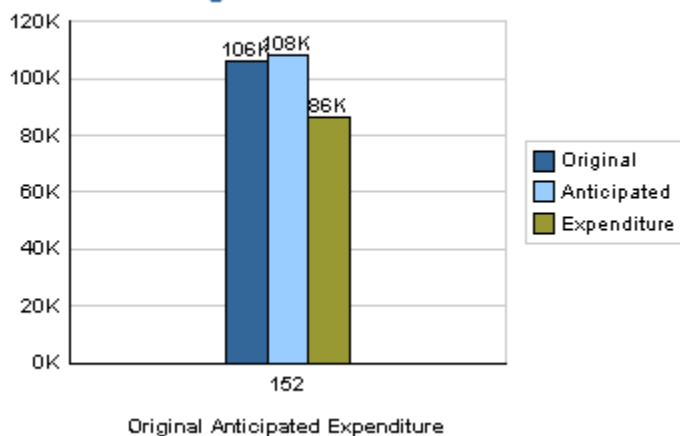

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	285
Number of Projects On Schedule	16
Number of Projects Delayed	37

Number of Projects Without Original Date of Commissioning	22
Number of Projects Without Date Of Commissioning	210

Brief Analysis


Project Status with respect to Original Schedule: Out of 285 projects, 16 projects are on schedule and 37 projects are delayed .210 projects do not have fixed dates of commissioning.22 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

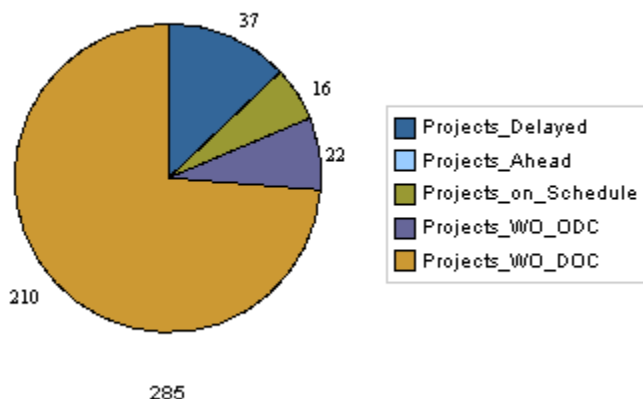

Investment Scenario

The Total Original cost of implementation of 285 projects when sanctioned, was of the order of Rs. 149113.53 crore but this was subsequently revised to Rs. 265521.61 crore implying a cost overrun of 78.1%. The expenditure incurred on these projects till December, 2013 is Rs. 77081.07 crore, which is 29% of the revised cost of the projects.

Figures are in Rs. Crore

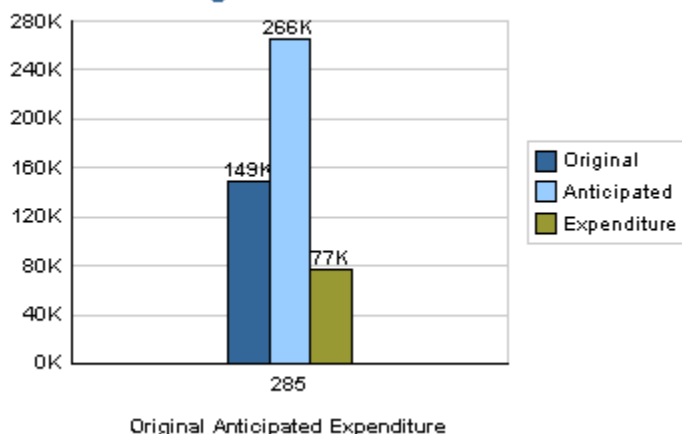

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	100
Number of Projects On Schedule	35
Number of Projects Delayed	51
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	12

Brief Analysis


Project Status with respect to Original Schedule: Out of 100 projects, 2 projects are ahead of schedule, 35 projects are on schedule and 51 projects are delayed .12 projects do not have fixed dates of commissioning.

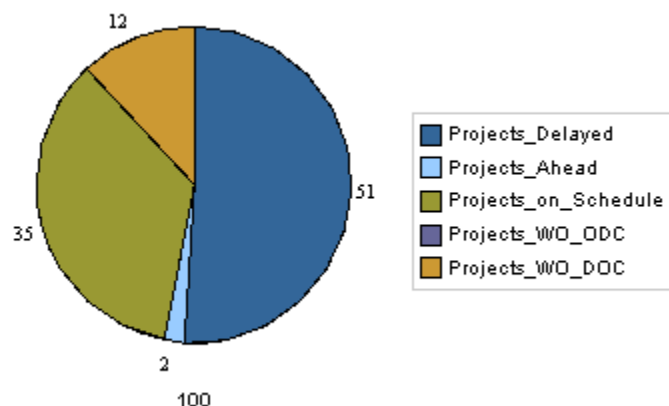

Investment Scenario

The Total Original cost of implementation of 100 projects when sanctioned, was of the order of Rs. 249166.39 crore but this was subsequently revised to Rs. 267559.81 crore implying a cost overrun of 7.4%. The expenditure incurred on these projects till December, 2013 is Rs. 122983.17 crore, which is 46% of the revised cost of the projects.

Figures are in Rs. Crore

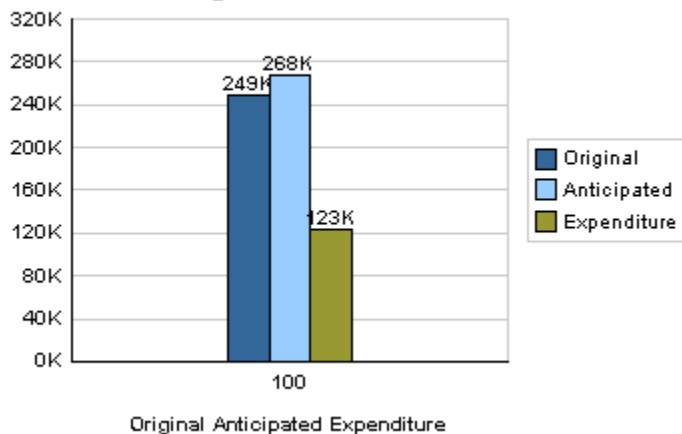

Sector wise current status of projects on the Flash Report

PETROLEUM


Current Status:

Number of Projects	82
Number of Projects On Schedule	18
Number of Projects Delayed	56

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7

Brief Analysis


Project Status with respect to Original Schedule: Out of 82 projects, 18 projects are on schedule and 56 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

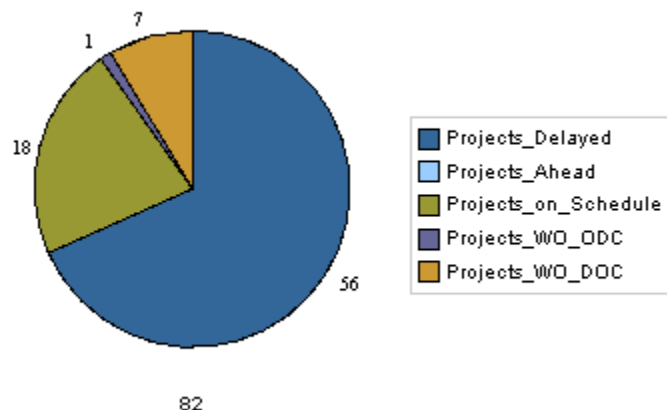

Investment Scenario

The Total Original cost of implementation of 82 projects when sanctioned, was of the order of Rs. 183103.4 crore but this was subsequently revised to Rs. 197993.73 crore implying a cost overrun of 8.1%. The expenditure incurred on these projects till December, 2013 is Rs. 100971.49 crore, which is 51% of the revised cost of the projects.

Figures are in Rs. Crore

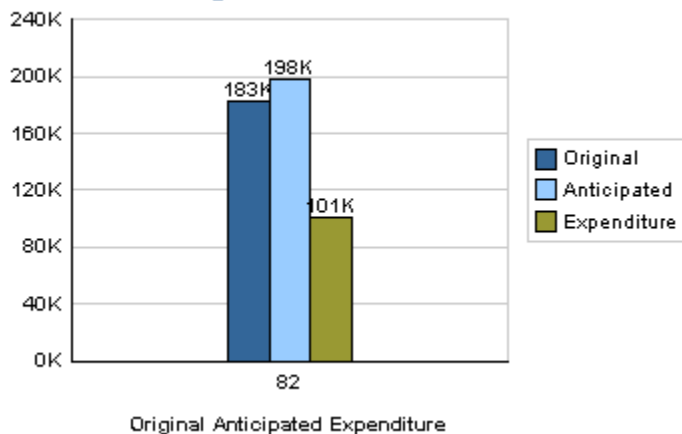

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	20
Number of Projects On Schedule	4
Number of Projects Delayed	13
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 1 project are ahead of schedule, 4 projects are on schedule and 13 projects are delayed .2 projects do not have fixed dates of commissioning.

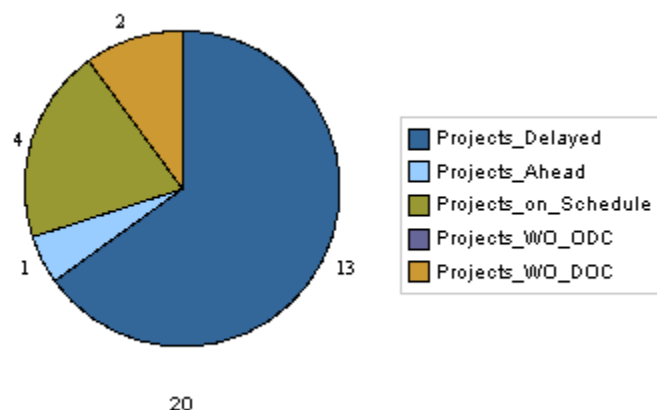

Investment Scenario

The Total Original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 65959.26 crore but this was subsequently revised to Rs. 72162.25 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till December, 2013 is Rs. 56685.8 crore, which is 78.6% of the revised cost of the projects.

Figures are in Rs. Crore

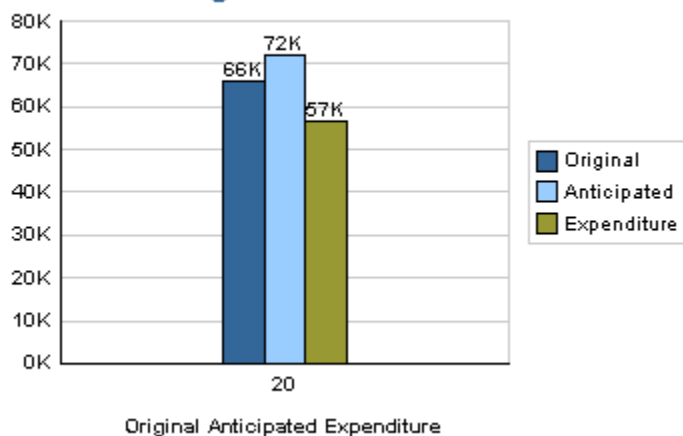

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	55
Number of Projects On Schedule	22
Number of Projects Delayed	27

Number of Projects Without Date Of Commissioning 6

Brief Analysis


Project Status with respect to Original Schedule: Out of 55 projects, 22 projects are on schedule and 27 projects are delayed .6 projects do not have fixed dates of commissioning.

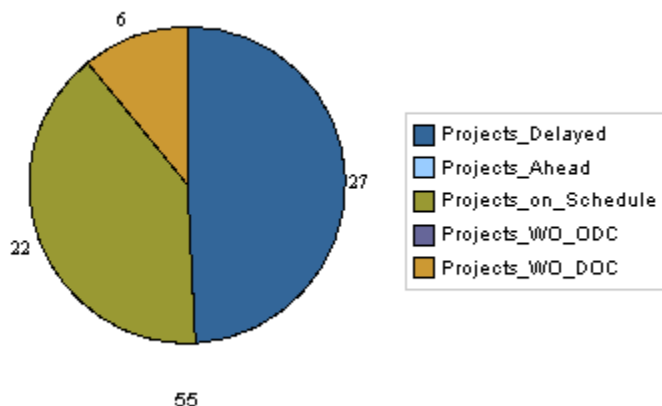

Investment Scenario

The Total Original cost of implementation of 55 projects when sanctioned, was of the order of Rs. 38127.05 crore but this was subsequently revised to Rs. 41525.17 crore implying a cost overrun of 8.9%. The expenditure incurred on these projects till December, 2013 is Rs. 16992.15 crore, which is 40.9% of the revised cost of the projects.

Figures are in Rs. Crore

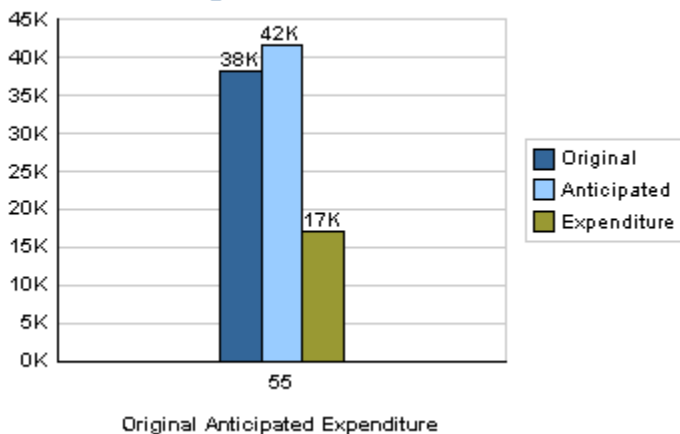

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule and 2 projects are delayed .4 projects do not have fixed dates of commissioning.

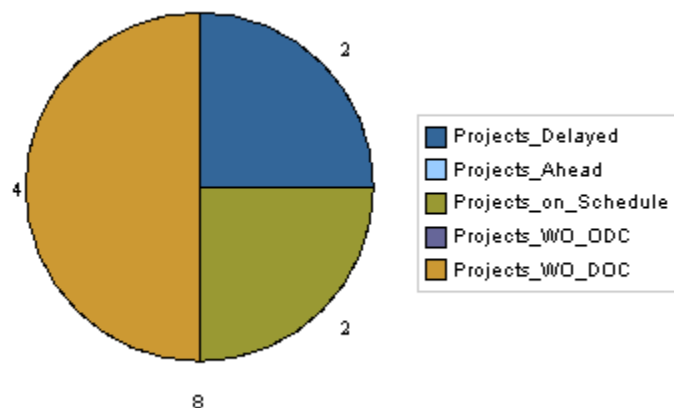

Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6946 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till December, 2013 is Rs. 5541.8 crore, which is 79.8% of the revised cost of the projects.

Figures are in Rs. Crore

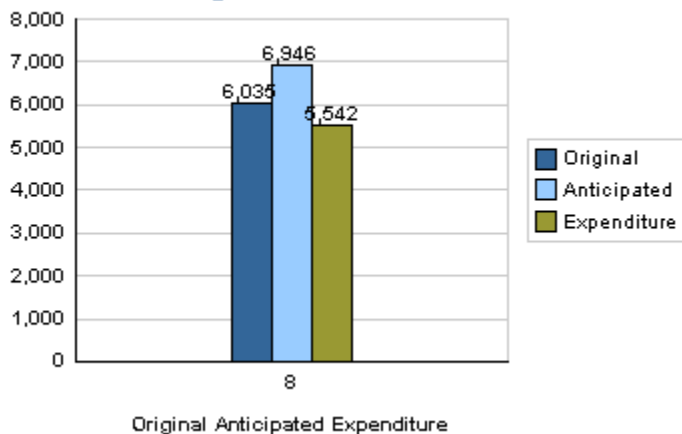

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

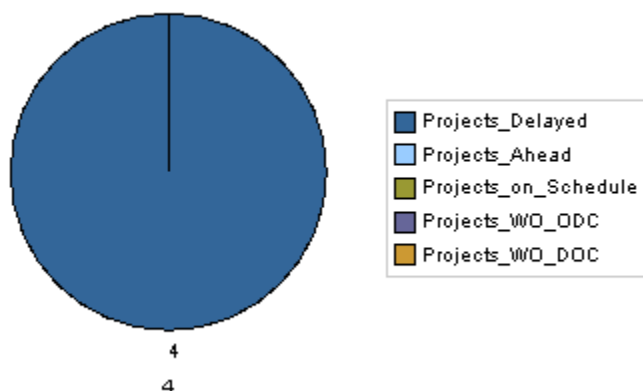

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till December, 2013 is Rs. 26358.16 crore, which is 56.4% of the revised cost of the projects.

Figures are in Rs. Crore

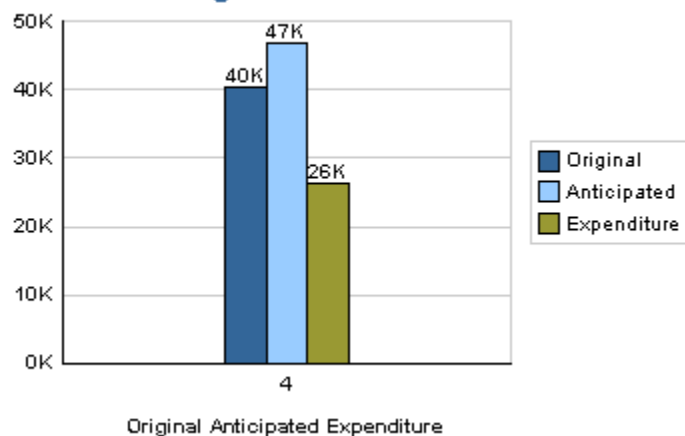

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDHRA PRADESH	46	36,933.79	45,110.39	23,662.47
2	ARUNACHAL PRADESH	4	9,512.22	17,331.9	10,235.42
3	ASSAM	41	24,155.49	39,221.81	25,879.85
4	BIHAR	46	32,579.04	40,999.96	29,207.76
5	CHANDIGARH	1	452	452	190.3
6	CHHATISGARH	24	58,278.32	59,362.92	20,984.11
7	DELHI	4	41,543.88	41,541.33	6,602.84
8	GOA	1	335.61	388.53	260.78
9	GUJARAT	33	38,022.74	39,924.34	12,403.85
10	HARYANA	9	4,399.88	6,104.07	7,221.92
11	HIMACHAL PRADESH	5	13,845.21	19,510.58	11,757.95
12	JAMMU AND KASHMIR	8	13,694.69	32,976.56	16,456.5
13	JHARKHAND	27	16,118.82	20,384.09	10,549.35
14	KARNATAKA	36	53,708.59	65,661.84	27,804.05
15	KERALA	11	22,003.59	24,528.37	7,809.07
16	MADHYA PRADESH	21	31,448.2	32,674.58	10,468.86
17	MAHARASHTRA	56	97,971.05	1,11,407.87	53,076.01
18	MANIPUR	1	727.56	5,996	1,770.51
19	MEGHALAYA	3	4,845.02	4,845.02	889.43
20	MIZORAM	2	1,532.97	3,307.11	612.92
21	MULTI STATE	176	1,83,255.26	2,06,983.09	84,837.66
22	NAGALAND	2	5,124	6,720.57	8.94
23	ODISHA	32	56,606.01	63,334.57	42,856.96
24	PUNJAB	6	2,360.24	2,435.24	2,902.26
25	RAJASTHAN	25	25,380.48	25,805.94	11,364.27
26	SIKKIM	2	1,648.94	3,684.88	308.73
27	TAMIL NADU	41	53,479.73	69,711.43	45,545.47
28	TRIPURA	6	2,966.26	4,409.22	2,359.95
29	UTTAR PRADESH	30	21,932.85	26,529.06	14,139.22
30	UTTARAKHAND	6	7,844.04	9,876.64	2,834.49
31	WEST BENGAL	36	49,851.13	61,412.42	31,625.49
TOTAL		741	9,12,557.61	10,92,632.33	5,16,627.39

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	16,485
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	4,666.16
3	IOR LAKWA - LAKHMANI (ONGCL)	PETROLEUM	09/2001	345.1	663.69	743.72
4	IOR GELEKI (ONGCL)	PETROLEUM	09/2001	390.09	1674.11	1,759.52
5	IOR, RUDRASAGAR (ONGCL)	PETROLEUM	09/2001	113.9	438.85	452.91
6	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,187.29
7	KOLDAM HEP (NTPC)	POWER	10/2002	4,527.15	-	5,285
8	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,454.75
9	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	2,624.41
10	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	8,976
11	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,424.82
12	URI H.E.P STAGE -II (NHPC)	POWER	08/2005	1,729.29	-	2,096.81
13	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	639.35
14	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	2500	8,822.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	LANJHIGARH- JUNAGARH NL(ECOR)	RAILWAYS	04/1993	100	142.98	231.83
16	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
17	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	412.91	776.7
18	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	155	765.59
19	NANDYAL-YERRAGUNTALA(NL), SCR	RAILWAYS	03/1996	155.74	429.49	669.19
20	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,000	1500	2,942.62
21	KOTTUR-HARIHAR(NL), (SWR)	RAILWAYS	04/1995	65.94	302.23	361.29
22	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	194.07	355.23
23	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	233	501.69	722.28
24	KATI HAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	100	492.98	742.18
25	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	377.28
26	JALANDHAR-PATHANKOT- JAMMU-TAWI (LD), NR	RAILWAYS	03/2002	409	625.3	836.79
27	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	100	556.59
28	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,485.28

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	907.69	3156.32	3,468.31
30	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	228.09	287.43
31	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	190.81	238.56	502.36
32	RAJATGARH-BARANG(LD), ECR	RAILWAYS	04/1999	166.16	-	287.33
33	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.53	1,770.51
34	DANIAWAN-BIHARSARIF (NL), ECR	RAILWAYS	04/2001	104.79	-	136.18
35	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	2,415.63
36	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	262.21
37	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	264.93
38	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	148.22	260.3
39	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	239.93
40	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	ROAD TRANSPORT AND HIGHWAYS	12/2003	166.27	-	198.8
41	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A	ROAD TRANSPORT AND HIGHWAYS	12/2003	284	-	350.7
42	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402	ROAD TRANSPORT AND HIGHWAYS	12/2003	240	-	295.42

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	ROAD TRANSPORT AND HIGHWAYS	03/2005	190	-	264.65
44	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	260.88
45	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	291.11
46	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	487.69
47	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	281.66
48	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	345.3
49	C/O INTEGRATED PASSENGER TER.BULD. NSCBI AIRPORT	CIVIL AVIATION	08/2008	1,942.51	2325	2,476.01
50	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	15,451.6
51	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	PETROLEUM	07/2009	238.68	-	293.12
52	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	PETROLEUM	04/2008	825	-	1,488.84
53	MOUNDED BULLET PROJECT AT CPCL	PETROLEUM	12/2012	279	-	283.87
54	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	-	776.95
55	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	-	691.11
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	114.01	332.92	444.46

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	739.35
58	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	343.17	716.15
59	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	170	414.94
60	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	RAILWAYS	09/1996	156	156	379.31
61	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	482.7	567.66
62	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	1676.31	3,822.52
63	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	461.76
64	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	558.08
65	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	784.34
66	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	233.4
67	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	266.48
68	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	459.92
69	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	945.82
70	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	527.31

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	1,033.04
72	PANVEL PEN DOUBLING	RAILWAYS	04/2006	191	-	198.31
73	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	194.64
74	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	791.4
75	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	308.16
76	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	249.37
77	NEW MANGALORE PORT NH-17 AND 48	ROAD TRANSPORT AND HIGHWAYS	04/2000	196.5	-	290.41
78	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
79	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	306.31
80	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	269.79
81	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	-	313.93
82	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	209.92
83	NAGPUR-KONDHALI, NH-6(NHAI)	ROAD TRANSPORT AND HIGHWAYS	03/2005	168	-	457.3
84	THANJAUR-TRICHY, NH-67(NHAI)	ROAD TRANSPORT AND HIGHWAYS	03/2005	280	-	581.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	GANJAM-ICCHAPURUM, NH-5(NHAI)	ROAD TRANSPORT AND HIGHWAYS	04/2000	263.27	-	276.46
86	JHANSI TO LALITPUR, NH-25, 26	ROAD TRANSPORT AND HIGHWAYS	12/2003	355.06	-	507.99
87	TRICHY - KORUR NH-67	ROAD TRANSPORT AND HIGHWAYS	03/2005	516	-	866.86
88	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,129.29
89	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	308.77
90	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	661.01
91	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,333.25
92	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,229.79
93	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,802
94	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,127.12
95	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.24
96	GURGAON-KOTPUTLI KM 42.70 TO 54.4 KM	ROAD TRANSPORT AND HIGHWAYS	04/2009	1,673.7	-	2,866.54
97	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,760.57
98	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.91

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
100	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,979.78
101	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	ROAD TRANSPORT AND HIGHWAYS	09/2010	946	-	1,842.77
102	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,260.86
103	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	948.41
104	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	772.4
105	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	856.01
106	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	938.4
107	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,161.4
108	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	621.67
109	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,325.75
110	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	723.34
111	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	1,936
112	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	597.22

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	548.4
114	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	394.61
115	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,153.77
116	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	1141	1,294.08
117	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	554.09
118	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	332.5
119	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	662.29
120	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	714.59
121	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	647.94
122	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	454.33
123	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	528.15
124	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	958.69
125	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	683.48
126	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,388

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,324.51
128	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	268.96
129	ACQUISITION OF TWO NOS. OF 3060 DWT	SHIPPING AND PORTS	04/2009	277.03	280	294.87
130	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

List of Projects Ahead of Schedule w.r.t. Original Schedule

							(Dec,2013)
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
1	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082	10/2012	160.48	160.48	-	09/2017 -	09/2014
	Total		160.48 -	160.48	.00		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74	1,508.74	-	06/2016 -	04/2015
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	470.32	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	470.32		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,325.75	10/2014 -	12/2013
	Total		807.00 -	807.00	1,325.75		
	Grand Total		4,411.57	4,411.57	1,796.07		

List of projects without Original Date of Commissioning

(Dec,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	0.04	- -	04/2015	-	0/0
	Total		10,281.00 -	10,281.00	.04				0/0
	<u>RAILWAYS</u>								
2	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
3	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	191.00	198.31	- -	01/2014	-	0/0
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,ANDHRA PRADESH	12/1994	124.43 495.68	925.30	639.35	- -	02/2014	-	0/0
5	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	410.08	235.39	- -	03/2014	-	0/0
6	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	217.40	- -	03/2014	-	0/0
7	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	511.92	- -	03/2014	-	0/1
8	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	148.47	- -	03/2014	-	0/0
9	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	407.98	379.31	- -	03/2014	-	0/0
10	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	168.60	- -	03/2014	-	0/0
11	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	203.00	164.54	- -	03/2014	-	0/0
12	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	121.85	- -	04/2014	-	0/0
13	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	1,995.25	279.43	- -	12/2014	-	0/0
14	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.17	250.35	- -	03/2015	-	0/0
15	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	3,019.17	2,415.63	- -	03/2015	-	0/0
16	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
17	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	0.51	- -	03/2015	-	0/0

(Dec,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	0.61	- -	03/2016	-	0/0
19	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	98.33	- -	03/2016	-	0/0
20	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	150.86	- -	03/2017	-	0/0
21	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	32.14	- -	03/2017	-	0/0
22	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	57.32	- -	03/2017	-	0/0
23	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	6.83	- 12/2017	12/2017	0(R3)	0/0
	Total		6,246.62 -	13,397.22	6,273.28				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
24	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	938.40	- -	06/2014	-	2/3
	Total		671.00 -	671.00	938.40				2/3
	Grand Total		17,198.62	24,349.22	7,211.72				2/4

List of projects without Date of Commissioning

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	11/2013
	Total		4,712.12 -		
	<u>COAL</u>				
5	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	03/2013 -	-
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,ANDHRA PRADESH	10/2006	249.03 -	03/2012 -	-
7	JALLARAM SHAFT PROJECT - [N06000025]SCCL,ANDHRA PRADESH	09/2007	467.78 -	03/2013 -	-
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	03/2012 -	-
9	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	03/2012 -	-
10	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,ANDHRA PRADESH	11/2012	430.14 -	03/2016 -	-
	Total		2,935.42 -		
	<u>STEEL</u>				
11	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	12/2009 08/2010	06/2013
12	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	01/2010 02/2011	11/2013
	Total		462.00 -		
	<u>PETROLEUM</u>				
13	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	01/2012 -	07/2013
14	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	09/2012 -	09/2013
15	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	09/2013 -	09/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	- -	-
17	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	07/2012 07/2012	-
18	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	-
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
	Total		6,710.38 -		
	<u>POWER</u>				
20	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
21	MOUDA STTP - [N18000048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	08/2012 -	03/2013
22	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	10/2012 -	03/2013
23	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	10/2012 -	10/2013
24	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	01/2012 -	-
25	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	09/2010 -	-
26	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	11/2011 -	-
27	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
28	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,MULTI STATE	10/2010	182.68 -	01/2013 -	-
29	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	10/2013 -	-
30	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	- -	-
31	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		23,827.14 -		
	<u>RAILWAYS</u>				
32	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	06/2007 -	06/2007
33	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,ANDHRA PRADESH	07/1998	125.00 363.26	07/2008 -	07/2008
34	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009
35	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010
36	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
37	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010
38	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	120.90 663.10	06/1999 03/2011	03/2011
39	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011
40	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
41	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	- -	02/2012
42	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012
43	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012
44	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012
45	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012
46	HARNOUT - SET. UP OF W/S TO UND. POH OF UP TO 50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	- -	03/2012
47	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	- -	03/2012
48	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 155.00	- -	10/2012
49	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR, KARNATAKA	04/1995	65.94 302.23	- -	12/2012
50	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012
51	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 343.17	- -	12/2012
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 412.91	- -	01/2013
53	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013
54	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 218.19	- -	02/2013
55	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 167.73	03/2012 -	02/2013
56	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013
57	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2013
58	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 842.35	- -	03/2013
59	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 228.09	02/2011 02/2011	03/2013
60	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013
61	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
62	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 385.60	03/2013 -	03/2013
63	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 611.03	12/2011 11/2013	11/2013
64	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
65	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-
66	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
67	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
68	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-
69	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
70	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	02/2006 -	-
71	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
72	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
73	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
74	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
75	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
76	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-
77	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-
78	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
79	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
80	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
81	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
82	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
83	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
84	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
85	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-
86	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	-
88	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2012	2,082.75 -	- -	-
89	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-
90	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
91	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
92	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 -	- -	-
93	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR, RAJASTHAN	04/2010	739.65 -	- -	-
94	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-
95	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	- -	-
96	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-
97	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	-
98	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
99	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR, MULTI STATE	04/2010	553.63 -	- -	-
100	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
101	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
102	NAWADA-LAXMIPUR (NL) - [N22000167]SER, BIHAR	04/2008	620.57 -	- -	-
103	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
104	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
105	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
106	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
107	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
108	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	366.73 -	- -	-
109	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
110	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
111	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
112	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
113	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
114	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
115	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
116	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
117	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
118	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-
119	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
120	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
121	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
122	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
123	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
124	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
125	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
126	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
127	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-
128	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-
129	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-
130	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
131	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
132	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	-
133	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
134	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
135	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-
136	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
137	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-
138	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
139	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-
140	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
141	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
142	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
143	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
144	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
145	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
146	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
147	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
148	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
149	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
150	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
151	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
152	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
153	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
154	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
155	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-
156	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
157	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
158	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
159	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
160	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
161	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
162	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
163	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
164	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
165	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
166	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-
167	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
168	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
169	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
170	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
171	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
172	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
173	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
174	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	- -	-
175	KONDAPALLI-KOTHAGUDEM - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	- -	-
176	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-
177	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-
178	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	- -	-
179	GUDUR-DURGARAJPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-
180	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	- -	-
181	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-
182	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
183	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
185	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
186	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
187	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
188	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
189	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
190	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
191	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
192	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-
193	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-
194	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	- -	-
195	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
196	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	- -	-
197	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	- -	-
198	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
199	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	- -	-
200	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
201	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
202	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
203	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
204	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
205	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
206	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
207	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
208	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
209	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
210	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	01/1999 -	-
211	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, ANDHRA PRADESH	04/2007	313.24 -	01/1999 -	-
212	MM FROM BURAMARA-CHAKULIA - [N22000305]SER, MULTI STATE	04/2008	466.48 -	01/1999 -	-
213	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	285.57 -	01/1999 -	-
214	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
215	MANSABHATINDA INCLUDING MM RAMAMNADI-MAURMANDI VIA TALWANDI SABOO NL - [N22000312]NR, PUNJAB	04/2009	396.04 -	- -	-
216	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 356.87	- 03/2010	-
217	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	353.08 514.68	- -	-
218	NANGALDAM-TALWARA(NL), NR - [220100188]NR, MULTI STATE	03/1981	37.68 450.00	07/2012 -	-
219	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	227.00 997.58	- -	-
220	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-
221	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-
222	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-
223	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	78.23 162.87	- -	-
224	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU	09/1995	100.00 100.00	- -	-
225	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-
226	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA	02/1999	138.00 901.62	- -	-
227	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	324.66 528.65	- -	-
228	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	104.79 -	- -	-
229	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	727.13 727.13	- -	-
230	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	726.96 810.78	- -	-
231	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, ANDHRA PRADESH	04/2006	378.56 671.82	- -	-
232	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	404.19 404.19	- -	-
233	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	125.00 125.00	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
234	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-
235	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-
236	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 603.04	03/2012 -	-
237	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
238	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
239	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
240	DELHI-SOHNAL-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
241	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
	Total		95,851.49 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
242	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	02/2012 -	06/2013
243	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,ODISHA	04/2000	263.27 -	02/2004 -	09/2013
244	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,TAMIL NADU	03/2005	941.00 -	01/2011 -	09/2013
245	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,KARNATAKA	04/2000	241.00 -	08/2004 -	10/2013
246	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,KARNATAKA	04/2000	318.00 -	08/2004 -	10/2013
247	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,ODISHA	04/2000	225.00 -	04/2004 -	10/2013
248	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,UTTAR PRADESH	03/2005	220.00 -	09/2007 -	11/2013
249	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,ODISHA	04/2000	228.70 -	02/2004 -	11/2013
250	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
251	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-
252	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-
253	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	-
254	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,PUNJAB	12/2003	284.00 -	05/2008 -	-
255	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,BIHAR	12/2003	240.00 -	10/2008 -	-
256	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,CHHATISGARH	03/2005	190.00 -	01/2009 -	-
258	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-
259	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-
260	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-
261	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-
262	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-
263	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
264	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
265	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,KARNATAKA	04/2000	196.50 -	06/2011 -	-
266	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,MAHARASHTRA	03/2005	168.00 -	12/2008 -	-
267	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,TAMIL NADU	03/2005	280.00 -	06/2009 -	-
268	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
269	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
270	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH-7 - [N24000094]NHAI,MADHYA PRADESH	12/2003	407.60 -	06/2010 -	-
271	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,MADHYA PRADESH	12/2003	263.17 -	09/2009 -	-
272	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,UTTAR PRADESH	12/2003	355.06 -	09/2009 -	-
273	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	09/2007 07/2011	-
274	TRICHY - KORUR NH-67 - [N24000101]NHAI,TAMIL NADU	03/2005	516.00 -	07/2010 -	-
275	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
276	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-
277	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-
278	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
279	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	-
280	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-
281	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
282	GURGAON-KOTPUTLI KM 42.70 TO 54.4 KM - [N24000130]NHAI,MULTI STATE	04/2009	1,673.70 -	10/2011 -	-
283	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
284	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
285	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
286	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-
287	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
288	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
289	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
290	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
291	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-
292	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-
293	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
294	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	-
295	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-
296	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
297	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-
298	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
299	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-
300	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-
301	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,KARNATAKA	03/2011	839.00 -	- -	-
302	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
303	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
304	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
305	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
306	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
307	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	06/2013 -	-
308	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	-
309	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-
310	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-
311	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	-
312	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	-
313	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, TAMIL NADU	04/2011	571.00 -	10/2013 -	-
314	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	03/2013 -	-
315	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 -	-
316	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-
317	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
318	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
319	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	08/2013 -	-
320	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	-
321	BAREILY-SITAPUR - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
322	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	-
323	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	08/2013 -	-
324	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	08/2013 -	-
325	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	08/2013 -	-
326	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
327	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	- -	-
328	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	- -	-
	Total		54,679.77 -		
	<u>SHIPPING AND PORTS</u>				
329	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
330	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011
331	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
332	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
333	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012
334	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012
335	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
336	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013
337	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
338	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
339	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
340	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
341	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
342	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
343	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-
	Total		12,760.79 -		
	<u>TELECOMMUNICATIONS</u>				
344	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012
345	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013
346	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013
347	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-
348	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
349	GSM EQUIPMENT OF 200000 LINES (2G) UP(WEST) PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL, UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-
	Total		3,061.14 -		
	<u>URBAN DEVELOPMENT</u>				
350	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
351	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX, MUMBAI - [N28000048]CPWD, MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>WATER RESOURCES</u>				
352	PAGLADIYA DAM PROJECT - [300100001]MOWR, ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		212,052.33		

List of on schedule Projects w.r.t. Original Schedule

(Dec,2013)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	190.30	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	190.32		
	<u>COAL</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	162.91	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	74.32	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	54.43	03/2015 -	03/2015
8	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016
9	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.66	03/2020 -	03/2020
11	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.15	07/2016 -	07/2016
12	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	3.62	06/2015 -	06/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	53.49	03/2016 -	03/2016
14	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
15	MURADIDH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.03	03/2015 -	03/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
18	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
19	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	49.77	03/2014 -	03/2014
20	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.42	03/2016 -	03/2016

(Dec,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
22	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	48.56	03/2016 -	03/2016
23	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	158.33	03/2017 -	03/2017
24	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	613.44	03/2016 03/2016	03/2016
	Total		10,739.01 -	10,367.67	1,705.25		
	PETROLEUM						
25	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	400.85	03/2015 -	03/2015
26	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
27	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	-	03/2015 -	03/2015
28	MARKETING TERMINAL AT PARADEEP - [N16000168]	7/2009	199.75 -	199.75	93.57	06/2014 -	06/2014
29	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
30	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
31	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
32	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	283.87	12/2014 -	12/2014
33	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	105.13	08/2015 -	08/2015
34	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	48.55	07/2015 -	07/2015
35	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	172.24	11/2015 -	11/2015
36	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	414.82	11/2015 -	11/2015
37	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]	1/1999	1,419.00 -	1,419.00	267.86	12/2014 -	12/2014
38	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	165.00	107.60	03/2014 -	03/2014
39	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	749.95	05/2014 -	05/2014
40	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	146.70	12/2014 -	12/2014
41	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014
42	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,697.89	05/2015 -	05/2015
	Total		21,870.36 -	21,314.03	4,492.58		

(Dec,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
43	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	-	05/2014 -	05/2014
44	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103	9/2011	1,940.13 -	1,940.13	1,151.72	09/2014 -	09/2014
45	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	-	12/2013 -	12/2013
46	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107	8/2011	1,391.97 -	1,391.97	-	12/2013 -	12/2013
47	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	355.82	02/2014 -	02/2014
48	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117	1/2012	1,422.85 -	1,422.85	-	01/2015 -	01/2015
49	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
50	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	484.37	11/2014 -	11/2014
51	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	260.51	11/2014 -	11/2014
52	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	901.77	514.53	08/2014 -	08/2014
53	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126	3/2012	206.44 -	206.44	42.36	06/2014 -	06/2014
54	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124	3/2012	213.78 -	213.78	24.20	03/2014 -	03/2014
55	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
56	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122	2/2012	1,927.16 -	1,927.16	464.64	10/2014 -	10/2014
57	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121	2/2012	324.33 -	324.33	19.51	08/2014 -	08/2014
58	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120	2/2012	1,310.85 -	1,310.85	571.22	02/2015 -	02/2015
59	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016
60	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016
61	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
63	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	2/2013	11,638.55 -	11,638.55	911.00	09/2017 -	09/2017

(Dec,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
64	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	313.73	06/2015 -	06/2015
65	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
66	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
67	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017
68	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,216.00	05/2017 -	05/2017
69	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	4.84	10/2014 -	10/2014
70	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	6.15	10/2014 -	10/2014
71	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
72	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	679.00	08/2015 -	08/2015
73	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,823.00	11/2016 -	11/2016
74	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,408.00	09/2016 -	09/2016
75	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	2,450.00	12/2016 -	12/2016
76	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	178.53	08/2014 -	08/2014
77	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,123.83	08/2014 -	08/2014
	Total		89,706.45 -	89,706.45	14,115.99		
	<u>RAILWAYS</u>						
78	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	-	02/2015 -	02/2015
79	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	4/2010	2,298.42 -	2,298.42	62.22	03/2014 -	03/2014
80	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	225.70	03/2016 -	03/2016
81	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	42.25	03/2015 -	03/2015
82	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]	4/2008	516.23 -	516.23	446.14	03/2014 -	03/2014
83	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016

(Dec,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
84	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	146.24	03/2017 -	03/2017
85	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	4/2009	257.42 -	257.42	32.19	03/2014 -	03/2014
86	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.26	03/2017 -	03/2017
87	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	8.96	03/2015 -	03/2015
88	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	388.67	56.07	12/2015 -	12/2015
89	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	1.39	02/2019 -	02/2019
90	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.80	02/2020 -	02/2020
91	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	707.00	03/2014 -	03/2014
92	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	653.47	249.80	03/2014 -	03/2014
93	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,619.02 -	2,913.51	366.80	03/2016 -	03/2016
	Total		20,652.70 -	25,739.36	2,347.82		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
94	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,424.72	08/2014 -	08/2014
95	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	1,004.65	07/2015 -	07/2015
96	NASHRI CHANANI - [N24000162]	6/2010	2,159.00 -	2,159.00	240.31	06/2015 -	06/2015
97	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,117.37	12/2013 -	12/2013
98	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	332.50	02/2014 -	02/2014
99	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014
100	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	558.46	09/2014 -	09/2014
101	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	334.61	04/2015 -	04/2015
102	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015
103	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	42.12	07/2014 -	07/2014
104	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	268.96	10/2014 -	10/2014
105	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	20.71	09/2015 -	09/2015

(Dec,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
107	PANVEL-INDAPUR - [N24000216	12/2011	942.69 -	942.69	263.68	06/2014 -	06/2014
108	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	153.76	09/2014 -	09/2014
109	BARSAT-KRISHNANAGAR - [N24000229	8/2012	867.00 -	867.00	598.56	02/2015 -	02/2015
110	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
111	REENGUS SIKAR - [N24000227	3/2012	333.51 -	333.51	256.68	09/2014 -	09/2014
112	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226	10/2011	1,565.00 -	1,565.00	908.44	10/2014 -	10/2014
113	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	958.69	05/2014 -	05/2014
114	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.60	01/2014 -	01/2014
115	PUNE-SHOLAPUR,PKG-II - [N24000193	9/2011	835.00 -	835.00	394.31	01/2014 -	01/2014
116	4-LANING OF BARHI-HAZARIBAGH - [N24000191	2/2012	398.00 -	398.00	454.33	02/2014 -	02/2014
117	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190	12/2011	325.00 -	325.00	161.49	05/2014 -	05/2014
118	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014
119	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	662.29	03/2014 -	03/2014
120	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184	5/2011	664.00 -	664.00	611.24	02/2014 -	02/2014
121	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	248.77	06/2015 -	06/2015
122	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213	4/2012	624.00 -	624.00	407.92	04/2014 -	04/2014
123	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR- BARAUNI - [N24000211	7/2012	356.40 -	356.40	3.26	07/2014 -	07/2014
124	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	283.09	10/2014 -	10/2014
125	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	588.54	07/2014 -	07/2014
126	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	100.21	01/2014 -	01/2014
127	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,113.79	09/2014 -	09/2014
128	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	233.48	06/2014 -	06/2014
129	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,725.30	06/2014 -	06/2014
130	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	930.16	03/2014 -	03/2014

(Dec,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
131	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	554.09	01/2014 -	01/2014
132	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171	6/2011	535.00 -	535.00	52.18	12/2013 -	12/2013
	Total		41,725.72 -	41,725.72	20,063.16		
	<u>SHIPPING AND PORTS</u>						
133	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 02/2014	02/2014
	Total		966.46 -	994.82	363.20		
	<u>STEEL</u>						
134	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078	7/2012	332.65 -	332.65	90.51	08/2014 -	08/2014
135	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079	6/2012	237.09 -	254.90	14.28	12/2014 -	12/2014
136	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080	11/2012	313.05 -	313.05	39.54	06/2015 -	06/2015
137	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016
	Total		1,128.46 -	1,146.27	151.24		
	<u>URBAN DEVELOPMENT</u>						
138	DELHI MRTS PHASE-III - [N28000056	9/2011	38,595.00 -	38,595.00	6,061.33	03/2016 -	03/2016
	Total		38,595.00 -	38,595.00	6,061.33		
	Grand Total		226,053.76	230,258.92	49,490.89		

List of Delayed Projects w.r.t. Original and Revised Schedule

(Dec,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	16,485.00	12/2008 -	06/2014	66	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,666.16	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	3,088.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	2,119.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,358.16				
	<u>CIVIL AVIATION</u>								
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	244.66	01/2011 04/2013	03/2015	50	23
	Total		653.74 -	653.74	244.66				
	<u>COAL</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,833.94	06/2009 -	03/2014	57	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	116.51	03/2010 -	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	118.26	03/2011 -	03/2014	36	-
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	381.07	03/2013 -	03/2014	12	-
11	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	122.60	03/2012 -	03/2014	24	-
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	4,940.31	03/2012 -	05/2014	26	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,143.43	03/2013 09/2012	10/2014	19	25
14	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	113.61	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	130.05	03/2010 -	03/2015	60	-
17	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	100.52	12/2012 -	03/2015	27	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	113.94	03/2013 -	03/2015	24	-
19	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	97.31	03/2013 -	03/2015	24	-
20	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,586.15	03/2014 -	03/2016	24	-
21	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,300.67	03/2014 -	03/2016	24	-
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	27.80	07/2012 -	03/2016	44	-
23	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	269.16	03/2014 -	03/2016	24	-
24	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	29.40	03/2014 -	03/2016	24	-
25	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.38	03/2014 -	03/2016	24	-
26	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
27	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.16	03/2014 -	03/2016	24	-
28	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.28	03/2011 -	03/2016	60	-
29	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	140.55	03/2012 -	03/2016	48	-
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72	-
31	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
32	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	62.43	03/2012 -	03/2017	60	-
33	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	246.90	12/2015 -	04/2018	28	-
	Total		24,452.62 -	28,222.08	14,133.16				
	<u>STEEL</u>								
34	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,654.93	10/2009 10/2012	03/2014	53	17
35	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	159.67	09/2008 12/2013	03/2014	66	3
36	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,191.41	12/2011 -	03/2014	27	-
37	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,451.60	12/2011 -	06/2014	30	-
38	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	296.11	09/2009 05/2012	06/2014	57	25
39	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	108.67	10/2013 -	08/2014	10	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
40	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	361.53	12/2011 09/2014	09/2014	33	0
41	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,400.65	03/2013 -	09/2014	18	-
42	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	352.49	04/2013 09/2014	09/2014	17	0
43	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	1,944.74	12/2012 -	12/2014	24	-
44	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	251.55	05/2013 01/2015	01/2015	20	0
45	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	11,718.09	03/2013 -	03/2015	24	-
46	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	96.38	11/2013 -	06/2015	19	-
	Total		64,208.32 -	70,162.28	55,987.82				
	<u>PETROCHEMICALS</u>								
47	ASSAM GAS CRACKER PROJECT - [N160000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	4,510.51				
	<u>PETROLEUM</u>								
48	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,MAHARASHTRA	10/2008	1,797.35 -	977.00	841.98	12/2011 -	12/2013	24	-
49	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N160000081]BPCL,MAHARASHTRA	04/2008	825.00 -	1,827.00	1,488.84	04/2013 -	12/2013	8	-
50	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N160000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20	-
51	GAS TURBINE GENERATION SET - [N180000146]OIL,ASSAM	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26	-
52	MRPL PHASE-III EXPANSION - [N160000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	10,921.92	01/2012 -	01/2014	24	-
53	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,ASSAM	09/2001	113.90 438.85	480.00	452.91	03/2006 03/2013	02/2014	95	11
54	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
55	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N160000031]ONGC,MAHARASHTRA	01/2007	740.02 -	740.02	731.38	03/2010 03/2012	02/2014	47	23
56	DEVELOPMENT OF SB-14 FIELD - [N160000116]ONGC,MULTI STATE	01/2011	410.44 -	410.44	229.63	11/2012 -	02/2014	15	-
57	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,ASSAM	09/2001	345.10 663.69	750.00	743.72	03/2007 03/2014	03/2014	84	0
58	DEVELOPMENT OF C-SERIES FIELDS - [N160000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
59	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N160000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	03/2014	46	12

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
60	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
61	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,543.40	09/2012 -	03/2014	18	-
62	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	1,975.56	09/2011 03/2012	03/2014	30	24
63	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	400.99	12/2013 -	03/2014	3	-
64	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	5,979.82	02/2014 -	03/2014	1	-
65	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	770.44	07/2012 -	03/2014	20	-
66	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	99.40	09/2012 -	03/2014	18	-
67	DEVELOPMENT OF BHE AND BH-35 AREA. - [N16000118]ONGC,MULTI STATE	08/2010	372.11 -	372.11	234.31	03/2013 -	03/2014	12	-
68	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	52.67	06/2012 -	03/2014	21	-
69	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	104.65	08/2013 -	03/2014	7	-
70	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	19.63	04/2012 -	03/2014	23	-
71	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	142.87	06/2012 -	03/2014	21	-
72	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,ASSAM	08/2008	126.18 -	159.54	62.95	06/2012 -	03/2014	21	-
73	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.46	08/2010 03/2012	05/2014	45	26
74	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,848.86	09/2011 05/2012	05/2014	32	24
75	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
76	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	204.57	08/2012 -	06/2014	22	-
77	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	434.72	05/2013 06/2014	06/2014	13	0
78	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	925.99	10/2011 -	06/2014	32	-
79	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	24,112.00	11/2012 -	09/2014	22	-
80	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20	0
81	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
82	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	445.92	09/2011 -	12/2014	39	-
83	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	32.51	03/2014 -	12/2014	9	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
84	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
85	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24	12
86	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	266.21	03/2012 -	03/2015	36	-
87	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	107.61	05/2014 -	05/2015	12	-
88	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	6.91	03/2015 -	06/2015	3	-
89	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	918.75	09/2012 -	08/2015	35	-
90	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	08/2015	8	-
91	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.47	10/2014 -	10/2015	12	-
92	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	771.02	10/2011 -	10/2015	48	-
93	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,054.78	01/2012 -	10/2015	45	-
94	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
95	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
96	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	990.56	01/2014 -	12/2015	23	-
97	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	991.96	12/2015 -	05/2016	5	-
98	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
99	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	10/2016	49	-
100	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.08	12/2014 -	12/2016	24	-
101	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.43	12/2014 -	12/2016	24	-
102	IOR GELEKI (ONGCL) - [160100216]ONGC,ASSAM	09/2001	390.09 1,674.11	1,674.11	1,759.52	03/2007 03/2017	03/2017	120	0
103	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23	-
	Total		144,241.66 -	160,147.14	93,864.65				
	POWER								
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	392.52	11/2011 -	12/2013	25	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	267.38	02/2012 -	12/2013	22	-
106	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-III - [N18000079]PGCIL,MULTI STATE	11/2009	1,075.12 -	1,075.12	-	05/2012 -	12/2013	19	-
107	ESTABLISHMENT OF POOLING STATIONS AT RAJGARH AND RAIPUR FOR IPP GENERATION PROJECTS IN CHATTISGARH - [N18000092]PGCIL,CHHATISGARH	12/2010	1,719.52 -	1,719.52	-	08/2013 -	12/2013	4	-
108	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS - [N18000097]PGCIL,MULTI STATE	08/2010	170.36 -	170.36	-	04/2013 -	12/2013	8	-
109	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,JAMMU AND KASHMIR	08/2005	1,729.29 -	2,081.00	2,096.81	11/2009 -	01/2014	50	-
110	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,MAHARASHTRA	07/2011	181.93 -	181.93	141.37	07/2013 -	01/2014	6	-
111	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,247.55	10/2010 -	03/2014	41	-
112	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,084.04	08/2012 -	03/2014	19	-
113	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,110.13	08/2012 -	03/2014	19	-
114	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	620.75	11/2012 -	03/2014	16	-
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	-	07/2013 -	03/2014	8	-
116	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,MULTI STATE	10/2006	975.96 -	975.96	887.66	10/2009 -	05/2014	55	-
117	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	623.44	691.11	07/2013 -	05/2014	10	-
118	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,340.45	03/2013 -	05/2014	14	-
119	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	1,873.82	12/2013 -	05/2014	5	-
120	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	6,414.56	5,285.00	04/2009 -	09/2014	65	-
121	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,117.92	776.95	08/2013 -	09/2014	13	-
122	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,621.00	08/2013 -	09/2014	13	-
123	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	214.68	11/2013 -	09/2014	10	-
124	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	241.34	06/2014 -	09/2014	3	-
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,MULTI STATE	02/2009	520.48 -	520.48	370.39	11/2011 -	12/2014	37	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
126	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	937.92	08/2012 -	12/2014	28	-
127	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,473.44	07/2014 -	12/2014	5	-
128	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	913.63 -	913.63	501.56	07/2006 02/2015	02/2015	103	0
129	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,611.92	10/2012 -	03/2015	29	-
130	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,835.50	11/2012 -	03/2015	28	-
131	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,506.60	12/2012 -	03/2015	27	-
132	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	953.10	04/2013 -	03/2015	23	-
133	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,162.88	03/2014 -	03/2015	12	-
134	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	771.27	11/2012 -	03/2015	28	-
135	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	115.07	01/2014 -	03/2015	14	-
136	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,424.82	09/2009 -	04/2015	67	-
137	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	226.33	08/2014 -	05/2015	9	-
138	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	72.00	04/2015 -	05/2015	1	-
139	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,218.89	08/2013 -	06/2015	22	-
140	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	62.98	01/2013 -	06/2015	29	-
141	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,117.87	11/2013 -	06/2015	19	-
142	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	664.72	08/2014 -	06/2015	10	-
143	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,198.22	10/2014 -	06/2015	8	-
144	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	424.04	01/2015 -	12/2015	11	-
145	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,245.08	06/2015 -	12/2015	6	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
146	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,422.44	379.49	07/2014 -	05/2016	22	-
147	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,216.00	07/2011 -	06/2016	59	-
148	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,016.95	01/2016 -	11/2016	10	-
149	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	557.11	07/2010 02/2016	02/2017	79	12
150	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	5,139.00	2,624.41	12/2009 06/2016	03/2017	87	9
151	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	8,976.00	12/2009 -	03/2017	87	-
152	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	1,949.00	03/2013 -	03/2017	48	-
153	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,454.75	09/2010 -	06/2018	93	-
154	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,187.29	09/2009 -	07/2018	106	-
	Total		132,188.71 -	149,240.03	93,148.16				
	<u>RAILWAYS</u>								
155	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	187.34	12/2012 -	12/2013	12	-
156	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 580.83	580.83	578.31	03/1994 -	01/2014	238	-
157	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,ODISHA	04/1993	100.00 142.98	227.94	231.83	03/2002 -	01/2014	142	-
158	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	394.86	12/2009 03/2011	03/2014	51	36
159	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTPT, TAMIL NADU	04/2006	495.74 -	495.74	259.09	06/2013 06/2013	03/2014	9	9
160	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
161	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	567.66	03/2013 -	03/2014	12	-
162	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	126.82	06/2013 -	06/2014	12	-
163	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	287.33	02/2009 02/2009	08/2014	66	66
164	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	262.21	03/2009 03/2009	08/2014	65	65
165	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	224.00	12/2008 -	09/2014	69	-
166	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTPT,MAHARASHTRA	03/1996	401.81 495.44	1,512.86	331.31	03/2004 12/2010	12/2014	129	48
167	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.90	355.23	06/2004 -	12/2014	126	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
168	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,229.17	03/2009 12/2012	12/2014	69	24
169	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240	-
170	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	31.42 393.46	535.40	179.02	03/2007 03/2007	03/2015	96	96
171	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	1,022.64	742.18	12/2010 12/2010	03/2015	51	51
172	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	1,953.38	10/2007 12/2012	12/2015	98	36
173	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	739.35	03/2010 -	12/2015	69	-
174	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	44.91	03/2015 -	12/2015	9	-
175	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	0.59	04/2012 -	03/2016	47	-
176	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.47	448.82	06/2005 07/2011	06/2016	132	59
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	65.16	03/2016 -	06/2016	3	-
178	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	483.68	03/2005 12/2008	12/2016	141	96
179	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,220.15	1,413.35	03/2014 03/2016	12/2016	33	9
180	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 325.00	1,116.53	245.54	03/2010 03/2017	03/2017	84	0
181	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	111.36	04/2014 -	03/2017	35	-
182	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	64.07	12/2015 -	03/2017	15	-
183	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	8.94	03/2015 -	03/2017	24	-
184	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,185.44	3,822.52	03/2009 -	03/2017	96	-
185	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	945.82	03/2007 -	03/2017	120	-
186	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
187	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	2,942.62	04/2008 03/2014	12/2017	116	45
188	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,485.28	12/2008 -	03/2018	111	-
189	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	128.11	12/2012 -	03/2018	63	-
190	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	518.45	03/2014 -	03/2019	60	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
191	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	1,770.51	03/2011 03/2014	03/2020	108	72
	Total		26,362.72 -	77,658.71	32,735.79				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
192	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 148.22	157.47	260.30	09/2007 03/2014	12/2013	75	-3
193	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR, NAGPUR BYPASS - [N24000124]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
194	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,153.77	11/2013 -	01/2014	2	-
195	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	249.37	04/2008 03/2014	03/2014	71	0
196	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	03/2014	69	-
197	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	-	06/2008 -	03/2014	69	-
198	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.01	05/2010 -	03/2014	46	-
199	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	308.49	10/2013 -	03/2014	5	-
200	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	226.29	10/2013 -	03/2014	5	-
201	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57	-
202	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	339.45	02/2009 -	05/2014	63	-
203	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	269.79	06/2008 05/2014	05/2014	71	0
204	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	73.71	09/2007 -	05/2014	80	-
205	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	1,294.08	08/2013 06/2014	06/2014	10	0
206	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	209.92	05/2008 07/2014	07/2014	74	0
207	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.40	09/2013 -	07/2014	10	-
208	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 382.02	382.02	101.21	04/2009 12/2014	12/2014	68	0
209	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 265.53	265.53	87.03	11/2008 12/2014	12/2014	73	0
210	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	241.28	146.70	11/2008 12/2014	12/2014	73	0
211	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 247.43	247.43	177.70	04/2009 12/2014	12/2014	68	0
212	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015	82	0

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
213	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	306.31	04/2008 01/2015	01/2015	81	0
214	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	313.93	04/2008 01/2015	01/2015	81	0
215	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	306.32	04/2010 09/2015	09/2015	65	0
	Total		8,428.93 -	9,272.81	7,204.06				
	<u>SHIPPING AND PORTS</u>								
216	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99	0
217	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
218	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	1,429.10	984.19	12/2010 09/2012	03/2015	51	30
	Total		1,889.87 -	2,540.97	1,230.71				
	<u>TELECOMMUNICATIONS</u>								
219	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.48	06/2009 -	12/2013	54	-
220	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	170.57	01/2009 -	12/2013	59	-
221	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	246.51	05/2011 -	12/2013	31	-
222	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41	24
	Total		2,018.15 -	1,843.90	531.01				
	<u>URBAN DEVELOPMENT</u>								
223	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	490.82	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	490.82				
	Grand Total		452,841.33	557,881.66	330,439.51				

List of ongoing projects having time and cost overrun w.r.t original schedule

(Dec,2013)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2014	31.12	66
	Total		16,663.00 -	22,947.00				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	10/2014	478.50	19
4	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	03/2014	49.09	57
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	05/2014	34.63	26
	Total		7,938.86 -	34,833.62				
	<u>PETROCHEMICALS</u>							
8	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	12/2013	63.35	20
	Total		5,460.61 -	43,753.62				
	<u>PETROLEUM</u>							
9	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	480.00	03/2006 -	02/2014	321.42	95
10	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44	21
11	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	03/2014	41.85	21
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	03/2014	12.16	23
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00	12
14	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	750.00	03/2007 -	03/2014	117.33	84
15	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	03/2007 -	03/2017	329.16	120

(Dec,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
16	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	2,735.65	04/2006 -	02/2014	536.46	94
17	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25	3
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	06/2014	54.46	32
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
20	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	04/2013 -	12/2013	121.45	8
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
22	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76	23
23	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63
24	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50	63
25	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
26	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40	45
27	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27	46
28	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	09/2014	9.85	22
	Total		55,566.37 -	119,543.51				
	POWER							
29	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	07/2013 -	05/2014	48.08	10
30	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,117.92	08/2013 -	09/2014	94.76	13
31	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	09/2009 -	04/2015	41.49	67
32	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79
33	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	11/2009 -	01/2014	20.34	50
34	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69	10
35	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85	41
36	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32	19

(Dec,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,422.44	07/2014 -	05/2016	37.36	22
38	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	12/2009 06/2016	03/2017	105.82	87
39	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14	48
40	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106
41	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69	65
42	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	06/2018	69.71	93
43	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87
	Total		43,738.85 -	180,333.68				
	<u>RAILWAYS</u>							
44	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01	96
45	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 119.29	227.94	03/2002 -	01/2014	127.94	142
46	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64	51
47	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67	51
48	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141
49	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49	69
50	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65
51	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38	12
52	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33	9
53	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	580.83	03/1994 -	01/2014	265.83	238
54	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66
55	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03	24
56	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57	126
57	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2018	45.41	63

(Dec,2013)

Date of Commissioning								
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
58	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50	132
59	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
60	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,512.86	03/2004 -	12/2014	276.51	129
61	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15	12
62	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
63	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46	35
64	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
65	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06	47
66	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
67	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	5,996.00	03/2011 -	03/2020	724.12	108
68	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	2,483.04	12/2008 -	03/2018	238.75	111
69	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2019	114.06	60
70	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83	24
71	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80	120
72	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
73	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62	116
74	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99	15
75	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34	96
76	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
77	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36	33
	Total		23,261.74 -	254,891.41				
	ROAD TRANSPORT AND HIGHWAYS							

(Dec,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
78	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	241.28	11/2008 -	12/2014	55.62	73
79	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45	73
80	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99	57
81	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	382.02	04/2009 -	12/2014	91.19	68
82	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	247.43	04/2009 -	12/2014	23.72	68
83	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	333.83	09/2007 -	05/2014	57.47	80
84	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	09/2015	42.25	65
85	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93	63
	Total		1,628.10 -	257,363.39				
	<u>SHIPPING AND PORTS</u>							
86	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00	99
87	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	1,429.10	12/2010 -	03/2015	16.38	51
	Total		1,378.00 -	259,392.49				
	<u>STEEL</u>							
88	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	03/2014	100.63	66
89	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	09/2014	105.20	33
90	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2014	41.41	53
91	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61	30
	Total		23,538.89 -	288,915.34				
	<u>TELECOMMUNICATIONS</u>							
92	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	12/2013	6.42	54
	Total		149.15 -	289,074.06				

(Dec,2013)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	Grand Total		179,323.57	1,751,048.12				

List of ongoing projects having cost overrun w.r.t. to original schedule

(Dec,2013)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	11/2013	15.77
	Total		4,086.12 -	27,943.66			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	03/2014	49.09
7	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
8	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	10/2014	478.50
9	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	05/2014	34.63
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		8,579.45 -	40,518.97			
	<u>PETROCHEMICALS</u>						
13	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	12/2013	63.35
	Total		5,460.61 -	49,438.97			

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
14	IOR LAKWA - LAKHMANI (ONGCL) - [N160100215]	09/2001	345.10 -	750.00	03/2007 -	03/2014	117.33
15	IOR GELEKI (ONGCL) - [N160100216]	09/2001	390.09 -	1,674.11	03/2007 -	03/2017	329.16
16	IOR, RUDRASAGAR (ONGCL) - [N160100217]	09/2001	113.90 -	480.00	03/2006 -	02/2014	321.42
17	DEV OF G1 AND GS-15 (ONGCL) - [N160100231]	04/2003	429.82 -	2,735.65	04/2006 -	02/2014	536.46
18	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27
22	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	09/2014	9.85
23	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070]	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
24	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	04/2008	825.00 -	1,827.00	04/2013 -	12/2013	121.45
25	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76
26	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29
27	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25
28	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
29	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
30	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	03/2014	12.16
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	06/2014	54.46
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
35	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
36	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	03/2014	41.85
37	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44
	Total		58,765.46 -	129,225.15			
	<u>POWER</u>						
38	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
39	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69
40	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	06/2018	69.71
41	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	12/2009 06/2016	03/2017	105.82
42	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
43	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	04/2015	41.49
44	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
45	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85
46	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	01/2014	20.34
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
48	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
49	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
50	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69
51	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,422.44	07/2014 -	05/2016	37.36
52	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	08/2013 -	09/2014	94.76
53	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
54	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32
55	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	07/2013 -	05/2014	48.08
	Total		51,573.87 -	199,192.44			

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
56	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	03/1994 -	01/2014	265.83
57	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
58	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
59	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
60	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
61	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
62	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
63	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	01/2014	127.94
64	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
65	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
66	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	03/2004 -	12/2014	276.51
67	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
68	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
69	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	412.91	- -	01/2013	39.97
70	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	- -	03/2014	170.07
71	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
72	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
73	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
74	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
75	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
76	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
77	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
79	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01
80	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	- -	12/2012	358.34
81	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57
82	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
83	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05
84	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
85	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
86	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67
87	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64
88	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
89	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
90	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47
91	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28
92	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	- -	-	108.19
93	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
94	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
95	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
96	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73
97	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2018	238.75
98	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
99	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
100	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67
101	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92
102	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	- -	-	553.35
103	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
104	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
105	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	12/2014	461.44
106	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
107	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
108	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2020	724.12
109	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	- -	-	62.83
110	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
111	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04
112	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
113	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
114	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
115	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
116	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
117	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
118	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49
119	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
120	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
121	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
122	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53
123	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
124	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
125	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
126	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	186.92 -	261.70	02/2006 -	-	40.01
127	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
128	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
129	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
130	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
131	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
132	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
133	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
134	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
135	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR [N22000083]	09/1996	156.00 -	407.98	- -	03/2014	161.53
136	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
137	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
138	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	- -	03/2017	115.17
139	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
140	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
141	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
142	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36
143	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
144	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50
145	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2019	114.06
146	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
147	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
148	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
149	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,619.02 -	2,913.51	03/2016 -	03/2016	11.24
151	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
152	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
153	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
154	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	04/2004	225.68 -	293.74	12/2010 -	12/2010	30.16
155	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
156	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	394.14 -	1,215.30	03/2013 -	03/2013	208.34
157	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
158	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
159	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
160	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2018	45.41
161	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34
162	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	- -	-	24.15
163	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
164	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
165	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
166	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
167	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
168	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
169	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
170	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
171	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
172	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
173	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38
174	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	12/2015	25.60
175	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
176	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
177	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
178	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
179	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
180	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
181	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
182	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
183	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	247.75	- -	03/2014	41.22
184	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
185	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
186	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
187	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
188	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
189	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	545.64	- -	-	229.06

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
190	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,418.21	- -	-	171.08
191	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	- -	-	47.95
192	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
193	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02
194	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	697.00 -	1,604.00	- -	-	130.13
195	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
196	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	182.06 -	184.06	- -	-	1.10
197	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
198	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97
199	BAGALKOT-KUDACHI NL - [N22000258	04/2010	377.93 -	986.30	- -	-	160.97
200	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263	04/2008	184.26 -	2,000.00	- -	-	985.42
201	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267	04/2012	289.79 -	377.44	- -	-	30.25
202	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
203	WHITE FIELD-KOLAR NL - [N22000280	04/2011	341.05 -	348.85	- -	-	2.29
204	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	444.18	- -	-	102.06
205	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
	Total		64,474.53 -	380,169.18			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
206	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	04/2004 -	10/2013	7.35
207	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	-	30.10
208	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	03/2008 -	-	16.14
209	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	05/2008 -	-	26.41
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93

(Dec,2013)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
211	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	382.02	04/2009 -	12/2014	91.19
212	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45
213	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	241.28	11/2008 -	12/2014	55.62
214	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281	12/2003	200.00 -	247.43	04/2009 -	12/2014	23.72
215	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	333.83	09/2007 -	05/2014	57.47
216	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99
217	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	09/2015	42.25
218	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
219	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	385.15	09/2007 -	-	10.62
220	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
	Total		4,189.53 -	386,590.91			
	<u>SHIPPING AND PORTS</u>						
221	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
222	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
223	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,429.10	12/2010 -	03/2015	16.38
224	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
225	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST - [N25000037	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
226	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
227	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
228	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	02/2014	2.93
229	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		8,628.97 -	397,778.51			
	<u>STEEL</u>						
230	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2014	41.41
231	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	09/2014	105.20
232	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	03/2014	100.63
233	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61
234	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09
235	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	08/2006	260.00 -	349.64	12/2009 -	06/2013	34.48
236	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
	Total		24,237.98 -	428,249.48			
	<u>TELECOMMUNICATIONS</u>						
237	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	06/2009 -	12/2013	6.42
238	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES (3G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
239	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES (3G) MP PHASE V.1 TELECOM CIRCLE - [N26000090	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	429,730.93			
	<u>URBAN DEVELOPMENT</u>						
240	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
241	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX, MUMBAI - [N28000048	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	441,513.01			
	<u>WATER RESOURCES</u>						
242	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64

(Dec,2013)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		542.90 -	442,700.01			
	Grand Total		255,105.58	3,375,998.22			

List of Projects without Milestones w.r.t. Original Schedule

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	05/2011 -	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	11/2013	0/0
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	10/2014	0/0
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	03/2015	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	03/2015	0/0
8	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015	0/0
	Total		6,035.46 -			0/0
	<u>COAL</u>					
9	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014	0/0
10	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
	Total		1,570.15 -			0/0
	<u>STEEL</u>					
11	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	09/2017 -	09/2014	0/0
12	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	06/2015 -	06/2015	0/0
13	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	05/2016 -	05/2016	0/0
	Total		719.20 -			0/0
	<u>PETROLEUM</u>					
14	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	04/2006 06/2012	02/2014	0/0
16	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,MAHARASHTRA	01/2007	740.02 -	03/2010 03/2012	02/2014	0/0
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	12/2008 04/2013	03/2014	0/0
18	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2014	0/0
19	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	07/2010 05/2012	03/2014	0/0
20	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	09/2012 -	03/2014	0/0
21	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	12/2013 -	03/2014	0/0
22	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	03/2014	0/0
23	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	09/2012 -	03/2014	0/0
24	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	04/2012 -	03/2014	0/0
25	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	06/2012 -	03/2014	0/0
26	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,ASSAM	08/2008	126.18 -	06/2012 -	03/2014	0/0
27	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	06/2012 -	05/2014	0/0
28	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	06/2014	0/0
29	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	06/2014 -	06/2014	0/0
30	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	10/2010 -	12/2014	0/0
31	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	12/2014	0/0
32	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
33	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	12/2014 -	12/2014	0/0
34	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	03/2015 -	03/2015	0/0
35	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
36	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	- -	04/2015	0/0
37	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	07/2015 -	07/2015	0/0
38	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	08/2015 -	08/2015	0/0
39	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	12/2014 -	08/2015	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	10/2014 -	10/2015	0/0
41	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	10/2015	0/0
42	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	10/2015	0/0
43	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
44	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
45	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	02/2016 -	02/2016	0/0
46	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
47	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0
48	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	09/2012 -	10/2016	0/0
49	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2016	0/0
50	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2016	0/0
51	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 -	03/2017	0/0
52	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	- -	-	0/0
53	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
	Total		89,457.33 -			0/0
	<u>POWER</u>					
54	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	09/2014	0/0
55	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	06/2015 -	06/2015	0/0
56	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,ANDHRA PRADESH	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
57	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	03/2016 -	03/2016	0/0
58	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
59	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	05/2016 -	05/2016	0/0
60	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	05/2016 -	05/2016	0/0
61	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	11/2016 -	11/2016	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
62	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	06/2018	0/0
	Total		14,218.44 -			0/0
	<u>RAILWAYS</u>					
63	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
64	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,ANDHRA PRADESH	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
65	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
66	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
67	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
68	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
69	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.10	06/1999 03/2011	03/2011	0/0
70	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
71	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
72	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
73	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
74	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
75	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
76	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012	0/0
77	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
78	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
79	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	- -	10/2012	0/0
80	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,KARNATAKA	04/1995	65.94 302.23	- -	12/2012	0/0
81	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
82	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	- -	12/2012	0/0
83	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 412.91	- -	01/2013	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
84	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
85	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	- -	02/2013	0/0
86	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
87	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
88	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2013	0/0
89	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
90	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
91	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
92	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
93	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
94	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013	0/0
95	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
96	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 580.83	03/1994 -	01/2014	0/0
97	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,ODISHA	04/1993	100.00 142.98	03/2002 -	01/2014	0/0
98	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	- -	01/2014	0/0
99	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,ANDHRA PRADESH	12/1994	124.43 495.68	- -	02/2014	0/0
100	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	- -	03/2014	0/0
101	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	- -	03/2014	0/0
102	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	03/2014	0/0
103	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	- -	03/2014	0/0
104	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
105	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N220000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	- -	03/2014	0/0
106	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
107	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
108	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2014	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
109	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
110	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
111	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
112	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2014	0/0
113	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
114	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014	0/0
115	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014	0/0
116	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	06/2013 -	06/2014	0/0
117	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
118	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
119	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	12/2008 -	09/2014	0/0
120	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
121	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	06/2004 -	12/2014	0/0
122	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	- -	12/2014	0/0
123	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
124	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
125	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
126	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2015	0/0
127	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
128	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
129	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	- -	03/2015	0/0
130	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	- -	03/2015	0/0
131	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
132	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	- -	03/2015	0/0
133	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
134	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
135	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
136	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2015	0/0
137	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	12/2015	0/0
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
139	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINAY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
140	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
141	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	03/2016	0/0
142	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	03/2016	0/0
143	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP, ANDHRA PRADESH	04/2012	632.68 -	04/2012 -	03/2016	0/0
144	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	06/2016	0/0
145	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
146	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
147	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
148	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
149	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
150	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2017	0/0
151	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
152	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
153	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	03/2009 -	03/2017	0/0
154	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	03/2007 -	03/2017	0/0
155	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	- -	03/2017	0/0
156	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR, ASSAM	04/2011	312.12 -	- -	03/2017	0/0
157	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
158	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
159	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
160	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2017	0/0
161	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	- 12/2017	12/2017	0/0
162	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
163	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	12/2012 -	03/2018	0/0
164	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
165	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2019	0/0
166	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
167	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	03/2011 03/2014	03/2020	0/0
168	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
169	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-	0/0
170	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
171	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
172	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-	0/0
173	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
174	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	02/2006 -	-	0/0
175	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
176	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
177	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
178	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
179	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
180	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-	0/0
181	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-	0/0
182	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
183	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
184	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
185	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
186	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
187	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
188	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
189	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-	0/0
190	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
191	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
192	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-	0/0
193	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
194	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
195	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
196	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
197	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
198	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
199	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
200	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
201	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
202	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
203	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-	0/0
204	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
205	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
206	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-	0/0
207	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
208	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
209	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
210	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
211	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
212	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-	0/0
213	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
214	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
215	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
216	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
217	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
218	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
219	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
220	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
221	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
222	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-	0/0
223	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
224	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
225	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
226	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
227	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-	0/0
228	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
229	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
230	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
231	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
232	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-	0/0
233	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
234	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
235	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
236	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	-	0/0
237	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
238	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
239	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-	0/0
240	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
241	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-	0/0
242	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-	0/0
243	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-	0/0
244	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
245	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
246	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-	0/0
247	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
248	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
249	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
250	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
251	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
252	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
253	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
254	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
255	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
256	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
257	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
258	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
259	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-	0/0
260	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
261	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
262	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
263	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
264	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
265	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
266	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
267	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
268	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
269	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
270	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-	0/0
271	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-	0/0
272	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
273	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
274	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
275	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
276	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
277	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
278	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	- -	-	0/0
279	KONDAPALLI-KOTHAGUDEM - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	- -	-	0/0
280	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
281	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-	0/0
282	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	- -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
283	GUDUR-DURGARAJAPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
284	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	- -	-	0/0
285	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-	0/0
286	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
287	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
288	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
289	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
290	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
291	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
292	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
293	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
294	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
295	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
296	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
297	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
298	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	- -	-	0/0
299	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
300	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	- -	-	0/0
301	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
302	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
303	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	- -	-	0/0
304	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
305	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
306	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
307	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
308	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
309	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
310	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
311	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
312	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
313	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-	0/0
314	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
315	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	01/1999 -	-	0/0
316	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
317	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
318	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
319	MANSA BHATINDA INCLUDING MM RAMAMNADI-MAURMANDI VIA TALWANDI SABOO NL - [N22000312]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
320	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 356.87	- 03/2010	-	0/0
321	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	- -	-	0/0
322	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-	0/0
323	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
324	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-	0/0
325	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-	0/0
326	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
327	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	- -	-	0/0
328	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-	0/0
329	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-	0/0
330	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	- -	-	0/0
331	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-	0/0
332	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
333	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	- -	-	0/0
334	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	- -	-	0/0
335	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,ANDHRA PRADESH	04/2006	378.56 671.82	- -	-	0/0
336	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-	0/0
337	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-	0/0
338	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-	0/0
339	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-	0/0
340	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 603.04	03/2012 -	-	0/0
341	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
342	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
343	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
344	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
345	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
	Total		148,510.13 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
346	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	02/2012 -	06/2013	0/0
347	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,ODISHA	04/2000	263.27 -	02/2004 -	09/2013	0/0
348	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,TAMIL NADU	03/2005	941.00 -	01/2011 -	09/2013	0/0
349	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,KARNATAKA	04/2000	241.00 -	08/2004 -	10/2013	0/0
350	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,KARNATAKA	04/2000	318.00 -	08/2004 -	10/2013	0/0
351	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,ODISHA	04/2000	225.00 -	04/2004 -	10/2013	0/0
352	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,UTTAR PRADESH	03/2005	220.00 -	09/2007 -	11/2013	0/0
353	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,ODISHA	04/2000	228.70 -	02/2004 -	11/2013	0/0
354	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
355	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 148.22	09/2007 03/2014	12/2013	0/0
356	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR, NAGPUR BYPASS - [N24000124]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2011 -	12/2013	0/0
357	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	12/2013	0/0
358	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	12/2013	0/0
359	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
360	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	01/2014	0/0
361	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	01/2014	0/0
362	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	01/2014	0/0
363	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	01/2014	0/0
364	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	01/2014	0/0
365	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
366	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0
367	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	02/2014	0/0
368	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 03/2014	03/2014	0/0
369	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	03/2014	0/0
370	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	03/2014	0/0
371	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2014	0/0
372	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
373	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	03/2014	0/0
374	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	03/2014	0/0
375	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	03/2014	0/0
376	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	07/2009 -	04/2014	0/0
377	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	04/2014	0/0
378	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	04/2014	0/0
379	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	02/2009 -	05/2014	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
380	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 05/2014	05/2014	0/0
381	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	09/2007 -	05/2014	0/0
382	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
383	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
384	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	05/2014	0/0
385	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	08/2013 06/2014	06/2014	0/0
386	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
387	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
388	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	06/2014	0/0
389	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 07/2014	07/2014	0/0
390	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	07/2014	0/0
391	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	07/2014	0/0
392	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	07/2014	0/0
393	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	07/2014	0/0
394	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
395	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
396	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
397	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	09/2014 -	09/2014	0/0
398	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	09/2014	0/0
399	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	10/2014	0/0
400	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014	0/0
401	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
402	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 382.02	04/2009 12/2014	12/2014	0/0
403	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 265.53	11/2008 12/2014	12/2014	0/0
404	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	11/2008 12/2014	12/2014	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
405	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 247.43	04/2009 12/2014	12/2014	0/0
406	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	01/2015	0/0
407	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	01/2015	0/0
408	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 01/2015	01/2015	0/0
409	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2015	0/0
410	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
411	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
412	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
413	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
414	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
415	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2015	09/2015	0/0
416	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
417	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
418	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	12/2015	0/0
419	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-	0/0
420	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-	0/0
421	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	-	0/0
422	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,PUNJAB	12/2003	284.00 -	05/2008 -	-	0/0
423	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,BIHAR	12/2003	240.00 -	10/2008 -	-	0/0
424	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
425	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,CHHATISGARH	03/2005	190.00 -	01/2009 -	-	0/0
426	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-	0/0
427	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-	0/0
428	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-	0/0
429	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
430	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
431	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
432	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
433	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, MAHARASHTRA	03/2005	168.00 -	12/2008 -	-	0/0
434	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, TAMIL NADU	03/2005	280.00 -	06/2009 -	-	0/0
435	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
436	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
437	LAKHNAADON TO MP/MH BORDER, KM 596.75-653.22 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, MADHYA PRADESH	12/2003	407.60 -	06/2010 -	-	0/0
438	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, MADHYA PRADESH	12/2003	263.17 -	09/2009 -	-	0/0
439	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, UTTAR PRADESH	12/2003	355.06 -	09/2009 -	-	0/0
440	AGRA-BYPASS (NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 385.15	09/2007 07/2011	-	0/0
441	TRICHY - KORUR NH-67 - [N24000101]NHAI, TAMIL NADU	03/2005	516.00 -	07/2010 -	-	0/0
442	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00 -	02/2010 -	-	0/0
443	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	09/2010 -	-	0/0
444	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	07/2012 -	-	0/0
445	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-	0/0
446	PUNE-SHOLAPUR, PKG1 - [N24000127]NHAI, MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	-	0/0
447	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	05/2012 -	-	0/0
448	CHENNAI-TADA (SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	10/2011 -	-	0/0
449	GURGAON-KOTPUTLI KM 42.70 TO 54.4 KM - [N24000130]NHAI, MULTI STATE	04/2009	1,673.70 -	10/2011 -	-	0/0
450	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	08/2011 -	-	0/0
451	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
452	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
453	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	-	0/0
454	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
455	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
456	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
457	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
458	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-	0/0
459	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
460	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	-	0/0
461	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-	0/0
462	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
463	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-	0/0
464	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-	0/0
465	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
466	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
467	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
468	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
469	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
470	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	-	0/0
471	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-	0/0
472	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
473	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
474	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
475	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
476	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	10/2013 -	-	0/0
477	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-	0/0
478	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
479	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
480	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
481	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0
482	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-	0/0
483	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-	0/0
484	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
485	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
486	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-	0/0
487	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-	0/0
488	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-	0/0
489	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0
490	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0
	Total		102,046.92 -			0/0
	<u>SHIPPING AND PORTS</u>					
491	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
492	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
493	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0
494	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
495	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0
496	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012	0/0
497	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013	0/0
498	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0
499	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
500	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
501	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
502	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
503	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 02/2014	02/2014	0/0
504	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014	0/0
505	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
506	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	03/2015	0/0
507	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
508	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		15,462.28 -			0/0
	<u>TELECOMMUNICATIONS</u>					
509	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012	0/0
510	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013	0/0
511	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
512	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	06/2009 -	12/2013	0/0
513	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	12/2013	0/0
514	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	12/2013	0/0
515	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 03/2012	03/2014	0/0
516	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-	0/0
517	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-	0/0
518	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-	0/0
	Total		5,079.29 -			0/0
	<u>URBAN DEVELOPMENT</u>					
519	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
520	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,595.00 -	03/2016 -	03/2016	0/0
521	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0

			(Dec,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		41,203.18 -			0/0
	<u>WATER RESOURCES</u>					
522	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		424,845.28			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(Dec,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
1	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207	12/2003	157.47 148.22	157.47	260.30	09/2007 03/2014	12/2013
	Total		157.47 -	157.47	260.30		
	<u>STEEL</u>						
2	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082	10/2012	160.48	160.48	-	09/2017 -	09/2014
	Total		160.48 -	160.48	.00		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74	1,508.74	-	06/2016 -	04/2015
4	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	470.32	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	470.32		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
5	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,325.75	10/2014 -	12/2013
	Total		807.00 -	807.00	1,325.75		
	Grand Total		4,569.04	4,569.04	2,056.37		

List of Projects on schedule w.r.t. Latest Schedule

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	190.30	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	190.32		
	<u>COAL</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	162.91	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014
5	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	48.56	03/2016 -	03/2016
6	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	74.32	03/2015 -	03/2015
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	158.33	03/2017 -	03/2017
8	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	613.44	03/2016 03/2016	03/2016
9	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.03	03/2015 -	03/2015
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
12	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
13	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
14	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	49.77	03/2014 -	03/2014
15	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016
16	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.42	03/2016 -	03/2016
17	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	54.43	03/2015 -	03/2015

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.66	03/2020 -	03/2020
20	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.15	07/2016 -	07/2016
21	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	3.62	06/2015 -	06/2015
22	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	53.49	03/2016 -	03/2016
23	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
24	MURAIIDH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
	Total		10,739.01 -	10,367.67	1,705.25		
	<u>PETROCHEMICALS</u>						
25	ASSAM GAS CRACKER PROJECT - [N16000106]	4/2006	5,460.61 -	8,920.00	4,510.51	04/2012 12/2013	12/2013
	Total		5,460.61 -	8,920.00	4,510.51		
	<u>PETROLEUM</u>						
26	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	9/2001	345.10 -	750.00	743.72	03/2007 03/2014	03/2014
27	IOR GELEKI (ONGCL) - [160100216]	9/2001	390.09 -	1,674.11	1,759.52	03/2007 03/2017	03/2017
28	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
29	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
30	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	283.87	12/2014 -	12/2014
31	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	105.13	08/2015 -	08/2015
32	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	48.55	07/2015 -	07/2015
33	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	172.24	11/2015 -	11/2015
34	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	414.82	11/2015 -	11/2015
35	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]	1/1999	1,419.00 -	1,419.00	267.86	12/2014 -	12/2014
36	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	165.00	107.60	03/2014 -	03/2014
37	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	-	03/2015 -	03/2015

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
38	MARKETING TERMINAL AT PARADEEP - [N16000168]	7/2009	199.75 -	199.75	93.57	06/2014 -	06/2014
39	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
40	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	749.95	05/2014 -	05/2014
41	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	146.70	12/2014 -	12/2014
42	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
43	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014
44	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,697.89	05/2015 -	05/2015
45	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	400.85	03/2015 -	03/2015
46	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	761.68	434.72	05/2013 06/2014	06/2014
47	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	3/2010	3,241.03 -	6,638.94	1,451.42	03/2013 11/2014	11/2014
	Total		26,708.37 -	31,138.76	8,881.96		
	<u>POWER</u>						
48	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	-	05/2014 -	05/2014
49	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	9/2011	1,940.13 -	1,940.13	1,151.72	09/2014 -	09/2014
50	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	-	12/2013 -	12/2013
51	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	178.53	08/2014 -	08/2014
52	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	355.82	02/2014 -	02/2014
53	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,123.83	08/2014 -	08/2014
54	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	-	12/2013 -	12/2013
55	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	-	01/2015 -	01/2015

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
56	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
57	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	260.51	11/2014 -	11/2014
58	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	514.53	08/2014 -	08/2014
59	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	42.36	06/2014 -	06/2014
60	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	24.20	03/2014 -	03/2014
61	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
62	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	464.64	10/2014 -	10/2014
63	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	19.51	08/2014 -	08/2014
64	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	571.22	02/2015 -	02/2015
65	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	1/2011	913.63 -	913.63	501.56	07/2006 02/2015	02/2015
66	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,216.00	05/2017 -	05/2017
67	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	4.84	10/2014 -	10/2014
68	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	6.15	10/2014 -	10/2014
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
70	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	679.00	08/2015 -	08/2015
71	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,823.00	11/2016 -	11/2016
72	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,408.00	09/2016 -	09/2016
73	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	2,450.00	12/2016 -	12/2016
74	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	484.37	11/2014 -	11/2014
75	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016
77	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
79	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	911.00	09/2017 -	09/2017
80	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	313.73	06/2015 -	06/2015
81	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
82	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
83	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017
	Total		90,620.08 -	90,620.08	14,617.55		
	<u>RAILWAYS</u>						
84	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	-	02/2015 -	02/2015
85	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088]	4/2006	325.00 -	1,116.53	245.54	03/2010 03/2017	03/2017
86	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,619.02 -	2,913.51	366.80	03/2016 -	03/2016
87	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	42.25	03/2015 -	03/2015
88	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	225.70	03/2016 -	03/2016
89	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	4/2010	2,298.42 -	2,298.42	62.22	03/2014 -	03/2014
90	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	653.47	249.80	03/2014 -	03/2014
91	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	707.00	03/2014 -	03/2014
92	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	146.24	03/2017 -	03/2017

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
93	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244	4/2009	257.42 -	257.42	32.19	03/2014 -	03/2014
94	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	1.26	03/2017 -	03/2017
95	PLASSEY-JIAGANJ DOUBLING - [N22000220	4/2011	248.07 -	248.07	8.96	03/2015 -	03/2015
96	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	4/2010	309.44 -	388.67	56.07	12/2015 -	12/2015
97	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	1.39	02/2019 -	02/2019
98	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	1.80	02/2020 -	02/2020
99	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
100	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114	4/2008	516.23 -	516.23	446.14	03/2014 -	03/2014
	Total		20,977.70 -	26,855.89	2,593.36		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
101	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	382.02	101.21	04/2009 12/2014	12/2014
102	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	265.63	87.03	11/2008 12/2014	12/2014
103	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	241.28	146.70	11/2008 12/2014	12/2014
104	SONAPUR TO GUWAHTI (AS-3) - [N24000044	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015
105	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	269.79	06/2008 05/2014	05/2014
106	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	160.00	209.92	05/2008 07/2014	07/2014
107	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	2,424.72	08/2014 -	08/2014
108	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI [N24000211	7/2012	356.40 -	356.40	3.26	07/2014 -	07/2014
109	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	283.09	10/2014 -	10/2014
110	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	588.54	07/2014 -	07/2014
111	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	100.21	01/2014 -	01/2014
112	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,113.79	09/2014 -	09/2014

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
113	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	233.48	06/2014 -	06/2014
114	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	1,725.30	06/2014 -	06/2014
115	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	153.76	09/2014 -	09/2014
116	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	958.69	05/2014 -	05/2014
117	BARSAT-KRISHNANAGAR - [N24000229]	8/2012	867.00 -	867.00	598.56	02/2015 -	02/2015
118	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
119	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	256.68	09/2014 -	09/2014
120	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	908.44	10/2014 -	10/2014
121	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	558.46	09/2014 -	09/2014
122	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	334.61	04/2015 -	04/2015
123	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015
124	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	42.12	07/2014 -	07/2014
125	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	268.96	10/2014 -	10/2014
126	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	20.71	09/2015 -	09/2015
127	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
128	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	263.68	06/2014 -	06/2014
129	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	248.77	06/2015 -	06/2015
130	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	407.92	04/2014 -	04/2014
131	NIROLI-ROXY-RAJAMUNDA - [N24000194]	7/2011	586.00 -	586.00	237.60	01/2014 -	01/2014
132	PUNE-SHOLAPUR,PKG-II - [N24000193]	9/2011	835.00 -	835.00	394.31	01/2014 -	01/2014
133	4-LANING OF BARHI-HAZARIBAGH - [N24000191]	2/2012	398.00 -	398.00	454.33	02/2014 -	02/2014
134	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]	12/2011	325.00 -	325.00	161.49	05/2014 -	05/2014
135	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	662.29	03/2014 -	03/2014
137	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]	5/2011	664.00 -	664.00	611.24	02/2014 -	02/2014
138	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014
139	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	930.16	03/2014 -	03/2014
140	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	332.50	02/2014 -	02/2014
141	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	554.09	01/2014 -	01/2014
142	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,117.37	12/2013 -	12/2013
143	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]	6/2011	535.00 -	535.00	52.18	12/2013 -	12/2013
144	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,294.08	08/2013 06/2014	06/2014
145	NASHRI CHANANI - [N24000162]	6/2010	2,159.00 -	2,159.00	240.31	06/2015 -	06/2015
146	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	1,004.65	07/2015 -	07/2015
147	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	306.32	04/2010 09/2015	09/2015
148	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	313.93	04/2008 01/2015	01/2015
149	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	306.31	04/2008 01/2015	01/2015
150	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	249.37	04/2008 03/2014	03/2014
151	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	247.43	177.70	04/2009 12/2014	12/2014
	Total		45,018.94 -	45,524.76	24,016.72		
	<u>SHIPPING AND PORTS</u>						
152	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	139.80	03/2006 06/2014	06/2014
153	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	363.20	02/2014 02/2014	02/2014
154	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		1,628.33 -	2,106.69	609.72		

(Dec,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
155	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	1/2007	295.89 -	607.17	361.53	12/2011 09/2014	09/2014
156	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]	4/2011	572.00 -	572.00	352.49	04/2013 09/2014	09/2014
157	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]	2/2011	898.55 -	898.55	251.55	05/2013 01/2015	01/2015
158	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	90.51	08/2014 -	08/2014
159	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	254.90	14.28	12/2014 -	12/2014
160	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	39.54	06/2015 -	06/2015
161	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016
	Total		2,894.90 -	3,223.99	1,116.81		
	<u>URBAN DEVELOPMENT</u>						
162	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,595.00 -	38,595.00	6,061.33	03/2016 -	03/2016
	Total		38,595.00 -	38,595.00	6,061.33		
	Grand Total		243,312.54	258,022.44	64,303.53		

List of Delayed Projects w.r.t. Latest Schedule

(Dec,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	16,485.00	12/2008 -	06/2014	66	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,666.16	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	3,088.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	2,119.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,358.16				
	<u>CIVIL AVIATION</u>								
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	244.66	01/2011 04/2013	03/2015	50	23
	Total		653.74 -	653.74	244.66				
	<u>COAL</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,833.94	06/2009 -	03/2014	57	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	116.51	03/2010 -	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	118.26	03/2011 -	03/2014	36	-
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	381.07	03/2013 -	03/2014	12	-
11	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	122.60	03/2012 -	03/2014	24	-
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	4,940.31	03/2012 -	05/2014	26	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,143.43	03/2013 09/2012	10/2014	19	25
14	NIGAIH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	113.61	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	130.05	03/2010 -	03/2015	60	-
17	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	100.52	12/2012 -	03/2015	27	-
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	113.94	03/2013 -	03/2015	24	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	97.31	03/2013 -	03/2015	24	-
20	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,586.15	03/2014 -	03/2016	24	-
21	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,300.67	03/2014 -	03/2016	24	-
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	27.80	07/2012 -	03/2016	44	-
23	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	269.16	03/2014 -	03/2016	24	-
24	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	29.40	03/2014 -	03/2016	24	-
25	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.38	03/2014 -	03/2016	24	-
26	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
27	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.16	03/2014 -	03/2016	24	-
28	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.28	03/2011 -	03/2016	60	-
29	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	140.55	03/2012 -	03/2016	48	-
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72	-
31	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
32	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	62.43	03/2012 -	03/2017	60	-
33	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	246.90	12/2015 -	04/2018	28	-
	Total		24,452.62 -	28,222.08	14,133.16				
	<u>STEEL</u>								
34	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,654.93	10/2009 10/2012	03/2014	53	17
35	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	159.67	09/2008 12/2013	03/2014	66	3
36	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,191.41	12/2011 -	03/2014	27	-
37	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,451.60	12/2011 -	06/2014	30	-
38	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	296.11	09/2009 05/2012	06/2014	57	25
39	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	108.67	10/2013 -	08/2014	10	-
40	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,400.65	03/2013 -	09/2014	18	-
41	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	1,944.74	12/2012 -	12/2014	24	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	11,718.09	03/2013 -	03/2015	24	-
43	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	96.38	11/2013 -	06/2015	19	-
	Total		62,441.88 -	68,084.56	55,022.25				
	PETROLEUM								
44	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,MAHARASHTRA	10/2008	1,797.35 -	977.00	841.98	12/2011 -	12/2013	24	-
45	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,MAHARASHTRA	04/2008	825.00 -	1,827.00	1,488.84	04/2013 -	12/2013	8	-
46	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20	-
47	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26	-
48	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	10,921.92	01/2012 -	01/2014	24	-
49	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,ASSAM	09/2001	113.90 438.85	480.00	452.91	03/2006 03/2013	02/2014	95	11
50	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
51	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,MAHARASHTRA	01/2007	740.02 -	740.02	731.38	03/2010 03/2012	02/2014	47	23
52	DEVELOPMENT OF SB-14 FIELD - [N16000116]ONGC,MULTI STATE	01/2011	410.44 -	410.44	229.63	11/2012 -	02/2014	15	-
53	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
54	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	03/2014	46	12
55	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
56	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,543.40	09/2012 -	03/2014	18	-
57	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	1,975.56	09/2011 03/2012	03/2014	30	24
58	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	400.99	12/2013 -	03/2014	3	-
59	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	5,979.82	02/2014 -	03/2014	1	-
60	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	770.44	07/2012 -	03/2014	20	-
61	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	99.40	09/2012 -	03/2014	18	-
62	DEVELOPMENT OF BHE AND BH-35 AREA. - [N16000118]ONGC,MULTI STATE	08/2010	372.11 -	372.11	234.31	03/2013 -	03/2014	12	-
63	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	52.67	06/2012 -	03/2014	21	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
64	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	104.65	08/2013 -	03/2014	7	-
65	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	19.63	04/2012 -	03/2014	23	-
66	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	142.87	06/2012 -	03/2014	21	-
67	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,ASSAM	08/2008	126.18 -	159.54	62.95	06/2012 -	03/2014	21	-
68	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.46	08/2010 03/2012	05/2014	45	26
69	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,848.86	09/2011 05/2012	05/2014	32	24
70	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
71	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	204.57	08/2012 -	06/2014	22	-
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	925.99	10/2011 -	06/2014	32	-
73	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	24,112.00	11/2012 -	09/2014	22	-
74	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
75	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	445.92	09/2011 -	12/2014	39	-
76	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	32.51	03/2014 -	12/2014	9	-
77	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
78	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24	12
79	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	266.21	03/2012 -	03/2015	36	-
80	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	107.61	05/2014 -	05/2015	12	-
81	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	6.91	03/2015 -	06/2015	3	-
82	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	918.75	09/2012 -	08/2015	35	-
83	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	08/2015	8	-
84	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.47	10/2014 -	10/2015	12	-
85	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	771.02	10/2011 -	10/2015	48	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,054.78	01/2012 -	10/2015	45	-
87	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
88	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
89	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	990.56	01/2014 -	12/2015	23	-
90	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	991.96	12/2015 -	05/2016	5	-
91	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
92	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	10/2016	49	-
93	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.08	12/2014 -	12/2016	24	-
94	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.43	12/2014 -	12/2016	24	-
95	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23	-
	Total		139,403.65 -	150,322.41	89,475.27				
	<u>POWER</u>								
96	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	392.52	11/2011 -	12/2013	25	-
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	267.38	02/2012 -	12/2013	22	-
98	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-III - [N18000079]PGCIL,MULTI STATE	11/2009	1,075.12 -	1,075.12	-	05/2012 -	12/2013	19	-
99	ESTABLISHMENT OF POOLING STATIONS AT RAJGARH AND RAIPUR FOR IPP GENERATION PROJECTS IN CHATTISGARH - [N18000092]PGCIL,CHHATISGARH	12/2010	1,719.52 -	1,719.52	-	08/2013 -	12/2013	4	-
100	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS - [N18000097]PGCIL,MULTI STATE	08/2010	170.36 -	170.36	-	04/2013 -	12/2013	8	-
101	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,JAMMU AND KASHMIR	08/2005	1,729.29 -	2,081.00	2,096.81	11/2009 -	01/2014	50	-
102	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,MAHARASHTRA	07/2011	181.93 -	181.93	141.37	07/2013 -	01/2014	6	-
103	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,247.55	10/2010 -	03/2014	41	-
104	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,084.04	08/2012 -	03/2014	19	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
105	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,110.13	08/2012 -	03/2014	19	-
106	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	620.75	11/2012 -	03/2014	16	-
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	-	07/2013 -	03/2014	8	-
108	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,MULTI STATE	10/2006	975.96 -	975.96	887.66	10/2009 -	05/2014	55	-
109	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEEPCO,TRIPURA	07/2009	421.01 -	623.44	691.11	07/2013 -	05/2014	10	-
110	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,340.45	03/2013 -	05/2014	14	-
111	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	1,873.82	12/2013 -	05/2014	5	-
112	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	6,414.56	5,285.00	04/2009 -	09/2014	65	-
113	PARE HYDRO ELECTRIC PROJECT - [N18000045]NNEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,117.92	776.95	08/2013 -	09/2014	13	-
114	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,621.00	08/2013 -	09/2014	13	-
115	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	214.68	11/2013 -	09/2014	10	-
116	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	241.34	06/2014 -	09/2014	3	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,MULTI STATE	02/2009	520.48 -	520.48	370.39	11/2011 -	12/2014	37	-
118	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	937.92	08/2012 -	12/2014	28	-
119	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,473.44	07/2014 -	12/2014	5	-
120	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,611.92	10/2012 -	03/2015	29	-
121	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,835.50	11/2012 -	03/2015	28	-
122	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,506.60	12/2012 -	03/2015	27	-
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	953.10	04/2013 -	03/2015	23	-
124	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,162.88	03/2014 -	03/2015	12	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
125	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	771.27	11/2012 -	03/2015	28	-
126	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	115.07	01/2014 -	03/2015	14	-
127	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,424.82	09/2009 -	04/2015	67	-
128	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	226.33	08/2014 -	05/2015	9	-
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	72.00	04/2015 -	05/2015	1	-
130	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,218.89	08/2013 -	06/2015	22	-
131	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	62.98	01/2013 -	06/2015	29	-
132	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,117.87	11/2013 -	06/2015	19	-
133	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	664.72	08/2014 -	06/2015	10	-
134	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,198.22	10/2014 -	06/2015	8	-
135	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	424.04	01/2015 -	12/2015	11	-
136	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,245.08	06/2015 -	12/2015	6	-
137	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,422.44	379.49	07/2014 -	05/2016	22	-
138	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,216.00	07/2011 -	06/2016	59	-
139	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,016.95	01/2016 -	11/2016	10	-
140	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	557.11	07/2010 02/2016	02/2017	79	12
141	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	5,139.00	2,624.41	12/2009 06/2016	03/2017	87	9
142	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	8,976.00	12/2009 -	03/2017	87	-
143	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	1,949.00	03/2013 -	03/2017	48	-
144	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,454.75	09/2010 -	06/2018	93	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
145	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,187.29	09/2009 -	07/2018	106	-
	Total		131,275.08 -	148,326.40	92,646.60				
	<u>RAILWAYS</u>								
146	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 207.52	207.52	187.34	12/2012 -	12/2013	12	-
147	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 580.83	580.83	578.31	03/1994 -	01/2014	238	-
148	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,ODISHA	04/1993	100.00 142.98	227.94	231.83	03/2002 -	01/2014	142	-
149	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	394.86	12/2009 03/2011	03/2014	51	36
150	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,TAMIL NADU	04/2006	495.74 -	495.74	259.09	06/2013 06/2013	03/2014	9	9
151	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
152	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	567.66	03/2013 -	03/2014	12	-
153	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	146.95 -	171.02	126.82	06/2013 -	06/2014	12	-
154	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	287.33	02/2009 02/2009	08/2014	66	66
155	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	262.21	03/2009 03/2009	08/2014	65	65
156	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	224.00	12/2008 -	09/2014	69	-
157	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTT,MAHARASHTRA	03/1996	401.81 495.44	1,512.86	331.31	03/2004 12/2010	12/2014	129	48
158	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.90	355.23	06/2004 -	12/2014	126	-
159	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,229.17	03/2009 12/2012	12/2014	69	24
160	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240	-
161	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	31.42 393.46	535.40	179.02	03/2007 03/2007	03/2015	96	96
162	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	1,022.64	742.18	12/2010 12/2010	03/2015	51	51
163	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	1,953.38	10/2007 12/2012	12/2015	98	36
164	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	739.35	03/2010 -	12/2015	69	-
165	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	44.91	03/2015 -	12/2015	9	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
166	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	0.59	04/2012 -	03/2016	47	-
167	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.47	448.82	06/2005 07/2011	06/2016	132	59
168	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	65.16	03/2016 -	06/2016	3	-
169	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	483.68	03/2005 12/2008	12/2016	141	96
170	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,220.15	1,413.35	03/2014 03/2016	12/2016	33	9
171	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	111.36	04/2014 -	03/2017	35	-
172	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	64.07	12/2015 -	03/2017	15	-
173	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	8.94	03/2015 -	03/2017	24	-
174	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,185.44	3,822.52	03/2009 -	03/2017	96	-
175	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	945.82	03/2007 -	03/2017	120	-
176	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
177	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	2,942.62	04/2008 03/2014	12/2017	116	45
178	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,485.28	12/2008 -	03/2018	111	-
179	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	128.11	12/2012 -	03/2018	63	-
180	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	518.45	03/2014 -	03/2019	60	-
181	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	1,770.51	03/2011 03/2014	03/2020	108	72
	Total		26,037.72 -	76,542.18	32,490.25				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
182	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR, NAGPUR BYPASS - [N24000124]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
183	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,153.77	11/2013 -	01/2014	2	-
184	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	03/2014	69	-
185	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	-	06/2008 -	03/2014	69	-
186	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.01	05/2010 -	03/2014	46	-

(Dec,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
187	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	308.49	10/2013 -	03/2014	5	-
188	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	226.29	10/2013 -	03/2014	5	-
189	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57	-
190	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	339.45	02/2009 -	05/2014	63	-
191	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	73.71	09/2007 -	05/2014	80	-
192	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.40	09/2013 -	07/2014	10	-
	Total		4,978.24 -	5,316.30	2,990.20				
	<u>SHIPPING AND PORTS</u>								
193	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	1,429.10	984.19	12/2010 09/2012	03/2015	51	30
	Total		1,228.00 -	1,429.10	984.19				
	<u>TELECOMMUNICATIONS</u>								
194	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.48	06/2009 -	12/2013	54	-
195	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	170.57	01/2009 -	12/2013	59	-
196	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	246.51	05/2011 -	12/2013	31	-
197	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41	24
	Total		2,018.15 -	1,843.90	531.01				
	<u>URBAN DEVELOPMENT</u>								
198	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	490.82	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	490.82				
	Grand Total		435,425.08	529,960.67	315,366.57				

List of ongoing projects having cost overrun w.r.t. to revised schedule

(Dec,2013)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	11/2013	15.77
	Total		2,278.12 -	25,928.66			
	<u>COAL</u>						
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	BHUBANESHWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		1,431.79 -	27,645.25			
	<u>PETROLEUM</u>						
9	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	750.00	03/2007 -	03/2014	117.33
10	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	480.00	03/2006 -	02/2014	321.42
11	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	09/2014	9.85
12	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070]	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
13	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	04/2008	825.00 -	1,827.00	04/2013 -	12/2013	121.45

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
14	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29
15	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25
16	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	03/2014	12.16
17	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
18	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	03/2014	41.85
19	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44
	Total		32,937.88 -	65,668.42			
	<u>POWER</u>						
20	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
21	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69
22	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	06/2018	69.71
23	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	12/2009 06/2016	03/2017	105.82
24	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
25	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	04/2015	41.49
26	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85
27	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	01/2014	20.34
28	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
29	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,422.44	07/2014 -	05/2016	37.36
30	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	08/2013 -	09/2014	94.76
31	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
32	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	07/2013 -	05/2014	48.08
	Total		42,941.51 -	123,267.72			
	<u>RAILWAYS</u>						

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
33	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
34	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
35	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
37	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
38	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	01/2014	127.94
39	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
40	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
41	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	03/2004 -	12/2014	276.51
42	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
43	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
44	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
45	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
46	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
47	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
48	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62
49	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
50	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01
51	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57
52	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
53	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
54	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
55	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
56	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64
57	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
58	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
59	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
61	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
62	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2018	238.75
63	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
64	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
65	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
66	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
67	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	12/2014	461.44
68	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
69	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
70	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2020	724.12
71	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
72	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
73	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
74	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
75	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
76	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
77	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
78	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88

(Dec,2013)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
79	RAICHUR-GUNTAKAL(DL)(SCR) - [N220100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
80	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
81	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
82	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
83	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
84	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
85	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
86	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
87	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
88	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
89	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	407.98	- -	03/2014	161.53
90	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
91	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
92	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	- -	03/2017	115.17
93	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
94	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
95	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36
96	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
97	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50
98	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2019	114.06
99	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
100	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
101	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
102	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,619.02 -	2,913.51	03/2016 -	03/2016	11.24
103	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
104	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
105	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	394.14 -	1,215.30	03/2013 -	03/2013	208.34
106	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	484.61	03/2012 -	-	52.28
107	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
108	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2018	45.41
109	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34
110	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
111	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	- -	-	184.87
112	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63
113	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152	04/2013	456.00 -	965.16	- -	-	111.66
114	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153	04/2010	739.65 -	872.22	- -	-	17.92
115	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	218.39	- -	-	2.34
116	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	553.63 -	651.17	- -	-	17.62
117	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
118	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38
119	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	175.69 -	325.00	- -	-	84.98
120	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	285.07 -	378.56	- -	-	32.80
121	ATTIPPATTU-PUTTUR - [N22000184	04/2008	446.87 -	528.00	- -	-	18.16
122	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	1,200.00	- -	-	129.22
123	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
124	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
125	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
126	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
127	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	247.75	- -	03/2014	41.22
128	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
129	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
130	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
131	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
132	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
133	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	545.64	- -	-	229.06
134	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,418.21	- -	-	171.08
135	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	-	47.95
136	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
137	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
138	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	697.00 -	1,604.00	- -	-	130.13
139	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
140	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
141	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
142	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
143	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
144	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
145	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]	04/2012	289.79 -	377.44	- -	-	30.25

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
146	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99 -	- -	- -	183.41
147	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85 -	- -	- -	2.29
148	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	444.18 -	- -	- -	102.06
149	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00 -	01/1999 -	- -	123.46
	Total		53,140.77 -	272,288.18 -			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
150	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47 -	157.47 -	09/2007 -	12/2013 -	0.00
151	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53 -	04/2004 -	10/2013 -	7.35
152	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66 -	09/2008 -	- -	30.10
153	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10 -	03/2008 -	- -	16.14
154	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00 -	05/2008 -	- -	26.41
155	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	265.63 -	11/2008 -	12/2014 -	58.45
156	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31 -	02/2010 -	- -	2.29
157	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00 -	11/2011 -	- -	106.50
	Total		2,538.38 -	276,275.88 -			
	<u>SHIPPING AND PORTS</u>						
158	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00 -	03/2006 -	06/2014 -	300.00
159	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST [N25000037]	04/2005	882.00 -	1,060.00 -	02/2011 -	12/2012 -	20.18
160	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50 -	03/2011 -	03/2013 -	7.62
161	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82 -	02/2014 -	02/2014 -	2.93
162	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22 -	04/2009 -	02/2011 -	51.92
	Total		2,946.13 -	280,059.42 -			

(Dec,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
163	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61
164	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
	Total		14,680.09 -	296,722.32			
	<u>TELECOMMUNICATIONS</u>						
165	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	12/2013	6.42
166	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES (3G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
167	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES (3G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	298,203.77			
	<u>URBAN DEVELOPMENT</u>						
168	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
	Total		6,395.00 -	309,812.77			
	<u>WATER RESOURCES</u>						
169	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	310,999.77			
	Grand Total		177,889.55	2,309,819.16			
