

**316th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
February, 2012**



NPCIL



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2011-12	6-13
Summary of Projects	14-15
Extent of Time and Cost Overrun	16-23
List of Projects Complete, Added, Milestones, Additional Delays	24-29
Trend and Graphical Analysis of Mega Projects	30-42
Sector wise analysis of projects	43-43
List of All Ongoing Projects	44-74
Cost and Graphical Analysis of Projects	75-86
ANNEXURE	87-87
Central Sector Projects	88-88
List of Projects Expenditure is more than Cost	89-94
List of On Schedule Projects	95-105
List of Projects with out Original Date of Commissioning	106-110
List of Projects with Date of Commissioning	111-115
List of Projects Delayed Projects w.r.t Original	116-129
List of Projects without Milestones	130-152
Abbreviation	153-154

EXECUTIVE SUMMARY

The Flash Report for February, 2012 contains information on the status of the 566 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During, February 2012, 4 projects (1 project each of Coal and Road Transport & Highways and 2 projects of Power Sectors) have reported completion.

During the reference month, 63 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 18 months, in respect of projects relating to Railways, Road Transport and Highways, Power, Petroleum, Coal, Shipping & Ports, Steel, Civil Aviation and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	131	2
2.	ROAD TRANSPORT & HIGHWAYS	135	14
3.	POWER	99	13
4.	PETROLEUM	69	18
5.	COAL	50	4
6.	TELECOMMUNICATION	18	1
7.	SHIPPING & PORTS	26	2
8.	STEEL	16	8
9.	FERTILISERS	6	0
10.	CIVIL AVIATION	5	1
11.	ATOMIC ENERGY	5	0
12.	URBAN DEVELOPMENT	4	0
13.	WATER RESOURCES	1	0
14.	PETROCHEMICALS	1	0
Total		566	63

3. The total original cost of implementation of the 566 projects was about ₹ 7,26,749.77 Crores and their anticipated completion cost is likely to be ₹ 8,45,950.57 Crores, which reflects an overall cost overrun of ₹ 1,19,200.8 Crores (16.4 % of original cost). The expenditure incurred on these projects till February, 2012 is ₹ 3,72,525.94 Crores, which is 44% of the revised cost of the projects.

4. Out of the 566 projects, 4 projects are ahead of schedule, 159 are on schedule, 246 projects are delayed, and 81 projects have been sanctioned without any commissioning schedule/date. Further, in case of 76 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. Out of 246 delayed projects, 64 projects had overall delay in the range of 1 to 12 months, 44 projects had a delay in the range of 13 to 24 months, 103 projects had a delay in the range of 25 to 60 months and 35 projects had a delay of 61 months and above.

5. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

6. The brief reasons for time overruns as reported by various projects implementing agencies are inadequate mobilization by the contractors, delay in land acquisitions, law and order problems, delays in engineering designs, change of scope, delays in pre-project activity, Maoist problems and forest and environment clearances, etc. Brief reasons for cost overruns are mainly due to inflation, fluctuation of exchange rate, higher tender value, change of scope etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

8. The Sector-wise details of additional delays are as under:-

i) In the **Shipping and Ports sector**, 2 projects of Shipping Corporation of India have reported additional delay. The project 'Acquisition of 6 Nos. of 57000 DWT, Handymax Bulk, SCI' has reported additional delay of 1 month and 'Construction and Development of 2 Offshore Container Berths and Terminal Mumbai Port' has reported additional delays of 3 months. However, the project authorities have not reported any specific reason for delay in these projects.

ii) In the **Telecommunications sector**, project 'Convergent Billing and CRM, MTNL' has reported an additional delay of 1 month due to customization delay by the vendor.

iii) In the **Petroleum Sector**, 18 projects have reported additional delays in the range of 1-18 months. Six projects have reported additional delay of one month each. The project 'MRPL Phase-III Expansion Mangalore Refinery' has reported additional delay of 5 months due delay in land acquisition and slow progress by contractors, 'Additional Development of D-1 Fields, ONGC' and 'Mumbai High North Development, Phase-II, ONGC' have reported additional delay of 6 and 12 months respectively due to slow progress achieved in progress of well platforms, 'Refrigerated LPG Storage at JNPT, BPCL' has reported additional delays of 12 months due to delay in clearance from JNPT and Railway, 'Development of C-Series Fields, ONGC' has reported additional delays of 13 months due to re-fabrication of decks and drilling of development wells, 'Development of B-22 Cluster Fields, ONGC' has reported additional delays of 13 months due to delay in finalization of tender and re-tendering and 'Development of B-193 Cluster Fields, ONGC' has reported additional delay of 18 months due to contractual problems. Besides the above projects, 'Development of B-46 Cluster Fields' has reported additional delay of 2 months, 'Development of SB-14 Fields, ONGC' has reported additional delay of 4 months, 'Construction of One Multiple Support Vessel, ONGC' has reported additional delay of 8 months, '102 MW Wind Power Project, ONGC' has reported additional delay of 10 months. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are land acquisition problem, statutory approvals, evaluation and procedural delays, re-tendering due to court cases, geo-technical surprises, poor performance of contractor, etc.

iv) In the **Power Sector**, 13 projects have reported additional delays in the range of 1-9 months. Three projects have reported an additional delay of 1 month each. The project 'Uri HEP, Stage-II, NHPC' has reported additional delay of 2 months due to local unrest, 'Mouda STTP, NTPC' has reported additional delay of 2 months due to delay in readiness of Fronts by M/s ERA, 'Transmission system Associated with Parbati-III, HEP, PGCIL' has reported additional delay of 3 months due to delay in forest clearance, 'Barh STTP, Stage-II, NTPC' and 'Vindhyachal STTP, Stage-IV, NTPC' has reported additional delay of 3 months each due to delay in supply of parts by BHEL, 'Bongaigaon Thermal Power Project, NTPC' has reported additional delay of 6 months due to delay in TG erection start, 'Chutak HEP, NHPC' has reported additional delay of 5 months due to delay in supply and erection of E & M components, 'Kudankulam-APP Transmission System, PGCIL' has reported additional delay of 9 months due to ROW problem in Karnataka. The project 'Barh STTP Stage-I, NTPC' and 'Rihand STTP, Stage-III, NTPC' have reported additional delays of 3 months each for which no reasons have been reported by the project authority.

v) In **Steel sector**, 8 projects have reported additional delays in the range of 1-9 months. 'Rebuilding of Coke Oven Battery No.1 and 2, SAIL' has reported additional delay of 1 month due to slow progress by the contractor. '67.5 MW TG-5 System Emergency Power Requirement, RINL' and '330 TPH Boiler-6, and Auxiliary System, RINL' have reported two months additional delays each, '700 TPD ARI Separation Unit-4 at Oxygen Plant-II, SAIL', 'Expansion Bhilai Steel Plant, SAIL' and 'Expansion of Durgapur Steel Plant, SAIL' have reported additional delays of 3 months each, 'Expansion of Bokaro Steel Plant, SAIL' has reported an additional delay of 7 months and 'Expansion of II SCO Steel Plant' has reported an additional delay of 9 months. However, no specific reasons have been reported by the project authorities for delay in these projects.

vi) In the **Road Transport and Highways Sector**, 14 projects of NHAI have reported additional delays in the range of 1-11 months. Three projects have reported additional delays of one month each, two projects have reported additional delay of two months each and four projects have reported additional delay of four months each. The project 'Upgradation of Hyderabad-Bangalore Section' has reported additional delay of 5 months, 'Gwalior-Jhansi, NH-75' has reported additional delay of 6 months, 'Jhansi to Lalitpur,

NH-25,26' and '4 Laning of Belgum- Khanpur Section' has reported additional delays of 10 months each, and 'Jammu-Udhampur, KM.27.5 – 67.00' has reported additional delay of 11 months. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

vii) In Railways sector, 2 projects of Railway have reported additional delay in the range of 12-15. The project, 'Ratlam-Mhow-Khandwa-Akola (GC), WR' and 'Ramanagram-Mysore doubling with electrification of SWR', has reported additional delay of 12 and 15 months respectively due to delay in land acquisition.

viii) In Civil Aviation Sector, project 'C/O Integrated Passenger Terminal Building, NSCBI Airport, AAI' has reported additional delay of 7 months due to non-availability of complete work site.

ix) In Coal Sector, 4 projects have been reported additional delays in the range of 5-12 months. The project 'Penganga OC, WCL' has reported additional delay of 5 months due to problem of resettlement and rehabilitation, 'Adriyala Shaft Project, SCCL' has reported additional delay of 10 months due to delay in supply of longwall equipments, 'Ramagundam OC-II Extension, SCCL' and 'Manuguru OC-II Extension, Phase-II, SCCL' have reported additional delays of 12 months each due to delay in diversion of forest land,

9. The status as on 01.03.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.

(Pankaj Jain)

Special Secretary

Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	135	14
2	Railways	131	2
3	Power	99	13
4	Petroleum	69	18
5	Coal	50	4
6	Shipping & Ports	26	2
7	Telecommunications	18	1
8	Steel	16	8
9	Fertilisers	6	0
10	Atomic Energy	5	0
11	Civil Aviation	5	1
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	566	63

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC AND MAITHON RB(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
<u>Road Transport & Highways</u>				
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
June,2011				
<u>Petroleum</u>				
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
<u>Power</u>				
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
<u>Railways</u>				
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
<u>Road Transport & Highways</u>				
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00

July,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Steel</u>				
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
<u>Petroleum</u>				
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
August,2011				
<u>Power</u>				
30	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]	262.10	09/2010	164.00
<u>Railways</u>				
31	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]	262.00	-	548.54
<u>Road Transport & Highways</u>				
32	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]	193.00	10/2008	338.70
33	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256]	359.00	03/2009	870.60
<u>Telecommunications</u>				
34	NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]	312.86	02/2008	204.43
<u>Urban Development</u>				
35	DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]	8,676.00	06/2010	18,304.30

September,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Petroleum</u>				
36	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF(INDIAN OIL CORPORATION LIMITED) - [N16000040]	293.60	12/2009	234.81
<u>Railways</u>				
37	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN(WESTERN RAILWAY) - [220100116]	112.53	03/1996	509.57
38	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves(NORTH WESTERN RAILWAY) - [N22000106]	643.36	03/2011	786.54
<u>Road Transport & Highways</u>				
39	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106225]	217.00	10/2008	352.26
October,2011				
<u>Power</u>				
40	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000043]	204.07	06/2011	129.60
November,2011				
41	WESTERN REGION STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000050]	230.89	01/2011	98.20
<u>Road Transport & Highways</u>				
42	RINGBUNDS TO JHAJHANPUR (BR-6)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000030]	340.00	06/2008	570.00
43	THRISSUR TO ANGAMALI (NH-47)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000037]	312.50	03/2009	604.40
December,2011				
<u>Mines</u>				
44	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [100100054]	4,091.51	12/2008	4,183.00
<u>Petroleum</u>				
45	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000024]	2,305.30	06/2010	1,266.47
46	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)(GAS AUTHORITY OF INDIA LIMITED) - [N16000052]	4,429.38	10/2010	2,325.60
<u>Power</u>				
47	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000023]	238.25	05/2011	220.82

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
48	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106246]	227.00	10/2008	403.60
49	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106276]	629.00	11/2010	910.00
50	LALITPUR TO SAGAR, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106299]	198.00	11/2008	187.30
51	JHANSI TO LALITPUR, NH-26(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000097]	276.09	09/2009	295.40
52	PONDICHERY - TINDIVANAU NH-66(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000100]	285.00	07/2010	359.40
<u>Shipping & Ports</u>				
53	Construction & License out the OPERATION, MANAG. &(PORT TRUST) - [N25000038]	230.00	12/2010	219.00
<u>Telecommunications</u>				
54	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000039]	601.49	12/2008	496.20
55	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1(BHARAT SANCHAR NIGAM LIMITED) - [N26000040]	192.48	03/2009	119.45
56	Procurement of 2.5G DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000066]	424.00	03/2009	.00
57	Procurement of 10G (40 chl) DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000067]	590.10	03/2009	.00
58	Procurement of 10G 40 CHL (12 chl equipped) DWDM(BHARAT SANCHAR NIGAM LIMITED) - [N26000068]	545.50	03/2010	.00
59	Procurement of STM-1 SDH equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000069]	154.03	03/2010	.00
60	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000070]	355.92	03/2010	.00
61	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000071]	477.00	03/2010	.00
62	Procurement of DXC equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000074]	229.00	03/2010	.00
63	GSM equipment of 900000Lines (2G) PunjabPhase V.2(BHARAT SANCHAR NIGAM LIMITED) - [N26000081]	241.49	09/2009	123.76
64	GSM equipment of 975000Lines (2G) 325000 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000083]	625.53	02/2010	.00
65	GSM equipment of 1100000Lines (2G) UP East Phase(BHARAT SANCHAR NIGAM LIMITED) - [N26000084]	624.75	09/2010	.00
66	GSM equipment of 375000Lines (2G) 75000lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000085]	170.23	06/2009	.00
67	GSM equipment of 849862Lines (2G) 150138 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000087]	584.33	02/2009	403.71
68	GSM equipment of 1900000Lines (2G) 401700 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000091]	760.20	-	819.57
69	GSM equipment of 1700000Lines (2G) 234100 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000092]	677.75	10/2009	461.56

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
January,2012				
<u>Railways</u>				
70	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)(WESTERN RAILWAY) - [220100322]	148.61	03/2008	260.07
<u>Road Transport & Highways</u>				
71	KASIA TO GORAKHPUR (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106291]	242.00	12/2008	434.10
72	SITAPUR-LUCKNOW(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000036]	322.00	06/2009	553.70
73	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000090]	418.04	03/2010	343.30
74	TRICHY - DINDIGUL NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000099]	576.00	07/2010	661.40
<u>Telecommunications</u>				
75	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3(BHARAT SANCHAR NIGAM LIMITED) - [N26000043]	1,799.94	09/2009	309.79
76	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN(BHARAT SANCHAR NIGAM LIMITED) - [N26000050]	335.91	03/2009	182.45
77	GSM equipment of 945000Lines (2G) 225000lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000086]	366.00	10/2008	227.39
78	GSM equipment of 1900000Lines (2G) 335500lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000094]	848.70	01/2010	712.86
February,2012				
<u>Coal</u>				
79	BARSINGSAR TPS (2 125MW) (NLC)(NEYVELI LIGNITE CORPORATION) - [060100089]	1,114.18	06/2009	1,714.72
<u>Power</u>				
80	EASTERN REGION STRENGTHENING SCHEME-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000033]	227.52	06/2010	140.70
81	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000062]	353.57	07/2010	221.20
<u>Road Transport & Highways</u>				
82	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106216]	412.78	11/2007	437.80

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2011				
<u>Civil Aviation</u>				
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97
January,2012				
<u>Power</u>				
2	TUIRIAL HE PROJECT(NEEPCO)(NORTH EAST ELECTRIC POWER CORPORATION) - [N16000049]	368.72	07/2006	295.47


Summary of projects in the Flash Report for the month of February, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	565
Number of Projects completed/dropped/frozen in Previous Month	10
Number of Projects completed/dropped/frozen in Current Month	4
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	3
Number of Projects Added in Current Month	12
Number of Projects in Current Month	566


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 566 projects, 4 projects are ahead of schedule, 159 projects are on schedule and 246 projects are delayed. Of the balance, 81 projects do not have fixed dates of commissioning while 76 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

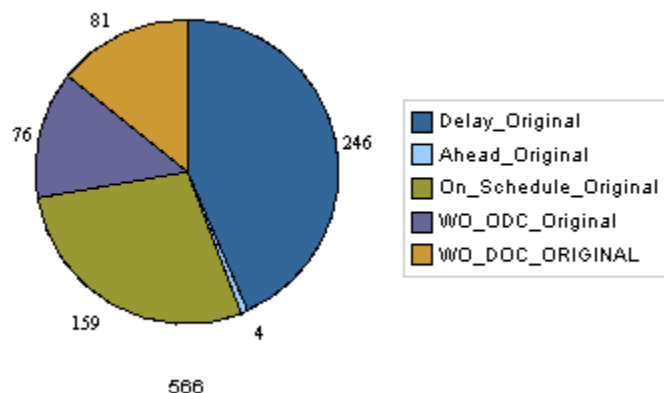

III. Investment Scenario

The Total Original cost of implementation of 566 projects when sanctioned, was of the order of Rs. 726749.77 crore but this was subsequently revised to Rs. 845950.57 crore implying a cost overrun of 16.4%. The expenditure incurred on these projects till February, 2012 is Rs. 372525.94 crore, which is 44% of the revised cost of the projects.

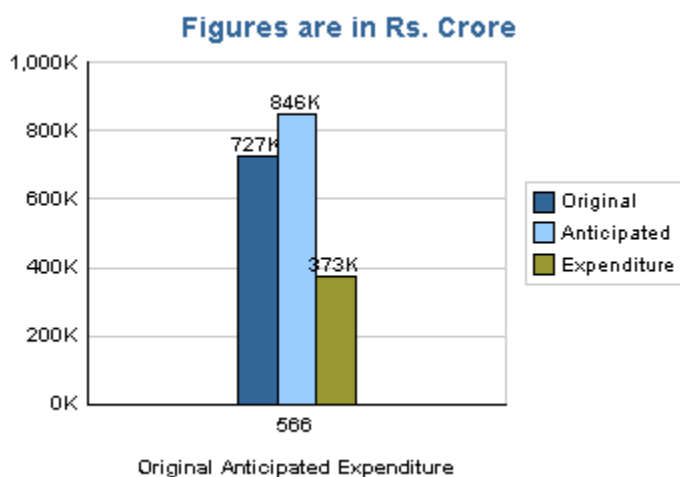

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	565
No of Projects Completed/Dropped/Frozen in Previous Month	10
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	3
No of Projects added in Current Month	12
No of Projects in Current Month	566

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	246	4	159	76	81	566	43.46
Latest Approved (Date)	257	7	206	45	53	566	45.41

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	447	588,444.15	631,252.35	247,221.33	39.20	42,808.20	7.30
Latest Approved (RCE)	119	192,922.48	214,698.22	125,304.61	58.40	21,775.74	11.30
Total (RCE)	566	781,366.63	845,950.57	372,525.94	44.04	64583.94	8.27
Original Cost of All Projects							
Original Cost	566	726,749.77	845,950.57	372,525.94	44.00	119,200.80	16.40

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	246	403,117.78	477,228.15	252,728.98	53.00	74,110.37	18.40
Latest Approved (RCE)	257	397,289.68	441,014.61	233,442.81	52.90	43,724.93	11.00
Total	503	800,407.46	918,242.76	486,171.79	52.95	117835.3	14.72

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	63	143,500.95	152,233.98	80,902.84	53.10	8,733.03	6.10
Total	63	143,500.95	152,233.98	80,902.84	53.14	8733.03	6.09

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	50	33,604.6	37,053.1	10.3	11	12,628.6	16,674.9	32.0
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	65,244.8	71,412.4	9.5	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	69	149,804.8	157,344.1	5.0	16	49,968.0	65,969.0	32.0
8	Power	99	203,409.9	218,750.9	7.5	19	42,231.6	57,637.4	36.5
9	Railways	131	65,286.3	134,407.2	105.9	101	37,605.2	106,782.9	184.0
10	Road Transport & Highways	135	79,768.5	81,624.3	2.3	13	3,826.3	6,251.2	63.4
11	Shipping & Ports	26	19,051.4	19,858.9	4.2	10	6,294.5	7,511.6	19.3
12	Telecommunications	18	8,443.6	8,559.9	1.4	3	1,315.9	1,514.8	15.1
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	726,749.8	845,950.6	16.4	187	210,825.1	340,288.4	61.4

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Proj- ects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	37	36,851.5	43,234.8	17.3	13	11,677.0	19,002.1	62.7
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	37	23,895.8	35,508.9	48.6	13	11,923.7	23,630.9	98.2
4	Bihar	31	30,278.5	35,051.8	15.8	14	12,952.4	17,725.6	36.9
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	27	32,792.3	33,045.3	0.8	5	2,413.7	2,875.2	19.1
7	Haryana	10	5,795.4	7,611.8	31.3	3	1,448.2	3,264.7	125.4
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	3	7,629.8	10,324.0	35.3
9	J and K	10	14,019.4	33,604.4	139.7	6	7,866.5	27,478.4	249.3
10	Karnataka	25	30,657.6	38,936.0	27.0	9	8,598.8	17,283.7	101.0
11	Kerala	7	6,086.2	6,775.2	11.3	2	795.7	1,587.2	99.5
12	Madhya pradesh	24	17,335.6	17,581.8	1.4	3	2,027.6	2,741.5	35.2
13	Maharashtra	52	70,396.4	83,640.3	18.8	18	29,685.2	45,706.8	54.0
14	Manipur	1	727.6	3,056.9	320.2	1	727.6	3,056.9	320.2
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	3	1,901.7	4,220.8	121.9	2	988.1	3,307.1	234.7
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	26	42,465.4	45,636.4	7.5	13	33,147.5	36,510.8	10.1
19	Punjab	7	4,613.2	5,598.2	21.4	3	761.4	1,746.5	129.4
20	Rajasthan	14	24,243.0	24,237.6	-0.0	3	570.8	950.0	66.4
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	35	52,241.3	61,099.8	17.0	13	27,364.2	36,222.7	32.4
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	24	17,544.0	21,597.8	23.1	9	3,729.2	7,783.0	108.7
25	West Bengal	25	37,585.8	46,969.4	25.0	12	20,281.1	29,664.7	46.3
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	26	58,044.3	61,275.6	5.6	7	4,746.6	7,977.9	68.1
28	Jharkhandd	22	14,396.5	15,999.9	11.1	6	1,897.3	3,672.5	93.6
29	Uttaranchal	5	9,815.9	11,738.4	19.6	3	3,942.3	5,864.9	48.8
30	Multi State	96	127,685.3	132,264.2	3.6	21	6,635.4	15,682.9	136.4
Total		566	726,749.8	845,950.6	16.4	187	210,825.1	340,288.4	61.4

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	3	36,950.0	39,603.0	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 23
3	Coal	50	33,604.6	37,053.1	10.3	18	11,310.7	14,299.7	12 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	8 - 9
5	Steel	16	65,244.8	71,412.4	9.5	6	49,832.9	55,396.9	3 - 36
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	149,804.8	157,344.1	5.0	37	102,089.7	110,505.3	1 - 120
8	Power	99	203,409.9	218,750.9	7.5	46	124,647.0	139,374.8	1 - 90
9	Railways	131	65,286.3	134,407.2	105.9	28	22,739.8	53,030.7	2 - 204
10	Road Transport & Highways	135	79,768.5	81,624.3	2.3	80	29,644.3	31,860.1	2 - 101
11	Shipping & Ports	26	19,051.4	19,858.9	4.2	12	10,100.4	10,737.2	1 - 93
12	Telecommunications	18	8,443.6	8,559.9	1.4	8	3,706.6	3,876.4	16 - 75
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	726,749.8	845,950.6	16.4	246	403,117.8	477,228.2	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	37	36,851.5	43,234.8	17.3	11	20,523.6	24,584.5	2 - 37
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	12 - 63
3	Assam	37	23,895.8	35,508.9	48.6	31	13,558.6	21,356.3	15 - 120
4	Bihar	31	30,278.5	35,051.8	15.8	10	22,923.4	23,749.0	5 - 62
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	3 - 3
6	Gujarat	27	32,792.3	33,045.3	0.8	7	15,308.1	15,331.1	11 - 31
7	Haryana	10	5,795.4	7,611.8	31.3	3	1,875.1	3,055.1	7 - 50
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	6	14,761.2	17,455.4	20 - 58
9	J and K	10	14,019.4	33,604.4	139.7	8	9,873.4	29,458.4	10 - 201
10	Karnataka	25	30,657.6	38,936.0	27.0	5	19,725.0	24,532.5	5 - 91
11	Kerala	7	6,086.2	6,775.2	11.3	4	5,049.0	4,946.5	2 - 52
12	Madhya pradesh	24	17,335.6	17,581.8	1.4	16	13,654.0	13,200.2	5 - 50
13	Maharashtra	52	70,396.4	83,640.3	18.8	23	45,842.6	54,318.3	1 - 42
14	Manipur	1	727.6	3,056.9	320.2	1	727.6	3,056.9	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	3	1,901.7	4,220.8	121.9	1	368.7	913.6	90 - 90
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	26	42,465.4	45,636.4	7.5	6	30,896.9	31,690.4	7 - 120
19	Punjab	7	4,613.2	5,598.2	21.4	4	1,591.9	1,721.9	7 - 51
20	Rajasthan	14	24,243.0	24,237.6	-0.0	5	19,197.2	19,178.9	3 - 47
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	23 - 23
22	Tamil Nadu	35	52,241.3	61,099.8	17.0	9	21,029.4	25,335.7	13 - 93
23	Tripura	3	1,522.4	2,053.2	34.9	0	0.0	0.0	-
24	Uttar Pradesh	24	17,544.0	21,597.8	23.1	14	11,381.9	13,483.0	5 - 87
25	West Bengal	25	37,585.8	46,969.4	25.0	16	24,829.4	30,961.8	2 - 132
26	Delhi	3	37,985.0	37,965.4	-0.1	1	249.0	229.4	61 - 61
27	Chhatisgarh	26	58,044.3	61,275.6	5.6	9	32,611.3	34,294.6	3 - 48
28	Jharkhandd	22	14,396.5	15,999.9	11.1	9	8,583.6	9,048.8	10 - 102
29	Uttaranchal	5	9,815.9	11,738.4	19.6	4	9,666.7	11,579.7	13 - 83
30	Multi State	96	127,685.3	132,264.2	3.6	38	48,888.8	49,363.3	1 - 204
Total		566	726,749.8	845,950.6	16.4	246	403,117.8	477,228.2	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	5	41,548.3	46,386.3	0 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 23
3	Coal	50	33,604.6	37,053.1	10.3	18	11,310.7	14,299.7	12 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	8 - 9
5	Steel	16	65,244.8	71,412.4	9.5	9	42,406.8	44,866.7	0 - 12
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	149,804.8	157,344.1	5.0	33	90,787.6	93,731.8	0 - 74
8	Power	99	203,409.9	218,750.9	7.5	41	114,540.0	124,814.6	1 - 66
9	Railways	131	65,286.3	134,407.2	105.9	35	15,618.0	48,580.4	0 - 213
10	Road Transport & Highways	135	79,768.5	81,624.3	2.3	81	29,840.8	32,056.6	0 - 101
11	Shipping & Ports	26	19,051.4	19,858.9	4.2	14	10,475.5	11,239.9	1 - 93
12	Telecommunications	18	8,443.6	8,559.9	1.4	13	6,315.4	6,494.7	7 - 75
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	726,749.8	845,950.6	16.4	257	374,939.5	441,014.6	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	50	35,232.3	37,053.1	5.2	8	7,991.2	10,279.7	28.6
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	71,120.1	71,412.4	0.4	3	598.0	910.3	52.2
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	69	163,049.4	157,344.1	-3.5	3	32,036.9	32,844.0	2.5
8	Power	99	208,224.6	218,750.9	5.1	12	34,160.8	44,752.0	31.0
9	Railways	131	89,833.8	134,407.2	49.6	80	45,931.4	90,796.4	97.7
10	Road Transport & Highways	135	79,935.0	81,624.3	2.1	13	3,826.3	6,251.2	63.4
11	Shipping & Ports	26	19,662.7	19,858.9	1.0	7	5,040.8	5,547.1	10.0
12	Telecommunications	18	8,447.5	8,559.9	1.3	1	250.0	425.5	70.2
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	781,366.6	845,950.6	8.3	132	155,378.7	228,428.1	47.0

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	0	0.00	0.00	0- 0
3	Coal	50	33,604.55	37,053.10	10.26	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	1	8,692.00	12,291.00	36- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	149,804.77	157,344.05	5.03	4	6,562.12	11,590.06	34- 120
8	Power	99	203,409.93	218,750.90	7.54	2	2,025.72	3,892.49	67- 90
9	Railways	131	65,286.30	134,407.18	105.87	2	1,624.47	4,619.99	62- 92
10	Road Transport & Highways	135	79,768.48	81,624.31	2.33	0	0.00	0.00	0- 0
11	Shipping & Ports	26	19,051.36	19,858.93	4.24	1	277.03	277.03	8- 8
12	Telecommunications	18	8,443.59	8,559.89	1.38	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		566	726749.77	845950.57	16.40	11	19651.12	33376.97	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	1	13,171.00	15,824.00	51- 51
2	Civil Aviation	5	5,021.58	5,611.07	11.74	2	3,750.51	4,340.00	13- 17
3	Coal	50	33,604.55	37,053.10	10.26	6	5,699.06	9,285.81	19- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	2	23,135.00	28,699.00	12- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	149,804.77	157,344.05	5.03	12	46,873.51	61,425.00	6- 120
8	Power	99	203,409.93	218,750.90	7.54	17	41,214.12	56,006.81	7- 90
9	Railways	131	65,286.30	134,407.18	105.87	18	10,483.03	40,778.80	12- 204
10	Road Transport & Highways	135	79,768.48	81,624.31	2.33	13	3,826.28	6,251.20	7- 99
11	Shipping & Ports	26	19,051.36	19,858.93	4.24	6	4,314.81	5,262.56	1- 93
12	Telecommunications	18	8,443.59	8,559.89	1.38	2	1,166.70	1,356.11	16- 75
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	24- 24
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		566	726749.77	845950.57	16.40	81	160571.92	242025.29	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Coal</u>						
BARSINGSAR TPS (2 125MW) (NLC)	12/2004	1,114.18	06/2009	1,868.71	01/2012	1,714.72
<u>Power</u>						
TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS	02/2009	353.57	07/2010	353.57	02/2012	221.20
EASTERN REGION STRENGTHENING SCHEME-II	12/2007	227.52	06/2010	227.52	02/2012	140.70
<u>Road Transport & Highways</u>						
GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	12/2003	412.78	11/2007	479.54	02/2012	437.80

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Power</u>					
SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P	2/2012	1,310.85	2/2015	1,310.85	2/2015
TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART	2/2012	324.33	8/2014	324.33	8/2014
TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART	2/2012	1,927.16	10/2014	1,927.16	10/2014
<u>Road Transport & Highways</u>					
JORBAT - BARAPANI	1/2011	536.00	1/2014	536.00	1/2014
2-LANNING OF SHILONG BYPASS	2/2011	226.00	2/2014	226.00	2/2014
VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	2,848.00	3/2014	2,848.00	3/2014
SIX LANNING OF NELLORE-CHILKALURIPET	11/2011	1,535.00	5/2014	1,535.00	5/2014
2-LANNING WITH PS KHAGARIA-PURNEA	5/2011	664.00	2/2014	664.00	2/2014
PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	574.00	3/2014	574.00	3/2014
2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	375.09	4/2014	375.09	4/2014
4-LANNING OF CHAPRA-HAJIPUR	1/2011	575.00	7/2013	575.00	7/2013
2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	511.54	11/2013	511.54	11/2013

VII. Milestones (Cumulative due & achieved)

Total	2463
Achieved up to month	939

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Civil Aviation</u>						
C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT AAI	1,942.51	2,325.00	05/2011	03/2012	10/2012	7
<u>Coal</u>						
PENGANGA OC WCL	339.77	339.77	N.A.	10/2014	03/2015	5
ADRIYALA SHAFT PROJECT SCCL	212.34	779.26	03/2013	12/2013	10/2014	10
RAMAGUNDAM OC-II EXTENSION SCCL	418.97	418.97	03/2012	03/2012	03/2013	12
MANUGURU OC-II EXTENSION PHASE-II SCCL	181.19	181.19	03/2012	03/2012	03/2013	12
<u>Steel</u>						
Rebuilding of coke oven battery No.1 and 2 (Bokar SAIL	500.90	500.90	N.A.	01/2012	02/2012	1
67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	N.A.	04/2012	06/2012	2
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	03/2012	05/2012	2
700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI SAIL	232.93	232.93	05/2011	02/2012	05/2012	3
EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	06/2013	09/2013	3
EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2012	03/2013	3
EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	03/2012	10/2012	7
EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	12/2011	03/2012	12/2012	9
<u>Petroleum</u>						
INTEGRATED DEV OF G1 and GS-15 (ONGCL) ONGC	429.82	2,218.01	04/2006	05/2012	06/2012	1
MNW-NF BRIDGE PROJECT ONGC	175.21	162.12	03/2009	01/2012	02/2012	1
COMPRESSOR STATIONS (KAILARAS AND CHAINSA) GAIL	1,167.00	798.00	04/2011	03/2012	04/2012	1
KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC GAIL	348.00	261.00	03/2012	03/2012	04/2012	1


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
Development of Cluster-7 Fields ONGC	3,241.03	3,241.03	03/2013	03/2013	04/2013	1
Development of BHE and BH-35 Area. ONGC	372.11	372.11	03/2013	03/2013	04/2013	1
DEVELOPMENT OF B-46 CLUSTER FIELD ONGC	1,436.21	1,436.21	07/2010	05/2012	07/2012	2
Development of SB-14 field ONGC	410.44	410.44	11/2012	01/2013	05/2013	4
MRPL Phase-III Expansion Mangalore Refin	12,412.00	12,160.26	01/2012	01/2012	06/2012	5
Construction of 23 Immediate Supply Vessels (ISV) ONGC	331.20	269.10	08/2013	08/2013	01/2014	5
ADDITIONAL DEV. OF D-1 FIELD ONGC	2,163.64	2,163.64	06/2012	06/2012	12/2012	6
Construction of one Multipurpose Support Vessel ONGC	723.64	723.64	03/2013	03/2013	11/2013	8
102 MW WIND POWER PROJECT ONGC	1,106.00	1,106.00	06/2012	06/2012	04/2013	10
MUMBAI HIGH NORTH DEVELOPMENT PHASE-II ONGC	7,133.39	6,855.93	09/2012	09/2012	09/2013	12
REFRIGERATED LPG STORAGE AT JNPT BPCL	304.40	304.40	09/2010	09/2010	09/2011	12
DEVELOPMENT OF C-SERIES FIELDS ONGC	3,195.16	2,800.00	N.A.	03/2012	04/2013	13
DEVELOPMENT OF B-22 CLUSTER FIELDS ONGC	2,323.40	2,920.82	09/2010	03/2012	04/2013	13
DEVELOPMENT OF B-193 CLUSTER FIELDS ONGC	3,248.78	5,633.44	08/2010	06/2012	12/2013	18
Power						
CHAMERA,STAGE-III (NHPC) NHPC	1,405.63	2,084.00	08/2010	03/2012	04/2012	1
WESTERN REGION STRENGTHENING SCHEME-X PGCIL	664.96	664.96	02/2012	02/2012	03/2012	1
INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P PGCIL	1,391.97	1,391.97	12/2013	11/2013	12/2013	1
URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	1,794.00	11/2009	06/2012	08/2012	2
MOUDA STPP (NTPC) NTPC	5,459.28	6,010.89	08/2012	01/2013	03/2013	2
BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	09/2014	12/2014	3
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	557.24	01/2010	06/2012	09/2012	3
BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	10/2013	01/2014	3


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
VINDHYACHAL STTP STAGE-IV (NTPC) NTPC	5,915.00	5,915.00	10/2012	12/2012	03/2013	3
RIHAND STTP STAGE-III (2X500MW) (NTPC) NTPC	6,230.81	6,230.81	10/2012	12/2012	03/2013	3
BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	06/2011	10/2013	04/2014	6
CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.26	913.25	02/2011	05/2012	12/2012	7
KUDANKULAM-APP TRANS. SYSTEM (PGCIL) PGCIL	1,779.29	1,779.29	09/2008	06/2012	03/2013	9
<u>Railways</u>						
Ratlam-Mhow-Khandwa-Akola (GC) WR	603.04	603.04	03/2012	03/2012	03/2013	12
Ramanagram-Mysore doubling with electrification of SWR	482.00	482.70	03/2013	12/2011	03/2013	15
<u>Road Transport & Highways</u>						
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	02/2012	03/2012	1
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	N.A.	02/2012	03/2012	1
DEVIHALLI-HASSAN NHAI	453.00	453.00	N.A.	05/2013	06/2013	1
HALDIA PORT (PORT CONNECTIVITY) (NH-41) NHAI	273.00	522.00	03/2005	01/2012	03/2012	2
SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 NHAI	941.00	941.00	01/2011	03/2012	05/2012	2
HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 NHAI	212.00	386.10	09/2007	12/2013	04/2014	4
HARANGAJO TO MAIBANG, NH-54 NHAI	196.00	363.74	07/2009	12/2013	04/2014	4
CHITRADURGA- TUMKUR(NH-4) NHAI	839.00	839.00	N.A.	08/2013	12/2013	4
BELGAUM-DHARWAD(NH-4) NHAI	480.00	480.00	N.A.	06/2013	10/2013	4
UGRADATION OF HYDERABAD-BANGALORE SECTION NHAI	680.00	680.00	N.A.	11/2012	04/2013	5
GWALIOR-JHANSI, NH-75 NHAI	604.00	604.00	12/2009	06/2012	12/2012	6
JHANSI TO LALITPUR, NH- 25,26 NHAI	355.06	355.06	09/2009	02/2012	12/2012	10
4 LANNING OF BELGUM- KHANPUR SECTION AND 2 LANING NHAI	359.00	359.00	09/2013	09/2013	07/2014	10

Trend and Graphical Analysis of All Projects

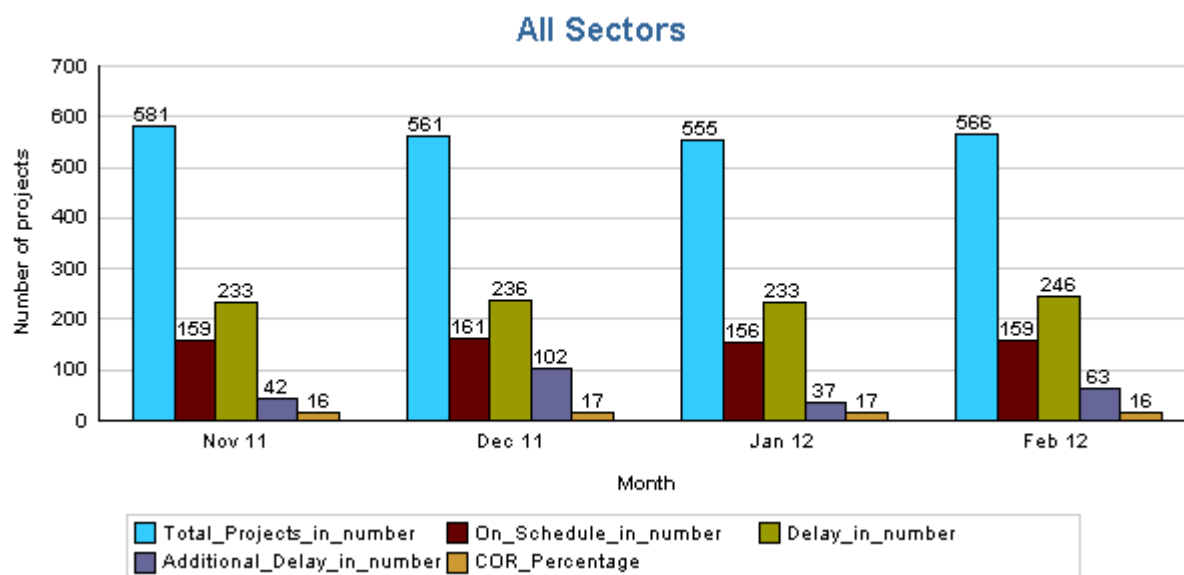


All Sectors Break-up of 246 Delayed projects in February 2012

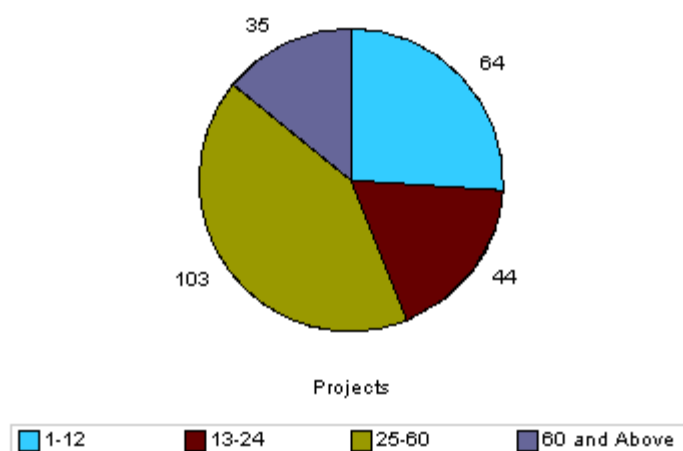


Trend and Graphical Analysis

Power Sector

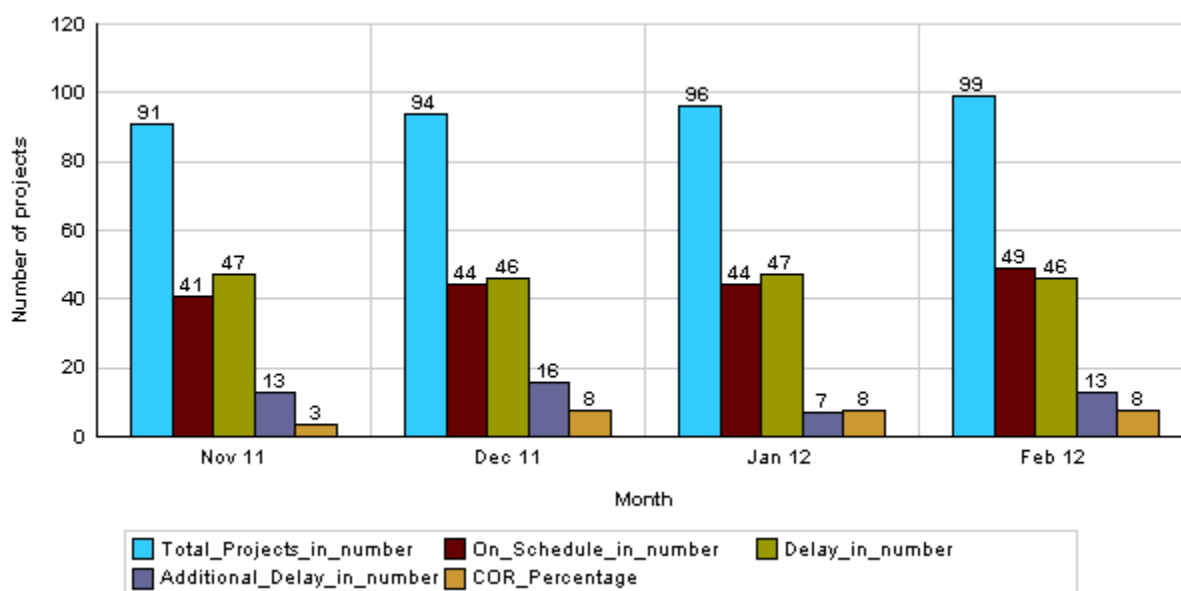


Power Sector Sector Break-up of 46 Delayed projects in February 2012

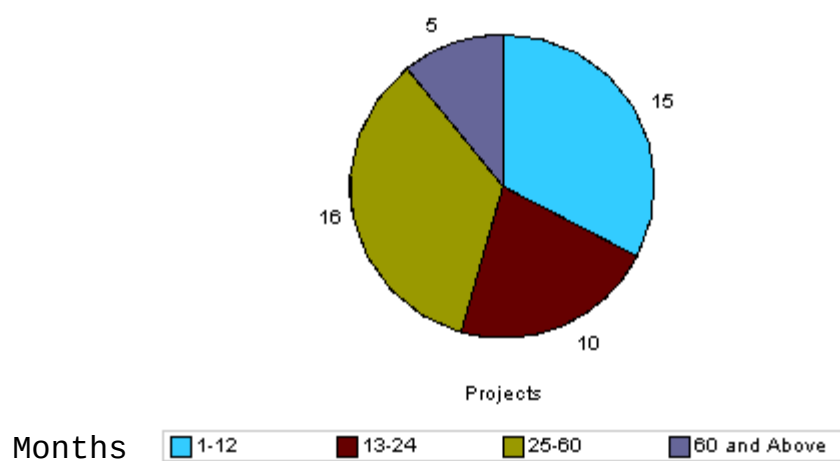


Trend and Graphical Analysis


Urban Development Sector

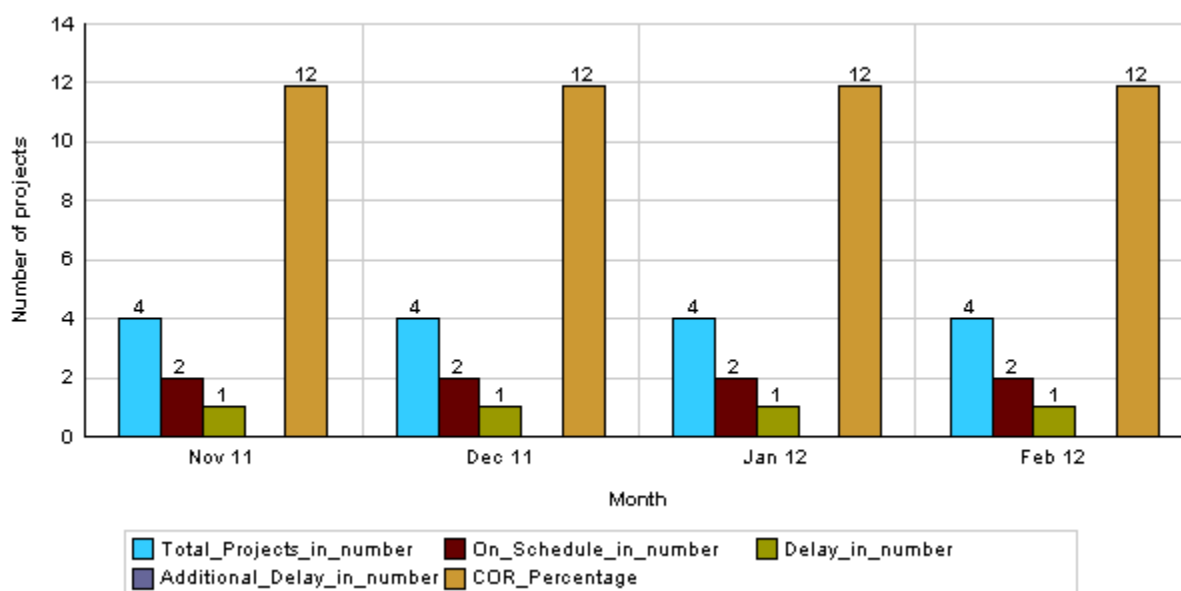


Urban Development Sector Break-up of 1 Delayed projects in February 2012

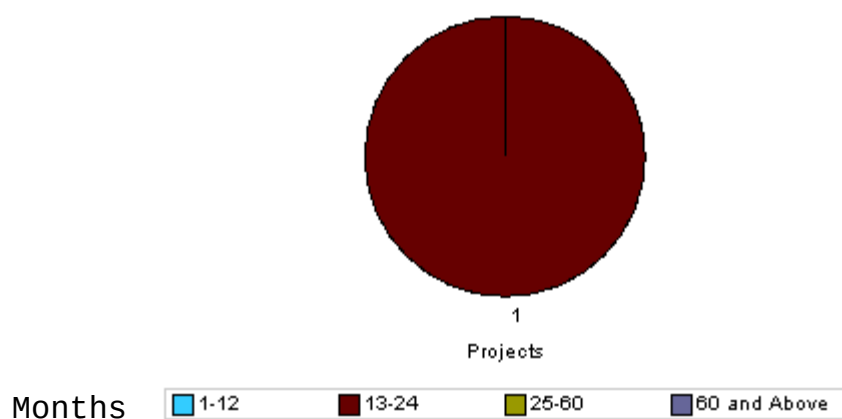


Trend and Graphical Analysis Shipping and Ports Sector

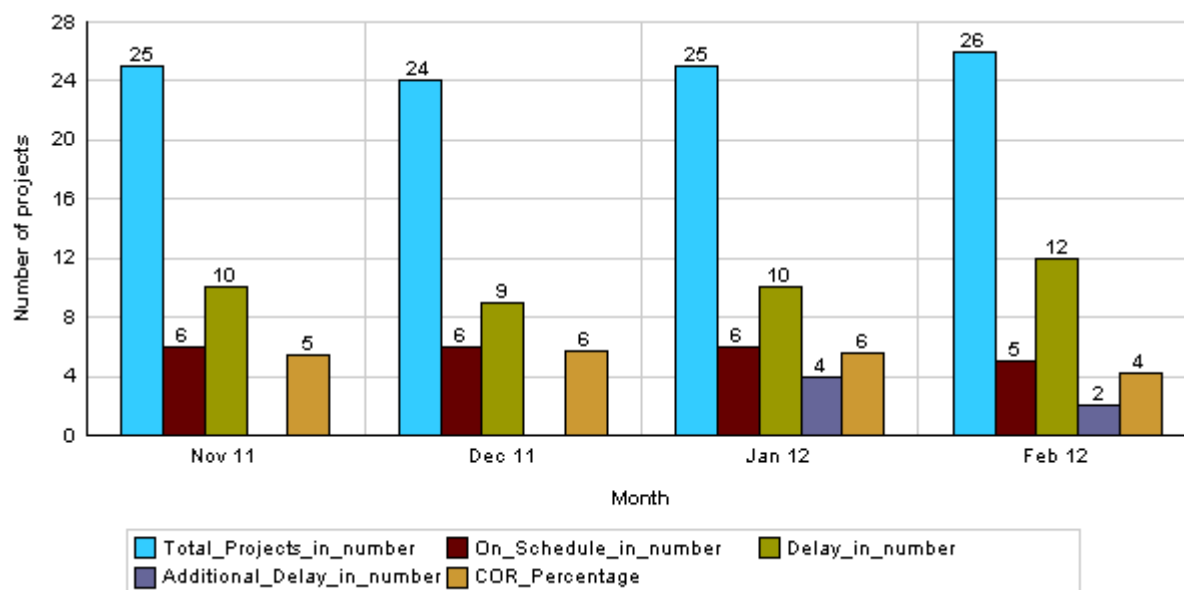


Sector Break-up of 12 Delayed projects in February 2012

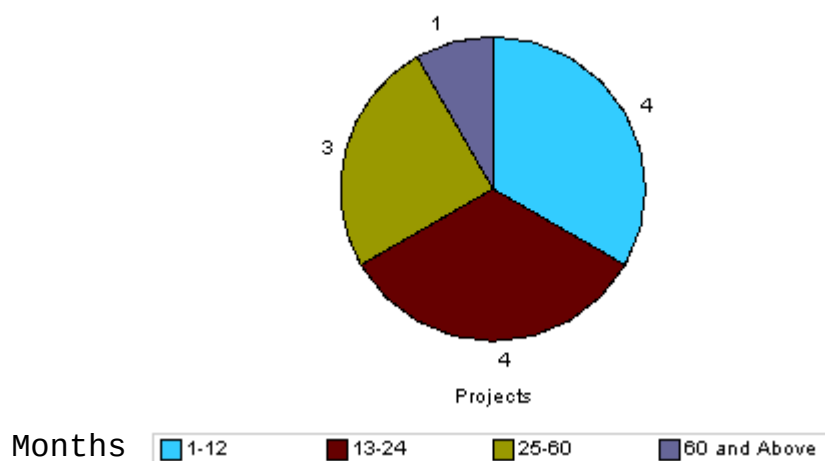

Trend and Graphical Analysis Road Transport and Highways Sector

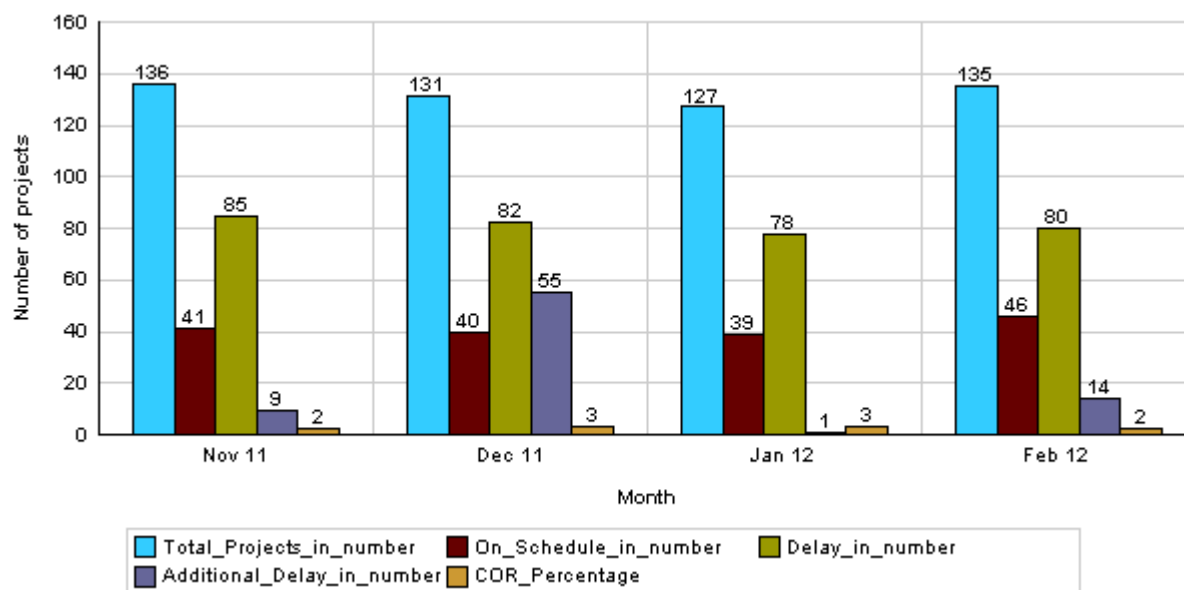


Sector Break-up of 80 Delayed projects in February 2012

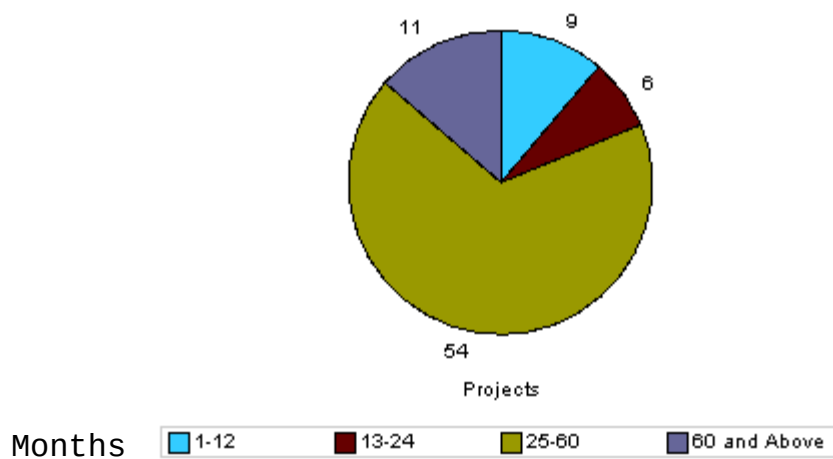


Trend and Graphical Analysis

Railways Sector

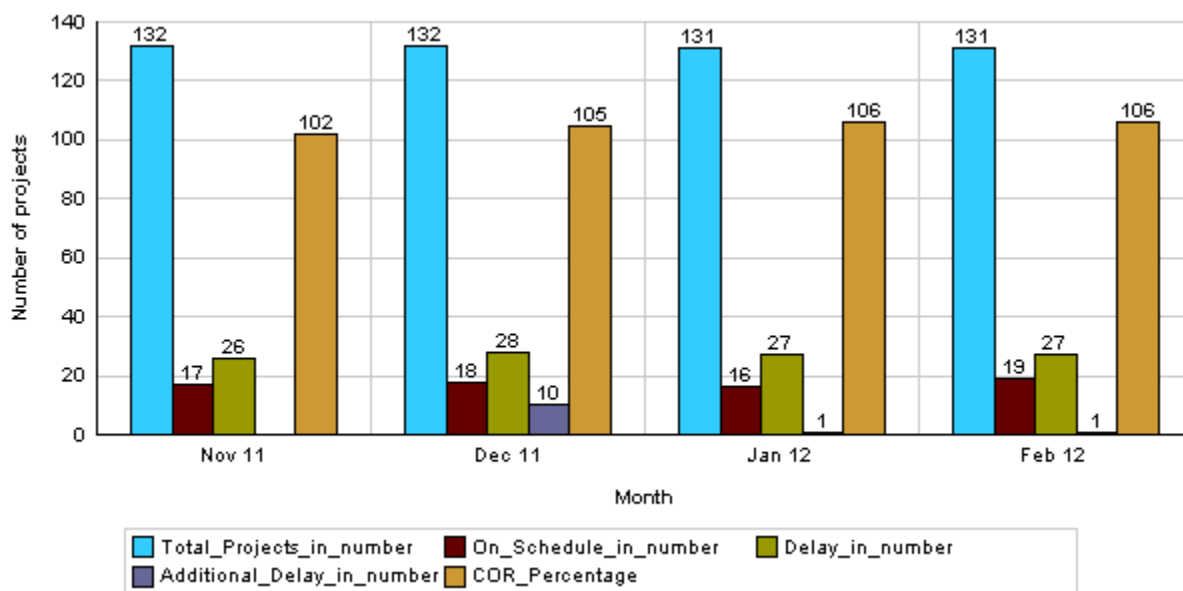


Railways Sector Sector Break-up of 27 Delayed projects in February 2012

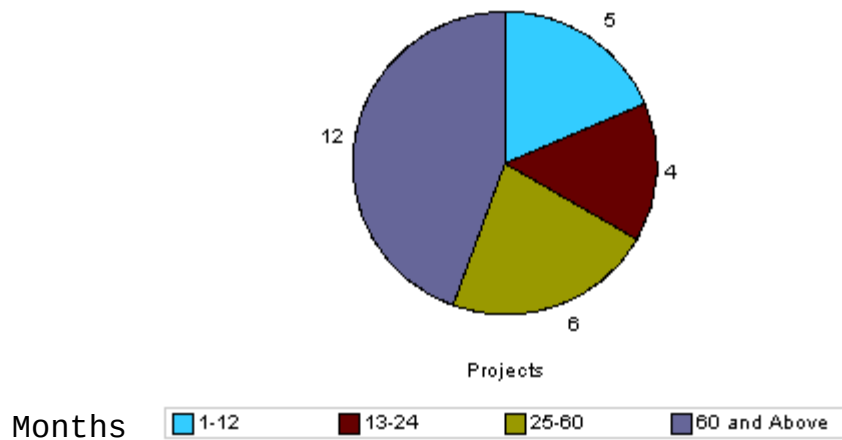


Trend and Graphical Analysis

Petroleum Sector

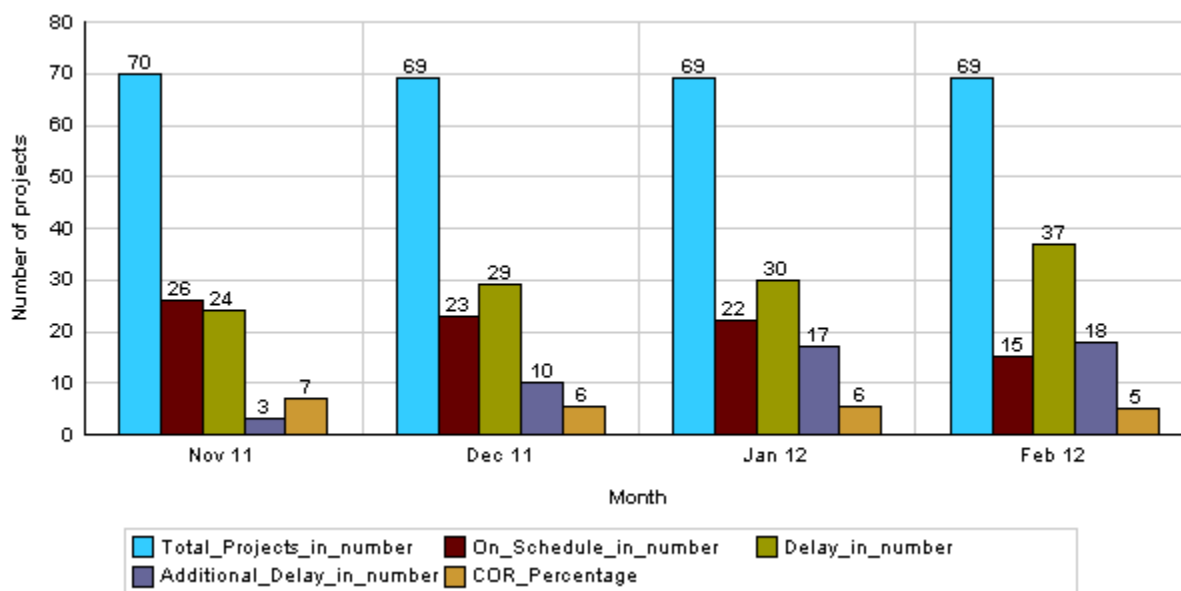


Petroleum Sector Sector Break-up of 37 Delayed projects in February 2012

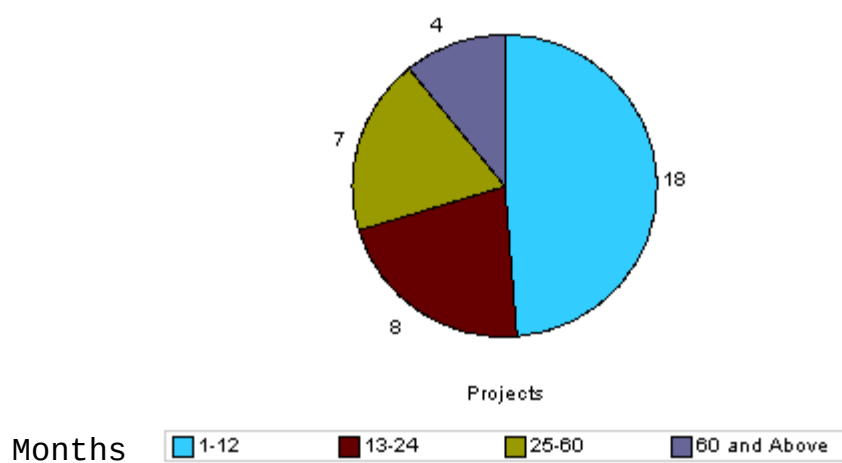


Trend and Graphical Analysis

Steel Sector

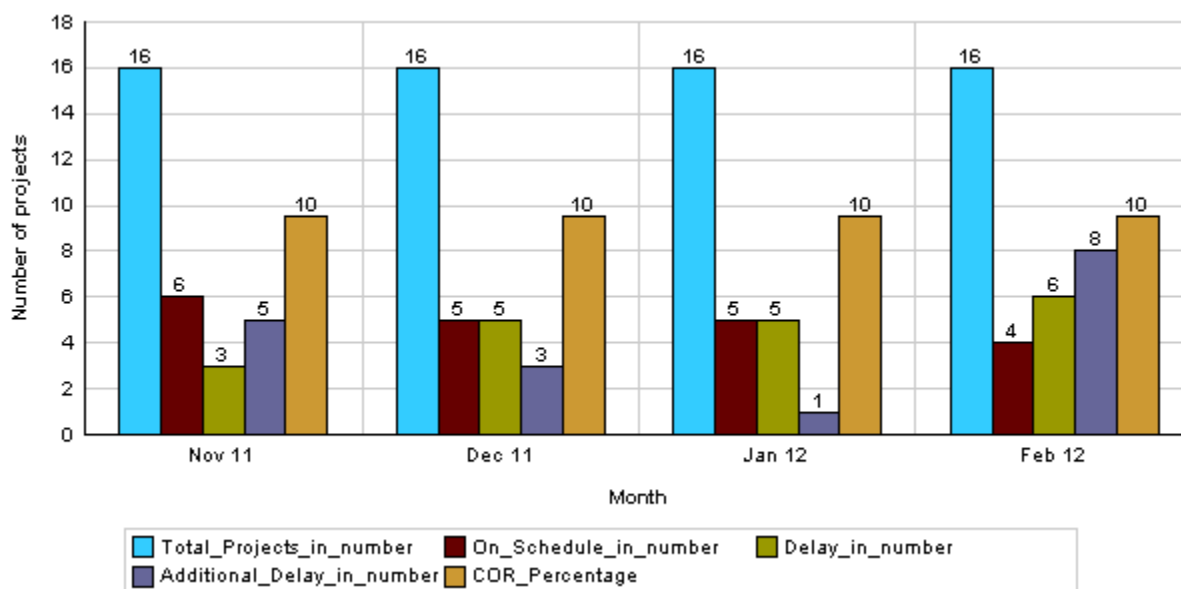


Steel Sector Break-up of 6 Delayed projects in February 2012

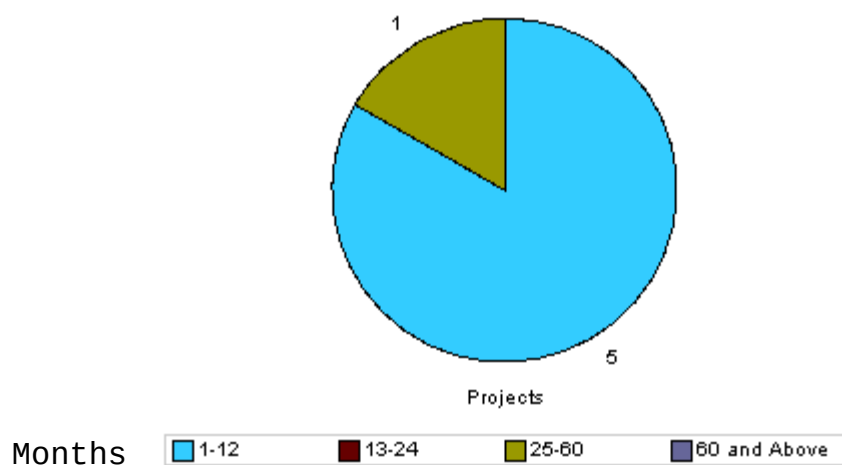


Trend and Graphical Analysis

Fertilisers Sector

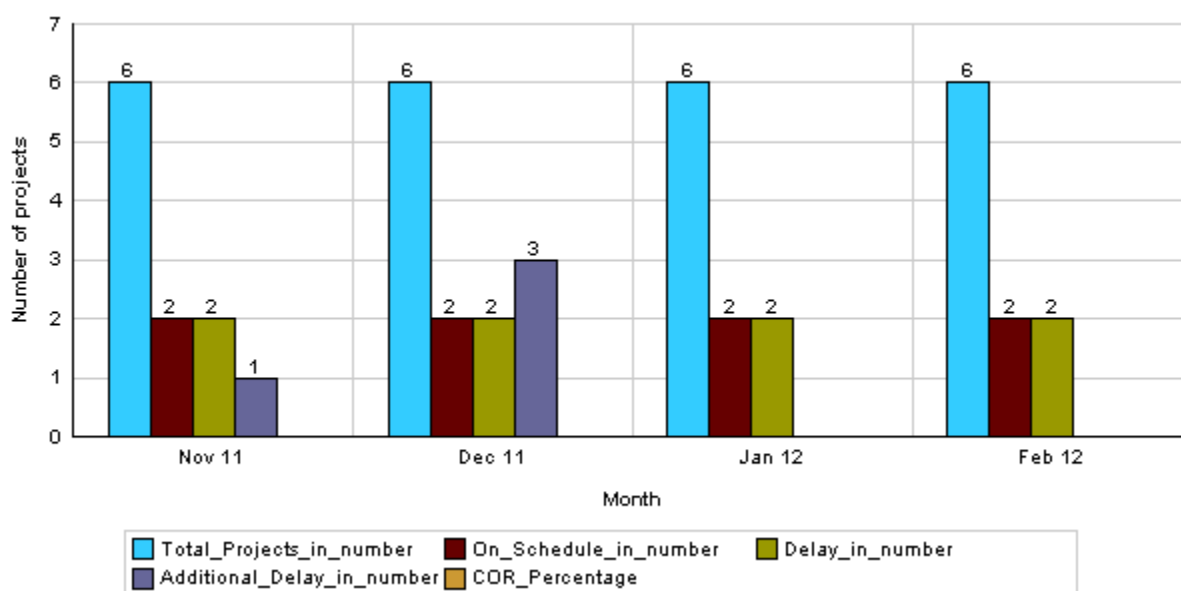


Fertilisers Sector Break-up of 2 Delayed projects in February 2012

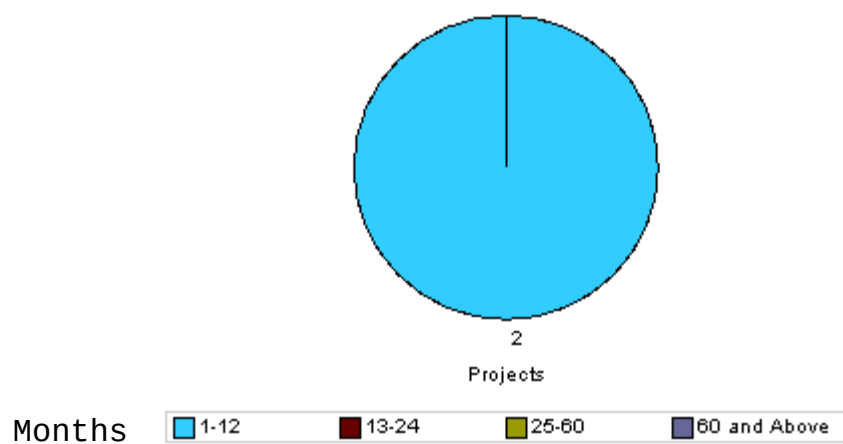


Trend and Graphical Analysis

Coal Sector

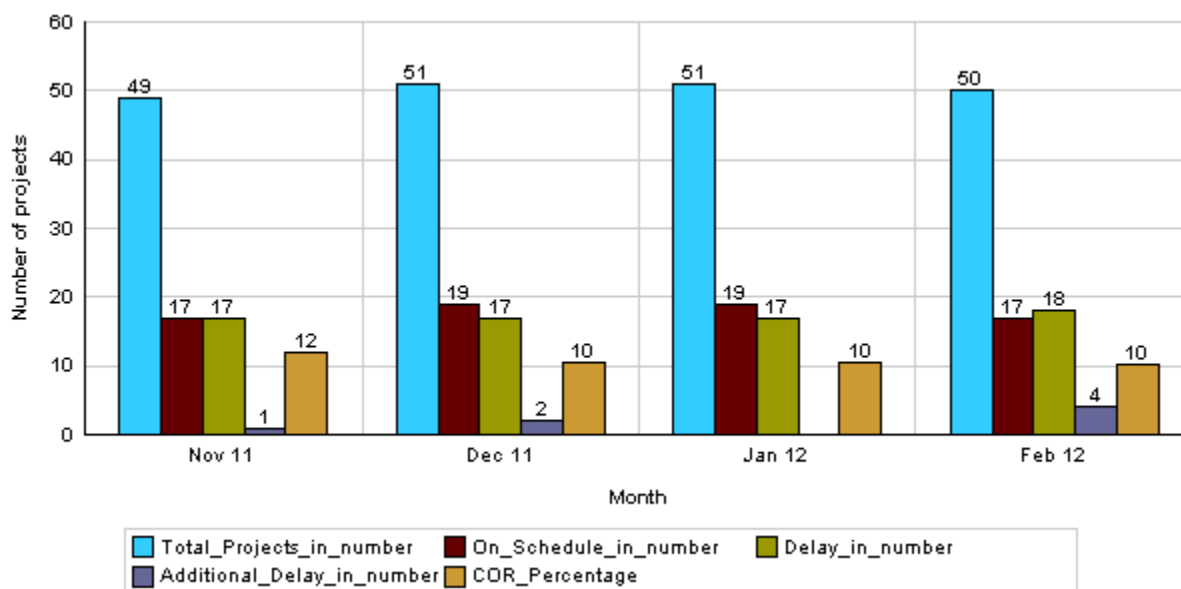


Coal Sector Sector Break-up of 18 Delayed projects in February 2012

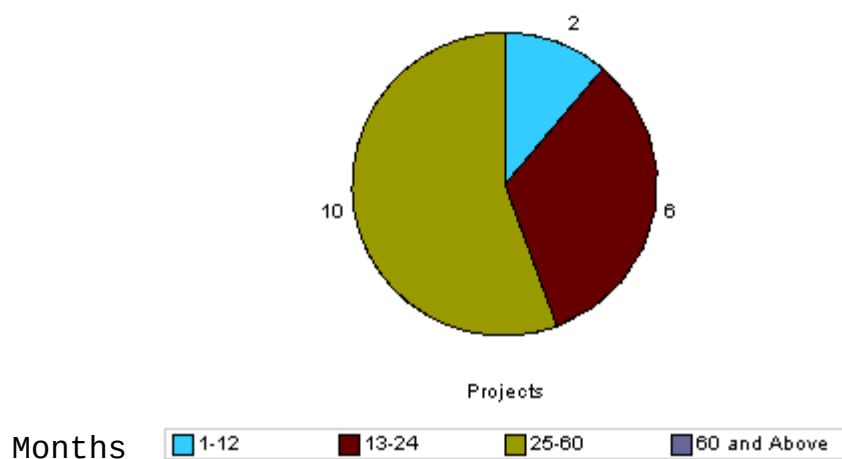


Trend and Graphical Analysis

Civil Aviation Sector

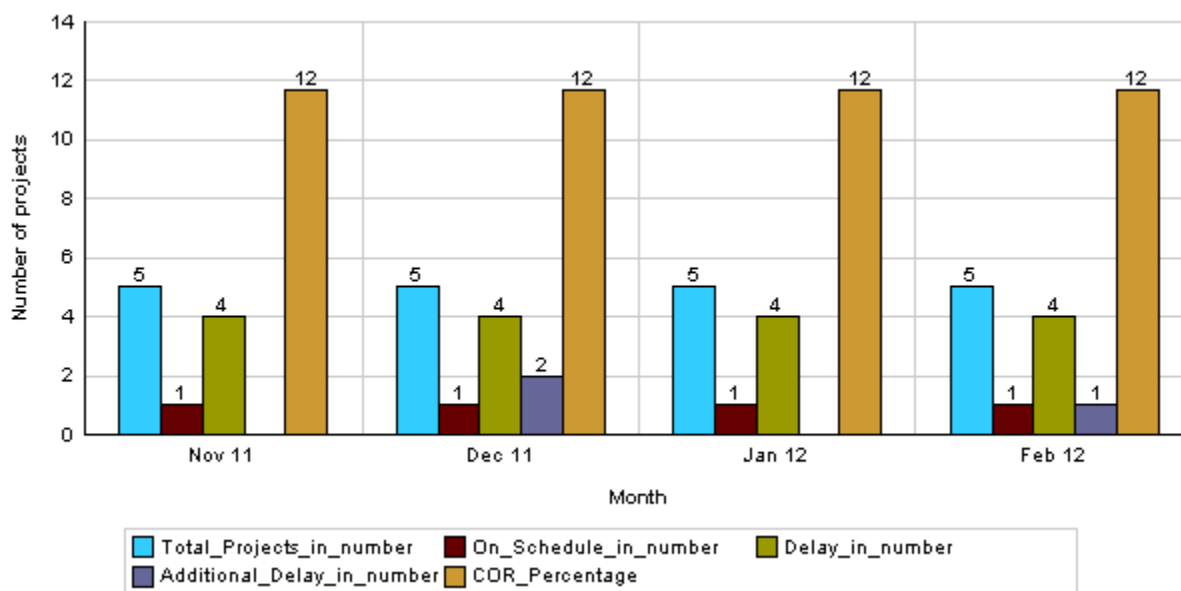


Civil Aviation Sector Break-up of 4 Delayed projects in February 2012

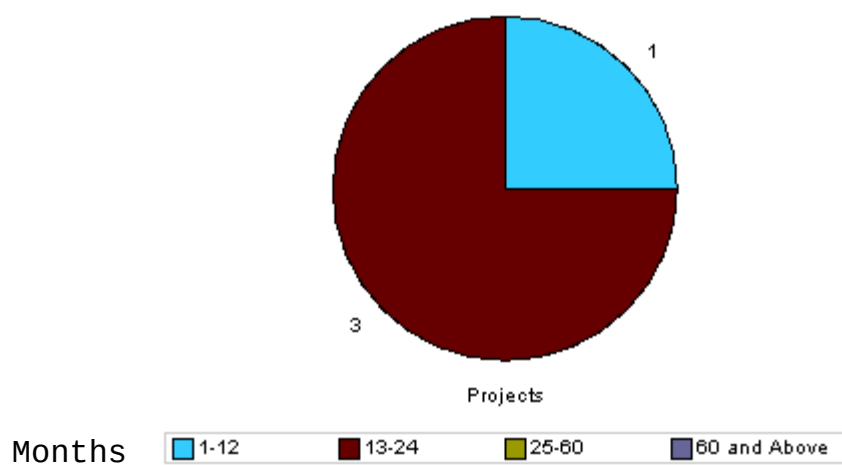


Trend and Graphical Analysis

Atomic Energy Sector

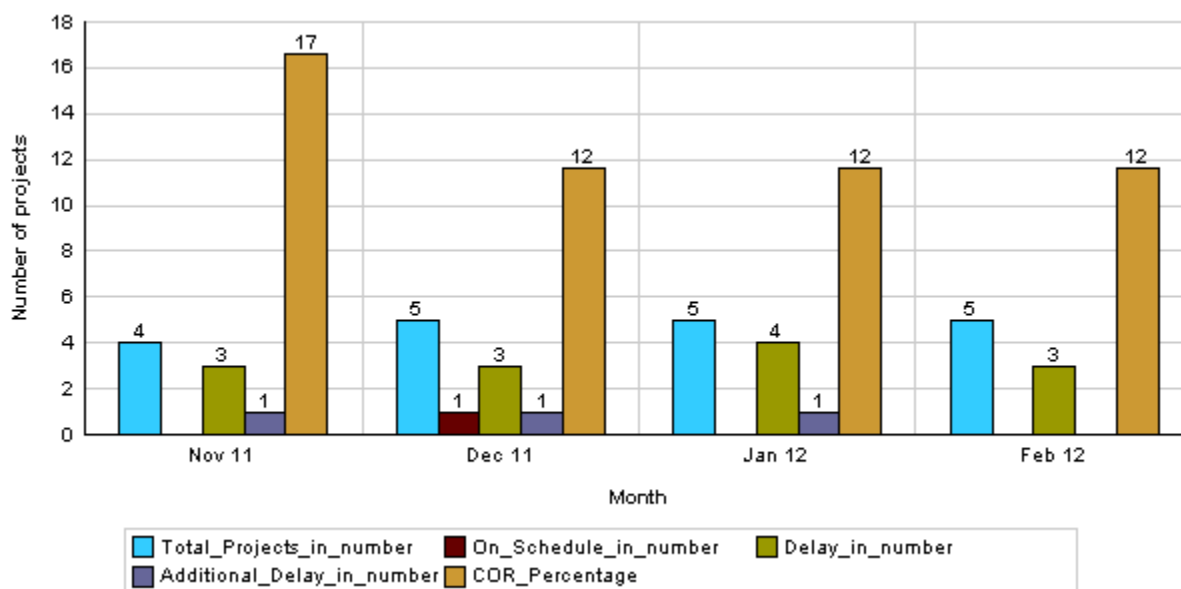


Atomic Energy Sector Sector Break-up of 3 Delayed projects in February 2012

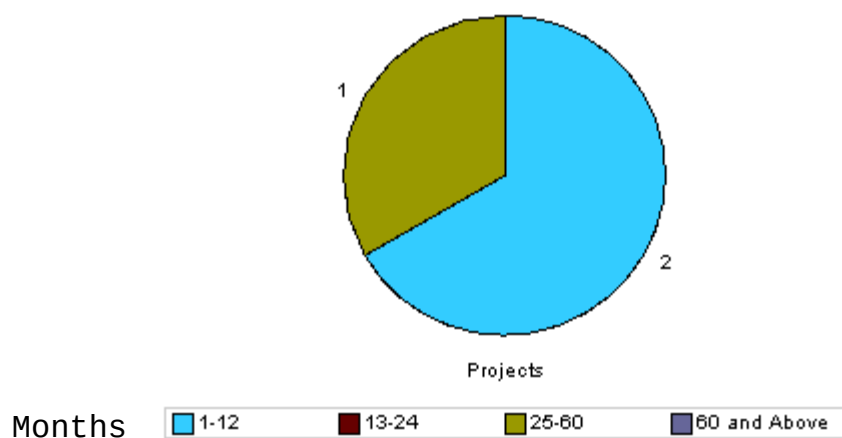


Trend and Graphical Analysis

Telecommunications Sector

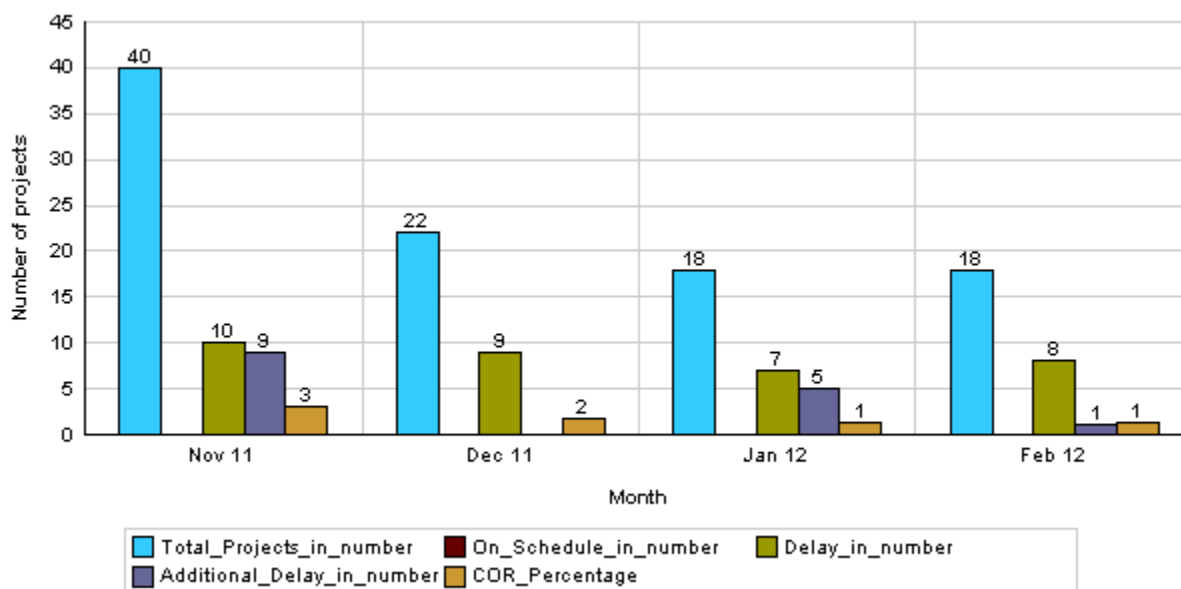

Telecommunications Sector Break-up of 8 Delayed projects in February 2012

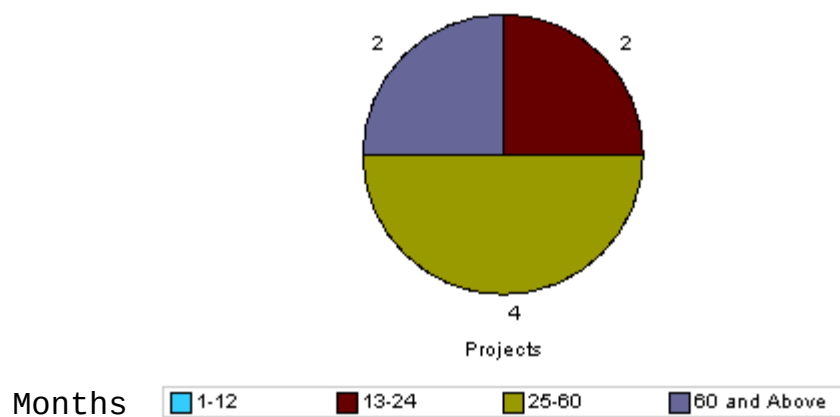

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	41,548.29	41,548.29	46,386.29
Civil Aviation	5	5,021.58	5,228.58	5,611.07
Coal	50	33,604.55	35,232.28	37,053.10
Fertilisers	6	5,317.41	5,317.41	5,317.41
Steel	16	65,244.82	71,120.10	71,412.36
Petrochemicals	1	5,460.61	8,920.00	8,920.00
Petroleum	69	149,804.77	163,049.42	157,344.05
Power	99	203,409.93	208,224.61	218,750.90
Railways	131	65,286.30	89,833.84	134,407.18
Road Transport & Highways	135	79,768.48	79,934.98	81,624.31
Shipping & Ports	26	19,051.36	19,662.67	19,858.93
Telecommunications	18	8,443.59	8,447.47	8,559.89
Urban Development	4	44,245.18	44,304.08	49,518.08
Water Resources	1	542.90	542.90	1,187.00
Grand total	566	726,749.77	781,366.63	845,950.57

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,418.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,326.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,410.82	09/2010	01/2012	16(O)	5/80
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	888.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/0
Total			41,548.29	46,386.29	21,043.52				44/325
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,770.64	05/2011	10/2012	17(O)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	178.46	01/2011	12/2012	23(O)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	86.87	05/2012	08/2012	3(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,631.72	01/2011	02/2012	13(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	344.55	06/2013	06/2013	0(O)	0/0
Total			5,021.58	5,611.07	4,012.24				0/0
<u>Coal</u>									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	249.11	03/2013 09/2012	10/2014	25(R3)	6/22
12	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	91.95	03/2016	03/2016	0(O)	0/1
13	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	276.55	03/2014	03/2016	24(O)	2/2

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	70.06	-	03/2012	-	5/7
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66	341.63	107.77	03/2011	03/2013	12(R3)	0/2
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	100.45	-	03/2010	-	4/4
17	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	105.16	-	03/2017	-	6/12
18	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.35	03/2014	03/2014	0(O)	1/2
19	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	155.37	03/2012	03/2015	36(O)	0/0
20	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
21	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	262.24	-	03/2014	-	0/4
22	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	33.66	03/2011	03/2014	24(R3)	1/2
23	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	1,182.40	03/2010	03/2014	48(O)	0/13
24	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,318.96	03/2010	03/2014	48(O)	0/15
25	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	59.22	-	03/2015	-	2/12
26	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	91.20	-	03/2013	-	5/7
27	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	1/1
28	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	-	03/2015	-	0/31
29	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013	03/2013	0(O)	3/83
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	0/1
31	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	71.46	12/2012	03/2015	27(O)	7/44
32	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	117.04	-	03/2013	-	6/11
33	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	31.63	03/2014	03/2014	0(O)	0/0
34	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/1
35	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	-	03/2018	03/2018	0(O)	0/0
36	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88	741.62	330.54	03/2010	03/2013	36(O)	2/2

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	87.87	03/2010	03/2012	24(O)	9/11
38	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	623.41	-	03/2013	-	0/8
39	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
40	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	18.16	07/2012	03/2016	24(R3)	1/2
41	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	209.33	-	03/2014	-	0/5
42	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	36.68	03/2012	03/2013	12(O)	8/34
43	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	1,230.27	-	04/2015	04/2015	0(O)	0/0
44	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	339.88	-	04/2014	04/2014	0(O)	0/0
45	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	6.57	-	12/2015	-	0/33
46	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	0.95	03/2012	03/2012	0(O)	0/1
47	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	62.45	03/2012	03/2014	24(R3)	0/2
48	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
49	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.70	-	03/2015	-	0/1
50	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98	210.98	32.02	03/2013	03/2013	0(O)	0/2
51	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08	153.82	19.96	03/2011	03/2014	36(O)	0/1
52	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	80.13	03/2012	03/2013	12(O)	21/27
53	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.21	-	03/2015	-	0/29
54	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78	209.78	21.53	03/2015	03/2015	0(O)	4/31
55	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	282.99	03/2016	03/2016	0(O)	1/2
56	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	43.19	03/2012	03/2012	0(O)	11/41
57	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	34.28	-	03/2016	-	1/12
58	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78	3,027.00	2,374.35	06/2009	07/2012	37(O)	19/24

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,570.74	- -	02/2013	-	0/39
60	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	94.75	03/2012 03/2013	03/2014	12(R3)	0/2
	Total		33,604.55 -	37,053.10	11,308.70				126/616
Fertilisers									
61	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	449.32	01/2013 -	01/2013	0(O)	0/5
62	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	168.93	07/2011 -	04/2012	9(O)	0/0
63	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	151.41	07/2011 -	03/2012	8(O)	0/0
64	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	449.28	- 01/2013	01/2013	0(R3)	8/8
65	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	386.72	01/2013 -	01/2013	0(O)	0/5
66	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	488.75	275.67	- 04/2012	04/2012	0(R3)	7/22
	Total		5,317.41 -	5,317.41	1,881.33				15/40
Steel									
67	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
68	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	232.76	- 08/2010	05/2012	21(R3)	0/1
69	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	240.27	- 02/2011	06/2012	16(R3)	2/3
70	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
71	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 -	232.93	183.65	05/2011 -	05/2012	12(O)	1/1
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	460.00	178.25	- 05/2012	12/2012	7(R3)	1/2
73	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	317.49	- 12/2011	03/2012	3(R3)	15/21
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	63.54	- 10/2012	10/2012	0(R3)	3/4

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
75	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55	254.55	3.05	11/2013	11/2013	0(O)	0/0
76	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00	17,265.00	4,758.04	03/2013	09/2013	6(O)	18/20
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00	6,325.00	2,419.04	12/2011	10/2012	10(O)	10/11
78	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, Chhatisgarh	06/2009	2,875.00	2,875.00	603.24	12/2012	03/2013	3(O)	5/6
79	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00	16,408.00	12,800.19	12/2011	12/2012	12(O)	13/14
80	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00	12,291.00	9,405.92	10/2009	10/2012	0(R3)	57/59
81	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Chhatisgarh	09/2008	11,812.00	11,812.00	6,478.70	03/2013	03/2013	0(O)	5/8
82	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL, Jharkhand)	10/2007	500.90	500.90	355.21	-	02/2012	-	3/3
Total			65,244.82	71,412.36	38,039.35				133/153
Petrochemicals									
83	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61	8,920.00	3,968.16	-	12/2013	0(R3)	9/30
Total			5,460.61	8,920.00	3,968.16	12/2013			9/30
Petroleum									
84	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00	1,106.00	-	06/2012	04/2013	10(O)	0/0
85	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64	2,163.64	642.22	06/2012	12/2012	6(O)	0/0
86	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11	370.11	166.82	04/2011	07/2012	15(O)	0/0
87	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35	977.00	157.05	12/2011	01/2013	13(O)	0/0
88	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	555.36	03/2013	03/2013	0(O)	0/0
89	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	5.57	12/2014	12/2014	0(O)	0/0
90	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	2,189.63	4.84	12/2014	12/2014	0(O)	0/0
91	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL, Multi State	11/2007	1,816.07	1,385.00	1,150.46	-	03/2012	3(R3)	0/9
92	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	460.70	180.44	-	03/2013	8(R2)	0/16

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]OCL,Gujarat	02/2009	250.00 349.00	250.00	229.08	03/2013 03/2013	03/2012	-12(R1)	0/0
94	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]OCL,Haryana	11/2009	341.50 -	341.50	46.28	- 02/2013	02/2013	0(R3)	29/42
95	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	85.97	- -	05/2012	-	21/36
96	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	695.80	04/2011 12/2011	04/2012	4(R3)	2/2
97	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	257.92	09/2011 -	12/2012	15(O)	0/0
98	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,524.63	05/2010 05/2012	05/2012	0(R3)	0/0
99	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	302.76	02/2011 08/2011	-	-	0/0
100	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	-	01/2014 -	01/2014	0(O)	0/0
101	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]OCL,Gujarat	02/2009	267.00 -	267.00	189.43	09/2012 09/2012	06/2012	-3(R3)	0/0
102	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	861.79	-	05/2013 -	05/2013	0(O)	0/0
103	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5(O)	0/0
104	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	38.42	09/2012 -	09/2012	0(O)	0/0
105	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O)	0/0
106	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,583.36	03/2012 08/2012	08/2012	0(R3)	0/17
107	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00 -	1,584.00	7.99	- -	-	-	0/0
108	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	2,498.70	08/2010 03/2012	12/2013	21(R3)	0/0
109	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	04/2013	13(R3)	0/0
110	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	477.60	07/2010 05/2012	07/2012	2(R3)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
111	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	- 12/2008	04/2013	52(R3)	0/0
112	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
113	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	777.00	09/2011 05/2012	05/2012	0(R3)	0/0
114	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	-	09/2011 03/2012	03/2012	0(R3)	0/0
115	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	04/2013	1(O)	0/0
116	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	1.50	03/2013 -	04/2013	1(O)	0/0
117	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	05/2013	6(O)	0/0
118	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
119	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,763.29	- -	12/2011	-	0/116
120	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	63.47	01/2013 -	01/2013	0(O)	14/18
121	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	696.52	04/2010 -	03/2012	23(O)	0/0
122	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	370.68	- 04/2013	04/2013	0(R3)	0/167
123	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,918.57	04/2006 05/2011	06/2012	13(R3)	0/0
124	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,300.00	984.57	06/2012 06/2012	06/2012	0(R3)	6/8
125	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,447.85	03/2007 03/2017	03/2017	0(R3)	6/6
126	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	597.20	03/2007 03/2014	03/2014	0(R3)	3/3
127	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	274.39	03/2006 03/2013	03/2013	0(R3)	6/6
128	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
129	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30(O)	0/0
130	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 252.37	204.00	162.35	01/2012 -	05/2012	4(O)	3/8
132	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	612.64	- 12/2012	04/2013	4(R3)	0/21
133	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	190.97	03/2012 08/2012	04/2012	-4(R3)	2/4
134	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	167.90	03/2009 02/2012	02/2012	0(R3)	0/0
135	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	7,883.30	01/2012 -	06/2012	5(O)	0/0
136	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,062.41	09/2012 -	09/2013	12(O)	0/0
137	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,819.59	05/2010 03/2013	03/2013	0(R3)	0/0
138	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	5.67	04/2015 -	04/2015	0(O)	0/0
139	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	296.85	04/2011 -	03/2012	11(O)	0/0
140	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	533.63	03/2011 05/2011	10/2012	17(R3)	0/0
141	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	417.93	03/2010 03/2012	03/2013	12(R1)	0/0
142	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	13,742.98	11/2012 -	06/2013	7(O)	57/100
143	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,400.00	557.13	09/2012 09/2012	09/2012	0(R3)	0/11
144	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	687.12	02/2014 -	02/2014	0(O)	0/0
145	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	527.41	07/2012 -	07/2012	0(O)	0/0
146	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	262.37	09/2010 -	09/2011	12(O)	10/60
147	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	812.91	09/2011 03/2012	03/2012	0(R3)	0/0
148	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	345.93	05/2010 04/2012	05/2012	1(R3)	0/0
149	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	145.16	08/2012 -	08/2012	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
150	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	194.58	- 03/2012	03/2012	0(R3)	0/20
151	WIND ENERGY - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	268.08	- -	03/2012	-	0/18
152	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	23.22	12/2013 12/2013	12/2013	0(R3)	0/0
Total			149,804.77 -	157,344.05	66,384.55				159/688
Power									
153	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	4,573.50	08/2012 -	08/2012	0(O)	0/0
154	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	964.20	02/2012 -	06/2012	4(O)	0/0
155	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	417.20	05/2012 -	05/2012	0(O)	0/0
156	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	694.20	06/2012 -	06/2012	0(O)	0/0
157	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,487.00	08/2013 -	01/2014	5(O)	5/18
158	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,509.00	12/2009 -	12/2014	60(O)	25/47
159	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,793.00	06/2011 -	04/2014	34(O)	1/29
160	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	2,084.00	1,780.21	08/2010 08/2011	04/2012	8(R3)	0/2
161	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.25	724.04	02/2011 08/2011	12/2012	16(R3)	1/4
162	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	24.10	08/2014 -	08/2014	0(O)	0/0
163	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	150.70	09/2014 -	09/2014	0(O)	0/0
164	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.66	748.40	10/2009 -	03/2012	29(O)	20/20
165	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	154.70	11/2012 -	11/2012	0(O)	0/0
166	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	135.60	05/2014 -	05/2014	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	268.20	08/2013	08/2013	0(O)	0/0
168	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	157.60	06/2012	03/2012	-3(O)	0/0
169	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	-	12/2013	12/2013	0(O)	0/0
170	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	77.60	12/2013	12/2013	0(O)	0/0
171	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	18.70	10/2012	10/2012	0(O)	0/0
172	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	1,007.16	824.20	12/2007	-	-	0/18
173	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,772.88	05/2013	06/2016	0(R3)	2/22
174	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67	3,642.00	1,127.55	01/2016	11/2016	10(R3)	0/2
175	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	4,112.00	04/2009	03/2013	47(O)	0/9
176	KOTESHWAR HEP(THDC) - [180100184]THDC,Uttaranchal	04/2000	1,301.56	2,283.69	2,595.25	04/2005	03/2012	0(R3)	10/11
177	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,779.29	1,786.98	09/2008	03/2013	54(O)	3/37
178	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	686.00	11/2011	12/2012	13(O)	6/34
179	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	210.10	10/2012	10/2012	0(O)	0/0
180	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	3,532.00	08/2012	03/2013	7(O)	6/16
181	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	710.09	08/2010	01/2013	16(R3)	0/3
182	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	3,596.20	08/2013	09/2014	13(O)	0/0
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	123.70	11/2011	06/2012	7(R3)	0/0
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	145.60	02/2012	12/2012	10(O)	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	263.80	11/2011	12/2012	13(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	167.30	08/2011 -	01/2012	5(O)	0/0
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	307.90	11/2011 -	12/2012	13(O)	0/0
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	26.80	01/2013 -	01/2013	0(O)	0/0
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	112.80	07/2013 -	07/2013	0(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	244.20	04/2013 -	04/2013	0(O)	0/0
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	31.60	08/2013 -	08/2013	0(O)	0/0
192	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	318.70	11/2012 -	11/2012	0(O)	0/0
193	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,694.25	10/2010 12/2011	01/2013	13(R3)	0/1
194	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,491.20	09/2009 07/2014	07/2014	0(R3)	1/20
195	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	297.95	08/2012 08/2013	08/2013	0(R3)	8/18
196	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,540.50	01/2012 -	09/2013	20(O)	0/0
197	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,644.00	10/2012 -	03/2013	5(O)	6/16
198	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,402.00	05/2011 -	03/2012	10(O)	4/6
199	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	7,676.00	12/2009 -	03/2012	27(O)	50/60
200	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,475.18	09/2010 08/2014	12/2015	16(R3)	11/11
201	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	15.70	04/2013 -	04/2013	0(O)	0/0
202	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,796.90	08/2012 -	08/2012	0(O)	0/0
203	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	121.10	07/2011 -	03/2012	8(O)	0/0
204	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJEC - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	-	08/2014 -	08/2014	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
205	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	-	02/2015 -	02/2015	0(O)	0/0
206	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	-	01/2015 -	01/2015	0(O)	0/0
207	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	-	08/2014 -	08/2014	0(O)	0/0
208	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	3.70	06/2014 -	06/2014	0(O)	0/0
209	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	132.80	04/2012 -	04/2012	0(O)	0/0
210	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	55.48	06/2012 -	06/2012	0(O)	0/0
211	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	599.90	08/2012 -	08/2012	0(O)	0/0
212	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,337.00	03/2013 -	06/2014	15(O)	2/13
213	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,085.43	09/2009 -	06/2013	45(O)	0/0
214	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.39	1,431.96	03/2007 -	09/2012	66(O)	25/25
215	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	303.71	07/2010 02/2016	02/2016	0(R3)	0/2
216	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	-	01/2013 -	01/2013	0(O)	0/0
217	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	181.93	0.02	07/2013 -	07/2013	0(O)	0/0
218	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	-	08/2014 -	08/2014	0(O)	0/0
219	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	308.93	07/2011 -	06/2012	11(O)	0/0
220	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,469.70	10/2012 -	10/2012	0(O)	0/0
221	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	-	01/2015 -	01/2015	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	216.90	03/2014 -	03/2014	0(O)	0/0
223	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 3,779.46	3,779.46	3,652.60	09/2009 -	06/2012	33(O)	11/30
224	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	228.40	08/2013 -	08/2013	0(O)	0/0
225	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	-	08/2014 -	08/2014	0(O)	0/0
226	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	-	10/2014 -	10/2014	0(O)	0/0
227	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	520.60	01/2010 -	09/2012	32(O)	0/22
228	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	140.20	11/2011 -	03/2013	16(O)	0/0
229	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	3,049.00	12/2012 -	12/2012	0(O)	0/0
230	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	-	02/2014 -	02/2014	0(O)	0/0
231	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	33.90	10/2013 -	10/2013	0(O)	0/0
232	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0
233	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	85.20	12/2013 -	12/2013	0(O)	0/0
234	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26 -	558.26	-	11/2013 -	11/2013	0(O)	0/0
235	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	333.90	03/2013 -	03/2013	0(O)	0/0
236	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	322.50	12/2013 -	12/2013	0(O)	0/0
237	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	745.00	11/2012 -	11/2012	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	-	07/2014 -	07/2014	0(O)	0/0
239	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	104.22	- 07/2013	07/2013	0(R3)	0/30
240	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	297.01	07/2006 01/2014	01/2014	0(R3)	7/24
241	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	297.01	01/2014 -	01/2014	0(O)	0/0
242	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	592.80	12/2012 -	06/2013	6(O)	0/0
243	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	136.00	11/2013 -	11/2013	0(O)	0/0
244	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	39.60	01/2013 -	01/2013	0(O)	0/0
245	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	1,794.00	1,671.01	11/2009 11/2011	08/2012	9(R3)	0/4
246	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	2,824.00	10/2012 -	03/2013	5(O)	4/15
247	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 3,422.44	3,422.44	242.75	07/2014 -	09/2016	26(O)	0/2
248	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96 -	664.96	352.70	02/2012 -	03/2012	1(O)	0/0
249	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,059.40	07/2010 -	06/2012	23(O)	20/20
250	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	389.00	09/2010 -	03/2013	30(O)	0/0
251	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	96.40	02/2012 02/2012	03/2012	1(R3)	0/0
Total			203,409.93 -	218,750.90	102,687.11				228/591
<u>Railways</u>									
252	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.75	305.62	03/2014 -	03/2014	0(O)	0/0
253	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
254	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	1,010.00	136.76	- -	-	-	0/0
255	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	320.37	03/2009 12/2008	12/2010	24(R1)	0/0
256	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	435.87	392.00	- 03/2011	03/2011	0(R3)	0/0
257	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	493.08	06/1999 03/2011	03/2011	0(R3)	0/0
258	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	73.76	- -	-	-	0/0
259	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.14	0.49	03/2013 -	03/2013	0(O)	0/0
260	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
261	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	1,173.79	419.77	03/2005 12/2008	03/2016	87(R1)	0/0
262	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	186.61	12/2010 03/2011	-	-	0/0
263	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	173.23	03/2004 12/2010	-	-	0/0
264	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.49	3.97	04/2014 -	03/2014	-1(O)	0/0
265	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	269.02	- -	-	-	0/0
266	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	469.74	03/2010 -	12/2012	33(O)	0/0
267	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	307.17	- 03/2009	03/2011	24(R1)	0/0
268	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	114.13	12/2012 -	12/2012	0(O)	0/0
269	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	177.03	03/2011 -	-	-	0/0
270	Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	3.27	03/2012 -	03/2012	0(O)	0/0
271	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.28	- -	02/2012	-	0/0
272	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,103.47	840.70	12/2012 -	12/2012	0(O)	0/0
273	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	944.25	- -	03/2012	-	0/0
274	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	415.73	230.81	- -	03/2012	-	0/0
276	CONV.OF 1500V DC TRACTION TO 25 KV AC,CR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	- 06/2012	-	-	0/0
277	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	99.64	12/2012 -	12/2012	0(O)	0/0
278	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	175.30	- -	03/2013	-	0/0
279	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	366.18	- 12/2012	-	-	0/0
280	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	489.24	- -	-	-	0/0
281	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	75.23	12/2011 02/2012	02/2012	0(R3)	0/0
282	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	0(O)	0/0
283	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12(O)	0/0
284	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	158.81	- 06/2013	06/2013	0(R3)	0/0
285	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	546.82	03/1995 -	03/2012	204(O)	0/0
286	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	246.26	- 02/2011	03/2012	13(R3)	0/0
287	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	283.10	39.12	02/2006 -	12/2013	94(O)	0/0
288	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	863.23	482.84	- -	-	-	0/0
289	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
290	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	303.09	- 05/2009	-	-	0/0
291	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O)	0/0
292	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	81.63	12/2011 11/2013	11/2013	0(R3)	0/0
293	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	174.38	- -	03/2015	-	0/0
294	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	208.06	- 09/2009	12/2011	27(R1)	0/0
295	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	197.98	- -	03/2012	-	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
296	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	483.14	- -	-	-	0/0
297	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	137.05	- -	-	-	0/0
298	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	156.91	03/2007 03/2007	03/2014	84(R1)	0/0
299	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.17	- -	-	-	0/0
300	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	2.59	03/2015 -	03/2015	0(O)	0/0
301	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	825.89	06/2007 -	-	-	0/0
302	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	903.56	590.94	- 03/2012	03/2012	0(R3)	0/0
303	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	389.55	- 03/2012	12/2012	9(R3)	0/0
304	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	622.67	03/2011 03/2014	03/2016	24(R3)	0/0
305	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	79.98	03/2014 -	03/2014	0(O)	0/0
306	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	212.77	- 03/2012	03/2012	0(R3)	0/0
307	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,238.88	- -	02/2012	-	0/0
308	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	466.14	- -	-	-	1/1
309	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	672.13	- -	-	-	0/0
310	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	724.41	- 12/2010	03/2015	51(R3)	0/0
311	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	88.62	- -	-	-	0/0
312	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	200.93	- 03/2009	04/2013	49(R1)	0/0
313	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	200.70	- -	03/2012	-	0/0
314	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.23	- -	03/2015	-	0/0
315	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	407.53	- -	-	-	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
316	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, Jharkhand	03/1999	491.19 1,099.20	1,099.20	1,191.78	07/2005 -	-	-	0/0
317	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, Jharkhand	04/2002	459.91 418.17	418.17	84.08	- -	-	-	0/0
318	KOSI BRIDGE (NL), ECR - [220100304] ECR, Bihar	04/2002	323.41 -	341.41	252.72	- 03/2012	12/2012	9(R3)	0/0
319	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265] SCR, Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
320	KOTTUR-HARIHAR (NL), (SWR) - [220100212] SWR, Karnataka	04/1995	65.94 302.23	302.23	331.25	- -	03/2011	-	0/0
321	Katakhal to Bhairabi - [N22000126] NEFR, Assam	04/1998	227.90 -	223.01	85.48	12/2012 -	03/2014	15(O)	0/0
322	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] NCR, Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
323	LANJHIGARH-JUNAGARH NL (ECOR) - [220100148] ECOR, Orissa	04/1993	100.00 142.98	227.94	196.49	03/2002 -	03/2012	120(O)	0/0
324	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127] NEFR, Assam	04/1996	1,676.31 -	4,027.93	2,936.77	03/2009 -	12/2013	57(O)	0/0
325	MACHERLA-NALGONDA (NL) (SCR) - [220100220] SCR, Andhra Pradesh	07/1998	125.00 363.26	458.26	0.35	07/2008 -	-	-	0/0
326	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316] NER, Bihar	04/2003	218.19 -	218.19	150.16	- -	-	-	0/0
327	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168] ER, Jharkhand	04/1995	184.00 254.07	675.00	498.92	- 12/2011	03/2012	3(R3)	0/0
328	MANOHARABAD-KOTHPALL NEW LINE (SCR) - [N22000032] SCR, Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
329	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002] ECR, Bihar	04/1996	114.01 332.92	427.89	370.05	- 03/2012	03/2012	0(R3)	0/0
330	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079] SR, Tamil Nadu	09/2007	404.19 -	900.00	226.41	- -	-	-	0/0
331	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093] MRT, Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,228.31	- 06/2011	06/2011	0(R3)	0/0
332	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092] MRT, Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	0(R3)	0/0
333	MUNEERABAD-MAHABOBNAGAR (NL), SCR - [220100205] SCR, Multi State	04/1997	218.24 377.32	537.47	107.40	- -	03/2012	-	0/0
334	MUZAFFARPUR-SITAMARHI (NL), ECR - [220100194] ECR, Bihar	04/1997	100.00 483.62	411.22	438.19	- 03/2012	03/2012	0(R3)	0/0
335	NANDYAL-YERRAGUNTALA (NL), SCR - [220100192] SCR, Andhra Pradesh	03/1996	155.74 164.36	840.32	547.76	02/2009 -	03/2012	37(O)	0/0
336	NANGALDAM-TALWARA (NL), NR - [220100188] (NR), Multi State	03/1981	37.68 450.00	730.00	333.85	- 07/2012	07/2012	0(R3)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
337	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	529.88	37.89	- -	-	-	0/0
338	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	92.24	- -	03/2014	-	0/0
339	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	1,066.29	12/2008 -	03/2014	63(O)	0/0
340	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	239.05	- -	03/2015	-	0/0
341	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
342	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	85.66	03/2016 -	03/2016	0(O)	0/0
343	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	2.75	03/2014 03/2016	03/2016	0(R3)	0/0
344	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	14.40	03/2016 -	03/2016	0(O)	0/0
345	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	8.17	03/2016 -	06/2016	3(O)	0/0
346	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	403.73	03/2008 06/2008	-	-	0/0
347	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	318.69	03/2009 12/2009	03/2011	15(R1)	0/0
348	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	227.13	02/2010 -	12/2015	70(O)	0/0
349	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,159.80	10/2007 12/2012	12/2012	0(R3)	0/0
350	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	820.32	547.46	- -	03/2012	-	0/0
351	Pandabeswar-Chinipai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	133.68	- 12/2010	-	-	0/0
352	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	724.37	- -	03/2013	-	0/0
353	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	191.73	12/2007 03/2010	12/2010	9(R1)	0/0
354	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	632.83	03/2009 12/2012	12/2012	0(R3)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	3,230.01	2,336.00	04/2008 03/2014	12/2015	21(R3)	0/0
356	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16 -	243.40	-	- 02/2009	04/2013	50(R1)	0/0
357	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat	04/2006	196.97 -	196.97	204.73	03/2011 -	03/2012	12(O)	0/0
358	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	217.36	- -	-	-	0/0
359	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, Jharkhand	04/1997	194.07 -	456.45	276.61	06/2004 -	12/2012	102(O)	0/0
360	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70 -	1,717.29	989.40	- -	03/2013	-	0/0
361	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	296.20	318.33	04/2003 03/2010	-	-	0/0
362	REWARI-ROHTAK (NL), NR - [220100279](NR), Haryana	01/2004	149.38 330.23	476.68	512.18	02/2010 02/2011	02/2011	0(R3)	0/0
363	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 604.04	639.97	176.59	03/1998 08/2005	08/2005	0(R1)	0/0
364	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	254.35	03/2013 -	03/2013	0(O)	0/0
365	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh	04/2008	603.04 -	603.04	55.89	03/2012 -	03/2013	12(O)	0/0
366	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhattisgarh	09/2006	324.90 -	324.90	211.31	03/2010 -	03/2012	24(O)	0/0
367	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.57	52.63	12/2015 -	12/2015	0(O)	0/0
368	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR, Rajasthan	04/2001	143.92 258.60	258.60	248.56	- 03/2011	03/2011	0(R3)	0/0
369	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23 -	638.00	60.78	02/2015 -	02/2015	0(O)	0/0
370	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR, Rajasthan	04/2008	516.23 -	516.23	164.14	03/2014 -	03/2014	0(O)	0/0
371	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, Orissa	04/2005	726.96 810.78	810.78	89.95	- -	03/2013	-	0/0
372	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 662.69	723.71	389.41	06/2005 07/2011	06/2015	47(R3)	0/0
373	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 762.33	762.33	461.93	- 12/2009	02/2012	26(R1)	0/0
374	TIDIVANAM-NAGARI (NL) - [N22000085]SR, Tamil Nadu	09/2006	456.00 582.83	582.83	95.58	- -	-	-	0/0
375	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, Tamil Nadu	09/2006	125.00 -	227.40	34.06	- -	-	-	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
376	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 -	548.96	490.98	- -	-	-	0/0
377	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,176.10	3,176.10	3,047.91	12/2006 08/2010	-	-	0/0
378	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 -	167.73	42.51	03/2012 -	03/2012	0(O)	0/0
379	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 8,000.00	20,000.00	7,816.76	03/2001 -	12/2017	201(O)	0/0
380	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00 -	819.40	108.30	03/2010 06/2014	06/2014	0(R3)	0/0
381	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62 -	1,389.62	237.64	03/2014 -	03/2014	0(O)	0/0
382	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	356.87	155.74	- 03/2010	-	-	0/0
Total			65,286.30 -	134,407.18	58,085.61				1/1
Road Transport & Highways									
383	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	163.90	05/2013 -	03/2014	10(O)	0/0
384	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O)	0/0
385	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00 -	226.00	129.80	02/2014 -	02/2014	0(O)	0/0
386	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	15.15	02/2014 -	02/2014	0(O)	0/0
387	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09 -	375.09	20.75	04/2014 -	04/2014	0(O)	0/0
388	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76 -	2,498.76	34.56	08/2014 -	08/2014	0(O)	0/0
389	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	1,008.50	1,079.00	06/2013 -	06/2013	0(O)	0/0
390	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	31.09	09/2013 -	07/2014	10(O)	0/0
391	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50 -	785.50	424.70	08/2013 -	08/2013	0(O)	0/0
392	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00 -	575.00	225.90	07/2013 -	07/2013	0(O)	0/0
393	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	137.30	09/2007 -	06/2013	69(O)	0/0
394	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	06/2012	87(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
395	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	870.50	11/2012	06/2013	7(O)	0/0
396	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	266.60	11/2008	03/2012	40(O)	0/0
397	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	251.60	01/2009	03/2012	38(O)	0/0
398	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	631.70	02/2012	04/2012	2(O)	0/0
399	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	182.07	02/2004	07/2012	101(O)	0/0
400	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	273.20	-	10/2013	-	0/1
401	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80	237.80	226.90	06/2008	12/2012	54(O)	0/0
402	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00	195.00	187.40	06/2008	06/2012	48(O)	0/0
403	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	218.10	06/2005	09/2012	87(O)	0/0
404	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	165.80	04/2010	12/2012	32(O)	0/0
405	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	1,373.00	-	03/2013	-	0/3
406	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41(O)	0/0
407	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	491.60	03/2013	03/2013	0(O)	0/0
408	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	-	-	12/2013	-	0/1
409	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	809.80	05/2013	05/2013	0(O)	0/0
410	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	227.70	10/2011	03/2014	29(O)	0/0
411	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	572.30	580.00	10/2011	10/2012	12(O)	0/0
412	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	266.10	06/2008	03/2012	45(O)	0/0
413	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	170.20	10/2008	06/2012	44(O)	0/0
414	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	573.30	05/2010	12/2012	31(O)	0/0
415	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	593.00	274.30	07/2013	07/2013	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
416	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
417	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	173.50	-	06/2013	-	1/1
418	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	207.80	06/2008	06/2012	48(O)	0/0
419	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	132.10	05/2008	06/2012	49(O)	0/0
420	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	173.60	09/2010	12/2012	27(O)	0/0
421	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	-	08/2013	08/2013	0(O)	0/0
422	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	533.80	01/2011	03/2012	14(O)	0/0
423	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	323.30	09/2008	03/2012	42(O)	0/0
424	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
425	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	100.30	09/2008	06/2012	45(O)	0/0
426	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	262.30	02/2004	05/2012	99(O)	0/0
427	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	300.00	09/2007	06/2012	57(O)	0/0
428	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	483.10	08/2013	08/2013	0(O)	0/0
429	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	750.80	10/2009	06/2012	32(O)	0/0
430	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	192.90	04/2008	12/2012	56(O)	0/0
431	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	129.50	04/2008	12/2012	56(O)	0/0
432	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.60	10/2009	06/2012	32(O)	0/0
433	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	470.10	12/2009	12/2012	36(O)	0/0
434	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,098.00	09/2012	09/2012	0(O)	0/0
435	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,406.00	10/2011	06/2012	8(O)	0/0
436	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	475.60	03/2005	03/2012	84(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
437	HAPUR-GARHUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	258.80	09/2007	06/2012	57(O)	0/0
438	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	256.20	02/2009	03/2013	49(O)	0/0
439	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	20.27	07/2009	04/2014	57(O)	0/0
440	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	2.11	09/2007	04/2014	79(O)	0/0
441	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	178.99	08/2004	03/2012	91(O)	0/0
442	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	169.48	08/2004 07/2010	03/2012	20(R3)	0/0
443	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07	625.07	758.60	01/2013	01/2013	0(O)	0/0
444	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	981.60	-	03/2013	-	2/2
445	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,416.00	10/2012	10/2012	0(O)	0/0
446	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	439.20	05/2012	05/2012	0(O)	0/0
447	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	274.40	05/2013	05/2013	0(O)	0/0
448	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
449	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
450	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	477.10	09/2008	03/2012	42(O)	0/0
451	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	436.30	09/2009	12/2012	39(O)	0/0
452	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	536.00	282.90	01/2014	01/2014	0(O)	0/0
453	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	838.20	12/2012	12/2012	0(O)	0/0
454	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	278.50	10/2008	09/2012	47(O)	0/0
455	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	285.60	10/2008	03/2012	41(O)	0/0
456	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	603.20	-	03/2013	-	0/1
457	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	917.50	05/2012	05/2012	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	185.50	06/2010	10/2012	28(O)	0/0
459	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.80	09/2009	10/2012	37(O)	0/0
460	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00	225.00	257.50	10/2008	04/2012	42(O)	0/0
461	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	85.39	11/2008	07/2013	56(O)	0/0
462	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	41.30	04/2009	07/2013	51(O)	0/0
463	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	2.50	11/2008	01/2014	62(O)	0/0
464	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	92.33	04/2009	03/2013	47(O)	0/0
465	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	1,069.00	06/2012	06/2012	0(O)	0/0
466	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	1,110.00	06/2013	06/2013	0(O)	0/0
467	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
468	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	268.70	06/2008	06/2012	48(O)	0/0
469	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2012	42(O)	0/0
470	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	235.50	04/2008	12/2012	56(O)	0/0
471	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	188.90	06/2008	06/2012	48(O)	0/0
472	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	271.70	06/2008	06/2012	48(O)	0/0
473	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
474	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	947.20	-	03/2012	-	0/0
475	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	241.70	-	03/2012	9(R3)	0/2
476	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
477	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	393.70	09/2013	09/2013	0(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
478	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	363.90	03/2008 -	03/2012	48(O)	0/0
479	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	640.10	10/2014 -	10/2014	0(O)	0/0
480	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00 -	284.00	351.20	05/2010 -	05/2012	24(O)	0/0
481	PATHANKOT- BHOGPUR, KM.26- KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	166.30	05/2008 -	08/2012	51(O)	0/0
482	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	574.00	42.00	03/2014 -	03/2014	0(O)	0/0
483	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	490.90	02/2013 -	02/2013	0(O)	0/0
484	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,141.00	07/2012 -	07/2012	0(O)	0/0
485	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	107.60	03/2013 -	03/2013	0(O)	0/0
486	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,337.00	11/2011 -	06/2012	7(O)	0/0
487	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	05/2012	0(O)	0/0
488	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	1,987.00	-	07/2015 -	07/2015	0(O)	0/0
489	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	292.50	10/2008 -	12/2012	50(O)	0/0
490	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	240.80	10/2008 -	09/2012	47(O)	0/0
491	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	-	11/2013 -	11/2013	0(O)	0/0
492	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	217.40	10/2008 -	12/2012	50(O)	0/0
493	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	177.10	10/2008 -	05/2012	43(O)	0/0
494	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	05/2012	16(O)	0/0
495	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	209.80	03/2013 -	03/2013	0(O)	0/0
496	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	187.50	09/2007 -	06/2012	57(O)	0/0
497	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	177.40	07/2008 -	12/2012	53(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
498	SIX LANNING OF HOSUR-KRISHNAGIRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
499	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
500	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00	1,535.00	542.80	05/2014	05/2014	0(O)	0/0
501	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
502	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.20	03/2008	05/2012	50(O)	0/0
503	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	97.16	04/2004	07/2012	99(O)	0/0
504	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,610.00	08/2011	03/2012	7(O)	0/0
505	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.50	06/2009	11/2012	41(O)	0/0
506	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	691.90	07/2010	03/2013	32(O)	0/0
507	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	361.30	11/2013	11/2013	0(O)	0/0
508	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
509	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	55.89	05/2013	05/2013	0(O)	0/0
510	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	-	04/2013	-	2/2
511	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	383.20	12/2008	03/2012	39(O)	0/0
512	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	459.40	03/2014	03/2014	0(O)	0/0
513	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09	166.30	184.60	03/2008	03/2012	48(O)	0/0
514	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	155.10	03/2008	03/2012	48(O)	0/0
515	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.71	11/2012	11/2012	0(O)	0/0
516	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	763.80	08/2010	03/2012	19(O)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
517	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	232.50	07/2013	07/2013	0(O)	0/0
	Total		79,768.48	81,624.31	55,320.65	-	-	-	5/13
			-	-	-	-	-	-	-
	<u>Shipping & Ports</u>								
518	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011 06/2011	06/2012	12(R3)	0/0
519	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	315.01	09/2012	09/2012	0(O)	0/0
520	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	1,011.15	03/2012	04/2012	1(O)	0/0
521	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50	241.50	157.81	09/2011	12/2011	3(O)	0/0
522	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	106.93	12/2012	12/2012	0(O)	0/0
523	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	0(R3)	0/0
524	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	06/2012	5(R3)	0/0
525	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	189.92	02/2014	02/2014	0(O)	0/0
526	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013	12/2013	0(O)	0/0
527	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.16	02/2011	03/2013	25(O)	0/0
528	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	677.00	12/2010	12/2012	24(O)	0/0
529	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24(O)	0/0
530	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.75	10/2008	-	-	0/0
531	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	253.36	-	12/2007 01/2009	-	-	0/0
532	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	399.13	-	08/2010	-	-	0/0
			-	-	-	-	-	-	-

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
533	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
534	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0
535	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	125.00	12/2005 01/2008	10/2011	45(R3)	0/0
536	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
537	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
538	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
539	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 -	373.22	336.26	04/2009 11/2009	02/2011	15(R3)	0/0
540	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	828.92	10/2008 -	-	-	0/0
541	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
542	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
543	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	07/2014	14(O)	0/0
	Total		19,051.36 -	19,858.93	4,938.55				0/0
Telecommunications									
544	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	03/2012	38(O)	0/0
545	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	71.51	02/2007 -	08/2011	54(O)	0/0
546	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 -	03/2012	61(O)	0/0
547	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.80	10/2010 03/2012	07/2012	4(R3)	0/0

Sector Wise Details

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
548	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
549	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
550	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
551	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	211.73	12/2008	03/2012	39(O)	0/0
552	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	-	03/2009	-	-	0/0
553	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	12/2011	23(O)	0/0
554	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) - [N26000090]BSNL,Madhya pradesh	11/2009	916.70	930.60	757.02	11/2010	03/2012	16(O)	0/0
555	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) - [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	366.90	08/2009	03/2012	31(O)	0/0
556	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
557	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	03/2012	36(O)	0/0
558	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
559	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
560	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	161.31	12/2005	03/2012	75(O)	0/0
561	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15	158.72	76.55	06/2009	12/2011	30(O)	0/0
	Total		8,443.59	8,559.89	2,442.29				0/0
Urban Development									
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	12/2013	24(O)	6/6
563	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0

Sector Wise Details

(Feb,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
564	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	110.82	03/2016	03/2016	0(O)	0/0
565	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	-	09/2014	09/2014	0(O)	0/0
	Total		44,245.18	49,518.08	2,378.39				6/6
			-						
	<u>Water Resources</u>								
566	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			726,749.77	845,950.57	372,525.94				726/2463

Sector wise current status of projects on the Flash Report

Telecommunications

I. Current Status:


Number of Projects **18**

Number of Projects Delayed **8**

Number of Projects Without Date Of Commissioning **10**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 18 projects, 8 projects are delayed .10 projects do not have fixed dates of commissioning.

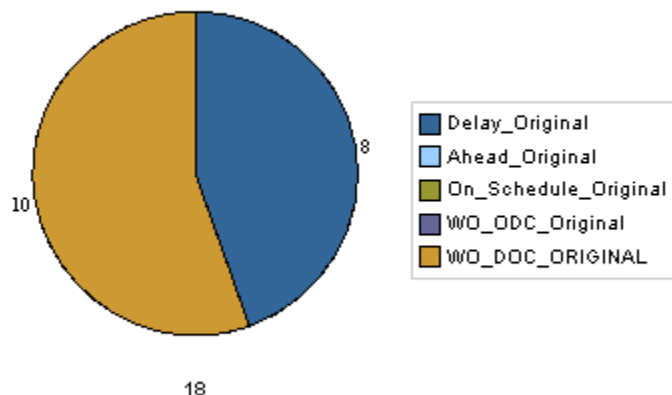

III. Investment Scenario

The Total Original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 8443.59 crore but this was subsequently revised to Rs. 8559.89 crore implying a cost overrun of 1.4%. The expenditure incurred on these projects till February, 2012 is Rs. 2442.29 crore, which is 28.5% of the revised cost of the projects.

Figures are in Rs. Crore

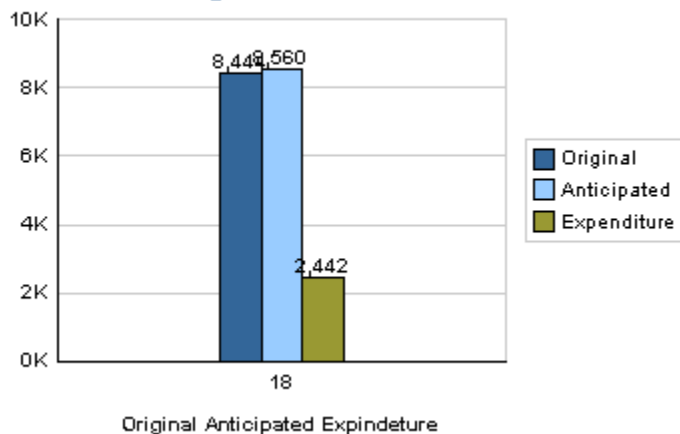

Sector wise current status of projects on the Flash Report


Power

I. Current Status:

Number of Projects	99
Number of Projects On Schedule	49
Number of Projects Delayed	46
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 99 projects, 1 project are ahead of schedule, 49 projects are on schedule and 46 projects are delayed .2 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

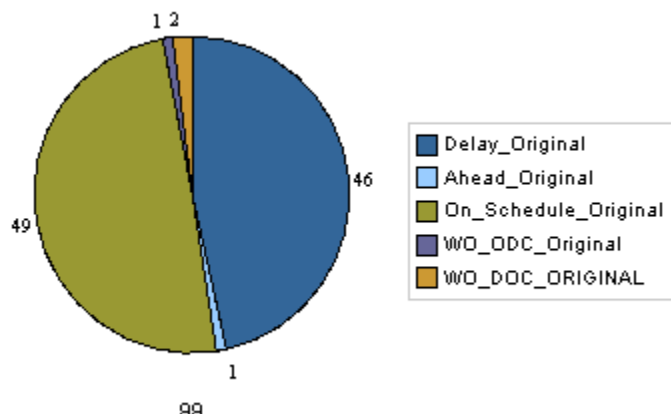

III. Investment Scenario

The Total Original cost of implementation of 99 projects when sanctioned, was of the order of Rs. 203409.93 crore but this was subsequently revised to Rs. 218750.9 crore implying a cost overrun of 7.5%. The expenditure incurred on these projects till February, 2012 is Rs. 102687.11 crore, which is 46.9% of the revised cost of the projects.

Figures are in Rs. Crore

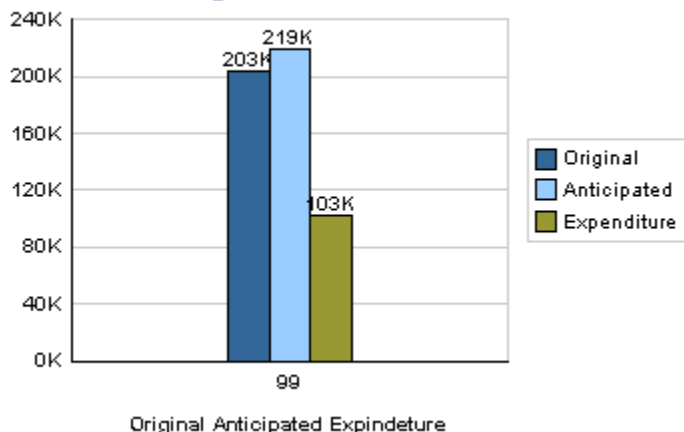

Sector wise current status of projects on the Flash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

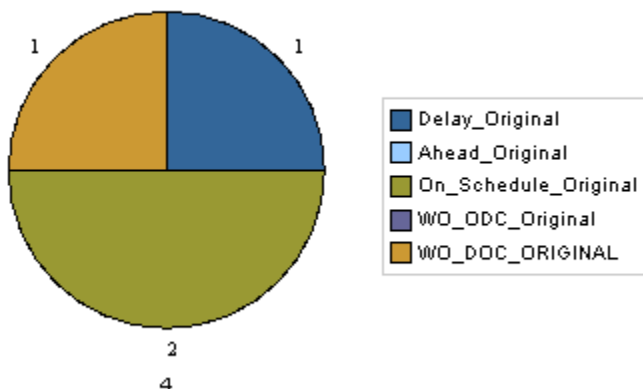

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till February, 2012 is Rs. 2378.39 crore, which is 4.8% of the revised cost of the projects.

Figures are in Rs. Crore

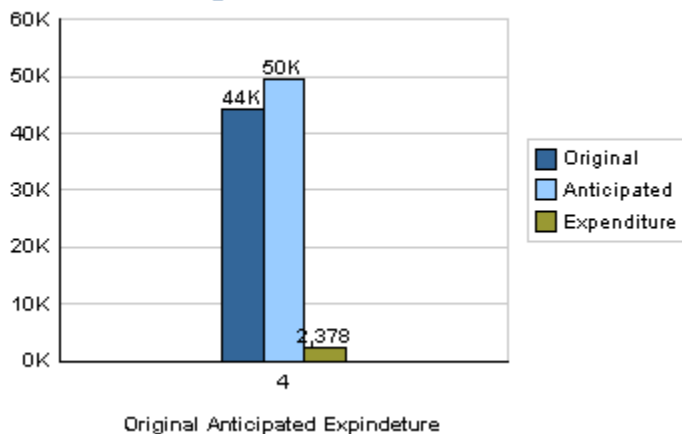

Sector wise current status of projects on the Flash Report

Shipping & Ports


I. Current Status:

Number of Projects	26
Number of Projects On Schedule	5
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning 9

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 26 projects, 5 projects are on schedule and 12 projects are delayed .9 projects do not have fixed dates of commissioning.

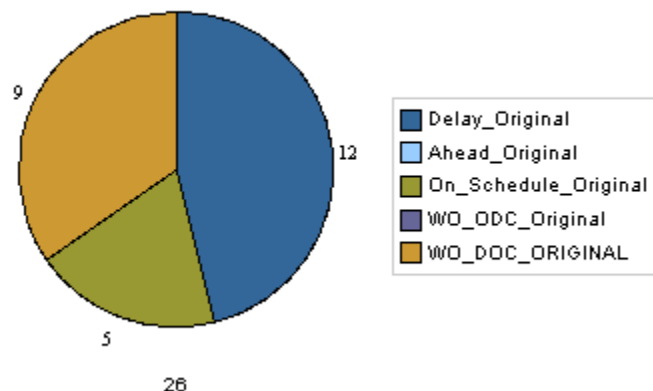

III. Investment Scenario

The Total Original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 19051.36 crore but this was subsequently revised to Rs. 19858.93 crore implying a cost overrun of 4.2%. The expenditure incurred on these projects till February, 2012 is Rs. 4852.09 crore, which is 24.4% of the revised cost of the projects.

Figures are in Rs. Crore

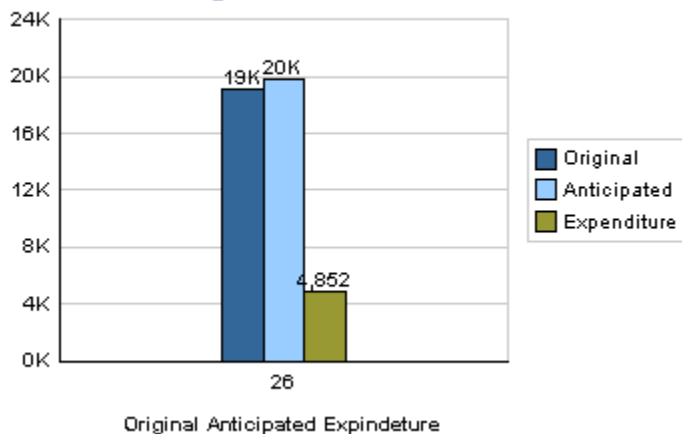

Sector wise current status of projects on the Flash Report

Road Transport & Highways


I. Current Status:

Number of Projects	135
Number of Projects On Schedule	46
Number of Projects Delayed	80

Number of Projects Without Original Date of Commissioning	9
---	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 135 projects, 46 projects are on schedule and 80 projects are delayed .9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

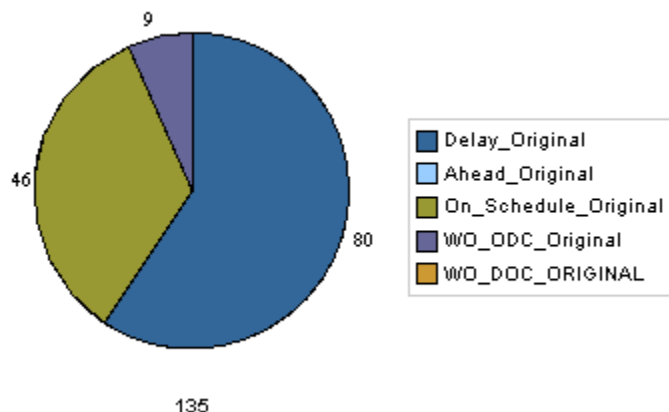

III. Investment Scenario

The Total Original cost of implementation of 135 projects when sanctioned, was of the order of Rs. 79768.48 crore but this was subsequently revised to Rs. 81624.31 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till February, 2012 is Rs. 55320.65 crore, which is 67.8% of the revised cost of the projects.

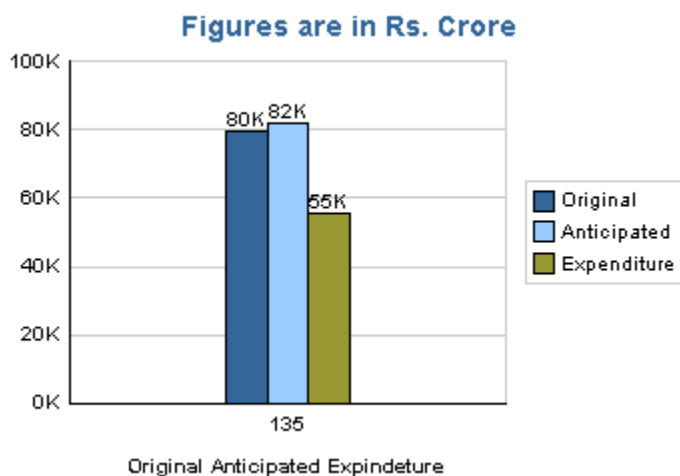

Sector wise current status of projects on the Flash Report


Railways

I. Current Status:

Number of Projects	131
Number of Projects On Schedule	18
Number of Projects Delayed	28
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	33
Number of Projects Without Date Of Commissioning	51

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 131 projects, 1 project are ahead of schedule, 18 projects are on schedule and 28 projects are delayed .51 projects do not have fixed dates of commissioning.33 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

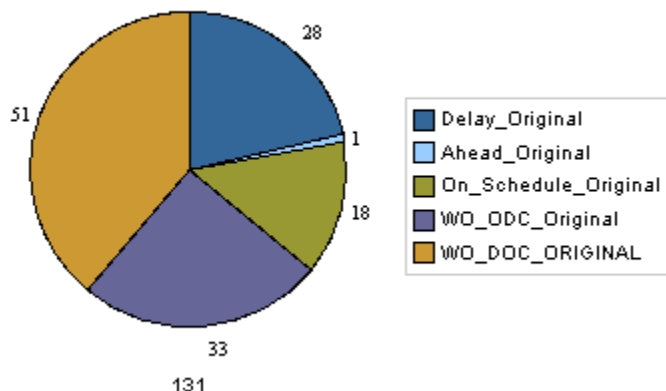

III. Investment Scenario

The Total Original cost of implementation of 131 projects when sanctioned, was of the order of Rs. 65286.3 crore but this was subsequently revised to Rs. 134407.18 crore implying a cost overrun of 105.9%. The expenditure incurred on these projects till February, 2012 is Rs. 58085.61 crore, which is 43.2% of the revised cost of the projects.

Figures are in Rs. Crore

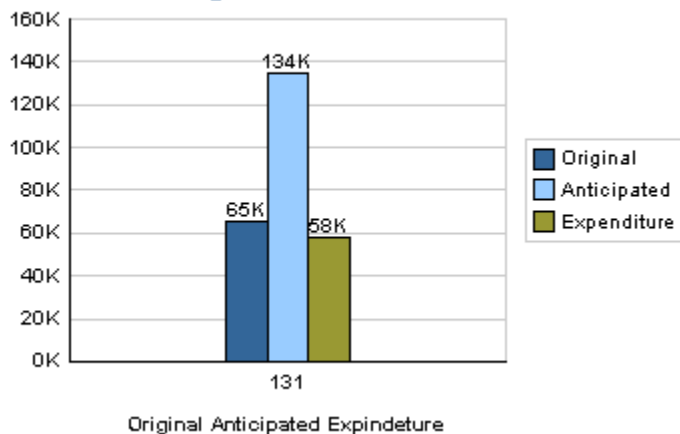

Sector wise current status of projects on the Flash Report


Petroleum

I. Current Status:

Number of Projects	69
Number of Projects On Schedule	15
Number of Projects Delayed	37
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	9
Number of Projects Without Date Of Commissioning	6

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 69 projects, 2 projects are ahead of schedule, 15 projects are on schedule and 37 projects are delayed .6 projects do not have fixed dates of commissioning.9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

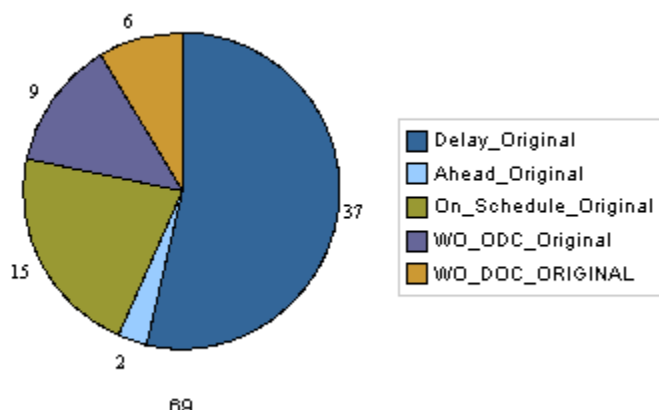

III. Investment Scenario

The Total Original cost of implementation of 69 projects when sanctioned, was of the order of Rs. 149804.77 crore but this was subsequently revised to Rs. 157344.05 crore implying a cost overrun of 5%. The expenditure incurred on these projects till February, 2012 is Rs. 66384.55 crore, which is 42.2% of the revised cost of the projects.

Figures are in Rs. Crore

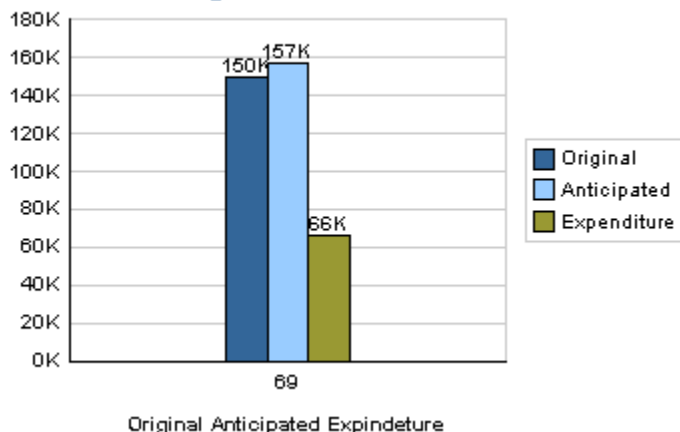

Sector wise current status of projects on the Flash Report

Steel


I. Current Status:

Number of Projects	16
Number of Projects On Schedule	4
Number of Projects Delayed	6

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 4 projects are on schedule and 6 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

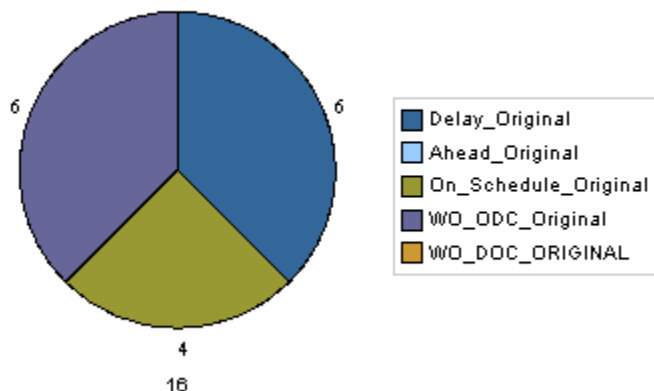

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 65244.82 crore but this was subsequently revised to Rs. 71412.36 crore implying a cost overrun of 9.5%. The expenditure incurred on these projects till February, 2012 is Rs. 38039.35 crore, which is 53.3% of the revised cost of the projects.

Figures are in Rs. Crore

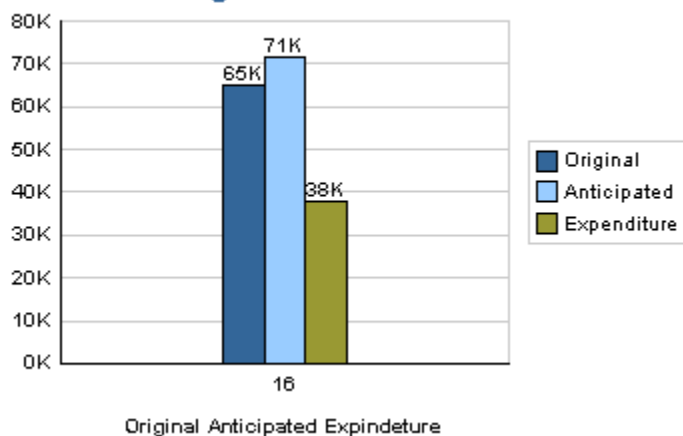

Sector wise current status of projects on the Flash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Original Date of Commissioning	2
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 2 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

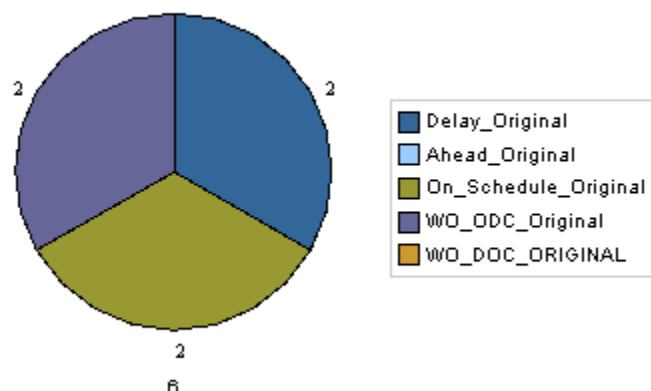

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till February, 2012 is Rs. 1881.33 crore, which is 35.4% of the revised cost of the projects.

Figures are in Rs. Crore

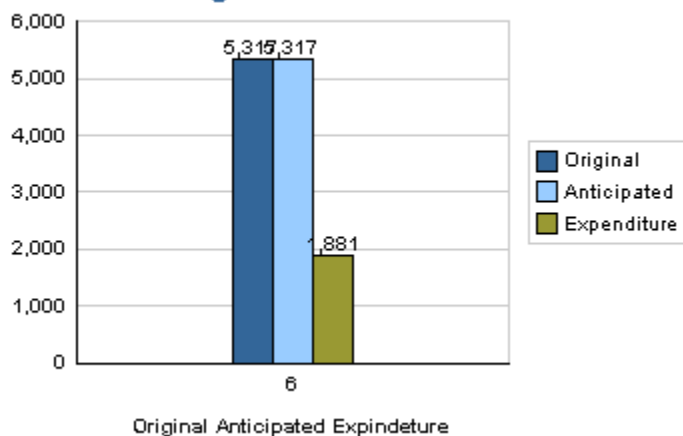

Sector wise current status of projects on the Flash Report

Coal


I. Current Status:

Number of Projects	50
Number of Projects On Schedule	17
Number of Projects Delayed	18

Number of Projects Without Original Date of Commissioning	14
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 50 projects, 17 projects are on schedule and 18 projects are delayed .1 project do not have fixed dates of commissioning.14 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

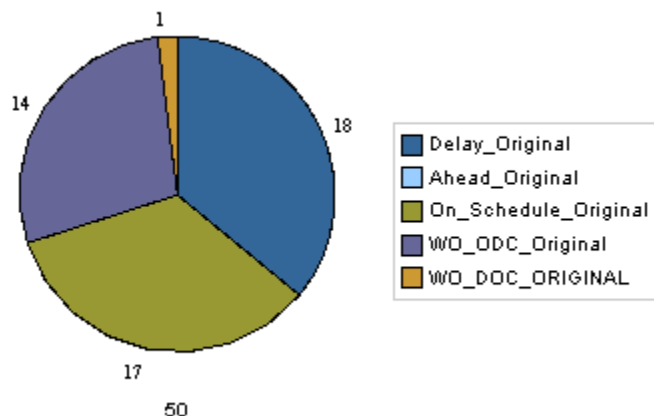

III. Investment Scenario

The Total Original cost of implementation of 50 projects when sanctioned, was of the order of Rs. 33604.55 crore but this was subsequently revised to Rs. 37053.1 crore implying a cost overrun of 10.3%. The expenditure incurred on these projects till February, 2012 is Rs. 11308.7 crore, which is 30.5% of the revised cost of the projects.

Figures are in Rs. Crore

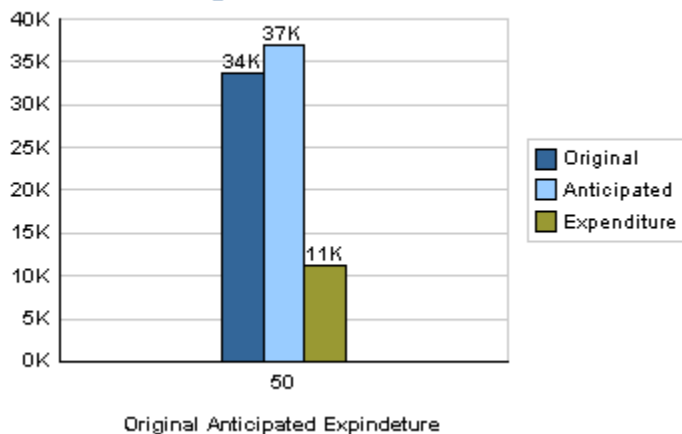

Sector wise current status of projects on the Flash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 4 projects are delayed.

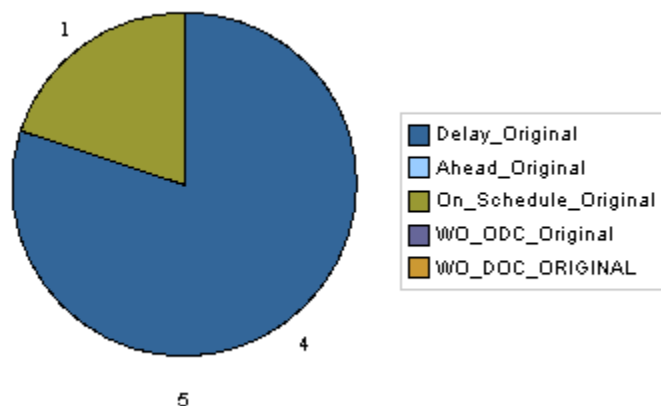

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till February, 2012 is Rs. 4012.24 crore, which is 71.5% of the revised cost of the projects.

Figures are in Rs. Crore

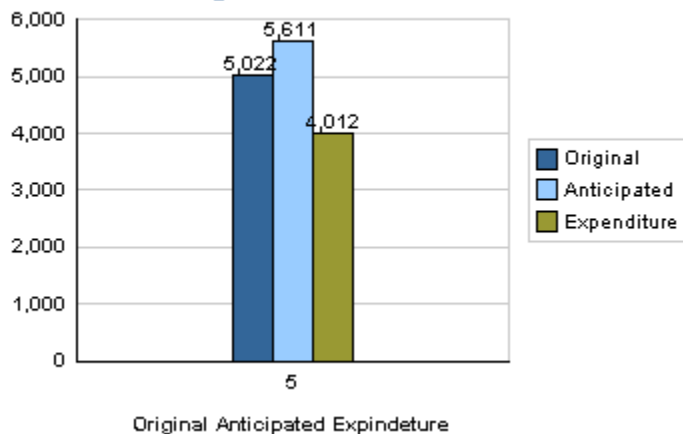

Sector wise current status of projects on the Flash Report


Atomic Energy

I. Current Status:

Number of Projects	5
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

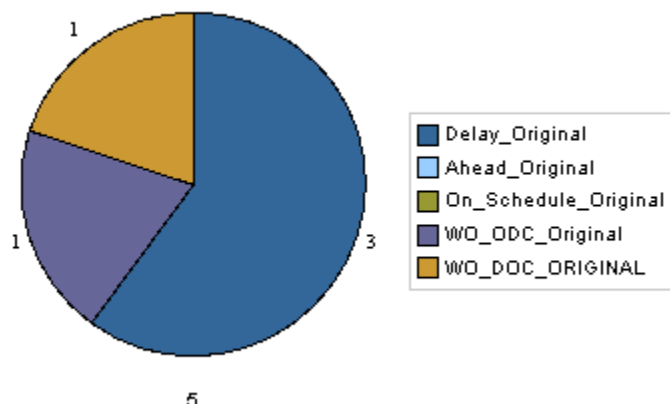

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 46386.29 crore implying a cost overrun of 11.6%. The expenditure incurred on these projects till February, 2012 is Rs. 21043.52 crore, which is 45.4% of the revised cost of the projects.

Figures are in Rs. Crore

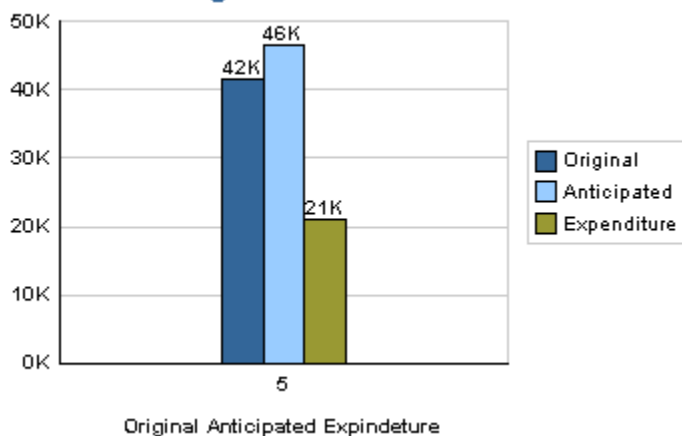

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	37	36851.48	43234.81	23640.69
2	Arunachal Pr.	4	9512.22	14153.62	7776.82
3	Assam	37	23895.78	35508.89	20770.14
4	Bihar	31	30278.54	35051.77	22587.53
5	Chhatisgarh	26	58044.28	61275.63	25512.73
6	Delhi	3	37985.00	37965.41	178.02
7	Goa	1	335.61	335.61	86.87
8	Gujarat	27	32792.31	33045.32	6705.11
9	Haryana	10	5795.35	7611.84	6164.21
10	Himachal Pr.	6	14761.20	17455.42	13138.76
11	J and K	10	14019.35	33604.41	12389.15
12	Jharkhandd	22	14396.48	15999.88	6901.41
13	Karnataka	25	30657.64	38935.96	18129.50
14	Kerala	7	6086.17	6775.22	1653.23
15	Madhya pradesh	24	17335.55	17581.76	7771.79
16	Maharashtra	52	70396.35	83640.27	42998.83
17	Manipur	1	727.56	3056.85	622.67
18	Meghalaya	2	762.00	762.00	412.70
19	Mizoram	3	1901.69	4220.75	597.99
20	Multi State	96	127685.27	132264.15	50100.39
21	Nagaland	1	850.00	850.00	8.44
22	Orissa	26	42465.41	45636.40	17727.31
23	Punjab	7	4613.20	5598.23	3339.03
24	Rajasthan	14	24243.00	24237.62	7272.97
25	Sikkim	2	1648.94	3690.03	231.09
26	Tamil Nadu	35	52241.33	61099.83	35892.17
27	Tripura	3	1522.39	2053.23	555.00
28	Uttar Pradesh	24	17544.03	21597.83	10771.65
29	Uttaranchal	5	9815.87	11738.43	4937.55
30	West Bengal	25	37585.77	46969.40	23652.19
TOTAL		566	726749.77	845950.57	372525.94

LIST OF PROJECTS IN WHICH EXPENDITURE MORE THAN COST

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	14326.00
2	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	Petroleum	HPCL	224.00	299.00	302.76
3	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	HPCL	613.54	0.00	671.52
4	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1431.96
5	KOTESHWAR HEP(THDC)	Power	THDCL	1301.56	0.00	2595.25
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	NHPC	1061.38	0.00	1085.43
7	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	PGCIL	297.37	297.91	308.93
8	CHAMERA,STAGE-III (NHPC)	Power	NHPC	1405.63	0.00	1780.21
9	CHUTAK HYDRO-ELECTRIC PROJECT	Power	NHPC	621.26	0.00	724.04
10	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	Power	PGCIL	1779.29	0.00	1786.98
11	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.01	0.00	710.09
12	GUNA-ETAWAH(NCR), NL	Railways	NCR	158.77	432.46	558.07
13	CALICUT-MANGALORE (DL) (SR)	Railways	SR	240.00	0.00	599.28
14	KARUR-SALEM(NL),SR	Railways	SR	155.55	229.88	672.13
15	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	ECR	491.19	1099.20	1191.78
16	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	248.44	576.27	840.70
17	BILASPUR-URKURA (DL)	Railways	RVNL	151.52	0.00	307.17
18	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	RVNL	136.62	0.00	191.73
19	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	233.00	501.69	590.94
20	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	NEFR	1000.00	1500.00	2336.00
21	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	ER	184.00	254.07	498.92
22	KODERMA GIRIDH (NL), ECR	Railways	ECR	371.36	0.00	407.53
23	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	100.00	142.98	196.49
24	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	Railways	M RTP	3125.20	4174.40	4228.31
25	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	114.01	332.92	370.05
26	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	489.24
27	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	RVNL	240.00	0.00	318.69

SN	PROJ TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
28	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	512.18
29	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	(NR)	409.00	625.30	825.89
30	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	466.14
31	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	NER	395.00	1062.36	1238.88
32	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	2936.77
33	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	230.81
34	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	0.00	392.00
35	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	NEFR	733.00	0.00	1066.29
36	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	250.82
37	RAJPIPLA-ANKELASHWAR, WR (GC)	Railways	WR	196.97	0.00	204.73
38	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	493.08
39	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	407.78	547.46
40	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	SR	100.00	0.00	490.98
41	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	SWR	295.00	412.91	483.14
42	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	302.23	331.25
43	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	276.61
44	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	164.36	547.76
45	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	227.48
46	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	Railways	RVNL	200.80	0.00	269.02
47	RENIGUNTA-GUNTAKAL(RE)	Railways	RVNL	168.34	0.00	318.33
48	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	NEFR	915.70	0.00	989.40
49	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	724.41
50	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	NER	381.17	0.00	482.84
51	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	228.09	246.26
52	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	389.55
53	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	285.60

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
54	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	187.50
55	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
56	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	NHAI	441.00	0.00	947.20
57	Bijapur-Hungund Section	Road Transport & Highways	NHAI	748.00	0.00	1373.00
58	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	1008.50	0.00	1079.00
59	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	691.90
60	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	NHAI	280.00	0.00	581.50
61	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
62	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	792.06	0.00	838.20
63	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	870.50
64	Pune-sholapur,pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1802.00
65	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	940.00	0.00	1141.00
66	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	835.00	0.00	1069.00
67	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	758.60
68	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	NHAI	946.00	0.00	981.60
69	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.90

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
70	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	NHAI	572.30	0.00	580.00
71	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2610.00
72	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	NHAI	1673.70	0.00	2406.00
73	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	NHAI	295.00	0.00	763.80
74	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	251.60
75	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER	Road Transport & Highways	NHAI	464.00	0.00	533.80
76	Armur to kadloor yellareddy	Road Transport & Highways	NHAI	390.56	0.00	631.70
77	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	NHAI	229.91	0.00	240.80
78	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	217.40
79	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	177.10
80	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	NHAI	200.00	0.00	207.80
81	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	NHAI	264.72	0.00	268.70
82	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	3337.00
83	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	917.50
84	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	388.00	0.00	439.20
85	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	NHAI	168.00	0.00	457.30

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
86	GORAKHPUR BYPASS, NH-28, PHASE II EAST-WEST CORRIDOR	Road Transport & Highways	NHAI	600.24	0.00	750.80
87	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	292.50
88	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	NHAI	227.00	0.00	383.20
89	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	NHAI	225.00	0.00	257.50
90	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	NHAI	355.06	0.00	436.30
91	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	278.50
92	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	363.90
93	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	477.10
94	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	266.60
95	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	271.70
96	NALBARI T BIJNI (AS-7)	Road Transport & Highways	NHAI	208.00	0.00	235.50
97	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	491.20
98	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	266.10
99	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	573.30
100	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	NHAI	229.00	0.00	351.20
101	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	NHAI	273.00	0.00	475.60

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
102	GARH Mukteshwar-Muradabad (NHAI) Others KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	300.00
103	Hapur-Garh Mukteswar (Others) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	258.80
104	Rail Connectivity to ICTT at Vallarpadam at Cochin Port Trust	Shipping & Ports	RVNL	245.67	0.00	336.26
105	67.5 MW TG-5 Aux. Stem Emergency Power Requirement Exp. Unit	Steel	RINL	230.00	0.00	240.27

LIST OF ON SCHEDULED PROJECTS as on 01-03-2012

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
1	GAGAN PROJECT	Civil Aviation	AAI	09/2008	06/2013	N.A.	06/2013	626.00	626.00
2	Muraidih UG Turn-key Project	Coal	BCCL	02/2011	04/2014	N.A.	04/2014	339.88	339.88
3	Moonidih XV Seam UG	Coal	BCCL	08/2011	04/2015	N.A.	04/2015	1230.27	1230.27
4	Purnadih OCP	Coal	CCL	07/2008	03/2013	N.A.	03/2013	210.98	210.98
5	KARMA OCP	Coal	CCL	06/2009	03/2014	N.A.	03/2014	162.46	162.46
6	Rajrappa RCE OCP	Coal	CCL	12/2009	03/2016	N.A.	03/2016	510.85	510.85
7	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	Coal	NCL	10/2007	03/2012	N.A.	03/2012	259.40	259.40
8	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	Coal	NCL	06/2011	03/2018	N.A.	03/2018	1131.28	1131.28
9	BINA EXTN. PROJ(6.0 Mtpa)	Coal	NCL	11/2006	03/2014	N.A.	03/2014	168.97	168.97
10	SHANTIKHANI LONGWALL PROJ-SCCL	Coal	SCCL	10/2006	03/2012	N.A.	03/2012	249.03	249.03
11	Kistaram OCP	Coal	SCCL	11/2010	03/2015	N.A.	03/2015	242.29	242.29
12	JALLARAM SHAFT PROJECT	Coal	SCCL	03/2013	03/2013	N.A.	03/2013	467.78	467.78
13	RKP OCP PHASE-I	Coal	SCCL	03/2010	03/2015	N.A.	03/2015	209.78	209.78
14	JAGANNATHPUR OCP(3.00 MTY)	Coal	SECL	09/2008	03/2015	N.A.	03/2015	152.43	152.43
15	Batura OCP (2.0 MTY)	Coal	SECL	09/2008	03/2015	N.A.	03/2015	203.82	203.82
16	KARTALI (EAST) OCP(2.50 MTY)	Coal	SECL	07/2008	03/2014	N.A.	03/2014	178.44	178.44
17	AMLAI OC EXPANSION SECTOR 1.50 MTY	Coal	SECL	11/2009	03/2016	N.A.	03/2016	198.59	198.59
18	PELMA OCP(10.00MTY)	Coal	SECL	07/2008	03/2015	N.A.	03/2015	448.32	448.32
19	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	Fertilisers	NFL	01/2010	01/2013	N.A.	01/2013	1294.19	1294.19
20	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	Fertilisers	NFL	01/2010	01/2013	N.A.	01/2013	1292.84	1292.84
21	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	Petroleum	GAIL	08/2010	02/2014	N.A.	02/2014	8140.00	8140.00
22	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	Petroleum	IOCL	07/2010	01/2013	N.A.	01/2013	1000.00	1000.00
23	PARADIP-RAIPUR-SAMBALPUR- RANCHI PIPELINE	Petroleum	IOCL	08/2009	09/2012	09/2012	09/2012	1793.00	1400.00
24	Integrated crude Oil handling facilities at Paradip(2nd SPM)	Petroleum	IOCL	12/2009	06/2012	06/2012	06/2012	1492.33	1300.00
25	Polypropylene unit	Petroleum	Mangalore Refin	05/2009	07/2012	N.A.	07/2012	1803.78	1803.78
26	Wax Project	Petroleum	NRL	06/2010	12/2013	12/2013	12/2013	576.60	576.60

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
27	ASSAM RENEWAL PROJECT FOR GROUP A	Petroleum	ONGC	03/2009	03/2013	N.A.	03/2013	2465.15	2378.86
28	Development of WO-16 Cluster Fields	Petroleum	ONGC	06/2010	01/2014	N.A.	01/2014	2523.00	2523.00
29	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	Petroleum	ONGC	03/2011	05/2013	N.A.	05/2013	861.79	861.79
30	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	Petroleum	ONGC	06/2010	01/2014	N.A.	01/2014	202.94	202.94
31	Construction of 6 ETps	Petroleum	ONGC	03/2009	09/2012	N.A.	09/2012	302.26	302.26
32	Mehesana Redevelopment	Petroleum	ONGC	11/2010	04/2015	N.A.	04/2015	3823.00	3823.00
33	Ankleswar Redevelopment	Petroleum	ONGC	11/2010	12/2014	N.A.	12/2014	2189.63	2189.63
34	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura	Petroleum	ONGC	07/2008	08/2012	N.A.	08/2012	288.04	288.04
35	Ahmedabad Redevelopment	Petroleum	ONGC	11/2010	12/2014	N.A.	12/2014	1916.10	1916.10
36	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	Power	NEEPCO	01/2011	01/2014	N.A.	01/2014	913.63	913.63
37	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHON RBC	Power	PGCIL	08/2008	08/2012	N.A.	08/2012	7075.33	7075.33
38	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT	Power	PGCIL	12/2008	12/2012	N.A.	12/2012	7031.88	7031.88
39	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC	Power	PGCIL	08/2008	08/2012	N.A.	08/2012	2360.95	2360.95
40	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID PART-II	Power	PGCIL	07/2009	06/2012	N.A.	06/2012	1736.36	1736.36
41	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT KALA IN UT DNH	Power	PGCIL	07/2011	07/2013	N.A.	07/2013	181.93	181.93
42	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	Power	PGCIL	08/2011	12/2013	N.A.	12/2013	1391.97	1391.97

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
43	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED	Power	PGCIL	08/2011	10/2013	N.A.	10/2013	425.51	425.51
44	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	Power	PGCIL	09/2011	12/2013	N.A.	12/2013	1366.34	1366.34
45	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power Madras Limited LT	Power	PGCIL	09/2011	09/2014	N.A.	09/2014	1940.13	1940.13
46	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A	Power	PGCIL	10/2011	11/2013	N.A.	11/2013	558.26	558.26
47	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH	Power	PGCIL	07/2011	07/2013	N.A.	07/2013	181.93	181.93
48	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	2422.66	2422.66
49	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-III	Power	PGCIL	11/2009	05/2012	N.A.	05/2012	1075.12	1075.12
50	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	Power	PGCIL	02/2012	10/2014	N.A.	10/2014	1927.16	1927.16
51	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1	Power	PGCIL	02/2012	08/2014	N.A.	08/2014	324.33	324.33
52	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH	Power	PGCIL	02/2012	02/2015	N.A.	02/2015	1310.85	1310.85
53	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD	Power	PGCIL	01/2012	01/2013	N.A.	01/2013	259.28	259.28
54	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	Power	PGCIL	01/2012	01/2015	N.A.	01/2015	1422.85	1422.85

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
55	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	1746.65	1746.65
56	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	297.33	297.33
57	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	Power	PGCIL	12/2011	02/2014	N.A.	02/2014	552.44	552.44
58	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH	Power	PGCIL	11/2011	07/2014	N.A.	07/2014	2127.51	2127.51
59	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL)	Power	PGCIL	08/2011	08/2014	N.A.	08/2014	1637.34	1637.34
60	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	Power	PGCIL	08/2011	12/2013	N.A.	12/2013	1391.97	1391.97
61	SYSTEM STRENGTHENING XIII OF SR GRID	Power	PGCIL	10/2011	06/2014	N.A.	06/2014	487.49	487.49
62	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA- PART A	Power	PGCIL	09/2010	03/2013	N.A.	03/2013	2074.86	2074.86
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX	Power	PGCIL	10/2010	01/2013	N.A.	01/2013	182.68	182.68
64	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	1719.52	1719.52
65	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND BANGLADESH -INDIAN PORTION	Power	PGCIL	10/2010	10/2012	N.A.	10/2012	160.32	160.32

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
66	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM BHU	Power	PGCIL	04/2010	01/2015	N.A.	01/2015	4404.57	4404.57
67	System Strengthening -X of SR	Power	PGCIL	12/2009	04/2012	N.A.	04/2012	276.61	276.61
68	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B	Power	PGCIL	03/2011	11/2013	N.A.	11/2013	1585.12	1585.12
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	209.78	209.78
70	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR TPS	Power	PGCIL	08/2010	04/2013	N.A.	04/2013	170.36	170.36
71	System Strengthening -XII of SR	Power	PGCIL	02/2010	06/2012	N.A.	06/2012	232.34	232.34
72	EASTERN REGION TRANSMISSION SYSTEM-III	Power	PGCIL	07/2010	11/2012	N.A.	11/2012	1272.80	1272.80
73	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A	Power	PGCIL	05/2010	01/2013	N.A.	01/2013	250.03	250.03
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	Power	PGCIL	07/2010	07/2013	N.A.	07/2013	752.64	752.64
75	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM PART A	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	779.21	779.21
76	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN ORISSA-B	Power	PGCIL	12/2010	12/2013	N.A.	12/2013	2743.19	2743.19
77	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-III Gen Project	Power	PGCIL	03/2010	11/2012	N.A.	11/2012	4672.99	4672.99
78	MAUDA TRANSMISSION SYSTEM	Power	PGCIL	02/2010	10/2012	N.A.	10/2012	469.38	469.38
79	System Strengthening in NR for SASAN & MUNDRA (UMPP)	Power	PGCIL	12/2009	08/2012	N.A.	08/2012	1216.83	1216.83
80	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C	Power	PGCIL	03/2011	03/2014	N.A.	03/2014	2569.25	2569.25

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
81	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	Power	PGCIL	03/2010	11/2012	N.A.	11/2012	965.58	965.58
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI	Power	PGCIL	08/2010	04/2013	N.A.	04/2013	1677.57	1677.57
83	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	Power	PGCIL	05/2011	05/2014	N.A.	05/2014	1961.87	1961.87
84	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	Power	PGCIL	10/2008	10/2012	N.A.	10/2012	4824.12	4824.12
85	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	07/1998	12/2012	N.A.	12/2012	248.44	1103.47
86	Tinpahar - Sahibganj (ER)	Railways	ER	04/2008	03/2012	N.A.	03/2012	167.73	167.73
87	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER)	Railways	ER	04/1999	12/2012	N.A.	12/2012	207.52	207.52
88	New Line from Dimapur to Zubza(Kohima) national project (NEFR)	Railways	NEFR	04/2006	03/2015	N.A.	03/2015	850.00	850.00
89	AGARTALA SABROOM, NL, NEFR	Railways	NEFR	04/2008	03/2014	N.A.	03/2014	813.34	1141.75
90	SEVOK RANGPO, NEFR	Railways	NEFR	04/2008	12/2015	N.A.	12/2015	1339.48	3380.57
91	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR)	Railways	NWR	04/2008	03/2014	N.A.	03/2014	653.19	653.19
92	Suratpura - Hanumangarh - Sriganganagar Gauge Conversion (NWR)	Railways	NWR	04/2008	03/2014	N.A.	03/2014	516.23	516.23
93	Himmatnagar - Udaipur Gauge Conversion (NWR)	Railways	NWR	04/2008	03/2015	N.A.	03/2015	829.74	829.74
94	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT	Railways	RE	02/2008	03/2012	N.A.	03/2012	171.10	171.10
95	SUKINDA ROAD - ANGUL (NL)(ECOR)	Railways	RVNL	04/1998	02/2015	N.A.	02/2015	183.23	638.00
96	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh.	Railways	RVNL	04/2010	03/2016	N.A.	03/2016	2619.02	2619.02
97	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP)	Railways	RVNL	04/2010	03/2016	N.A.	03/2016	3951.98	3951.98

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
98	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA- JAGDALPUR),NL,RVNL	Railways	RVNL	04/1995	12/2012	N.A.	12/2012	304.00	968.60
99	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)	Railways	SWR	04/2007	03/2013	N.A.	03/2013	482.00	482.70
100	Udhna-Jalgaon with electrification(doubling) (WR)	Railways	WR	04/2008	03/2014	N.A.	03/2014	1389.62	1389.62
101	Bhuj-Naliya(GC) with extension from naliyate vayor (WR)	Railways	WR	04/2008	03/2012	N.A.	03/2012	318.24	468.62
102	Ahmedabad-Himmatnagar- Udaipur (WR)	Railways	WR	04/2008	03/2013	N.A.	03/2013	394.13	394.14
103	Talegaon-amravati	Road Transport & Highways	NHAI	11/2009	11/2013	N.A.	11/2013	567.00	567.00
104	Hyderabad-yadgiri N.H no- 202	Road Transport & Highways	NHAI	08/2010	05/2012	N.A.	05/2012	388.00	388.00
105	DEOLI-KOTA	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	953.00	593.00
106	Hyderabad-Vijaywada Km. 40 to 221.50 Km	Road Transport & Highways	NHAI	04/2010	10/2012	N.A.	10/2012	1740.00	1740.00
107	PANIPAT-ROHTAK	Road Transport & Highways	NHAI	04/2011	10/2014	N.A.	10/2014	807.00	807.00
108	4 LANING OF NAGPUR- BETUL	Road Transport & Highways	NHAI	02/2011	08/2014	N.A.	08/2014	2498.76	2498.76
109	INDORE-DEWAS(NH-3)	Road Transport & Highways	NHAI	11/2010	05/2013	N.A.	05/2013	325.00	325.00
110	CUDDAPAH-MYDUKUR- KURNOOL KM-167.750- 356.502 KM	Road Transport & Highways	NHAI	11/2010	05/2013	N.A.	05/2013	1585.00	1585.00
111	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4	Road Transport & Highways	NHAI	09/2010	09/2013	N.A.	09/2013	1655.00	1655.00

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
112	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	06/2010	12/2012	N.A.	12/2012	792.06	792.06
113	Pune-sholapur, pkg1	Road Transport & Highways	NHAI	11/2009	05/2012	N.A.	05/2012	1110.00	1110.00
114	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	03/2005	07/2012	N.A.	07/2012	940.00	940.00
115	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	12/2009	06/2012	N.A.	06/2012	835.00	835.00
116	Indore-Jhabua-Gujrat/MP	Road Transport & Highways	NHAI	10/2010	04/2013	N.A.	04/2013	1175.00	1175.00
117	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	08/2010	01/2013	N.A.	01/2013	625.07	625.07
118	Gujarat/Maharashtra Border Surat-Hazira Port Section	Road Transport & Highways	NHAI	03/2010	09/2012	N.A.	09/2012	1509.10	1509.10
119	Two laning of Trichy - Karaikudi and Trychi Bypass	Road Transport & Highways	NHAI	05/2010	05/2013	N.A.	05/2013	374.00	374.00
120	Kandla - Mundra port	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	953.88	953.88
121	2 Laning of Muzaffarpur - Sonbarsa	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	511.54	511.54
122	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	Road Transport & Highways	NHAI	06/2011	06/2013	N.A.	06/2013	600.00	600.00
123	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	Road Transport & Highways	NHAI	09/2011	12/2013	N.A.	12/2013	1250.00	1250.00
124	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	Road Transport & Highways	NHAI	06/2011	12/2013	N.A.	12/2013	535.00	535.00

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
125	GHAZIABAD-ALIGARH NH-91	Road Transport & Highways	NHAI	02/2011	08/2013	N.A.	08/2013	1141.00	1141.00
126	ROHTAK-BAWAL	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	650.00	650.00
127	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	Road Transport & Highways	NHAI	03/2011	08/2013	N.A.	08/2013	785.50	785.50
128	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	511.54	511.54
129	4-LANNING OF CHAPRA-HAJIPUR	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	575.00	575.00
130	2-LANNING WITH PS MOTIHARI-RAXAUL	Road Transport & Highways	NHAI	10/2011	04/2014	N.A.	04/2014	375.09	375.09
131	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	Road Transport & Highways	NHAI	09/2011	03/2014	N.A.	03/2014	574.00	574.00
132	2-LANNING WITH PS KHAGARIA-PURNEA	Road Transport & Highways	NHAI	05/2011	02/2014	N.A.	02/2014	664.00	664.00
133	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	Road Transport & Highways	NHAI	11/2011	05/2014	N.A.	05/2014	1535.00	1535.00
134	VARANASI-AURANGABAD KM.786 TO KM.978.40	Road Transport & Highways	NHAI	09/2011	03/2014	N.A.	03/2014	2848.00	2848.00
135	2-LANNING OF SHILONG BYPASS	Road Transport & Highways	NHAI	02/2011	02/2014	N.A.	02/2014	226.00	226.00
136	JORBAT - BARAPANI	Road Transport & Highways	NHAI	01/2011	01/2014	N.A.	01/2014	536.00	536.00
137	SAMAIKHIALI - GANDHIDHAM	Road Transport & Highways	NHAI	09/2010	03/2013	N.A.	03/2013	805.39	805.39

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
138	Tirupati - Tiruthani - Chennai	Road Transport & Highways	NHAI	04/2011	10/2013	N.A.	10/2013	571.00	571.00
139	2 laning of Dindigul - Perigulam Theni- kumili	Road Transport & Highways	NHAI	09/2011	08/2013	N.A.	08/2013	485.00	485.00
140	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	12/2010	06/2013	N.A.	06/2013	1008.50	1008.50
141	PATNA-MUZZAFFARPUR	Road Transport & Highways	NHAI	08/2010	02/2013	N.A.	02/2013	671.30	671.30
142	NASHRI CHANANI	Road Transport & Highways	NHAI	06/2010	06/2015	N.A.	06/2015	2159.00	2159.00
143	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	Road Transport & Highways	NHAI	07/2010	07/2015	N.A.	07/2015	1987.00	1987.00
144	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	Road Transport & Highways	NHAI	09/2010	03/2013	N.A.	03/2013	852.00	852.00
145	PUNE-SATARA(NH-4)	Road Transport & Highways	NHAI	10/2010	03/2013	N.A.	03/2013	1724.55	1724.55
146	MURADABAD-BAREILY	Road Transport & Highways	NHAI	04/2010	06/2013	N.A.	06/2013	1267.00	1267.00
147	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	Road Transport & Highways	NHAI	02/2011	11/2012	N.A.	11/2012	193.45	193.45
148	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	11/2009	05/2012	N.A.	05/2012	795.00	795.00
149	Modification & Strengthening of Existing Berth No. 1 to 6	Shipping & Ports	PORT TRUST	06/2010	03/2012	N.A.	03/2012	277.00	277.00
150	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS	Shipping & Ports	SHIPP.	08/2008	09/2012	N.A.	09/2012	1066.91	968.35

SN	TITLE	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
151	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries	Shipping & Ports	SHIPP.	08/2010	12/2012	N.A.	12/2012	612.72	627.64
152	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd.	Shipping & Ports	SHIPP.	10/2010	12/2013	N.A.	12/2013	1028.10	1028.10
153	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy	Shipping & Ports	SHIPP.	10/2010	02/2014	N.A.	02/2014	966.46	994.82
154	1.2 MTPA PELLET PLANT DONIMALAI	Steel	NMDC	04/2011	04/2013	N.A.	04/2013	572.00	572.00
155	7.0 MTPA KUMARASWAMY IRON ORE MINE	Steel	NMDC	02/2011	05/2013	N.A.	05/2013	898.55	898.55
156	EXPENSION OF ROURKELA STEEL PLANT	Steel	SAIL	09/2008	03/2013	N.A.	03/2013	11812.00	11812.00
157	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES	Steel	SAIL	11/2011	11/2013	N.A.	11/2013	254.55	254.55
158	DELHI MRTS PHASE-III	Urban Development	DMRC	09/2011	03/2016	N.A.	03/2016	35242.00	35242.00
159	FARIDABAD EXTENSION	Urban Development	DMRC	09/2011	09/2014	N.A.	09/2014	2494.00	2494.00

List of project Without Original Date of Commissioning

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/0
	Total		1,106.29	1,106.29	1,000.70				0/0
<u>Coal</u>									
2	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	70.06	-	03/2012	-	5/7
3	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,570.74	-	02/2013	-	0/39
4	KUSMUNDA EXPN.OC(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	623.41	-	03/2013	-	0/8
5	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	117.04	-	03/2013	-	6/11
6	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	91.20	-	03/2013	-	5/7
7	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	262.24	-	03/2014	-	0/4
8	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	209.33	-	03/2014	-	0/5
9	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	59.22	-	03/2015	-	2/12
10	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.70	-	03/2015	-	1/1
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.21	-	03/2015	-	0/29
12	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	-	03/2015	-	0/31
13	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	6.57	-	12/2015	-	0/33
14	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	34.28	-	03/2016	-	1/12
15	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	105.16	-	03/2017	-	6/12
	Total		15,757.23	16,216.77	4,151.16				26/211
<u>Fertilisers</u>									
16	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	275.67	- 04/2012	04/2012	0(R3)	7/22
17	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	449.28	- 01/2013	01/2013	0(R3)	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			1,967.38	1,967.38	724.95				7/30
<u>Steel</u>									
18	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	355.21	-	02/2012	-	1/3
19	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	317.49	-	03/2012	3(R3)	18/21
20	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	232.76	-	05/2012	21(R3)	1/1
21	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	240.27	-	06/2012	16(R3)	2/3
22	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	63.54	-	10/2012	0(R3)	3/4
23	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	460.00	178.25	-	12/2012	7(R3)	1/2
Total			1,874.79	2,478.33	1,387.52				26/34
<u>Petrochemicals</u>									
24	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61	8,920.00	3,968.16	-	12/2013	0(R3)	9/30
Total			5,460.61	8,920.00	3,968.16				9/30
<u>Petroleum</u>									
25	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07	1,385.00	1,150.46	-	03/2012	3(R3)	0/9
26	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	330.47	194.58	-	03/2012	0(R3)	3/20
27	WIND ENERGY - [N16000126]GAIL,Multi State	05/2011	616.00	616.00	268.08	-	03/2012	-	0/18
28	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	85.97	-	05/2012	-	21/36
29	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	46.28	-	02/2013	0(R3)	29/42
30	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	460.70	180.44	-	03/2013	8(R2)	7/16
31	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	-	04/2013	52(R3)	0/0
32	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00	1,827.00	370.68	-	04/2013	0(R3)	0/167
33	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,300.00	612.64	-	04/2013	4(R3)	0/21

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		11,046.96	10,394.66	5,430.04				60/329
	<u>Power</u>								
34	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01 623.44	623.44	104.22	- 07/2013	07/2013	0(R3)	0/30
	Total		421.01	623.44	104.22				0/30
	<u>Railways</u>								
35	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.28	- -	02/2012	-	0/0
36	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,238.88	- -	02/2012	-	0/0
37	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	461.93	- 12/2009	02/2012	26(R1)	0/0
38	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	820.32	547.46	- -	03/2012	-	0/0
39	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	498.92	- 12/2011	03/2012	3(R3)	0/0
40	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	212.77	- 03/2012	03/2012	0(R3)	0/0
41	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	411.22	438.19	- 03/2012	03/2012	0(R3)	0/0
42	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	107.40	- -	03/2012	-	0/0
43	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	903.56	590.94	- 03/2012	03/2012	0(R3)	0/0
44	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	246.26	- 02/2011	03/2012	13(R3)	0/0
45	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	200.70	- -	03/2012	-	0/0
46	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	427.89	370.05	- 03/2012	03/2012	0(R3)	0/0
47	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	197.98	- -	03/2012	-	0/0
48	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	944.25	- -	03/2012	-	0/0
49	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	415.73	230.81	- -	03/2012	-	0/0
50	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	333.85	- 07/2012	07/2012	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
51	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	389.55	- 03/2012	12/2012	9(R3)	0/0
52	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	252.72	- 03/2012	12/2012	9(R3)	0/0
53	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	175.30	- -	03/2013	-	0/0
54	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	724.37	- -	03/2013	-	0/0
55	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	989.40	- -	03/2013	-	0/0
56	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	89.95	- -	03/2013	-	0/0
57	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	- 02/2009	04/2013	50(R1)	0/0
58	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	200.93	- 03/2009	04/2013	49(R1)	0/0
59	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTPT,Tamil Nadu	04/2006	495.74 -	495.74	158.81	- 06/2013	06/2013	0(R3)	0/0
60	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
61	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	92.24	- -	03/2014	-	0/0
62	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	239.05	- -	03/2015	-	0/0
63	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	724.41	- 12/2010	03/2015	51(R3)	0/0
64	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	174.38	- -	03/2015	-	0/0
65	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.23	- -	03/2015	-	0/0
66	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	366.18	- 12/2012	-	-	0/0
67	CONV.OF 1500V DC TRACTION TO 25 KV AC,CR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	- 06/2012	-	-	0/0
Total			8,638.20 -	22,021.86	12,602.07				0/0
Road Transport & Highways									
68	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	241.70	- 06/2011	03/2012	9(R3)	0/2
69	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00 -	441.00	947.20	- -	03/2012	-	0/0
70	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00 -	748.00	1,373.00	- -	03/2013	-	0/3

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
71	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00 -	946.00	981.60	- -	03/2013	-	2/2
72	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00 -	671.00	603.20	- -	03/2013	-	0/1
73	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	-	2/2
74	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00 -	453.00	173.50	- -	06/2013	-	1/1
75	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00 -	480.00	273.20	- -	10/2013	-	0/1
76	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00 -	839.00	-	- -	12/2013	-	0/1
Total			5,454.50 -	5,454.50	4,593.40				5/13
Grand Total			51,726.97	69,183.23	33,962.22				133/677

List of project Without Date of Commissioning

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	-		09/2010	01/2012		
	Total		3,492.00	-					
	<u>Coal</u>								
2	BALRAM OCP EXTENSION,MCL (8.00 Mt) - [N06000044]MCL,Orissa	12/2007	172.08	-		-	03/2010		
	Total		172.08	-					
	<u>Petroleum</u>								
3	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	-		12/2010	06/2011		
4	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39			09/2009	08/2011		
5	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	-		09/2010	09/2011		
6	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	-		-	12/2011		
7	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-		-	-		
8	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00			02/2011 08/2011	-		
	Total		6,773.54	-					
	<u>Power</u>								
9	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	-		08/2011	01/2012		
10	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16			12/2007 12/2009	-		
	Total		807.24	-					
	<u>Railways</u>								
11	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04			03/1998 08/2005	08/2005		
12	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	-		12/2007 03/2010	12/2010		

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
13	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73			03/2009 12/2008	12/2010		
14	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23			02/2010 02/2011	02/2011		
15	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27			06/1999 03/2011	03/2011		
16	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23			- -	03/2011		
17	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60			- 03/2011	03/2011		
18	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -			- 03/2009	03/2011		
19	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -			03/2009 12/2009	03/2011		
20	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -			- 03/2011	03/2011		
21	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTPT,Maharashtra	04/2003	3,125.20 4,174.40			- 06/2011	06/2011		
22	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46			03/1994 -	12/2011		
23	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -			- 09/2009	12/2011		
24	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87			- 03/2010	-		
25	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68			- -	-		
26	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91			- -	-		
27	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00			03/1998 -	-		
28	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88			- -	-		
29	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -			- -	-		
30	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26			07/2008 -	-		
31	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20			07/2005 -	-		
32	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -			- -	-		
33	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70			- 05/2009	-		
34	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87			- -	-		
35	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30			06/2007 -	-		

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -			04/2003 03/2010	-		
37	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -			- -	-		
38	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -			- -	-		
39	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -			- -	-		
40	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17			- -	-		
41	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13			- -	-		
42	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82			- -	-		
43	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -			03/2008 06/2008	-		
44	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -			- -	-		
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -			- -	-		
46	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -			- -	-		
47	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -			- -	-		
48	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83			- -	-		
49	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -			- -	-		
50	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95			03/2011 -	-		
51	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44			03/2004 12/2010	-		
52	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -			05/2008 03/2011	-		
53	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09			12/2009 03/2011	-		
54	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -			- -	-		
55	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -			- -	-		

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
56	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,176.10			12/2006 08/2010	-		
57	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 -			- -	-		
58	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, Bihar	04/2003	218.19 -			- -	-		
59	HATHUA-BHATNI (N L) (NER) - [220100319]NER, Multi State	04/2005	230.03 -			- -	-		
60	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER, West Bengal	04/2007	245.15 -			12/2010 03/2011	-		
61	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 -			- 12/2010	-		
	Total		17,849.93 -						
Shipping & Ports									
62	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67 -			04/2009 11/2009	02/2011		
63	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK, Tamil Nadu	10/2004	196.25 -			06/2006 09/2011	09/2011		
64	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00 165.00			12/2005 01/2008	10/2011		
65	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP., Kerala	12/2010	241.50 -			09/2011 -	12/2011		
66	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST, Maharashtra	10/2005	800.00 -			10/2008 -	-		
67	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84 -			12/2007 01/2009	-		
68	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD, Tamil Nadu	09/2006	399.13 -			08/2010 -	-		
69	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD, Tamil Nadu	09/2006	370.00 -			08/2010 -	-		
70	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40 -			10/2008 -	-		
	Total		4,999.79 -						
Telecommunications									
71	Implementation of FTTH, the state of the art access, upon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -			03/2010 -	10/2010		
72	GSM equipment of 200000 Lines (2G) UP (West) Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84 -			10/2009 -	03/2011		

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
73	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	-		02/2007	08/2011		
74	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	-		09/2011	09/2011		
75	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72			06/2009	12/2011		
76	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	-		01/2010	12/2011		
77	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	-		10/2007	-		
78	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	-		03/2009	-		
79	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	-		03/2009	-		
80	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	-		03/2010	-		
	Total		4,737.01	-					
Urban Development									
81	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08			04/2009	-		
	Total		114.18						0/0
Grand Total			38,945.77						

List of Delay Project

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,326.00	12/2008	03/2013	51	
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,418.00	12/2015	11/2016	11	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	888.00	12/2016	03/2017	3	
Total			36,950.00	39,603.00	16,632.00				
<u>Civil Aviation</u>									
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,631.72	01/2011	02/2012	13	
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	86.87	05/2012	08/2012	3	
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,770.64	05/2011	10/2012	17	
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	178.46	01/2011	12/2012	23	
Total			4,395.58	4,985.07	3,667.69				
<u>Coal</u>									
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	87.87	03/2010	03/2012	24	
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,980.00	3,027.00	2,374.35	06/2009	07/2012	37	
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	107.77	03/2011 03/2012	03/2013	24	
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88	741.62	330.54	03/2010	03/2013	36	
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	80.13	03/2012	03/2013	12	
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	36.68	03/2012	03/2013	12	
14	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,318.96	03/2010	03/2014	48	
15	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	1,182.40	03/2010	03/2014	48	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	19.96	03/2011 -	03/2014	36	
17	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.66	03/2011 03/2012	03/2014	36	
18	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	62.45	03/2012 03/2012	03/2014	24	
19	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	94.75	03/2012 03/2013	03/2014	24	
20	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	249.11	03/2013 09/2012	10/2014	19	
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 -	535.10	155.37	03/2012 -	03/2015	36	
22	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48	
23	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	71.46	12/2012 -	03/2015	27	
24	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 -	1,143.54	276.55	03/2014 -	03/2016	24	
25	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	18.16	07/2012 03/2014	03/2016	44	
	Total		11,310.67 -	14,299.68	6,500.17				
Fertilisers									
26	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	151.41	07/2011 -	03/2012	8	
27	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	168.93	07/2011 -	04/2012	9	
	Total		763.00 -	763.00	320.34				
Steel									
28	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 -	232.93	183.65	05/2011 -	05/2012	12	
29	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,405.92	10/2009 10/2012	10/2012	36	
30	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	6,325.00 -	6,325.00	2,419.04	12/2011 -	10/2012	10	
31	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	12,800.19	12/2011 -	12/2012	12	
32	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,Chhatisgarh	06/2009	2,875.00 -	2,875.00	603.24	12/2012 -	03/2013	3	
33	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	4,758.04	03/2013 -	09/2013	6	
	Total		49,832.93 -	55,396.93	30,170.08				

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Petroleum</u>								
34	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	167.90	03/2009 02/2012	02/2012	35	
35	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	812.91	09/2011 03/2012	03/2012	6	
36	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	696.52	04/2010 -	03/2012	23	
37	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	296.85	04/2011 -	03/2012	11	
38	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	-	09/2011 03/2012	03/2012	6	
39	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	695.80	04/2011 12/2011	04/2012	12	
40	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	190.97	03/2012 08/2012	04/2012	1	
41	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,524.63	05/2010 05/2012	05/2012	24	
42	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	345.93	05/2010 04/2012	05/2012	24	
43	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	777.00	09/2011 05/2012	05/2012	8	
44	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 252.37	204.00	162.35	01/2012 -	05/2012	4	
45	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,918.57	04/2006 05/2011	06/2012	74	
46	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	7,883.30	01/2012 -	06/2012	5	
47	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	477.60	07/2010 05/2012	07/2012	24	
48	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	166.82	04/2011 -	07/2012	15	
49	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,583.36	03/2012 08/2012	08/2012	5	
50	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	533.63	03/2011 05/2011	10/2012	19	
51	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	257.92	09/2011 -	12/2012	15	
52	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	642.22	06/2012 -	12/2012	6	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
53	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	977.00	157.05	12/2011	01/2013	13	
54	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90	438.85	274.39	03/2006	03/2013	84	
55	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	417.93	03/2010	03/2013	36	
56	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	8,813.41	6,819.59	05/2010	03/2013	34	
57	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	2,920.82	1,173.84	09/2010	04/2013	31	
58	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	1.50	03/2013	04/2013	1	
59	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	-	03/2013	04/2013	1	
60	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	1,106.00	-	06/2012	04/2013	10	
61	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	-	11/2012	05/2013	6	
62	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	13,742.98	11/2012	06/2013	7	
63	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	3,062.41	09/2012	09/2013	12	
64	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8	
65	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	5,633.44	2,498.70	08/2010	12/2013	40	
66	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	-	08/2013	01/2014	5	
67	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	597.20	03/2007	03/2014	84	
68	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.41	10/2010	12/2014	50	
69	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.20	01/2013	07/2015	30	
70	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,447.85	03/2007	03/2017	120	
	Total		102,089.65	110,505.29	52,333.33				
Power									
71	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,283.69	2,595.25	04/2005	03/2012	83	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
72	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC, Chhatisgarh	12/2003	8,323.39	8,323.39	7,676.00	12/2009	03/2012	27	
73	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL, Multi State	10/2006	975.96	975.66	748.40	10/2009	03/2012	29	
74	SIMHADRI STPP STAGE -II - [N18000032]NTPC, Andhra Pradesh	08/2007	5,103.39	5,038.83	4,402.00	05/2011	03/2012	10	
75	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL, Multi State	02/2009	664.96	664.96	352.70	02/2012	03/2012	1	
76	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL, Multi State	02/2009	409.50	409.50	96.40	02/2012	03/2012	1	
77	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL, Multi State	03/2009	196.10	196.10	121.10	07/2011	03/2012	8	
78	CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.	08/2005	1,405.63	2,084.00	1,780.21	08/2010	04/2012	20	
79	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT (P.G.R.) - [180100260]PGCIL, Bihar	12/2005	3,779.46	3,779.46	3,652.60	09/2009	06/2012	33	
80	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL, Rajasthan	07/2006	5,221.23	5,221.23	3,059.40	07/2010	06/2012	23	
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL, Multi State	02/2009	317.69	317.69	123.70	11/2011	06/2012	7	
82	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL, Multi State	04/2008	297.37	297.91	308.93	07/2011	06/2012	11	
83	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL, Multi State	02/2009	1,347.32	1,347.32	964.20	02/2012	06/2012	4	
84	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC, J and K	08/2005	1,729.29	1,794.00	1,671.01	11/2009	08/2012	33	
85	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC, West Bengal	10/2003	768.92	1,628.39	1,431.96	03/2007	09/2012	66	
86	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL, Himachal Pr.	07/2006	557.24	557.24	520.60	01/2010	09/2012	32	
87	LOHARINAG-PAL HEP (4X150MW) - [N18000005]NTPC, Uttarakhand	06/2006	2,895.10	2,895.10	686.00	11/2011	12/2012	13	
88	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC, J and K	08/2006	621.26	913.25	724.04	02/2011	12/2012	22	
89	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL, Multi State	02/2009	520.48	520.48	263.80	11/2011	12/2012	13	
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State	02/2009	509.66	509.66	307.90	11/2011	12/2012	13	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	145.60	02/2012 -	12/2012	10	
92	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,694.25	10/2010 12/2011	01/2013	27	
93	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	710.09	08/2010 09/2011	01/2013	29	
94	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,112.00	04/2009 -	03/2013	47	
95	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,779.29	1,786.98	09/2008 -	03/2013	54	
96	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	389.00	09/2010 -	03/2013	30	
97	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	3,532.00	08/2012 -	03/2013	7	
98	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	140.20	11/2011 -	03/2013	16	
99	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	2,824.00	10/2012 -	03/2013	5	
100	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,644.00	10/2012 -	03/2013	5	
101	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,085.43	09/2009 -	06/2013	45	
102	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	592.80	12/2012 -	06/2013	6	
103	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	297.95	08/2012 08/2013	08/2013	12	
104	RAMPUR HEP(412 MW) - [N18000024]SJVN,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,540.50	01/2012 -	09/2013	20	
105	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	297.01	07/2006 01/2014	01/2014	90	
106	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,487.00	08/2013 -	01/2014	5	
107	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,793.00	06/2011 -	04/2014	34	
108	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,337.00	03/2013 -	06/2014	15	
109	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,491.20	09/2009 07/2014	07/2014	58	
110	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	3,596.20	08/2013 -	09/2014	13	
111	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,509.00	12/2009 -	12/2014	60	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
112	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,475.18	09/2010 08/2014	12/2015	63	
113	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	303.71	07/2010 02/2016	02/2016	67	
114	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,772.88	05/2013 06/2016	06/2016	37	
115	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 3,422.44	3,422.44	242.75	07/2014 -	09/2016	26	
116	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,127.55	01/2016 01/2016	11/2016	10	
	Total		124,647.00 -	139,374.83	83,413.48				
Railways									
117	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	75.23	12/2011 02/2012	02/2012	2	
118	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	546.82	03/1995 -	03/2012	204	
119	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	196.49	03/2002 -	03/2012	120	
120	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	840.32	547.76	02/2009 -	03/2012	37	
121	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	211.31	03/2010 -	03/2012	24	
122	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12	
123	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	204.73	03/2011 -	03/2012	12	
124	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	276.61	06/2004 -	12/2012	102	
125	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	632.83	03/2009 12/2012	12/2012	45	
126	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,159.80	10/2007 12/2012	12/2012	62	
127	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	469.74	03/2010 -	12/2012	33	
128	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	55.89	03/2012 -	03/2013	12	
129	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	81.63	12/2011 11/2013	11/2013	23	
130	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	283.10	39.12	02/2006 -	12/2013	94	
131	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,027.93	2,936.77	03/2009 -	12/2013	57	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
132	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	156.91	03/2007 03/2007	03/2014	84	
133	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	1,066.29	12/2008 -	03/2014	63	
134	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	85.48	12/2012 -	03/2014	15	
135	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	819.40	108.30	03/2010 06/2014	06/2014	51	
136	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	12	
137	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	723.71	389.41	06/2005 07/2011	06/2015	120	
138	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,336.00	04/2008 03/2014	12/2015	92	
139	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	227.13	02/2010 -	12/2015	70	
140	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	1,173.79	419.77	03/2005 12/2008	03/2016	132	
141	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	622.67	03/2011 03/2014	03/2016	60	
142	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	2.75	03/2014 03/2016	03/2016	24	
143	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	8.17	03/2016 -	06/2016	3	
144	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	7,816.76	03/2001 -	12/2017	201	
	Total		22,739.84 -	53,030.72	21,299.38				
Road Transport & Highways									
145	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	169.48	08/2004 07/2010	03/2012	91	
146	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	178.99	08/2004 -	03/2012	91	
147	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	03/2012	84	
148	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	166.30	184.60	03/2008 -	03/2012	48	
149	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	155.10	03/2008 -	03/2012	48	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
150	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	285.60	10/2008	03/2012	41	
151	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	363.90	03/2008	03/2012	48	
152	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	251.60	01/2009	03/2012	38	
153	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	266.10	06/2008	03/2012	45	
154	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	383.20	12/2008	03/2012	39	
155	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	323.30	09/2008	03/2012	42	
156	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	477.10	09/2008	03/2012	42	
157	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	266.60	11/2008	03/2012	40	
158	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	763.80	08/2010	03/2012	19	
159	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	533.80	01/2011	03/2012	14	
160	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,610.00	08/2011	03/2012	7	
161	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	257.50	10/2008	04/2012	42	
162	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.70	02/2012	04/2012	2	
163	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	177.10	10/2008	05/2012	43	
164	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.20	03/2008	05/2012	50	
165	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	262.30	02/2004	05/2012	99	
166	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	05/2012	16	
167	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27	
168	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00	284.00	351.20	05/2010	05/2012	24	
169	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	187.50	09/2007	06/2012	57	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
170	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	06/2012	87	
171	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	300.00	09/2007	06/2012	57	
172	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	258.80	09/2007	06/2012	57	
173	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	100.30	09/2008	06/2012	45	
174	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.20	10/2008	06/2012	44	
175	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	187.40	06/2008	06/2012	48	
176	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	271.70	06/2008	06/2012	48	
177	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	268.70	06/2008	06/2012	48	
178	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	188.90	06/2008	06/2012	48	
179	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	132.10	05/2008	06/2012	49	
180	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	207.80	06/2008	06/2012	48	
181	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2012	42	
182	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	750.80	10/2009	06/2012	32	
183	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.60	10/2009	06/2012	32	
184	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,406.00	10/2011	06/2012	8	
185	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,337.00	11/2011	06/2012	7	
186	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	97.16	04/2004	07/2012	99	
187	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	182.07	02/2004	07/2012	101	
188	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	166.30	05/2008	08/2012	51	
189	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	218.10	06/2005	09/2012	87	
190	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	278.50	10/2008	09/2012	47	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
191	RAJMARG CHORAH TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI, Madhya Pradesh)	12/2003	229.91	229.91	240.80	10/2008	09/2012	47	
192	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	407.60	185.50	06/2010	10/2012	28	
193	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	233.80	09/2009	10/2012	37	
194	Four Lanning from MP/Maharashtra Border to Nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16	
195	Chikaluripet-Vijaywada 6 lane (km 355 to km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	572.30	580.00	10/2011	10/2012	12	
196	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	581.50	06/2009	11/2012	41	
197	BIJNI TO ASSAM /WB BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80	237.80	226.90	06/2008	12/2012	54	
198	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	217.40	10/2008	12/2012	50	
199	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	251.03	292.50	10/2008	12/2012	50	
200	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	177.40	07/2008	12/2012	53	
201	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	129.50	04/2008	12/2012	56	
202	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	192.90	04/2008	12/2012	56	
203	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	235.50	04/2008	12/2012	56	
204	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	165.80	04/2010	12/2012	32	
205	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	470.10	12/2009	12/2012	36	
206	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	436.30	09/2009	12/2012	39	
207	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	173.60	09/2010	12/2012	27	
208	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	573.30	05/2010	12/2012	31	
209	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	256.20	02/2009	03/2013	49	
210	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	92.33	04/2009	03/2013	47	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
211	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	691.90	07/2010	03/2013	32	
212	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	137.30	09/2007	06/2013	69	
213	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	870.50	11/2012	06/2013	7	
214	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	41.30	04/2009	07/2013	51	
215	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	85.39	11/2008	07/2013	56	
216	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41	
217	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14	
218	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	2.50	11/2008	01/2014	62	
219	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	227.70	10/2011	03/2014	29	
220	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	163.90	05/2013	03/2014	10	
221	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	2.11	09/2007	04/2014	79	
222	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	20.27	07/2009	04/2014	57	
223	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11	
224	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	31.09	09/2013	07/2014	10	
	Total		29,644.25	31,860.08	31,679.98				
	Shipping & Ports								
225	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2	
226	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	1,011.15	03/2012	04/2012	1	
227	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011 06/2011	06/2012	14	
228	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	06/2012	12	
229	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
230	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	
231	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	677.00	12/2010 -	12/2012	24	
232	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25	
233	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	
234	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52	
235	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93	
236	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	07/2014	14	
Total			10,100.38 -	10,737.16	2,500.95				
<u>Telecommunications</u>									
237	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	161.31	12/2005 -	03/2012	75	
238	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 -	03/2012	61	
239	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	211.73	12/2008 -	03/2012	39	
240	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	03/2012	38	
241	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	03/2012	36	
242	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	366.90	08/2009 -	03/2012	31	
243	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	757.02	11/2010 -	03/2012	16	
244	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.80	10/2010 03/2012	07/2012	21	
Total			3,706.58 -	3,876.39	1,908.52				

Urban Development

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
245	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	12/2013	24	
			-			-			
	Total		6,395.00	11,609.00	2,267.57				
			-						
	<u>Water Resources</u>								
246	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60	
			-			-			
	Total		542.90	1,187.00	35.49				
			-						
Grand Total			403,117.78	477,228.15	252,728.98				

List of Projects Without Milestones

(Feb,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -			- 04/2011	04/2012		0/0
	Total		1,106.29 -	.00	.00				0/0
	<u>Civil Aviation</u>								
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00			01/2011 -	02/2012		0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -			05/2012 -	08/2012		0/0
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -			05/2011 -	10/2012		0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -			01/2011 -	12/2012		0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -			06/2013 -	06/2013		0/0
	Total		5,021.58 -	.00	.00				0/0
	<u>Coal</u>								
7	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -			03/2014 -	03/2014		0/0
8	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -			04/2014 -	04/2014		0/0
9	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 -			03/2012 -	03/2015		0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -			04/2015 -	04/2015		0/0
11	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28			03/2018 -	03/2018		0/0
	Total		3,609.93 -	.00	.00				0/0
	<u>Fertilisers</u>								
12	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -			07/2011 -	03/2012		0/0
13	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -			07/2011 -	04/2012		0/0
	Total		763.00 -	.00	.00				0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Steel									
14	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	-	-	04/2013	04/2013	-	0/0
15	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	-	-	05/2013	05/2013	-	0/0
16	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55	-	-	11/2013	11/2013	-	0/0
	Total		1,725.10	.00	.00				0/0
Petroleum									
17	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	-	-	12/2010	06/2011	-	0/0
18	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	-	-	09/2009	08/2011	-	0/0
19	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	-	-	03/2009 02/2012	02/2012	-	0/0
20	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	-	-	09/2011 03/2012	03/2012	-	0/0
21	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	-	-	03/2013 03/2013	03/2012	-	0/0
22	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70	-	-	04/2010	03/2012	-	0/0
23	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08	-	-	04/2011	03/2012	-	0/0
24	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	-	-	09/2011 03/2012	03/2012	-	0/0
25	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	-	-	05/2010 05/2012	05/2012	-	0/0
26	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	-	-	05/2010 04/2012	05/2012	-	0/0
27	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	-	-	09/2011 05/2012	05/2012	-	0/0
28	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	-	-	04/2006 05/2011	06/2012	-	0/0
29	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	-	-	01/2012	06/2012	-	0/0
30	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00	-	-	09/2012 09/2012	06/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
31	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96			07/2010 05/2012	07/2012		0/0
32	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -			04/2011 -	07/2012		0/0
33	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -			07/2012 -	07/2012		0/0
34	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04			08/2012 -	08/2012		0/0
35	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -			09/2012 -	09/2012		0/0
36	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76			03/2011 05/2011	10/2012		0/0
37	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -			09/2011 -	12/2012		0/0
38	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -			06/2012 -	12/2012		0/0
39	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -			12/2011 -	01/2013		0/0
40	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -			03/2010 03/2012	03/2013		0/0
41	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41			05/2010 03/2013	03/2013		0/0
42	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -			03/2013 -	03/2013		0/0
43	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -			- 12/2008	04/2013		0/0
44	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82			09/2010 03/2012	04/2013		0/0
45	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -			03/2013 -	04/2013		0/0
46	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -			03/2013 -	04/2013		0/0
47	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -			06/2012 -	04/2013		0/0
48	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -			11/2012 -	05/2013		0/0
49	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -			05/2013 -	05/2013		0/0
50	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -			09/2012 -	09/2013		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
51	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	-		03/2013	11/2013		0/0
52	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44			08/2010 03/2012	12/2013		0/0
53	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	-		12/2013 12/2013	12/2013		0/0
54	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	-		01/2014	01/2014		0/0
55	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	-		08/2013	01/2014		0/0
56	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94	-		01/2014	01/2014		0/0
57	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	-		02/2014	02/2014		0/0
58	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	-		10/2010	12/2014		0/0
59	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	-		12/2014	12/2014		0/0
60	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	-		12/2014	12/2014		0/0
61	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	-		04/2015	04/2015		0/0
62	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	-		01/2013	07/2015		0/0
63	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-		-	-		0/0
64	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00			02/2011 08/2011	-		0/0
	Total		97,824.35	.00	.00				0/0
	Power								
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	-		08/2011	01/2012		0/0
66	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	-		02/2012	03/2012		0/0
67	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	-		02/2012 02/2012	03/2012		0/0
68	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	-		07/2011	03/2012		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
69	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	-		06/2012	03/2012		0/0
70	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	-		04/2012	04/2012		0/0
71	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	-		05/2012	05/2012		0/0
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	-		11/2011	06/2012		0/0
73	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.91		07/2011	06/2012		0/0
74	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	-		02/2012	06/2012		0/0
75	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	-		06/2012	06/2012		0/0
76	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	-		06/2012	06/2012		0/0
77	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	-		08/2012	08/2012		0/0
78	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	-		08/2012	08/2012		0/0
79	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	-		08/2012	08/2012		0/0
80	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	-		10/2012	10/2012		0/0
81	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	-		10/2012	10/2012		0/0
82	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	-		10/2012	10/2012		0/0
83	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	-		11/2012	11/2012		0/0
84	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	-		11/2012	11/2012		0/0
85	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	-		11/2012	11/2012		0/0
86	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	-		12/2012	12/2012		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	-		11/2011	12/2012		0/0
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	-		11/2011	12/2012		0/0
89	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	-		02/2012	12/2012		0/0
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	-		01/2013	01/2013		0/0
91	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	-		01/2013	01/2013		0/0
92	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	-		01/2013	01/2013		0/0
93	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	-		09/2010	03/2013		0/0
94	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	-		11/2011	03/2013		0/0
95	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	-		03/2013	03/2013		0/0
96	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	-		04/2013	04/2013		0/0
97	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	-		04/2013	04/2013		0/0
98	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	-		09/2009	06/2013		0/0
99	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	-		12/2012	06/2013		0/0
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	-		07/2013	07/2013		0/0
101	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	-		07/2013	07/2013		0/0
102	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93	-		07/2013	07/2013		0/0
103	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	-		08/2013	08/2013		0/0
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	-		08/2013	08/2013		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
105	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	-		08/2013	08/2013		0/0
106	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	-		01/2012	09/2013		0/0
107	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya Pradesh	08/2011	425.51	-		10/2013	10/2013		0/0
108	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL, Multi State	03/2011	1,585.12	-		11/2013	11/2013		0/0
109	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL, Jharkhand	10/2011	558.26	-		11/2013	11/2013		0/0
110	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19	-		12/2013	12/2013		0/0
111	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34	-		12/2013	12/2013		0/0
112	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL, Chhatisgarh	08/2011	1,391.97	-		12/2013	12/2013		0/0
113	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL, Multi State	08/2011	1,391.97	-		12/2013	12/2013		0/0
114	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, Mizoram	01/2011	913.63	-		01/2014	01/2014		0/0
115	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL, Gujarat	12/2011	552.44	-		02/2014	02/2014		0/0
116	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25	-		03/2014	03/2014		0/0
117	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL, Chhatisgarh	05/2011	1,961.87	-		05/2014	05/2014		0/0
118	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, Multi State	10/2011	487.49	-		06/2014	06/2014		0/0
119	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL, Chhatisgarh	11/2011	2,127.51	-		07/2014	07/2014		0/0
120	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL, Andhra Pradesh	08/2011	1,637.34	-		08/2014	08/2014		0/0
121	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL, Multi State	12/2011	2,422.66	-		08/2014	08/2014		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
122	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	-		08/2014	08/2014		0/0
123	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJEC - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	-		08/2014	08/2014		0/0
124	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33	-		08/2014	08/2014		0/0
125	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	-		08/2013	09/2014		0/0
126	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	-		09/2014	09/2014		0/0
127	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16	-		10/2014	10/2014		0/0
128	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	-		01/2015	01/2015		0/0
129	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	-		01/2015	01/2015		0/0
130	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	-		02/2015	02/2015		0/0
	Total		99,463.32	.00	.00				0/0
	Railways								
131	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	604.04		03/1998	08/2005		0/0
132	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	-		12/2007	12/2010		0/0
133	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73	399.73		03/2009	12/2010		0/0
134	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38	330.23		02/2010	02/2011		0/0
135	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90	284.27		06/1999	03/2011		0/0
136	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94	302.23		-	03/2011		0/0
137	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92	258.60		-	03/2011		0/0
138	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	-		-	03/2011		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
139	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -			03/2009 12/2009	03/2011		0/0
140	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -			- 03/2011	03/2011		0/0
141	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTPT,Maharashtra	04/2003	3,125.20 4,174.40			- 06/2011	06/2011		0/0
142	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46			03/1994 -	12/2011		0/0
143	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -			- 09/2009	12/2011		0/0
144	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -			- -	02/2012		0/0
145	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36			- -	02/2012		0/0
146	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33			- 12/2009	02/2012		0/0
147	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -			12/2011 02/2012	02/2012		0/0
148	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13			03/1995 -	03/2012		0/0
149	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78			- -	03/2012		0/0
150	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98			03/2002 -	03/2012		0/0
151	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07			- 12/2011	03/2012		0/0
152	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82			- 03/2012	03/2012		0/0
153	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36			02/2009 -	03/2012		0/0
154	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62			- 03/2012	03/2012		0/0
155	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32			- -	03/2012		0/0
156	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69			- 03/2012	03/2012		0/0
157	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09			- 02/2011	03/2012		0/0
158	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21			- -	03/2012		0/0
159	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92			- 03/2012	03/2012		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
160	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51			- -	03/2012		0/0
161	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97			- -	03/2012		0/0
162	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -			03/2010 -	03/2012		0/0
163	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -			- -	03/2012		0/0
164	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -			03/2012 -	03/2012		0/0
165	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -			03/2011 -	03/2012		0/0
166	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -			03/2011 -	03/2012		0/0
167	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -			03/2012 -	03/2012		0/0
168	Bhuj-Naliya(GC) with extension from naliyate vaylor - [N22000123]WR,Gujarat	04/2008	318.24 -			03/2012 -	03/2012		0/0
169	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00			- 07/2012	07/2012		0/0
170	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -			12/2012 -	12/2012		0/0
171	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -			06/2004 -	12/2012		0/0
172	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27			12/2012 -	12/2012		0/0
173	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56			- 03/2012	12/2012		0/0
174	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -			- 03/2012	12/2012		0/0
175	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -			03/2009 12/2012	12/2012		0/0
176	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98			10/2007 12/2012	12/2012		0/0
177	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -			03/2010 -	12/2012		0/0
178	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -			12/2012 -	12/2012		0/0
179	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08			- -	03/2013		0/0
180	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35			- -	03/2013		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
181	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70	-	-	-	03/2013		0/0
182	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96	810.78	-	-	03/2013		0/0
183	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00	482.70	-	03/2013	03/2013		0/0
184	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04	-	-	03/2012	03/2013		0/0
185	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13	-	-	03/2013	03/2013		0/0
186	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	-	-	02/2009	04/2013		0/0
187	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41	207.00	-	03/2009	04/2013		0/0
188	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTS,Tamil Nadu	04/2006	495.74	-	-	06/2013	06/2013		0/0
189	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97	-	-	12/2011	11/2013		0/0
190	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79	-	-	-	12/2013		0/0
191	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92	261.70	-	02/2006	12/2013		0/0
192	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31	-	-	03/2009	12/2013		0/0
193	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42	393.46	-	03/2007	03/2014		0/0
194	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00	-	-	12/2008	03/2014		0/0
195	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00	-	-	-	03/2014		0/0
196	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	-	-	03/2014	03/2014		0/0
197	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	-	-	04/2014	03/2014		0/0
198	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19	-	-	03/2014	03/2014		0/0
199	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23	-	-	03/2014	03/2014		0/0
200	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62	-	-	03/2014	03/2014		0/0
201	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90	-	-	12/2012	03/2014		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
202	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -			03/2010 06/2014	06/2014		0/0
203	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -			02/2015 -	02/2015		0/0
204	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41			- -	03/2015		0/0
205	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98			- 12/2010	03/2015		0/0
206	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65			- -	03/2015		0/0
207	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -			03/2014 03/2015	03/2015		0/0
208	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -			- -	03/2015		0/0
209	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -			03/2015 -	03/2015		0/0
210	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -			03/2015 -	03/2015		0/0
211	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69			06/2005 07/2011	06/2015		0/0
212	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00			04/2008 03/2014	12/2015		0/0
213	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23			02/2010 -	12/2015		0/0
214	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -			12/2015 -	12/2015		0/0
215	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10			03/2005 12/2008	03/2016		0/0
216	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -			03/2011 03/2014	03/2016		0/0
217	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -			03/2014 03/2016	03/2016		0/0
218	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -			03/2016 -	03/2016		0/0
219	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -			03/2016 -	03/2016		0/0
220	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -			03/2016 -	06/2016		0/0
221	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00			03/2001 -	12/2017		0/0
222	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87			- 03/2010	-		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
223	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68			- -	-		0/0
224	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91			- -	-		0/0
225	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00			03/1998 -	-		0/0
226	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88			- -	-		0/0
227	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -			- -	-		0/0
228	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26			07/2008 -	-		0/0
229	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20			07/2005 -	-		0/0
230	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -			- -	-		0/0
231	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70			- 05/2009	-		0/0
232	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87			- -	-		0/0
233	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30			06/2007 -	-		0/0
234	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -			04/2003 03/2010	-		0/0
235	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -			- -	-		0/0
236	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -			- -	-		0/0
237	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67			- 12/2012	-		0/0
238	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -			- -	-		0/0
239	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17			- -	-		0/0
240	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13			- -	-		0/0
241	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82			- -	-		0/0
242	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -			03/2008 06/2008	-		0/0
243	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -			- -	-		0/0
244	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -			- -	-		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
245	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80	-		-	-		0/0
246	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	-		-	-		0/0
247	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83		-	-		0/0
248	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	-		-	-		0/0
249	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36	196.95		03/2011	-		0/0
250	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81	495.44		03/2004	-		0/0
251	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00	-		05/2008	-		0/0
252	CONV.OF 1500V DC TRACTION TO 25 KV AC,CR - [220100233]RE,Maharashtra	07/1996	653.84	1,302.12		06/2012	-		0/0
253	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00	214.09		12/2009	-		0/0
254	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17	-		-	-		0/0
255	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69	3,176.10		12/2006	-		0/0
256	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36	-		-	-		0/0
257	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19	-		-	-		0/0
258	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03	-		-	-		0/0
259	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15	-		12/2010	-		0/0
260	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68	-		-	-		0/0
	Total		64,962.90	.00	.00				0/0
			-						
Road Transport & Highways									
261	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	-		08/2004	03/2012		0/0
262	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	-		08/2004	03/2012		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
263	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	-	-	03/2005	03/2012	-	0/0
264	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09	-	-	03/2008	03/2012	-	0/0
265	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27	-	-	03/2008	03/2012	-	0/0
266	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	-	-	10/2008	03/2012	-	0/0
267	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	-	-	03/2008	03/2012	-	0/0
268	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	-	-	01/2009	03/2012	-	0/0
269	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	-	-	06/2008	03/2012	-	0/0
270	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	-	-	12/2008	03/2012	-	0/0
271	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	-	-	09/2008	03/2012	-	0/0
272	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	-	-	09/2008	03/2012	-	0/0
273	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	-	-	11/2008	03/2012	-	0/0
274	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	-	-	-	03/2012	-	0/0
275	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	-	-	08/2010	03/2012	-	0/0
276	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	-	-	01/2011	03/2012	-	0/0
277	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	-	-	08/2011	03/2012	-	0/0
278	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00	-	-	10/2008	04/2012	-	0/0
279	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	-	-	02/2012	04/2012	-	0/0
280	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30	-	-	10/2008	05/2012	-	0/0
281	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	-	-	03/2008	05/2012	-	0/0
282	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	-	-	02/2004	05/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
283	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -			01/2011 -	05/2012		0/0
284	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -			02/2010 -	05/2012		0/0
285	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00 -			05/2010 -	05/2012		0/0
286	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -			05/2012 -	05/2012		0/0
287	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -			05/2012 -	05/2012		0/0
288	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -			05/2012 -	05/2012		0/0
289	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -			09/2007 -	06/2012		0/0
290	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -			03/2005 -	06/2012		0/0
291	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -			09/2007 -	06/2012		0/0
292	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -			09/2007 -	06/2012		0/0
293	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -			09/2008 -	06/2012		0/0
294	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -			10/2008 -	06/2012		0/0
295	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -			06/2008 -	06/2012		0/0
296	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -			06/2008 -	06/2012		0/0
297	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -			06/2008 -	06/2012		0/0
298	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -			06/2008 -	06/2012		0/0
299	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -			05/2008 -	06/2012		0/0
300	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -			06/2008 -	06/2012		0/0
301	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -			12/2008 -	06/2012		0/0
302	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -			10/2009 -	06/2012		0/0
303	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -			10/2009 -	06/2012		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
304	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	-	-	06/2012	06/2012	-	0/0
305	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	-	-	10/2011	06/2012	-	0/0
306	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	-	-	11/2011	06/2012	-	0/0
307	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	-	-	04/2004	07/2012	-	0/0
308	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	-	-	02/2004	07/2012	-	0/0
309	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	-	-	07/2012	07/2012	-	0/0
310	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	-	-	05/2008	08/2012	-	0/0
311	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	-	-	06/2005	09/2012	-	0/0
312	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	-	-	10/2008	09/2012	-	0/0
313	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91	-	-	10/2008	09/2012	-	0/0
314	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	-	-	09/2012	09/2012	-	0/0
315	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	-	-	06/2010	10/2012	-	0/0
316	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	-	-	09/2009	10/2012	-	0/0
317	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	-	-	06/2011	10/2012	-	0/0
318	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	-	-	10/2011	10/2012	-	0/0
319	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	-	-	10/2012	10/2012	-	0/0
320	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	-	-	06/2009	11/2012	-	0/0
321	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	-	-	11/2012	11/2012	-	0/0
322	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80	-	-	06/2008	12/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
323	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	-		10/2008	12/2012		0/0
324	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	-		10/2008	12/2012		0/0
325	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	-		07/2008	12/2012		0/0
326	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	-		04/2008	12/2012		0/0
327	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	-		04/2008	12/2012		0/0
328	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	-		04/2008	12/2012		0/0
329	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	-		04/2010	12/2012		0/0
330	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	-		12/2009	12/2012		0/0
331	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	-		09/2009	12/2012		0/0
332	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	-		09/2010	12/2012		0/0
333	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	-		05/2010	12/2012		0/0
334	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	-		12/2012	12/2012		0/0
335	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	-		01/2013	01/2013		0/0
336	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	-		02/2013	02/2013		0/0
337	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	-		02/2009	03/2013		0/0
338	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	-		04/2009	03/2013		0/0
339	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	-		07/2010	03/2013		0/0
340	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	-		03/2013	03/2013		0/0
341	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	-		03/2013	03/2013		0/0
342	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	-		03/2013	03/2013		0/0
343	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	-		04/2013	04/2013		0/0
344	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	-		05/2013	05/2013		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
345	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	-	-	05/2013	05/2013	-	0/0
346	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	-	-	05/2013	05/2013	-	0/0
347	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	-	-	09/2007	06/2013	-	0/0
348	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	-	-	11/2012	06/2013	-	0/0
349	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	-	-	06/2013	06/2013	-	0/0
350	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50	-	-	06/2013	06/2013	-	0/0
351	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI - [N24000173]NHAI, Tamil Nadu	06/2011	600.00	-	-	06/2013	06/2013	-	0/0
352	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	-	-	04/2009	07/2013	-	0/0
353	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	-	-	11/2008	07/2013	-	0/0
354	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	-	-	02/2010	07/2013	-	0/0
355	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	-	-	07/2013	07/2013	-	0/0
356	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88	-	-	07/2013	07/2013	-	0/0
357	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00	-	-	07/2013	07/2013	-	0/0
358	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	-	-	08/2013	08/2013	-	0/0
359	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00	-	-	08/2013	08/2013	-	0/0
360	Dindigul - Kumli - [N24000177]NHAI, Tamil Nadu	09/2011	485.00	-	-	08/2013	08/2013	-	0/0
361	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	-	-	09/2013	09/2013	-	0/0
362	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	-	-	08/2012	10/2013	-	0/0
363	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00	-	-	10/2013	10/2013	-	0/0
364	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	-	-	11/2013	11/2013	-	0/0
365	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00	-	-	11/2013	11/2013	-	0/0
366	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	-	-	11/2013	11/2013	-	0/0
367	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54	-	-	11/2013	11/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
368	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	-		12/2013	12/2013		0/0
369	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	-		12/2013	12/2013		0/0
370	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	-		11/2008	01/2014		0/0
371	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	-		01/2014	01/2014		0/0
372	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00	-		02/2014	02/2014		0/0
373	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00	-		02/2014	02/2014		0/0
374	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	-		10/2011	03/2014		0/0
375	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	-		05/2013	03/2014		0/0
376	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	-		03/2014	03/2014		0/0
377	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00	-		03/2014	03/2014		0/0
378	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	-		09/2007	04/2014		0/0
379	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	-		07/2009	04/2014		0/0
380	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09	-		04/2014	04/2014		0/0
381	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00	-		05/2014	05/2014		0/0
382	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	-		07/2013	06/2014		0/0
383	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	-		09/2013	07/2014		0/0
384	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	-		08/2014	08/2014		0/0
385	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	-		10/2014	10/2014		0/0
386	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00	-		06/2015	06/2015		0/0
387	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	-		07/2015	07/2015		0/0
	Total		74,754.98	.00	.00				0/0

Shipping & Ports

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
388	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 -			04/2009 11/2009	02/2011		0/0
389	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -			06/2006 09/2011	09/2011		0/0
390	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00			12/2005 01/2008	10/2011		0/0
391	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -			09/2011 -	12/2011		0/0
392	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -			01/2012 -	03/2012		0/0
393	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -			03/2012 -	03/2012		0/0
394	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60			03/2012 -	04/2012		0/0
395	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -			04/2011 06/2011	06/2012		0/0
396	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00			06/2011 01/2012	06/2012		0/0
397	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00			12/2011 08/2012	08/2012		0/0
398	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -			09/2012 -	09/2012		0/0
399	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -			06/2010 -	11/2012		0/0
400	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00			12/2010 -	12/2012		0/0
401	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64			12/2012 -	12/2012		0/0
402	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -			02/2011 -	03/2013		0/0
403	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -			03/2011 -	03/2013		0/0
404	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50			01/2009 -	05/2013		0/0
405	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00			03/2006 -	12/2013		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
406	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23			12/2013 -	12/2013		0/0
407	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -			02/2014 -	02/2014		0/0
408	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -			05/2013 -	07/2014		0/0
409	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -			10/2008 -	-		0/0
410	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -			12/2007 01/2009	-		0/0
411	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -			08/2010 -	-		0/0
412	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -			08/2010 -	-		0/0
413	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -			10/2008 -	-		0/0
	Total		19,051.36 -	.00	.00				0/0
Telecommunications									
414	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -			03/2010 -	10/2010		0/0
415	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -			10/2009 -	03/2011		0/0
416	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -			02/2007 -	08/2011		0/0
417	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -			09/2011 -	09/2011		0/0
418	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72			06/2009 -	12/2011		0/0
419	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -			01/2010 -	12/2011		0/0
420	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -			12/2005 -	03/2012		0/0
421	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41			02/2007 -	03/2012		0/0
422	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -			12/2008 -	03/2012		0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
423	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	-		01/2009	03/2012		0/0
424	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13	-		03/2009	03/2012		0/0
425	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	-		08/2009	03/2012		0/0
426	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60			11/2010	03/2012		0/0
427	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	-		10/2010 03/2012	07/2012		0/0
428	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	-		10/2007	-		0/0
429	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	-		03/2009	-		0/0
430	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	-		03/2009	-		0/0
431	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	-		03/2010	-		0/0
	Total		8,443.59	.00	.00				0/0
	Urban Development								
432	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	-		09/2014	09/2014		0/0
433	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	-		03/2016	03/2016		0/0
434	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08			04/2009	-		0/0
	Total		37,850.18	.00	.00				0/0
	Water Resources								
435	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	-		12/2007	12/2012		0/0
	Total		542.90	.00	.00				0/0
	Grand Total		415,119.48	.00	.00				0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
