

**328th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
February 2013**



ONGC - Ahmedabad Redevelopmen



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

फरवरी, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 564 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। फरवरी, 2013 के दौरान 9 परियोजनाओं (पेट्रोलियम क्षेत्र की 4, सड़क क्षेत्र की 2 एवं परमाणु ऊर्जा, पोत-परिवहन तथा बंदरगाह और रेलवे क्षेत्र प्रत्येक की 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 564 परियोजनाओं में से 274 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 55 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 55 परियोजनाओं में से, 21 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। रेलवे, पेट्रोलियम, इस्पात, विद्युत, पोत-परिवहन तथा पत्तन दूरसंचार, कोयला एवं सड़क परिवहन एवं राजमार्ग क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 36 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	सड़क परिवहन एवं राजमार्ग	147	93	23	4
2.	रेलवे	125	37	4	2
3.	विद्युत	102	54	15	10
4.	पेट्रोलियम	71	32	3	2
5.	कोयला	51	26	4	0
6.	इस्पात	19	5	2	2
7.	दूरसंचार	17	13	3	1
8.	पोत परिवहन एवं पत्तन	15	7	1	0
9.	नागर विमानन	6	3	0	0
10.	परमाणु ऊर्जा	4	3	0	0
11.	शहरी विकास	4	1	0	0
12.	उर्वरक	1	0	0	0
13.	पेट्रोरसायन	1	0	0	0
14.	जल संसाधन	1	0	0	0
कुल		564	274	55	21

3. 564 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,90,030.49 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,33,387.35 करोड़ रुपए होने की संभावना है जो 1,43,356.86 करोड़ रुपए (मूल लागत का 18.10%) की समग्र लागत वृद्धि को दर्शाता है। फरवरी, 2013 तक इन परियोजनाओं पर किया गया व्यय 4,40,593.12 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 47.20% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (28.02.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. 564 परियोजनाओं में से, 2 परियोजनाएं समय से पहले चल रही हैं, 163 समय पर तथा 274 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या 285 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है। इसके अलावा, 23 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 103 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया गया है। 274 विलंबित परियोजनाओं में से, 74 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 65 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 84 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 51 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (28.02.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावा बारास्ता शिवपुरी-ग्वालियर-भिंड एनएलए(एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
2	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2013	216
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	06/2016	135
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	01/2013	132

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की समीक्षा करेंगे ।

5. विभिन्न परियोजना कार्यान्वयनकर्ता एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, वन संबंधी स्वीकृति में विलंब, सामग्री की आपूर्ति में विलंब, ठेकेदारों के चयन को अंतिम रूप देने में विलंब, भू-वैज्ञानिक गतिविधि, स्थानीय उपद्रव, यांत्रिक ठेकेदारों द्वारा धीमी प्रगति, माउवादी गतिविधियां, वन भूमि का विपथन, काम का रूकना, कार्य प्रक्रिया में परिवर्तन, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था आदि शामिल हैं ।

6. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाओं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दिए गए हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (28.02.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

7. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (28.02.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)
				मूल	अनुमानित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेडापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (28.02.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेडापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है :-

(i) दूरसंचार क्षेत्र में 15 परियोजनाओं में से 7 परियोजनाएं विलंबित हैं । माह के दौरान 'टर्न की आधार पर बीएसएनएच में ईआरपी कार्यान्वयन, बीएसएनएल' नामक परियोजना में कार्य प्रक्रिया में परिवर्तन के कारण 3 माह के अतिरिक्त विलंब की सूचना दी गई है ।

(ii) पोत परिवहन तथा पत्तन क्षेत्र में 19 परियोजनाओं में से 5 परियोजनाएं विलंबित हैं । माह के दौरान 2 परियोजनाओं के संबंध में 1 और 2 माह के अतिरिक्त विलंब की सूचना दी गई है । ये दोनों मेगा परियोजनाएं हैं । 'पुथु पोर्टट्रस्ट में एलएनजी पुनःगैसीकरण टर्मिनल को स्थापित करना' तथा '2 ऑफशोर कंटेनर वर्थ और टर्मिनल का निर्माण एवं विकास, मुंबई पोर्ट ट्रस्ट' के संबंध में क्रमशः 1 तथा 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । तथापि, इन परियोजनाओं के विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी कोई विशेष कारण सूचित नहीं दी गई है ।

(iii) इस्पात क्षेत्र में, 17 परियोजनाओं में से 13 परियोजनाएं विलंबित हैं । माह के दौरान 3 परियोजनाओं के संबंध में 3-8 माह तक के अतिरिक्त विलंब की सूचना दी गई है, जिनमें एक मेगा परियोजना है । 'बेलाडिला लौह अयस्क परियोजना डिपोजिट-11बी, एनएमडीसी' नामक परियोजना के संबंध में आठवादी गतिविधियों के कारण 3 माह के अतिरिक्त विलंब की सूचना दी गई है । 'राउरकेला इस्पात संयंत्र का विस्तार' सेल तथा '1.2 एमटीपीए पैल्ट संयंत्र परियोजना दोनीमलाई, एनएमडीसी' के संबंध में क्रमशः 3 और 8 माह के अतिरिक्त विलंब की सूचना दी गई है । तथापि, इन परियोजनाओं के विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी कोई विशेष कारण सूचित नहीं दी गई है ।

(iv) पेट्रोलियम क्षेत्र में, 71 परियोजनाओं में से 32 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 1-7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 बड़ी परियोजनाएं हैं । 'पानीपत में बूटाडीन एक्सट्रेक्शन यूनिट (बीडीईयू), आईओसीएल' नामक परियोजना के संबंध में यांत्रिक ठेकेदारों की धीमी प्रगति के कारण एक माह के अतिरिक्त विलंब की सूचना दी गई है तथा 'कोच्ची-कूटआनद बंगलोर मंगलोर पाइपलाइन परियोजना, जीएआईएल के संबंध में आरओयू समस्या के कारण 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'आईआरईपी, बीपीसीएल नामक परियोजना के संबंध में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी विशेष कारण की सूचना नहीं दी गई है ।

(V) रेलवे क्षेत्र में, 125 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं। माह के दौरान, 4 परियोजनाओं के संबंध में 1-36 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। जिनमें से 2 बड़ी परियोजनाएं हैं। 'लुंडिंग-सिलचर-जिरीबाम, बदरपुर-बारेग्राम कुमार्ग, एनईएफआर' नामक परियोजना के संबंध में वन संबंधी अनुमति के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'गोएलकेरा-मनोहरपुर (एलडी), एसईआर' परियोजना के संबंध में बारंबार स्थानीय उपद्रवों के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'खुर्जा-मेरठ-सहारनपुर, आरई का विद्युतीकरण' नामक परियोजना के संबंध में काम रुकने के कारण 21 माह के अतिरिक्त विलंब की सूचना दी गई है। 'पटना-गंगा ब्रिज (एनएल), ईसीआर' नामक परियोजना के संबंध में 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। तथापि, परियोजना प्राधिकारियों द्वारा इस परियोजना के विलंब के लिए कोई विशेष कारण सूचित नहीं किया गया है।

(Vi) कोयला क्षेत्र में, 51 परियोजनाओं में से 26 परियोजनाएं विलंबित हैं, माह के दौरान, '4 परियोजनाओं के संबंध में 12-24 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'मनुगुरु ओसी-|| विस्तार चरण-||, एसीसीसएल' नामक परियोजना के संबंध में वनभूमि के बिपथन में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'झंजरा आर-V सीम पीएसएलडब्ल्यू, ईसीएल' तथा 'कुर्चा रॉग (1.35 एमटीवाई), एसईसीएल' नामक परियोजनाओं के संबंध में क्रमशः मेसर्स सीओडीसीओ के साथ संवेदा को अंतिम रूप देने में विलंब तथा वन संबंधी अनुमति में विलंब के कारण प्रत्येक में 24 माह के अतिरिक्त विलंब की सूचना हुई है। 'जगन्नाथपुर ओसीपी (3.00 एमटीवाई), एसईसीएल' नामक परियोजना के संबंध में 24 माह के विलंब की सूचना प्राप्त हुई है। तथापि, परियोजना प्राधिकारियों द्वारा इस परियोजना के विलंब के लिए कोई विशेष कारण सूचित नहीं किया गया है।

(vii) विद्युत क्षेत्र में, 102 परियोजनाओं में से 54 परियोजनाएं विलंबित हैं। माह के दौरान, 15 परियोजनाओं के संबंध में 1-11 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 10 बड़ी परियोजनाएं हैं। इन 14 परियोजनाओं में से, 1 परियोजना के संबंध में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 2 परियोजनाओं के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 5 परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है और 2 परियोजनाओं के संबंध में क्रमशः 4 और 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'पार्वती एचईपी स्टेज-|||, एनएचपीसी' नामक परियोजना के संबंध में सामग्री की आपूर्ति में विलंब के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'तपोवन-विष्णुगढ़ एचईपी (4X130 मे.वाट), एनटीपीसी' तथा 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना XI, पीजीसीआईएल' के संबंध में भू-वैज्ञानिक गतिविधियों के कारण क्रमशः 6 और 8 माह के अतिरिक्त विलंब की सूचना दी गई है। 'सुवनसीरी लोअर एचईपी, एनटीपीसी' नामक परियोजना के संबंध में कानून और व्यवस्था के कारण 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'बाढ़ एसटीटीपी स्टेज-I (3X660 मे.वाट), एनटीपीसी' परियोजनाओं के संबंध में क्रमशः मेसर्स टीपीई तथा मेसर्स पीएम द्वारा वायलर तथा टर्वाइन सामग्री की आपूर्ति में विलंब के कारण 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(viii) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 147 परियोजनाओं में से 93 परियोजनाएं विलंबित हैं। माह के दौरान, 23 परियोजनाओं के संबंध में 1-13 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 4 बड़ी

परियोजना है। इन 37 परियोजनाओं में से, 10 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 2 परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 3 परियोजनाओं के संबंध में प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 2 परियोजनाओं के संबंध में प्रत्येक में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है और 2 परियोजनाओं के संबंध में प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'चंबल पुल, एनएच-76 (आरजे-5), एनएचएआई' परियोजनाओं के संबंध में सात माह के विलंब की सूचना प्राप्त हुई है तथा 'पटना-मुजफ्फरपुर, एनएचएआई' के संबंध में 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'चार लेन के नागपुर-बेतुल, एनएचएआई' तथा 'पुणे-सतारा (एनएच- 4), एनएचएआई' परियोजनाओं के संबंध में 13 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। परियोजना कार्यान्वयन एजेंसी ने इन परियोजनाओं में विलंब के लिए किसी विशेष कारण का उल्लेख नहीं किया है। तथापि, इन परियोजनाओं में विलंब के सामान्य कारण भूमि अधिग्रहणमेंदेरी, वन तथा पर्यावरण संबंधी अनुमतियों में विलंब, जनोपयोगी सुविधाओं को प्रतिस्थापन की समस्या, ठेकेदारों का घटिया कार्य-निष्पादन आदि रहा है।

9. दिनांक 28.02.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपए तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

10. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for February 2013 contains information on the status of the 564 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During February 2013, 9 projects (4 projects in Petroleum, 2 projects in Road and 1 project each in Atomic Energy, Shipping & Ports and Railways Sector) have reported completion.

2. During the reference month, out of 564 projects, 274 projects are delayed with respect to latest schedule and 55 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 55 projects, 21 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 36 months in respect of projects relating to Railways, Petroleum, Steel, Power, Shipping & Ports, Telecommunication, Coal and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Road Transport & Highways	147	93	23	4
2.	Railways	125	37	4	2
3.	Power	102	54	15	10
4.	Petroleum	71	32	3	2
5.	Coal	51	26	4	0
6.	Shipping & Ports	19	5	2	2
7.	Steel	17	13	3	1
8.	Telecommunications	15	7	1	0
9.	Civil Aviation	6	3	0	0
10.	Atomic Energy	4	3	0	0
11.	Urban Development	4	1	0	0
12.	Fertilizers	1	0	0	0
13.	Petrochemicals	1	0	0	0
14.	Water Resources	1	0	0	0
Total		564	274	55	21

3. Total original cost of implementation of the 564 projects was about ₹ 7,90,030.49 crore and their anticipated completion cost is likely to be ₹ 9,33,387.35 crore, which reflects an overall cost overruns of ₹ 1,43,356.86 crore (18.10 % of original cost). The expenditure incurred on these projects till February 2013 is ₹ 4,40,593.12 crore, which is 47.20 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 28-02-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. Out of the 564 projects, 2 projects are ahead of schedule, 163 are on schedule and 274 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 285 if delay is calculated on the basis of original schedule of completion. Further, 23 projects have been sanctioned without any commissioning schedule/date and for 103 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 274 delayed projects, 74 projects have overall delay in the range of 1 to 12 months, 65 projects have a delay in the range of 13 to 24 months, 84 projects have a delay in the range of 25 to 60 months and 51 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 28-02-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI- GWALIOR - BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
3	UDHAMPUR- SRINAGAR- BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
5	LANJHIGARH- JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

5. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of material, delay in finalization of contractor, geological surprises, local disturbances, slow progress by mechanical contractor, Maoist activities, diversion of forest land, frozen of work, change in business process, ROU/ROW problems, law and order, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 28-02-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		EXPENDITURE CUMULATIVE (₹ ; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADAN GA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

7. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 28-02-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 28.02.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

8. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Telecommunication Sector**, out of 15 projects, 7 projects are delayed. During the month project 'ERP implementation in BSNL on Turnkey basis, BSNL' has reported additional delays of 3 months due to delay in change of business process.

ii) In the **Shipping & Ports Sector**, out of 19 projects, 5 projects are delayed. During the month 2 projects have reported additional delays of 1 & 2 months, both are Mega projects. The projects 'Setting up of LNG Regasification Terminal at Puthu, Port Trust' and 'Construction. & Development of 2 Offshore Container Berths & Terminal, Mumbai Port Trust' have reported additional delay of 1 and 2 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

iii) In the **Steel Sector**, out of 17 projects, 13 projects are delayed. During the month 3 projects have reported additional delays in the range of 3-8 months, out of which 1 is a Mega project. The project 'Bailadila Iron Ore Project Deposit- 11B, NMDC' has reported additional delay of 3 months due to Maoist activities. The Projects 'Expansion of Rourkela Steel Plant, SAIL' and '1.2 MTPA Pellet Plant Project Donimalai, NMDC' have reported additional delay of 3 and 8 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects

iv) In the **Petroleum Sector**, out of 71 projects, 32 projects are delayed. During the month 3 projects have reported additional delays in the range of 1-7 months, out of which 2 are Mega projects. The projects 'Butadiene Extraction Unit (BDEU) at Panipat, IOCL' has reported additional delay of 1 month due to slow progress of mechanical contractor and 'Kochi-Kootanad Bangalore Mangalore Pipeline Project, GAIL' has reported additional delay of 8 months due to delay in ROU problem. The project 'IREP, BPCL' has reported additional delay of 5 months. However, no specific reasons have been reported by the project authorities for delay in this project.

v) In the **Railways Sector**, out of 125 projects, 37 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-36 months, out of which 2 are Mega projects. The project 'Lumding-Silchar Jiribam, Badarpur-Baraigram Kumarg, NEFR' has reported additional delay of 3 months due to forest clearance. The projects 'Goelkera-Manoharpur (LD), SER' has reported additional delay of 6 months due to frequent local disturbance and 'Electrification of Khurja-Meerut-Saharanpur, RE' has reported additional delay of 21 months due to frozen of work. The project 'Patna Ganga

Bridge (NL), ECR' has reported additional delay of 36 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vi) In the **Coal Sector**, out of 51 projects, 26 projects are delayed. During the month 4 projects have reported additional delays in the range of 12-24 months. The project 'Manuguru OC-II Extension Phase-II, SCCL' has reported additional delay of 12 months due to delay in diversion of forest land. The projects 'Jhanjra R-VI Seam PSLW, ECL' and 'Churcha Roug (1.35MTY), SECL' have reported additional delay of 24 months each due to delay in finalization of contract with M/s CODCO and forest clearance respectively. The project 'Jagannathpur OCP (3.00 MTY), SECL' has reported additional delay of 24 months. However, no specific reasons have been reported by the project authorities for delay in this project.

v) In the **Power Sector**, out of 102 projects, 54 projects are delayed. During the month 15 projects have reported additional delays in the range of 1-11 months, out of which 10 are Mega projects. Of these 14 projects, 1 project has reported additional delay of 1 month, 2 projects have reported additional delay of 2 months each, 5 projects have reported additional delay of 3 months each and 2 projects have reported additional delay of 4 and 5 months respectively. The project 'Parbati HEP Stage-III, NHPC' has reported additional delay of 6 months due to delay in supply of materials. The projects 'Tapovan-Vishnugad HEP (4x130MW), NTPC' and 'Northern Region System Strengthening Scheme XVI, PGCIL' have reported additional delay of 6 and 8 months respectively due to geological surprises. The projects 'Subansiri Lower HEP, NHPC' has reported additional delay of 9 months due to law and order and 'Barh STPP Stage I (3X660MW), NTPC' has reported additional delay of 11 months due to delay in supply of boiler and turbine materials by M/s TPE and M/s PM respectively.

vii) In the **Road Transport & Highways Sector**, out of 147 projects, 93 are delayed. During the month 23 projects have reported additional delays in the range of 1-13 months, out of which 4 are Mega Projects. Of these 37 projects, 10 projects have reported additional delay of 1 month each, 2 projects have reported additional delay of 3 months each, 3 projects have reported additional delay of 4 months each, 2 projects have reported additional delay of 5 months each and 2 projects have reported additional delay of 6 months each. The projects 'Chambal Bridge, NH-76 (RJ-5), NHAI' has reported additional delay of 7 months and 'Patna-Muzzaffarpur, NHAI' has reported additional of 8 months. The projects '4 Laning of Nagpur-Betul, NHAI' and 'Pune-Satara (NH-4), NHAI' has reported additional delay of 13 months. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for

delay in these projects are delay in land acquisition, delay in forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

9. The status as on 28.02.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

10. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Road Transport & Highways	147	23
2	Railways	125	4
3	Power	102	15
4	Petroleum	71	3
5	Coal	51	4
6	Shipping & Ports	19	2
7	Steel	17	3
8	Telecommunications	15	1
9	Civil Aviation	6	0
10	Atomic Energy	4	0
11	Urban Development	4	0
12	Fertilisers	1	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	564	55

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	1438
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
<u>Railways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
<u>Road Transport & Highways</u>				
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
<u>Shipping & Ports</u>				
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
June,2012				
<u>Steel</u>				
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
<u>Power</u>				
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	3779.46
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
<u>Railways</u>				
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
<u>Road Transport & Highways</u>				
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9
July,2012				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Power</u>				
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
<u>Railways</u>				
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096]	196.97	03/2011	218.66
August,2012				
<u>Steel</u>				
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
<u>Power</u>				
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
<u>Road Transport & Highways</u>				
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235]	193.09	03/2008	189.15
September,2012				
<u>Petroleum</u>				
34	REVAMPING OF WIN PLATFORM AT MH ASSET(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000044]	333.40	05/2010	680.85
<u>Telecommunications</u>				
35	PROJ.III OF NIB-II OF MESSAGING STORAGE(BHARAT SANCHAR NIGAM LIMITED) - [260100099]	250.00	12/2005	80.47
36	NIB Project Capacity Expansion(BHARAT SANCHAR NIGAM LIMITED) - [N26000098]	175.52	12/2008	60.84
October,2012				
<u>Road Transport & Highways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
37	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106204]	275.00	09/2007	306.65
38	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106301]	151.30	10/2008	190.61
November,2012				
<u>Petroleum</u>				
39	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC(GAS AUTHORITY OF INDIA LIMITED) - [N16000071]	348.00	03/2012	203.31
December,2012				
<u>Fertilisers</u>				
40	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS(NATIONAL FERTILISER LIMITED) - [N08000007]	325.00	07/2011	185.1
41	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ(NATIONAL FERTILISER LIMITED) - [N08000008]	438.00	07/2011	239.93
<u>Power</u>				
42	WESTERN REGION STRENGTHENING SCHEME-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000022]	5,221.23	07/2010	3175.3
<u>Railways</u>				
43	MUMBAI URBAN TRANSPORT PROJECT PHASE-I(METROPOLITAN RAPID TRANSPORT PROJECTS) - [N22000093]	3,125.20	06/2011	4334
<u>Road Transport & Highways</u>				
44	DAKOPA TO NAGAON (NH-36)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106288]	225.00	06/2008	285.2
45	JHAJHARPUR TO DARBANGA (BR-7)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000031]	340.00	09/2008	575.32
46	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000118]	464.00	01/2011	535.62
47	Hyderabad-yadgiri N.H no-202(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000142]	388.00	05/2012	537.91
<u>Shipping & Ports</u>				
48	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA(SHIPPING crp. of india) - [N25000031]	1,066.91	09/2012	1027.12
January,2013				
<u>Fertilisers</u>				
49	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE(NATIONAL FERTILISER LIMITED) - [N08000004]	1,292.84	01/2013	987.72

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
50	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ(NATIONAL FERTILISER LIMITED) - [N08000005]	1,294.19	01/2013	972.95
<u>Railways</u>				
51	REWARI-ROHTAK (NL),NR(NORTHERN RAILWAY) - [220100279]	149.38	02/2010	508.76
52	PODAPAHAR-BANSPANI,(LD)(SER)(SOUTH EASTERN RAILWAY) - [N22000046]	129.74	03/2006	162.27
February,2013				
<u>Atomic Energy</u>				
53	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP(URANIUM CORPORATION OF INDIA LIMITED) - [N02000007]	1,106.29	04/2011	1084.24
<u>Petroleum</u>				
54	COMPRESSOR STATIONS (KAILARAS AND CHAINSA)(GAS AUTHORITY OF INDIA LIMITED) - [N16000054]	1,167.00	04/2011	715.73
55	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000073]	4,543.43	03/2012	1709.62
56	EURO-IV DHDT(CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000109]	2,615.69	-	1981.03
57	CDU/VDU-II(CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000110]	333.99	-	228.26
<u>Railways</u>				
58	ELECTRIFICATION OF MORADABAD-ROZA(RAILWAY ELECTRIFICATION) - [N22000095]	129.17	03/2011	227.48
<u>Road Transport & Highways</u>				
59	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH- 2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101173]	367.49	03/2005	453.68
60	TUTICORIN-PORT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000217]	182.25	02/2013	N.A.
<u>Shipping & Ports</u>				
61	Acquisition of two nos. of 120 B.P BY 079& 080(SHIPPING crp. of india) - [N25000042]	290.85	06/2011	294.52


Summary of projects in the Flash Report for the month of February, 2013

I. Project Implementation - Current Status:

Number of Projects in Previous Month	571
Number of Projects completed/dropped/frozen in Current Month	9
Number of Projects Added in Current Month	2
Number of Projects in Current Month	564


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 564 projects, 2 projects are ahead of schedule, 151 projects are on schedule and 285 projects are delayed. Of the balance, 103 projects do not have fixed dates of commissioning while 23 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

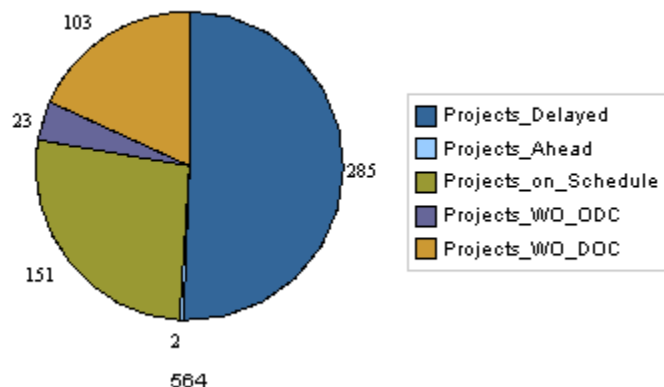

III. Investment Scenario

The Total Original cost of implementation of 564 projects when sanctioned, was of the order of Rs. 790030.49 crore but this was subsequently revised to Rs. 933387.35 crore implying a cost overrun of 18.1%. The expenditure incurred on these projects till February, 2013 is Rs. 440593.12 crore, which is 47.2% of the revised cost of the projects.

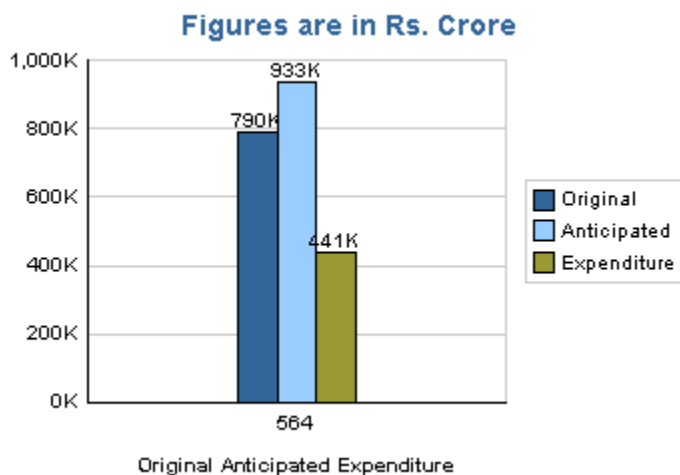

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	571
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects added in Current Month	2
No of Projects in Current Month	564

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	285	2	151	23	103	564	50.53
Latest Approved (Date)	274	2	163	23	103	564	48.58

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	418	666,505.54	701,769.46	303,810.47	43.30	35,263.92	5.30
Latest Approved (RCE)	146	181,292.77	231,617.89	136,782.65	59.10	50,325.12	27.80
Total (RCE)	564	847,798.31	933,387.35	440,593.12	47.20	85589.04	10.10
Original Cost of All Projects							
Original Cost	564	790,030.49	933,387.35	440,593.12	47.20	143,356.86	18.10

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	285	456,629.97	552,420.63	339,608.38	61.50	95,790.66	21.00
Latest Approved (RCE)	274	459,318.47	520,889.88	319,219.92	61.30	61,571.41	13.40

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	55	84,128.40	97,495.06	62,569.17	64.20	13,366.66	15.90

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	36,056.5	37,510.5	4.0	7	8,579.5	10,631.3	23.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	71	169,219.4	181,912.6	7.5	16	54,272.1	73,391.0	35.2
8	Power	102	241,378.9	257,209.1	6.6	19	46,019.4	61,849.6	34.4
9	Railways	125	61,244.6	148,185.6	142.0	107	38,023.5	125,011.1	228.8
10	Road Transport & Highways	147	96,472.1	98,410.7	2.0	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	9	8,629.0	11,218.5	30.0
12	Telecommunications	15	7,113.1	6,920.2	-2.7	2	477.3	550.9	15.4
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		564	790,030.5	933,387.4	18.1	185	216,280.0	367,490.0	69.9

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	35	29,991.0	37,614.8	25.4	14	12,420.0	20,910.9	68.4
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	2	6,441.3	11,073.4	71.9
3	Assam	34	22,035.9	35,405.4	60.7	12	10,491.8	23,955.3	128.3
4	Bihar	30	26,917.6	34,877.4	29.6	14	12,668.3	20,628.1	62.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	8	4,054.4	5,741.1	41.6	2	1,298.8	2,985.5	129.9
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	4	11,308.5	15,199.7	34.4
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	26	46,344.4	55,830.8	20.5	9	8,598.8	18,491.8	115.1
11	Kerala	7	20,376.7	21,818.2	7.1	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	22	18,978.9	19,259.5	1.5	2	1,110.9	1,810.9	63.0
13	Maharashtra	51	92,916.6	107,824.4	16.0	16	28,503.0	45,882.6	61.0
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Odisha	31	57,664.0	62,099.1	7.7	12	32,671.6	37,106.7	13.6
19	Punjab	6	3,542.0	4,483.8	26.6	2	532.4	1,474.2	176.9
20	Rajasthan	14	21,115.8	20,928.0	-0.9	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	48,788.1	59,567.9	22.1	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	22	18,455.9	22,677.6	22.9	9	3,670.1	7,940.1	116.3
25	West Bengal	27	42,286.1	54,396.5	28.6	15	20,928.4	33,038.8	57.9
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	25	58,429.8	59,712.9	2.2	6	1,548.3	2,831.4	82.9
28	Jharkhand	23	14,447.4	18,493.0	28.0	7	2,225.5	6,442.8	189.5
29	Uttarakhand	5	7,624.2	8,564.6	12.3	2	2,640.7	3,581.2	35.6
30	Multi State	109	141,561.5	152,959.8	8.1	21	10,501.3	24,497.4	133.3
Total		564	790,030.5	933,387.4	18.1	185	216,280.0	367,490.0	69.9

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	13 - 35
3	Coal	51	36,056.5	37,510.5	4.0	26	23,325.5	25,199.2	16 - 72
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	13	63,227.8	69,385.3	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	71	169,219.4	181,912.6	7.5	37	99,791.5	110,271.3	1 - 120
8	Power	102	241,378.9	257,209.1	6.6	54	133,486.4	148,411.8	1 - 102
9	Railways	125	61,244.6	148,185.6	142.0	41	25,396.2	71,545.3	2 - 235
10	Road Transport & Highways	147	96,472.1	98,410.7	2.0	93	50,182.9	52,121.5	2 - 109
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	6	6,413.2	7,718.8	5 - 87
12	Telecommunications	15	7,113.1	6,920.2	-2.7	7	3,413.3	3,219.4	11 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		564	790,030.5	933,387.4	18.1	285	456,630.0	552,420.6	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	35	29,991.0	37,614.8	25.4	12	16,856.0	20,665.4	5 - 41
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	3	9,356.2	13,737.9	25 - 87
3	Assam	34	22,035.9	35,405.4	60.7	31	20,716.4	33,256.6	12 - 120
4	Bihar	30	26,917.6	34,877.4	29.6	13	20,676.7	25,738.9	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	13 - 13
6	Gujarat	22	31,111.6	31,313.5	0.6	7	16,101.7	16,093.9	6 - 24
7	Haryana	8	4,054.4	5,741.1	41.6	4	2,216.6	3,396.6	2 - 50
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	5	13,355.6	17,246.7	25 - 102
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	8	13,205.0	32,811.9	10 - 201
10	Karnataka	26	46,344.4	55,830.8	20.5	8	9,952.3	15,188.7	10 - 103
11	Kerala	7	20,376.7	21,818.2	7.1	5	19,581.0	20,231.0	5 - 58
12	Madhya pradesh	22	18,978.9	19,259.5	1.5	11	9,281.2	9,281.2	5 - 60
13	Maharashtra	51	92,916.6	107,824.4	16.0	26	50,128.1	56,237.6	2 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	72 - 72
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 35
17	Nagaland	1	850.0	850.0	0.0	1	850.0	850.0	24 - 24
18	Odisha	31	57,664.0	62,099.1	7.7	14	47,209.6	48,171.9	3 - 132
19	Punjab	6	3,542.0	4,483.8	26.6	3	1,237.4	2,179.2	2 - 58
20	Rajasthan	14	21,115.8	20,928.0	-0.9	7	15,830.9	15,384.6	3 - 59
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 35
22	Tamil Nadu	32	48,788.1	59,567.9	22.1	12	31,380.8	37,311.4	4 - 87
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,101.4	1,395.4	9 - 21
24	Uttar Pradesh	22	18,455.9	22,677.6	22.9	12	11,351.4	13,331.5	7 - 78
25	West Bengal	27	42,286.1	54,396.5	28.6	15	25,309.8	32,251.1	3 - 135
26	Delhi	4	38,214.4	38,194.8	-0.1	2	478.4	458.8	11 - 72
27	Chhatisgarh	25	58,429.8	59,712.9	2.2	9	23,484.9	23,796.2	12 - 59
28	Jharkhand	23	14,447.4	18,493.0	28.0	12	9,403.0	10,300.4	5 - 100
29	Uttarakhand	5	7,624.2	8,564.6	12.3	4	6,097.2	7,037.6	5 - 45
30	Multi State	109	141,561.5	152,959.8	8.1	53	77,223.3	84,289.3	1 - 235
Total		564	790,030.5	933,387.4	18.1	285	456,630.0	552,420.6	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	13 - 35
3	Coal	51	36,056.5	37,510.5	4.0	26	23,325.5	25,199.2	16 - 72
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	13	63,227.8	69,385.3	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	71	169,219.4	181,912.6	7.5	32	90,034.2	94,990.8	1 - 86
8	Power	102	241,378.9	257,209.1	6.6	54	133,486.4	148,411.8	1 - 102
9	Railways	125	61,244.6	148,185.6	142.0	37	19,468.8	64,815.0	2 - 235
10	Road Transport & Highways	147	96,472.1	98,410.7	2.0	93	50,182.9	52,121.5	2 - 109
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	5	6,263.2	7,118.8	5 - 36
12	Telecommunications	15	7,113.1	6,920.2	-2.7	7	3,413.3	3,219.4	11 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		564	790,030.5	933,387.4	18.1	274	435,334.7	520,889.9	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	37,022.5	37,510.5	1.3	6	7,115.6	7,603.7	6.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	71	184,731.1	181,912.6	-1.5	2	30,602.0	32,253.0	5.4
8	Power	102	244,983.6	257,209.1	5.0	14	39,450.6	51,676.2	31.0
9	Railways	125	90,989.8	148,185.6	62.9	77	42,007.1	99,234.7	136.2
10	Road Transport & Highways	147	96,638.6	98,410.7	1.8	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	17,389.4	17,902.4	3.0	6	3,312.5	4,036.9	21.9
12	Telecommunications	15	7,113.1	6,920.2	-2.7	2	477.3	550.9	15.4
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		564	847,798.3	933,387.4	10.1	127	161,122.7	252,069.7	56.4

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	0	0.00	0.00	0- 0
3	Coal	51	36,056.46	37,510.52	4.03	0	0.00	0.00	0- 0
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	0	0.00	0.00	0- 0
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	71	169,219.44	181,912.59	7.50	2	735.19	2,337.80	84- 120
8	Power	102	241,378.89	257,209.13	6.56	1	1,657.00	2,978.86	76- 76
9	Railways	125	61,244.63	148,185.62	141.96	2	1,189.97	5,627.03	23- 92
10	Road Transport & Highways	147	96,472.10	98,410.72	2.01	0	0.00	0.00	0- 0
11	Shipping & Ports	19	15,617.12	17,902.42	14.63	0	0.00	0.00	0- 0
12	Telecommunications	15	7,113.08	6,920.16	-2.71	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		564	790030.49	933387.35	18.15	6	9042.77	19863.69	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	22- 22
3	Coal	51	36,056.46	37,510.52	4.03	5	7,938.86	9,942.56	16- 51
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	8- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	71	169,219.44	181,912.59	7.50	12	49,613.82	63,945.58	12- 120
8	Power	102	241,378.89	257,209.13	6.56	16	44,380.63	59,305.99	7- 102
9	Railways	125	61,244.63	148,185.62	141.96	34	15,749.62	61,903.59	2- 235
10	Road Transport & Highways	147	96,472.10	98,410.72	2.01	11	3,324.28	5,445.20	21- 107
11	Shipping & Ports	19	15,617.12	17,902.42	14.63	4	5,580.00	6,965.50	14- 87
12	Telecommunications	15	7,113.08	6,920.16	-2.71	1	149.15	158.72	45- 45
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	21- 21
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		564	790030.49	933387.35	18.15	93	177734.37	278007.57	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

S.no	Project	DOA	Original		Now anticipated		Final
			Cost	DOC	Cost	DOC	Expenditure
<u>Atomic Energy</u>							
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP	09/2007	1,106.29	04/2011	1,106.29	02/2013	1,084.24
<u>Petroleum</u>							
2	COMPRESSOR STATIONS (KAILARAS AND CHAINSA)	11/2007	1,167.00	04/2011	798.00	02/2013	715.73
3	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I	06/2009	4,543.43	03/2012	2,500.00	02/2013	1,709.62
4	CDU/VDU-II	03/2010	333.99	N.A.	333.99	10/2012	228.26
5	EURO-IV DHDT	09/2008	2,615.69	N.A.	2,615.69	01/2013	1,981.03
<u>Railways</u>							
6	ELECTRIFICATION OF MORADABAD-ROZA	12/2004	129.17	03/2011	404.67	03/2012	227.48
<u>Road Transport & Highways</u>							
7	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	04/2000	367.49	03/2005	367.49	02/2013	453.68
8	TUTICORIN-PORT	04/2010	182.25	02/2013	182.25	02/2013	.00
<u>Shipping & Ports</u>							
9	Acquisition of two nos. of 120 B.P BY 079& 080	04/2009	290.85	06/2011	272.50	02/2013	294.52

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
1	<u>Petroleum</u>					
	Mounded Bullet	12/2012	279.00	12/2014	279.00	12/2014
2	<u>Power</u>					
	Lata-Tapovan HPP 3x57MW	7/2012	1,527.00	8/2017	1,527.00	8/2017

VII. Milestones (Cumulative due & achieved)

Total	3320
Achieved up to month	1187

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
<u>Coal</u>							
1	MANUGURU OC-II EXTENSION PHASE-II SCCL	181.19	181.19	03/2012	03/2014	03/2015	12
2	JHANJRA R-VI SEAM PSLW ECL	287.18	287.17	03/2011	03/2015	03/2017	24
3	CHURCHA ROUG(1.35MTY) SECL	462.35	462.35	03/2014	03/2014	03/2016	24
4	JAGANNATHPUR OCP(3.00 MTY) SECL	152.43	152.43	03/2015	03/2015	03/2017	24
<u>Steel</u>							
5	Bailadila Iron Ore Project Deposit- 11B (NMDC) NMDC	295.89	607.17	12/2011	03/2013	06/2013	3
6	Expansion of Rourkela Steel Plant SAIL	11,812.00	11,812.00	03/2013	09/2013	12/2013	3
7	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) NMDC	572.00	572.00	N.A.	04/2013	12/2013	8
<u>Petroleum</u>							
8	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT IOCL	341.50	341.50	02/2013	03/2013	04/2013	1
9	IREP BPCL	14,225.00	14,225.00	12/2015	12/2015	05/2016	5
10	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC GAIL	2,915.00	2,915.00	12/2012	05/2014	12/2014	7
<u>Power</u>							
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE NHPC	768.92	1,628.00	03/2007	02/2013	03/2013	1
12	URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	2,081.00	11/2009	03/2013	05/2013	2
13	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA PGCIL	1,347.32	1,347.32	02/2012	03/2013	05/2013	2
14	TEHRI PUMPED STORAGE PLANT(1000MW) THDCL	1,657.00	2,978.86	07/2010	08/2016	11/2016	3
15	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G PGCIL	1,736.36	1,736.36	06/2012	03/2013	06/2013	3
16	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR PGCIL	1,075.12	1,075.12	05/2012	06/2013	09/2013	3
17	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	03/2013	06/2013	3
18	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX PGCIL	182.68	182.68	01/2013	06/2013	09/2013	3
19	Transmission system for transfer of power from Gen. PGCIL	250.03	250.03	01/2013	11/2013	03/2014	4
20	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR PGCIL	170.36	170.36	04/2013	04/2013	09/2013	5
21	PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.56	2,716.00	10/2010	09/2013	03/2014	6
22	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	03/2013	09/2015	03/2016	6
23	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI PGCIL	752.64	752.64	07/2013	07/2013	03/2014	8
24	SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	10,667.00	09/2010	03/2017	12/2017	9
25	BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	03/2016	02/2017	11


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay
		Original	Anticipated	Original	Last month	This month	(in months)
	<u>Railways</u>						
26	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg NEFR	1,676.31	4,255.37	03/2009	12/2014	03/2015	3
27	GOELKERA-MANOHARPUR,(LD)(SER) SER	186.92	261.70	02/2006	12/2013	06/2014	6
28	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR & G'BA RE	171.10	224.89	03/2012	03/2012	12/2013	21
29	PATNA GANGA BRIDGE (NL), ECR ECR	624.47	2,921.00	10/2007	12/2012	12/2015	36
	<u>Road Transport & Highways</u>						
30	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH- 4) NHAI	241.00	196.65	08/2004	02/2013	03/2013	1
31	HARIHAR-CHITRADURGA (GQ) KM.284- KM.207 (NH-4) NHAI	318.00	207.56	08/2004	02/2013	03/2013	1
32	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	02/2013	03/2013	1
33	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) NHAI	203.43	203.43	10/2008	02/2013	03/2013	1
34	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA NHAI	229.91	229.91	10/2008	02/2013	03/2013	1
35	THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	03/2013	04/2013	1
36	GWALIOR BYPSS, NH-75,3 NHAI	300.93	300.93	10/2009	02/2013	03/2013	1
37	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE NHAI	232.45	232.45	09/2010	12/2013	01/2014	1
38	Jaipur-Tonk-Deoli NHAI	792.06	792.06	12/2012	03/2013	04/2013	1
39	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	02/2013	03/2013	1
40	KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	06/2013	09/2013	3
41	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) NHAI	193.45	193.45	11/2012	12/2013	03/2014	3
42	Kishangarh-Ajmer-Beawer NHAI	795.00	795.00	05/2012	02/2013	06/2013	4
43	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	02/2013	06/2013	4
44	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM NHAI	852.00	852.00	03/2013	03/2013	07/2013	4
45	DEEWAPUR TO UP/BIHAR BORDER (LMNHP- 9)-NH-28, KM.402-360.915 NHAI	300.00	300.00	10/2008	01/2014	06/2014	5
46	JAIPUR-REENGUS NHAI	267.81	267.81	02/2013	02/2013	07/2013	5
47	TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	03/2013	09/2013	6
48	Gurgaon-Kotputli Km 42.70 to 54.4 Km NHAI	1,673.70	1,673.70	10/2011	06/2013	12/2013	6
49	CHAMBAL BRIDGE, NH-76 (RJ-5) NHAI	275.00	281.31	02/2010	12/2013	07/2014	7
50	PATNA-MUZZAFFARPUR NHAI	671.30	671.30	02/2013	02/2013	10/2013	8
51	4 LANING OF NAGPUR-BETUL NHAI	2,498.76	2,498.76	08/2014	08/2014	07/2015	11
52	PUNE-SATARA(NH-4) NHAI	1,724.55	1,724.55	03/2013	03/2013	04/2014	13
	<u>Shipping & Ports</u>						
53	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	02/2013	03/2013	1


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
54	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER MUMBAI PORT TRU	1,228.00	1,460.00	12/2010	10/2013	12/2013	2
	<u>Telecommunications</u>						
55	ERP implementation in BSNL on Turnkey basis BSNL	384.00	384.00	10/2010	06/2013	09/2013	3
55							

Graphical Analysis of All Projects w.r.t. Original Schedule

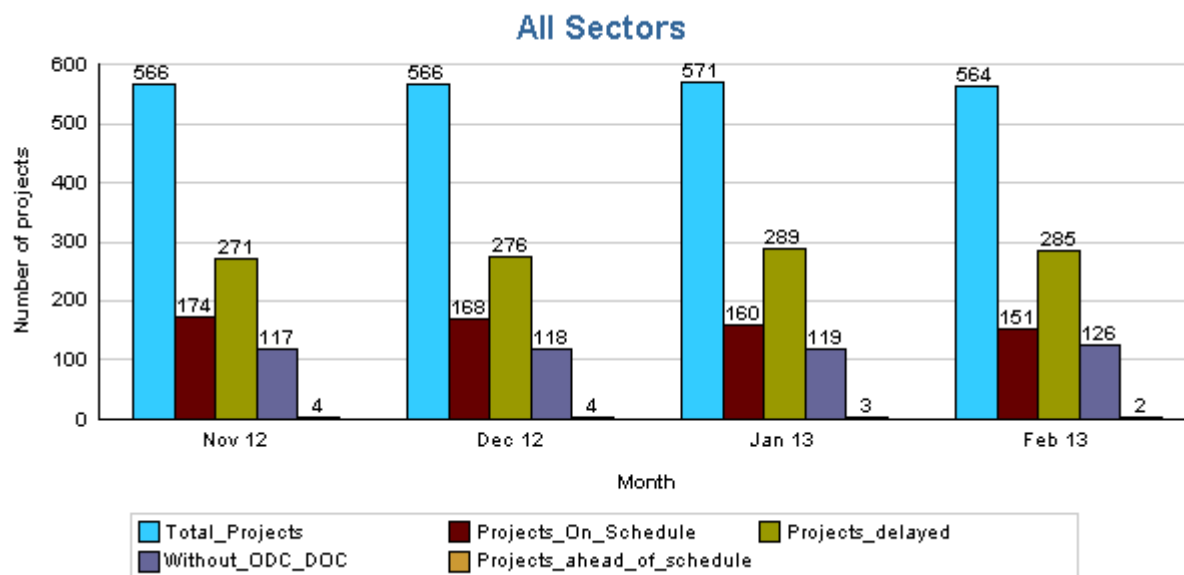


Break-up of 285 Delayed projects in February 2013

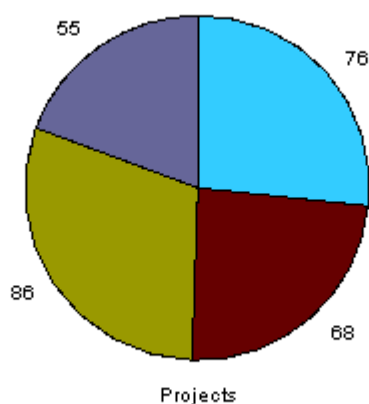


Delay in Months



Graphical Analysis of All Projects w.r.t. Revised Schedule

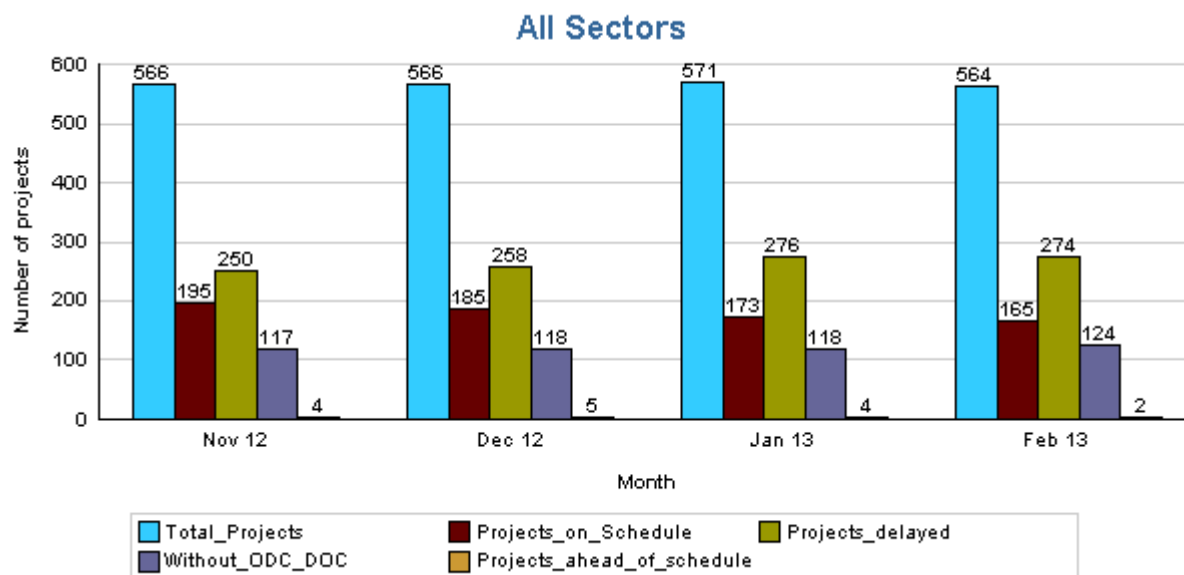


Break-up of 274 Delayed projects in February 2013

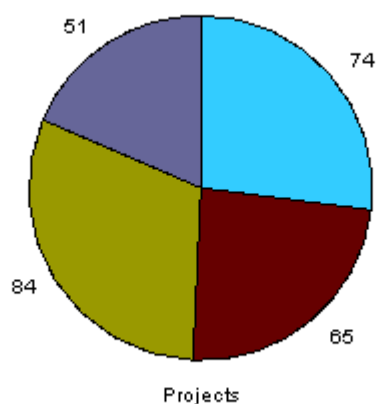


Delay in Months



Graphical Analysis of Urban Development Sector

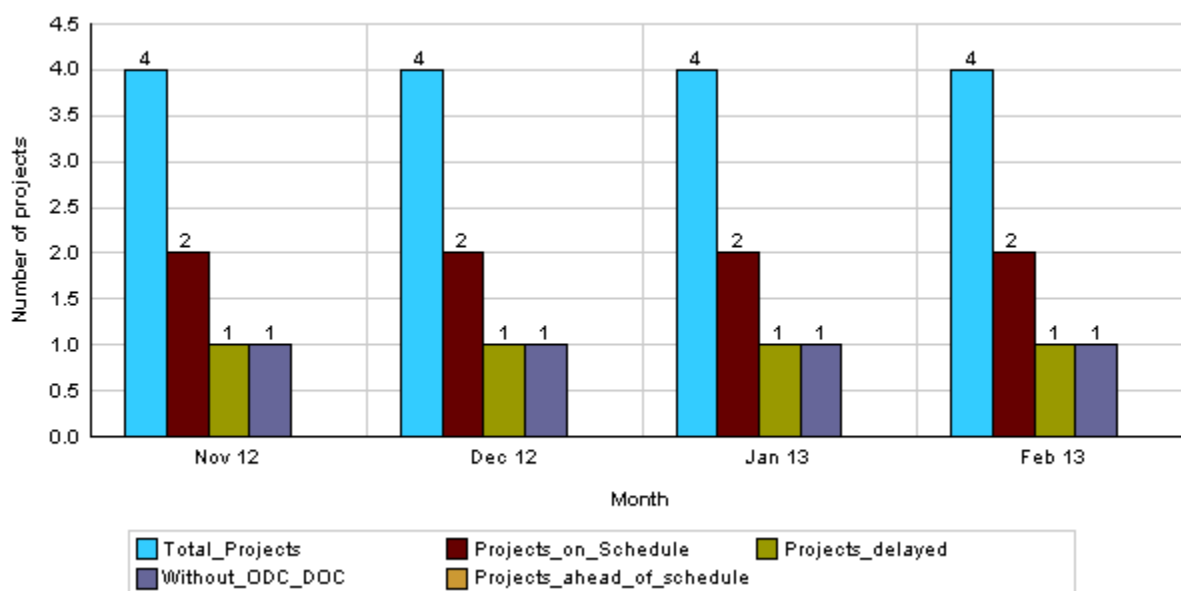


Break-up of 1 Delayed projects in February 2013

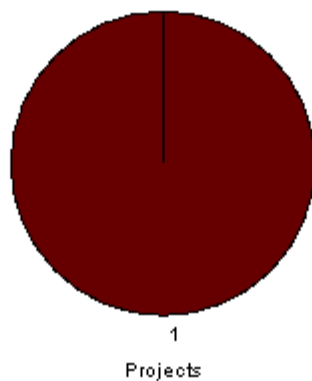


Delay in Months



Graphical Analysis of Telecommunications Sector

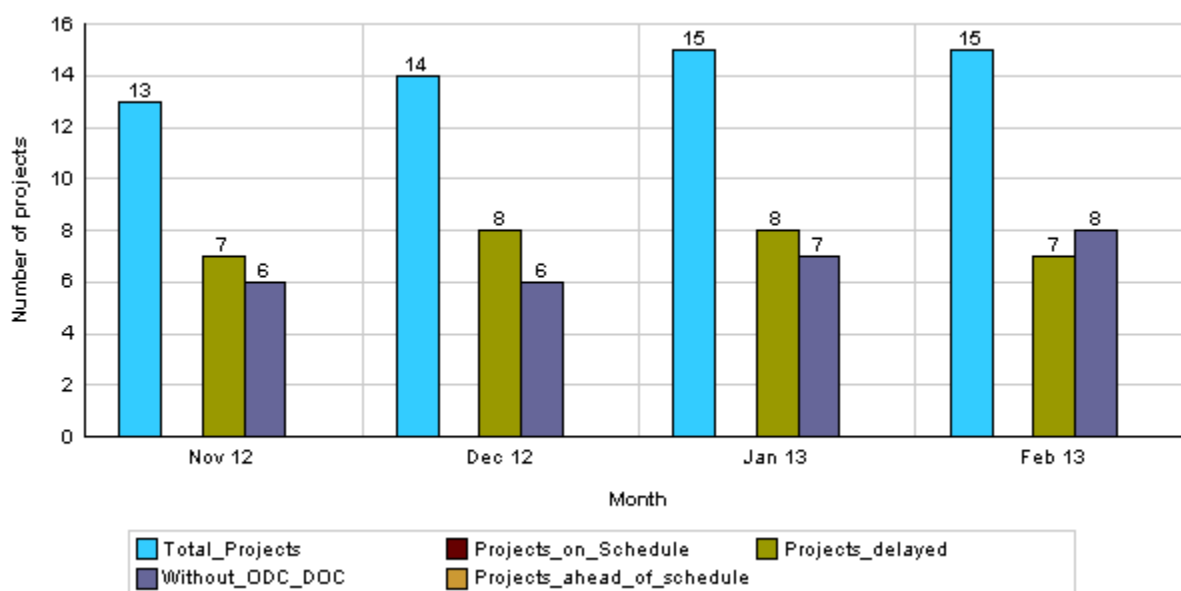


Break-up of 7 Delayed projects in February 2013

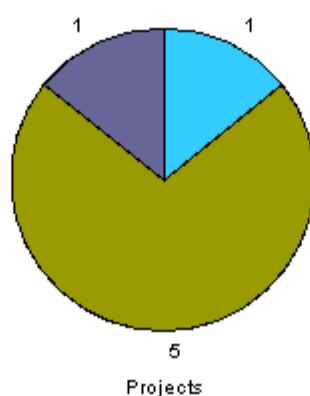


Delay in Months



Graphical Analysis of Shipping and Ports Sector

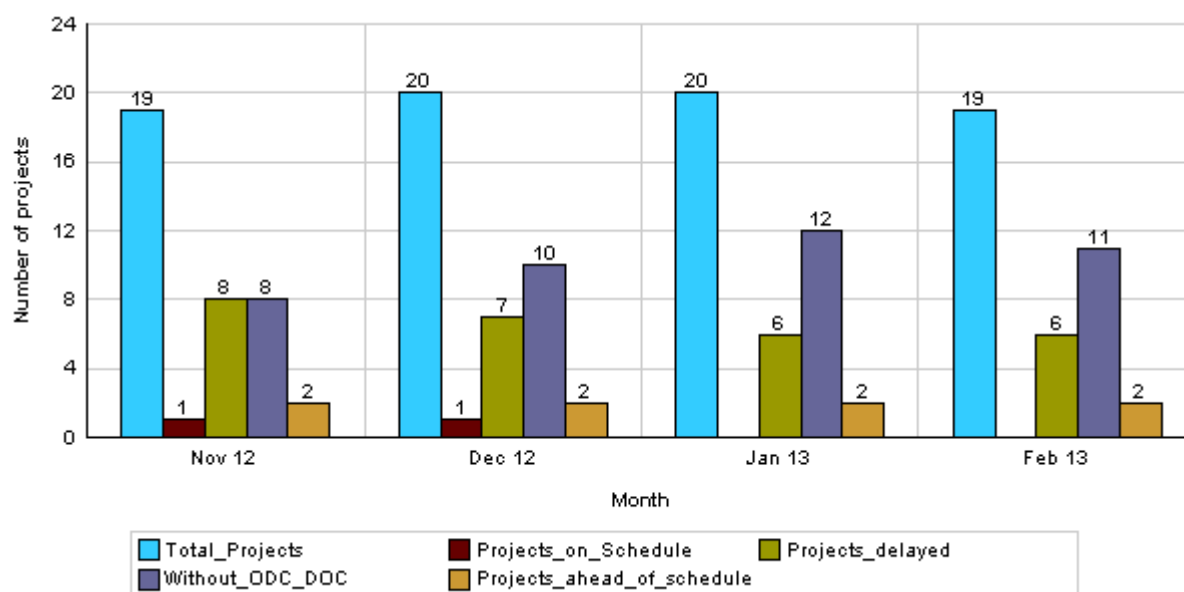


Break-up of 6 Delayed projects in February 2013

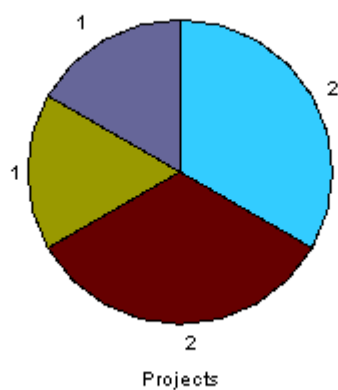


Delay in Months

■ 1-12 ■ 13-24 ■ 25-60 ■ 60 and Above

Graphical Analysis of Road Transport and Highways Sector

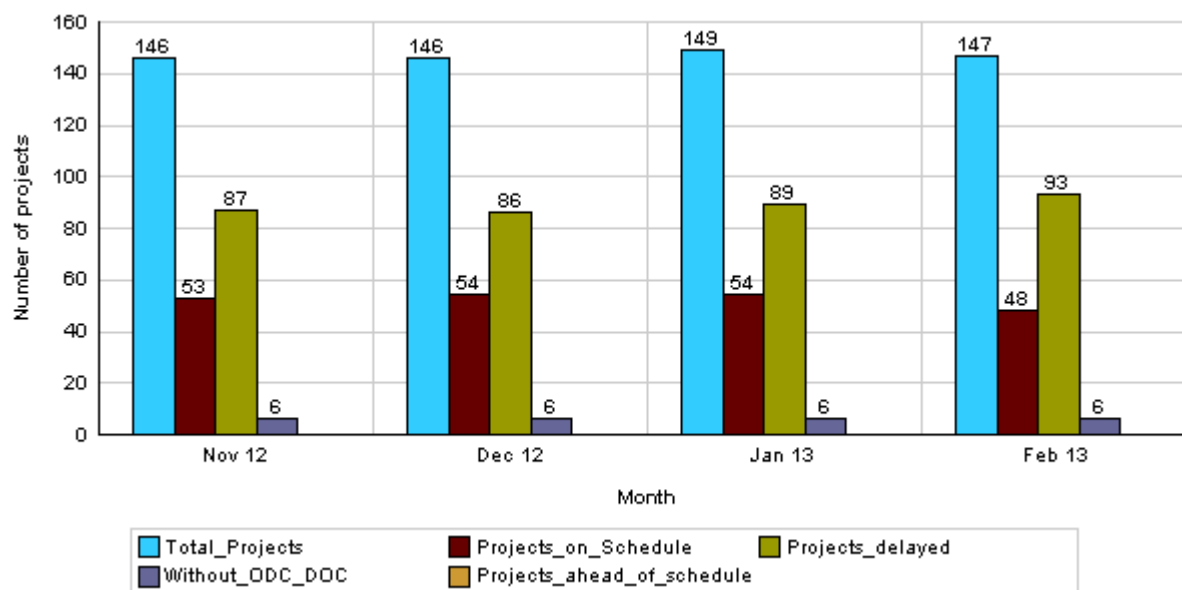


Sector Break-up of 93 Delayed projects in February 2013

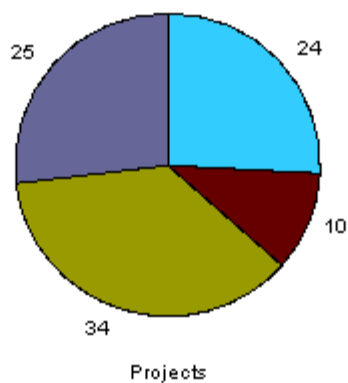


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above

Graphical Analysis of Railways Sector

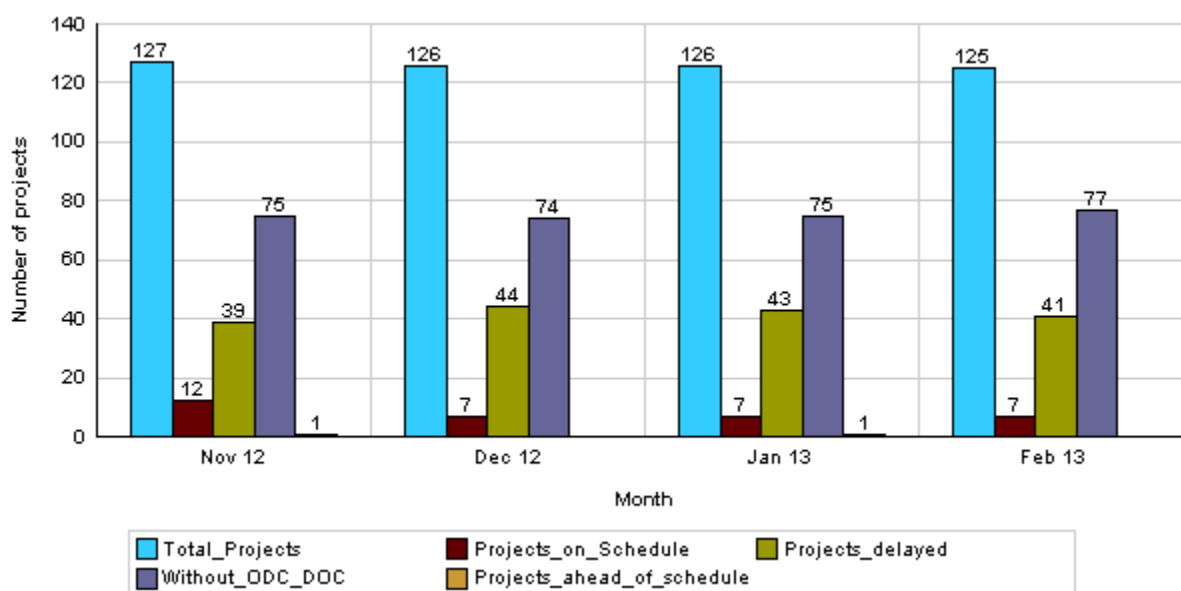


Break-up of 41 Delayed projects in February 2013

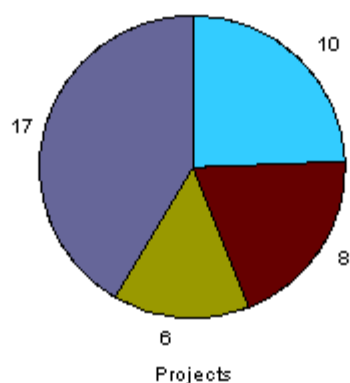


Delay in Months



Graphical Analysis of Power Sector

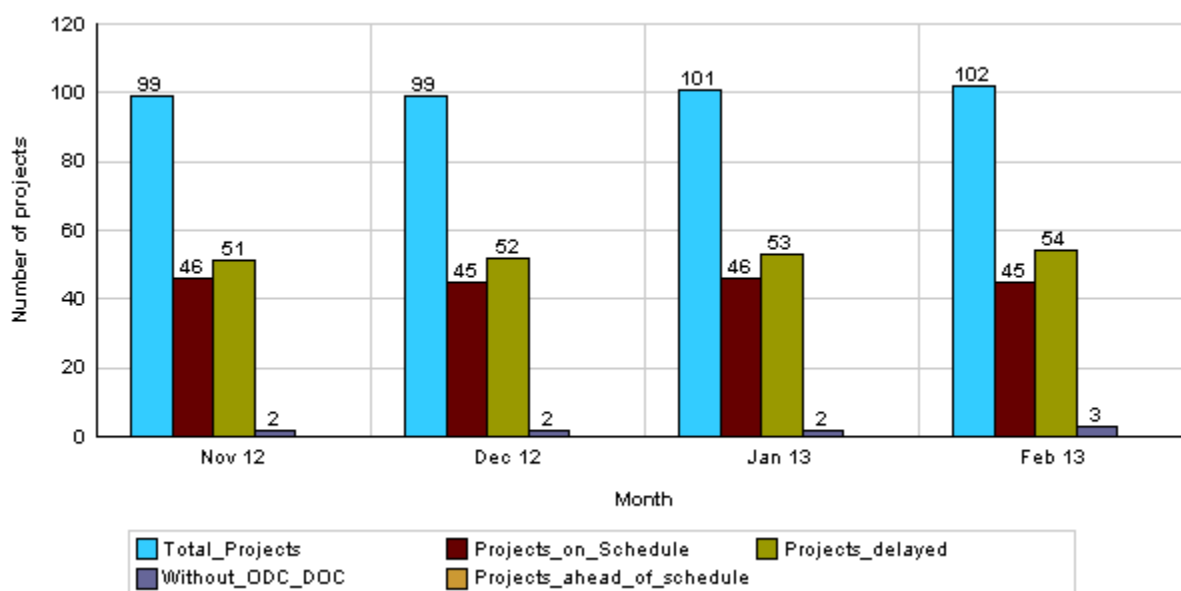


Break-up of 54 Delayed projects in February 2013

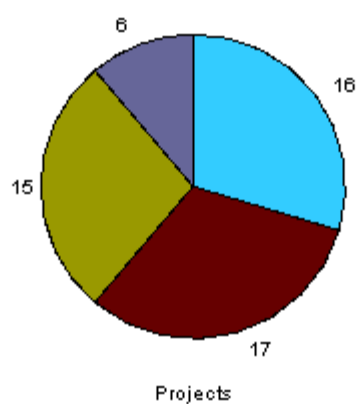


Delay in Months



Graphical Analysis of Petroleum Sector

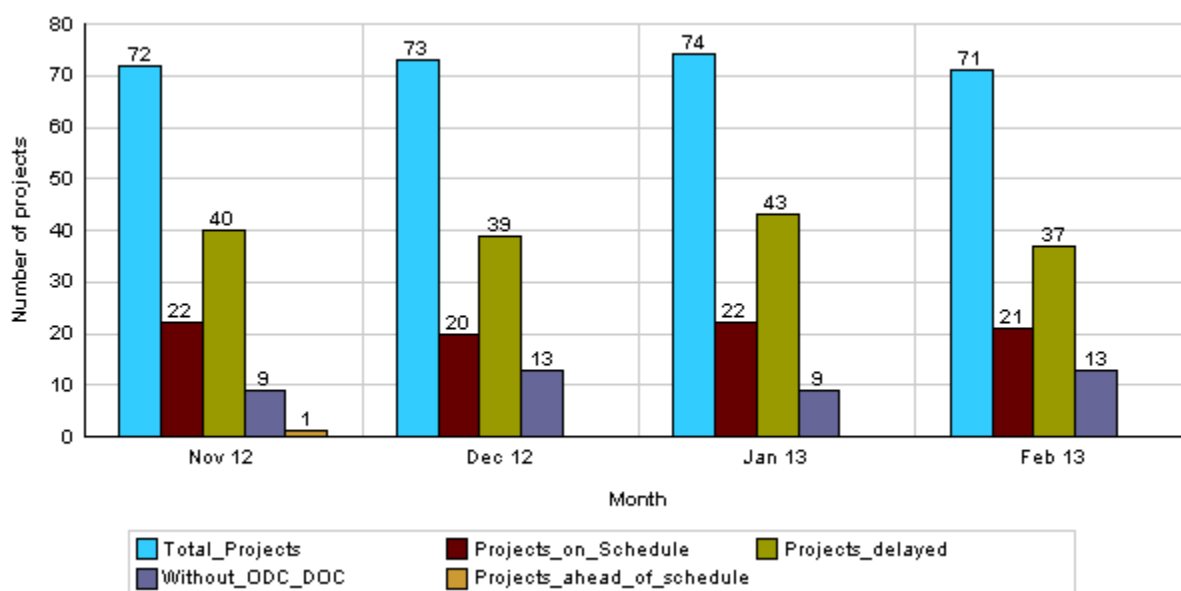


Break-up of 37 Delayed projects in February 2013

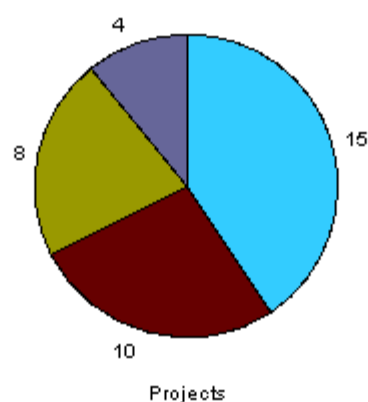


Delay in Months



Graphical Analysis of Steel Sector

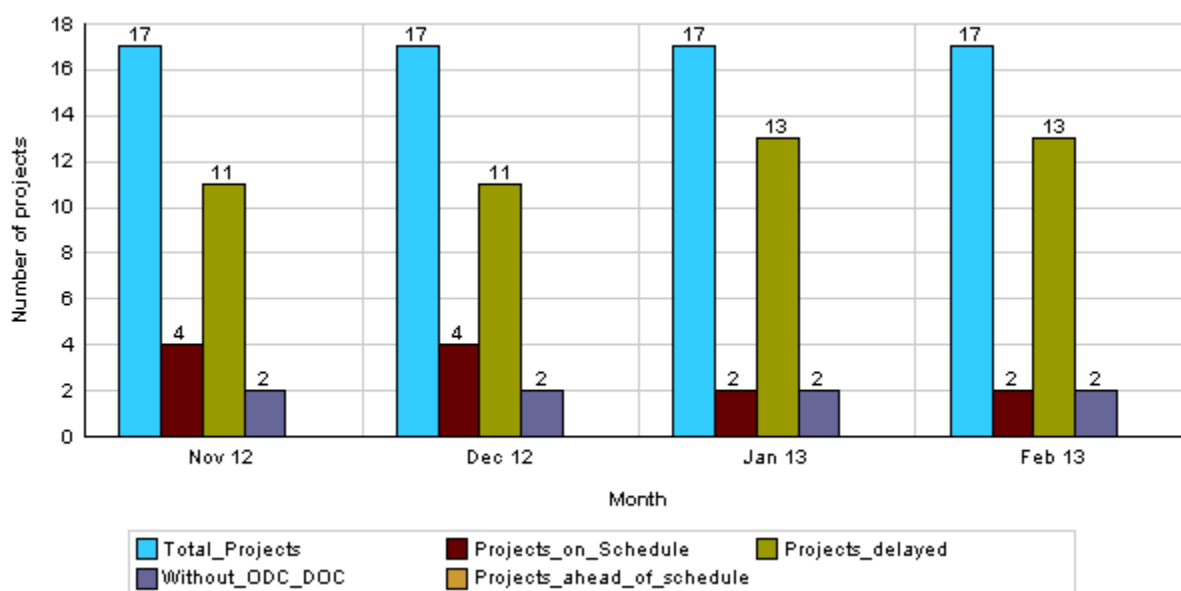


Break-up of 13 Delayed projects in February 2013

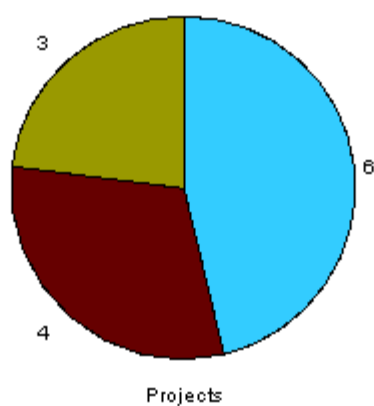


Delay in Months



Graphical Analysis of Coal Sector

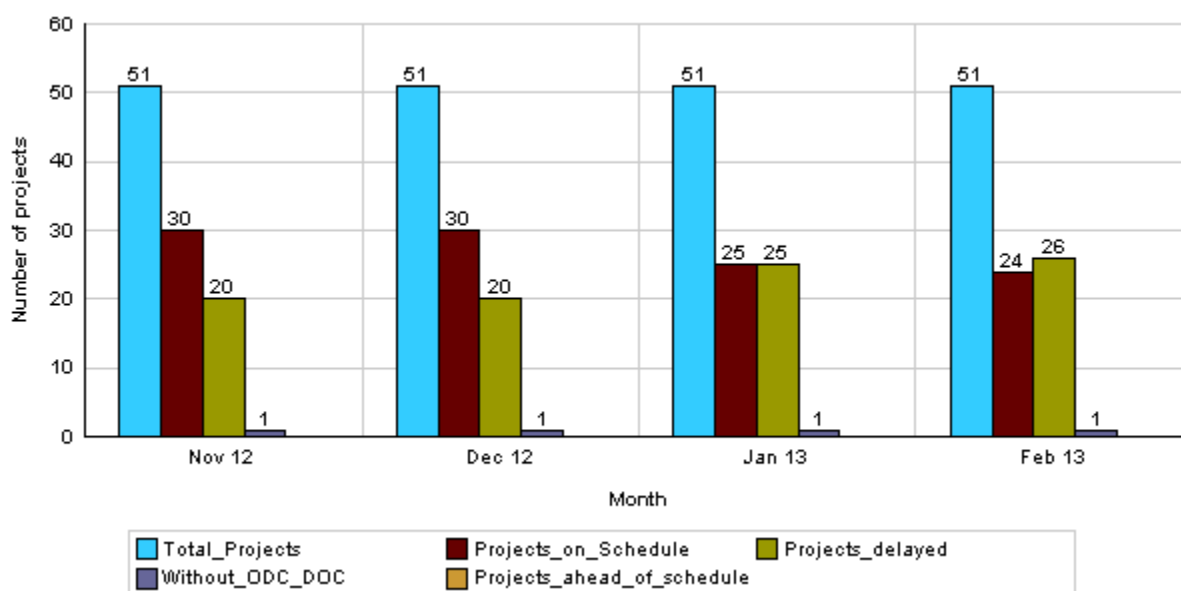


Break-up of 26 Delayed projects in February 2013

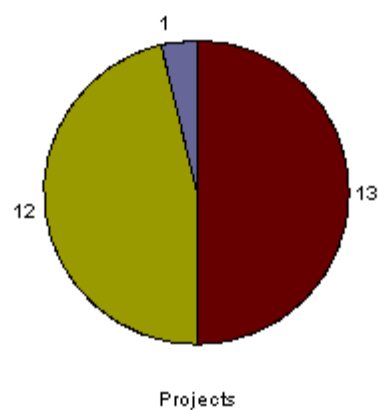


Delay in Months



Graphical Analysis of Civil Aviation Sector

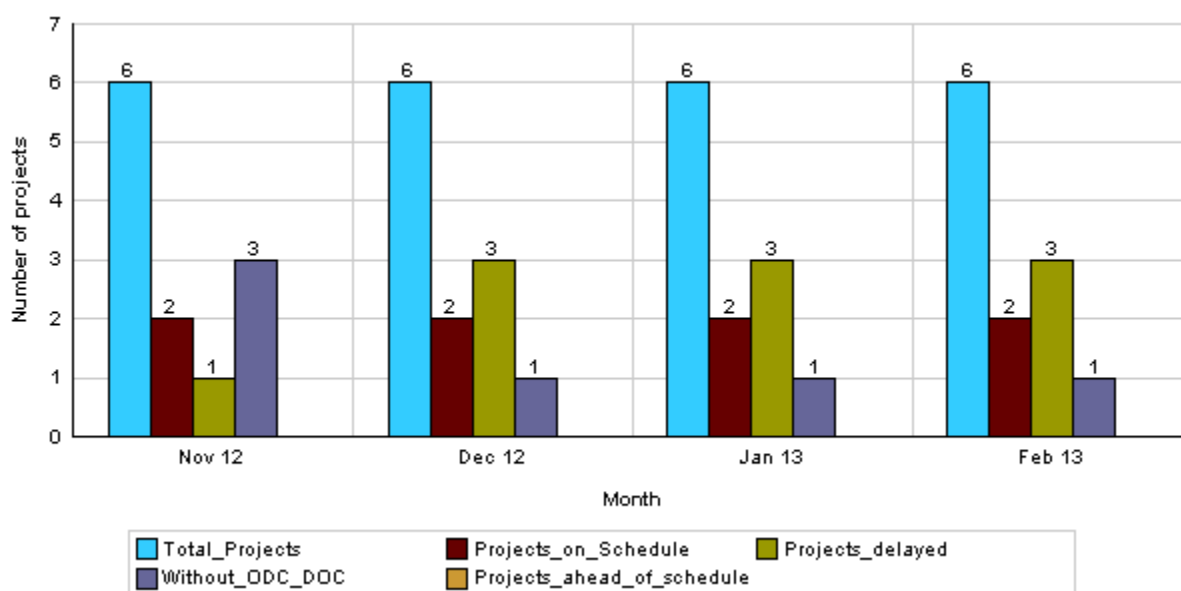


Break-up of 3 Delayed projects in February 2013

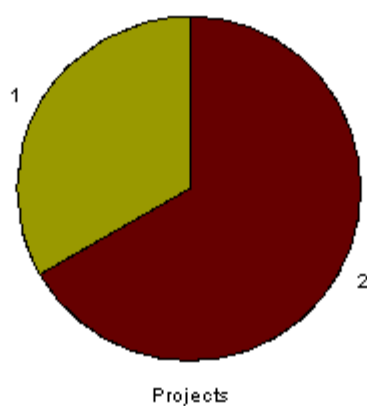


Delay in Months



Graphical Analysis of Atomic Energy Sector

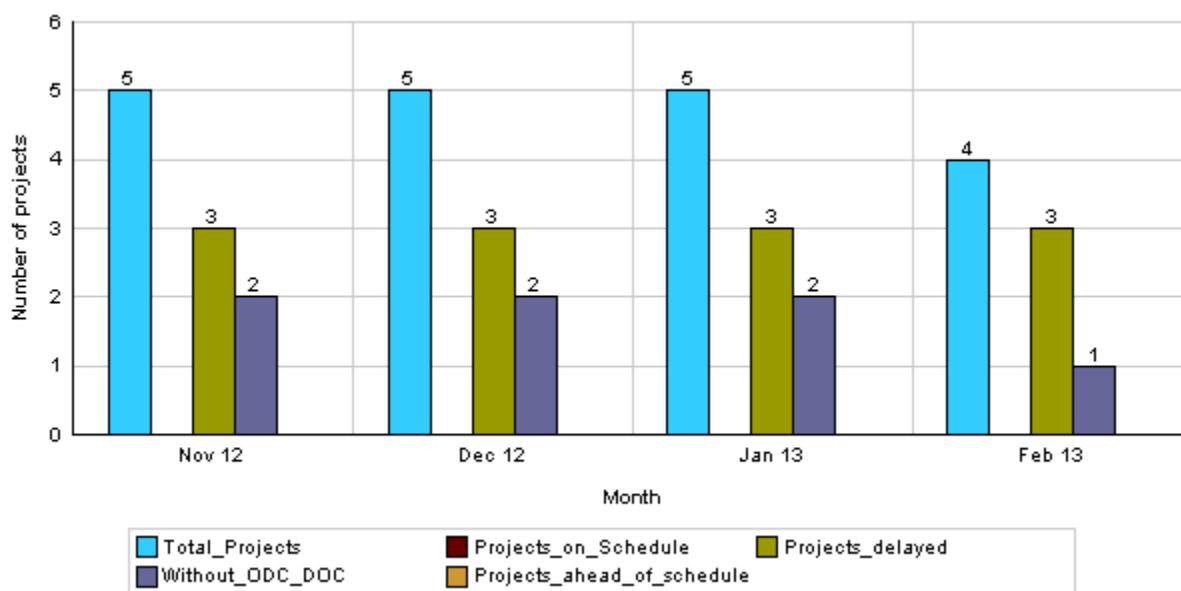

Break-up of 3 Delayed projects in February 2013



Delay in Months



Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	4	40,442.00	40,442.00	46,726.00	23,535.33
Civil Aviation	6	5,473.58	5,680.58	6,063.07	4,946.52
Coal	51	36,056.46	37,022.46	37,510.52	13,866.49
Fertilisers	1	1,478.63	1,478.63	1,478.63	1,087.00
Steel	17	65,285.87	67,562.15	71,443.41	47,807.33
Petrochemicals	1	5,460.61	8,920.00	8,920.00	6,229.56
Petroleum	71	169,219.44	184,731.06	181,912.59	71,092.10
Power	102	241,378.89	244,983.58	257,209.13	116,014.86
Railways	125	61,244.63	90,989.76	148,185.62	62,617.39
Road Transport & Highways	147	96,472.10	96,638.60	98,410.72	73,510.81
Shipping & Ports	19	15,617.12	17,389.43	17,902.42	8,107.64
Telecommunications	15	7,113.08	7,113.08	6,920.16	1,296.96
Urban Development	4	44,245.18	44,304.08	49,518.08	10,445.64
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	564	790,030.49	847,798.31	933,387.35	440,593.12

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Atomic Energy									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	2,432.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,454.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	4,005.33	09/2010	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,644.00	12/2016	03/2017	3(O)	0/69
Total			40,442.00	46,726.00	23,535.33				47/327
Civil Aviation									
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,303.26	05/2011	03/2013	22(O)	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	214.03	01/2011 04/2013	12/2013	35(O) 8(R)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	190.40	05/2012	06/2013	13(O)	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,796.60	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	452.00	65.26	03/2015	03/2015	0(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	376.97	06/2013	06/2013	0(O)	0/0
Total			5,473.58	6,063.07	4,946.52				0/0
Coal									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	455.09	03/2013 09/2012	07/2014	16(O) 22(R)	7/22
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	150.59	198.59	95.10	03/2016	03/2016	0(O)	2/6
13	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	416.83	03/2016 03/2016	03/2016	0(O) 0(R)	2/4

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28	207.28	101.39	03/2012	03/2014	24(O)	5/9
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66	341.63	143.89	03/2011	03/2014	36(O)	0/4
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08	172.08	119.64	03/2010	03/2015	60(O)	4/5
17	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	258.56	40.18	03/2016	03/2016	0(O)	0/1
18	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00	490.10	122.75	03/2017	03/2017	0(O)	6/12
19	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.86	03/2014	03/2014	0(O)	1/4
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04	535.10	167.29	03/2015	03/2015	0(O)	0/3
21	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	1/2
22	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	265.47	03/2014	03/2016	24(O)	2/7
23	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.88	03/2011	03/2016	60(O)	0/2
24	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66	1,943.66	1,262.91	03/2014	03/2016	24(O)	6/12
25	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67	2,675.67	1,407.50	03/2014	03/2016	24(O)	10/15
26	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87	395.87	71.92	03/2015	03/2015	0(O)	2/12
27	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63	479.63	118.39	03/2013	03/2013	0(O)	5/10
28	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24(O)	1/7
29	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	3.02	03/2015	03/2015	0(O)	4/31
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78	467.78	12.31	03/2013	03/2013	0(O)	4/83
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.82	03/2011	03/2017	72(O)	0/2
32	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63	453.63	82.44	12/2012	03/2016	39(O)	8/44
33	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77	457.77	114.99	03/2013	03/2013	0(O)	6/11
34	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46	162.46	34.89	03/2014	03/2014	0(O)	0/3
35	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24(O)	1/7
36	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	3.87	03/2018	03/2018	0(O)	0/3
37	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88	741.62	345.20	03/2013	03/2013	0(O)	2/5

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
38	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96	302.96	109.03	03/2010	03/2014	48(O)	7/10
39	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31	1,188.31	716.90	03/2013	03/2013	0(O)	0/9
40	Kistaram OCP - [N060000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
41	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78	706.40	19.23	07/2012	03/2016	44(O)	1/5
42	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42	321.50	205.44	03/2014	03/2016	24(O)	1/6
43	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	39.77	03/2012	03/2015	36(O)	7/20
44	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27	1,230.27	-	04/2015	04/2015	0(O)	0/0
45	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88	339.88	-	04/2014	04/2014	0(O)	0/0
46	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	26.99	12/2015	08/2017	20(O)	0/33
47	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	3.28	03/2012	03/2015	36(O)	0/2
48	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87	179.87	60.74	03/2012	03/2017	60(O)	0/4
49	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	1/1
50	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.88	03/2014	03/2016	24(O)	0/1
51	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98	210.98	91.35	03/2013	03/2015	24(O)	2/4
52	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82	153.82	24.39	03/2014	03/2016	24(O)	0/2
53	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	134.00	03/2012	03/2015	36(O)	24/27
54	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	2.48	03/2015	03/2015	0(O)	4/29
55	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78	209.78	31.29	03/2015	03/2015	0(O)	4/31
56	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85	510.85	269.01	03/2016	03/2016	0(O)	1/4
57	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	49.64	03/2012	-	-	11/42
58	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72	447.72	43.33	03/2016	03/2016	0(O)	0/10
59	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,611.71	06/2009	09/2013	51(O)	19/24
60	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,838.87	03/2012	03/2014	24(O)	0/39
61	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	126.53	03/2012	03/2016	48(O)	0/4

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		36,056.46	37,510.52	13,866.49				161/661
	<u>Fertilisers</u>								
62	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	1,087.00	01/2013	01/2013	-	0/8
	Total		1,478.63	1,478.63	1,087.00				0/8
	<u>Steel</u>								
63	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	242.77	- 12/2013	12/2013	- 0(R)	15/19
64	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	251.98	08/2010	02/2013	30(O)	0/1
65	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	254.51	02/2011	03/2013	25(O)	2/3
66	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	173.58	- 11/2013	11/2013	- 0(R)	11/21
67	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	234.56	05/2012	06/2013	13(O)	1/2
68	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	347.44	12/2011 03/2012	06/2013	18(O) 15(R)	16/21
69	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	136.95	10/2012	06/2013	8(O)	3/4
70	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	332.65	22.45	08/2014	08/2014	0(O)	0/0
71	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55	254.55	16.28	11/2013	03/2014	4(O)	1/1
72	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	7,995.11	03/2013	03/2014	12(O)	22/27
73	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00	6,325.00	3,314.41	12/2011	06/2013	18(O)	16/16
74	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00	2,875.00	1,420.06	12/2012	12/2013	12(O)	10/12
75	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	14,280.71	12/2011	06/2013	18(O)	19/19
76	EXPANSION OF RINL/VSP FROM 3 MTPY- 6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	10,193.53	10/2009	03/2013	41(O)	62/64
77	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 11,812.00	11,812.00	8,862.42	03/2013	12/2013	9(O)	11/14
78	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33	187.33	57.69	10/2013	12/2013	2(O)	0/1

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
79	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]SAIL, Odisha	01/2012	254.90	254.90	2.88	12/2014	12/2014	0(O)	0/0
			-	-	-	-	-	-	-
	Total		65,285.87	71,443.41	47,807.33				189/225
			-	-	-				
	<u>Petrochemicals</u>								
80	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61	8,920.00	6,229.56	04/2012	12/2013	20(O)	19/29
			8,920.00	-	-	12/2013	-	0(R)	-
	Total		5,460.61	8,920.00	6,229.56				19/29
			-	-	-				
	<u>Petroleum</u>								
81	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00	678.02	-	06/2012	03/2014	21(O)	0/0
			-	-	-	-	-	-	-
82	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64	2,163.64	1,483.80	06/2012	06/2013	12(O)	0/0
			-	-	-	-	-	-	-
83	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11	370.11	279.73	04/2011	02/2013	22(O)	0/0
			-	-	-	-	-	-	-
84	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35	977.00	683.37	12/2011	07/2013	19(O)	0/0
			-	-	-	-	-	-	-
85	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	1,353.63	03/2013	03/2014	12(O)	0/0
			-	-	-	-	-	-	-
86	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00	586.00	-	07/2015	07/2015	0(O)	0/0
			-	-	-	-	-	-	-
87	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	783.72	12/2014	12/2014	0(O)	0/0
			-	-	-	-	-	-	-
88	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	2,189.63	1,039.14	12/2014	12/2014	0(O)	0/0
			-	-	-	-	-	-	-
89	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	460.70	-	07/2012	-	-	0/17
			-	-	-	07/2012	-	-	-
90	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50	341.50	165.28	02/2013	04/2013	2(O)	38/42
			-	-	-	-	-	-	-
91	Butene-1 at Panipat - [N16000139]IOCL, Haryana	02/2012	190.00	190.00	34.37	03/2014	03/2014	0(O)	0/24
			-	-	-	-	-	-	-
92	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65	736.65	344.88	09/2011	12/2013	27(O)	0/0
			-	-	-	-	-	-	-
93	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29	6,326.40	5,659.05	05/2010	01/2013	-	0/0
			6,326.40	-	-	05/2012	-	-	-
94	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00	394.00	381.67	-	03/2013	-	18/19
			394.00	-	-	-	-	-	-
95	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79	756.65	97.69	05/2013	11/2013	6(O)	0/0
			-	-	-	-	-	-	-
96	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL, Rajasthan	04/2011	152.89	152.89	-	06/2013	06/2013	0(O)	0/0
			-	-	-	-	-	-	-

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	27.13	08/2013	01/2014	5(O)	0/0
98	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	240.95	69.30	09/2012	09/2013	12(O)	0/0
99	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
100	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	267.00	224.41	09/2012	-	-	0/0
101	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00	486.00	41.89	09/2013	-	-	0/0
102	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	-	-	-	-	0/0
103	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	2,735.65	2,184.01	04/2006	06/2013	86(O)	0/0
104	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	5,633.44	4,184.58	08/2010	12/2013	40(O)	0/0
105	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	2,920.82	1,858.42	09/2010	04/2013	31(O)	0/0
106	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21	1,436.21	872.82	07/2010	05/2013	34(O)	0/0
107	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	3,690.37	2,520.91	12/2008	04/2013	52(O)	0/0
108	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	2,174.00	1,302.79	09/2011	06/2013	21(O)	5/76
109	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	2,730.00	1,488.99	09/2011	03/2013	18(O)	0/0
110	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	155.49	03/2013	04/2013	1(O)	0/0
111	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17	2,592.17	-	05/2014	05/2014	0(O)	0/0
112	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	5,916.65	932.51	03/2013	04/2014	13(O)	0/0
113	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	96.19	11/2012	10/2013	11(O)	0/0
114	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	499.77	01/2014	01/2014	0(O)	0/0
115	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17	600.17	-	12/2014	12/2014	0(O)	0/0
116	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	422.00	01/2013	08/2013	7(O)	18/18
117	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00	1,827.00	1,249.81	04/2013	04/2013	0(O)	0/167
118	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40	5,608.40	483.04	05/2015	05/2015	0(O)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
119	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Odisha	12/2009	1,492.33	1,492.33	1,219.50	06/2012	03/2013	9(O)	8/8
120	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
121	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
122	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49	352.49	-	03/2014	03/2014	0(O)	0/0
123	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
124	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00	14,225.00	226.44	12/2015	05/2016	5(O)	0/0
125	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	2,059.63	69.89	03/2015	03/2015	0(O)	0/0
126	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	-	01/2013	-	-	0/0
127	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	-	10/2010	12/2014	50(O)	0/0
128	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68	204.00	-	01/2012	-	-	0/1
129	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	-	12/2012	12/2014	24(O)	0/21
130	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00	666.00	-	11/2015	11/2015	0(O)	0/0
131	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	12,160.26	-	01/2012	-	-	0/108
132	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	5,067.86	09/2012	09/2013	12(O)	0/0
133	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,185.52	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
134	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	701.81	04/2015	04/2015	0(O)	0/0
135	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00	279.00	-	12/2014	12/2014	0(O)	0/0
136	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24(O) 22(R)	0/0
137	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	631.71	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
138	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00	913.00	21.84	07/2015	07/2015	0(O)	0/0
139	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00	30,426.00	20,426.00	11/2012	11/2013	12(O)	60/100
140	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	-	09/2012	-	-	0/11

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
141	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	-	02/2014	02/2014	0(O)	0/0
142	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	211.00	04/2012	06/2013	14(O)	0/0
143	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	1,417.00	118.77	05/2014	05/2014	0(O)	0/0
144	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	-	07/2012	10/2013	15(O)	0/31
145	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	915.58	-	-	-	51/53
146	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64	1,210.64	40.57	11/2015	11/2015	0(O)	3/25
147	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00	1,419.00	1.07	12/2014	12/2014	0(O)	0/0
148	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57	1,043.57	-	04/2012	-	-	0/0
149	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	253.66	165.66	08/2012	05/2013	9(O)	0/0
150	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	330.47	-	03/2012	-	-	13/20
151	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	576.60	-	12/2013	12/2013	0(O)	0/0
Total			169,219.44	181,912.59	71,092.10				229/756
Power									
152	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	5,601.90	08/2012	01/2014	17(O)	0/11
153	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,165.70	02/2012	05/2013	15(O)	0/7
154	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	729.10	05/2012	09/2013	16(O)	0/11
155	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	1,110.50	06/2012	06/2013	12(O)	0/4
156	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04	156.04	-	10/2014	10/2014	0(O)	0/0
157	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	5,105.00	08/2013	09/2014	13(O)	8/19
158	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	7,975.00	12/2009	02/2017	86(O)	27/47

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
159	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, Assam	01/2008	4,375.35	4,375.35	3,580.00	07/2011	10/2015	51(O)	5/28
160	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC, Jammu and Kashmir	08/2006	621.26	913.00	775.32	02/2011 10/2012	01/2013	-	2/4
161	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL, Andhra Pradesh	08/2011	1,637.34	1,637.34	468.90	08/2014	08/2014	0(O)	0/20
162	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL, Andhra Pradesh	03/2012	206.44	206.44	33.90	06/2014	06/2014	0(O)	0/20
163	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL, Tamil Nadu	01/2013	182.80	182.80	-	10/2014	10/2014	0(O)	0/0
164	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL, Tamil Nadu	09/2011	1,940.13	1,940.13	609.90	09/2014	09/2014	0(O)	8/19
165	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL, Multi State	10/2006	975.96	975.96	871.40	10/2009	06/2013	44(O)	20/20
166	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL, Multi State	07/2010	1,272.80	1,272.80	543.70	11/2012	03/2014	16(O)	3/11
167	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL, Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O)	0/0
168	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL, Chhatisgarh	05/2011	1,961.87	1,961.87	638.30	05/2014	05/2014	0(O)	0/16
169	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL, Chhatisgarh	12/2010	1,719.52	1,719.52	858.50	08/2013	08/2013	0(O)	0/14
170	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL, Bihar	12/2011	901.77	901.77	139.80	08/2014	08/2014	0(O)	0/21
171	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL, Chhatisgarh	08/2011	1,391.97	1,391.97	775.10	12/2013	12/2013	0(O)	0/13
172	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL, Multi State	10/2010	160.32	160.32	63.60	10/2012	03/2013	5(O)	5/14
173	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45	1,007.16	871.13	12/2007 12/2009	-	-	0/10
174	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pradesh	12/2004	2,496.90	2,496.90	2,176.62	05/2013 06/2016	03/2017	46(O) 9(R)	6/22
175	KISHANGANGA HEP - [N18000031]NHPC, Jammu and Kashmir	07/2007	2,238.67	3,642.00	2,095.31	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
176	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pradesh	10/2002	4,527.15	6,358.91	4,793.00	04/2009	09/2014	65(O)	0/9
177	KUDGI STPP STAGE 1 - [N18000131]NTPC, Karnataka	12/2011	15,166.19	15,166.19	1,258.00	12/2016	12/2016	0(O)	4/7
178	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, Tamil Nadu	05/2005	1,779.29	2,159.07	1,845.21	09/2008	03/2013	54(O)	17/37
179	LARA STPP STAGE-I - [N18000140]NTPC, Chhatisgarh	11/2012	11,846.00	11,846.00	722.00	05/2017	05/2017	0(O)	2/2

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
180	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00	1,527.00	36.00	08/2017	08/2017	0(O)	0/0
181	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,818.00	08/2012	03/2013	7(O)	16/16
182	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47	7,921.47	692.00	09/2016	09/2016	0(O)	13/14
183	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01	936.00	829.31	08/2010 01/2013	06/2013	34(O) 5(R)	0/3
184	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	5,518.40	08/2013	09/2014	13(O)	0/17
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	251.00	02/2012	12/2013	22(O)	0/14
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	339.00	11/2011	12/2013	25(O)	0/11
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	348.20	11/2011	12/2013	25(O)	0/14
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	89.60	01/2013	09/2013	8(O)	0/7
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	238.20	07/2013	03/2014	8(O)	0/12
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	715.40	04/2013	03/2014	11(O)	0/12
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	114.70	08/2013	08/2013	0(O)	0/16
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63	723.63	81.70	11/2014	11/2014	0(O)	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34	803.34	-	03/2015	03/2015	0(O)	0/0
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40	524.40	14.90	04/2015	05/2015	1(O)	0/0
195	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	518.80	11/2012	12/2013	13(O)	0/10
196	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56	2,716.00	2,029.68	10/2010 01/2013	03/2014	41(O) 14(R)	0/6
197	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59	5,366.00	3,779.86	09/2009 07/2014	03/2018	102(O) 44(R)	1/20
198	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99	573.99	485.51	08/2012 08/2013	09/2014	25(O) 13(R)	16/22

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
199	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pradesh	01/2007	2,047.03	2,047.03	2,235.18	01/2012	02/2014	25(O)	0/27
200	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	4,012.00	10/2012	11/2013	13(O)	12/16
201	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18	9,395.18	1,243.00	11/2016	11/2016	0(O)	13/13
202	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33	10,667.00	6,056.50	09/2010 08/2014	12/2017	87(O) 40(R)	11/11
203	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	72.10	04/2013	09/2013	5(O)	0/15
204	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	2,011.70	08/2012	12/2013	16(O)	0/7
205	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	1,508.74	-	06/2016	06/2016	0(O)	0/0
206	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	1,935.35	-	12/2014	12/2014	0(O)	0/0
207	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/0
208	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	67.40	08/2014	08/2014	0(O)	0/20
209	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	172.80	02/2015	02/2015	0(O)	0/0
210	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	1,263.26	183.60	11/2014	11/2014	0(O)	0/0
211	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	180.50	01/2015	01/2015	0(O)	0/19
212	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	63.80	08/2014	08/2014	0(O)	0/20
213	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	107.00	06/2014	06/2014	0(O)	0/19
214	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	169.80	04/2012	03/2013	11(O)	0/0
215	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	135.68	06/2012	06/2013	12(O)	0/9
216	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	831.80	08/2012	03/2014	19(O)	0/11
217	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48	2,978.48	1,704.00	03/2013	03/2016	36(O)	2/15
218	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,292.14	09/2009 06/2013	03/2014	54(O) 9(R)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
219	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC, West Bengal	10/2003	768.92 -	1,628.00	1,662.25	03/2007 09/2012	03/2013	72(O) 6(R)	25/25
220	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00 2,978.88	2,978.86	446.79	07/2010 02/2016	11/2016	76(O) 9(R)	1/10
221	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL, Gujarat	01/2012	259.28 -	259.28	69.10	01/2014 -	01/2014	0(O) -	0/17
222	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL, Multi State	12/2011	2,422.66 -	2,422.66	173.80	08/2014 -	08/2014	0(O) -	0/0
223	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - - [N18000129]PGCIL, Multi State	02/2012	3,201.44 -	3,201.44	330.80	10/2014 -	10/2014	0(O) -	0/21
224	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL, Multi State	04/2008	297.37 386.32	386.32	337.73	07/2011 -	03/2013	20(O) -	0/5
225	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, Multi State	10/2008	4,824.12 -	4,824.12	3,249.40	10/2012 -	12/2013	14(O) -	0/12
226	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57 -	4,404.57	361.10	01/2015 -	01/2015	0(O) -	0/20
227	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25 -	2,569.25	1,180.80	03/2014 -	03/2014	0(O) -	0/15
228	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL, Andhra Pradesh	12/2010	779.21 -	779.21	741.50	08/2013 -	08/2013	0(O) -	0/14
229	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL, Andhra Pradesh	02/2012	324.33 -	324.33	10.60	08/2014 -	08/2014	0(O) -	0/20
230	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL, Andhra Pradesh	02/2012	1,927.16 -	1,927.16	85.40	10/2014 -	10/2014	0(O) -	0/20
231	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATHI-III HEP - [N18000018]PGCIL, Himachal Pradesh	07/2006	557.24 -	758.75	598.00	01/2010 -	03/2013	38(O) -	0/22
232	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19 -	184.19	155.80	11/2011 -	09/2013	22(O) -	0/7
233	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88 -	7,031.88	4,246.60	12/2012 -	06/2013	6(O) -	0/11
234	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL, Gujarat	12/2011	552.44 -	552.44	161.70	02/2014 -	02/2014	0(O) -	0/20
235	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya Pradesh	08/2011	425.51 -	425.51	229.20	10/2013 -	10/2013	0(O) -	0/18

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
236	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	65.40	07/2013 -	07/2013	0(O) -	0/0
237	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	461.50	12/2013 -	12/2013	0(O) -	0/18
238	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	113.50	11/2013 -	11/2013	0(O) -	0/20
239	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	874.20	03/2013 -	06/2013	3(O) -	0/14
240	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,280.60	12/2013 -	12/2013	0(O) -	0/13
241	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,112.00	11/2012 -	03/2014	16(O) -	0/15
242	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	480.50	07/2014 -	07/2014	0(O) -	0/19
243	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEEPCO,Tripura	07/2009	421.01 -	623.44	454.21	-	07/2013	-	6/29
244	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NNEEPCO,Mizoram	01/2011	913.63 -	913.63	389.14	07/2014 -	02/2015	7(O) -	0/16
245	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,178.20	12/2012 -	12/2013	12(O) -	0/11
246	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	727.50	11/2013 -	11/2013	0(O) -	0/15
247	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	61.30	01/2013 -	03/2014	14(O) -	0/16
248	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,903.38	11/2009 02/2013	05/2013	42(O) 3(R)	0/4
249	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	158.00	08/2015 -	08/2015	0(O) -	5/7
250	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	4,204.00	10/2012 -	03/2013	5(O) -	15/15
251	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	339.11	07/2014 -	05/2016	22(O) -	1/1
252	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	426.00	09/2010 -	03/2013	30(O) -	0/9
253	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	499.60	06/2015 -	06/2015	0(O) -	0/24
Total			241,378.89 -	257,209.13	116,014.86				244/1289

Railways

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
254	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura	04/2008	813.34 813.34	1,141.75	449.62	03/2014 -	12/2015	21(O) -	0/0
255	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00 427.21	432.72	366.38	12/2009 03/2011	10/2013	46(O) 31(R)	0/0
256	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 1,010.00	2,820.00	226.28	- -	-	-	0/0
257	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	453.04	396.44	03/2011 03/2011	03/2011	-	0/0
258	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	548.95	544.30	06/1999 03/2011	03/2011	-	0/0
259	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
260	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR, Gujarat	04/2008	394.14 385.60	404.39	15.90	03/2013 -	-	-	0/0
261	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 901.62	901.62	0.29	- -	-	-	0/0
262	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	1,423.98	468.58	03/2005 12/2008	06/2016	135(O) 90(R)	0/0
263	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	1,106.62	214.91	12/2010 03/2011	03/2011	-	0/0
264	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, Maharashtra	03/1996	401.81 495.44	1,512.86	226.08	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
265	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 619.34	2,393.48	32.72	04/2014 -	03/2017	35(O) -	0/0
266	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20 -	687.20	691.50	03/2010 -	-	-	0/0
267	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	350.00	332.07	- 03/2009	-	-	0/0
268	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	5,016.00	2,650.10	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
269	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52 207.52	207.52	157.96	12/2012 -	12/2013	12(O) -	0/0
270	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36 196.95	196.95	194.97	03/2011 -	-	-	0/0
271	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR, Gujarat	04/2008	318.24 -	468.62	1.52	03/2012 -	-	-	0/0
272	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
273	CHANDIGARH-LUDHIANA(NEW BG LINE), NR - [220100241]NR, Punjab	07/1998	248.44 576.27	1,115.21	939.49	12/2012 01/2013	02/2013	2(O) 1(R)	0/0
274	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
275	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
276	CHURCHGATE-VIRAR: CONV.OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233]RE, Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2013	06/2013	0(O) 0(R)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
277	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	308.05	- -	06/2013	- -	0/0
278	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	119.46	12/2012 -	-	-	0/0
279	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	90.17	- -	-	-	0/0
280	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	210.76	- -	03/2013	-	0/0
281	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	471.60	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
282	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	592.35	- -	12/2012	-	0/0
283	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	94.51	12/2011 02/2012	02/2012	-	0/0
284	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	224.89	141.55	03/2012 -	12/2013	21(O) -	0/0
285	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	204.65	12/2008 -	09/2014	69(O) -	0/0
286	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	220.91	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
287	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
288	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	272.71	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
289	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	116.99	02/2006 -	06/2014	100(O) -	0/0
290	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	611.87	- -	03/2012	-	0/0
291	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
292	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	345.44	- 05/2009	05/2009	-	0/0
293	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	548.65	03/1994 -	10/2013	235(O) -	0/0
294	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	120.59	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
295	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	184.87	- -	-	-	0/0
296	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	735.10	224.33	- 09/2009	-	-	0/0
297	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
298	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	574.88	- -	01/2013	-	0/0
299	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	141.55	- -	03/2014	- -	0/0
300	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.33	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
301	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	71.53	- -	-	-	0/0
302	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	16.23	03/2015 -	03/2015	0(O) -	0/0
303	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	835.94	06/2007 -	06/2007	-	0/0
304	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	679.24	03/2012 08/2012	-	-	0/0
305	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	697.50	433.79	03/2012 03/2012	12/2012	-	0/0
306	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	1,172.32	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
307	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	228.10	03/2014 -	03/2014	0(O) -	0/0
308	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	279.98	03/2012 03/2012	03/2013	12(O) 12(R)	0/0
309	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,379.64	- -	03/2013	- -	0/0
310	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	495.77	- -	03/2014	- -	1/1
311	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	762.61	- -	10/2012	-	0/0
312	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	737.21	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
313	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	106.63	- -	-	-	0/0
314	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	225.00	220.09	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
315	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	239.15	- -	03/2014	-	0/0
316	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
317	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	449.89	- 03/2010	03/2010	-	0/0
318	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,390.14	07/2005 -	-	-	0/0
319	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	134.12	- -	-	-	0/0
320	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	281.81	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
321	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
322	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	345.93	- -	12/2012	-	0/0
323	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	116.67	12/2012 -	03/2015	27(O) -	0/0
324	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	349.77	05/2008 03/2011	-	-	0/0
325	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	212.91	03/2002 -	03/2013	132(O) -	0/0
326	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,367.54	03/2009 -	03/2015	72(O) -	0/0
327	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
328	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.50	- -	02/2013	- -	0/0
329	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	663.17	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
330	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
331	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	413.84	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
332	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	900.00	295.40	- -	-	-	0/0
333	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	1,008.73	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
334	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	156.28	- -	03/2012	-	0/0
335	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	635.20	02/2009 -	03/2012	-	0/0
336	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	360.00	07/2012 -	-	-	0/0
337	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	40.88	- -	-	-	0/0
338	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	123.57	- -	03/2016	- -	0/0
339	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,340.39	12/2008 -	03/2014	63(O) -	0/0
340	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	248.05	- -	03/2015	- -	0/0
341	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24(O) -	0/0
342	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	260.58	03/2016 -	03/2016	0(O) -	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
343	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	22.86	03/2014 -	03/2014	0(O) -	0/0
344	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	93.62	03/2016 -	03/2016	0(O) -	0/0
345	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	33.27	03/2016 -	06/2016	3(O) -	0/0
346	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	441.67	03/2008 06/2008	-	-	0/0
347	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	355.00	378.12	03/2009 11/2012	-	-	0/0
348	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	249.36	02/2010 11/2012	12/2015	70(O) 37(R)	0/0
349	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,649.50	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
350	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	598.00	- -	03/2012	-	0/0
351	Pandabeswar-Chinpa doubling (ER) - [N220000118]ER,West Bengal	04/2004	225.68 293.74	293.74	136.16	12/2010 12/2010	12/2010	-	0/0
352	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	792.25	- -	03/2013	- -	0/6
353	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	242.03	12/2007 03/2010	-	-	0/0
354	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	940.76	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
355	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	243.40	257.30	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
356	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	227.53	- -	-	-	0/0
357	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	326.81	06/2004 -	12/2012	-	0/0
358	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	2,232.50	1,660.03	- -	03/2014	- -	0/0
359	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	343.36	04/2003 03/2010	-	-	0/0
360	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	639.97	175.25	03/1998 08/2005	08/2005	-	0/0
361	Ramanagram-Mysore doubling with electrification of - [N220000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	434.58	03/2013 -	03/2014	12(O) -	0/0
362	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	171.44	03/2012 -	-	-	0/0
363	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	230.01	03/2010 -	-	-	0/0
364	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017	15(O) -	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
365	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	818.29	75.76	02/2015 -	-	-	0/0
366	Suratpura - Hanumangarh - Sriganaganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	337.94	03/2014 -	03/2014	0(O)	0/0
367	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	118.16	- -	-	-	0/0
368	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	434.55	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
369	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	586.63	- 12/2009	02/2012	-	0/0
370	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	145.76	- -	-	-	0/0
371	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	40.72	- -	-	-	0/0
372	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	548.96	536.30	- -	-	-	0/0
373	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,363.87	12/2006 08/2010	08/2010	-	0/0
374	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	64.92	03/2012 -	02/2013	11(O) -	0/0
375	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	9,001.45	03/2001 -	12/2017	201(O) -	0/0
376	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	819.40	158.04	03/2010 03/2017	-	-	0/0
377	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	510.92	03/2014 -	-	-	0/0
378	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	177.66	- 03/2010	-	-	0/0
Total			61,244.63 -	148,185.62	62,617.39				1/7
Road Transport & Highways									
379	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	392.02	05/2013 -	03/2014	10(O) -	0/0
380	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	275.47	11/2013 -	11/2013	0(O) -	0/0
381	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	624.00	120.14	04/2014 -	04/2014	0(O) -	0/0
382	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
383	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	47.45	01/2014 -	01/2014	0(O) -	0/0
384	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	280.35	02/2014 -	02/2014	0(O) -	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
385	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00	664.00	359.69	02/2014	04/2014	2(O)	0/0
386	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09	375.09	45.59	04/2014	04/2014	0(O)	0/0
387	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00	325.00	160.02	05/2014	05/2014	0(O)	0/0
388	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	1,626.70	08/2014	07/2015	11(O)	0/0
389	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	1,138.00	06/2013	06/2013	0(O)	0/0
390	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	37.94	09/2013	07/2014	10(O)	0/0
391	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	710.10	08/2013	08/2013	0(O)	0/0
392	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	575.00	712.50	07/2013	07/2013	0(O)	0/0
393	4-laning of Barhi-Hazariabagh - [N24000191]NHAI,Jharkhand	02/2012	398.00	398.00	311.92	02/2014	02/2014	0(O)	0/0
394	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	998.79	725.68	08/2013	08/2013	0(O)	0/0
395	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	919.85	08/2013	08/2013	0(O)	0/0
396	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
397	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18	1,396.18	529.67	09/2014	09/2014	0(O)	0/0
398	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	204.17	09/2007	03/2014	78(O)	0/0
399	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,252.70	11/2012	06/2013	7(O)	0/0
400	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	299.96	11/2008	03/2013	52(O)	0/0
401	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	261.42	01/2009	12/2013	59(O)	0/0
402	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	03/2013	13(O)	0/0
403	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70	228.70	194.51	02/2004	03/2013	109(O)	0/0
404	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	266.89	09/2013	09/2013	0(O)	0/0
405	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	839.93	06/2014	06/2014	0(O)	0/0
406	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	425.48	-	10/2013	-	2/2
407	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	8.04	01/2013	10/2013	9(O)	0/0
408	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29	500.29	450.94	08/2013	08/2013	0(O)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
409	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	263.14	06/2008	03/2014	69(O)	0/0
410	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	223.86	06/2008	03/2014	69(O)	0/0
411	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	231.64	06/2005	03/2014	105(O)	0/0
412	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	248.44	04/2010	11/2014	55(O)	0/0
413	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	07/2014	53(O)	0/0
414	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	784.25	03/2013	07/2013	4(O)	0/0
415	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	500.43	-	12/2013	-	0/1
416	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	05/2013	0(O)	0/0
417	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	391.77	10/2011	03/2014	29(O)	0/0
418	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	749.58	10/2011	06/2013	20(O)	0/0
419	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	175.59	10/2008	06/2014	68(O)	0/0
420	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	637.97	05/2010	03/2013	34(O)	0/0
421	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00	593.00	465.75	07/2013	07/2013	0(O)	0/0
422	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.82	06/2013	06/2013	0(O)	0/0
423	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	460.37	-	06/2013	-	1/1
424	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	241.19	06/2008	05/2013	59(O)	0/0
425	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	194.26	05/2008	12/2013	67(O)	0/0
426	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	283.52	09/2010	01/2014	40(O)	0/0
427	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	300.48	08/2013	08/2013	0(O)	0/0
428	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	435.22	09/2008	05/2013	56(O)	0/0
429	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00	682.00	-	10/2013	03/2014	5(O)	0/0
430	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	12/2013	30(O)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
431	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	137.88	09/2008	03/2013	54(O)	0/0
432	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27	263.27	272.36	02/2004	03/2013	109(O)	0/0
433	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	1,039.20	08/2013	08/2013	0(O)	0/0
434	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	232.80	04/2008	03/2014	71(O)	0/0
435	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	171.49	04/2008	03/2014	71(O)	0/0
436	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	303.02	10/2009	03/2013	41(O)	0/0
437	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	495.37	12/2009	07/2013	43(O)	0/0
438	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,675.00	09/2012	03/2013	6(O)	0/0
439	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,777.00	10/2011	12/2013	26(O)	0/0
440	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	282.68	09/2007	03/2013	66(O)	0/0
441	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	292.91	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
442	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	107.64	07/2009	05/2014	58(O)	0/0
443	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	43.31	09/2007	04/2014	79(O)	0/0
444	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00	478.00	245.01	10/2013	03/2014	5(O)	0/0
445	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	190.77	08/2004	03/2013	103(O)	0/0
446	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	191.57	08/2004 07/2010	03/2013	103(O) 32(R)	0/0
447	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	625.07	928.03	01/2013	06/2013	5(O)	0/0
448	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
449	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,944.20	10/2012	03/2013	5(O)	0/0
450	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	431.34	05/2013	02/2014	9(O)	0/0
451	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
452	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	267.81	560.96	02/2013	07/2013	5(O)	0/0
453	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
454	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	501.18	09/2009	06/2013	45(O)	0/0
455	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	536.00	436.99	01/2014	01/2014	0(O)	0/0
456	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	1,638.70	12/2012	04/2013	4(O)	0/0
457	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.76	10/2008	09/2013	59(O)	0/0
458	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	294.50	10/2008	03/2013	53(O)	0/0
459	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16	702.16	299.08	07/2014	07/2014	0(O)	0/0
460	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	957.76	-	03/2013	-	2/3
461	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,055.70	05/2012	06/2013	13(O)	0/0
462	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	186.29	06/2010	12/2013	42(O)	0/0
463	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
464	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24(O)	0/0
465	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	105.66	11/2008	06/2014	67(O)	0/0
466	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	73.96	04/2009	12/2014	68(O)	0/0
467	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	34.01	11/2008	12/2014	73(O)	0/0
468	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	131.41	04/2009	12/2014	68(O)	0/0
469	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	03/2013	9(O)	0/0
470	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	1,313.30	06/2013	06/2013	0(O)	0/0
471	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00	754.00	510.99	03/2013	03/2014	12(O)	0/0
472	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	269.32	11/2013	11/2013	0(O)	0/0
473	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	297.51	06/2008	05/2013	59(O)	0/0
474	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2013	54(O)	0/0
475	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19	484.19	34.07	10/2014	10/2014	0(O)	0/0
476	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	285.37	04/2008	05/2014	73(O)	0/0

Sector Wise Details

(Feb,2013)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
477	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	256.56	06/2008	09/2013	63(O)	0/0
478	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	279.47	06/2008	09/2013	63(O)	0/0
479	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
480	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	268.59	06/2011	04/2013	22(O)	0/2
481	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	932.27	02/2010	12/2014	58(O)	0/0
482	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00	586.00	237.56	01/2014	01/2014	0(O)	0/0
483	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	485.07	09/2013	09/2013	0(O)	0/0
484	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	396.58	03/2008	03/2013	60(O)	0/0
485	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00	1,410.00	152.77	09/2014	09/2014	0(O)	0/0
486	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	995.04	10/2014	10/2014	0(O)	0/0
487	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69	942.69	128.49	06/2014	06/2014	0(O)	0/0
488	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	267.88	05/2008	03/2013	58(O)	0/0
489	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00	574.00	516.26	03/2014	03/2014	0(O)	0/0
490	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	671.30	600.33	02/2013	10/2013	8(O)	0/0
491	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	1,263.20	07/2012	06/2013	11(O)	0/0
492	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	1,112.80	03/2013	04/2014	13(O)	0/0
493	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	835.00	122.65	01/2014	01/2014	0(O)	0/0
494	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,465.90	11/2011	08/2013	21(O)	0/0
495	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17(O)	0/0
496	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00	1,987.00	670.55	07/2015	06/2016	11(O)	0/0
497	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	323.83	10/2008	06/2013	56(O)	0/0
498	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	289.95	10/2008	03/2013	53(O)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
499	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00	1,479.00	156.85	06/2015	06/2015	0(O)	0/0
500	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	858.06	11/2013	11/2013	0(O)	0/0
501	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	256.53	10/2008	03/2013	53(O)	0/0
502	SALEM - U / UNDRUPET(BOT -1/TN-06) NH - 68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	05/2013	28(O)	0/0
503	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	805.39	451.09	03/2013	12/2013	9(O)	0/0
504	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
505	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	223.76	09/2007	03/2013	66(O)	0/0
506	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	189.77	07/2008	03/2013	56(O)	0/0
507	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
508	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	14.58	12/2013	12/2013	0(O)	0/0
509	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
510	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2015	31(O)	0/0
511	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
512	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.21	03/2008	06/2013	63(O)	0/0
513	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00	241.53	156.85	04/2004	03/2013	107(O)	0/0
514	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,677.40	08/2011	06/2013	22(O)	0/0
515	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	04/2013	46(O)	0/0
516	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	09/2013	38(O)	0/0
517	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	882.40	11/2013	11/2013	0(O)	0/0
518	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
519	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	98.06	05/2013	05/2013	0(O)	0/0
520	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	184.63	-	04/2013	-	2/2

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
521	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	742.93	03/2014	03/2014	0(O)	0/0
522	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27	193.10	164.10	03/2008	03/2013	60(O)	0/0
523	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	41.09	11/2012	03/2014	16(O)	0/0
524	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	515.07	07/2013	06/2014	11(O)	0/0
525	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	201.61	06/2014	06/2014	0(O)	0/0
	Total		96,472.10	98,410.72	73,510.81				10/14
Shipping & Ports									
526	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011	11/2012	-	0/0
527	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49	220.49	98.31	01/2013	06/2013	5(O)	0/0
528	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87	511.87	107.56	03/2014	-	-	0/0
529	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	364.52	12/2012 12/2012	10/2013	10(O) 10(R)	0/0
530	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
531	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	306.12	02/2014	-	-	0/0
532	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,012.23	433.54	12/2013 10/2013	10/2013	-2(O) 0(R)	0/0
533	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	927.92	12/2010 09/2012	12/2013	36(O) 15(R)	0/0
534	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24(O)	0/0
535	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.93	02/2011	12/2012	-	0/0
536	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008	10/2008	-	0/0
537	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84	253.36	-	-	01/2009	-	0/1
538	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	137.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
539	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
540	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
541	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
542	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	830.85	10/2008 11/2010	-	-	0/0
543	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,651.10	01/2012 09/2012	03/2013	14(O) 6(R)	0/0
544	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
	Total		15,617.12 -	17,902.42	8,107.64				0/1
Telecommunications									
545	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53(O) -	0/0
546	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	-	02/2007 12/2010	-	-	0/0
547	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	-	02/2007 03/2012	02/2013	72(O) 11(R)	0/0
548	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	229.41	-	03/2012 -	02/2013	11(O) -	0/0
549	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 -	09/2013	35(O) -	0/0
550	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
551	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
552	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013	45(O) -	0/0
553	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	-	12/2008 -	12/2012	-	0/0
554	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	823.48	11/2010 -	03/2013	28(O) -	0/0
555	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	-	-	0/0
556	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	-	03/2009 -	01/2013	-	0/0

Sector Wise Details

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
557	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
558	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	-	-	0/0
559	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19	964.37	170.25	05/2011	06/2013	25(O)	0/0
	Total		7,113.08	6,920.16	1,296.96				0/0
			-						
	<u>Urban Development</u>								
560	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	8,473.08	06/2011	03/2013	21(O)	3/3
561	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
562	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	1,788.69	03/2016	03/2016	0(O)	0/0
563	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	183.87	09/2014	09/2014	0(O)	0/0
	Total		44,245.18	49,518.08	10,445.64				3/3
			-						
	<u>Water Resources</u>								
564	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	-	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			790,030.49	933,387.35	440,593.12				903/3320

Sector wise current status of projects on the Flash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

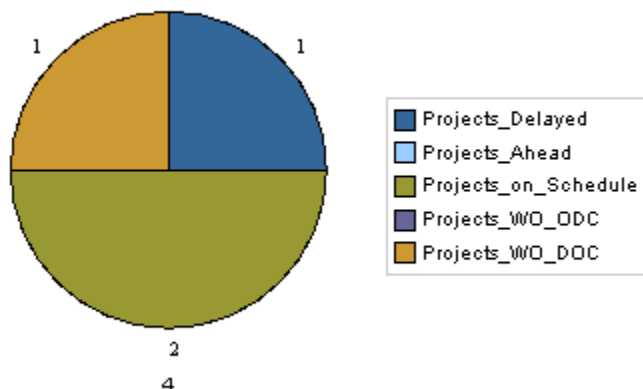

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till February, 2013 is Rs. 10445.64 crore, which is 21.1% of the revised cost of the projects.

Figures are in Rs. Crore

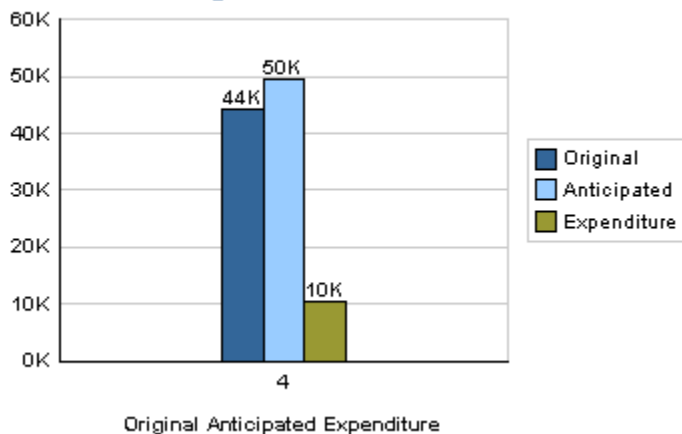

Sector wise current status of projects on the Flash Report

Telecommunications

I. Current Status:


Number of Projects 15

Number of Projects Delayed 7

Number of Projects Without Date Of Commissioning 8

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 7 projects are delayed .8 projects do not have fixed dates of commissioning.

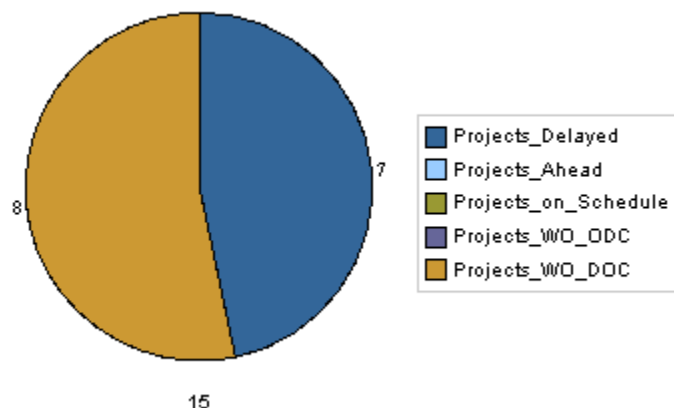

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 7113.08 crore but this was subsequently revised to Rs. 6920.16 crore implying a cost overrun of -2.7%. The expenditure incurred on these projects till February, 2013 is Rs. 1296.96 crore, which is 18.7% of the revised cost of the projects.

Figures are in Rs. Crore

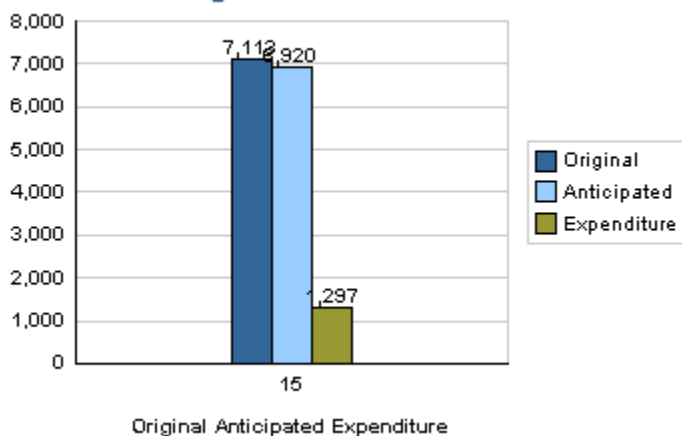

Sector wise current status of projects on the Flash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects Delayed	6
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	11


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 2 projects are ahead of schedule, 6 projects are delayed .11 projects do not have fixed dates of commissioning.

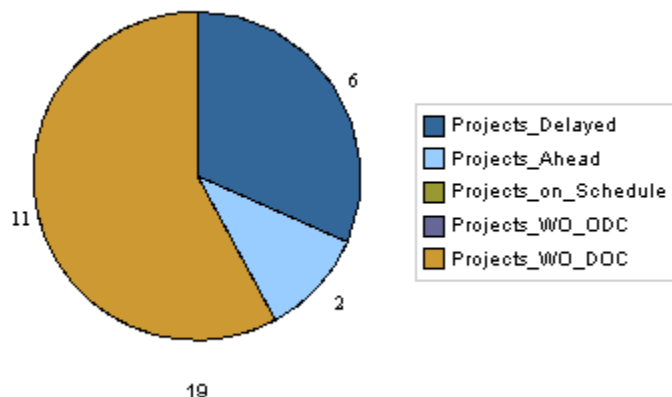

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17902.42 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till February, 2013 is Rs. 8107.64 crore, which is 45.3% of the revised cost of the projects.

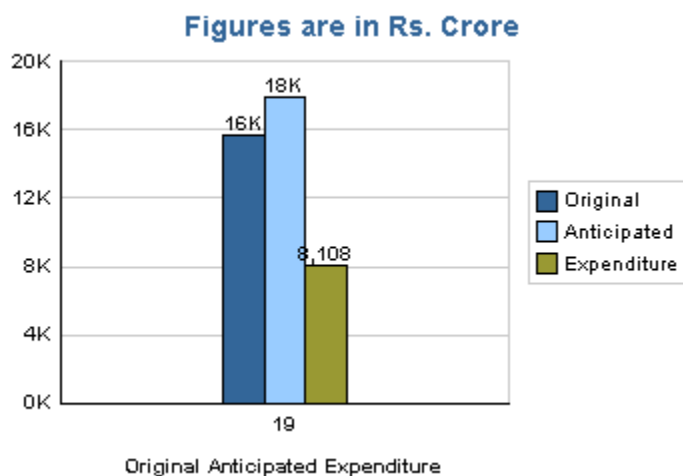

Sector wise current status of projects on the Flash Report

Road Transport & Highways


I. Current Status:

Number of Projects	147
Number of Projects On Schedule	48
Number of Projects Delayed	93

Number of Projects Without Original Date of Commissioning	6
---	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 147 projects, 48 projects are on schedule and 93 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

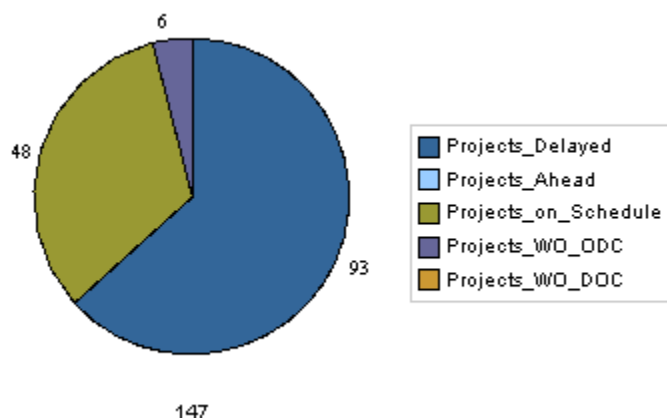

III. Investment Scenario

The Total Original cost of implementation of 147 projects when sanctioned, was of the order of Rs. 96472.1 crore but this was subsequently revised to Rs. 98410.72 crore implying a cost overrun of 2%. The expenditure incurred on these projects till February, 2013 is Rs. 73510.81 crore, which is 74.7% of the revised cost of the projects.

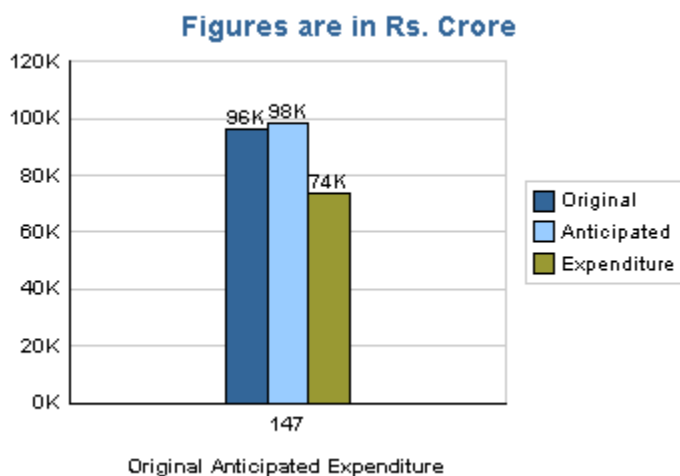

Sector wise current status of projects on the Flash Report

Railways


I. Current Status:

Number of Projects	125
Number of Projects On Schedule	7
Number of Projects Delayed	41

Number of Projects Without Original Date of Commissioning	13
Number of Projects Without Date Of Commissioning	64

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 125 projects, 7 projects are on schedule and 41 projects are delayed .64 projects do not have fixed dates of commissioning.13 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

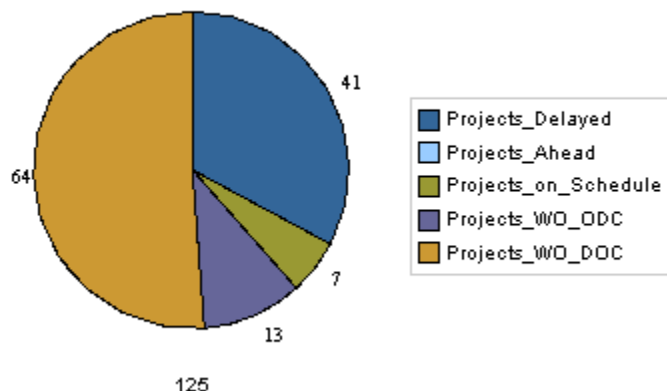

III. Investment Scenario

The Total Original cost of implementation of 125 projects when sanctioned, was of the order of Rs. 61244.63 crore but this was subsequently revised to Rs. 148185.62 crore implying a cost overrun of 142%. The expenditure incurred on these projects till February, 2013 is Rs. 62617.39 crore, which is 42.3% of the revised cost of the projects.

Figures are in Rs. Crore

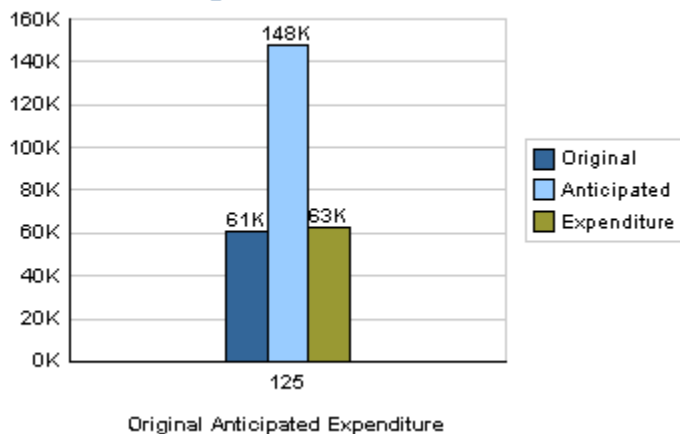

Sector wise current status of projects on the Flash Report

Power


I. Current Status:

Number of Projects	102
Number of Projects On Schedule	45
Number of Projects Delayed	54

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 102 projects, 45 projects are on schedule and 54 projects are delayed .2 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

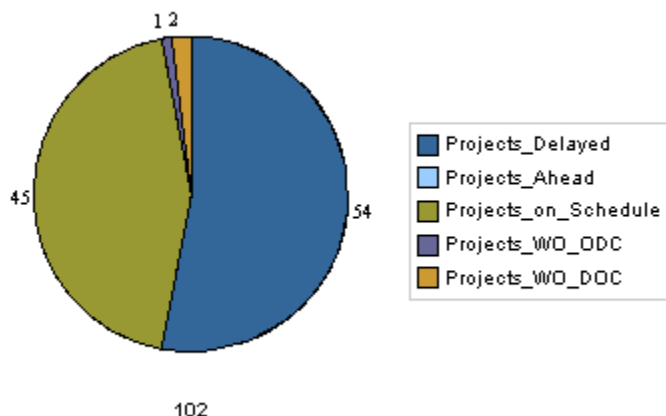

III. Investment Scenario

The Total Original cost of implementation of 102 projects when sanctioned, was of the order of Rs. 241378.89 crore but this was subsequently revised to Rs. 257209.13 crore implying a cost overrun of 6.6%. The expenditure incurred on these projects till February, 2013 is Rs. 116014.86 crore, which is 45.1% of the revised cost of the projects.

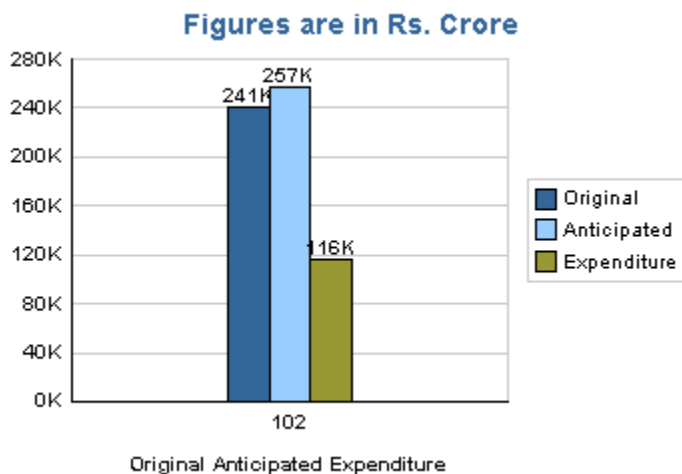

Sector wise current status of projects on the Flash Report

Petroleum


I. Current Status:

Number of Projects	71
Number of Projects On Schedule	21
Number of Projects Delayed	37

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	12

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 71 projects, 21 projects are on schedule and 37 projects are delayed .12 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

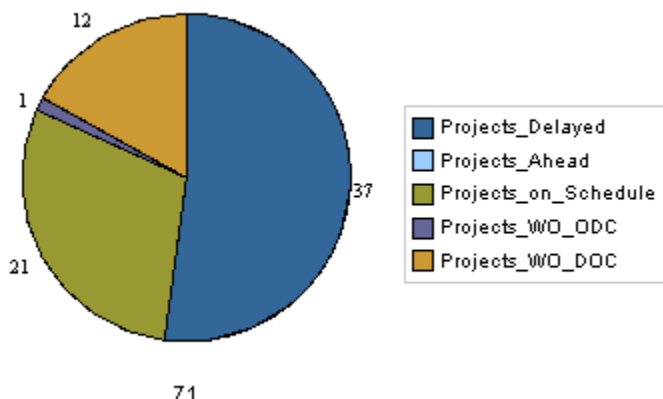

III. Investment Scenario

The Total Original cost of implementation of 71 projects when sanctioned, was of the order of Rs. 169219.44 crore but this was subsequently revised to Rs. 181912.59 crore implying a cost overrun of 7.5%. The expenditure incurred on these projects till February, 2013 is Rs. 71092.1 crore, which is 39.1% of the revised cost of the projects.

Figures are in Rs. Crore

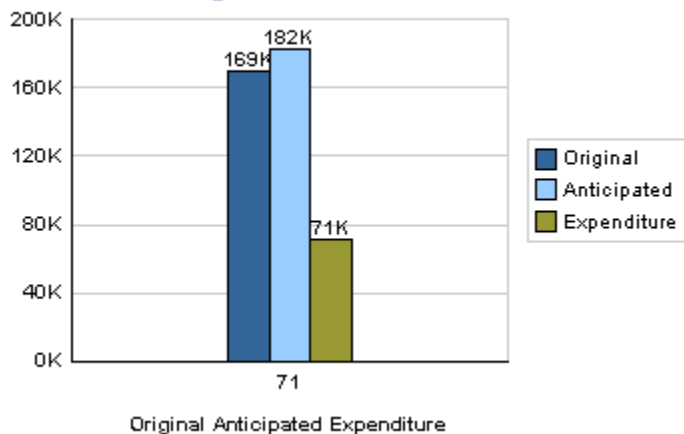

Sector wise current status of projects on the Flash Report

Steel


I. Current Status:

Number of Projects	17
Number of Projects On Schedule	2
Number of Projects Delayed	13

Number of Projects Without Original Date of Commissioning	2
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 2 projects are on schedule and 13 projects are delayed. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

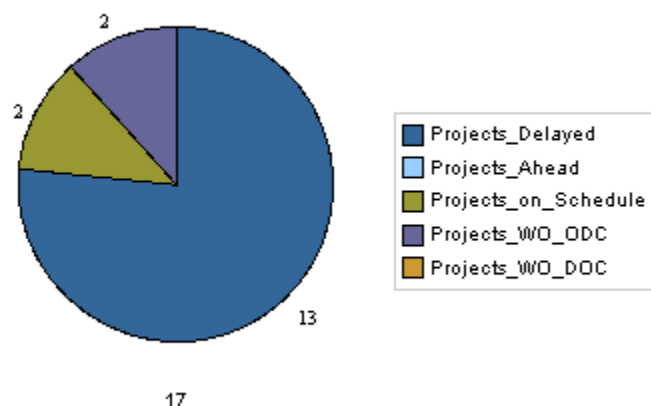

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till February, 2013 is Rs. 47807.33 crore, which is 66.9% of the revised cost of the projects.

Figures are in Rs. Crore

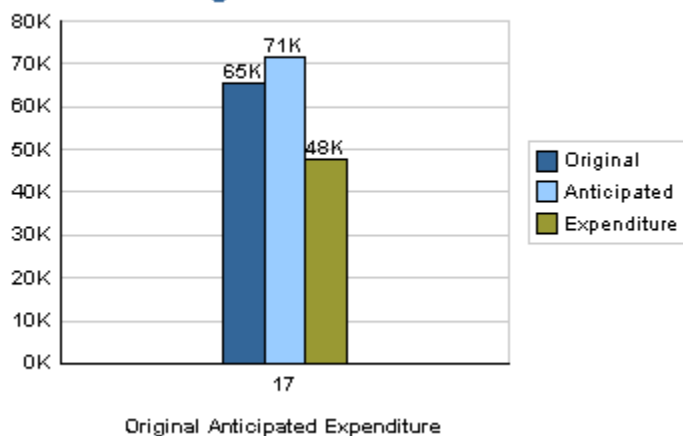

Sector wise current status of projects on the Flash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	24
Number of Projects Delayed	26

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 24 projects are on schedule and 26 projects are delayed .1 project do not have fixed dates of commissioning.

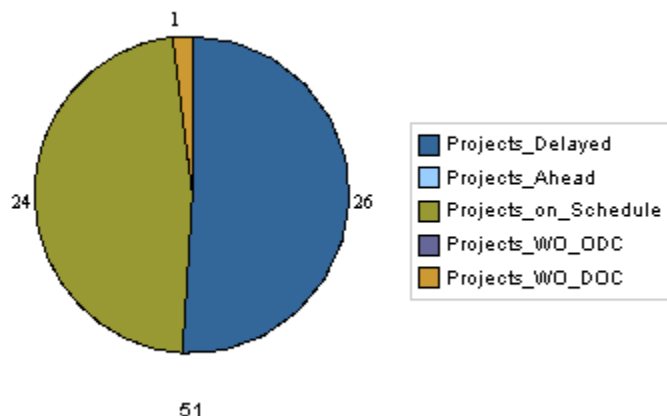

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37510.52 crore implying a cost overrun of 4%. The expenditure incurred on these projects till February, 2013 is Rs. 13866.49 crore, which is 37% of the revised cost of the projects.

Figures are in Rs. Crore

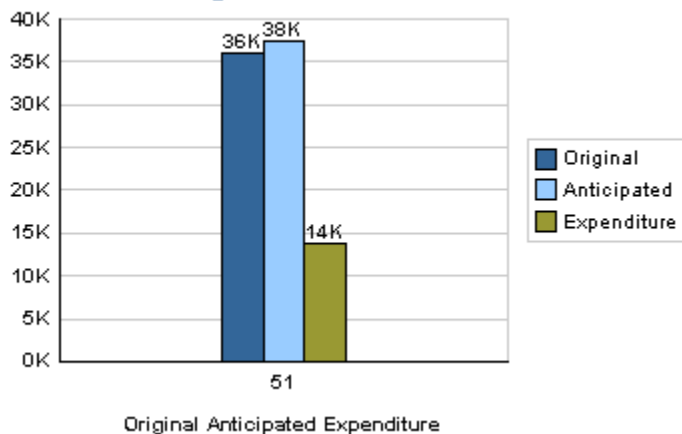

Sector wise current status of projects on the Flash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

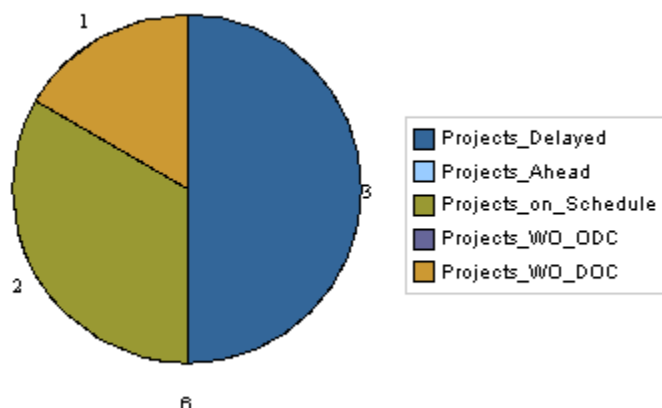

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till February, 2013 is Rs. 4946.52 crore, which is 81.6% of the revised cost of the projects.

Figures are in Rs. Crore

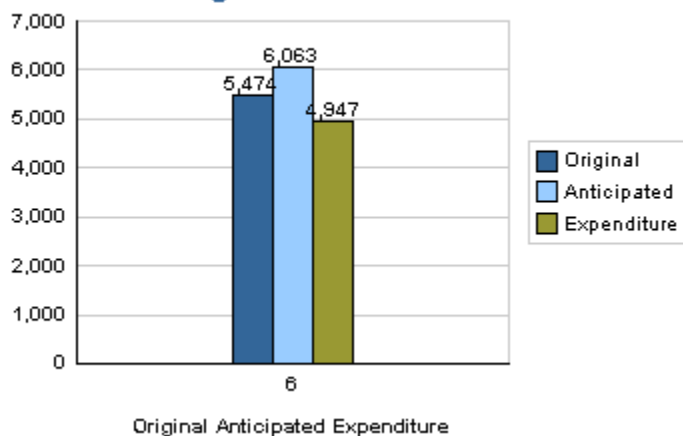

Sector wise current status of projects on the Flash Report


Atomic Energy

I. Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project do not have fixed dates of commissioning.

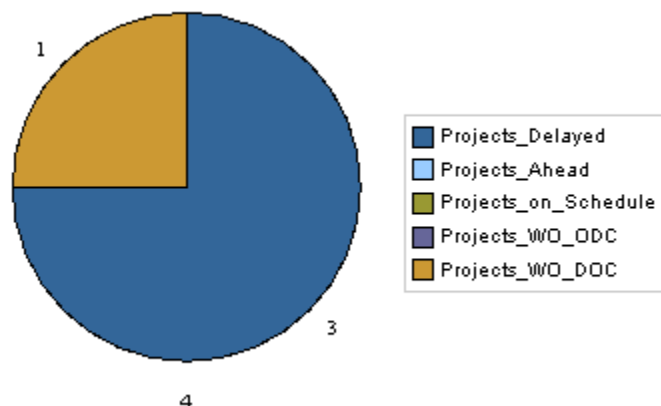

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till February, 2013 is Rs. 23535.33 crore, which is 50.4% of the revised cost of the projects.

Figures are in Rs. Crore

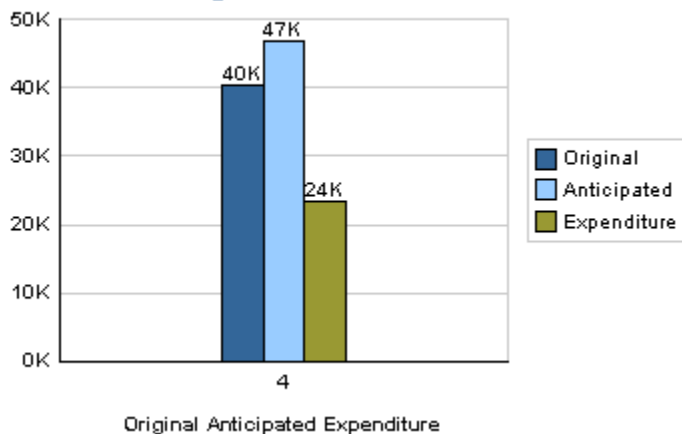

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	35	29990.96	37614.83	22768.80
2	Arunachal Pradesh	4	9512.22	14144.29	9026.68
3	Assam	34	22035.93	35405.41	24534.64
4	Bihar	30	26917.64	34877.43	23981.10
5	Chhatisgarh	25	58429.84	59712.92	17523.36
6	Delhi	4	38214.41	38194.82	1972.56
7	Goa	1	335.61	335.61	190.40
8	Gujarat	22	31111.55	31313.49	11193.62
9	Haryana	8	4054.38	5741.07	6590.41
10	Himachal Pradesh	5	13355.57	17246.69	13435.72
11	Jammu and Kashmir	10	14926.96	34825.56	15439.42
12	Jharkhand	23	14447.40	18492.99	8618.81
13	Karnataka	26	46344.40	55830.82	17683.13
14	Kerala	7	20376.67	21818.22	5432.47
15	Madhya pradesh	22	18978.92	19259.49	9458.90
16	Maharashtra	51	92916.58	107824.36	51649.88
17	Manipur	1	727.56	4444.00	1172.32
18	Meghalaya	2	762.00	762.00	717.34
19	Mizoram	2	1532.97	3307.11	421.86
20	Multi State	109	141561.53	152959.75	65497.63
21	Nagaland	1	850.00	850.00	8.45
22	Odisha	31	57663.96	62099.12	37315.31
23	Punjab	6	3542.01	4483.78	3612.33
24	Rajasthan	14	21115.76	20927.99	7457.06
25	Sikkim	2	1648.94	3690.04	273.77
26	Tamil Nadu	32	48788.07	59567.94	39524.77
27	Tripura	3	1522.39	2018.85	1069.49
28	Uttar Pradesh	22	18455.94	22677.61	12317.07
29	Uttarakhand	5	7624.21	8564.64	2404.17
30	West Bengal	27	42286.11	54396.52	29301.65
TOTAL		564	790030.49	933387.35	440593.12

LIST OF PROJECT MORE THAN COST

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	0.00	15454.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2003	3492.00	0.00	4005.33
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	08/2008	1942.51	0.00	2303.26
4	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	04/2008	825.00	0.00	1249.81
5	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	01/2009	756.00	898.00	915.58
6	CHUTAK HYDRO-ELECTRIC PROJECT	Power	08/2006	621.26	0.00	775.32
7	KOLDAM HEP (NTPC)	Power	10/2002	4527.15	0.00	4793.00
8	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2006	611.01	0.00	829.31
9	RAMPUR HEP(412 MW)	Power	01/2007	2047.03	0.00	2235.18
10	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	1061.38	0.00	1292.14
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	10/2003	768.92	0.00	1662.25
12	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	Power	07/2006	557.24	0.00	598.00
13	TRIPURA GAS BASED POWER PROJECT	Power	07/2009	421.01	0.00	454.21
14	URI H.E.P STAGE -II (NHPC)	Power	08/2005	1729.29	0.00	1903.38
15	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	12/2006	170.00	170.00	396.44
16	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	544.30
17	BHOPAL BINA 3D LINE DOUBLING	Railways	09/2007	687.20	0.00	691.50
18	BILASPUR-URKURA (DL)	Railways	04/1997	151.52	0.00	332.07
19	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	1500.00	2650.10
20	CALICUT-MANGALORE (DL) (SR)	Railways	02/1996	240.00	0.00	600.41
21	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	07/1998	248.44	576.27	939.49
22	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	09/1996	156.00	156.00	308.05

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
23	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	09/2006	343.17	343.17	592.35
24	GADWAL - RAICHUR (NL), SCR	Railways	04/1998	92.63	228.09	272.71
25	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	03/2002	381.17	381.17	611.87
26	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	02/1997	295.00	412.91	574.88
27	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	03/2002	409.00	625.30	835.94
28	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	04/1997	233.00	501.69	679.24
29	JIND-SONEPAT (NL),NR	Railways	01/2004	190.81	238.56	433.79
30	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	727.53	1172.32
31	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	Railways	04/1996	157.00	262.82	279.98
32	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	04/1999	323.40	323.40	495.77
33	KARUR-SALEM(NL),SR	Railways	02/1997	155.55	155.00	762.61
34	KATIHAR - JOGBANI (GC)(NEFR)	Railways	09/2001	100.00	492.98	737.21
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	Railways	04/2000	133.41	207.00	220.09
36	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	345.93
37	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	212.91
38	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	1676.31	1676.31	3367.54
39	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	04/1996	114.01	332.92	413.84
40	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	03/1996	155.74	429.49	635.20
41	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	04/2000	733.00	733.00	1340.39
42	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	598.00
43	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	04/2003	136.62	0.00	242.03
44	RAJATGARH-BARANG(LD),ECOR	Railways	04/1999	166.16	0.00	257.30
45	RANCHI-LOHARDAGA(GC),SER	Railways	04/1997	194.07	194.07	326.81

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
46	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	01/2004	915.70	915.70	1660.03
47	RENIGUNTA-GUNTAKAL(RE)	Railways	06/2000	168.34	0.00	343.36
48	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	09/1995	100.00	100.00	536.30
49	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	03/2000	907.69	3156.32	3363.87
50	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	9001.45
51	2 LANNING OF MOKAMA-MUNGER	Road Transport & Highways	05/2011	351.54	0.00	392.02
52	2-LANNING OF SHILONG BYPASS	Road Transport & Highways	02/2011	226.00	0.00	280.35
53	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	12/2010	1008.50	0.00	1138.00
54	4-LANNING OF CHAPRA-HAJIPUR	Road Transport & Highways	01/2011	575.00	0.00	712.50
55	AMRITSAR-PATHANKOT	Road Transport & Highways	05/2010	705.00	0.00	1252.70
56	Armur to kadloor yellareddy	Road Transport & Highways	02/2010	390.56	0.00	631.65
57	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	12/2003	221.82	0.00	299.96
58	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	03/2005	190.00	0.00	261.42
59	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	12/2003	237.80	0.00	263.14
60	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	12/2003	195.00	0.00	223.86
61	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Road Transport & Highways	12/2003	230.00	0.00	231.64
62	BRAHMPUTRA BRIDGE,NH NO-31	Road Transport & Highways	12/2003	217.61	0.00	248.44
63	Chennai-Tada(Six lane)	Road Transport & Highways	04/2009	353.37	0.00	391.77

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
64	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	05/2009	572.30	0.00	749.58
65	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	04/2007	486.00	0.00	637.97
66	DEVIHALLI-HASSAN	Road Transport & Highways	12/2010	453.00	0.00	460.37
67	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	12/2003	200.00	0.00	241.19
68	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	12/2003	160.00	0.00	194.26
69	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	12/2003	232.45	0.00	283.52
70	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	12/2003	332.94	0.00	435.22
71	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	04/2000	263.27	0.00	272.36
72	Gujarat/Maharashtra BorderSurat-Hazira Port Section	Road Transport & Highways	03/2010	1509.10	0.00	1675.00
73	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	04/2009	1673.70	0.00	2777.00
74	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	12/2003	198.16	0.00	232.80
75	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	12/2003	300.93	0.00	303.02
76	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	03/2005	220.00	0.00	282.68
77	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport & Highways	12/2003	280.00	0.00	292.91
78	Hazaribagh-Ranchi	Road Transport & Highways	08/2010	625.07	0.00	928.03
79	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	09/2010	946.00	0.00	1394.40
80	Hyderabad-Vijaywada Km. 40 to 221.50 Km	Road Transport & Highways	04/2010	1740.00	0.00	1944.20

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
81	INDORE-DEWAS(NH-3)	Road Transport & Highways	11/2010	325.00	0.00	431.34
82	JAIPUR-REENGUS	Road Transport & Highways	08/2010	267.81	0.00	560.96
83	Jaipur-Tonk-Deoli	Road Transport & Highways	06/2010	792.06	0.00	1638.70
84	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	12/2003	355.06	0.00	501.18
85	Kishangarh-Ajmer-Beawer	Road Transport & Highways	11/2009	795.00	0.00	1055.70
86	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	12/2003	275.00	0.00	279.76
87	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	12/2003	240.00	0.00	294.50
88	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport & Highways	09/2010	671.00	0.00	957.76
89	MP/Maharashtra Border-Dhula	Road Transport & Highways	12/2009	835.00	0.00	1068.70
90	MURADABAD-BAREILY	Road Transport & Highways	04/2010	1267.00	0.00	1313.30
91	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	12/2003	264.72	0.00	297.51
92	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	03/2005	168.00	0.00	457.30
93	NALBARI T BIJNI (AS-7)	Road Transport & Highways	12/2003	208.00	0.00	285.37
94	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	12/2003	225.00	0.00	256.56
95	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	12/2003	200.00	0.00	279.47
96	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	03/2005	557.00	0.00	932.27
97	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	12/2003	340.68	0.00	396.58

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
98	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	05/2009	1108.00	0.00	3465.90
99	PANIPAT-ROHTAK	Road Transport & Highways	04/2011	807.00	0.00	995.04
100	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	03/2005	940.00	0.00	1263.20
101	Pune-sholapur, pkg1	Road Transport & Highways	11/2009	1110.00	0.00	1802.10
102	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	12/2003	251.03	0.00	323.83
103	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA)	Road Transport & Highways	12/2003	229.91	0.00	289.95
104	ROHTAK-BAWAL	Road Transport & Highways	05/2011	650.00	0.00	858.06
105	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	12/2003	203.43	0.00	256.53
106	SALEM - U / UNDRUPET (BOT - 1/TN-06) NH -68	Road Transport & Highways	03/2005	941.00	0.00	1901.00
107	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	12/2003	157.47	0.00	223.76
108	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	12/2003	245.00	0.00	491.21
109	Surat- Dahisar (Six Lane) Km 263 to Km 502	Road Transport & Highways	02/2009	1693.75	0.00	2677.40
110	Talegaon-amravati	Road Transport & Highways	11/2009	567.00	0.00	882.40
111	THANJAUR-TRICHY, NH-67 (NHAI)	Road Transport & Highways	03/2005	280.00	0.00	581.49
112	TRICHY - KORUR NH-67	Road Transport & Highways	03/2005	516.00	0.00	760.07
113	Acquisition of Two nos. of 3060 DWT	Shipping & Ports	04/2009	277.03	280.00	294.87
114	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	03/2007	245.67	298.17	371.18

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
115	67.5 MW TG-5 AUX. SYSTEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	07/2007	230.00	0.00	254.51
116	COKE OVEN BATTERY NO. 4 PHASE-II	Steel	08/2007	108.00	0.00	136.95
117	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	Steel	10/2005	8692.00	0.00	10193.53
118	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	0.00	8473.08

List of Projects Ahead of Schedule

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Shipping & Ports</u>						
1	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	433.54	12/2013 10/2013	10/2013
2	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060	2/2011	830.00 -	621.53	-	05/2013 -	03/2013
	Total		1,858.10 -	1,633.76	433.54		
	Grand Total		1,858.10 -	1,633.76	433.54		

List of project Without Original Date of Commissioning

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Steel</u>								
1	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	173.58	- 11/2013	11/2013	0(R3)	17/21
2	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	242.77	- 12/2013	12/2013	0(R3)	15/19
	Total		1,470.55 -	1,470.55	416.35				32/40
	<u>Petroleum</u>								
3	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	381.67	- -	03/2013	-	21/19
	Total		224.00 -	394.00	381.67				21/19
	<u>Power</u>								
4	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	454.21	- -	07/2013	-	6/29
	Total		421.01 -	623.44	454.21				6/29
	<u>Railways</u>								
5	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.50	- -	02/2013	-	0/0
6	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	210.76	- -	03/2013	-	0/0
7	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,379.64	- -	03/2013	-	0/0
8	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	792.25	- -	03/2013	-	0/6
9	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	308.05	- -	06/2013	-	0/0
10	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
11	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	495.77	- -	03/2014	-	0/1
12	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	239.15	- -	03/2014	-	0/0
13	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	2,232.50	1,660.03	- -	03/2014	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	141.55	- -	03/2014	-	0/0
15	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	248.05	- -	03/2015	-	0/0
16	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
17	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	123.57	- -	03/2016	-	0/0
	Total		3,929.05 -	11,014.91	5,960.45				0/7
Road Transport & Highways									
18	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
19	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	957.76	- -	03/2013	-	2/3
20	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	184.63	- -	04/2013	-	2/2
21	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	460.37	- -	06/2013	-	1/1
22	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	425.48	- -	10/2013	-	2/2
23	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	500.43	- -	12/2013	-	0/1
	Total		4,069.00 -	4,069.00	3,923.07				10/12
Grand Total			10,113.61	17,571.90	11,135.75				69/107

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Atomic Energy</u>				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, Tamil Nadu	09/2003	3,492.00	09/2010	-
	Total		3,492.00		
	<u>Civil Aviation</u>				
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI, Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
	Total		1,808.00	02/2012	
	<u>Coal</u>				
3	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, Andhra Pradesh	10/2006	249.03	03/2012	-
	Total		249.03		
	<u>Fertilisers</u>				
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL, Punjab	01/2010	1,478.63	01/2013	01/2013
	Total		1,478.63		
	<u>Petroleum</u>				
5	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29	05/2010	01/2013
6	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00	-	-
7	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68	01/2012	-
8	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18	01/2013	-
9	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, Multi State	08/2009	1,793.00	09/2012	-
10	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00	-	-
11	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32	03/2012	-
12	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	07/2012	-
13	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00	01/2012	-
14	Construction of tanks and blending facility at Vad - [N16000115]IOCL, Gujarat	02/2009	267.00	09/2012	-
15	DBPL-II - [N16000147]GAIL, Multi State	06/2009	486.00	09/2013	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
16	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57	04/2012	-
	Total		30,033.96		
	<u>Power</u>				
17	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26	02/2011	01/2013
			-	10/2012	
18	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	12/2007	-
			1,007.16	12/2009	
	Total		1,217.71		
	<u>Railways</u>				
19	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94	03/1998	08/2005
			604.04	08/2005	
20	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00	06/2007	06/2007
			625.30	-	
21	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00	07/2008	07/2008
			363.26	-	
22	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42	-	05/2009
			369.70	05/2009	
23	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36	-	03/2010
			768.87	03/2010	
24	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTT,West Bengal	03/2000	907.69	12/2006	08/2010
			3,156.32	08/2010	
25	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68	12/2010	12/2010
			293.74	12/2010	
26	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90	06/1999	03/2011
			284.27	03/2011	
27	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00	03/2011	03/2011
			170.00	03/2011	
28	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15	12/2010	03/2011
			1,106.62	03/2011	
29	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	-	02/2012
			-	-	
30	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96	-	02/2012
			1,188.91	12/2009	
31	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51	12/2011	02/2012
			533.38	02/2012	
32	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43	-	03/2012
			495.68	-	
33	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74	02/2009	03/2012
			429.49	-	
34	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24	-	03/2012
			377.32	-	
35	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17	-	03/2012
			381.17	-	
36	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74	-	03/2012
			224.51	-	
37	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09	-	03/2012
			1,417.97	-	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
38	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
39	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
40	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012
41	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
42	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
43	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013
44	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
45	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
46	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
47	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
48	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-
49	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
50	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	-
51	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	-
52	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
53	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	-
54	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
55	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
56	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	-
57	VIRAMGAM-BHILD(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
58	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	-
59	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
60	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
61	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
62	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
63	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
64	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
65	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
66	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
67	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
68	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
69	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
70	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13 727.13	- -	-
71	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-
72	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
73	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
74	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
75	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
76	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
77	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	-
78	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya Pradesh	04/2008	603.04 603.04	03/2012 -	-
79	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	-
80	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	-
81	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
82	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		20,625.75 -		
Shipping & Ports					
83	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
84	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 -	- 01/2009	01/2009
85	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
86	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
87	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
88	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012
89	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
90	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
91	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	-
92	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
93	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	-
	Total		7,345.81 -		
Telecommunications					
94	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012
95	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013
96	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
97	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
98	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
99	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
100	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
101	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	-
	Total		3,699.82 -		
Urban Development					
102	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Water Resources					
103	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
Grand Total			70,607.79		

List of On schedule Projects

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	376.97	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070	2/2011	452.00 -	452.00	65.26	03/2015 -	03/2015
	Total		1,078.00 -	1,078.00	442.23		
	<u>Coal</u>						
3	KRISHNASHILA (NCL) (4MTY) - [N06000007	6/2011	789.88 -	741.62	345.20	03/2013 -	03/2013
4	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	167.29	03/2015 03/2015	03/2015
5	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.86	03/2014 03/2014	03/2014
6	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	122.75	03/2017 -	03/2017
7	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	71.92	03/2015 -	03/2015
8	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
9	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.63 -	479.63	118.39	03/2013 -	03/2013
10	Muraidih UG Turn-key Project - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
11	JALAGAM VENGALA RAO OCP-II - [N06000094	7/2011	447.06 -	447.06	3.02	03/2015 -	03/2015
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
13	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	3.87	03/2018 03/2018	03/2018
14	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
15	KARMA OCP (1.0MTY) - [N06000088	6/2009	162.46 -	162.46	34.89	03/2014 -	03/2014
16	Rajrappa RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	269.01	03/2016 -	03/2016
17	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	95.10	03/2016 -	03/2016
18	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	31.29	03/2015 -	03/2015
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	40.18	03/2016 -	03/2016

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
20	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
21	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
22	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	43.33	03/2016 -	03/2016
23	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]	12/2007	457.77 -	457.77	114.99	03/2013 -	03/2013
24	JALLARAM SHAFT PROJECT - [N06000025]	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	416.83	03/2016 03/2016	03/2016
26	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]	6/2008	1,188.31 -	1,188.31	716.90	03/2013 -	03/2013
	Total		12,481.93 -	12,062.33	2,650.61		
<u>Petroleum</u>							
27	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	4/2008	825.00 -	1,827.00	1,249.81	04/2013 -	04/2013
28	Development of WO-16 Cluster Fields - [N16000105]	6/2010	2,523.00 -	2,523.00	499.77	01/2014 -	01/2014
29	Wax Project - [N16000101]	6/2010	576.60 -	576.60	-	12/2013 -	12/2013
30	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	-	02/2014 -	02/2014
31	Mehesana Redevelopment - [N16000121]	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
32	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,059.63	69.89	03/2015 -	03/2015
33	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
34	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	118.77	05/2014 -	05/2014
35	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline - [N16000153]	4/2011	152.89 -	152.89	-	06/2013 -	06/2013
36	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	-	07/2015 -	07/2015
37	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	21.84	07/2015 -	07/2015
38	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	666.00	-	11/2015 -	11/2015
39	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	40.57	11/2015 -	11/2015
40	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
41	IOR of B-173A Field - [N16000140]	1/2012	352.49 -	352.49	-	03/2014 -	03/2014
42	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	34.37	03/2014 -	03/2014
43	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
44	Mounded Bullet Project at CPCL - [N16000154]	12/2012	279.00 -	279.00	-	12/2014 -	12/2014
45	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	483.04	05/2015 -	05/2015
46	Ankleswar Redevelopment - [N16000122]	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014
47	Ahmedabad Redevelopment - [N16000120]	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014
	Total		39,169.98 -	39,041.72	5,043.80		
<u>Power</u>							
48	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016
49	Northern Region system strengthening scheme-XXII - [N18000091]	12/2010	209.78 -	209.78	114.70	08/2013 -	08/2013
50	Transmission system for phase-I generation projects in orissa-part B - [N18000093]	12/2010	2,743.19 -	2,743.19	1,280.60	12/2013 -	12/2013
51	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]	3/2011	1,585.12 -	1,585.12	727.50	11/2013 -	11/2013
52	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	36.00	08/2017 -	08/2017
53	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	722.00	05/2017 -	05/2017
54	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	172.80	02/2015 -	02/2015
55	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	69.10	01/2014 -	01/2014
56	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	180.50	01/2015 -	01/2015
57	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	67.40	08/2014 -	08/2014
58	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	63.80	08/2014 -	08/2014
59	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	161.70	02/2014 -	02/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
60	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	173.80	08/2014 -	08/2014
61	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	480.50	07/2014 -	07/2014
62	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	468.90	08/2014 -	08/2014
63	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	330.80	10/2014 -	10/2014
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	81.70	11/2014 -	11/2014
65	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	139.80	08/2014 -	08/2014
66	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	33.90	06/2014 -	06/2014
67	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	499.60	06/2015 -	06/2015
68	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
69	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
70	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	85.40	10/2014 -	10/2014
71	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	10.60	08/2014 -	08/2014
72	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	-	10/2014 -	10/2014
73	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
74	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]	9/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
76	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	158.00	08/2015 -	08/2015
77	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,243.00	11/2016 -	11/2016
78	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	692.00	09/2016 -	09/2016

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	1,258.00	12/2016 -	12/2016
80	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID [N18000130	6/2012	1,263.26 -	1,263.26	183.60	11/2014 -	11/2014
81	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	107.00	06/2014 -	06/2014
82	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107	8/2011	1,391.97 -	1,391.97	775.10	12/2013 -	12/2013
83	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED [N18000106	8/2011	425.51 -	425.51	229.20	10/2013 -	10/2013
84	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	461.50	12/2013 -	12/2013
85	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104	10/2011	558.26 -	558.26	113.50	11/2013 -	11/2013
86	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103	9/2011	1,940.13 -	1,940.13	609.90	09/2014 -	09/2014
87	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102	7/2011	181.93 -	181.93	65.40	07/2013 -	07/2013
88	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	638.30	05/2014 -	05/2014
89	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096	3/2011	2,569.25 -	2,569.25	1,180.80	03/2014 -	03/2014
90	Establishment of pooling stations at Raigarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	858.50	08/2013 -	08/2013
91	Transmission system associated with krishnapatnam- Part-A - [N18000090	12/2010	779.21 -	779.21	741.50	08/2013 -	08/2013
92	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077	4/2010	4,404.57 -	4,404.57	361.10	01/2015 -	01/2015
	Total		106,253.76 -	106,253.76	15,577.50		
Railways							
93	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	7/1996	653.84 654.51	1,302.12	608.97	06/2013 06/2013	06/2013
94	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112	4/2008	829.74 -	829.74	16.23	03/2015 -	03/2015
95	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) [N22000114	4/2008	516.23 -	516.23	337.94	03/2014 -	03/2014
96	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) [N22000113	4/2008	653.19 -	653.46	228.10	03/2014 -	03/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
97	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02	2,619.02	260.58	03/2016	03/2016
98	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]	4/2010	2,069.60	2,069.60	22.86	03/2014	03/2014
99	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98	3,951.98	93.62	03/2016	03/2016
	Total		11,293.60	11,942.15	1,568.30		
Road Transport & Highways							
100	Indore-Jhabua-Gujrat/MP - [N24000136]	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013
101	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]	11/2010	1,585.00	1,585.00	957.76	05/2013	05/2013
102	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00	807.00	995.04	10/2014	10/2014
103	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]	12/2010	1,008.50	1,008.50	1,138.00	06/2013	06/2013
104	ROHTAK-BAWAL - [N24000169]	5/2011	650.00	650.00	858.06	11/2013	11/2013
105	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19	484.19	34.07	10/2014	10/2014
106	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16	702.16	299.08	07/2014	07/2014
107	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36	291.36	47.45	01/2014	01/2014
108	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18	1,396.18	529.67	09/2014	09/2014
109	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]	12/2011	1,047.00	1,047.00	201.61	06/2014	06/2014
110	4-laning of Raiganj-Dalkola - [N24000204]	2/2011	580.43	580.43	218.49	08/2013	08/2013
111	4-laning of Brahampore-Faraka - [N24000203]	2/2011	998.79	998.79	725.68	08/2013	08/2013
112	4-laning of Faraka-Raiganj - [N24000202]	2/2011	1,078.84	1,078.84	919.85	08/2013	08/2013
113	BAREILY-SITAPUR - [N24000200]	3/2011	1,046.00	1,046.00	266.89	09/2013	09/2013
114	PANVEL-INDAPUR - [N24000216]	12/2011	942.69	942.69	128.49	06/2014	06/2014
115	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00	1,479.00	156.85	06/2015	06/2015
116	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]	4/2012	624.00	624.00	120.14	04/2014	04/2014
117	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40	356.40	-	07/2014	07/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	839.93	06/2014 -	06/2014
119	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	152.77	09/2014 -	09/2014
120	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
121	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	450.94	08/2013 -	08/2013
122	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.56	01/2014 -	01/2014
123	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	122.65	01/2014 -	01/2014
124	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	311.92	02/2014 -	02/2014
125	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	436.99	01/2014 -	01/2014
126	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
127	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	300.48	08/2013 -	08/2013
128	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	98.06	05/2013 -	05/2013
129	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
130	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.82	06/2013 -	06/2013
131	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	14.58	12/2013 -	12/2013
132	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
133	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,039.20	08/2013 -	08/2013
134	2laning with PS Gopalganj- Chappra - [N24000190	12/2011	325.00 -	325.00	160.02	05/2014 -	05/2014
135	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
136	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	275.47	11/2013 -	11/2013
137	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	712.50	07/2013 -	07/2013
138	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	45.59	04/2014 -	04/2014
139	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	516.26	03/2014 -	03/2014
140	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	742.93	03/2014 -	03/2014
142	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	280.35	02/2014 -	02/2014
143	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	710.10	08/2013 -	08/2013
144	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,313.30	06/2013 -	06/2013
145	DEOLI-KOTA - [N24000148	1/2011	593.00 -	593.00	465.75	07/2013 -	07/2013
146	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	882.40	11/2013 -	11/2013
147	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4 [N24000139	9/2010	1,655.00 -	1,655.00	485.07	09/2013 -	09/2013
	Total		42,220.20 -	42,220.20	20,342.76		
	<u>Steel</u>						
148	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	22.45	08/2014 -	08/2014
149	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	2.88	12/2014 -	12/2014
	Total		587.55 -	587.55	25.33		
	<u>Urban Development</u>						
150	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	1,788.69	03/2016 -	03/2016
151	FARIDABAD EXTENSION - [N28000057	9/2011	2,494.00 -	2,494.00	183.87	09/2014 -	09/2014
	Total		37,736.00 -	37,736.00	1,972.56		
	Grand Total		250,821.02	250,921.71	47,623.09		

List of Delay Project

(Feb,2013)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	15,454.00	12/2008 -	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,432.00	12/2015 -	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,644.00	12/2016 -	03/2017	3	-
Total			36,950.00 -	41,049.00	19,530.00				
<u>Civil Aviation</u>									
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,303.26	05/2011 -	03/2013	22	-
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	190.40	05/2012 -	06/2013	13	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	214.03	01/2011 04/2013	12/2013	35	8
Total			2,587.58 -	2,970.07	2,707.69				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,611.71	06/2009 -	09/2013	51	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	109.03	03/2010 -	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	143.89	03/2011 -	03/2014	36	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	3,838.87	03/2012 -	03/2014	24	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	101.39	03/2012 -	03/2014	24	-
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	455.09	03/2013 09/2012	07/2014	16	22
13	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya Pradesh	10/2007	259.40 -	259.40	3.28	03/2012 -	03/2015	36	-
14	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	119.64	03/2010 -	03/2015	60	-
15	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	134.00	03/2012 -	03/2015	36	-
16	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.77	03/2012 -	03/2015	36	-
17	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	91.35	03/2013 -	03/2015	24	-
18	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,407.50	03/2014 -	03/2016	24	-
19	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,262.91	03/2014 -	03/2016	24	-
20	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44	-
21	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	265.47	03/2014 -	03/2016	24	-
22	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	82.44	12/2012 -	03/2016	39	-
23	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.39	03/2014 -	03/2016	24	-
24	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.88	03/2014 -	03/2016	24	-
25	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
26	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, Chhatisgarh	12/2009	321.42	321.50	205.44	03/2014	03/2016	24	-
27	Churi Benti UG (0.81 MTY) - [N06000083]CCL, Jharkhand	08/2007	163.51	163.51	34.88	03/2011	03/2016	60	-
28	Tapin OCP (2.5 MTY) - [N06000086]CCL, Jharkhand	08/2008	264.68	264.68	126.53	03/2012	03/2016	48	-
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, West Bengal	11/2006	287.18	287.17	0.82	03/2011	03/2017	72	-
30	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL, Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24	-
31	North Urimari OCP (3.0 MTY) - [N06000084]CCL, Jharkhand	12/2007	179.87	179.87	60.74	03/2012	03/2017	60	-
32	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC, Tamil Nadu	06/2011	5,907.11	5,907.11	26.99	12/2015	08/2017	20	-
Total			23,325.50	25,199.16	11,166.24				
Steel									
33	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00	350.00	251.98	08/2010	02/2013	30	-
34	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00	12,291.00	10,193.53	10/2009	03/2013	41	-
35	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00	343.58	254.51	02/2011	03/2013	25	-
36	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	347.44	12/2011 03/2012	06/2013	18	15
37	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00	216.68	136.95	10/2012	06/2013	8	-
38	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	14,280.71	12/2011	06/2013	18	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
39	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	234.56	05/2012 -	06/2013	13	-
40	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,314.41	12/2011 -	06/2013	18	-
41	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 11,812.00	11,812.00	8,862.42	03/2013 -	12/2013	9	-
42	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,420.06	12/2012 -	12/2013	12	-
43	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	57.69	10/2013 -	12/2013	2	-
44	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhattisgarh	09/2008	17,265.00 -	17,265.00	7,995.11	03/2013 -	03/2014	12	-
45	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	16.28	11/2013 -	03/2014	4	-
	Total		63,227.77 -	69,385.31	47,365.65				
Petrochemicals									
46	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	6,229.56	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	6,229.56				
Petroleum									
47	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Odisha	12/2009	1,492.33 -	1,492.33	1,219.50	06/2012 -	03/2013	9	-
48	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	279.73	04/2011 -	02/2013	22	-
49	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	03/2013	84	0
50	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,185.52	05/2010 03/2013	03/2013	34	0

(Feb,2013)

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
51	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,488.99	09/2011 03/2012	03/2013	18	12
52	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24	22
53	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
54	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
55	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	165.28	02/2013 -	04/2013	2	-
56	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	155.49	03/2013 -	04/2013	1	-
57	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	631.71	03/2010 03/2012	05/2013	38	14
58	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34	12
59	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	165.66	08/2012 -	05/2013	9	-
60	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.01	04/2006 06/2012	06/2013	86	12
61	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,302.79	09/2011 05/2012	06/2013	21	13
62	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,483.80	06/2012 -	06/2013	12	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
63	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	211.00	04/2012 -	06/2013	14	-
64	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	683.37	12/2011 -	07/2013	19	-
65	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	422.00	01/2013 -	08/2013	7	-
66	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,067.86	09/2012 -	09/2013	12	-
67	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	69.30	09/2012 -	09/2013	12	-
68	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	-	07/2012 -	10/2013	15	-
69	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	96.19	11/2012 -	10/2013	11	-
70	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	30,426.00	20,426.00	11/2012 -	11/2013	12	-
71	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
72	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	97.69	05/2013 -	11/2013	6	-
73	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,184.58	08/2010 03/2012	12/2013	40	21
74	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.88	09/2011 -	12/2013	27	-
75	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	27.13	08/2013 -	01/2014	5	-
76	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84	0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
77	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	1,353.63	03/2013	03/2014	12	-
78	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	678.02	-	06/2012	03/2014	21	-
79	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	932.51	03/2013	04/2014	13	-
80	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	-	10/2010	12/2014	50	-
81	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	-	12/2012	12/2014	24	-
82	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00	14,225.00	226.44	12/2015	05/2016	5	-
83	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120	0
	Total		99,791.50	110,271.25	58,825.70				
	Power								
84	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,662.25	03/2007 09/2012	03/2013	72	6
85	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,845.21	09/2008	03/2013	54	-
86	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24	758.75	598.00	01/2010	03/2013	38	-
87	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	426.00	09/2010	03/2013	30	-
88	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,818.00	08/2012	03/2013	7	-
89	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	337.73	07/2011	03/2013	20	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
90	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	4,204.00	10/2012 -	03/2013	5	-
91	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	169.80	04/2012 -	03/2013	11	-
92	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	63.60	10/2012 -	03/2013	5	-
93	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,903.38	11/2009 02/2013	05/2013	42	3
94	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,165.70	02/2012 -	05/2013	15	-
95	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	871.40	10/2009 -	06/2013	44	-
96	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	829.31	08/2010 01/2013	06/2013	34	5
97	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,246.60	12/2012 -	06/2013	6	-
98	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,110.50	06/2012 -	06/2013	12	-
99	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	135.68	06/2012 -	06/2013	12	-
100	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	874.20	03/2013 -	06/2013	3	-
101	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	155.80	11/2011 -	09/2013	22	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
102	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	729.10	05/2012 -	09/2013	16	-
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	89.60	01/2013 -	09/2013	8	-
104	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	72.10	04/2013 -	09/2013	5	-
105	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,012.00	10/2012 -	11/2013	13	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	339.00	11/2011 -	12/2013	25	-
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	348.20	11/2011 -	12/2013	25	-
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	251.00	02/2012 -	12/2013	22	-
109	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,249.40	10/2012 -	12/2013	14	-
110	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	2,011.70	08/2012 -	12/2013	16	-
111	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,178.20	12/2012 -	12/2013	12	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
112	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	518.80	11/2012 -	12/2013	13	-
113	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,601.90	08/2012 -	01/2014	17	-
114	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,235.18	01/2012 -	02/2014	25	-
115	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38 -	1,501.75	1,292.14	09/2009 06/2013	03/2014	54	9
116	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC, Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,029.68	10/2010 01/2013	03/2014	41	14
117	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,112.00	11/2012 -	03/2014	16	-
118	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	831.80	08/2012 -	03/2014	19	-
119	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	238.20	07/2013 -	03/2014	8	-
120	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	715.40	04/2013 -	03/2014	11	-
121	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	61.30	01/2013 -	03/2014	14	-
122	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	543.70	11/2012 -	03/2014	16	-
123	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pradesh	10/2002	4,527.15 -	6,358.91	4,793.00	04/2009 -	09/2014	65	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
124	PARE HYDRO ELECTRIC PROJECT (110 MW) - [N18000045]NEEPCO, Arunachal Pradesh	12/2008	573.99 -	573.99	485.51	08/2012 08/2013	09/2014	25	13
125	BARH STPP STAGE -II - [N18000047]NTPC, Bihar	02/2008	7,341.04 -	7,341.04	5,105.00	08/2013 -	09/2014	13	-
126	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19 -	11,130.19	5,518.40	08/2013 -	09/2014	13	-
127	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, Mizoram	01/2011	913.63 -	913.63	389.14	07/2014 -	02/2015	7	-
128	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL, Multi State	09/2012	524.40 -	524.40	14.90	04/2015 -	05/2015	1	-
129	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, Assam	01/2008	4,375.35 -	4,375.35	3,580.00	07/2011 -	10/2015	51	-
130	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttarakhand	11/2006	2,978.48 -	2,978.48	1,704.00	03/2013 -	03/2016	36	-
131	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttarakhand	08/2008	2,491.58 -	3,422.44	339.11	07/2014 -	05/2016	22	-
132	TEHRI PUMPED STORAGE PLANT (1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00 2,978.88	2,978.86	446.79	07/2010 02/2016	11/2016	76	9
133	KISHANGANGA HEP - [N18000031]NHPC, Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,095.31	01/2016 01/2016	11/2016	10	10
134	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97 -	8,693.00	7,975.00	12/2009 -	02/2017	86	-
135	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pradesh	12/2004	2,496.90 -	2,496.90	2,176.62	05/2013 06/2016	03/2017	46	9
136	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,056.50	09/2010 08/2014	12/2017	87	40
137	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,779.86	09/2009 07/2014	03/2018	102	44

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
	Total		133,486.41	148,411.77	98,336.70				
	Railways								
138	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	939.49	12/2012 01/2013	02/2013	2	1
139	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	272.71	02/2011 02/2011	02/2013	24	24
140	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	471.60	12/2012 12/2012	02/2013	2	2
141	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	64.92	03/2012 -	02/2013	11	-
142	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-
143	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	212.91	03/2002 -	03/2013	132	-
144	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	663.17	12/2011 12/2011	03/2013	15	15
145	KADUR-CHIKMAGALUR-SAKLLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	279.98	03/2012 03/2012	03/2013	12	12
146	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	281.81	03/2012 03/2013	03/2013	12	0
147	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	413.84	03/2012 03/2013	03/2013	12	0
148	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	243.40	257.30	02/2009 02/2009	04/2013	50	50
149	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	225.00	220.09	03/2009 03/2009	04/2013	49	49
150	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	548.65	03/1994 -	10/2013	235	-
151	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	366.38	12/2009 03/2011	10/2013	46	31
152	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	120.59	12/2011 11/2013	11/2013	23	0

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9		
153	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	224.89	141.55	03/2012 -	12/2013	21	-	
154	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	157.96	12/2012 -	12/2013	12	-	
155	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	226.08	03/2004 12/2010	03/2014	120	39	
156	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,340.39	12/2008 -	03/2014	63	-	
157	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	220.91	06/2013 06/2013	03/2014	9	9	
158	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	434.58	03/2013 -	03/2014	12	-	
159	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	116.99	02/2006 -	06/2014	100	-	
160	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	204.65	12/2008 -	09/2014	69	-	
161	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	940.76	03/2009 12/2012	12/2014	69	24	
162	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.33	03/2007 03/2007	03/2015	96	96	
163	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	737.21	12/2010 12/2010	03/2015	51	51	
164	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	116.67	12/2012 -	03/2015	27	-	
165	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,367.54	03/2009 -	03/2015	72	-	
166	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	5,016.00	2,650.10	04/2008 03/2014	12/2015	92	21	

(Feb,2013)

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
167	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,649.50	10/2007 12/2012	12/2015	98		36
168	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	249.36	02/2010 11/2012	12/2015	70		37
169	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	449.62	03/2014 -	12/2015	21		-
170	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	1,008.73	03/2014 03/2016	03/2016	24		0
171	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	468.58	03/2005 12/2008	06/2016	135		90
172	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	434.55	06/2005 07/2011	06/2016	132		59
173	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	33.27	03/2016 -	06/2016	3		-
174	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	1,172.32	03/2011 03/2014	03/2017	72		36
175	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	32.72	04/2014 -	03/2017	35		-
176	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017	15		-
177	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24		-
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	9,001.45	03/2001 -	12/2017	201		-
Total			25,396.23 -	71,545.31	31,069.72					
Road Transport & Highways										
179	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	223.76	09/2007 -	03/2013	66		-
180	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	191.57	08/2004 07/2010	03/2013	103		32

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
181	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	190.77	08/2004 -	03/2013	103	-
182	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	156.85	04/2004 -	03/2013	107	-
183	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	282.68	09/2007 -	03/2013	66	-
184	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	137.88	09/2008 -	03/2013	54	-
185	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	193.10	164.10	03/2008 -	03/2013	60	-
186	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	267.88	05/2008 -	03/2013	58	-
187	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.50	10/2008 -	03/2013	53	-
188	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	396.58	03/2008 -	03/2013	60	-
189	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHA) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	256.53	10/2008 -	03/2013	53	-
190	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	289.95	10/2008 -	03/2013	53	-
191	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	189.77	07/2008 -	03/2013	56	-
192	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	299.96	11/2008 -	03/2013	52	-
193	GANJAM-ICCHAPURUM,NH-5(NHA) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	272.36	02/2004 -	03/2013	109	-

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9		
194	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	03/2013	41	-	
195	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	03/2013	109	-	
196	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	637.97	05/2010 -	03/2013	34	-	
197	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	03/2013	6	-	
198	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	03/2013	9	-	
199	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,944.20	10/2012 -	03/2013	5	-	
200	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	03/2013	13	-	
201	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	268.59	06/2011 06/2011	04/2013	22	22	
202	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	04/2013	46	-	
203	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	792.06	1,638.70	12/2012 -	04/2013	4	-	
204	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	435.22	09/2008 -	05/2013	56	-	
205	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	297.51	06/2008 -	05/2013	59	-	
206	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	241.19	06/2008 -	05/2013	59	-	
207	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	05/2013	28	-	
208	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	323.83	10/2008 -	06/2013	56	-	

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
209	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	06/2013	63	-
210	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54	-
211	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	501.18	09/2009 -	06/2013	45	-
212	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	1,263.20	07/2012 -	06/2013	11	-
213	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	795.00	1,055.70	05/2012 -	06/2013	13	-
214	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,677.40	08/2011 -	06/2013	22	-
215	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	749.58	10/2011 -	06/2013	20	-
216	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	625.07	928.03	01/2013 -	06/2013	5	-
217	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	1,252.70	11/2012 -	06/2013	7	-
218	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	495.37	12/2009 -	07/2013	43	-
219	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	852.00	784.25	03/2013 -	07/2013	4	-
220	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81 -	267.81	560.96	02/2013 -	07/2013	5	-
221	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	08/2013	21	-
222	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	250.39	279.76	10/2008 -	09/2013	59	-
223	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	279.47	06/2008 -	09/2013	63	-
224	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	256.56	06/2008 -	09/2013	63	-
225	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	09/2013	38	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
226	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-
227	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	671.30	600.33	02/2013 -	10/2013	8	-
228	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	209.00	8.04	01/2013 -	10/2013	9	-
229	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	190.00	261.42	01/2009 -	12/2013	59	-
230	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	194.26	05/2008 -	12/2013	67	-
231	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60 -	407.60	186.29	06/2010 -	12/2013	42	-
232	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
233	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,777.00	10/2011 -	12/2013	26	-
234	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	805.39	451.09	03/2013 -	12/2013	9	-
235	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	283.52	09/2010 -	01/2014	40	-
236	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	431.34	05/2013 -	02/2014	9	-
237	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	231.64	06/2005 -	03/2014	105	-
238	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	223.86	06/2008 -	03/2014	69	-
239	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	263.14	06/2008 -	03/2014	69	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
240	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	171.49	04/2008 -	03/2014	71	-
241	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	232.80	04/2008 -	03/2014	71	-
242	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	204.17	09/2007 -	03/2014	78	-
243	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	391.77	10/2011 -	03/2014	29	-
244	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	193.45	41.09	11/2012 -	03/2014	16	-
245	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	392.02	05/2013 -	03/2014	10	-
246	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	510.99	03/2013 -	03/2014	12	-
247	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, Uttarakhand	11/2011	478.00 -	478.00	245.01	10/2013 -	03/2014	5	-
248	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, Kerala	04/2011	682.00 -	682.00	-	10/2013 -	03/2014	5	-
249	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	43.31	09/2007 -	04/2014	79	-
250	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	1,724.55	1,112.80	03/2013 -	04/2014	13	-
251	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	359.69	02/2014 -	04/2014	2	-
252	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	292.91	02/2009 03/2014	05/2014	63	2
253	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	285.37	04/2008 -	05/2014	73	-
254	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	107.64	07/2009 -	05/2014	58	-

(Feb,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
255	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	175.59	10/2008 -	06/2014	68	-
256	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	105.66	11/2008 -	06/2014	67	-
257	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
258	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	515.07	07/2013 -	06/2014	11	-
259	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53	-
260	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	37.94	09/2013 -	07/2014	10	-
261	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	-	07/2012 -	07/2014	24	-
262	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
263	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	248.44	04/2010 -	11/2014	55	-
264	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	73.96	04/2009 -	12/2014	68	-
265	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	34.01	11/2008 -	12/2014	73	-
266	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	131.41	04/2009 -	12/2014	68	-
267	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	932.27	02/2010 -	12/2014	58	-
268	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
269	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	1,626.70	08/2014	07/2015	11	-
270	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11	-
271	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, Jammu and Kashmir	07/2010	1,987.00	1,987.00	670.55	07/2015	06/2016	11	-
Total			50,182.90	52,121.52	49,244.98				
<u>Shipping & Ports</u>									
272	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24	-
273	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00	4,150.00	3,651.10	01/2012	03/2013	14	6
274	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00	600.00	137.00	03/2006	06/2013	87	0
275	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP., Multi State	07/2011	220.49	220.49	98.31	01/2013	06/2013	5	-
276	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP., Mahara shtra	08/2010	612.72	532.83	364.52	12/2012	10/2013	10	10
277	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00	1,460.00	927.92	12/2010	12/2013	36	15
Total			6,413.21	7,718.82	5,397.85				
<u>Telecommunications</u>									
278	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00	229.41	-	02/2007	02/2013	72	11

(Feb,2013)

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9		
279	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL, Delhi	02/2006	229.41	229.41	-	03/2012	02/2013	11	-	
280	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttarakhand	01/2009	149.15	158.72	80.05	06/2009	03/2013	45	-	
281	GSM equipment of 1625000 Lines (2G) 325000 lines 3(- [N26000090]BSNL, Madhya Pradesh	11/2009	916.70	916.70	823.48	11/2010	03/2013	28	-	
282	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81	336.81	157.98	01/2009	06/2013	53	-	
283	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL, Multi State	07/2010	1,148.19	964.37	170.25	05/2011	06/2013	25	-	
284	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00	384.00	29.45	10/2010	09/2013	35	-	
Total			3,413.26	3,219.42	1,261.21					
<u>Urban Development</u>										
285	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00	11,609.00	8,473.08	06/2011	03/2013	21	-	
Total			6,395.00	11,609.00	8,473.08					
Grand Total			456,629.97	552,420.63	339,608.38					

List of Projects Without Milestones

(Feb,2013)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Civil Aviation</u>						
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	06/2013	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	12/2013	0/0
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	03/2015 -	03/2015	0/0
	Total		5,473.58 -			0/0
<u>Coal</u>						
7	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	04/2014 -	04/2014	0/0
8	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
	Total		1,570.15 -			0/0
<u>Steel</u>						
9	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	08/2014 -	08/2014	0/0
10	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	12/2014 -	12/2014	0/0
	Total		587.55 -			0/0
<u>Petroleum</u>						
11	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
12	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	07/2015 -	07/2015	0/0
13	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	01/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
14	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	02/2013	0/0
15	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
16	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	03/2013	0/0
17	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	03/2013	0/0
18	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
20	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
21	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
22	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
23	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	05/2013	0/0
24	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
25	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
26	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	04/2012 -	06/2013	0/0
27	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013	0/0
28	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	07/2013	0/0
29	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
30	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
31	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
32	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	11/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
34	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2013	0/0
36	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0
37	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
38	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
39	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
40	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
41	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	03/2014	0/0
42	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	03/2014	0/0
43	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	03/2013 -	04/2014	0/0
44	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
45	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
46	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
47	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
48	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
49	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
50	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
51	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	12/2014 -	12/2014	0/0
52	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
53	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
54	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
55	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
56	I REP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
57	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	-	0/0
58	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
59	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 -	-	0/0
60	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	-	0/0
61	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	-	0/0
	Total		109,103.18 -			0/0
Power						
62	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	03/2013	0/0
63	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
64	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	03/2014	0/0
65	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
66	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
67	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
68	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	10/2014 -	10/2014	0/0
69	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
71	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	11/2014 -	11/2014	0/0
72	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	12/2014	0/0
73	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	03/2015 -	03/2015	0/0
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	04/2015 -	05/2015	0/0
76	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	06/2016 -	06/2016	0/0
77	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	08/2017 -	08/2017	0/0
	Total		14,290.40 -			0/0
Railways						
78	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
79	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
80	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
81	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
82	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
83	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTPL,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
84	Pandabeswar-Chinrai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
85	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
86	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
87	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
88	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
89	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
90	Dakshin-barasat-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
91	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
92	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
93	MUNEERABAD-MAHABOONNAGAR(NL), SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
94	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
95	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
96	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
97	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
98	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
99	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
100	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
101	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
102	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
103	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	02/2013	0/0
104	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
105	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
106	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
107	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
108	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
109	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	03/2013	0/0
110	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
111	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
112	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
113	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
114	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
115	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
116	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
117	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
118	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2013	06/2013	0/0
119	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	06/2013	0/0
120	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
121	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
122	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
123	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
124	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 -	12/2013	0/0
125	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
126	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
127	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
128	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
129	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
130	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
131	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
132	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
133	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 -	03/2014	0/0
134	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
135	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
136	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	06/2014	0/0
137	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
138	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
139	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
140	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
141	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
142	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
143	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
144	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0
145	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	03/2015	0/0
146	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
147	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
148	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 11/2012	12/2015	0/0
149	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
150	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2016	0/0
151	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
152	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
153	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
154	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
155	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
156	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
157	JIRIBAM TO IMPHAL (TUPU)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
158	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 619.34	04/2014 -	03/2017	0/0
159	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
160	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
161	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
162	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
163	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
164	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	- -	-	0/0
165	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
166	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Odisha	04/1996	301.64 -	- 09/2009	-	0/0
167	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-	0/0
168	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	- 03/2009	-	0/0
169	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Odisha	04/1998	183.23 -	02/2015 -	-	0/0
170	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
171	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 380.00	03/2009 11/2012	-	0/0
172	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
173	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
174	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20 -	03/2010 -	-	0/0
175	VIRAMGAM-BHILD(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
176	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 1,010.00	- -	-	0/0
177	NANGALDAM-TALWARA(NL), NR - [220100188]NR, Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
178	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1997	227.00 997.58	- -	-	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
179	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
180	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
181	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240] ECR, Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
182	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, Bihar	04/1997	78.23 162.87	- -	-	0/0
183	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262] SR, Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
184	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265] SCR, Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
185	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274] SWR, Karnataka	02/1999	138.00 901.62	- -	-	0/0
186	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303] ECR, Bihar	04/2003	324.66 528.65	- -	-	0/0
187	DANIWAN-BIHARSARIF (NL), ECR - [220100311] ECR, Bihar	04/2001	104.79 -	- -	-	0/0
188	RAMGANJ MUNDI-BHOPAL (NL), WCR - [220100314] WCR, Madhya Pradesh	04/2001	727.13 727.13	- -	-	0/0
189	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328] ECR, Odisha	04/2005	726.96 810.78	- -	-	0/0
190	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032] SCR, Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
191	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079] SR, Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
192	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084] SR, Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
193	TIDIVANAM-NAGARI (NL) - [N22000085] SR, Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087] NEFR, Bihar	09/2006	300.00 300.00	- -	-	0/0
195	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088] NR, Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	-	0/0
196	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120] WR, Madhya Pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
197	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121] WR, Gujarat	04/2008	394.14 385.60	03/2013 -	-	0/0
198	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122] WR, Gujarat	04/2008	1,389.62 -	03/2014 -	-	0/0
199	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123] WR, Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
200	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125] WR, Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		60,641.23	-		0/0
<u>Road Transport & Highways</u>						
201	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	09/2007	03/2013	0/0
202	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	08/2004 07/2010	03/2013	0/0
203	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	08/2004	03/2013	0/0
204	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00	04/2004	03/2013	0/0
205	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	09/2007	03/2013	0/0
206	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	09/2008	03/2013	0/0
207	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27	03/2008	03/2013	0/0
208	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	05/2008	03/2013	0/0
209	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	10/2008	03/2013	0/0
210	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	03/2008	03/2013	0/0
211	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	10/2008	03/2013	0/0
212	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	10/2008	03/2013	0/0
213	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	07/2008	03/2013	0/0
214	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	11/2008	03/2013	0/0
215	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27	02/2004	03/2013	0/0
216	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	10/2009	03/2013	0/0
217	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70	02/2004	03/2013	0/0
218	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	05/2010	03/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
219	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	09/2012 -	03/2013	0/0
220	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	06/2012 -	03/2013	0/0
221	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	03/2013	0/0
222	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	02/2012 -	03/2013	0/0
223	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	06/2009 -	04/2013	0/0
224	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	12/2012 -	04/2013	0/0
225	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
226	FORBESGANJ TO SIMRAHI (NH-57) (NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	09/2008 -	05/2013	0/0
227	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	06/2008 -	05/2013	0/0
228	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	06/2008 -	05/2013	0/0
229	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	01/2011 -	05/2013	0/0
230	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
231	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
232	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	10/2008 -	06/2013	0/0
233	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	03/2008 -	06/2013	0/0
234	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	12/2008 -	06/2013	0/0
235	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	09/2009 -	06/2013	0/0
236	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	07/2012 -	06/2013	0/0
237	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	05/2012 -	06/2013	0/0
238	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	08/2011 -	06/2013	0/0
239	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
240	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	01/2013 -	06/2013	0/0
241	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
242	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
243	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
244	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
245	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	07/2013	0/0
246	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	07/2013	0/0
247	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	07/2013 -	07/2013	0/0
248	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
249	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	07/2013	0/0
250	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
251	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
252	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
253	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
254	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	08/2013 -	08/2013	0/0
255	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
256	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
257	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
258	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2013	0/0
259	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	09/2013	0/0
260	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	09/2013	0/0
261	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	09/2013	0/0
262	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
263	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
264	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2013	0/0
265	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	10/2013	0/0
266	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
267	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	01/2013 -	10/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
268	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
269	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
270	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
271	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
272	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	01/2009	12/2013	0/0
273	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	05/2008	12/2013	0/0
274	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	06/2010	12/2013	0/0
275	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	06/2011	12/2013	0/0
276	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	10/2011	12/2013	0/0
277	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
278	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
279	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	03/2013	12/2013	0/0
280	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	09/2010	01/2014	0/0
281	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	01/2014	01/2014	0/0
282	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	01/2014	01/2014	0/0
283	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00	01/2014	01/2014	0/0
284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36	01/2014	01/2014	0/0
285	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	05/2013	02/2014	0/0
286	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00	02/2014	02/2014	0/0
287	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00	02/2014	02/2014	0/0
288	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	06/2005	03/2014	0/0
289	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	06/2008	03/2014	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
290	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
291	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
292	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
293	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
294	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
295	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
296	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
297	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
298	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
299	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
300	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
301	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	03/2014	0/0
302	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
303	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
304	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
305	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
306	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
307	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
308	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
309	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
310	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
311	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
312	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
313	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
314	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
315	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
316	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
317	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
318	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
319	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
320	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
321	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2014	0/0
322	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
323	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
324	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
325	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
326	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
327	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
328	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
329	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
330	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
331	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	11/2014	0/0
332	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
333	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
334	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
335	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
336	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
337	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
338	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
339	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
340	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		92,206.60 -			0/0
Shipping & Ports						
341	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008	0/0
342	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
343	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
344	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
345	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012	0/0
346	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
347	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
348	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
349	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	03/2013	0/0
350	Setting up of Single Point Mooring (SPM) and allied - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
351	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
352	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 -	06/2013	0/0
353	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 12/2012	10/2013	0/0
354	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 10/2013	10/2013	0/0
355	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	12/2013	0/0
356	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	-	0/0
357	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
358	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	-	0/0
	Total		15,462.28 -			0/0
Telecommunications						
359	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
360	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
361	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
362	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	02/2013	0/0
363	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	03/2013	0/0
364	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 -	03/2013	0/0
365	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2013	0/0
366	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	06/2013	0/0
367	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 -	09/2013	0/0

(Feb,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
368	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
369	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
370	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
371	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
372	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
373	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	-	0/0
	Total		7,113.08 -			0/0
Urban Development						
374	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
375	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
376	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
377	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Dummy sector						
378	PROJECT_2 DUMMY - [N35000002]DA,	10/2010	1,000.00 -	12/2013 -	02/2013	0/0
	Total		1,000.00 -			0/0
Grand Total			345,841.13			0/0

List of ongoing projects having time and cost overrun w.r.to original

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	15,454.00	12/2008 -	03/2013
	Total		13,171.00 -	17,270.00	15,454.00		
	<u>Civil Aviation</u>						
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,303.26	05/2011 -	03/2013
	Total		1,942.51 -	19,595.00	17,757.26		
	<u>Coal</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,611.71	06/2009 -	09/2013
4	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	455.09	03/2013 -	07/2014
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	4,909.54	3,838.87	03/2012 -	03/2014
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	205.44	03/2014 -	03/2016
	Total		7,938.86 -	29,537.56	24,887.60		
	<u>Petrochemicals</u>						
8	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	6,229.56	04/2012 -	12/2013
	Total		5,460.61 -	38,457.56	31,117.16		
	<u>Petroleum</u>						
9	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	637.21	03/2007 -	03/2014
10	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	1,556.44	03/2007 -	03/2017
11	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	438.85	296.85	03/2006 -	03/2013
12	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	2,184.01	04/2006 -	06/2013
13	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
15	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,184.58	08/2010 03/2012	12/2013
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,185.52	05/2010 -	03/2013
17	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	20,426.00	11/2012 -	11/2013
18	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
19	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	932.51	03/2013 -	04/2014
20	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	211.00	04/2012 -	06/2013
	Total		49,613.82 -	102,403.14	73,788.60		
<u>Power</u>							
21	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,779.86	09/2009 -	03/2018
22	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,793.00	04/2009 -	09/2014
23	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	6,056.50	09/2010 -	12/2017
24	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,662.25	03/2007 -	03/2013
25	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,975.00	12/2009 -	02/2017
26	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,292.14	09/2009 -	03/2014
27	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	2,029.68	10/2010 -	03/2014
28	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,903.38	11/2009 -	05/2013
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,845.21	09/2008 -	03/2013
30	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	829.31	08/2010 -	06/2013
31	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	446.79	07/2010 -	11/2016
32	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	598.00	01/2010 -	03/2013
33	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	2,095.31	01/2016 -	11/2016
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	339.11	07/2014 -	05/2016
35	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,818.00	08/2012 -	03/2013

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064 Total	04/2008	297.37 - 44,380.63	386.32 - 161,709.13	337.73 - 114,589.87	07/2011 - -	03/2013 - -
<u>Railways</u>							
37	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	548.65	03/1994	10/2013
38	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995	03/2013
39	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	9,001.45	03/2001	12/2017
40	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	212.91	03/2002	03/2013
41	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	226.08	03/2004	03/2014
42	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	663.17	12/2011 12/2010	03/2013
43	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	279.98	03/2012	03/2013
44	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	5,016.00	2,650.10	04/2008 12/2011	12/2015
45	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	177.33	03/2007 03/2007	03/2015
46	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	939.49	12/2012	02/2013
47	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	366.38	12/2009	10/2013
48	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	737.21	12/2010	03/2015
49	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,340.39	12/2008	03/2014
50	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	272.71	02/2011	02/2013
51	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	471.60	12/2012 12/2012	02/2013
52	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	468.58	03/2005 12/2008	06/2016
53	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	257.30	02/2009 02/2009	04/2013
54	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	1,172.32	03/2011	03/2017
55	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	281.81	03/2012	03/2013
56	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	940.76	03/2009	12/2014
57	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,649.50	10/2007	12/2015
58	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	204.65	12/2008	09/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	220.09	03/2009 03/2009	04/2013
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	413.84	03/2012 -	03/2013
61	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	116.99	02/2006 -	06/2014
62	PANSPURA-KHARAGPUR 3D LINE - [N22000076	09/2007	252.50 -	529.23	249.36	02/2010 -	12/2015
63	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR & G'BAD-MEERUT - [N22000094	02/2008	171.10 -	224.89	141.55	03/2012 -	12/2013
64	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.47	434.55	06/2005 -	06/2016
65	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,141.75	449.62	03/2014 -	12/2015
66	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	32.72	04/2014 -	03/2017
67	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017
68	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	434.58	03/2013 -	03/2014
69	Ghutiasarif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	120.59	12/2011 -	11/2013
70	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	4,255.37	3,367.54	03/2009 -	03/2015
	Total		15,749.62 -	223,612.72	144,048.68		
Road Transport & Highways							
71	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	156.85	04/2004 -	03/2013
72	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	137.88	09/2008 -	03/2013
73	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	164.10	03/2008 -	03/2013
74	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	267.88	05/2008 -	03/2013
75	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	73.96	04/2009 -	12/2014
76	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	105.66	11/2008 -	06/2014
77	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	43.31	09/2007 -	04/2014
78	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	107.64	07/2009 -	05/2014
79	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
80	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	204.17	09/2007 -	03/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133 Total	05/2009	1,108.00 - 3,324.28	2,288.00 229,057.92	3,465.90 148,955.26	11/2011 - 	08/2013
<u>Shipping & Ports</u>							
82	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	1,460.00	927.92	12/2010 -	12/2013
83	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	137.00	03/2006 -	06/2013
84	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
85	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048 Total	03/2009	3,500.00 - 5,580.00	4,150.00 236,023.42	3,651.10 153,890.28	01/2012 - 	03/2013
<u>Steel</u>							
86	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10,193.53	10/2009 -	03/2013
87	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	347.44	12/2011 06/2010	06/2013
88	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68	136.95	10/2012 -	06/2013
89	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00	14,280.71	12/2011 -	06/2013
90	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068	07/2007	230.00 -	343.58	254.51	02/2011 -	03/2013
91	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069 Total	07/2007	260.00 - 24,028.89	350.00 266,239.85	251.98 179,355.40	08/2010 - 	02/2013
<u>Telecommunications</u>							
92	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058 Total	01/2009	149.15 - 149.15	158.72 266,398.57	80.05 179,435.45	06/2009 - 	03/2013
<u>Urban Development</u>							
93	BANGALORE METRO RAIL PROJECT - [N28000008 Total	05/2006	6,395.00 - 6,395.00	11,609.00 278,007.57	8,473.08 187,908.53	06/2011 - 	03/2013



(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		177,734.37	1,868,312.44	1,271,188.09		

List of ongoing projects having cost overrun w.r.to original

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	15,454.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	4,005.33	09/2010 -	-
	Total		16,663.00 -	22,947.00	19,459.33		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,303.26	05/2011 -	03/2013
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) [N04000038]	08/2008	1,808.00 -	2,015.00	1,796.60	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	23,559.19		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,611.71	06/2009 -	09/2013
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	455.09	03/2013 -	07/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	122.75	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	4,909.54	3,838.87	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	205.44	03/2014 -	03/2016
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	95.10	03/2016 -	03/2016
	Total		8,579.45 -	37,918.25	30,907.38		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	6,229.56	04/2012 -	12/2013
	Total		5,460.61 -	46,838.25	37,136.94		
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	637.21	03/2007 -	03/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.44	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	296.85	03/2006 -	03/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.01	04/2006 -	06/2013
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
18	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,659.05	05/2010 -	01/2013
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,184.58	08/2010 03/2012	12/2013
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,185.52	05/2010 -	03/2013
22	RESITMENT OF MARKETING INSTALATION AT VISAKH [N16000057	01/2009	756.00 -	898.00	915.58	- -	-
23	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	20,426.00	11/2012 -	11/2013
24	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI [N16000066	01/2008	224.00 -	394.00	381.67	- -	03/2013
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	1,249.81	04/2013 -	04/2013
26	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
27	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	932.51	03/2013 -	04/2014
28	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	211.00	04/2012 -	06/2013
	Total		54,272.11 -	120,229.23	88,014.49		
<u>Power</u>							
29	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,779.86	09/2009 -	03/2018
30	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,793.00	04/2009 -	09/2014
31	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	6,056.50	09/2010 -	12/2017
32	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,662.25	03/2007 -	03/2013
33	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,975.00	12/2009 -	02/2017
34	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,292.14	09/2009 -	03/2014

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	871.13	12/2007 -	-
36	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	2,029.68	10/2010 -	03/2014
37	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,903.38	11/2009 -	05/2013
38	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,845.21	09/2008 -	03/2013
39	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	829.31	08/2010 -	06/2013
40	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	775.32	02/2011 -	01/2013
41	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	446.79	07/2010 -	11/2016
42	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	598.00	01/2010 -	03/2013
43	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	2,095.31	01/2016 -	11/2016
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	339.11	07/2014 -	05/2016
45	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,818.00	08/2012 -	03/2013
46	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.32	337.73	07/2011 -	03/2013
47	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	454.21	- -	07/2013
	Total		46,019.35 -	182,078.82	130,916.42		
<u>Railways</u>							
48	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	548.65	03/1994 -	10/2013
49	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
50	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	177.66	- 03/2010	-
51	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	598.00	- -	03/2012
52	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	548.95	544.30	06/1999 -	03/2011
53	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	9,001.45	03/2001 -	12/2017
54	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	248.05	- -	03/2015
55	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	212.91	03/2002 -	03/2013
56	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	119.46	12/2012 -	-

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	600.41	- -	02/2012
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	226.08	03/2004 -	03/2014
59	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	663.17	12/2011 12/2010	03/2013
60	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	226.28	- -	-
61	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	574.88	- -	01/2013
62	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	210.76	- -	03/2013
63	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
64	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	360.00	07/2012 -	-
65	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	279.98	03/2012 -	03/2013
66	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	712.00	762.61	- -	10/2012
67	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	635.20	02/2009 -	03/2012
68	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	71.53	- -	-
69	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	1,379.64	- -	03/2013
70	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	5,016.00	2,650.10	04/2008 12/2011	12/2015
71	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	156.28	- -	03/2012
72	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	177.33	03/2007 03/2007	03/2015
73	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	345.93	- -	12/2012
74	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	326.81	06/2004 -	12/2012
75	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.35	07/2008 -	07/2008
76	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,390.14	07/2005 -	-
77	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	349.77	05/2008 -	-
78	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	07/1996	653.84 654.51	1,302.12	608.97	06/2013 -	06/2013
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	679.24	03/2012 -	-
80	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	939.49	12/2012 -	02/2013

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	366.38	12/2009 -	10/2013
82	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	737.21	12/2010 -	03/2015
83	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,214.00	96.96	- -	-
84	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	345.44	- 05/2009	05/2009
85	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	611.87	- -	03/2012
86	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	495.77	- -	03/2014
87	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	106.63	- -	-
88	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	835.94	06/2007 -	06/2007
89	RENIGUNTA-GUNTAKAL(RE) - [220100260	06/2000	168.34 -	370.00	343.36	04/2003 03/2010	-
90	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	548.96	536.30	- -	-
91	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.00	792.25	- -	03/2013
92	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
93	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,340.39	12/2008 -	03/2014
94	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,363.87	12/2006 -	08/2010
95	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	272.71	02/2011 -	02/2013
96	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	586.63	- 12/2009	02/2012
97	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	471.60	12/2012 12/2012	02/2013
98	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.29	- -	-
99	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	468.58	03/2005 12/2008	06/2016
100	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	697.50	433.79	03/2012 -	12/2012
101	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	239.15	- -	03/2014
102	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	735.10	224.33	- 09/2009	-
103	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	257.30	02/2009 02/2009	04/2013
104	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	1,172.32	03/2011 -	03/2017

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	184.87	- -	-
106	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	281.81	03/2012 -	03/2013
107	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	449.89	- -	03/2010
108	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	940.76	03/2009 -	12/2014
109	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,649.50	10/2007 -	12/2015
110	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	90.17	- -	-
111	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	227.53	- -	-
112	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	2,232.50	1,660.03	- -	03/2014
113	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	204.65	12/2008 -	09/2014
114	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	332.07	- 03/2009	-
115	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	175.25	03/1998 08/2005	08/2005
116	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
117	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	75.76	02/2015 -	-
118	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	220.09	03/2009 03/2009	04/2013
119	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	118.16	- -	-
120	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	242.03	12/2007 03/2010	-
121	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	413.84	03/2012 -	03/2013
122	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027	04/2005	240.00 -	355.00	378.12	03/2009 12/2009	-
123	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.60	0.76	- -	-
124	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	116.99	02/2006 -	06/2014
125	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	441.67	03/2008 06/2008	-
126	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU [N22000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
127	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
128	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	230.01	03/2010 -	-

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
129	PANSPURA-KHARAGPUR 3D LINE - [N22000076	09/2007	252.50 -	529.23	249.36	02/2010 -	12/2015
130	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079	09/2007	404.19 -	900.00	295.40	- -	-
131	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N22000080	09/2006	343.17 -	900.00	592.35	- -	12/2012
132	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	453.04	396.44	03/2011 -	03/2011
133	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083	09/1996	156.00 -	406.40	308.05	- -	06/2013
134	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	227.40	40.72	- -	-
135	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	582.83	145.76	- -	-
136	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086	09/2006	200.00 -	385.20	123.57	- -	03/2016
137	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	532.87	40.88	- -	-
138	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	819.40	158.04	03/2010 -	-
139	BARDHAMAN-KATWA (GC) - [N22000091	04/2007	245.15 -	1,106.62	214.91	12/2010 -	03/2011
140	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR & G'BAD-MEERUT - [N22000094	02/2008	171.10 -	224.89	141.55	03/2012 -	12/2013
141	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.47	434.55	06/2005 -	06/2016
142	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,141.75	449.62	03/2014 -	12/2015
143	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	32.72	04/2014 -	03/2017
144	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	359.86	1.22	- -	03/2015
145	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017
146	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	434.58	03/2013 -	03/2014
147	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113	04/2008	653.19 -	653.46	228.10	03/2014 -	03/2014
148	Dakshin-barasal-lakshmikanthapur - [N22000116	04/2009	259.51 -	533.38	94.51	12/2011 -	02/2012
149	Ghutiasharif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	120.59	12/2011 -	11/2013
150	Pandabeswar-Chinpai doubling (ER) - [N22000118	04/2004	225.68 -	293.74	136.16	12/2010 -	12/2010
151	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	04/2008	394.14 -	404.39	15.90	03/2013 -	-

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123	04/2008	318.24 -	468.62	1.52	03/2012 -	-
153	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125	04/2006	117.36 196.95	196.95	194.97	03/2011 -	-
154	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project [N22000127	04/1996	1,676.31 -	4,255.37	3,367.54	03/2009 -	03/2015
	Total		38,023.46 -	307,089.90	189,376.64		
<u>Road Transport & Highways</u>							
155	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	156.85	04/2004 -	03/2013
156	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221	12/2003	155.00 -	201.66	137.88	09/2008 -	03/2013
157	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	164.10	03/2008 -	03/2013
158	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	267.88	05/2008 -	03/2013
159	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	73.96	04/2009 -	12/2014
160	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	105.66	11/2008 -	06/2014
161	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	43.31	09/2007 -	04/2014
162	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	107.64	07/2009 -	05/2014
163	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
164	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	204.17	09/2007 -	03/2014
165	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	08/2013
	Total		3,324.28 -	312,535.10	194,283.22		
<u>Shipping & Ports</u>							
166	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,571.60	5.75	10/2008 -	10/2008
167	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
168	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	1,460.00	927.92	12/2010 -	12/2013
169	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	137.00	03/2006 -	06/2013
170	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
171	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039]	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
172	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	3,651.10	01/2012 -	03/2013
173	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	306.12	02/2014 -	-
174	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	371.18	04/2009 -	02/2011
	Total		8,628.97 -	323,753.60	199,902.22		
<u>Steel</u>							
175	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10,193.53	10/2009 -	03/2013
176	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	347.44	12/2011 06/2010	06/2013
177	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	136.95	10/2012 -	06/2013
178	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	14,280.71	12/2011 -	06/2013
179	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	230.00 -	343.58	254.51	02/2011 -	03/2013
180	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	350.00	251.98	08/2010 -	02/2013
	Total		24,028.89 -	353,970.03	225,367.34		
<u>Telecommunications</u>							
181	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013
182	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]	03/2008	328.13 -	392.13	-	03/2009 -	01/2013
	Total		477.28 -	354,520.88	225,447.39		
<u>Urban Development</u>							
183	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	8,473.08	06/2011 -	03/2013
184	C/o office building for IDBI at bandra Kurla Complex, Mumbai - [N28000048]	11/2006	114.18 173.08	173.08	-	04/2009 -	-
	Total		6,509.18 -	366,302.96	233,920.47		

(Feb,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Water Resources</u>						
185	PAGLADIYA DAM PROJECT	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	- [300100001		-			-	
	Total		542.90	367,489.96	233,955.96		
			-				
	Grand Total		216,279.99	2,822,960.98	1,832,246.99		
