

**291th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.100 Crores and above)
January, 2010**



Krishna Godavari basin



**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary	1 -4
Month wise list of completed projects Costing Rs. 100 Crore and Above During 2008-09	5-10
Summary of Projects	1-20
Sector wise analysis of projects	21-59

EXECUTIVE SUMMARY

The 291st Flash Report for January' 2010, that contains information on the status of 620 projects in the Central Sector, each costing Rs. 100 Crores and above. During January' 2010, two projects reported completion and have been dropped from the monitor of this Ministry. During the month under reference, twenty five new projects have been added. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	151
2.	RAILWAYS	157
3.	POWER	85
4.	PETROLEUM	78
5.	COAL	43
6.	TELECOMMUNICATION	29
7.	STEEL	28
8.	SHIPPING & PORTS	20
9.	CIVIL AVIATION	18
10.	ATOMIC ENERGY	5
11.	URBAN DEVELOPMENT	3
12.	MINES	1
13.	HEALTH & FW	1
14.	WATER RESOURCES	1
Total		620

2. Sixty four (64) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1-60 months in respect of projects relating to Civil Aviation, Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways and Shipping & Ports sectors.

3. In the **Civil Aviation Sector**, 2 projects have shown additional delays of 3-11 months, however no specific reasons have been provided by the project authorities for such delays.

4. In the **Coal sector**, 4 projects have reported additional delays in the range of 2-6 months while Jhanjra Continuous Miner for Jhanjra UG-II and Jhanjra Longwall UG Phase-II, have reported considerable improvement over the completion schedule by 15 months and 2 months respectively. Thermal Power Station -II Expansion (1470 MW to 1970 MW) project of National Lignite Corporation, (NLC), has reported additional delay of 4 months due to delay in equipment erection and inadequate mobilization by the contractor. Barsingsar Thermal Power Station (2X125 MW) (NLC), has reported additional delay of 6 months due to delay in supply of indigenous equipments by Private and Public Sector and delay in equipment erection.
3. In the **Steel Sector**, 11 projects have reported additional delays in the range of 5-12 months. Power Plant – 1 has reported additional delay of 5 months due to delay in supply of equipment by M/s BHEL. Coal Dust Injection in BF-2 and 3 has reported additional delay of one month, due to relocation of Coal Handling & Storage site for SMS-III. Simultaneous Blowing of BOF Converter of SMS-II has reported additional delay of 2 months, due to slow progress of work. Rebuilding of coke oven battery No.10 has reported additional delay of 3 months due to poor performance by the contractor. Enhancement of Loading Capacity at Bolani Iron ore has reported additional delay of 4 months due to slow progress of design engineering & fabrication work by M/s TECPRO. Pulverised Coal Injection System for Blast Furnace -1&2, has reported additional delay of 5 months due to delay in design & engineering work and inadequate supplies & mobilization of resources for site activities by the contractor. Installation of 700 TPD Oxygen Plant, Rourkela has reported additional delay of 6 months, due to delay in supply of booster air compressor. Rebuilding of coke oven battery No. 1 & 2 Bokaro Steel Plant, Expansion of Bhilai Steel Plant and Rourkela Steel Plant have reported additional delay of 6 months, 6 months and 12 months respectively due to inadequate mobilization of resources by the respective contractors.
4. In the **Petroleum Sector**, 8 projects have reported additional delays in the range of 1-24 months. Panipat Naphta Cracker Project has reported additional delay of 1 month due to delay in completion of Captive Power Plant by L&T. Installation of FCC Gasoline Desulphur Unit at Mathura Refinery has reported additional delay of 1 month, due to continuous delay in supply of compressor's piping and instrumentation items by BPCL. Installation of FCCV at Mumbai Refinery has reported additional delay of one month however no specific reason has been given by the project authority. Residue Upgradation

and MS/HSD Quality Improvement has reported additional delays of 5 months due to slow progress in supply of critical equipments. IOR Lakwa-Lakhmani (ONGC) has reported additional delay of 12 months, however no specific reason has been reported by the project authority. IOR, Rudrasagar (ONGC) has reported additional delay of 12 months, due to re-prioritization of wells. Revamping of Win Platform at MH Asset has reported additional delay of 12 months, due to high quoted price & fresh tender is to be invited. Development of B-46 Cluster Field has reported additional delay of 24 months, due to revision of works.

5. In the **Power Sector**, 13 projects have reported additional delays in the range of 1-21 months. Parbati Hydro Electric Project Stage-III 4x130 MW (NHPC) has reported additional delay of 7 months due to delay in land acquisition for Sainj bypass and delay in award of E&M contract. Chamara, Hydro Electric Project Stage III (NHPC) has reported additional delays of 4 months due to violence among contractor's laborers and court stay on crushing Plant leading to huge shortage of aggregate for concrete work. NIMOO BAZGO Hydro Electric Project has reported additional delay of 4 months due to highly inclement weather condition, delay in award of E&M works due to poor participation, delay in HM works due to abnormal high price bid and retendering thereof. Bongaigaon Thermal Power Project (NTPC) has reported additional delay of 3 months due to delay in slow progress by civil agency. Korba STPP Stage-III, 1x500 MW (NTPC) has reported additional delay of 6 months due to delay in civil and structural work by M/s SPML. Farakka STPP Stage-III (NTPC) has reported additional delay of 3 months due to delay in finalization of erection by M/s BHEL. Transmission system associated with Parbati HEP stage III, 543 CKM has reported additional delay of 7 months due to court cases. Kaiga 3 & 4 Transmission System (PGCIL) has reported additional delay of 3 months due to revision of works in 50 km Karnatka portion. Kunadankulam Atomic Power Project HEP Transmission Line 1838 CKM (PGCIL) has reported additional delay of one month, to match with the commissioning of linked Generation Projects. Neyveli Transmission System-II 838 CKM (PGCIL) has reported additional delay of 1 month due to court cases. Transmission System for Startup Power to DVC & Maithon RB Generation project (PGCIL) has report additional delay of 2 months due to delay in forest clearance. Northern Region System Strengthening Scheme-VI 54 CKM (PGCIL) has reported additional delay of one month due to revision of

works. Vishnugad-Pipalkoti Hydro Electric Project (THDCL) has reported additional delays of 21 months due to delay in acquisition of forest land.

6. In the Road Transport and Highways Sector, 17 projects have reported additional delays in the range of 1-9 months. No specific reasons have been reported by the project authorities for such additional delays.

7. In the Railway Sector, 8 projects have shown additional delays in the range of 3-60 months. Udhampur-Srinagar-Baramulla (NL), NR has reported additional delays of 60 months due to delay in land acquisition of Army Land. Tollyganj-Garia (MTP) project, Sitamarhi- Raxaul- Narkataiganj (GC) and Palwal-Bhuteswar 3rd line doubling (NCR), have reported additional delays of 3 months, 9 months and 9 months, respectively, however, no specific reasons have been reported by the concerned project authorities. Rajatgarh-Barang (Line Doubling) ECoR, and Cuttack-Barang (Line Doubling), ECoR of RVNL has reported additional delays of 3 months and 6 months due to inadequate mobilization by the contractor. Deograh- Dumka New BG Line (LD) ER of RVNL has reported additional delays of 8 months due to Maoists movement. New Guwahati- Digaru Patch (LD) Phase-I has reported additional delays of 12 months due to ban on cutting of hills.

8. In the Shipping & Ports Sector, Deepening of Channel at Paradip Port has reported additional delay of 1 month, however, no specific reason has been reported by the concerned project authority.

Status as on 01.02.2010 in respect of completion of projects costing Rs.100 Crores and above in different sectors during 2010-11 is indicated in the following tables.



(Pankaj Jain)

Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	157	8
2	Road Transport & Highways	151	17
3	Power	85	13
4	Petroleum	78	8
5	Coal	43	4
6	Telecommunications	29	0
7	Steel	28	11
8	Shipping & Ports	20	1
9	Civil Aviation	18	2
10	Atomic Energy	5	0
11	Urban Development	3	0
12	Mines	1	0
13	Health & Family Welfare	1	0
14	Water Resources	1	0
	Total	620	64

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 100 Crores and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2009				
<u>Steel</u>				
1	COKE OVEN BATTERY NO. 4(PHASE-1) (RINL)(RASTRIYA ISPAT NIGAM LIMITED) - [120100061]	286.63	12/2006	301.25
May,2009				
<u>Petroleum</u>				
2	AUGMENTATION OF MUNDRA-PANIPAT CRUDE OIL PIPELINE(INDIAN OIL CORPORATION LIMITED) - [160100291]	205.00	03/2008	140.55
<u>Road Transport & Highways</u>				
3	JHANSI-SHIVPURI ,NH-25,NH-25 KM-91-50(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [240106251]	220.31	05/2008	149.02
4	BHARATPUR MAHAVA, NH-11, KM.63 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106259]	250.00	01/2010	341.10
5	AMBALA-ZIRAKPUR, NH-21AND22, KM.5/735 TO KM.39/961(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106261]	298.00	11/2010	364.62
6	KONDHALI-TELEGAON(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000041]	212.00	03/2010	331.87
<u>Telecommunications</u>				
7	GSM BASED NETWORK EXPANSION PH-IV (BSNL) (U.P. WEST)(BHARAT SANCHAR NIGAM LIMITED) - [260100081]	359.07	06/2009	36.19
8	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(PUNJAB)(BHARAT SANCHAR NIGAM LIMITED) - [260100089]	508.63	06/2010	365.16
9	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(RAJASTHAN)(BHARAT SANCHAR NIGAM LIMITED) - [260100090]	448.91	06/2009	154.52
10	GSM BASED NETWORK(PH-IV)(BSNL) ORISSA(BHARAT SANCHAR NIGAM LIMITED) - [260100093]	164.06	12/2009	89.29
11	GSM-NETWORK EXPANSION(PH-IV) (BSNL) W. BENGAL(BHARAT SANCHAR NIGAM LIMITED) - [260100094]	428.00	06/2009	200.00
June,2009				
<u>Petroleum</u>				
12	GREEN FUELS & EMISSION CONTROL (HPCL) MUMBAI REF.(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100236]	1,152.00	06/2009	1,551.79
<u>Railways</u>				
13	THANE-TURBHE-NERUL-VASHI(MTP)(METROPOLITAN RAPID TRANSPORT PROJECTS) - [220100159]	403.39	03/2000	400.60

**Month wise List of Completed Project Costing Rs. 100 Crores and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
14	PARADIP PORT, NH-5A (PORT CONNECTIVITY) KM 0 - KM 77(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100202]	428.00	02/2007	459.38
15	SWAROOPGANJ TO BAKARIA (RJ-1) PH.II, KM.29-KM.0 (NH-76)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106229]	220.00	04/2010	244.47
16	RAJASTHAN/MP BORDER TO KOTA(RJ-10), KM.509- 449.15, NH-76(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106254]	378.22	04/2008	365.05
17	RJ/MP BORDER TO KOTA(RJ-9) NH-76, KM.449.15 TO KM.406(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106255]	297.72	04/2008	289.88
18	AGRA-BHARATPUR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000027]	195.00	03/2009	192.10
19	PALANPUR TO SWAROOPGANJ, NH-14(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000067]	498.00	03/2009	82.09
July, 2009				
<u>Power</u>				
20	KAHAL GAON STPP STAGE - II (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100230]	5,868.31	05/2007	4,881.17
<u>Road Transport & Highways</u>				
21	GARAMORE TO BAMANBORE (PACK.-III) PH.-II, KM.254-KM.182.60(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106215]	360.70	11/2007	334.72
22	TINDIVANAM-UIUNDURPET, KM 121-192.25 NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000082]	480.00	03/2009	1,130.80
<u>Telecommunications</u>				
23	COMM. OF GSM EQU. OF 600K LINES(PH-4)(BHARAT SANCHAR NIGAM LIMITED) - [N26000032]	214.00	01/2007	120.48
24	PROJECT NIB-II BROADBAND MULTIPLY(BHARAT SANCHAR NIGAM LIMITED) - [N26000047]	1,008.00	03/2009	337.50
August, 2009				
<u>Power</u>				
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000025]	220.69	04/2009	131.26
<u>Railways</u>				
26	MADURAI-DINDIGUL,(LD)(SR)(SOUTHERN RAILWAY) - [N22000047]	73.19	-	181.81
<u>Road Transport & Highways</u>				
27	TIRUNELVEI-PANAGUDI, KM 160-203(T.N)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106242]	423.54	03/2008	220.40

**Month wise List of Completed Project Costing Rs. 100 Crores and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
28	SALEM TO KARUR (NS-21 OF TN-2), KM.207.050-KM.248.625, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106270]	253.50	01/2009	333.34
29	SALEM TO KARUR, KM.258-645 TO KM.292.6(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106271]	205.60	08/2008	323.94
30	SALEM TO KERALA BORDER SEC. (TN-7), KM.53 TO KM.100, NH-47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106274]	379.80	12/2008	453.20
September,2009				
31	MADURAI-KANNIAKUMARI, KM.42 TO KM.80, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106238]	474.21	03/2008	246.20
32	MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106239]	567.38	03/2008	382.50
33	MAHUA-JAIPUR, NH-11, KM.120 TO KM.228(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106258]	483.00	03/2009	578.30
34	KARUR TO MADURAI (TN-5), KM.373.275 TO KM.426.6, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106275]	283.50	12/2008	448.30
35	INDORE-KALAGHAT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000034]	472.00	09/2009	663.90
36	Bharuch-Surat Package BOT-II(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000070]	492.00	07/2009	448.87
37	Vadodara-Bharuch Package BOT-I(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000071]	660.00	07/2009	789.84
38	UIUWDURPET-PADALUR,NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000084]	460.00	06/2009	799.19
Shipping & Ports				
39	ACQUISITION OF 2-300,000 DWT VERY LARGE CRUDE CARRIERS(SHIPPING) - [250100174]	1,136.08	09/2009	1,196.24
October,2009				
Petroleum				
40	DEVELOPMENT OF BASSEIN EAST (ONGCL)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100232]	985.17	03/2006	1,568.46
Railways				
41	2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR)(RAIL VIKAS NIGAM LTD.) - [220100221]	93.10	-	126.11
Telecommunications				
42	GSM EQUIPMENT OF 1015K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000044]	350.84	11/2008	182.06
43	ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM(BHARAT SANCHAR NIGAM LIMITED) - [N26000059]	567.40	06/2009	241.85
November,2009				

**Month wise List of Completed Project Costing Rs. 100 Crores and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
44	KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106272]	327.20	01/2009	457.60
45	HYDERABAD BANGALORE SECTION(NH-7)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106284]	611.44	03/2009	834.20
46	KADAL TO ARMUR, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000092]	271.73	11/2009	303.80
<u>Telecommunications</u>				
47	GSM BASED NETWORK PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000033]	174.36	11/2007	71.50
December,2009				
<u>Steel</u>				
48	INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000024]	123.22	06/2009	77.00
<u>Telecommunications</u>				
49	GSM EQUIPMENT OF 1162K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000045]	325.00	12/2008	237.85
January,2010				
<u>Road Transport & Highways</u>				
50	GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106231]	266.00	08/2007	NR
51	CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106232]	133.03	08/2005	NR

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 100 Crore and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Telecommunications</u>				
1	500K BROAD BAND ACCESS N/W PH-III(MAHANAGAR TELEPHONE NIGAM LIMITED) - [120100061]	134.25	10/2009	31.95


Summary of projects on the Flash Report for the month of January, 2010

I. Project Implementation – Current Status:

Number of Projects Previous Month	599
Number of Projects Completed/Dropped/Frozen in Previous Month	2
Number of Projects Completed/Dropped/Frozen in Current month	2
Number of Projects Added in Current month	25
Number of Projects in Current Month	620

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 620 projects, 12 projects are ahead of schedule, 135 projects are on schedule and 317 projects are delayed. Of the balance, 113 projects do not have fixed dates of commissioning while 43 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

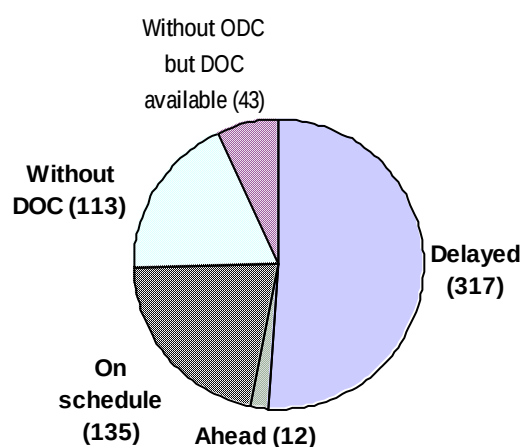

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 620 projects when sanctioned, was of the order of Rs. 597330.51 crore but this was subsequently revised to Rs. 650395.25 crore implying a cost overrun of 8.88%. The expenditure incurred on these projects till January, 2010 is Rs. 253091.44 crore, which is 36.80% of the revised cost of the projects.

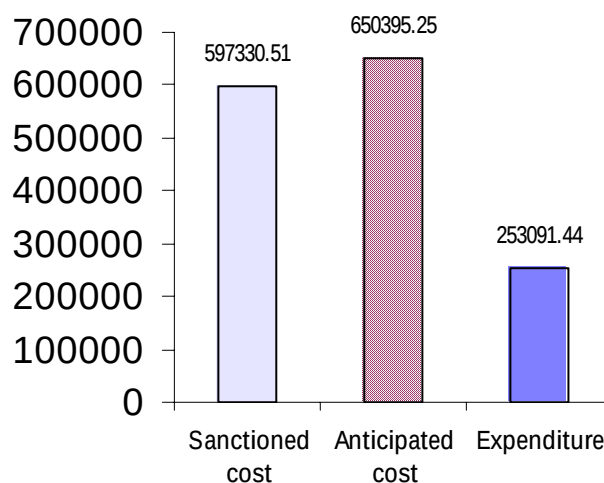

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	599
No of Projects Completed/Dropped/Frozen in Previous Month	2
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	25
No of Projects in Current Month	620

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original	317	12	135	43	113	620	51.13
Latest Approved	351	14	146	31	78	620	56.61

III. (A) Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Original	515	504,220.58	538,516.88	198,169.73	36.80	34,296.30	6.80
Latest Approved	105	93,109.93	111,878.37	54,921.71	49.10	18,768.44	20.20
Total	620	597,330.51	650,395.25	253,091.44	38.91	53064.74	8.88

III. (B) Delayed Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Original	317	320,577.26	376,622.81	186,264.67	49.50	56,045.55	17.50
Latest Approved	351	65,759.23	391,827.50	194,238.83	49.60	326,068.27	495.90

IV. Additional Delayed Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Latest Approved	64	72,061.78	87,914.29	44,809.32	51.00	15,852.51	22.00
Total	64	72,061.78	87,914.29	44,809.32	50.97	15852.51	22.00

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Road Transport & Highways</u>						
GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73	12/2003	266.00	08/2007	288.06	12/2009	NR
CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213	03/2005	133.03	08/2005	133.03	10/2009	NR

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
Civil Aviation					
C/o new Airport-SH: E/W in cutting and filling geogrid	1/2009	264.29	1/2011	264.00	-
Petroleum					
VKPL Upgradation and Laying of Superlines	12/2009	463.32	5/2011	463.32	5/2011
Civil Aviation					
Construction of New Integrated terminal building	4/2007	128.96	2/2009	128.96	3/2010
Petroleum					
NORTH TAPTI GAS FIELD DEV.	7/2008	589.70	3/2011	589.70	3/2011
Railways					
KISHANGANJ JALALGARH	4/2008	282.92	/	359.86	-
Civil Aviation					
Construction of New Expandable Modular Integrated	3/2008	135.72	9/2009	135.72	3/2010
Telecommunications					
MANAGED LEASED LINE NETWORK PH-VI	11/2008	350.00	/	350.00	-
Civil Aviation					
C/o new Integrated terminal Bldg. at Birsa Munda	1/2009	137.79	1/2010	137.79	6/2010

GAGAN PROJECT	9/2008	393.60	6/2013	393.60	-
Railways					
SEVOK RANGPO	4/2008	1,339.48	12/2015	1,339.48	12/2015
Telecommunications					
CENTRALISED TRANSMISSION NMS	8/2009	300.00	/	300.00	-
Shipping & Ports					
Acquisition of Two nos. of 3060 DWT	4/2009	2,770.32	9/2011	2,770.42	12/2011
Petroleum					
ADDITIONAL DEV. OF D-1 FIELD	1/2010	2,163.64	12/2011	2,163.64	12/2011
Road Transport & Highways					
DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	300.00	10/2008	300.00	-
Civil Aviation					
Construction of New Integrated Terminal Building	10/2006	147.00	9/2008	147.00	10/2009
Petroleum					
Paradip-Sambalpur-Raipur-Ranchi Pipeline	8/2009	1,793.00	9/2012	1,793.00	9/2012
Civil Aviation					
Construction of New Integrated Passenger Terminal	3/2006	129.38	4/2009	129.38	3/2010
DEV. OF KAMRAJ DOMESTIC CHENNAI AIRPORT	8/2008	1,808.00	1/2011	1,808.00	-
Petroleum					
BNPL superlines(Uttranchal & Punjab)	12/2009	540.92	5/2011	540.92	5/2011
Shipping & Ports					
Acquisition of two nos. of 120 B.P	4/2009	2,908.48	3/2011	2,908.48	6/2011
Petroleum					
Integrated crude Oil handling facilities at Paradip	12/2009	1,492.33	6/2012	1,492.33	3/2012
De-bottlenecking of SMPL	12/2009	1,584.00	/	1,584.00	12/2012
CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	6/2007	736.65	12/2011	736.65	12/2011
Civil Aviation					
C/O PASSENGER LOUNGE BIRSI AIRPORT	3/2006	108.07	8/2008	108.07	10/2009
Railways					

RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN	4/1993	100.41	12/2009	949.22	12/2009
---	--------	--------	---------	--------	---------

VII. Milestones (Cumulative due & achieved)

Total	2007
Achieved up to month	0

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Civil Aviation</u>						
C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE	135.60	135.60	10/2009	02/2010	05/2010	3
C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A	144.94	144.94	04/2010	01/2010	12/2010	11
<u>Coal</u>						
JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II	122.35	122.35	03/2010	03/2013	12/2011	-15
JHANJRA LONGWAL UG PHASE II	287.18	287.17	11/2009	03/2012	01/2012	-2
TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	2,030.78	2,453.57	06/2009	02/2011	06/2011	4
BARSINGSAR TPS (2X125MW) (NLC)	1,114.18	1,626.09	06/2009	03/2010	09/2010	6
<u>Steel</u>						
POWER PLANT-I	462.00	350.00	12/2009	01/2011	08/2010	-5
COAL DUST INJECTION IN BF-2 and 3	132.73	133.92	05/2008	03/2010	04/2010	1
SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II	197.66	197.66	10/2009	01/2010	03/2010	2
EXPANSION OF BOKARO STEEL PLANT	3,316.00	3,316.00	12/2010	10/2011	12/2011	2
REBUILDING OF COKE OVEN BATTERY-10	416.50	416.50	09/2009	03/2010	06/2010	3
ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE	124.88	119.88	12/2009	02/2010	06/2010	4
Pulverised coal injection system for bf-1&2	125.00	133.00	09/2009	03/2010	08/2010	5
INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA	302.70	302.70	06/2009	01/2010	07/2010	6
Rebuilding of coke oven battery No.1 & 2 (Bokaro S	500.90	500.90	04/2010	10/2010	04/2011	6
EXPANSION OF BHILAI STEEL PLANT	5,185.00	5,516.00	05/2011	09/2012	03/2013	6
EXPENSION OF ROURKELA STEEL PLANT	6,133.00	6,878.00	02/2011	03/2012	03/2013	12
<u>Petroleum</u>						
PANIPAT NAPHTA CRACKER PROJECT	12,138.00	14,439.00	09/2009	02/2010	03/2010	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE	348.00	348.00	12/2009	01/2010	02/2010	1
INSTALLATION OF FCCV AT MUMBAI REFINERY	900.47	900.47	09/2009	05/2010	06/2010	1
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT	5,693.00	6,898.00	01/2010	01/2010	06/2010	5
IOR LAKWA - LAKHMANI (ONGCL)	345.10	600.00	03/2007	03/2010	03/2011	12
IOR, RUDRASAGAR (ONGCL)	113.90	219.22	03/2006	03/2010	03/2011	12
REVAMPING OF WIN PLATFORM AT MH ASSET	333.40	333.40	05/2010	05/2010	05/2011	12
DEVELOPMENT OF B-46 CLUSTER FIELD	1,436.21	1,436.21	07/2010	05/2010	05/2012	24
Power						
NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL)	691.83	913.33	12/2007	02/2010	03/2010	1
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	1,779.29	1,896.65	11/2008	02/2010	03/2010	1
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI	186.95	186.95	07/2009	02/2010	03/2010	1
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G	290.49	290.49	04/2010	04/2010	06/2010	2
KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL)	596.45	1,007.16	12/2007	03/2010	06/2010	3
Farakka STPP Stage-III	2,570.44	2,570.44	08/2010	08/2010	11/2010	3
BONGAIGAON THERMAL POWER PROJECT	4,375.35	4,375.35	07/2011	11/2011	02/2012	3
CHAMERA, STAGE-III (NHPC)	1,405.63	1,405.63	08/2010	08/2010	12/2010	4
NIMOO BAZGO HYDROELECTRIC PROJECT	611.01	611.02	08/2010	08/2010	12/2010	4
KORBA STPP STAGE-III	2,448.50	2,448.49	02/2010	02/2010	08/2010	6
PARBATI H.E.P. STAGE -III (NHPC)	2,304.56	2,304.52	10/2010	11/2010	06/2011	7
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE	557.24	557.25	01/2010	11/2010	06/2011	7
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	2,491.58	06/2013	06/2013	03/2015	21
Railways						
TOLLYGANJ-GARIA(MTP)	907.69	1,032.76	12/2006	03/2010	06/2010	3
RAJATGARH- BARANG(LD),ECOR	166.16	243.40	N.A.	03/2010	06/2010	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
CUTTACK - BARANG (LD)	127.13	135.10	N.A.	06/2010	12/2010	6
DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	180.73	335.00	12/2006	03/2010	11/2010	8
PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	240.00	329.70	03/2009	06/2010	03/2011	9
SITAMARHI-RAXAUL- NARKATIAGANJ (GC)	501.69	501.69	03/2010	06/2011	03/2012	9
NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I	99.84	110.94	03/2010	03/2010	03/2011	12
UDHAMPUR-SRINAGAR- BARAMULLA (NL),NR	2,500.00	11,270.00	03/2001	12/2012	12/2017	60
Road Transport & Highways						
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS- 1/BOT/MP-2),NH7	407.60	407.60	06/2010	09/2010	06/2010	-3
NALBARI TO BIJNI (AS-8)	200.00	200.00	06/2008	06/2010	07/2010	1
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	193.09	193.09	03/2008	05/2010	07/2010	2
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80	166.27	166.27	03/2008	04/2010	07/2010	3
AURANG-RAIPUR, NH-6, KM.232 TO KM.281	190.00	190.00	01/2009	02/2010	05/2010	3
FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	332.94	332.94	09/2008	12/2010	03/2011	3
THANJAUR-TRICHY,NH- 67(NHAI)	280.00	280.00	06/2009	03/2010	06/2010	3
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	629.00	629.00	11/2010	01/2010	06/2010	5
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	225.00	225.00	10/2008	05/2010	10/2010	5
TRICHY - KORUR NH-67	516.00	516.00	07/2010	07/2010	12/2010	5
KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203- 233.60), NH-7	120.00	120.00	09/2006	04/2010	10/2010	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	227.00	227.00	12/2008	06/2010	12/2010	6
LALITPUR TO SAGAR, NH-26 (NHAI)	198.00	198.00	11/2008	09/2010	03/2011	6
SITAPUR-LUCKNOW	322.00	322.00	06/2009	06/2010	12/2010	6
NALBARI TO BIJNI (AS-9)	142.00	142.00	06/2008	06/2010	12/2010	6
TRICHY - DINDIGUAL NH-45	576.00	576.00	07/2010	07/2010	01/2011	6
KUNJWANI-VIJAYPUR(NS- 15) (NS & EW-PH-I) KM.80- KM.97.20,NH-1A	110.00	110.00	12/2004	03/2010	12/2010	9

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Shipping & Ports</u>						
DEEPENING OF CHEENEL AT PARADIP PORT	154.84	253.36	06/2007	03/2010	04/2010	1
Number of projects reporting additional delay = 64						

Sector wise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	25,054.29	25,054.29	26,308.29
Civil Aviation	18	8,085.05	8,079.54	8,084.76
Coal	43	26,110.40	27,853.79	28,183.41
Mines	1	4,091.51	4,091.51	4,091.51
Steel	28	45,473.36	45,473.36	50,679.38
Petroleum	78	150,389.80	160,317.67	171,409.05
Power	85	165,980.96	167,795.04	170,607.00
Health & Family Welfare	1	71.18	422.60	443.15
Railways	157	53,764.93	67,043.80	100,114.94
Road Transport & Highways	151	43,916.82	43,916.82	44,119.51
Shipping & Ports	20	18,154.63	18,154.63	18,426.49
Telecommunications	29	11,916.06	11,737.53	11,534.73
Urban Development	3	14,596.67	16,847.03	15,206.03
Water Resources	1	542.90	542.90	1,187.00
Grand total	620	568,148.56	597,330.51	650,395.25


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	5
Number of Projects on schedule	1
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are on schedule and 4 projects are delayed.



Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 5 projects when sanctioned, was of the order of Rs. 25054.29 Crores but this was subsequently revised to Rs. 26308.29 Crores. The expenditure incurred on these projects till Jan, 2010 is Rs. 19902.92 Crores.

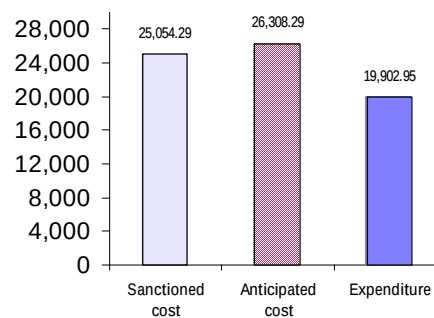


2. Sector: - Civil Aviation

Number of Projects	18
Number of Projects on schedule	3
Number of Projects Delayed	8
Number of Projects Wo_Doc_Original	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 18 projects, 3 projects are on schedule, 8 projects are delayed and 7 projects are original date of



Investment Scenario

The total cost of implementation of 18 projects when sanctioned, was of the order of Rs. 8085.05 Crores but this was subsequently revised to Rs. 8084.76 Crores. The expenditure incurred on these projects till Jan, 2010 is Rs 2250.69 Crores.

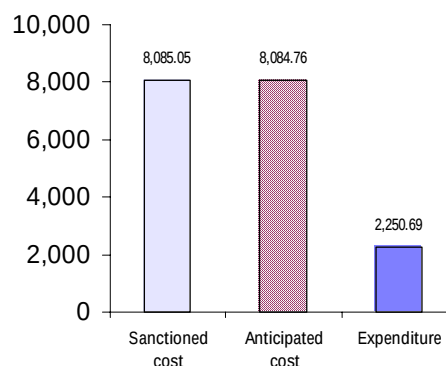


3. Sector: - Coal

Number of Projects	43
Number of Projects on schedule	18
Number of Projects Delayed	20
Number of Projects Ahead	4
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 43 projects, 18 projects are on schedule, 20 projects are delayed and 4 projects are ahead and 1 Project without original date of commissioning.



Investment Scenario

The total cost of implementation of 43 projects when sanctioned, was of the order of Rs. 26110.40 Crores but this was subsequently revised to Rs. 28183.41 Crores. The expenditure incurred on these projects till January, 2010 is Rs. 10914.25 Crores

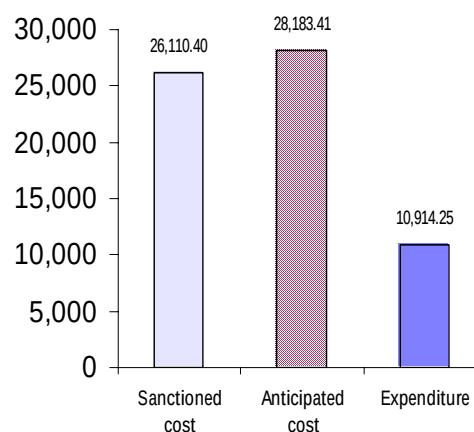


4. Sector: - Petroleum

Number of Projects	78
Number of Projects on schedule	34
Number of Projects Delayed	37
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	3
Number of Projects Without original date of commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 34 projects are on schedule, 37 projects are delayed and 3 projects are ahead and 3 projects are without date of commissioning and 1 Project is Without original date of commissioning.

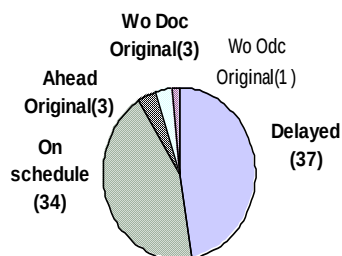

Investment Scenario

The total cost of implementation of 78 projects when sanctioned, was of the order of Rs. 150389.80 Crores but this was subsequently revised to Rs. 171409.05 Crores. The expenditure incurred on these projects till January, 2010 is Rs. 48683.77 Crores.

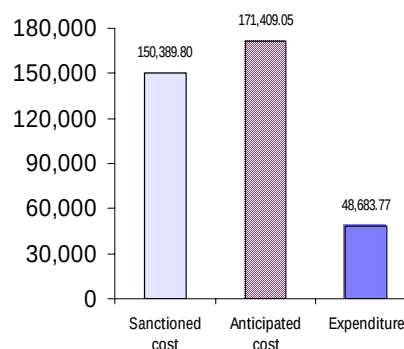


5. Sector: - Power

Number of Projects	85
Number of Projects on schedule	43
Number of Projects Delayed	39
Number of Projects Wo_Doc_Original	2
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 85 projects, 43 projects are on schedule, 39 projects are delayed, 2 projects is without date of commissioning and 1 projects is without original date of commissioning



Investment Scenario

The total cost of implementation of 85 projects when sanctioned, was of the order of Rs. 165980.96 Crores but this was subsequently revised to Rs. 170607.00 Crores. The expenditure incurred on these projects till Jan, 2010 is Rs. 61373.69 Crores.

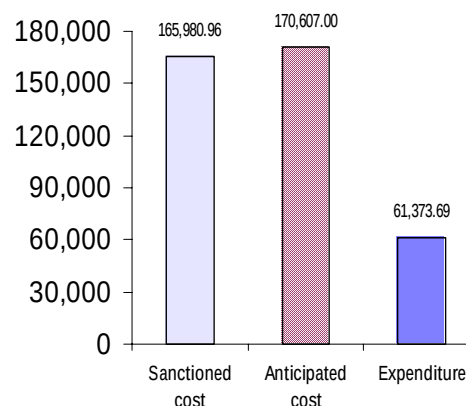


6. Sector: - Railways

Number of Projects	157
Number of Projects on schedule	9
Number of Projects Delayed	39
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	67
Number of Projects Wo_Odc_Original	41


Brief Analysis

Project Status with out respect Original Schedule: Out of 157 projects, 9 projects are on schedule, 39 projects are delayed, 1 projects is ahead. 67 projects are Without date of commissioning and 41 projects are without original date of commissioning.

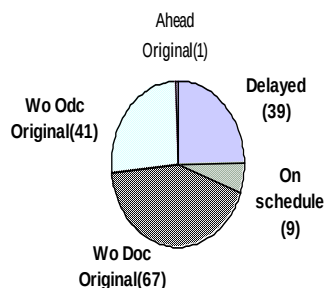

Investment Scenario

The total cost of implementation of 157 projects when sanctioned, was of the order of Rs. 53764.93 Crores but this was subsequently revised to Rs. 100114.94 Crores. The expenditure incurred on these projects till January, 2010 is Rs. 38101.27 Crores.

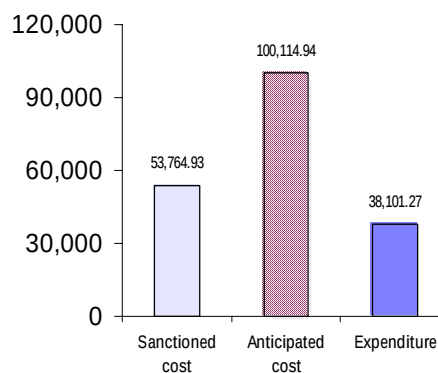


7. Sector: - Road Transport and Highways

Number of Projects	151
Number of Projects on schedule	13
Number of Projects Delayed	127
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 151 projects, 13 projects are on schedule, 127 projects are delayed, 2 projects are ahead and 9 projects is with out date of commissioning .

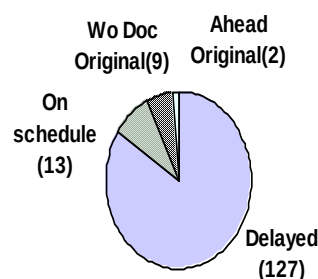

Investment Scenario

The total cost of implementation of 151 projects when sanctioned, was of the order of Rs 43916.82 Crores but this was subsequently revised to Rs. 44119.51 Crores. The expenditure incurred on these projects till January, 2010 is Rs. 27818.31 Crores.

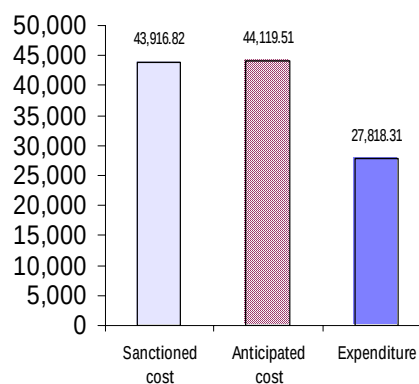


8. Sector: - Shipping and Ports

Number of Projects	20
Number of Projects on schedule	9
Number of Projects Delayed	7
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 9 projects are on schedule, 7 projects are delayed, 2 projects are ahead and 2 projects are without date of commissioning.



Investment Scenario

The total cost of implementation of 20 projects when sanctioned, was of the order of Rs.18154.63 Crores but this was subsequently revised to Rs. 18426.49 Crores. The expenditure incurred on these projects till Jan, 2010 is Rs. 3943.71 Crores.

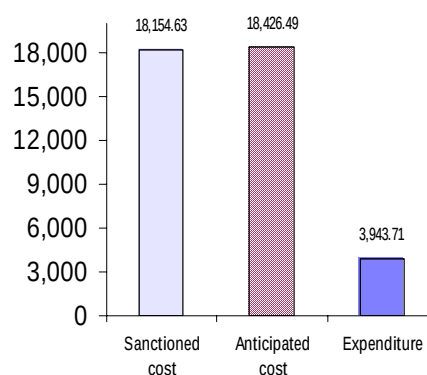


9. Sector: - Steel

Number of Projects	28
Number of Projects on schedule	3
Number of Projects Delayed	22
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 3 projects are on schedule, 22 projects are delayed and 3 projects are without date of commissioning .



Investment Scenario

The total cost of implementation of 28 projects when sanctioned, was of the order of Rs. 45473.36 Crores but this was subsequently revised to Rs. 50679.38 Crores. The expenditure incurred on these projects till January, 2010 is Rs. 18707.24 Crores.

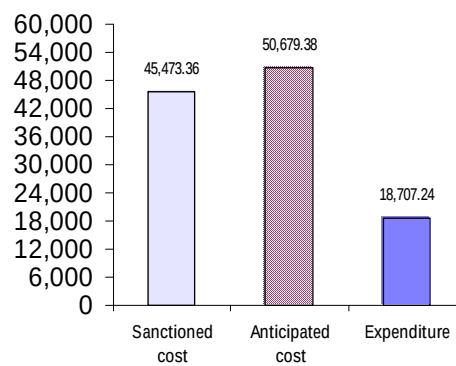


10. Sector: - Telecommunications

Number of Projects	29
Number of Projects Delayed	12
Number of Projects Wo_Doc_Original	17


Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 12 projects are delayed and 17 projects are with our date of commissioning.



Investment Scenario

The total cost of implementation of 29 projects when sanctioned, was of the order of Rs 11916.06 Crores but this was subsequently revised to Rs. 11534.73 Crores. The expenditure incurred on these projects till January, 2010 is Rs 3702.06 Crores.

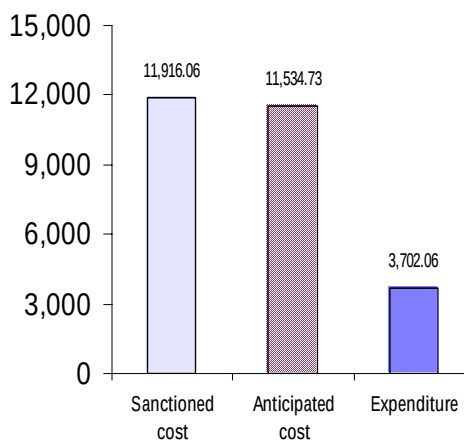

(Jan,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL) - [020100042]	04/2002	3,072.00	3,072.00	2,109.00	02/2008	02/2010	24(O)	0/75
2	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,508.00	10/2009 09/2007	03/2010	30(R1)	0/75
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	12,571.00	12/2008	03/2011	27(O)	0/119
4	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	467.22	04/2011	04/2011	0(O)	0/0
5	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,247.73	09/2010	09/2011	12(O)	0/80
Total			25,054.29	26,308.29	19,902.95				0/349
<u>Civil Aviation</u>									
6	Construction of New Integrated Terminal Building - [N04000052]	10/2006	147.00	147.00	125.52	09/2008 02/2009	10/2009	8(R2)	0/0
7	C/O PASSENGER LOUNGE BIRSI AIRPORT - [N04000057]	03/2006	108.07	108.07	130.02	08/2008	10/2009	14(O)	0/0
8	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING - [N04000016]	10/2006	245.58 295.00	245.58	224.79	12/2008	12/2009	12(O)	0/28
9	C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR - [N04000034]	03/2008	129.65 135.72	129.65	35.92	09/2009 03/2010	03/2010	0(R3)	0/0
10	C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA - [N04000035]	03/2008	135.04	135.04	58.25	09/2009	03/2010	6(O)	0/0
11	Construction of New Integrated Passenger Terminal - [N04000042]	03/2006	129.38	129.38	47.16	04/2009 10/2009	03/2010	5(R2)	0/0
12	Construction of New Expandable Modular Integrated - [N04000047]	03/2008	135.72	135.72	31.20	09/2009 12/2009	03/2010	3(R2)	0/0
13	Construction of New Integrated terminal building - [N04000051]	04/2007	128.96	128.96	53.91	02/2009 06/2009	03/2010	9(R2)	0/0
14	C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE - [N04000036]	02/2008	135.60	135.60	44.76	10/2009	05/2010	7(O)	0/0
15	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	143.97	06/2010	06/2010	0(O)	0/0
16	C/o new Integrated terminal Bldg. at Birsu Munda - [N04000049]	01/2009	137.79	137.79	12.50	01/2010 02/2010	06/2010	4(R2)	0/0
17	C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A - [N04000039]	08/2008	144.94	144.94	21.86	04/2010	12/2010	8(O)	0/1
18	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE - [N04000038]	08/2008	1,273.00 1,212.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	245.58	05/2011	05/2011	0(O)	0/0
20	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	227.34	02/2009	-	-	0/24
21	C/o new Airport-SH: E/W in cutting and filling geogrid - [N04000050]	01/2009	264.29	264.00	15.02	01/2011	-	-	0/0
22	DEV. OF KAMRAJ DOMESTIC CHENNAI AIRPORT - [N04000056]	08/2008	1,808.00	1,808.00	417.36	01/2011	-	-	0/0
23	GAGAN PROJECT - [N04000065]	09/2008	393.60	393.60	160.29	06/2013	-	-	0/0
Total			8,085.05	8,084.76	2,250.69				0/53
<u>Coal</u>									
24	EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC) - [060100088]	10/2004	2,161.28	2,295.93	1,767.74	06/2009	02/2010	8(O)	0/23
25	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07	254.60	211.48	06/2009	02/2010	8(O)	0/21
26	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	956.59	03/2010	03/2010	0(O)	0/7
27	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53	1,268.53	767.80	03/2010	03/2010	0(O)	0/6
28	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88	789.88	134.46	03/2010	03/2010	0(O)	0/1
29	BHARATPUR OC EXPANSION PHASE-III PROJECT - [N06000030]	02/2007	131.39	131.39	382.90	03/2010	03/2010	0(O)	0/0
30	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	473.97	03/2009	03/2010	12(O)	0/0
31	KTK OC Sector-I - [N06000077]	01/2008	91.50	115.33	115.33	09/2010	03/2010	-6(O)	0/0
32	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,373.06	06/2009	09/2010	15(O)	0/26
33	LAKHANPUR OC EXP. PROJECT PH-II - [N06000069]	03/2004	98.74	116.54	247.82	03/2007	03/2011	48(O)	0/0
34	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,905.58	06/2009	06/2011	24(O)	0/24
35	JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II - [N06000057]	02/2009	122.35	122.35	-	03/2010	12/2011	0(R3)	0/0
36	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18	287.17	-	11/2009	01/2012	0(R3)	0/0
37	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	57.90	03/2010	03/2012	24(O)	0/4
38	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66	341.63	100.54	03/2011	03/2012	12(O)	0/0
39	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04	746.04	134.83	03/2012	03/2012	0(O)	0/1
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	249.03	31.43	03/2012	03/2012	0(O)	0/0
41	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	-	03/2012	03/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	249.85	03/2012	03/2012	0(O)	0/0
43	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	542.84	08/2012	08/2012	0(O)	0/0
44	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34	779.26	18.65	03/2013	09/2012	-6(O)	0/11
45	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63	453.63	42.48	12/2012	12/2012	0(O)	0/0
46	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	581.69	03/2011 03/2013	03/2013	0(R3)	0/4
47	MAGADH OC (CCL) - [N06000015]	07/2006	469.78	706.40	12.12	07/2012	03/2013	8(O)	0/1
48	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78	467.78	11.29	03/2013	03/2013	0(O)	0/7
49	KANIHA OCP - [N06000035]	12/2007	457.77	457.77	48.96	03/2012	03/2013	12(O)	0/0
50	NARAYANKURI UG - [N06000059]	02/2009	149.06	149.06	-	03/2013	03/2013	0(O)	0/0
51	CHITRA EAST OCP - [N06000060]	08/2007	112.69	112.69	-	11/2010	03/2013	28(O)	0/0
52	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93	479.53	175.35	03/2013	03/2013	0(O)	0/0
53	BINA EXTN. PROJ - [N06000019]	11/2006	168.97	168.97	135.46	03/2014	11/2013	-4(O)	0/1
54	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04	1,352.04	26.98	03/2014	03/2014	0(O)	0/1
55	CHURCHA UG - [N06000046]	06/2008	462.35	462.35	270.62	06/2014	03/2014	-3(O)	0/0
56	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	3.14	03/2010	03/2014	48(O)	0/0
57	PENGANGA OC - [N06000066]	10/2008	339.77	339.77	-	03/2014	03/2014	0(O)	0/0
58	KARTALI (EAST) OC - [N06000076]	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
59	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87	395.87	22.73	03/2013	03/2015	24(O)	0/0
60	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0
61	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
62	BAROUD OC EXPANSION - [N06000065]	07/2008	135.58	135.58	23.32	03/2015	03/2015	0(O)	0/0
63	JAGANNATHPOR OC - [N06000075]	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
64	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	56.52	03/2014	03/2016	24(O)	0/0
65	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	5.32	03/2015	03/2016	12(O)	0/0
66	AUGMENTATION OF PRODUCTION AT SAPRI UG MINE - [N06000058]	09/1987	147.86	147.86	25.50	03/2012	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		26,110.40	28,183.41	10,914.25				0/138
	<u>Mines</u>								
67	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	0/111
	Total		4,091.51	4,091.51	3,316.00				0/111
	<u>Steel</u>								
68	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	68.46	01/2010	01/2010	0(O)	0/0
69	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89	607.17	206.09	10/2009	10/2009	0(O)	0/21
70	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	164.48	08/2009	02/2010	6(O)	0/0
71	REBUILDING OF BLAST FURNACE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	497.49	08/2009	03/2010	7(O)	0/0
72	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	102.03	10/2009	03/2010	5(O)	0/0
73	COAL DUST INJECTION IN BF-2 and 3 - [120100069]	04/2006	132.73	133.92	86.34	05/2008	04/2010	23(O)	0/2
74	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	234.87	09/2009	06/2010	9(O)	0/0
75	ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE - [N12000049]	06/2008	124.88	119.88	46.80	12/2009	06/2010	6(O)	0/0
76	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,294.03	03/2010	06/2010	3(O)	0/0
77	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	42.02	06/2010	06/2010	0(O)	0/0
78	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	225.32	06/2009	07/2010	13(O)	0/0
79	Pulverised coal injection system for bf-1&2 - [N12000037]	11/2007	125.00	133.00	36.47	09/2009	08/2010	11(O)	0/0
80	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	84.40	12/2009	08/2010	8(O)	0/0
81	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	80.00	02/2010	08/2010	6(O)	0/0
82	Air Separation Plant(ASU-5) - [N12000052]	06/2008	129.50	145.00	6.64	12/2010	12/2010	0(O)	0/0
83	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	114.32	02/2010	01/2011	11(O)	0/0
84	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	146.77	04/2010	04/2011	12(O)	0/0
85	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	244.30	232.93	48.40	07/2009	05/2011	22(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
86	INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S - [N12000034]	10/2007	105.33	116.33	10.00	08/2009	05/2011	21(O)	0/0
87	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	5,523.00	10/2009	06/2011	20(O)	0/126
88	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	12.00	10/2009	06/2011	20(O)	0/0
89	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	6,085.01	07/2010	06/2011	11(O)	0/0
90	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	4.04	09/2010	12/2011	15(O)	0/0
91	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,316.00	812.56	12/2010	12/2011	12(O)	0/0
92	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	6,878.00	1,146.79	02/2011	03/2013	25(O)	0/0
93	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	5,516.00	1,421.42	05/2011	03/2013	22(O)	0/0
94	COKING COAL FACILITIES IN COAL HANDLING PLANT - [N12000010]	09/2006	133.91	134.32	103.00	03/2008	-	-	0/3
95	INSTALLATION OF MSDS-V AND TRANSMISSION NETWORK F - [N12000022]	05/2007	143.02	143.02	104.49	11/2008	-	-	0/0
Total			45,473.36	50,679.38	18,707.24				0/152
Petroleum									
96	CLEAN FUELS PROJECT AT VISAKH REFINERY (HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	43(O)	0/45
97	CRUDE OIL RECEIPT FACILITIES, KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.00	09/2009	12/2009	3(O)	0/0
98	CHENNAI-BANGALORE PIPELINE - [N16000029]	07/2007	232.11	273.00	227.75	07/2009	12/2009	5(O)	0/0
99	MSQ UPGRADE PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	750.71	12/2009	01/2010	1(O)	0/0
100	SHORT TERM LOW COST MUMBAI REFINERY - [N16000082]	12/2006	390.00	230.00	164.51	01/2010	01/2010	0(O)	0/0
101	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00 2,869.00	2,869.00	2,454.13	04/2009 12/2009	02/2010	2(R1)	0/36
102	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66 350.00	389.00	320.18	06/2008	02/2010	20(O)	0/0
103	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	186.58	12/2009	02/2010	2(O)	0/0
104	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]	09/2009	2,591.80 3,941.41	3,941.41	2,176.19	12/2009	02/2010	2(O)	0/0
105	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	12,138.00	14,439.00	10,968.78	09/2009 11/2009	03/2010	4(R1)	0/101
106	CHAINSAR-JHAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77	565.00	369.08	09/2009	03/2010	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
107	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13	396.13	-	10/2009	03/2010	5(O)	0/0
108	BINA DESPATCH TERMINAL - [N16000078]	05/2007	490.71	639.11	520.92	12/2009	03/2010	3(O)	0/0
109	BINA KOTA PIPE LINE PROJECT - [N16000079]	07/2007	405.82	405.82	277.56	12/2009	03/2010	3(O)	0/0
110	LPG PROCESSING & COMPRESSION - [N16000041]	08/2007	142.00	139.07	57.04	10/2009	04/2010	6(O)	0/0
111	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	3,039.32	11/2009 04/2010	04/2010	0(R3)	0/0
112	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70	706.70	102.23	04/2010	04/2010	0(O)	0/0
113	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16	2,800.00	1,557.81	12/2008	05/2010	17(O)	0/0
114	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90	1,030.00	576.70	04/2009	05/2010	13(O)	0/0
115	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	-	03/2009	05/2010	14(O)	0/0
116	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	173.95	05/2010	05/2010	0(O)	0/0
117	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	306.39	05/2010	05/2010	0(O)	0/0
118	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]	06/2006	1,431.91	1,675.72	1,218.02	09/2009	06/2010	9(O)	0/0
119	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00	6,898.00	4,774.04	01/2010	06/2010	5(O)	0/0
120	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30	2,305.30	1,144.34	06/2010 06/2010	06/2010	0(R1)	0/0
121	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00	372.00	163.13	02/2010	06/2010	4(O)	0/0
122	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00	356.00	143.77	02/2010	06/2010	4(O)	0/0
123	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00	1,492.00	543.11	04/2010	06/2010	2(O)	0/0
124	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60	293.60	129.22	12/2009	06/2010	6(O)	0/0
125	TWO PIPELINE REPLACEMENT PROJECT AT AHMEDABAD MEHS - [N16000042]	03/2008	188.18	143.84	-	06/2010	06/2010	0(O)	0/0
126	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	493.93	09/2009	06/2010	9(O)	0/0
127	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92	1,493.49	595.34	06/2006 05/2008	07/2010	26(R1)	0/2
128	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA - [N16000017]	06/2005	806.00	1,007.83	593.33	03/2008 12/2009	08/2010	8(R1)	0/48
129	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07	1,816.07	-	10/2010	10/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
130	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07 -	281.07	-	10/2010 -	10/2010	0(O)	0/0
131	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38 -	3,000.00	-	10/2010 -	10/2010	0(O)	0/0
132	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00 -	1,212.85	-	10/2011 -	10/2010	-12(O)	0/0
133	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00 -	224.00	37.24	12/2010 -	12/2010	0(O)	0/0
134	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40 605.40	605.40	103.23	12/2010 12/2010	12/2010	0(R3)	0/18
135	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]	06/2008	304.40 -	304.40	32.06	12/2010 -	12/2010	0(O)	0/0
136	CAPACITY AUGMENTATION OF AGRA& FERROZABAD REGION - [N16000074]	07/2009	199.57 -	199.57	-	01/2011 -	01/2011	0(O)	0/0
137	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	600.00	523.08	03/2007 03/2010	03/2011	12(R3)	0/3
138	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 834.90	1,200.00	987.26	03/2007 03/2011	03/2011	0(R3)	0/6
139	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	219.22	142.38	03/2006 -	03/2011	60(O)	0/6
140	NORTH TAPTI GAS FIELD DEV. - [N16000085]	07/2008	589.70 -	589.70	-	03/2011 -	03/2011	0(O)	0/0
141	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75 -	8,061.42	3,818.71	06/2009 -	04/2011	22(O)	0/0
142	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93 -	1,061.78	-	11/2011 -	04/2011	-7(O)	0/0
143	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08 -	305.08	-	04/2011 -	04/2011	0(O)	0/0
144	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82 1,262.93	1,262.93	1,231.40	03/2005 -	05/2011	74(O)	0/0
145	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40 -	333.40	-	05/2010 05/2010	05/2011	12(R3)	0/0
146	BNPL superlines(Uttranchal & Punjab) - [N16000091]	12/2009	540.92 -	540.92	-	05/2011 -	05/2011	0(O)	0/0
147	VKPL Upgradation and Laying of Superlines - [N16000092]	12/2009	463.32 -	463.32	-	05/2011 -	05/2011	0(O)	0/0
148	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00 -	349.00	3.58	08/2011 -	08/2011	0(O)	0/0
149	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00 -	267.00	26.60	08/2011 -	08/2011	0(O)	0/0
150	Construction of Tanks and Blending Facility at Vad - [N16000077]	02/2009	267.00 -	349.00	26.60	08/2011 -	08/2011	0(O)	0/0
151	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00 -	3,597.00	49.88	09/2011 -	09/2011	0(O)	0/0
152	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00 -	3,284.00	54.39	09/2011 -	09/2011	0(O)	0/0
153	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00 -	756.00	139.59	12/2011 -	12/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
154	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35	1,797.35	-	12/2011	12/2011	0(O)	0/0
155	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11	370.11	-	04/2011	12/2011	8(O)	0/0
156	HYDROCRACKER REVAMP & SETTING - [N16000081]	02/2008	825.00	825.00	48.11	12/2011	12/2011	0(O)	0/0
157	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	06/2007	736.65	736.65	0.10	12/2011	12/2011	0(O)	0/0
158	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64	2,163.64	-	12/2011	12/2011	0(O)	0/0
159	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT. - [N16000070]	07/2009	238.68	238.68	-	01/2012	01/2012	0(O)	0/0
160	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	266.78	03/2010 03/2012	03/2012	0(R1)	0/0
161	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 5,633.44	5,633.44	-	03/2010 08/2010	03/2012	19(R1)	0/0
162	Integrated crude Oil handling facilities at Paradip - [N16000090]	12/2009	1,492.33	1,492.33	16.97	06/2012	03/2012	-3(O)	0/0
163	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63	2,920.82	5.24	02/2009 09/2010	04/2012	19(R1)	0/0
164	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29 6,326.40	6,326.40	188.14	05/2010	05/2012	24(O)	0/0
165	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2012	22(O)	0/0
166	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	478.71	09/2012	09/2012	0(O)	0/0
167	Paradip-Sambalpur-Raipur-Ranchi Pipeline - [N16000088]	08/2009	1,793.00	1,793.00	4.07	09/2012	09/2012	0(O)	0/0
168	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	29,777.00	2,581.72	03/2012	11/2012	8(O)	0/0
169	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00	3,032.00	-	12/2012	12/2012	0(O)	0/0
170	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43	4,543.43	-	12/2012	12/2012	0(O)	0/0
171	De-bottlenecking of SMPL - [N16000089]	12/2009	1,584.00	1,584.00	1.51	-	12/2012	-	0/0
172	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18	7,596.18	-	01/2013	01/2013	0(O)	0/0
173	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	-	03/2013	03/2013	0(O)	0/0
Total			150,389.80	171,409.05	48,683.77				0/265
Power									
174	SIPAT-II SUPP. TRANS. SYSTEM (PGCIL) - [180100257]	06/2005	813.67	777.15	783.41	06/2008	11/2009	17(O)	0/22
175	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,016.74	897.10	09/2007	01/2010	28(O)	0/36

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
176	SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL) - [180100253]	05/2005	279.30 -	340.14	286.17	07/2009 -	02/2010	7(O)	0/18
177	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-V - [N18000017]	06/2006	721.25 -	721.25	554.71	06/2009 -	02/2010	8(O)	0/19
178	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72 -	836.14	319.14	07/2006 -	03/2010	44(O)	0/5
179	NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL) - [180100247]	01/2005	691.83 -	913.33	713.51	12/2007 -	03/2010	27(O)	0/20
180	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34 -	241.27	128.27	06/2008 -	03/2010	21(O)	0/20
181	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	1,896.65	1,498.82	11/2008 -	03/2010	16(O)	0/38
182	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]	12/2005	3,779.46 -	3,779.46	3,241.96	09/2009 -	03/2010	6(O)	0/30
183	KOLDAM HEP TRANSMISSION LINE (PGCIL) - [180100263]	09/2005	464.91 -	464.91	162.16	09/2008 09/2008	03/2010	18(R1)	0/22
184	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]	06/2006	803.70 -	803.76	553.94	06/2009 -	03/2010	9(O)	0/20
185	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96 -	975.96	498.78	10/2009 -	03/2010	5(O)	0/20
186	SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN - [N18000020]	10/2006	150.26 -	153.24	109.35	10/2009 -	03/2010	5(O)	0/20
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI - [N18000021]	01/2007	186.95 -	186.95	146.14	07/2009 -	03/2010	8(O)	0/21
188	ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST - [N18000026]	10/2006	103.80 -	103.80	70.07	06/2009 -	03/2010	9(O)	0/0
189	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 1,007.16	1,007.16	725.60	12/2007 -	06/2010	30(O)	0/18
190	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52 -	227.52	90.72	06/2010 -	06/2010	0(O)	0/0
191	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49 -	290.49	221.38	04/2010 -	06/2010	2(O)	0/0
192	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23 -	5,221.23	1,962.04	07/2010 -	07/2010	0(O)	0/20
193	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57 -	353.57	38.88	07/2010 -	07/2010	0(O)	0/0
194	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50 -	2,448.49	1,777.50	02/2010 -	08/2010	6(O)	0/24
195	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	477.69	266.01	09/2010 -	09/2010	0(O)	0/0
196	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10 -	262.10	126.06	09/2010 -	09/2010	0(O)	0/0
197	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33 -	5,135.33	3,599.20	10/2010 -	10/2010	0(O)	0/40

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
198	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44	2,570.44	1,491.00	08/2010	11/2010	3(O)	0/26
199	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72	340.72	98.18	11/2010	11/2010	0(O)	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55	261.55	85.89	11/2010	11/2010	0(O)	0/0
201	SYSTEM STRENGTHENING SCHEME-VIII OF SOUTHERN REGION - [N18000070]	02/2008	105.84	105.84	51.33	11/2010	11/2010	0(O)	0/0
202	KOTESHWAR HEP (THDC) - [180100184]	04/2000	1,301.56	1,301.56	1,487.95	04/2005	12/2010	68(O)	0/0
203	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63	1,405.63	1,033.14	08/2010	12/2010	4(O)	0/0
204	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01	611.02	404.57	08/2010	12/2010	4(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76	417.76	206.78	12/2010	12/2010	0(O)	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36	408.36	243.46	12/2010	12/2010	0(O)	0/0
207	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89	230.89	5.58	01/2011	01/2011	0(O)	0/0
208	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92	1,279.40	1,032.85	03/2007	02/2011	47(O)	0/25
209	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29	1,724.79	971.14	11/2009	02/2011	15(O)	0/0
210	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26	621.28	358.71	02/2011	02/2011	0(O)	0/0
211	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]	10/2006	238.25	238.25	165.77	-	05/2011	-	0/0
212	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	2,434.30	05/2011	05/2011	0(O)	0/0
213	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,304.52	865.27	10/2010	06/2011	8(O)	0/0
214	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24	557.25	276.07	01/2010	06/2011	17(O)	0/22
215	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	38.25	06/2011	06/2011	0(O)	0/0
216	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	62.80	06/2011	06/2011	0(O)	0/0
217	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	261.65	07/2011	07/2011	0(O)	0/0
218	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	133.39	07/2011	07/2011	0(O)	0/0
219	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	8.77	07/2011	07/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
220	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,307.03	634.93	09/2009	08/2011	23(O)	0/0
221	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIV - [N18000057]	02/2009	132.19	132.19	9.62	08/2011	08/2011	0(O)	0/0
222	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	14.90	08/2011	08/2011	0(O)	0/0
223	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97	328.97	46.66	09/2011	09/2011	0(O)	0/0
224	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39	8,323.39	6,547.60	12/2009	10/2011	22(O)	0/56
225	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48	520.48	99.63	11/2011	11/2011	0(O)	0/0
226	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66	509.66	3.50	11/2011	11/2011	0(O)	0/0
227	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69	317.69	2.51	11/2011	11/2011	0(O)	0/0
228	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19	184.19	11.86	11/2011	11/2011	0(O)	0/0
229	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15	4,527.15	2,980.60	04/2009	12/2011	32(O)	0/41
230	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01	623.44	60.45	01/2012	01/2012	0(O)	0/0
231	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35	4,375.35	801.00	07/2011	02/2012	7(O)	0/0
232	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96	664.96	18.55	02/2012	02/2012	0(O)	0/0
233	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50	409.50	-	02/2012	02/2012	0(O)	0/0
234	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29	410.29	27.86	02/2012	02/2012	0(O)	0/0
235	SYSTEM STRENGTHENING SCHEME-IX OF SOUTHERN REGIONA - [N18000060]	02/2009	120.62	120.62	7.53	02/2012	02/2012	0(O)	0/0
236	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32	1,347.32	116.73	02/2012	02/2012	0(O)	0/0
237	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03	2,047.03	757.30	01/2012	03/2012	2(O)	0/10
238	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]	12/2008	573.99	573.99	77.90	08/2012	08/2012	0(O)	0/0
239	MOUDA STPP - [N18000048]	11/2007	5,459.28	5,459.28	708.10	02/2012	08/2012	6(O)	0/0
240	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95	2,360.95	603.88	08/2012	08/2012	0(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
241	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33	7,075.33	1,285.07	08/2012	08/2012	0(O)	0/0
242	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12	4,824.12	249.55	10/2012	10/2012	0(O)	0/0
243	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00	5,915.00	411.80	11/2012	11/2012	0(O)	0/0
244	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81	6,230.81	364.92	11/2012	11/2012	0(O)	0/0
245	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33	6,285.33	3,596.26	09/2010	12/2012	27(O)	0/11
246	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	358.42	6.09	12/2008 09/2010	12/2012	27(R1)	0/15
247	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	0/34
248	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	364.96	12/2012	12/2012	0(O)	0/0
249	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,919.59	2,612.40	09/2009	03/2013	42(O)	0/20
250	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	714.70	03/2013	03/2013	0(O)	0/31
251	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	252.91	07/2010	04/2013	33(O)	0/0
252	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	1,033.97	05/2013	05/2013	0(O)	0/161
253	BARH STTP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	642.00	08/2013	08/2013	0(O)	0/0
254	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	356.78	08/2013	08/2013	0(O)	0/0
255	BARH STTP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,573.80	11/2010	10/2013	35(O)	0/51
256	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	93.25	06/2013	03/2015	21(O)	0/0
257	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	215.69	07/2014	01/2016	18(O)	0/0
258	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
Total			165,980.96	170,607.00	61,373.69				0/916
Health & Family Welfare									
259	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	477.33	03/1999 03/2005	-	-	0/16
Total			71.18	443.15	477.33				0/16
Railways									

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
260	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]	04/1993	100.41	949.22	148.45	12/2009	12/2009	0(O)	0/0
261	HAPUR-KANKATHER (LD),NR - [220100278]	04/2003	106.64	106.64	139.06	03/2007	05/2008	14(O)	0/0
262	AMROHA-KANKATHER,NR - [N22000058]	04/2000	57.00	103.57	106.47	03/2005	05/2009	8(R3)	0/0
263	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50	246.50	-	03/2009	11/2009	8(R3)	0/0
264	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00	214.09	113.40	12/2009	12/2009	0(O)	0/0
265	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70	142.48	98.84	12/2008	12/2009	12(O)	0/0
266	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74	224.51	41.39	-	12/2009	-	0/0
267	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44	209.57	153.00	03/2009	02/2010	11(O)	0/0
268	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00	634.13	456.48	03/1995	03/2010	180(O)	0/0
269	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21	265.00	265.33	03/1998	03/2010	144(O)	0/0
270	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00	170.00	99.32	03/2002	03/2010	96(O)	0/0
271	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00	571.55	567.85	-	03/2010	-	0/0
272	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00	816.40	693.99	03/2001	03/2010	108(O)	0/0
273	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94	281.20	68.64	-	03/2010	-	0/0
274	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85	960.48	976.28	03/2003	03/2010	84(O)	0/0
275	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00	501.69	278.12	-	03/2010	-	0/0
276	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00	425.90	122.25	-	03/2010	16(R3)	0/0
277	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00	502.14	459.07	-	03/2010	-	0/0
278	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00	639.54	753.18	06/2007	03/2010	33(O)	0/0
279	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63	219.00	115.17	-	03/2010	-	0/0
280	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00	610.07	532.11	-	03/2010	13(R1)	0/0
281	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74	479.00	-	-	03/2010	12(R1)	0/0
282	KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR - [220100300]	04/1995	49.84	136.45	131.28	03/2002	03/2010	96(O)	0/0
283	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92	168.80	4.77	-	03/2010	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
284	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 -	227.52	-	03/2008 03/2009	03/2010	12(R1)	0/0
285	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 137.56	137.57	134.52	03/1998 08/2005	03/2010	55(R3)	0/0
286	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	211.90	-	- 03/2009	03/2010	12(R1)	0/0
287	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	322.87	35.59	- -	03/2010	-	0/0
288	PODAPAHAR-BANSPANI,(LD)(SER) - [N22000046]	04/2006	129.74 129.74	129.74	126.50	03/2006 -	03/2010	48(O)	0/0
289	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	-	03/2008 06/2008	03/2010	21(R3)	0/0
290	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	158.95	218.78	- -	03/2010	-	0/0
291	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 654.51	1,160.52	434.32	- -	06/2010	-	0/0
292	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	296.20	216.60	04/2003 03/2010	06/2010	3(R1)	0/0
293	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	-	12/2006 -	06/2010	42(O)	0/0
294	BARAMATI - LONAND (NL), CR - [220100271]	03/1998	75.00 138.48	138.48	35.75	- -	06/2010	-	0/0
295	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	243.40	-	- 02/2009	06/2010	16(R1)	0/0
296	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	221.90	-	12/2007 03/2010	07/2010	4(R1)	0/0
297	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
298	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	-	- -	09/2010	-	0/0
299	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]	02/1999	180.73 320.66	335.00	297.15	12/2006 12/2008	11/2010	23(R3)	0/0
300	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 -	273.00	-	- 03/2009	11/2010	20(R1)	0/0
301	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	-	02/2015 -	11/2010	-51(O)	0/0
302	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	262.88	03/2004 -	12/2010	81(O)	0/0
303	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	672.38	650.02	- -	12/2010	-	0/0
304	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 479.20	567.00	193.47	- 12/2009	12/2010	12(R1)	0/0
305	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	135.10	-	- -	12/2010	-	0/0
306	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 716.64	718.30	-	03/2008 08/2008	12/2010	28(R1)	0/0
307	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	254.47	03/2009 12/2008	12/2010	24(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
308	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	245.15	4.00	12/2010 -	12/2010	0(O)	0/0
309	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,174.00	3,182.58	12/2010 -	12/2010	0(O)	0/0
310	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	323.40	02/2010 -	02/2011	12(O)	0/0
311	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38 -	1,000.00	79.07	- -	02/2011	-	0/0
312	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 810.78	810.78	32.36	- -	02/2011	-	0/0
313	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	356.87	183.42	- 03/2010	03/2011	12(R1)	0/0
314	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 284.27	475.00	276.51	06/1999 -	03/2011	141(O)	0/0
315	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	50.70	- -	03/2011	-	0/0
316	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	456.45	240.05	06/2004 -	03/2011	81(O)	0/0
317	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	381.10	05/2008 -	03/2011	34(O)	0/0
318	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	341.81	- 06/2009	03/2011	21(R3)	0/0
319	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	25.89	- -	03/2011	-	0/0
320	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	371.36	234.34	- -	03/2011	-	0/0
321	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
322	NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I - [N22000078]	09/2007	99.84 99.84	110.94	77.17	03/2010 -	03/2011	12(O)	0/0
323	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
324	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.30	03/2011 -	03/2011	0(O)	0/0
325	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97 -	196.97	36.78	03/2011 -	03/2011	0(O)	0/0
326	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 252.50	252.50	-	02/2010 -	11/2011	21(O)	0/0
327	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44 576.27	587.08	628.48	- -	12/2011	-	0/0
328	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
329	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	496.03	26.97	03/2010 -	12/2011	21(O)	0/0
330	LUMDING-SILCHAR(GC),NEFR - [220100170]	04/1996	648.00 1,676.31	4,074.10	1,965.78	03/2009 -	03/2012	36(O)	0/0
331	DLW GM 4000 / 3000 HP DIESEL LOCOS - [220100226]	04/1999	155.54 -	141.40	103.18	03/2003 -	03/2012	108(O)	0/0
332	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 238.56	234.45	57.84	- -	03/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
333	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41	322.95	40.56	-	03/2012	-	0/0
			-			-			
334	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59	495.74	61.49	-	03/2012	-	0/0
			-			-			
335	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90	324.90	-	03/2010	03/2012	24(O)	0/0
			324.90			-			
336	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69	501.69	45.90	03/2010	03/2012	24(O)	0/0
			-			-			
337	TAMLUK DIGHA - [N22000097]	03/1984	293.97	293.97	298.27	06/2005	04/2012	82(O)	0/0
			-			-			
338	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00	921.00	236.87	03/2009	12/2012	45(O)	0/0
			-			-			
339	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47	1,480.71	445.84	10/2007	12/2012	62(O)	0/0
			-			-			
340	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20	687.20	-	03/2010	12/2012	33(O)	0/0
			-			-			
341	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84	410.08	88.28	-	03/2013	-	0/0
			-			-			
342	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00	899.42	535.46	-	03/2013	-	0/0
			280.00			-			
343	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70	1,556.23	158.87	-	03/2013	-	0/0
			915.70			-			
344	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00	3,087.44	1,682.94	04/2008	03/2014	27(R1)	0/0
			1,500.00			12/2011			
345	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00	1,502.29	424.34	12/2008	03/2014	63(O)	0/0
			733.00			-			
346	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00	160.48	72.47	-	03/2014	-	0/0
			156.00			-			
347	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00	546.47	0.54	-	03/2014	-	0/0
			200.00			-			
348	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00	5,300.00	120.00	03/2014	03/2014	0(O)	0/0
			-			-			
349	AGARTALA SABROOM - [N22000099]	04/2008	813.34	813.34	15.03	03/2014	03/2014	0(O)	0/0
			-			-			
350	BHAIRABI SAIRONG - [N22000100]	04/2008	619.34	619.34	0.59	04/2014	04/2014	0(O)	0/0
			-			-			
351	SEVOK RANGPO - [N22000102]	04/2008	1,339.48	1,339.48	-	12/2015	12/2015	0(O)	0/0
			-			-			
352	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56	2,492.53	129.76	03/2011	03/2016	60(O)	0/0
			727.53			-			
353	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	11,270.00	5,956.55	03/2001	12/2017	201(O)	0/0
			8,000.00			-			
354	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77	432.46	433.90	03/1994	-	-	0/0
			274.56			-			
355	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43	617.63	312.05	-	-	-	0/0
			407.78			-			
356	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53	564.50	471.30	03/1996	-	-	0/0
			193.61			06/2009			

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
357	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00	318.66	452.61	03/1999 03/2003	-	-	0/0
358	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	231.68	-	-	-	0/0
359	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00	968.60	0.43	-	-	-	0/0
360	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00	412.91	42.86	-	-	-	0/0
361	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	-	-	-	0/0
362	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00	511.86	413.02	03/1998	-	-	0/0
363	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40	563.25	535.40	03/2004 03/2005	-	-	0/0
364	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 450.00	730.00	216.45	-	-	-	0/0
365	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00	274.29	71.76	-	-	-	0/0
366	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.11	290.22	-	-	-	0/0
367	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	247.05	02/2009	-	-	0/0
368	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00	103.72	4.65	-	-	-	0/0
369	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22	268.00	-	12/1999 03/2008	-	-	0/0
370	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	-	-	-	0/0
371	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	-	-	-	-	0/0
372	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	89.61	03/2007 03/2007	-	-	0/0
373	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00	363.26	0.27	07/2008	-	-	0/0
374	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19	1,099.20	540.09	07/2005	-	-	0/0
375	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	-	-	-	0/0
376	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	62.05	-	-	-	0/0
377	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00	497.63	477.14	-	-	-	0/0
378	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	126.86	-	-	-	0/0
379	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15	381.17	80.12	-	-	-	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
380	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
381	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	3.99	- -	-	-	0/0
382	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	374.84	- -	-	-	0/0
383	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
384	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	901.62	0.28	- -	-	-	0/0
385	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	325.17	278.36	03/2005 12/2008	-	-	0/0
386	SURAT-KOSAMBA (LD),WR - [220100281]	04/2000	133.00 -	133.00	-	- -	-	-	0/0
387	TANUR (KUTTIPURAM) GURUVAYUR (NL) (SR) - [220100283]	04/1995	40.00 -	137.71	9.71	- -	-	-	0/0
388	REWARI-SADULPUR-HISSAR (GC),NWR - [220100290]	04/1997	198.96 364.19	410.00	377.20	- -	-	-	0/0
389	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	459.91	36.40	- -	-	-	0/0
390	BARBIGHA - SHEKHPURA + NEORA-DANIAWAN (NL), ECR - [220100309]	04/2002	120.23 -	120.23	220.17	- -	-	-	0/0
391	BIHARSHARIFF-BARBIGHA (NL), ECR - [220100310]	04/2001	103.86 -	103.86	28.93	- -	-	-	0/0
392	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	104.79	34.13	- -	-	-	0/0
393	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	230.44	03/2006 -	-	-	0/0
394	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	1,225.00	109.16	- -	-	-	0/0
395	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	104.10 -	113.75	40.35	- -	-	-	0/0
396	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
397	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73 -	230.03	45.76	- -	-	-	0/0
398	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	102.78	- -	-	-	0/0
399	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
400	BHATNI-JIRADEI PATCH DOUBLING (NER) - [N22000029]	04/2006	100.27 -	100.27	0.01	- -	-	-	0/0
401	MUNDERWA-BABHNAN PATCH DOUBLING(NER) - [N22000030]	04/2006	102.10 -	102.10	22.75	- -	-	-	0/0
402	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	670.00	0.74	- -	-	-	0/0
403	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92 261.70	261.70	0.08	02/2006 -	-	-	0/0
404	SETTING UP EAST COAST RLY.ZN. (SER) - [N22000054]	04/1997	41.67 -	129.78	90.84	- -	-	-	0/0
405	PATTABIRAM-ARAKKONAM,SR - [N22000057]	04/2002	71.94 -	124.00	151.76	03/2004 07/2008	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
406	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDIA' - [N22000079]	09/2007	404.19 404.19	711.15	38.83	- -	-	-	0/0
407	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 343.17	639.00	163.05	- -	-	-	0/0
408	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00 170.00	255.96	75.34	- -	-	-	0/0
409	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 125.00	227.40	11.32	- -	-	-	0/0
410	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 456.00	582.83	24.27	- -	-	-	0/0
411	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00 300.00	529.88	20.46	- -	-	-	0/0
412	BHAKURA DAMODAR - [N22000098]	03/1998	282.70 -	325.17	274.56	07/2008 -	-	-	0/0
413	KISHANGANJ JALALGARH - [N22000101]	04/2008	282.92 -	359.86	0.10	- -	-	-	0/0
414	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 254.07	676.00	288.03	- 12/2011	06/2011	-6(R3)	0/0
415	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08 353.08	1,010.00	45.16	- 12/2012	12/2012	0(R3)	0/0
416	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	168.42	- 12/2012	12/2012	0(R1)	0/0
Total			53,764.93 -	100,114.94	38,101.27				0/0
Road Transport & Highways									
417	JAWAHARLAL NEHRU PORT PHASE-II,SH-54 - [N24000039]	04/2000	143.00 -	143.00	-	05/2007 -	10/2009	29(O)	0/0
418	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93 -	440.93	-	12/2006 -	12/2009	36(O)	0/0
419	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39 -	534.39	-	05/2007 -	12/2009	31(O)	0/0
420	BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5) - [240101151]	04/2000	140.85 -	140.85	148.17	01/2004 -	12/2009	71(O)	0/0
421	TOVARAMKURCHI-MADURAI,NH45B (NHAI) - [N24000054]	04/2000	263.00 -	263.00	-	08/2008 -	12/2009	16(O)	0/0
422	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80 -	402.80	453.70	03/2009 -	12/2009	9(O)	0/0
423	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00 -	465.00	30.66	04/2009 -	12/2009	8(O)	0/0
424	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93 -	467.93	-	03/2005 -	01/2010	58(O)	0/0
425	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50 -	196.50	-	06/2008 -	01/2010	19(O)	0/0
426	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00 -	450.00	-	07/2008 -	01/2010	18(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
427	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	-	05/2009	02/2010	9(O)	0/0
428	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]	03/2005	557.00	557.00	-	02/2010	02/2010	0(O)	0/0
429	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	418.14	03/2005	03/2010	60(O)	0/0
430	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40	372.40	396.04	07/2004	03/2010	68(O)	0/0
431	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	401.82	03/2005	03/2010	60(O)	0/0
432	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	240.89	07/2004	03/2010	68(O)	0/0
433	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	-	11/2007	03/2010	28(O)	0/0
434	DEVDHARI-KELAPUR - [240106207]	12/2003	144.00	144.00	95.12	07/2005	03/2010	56(O)	0/0
435	BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7 - [240106210]	12/2003	110.00	110.00	105.70	06/2005	03/2010	57(O)	0/0
436	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00	276.00	343.51	04/2008	03/2010	23(O)	0/0
437	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00	310.00	371.65	04/2008	03/2010	23(O)	0/0
438	MADURAI -KANIYAKUMARI SECTION (NS-41/TN) NH-7, KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.84	03/2008	03/2010	24(O)	0/0
439	MADURAI -KANNIYAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	314.50	03/2008	03/2010	24(O)	0/0
440	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	568.50	03/2009	03/2010	12(O)	0/0
441	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	367.74	02/2009	03/2010	13(O)	0/0
442	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	665.80	12/2008	03/2010	15(O)	0/0
443	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00	261.00	-	08/2008	03/2010	19(O)	0/0
444	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	137.10	06/2008	03/2010	21(O)	0/0
445	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	03/2010	17(O)	0/0
446	SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4) - [N24000029]	12/2003	100.50	100.50	160.97	04/2008	03/2010	23(O)	0/0
447	SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS - [N24000086]	03/2005	110.00	110.00	113.49	07/2008	03/2010	20(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
448	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]	12/2003	360.42	360.42	438.00	11/2009	03/2010	4(O)	0/0
449	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]	03/2005	445.00	445.00	719.60	07/2010	03/2010	-4(O)	0/0
450	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	108.41	08/2006	04/2010	44(O)	0/0
451	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]	03/2005	168.00	168.00	227.74	12/2008	04/2010	16(O)	0/0
452	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	163.51	08/2009	04/2010	8(O)	0/0
453	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	168.42	08/2009	04/2010	8(O)	0/0
454	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	222.40	08/2009	04/2010	8(O)	0/0
455	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	144.81	08/2009	04/2010	8(O)	0/0
456	CHITRADURGA BY PASS (GQ) KM.207-KM.189 (NH-4) - [240101134]	04/2000	104.00	104.00	143.38	08/2004	05/2010	69(O)	0/0
457	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	-	01/2009	05/2010	16(O)	0/0
458	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	510.08	04/2009	05/2010	13(O)	0/0
459	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	64.42	05/2010	05/2010	0(O)	0/0
460	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	122.06	09/2007	06/2010	33(O)	0/0
461	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	47.34	08/2004	06/2010	70(O)	0/0
462	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	406.66	11/2007	06/2010	31(O)	0/0
463	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	144.43	08/2005	06/2010	58(O)	0/0
464	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	262.59	10/2008	06/2010	20(O)	0/0
465	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	287.60	10/2008	06/2010	20(O)	0/0
466	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	325.95	10/2008	06/2010	20(O)	0/0
467	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	238.61	10/2008	06/2010	20(O)	0/0
468	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	292.12	10/2008	06/2010	20(O)	0/0
469	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	408.96	04/2008	06/2010	26(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
470	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	533.81	03/2009	06/2010	15(O)	0/0
471	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	787.61	11/2010	06/2010	-5(O)	0/0
472	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	342.00	06/2008	06/2010	24(O)	0/0
473	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	359.65	06/2008	06/2010	24(O)	0/0
474	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	189.13	10/2008	06/2010	20(O)	0/0
475	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	144.10	07/2008	06/2010	23(O)	0/0
476	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	391.84	06/2008	06/2010	24(O)	0/0
477	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	06/2010	15(O)	0/0
478	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	155.79	11/2008	06/2010	19(O)	0/0
479	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	533.50	06/2009	06/2010	12(O)	0/0
480	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	189.54	02/2004	06/2010	76(O)	0/0
481	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	191.72	09/2009	06/2010	9(O)	0/0
482	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	203.10	09/2008	06/2010	21(O)	0/0
483	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	301.43	06/2010	06/2010	0(O)	0/0
484	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	223.00	03/2010	06/2010	3(O)	0/0
485	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]	12/2003	407.60	407.60	177.60	06/2010	06/2010	0(O)	0/0
486	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	240.10	09/2009	06/2010	9(O)	0/0
487	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	164.00	06/2010	06/2010	0(O)	0/0
488	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	44.98	08/2004	07/2010	71(O)	0/0
489	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	111.60	03/2008	07/2010	28(O)	0/0
490	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	83.56	03/2008	07/2010	28(O)	0/0
491	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	148.82	06/2008	07/2010	25(O)	0/0
492	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.40	07/2010	07/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
493	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	321.10	07/2010	07/2010	0(O)	0/0
494	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	631.90	07/2010	07/2010	0(O)	0/0
495	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	666.70	03/2010	07/2010	4(O)	0/0
496	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	-	04/2004	08/2010	76(O)	0/0
497	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	99.85	06/2008	08/2010	26(O)	0/0
498	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	250.80	08/2010	08/2010	0(O)	0/0
499	LUCKNOW-BYPASS (EW) (NS & EW-PH-I) NH-25 & NH-28 VIA NH-56 - [240103192]	04/2000	182.52	111.78	0.52	06/2004	09/2010	75(O)	0/0
500	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	249.75	03/2005	09/2010	66(O)	0/0
501	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	214.80	09/2009	09/2010	12(O)	0/0
502	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	184.60	09/2009	09/2010	12(O)	0/0
503	LUMDING TO DABOKA - [N24000110]	12/2003	130.00	130.00	45.56	08/2010	09/2010	1(O)	0/0
504	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	275.60	09/2010	09/2010	0(O)	0/0
505	KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7 - [240102202]	01/2004	120.00	120.00	84.51	09/2006	10/2010	49(O)	0/0
506	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	164.40	10/2008	10/2010	24(O)	0/0
507	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	172.18	10/2009	10/2010	12(O)	0/0
508	KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20,NH-1A - [240102193]	04/2000	110.00	110.00	142.24	12/2004	12/2010	72(O)	0/0
509	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	-	04/2007	12/2010	44(O)	0/0
510	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00	275.00	-	09/2007	12/2010	39(O)	0/0
511	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	129.09	09/2007	12/2010	39(O)	0/0
512	JAM-WADNER - [240106209]	12/2003	145.00	145.00	68.18	07/2005	12/2010	65(O)	0/0
513	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	91.60	06/2005	12/2010	66(O)	0/0
514	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	276.40	05/2008	12/2010	31(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
515	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00 -	227.00	205.72	10/2008 -	12/2010	26(O)	0/0
516	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68 -	340.68	213.33	03/2008 -	12/2010	33(O)	0/0
517	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	280.00	114.18	02/2009 -	12/2010	22(O)	0/0
518	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	199.81	27.66	04/2009 -	12/2010	20(O)	0/0
519	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	167.64	39.49	11/2008 -	12/2010	25(O)	0/0
520	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	155.04	27.96	11/2008 -	12/2010	25(O)	0/0
521	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	200.00	55.40	04/2009 -	12/2010	20(O)	0/0
522	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00 -	225.00	86.47	06/2008 -	12/2010	30(O)	0/0
523	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]	12/2003	195.00 -	195.00	85.85	06/2008 -	12/2010	30(O)	0/0
524	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00 -	242.00	286.26	12/2008 -	12/2010	24(O)	0/0
525	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00 -	227.00	254.70	12/2008 -	12/2010	24(O)	0/0
526	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]	12/2003	237.80 -	237.80	86.79	06/2008 -	12/2010	30(O)	0/0
527	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30 -	151.30	100.10	10/2008 -	12/2010	26(O)	0/0
528	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43 -	203.43	95.49	10/2008 -	12/2010	26(O)	0/0
529	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]	12/2003	251.03 -	251.03	62.13	10/2008 -	12/2010	26(O)	0/0
530	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91 -	229.91	29.18	10/2008 -	12/2010	26(O)	0/0
531	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00 -	322.00	254.27	06/2009 -	12/2010	18(O)	0/0
532	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	53.52	04/2008 -	12/2010	32(O)	0/0
533	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72 -	264.72	75.54	06/2008 -	12/2010	30(O)	0/0
534	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	227.00	03/2008 -	12/2010	33(O)	0/0
535	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	82.87	04/2008 -	12/2010	32(O)	0/0
536	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	113.13	06/2008 -	12/2010	30(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
537	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	106.16	04/2008	12/2010	32(O)	0/0
538	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	54.05	05/2008	12/2010	31(O)	0/0
539	NALBARI TO BIJNI (AS-9) - [N24000050]	12/2003	142.00	142.00	113.51	06/2008	12/2010	30(O)	0/0
540	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	78.52	06/2008	12/2010	30(O)	0/0
541	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	34.11	09/2007	12/2010	39(O)	0/0
542	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.32	07/2009	12/2010	17(O)	0/0
543	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	63.87	04/2010	12/2010	8(O)	0/0
544	PANIPAT TO PANCHI GUJRAN, NH-1 - [N24000066]	12/2003	109.00	109.00	138.90	10/2008	12/2010	26(O)	0/0
545	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	176.32	02/2010	12/2010	10(O)	0/0
546	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	404.32	10/2009	12/2010	14(O)	0/0
547	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	189.26	12/2009	12/2010	12(O)	0/0
548	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	12/2010	5(O)	0/0
549	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	-	02/2004	12/2010	82(O)	0/0
550	TRICHY - DINDIGUAL NH-45 - [N24000099]	03/2005	576.00	576.00	173.00	07/2010	01/2011	6(O)	0/0
551	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	266.60	01/2011	01/2011	0(O)	0/0
552	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	207.70	01/2011	01/2011	0(O)	0/0
553	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	102.80	09/2007	02/2011	41(O)	0/0
554	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	182.61	07/2005	03/2011	68(O)	0/0
555	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	207.19	07/2005	03/2011	68(O)	0/0
556	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	153.18	10/2008	03/2011	29(O)	0/0
557	FORBESGANJ TO SIMRAHI (NH-57)(NHA) - [240106294]	12/2003	332.94	332.94	134.40	09/2008	03/2011	30(O)	0/0
558	LALITPUR TO SAGAR, NH-26 (NHA) - [240106299]	12/2003	198.00	198.00	100.84	11/2008	03/2011	28(O)	0/0
559	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	224.54	09/2008	03/2011	30(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
560	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108])	12/2003	232.45	232.45	80.84	09/2010	03/2011	6(O)	0/0
561	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	414.40	05/2010	05/2011	12(O)	0/0
562	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	46.66	09/2008	06/2011	33(O)	0/0
563	KELARPUR-PIMPALKATTI-KM 153 TO KM 175 - [240106283]	12/2003	117.40	117.40	29.83	11/2008	06/2011	31(O)	0/0
564	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	-	07/2012	07/2012	0(O)	0/0
565	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	6.05	05/2010	08/2012	27(O)	0/0
566	DEVDHARI-WADNER - [240106208]	12/2003	145.00	145.00	24.71	07/2005	-	-	0/0
567	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]	12/2003	300.00	300.00	-	10/2008	-	-	0/0
Total			43,916.82	44,119.51	27,818.31				0/0
Shipping & Ports									
568	CONSTRUCTION OF CAR /CLEAN CARGO TERMINAL - [N25000034]	01/2009	100.00	100.00	0.50	01/2010	01/2010	0(O)	0/0
569	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	72.76	12/2005	03/2010	51(O)	0/0
570	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	406.28	03/2010	03/2010	0(O)	0/0
571	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	290.01	04/2009	03/2010	11(O)	0/0
572	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	129.62	06/2007 01/2009	04/2010	15(R1)	0/0
573	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	318.24	07/2010	07/2010	0(O)	0/0
574	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	813.75	10/2008	11/2010	25(O)	0/0
575	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	241.64	11/2010	11/2010	0(O)	0/0
576	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
577	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
578	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	882.00	0.16	02/2011	02/2011	0(O)	0/0
579	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	702.00	0.73	03/2011	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
580	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	211.21	04/2011	04/2011	0(O)	0/0
581	Acquisition of two nos. of 120 B.P - [N25000042]	04/2009	2,908.48	2,908.48	58.18	03/2011	06/2011	3(O)	0/0
582	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	374.36	04/2011	12/2011	8(O)	0/0
583	Acquisition of Two nos. of 3060 DWT - [N25000043]	04/2009	2,770.32	2,770.42	554.06	09/2011	12/2011	3(O)	0/0
584	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
585	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
586	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.63	10/2008	-	-	0/0
587	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
Total			18,154.63	18,426.49	3,943.71				0/0
Telecommunications									
588	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	10/2009	46(O)	0/0
589	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	34(O)	0/0
590	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007	11/2009	33(O)	0/0
591	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007	12/2009	34(O)	0/0
592	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	93.99	10/2007	12/2009	26(O)	0/0
593	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	12/2009	20(O)	0/0
594	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	15(O)	0/0
595	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	422.85	12/2008	12/2009	12(O)	0/0
596	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	113.34	03/2009	12/2009	9(O)	0/0
597	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	483.54	470.24	12/2008	12/2009	12(O)	0/0
598	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	180.93	03/2009	12/2009	9(O)	0/0
599	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	366.00	-	09/2009	12/2009	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
600	500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB - [N26000038]	04/2007	134.25	133.75	34.05	06/2008 12/2009	01/2010	1(R3)	0/0
601	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	169.33	12/2008	01/2010	13(O)	0/0
602	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	278.16	278.16	175.77	12/2008 12/2009	01/2010	1(R3)	0/0
603	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	110.83	03/2009	01/2010	10(O)	0/0
604	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]	01/2009	149.15	149.15	40.87	06/2009	01/2010	7(O)	0/0
605	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	336.81	64.50	01/2009	01/2010	12(O)	0/0
606	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.23	12/2004	02/2010	62(O)	0/0
607	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	463.61	104.60	12/2009 12/2009	03/2010	3(R3)	0/0
608	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	161.35	02/2008	05/2010	27(O)	0/0
609	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	73.54	09/2009	06/2010	9(O)	0/0
610	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	06/2010	10(O)	0/0
611	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53 2.00	180.53	22.42	12/2009	06/2010	6(O)	0/0
612	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
613	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	135.00	94.77	06/2006	-	-	0/0
614	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
615	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]	11/2008	350.00	350.00	-	-	-	-	0/0
616	CENTRALISED TRANSMISSION NMS - [N26000064]	08/2009	300.00	300.00	-	-	-	-	0/0
Total			11,916.06	11,534.73	3,702.06				0/0
<u>Urban Development</u>									
617	C/O GENERAL POOL OFFICE COMPLEX AT INA - [N28000016]	10/2004	83.67	135.03	-	02/2010	02/2010	0(O)	0/0
618	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00 8,605.36	8,676.00	12,228.48	06/2010	10/2010	4(O)	0/7
619	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 8,158.00	6,395.00	1,636.20	12/2011 09/2012	12/2011	-9(R3)	0/0
Total			14,596.67	15,206.03	13,864.68				0/7

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Water Resources</u>									
620	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			568,148.56	650,395.25	253,091.44				
									0/2007
