

**303rd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
January, 2011**



Teesta Low Dam Project



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -6
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	7-12
List of Delete Projects	13
Summary of Projects	14-22
Sector wise Trend and Graphicalf Analysis	23-35
Sector wise analysis of projects	36-65
Graph	66-77
Statewise Summary of All Ongoing Projects	78
List of Abbreviations	79-80

EXECUTIVE SUMMARY

The Flash Report for January 2011 (the 303rd Flash Report) contains information on the status of 563 projects in the Central Sector, each costing ` 150 Crores and above. During January 2011, 20 projects reported completion (which have now been dropped from the monitor of this Ministry) and 7 (seven) new projects have been added.

The online submission of the implementation Status Report of the ongoing projects has been improving, 100% projects are reported online during the current month. Sector-wise number of ongoing projects along with status of online reporting is given below:

S. No.	Sector	Projects on monitor	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	125	16
2.	RAILWAYS	146	3
3.	POWER	79	10
4.	PETROLEUM	68	11
5.	COAL	45	1
6.	TELECOMMUNICATION	41	1
7.	STEEL	14	4
8.	SHIPPING & PORTS	23	2
9.	CIVIL AVIATION	8	3
10.	FERTILISERS	6	0
11.	ATOMIC ENERGY	3	0
12.	URBAN DEVELOPMENT	3	1
13.	MINES	1	0
14.	WATER RESOURCES	1	0
Total		563	52

2. During January 2011, fifty two (52) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 72 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road

Transport and Highways, Telecommunications, Shipping & Ports, Urban Development and Civil Aviation Sectors.

3. Out of 563 projects, 9 projects are ahead of schedule, 122 are on schedule and 289 projects are delayed. Of the balance, 84 projects do not have fixed dates of commissioning i.e. neither the year of commissioning nor the tentative gestation period of the projects have been reported. A large number of projects (59) have been sanctioned without any commissioning schedule/date. The concerned ministries have been asked to fix the date of commissioning at the earliest.

4. The total original cost of implementation of the 563 projects was of the order of ` 5,88,252.31 Crores and their anticipated completion cost was ` 7,09,713.17 Crores, which reflects a cost overrun of 20.30%. The expenditure incurred on these projects till January, 2011 is ` 3,09,117.75 Crores.

5. Out of 563 projects, presently on the monitor at the end of January 2011, 9 projects were ahead of schedule, 122 projects were on schedule (22%), 289 projects were delayed (51%) (this excludes the 84 projects without date of commissioning and those that have not reported during the month). During the month, 52 projects have reported additional delays in the range of 1-72 months. The analysis of pictorial presentation shows that during current month, the project reporting delays have marginally decreased to 289 from 295 reported in December'2010. The overall cost overrun has been somewhat constant since September 2010. It may be seen that out of 289 delayed projects, at the end of January, 2011, 69 projects had overall delay in the range of 1 to 12 months, 73 projects had delay in the range of 13 to 24 months, 112 projects had delay in the range of 25 to 60 months and 34 projects had time overrun of 61 months and above.

6. In the **Coal sector**, the Barsingsar TPS Project has reported additional delay of Two month due to delay in slow progress by contractor.

7. In the **Steel Sector**, 4 projects have reported additional delays in the range of 1-13 months. Rebuilding of Coke Oven Battery No-6 (BSP) SAIL has reported an additional delay of 2 months due to delay in supply of fireclay & silica brick by the contractor. AIR Separation Plant (ASU-4) RINL has reported an additional delay of 3 months due to delay in prolongation of the project beyond the contractual schedule. Development of Bailadila Iron Ore Deposit – II (B) NMDC has reported additional delay of 4 months due to delay in Site conditions, scope of design work has changed and also the Maoist activities is disrupting the progress of works.

Expansion of Visag Steel Plant from 3 MTPY – 6.3 MTPY of Liquid Steel of RINL has reported additional delay of 13 months due to delay in change in scope and change in site conditions.

8. In the **Petroleum Sector**, 11 projects have reported additional delays in the range of 1-72 months. Residue Upgradation and MS/HSD Quality Improvement project of IOCL and BNPL Superlines (Uttranchal & Punjab) of GAIL have reported additional delay of one month each, However no specific reasons have been given. Bawana Nangal Pipe line Project of GAIL has reported additional delays of 2 months due to delay in Row. Compressor Stations (Kailaras & Chainsa) and Compressor station (Vijaypur & Jhabua) Phase I of project GAIL has reported on additional delay of 2 months and 6 months respectively due to delay in electrical and instrumentation works. VKPL Upgradation and Laying of Spur line (to Bhilwara and Chittorgarh) of GAIL has reported on additional delay of 2 months due to delay in survey report. BNPL Superlines (Uttranchal & Punjab) of GAIL permission needs from the Supreme Court for laying of pipeline. Additional Development of D-1 Field project of ONGC has reported additional delay of 6 months due to pending Court case. Improved Oil Recovery project of Rudrasagar, Improved Oil Recovery, Lakwa- Lakhmani and Improved Oil Recovery, Geleki of ONGC have additional delays of 24 months, 36 months and 72 months due to law & order problem in the North East Region.

In the **Power Sector**, 10 projects have reported additional delays in the range of 1-37 months. East – West Transnission corridor Strengthening Scheme of PGCIL has reported additional delay of 1 month due to delay in final environment clearance is awaited. Eastern Region Strengthening Scheme II of PGCIL has reported additional delay of 1 month due to delay in ROW problem. Transmission System for Startup Power to DVC & Maithon RB G of PGCIL has reported additional delay of 1 month due to forest clearance of about 13 hq for Bihar portion in Koderma –Bihar Shariff line is awaited. System Strenghtening in Northern GRID for Karcham Wangto PGCIL, Transmission System Associated with Chamera III HEP PGCIL and the Establishment of 400/220 KV GIS Pooling Station Near Chamera PGCIL have reported additional delay of 1 month, 1 month and 2 months respectively but no specific reason have been given. Sipat STPP Stage – I NTPC has reported additional delay of 3 months due to delay in supply of Turbo generator and auxiliary equipments supply by M/s Power

Machine. Simhadri STPP Stage-II NTPC has reported additional delay of 7 months due to delay in supply of Turbine and in handing over civil works respectively. Tripura Gas Based Power Project of NEEPCO has reported additional delay of 18 months due to delay in the approval of RCE. Kameng Hydroelectric Project of NEEPCO has reported additional delay of 37 months due to slow progress of tunnel boring and sudden geological surprises poor ventilation system reducing

10. In the **Road Transport and Highways Sector**, 16 projects have reported additional delay in the range of 1-16 months. 6 projects have reported additional delay of one month each due to slow progress of work by the contractor. GONDE-VADAPE(Thane), NH-3 of NHAI has reported additional delay of 2 months due to delay in Forest clearance, Land acquisition, & utility shifting. Thrissur to Angamali (NH-47) Bangalore, Hoskote Mudbogal Section, NH-4 of NHAI have reported additional delay of 2 months each due to delay in land acquisition. Ayodhya-Lucknow , NH-28 of NHAI has reported additional delay of 3 due to delay in handing over encumbrance free site . Gorakhpur-Ayodhya NH-28 of NHAI and Ayodhya Lucknow , NH-28 of NHAI has reported additional delay of 3 months each due to delay in forest clearance and land acquisition problems. Napur-Kondhali, NH-6 and Siliguri to Islampur of NHAI have reported additional delay of 5 months and 16 months due to delay in land acquisition. Dholpur-Morena Section (including Chambol Bridge) of NHAI has reported additional delay of 6 months due to delay in obtaining wild life clearance. Gurgaon – Kotputli of NHAI has reported additional delay of 8 months, however, the project authorities has not mentioned any specific reason for such additional delay.

11. In the **Urban Development Sector**, Delhi MRTS Phase –II Project DMRC has reported additional delay of two months due to land and Rehabilitation problem and late release of fund.

12. In the **Railway Sector**, 3 projects have shown additional delay in the range of 1-9 months. Gonda-Gorakhpur Loop with Anand Nagar, Nautanwa GC NER has reported additional delay of 3 months due to slow progress of work. Kottur- Harihar, ((NL) SWR has reported additional delay of 6 months, due to finalization of site condition. However, . Ramanagram –Mysore line doubling with electrification of SWR has reported additional delay of 9 months due to increased in electrical loops .

13. In the **Telecommunication Sector**, Convergent Billing and CRM (Mumbai of MTNL) has reported additional delay of 3 months due to delay in supply of equipment.

14. In the **Shipping & Ports Sector**, 2 projects have shown additional delays of the range of 2 months namely Establishment of Vessel Traffic Services in Gulf of Kutch has reported additional delay of 2 months due to slow progress by the a contractor/ , .Setting of NG Regasification Terminal at Puthu Port Trust has reported 2 months, however, no specific reason has been given.

15. In the **Civil Aviation Sector**, 3 projects have shown additional delay in the range of 1-2 months. Construction of New International Terminal Building A AAI has reported additional delay of 1 month due to slow progress of work. Construction of RCC/PRE Stressed Concrete Bridge K3 AAI and Extension of Secondary Runway (K2) AAI have reported additional delay of 1 month and 2 months, However, no specific reasons have been given.

The status as on 01.01.2011 in respect of completion of projects costing ` 150 Crores and above in different sectors during 2010-11 is indicated in the Report.



(Pankaj Jain)

**Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation**

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	146	3
2	Road Transport & Highways	125	16
3	Power	79	10
4	Petroleum	68	11
5	Coal	45	1
6	Telecommunications	41	1
7	Shipping & Ports	23	2
8	Steel	14	4
9	Civil Aviation	8	3
10	Fertilisers	6	0
11	Atomic Energy	3	0
12	Urban Development	3	1
13	Mines	1	0
14	Water Resources	1	0
	Total	563	52

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	168.33	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93
September,2010				
<u>Coal</u>				
8	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)(NEYVELI LIGNITE CORPORATION) - [060100090]	254.07	06/2009	1,687.78
<u>Steel</u>				
9	REBUILDING OF COKE OVEN BATTERY-10(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000016]	416.50	09/2009	305.14
<u>Petroleum</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
10	PANIPAT NAPHTHA CRACKER PROJECT(INDIAN OIL CORPORATION LIMITED) - [160100292]	12,138.00	09/2009	12,054.37
11	DADRI- PANIPAT R-LNG SPUR PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000018]	250.66	06/2008	350.96
12	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000026]	638.90	04/2009	796.21
13	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE(INDIAN OIL CORPORATION LIMITED) - [N16000034]	348.00	12/2009	186.58
14	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000035]	1,131.00	12/2009	750.71
15	CHAINS- JHAJJAR PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000047]	967.77	09/2009	416.90
16	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000067]	643.46	-	726.45
17	Construction of Tank and Blending Facility at Vadi(INDIAN OIL CORPORATION LIMITED) - [N16000075]	267.00	-	72.99
18	BINA DESPATCH TERMINAL(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000078]	490.71	12/2009	590.52
<u>Railways</u>				
19	HOSPET-GUNTAKAL(LD),SCR(RAIL VIKAS NIGAM LTD.) - [220100195]	105.22	12/1999	283.49
20	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100224]	536.85	03/2003	1,005.50
21	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)(RAIL VIKAS NIGAM LTD.) - [220100244]	223.00	-	586.85
22	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000033]	352.00	03/2008	616.44
23	ABOHAR- FAZILKA, NR, NL(NORTHERN RAILWAY) - [N22000055]	86.44	03/2009	201.79
<u>Road Transport & Highways</u>				
24	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100203]	440.93	12/2006	641.40
25	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100204]	534.39	05/2007	716.15
26	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101178]	372.40	07/2004	406.05
27	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101181]	467.93	03/2005	453.64
28	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101187]	399.75	03/2005	424.96
29	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106227]	276.00	04/2008	360.00
30	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106228]	310.00	04/2008	392.26
31	MADURAI - KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106241]	507.49	03/2008	342.80
32	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106257]	556.00	03/2009	568.50

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
33	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106273]	469.80	12/2008	665.80
34	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106285]	261.00	08/2008	286.30
35	TOVARAMKURCHI-MADURAI,NH45B (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000054]	263.00	08/2008	317.74
36	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000060]	402.80	03/2009	453.70
37	PADALUR-TRICHY, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000083]	320.00	05/2009	636.10
38	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000093]	360.42	11/2009	478.40
39	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000105]	450.00	07/2008	876.61
40	ISLAM NAGAR TO KADTAL(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000109]	546.83	03/2010	667.80
41	WAINGANGA BRIDGE -CHHATISGARH-MAHARASHTRA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000120]	424.00	09/2010	298.40
<u>Shipping & Ports</u>				
42	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS(SHIPPING corp. of india) - [N25000013]	411.32	03/2010	406.28
43	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA(PORT TRUST) - [N25000046]	2,118.00	11/2004	.00
<u>Telecommunications</u>				
44	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I(DEPARTMENT OF TELECOMMUNICATION) - [260100051]	279.97	12/2004	136.24
45	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA(BHARAT SANCHAR NIGAM LIMITED) - [260100095]	1,174.75	03/2006	371.41
46	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000026]	741.77	10/2007	151.37
47	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-(BHARAT SANCHAR NIGAM LIMITED) - [N26000028]	364.52	-	51.44
48	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000042]	409.21	12/2008	470.24
49	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000061]	180.53	12/2009	25.97

October,2010

Health & Family Welfare

50	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS(HEALTH & FAMILY WELFARE) - [210100001]	71.18	03/1999	547.78
----	---	-------	---------	--------

Railways

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
51	DHARMAVARAM-PAKALA (GC), SCR(SOUTH CENTRAL RAILWAY) - [220100282]	200.00	-	567.49
<u>Road Transport & Highways</u>				
52	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106268]	263.00	02/2009	420.80
53	AMRITSAR-WAGHA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000121]	205.88	06/2010	214.90
<u>Shipping & Ports</u>				
54	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE(SHIPPING crp. of india) - [N25000029]	1,658.59	07/2010	1,657.45
<u>Telecommunications</u>				
55	GSM BASED NETWORK EXPANSION PLAN PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000034]	239.19	04/2008	96.97
56	Provision of data network for CWG delhi(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000076]	488.76	10/2010	198.65
57	Expn of existing 2G & 3G GSM N/W by 750k(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000077]	180.53	06/2010	40.92
58	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph(BHARAT SANCHAR NIGAM LIMITED) - [N26000079]	577.35	09/2010	40.76
November,2010				
<u>Petroleum</u>				
59	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL)(INDIAN OIL CORPORATION LIMITED) - [160100289]	1,876.00	04/2009	2,747.34
60	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA(INDIAN OIL CORPORATION LIMITED) - [N16000017]	806.00	03/2008	840.06
<u>Power</u>				
61	SEWA- II H.E.P (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100220]	665.46	09/2007	982.76
62	NORTHERN REGION SYSTEM STRENGTHENING-XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000034]	417.76	12/2010	266.87
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000036]	408.36	12/2010	304.83
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000039]	261.55	11/2010	143.36
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000055]	525.14	07/2011	354.99
<u>Railways</u>				
66	RAJGIR-TILAIYA (NL), ECR(EAST CENTRAL RAILWAYS) - [220100312]	180.82	03/2006	272.46

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
67	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000079]	205.92	08/2009	204.50
68	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000080]	243.64	08/2009	256.40
<u>Telecommunications</u>				
69	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M(BHARAT SANCHAR NIGAM LIMITED) - [N26000051]	908.30	08/2009	211.83
70	CENTRALISED TRANSMISSION NMS(BHARAT SANCHAR NIGAM LIMITED) - [N26000064]	300.00	-	.00
December,2010				
<u>Petroleum</u>				
71	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000036]	372.00	-	229.04
72	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000037]	356.00	-	222.69
73	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000038]	1,492.00	04/2010	1,113.09
<u>Road Transport & Highways</u>				
74	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106302]	206.96	10/2008	281.90
75	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000078]	243.38	09/2008	286.40
76	BANGALORE-NEELAMANGAL NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000104]	445.00	07/2010	803.40
<u>Shipping & Ports</u>				
77	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS(SHIPPING corp. of india) - [N25000030]	586.58	11/2010	634.09
<u>Telecommunications</u>				
78	KOLKATA TELECOM DISTRICT PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000036]	208.50	09/2008	146.00
January,2011				
<u>Atomic Energy</u>				
79	KAIGA 3 and 4 UNITS (NPCIL)(NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100041]	4,213.00	10/2009	2,610.00
<u>Steel</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
80	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000025]	302.70	06/2009	244.97
81	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000035]	892.32	-	616.57
82	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS- II(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000036]	197.66	11/2009	130.32
83	POWER PLANT-I(RASTRIYA ISPAT NIGAM LIMITED) - [N12000039]	462.00	12/2009	84.40
84	EXPANSION OF SALEM STEEL PLANT(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000050]	1,902.00	06/2011	1,754.78
<u>Petroleum</u>				
85	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000048]	5,595.31	11/2009	3,326.01
<u>Power</u>				
86	KORBA STPP STAGE-III(NATIONAL THERMAL POWER CORPORATION) - [N18000011]	2,448.50	02/2010	2,119.00
87	National Capital Thermal Power Project Stage-II(NATIONAL THERMAL POWER CORPORATION) - [N18000013]	5,135.33	10/2010	4,062.00
88	WESTERN REGION STRENGTHENING SCHEME-VI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000038]	340.72	11/2010	164.37
<u>Railways</u>				
89	HOTGI-GADAG(GC),SWR(SOUTH WESTERN RAILWAY) - [220100125]	180.00	03/1999	360.21
90	BHILDI-SAMDARI (GC)(RAIL VIKAS NIGAM LTD.) - [220100291]	244.74	-	476.85
91	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN(GAUGE CONVERSION) - [N22000103]	100.41	12/2009	911.24
<u>Road Transport & Highways</u>				
92	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100206]	106.00	08/2006	141.70
93	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106202]	480.00	11/2007	846.20
94	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251- 293(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000076]	208.46	08/2009	197.80
95	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4- 3(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000077]	239.19	09/2009	224.80
96	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211- 251(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000081]	194.80	08/2009	179.70

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
September,2011				
<u>Road Transport & Highways</u>				
1	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N16000082]	300.00	10/2008	.00
November,2011				
<u>Civil Aviation</u>				
2	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N12000021]	535.00	06/2010	331.80


Summary of projects in the Flash Report for the month of January, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	575
Number of Projects completed/dropped/frozen in Previous Month	8
Number of Projects completed/dropped/frozen in Current Month	19
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	8
Number of Projects Added in Current Month	7
Number of Projects in Current Month	563

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 563 projects, 9 projects are ahead of schedule, 122 projects are on schedule and 289 projects are delayed. Of the balance, 84 projects do not have fixed dates of commissioning while 59 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

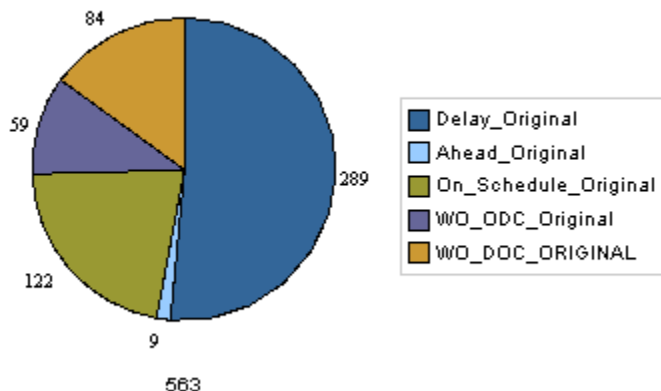

III. Investment Scenario

The Total Original cost of implementation of 563 projects when sanctioned, was of the order of Rs. 588252.31 crore but this was subsequently revised to Rs. 709713.17 crore implying a cost overrun of 20.6%. The expenditure incurred on these projects till January, 2011 is Rs. 309117.75 crore, which is 43.6% of the revised cost of the projects.

Figures are in Rs. Crore

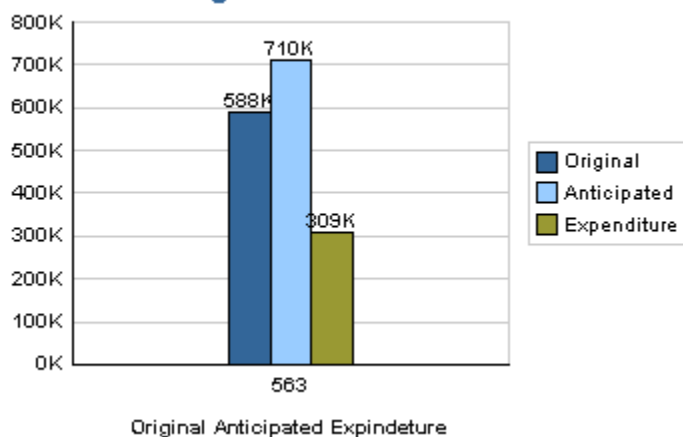

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	575
No of Projects Completed/Dropped/Frozen in Previous Month	8
No of Projects Completed/Dropped/Frozen in Current Month	19
No of Projects Having Anticipated Cost Greater than 150 Cr. In Current Months	8
No of Projects added in Current Month	7
No of Projects in Current Month	563

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original (Date)	289	9	122	59	84	563	51.33
Latest Approved (Date)	293	10	156	45	60	563	52.04

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	472	494,565.09	535,320.08	218,074.76	40.70	40,754.99	8.20
Latest Approved (RCE)	91	142,559.70	174,393.09	91,042.99	52.20	31,833.39	22.30
Total (RCE)	563	637,124.79	709,713.17	309,117.75	43.56	72588.38	11.39
Original Cost of All Projects							
Original Cost	563	588,252.31	709,713.17	309,117.75	43.60	121,460.86	20.60

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	289	307,176.36	381,428.82	219,159.63	57.50	74,252.46	24.20
Latest Approved (RCE)	293	308,303.15	359,000.67	210,698.07	58.70	50,697.52	16.40
Total	582	615,479.51	740,429.49	429,857.70	58.06	124949.98	20.30

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	52	64,232.28	81,376.64	61,804.38	75.90	17,144.36	26.70
Total	52	64,232.28	81,376.64	61,804.38	75.95	17144.36	26.69

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
LOKTAK D/S HEP(NHPC)	12/1999	578.62	06/2006	578.62	N.A.	28.33
<u>Railways</u>						
HOTGI-GADAG(GC),SWR	04/1994	180.00	03/1999	417.07	N.A.	360.21
BHILDI-SAMDARI (GC)	04/1999	244.74	N.A.	479.00	07/2010	476.85
<u>Road Transport & Highways</u>						
COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358	04/2000	106.00	08/2006	193.00	01/2011	141.70
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5	12/2003	480.00	11/2007	480.00	01/2011	846.20
<u>Steel</u>						
POWER PLANT-I	09/2007	462.00	12/2009	350.00	N.A.	84.40
<u>Petroleum</u>						
VIJAPUR DADRI-BAWANA PIPE LINE PROJECT	11/2007	5,595.31	11/2009	3,700.00	01/2011	3,326.01
<u>Power</u>						
KORBA STPP STAGE-III	08/2006	2,448.50	02/2010	2,448.49	12/2010	2,119.00
National Capital Thermal Power Project Stage-II	10/2006	5,135.33	10/2010	5,135.33	07/2010	4,062.00
WESTERN REGION STRENGTHENING SCHEME-VI	02/2008	340.72	11/2010	340.72	12/2010	164.37
<u>Railways</u>						
RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN	04/1993	100.41	12/2009	955.29	N.A.	911.24

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Road Transport & Highways</u>						
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293	12/2003	208.46	08/2009	208.46	01/2011	197.80
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3	12/2003	239.19	09/2009	239.19	01/2011	224.80
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251	12/2003	194.80	08/2009	194.80	01/2011	179.70
<u>Steel</u>						
EXPANSION OF SALEM STEEL PLANT	01/2008	1,902.00	06/2011	1,902.00	09/2010	1,754.78
SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II	01/2008	197.66	11/2009	197.66	10/2010	130.32
REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL	10/2007	892.32	N.A.	892.32	N.A.	616.57
INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA	07/2007	302.70	06/2009	302.70	10/2010	244.97
<u>Atomic Energy</u>						
KAIGA 3 and 4 UNITS (NPCIL)	05/2001	4,213.00	10/2009	4,213.00	12/2010	2,610.00

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Road Transport & Highways</u>					
Hazaribagh-Ranchi	8/2010	625.07	1/2013	625.07	1/2013
Hyderabad-yadgiri N.H no-202	8/2010	388.00	5/2012	388.00	5/2012
<u>Petroleum</u>					
Petrochemical Complex-II	8/2010	8,140.00	2/2014	8,140.00	2/2014
<u>Road Transport & Highways</u>					
Armur to kadloor yellareddy	2/2010	390.56	2/2012	390.56	2/2012
New 4 Lane elevated road from chennai airport	9/2010	1,655.00	9/2013	1,655.00	9/2013
Talegaon-amravati	11/2009	567.00	11/2013	567.00	11/2013
<u>Railways</u>					
Lumding-silchar jiribam, badarpur-baraigram kumarghat	4/1996	1,676.31	3/2009	3,909.49	12/2013

VII. Milestones (Cumulative due & achieved)

Total	1973
Achieved up to month	819

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Civil Aviation</u>						
CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A AAI	290.92	290.92	01/2011	01/2011	02/2011	1
CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 AAI	213.35	213.35	09/2010	02/2011	03/2011	1
Extension of Secondary Runway(K2) AAI	230.00	230.00	01/2011	01/2011	03/2011	2
<u>Coal</u>						
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	01/2011	03/2011	2
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) SAIL	172.78	172.78	01/2010	02/2011	04/2011	2
AIR SEPARATION PLANT (ASU-4) RINL	96.00	170.00	06/2010	12/2010	03/2011	3
Deve. of Bailadila Iron Ore Deposit- II(B)(NMDC) NMDC	295.89	607.17	N.A.	06/2011	10/2011	4
EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,499.00	10/2009	02/2011	03/2012	13
<u>Petroleum</u>						
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT IOCL	5,693.00	6,898.00	N.A.	01/2011	02/2011	1
BNPL superlines(Uttranchal & Punjab) GAIL	540.92	375.00	05/2011	10/2011	11/2011	1
BAWANA NANGAL PIPE LINE PROJECT GAIL	1,816.07	1,200.00	N.A.	04/2011	06/2011	2
COMPRESSOR STATIONS (KAILARAS & CHAINSA) GAIL	1,167.00	810.00	04/2011	04/2011	06/2011	2
VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI) GAIL	463.32	375.00	06/2011	06/2011	08/2011	2
BNPL SPURLINE (UTTRANCHAL & PUNJAB) GAIL	540.92	540.92	06/2011	06/2011	11/2011	5
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I GAIL	1,512.00	975.00	N.A.	04/2011	10/2011	6

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
ADDITIONAL DEV. OF D-1 FIELD ONGC	2,163.64	2,163.64	12/2011	12/2011	06/2012	6
IOR, RUDRASAGAR (ONGCL) ONGC	113.90	438.85	03/2006	03/2011	03/2013	24
IOR LAKWA - LAKHMANI (ONGCL) ONGC	345.10	663.69	03/2007	03/2011	03/2014	36
IOR GELEKI (ONGCL) ONGC	390.09	1,674.11	03/2007	03/2011	03/2017	72
Power						
EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME PGCIL	803.70	803.76	06/2009	02/2011	03/2011	1
EASTERN REGION STRENGTHENING SCHEME- II PGCIL	227.52	227.52	06/2010	02/2011	03/2011	1
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G PGCIL	290.49	299.08	04/2010	02/2011	03/2011	1
SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO PGCIL	328.97	328.97	09/2011	01/2011	02/2011	1
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	297.37	07/2011	02/2011	03/2011	1
EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER PGCIL	262.10	262.10	09/2010	01/2011	03/2011	2
SIPAT STPP STAGE - I (NTPC) NTPC	8,323.39	8,323.39	12/2009	12/2011	03/2012	3
SIMHADRI STPP STAGE -II (NTPC) NTPC	5,103.39	5,038.53	05/2011	05/2011	12/2011	7
TRIPURA GAS BASED POWER PROJECT NEEPCO	421.01	623.44	01/2012	01/2012	07/2013	18
KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	2,496.90	05/2013	05/2013	06/2016	37
Railways						
GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) NER	383.15	863.23	N.A.	12/2012	03/2013	3
KOTTUR- HARIHAR(NL),(SWR) SWR	65.94	281.20	N.A.	09/2010	03/2011	6
Ramanagram-Mysore doubling with electrification of SWR	482.00	482.00	03/2013	03/2013	12/2013	9
Road Transport & Highways						
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS NHAI	210.00	210.00	04/2007	01/2011	02/2011	1

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	01/2011	02/2011	1
DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) NHAI	291.80	291.80	06/2008	01/2011	02/2011	1
ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	08/2011	09/2011	1
THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	01/2011	02/2011	1
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	03/2011	04/2011	1
GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 NHAI	579.00	579.00	04/2009	01/2011	03/2011	2
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	01/2011	03/2011	2
BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 NHAI	565.00	565.00	07/2010	01/2011	03/2011	2
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 NHAI	217.00	217.00	10/2008	12/2010	03/2011	3
GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 NHAI	205.00	205.00	10/2008	12/2010	03/2011	3
AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 NHAI	212.00	212.00	10/2008	12/2010	03/2011	3
NAGPUR-KONDHALI,NH-6(NHAI) NHAI	168.00	168.00	12/2008	03/2011	08/2011	5
DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE NHAI	232.45	232.45	09/2010	12/2011	06/2012	6
Gurgaon-Kotputli Km 42.70 to 54.4 Km NHAI	1,673.70	1,673.70	10/2011	10/2011	06/2012	8
SILIGURI TO ISLAMPUR (WB-7) NHAI	225.00	225.00	07/2008	08/2011	12/2012	16
Shipping & Ports						
ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH SHIPP.	165.00	165.00	12/2005	01/2011	03/2011	2
SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	3,512.00	01/2012	01/2012	03/2012	2
Telecommunications						
CONVERGENT BILLING AND CRM(MUMBAI) MTNL	247.00	247.00	02/2007	12/2010	03/2011	3

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT DMRC	8,676.00	18,894.36	06/2010	12/2010	02/2011	2
Number of projects reporting additional delay = 52						

Sector Wise Trend and Graphical Analysis


(Jan 11, Dec 10, Nov 10, Oct 10)

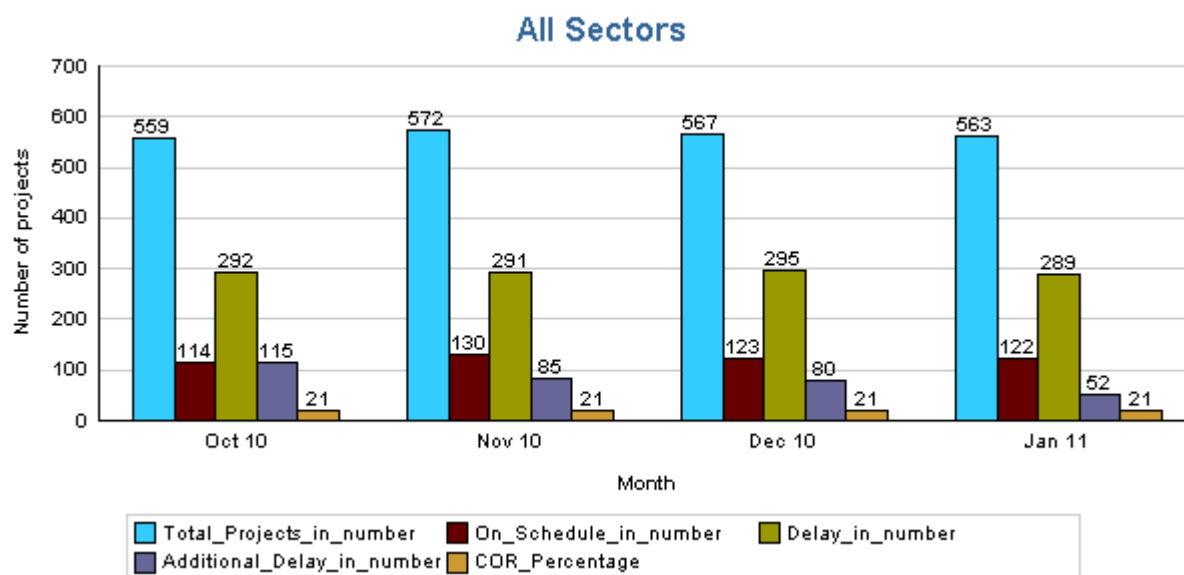


All Sectors Break-up of 289 Delayed projects in January 2011

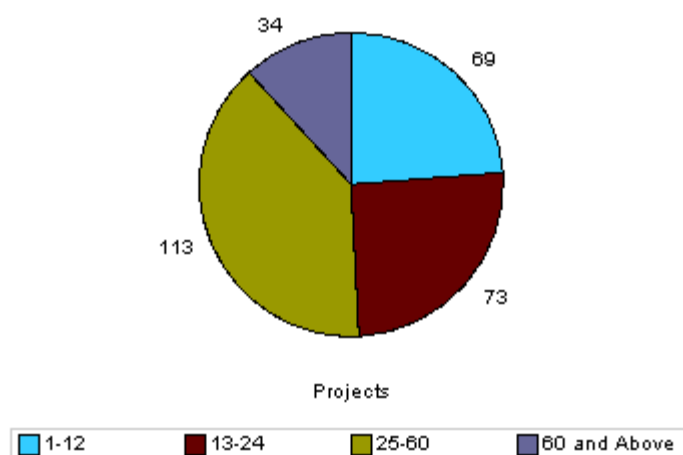


Telecommunications

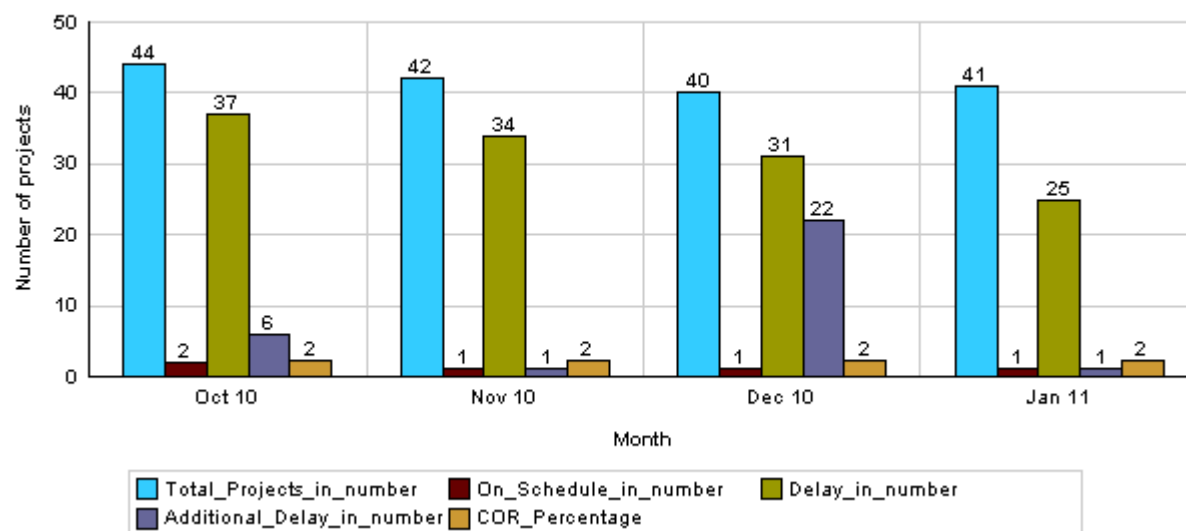


Telecommunications Sector Break-up of 25 Delayed projects in January 2011

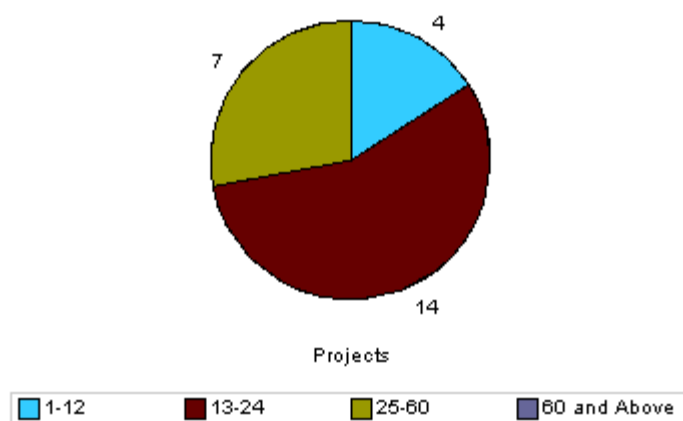


Shipping and Ports

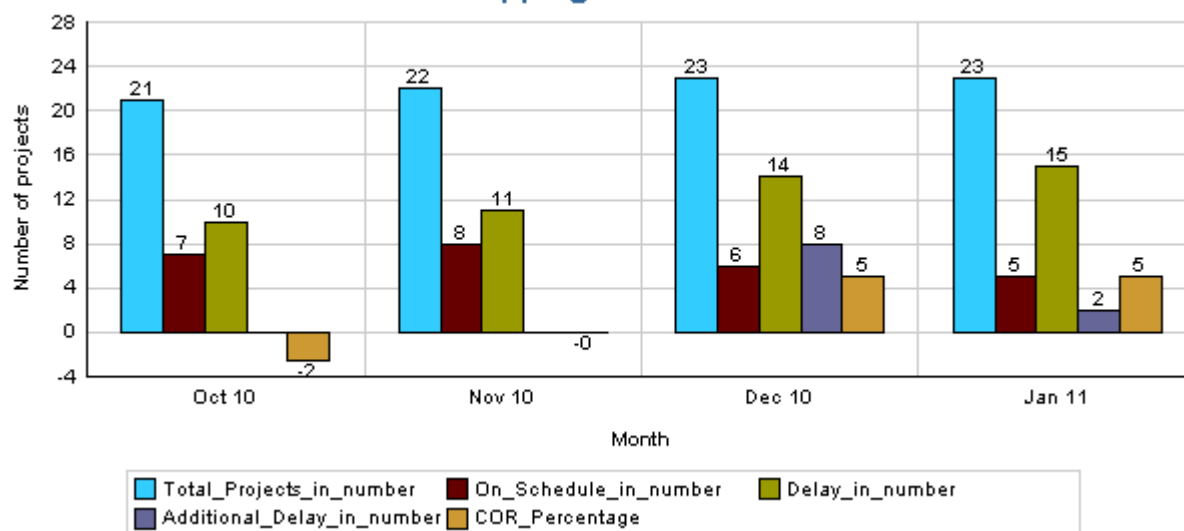


Sector Break-up of 15 Delayed projects in January 2011

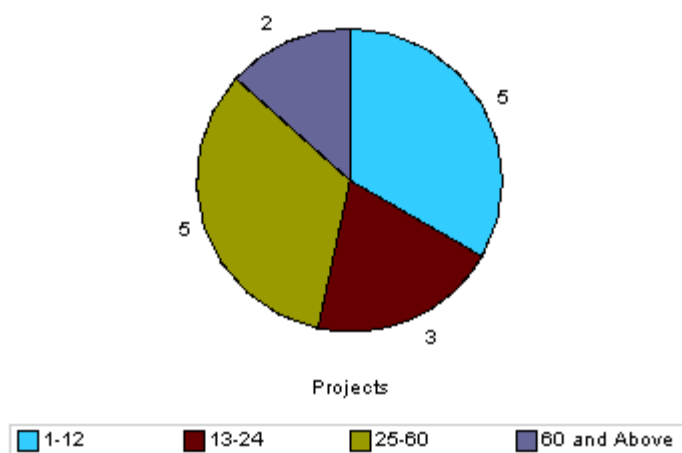


Road Transport and Highways

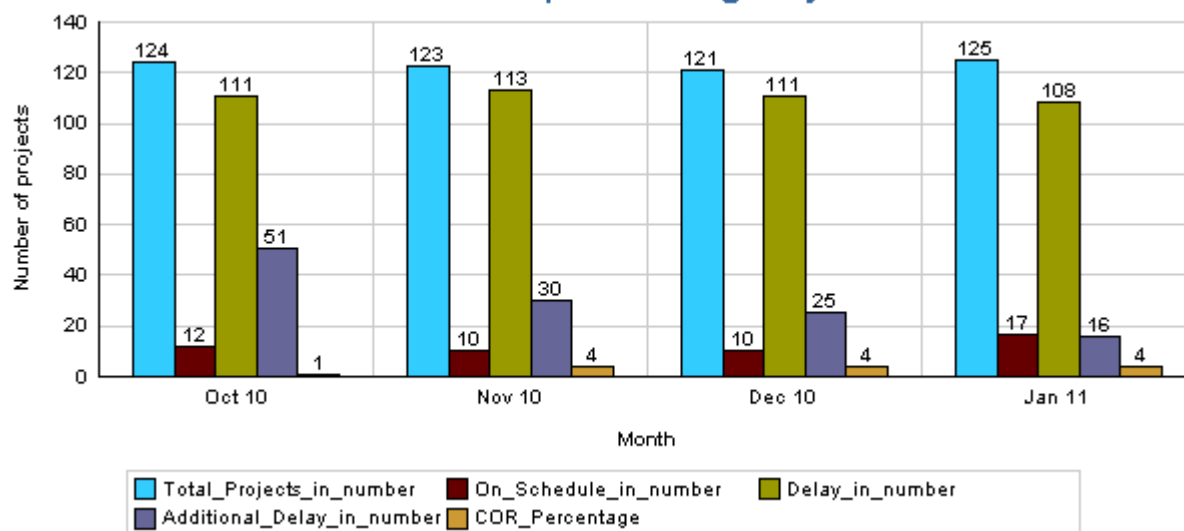


Sector Break-up of 108 Delayed projects in January 2011

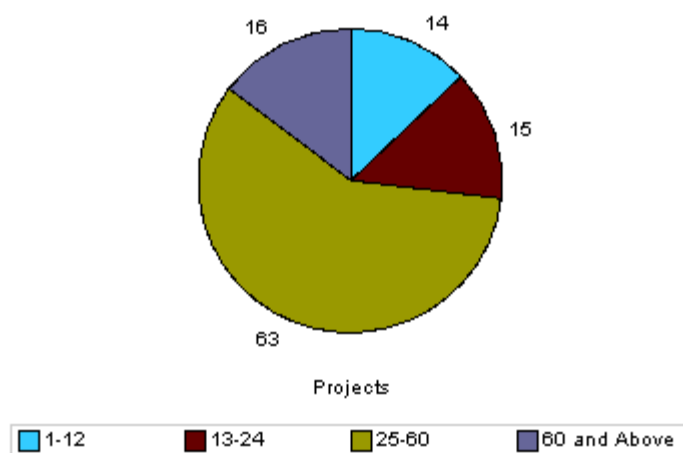


Railways

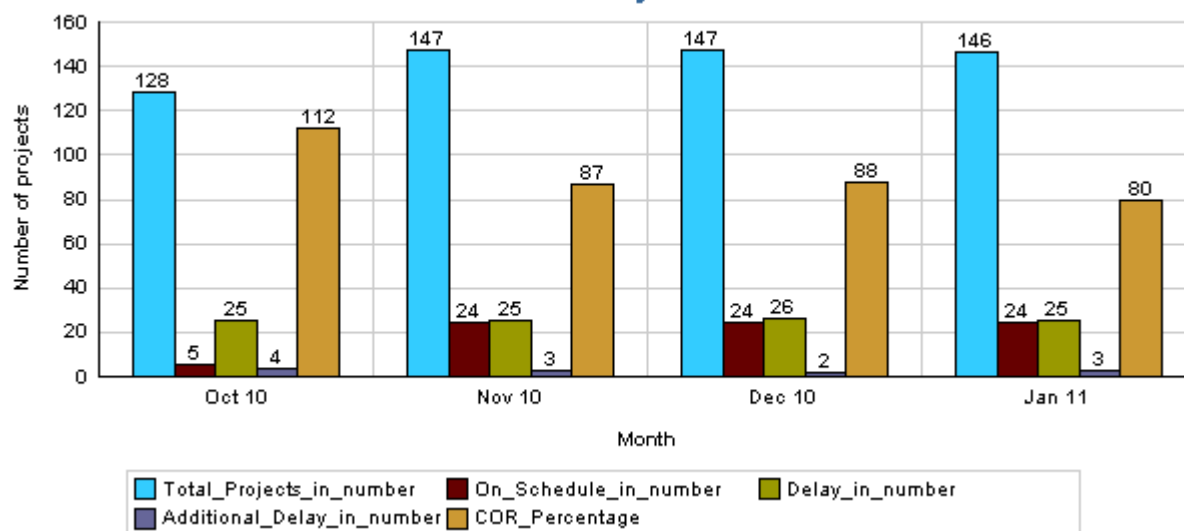



Railways Sector Break-up of 25 Delayed projects in January 2011

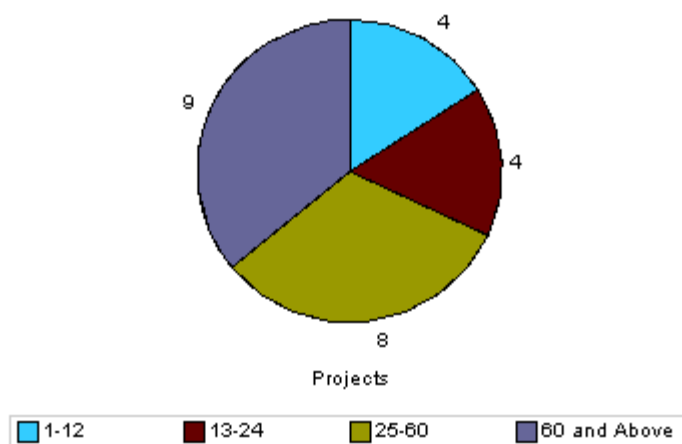

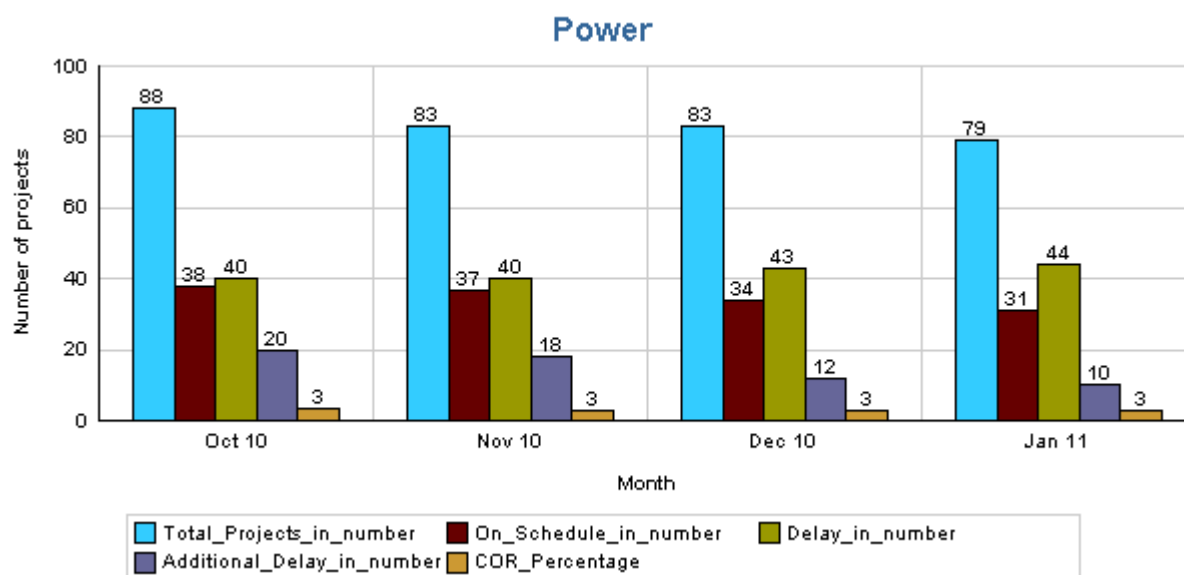



Power Sector Break-up of 44 Delayed projects in January 2011

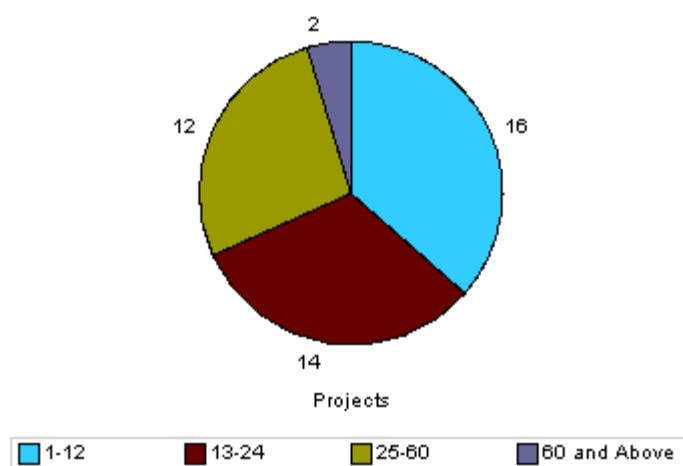

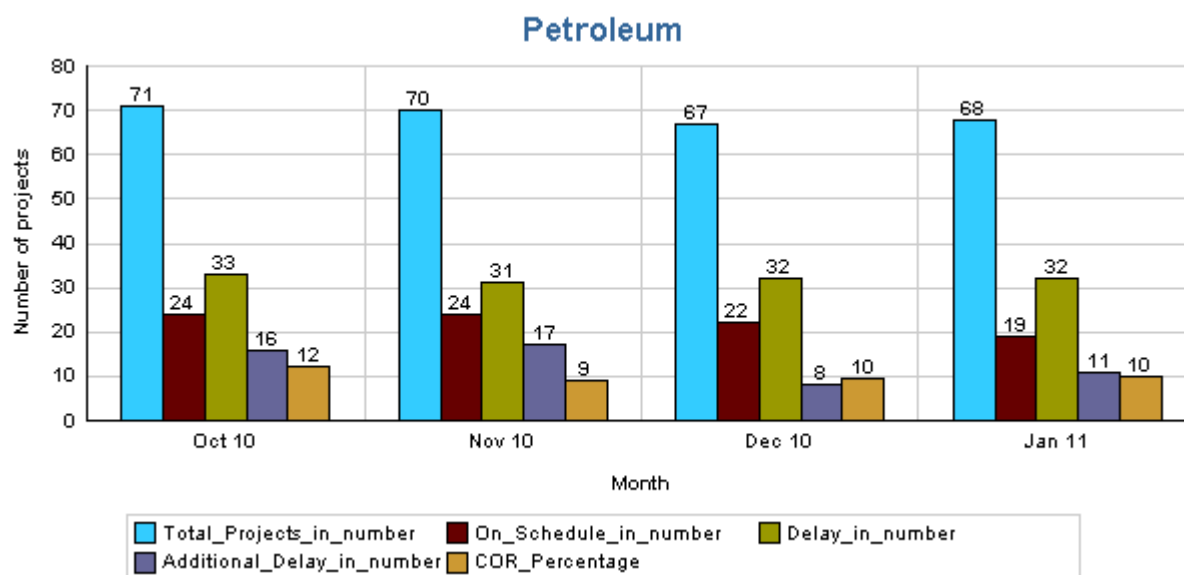



Petroleum Sector Break-up of 32 Delayed projects in January 2011

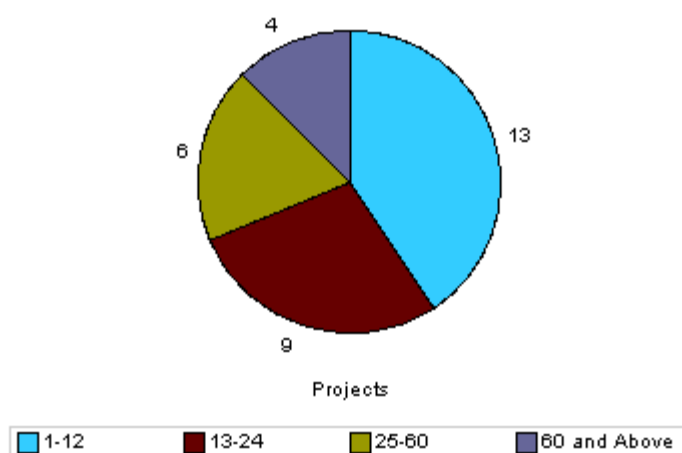

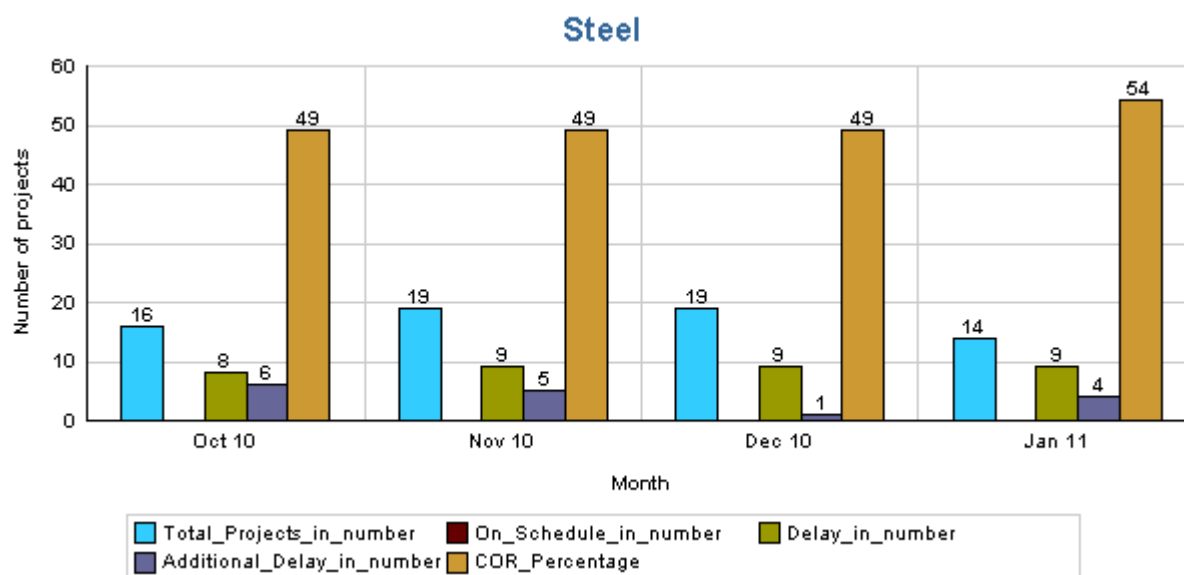



Steel Sector Break-up of 9 Delayed projects in January 2011

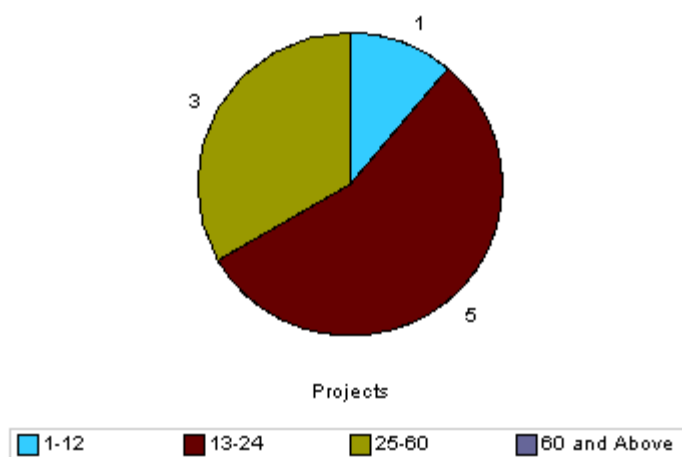

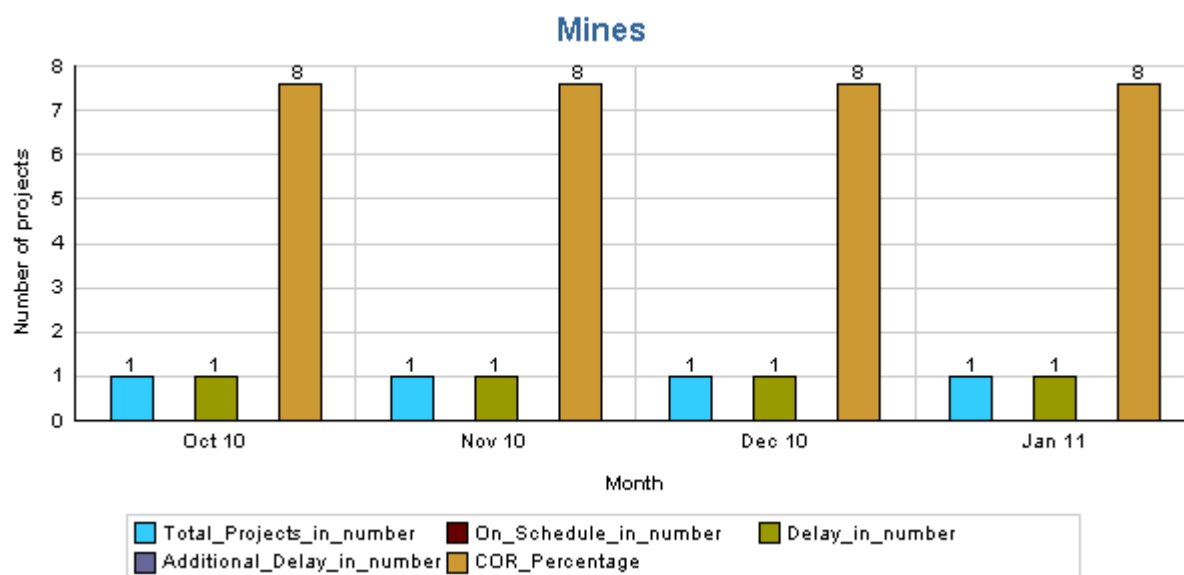


Mines Sector Break-up of 1 Delayed projects in January 2011

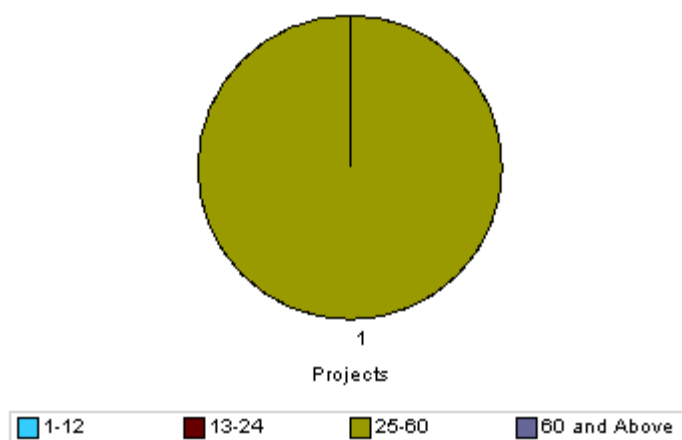

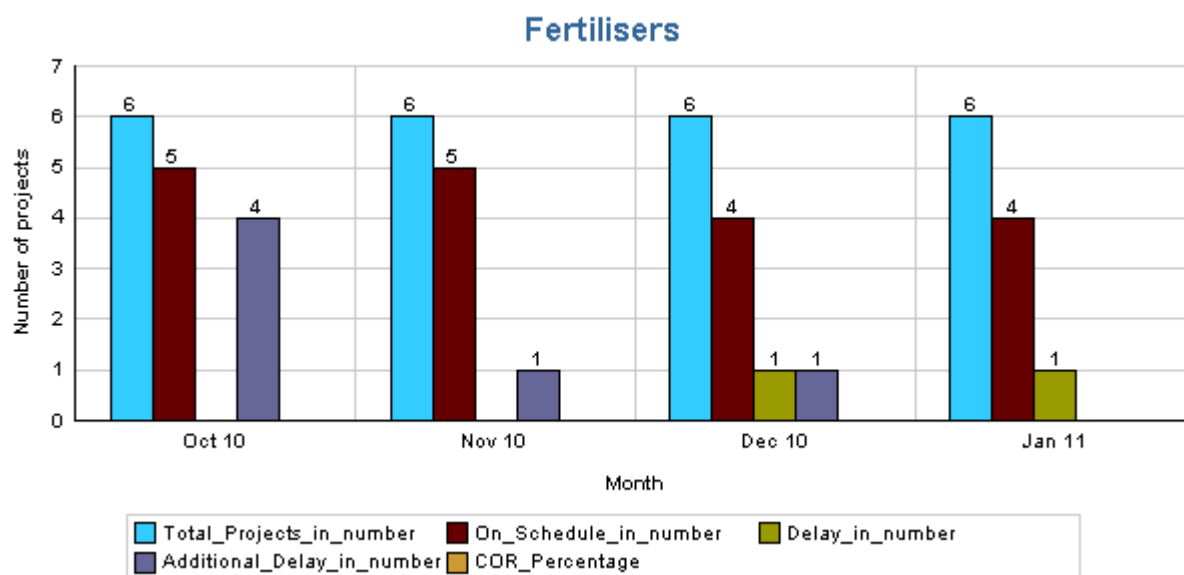



Fertilisers Sector Break-up of 1 Delayed projects in January 2011



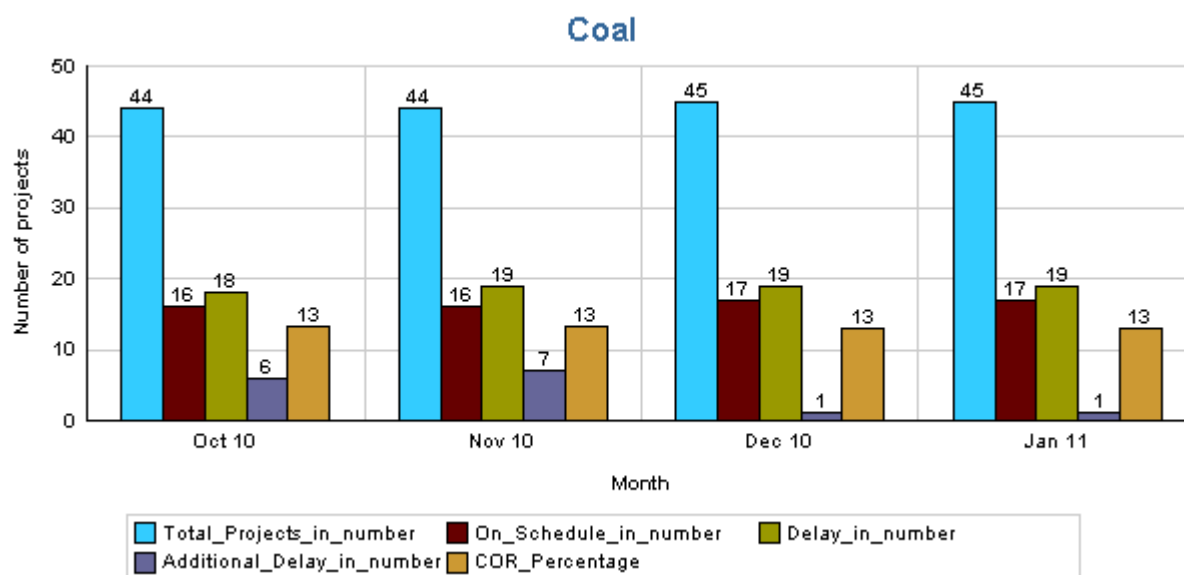



Coal Sector Break-up of 19 Delayed projects in January 2011

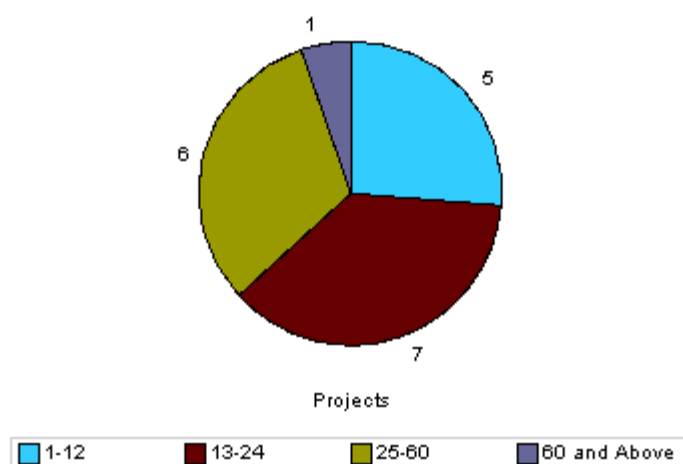

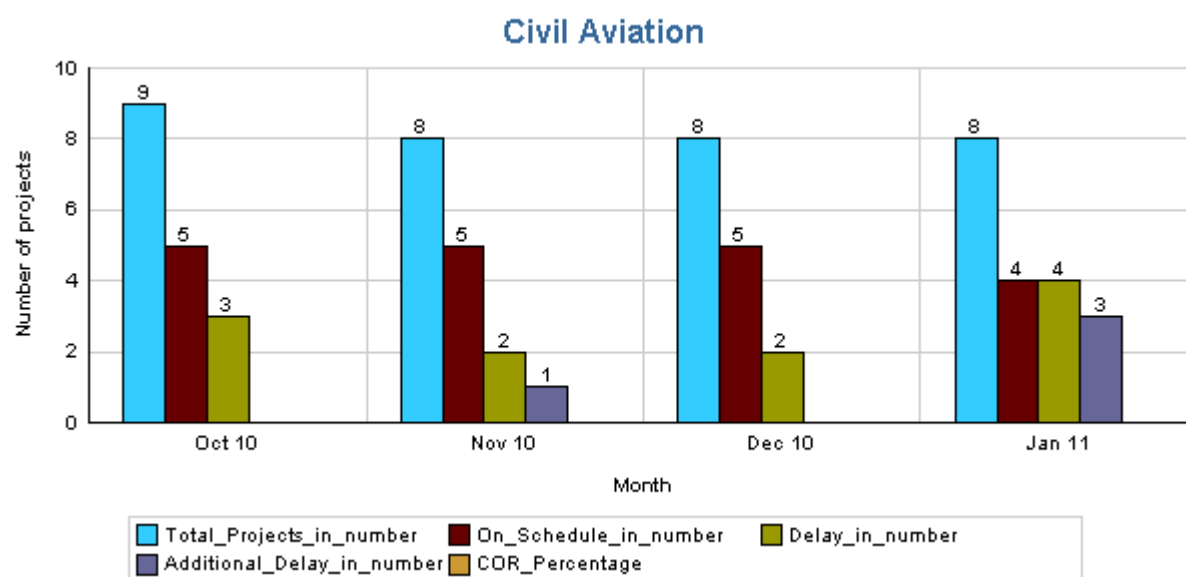


Civil Aviation Sector Break-up of 4 Delayed projects in January 2011

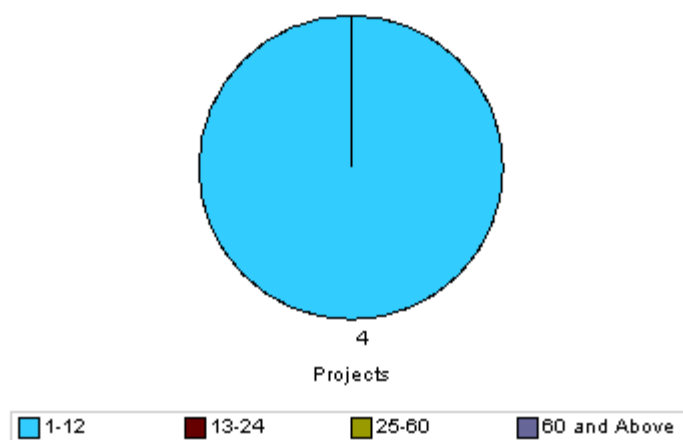

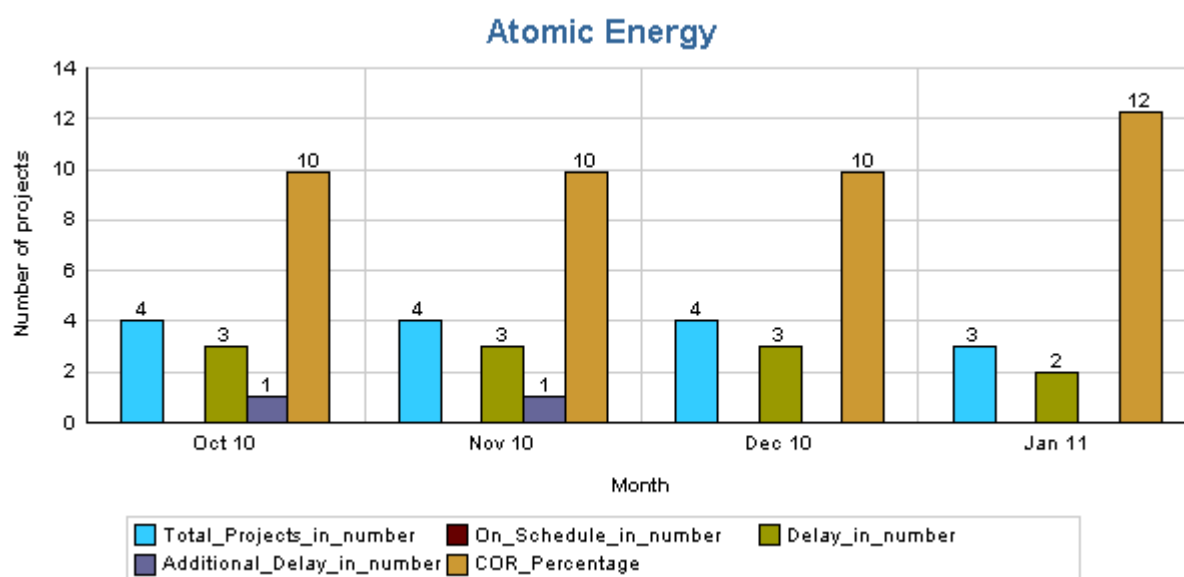

Atomic Energy Sector Break-up of 2 Delayed projects in January 2011

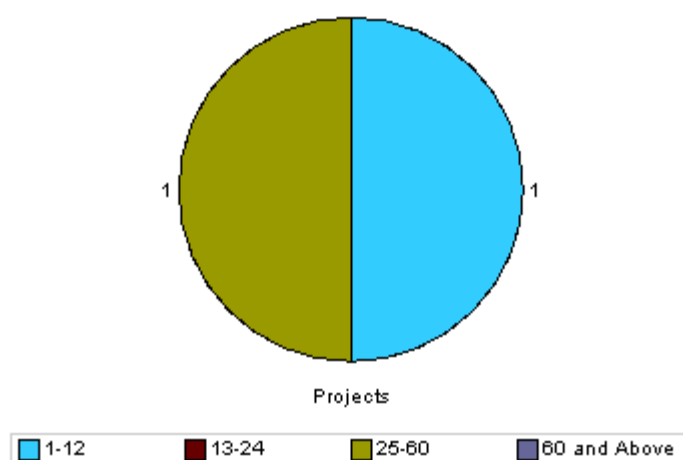

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	3	17,769.29	17,769.29	19,954.29
Civil Aviation	8	4,812.40	4,812.40	4,812.40
Coal	45	25,452.49	29,090.13	28,789.58
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	14	40,023.85	55,234.50	61,734.88
Petroleum	68	145,208.56	167,099.22	159,605.17
Power	79	171,256.40	171,667.11	176,509.08
Railways	146	68,907.72	82,150.11	123,735.87
Road Transport & Highways	125	51,306.01	51,306.01	53,204.42
Shipping & Ports	23	18,352.60	18,953.62	19,288.36
Telecommunications	41	20,025.99	19,998.89	20,488.29
Urban Development	3	15,185.18	8,781.44	30,684.66
Water Resources	1	542.90	542.90	1,187.00
Grand total	563	588,252.31	637,124.79	709,713.17

(Jan,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	486.37	- -	04/2011	-	0/1
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	2,592.29	09/2010 -	09/2011	12(O)	8/80
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	13,171.00	13,398.00	12/2008 -	12/2011	36(O)	61/119
Total			17,769.29 -	19,954.29	16,476.66				69/200
<u>Civil Aviation</u>									
4	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 -	1,273.00	703.37	01/2011 -	01/2011	0(O)	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29 -	264.29	85.64	01/2011 -	01/2011	0(O)	0/0
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]AAI,Gujarat	02/2007	290.92 -	290.92	264.05	01/2011 -	02/2011	1(O)	1/24
7	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00 -	230.00	232.82	01/2011 -	03/2011	2(O)	0/0
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35 -	213.35	211.18	09/2010 -	03/2011	6(O)	0/0
9	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	945.06	05/2011 -	08/2011	3(O)	0/0
10	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	21.65	05/2012 -	05/2012	0(O)	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	262.67	06/2013 -	06/2013	0(O)	0/0
Total			4,812.40 -	4,812.40	2,726.44				1/24
<u>Coal</u>									
12	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,549.53	06/2009 -	03/2011	21(O)	59/26
13	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	156.45	03/2009 03/2011	03/2011	0(R3)	0/2
14	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.46	03/2011 -	03/2011	0(O)	0/2
15	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,099.47	06/2009 -	10/2011	28(O)	41/24
16	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	75.50	03/2010 -	03/2012	24(O)	0/4

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	102.73	03/2011 03/2012	03/2012	0(R3)	0/2
18	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	39.34	03/2012 -	03/2012	0(O)	8/42
19	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.23	03/2012 03/2012	03/2012	0(R3)	0/1
20	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	65.33	03/2012 -	03/2012	0(O)	0/0
21	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.57 418.97	418.97	71.60	- -	03/2012	-	7/7
22	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.91 -	181.19	0.90	- -	03/2012	-	2/8
23	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	68.38	03/2012 -	03/2012	0(O)	0/2
24	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	78.68	03/2012 -	03/2012	0(O)	0/2
25	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	1,362.27	08/2012 -	08/2012	0(O)	0/3
26	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.56	741.56	137.23	03/2010 03/2013	03/2013	0(R3)	0/2
27	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 1,188.31	1,188.31	556.01	03/2011 -	03/2013	24(O)	0/4
28	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.24	07/2012 03/2013	03/2013	0(R3)	0/2
29	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	11.86	03/2013 -	03/2013	0(O)	0/83
30	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	68.63	- -	03/2013	-	0/2
31	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	29.75	03/2013 -	03/2013	0(O)	0/2
32	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	22.83	03/2013 -	03/2013	0(O)	0/2
33	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	142.88	03/2013 07/2012	06/2013	11(R3)	2/22
34	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 2,675.67	2,675.67	1,023.17	03/2010 03/2014	03/2014	0(R3)	3/10
35	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 1,943.66	1,943.66	915.18	03/2010 03/2014	03/2014	0(R3)	2/8
36	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	140.85	03/2014 03/2014	03/2014	0(R3)	1/1
37	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	254.63	06/2014 -	03/2014	-3(O)	0/0
38	RAJMAHAL OC EXP. - [N06000056]ECL,	02/2006	50.08 153.82	153.82	15.29	- 03/2014	03/2014	0(R3)	0/1
39	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77 -	339.77	0.05	03/2014 -	03/2014	0(O)	0/2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
40	KARTALI (EAST) OC - [N06000076]SECL, Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
41	MANIKPUR OC EXPANTION - [N06000081]SECL, Chhatisgarh	11/2009	321.42	321.50	213.98	03/2013	03/2014	12(O)	0/0
42	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, Madhya pradesh	06/2006	746.04	437.34	137.01	03/2012 03/2015	03/2015	0(R3)	0/1
43	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,	11/2006	287.18	287.17	-	11/2009	03/2015	64(O)	1/1
44	GOPAL PRASAD OCP - [N06000042]MCL, Orissa	02/2008	395.87	395.87	24.33	03/2013	03/2015	24(O)	0/3
45	PELMA OC - [N06000045]SECL, Chhatisgarh	07/2008	448.32	448.32	-	03/2012 03/2015	03/2015	0(R3)	0/0
46	KAKATIYA LAONGWALL - [N06000048]SCCL, Multi State	12/2008	453.63	453.63	56.08	- 12/2012	03/2015	27(R3)	7/44
47	Batura OC - [N06000049]BCCL, Madhya pradesh	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
48	JAGANNATHPOR OC - [N06000075]SECL, Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
49	RKP OCP PHASE-I - [N06000079]SCCL, Uttaranchal	03/2010	201.58 209.78	209.78	15.31	- -	03/2015	-	0/8
50	Kistaram OCP - [N06000089]SCCL, Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/26
51	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL, Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	44.65	03/2014 03/2016	03/2016	0(R3)	1/2
52	TALABIRA OCP - [N06000043]MCL, Orissa	03/2008	447.72	447.72	6.04	03/2015	03/2016	12(O)	0/2
53	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL, Chhatisgarh	11/2009	158.59 198.59	198.59	101.01	03/2016	03/2016	0(O)	0/0
54	Rajrappa RCE OCP - [N06000087]CCL, Jharkhand	12/2009	510.85	510.85	291.00	03/2016	03/2016	0(O)	0/2
55	BHUBANESWARI OCP - [N06000034]MCL, Orissa	12/2007	490.00	490.10	71.47	-	03/2017	-	0/1
56	KARMA OCP - [N06000088]CCL, Jharkhand	06/2009	162.46	162.46	-	-	-	-	0/0
Total			25,452.49	28,789.58	10,000.35				134/356
Fertilisers									
57	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL, Madhya pradesh	09/2008	325.00	325.00	18.28	07/2011	07/2011	0(O)	0/0
58	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL, Madhya pradesh	09/2008	438.00	438.00	33.62	07/2011	07/2011	0(O)	0/0
59	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF, Haryana	01/2009	488.75	488.75	29.87	- 11/2011	11/2011	0(R3)	2/22
60	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL, Haryana	01/2010	1,292.84	1,292.84	79.30	01/2013	01/2013	0(O)	0/5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	67.81	01/2013	01/2013	0(O)	0/5
62	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	73.75	12/2012	01/2013	1(O)	0/8
	Total		5,317.41	5,317.41	302.63				2/40
	Mines								
63	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51	4,401.76	3,928.00	12/2008	03/2011	2(R3)	117/110
	Total		4,091.51	4,401.76	3,928.00				117/110
	Steel								
64	AIR SEPARATION PLANT (ASU-4) - [N12000060]RINL,Andhra Pradesh	03/2008	96.00	170.00	74.39	06/2010	03/2011	9(O)	0/0
65	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL,	07/2008	172.78	172.78	121.17	01/2010	04/2011	15(O)	0/1
66	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,	07/2007	111.28	232.93	116.31	-	05/2011	-	0/1
67	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	195.69	-	06/2011	-	0/1
68	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL,	10/2007	500.90	500.90	244.25	04/2010	08/2011	16(O)	0/2
69	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	209.45	02/2010	08/2011	18(O)	0/0
70	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2003	295.89	607.17	247.84	-	10/2011	-	2/21
71	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,	02/2008	14,443.00	14,443.00	10,174.60	09/2010	12/2011	0(R3)	0/6
72	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,	01/2008	3,316.00	6,325.00	1,708.74	-	12/2011	0(R3)	0/7
73	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,499.00	7,766.00	10/2009	03/2012	29(O)	5/16
74	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Andhra Pradesh	05/2008	480.00	480.84	62.90	09/2010	05/2012	20(O)	0/0
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	29.93	10/2009	10/2012	36(O)	0/0
76	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	8,128.00	2,506.34	02/2011	03/2013	25(O)	0/0
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,	09/2008	5,185.00	17,265.00	1,962.52	-	03/2013	0(R3)	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			40,023.85	61,734.88	25,420.13				7/63
<u>Petroleum</u>									
78	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL,Maharashtra	03/2007	900.47	900.47	750.98	09/2009	12/2010	15(O)	0/0
79	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL,Punjab	01/2009	605.40	510.00	357.22	12/2010	12/2010	0(R3)	17/17
80	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80	3,941.41	3,179.39	12/2009	12/2010	12(O)	0/0
81	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL,Multi State	11/2007	396.13	396.13	185.56	10/2009	01/2011	15(O)	0/0
82	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	727.88	425.52	12/2010	01/2011	1(O)	0/0
83	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92	976.08	759.93	06/2006	02/2011	7(R3)	0/2
84	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL,Gujarat	01/2007	5,693.00	6,898.00	5,938.42	-	02/2011	8(R3)	57/42
85	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	224.00	160.55	12/2010	02/2011	0(R3)	0/0
86	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	1,690.00	1,504.04	09/2009	03/2011	18(O)	0/0
87	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.63	12/2008	03/2011	27(R3)	0/0
88	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30	2,305.30	2,061.15	06/2010	03/2011	9(R3)	0/0
89	MSQ IMPROVMENT PROJECT - [N16000040]IOCL,Assam	04/2008	293.60	293.60	207.62	12/2009	03/2011	15(O)	0/0
90	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	304.40	190.93	12/2010	03/2011	3(O)	0/0
91	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38	2,500.00	1,927.55	10/2011	04/2011	0(R3)	0/2
92	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70	706.70	551.47	04/2010	04/2011	12(O)	0/0
93	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08	305.08	102.51	04/2011	04/2011	0(O)	0/0
94	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	2,218.01	1,237.61	03/2005	05/2011	0(R3)	0/0
95	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	58.26	03/2009	05/2011	26(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
96	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	01/2010	589.70 755.76	755.76	166.71	03/2011 05/2011	05/2011	0(R3)	0/0
97	Pipeline Replacement project-2 - [N16000111]ONGC,Multi State	12/2007	2,553.28 -	2,553.28	3,189.09	05/2011 -	05/2011	0(O)	0/0
98	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	07/2011	1,816.07 1,816.07	1,200.00	636.46	- 04/2011	06/2011	2(R3)	0/1
99	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	810.00	221.44	04/2011 04/2011	06/2011	2(R3)	0/2
100	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	375.00	2.48	06/2011 -	08/2011	2(O)	3/9
101	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 -	3,597.00	188.34	09/2011 -	09/2011	0(O)	0/0
102	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	149.90	09/2011 -	09/2011	0(O)	0/0
103	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Madhya pradesh	11/2007	1,512.00 1,434.00	975.00	819.56	- 04/2011	10/2011	6(R3)	0/3
104	BNPL superlines(Uttranchal & Punjab) - [N16000091]GAIL,Multi State	12/2009	540.92 -	375.00	1.35	05/2011 -	11/2011	6(O)	0/0
105	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	540.92	1.35	06/2011 -	11/2011	5(O)	7/9
106	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	547.25	12/2011 -	12/2011	0(O)	0/0
107	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	349.00 -	349.00	138.73	08/2011 -	12/2011	4(O)	0/0
108	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Multi State	06/2009	348.00 348.00	348.00	72.59	03/2012 -	12/2011	-3(O)	6/12
109	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL,Maharashtra	02/2008	825.00 -	825.00	100.19	- -	12/2011	-	0/203
110	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	180.36	12/2011 -	12/2011	0(O)	0/0
111	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	34.39	- -	12/2011	-	0/116
112	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	411.58	03/2010 03/2012	03/2012	0(R1)	0/0
113	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	6,652.22	0.65	01/2013 -	03/2012	-10(O)	0/0
114	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	49.60	03/2012 -	03/2012	0(O)	11/10

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
115	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	19.99	- -	03/2012	-	5/36
116	Assam gas Cracker project - [N16000106]BCPL,Assam	04/2006	5,460.61 -	5,460.61	1,391.19	- -	04/2012	-	0/2
117	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	1,927.01	05/2010 05/2012	05/2012	0(R3)	0/0
118	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	1,552.63 2,920.82	2,920.82	356.78	02/2009 03/2012	05/2012	2(R3)	0/0
119	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 -	330.40	3.25	05/2010 -	05/2012	24(O)	0/0
120	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	-	07/2010 05/2012	05/2012	0(R3)	0/0
121	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	342.36	03/2010 03/2012	06/2012	3(R3)	0/0
122	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	214.37	12/2011 -	06/2012	6(O)	0/0
123	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	214.05	06/2012 -	06/2012	0(O)	0/0
124	Additional Development of D-1 Field - [N16000097]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	296.66	12/2011 06/2012	06/2012	0(R3)	0/0
125	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	19.05	04/2011 -	07/2012	15(O)	0/0
126	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	21.00	08/2012 -	08/2012	0(O)	0/0
127	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	6,855.93 -	6,855.93	1,364.40	09/2012 -	09/2012	0(O)	0/0
128	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	70.05	- -	09/2012	-	0/15
129	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
130	PARADIP REFINERY PROJECT - [N16000058]IOCL,	02/2009	29,777.00 -	29,777.00	5,265.79	- -	11/2012	-	107/103
131	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	13.66	12/2011 -	01/2013	13(O)	0/0
132	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	8.57	01/2013 -	01/2013	0(O)	0/0
133	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	1.38	02/2013 -	02/2013	0(O)	0/0
134	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	198.22	03/2006 03/2013	03/2013	0(R3)	6/6

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
135	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	06/2007	1,252.75 8,813.41	8,813.41	5,728.57	06/2009 03/2013	03/2013	0(R3)	0/0
136	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	263.44	03/2013 -	03/2013	0(O)	0/0
137	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
138	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
139	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
140	Wax Project - [N16000101]NRL,Assam	08/2010	576.60 -	576.60	6.48	02/2014 -	02/2014	0(O)	0/0
141	Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	-	02/2014 -	02/2014	0(O)	0/0
142	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	552.27	03/2007 03/2014	03/2014	0(R3)	3/3
143	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,138.77	03/2007 03/2017	03/2017	0(R3)	6/6
144	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	2.44	10/2010 -	-	-	0/0
145	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	1.60	- -	-	-	0/0
Total			145,208.56 -	159,605.17	48,452.71				228/599
Power									
146	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34 -	241.27	158.18	06/2008 -	02/2011	32(O)	9/20
147	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44 -	2,570.44	1,836.00	08/2010 -	02/2011	6(O)	13/26
148	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL,Multi State	12/2008	328.97 -	328.97	170.12	09/2011 -	02/2011	-7(O)	0/0
149	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70 -	803.76	639.45	06/2009 -	03/2011	21(O)	1/20
150	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Uttar Pradesh	10/2006	975.96 -	894.26	636.88	10/2009 -	03/2011	17(O)	2/20
151	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	119.61	06/2010 -	03/2011	9(O)	0/0
152	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49 -	299.08	315.85	04/2010 -	03/2011	11(O)	0/0
153	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10 -	262.10	143.69	09/2010 -	03/2011	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
154	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	64.46	01/2011	03/2011	2(O)	0/1
155	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	263.87	07/2011	03/2011	-4(O)	0/0
156	Transmission system associated with Uri-II HEP - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	204.44	-	05/2011	-	0/0
157	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,651.19	11/2008	06/2011	31(O)	25/38
158	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,430.00	09/2009	06/2011	21(O)	15/30
159	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	420.70	01/2010	06/2011	17(O)	0/22
160	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,730.71	07/2010	06/2011	11(O)	3/20
161	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	331.86	09/2010	06/2011	9(O)	0/0
162	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	94.43	06/2011	06/2011	0(O)	0/0
163	TRANSMISSION SYSTEM ASSOCIATED WITH CORBA III GENE - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	175.11	06/2011	06/2011	0(O)	0/0
164	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	44.35	07/2011	07/2011	0(O)	0/0
165	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,425.66	08/2010	08/2011	12(O)	0/0
166	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.26	621.28	584.86	02/2011	08/2011	6(O)	0/1
167	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	115.49	08/2011	08/2011	0(O)	0/0
168	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC,J & K	08/2006	611.01	611.02	584.25	08/2010	09/2011	13(O)	0/0
169	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,729.29	1,724.79	1,327.87	11/2009	11/2011	24(O)	0/0
170	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	206.61	11/2011	11/2011	0(O)	0/0
171	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	194.72	11/2011	11/2011	0(O)	0/0
172	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	23.97	11/2011	11/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
173	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	97.74	11/2011	11/2011	0(O)	0/0
174	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,252.59	03/2007	12/2011	57(O)	1/25
175	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,304.52	1,288.02	10/2010	12/2011	14(O)	0/0
176	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.53	3,535.00	05/2011	12/2011	7(O)	0/0
177	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	183.78	02/2012	02/2012	0(O)	0/0
178	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	13.64	02/2012	02/2012	0(O)	0/0
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	108.13	02/2012	02/2012	0(O)	0/0
180	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	176.33	07/2010	02/2012	19(O)	0/0
181	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	588.36	02/2012	02/2012	0(O)	0/0
182	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,219.26	04/2005	03/2012	83(O)	2/1
183	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	6,736.00	12/2009	03/2012	27(O)	33/56
184	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	18.09	04/2012	04/2012	0(O)	0/0
185	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	142.39	05/2012	05/2012	0(O)	0/0
186	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	50.84	06/2012	06/2012	0(O)	0/0
187	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	62.65	06/2012	06/2012	0(O)	0/0
188	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	6.09	06/2012	06/2012	0(O)	0/0
189	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	872.63	09/2009	08/2012	35(O)	0/0
190	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,491.17	08/2012	08/2012	0(O)	0/0
191	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	2,968.18	08/2012	08/2012	0(O)	0/0
192	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	156.30	08/2012	08/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
193	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	1,671.00	07/2011	10/2012	15(O)	0/0
194	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	1,800.00	02/2012 08/2012	10/2012	2(R3)	0/0
195	TRANSMISSION SYSTEM ASSOCIATED WITH MUNDRA ULTRA M - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,225.16	10/2012	10/2012	0(O)	0/0
196	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	33.78	10/2012	10/2012	0(O)	0/0
197	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF I - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	-	10/2012	10/2012	0(O)	0/0
198	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	36.64	11/2012	11/2012	0(O)	0/0
199	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	101.32	11/2012	11/2012	0(O)	0/0
200	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42	358.42	14.74	12/2008 09/2010	12/2012	27(R1)	0/15
201	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
202	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	1,777.87	12/2012	12/2012	0(O)	0/0
203	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	1,372.00	11/2012	12/2012	1(O)	0/0
204	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	1,300.00	11/2012	12/2012	1(O)	0/0
205	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	107.63	12/2012	12/2012	0(O)	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	-	01/2013	01/2013	0(O)	0/0
207	Transmission System for phase-1 generation project - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	-	02/2013	02/2013	0(O)	0/0
208	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,421.00	04/2009	03/2013	47(O)	19/41
209	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	61.18	01/2012	07/2013	18(O)	0/0
210	PARE HYDRO ELECTRIC PROJECT (110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	157.28	08/2012 08/2013	08/2013	0(R3)	8/17
211	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	1,807.62	08/2013	08/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
212	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,058.85	01/2012	09/2013	20(O)	2/10
213	BARH STPP STAGE -II (NTPC) - [N18000047]NTPC, Bihar	02/2008	7,341.04	7,341.04	1,478.00	08/2013	10/2013	2(O)	0/0
214	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33	6,285.33	4,429.97	09/2010	12/2013	39(O)	2/11
215	TUIRIAL HE PROJECT(NEPCO) - [180100165]NEPCO, Mizoram	07/1998	368.72	913.63	218.73	07/2006	01/2014	90(O)	2/5
216	Tapovan-Vishnugad HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttaranchal	11/2006	2,978.48	2,978.48	978.00	03/2013	02/2014	11(O)	5/31
217	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59	3,919.59	3,030.47	09/2009	07/2014	58(O)	1/20
218	BARH STPP(3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97	8,693.00	5,291.00	11/2010	09/2014	46(O)	15/51
219	Transm System for development of Pooling str. in N - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
220	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttaranchal	07/2006	1,657.00	2,978.86	250.83	07/2010	03/2015	56(O)	0/0
221	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67	3,642.04	540.01	07/2014	01/2016	18(O)	0/0
222	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttaranchal	08/2008	2,491.58	2,491.58	141.61	07/2014	03/2016	20(O)	0/8
223	KAMENG HYDROELECTRIC PROJECT (NEPCO) - [180100239]NEPCO, Arunachal Pr.	12/2004	2,496.90	2,496.90	1,377.47	05/2013 06/2016	06/2016	0(R3)	77/22
224	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45 1,007.16	947.96	796.63	12/2007	-	-	14/18
Total			171,256.40	176,509.08	74,892.64				255/563
Railways									
225	VALLAPARPADM-IDAPALLY, (NL)(RVNL) - [N22000048]RVNL, Kerala	07/2006	246.50	246.50	-	03/2009	11/2009	8(O)	0/0
226	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR, Gujarat	04/2005	148.61	227.52	256.08	03/2008 03/2009	10/2010	19(R1)	0/0
227	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR, Multi State	09/2001	100.00 492.98	724.31	700.83	-	12/2010	-	0/0
228	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16	243.40	217.03	- 02/2009	12/2010	22(R1)	0/0
229	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41 207.00	211.90	171.39	- 03/2009	12/2010	21(R1)	0/0
230	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	221.90	136.03	12/2007 03/2010	12/2010	9(R1)	0/0
231	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73 399.73	399.50	284.43	03/2009 12/2008	12/2010	24(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
232	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	199.25	- -	12/2010	-	0/0
233	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	115.13	12/2010 -	12/2010	0(O)	0/0
234	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]ER,Jharkhandd	02/1999	180.73 -	358.00	335.51	12/2006 12/2008	02/2011	26(R1)	0/0
235	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 -	228.09	199.38	- -	02/2011	-	0/0
236	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.16	431.86	02/2010 -	02/2011	12(O)	0/0
237	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 -	810.78	71.11	- -	02/2011	-	0/0
238	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056]SWR,Karnataka	12/1992	46.00 -	218.00	237.35	- -	02/2011	-	0/0
239	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	401.10	06/1999 -	03/2011	141(O)	0/0
240	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 119.29	170.00	159.90	03/2002 -	03/2011	108(O)	0/0
241	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	03/1997	100.00 -	322.29	382.47	- -	03/2011	-	0/0
242	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	281.20	317.98	- -	03/2011	-	0/0
243	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	193.78 -	456.45	247.29	06/2004 -	03/2011	81(O)	0/0
244	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	484.10	05/2008 -	03/2011	34(O)	0/0
245	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 -	214.09	178.90	12/2009 -	03/2011	15(O)	0/0
246	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	09/2001	320.10 -	522.56	328.71	- -	03/2011	-	0/1
247	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]SCR,Andhra Pradesh	05/2002	304.50 -	306.00	341.81	- -	03/2011	-	0/0
248	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69 -	3,040.89	2,640.95	12/2006 08/2010	03/2011	7(R3)	0/0
249	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 -	700.00	131.28	- -	03/2011	-	0/0
250	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/1997	143.92 -	258.60	167.88	- -	03/2011	-	0/0
251	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	104.10 -	218.19	79.22	- -	03/2011	-	0/0
252	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	200.73 -	230.03	132.93	- -	03/2011	-	0/0
253	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	265.04	- 03/2009	03/2011	24(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
254	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	348.78	319.92	- -	03/2011	-	0/0
255	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
256	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	272.11	243.30	- -	03/2011	-	0/0
257	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	106.45	12/2010 -	03/2011	3(O)	0/0
258	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
259	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	03/2006	258.35 -	258.35	9.38	03/2011 -	03/2011	0(O)	0/0
260	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	134.11	03/2011 -	03/2011	0(O)	0/0
261	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	738.37	03/2011 -	03/2011	0(O)	0/0
262	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	150.92	03/2011 -	03/2011	0(O)	0/0
263	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,085.98	- 12/2010	06/2011	6(R3)	0/1
264	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	127.07	02/2010 -	11/2011	21(O)	0/0
265	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 -	675.00	382.83	- 12/2011	12/2011	0(R3)	0/0
266	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
267	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	39.33	12/2011 -	12/2011	0(O)	0/0
268	Ghutiarisharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	36.24	12/2011 -	12/2011	0(O)	0/0
269	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,548.95	1,222.25	- -	02/2012	-	0/0
270	KADUR-CHIKMAGALUR-SAKLHESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	155.83	- 03/2012	03/2012	0(R3)	0/0
271	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	727.52	491.86	- -	03/2012	-	0/0
272	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	415.59 -	495.74	98.51	- -	03/2012	-	0/0
273	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	158.21	03/2010 -	03/2012	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
274	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	160.48	109.90	- -	03/2012	-	0/0
275	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	33.29	03/2012 -	03/2012	0(O)	0/0
276	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	34.53	03/2012 -	03/2012	0(O)	0/0
277	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]ER,Gujarat	04/2008	318.24 -	318.24	-	03/2012 -	03/2012	0(O)	0/0
278	TAMLUK DIGHA - [N22000097]LD,West Bengal	03/1984	293.97 -	293.97	313.13	06/2005 -	04/2012	82(O)	0/0
279	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	296.79	- -	07/2012	-	0/0
280	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	514.70	03/1994 -	12/2012	225(O)	0/0
281	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	2,100.00	532.97	- -	12/2012	-	0/0
282	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1997	248.44 576.27	1,103.47	726.64	- -	12/2012	-	0/0
283	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	234.45	170.23	- 03/2012	12/2012	9(R3)	0/0
284	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	194.54	- -	12/2012	-	0/0
285	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	437.04	03/2009 -	12/2012	45(O)	0/0
286	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.00	780.86	10/2007 -	12/2012	62(O)	0/0
287	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	248.10	03/2010 -	12/2012	33(O)	0/0
288	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	93.24	12/2012 -	12/2012	0(O)	0/0
289	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	227.90	79.31	12/2012 -	12/2012	0(O)	0/0
290	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 -	356.87	135.59	- 03/2013	03/2013	0(R3)	0/0
291	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 -	410.08	129.55	- -	03/2013	-	0/0
292	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	383.15 -	863.23	347.35	- -	03/2013	-	0/0
293	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	608.40	- -	03/2013	-	0/0
294	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	912.70 912.70	1,556.23	387.73	- -	03/2013	-	0/0
295	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.13	0.03	03/2013 -	03/2013	0(O)	0/0
296	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	146.61	- -	12/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
297	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.00	153.05	03/2013 -	12/2013	9(O)	0/0
298	Lumding-silchar jiribam, badarpur- baraigram kumarghat - [N22000127]NEFR,Multi State	04/1996	1,676.31 -	3,909.49	2,457.69	03/2009 -	12/2013	57(O)	0/0
299	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	04/1996	1,000.00 1,500.00	3,230.02	2,030.00	04/2008 12/2011	03/2014	27(R1)	0/0
300	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	02/2000	733.00 -	1,655.80	607.72	12/2008 -	03/2014	63(O)	0/0
301	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	122.88	03/2014 -	03/2014	0(O)	0/0
302	BHAIRABI SAIRONG, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	1.61	04/2014 -	03/2014	-1(O)	0/0
303	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	-	03/2014 -	03/2014	0(O)	0/0
304	Jaipur - Ringus - Churu and Sikar - Lohatu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	2.97	03/2014 -	03/2014	0(O)	0/0
305	Suratpura - Hanumangarh - Sriganganagar Guage Canv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	2.62	03/2014 -	03/2014	0(O)	0/0
306	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	97.20	03/2014 -	03/2014	0(O)	0/0
307	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	88.60	03/2010 -	06/2014	51(O)	0/0
308	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	24.70	02/2015 -	02/2015	0(O)	0/0
309	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	140.08	- -	03/2015	-	0/0
310	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	165.22	03/2014 -	03/2015	12(O)	0/0
311	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.91	12/2015 -	03/2015	-9(O)	0/0
312	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
313	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	5.46	03/2015 -	03/2015	0(O)	0/0
314	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,056.85	327.06	03/2011 -	03/2016	60(O)	0/0
315	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	12.04	03/2016 -	03/2016	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
316	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98 -	3,951.98	-	03/2016 -	03/2016	0(O)	0/0
317	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	2,619.02	-	03/2016 -	03/2016	0(O)	0/0
318	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J & K	03/1995	2,500.00 8,000.00	11,270.00	6,844.11	03/2001 -	12/2017	201(O)	0/0
319	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 422.79	634.13	526.02	03/1995 -	-	-	0/0
320	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 -	617.63	440.41	- -	-	-	0/0
321	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR, Gujarat	04/1992	112.53 320.66	464.50	500.53	03/1996 06/2009	-	-	0/0
322	AMBALA-MORADABAD(RE) - [220100131]RE, Multi State	03/1993	152.21 157.76	265.00	265.33	03/1998 -	-	-	0/0
323	New BG line Rly line from Eklakhi-Balughat includ - [220100135]NEFR, West Bengal	01/1986	36.80 274.41	285.93	232.50	- -	-	-	0/0
324	DALLIRAJHARA-JAGDALPUR, NL, SECR - [220100149]SECR, Chhatisgarh	04/1995	369.00 968.60	1,317.24	50.08	- -	-	-	0/0
325	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	581.69	- -	-	-	0/0
326	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	1,010.00	89.98	- -	-	-	0/0
327	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 -	412.91	441.40	- -	-	-	0/0
328	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	356.00 -	1,038.00	501.08	03/1998 -	-	-	0/0
329	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 -	712.00	432.80	- -	-	-	0/0
330	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1997	155.74 164.36	429.49	382.83	02/2009 -	-	-	0/0
331	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00 -	997.58	57.54	- -	-	-	0/0
332	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1996	377.32 236.41	497.47	75.83	- -	-	-	0/0
333	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 154.30	154.30	106.79	03/2007 03/2007	-	-	0/0
334	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
335	KODERMA-RANCHI VIA BARKAKHANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 -	1,099.20	890.16	07/2005 -	-	-	0/0
336	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR, Kerala	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
337	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00	513.16	520.42	-	-	-	0/0
338	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	550.00	65.39	-	-	-	0/0
339	PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra	02/2000	228.00	497.63	477.14	-	-	-	0/0
340	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1999	242.42 369.70	369.70	168.23	- 05/2009	-	-	0/0
341	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	03/1997	78.23	162.87	79.22	-	-	-	0/0
342	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 408.76	639.54	788.83	06/2007	-	-	0/0
343	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34	296.20	275.30	04/2003 03/2010	-	-	0/0
344	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	548.96	432.28	-	-	-	0/0
345	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00	695.00	9.44	-	-	-	0/0
346	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 240.59	607.09	265.25	- 12/2012	-	-	0/0
347	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
348	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	325.17	311.98	03/2005 12/2008	-	-	0/0
349	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91	418.17	66.02	-	-	-	0/0
350	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	160.54	-	-	-	0/0
351	KICHHA-KHATIMA (NL) - NER - [220100317]NER,Uttaranchal	04/2003	165.67	165.67	0.15	-	-	-	0/0
352	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh	04/1992	458.45	573.12	555.49	-	-	-	0/0
353	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	-	-	-	0/0
354	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1998	186.92	261.70	4.46	02/2006	-	-	0/0
355	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	245.32	03/2008 06/2008	-	-	0/0
356	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74	224.51	41.39	-	-	-	0/0
357	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09	881.19	86.35	-	-	-	0/0
358	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	98.25	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
359	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	284.20	- -	-	-	0/0
360	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	17.44	- -	-	-	0/0
361	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	42.02	- -	-	-	0/0
362	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	29.04	- -	-	-	0/0
363	KISHANGANJ JALALGARH, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	333.76	0.71	- -	-	-	0/0
364	MIRAJ-LATUR ROAD(GC),CR - [220100162]CR,Maharashtra	04/1993	225.00 360.63	816.40	830.52	03/2001 03/2010	-	-	0/0
365	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 -	495.44	158.30	03/2004 -	-	-	0/0
366	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	546.06	- 11/2010	11/2010	0(R3)	0/0
367	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 -	563.25	541.56	03/2004 03/2010	-	-	0/0
368	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 -	762.33	325.85	- 12/2009	-	-	0/0
369	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	310.97	- -	-	-	0/0
370	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	0.93	- -	-	-	0/0
Total			68,907.72 -	123,735.87	51,121.59				0/2
Road Transport & Highways									
371	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	662.10	04/2007 -	02/2011	46(O)	0/0
372	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]NHAI,Uttar Pradesh	12/2003	239.00 -	239.00	396.30	10/2008 -	02/2011	28(O)	0/0
373	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	909.10	11/2010 -	02/2011	3(O)	0/0
374	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]NHAI,Bihar	12/2003	291.80 -	291.80	455.00	06/2008 -	02/2011	32(O)	0/0
375	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	268.10	10/2008 -	02/2011	28(O)	0/0
376	THANJAVUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	577.80	06/2009 -	02/2011	20(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
377	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	151.60	09/2007 -	03/2011	42(O)	0/0
378	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	120.81	08/2004 -	03/2011	79(O)	0/0
379	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	131.71	08/2004 -	03/2011	79(O)	0/0
380	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	03/2011	72(O)	0/0
381	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73 -	205.73	247.70	07/2004 -	03/2011	80(O)	0/0
382	GARHMUKTESHVAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	286.80	09/2007 -	03/2011	42(O)	0/0
383	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	425.40	11/2007 -	03/2011	40(O)	0/0
384	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]NHAI,Uttar Pradesh	12/2003	158.06 -	158.06	163.40	08/2005 -	03/2011	67(O)	0/0
385	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	307.30	10/2008 -	03/2011	29(O)	0/0
386	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00 -	239.00	292.70	07/2005 -	03/2011	68(O)	0/0
387	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]NHAI,Bihar	12/2003	275.00 -	275.00	326.50	07/2005 -	03/2011	68(O)	0/0
388	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00 -	217.00	343.70	10/2008 -	03/2011	29(O)	0/0
389	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36 -	323.36	189.90	03/2008 -	03/2011	36(O)	0/0
390	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	223.80	10/2008 -	03/2011	29(O)	0/0
391	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI,Uttar Pradesh	12/2003	205.00 -	205.00	344.30	10/2008 -	03/2011	29(O)	0/0
392	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI,Uttar Pradesh	12/2003	212.00 -	212.00	388.50	10/2008 -	03/2011	29(O)	0/0
393	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]NHAI,Uttar Pradesh	12/2003	451.97 -	451.97	533.70	04/2008 -	03/2011	35(O)	0/0
394	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	322.00	03/2008 -	03/2011	36(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
395	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00	359.00	696.40	03/2009	03/2011	24(O)	0/0
396	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	03/2011	26(O)	0/0
397	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra	03/2005	579.00	579.00	737.10	04/2009	03/2011	23(O)	0/0
398	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI,Assam	12/2003	225.00	225.00	217.10	06/2008	03/2011	33(O)	0/0
399	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	159.70	11/2008	03/2011	28(O)	0/0
400	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	225.30	10/2008	03/2011	29(O)	0/0
401	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	514.00	06/2008	03/2011	33(O)	0/0
402	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	218.20	06/2008	03/2011	33(O)	0/0
403	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	03/2011	21(O)	0/0
404	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	575.20	03/2009	03/2011	24(O)	0/0
405	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	214.50	06/2008	03/2011	33(O)	0/0
406	BARA TO ORAI, NH-2, 25 - [N24000069]NHAI,Uttar Pradesh	12/2003	465.00	465.00	607.80	04/2009	03/2011	23(O)	0/0
407	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00	309.00	549.60	06/2010	03/2011	9(O)	0/0
408	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	285.50	10/2009	03/2011	17(O)	0/0
409	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	294.30	09/2009	03/2011	18(O)	0/0
410	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	294.70	09/2009	03/2011	18(O)	0/0
411	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	605.80	07/2010	03/2011	8(O)	0/0
412	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	718.60	07/2010	03/2011	8(O)	0/0
413	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka	03/2005	565.00	565.00	1,002.00	07/2010	03/2011	8(O)	0/0
414	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	121.06	02/2004	03/2011	85(O)	0/0
415	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam	12/2003	230.00	230.00	304.60	06/2008	04/2011	34(O)	0/0
416	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	234.24	02/2004	04/2011	86(O)	0/0
417	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	332.70	07/2010	04/2011	9(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
418	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	415.40	01/2011 -	04/2011	3(O)	0/0
419	KASIA TO GORAKHPUR (NH- 28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00 -	242.00	348.10	12/2008 -	05/2011	29(O)	0/0
420	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00 -	295.00	621.70	08/2010 -	05/2011	9(O)	0/0
421	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI, Madhya pradesh	11/2008	549.00 -	549.00	697.00	05/2010 -	05/2011	12(O)	0/0
422	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	475.30	05/2010 -	05/2011	12(O)	0/0
423	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00 -	522.00	347.80	03/2005 -	06/2011	75(O)	0/0
424	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	187.00	09/2007 -	06/2011	45(O)	0/0
425	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	72.30	09/2008 -	06/2011	33(O)	0/0
426	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K	12/2003	193.09 -	166.30	158.70	03/2008 -	06/2011	39(O)	0/0
427	VIJAYAPUR TO PATHANKOT (NS- 35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K	12/2003	166.27 -	193.10	126.30	03/2008 -	06/2011	39(O)	0/0
428	GORAKHPUR-AYODHYA (LMNHP- 5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00	313.30	10/2008 -	06/2011	32(O)	0/0
429	UP/BIHAR BORDER TO KASIA (NH- 28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00	275.60	12/2008 -	06/2011	30(O)	0/0
430	FORBESGANJ TO SIMRAHI (NH- 57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	234.90	09/2008 -	06/2011	33(O)	0/0
431	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03 -	251.03	205.60	10/2008 -	06/2011	32(O)	0/0
432	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91 -	229.91	153.20	10/2008 -	06/2011	32(O)	0/0
433	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24 -	600.24	600.90	10/2009 -	06/2011	20(O)	0/0
434	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	395.90	12/2009 -	06/2011	18(O)	0/0
435	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04 -	418.04	267.90	03/2010 -	06/2011	15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
436	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	518.00	07/2010	06/2011	11(O)	0/0
437	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,764.00	01/2011	06/2011	5(O)	0/0
438	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.30	12/2008	08/2011	32(O)	0/0
439	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	1,900.00	08/2011	08/2011	0(O)	0/0
440	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	199.30	11/2008	09/2011	34(O)	0/0
441	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	50.95	04/2004	10/2011	90(O)	0/0
442	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	227.70	06/2008	10/2011	40(O)	0/0
443	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	169.30	10/2011	10/2011	0(O)	0/0
444	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	205.80	10/2011	10/2011	0(O)	0/0
445	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI,Bihar	12/2003	305.00	305.00	488.70	06/2008	11/2011	41(O)	0/0
446	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	150.10	10/2008	11/2011	37(O)	0/0
447	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	1,990.00	11/2011	11/2011	0(O)	0/0
448	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	166.90	06/2005	12/2011	78(O)	0/0
449	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	195.50	02/2009	12/2011	34(O)	0/0
450	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	69.59	04/2009	12/2011	32(O)	0/0
451	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	135.50	06/2008	12/2011	42(O)	0/0
452	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	163.30	06/2008	12/2011	42(O)	0/0
453	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	170.30	10/2008	12/2011	38(O)	0/0
454	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	375.30	09/2008	12/2011	39(O)	0/0
455	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	207.50	06/2008	12/2011	42(O)	0/0
456	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	269.80	03/2008	12/2011	45(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
457	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	157.50	06/2008	12/2011	42(O)	0/0
458	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	173.60	04/2008	12/2011	44(O)	0/0
459	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	93.55	05/2008	12/2011	43(O)	0/0
460	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	162.50	06/2008	12/2011	42(O)	0/0
461	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	209.70	02/2012	02/2012	0(O)	0/0
462	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	100.30	04/2008	03/2012	47(O)	0/0
463	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	151.80	04/2008	03/2012	47(O)	0/0
464	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	77.58	04/2010	03/2012	23(O)	0/0
465	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	178.10	02/2010	03/2012	25(O)	0/0
466	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	926.10	02/2010	05/2012	27(O)	0/0
467	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	490.70	05/2012	05/2012	0(O)	0/0
468	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	492.00	05/2012	05/2012	0(O)	0/0
469	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	146.20	05/2012	05/2012	0(O)	0/0
470	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	139.70	10/2008	06/2012	44(O)	0/0
471	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	146.90	09/2010	06/2012	21(O)	0/0
472	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	289.10	06/2012	06/2012	0(O)	0/0
473	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	1,368.00	10/2011	06/2012	8(O)	0/0
474	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	250.80	07/2012	07/2012	0(O)	0/0
475	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	73.23	05/2008	08/2012	51(O)	0/0
476	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	359.00	73.23	05/2010	08/2012	27(O)	0/0
477	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	182.30	06/2010	10/2012	28(O)	0/0
478	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	232.50	09/2009	10/2012	37(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
479	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
480	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	466.50	09/2012	10/2012	1(O)	0/0
481	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	393.30	10/2012	10/2012	0(O)	0/0
482	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	173.00	07/2008	12/2012	53(O)	0/0
483	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	302.50	12/2012	12/2012	0(O)	0/0
484	Haziribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	122.90	01/2013	01/2013	0(O)	0/0
485	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	-	09/2010	03/2013	30(O)	0/0
486	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
487	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	-	04/2013	04/2013	0(O)	0/0
488	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	109.40	09/2007	06/2013	69(O)	0/0
489	New 4 Lane elevated road from Chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
490	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	0.23	11/2013	11/2013	0(O)	0/0
491	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	29.51	04/2009	12/2013	56(O)	0/0
492	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.68	11/2008	12/2013	61(O)	0/0
493	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	29.09	11/2008	12/2013	61(O)	0/0
494	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	38.03	09/2007	12/2013	75(O)	0/0
495	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	27.54	07/2009	12/2013	53(O)	0/0
	Total		51,306.01	53,204.42	41,763.40				0/0
Shipping & Ports									
496	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40	2,427.40	819.91	10/2008	11/2010	25(O)	0/0
497	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]PORT TRUST, Kerala	03/2007	245.67	298.17	304.01	04/2009	02/2011	15(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
498	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 -	165.00	110.33	12/2005 01/2008	03/2011	38(R3)	0/0
499	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 253.36	253.36	223.20	06/2007 07/2009	03/2011	20(R3)	0/0
500	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	344.58	04/2011 -	04/2011	0(O)	0/0
501	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	230.00	219.00	12/2010 -	06/2011	6(O)	0/0
502	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	290.85 -	290.85	72.59	03/2011 -	06/2011	3(O)	0/0
503	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra	08/2008	1,108.12 -	1,168.42	917.67	04/2011 -	12/2011	8(O)	0/0
504	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 -	277.03	55.41	09/2011 -	12/2011	3(O)	0/0
505	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 -	1,061.96	219.98	03/2012 -	03/2012	0(O)	0/0
506	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	09/2005 -	03/2012	78(O)	0/0
507	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,512.00	1,718.50	01/2012 01/2012	03/2012	2(R3)	0/0
508	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	08/2012	-1(O)	0/0
509	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	432.69	12/2010 -	09/2012	21(O)	0/0
510	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
511	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 -	612.72	61.31	12/2012 -	12/2012	0(O)	0/0
512	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.38	02/2011 -	03/2013	25(O)	0/0
513	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	1.02	03/2011 -	03/2013	24(O)	0/0
514	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 -	272.50	-	01/2009 -	05/2013	52(O)	0/0
515	Acquistion of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 -	1,028.10	-	12/2013 -	12/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
516	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	966.46	-	02/2014	02/2014	0(O)	0/0
517	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.04	03/2012	03/2015	36(O)	0/0
518	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.22	10/2008	-	-	0/0
	Total		18,352.60	19,288.36	5,795.75				0/0
Telecommunications									
519	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	216.14	09/2009	02/2010	5(O)	0/0
520	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	109.31	12/2005	10/2010	58(O)	0/0
521	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
522	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
523	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
524	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	234.24	02/2008	12/2010	34(O)	0/0
525	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
526	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
527	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
528	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
529	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
530	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	127.42	06/2009	01/2011	19(O)	0/0
531	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	392.44	164.58	03/2009	01/2011	22(O)	0/0
532	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.88	03/2009	02/2011	23(O)	0/0
533	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	176.33	12/2008	02/2011	26(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
534	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	308.13	03/2009	02/2011	23(O)	0/0
535	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	88.17	06/2009	02/2011	20(O)	0/0
536	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	02/2011	25(O)	0/0
537	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	02/2011	12(O)	0/0
538	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	219.08	10/2008	02/2011	28(O)	0/0
539	GSM equipment of 1900000Lines (2G) 401700 lines 3(-) - [N26000091]BSNL,Tamil Nadu	01/2009	760.20	810.37	748.30	01/2010 03/2011	02/2011	-1(R3)	0/0
540	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.88	01/2010	02/2011	13(O)	0/0
541	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	442.33	01/2010	02/2011	13(O)	0/0
542	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	110.54	01/2010	02/2011	13(O)	0/0
543	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007 12/2010	03/2011	3(R3)	0/0
544	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	73.73	02/2007	03/2011	49(O)	0/0
545	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	477.44	12/2008	03/2011	27(O)	0/0
546	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	169.43	03/2009	03/2011	24(O)	0/0
547	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	90.50	09/2009	03/2011	18(O)	0/0
548	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	31.15	10/2009	03/2011	17(O)	0/0
549	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	74.65	09/2010	03/2011	6(O)	0/0
550	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	395.77	02/2009	03/2011	25(O)	0/0
551	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) - [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	274.30	08/2009	03/2011	19(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
552	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	211.83	11/2010	03/2011	4(O)	0/0
553	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.70	719.70	395.06	10/2009	03/2011	17(O)	0/0
554	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	138.65	10/2010	04/2011	6(O)	0/0
555	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	2.13	09/2011	09/2011	0(O)	0/0
556	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
557	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
558	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	-	-	0/0
559	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
	Total		20,025.99	20,488.29	7,086.02				0/0
	<u>Urban Development</u>								
560	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	181.30	93.80	04/2009	01/2011	21(O)	0/0
561	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00 8,605.36	18,894.36	16,929.53	06/2010	02/2011	8(O)	0/10
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 3.00	11,609.00	4,092.61	12/2011	03/2013	15(O)	6/6
	Total		15,185.18	30,684.66	21,115.94				6/16
	<u>Water Resources</u>								
563	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			588,252.31	709,713.17	309,117.75				819/1973

Sector wise current status of projects on the Flash Report


Urban Development

I. Current Status:

Number of Projects	3
Number of Projects Delayed	3


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are delayed .

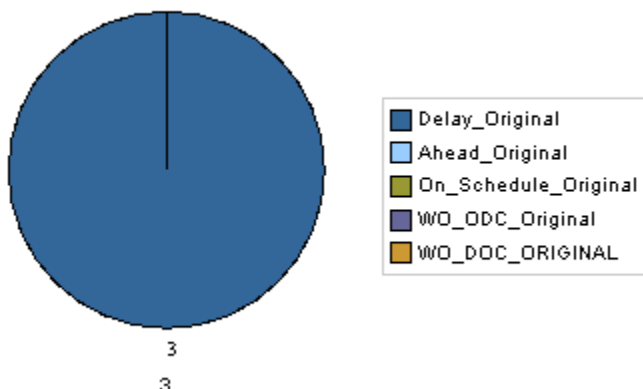

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15185.18 crore but this was subsequently revised to Rs. 30684.66 crore implying a cost overrun of 102.1%. The expenditure incurred on these projects till January, 2011 is Rs. 21115.94 crore, which is 68.8% of the revised cost of the projects.

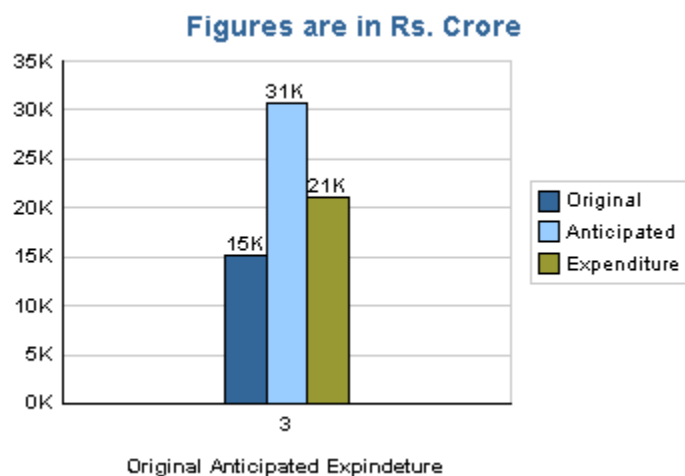

Sector wise current status of projects on the Flash Report

Telecommunications


I. Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	25

Number of Projects Without Date Of Commissioning 15

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 41 projects, 1 project are on schedule and 25 projects are delayed .15 projects do not have fixed dates of commissioning.

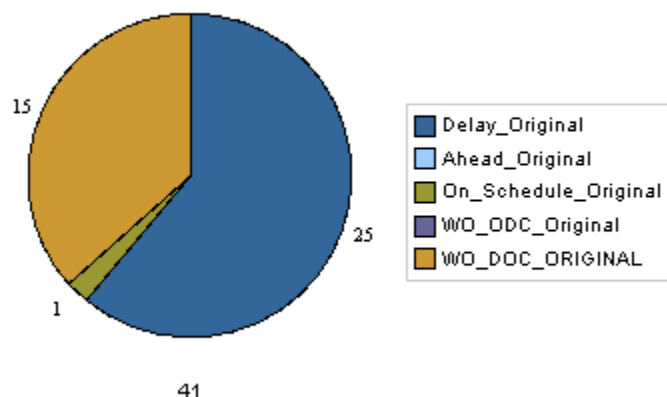

III. Investment Scenario

The Total Original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 20025.99 crore but this was subsequently revised to Rs. 20488.29 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till January, 2011 is Rs. 7086.02 crore, which is 34.6% of the revised cost of the projects.

Figures are in Rs. Crore

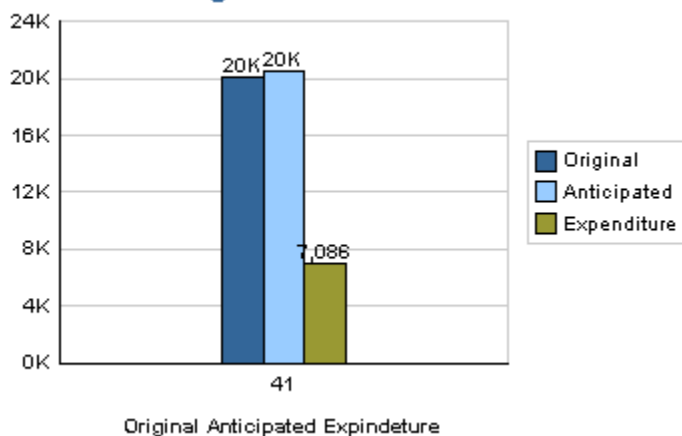

Sector wise current status of projects on the Flash Report


Shipping & Ports

I. Current Status:

Number of Projects	23
Number of Projects On Schedule	5
Number of Projects Delayed	15
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 23 projects, 1 project are ahead of schedule, 5 projects are on schedule and 15 projects are delayed .2 projects do not have fixed dates of commissioning.

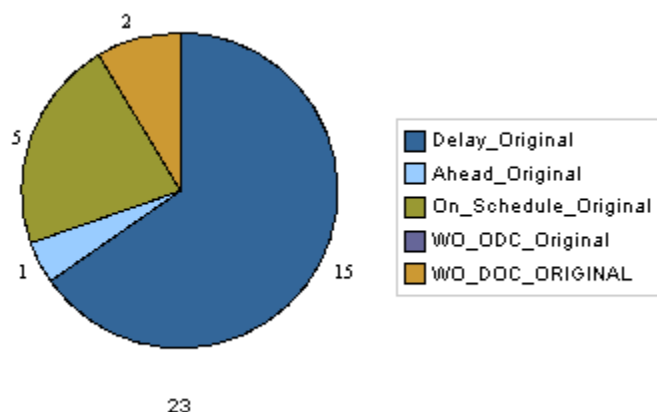

III. Investment Scenario

The Total Original cost of implementation of 23 projects when sanctioned, was of the order of Rs. 18352.6 crore but this was subsequently revised to Rs. 19288.36 crore implying a cost overrun of 5.1%. The expenditure incurred on these projects till January, 2011 is Rs. 5795.75 crore, which is 30% of the revised cost of the projects.

Figures are in Rs. Crore

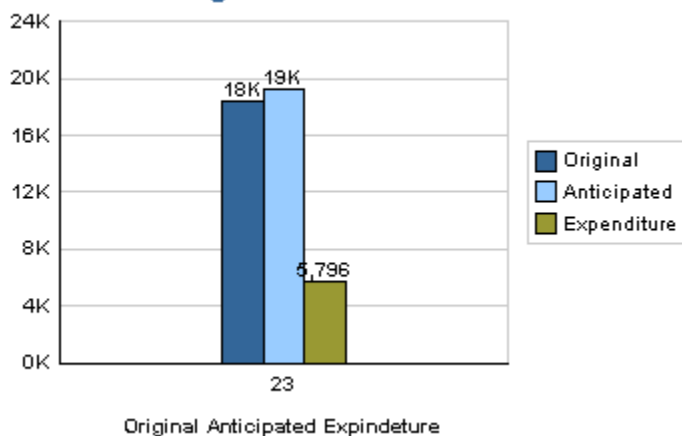

Sector wise current status of projects on the Flash Report


Road Transport & Highways

I. Current Status:

Number of Projects	125
Number of Projects On Schedule	17
Number of Projects Delayed	108

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 125 projects, 17 projects are on schedule and 108 projects are delayed.

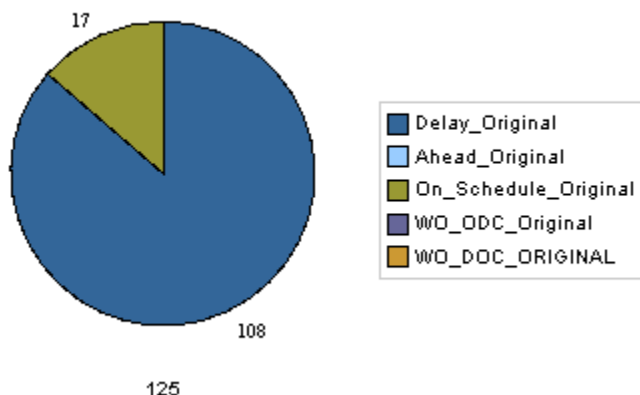

III. Investment Scenario

The Total Original cost of implementation of 125 projects when sanctioned, was of the order of Rs. 51306.01 crore but this was subsequently revised to Rs. 53204.42 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till January, 2011 is Rs. 41763.4 crore, which is 78.5% of the revised cost of the projects.

Figures are in Rs. Crore

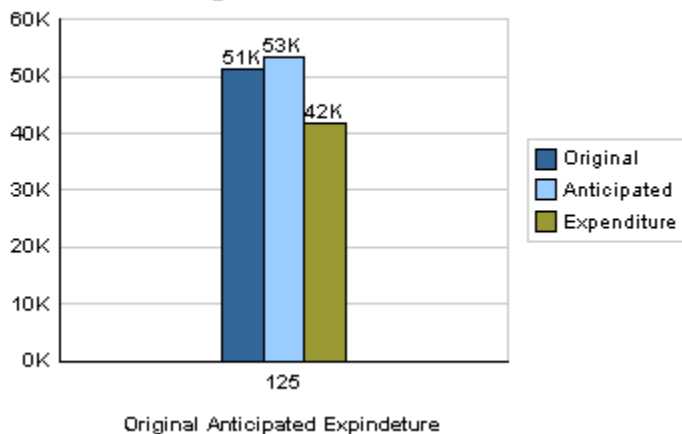

Sector wise current status of projects on the Flash Report


Railways

I. Current Status:

Number of Projects	146
Number of Projects On Schedule	24
Number of Projects Delayed	25
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	35
Number of Projects Without Date Of Commissioning	60

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 146 projects, 2 projects are ahead of schedule, 24 projects are on schedule and 25 projects are delayed .60 projects do not have fixed dates of commissioning.35 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

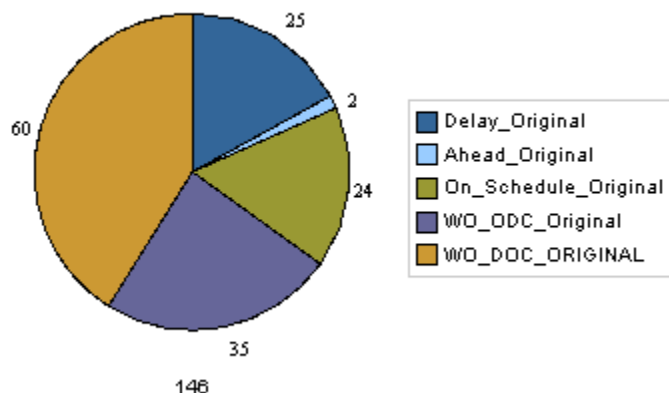

III. Investment Scenario

The Total Original cost of implementation of 146 projects when sanctioned, was of the order of Rs. 68907.72 crore but this was subsequently revised to Rs. 123735.87 crore implying a cost overrun of 79.6%. The expenditure incurred on these projects till January, 2011 is Rs. 51121.59 crore, which is 41.3% of the revised cost of the projects.

Figures are in Rs. Crore

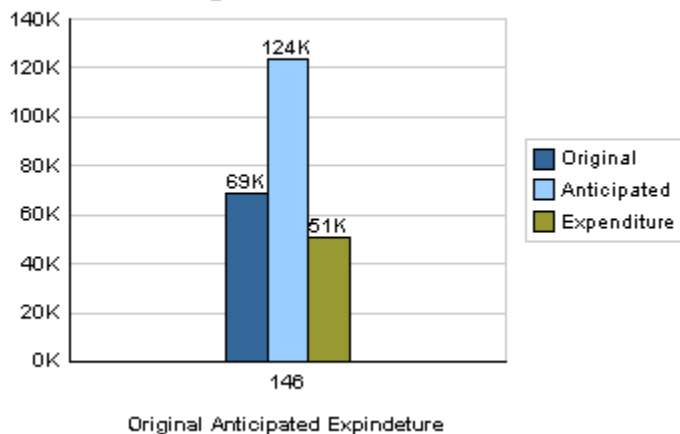

Sector wise current status of projects on the Flash Report


Power

I. Current Status:

Number of Projects	79
Number of Projects On Schedule	31
Number of Projects Delayed	44
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 79 projects, 2 projects are ahead of schedule, 31 projects are on schedule and 44 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

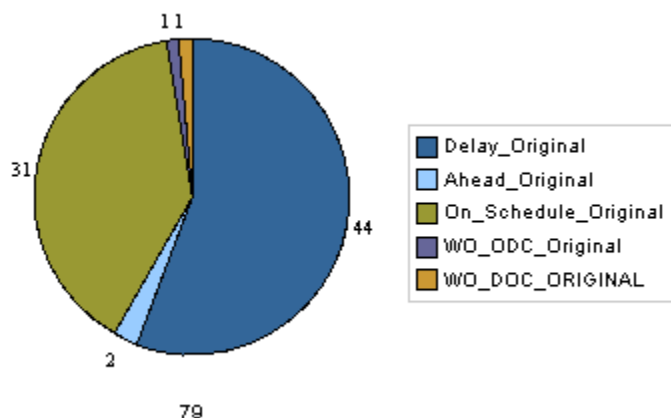

III. Investment Scenario

The Total Original cost of implementation of 79 projects when sanctioned, was of the order of Rs. 171256.4 crore but this was subsequently revised to Rs. 176509.08 crore implying a cost overrun of 3.1%. The expenditure incurred on these projects till January, 2011 is Rs. 74892.64 crore, which is 42.4% of the revised cost of the projects.

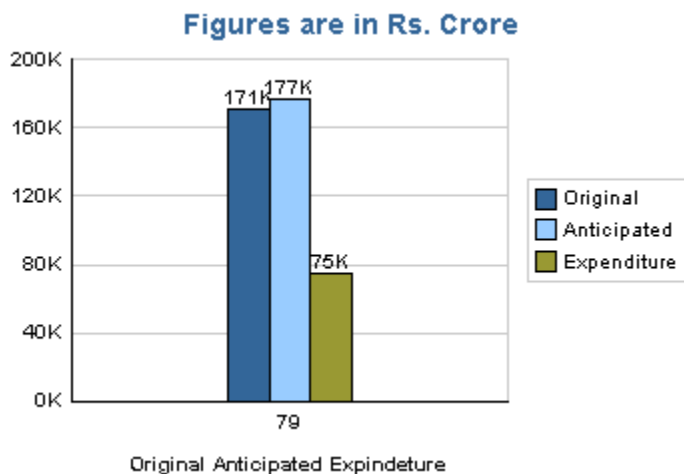

Sector wise current status of projects on the Flash Report


Petroleum

I. Current Status:

Number of Projects	68
Number of Projects On Schedule	19
Number of Projects Delayed	32
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	9
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 68 projects, 3 projects are ahead of schedule, 19 projects are on schedule and 32 projects are delayed .5 projects do not have fixed dates of commissioning.9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

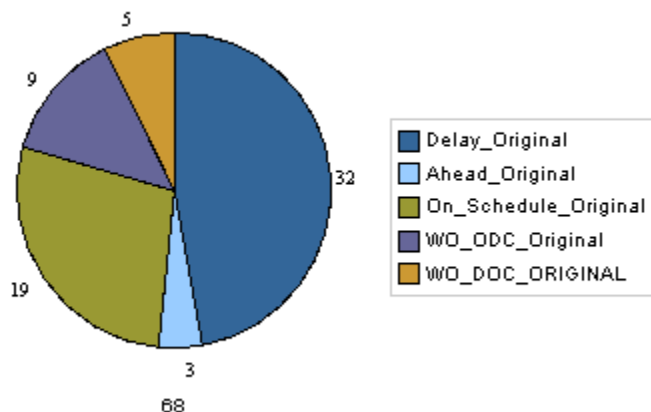

III. Investment Scenario

The Total Original cost of implementation of 68 projects when sanctioned, was of the order of Rs. 145208.56 crore but this was subsequently revised to Rs. 159605.17 crore implying a cost overrun of 9.9%. The expenditure incurred on these projects till January, 2011 is Rs. 48452.71 crore, which is 30.4% of the revised cost of the projects.

Figures are in Rs. Crore

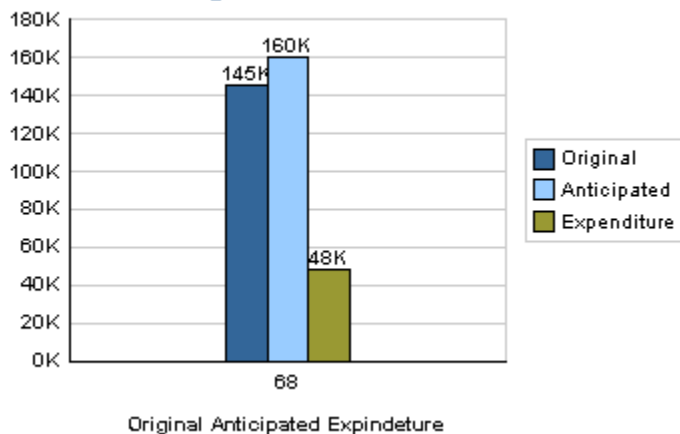

Sector wise current status of projects on the Flash Report


Steel

I. Current Status:

Number of Projects	14
Number of Projects Delayed	9
Number of Projects Without Original Date of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 14 projects, 9 projects are delayed .5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

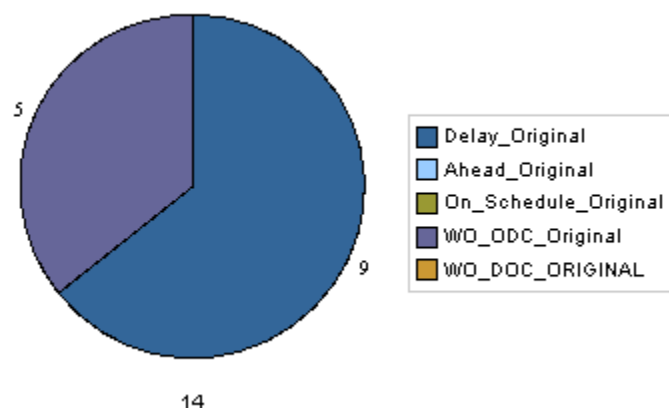

III. Investment Scenario

The Total Original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 40023.85 crore but this was subsequently revised to Rs. 61734.88 crore implying a cost overrun of 54.2%. The expenditure incurred on these projects till January, 2011 is Rs. 25420.13 crore, which is 41.2% of the revised cost of the projects.

Figures are in Rs. Crore

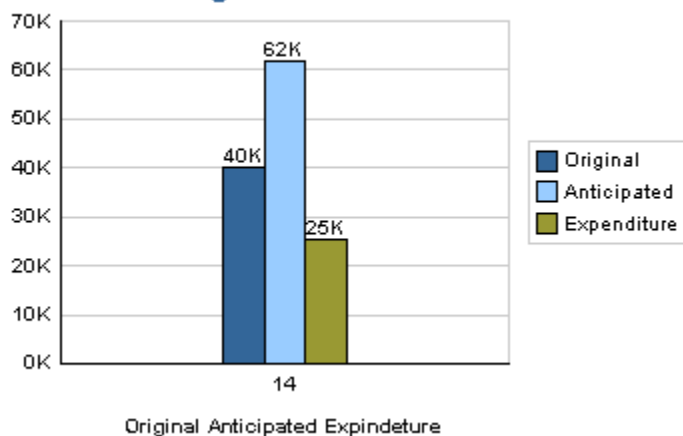

Sector wise current status of projects on the Flash Report


Mines

I. Current Status:

Number of Projects	1
Number of Projects Delayed	1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project are delayed .



III. Investment Scenario

The Total Original cost of implementation of 1 projects when sanctioned, was of the order of Rs. 4091.51 crore but this was subsequently revised to Rs. 4401.76 crore implying a cost overrun of 7.6%. The expenditure incurred on these projects till January, 2011 is Rs. 3928 crore, which is 89.2% of the revised cost of the projects.

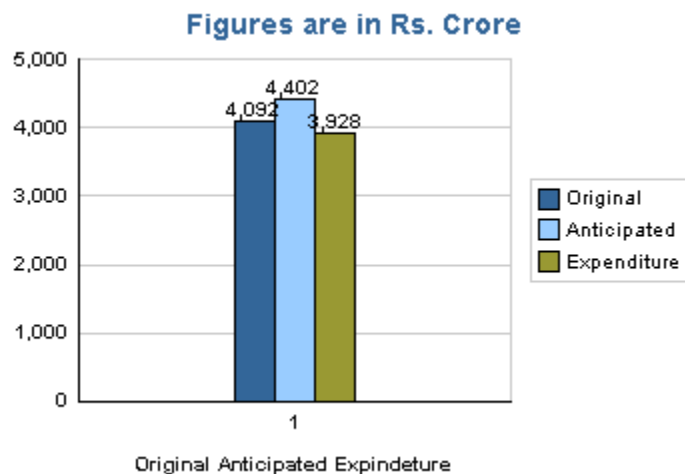

Sector wise current status of projects on the Flash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	1

Number of Projects Without Original Date of Commissioning	1
---	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule and 1 project are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

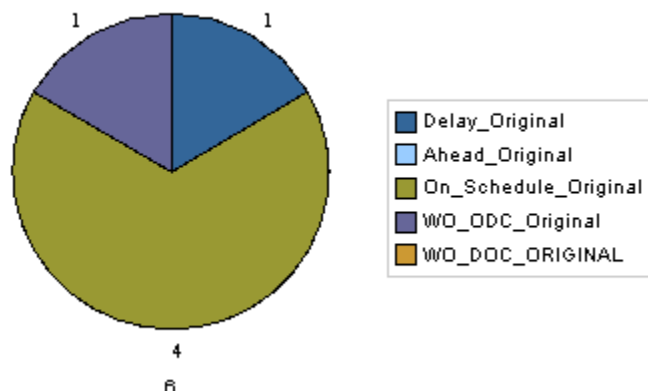

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till January, 2011 is Rs. 302.63 crore, which is 5.7% of the revised cost of the projects.

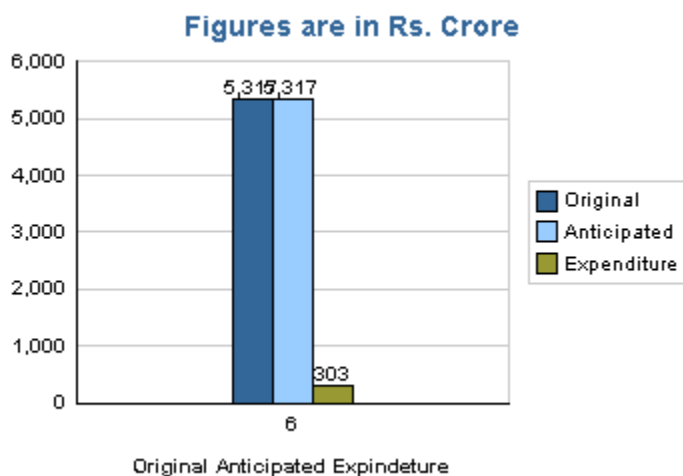

Sector wise current status of projects on the Flash Report


Civil Aviation

I. Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule and 4 projects are delayed.

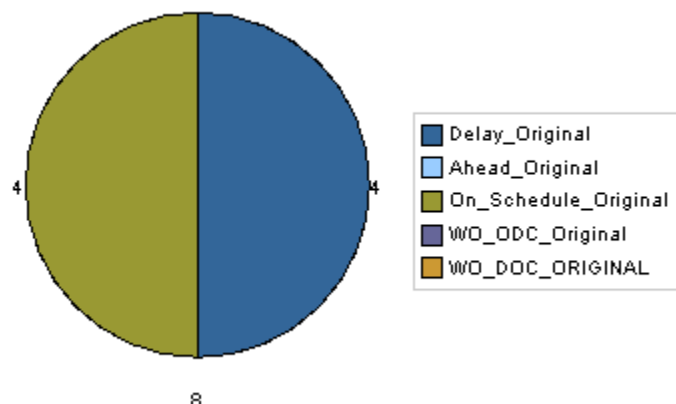

III. Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4812.4 crore but this was subsequently revised to Rs. 4812.4 crore implying a cost overrun of 0%. The expenditure incurred on these projects till January, 2011 is Rs. 2726.44 crore, which is 56.7% of the revised cost of the projects.

Figures are in Rs. Crore

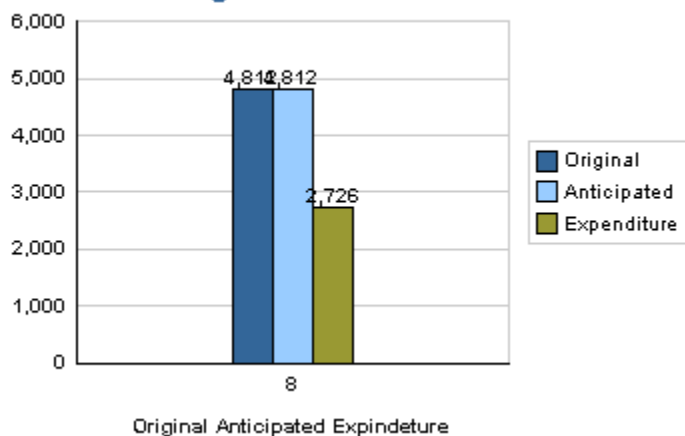

Sector wise current status of projects on the Flash Report


Atomic Energy

I. Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Original Date of Commissioning	1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

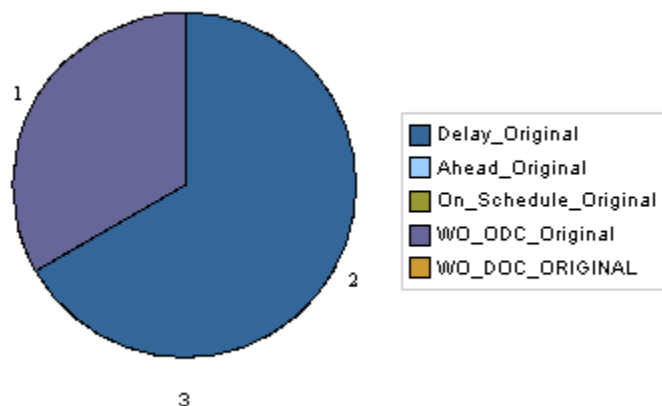

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 17769.29 crore but this was subsequently revised to Rs. 19954.29 crore implying a cost overrun of 12.3%. The expenditure incurred on these projects till January, 2011 is Rs. 16476.66 crore, which is 82.6% of the revised cost of the projects.

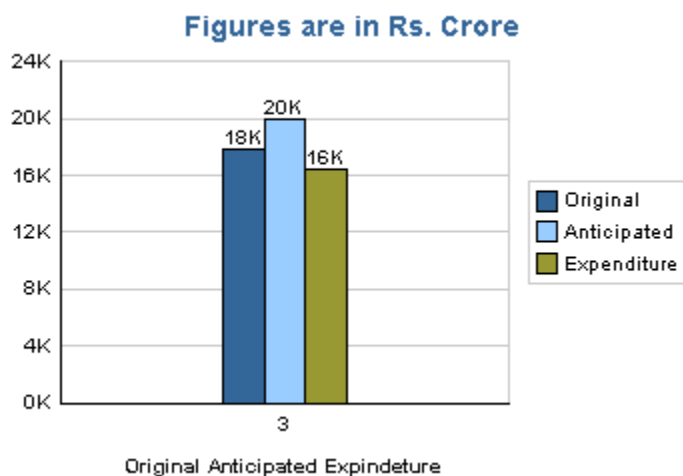

Summary of Central Sector Projects in Various States/UTs
(Status of projects as on 30.1.2011)

(Rs. Crores)

Sr N.	State Name	No of Projects	Cost Original	Cost Anticipated	Expenditure
1	Andhra Pradesh	33	29922.88	36721.08	17051.47
2	Arunachal Pr.	4	9512.22	9516.70	6074.62
3	Assam	38	22765.13	28230.16	12592.89
4	Bihar	30	28271.01	31304.80	17535.15
5	Chhatisgarh	16	15513.98	19068.97	11163.55
6	Delhi	2	8925.00	19123.77	16995.73
7	Goa	1	204.73	204.73	21.65
8	Gujarat	22	15970.27	18185.01	10277.83
9	Haryana	10	4821.32	6379.33	3607.11
10	Himachal Pr.	8	15381.72	15463.96	10803.13
11	J & K	8	8297.84	18455.56	10370.54
12	Jharkhandd	18	5622.61	7446.49	3171.33
13	Karnataka	19	13008.06	20733.20	9222.59
14	Kerala	10	9405.93	10758.72	7401.41
15	Madhya pradesh	25	18938.72	18536.21	5851.70
16	Maharashtra	53	67041.16	87348.29	30512.01
17	Mizoram	2	988.06	3343.04	220.34
18	Multi State	97	120140.81	127571.62	38045.64
19	Nagaland	1	850.00	850.00	5.46
20	Orissa	23	19399.47	23365.97	8790.25
21	Punjab	9	5064.09	6028.72	2188.31
22	Rajasthan	15	12485.03	13574.15	7701.32
23	Sikkim	2	1603.77	3644.86	138.55
24	Tamil Nadu	33	41863.66	47849.77	31866.07
25	Tripura	3	1522.39	2053.24	205.06
26	Uttar Pradesh	37	18608.18	20526.93	12681.26
27	Uttaranchal	9	12100.46	14517.85	4403.84
28	West Bengal	26	26180.59	29752.44	10610.27
29		9	53843.22	69157.60	19608.67
	TOTAL	563	588252.31	709713.17	309117.75

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
