

**315th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
January, 2012**



NPCIL



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for January, 2012 contains information on the status of the 555 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During January, 2012, 9 projects (1 project of Railways, 4 projects each of Road Transport & Highways and Telecommunication Sectors) have reported completion.

The online reporting of the implementation status of the ongoing projects from the project authorities has improved considerably with majority of project authorities reporting online during the current month. During January, 2012, 37 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 18 months, in respect of projects relating to Railways, Road Transport and Highways, Power, Petroleum, Shipping & Ports, Steel , Atomic Energy and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	131	1
2.	ROAD TRANSPORT & HIGHWAYS	127	1
3.	POWER	96	7
4.	PETROLEUM	69	16
5.	COAL	51	0
6.	TELECOMMUNICATION	18	5
7.	SHIPPING & PORTS	25	4
8.	STEEL	16	1
9.	FERTILISERS	6	0
10.	CIVIL AVIATION	5	0
11.	ATOMIC ENERGY	5	1
12.	URBAN DEVELOPMENT	4	0
13.	WATER RESOURCES	1	0
14.	PETROCHEMICALS	1	0
Total		555	36

3. The total original cost of implementation of the 555 projects was about ₹ 713744.45 Crores and their anticipated completion cost is likely to be ₹ 8,34,456.40 Crores, which reflects an overall cost overrun of 16.9 %. The expenditure incurred on these projects till January, 2012 is ₹ 3,63,343.03 Crores, which is 43.5 % of the revised cost of the projects.

4. Out of the 555 projects, 5 projects are ahead of schedule, 158 are on schedule, 233 projects are delayed and 85 projects have been sanctioned without any commissioning schedule/date. Further, in case of 74 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized.

5. During the month under reference 233 projects are reporting delay. Out of 233 delayed projects, 51 projects had overall delay in the range of 1 to 12 months, 45 projects had a delay in the range of 13 to 24 months, 104 projects had a delay in the range of 25 to 60 months and 33 projects had a delay of 61 months and above.

6. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

7. The brief reasons for time overruns as reported by various projects implementing agencies are inadequate mobilization by the contractors, law and order problems, delays in engineering designs, change of scope delays in pre-project activity, Maoist problems and forest and environment clearances etc. Brief reasons for cost overruns are mainly due to inflation, fluctuation of exchange rate, higher tender value, change of scope etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

The Sector-wise details of additional delays are as under:-

i) In the **Shipping and Ports sector**, 4 projects have reported additional delays in the range of 3-7 months .Acquisition of two Nos.of 3060 DWT, Port Trust, and Acquisition of two Nos. of 120 BP, AHTS, Shipping have reported additional delays of 3 months each . Acquisition of two Nos. of 120 BP, Shipping has reported additional delay of 5 months and Acquisition of 4 Nos. of Anchor Handling cum supply, Shipping has reported additional delay of 7 months , however the project authorities have not reported any specific reason for the delay .

ii) In the **Telecommunications sector**, 5 projects have reported additional delays in the range of 3 -13 months. Project-III of NIB-II of Messaging Storage, BSNL, Assam Telecom Circle,Phase-V.1,2G and 3G,BSNL, GSM equipment of 1625K lines(2G) 325K (3G) and GSM equipment of 1867000 lines (2G) 383000 Lines (3G),BSNL have reported additional delays of 3 months each. GSM Equipment of 390K lines (2G) and 130K Lines (3G), BSNL has reported an additional delay of 13 months. However, no reasons for delay have been reported by the project authorities for all the projects.

iii) In the **Petroleum Sector**, 16 projects have reported additional delays in the range of 1-18 months. Karanpur Moradabad-Kashipur-Rudrapur Pipeline Project, GAIL, has reported an additional delay of 1 months as the land owners are demanding for high compensation, Heera Reconstruction, ONGC has an additional delay of 3 months due to delay in revamping jobs and installation of revamped equipments, Neelam Reconstruction, ONGC has an additional delay of 3 months due to contractual problems, Development of C- Series Fields, ONGC has an additional delay of 13 months due to delay in drilling of development wells, North Tapti Gas Field Development, ONGC has an additional delay of 16 months due to increased facility costs, Offshore Grid Interconnectivity Project in Mumbai High, ONGC has an additional delay of 12 months due to contractual problems, Development of B-46 cluster fields, ONGC has reported additional delay of 2 months due to delay in New MHN Complex project, which is linked with this project, Kochi Kootanad Bangalore Mangalore Pipeline project. Phase-II,GAIL has reported additional delay of 4 months due to delay in approval of BBC , BNPL Spurline, GAIL has reported additional delay of 8 months due to stiff resistance from farmers and Dev. of B-193 Cluster Fields, ONGC has reported additional delay of 18 months due to contractual problems . Branch

Pipeline from KSPL Viramgaon to Kandla, IOCL has reported additional delay of 2 months, Construction of Tanks and Blending facility at Vad, IOCL has reported additional delay of 3 months, Development of SB-14 Fields, ONGC has reported additional delay of 4 months, 102 MW Wind Power Project, ONGC has reported additional delay of 10 months, Mumbai High North Development, Phase-II, ONGC has reported additional delay of 12 months and Development of B-22 Cluster Fields, ONGC has reported additional delay of 13 months, however; no reason has been reported by the project authorities for delay in these projects .

iv) In the **Power Sector**, 7 projects have reported additional delays in the range of 1-6 months. Two projects have reported an additional delay of 1 month each, one projects has reported an additional delay of 6 months for which no reasons have been reported by the project authority. The project, Barh STTP,Stage-1,NTPC has reported additional delay of 2 months due to delay in ordering of critical BOIs, Barh STTP,Stage-II,NTPC has reported additional delay of 3 months due to delay in supply of equipments by M/s BHEL, Transmission system associated with Chamara-III,HEP,PGCIL has reported additional delay of 3 months due to delay in generation work and Bongaigaon Thermal Power Project,NTPC has reported additional delay of 6 months due to delay in TG erection work .

v) In the **Atomic Energy Sector**, Rajasthan Atomic Power Project-7 and 8, NPCIL has reported an additional delay of 3 months due to Fukushima incident of Japan in March, 2011 .

vi) In **Steel sector**, Rebuilding of Coke Oven Battery No.1 and 2,SAIL has reported additional delay of 1 month due to slow progress by the contractor .

Aquisition of two Nos.of

vii) In the **Road Transport and Highways Sector**, 1 Project “2 laning of Mokama-Munger, NHAI has reported additional of 10 months .However, no reason has been reported by the project authority for the delay .

viii) **In Railways sector**, Project “Rail-cum-road bridge over river Brahmaputra Bridge, NEFR has reported additional delay of 12 months due to delay in tendering process .

The status as on 31.01.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.



(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	131	1
2	Road Transport & Highways	127	1
3	Power	96	7
4	Petroleum	69	16
5	Coal	51	0
6	Shipping & Ports	25	4
7	Telecommunications	18	5
8	Steel	16	1
9	Fertilisers	6	0
10	Atomic Energy	5	1
11	Civil Aviation	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	555	36

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC AND MAITHON RB(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
<u>Road Transport & Highways</u>				
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
June,2011				
<u>Petroleum</u>				
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
<u>Power</u>				
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
<u>Railways</u>				
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
<u>Road Transport & Highways</u>				
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00
July,2011				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Steel</u>				
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
<u>Petroleum</u>				
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
August,2011				
<u>Power</u>				
30	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]	262.10	09/2010	164.00
<u>Railways</u>				
31	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]	262.00	-	548.54
<u>Road Transport & Highways</u>				
32	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]	193.00	10/2008	338.70
33	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256]	359.00	03/2009	870.60
<u>Telecommunications</u>				
34	NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]	312.86	02/2008	204.43
<u>Urban Development</u>				
35	DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]	8,676.00	06/2010	18,304.30

September,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Petroleum</u>				
36	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF(INDIAN OIL CORPORATION LIMITED) - [N16000040]	293.60	12/2009	234.81
<u>Railways</u>				
37	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN(WESTERN RAILWAY) - [220100116]	112.53	03/1996	509.57
38	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves(NORTH WESTERN RAILWAY) - [N22000106]	643.36	03/2011	786.54
<u>Road Transport & Highways</u>				
39	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106225]	217.00	10/2008	352.26
October,2011				
<u>Power</u>				
40	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000043]	204.07	06/2011	129.60
November,2011				
41	WESTERN REGION STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000050]	230.89	01/2011	98.20
<u>Road Transport & Highways</u>				
42	RINGBUNDS TO JHAJHANPUR (BR-6)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000030]	340.00	06/2008	570.00
43	THRISSUR TO ANGAMALI (NH-47)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000037]	312.50	03/2009	604.40
December,2011				
<u>Mines</u>				
44	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [100100054]	4,091.51	12/2008	4,183.00
<u>Petroleum</u>				
45	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000024]	2,305.30	06/2010	1,266.47
46	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)(GAS AUTHORITY OF INDIA LIMITED) - [N16000052]	4,429.38	10/2010	2,325.60
<u>Power</u>				
47	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000023]	238.25	05/2011	220.82

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
48	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106246]	227.00	10/2008	403.60
49	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106276]	629.00	11/2010	910.00
50	LALITPUR TO SAGAR, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106299]	198.00	11/2008	187.30
51	JHANSI TO LALITPUR, NH-26(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000097]	276.09	09/2009	295.40
52	PONDICHERY - TINDIVANAU NH-66(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000100]	285.00	07/2010	359.40
<u>Shipping & Ports</u>				
53	Construction & License out the OPERATION, MANAG. &(PORT TRUST) - [N25000038]	230.00	12/2010	219.00
<u>Telecommunications</u>				
54	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000039]	601.49	12/2008	496.20
55	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1(BHARAT SANCHAR NIGAM LIMITED) - [N26000040]	192.48	03/2009	119.45
56	Procurement of 2.5G DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000066]	424.00	03/2009	.00
57	Procurement of 10G (40 chl) DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000067]	590.10	03/2009	.00
58	Procurement of 10G 40 CHL (12 chl equipped) DWDM(BHARAT SANCHAR NIGAM LIMITED) - [N26000068]	545.50	03/2010	.00
59	Procurement of STM-1 SDH equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000069]	154.03	03/2010	.00
60	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000070]	355.92	03/2010	.00
61	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000071]	477.00	03/2010	.00
62	Procurement of DXC equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000074]	229.00	03/2010	.00
63	GSM equipment of 900000Lines (2G) PunjabPhase V.2(BHARAT SANCHAR NIGAM LIMITED) - [N26000081]	241.49	09/2009	123.76
64	GSM equipment of 975000Lines (2G) 325000 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000083]	625.53	02/2010	.00
65	GSM equipment of 1100000Lines (2G) UP East Phase(BHARAT SANCHAR NIGAM LIMITED) - [N26000084]	624.75	09/2010	.00
66	GSM equipment of 375000Lines (2G) 75000lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000085]	170.23	06/2009	.00
67	GSM equipment of 849862Lines (2G) 150138 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000087]	584.33	02/2009	403.71
68	GSM equipment of 1900000Lines (2G) 401700 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000091]	760.20	-	819.57
69	GSM equipment of 1700000Lines (2G) 234100 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000092]	677.75	10/2009	461.56

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
January, 2012				
<u>Railways</u>				
70	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)(WESTERN RAILWAY) - [220100322]	148.61	03/2008	260.07
<u>Road Transport & Highways</u>				
71	KASIA TO GORAKHPUR (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106291]	242.00	12/2008	434.10
72	SITAPUR-LUCKNOW(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000036]	322.00	06/2009	553.70
73	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000090]	418.04	03/2010	343.30
74	TRICHY - DINDIGUL NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000099]	576.00	07/2010	661.40
<u>Telecommunications</u>				
75	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3(BHARAT SANCHAR NIGAM LIMITED) - [N26000043]	1,799.94	09/2009	309.79
76	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN(BHARAT SANCHAR NIGAM LIMITED) - [N26000050]	335.91	03/2009	182.45
77	GSM equipment of 945000Lines (2G) 225000lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000086]	366.00	10/2008	227.39
78	GSM equipment of 1900000Lines (2G) 335500lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000094]	848.70	01/2010	712.86

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2012				
<u>Civil Aviation</u>				
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97
January,2012				
<u>Power</u>				
2	TUIRIAL HE PROJECT(NEEPCO)(NORTH EAST ELECTRIC POWER CORPORATION) - [N16000049]	368.72	07/2006	295.47


Summary of projects in the Flash Report for the month of January, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	587
Number of Projects completed/dropped/frozen in Previous Month	26
Number of Projects completed/dropped/frozen in Current Month	10
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	1
Number of Projects Added in Current Month	3
Number of Projects in Current Month	555


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 555 projects, 5 projects are ahead of schedule, 158 projects are on schedule and 233 projects are delayed. Of the balance, 85 projects do not have fixed dates of commissioning while 74 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

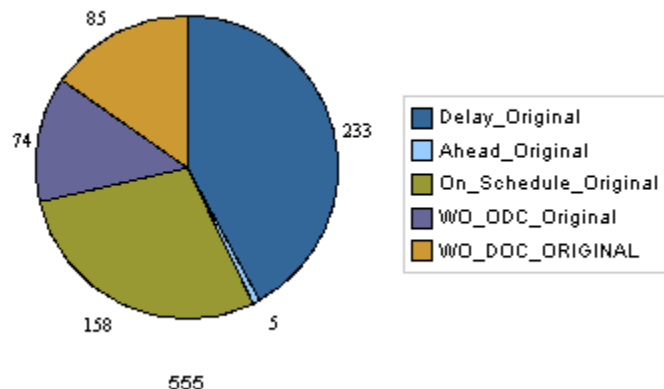

III. Investment Scenario

The Total Original cost of implementation of 555 projects when sanctioned, was of the order of Rs. 713744.45 crore but this was subsequently revised to Rs. 834456.4 crore implying a cost overrun of 16.9%. The expenditure incurred on these projects till January, 2012 is Rs. 363343.03 crore, which is 43.5% of the revised cost of the projects.

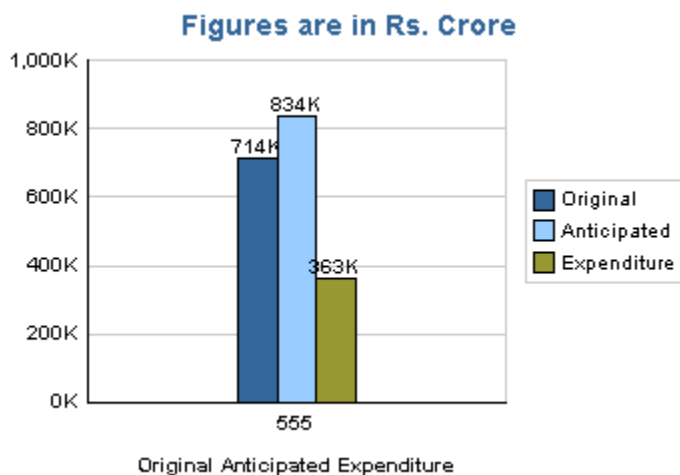

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	587
No of Projects Completed/Dropped/Frozen in Previous Month	26
No of Projects Completed/Dropped/Frozen in Current Month	10
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	1
No of Projects added in Current Month	3
No of Projects in Current Month	555

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	233	5	158	74	85	555	41.98
Latest Approved (Date)	241	13	203	44	55	555	43.42

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	437	576,442.17	620,958.76	238,916.24	38.50	44,516.59	7.70
Latest Approved (RCE)	118	190,428.94	213,497.64	124,426.79	58.30	23,068.70	12.10
Total (RCE)	555	766,871.11	834,456.40	363,343.03	43.54	67585.29	8.81
Original Cost of All Projects							
Original Cost	555	713,744.45	834,456.40	363,343.03	43.50	120,711.95	16.90

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	233	370,038.47	446,717.12	244,377.54	54.70	76,678.65	20.70
Latest Approved (RCE)	241	367,603.45	413,237.45	218,772.42	52.90	45,634.00	12.40

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	37	67,124.73	71,906.40	32,615.61	45.40	4,781.67	7.10

Extent of cost overrun in projects with respect to original schedule

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	33	32,855.2	39,238.5	19.4	13	11,677.0	19,002.1	62.7
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	37	23,895.8	35,508.8	48.6	13	11,923.7	23,630.9	98.2
4	Bihar	26	27,578.9	32,829.3	19.0	15	16,731.8	21,982.3	31.4
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	27	32,375.1	32,903.3	1.6	6	2,826.5	3,354.8	18.7
7	Haryana	10	5,795.4	7,611.8	31.3	3	1,448.2	3,264.7	125.4
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	3	7,629.8	10,324.0	35.3
9	J and K	10	14,019.4	33,604.4	139.7	6	7,866.5	27,478.4	249.3
10	Karnataka	25	30,657.6	39,102.5	27.5	10	8,795.3	17,646.7	100.6
11	Kerala	7	6,086.2	6,775.2	11.3	2	795.7	1,587.2	99.5
12	Madhya pradesh	24	17,335.6	17,581.8	1.4	3	2,027.6	2,741.5	35.2
13	Maharashtra	51	68,705.3	82,228.7	19.7	18	29,305.0	45,606.1	55.6
14	Manipur	1	727.6	3,056.9	320.2	1	727.6	3,056.9	320.2
15	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
16	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
17	Orissa	26	42,465.4	45,636.4	7.5	13	33,147.5	36,510.8	10.1
18	Punjab	7	4,613.2	5,598.2	21.4	3	761.4	1,746.5	129.4
19	Rajasthan	15	25,357.2	26,106.3	3.0	4	1,684.9	2,818.7	67.3
20	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
21	Tamil Nadu	35	52,241.3	60,526.4	15.9	13	27,364.2	35,649.3	30.3
22	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
23	Uttar Pradesh	24	17,544.0	21,597.8	23.1	9	3,729.2	7,783.0	108.7
24	West Bengal	25	37,585.8	46,969.0	25.0	12	20,281.1	29,664.3	46.3
25	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
26	Chhatisgarh	25	55,916.8	59,148.1	5.8	7	4,746.6	7,977.9	68.1
27	Jharkhandd	22	14,396.5	15,999.9	11.1	6	1,897.3	3,672.5	93.6
28	Uttaranchal	6	10,025.7	11,948.2	19.2	3	3,942.3	5,864.9	48.8
29	Multi State	97	125,418.4	130,674.3	4.2	21	6,635.4	15,682.9	136.4
Total		555	713,744.5	834,456.4	16.9	190	215,579.1	345,668.1	60.3

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	51	34,718.7	38,348.4	10.5	12	13,742.8	17,970.2	30.8
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	65,244.8	71,412.4	9.5	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	69	149,804.8	158,021.2	5.5	16	49,968.0	65,969.0	32.0
8	Power	96	197,932.5	213,231.6	7.7	19	45,642.3	61,006.4	33.7
9	Railways	131	64,906.1	134,280.0	106.9	101	37,225.0	106,655.8	186.5
10	Road Transport & Highways	127	72,336.6	74,425.7	2.9	15	4,435.6	7,093.7	59.9
11	Shipping & Ports	25	18,221.4	19,237.4	5.6	10	6,294.5	7,511.6	19.3
12	Telecommunications	18	8,443.6	8,559.9	1.4	3	1,315.9	1,514.8	15.1
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		555	713,744.5	834,456.4	16.9	190	215,579.1	345,668.1	60.3

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	3	28,983.0	33,821.0	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 23
3	Coal	51	34,718.7	38,348.4	10.5	17	11,824.7	14,994.8	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	8 - 9
5	Steel	16	65,244.8	71,412.4	9.5	5	46,957.9	52,521.9	3 - 36
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	149,804.8	158,021.2	5.5	31	84,314.1	92,699.5	4 - 120
8	Power	96	197,932.5	213,231.6	7.7	47	124,405.2	139,091.3	1 - 83
9	Railways	131	64,906.1	134,280.0	106.9	27	22,136.8	52,427.2	2 - 204
10	Road Transport & Highways	127	72,336.6	74,425.7	2.9	78	27,654.3	29,936.9	2 - 101
11	Shipping & Ports	25	18,221.4	19,237.4	5.6	10	8,208.4	9,033.6	2 - 93
12	Telecommunications	18	8,443.6	8,559.9	1.4	7	3,457.6	3,647.0	16 - 75
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		555	713,744.5	834,456.4	16.9	233	370,038.5	446,717.1	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	5	41,548.3	46,386.3	0 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 23
3	Coal	51	34,718.7	38,348.4	10.5	17	11,824.7	14,994.8	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	8 - 9
5	Steel	16	65,244.8	71,412.4	9.5	8	39,531.8	41,991.7	0 - 9
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	149,804.8	158,021.2	5.5	27	71,544.0	75,417.0	0 - 73
8	Power	96	197,932.5	213,231.6	7.7	36	110,821.7	121,114.5	1 - 83
9	Railways	131	64,906.1	134,280.0	106.9	34	15,014.9	47,950.8	0 - 213
10	Road Transport & Highways	127	72,336.6	74,425.7	2.9	80	28,080.8	30,529.9	0 - 101
11	Shipping & Ports	25	18,221.4	19,237.4	5.6	12	8,583.6	9,536.3	2 - 93
12	Telecommunications	18	8,443.6	8,559.9	1.4	14	6,592.7	6,772.1	7 - 75
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		555	713,744.5	834,456.4	16.9	241	345,638.9	413,237.5	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	51	36,331.9	38,348.4	5.6	8	6,637.3	9,121.4	37.4
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	71,120.1	71,412.4	0.4	3	598.0	910.3	52.2
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	69	163,049.4	158,021.2	-3.1	3	32,036.9	32,844.0	2.5
8	Power	96	201,774.5	213,231.6	5.7	13	36,652.4	48,174.4	31.4
9	Railways	131	89,130.1	134,280.0	50.7	81	46,265.6	91,707.3	98.2
10	Road Transport & Highways	127	72,503.1	74,425.7	2.7	14	4,239.1	6,730.7	58.8
11	Shipping & Ports	25	18,653.2	19,237.4	3.1	8	6,321.3	7,007.1	10.8
12	Telecommunications	18	8,447.5	8,559.9	1.3	1	250.0	425.5	70.2
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		555	766,871.1	834,456.4	8.8	136	158,544.0	233,542.7	47.3

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	0	0.00	0.00	0- 0
3	Coal	51	34,718.73	38,348.38	10.45	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	1	8,692.00	12,291.00	36- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	149,804.77	158,021.15	5.48	7	11,185.02	20,009.18	24- 120
8	Power	96	197,932.45	213,231.64	7.73	1	1,657.00	2,978.86	67- 67
9	Railways	131	64,906.13	134,280.01	106.88	2	1,624.47	4,619.99	62- 92
10	Road Transport & Highways	127	72,336.63	74,425.72	2.89	0	0.00	0.00	0- 0
11	Shipping & Ports	25	18,221.36	19,237.40	5.58	1	277.03	277.03	8- 8
12	Telecommunications	18	8,443.59	8,559.89	1.38	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		555	713744.45	834456.4	16.91	13	23905.3	40882.46	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	1	13,171.00	15,824.00	51- 51
2	Civil Aviation	5	5,021.58	5,611.07	11.74	0	0.00	0.00	0- 0
3	Coal	51	34,718.73	38,348.38	10.45	6	5,699.06	8,712.38	9- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	1	8,692.00	12,291.00	36- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	149,804.77	158,021.15	5.48	11	46,117.51	60,527.00	7- 120
8	Power	96	197,932.45	213,231.64	7.73	14	37,998.08	49,484.08	7- 67
9	Railways	131	64,906.13	134,280.01	106.88	14	9,578.12	38,825.97	45- 201
10	Road Transport & Highways	127	72,336.63	74,425.72	2.89	11	3,387.01	5,536.10	7- 99
11	Shipping & Ports	25	18,221.36	19,237.40	5.58	5	3,252.85	4,180.50	12- 93
12	Telecommunications	18	8,443.59	8,559.89	1.38	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	24- 24
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		555	713744.45	834456.4	16.91	65	134833.53	208177.03	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
TUIRIAL HE PROJECT(NEEPCO)	07/1998	368.72	07/2006	913.63	01/2014	295.47
<u>Railways</u>						
PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	04/2005	148.61	03/2008	227.52	10/2010	260.07
<u>Road Transport & Highways</u>						
KASIA TO GORAKHPUR (NH-28)(NHAI)	12/2003	242.00	12/2008	242.00	01/2012	434.10
KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN	12/2003	418.04	03/2010	418.04	01/2012	343.30
TRICHY - DINDIGUAL NH-45	03/2005	576.00	07/2010	576.00	01/2012	661.40
SITAPUR-LUCKNOW	03/2005	322.00	06/2009	322.00	01/2012	553.70
<u>Telecommunications</u>						
GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3	09/2008	1,799.94	09/2009	1,799.94	03/2012	309.79
GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN	05/2007	335.91	03/2009	335.91	03/2012	182.45
GSM equipment of 945000Lines (2G) 225000lines 3(G)	10/2007	366.00	10/2008	366.00	03/2012	227.39
GSM equipment of 1900000Lines (2G) 335500lines 3(G)	01/2009	848.70	01/2010	848.70	03/2012	712.86

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Power</u>					
SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC	1/2012	1,422.85	1/2015	1,422.85	1/2015
TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT	1/2012	259.28	1/2013	259.28	1/2013
TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	1/2011	913.63	1/2014	913.63	1/2014

VII. Milestones (Cumulative due & achieved)

Total	2398
Achieved up to month	987

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) NPCIL	12,320.00	12,320.00	12/2016	12/2016	03/2017	3
<u>Steel</u>						
Rebuilding of coke oven battery No.1 and 2 (Bokar SAIL	500.90	500.90	N.A.	01/2012	02/2012	1
<u>Petroleum</u>						
KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-GAIL	238.68	204.00	01/2012	04/2012	05/2012	1
DEVELOPMENT OF B-46 CLUSTER FIELD ONGC	1,436.21	1,436.21	07/2010	05/2012	07/2012	2
BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA IOCL	250.00	250.00	03/2013	01/2012	03/2012	2
HEERA RECONSTRUCTION ONGC	706.70	706.70	04/2010	12/2011	03/2012	3
NEELAM RECONSTRUCTION ONGC	305.08	305.08	04/2011	12/2011	03/2012	3
CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD IOCL	267.00	267.00	09/2012	03/2012	06/2012	3
Development of SB-14 field ONGC	410.44	410.44	11/2012	01/2013	05/2013	4
KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II GAIL	2,915.00	2,915.00	N.A.	12/2012	04/2013	4
BNPL SPURLINE (UTTRANCHAL AND PUNJAB) GAIL	540.92	460.70	N.A.	07/2012	03/2013	8
102 MW WIND POWER PROJECT ONGC	1,106.00	1,106.00	06/2012	06/2012	04/2013	10
OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2012	03/2013	12
MUMBAI HIGH NORTH DEVELOPMENT PHASE-II ONGC	7,133.39	6,855.93	09/2012	09/2012	09/2013	12


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
DEVELOPMENT OF C-SERIES FIELDS ONGC	3,195.16	2,800.00	N.A.	03/2012	04/2013	13
DEVELOPMENT OF B-22 CLUSTER FIELDS ONGC	2,323.40	2,920.82	09/2010	03/2012	04/2013	13
North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	06/2011	10/2012	16
DEVELOPMENT OF B-193 CLUSTER FIELDS ONGC	3,248.78	5,633.44	08/2010	06/2012	12/2013	18
Power						
WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI PGCIL	409.50	409.50	02/2012	02/2012	03/2012	1
SYSTEM STRENGTHENING - XI IN SOUTHERN REGION PGCIL	196.10	196.10	07/2011	02/2012	03/2012	1
BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	10/2014	12/2014	2
BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	10/2013	01/2014	3
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	297.91	07/2011	03/2012	06/2012	3
BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	06/2011	10/2013	04/2014	6
Trans. System associated with PALLATANA GBPP & BPT PGCIL	2,144.00	2,144.00	12/2012	12/2012	06/2013	6
Railways						
RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE NEFR	1,000.00	3,230.01	04/2008	12/2014	12/2015	12
Road Transport & Highways						
2 LANNING OF MOKAMA-MUNGER NHAI	351.54	351.54	05/2013	05/2013	03/2014	10
Shipping & Ports						
Acquisition of Two nos. of 3060 DWT PORT TRUST	277.03	277.03	12/2011	05/2012	08/2012	3
ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS SHIPP.	241.50	241.50	09/2011	09/2011	12/2011	3
Acquisition of two nos. of 120 B.P SHIPP.	290.85	305.00	06/2011	01/2012	06/2012	5
ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY SHIPP.	359.44	359.44	04/2011	11/2011	06/2012	7


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Telecommunications</u>						
PROJ.III OF NIB-II OF MESSAGING STORAGE BSNL	250.00	425.51	12/2005	12/2011	03/2012	3
Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	12/2011	03/2012	3
GSM equipment of 1867000Lines (2G) 383000 lines 3(BSNL	868.00	868.00	08/2009	12/2011	03/2012	3
GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	930.60	11/2010	12/2011	03/2012	3
GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) BSNL	373.94	373.94	12/2008	02/2011	03/2012	13
Number of projects reporting additional delay = 36						

Trend and Graphical Analysis of All Projects

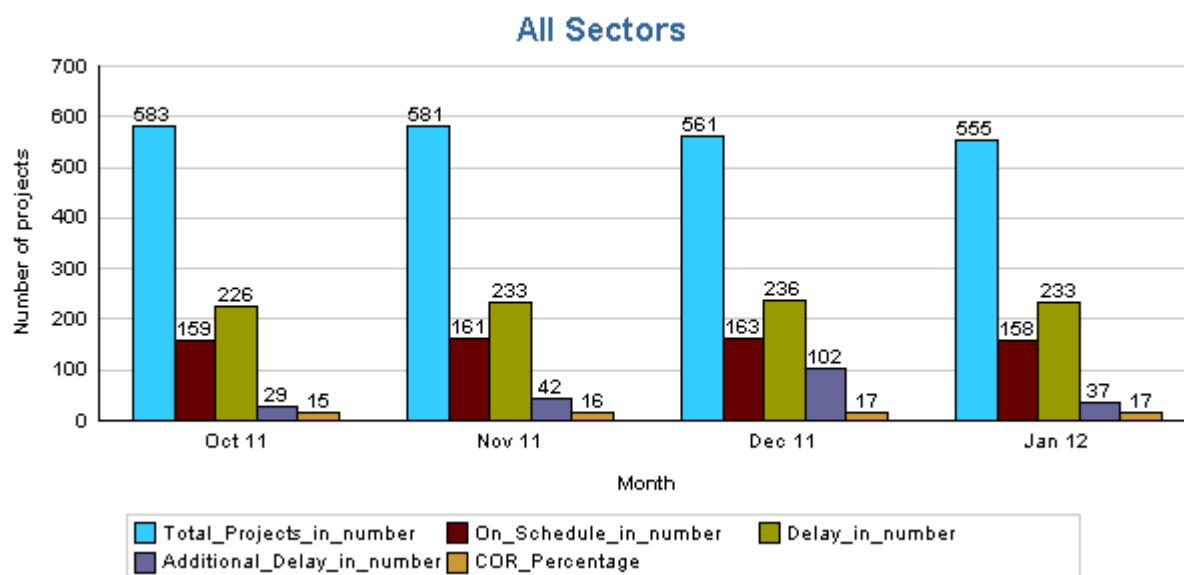


All Sectors Break-up of 233 Delayed projects in January 2012

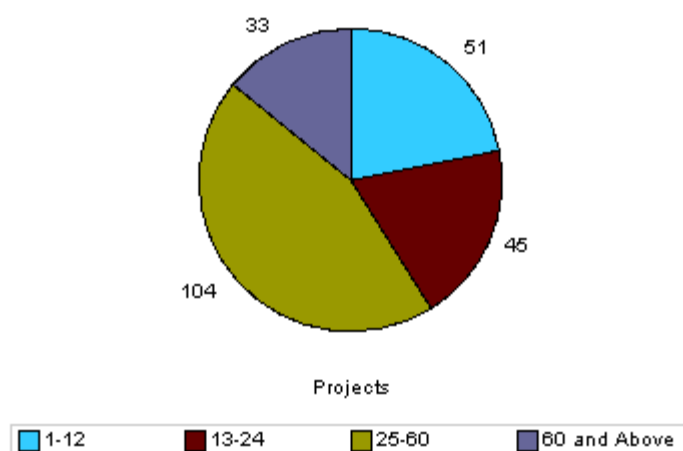


Trend and Graphical Analysis


Urban Development Sector

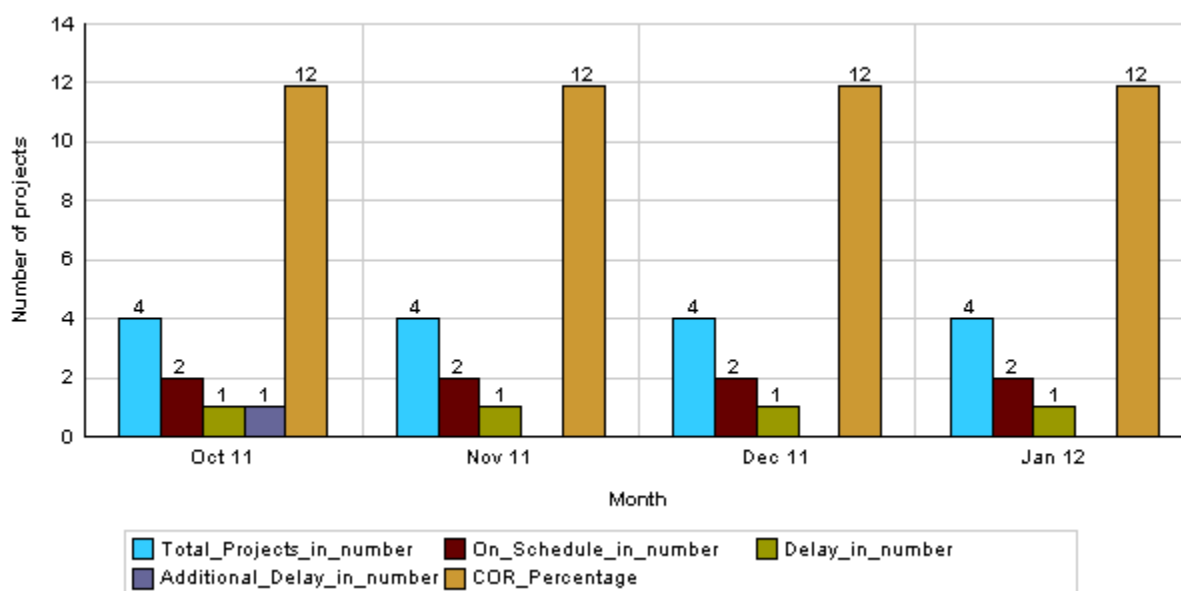


Urban Development Sector Break-up of 1 Delayed projects in January 2012

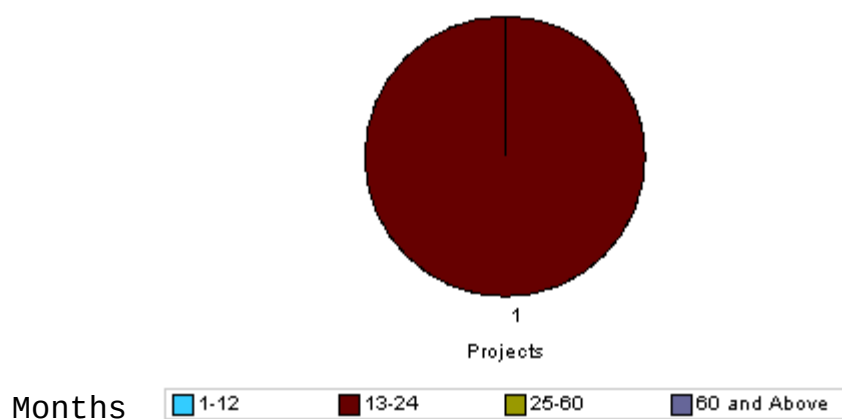

Trend and Graphical Analysis Telecommunications Sector

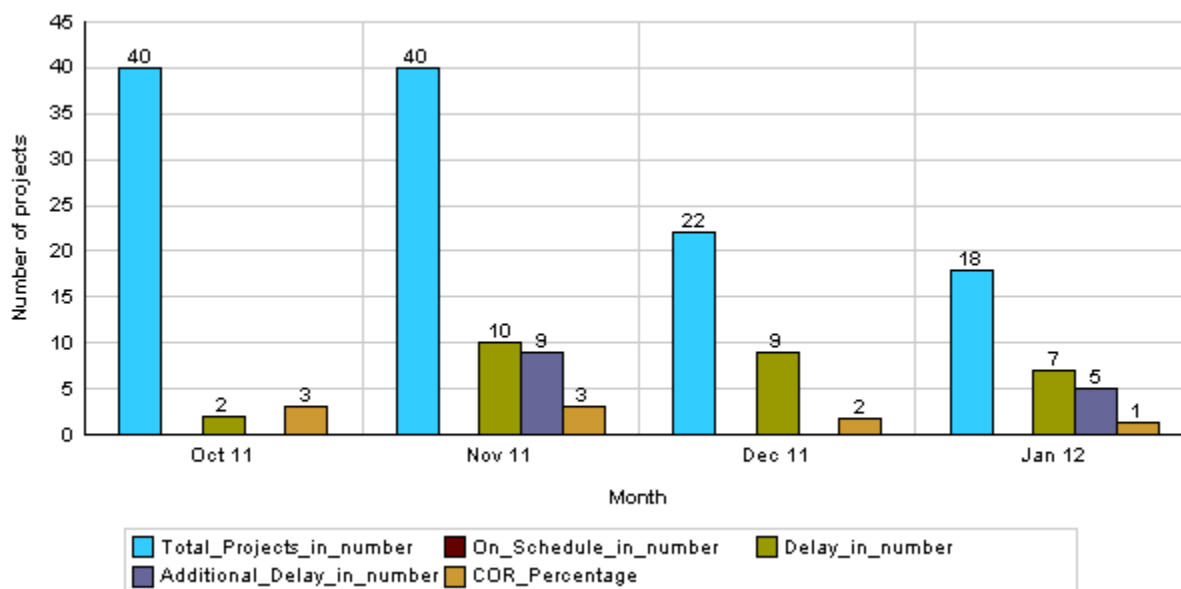


Telecommunications Sector Break-up of 7 Delayed projects in January 2012

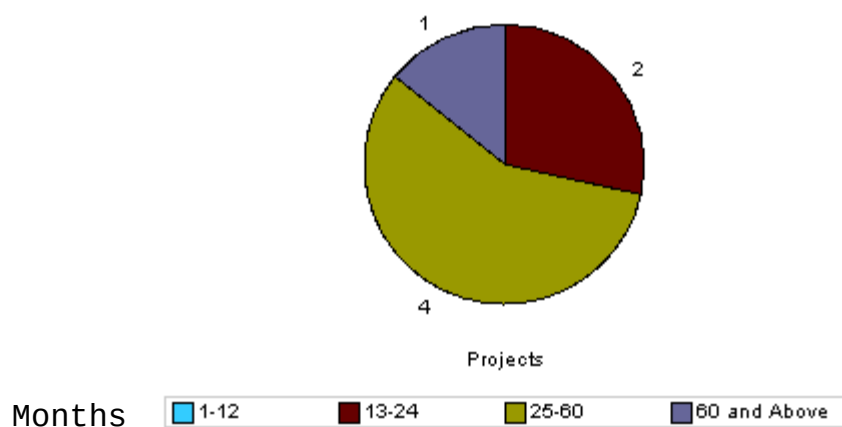


Trend and Graphical Analysis


Shipping and Ports Sector

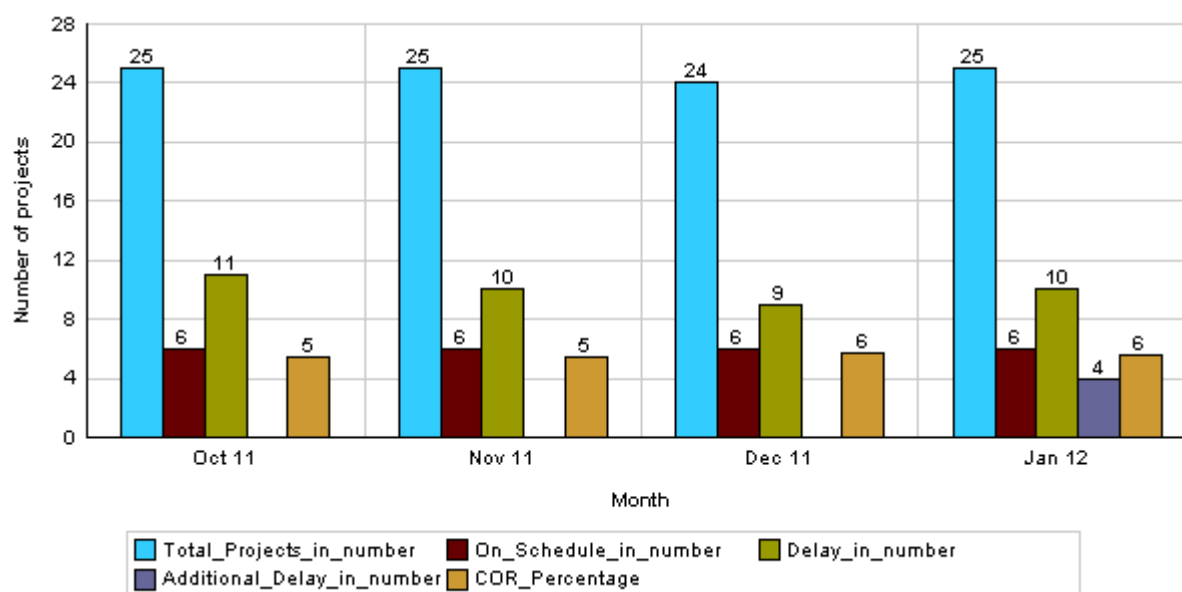


Sector Break-up of 10 Delayed projects in January 2012

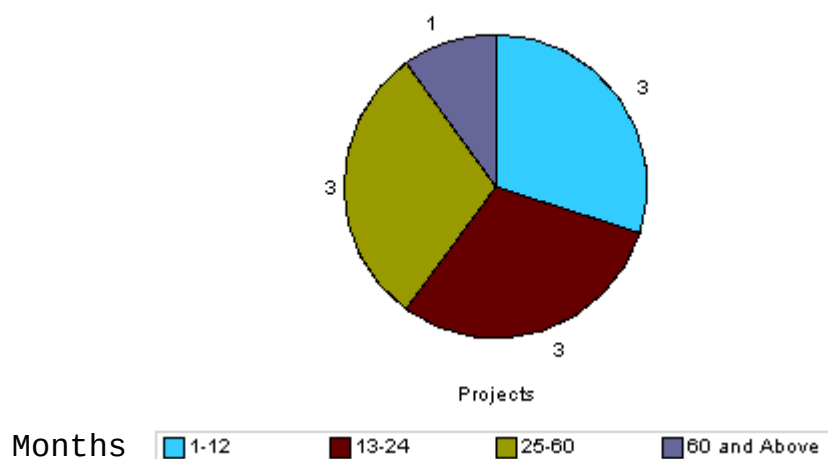

Trend and Graphical Analysis Road Transport and Highways Sector

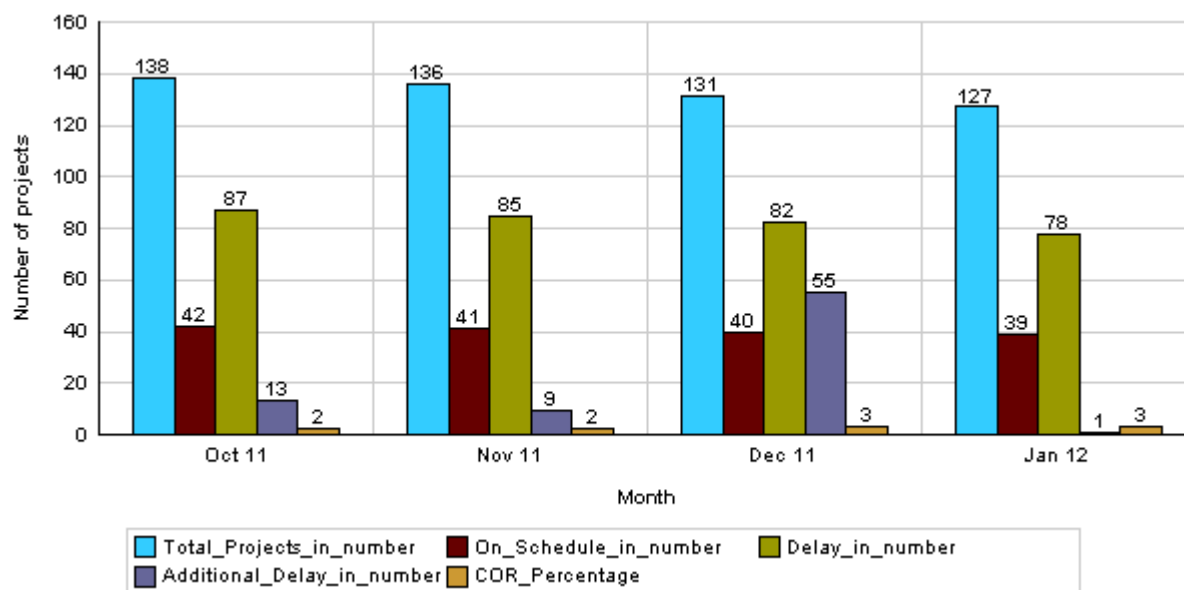


Sector Break-up of 78 Delayed projects in January 2012

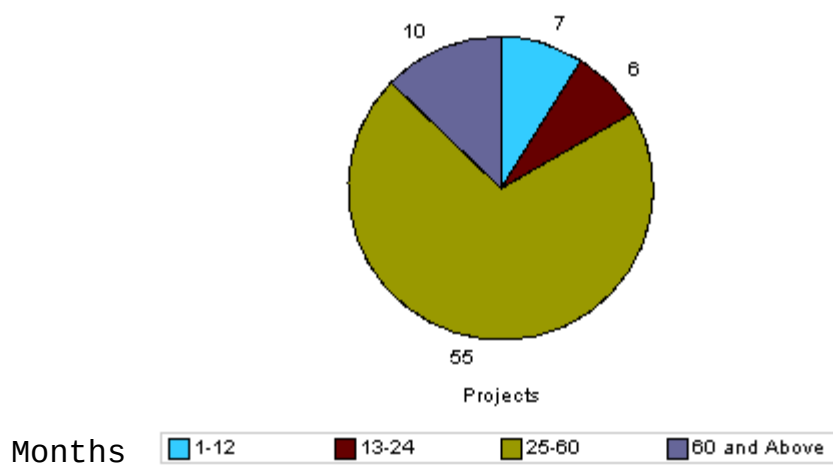


Trend and Graphical Analysis

Railways Sector

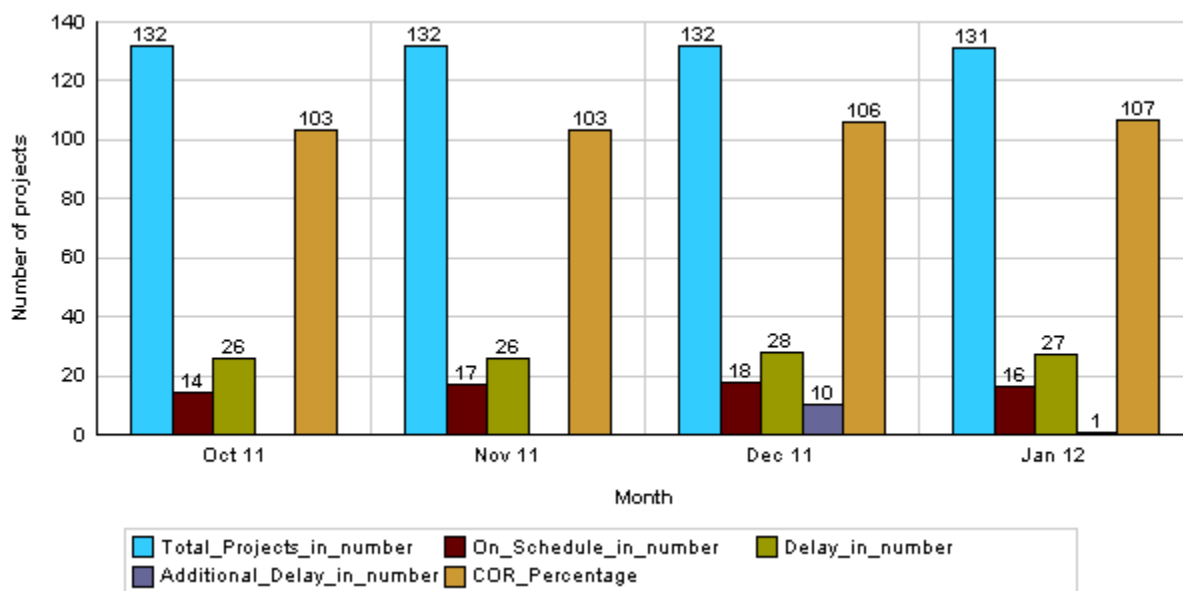


Railways Sector Sector Break-up of 27 Delayed projects in January 2012

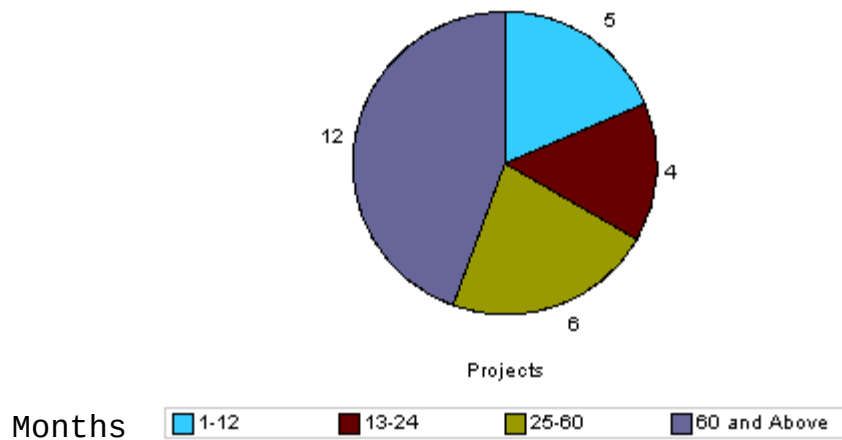


Trend and Graphical Analysis

Power Sector

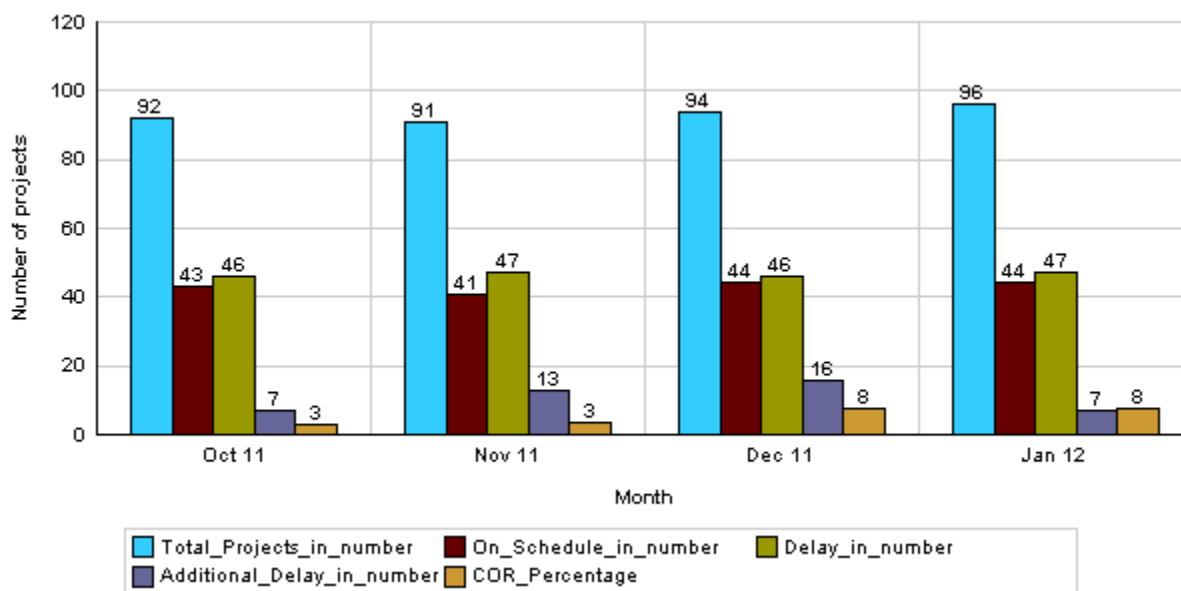


Power Sector Sector Break-up of 47 Delayed projects in January 2012

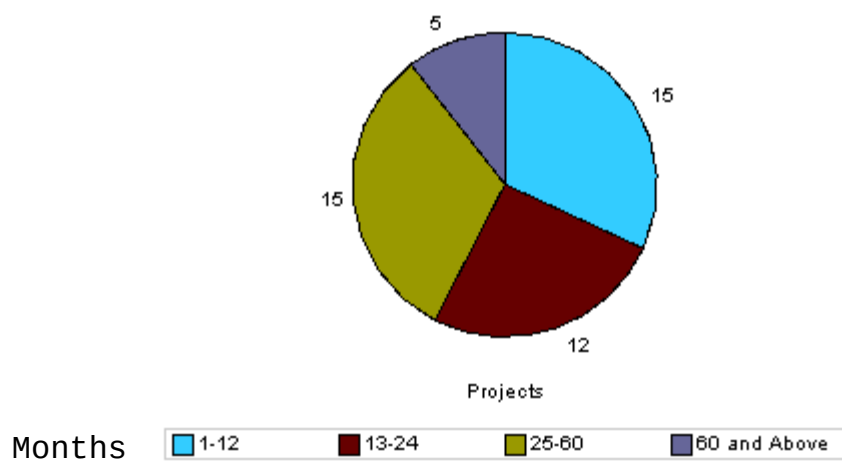


Trend and Graphical Analysis

Petroleum Sector

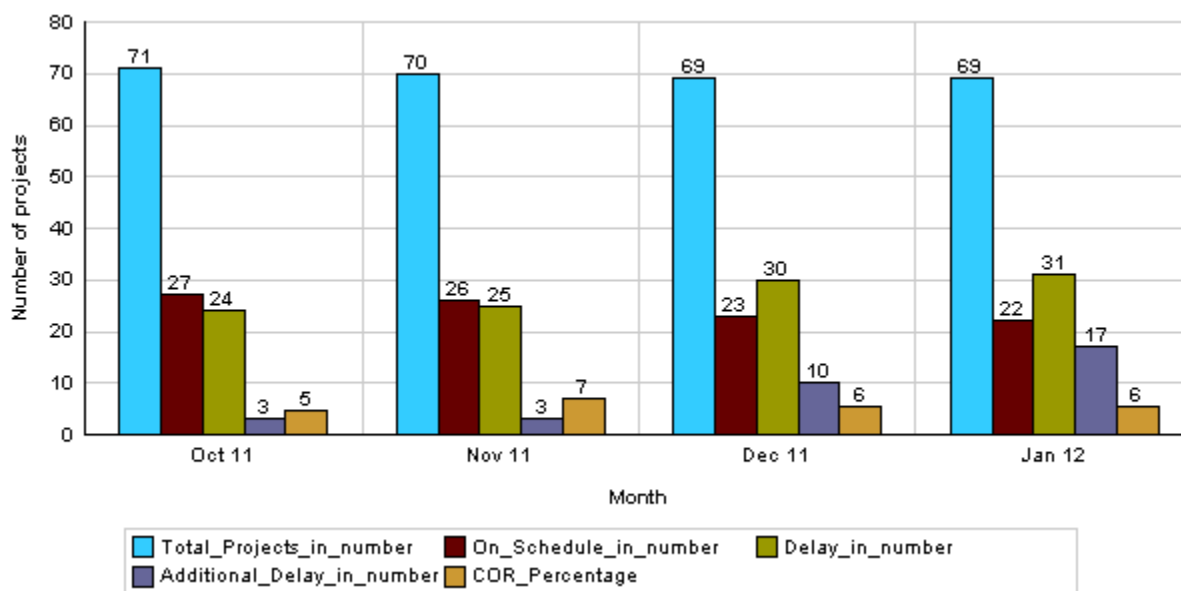


Petroleum Sector Break-up of 31 Delayed projects in January 2012

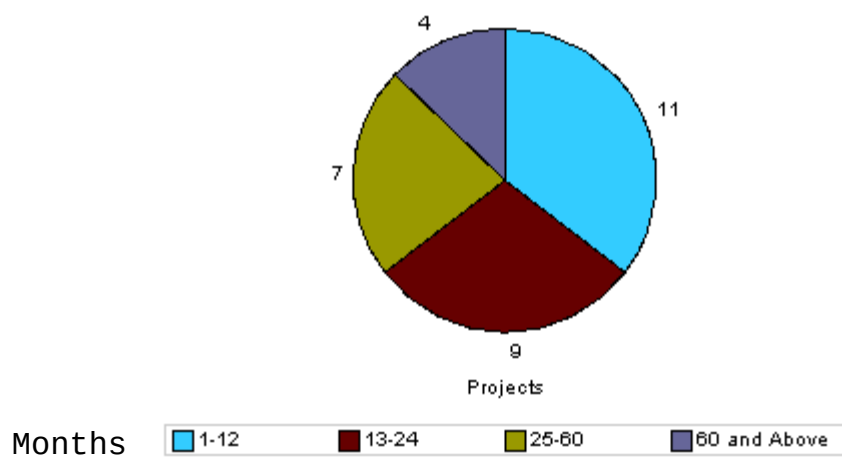


Trend and Graphical Analysis

Steel Sector

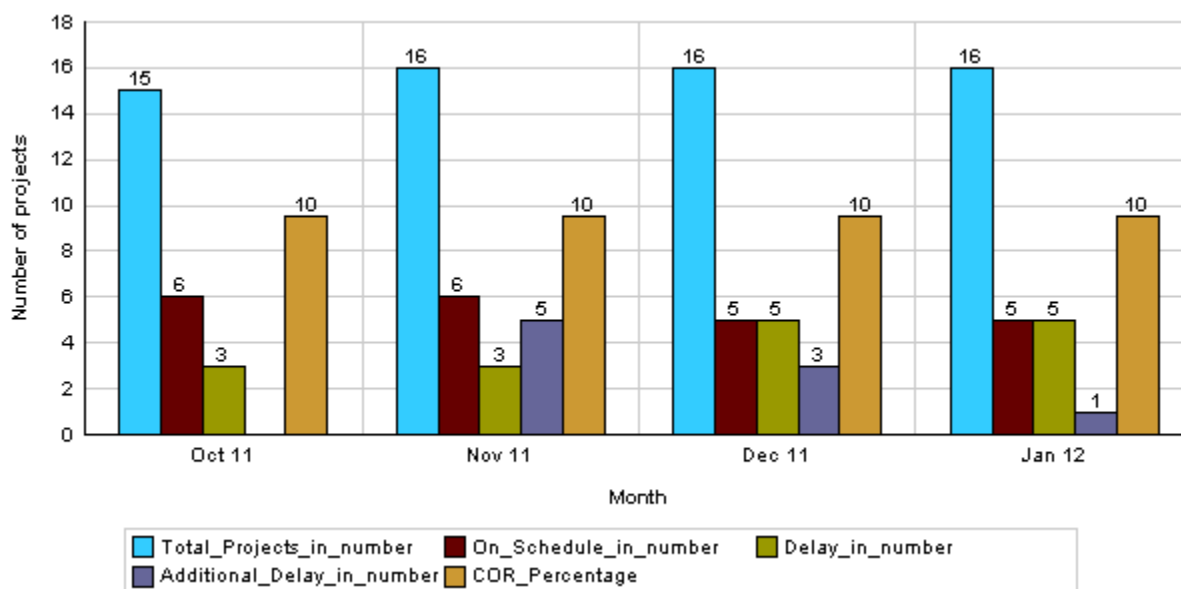


Steel Sector Sector Break-up of 5 Delayed projects in January 2012

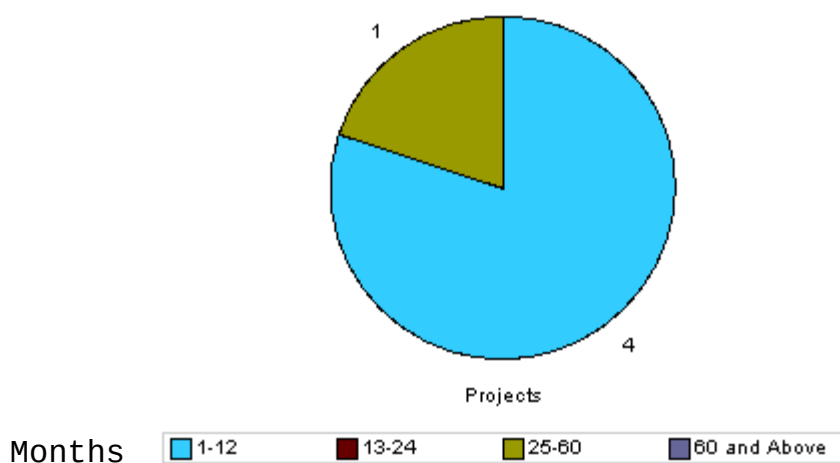


Trend and Graphical Analysis

Fertilisers Sector

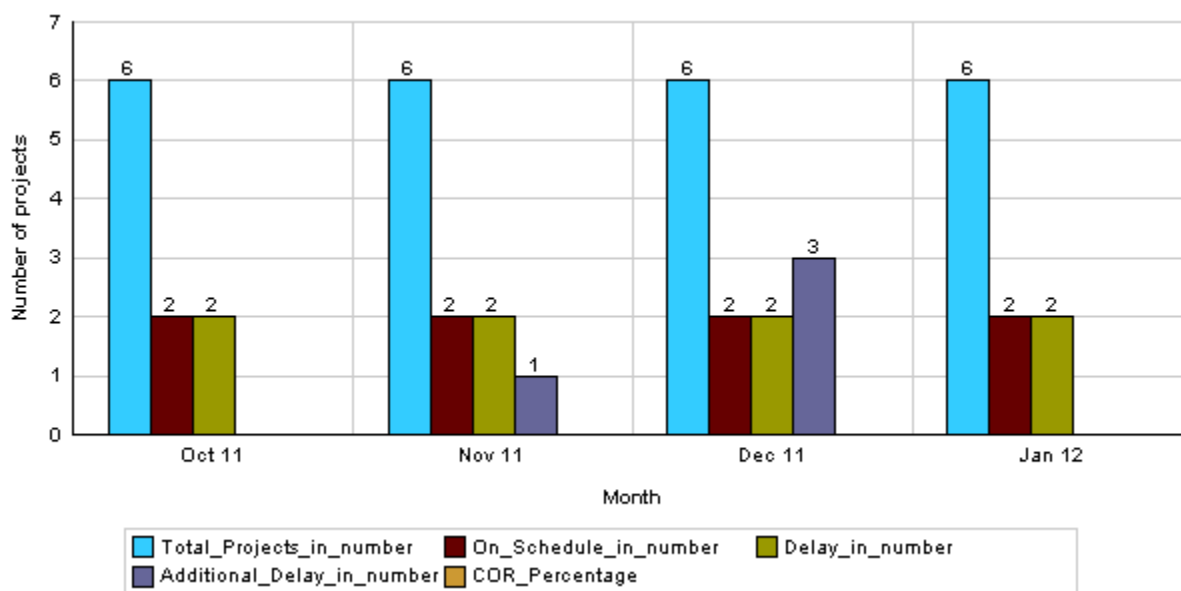


Fertilisers Sector Sector Break-up of 2 Delayed projects in January 2012

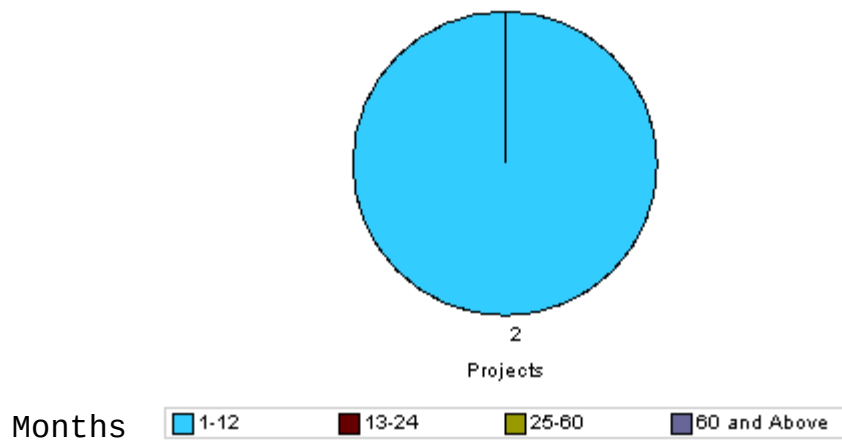


Trend and Graphical Analysis

Coal Sector

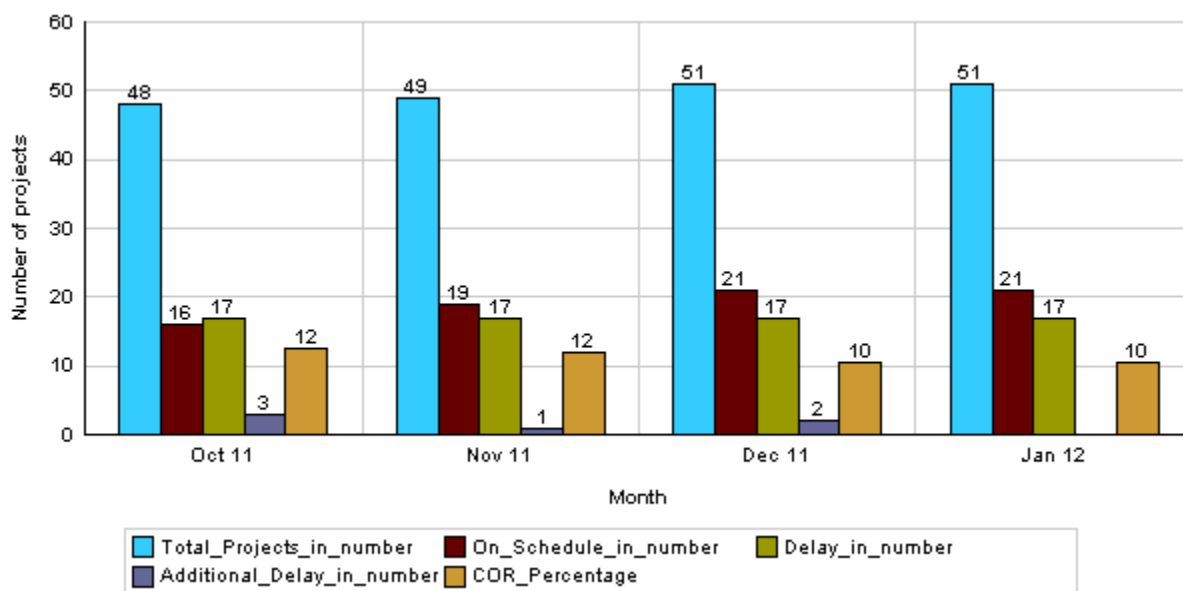


Coal Sector Break-up of 17 Delayed projects in January 2012

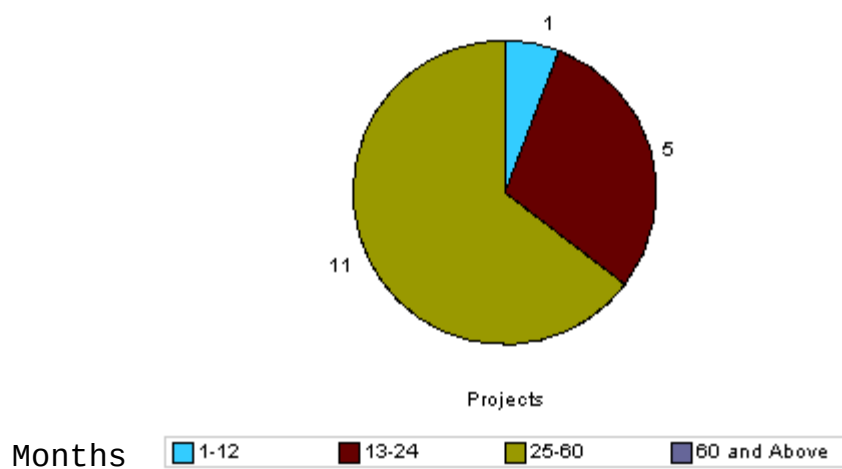


Trend and Graphical Analysis

Civil Aviation Sector

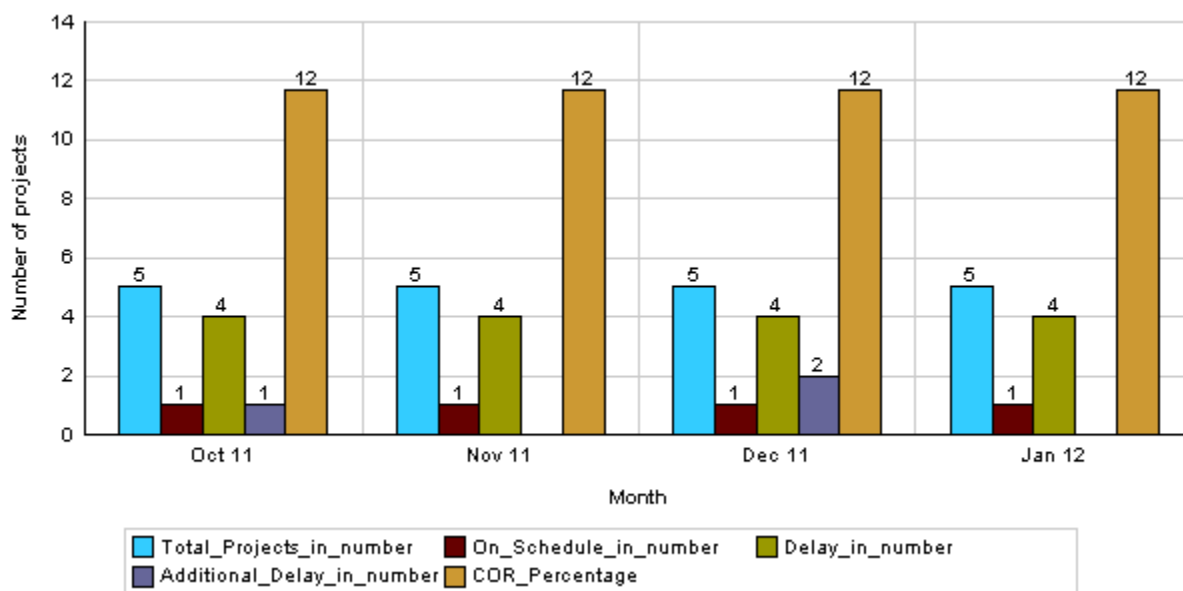


Civil Aviation Sector Break-up of 4 Delayed projects in January 2012

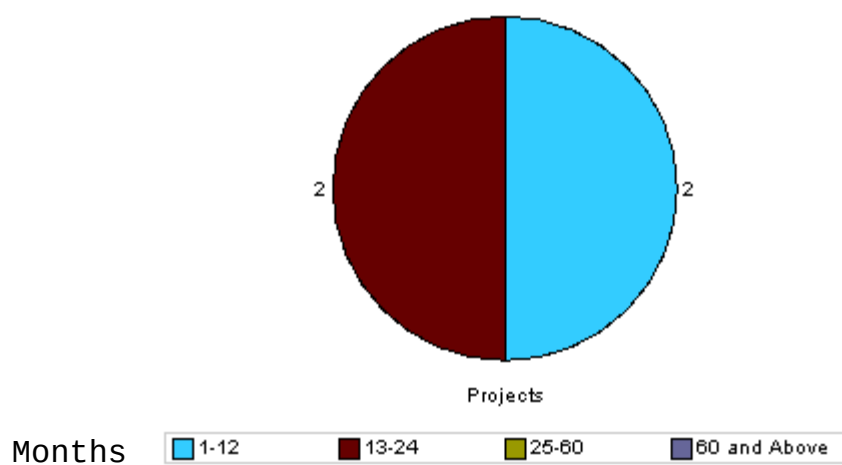


Trend and Graphical Analysis

Atomic Energy Sector

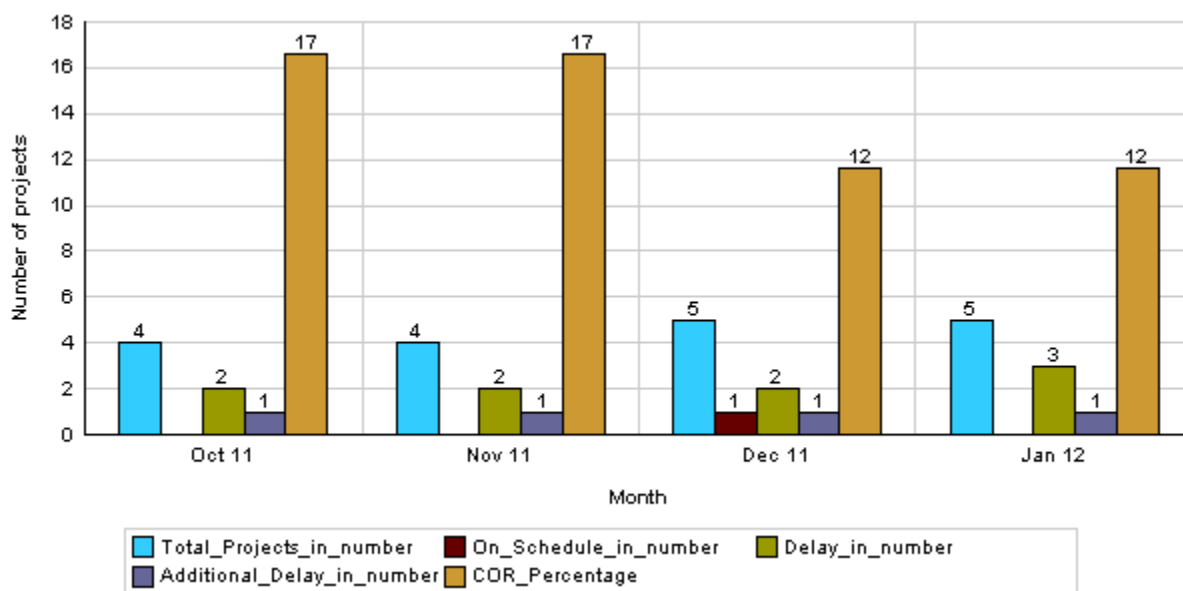

Atomic Energy Sector Sector Break-up of 3 Delayed projects in January 2012

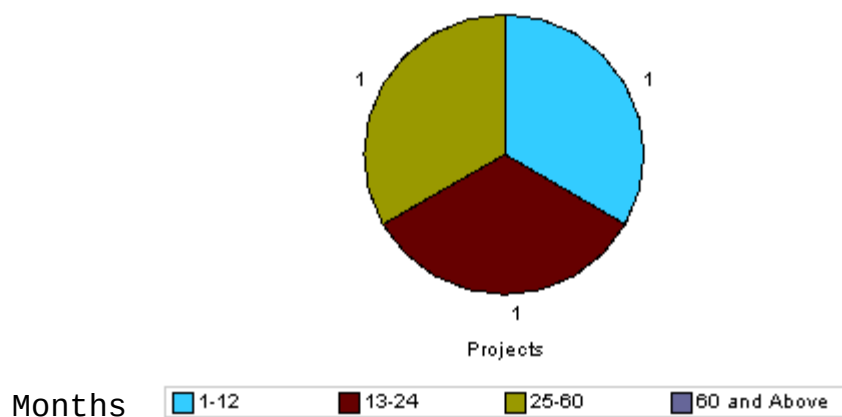

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	41,548.29	41,548.29	46,386.29
Civil Aviation	5	5,021.58	5,228.58	5,611.07
Coal	51	34,718.73	36,331.94	38,348.38
Fertilisers	6	5,317.41	5,317.41	5,317.41
Steel	16	65,244.82	71,120.10	71,412.36
Petrochemicals	1	5,460.61	8,920.00	8,920.00
Petroleum	69	149,804.77	163,049.42	158,021.15
Power	96	197,932.45	201,774.49	213,231.64
Railways	131	64,906.13	89,130.13	134,280.01
Road Transport & Highways	127	72,336.63	72,503.13	74,425.72
Shipping & Ports	25	18,221.36	18,653.17	19,237.40
Telecommunications	18	8,443.59	8,447.47	8,559.89
Urban Development	4	44,245.18	44,304.08	49,518.08
Water Resources	1	542.90	542.90	1,187.00
Grand total	555	713,744.45	766,871.11	834,456.40

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,341.00	- 05/2016	11/2016	6(R1)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	14,268.00	12/2008 -	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,410.82	09/2010 -	01/2012	16(O)	5/80
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	860.00	12/2016 -	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/0
Total			41,548.29 -	46,386.29	20,880.52				44/325
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,730.76	05/2011 -	03/2012	10(O)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	170.82	01/2011 -	12/2012	23(O)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	68.61	05/2012 -	08/2012	3(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,598.13	01/2011 -	02/2012	13(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	340.12	06/2013 -	06/2013	0(O)	0/0
Total			5,021.58 -	5,611.07	3,908.44				0/0
<u>Coal</u>									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	229.64	03/2013 09/2012	12/2013	15(R3)	6/22
12	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	198.59 -	198.59	91.57	03/2016 -	03/2016	0(O)	0/1
13	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 -	1,143.54	248.98	03/2014 -	03/2016	24(O)	2/2

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	72.00	-	03/2012	-	5/7
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66	341.63	105.51	03/2011	03/2013	12(R3)	0/2
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	99.91	-	03/2010	-	4/4
17	BARSINGSAR TPS (2 125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18	1,868.71	1,714.72	06/2009	01/2012	31(O)	26/26
18	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	102.10	-	03/2017	-	6/12
19	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.35	03/2014	03/2014	0(O)	1/2
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	141.38	03/2012	03/2015	36(O)	0/0
21	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
22	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	261.83	-	03/2014	-	0/4
23	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	33.66	03/2011	03/2014	24(R3)	1/2
24	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	1,142.56	03/2010	03/2014	48(O)	0/13
25	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,291.82	03/2010	03/2014	48(O)	0/15
26	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	59.22	-	03/2015	-	2/12
27	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	90.84	-	03/2013	-	5/7
28	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	1/1
29	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015	03/2015	0(O)	0/0
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013	03/2013	0(O)	3/83
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	1/5
32	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	71.05	12/2012	03/2015	27(O)	7/44
33	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	116.04	-	03/2013	-	6/11
34	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	31.59	03/2014	03/2014	0(O)	0/0
35	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/1
36	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	-	03/2018	03/2018	0(O)	0/0
37	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88	741.62	292.07	03/2010	03/2013	36(O)	2/2

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
38	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	87.85	03/2010	03/2012	24(O)	9/11
39	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	611.75	-	03/2013	-	0/8
40	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
41	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	18.16	07/2012	03/2016	24(R3)	1/2
42	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	204.10	-	03/2014	-	0/5
43	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	31.90	03/2012	03/2012	0(O)	8/34
44	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	1,230.27	-	04/2015	04/2015	0(O)	0/0
45	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	339.88	-	04/2014	04/2014	0(O)	0/0
46	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	6.57	-	12/2015	-	0/33
47	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	1.51	03/2012	03/2012	0(O)	0/1
48	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	61.24	03/2012	03/2014	24(R3)	0/2
49	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
50	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.70	-	10/2014	-	0/1
51	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98	210.98	31.39	03/2013	03/2013	0(O)	0/2
52	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08	153.82	19.96	03/2011	03/2014	36(O)	0/3
53	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	79.26	03/2012	03/2012	0(O)	21/27
54	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.21	03/2015	03/2015	0(O)	0/0
55	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	20.17	03/2015	03/2015	0(O)	4/31
56	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	282.99	03/2016	03/2016	0(O)	1/2
57	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	43.20	03/2012	03/2012	0(O)	11/42
58	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	34.28	-	03/2016	-	1/12
59	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78	2,453.57	2,361.58	06/2009	07/2012	37(O)	19/24

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
60	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,489.81	- -	02/2013	-	0/39
61	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	93.47	03/2012 03/2013	03/2014	12(R3)	0/2
	Total		34,718.73 -	38,348.38	12,730.25				153/589
Fertilisers									
62	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	335.32	01/2013 -	01/2013	0(O)	0/5
63	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	159.38	07/2011 -	04/2012	9(O)	0/0
64	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	147.84	07/2011 -	03/2012	8(O)	0/0
65	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,	01/2010	1,478.63 -	1,478.63	413.05	- -	01/2013	-	8/8
66	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	308.72	01/2013 -	01/2013	0(O)	0/5
67	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	488.75	214.81	- 04/2012	04/2012	0(R3)	7/22
	Total		5,317.41 -	5,317.41	1,579.12				15/40
Steel									
68	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	231.99	- 08/2010	03/2012	19(R3)	0/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	238.81	- 02/2011	04/2012	14(R3)	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
72	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 -	232.93	178.90	05/2011 -	02/2012	9(O)	1/1
73	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	460.00	176.28	- 05/2012	12/2012	7(R3)	1/2
74	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	314.31	- 12/2011	03/2012	3(R3)	15/21
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	59.11	- 10/2012	10/2012	0(R3)	3/4

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
76	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55 -	254.55	1.11	11/2013 -	11/2013	0(O)	0/0
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00 -	17,265.00	4,575.39	03/2013 -	06/2013	3(O)	17/20
78	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00 -	6,325.00	2,367.36	12/2011 -	03/2012	3(O)	10/11
79	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, Chhatisgarh	06/2009	2,875.00 -	2,875.00	526.87	12/2012 -	12/2012	0(O)	4/6
80	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	12,663.88	12/2011 -	03/2012	3(O)	13/14
81	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,130.48	10/2009 10/2012	10/2012	0(R3)	57/59
82	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Chhatisgarh	09/2008	11,812.00 11,812.00	11,812.00	6,321.78	03/2013 -	03/2013	0(O)	5/8
83	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL, Jharkhand)	10/2007	500.90 -	500.90	355.21	- -	02/2012	-	3/3
Total			65,244.82 -	71,412.36	37,141.48				131/153
<u>Petrochemicals</u>									
84	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	3,800.09	- 12/2013	12/2013	0(R3)	9/30
Total			5,460.61 -	8,920.00	3,800.09				9/30
<u>Petroleum</u>									
85	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	04/2013	10(O)	0/0
86	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	-	06/2012 -	06/2012	0(O)	0/0
87	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	-	04/2011 -	07/2012	15(O)	0/0
88	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	-	12/2011 -	01/2013	13(O)	0/0
89	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	523.86	03/2013 -	03/2013	0(O)	0/0
90	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	-	12/2014 -	12/2014	0(O)	0/0
91	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014	0(O)	0/0
92	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL, Multi State	11/2007	1,816.07 -	1,385.00	1,082.05	10/2010 12/2011	03/2012	3(R3)	0/1
93	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,	12/2009	540.92 -	460.70	171.29	- 07/2012	03/2013	8(R2)	0/16

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
94	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	226.70	03/2013 03/2013	03/2012	-12(R1)	0/0
95	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	41.18	- 02/2013	02/2013	0(R3)	29/42
96	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	85.97	- -	05/2012	-	21/36
97	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	686.69	04/2011 12/2011	03/2012	3(R3)	2/2
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.71	09/2011 -	12/2012	15(O)	0/0
99	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,335.28	05/2010 05/2012	05/2012	0(R3)	0/0
100	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	292.80	02/2011 08/2011	-	-	0/0
101	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	-	01/2014 -	01/2014	0(O)	0/0
102	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	188.90	09/2012 09/2012	06/2012	-3(R3)	0/0
103	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	861.79	-	05/2013 -	05/2013	0(O)	0/0
104	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
105	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	24.71	09/2012 -	09/2012	0(O)	0/0
106	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
107	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,	06/2009	4,543.43 4,508.38	2,300.00	1,539.07	03/2012 08/2012	08/2012	0(R3)	0/17
108	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	7.11	- -	-	-	0/0
109	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	2,393.39	08/2010 03/2012	12/2013	21(R3)	0/0
110	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	04/2013	13(R3)	0/0
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	465.50	07/2010 05/2012	07/2012	2(R3)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
112	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	- 12/2008	04/2013	52(R3)	0/0
113	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
114	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	715.36	09/2011 05/2012	05/2012	0(R3)	0/0
115	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	934.05	09/2011 03/2012	03/2012	0(R3)	0/0
116	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0
117	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	1.50	03/2013 -	03/2013	0(O)	0/0
118	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	05/2013	6(O)	0/0
119	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
120	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,763.29	- -	12/2011	-	0/116
121	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	59.50	01/2013 01/2013	01/2013	0(R3)	14/18
122	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	686.67	04/2010 -	03/2012	23(O)	0/0
123	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	370.68	- 04/2013	04/2013	0(R3)	0/167
124	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,450.37	04/2006 05/2011	05/2012	12(R3)	0/0
125	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,300.00	928.88	06/2012 06/2012	06/2012	0(R3)	6/8
126	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,413.90	03/2007 03/2017	03/2017	0(R3)	6/6
127	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	595.83	03/2007 03/2014	03/2014	0(R3)	3/3
128	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	258.24	03/2006 03/2013	03/2013	0(R3)	6/6
129	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
130	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30(O)	0/0
131	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
132	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 252.37	204.00	155.45	01/2012 -	05/2012	4(O)	3/8
133	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,	06/2009	2,915.00 -	2,915.00	551.11	- 12/2012	04/2013	4(R3)	0/21
134	KOCHI-KOOTANAD BANGLORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	186.75	03/2012 08/2012	03/2012	-5(R3)	1/4
135	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	149.79	03/2009 02/2012	01/2012	-1(R3)	0/0
136	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	7,726.62	01/2012 -	01/2012	0(O)	0/0
137	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,018.35	09/2012 -	09/2013	12(O)	0/0
138	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,808.47	05/2010 03/2013	03/2013	0(R3)	0/0
139	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	-	04/2015 -	04/2015	0(O)	0/0
140	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	290.05	04/2011 -	03/2012	11(O)	0/0
141	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	531.38	03/2011 05/2011	10/2012	17(R3)	0/0
142	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	417.93	03/2010 03/2012	03/2013	12(R1)	0/0
143	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	13,027.63	11/2012 -	06/2013	7(O)	57/100
144	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,400.00	544.09	09/2012 09/2012	09/2012	0(R3)	0/11
145	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	452.61	02/2014 -	02/2014	0(O)	0/0
146	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	512.67	07/2012 -	07/2012	0(O)	0/0
147	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	261.76	09/2010 -	09/2011	12(O)	10/60
148	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	804.61	09/2011 03/2012	03/2012	0(R3)	0/0
149	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	246.28	05/2010 04/2012	05/2012	1(R3)	0/0
150	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	145.16	08/2012 -	08/2012	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,	12/2009	463.32 -	330.47	185.36	- 03/2012	03/2012	0(R3)	0/20
152	WIND ENERGY - [N16000126]GAIL,	05/2011	616.00 -	616.00	84.75	- -	03/2012	-	0/0
153	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	20.54	12/2013 12/2013	12/2013	0(R3)	0/0
Total			149,804.77 -	158,021.15	63,543.52				158/662
Power									
154	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	4,495.30	08/2012 -	08/2012	0(O)	0/0
155	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	950.90	02/2012 -	06/2012	4(O)	0/0
156	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	406.30	05/2012 -	05/2012	0(O)	0/0
157	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	642.00	06/2012 -	06/2012	0(O)	0/0
158	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,433.00	08/2013 -	01/2014	5(O)	5/18
159	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,431.00	12/2009 -	12/2014	60(O)	45/46
160	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,735.00	06/2011 -	04/2014	34(O)	1/29
161	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	2,084.00	1,724.30	08/2010 04/2012	03/2012	-1(R3)	0/2
162	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.25	718.76	02/2011 10/2012	05/2012	-5(R3)	1/4
163	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	-	08/2014 -	08/2014	0(O)	0/0
164	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	-	09/2014 -	09/2014	0(O)	0/0
165	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.66	726.70	10/2009 -	03/2012	29(O)	20/20
166	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	139.80	06/2010 06/2010	01/2012	19(R3)	0/0
167	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	142.00	11/2012 -	11/2012	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
168	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	31.00	05/2014	05/2014	0(O)	0/0
169	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	214.60	08/2013	08/2013	0(O)	0/0
170	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	137.30	06/2012	03/2012	-3(O)	0/0
171	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	-	12/2013	11/2013	-1(O)	0/0
172	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	-	12/2013	12/2013	0(O)	0/0
173	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	16.90	10/2012	10/2012	0(O)	0/0
174	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	1,007.16	822.50	12/2007	-	-	0/18
175	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,715.85	05/2013	06/2016	0(R3)	2/22
176	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67	3,642.00	1,131.52	01/2016	11/2016	10(R3)	0/2
177	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	4,087.00	04/2009	03/2013	47(O)	0/9
178	KOTESHWAR HEP(THDC) - [180100184]THDC,Uttaranchal	04/2000	1,301.56	2,283.69	2,574.64	04/2005	03/2012	83(O)	10/11
179	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,779.29	1,775.08	09/2008	06/2012	45(O)	3/38
180	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	685.00	11/2011	12/2012	13(O)	6/34
181	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	203.10	10/2012	10/2012	0(O)	0/0
182	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	3,424.00	08/2012	03/2013	7(O)	6/16
183	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	704.32	08/2010	01/2013	0(R3)	0/3
184	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	3,596.20	08/2013	09/2014	13(O)	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	122.40	11/2011	06/2012	7(R3)	0/0
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	145.30	02/2012	12/2012	10(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	256.30	11/2011 -	12/2012	13(O)	0/0
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	167.10	08/2011 -	01/2012	5(O)	0/0
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	306.30	11/2011 -	12/2012	13(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	26.80	01/2013 -	01/2013	0(O)	0/0
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	105.90	07/2013 -	07/2013	0(O)	0/0
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	212.40	04/2013 -	04/2013	0(O)	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	24.70	08/2013 -	08/2013	0(O)	0/0
194	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	306.50	11/2012 -	11/2012	0(O)	0/0
195	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,666.39	10/2010 01/2013	01/2013	0(R3)	0/1
196	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,461.64	09/2009 07/2014	12/2014	5(R3)	1/20
197	PARE HYDRO ELECTRIC PROJECT (110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	280.37	08/2012 08/2013	08/2013	0(R3)	8/18
198	RAMPUR HEP (412 MW) - [N18000024]SJVN,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,493.95	01/2012 -	09/2013	20(O)	0/0
199	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,529.00	10/2012 -	03/2013	5(O)	6/16
200	SIMHADRI STTP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,354.00	05/2011 -	03/2012	10(O)	4/6
201	SIPAT STTP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	7,616.00	12/2009 -	03/2012	27(O)	50/60
202	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,312.61	09/2010 08/2014	12/2015	16(R3)	11/11
203	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	13.10	04/2013 -	04/2013	0(O)	0/0
204	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,790.10	08/2012 -	08/2012	0(O)	0/0
205	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	114.10	07/2011 -	03/2012	8(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
206	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJEC - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	-	08/2014 -	08/2014	0(O)	0/0
207	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	-	01/2015 -	01/2015	0(O)	0/0
208	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	-	08/2014 -	-	-	0/0
209	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	-	06/2014 -	06/2014	0(O)	0/0
210	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	129.50	04/2012 -	04/2012	0(O)	0/0
211	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	46.08	06/2012 -	06/2012	0(O)	0/0
212	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	583.30	08/2012 -	08/2012	0(O)	0/0
213	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,307.00	03/2013 -	06/2014	15(O)	2/13
214	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,072.97	09/2009 06/2013	06/2013	0(R3)	0/0
215	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.39	1,419.95	03/2007 09/2012	09/2012	0(R3)	25/25
216	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	285.17	07/2010 02/2016	02/2016	0(R3)	0/10
217	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	-	01/2013 -	01/2013	0(O)	0/0
218	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0
219	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	-	08/2014 -	08/2014	0(O)	0/0
220	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	307.83	07/2011 -	06/2012	11(O)	0/0
221	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,371.70	10/2012 -	10/2012	0(O)	0/0
222	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	219.00	07/2010 02/2012	01/2012	-1(R3)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
223	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
224	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25	2,569.25	154.30	03/2014	03/2014	0(O)	0/0
225	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL, Bihar	12/2005	3,779.46	4,282.59	3,648.00	09/2009	06/2012	33(O)	11/30
226	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL, Andhra Pradesh	12/2010	779.21	779.21	192.40	08/2013	08/2013	0(O)	0/0
227	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL, Himachal Pr.	07/2006	557.24	557.24	518.50	01/2010	06/2012	29(O)	0/22
228	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19	184.19	139.70	11/2011	09/2013	22(O)	0/0
229	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88	7,031.88	2,953.70	12/2012	12/2012	0(O)	0/0
230	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL, Gujarat	12/2011	552.44	552.44	-	02/2014	02/2014	0(O)	0/0
231	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya pradesh	08/2011	425.51	425.51	-	10/2013	10/2013	0(O)	0/0
232	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL, Maharashtra	07/2011	181.93	181.93	-	07/2013	07/2013	0(O)	0/0
233	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34	1,366.34	-	12/2013	12/2013	0(O)	0/0
234	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL, Jharkhand	10/2011	558.26	558.26	-	11/2013	11/2013	0(O)	0/0
235	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL, Orissa	09/2010	2,074.86	2,074.86	290.30	03/2013	03/2013	0(O)	0/0
236	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19	2,743.19	258.30	12/2013	12/2013	0(O)	0/0
237	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL, Multi State	03/2010	4,672.99	4,672.99	635.40	11/2012	11/2012	0(O)	0/0
238	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,	07/2009	421.01	623.44	95.88	-	07/2013	0(R3)	0/30
239	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, Mizoram	01/2011	913.63	913.63	295.47	01/2014	01/2014	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
240	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	547.40	12/2012	06/2013	6(O)	0/0
241	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	117.20	11/2013	11/2013	0(O)	0/0
242	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	34.50	01/2013	01/2013	0(O)	0/0
243	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29	1,794.00	1,653.86	11/2009 02/2013	06/2012	-8(R3)	0/4
244	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	2,741.00	10/2012	03/2013	5(O)	4/15
245	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	238.12	07/2014	09/2016	26(O)	4/7
246	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	348.90	02/2012	02/2012	0(O)	0/0
247	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	5,221.23	3,034.30	07/2010	06/2012	23(O)	20/20
248	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	387.90	09/2010	03/2013	30(O)	0/0
249	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	95.60	02/2012 02/2012	03/2012	1(R3)	0/0
Total			197,932.45	213,231.64	100,092.26				245/580
<u>Railways</u>									
250	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	1,141.75	294.54	03/2014	03/2014	0(O)	0/0
251	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
252	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	113.98	- -	-	-	0/0
253	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	317.98	03/2009 12/2008	12/2010	24(R1)	0/0
254	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00	435.87	359.10	- 03/2011	03/2011	0(R3)	0/0
255	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	485.95	06/1999 03/2011	03/2011	0(R3)	0/0
256	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	1,214.00	73.75	- -	-	-	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
257	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13	394.14	0.49	03/2013	03/2013	0(O)	0/0
258	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
259	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	1,173.79	414.38	03/2005	03/2016	87(R1)	0/0
260	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15	245.15	183.24	12/2010	-	-	0/0
261	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTMP,Maharashtra	03/1996	401.81	1,412.17	172.18	03/2004	-	-	0/0
262	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	2,393.49	3.80	04/2014	03/2014	-1(O)	0/0
263	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80	200.80	269.02	-	-	-	0/0
264	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya Pradesh	09/2007	687.20	687.20	-	03/2010	12/2012	33(O)	0/0
265	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	273.00	-	-	03/2011	24(R1)	0/0
266	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52	207.52	113.58	12/2012	12/2012	0(O)	0/0
267	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36	196.95	176.10	03/2011	-	-	0/0
268	Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat	04/2008	318.24	468.62	5.99	03/2012	03/2012	0(O)	0/0
269	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	597.49	-	02/2012	-	0/0
270	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44	1,103.47	825.08	12/2012	12/2012	0(O)	0/0
271	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09	1,417.97	944.25	-	03/2012	-	0/0
272	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya Pradesh	04/2005	383.79	585.93	180.24	-	12/2013	-	0/0
273	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00	415.73	222.85	-	03/2012	-	0/0
274	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67	1,302.12	608.97	-	-	-	0/0
275	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00	968.60	92.66	12/2012	-	-	0/0
276	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84	410.08	165.07	-	03/2013	-	0/0
277	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00	607.09	357.47	-	-	-	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
278	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	475.81	- -	-	-	0/0
279	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	72.61	12/2011 02/2012	02/2012	0(R3)	0/0
280	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	0(O)	0/0
281	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12(O)	0/0
282	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	147.46	- 06/2013	06/2013	0(R3)	0/0
283	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	546.82	03/1995 -	03/2012	204(O)	0/0
284	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	242.14	- 02/2011	03/2012	13(R3)	0/0
285	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	283.10	36.90	02/2006 -	12/2013	94(O)	0/0
286	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	863.23	464.52	- -	-	-	0/0
287	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	570.21	03/1998 -	-	-	0/0
288	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	303.09	- 05/2009	-	-	0/0
289	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O)	0/0
290	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	78.02	12/2011 11/2013	11/2013	0(R3)	0/0
291	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	172.64	- -	03/2015	-	0/0
292	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	205.80	- 09/2009	12/2011	27(R1)	0/0
293	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	197.98	- -	03/2012	-	0/0
294	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	483.14	- -	-	-	0/0
295	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	136.38	- -	-	-	0/0
296	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	153.40	03/2007 03/2007	03/2014	84(R1)	0/0
297	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.17	- -	-	-	0/0
298	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	1.91	03/2015 -	03/2015	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
299	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	823.54	06/2007 -	-	-	0/0
300	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	903.56	584.97	- 03/2012	03/2012	0(R3)	0/0
301	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	349.46	- 03/2012	12/2012	9(R3)	0/0
302	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	592.92	03/2011 03/2014	03/2016	24(R3)	0/0
303	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	54.36	03/2014 -	03/2014	0(O)	0/0
304	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	212.77	- 03/2012	03/2012	0(R3)	0/0
305	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,214.15	- -	02/2012	-	0/0
306	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	465.29	- -	-	-	1/1
307	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	666.27	- -	-	-	0/0
308	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	724.29	- 12/2010	03/2015	51(R3)	0/0
309	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	88.18	- -	-	-	0/0
310	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	200.91	- 03/2009	04/2013	49(R1)	0/0
311	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	184.37	- -	03/2012	-	0/0
312	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.23	- -	03/2015	-	0/0
313	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	385.73	- -	-	-	0/0
314	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,177.98	07/2005 -	-	-	0/0
315	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	81.36	- -	-	-	0/0
316	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	248.07	- 03/2012	12/2012	9(R3)	0/0
317	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
318	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	331.25	- -	03/2011	-	0/0
319	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	222.92	85.29	12/2012 -	03/2014	15(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
320	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
321	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	190.98	03/2002 -	03/2012	120(O)	0/0
322	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,027.93	2,903.63	03/2009 -	12/2013	57(O)	0/0
323	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	458.26	0.35	07/2008 -	-	-	0/0
324	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	143.65	- -	-	-	0/0
325	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	492.19	- 12/2011	03/2012	3(R3)	0/0
326	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
327	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	427.89	367.91	- 03/2012	03/2012	0(R3)	0/0
328	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	222.13	- -	-	-	0/0
329	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,228.31	- 06/2011	06/2011	0(R3)	1/1
330	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	0(R3)	0/0
331	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	99.52	- -	03/2012	-	0/0
332	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	411.22	432.27	- 03/2012	03/2012	0(R3)	0/0
333	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	840.32	527.52	02/2009 -	03/2012	37(O)	0/0
334	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	334.89	- 07/2012	07/2012	0(R3)	0/0
335	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	529.88	37.89	- -	-	-	0/0
336	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	91.54	- -	03/2014	-	0/0
337	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	1,076.88	12/2008 -	03/2014	63(O)	0/0
338	New BG line Rly line from Eklakhi-Balughat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	239.45	- -	03/2015	-	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
339	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
340	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	71.47	03/2016 -	03/2016	0(O)	0/0
341	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	4.01	03/2014 03/2016	03/2016	0(R3)	0/0
342	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	14.28	03/2016 -	03/2016	0(O)	0/0
343	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	8.17	03/2016 -	06/2016	3(O)	0/0
344	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	403.06	03/2008 06/2008	-	-	0/0
345	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	309.90	03/2009 12/2009	03/2011	15(R1)	0/0
346	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	208.25	02/2010 -	12/2015	70(O)	0/0
347	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,134.54	10/2007 12/2012	12/2012	0(R3)	0/0
348	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	820.32	538.98	- -	03/2012	-	0/0
349	Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	133.35	- 12/2010	-	-	0/0
350	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	719.39	- -	03/2013	-	0/0
351	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	186.79	12/2007 03/2010	12/2010	9(R1)	0/0
352	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	616.60	03/2009 12/2012	12/2012	0(R3)	0/0
353	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,308.03	04/2008 03/2014	12/2015	21(R3)	0/0
354	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	- 02/2009	04/2013	50(R1)	0/0
355	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	190.24	03/2011 -	03/2012	12(O)	0/0
356	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	215.73	- -	-	-	0/0
357	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	295.54	06/2004 -	12/2012	102(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
358	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	897.04	- -	03/2013	-	0/0
359	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	311.49	04/2003 03/2010	-	-	0/0
360	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	476.68	509.60	02/2010 02/2011	02/2011	0(R3)	0/0
361	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	176.58	03/1998 08/2005	08/2005	0(R1)	0/0
362	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	254.35	03/2013 -	12/2011	-15(O)	0/0
363	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	55.27	03/2012 -	03/2012	0(O)	0/0
364	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	207.45	03/2010 -	03/2012	24(O)	0/0
365	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.63	12/2015 -	12/2015	0(O)	0/0
366	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	246.88	- 03/2011	03/2011	0(R3)	0/0
367	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0
368	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	149.03	03/2014 -	03/2014	0(O)	0/0
369	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	89.02	- -	03/2013	-	0/0
370	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	723.27	387.66	06/2005 07/2011	06/2015	47(R3)	0/0
371	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	453.25	- 12/2009	02/2012	26(R1)	0/0
372	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	582.83	93.07	- -	-	-	0/0
373	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	33.51	- -	-	-	0/0
374	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	488.57	- -	-	-	0/0
375	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	3,176.10	3,225.00	12/2006 08/2010	-	-	0/0
376	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	37.18	03/2012 -	03/2012	0(O)	0/0
377	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	7,787.91	03/2001 -	12/2017	201(O)	0/0
378	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	819.40	114.15	03/2010 06/2014	06/2014	0(R3)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
379	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62	1,389.62	218.94	03/2014	03/2014	0(O)	0/0
380	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	152.01	-	-	-	0/0
	Total		64,906.13	134,280.01	56,595.71	03/2010			2/2
			-						
Road Transport & Highways									
381	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	154.70	05/2013	03/2014	10(O)	0/0
382	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	34.56	08/2014	08/2014	0(O)	0/0
383	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	893.30	06/2013	06/2013	0(O)	0/0
384	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	31.09	09/2013	09/2013	0(O)	0/0
385	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	409.10	08/2013	08/2013	0(O)	0/0
386	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	135.60	09/2007	06/2013	69(O)	0/0
387	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	06/2012	87(O)	0/0
388	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7(O)	0/0
389	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	261.00	11/2008	03/2012	40(O)	0/0
390	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	247.30	01/2009	03/2012	38(O)	0/0
391	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	616.00	02/2012	04/2012	2(O)	0/0
392	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	182.03	02/2004	07/2012	101(O)	0/0
393	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	126.40	-	06/2013	-	0/1
394	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	217.70	06/2008	12/2012	54(O)	0/0
395	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	182.68	06/2008	06/2012	48(O)	0/0
396	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	212.78	06/2005	12/2011	78(O)	0/0
397	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	165.80	04/2010	12/2012	32(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
398	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00	748.00	1,214.00	-	03/2013	-	0/3
399	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41(O)	0/0
400	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	468.00	03/2013	03/2013	0(O)	0/0
401	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	-	-	08/2013	-	0/1
402	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	565.90	05/2013	05/2013	0(O)	0/0
403	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	225.80	10/2011	03/2014	29(O)	0/0
404	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	580.00	10/2011	10/2012	12(O)	0/0
405	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	264.70	06/2008	03/2012	45(O)	0/0
406	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.20	10/2008	06/2012	44(O)	0/0
407	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	573.30	05/2010	12/2012	31(O)	0/0
408	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	256.10	07/2013	07/2013	0(O)	0/0
409	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
410	DEVIHALLI-HASSAN - [N24000152]NHAI,	12/2010	453.00	453.00	166.20	-	05/2013	-	0/1
411	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	204.70	06/2008	06/2012	48(O)	0/0
412	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	132.10	05/2008	06/2012	49(O)	0/0
413	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	173.60	09/2010	12/2012	27(O)	0/0
414	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	-	08/2013	08/2013	0(O)	0/0
415	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	531.90	01/2011	03/2012	14(O)	0/0
416	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	323.30	09/2008	03/2012	42(O)	0/0
417	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
418	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	437.80	11/2007	02/2012	51(O)	0/0
419	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	100.30	09/2008	06/2012	45(O)	0/0
420	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	259.07	02/2004	05/2012	99(O)	0/0
421	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	300.00	09/2007	06/2012	57(O)	0/0
422	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	483.10	08/2013	08/2013	0(O)	0/0
423	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	742.00	10/2009	06/2012	32(O)	0/0
424	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	192.90	04/2008	12/2012	56(O)	0/0
425	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	129.50	04/2008	12/2012	56(O)	0/0
426	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.60	10/2009	06/2012	32(O)	0/0
427	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	470.10	12/2009	06/2012	30(O)	0/0
428	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,098.00	09/2012	09/2012	0(O)	0/0
429	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,406.00	10/2011	06/2012	8(O)	0/0
430	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	475.60	03/2005	01/2012	82(O)	0/0
431	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	258.80	09/2007	06/2012	57(O)	0/0
432	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	244.10	02/2009	03/2013	49(O)	0/0
433	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	-	07/2009	04/2014	57(O)	0/0
434	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	-	09/2007	04/2014	79(O)	0/0
435	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	177.69	08/2004	02/2012	90(O)	0/0
436	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	167.83	08/2004 07/2010	03/2012	20(R3)	0/0
437	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	625.07	758.60	01/2013	01/2013	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
438	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	863.20	-	03/2013	-	0/2
439	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,266.00	10/2012	10/2012	0(O)	0/0
440	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	408.50	05/2012	05/2012	0(O)	0/0
441	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
442	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
443	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	07/2013	0(O)	0/0
444	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	477.10	09/2008	03/2012	42(O)	0/0
445	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	436.10	09/2009	02/2012	29(O)	0/0
446	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	838.20	12/2012	12/2012	0(O)	0/0
447	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	278.50	10/2008	09/2012	47(O)	0/0
448	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	285.60	10/2008	03/2012	41(O)	0/0
449	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	173.20	-	03/2013	-	0/1
450	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	892.10	05/2012	05/2012	0(O)	0/0
451	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	185.50	06/2010	10/2012	28(O)	0/0
452	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.40	09/2009	10/2012	37(O)	0/0
453	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	257.50	10/2008	04/2012	42(O)	0/0
454	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	65.49	11/2008	07/2013	56(O)	0/0
455	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	38.05	04/2009	07/2013	51(O)	0/0
456	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	2,047.00	11/2008	01/2014	62(O)	0/0
457	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	89.64	04/2009	03/2013	47(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	1,069.00	06/2012	06/2012	0(O)	0/0
459	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	1,110.00	06/2013	06/2013	0(O)	0/0
460	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
461	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	267.80	06/2008	06/2012	48(O)	0/0
462	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2012	42(O)	0/0
463	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	235.50	04/2008	12/2012	56(O)	0/0
464	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	188.90	06/2008	06/2012	48(O)	0/0
465	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	266.44	06/2008	06/2012	48(O)	0/0
466	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
467	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,	03/2005	441.00	441.00	946.80	-	02/2012	-	0/0
468	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	363.00	241.30	-	03/2012	9(R3)	0/0
469	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
470	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	5.59	09/2013	09/2013	0(O)	0/0
471	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	362.10	03/2008	03/2012	48(O)	0/0
472	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	575.20	10/2014	10/2014	0(O)	0/0
473	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	349.30	05/2010	05/2012	24(O)	0/0
474	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	157.40	05/2008	08/2012	51(O)	0/0
475	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	385.20	02/2013	02/2013	0(O)	0/0
476	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,141.00	07/2012	07/2012	0(O)	0/0
477	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	107.60	03/2013	03/2013	0(O)	0/0
478	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	3,196.00	11/2011	06/2012	7(O)	0/0
479	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.00	05/2012	05/2012	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
480	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
481	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	287.80	10/2008	12/2012	50(O)	0/0
482	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	235.00	10/2008	09/2012	47(O)	0/0
483	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	-	11/2013	11/2013	0(O)	0/0
484	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	217.30	10/2008	12/2012	50(O)	0/0
485	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	177.00	10/2008	05/2012	43(O)	0/0
486	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	03/2012	14(O)	0/0
487	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	805.39	209.80	03/2013	03/2013	0(O)	0/0
488	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	186.00	09/2007	06/2012	57(O)	0/0
489	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	177.40	07/2008	12/2012	53(O)	0/0
490	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
491	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
492	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
493	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.20	03/2008	05/2012	50(O)	0/0
494	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	91.40	04/2004	07/2012	99(O)	0/0
495	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,610.00	08/2011	03/2012	7(O)	0/0
496	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.50	06/2009	11/2012	41(O)	0/0
497	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	691.90	07/2010	03/2013	32(O)	0/0
498	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	358.40	11/2013	11/2013	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
499	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
500	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	374.00	33.88	05/2013	05/2013	0(O)	0/0
501	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	-	-	11/2012	-	0/2
502	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	383.00	12/2008	03/2012	39(O)	0/0
503	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09	166.30	184.60	03/2008	03/2012	48(O)	0/0
504	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27	193.10	155.10	03/2008	03/2012	48(O)	0/0
505	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	29.71	11/2012	11/2012	0(O)	0/0
506	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	759.90	08/2010	03/2012	19(O)	0/0
507	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88	953.88	100.80	07/2013	07/2013	0(O)	0/0
	Total		72,336.63	74,425.72	53,266.25				0/11
Shipping & Ports									
508	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	359.44	358.79	04/2011 06/2011	06/2012	12(R3)	0/0
509	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP., Maharashtra	08/2008	1,066.91	968.35	315.01	09/2012	09/2012	0(O)	0/0
510	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP., Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	987.34	03/2012	03/2012	0(O)	0/0
511	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP., Kerala	12/2010	241.50	241.50	157.81	09/2011	12/2011	3(O)	0/0
512	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP., Maharashtra	08/2010	612.72 627.64	627.64	193.11	12/2012	12/2012	0(O)	0/0
513	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST, Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	0(R3)	0/0
514	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP., Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	06/2012	5(R3)	0/0
515	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP., Maharashtra	10/2010	966.46	994.82	189.92	02/2014	02/2014	0(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
516	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	12/2013	0(O)	0/0
517	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
518	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	652.40	12/2010 -	09/2012	21(O)	0/0
519	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O)	0/0
520	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
521	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
522	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	-	-	0/0
523	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
524	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0
525	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	125.00	12/2005 01/2008	10/2011	45(R3)	0/0
526	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
527	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
528	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
529	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	336.25	04/2009 11/2009	02/2011	15(R3)	0/0
530	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.85	10/2008 -	-	-	0/0
531	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
532	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2(O)	0/0
	Total		18,221.36	19,237.40	4,969.25				0/0
<u>Telecommunications</u>									
533	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	155.71	01/2009	03/2012	38(O)	0/0
534	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
535	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007	08/2011	54(O)	0/0
536	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	21.80	10/2010 03/2012	07/2012	4(R3)	0/0
537	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
538	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
539	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
540	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	211.36	12/2008	03/2012	39(O)	0/0
541	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	-	03/2009	02/2011	23(O)	0/0
542	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	12/2011	23(O)	0/0
543	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) - [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	757.02	11/2010	03/2012	16(O)	0/0
544	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) - [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	362.62	08/2009	03/2012	31(O)	0/0
545	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
546	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	03/2012	36(O)	0/0
547	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0

Sector Wise Details

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
548	Implementation of FTTH, the state of the art access, upon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
549	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	161.31	12/2005	03/2012	75(O)	0/0
550	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15	158.72	76.55	06/2009	12/2011	30(O)	0/0
	Total		8,443.59	8,559.89	2,438.75				0/0
	Urban Development								
551	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	12/2013	24(O)	6/6
552	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
553	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	94.33	03/2016	03/2016	0(O)	0/0
554	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	-	09/2014	09/2014	0(O)	0/0
	Total		44,245.18	49,518.08	2,361.90				6/6
	Water Resources								
555	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			713,744.45	834,456.40	363,343.03				763/2398

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

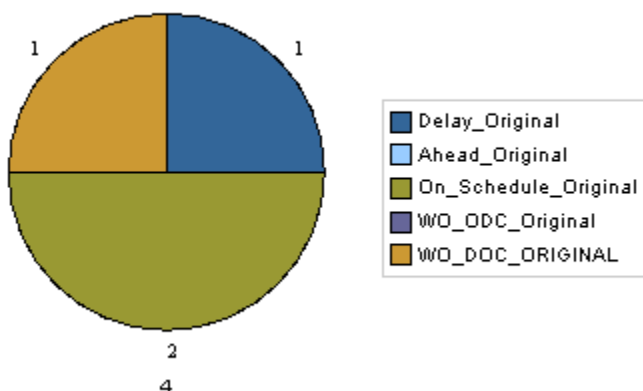

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till January, 2012 is Rs. 2361.9 crore, which is 4.8% of the revised cost of the projects.

Figures are in Rs. Crore

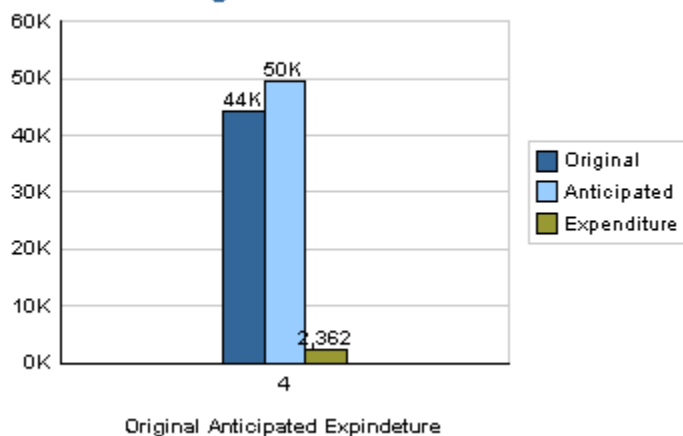

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **18**

Number of Projects Delayed **7**

Number of Projects Without Date Of Commissioning **11**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 18 projects, 7 projects are delayed .11 projects do not have fixed dates of commissioning.

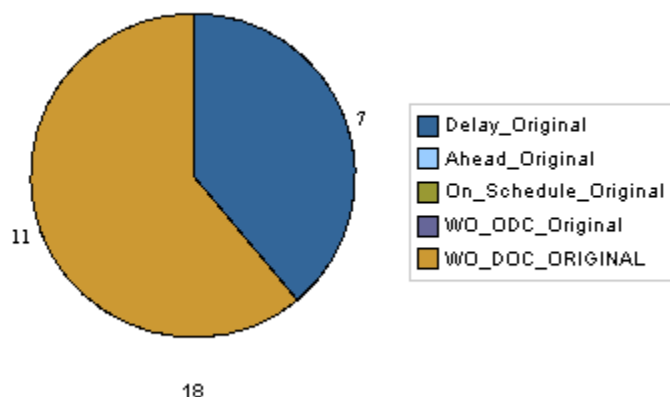

III. Investment Scenario

The Total Original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 8443.59 crore but this was subsequently revised to Rs. 8559.89 crore implying a cost overrun of 1.4%. The expenditure incurred on these projects till January, 2012 is Rs. 2438.75 crore, which is 28.5% of the revised cost of the projects.

Figures are in Rs. Crore

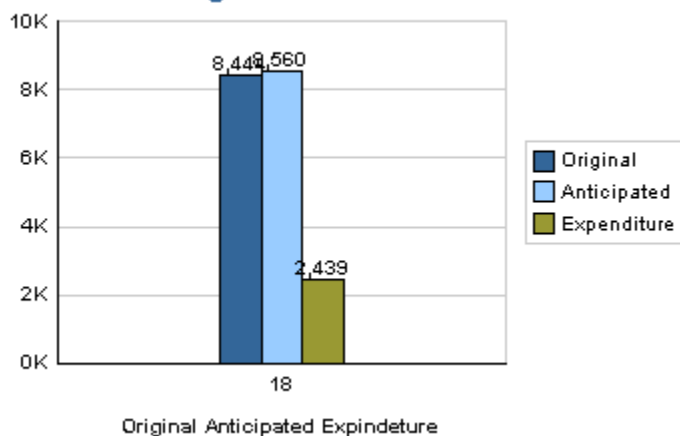

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	25
Number of Projects On Schedule	6
Number of Projects Delayed	10

Number of Projects Without Date Of Commissioning	9
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 6 projects are on schedule and 10 projects are delayed .9 projects do not have fixed dates of commissioning.

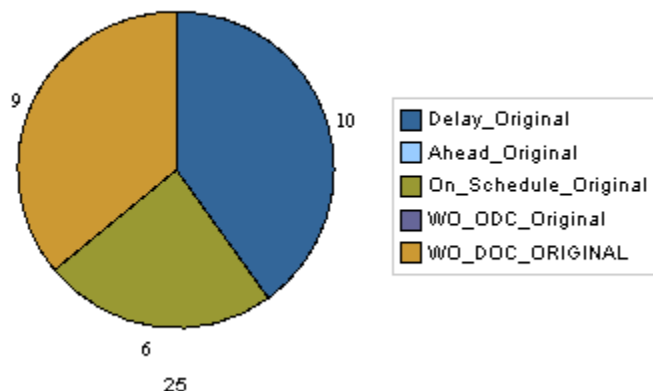

III. Investment Scenario

The Total Original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 18221.36 crore but this was subsequently revised to Rs. 19237.4 crore implying a cost overrun of 5.6%. The expenditure incurred on these projects till January, 2012 is Rs. 4969.25 crore, which is 25.8% of the revised cost of the projects.

Figures are in Rs. Crore

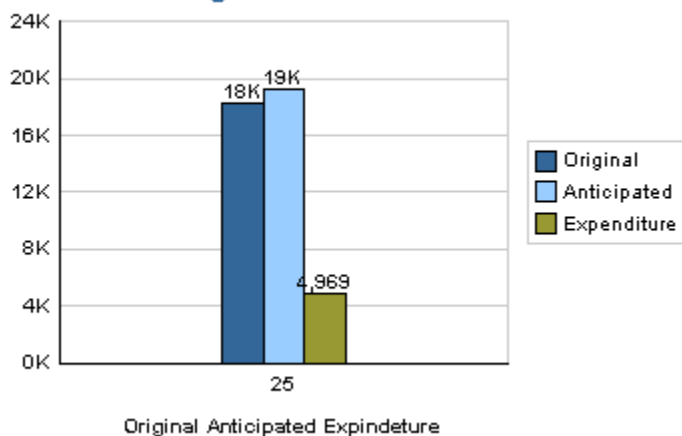

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	127
Number of Projects On Schedule	39
Number of Projects Delayed	78

Number of Projects Without Original Date of Commissioning	9
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 127 projects, 39 projects are on schedule and 78 projects are delayed .1 project do not have fixed dates of commissioning.9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

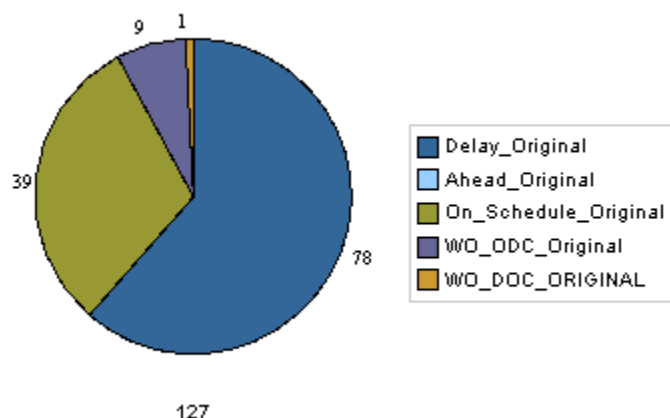

III. Investment Scenario

The Total Original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 72336.63 crore but this was subsequently revised to Rs. 74425.72 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till January, 2012 is Rs. 53266.25 crore, which is 71.6% of the revised cost of the projects.

Figures are in Rs. Crore

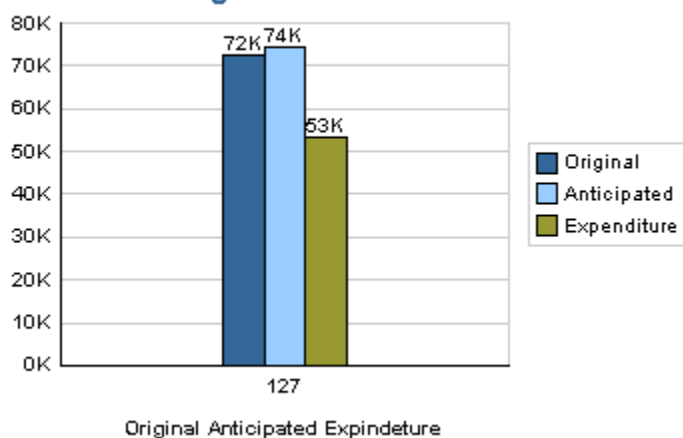

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	131
Number of Projects On Schedule	16
Number of Projects Delayed	27
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	33
Number of Projects Without Date Of Commissioning	54

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 131 projects, 1 project are ahead of schedule, 16 projects are on schedule and 27 projects are delayed .54 projects do not have fixed dates of commissioning.33 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

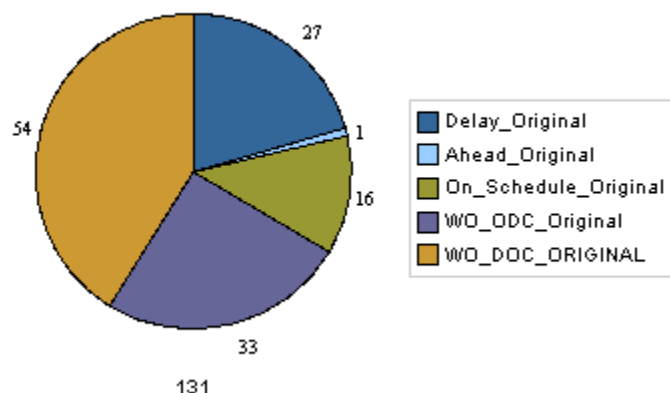

III. Investment Scenario

The Total Original cost of implementation of 131 projects when sanctioned, was of the order of Rs. 64906.13 crore but this was subsequently revised to Rs. 134280.01 crore implying a cost overrun of 106.9%. The expenditure incurred on these projects till January, 2012 is Rs. 56595.71 crore, which is 42.1% of the revised cost of the projects.

Figures are in Rs. Crore

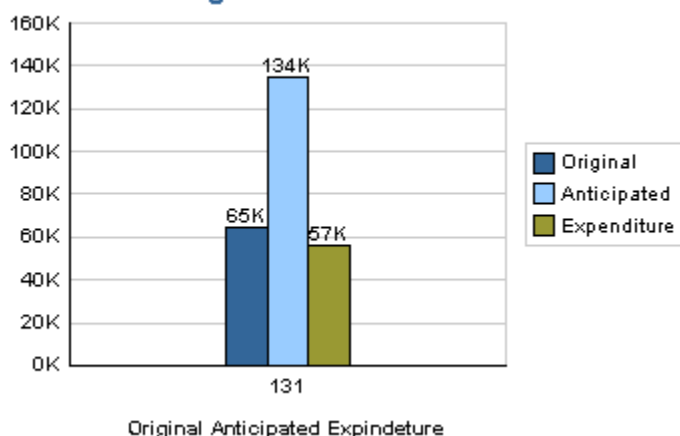

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	96
Number of Projects On Schedule	44
Number of Projects Delayed	47
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 96 projects, 2 projects are ahead of schedule, 44 projects are on schedule and 47 projects are delayed .2 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

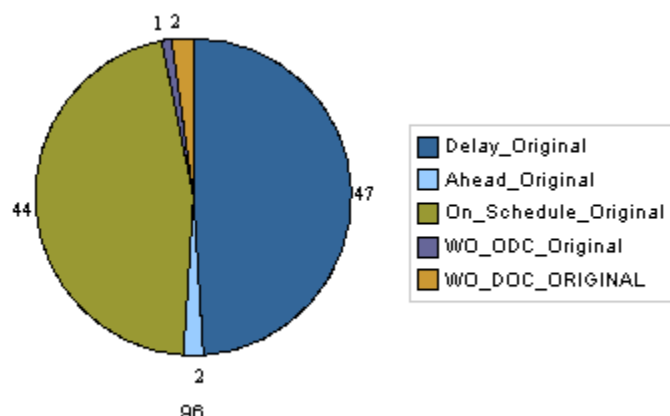

III. Investment Scenario

The Total Original cost of implementation of 96 projects when sanctioned, was of the order of Rs. 197932.45 crore but this was subsequently revised to Rs. 213231.64 crore implying a cost overrun of 7.7%. The expenditure incurred on these projects till January, 2012 is Rs. 100092.26 crore, which is 46.9% of the revised cost of the projects.

Figures are in Rs. Crore

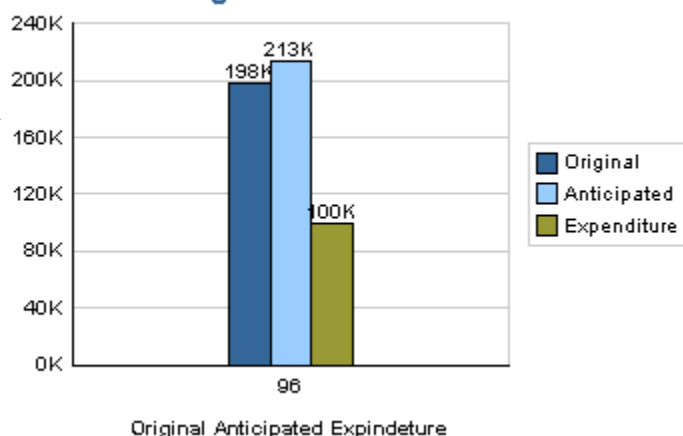

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	69
Number of Projects On Schedule	22
Number of Projects Delayed	31
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	8
Number of Projects Without Date Of Commissioning	6

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 69 projects, 2 projects are ahead of schedule, 22 projects are on schedule and 31 projects are delayed .6 projects do not have fixed dates of commissioning.8 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

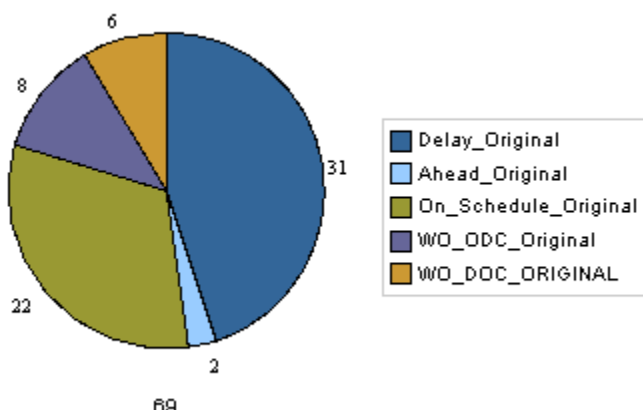

III. Investment Scenario

The Total Original cost of implementation of 69 projects when sanctioned, was of the order of Rs. 149804.77 crore but this was subsequently revised to Rs. 158021.15 crore implying a cost overrun of 5.5%. The expenditure incurred on these projects till January, 2012 is Rs. 63543.52 crore, which is 40.2% of the revised cost of the projects.

Figures are in Rs. Crore

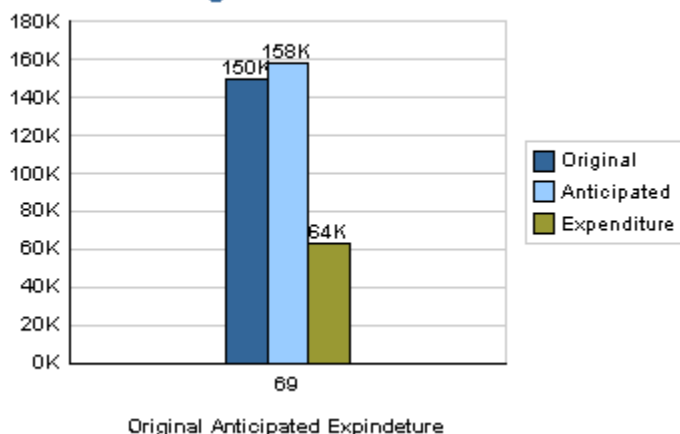

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	16
Number of Projects On Schedule	5
Number of Projects Delayed	5

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 5 projects are on schedule and 5 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

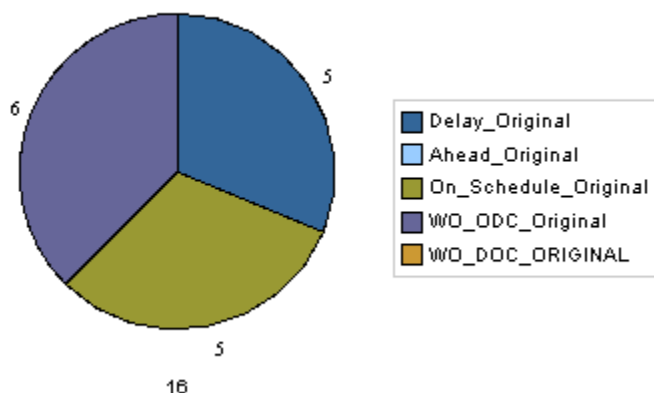

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 65244.82 crore but this was subsequently revised to Rs. 71412.36 crore implying a cost overrun of 9.5%. The expenditure incurred on these projects till January, 2012 is Rs. 37141.48 crore, which is 52% of the revised cost of the projects.

Figures are in Rs. Crore

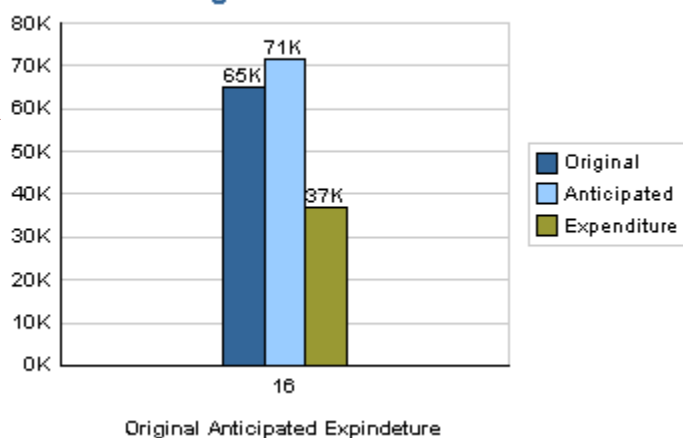

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Original Date of Commissioning	2
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 2 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

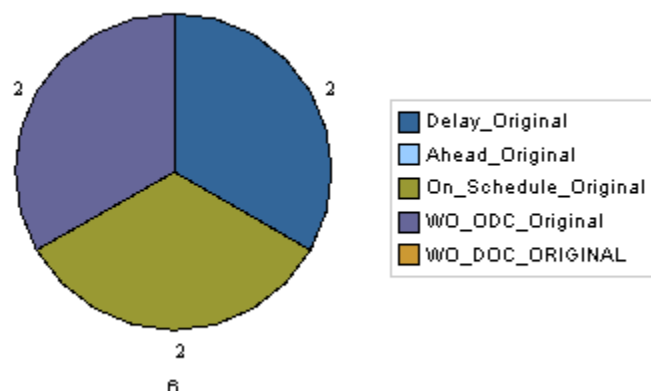

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till January, 2012 is Rs. 1579.12 crore, which is 29.7% of the revised cost of the projects.

Figures are in Rs. Crore

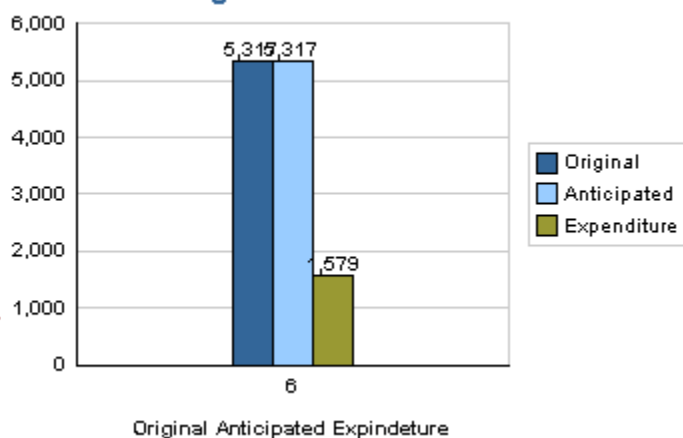

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	21
Number of Projects Delayed	17

Number of Projects Without Original Date of Commissioning	12
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 21 projects are on schedule and 17 projects are delayed .1 project do not have fixed dates of commissioning.12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

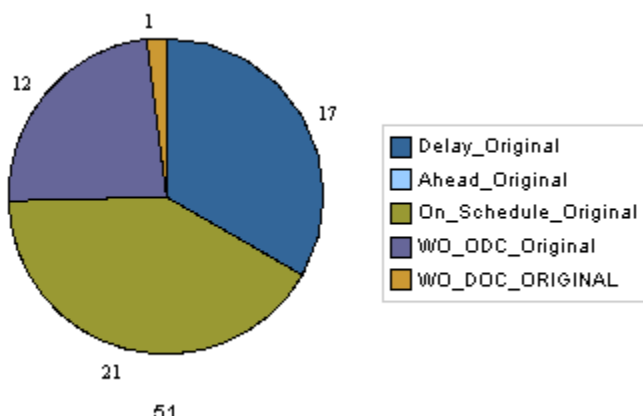

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 34718.73 crore but this was subsequently revised to Rs. 38348.38 crore implying a cost overrun of 10.5%. The expenditure incurred on these projects till January, 2012 is Rs. 12730.25 crore, which is 33.2% of the revised cost of the projects.

Figures are in Rs. Crore

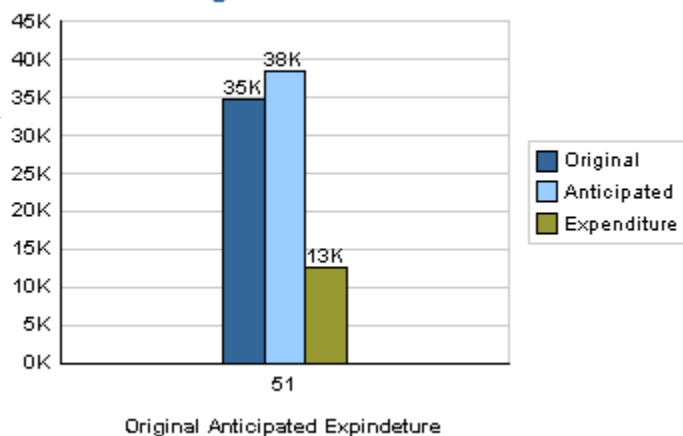

Sector wise current status of projects on theFlash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 4 projects are delayed.

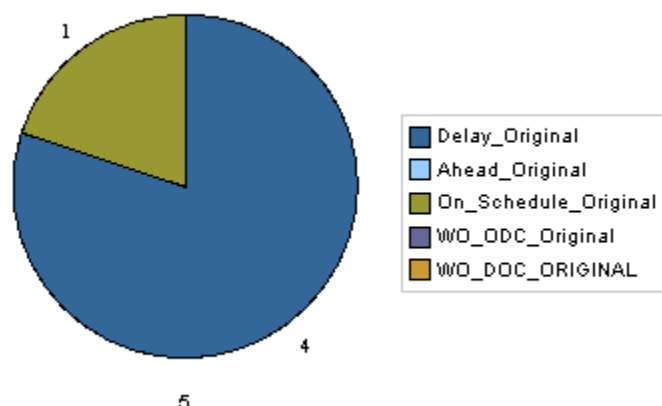

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till January, 2012 is Rs. 3908.44 crore, which is 69.7% of the revised cost of the projects.

Figures are in Rs. Crore

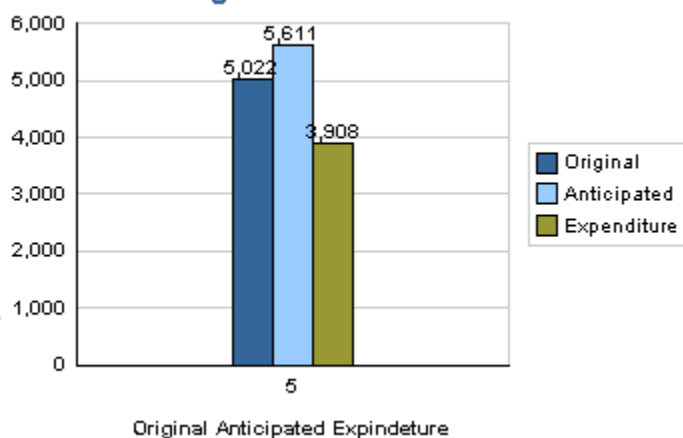

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	5
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

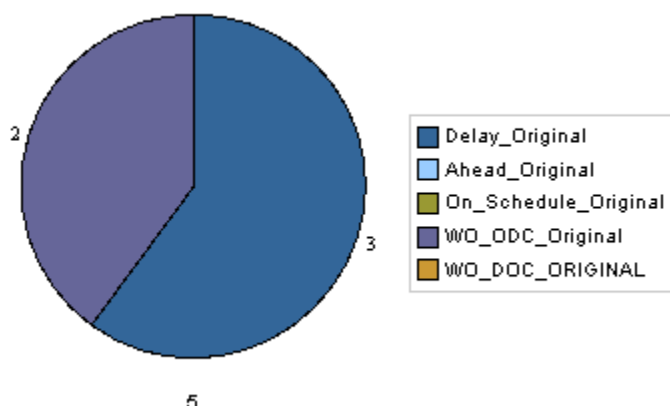

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 46386.29 crore implying a cost overrun of 11.6%. The expenditure incurred on these projects till January, 2012 is Rs. 20880.52 crore, which is 45% of the revised cost of the projects.

Figures are in Rs. Crore

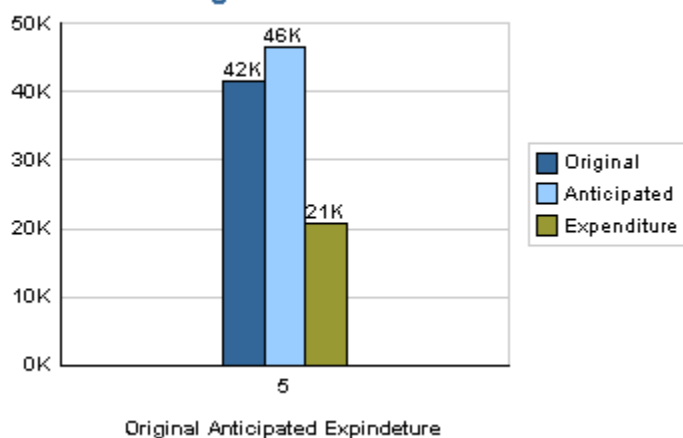

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	33	32855.21	39238.54	23105.33
2	Arunachal Pr.	4	9512.22	14153.62	7531.68
3	Assam	37	23895.78	35508.80	22346.93
4	Bihar	26	27578.91	32829.32	21877.17
5	Chhatisgarh	25	55916.77	59148.12	24461.79
6	Delhi	3	37985.00	37965.41	160.53
7	Goa	1	335.61	335.61	68.61
8	Gujarat	27	32375.09	32903.33	6497.71
9	Haryana	10	5795.35	7611.84	5771.68
10	Himachal Pr.	6	14761.20	17455.42	12951.78
11	J and K	10	14019.35	33604.41	12336.07
12	Jharkhandd	22	14396.48	15999.88	6810.64
13	Karnataka	25	30657.64	39102.46	17091.13
14	Kerala	7	6086.17	6775.22	1653.21
15	Madhya pradesh	24	17335.55	17581.76	6928.92
16	Maharashtra	51	68705.33	82228.73	42174.50
17	Manipur	1	727.56	3056.85	592.92
18	Mizoram	2	1532.97	3307.12	299.27
19	Multi State	97	125418.36	130674.34	47095.44
20	Nagaland	1	850.00	850.00	8.44
21	Orissa	26	42465.41	45636.40	16748.62
22	Punjab	7	4613.20	5598.23	3138.01
23	Rajasthan	15	25357.18	26106.33	8837.47
24	Sikkim	2	1648.94	3690.03	223.45
25	Tamil Nadu	35	52241.33	60526.40	35051.24
26	Tripura	3	1522.39	2053.23	535.58
27	Uttar Pradesh	24	17544.03	21597.83	10581.75
28	Uttaranchal	6	10025.65	11948.21	4901.48
29	West Bengal	25	37585.77	46968.96	23561.68
TOTAL		555	713744.45	834456.40	363343.03

LIST OF PROJECTS IN WHICH EXPENDITURE MORE THEN COST

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	14268.00
2	BARSINGSAR TPS (2 125MW) (NLC)	Coal	NLC	1114.18	1626.09	1714.72
3	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	HPCL	613.54	0.00	671.52
4	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1419.95
5	KOTESHWAR HEP(THDC)	Power	THDCL	1301.56	0.00	2574.64
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	NHPC	1061.38	0.00	1072.97
7	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	PGCIL	297.37	297.91	307.83
8	CHAMERA,STAGE-III (NHPC)	Power	NHPC	1405.63	0.00	1724.30
9	CHUTAK HYDRO-ELECTRIC PROJECT	Power	NHPC	621.26	0.00	718.76
10	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.01	0.00	704.32
11	GUNA-ETAWAH(NCR), NL	Railways	NCR	158.77	432.46	558.07
12	CALICUT-MANGALORE (DL) (SR)	Railways	SR	240.00	0.00	597.49
13	KARUR-SALEM(NL),SR	Railways	SR	155.55	229.88	666.27
14	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	ECR	491.19	1099.20	1177.98
15	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	248.44	576.27	825.08
16	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	724.29
17	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	RVNL	136.62	0.00	186.79
18	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	NEFR	733.00	0.00	1076.88
19	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	250.82
20	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	233.00	501.69	584.97
21	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	NEFR	1000.00	1500.00	2308.03
22	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	ER	184.00	254.07	492.19
23	KODERMA GIRIDH (NL), ECR	Railways	ECR	371.36	0.00	385.73
24	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	100.00	142.98	190.98
25	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	Railways	M RTP	3125.20	4174.40	4228.31
26	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	114.01	332.92	367.91
27	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	Railways	RVNL	200.80	0.00	269.02
28	RENIGUNTA-GUNTAKAL(RE)	Railways	RVNL	168.34	0.00	311.49
29	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	509.60
30	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	(NR)	409.00	625.30	823.54
31	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	465.29
32	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	NER	395.00	1062.36	1214.15
33	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	2903.63
34	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	222.85
35	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	0.00	359.10
36	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	485.95
37	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	407.78	538.98
38	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	SR	100.00	0.00	488.57
39	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	SWR	295.00	412.91	483.14

40	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	302.23	331.25
41	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	295.54
42	GONDIA-JABALPUR(GC),(SECR)	Railways	SECR	386.30	0.00	570.21
43	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	164.36	527.52
44	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	227.48
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	475.81
46	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	RVNL	240.00	0.00	309.90
47	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	NER	381.17	0.00	464.52
48	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	M RTP	907.69	3176.10	3225.00
49	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	228.09	242.14
50	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	349.46
51	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Road Transport & Highways	NHAI	412.78	0.00	437.80
52	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	NHAI	229.00	0.00	349.30
53	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	NHAI	441.00	0.00	946.80
54	Bijapur-Hungund Section	Road Transport & Highways	NHAI	748.00	0.00	1214.00
55	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	792.06	0.00	838.20
56	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	846.50
57	Pune-sholapur,pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1802.00
58	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	940.00	0.00	1141.00
59	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	835.00	0.00	1069.00
60	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	758.60
61	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	NHAI	295.00	0.00	759.90
62	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	247.30
63	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	Road Transport & Highways	NHAI	464.00	0.00	531.90
64	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.90

65	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	NHAI	572.30	0.00	580.00
66	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2610.00
67	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	NHAI	1673.70	0.00	2406.00
68	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	691.90
69	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	NHAI	280.00	0.00	581.50
70	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
71	Armur to kadloor yellareddy	Road Transport & Highways	NHAI	390.56	0.00	616.00
72	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	NHAI	229.91	0.00	235.00
73	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	217.30
74	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	177.00
75	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	NHAI	225.00	0.00	257.50
76	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	NHAI	355.06	0.00	436.10
77	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	278.50
78	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	3196.00
79	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	892.10
80	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	388.00	0.00	408.50
81	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	NHAI	168.00	0.00	457.30
82	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	NHAI	600.24	0.00	742.00
83	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	287.80

84	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	NHAI	227.00	0.00	383.00
85	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	264.70
86	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	573.30
87	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	362.10
88	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	477.10
89	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	261.00
90	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	266.44
91	NALBARI T BIJNI (AS-7)	Road Transport & Highways	NHAI	208.00	0.00	235.50
92	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	491.20
93	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	NHAI	200.00	0.00	204.70
94	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	NHAI	264.72	0.00	267.80
95	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	300.00
96	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	258.80
97	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	NHAI	273.00	0.00	475.60
98	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	285.60
99	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	186.00
100	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
101	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54	Road Transport & Highways	NHAI	167.64	0.00	2047.00
102	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	RVNL	245.67	298.17	336.25
103	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	RINL	230.00	0.00	238.81

List of project Without Original Date of Commissioning

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/0
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,341.00	- 05/2016	11/2016	6(R1)	0/70
Total			12,565.29	12,565.29	2,341.70				0/70
<u>Coal</u>									
3	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	72.00	- -	03/2012	-	5/7
4	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	2,489.81	- -	02/2013	-	0/39
5	KUSMUNDA EXPN.OC(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	611.75	- -	03/2013	-	0/8
6	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	116.04	- -	03/2013	-	6/11
7	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	90.84	- -	03/2013	-	5/7
8	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	261.83	- -	03/2014	-	0/4
9	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	204.10	- -	03/2014	-	0/5
10	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.70	- -	10/2014	-	1/1
11	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	59.22	- -	03/2015	-	2/12
12	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	6.57	- -	12/2015	-	0/33
13	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	34.28	- -	03/2016	-	1/12
14	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	102.10	- -	03/2017	-	6/12
Total			15,147.41	15,606.95	4,049.24				26/151
<u>Fertilisers</u>									
15	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	214.81	- 04/2012	04/2012	0(R3)	7/22
16	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	413.05	- -	01/2013	-	0/8

List of project Without Original Date of Commissioning

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			1,967.38	1,967.38	627.86				7/30
			-						
<u>Steel</u>									
17	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	355.21	-	02/2012	-	1/3
			-			-			
18	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	314.31	-	03/2012	3(R3)	18/21
			607.17			12/2011			
19	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	231.99	-	03/2012	19(R3)	1/1
			-			08/2010			
20	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	238.81	-	04/2012	14(R3)	2/3
			-			02/2011			
21	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	59.11	-	10/2012	0(R3)	3/4
			-			10/2012			
22	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	460.00	176.28	-	12/2012	7(R3)	1/2
			-			05/2012			
Total			1,874.79	2,478.33	1,375.71				26/34
			-						
<u>Petrochemicals</u>									
23	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61	8,920.00	3,800.09	-	12/2013	0(R3)	9/30
			8,920.00			12/2013			
Total			5,460.61	8,920.00	3,800.09				9/30
			-						
<u>Petroleum</u>									
24	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	330.47	185.36	-	03/2012	0(R3)	3/20
			-			03/2012			
25	WIND ENERGY - [N16000126]GAIL,Multi State	05/2011	616.00	616.00	84.75	-	03/2012	-	0/0
			-			-			
26	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	85.97	-	05/2012	-	21/36
			-			-			
27	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	41.18	-	02/2013	0(R3)	29/42
			-			02/2013			
28	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	460.70	171.29	-	03/2013	8(R2)	7/16
			-			07/2012			
29	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	-	04/2013	52(R3)	0/0
			-			12/2008			
30	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00	1,827.00	370.68	-	04/2013	0(R3)	0/167
			1,827.00			04/2013			
31	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	551.11	-	04/2013	4(R3)	0/21
			-			12/2012			
Total			9,230.89	9,624.66	4,011.25				60/302
			-						

List of project Without Original Date of Commissioning

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Power</u>									
32	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01 623.44	623.44	95.88	- 07/2013	07/2013	0(R3)	0/30
	Total		421.01 -	623.44	95.88				0/30
<u>Railways</u>									
33	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	597.49	- -	02/2012	-	0/0
34	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,214.15	- -	02/2012	-	0/0
35	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 762.33	762.33	453.25	- 12/2009	02/2012	26(R1)	0/0
36	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 407.78	820.32	538.98	- -	03/2012	-	0/0
37	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, Jharkhand	04/1995	184.00 254.07	675.00	492.19	- 12/2011	03/2012	3(R3)	0/0
38	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR, Karnataka	04/1996	157.00 262.82	262.82	212.77	- 03/2012	03/2012	0(R3)	0/0
39	MUZAFFARPUR-SITAMARHI(NL), ECR - [220100194]ECR, Bihar	04/1997	100.00 483.62	411.22	432.27	- 03/2012	03/2012	0(R3)	0/0
40	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	537.47	99.52	- -	03/2012	-	0/0
41	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 501.69	903.56	584.97	- 03/2012	03/2012	0(R3)	0/0
42	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, Multi State	04/1998	92.63 228.09	270.00	242.14	- 02/2011	03/2012	13(R3)	0/0
43	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, Orissa	04/1994	355.38 470.21	1,100.00	184.37	- -	03/2012	-	0/0
44	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, Bihar	04/1996	114.01 332.92	427.89	367.91	- 03/2012	03/2012	0(R3)	0/0
45	HARNOUT - SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 224.51	337.30	197.98	- -	03/2012	-	0/0
46	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	1,417.97	944.25	- -	03/2012	-	0/0
47	CONSTRUCTION OF NEW LINE FROM HARMATHITANAGAR/NAR - [N22000083]NEFR, Arunachal Pr.	09/1996	156.00 -	415.73	222.85	- -	03/2012	-	0/0
48	NANGALDAM-TALWARA(NL), NR - [220100188](NR), Multi State	03/1981	37.68 450.00	730.00	334.89	- 07/2012	07/2012	0(R3)	0/0

List of project Without Original Date of Commissioning

(Jan,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
49	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	349.46	- 03/2012	12/2012	9(R3)	0/0
50	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	248.07	- 03/2012	12/2012	9(R3)	0/0
51	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	165.07	- -	03/2013	-	0/0
52	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	719.39	- -	03/2013	-	0/0
53	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	897.04	- -	03/2013	-	0/0
54	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	89.02	- -	03/2013	-	0/0
55	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	- 02/2009	04/2013	50(R1)	0/0
56	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	200.91	- 03/2009	04/2013	49(R1)	0/0
57	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTPT,Tamil Nadu	04/2006	495.74 -	495.74	147.46	- 06/2013	06/2013	0(R3)	0/0
58	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	180.24	- -	12/2013	-	0/0
59	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	91.54	- -	03/2014	-	0/0
60	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	239.45	- -	03/2015	-	0/0
61	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	724.29	- 12/2010	03/2015	51(R3)	0/0
62	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	172.64	- -	03/2015	-	0/0
63	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.23	- -	03/2015	-	0/0
64	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	357.47	- 12/2012	-	-	0/0
65	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,302.12	1,302.12	608.97	- 06/2012	-	-	0/0
Total			8,258.03 -	21,995.91	12,312.23				0/0
<u>Road Transport & Highways</u>									
66	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00 -	441.00	946.80	- -	02/2012	-	0/0
67	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	363.00	241.30	- 06/2011	03/2012	9(R3)	0/0
68	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	- -	11/2012	-	0/2

List of project Without Original Date of Commissioning

(Jan,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
69	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	1,214.00	-	03/2013	-	0/3
70	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	863.20	-	03/2013	-	0/2
71	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	-	03/2013	-	0/1
72	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	166.20	-	05/2013	-	0/1
73	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	126.40	-	06/2013	-	0/1
74	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	-	-	08/2013	-	0/1
Total			5,454.50	5,621.00	3,731.10				0/11
Grand Total			60,379.91	79,402.96	32,345.06				128/658

List of project Without Date of Commissioning

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning	
				Original / Revised	Anticipated
1	2	3	4	7	8
<u>Coal</u>					
1	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	-	03/2010
			-	-	
	Total		172.08		
			-		
<u>Petroleum</u>					
2	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	12/2010	06/2011
			-	-	
3	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	09/2009	08/2011
			1,646.39	-	
4	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	09/2010	09/2011
			-	-	
5	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	-	12/2011
			-	-	
6	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	02/2011	-
			299.00	08/2011	
7	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
			-	-	
	Total		6,773.54		
			-		
<u>Power</u>					
8	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	08/2014	-
			-	-	
9	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	12/2007	-
			1,007.16	12/2009	
	Total		893.78		
			-		
<u>Railways</u>					
10	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	03/1998	08/2005
			604.04	08/2005	
11	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	12/2007	12/2010
			-	03/2010	
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73	03/2009	12/2010
			399.73	12/2008	
13	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38	02/2010	02/2011
			330.23	02/2011	
14	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90	06/1999	03/2011
			284.27	03/2011	
15	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94	-	03/2011
			302.23	-	
16	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92	-	03/2011
			258.60	03/2011	

List of project Without Date of Commissioning

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
17	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52	-	03/2011
18	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00	03/2009 12/2009	03/2011
19	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00	- 03/2011	03/2011
20	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP, Maharashtra	04/2003	3,125.20 4,174.40	- 06/2011	06/2011
21	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
22	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64	- 09/2009	12/2011
23	Ramanagaram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	03/2013 -	12/2011
24	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	- 03/2010	-
25	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD) - [220100149]RVNL, Chhatisgarh	04/1995	304.00	12/2012 -	-
26	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	- -	-
27	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 412.91	- -	-
28	GONDIA-JABALPUR(GC), (SECR) - [220100186]SECR, Multi State	02/1997	386.30	03/1998 -	-
29	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 229.88	- -	-
30	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00	- -	-
31	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	-
32	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 1,099.20	07/2005 -	-
33	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00	- -	-
34	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	-
35	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, Bihar	04/1997	78.23 162.87	- -	-
36	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00 625.30	06/2007 -	-
37	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34	04/2003 03/2010	-
38	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00	- -	-
39	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00	- -	-
40	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00	- -	-

List of project Without Date of Commissioning

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
41	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
42	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
43	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-
44	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
45	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
46	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-
48	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	-
49	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-
50	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
51	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-
52	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
53	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	-
54	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
55	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	-
56	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-
57	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	- -	-
58	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	-
59	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	- -	-
60	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-
61	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-
62	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	12/2010 03/2011	-
63	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	- 12/2010	-

List of project Without Date of Commissioning

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
	Total		18,819.16		
			-		
	<u>Road Transport & Highways</u>				
64	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	06/2005	12/2011
			-	-	
	Total		230.00		
			-		
	<u>Shipping & Ports</u>				
65	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	04/2009	02/2011
			298.17	11/2009	
66	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	06/2006	09/2011
			-	09/2011	
67	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00	12/2005	10/2011
			165.00	01/2008	
68	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50	09/2011	12/2011
			-	-	
69	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	10/2008	-
			-	-	
70	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	12/2007	-
			-	01/2009	
71	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	08/2010	-
			-	-	
72	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	08/2010	-
			-	-	
73	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	10/2008	-
			-	-	
	Total		4,999.79		
			-		
	<u>Telecommunications</u>				
74	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	03/2009	02/2011
			-	-	
75	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	03/2010	10/2010
			-	-	
76	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	10/2009	03/2011
			-	-	
77	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	02/2007	08/2011
			229.41	-	
78	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	02/2007	08/2011
			-	-	
79	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	09/2011	09/2011
			-	-	
80	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15	06/2009	12/2011
			158.72	-	

List of project Without Date of Commissioning

(Jan,2012)

S.No Project		Date of Approval	Original / Revised Cost	Date of Commissioning	
				Original / Revised	Anticipated
1	2	3	4	7	8
81	GSM equipment of 1500000Lines (2G) 264700lines 3(G - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	01/2010 -	12/2011
82	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
83	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
84	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
	Total		4,986.01 -		
<u>Urban Development</u>					
85	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Grand Total			36,988.54		

LIST OH AHEAD PROJECTS as on 31-01-2012

SN	PROJECT	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
1	BHAIRABI SAIRONG, NL, NEFR	04/2008	04/2014	N.A.	03/2014	619.34	2393.49
2	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS	02/2010	06/2012	N.A.	03/2012	215.86	215.86
3	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA	02/2009	03/2013	03/2013	03/2012	250.00	250.00
4	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	08/2011	12/2013	N.A.	11/2013	1391.97	1391.97
5	Construction of tanks and blending facility at vadinar	02/2009	09/2012	09/2012	06/2012	267.00	267.00

LIST OF ON SCHEDULED PROJECTS as on 31-01-2012

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
1	GAGAN PROJECT	Civil Aviation	AAI	09/2008	06/2013	N.A.	06/2013	626.00	626.00
2	Muraidih UG Turn-key Project	Coal	BCCL	02/2011	04/2014	N.A.	04/2014	339.88	339.88
3	Moonidih XV Seam UG	Coal	BCCL	08/2011	04/2015	N.A.	04/2015	1230.27	1230.27
4	Purnadih OCP	Coal	CCL	07/2008	03/2013	N.A.	03/2013	210.98	210.98
5	KARMA OCP	Coal	CCL	06/2009	03/2014	N.A.	03/2014	162.46	162.46
6	Rajrappa RCE OCP	Coal	CCL	12/2009	03/2016	N.A.	03/2016	510.85	510.85
7	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	Coal	NCL	10/2007	03/2012	N.A.	03/2012	259.40	259.40
8	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	Coal	NCL	06/2011	03/2018	N.A.	03/2018	1131.28	1131.28
9	BINA EXTN. PROJ(6.0 Mtpa)	Coal	NCL	11/2006	03/2014	N.A.	03/2014	168.97	168.97
10	RANAGUNDAM OC-II EXTENSION	Coal	SCCL	12/2009	03/2012	N.A.	03/2012	418.97	418.97
11	JALAGAM VENGALA RAO OCP	Coal	SCCL	07/2011	03/2015	N.A.	03/2015	447.06	447.06
12	RCE OF INDARAM OCP(1.20 MTPA)	Coal	SCCL	07/2011	03/2015	N.A.	03/2015	162.76	162.76
13	RKP OCP PHASE-I	Coal	SCCL	03/2010	03/2015	N.A.	03/2015	209.78	209.78
14	Kistaram OCP	Coal	SCCL	11/2010	03/2015	N.A.	03/2015	242.29	242.29
15	MANUGURU OC-II EXTENSION PHASE-II	Coal	SCCL	03/2010	03/2012	N.A.	03/2012	181.19	181.19
16	JALLARAM SHAFT PROJECT	Coal	SCCL	03/2013	03/2013	N.A.	03/2013	467.78	467.78
17	SHANTIKHANI LONGWALL PROJ-SCCL	Coal	SCCL	10/2006	03/2012	N.A.	03/2012	249.03	249.03
18	JAGANNATHPUR OCP(3.00 MTY)	Coal	SECL	09/2008	03/2015	N.A.	03/2015	152.43	152.43
19	PELMA OCP(10.00MTY)	Coal	SECL	07/2008	03/2015	N.A.	03/2015	448.32	448.32
20	AMLAI OC EXPANSION SECTOR 1.50 MTY	Coal	SECL	11/2009	03/2016	N.A.	03/2016	198.59	198.59
21	KARTALI (EAST) OCP(2.50 MTY)	Coal	SECL	07/2008	03/2014	N.A.	03/2014	178.44	178.44
22	Batura OCP (2.0 MTY)	Coal	SECL	09/2008	03/2015	N.A.	03/2015	203.82	203.82
23	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	Fertilisers	NFL	01/2010	01/2013	N.A.	01/2013	1294.19	1294.19
24	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	Fertilisers	NFL	01/2010	01/2013	N.A.	01/2013	1292.84	1292.84
25	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	Petroleum	GAIL	08/2010	02/2014	N.A.	02/2014	8140.00	8140.00
26	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I	Petroleum	GAIL	06/2009	03/2012	08/2012	03/2012	348.00	261.00
27	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	Petroleum	IOCL	07/2010	01/2013	01/2013	01/2013	1000.00	1000.00
28	PARADIP-RAIPUR-SAMBALPUR- RANCHI PIPELINE	Petroleum	IOCL	08/2009	09/2012	09/2012	09/2012	1793.00	1400.00
29	Integrated crude Oil handling facilities at Paradip(2nd SPM)	Petroleum	IOCL	12/2009	06/2012	06/2012	06/2012	1492.33	1300.00

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
30	MRPL Phase-III Expansion	Petroleum	Mangalore Refin	08/2008	01/2012	N.A.	01/2012	12412.00	12160.26
31	Polypropylene unit	Petroleum	Mangalore Refin	05/2009	07/2012	N.A.	07/2012	1803.78	1803.78
32	Wax Project	Petroleum	NRL	06/2010	12/2013	12/2013	12/2013	576.60	576.60
33	ASSAM RENEWAL PROJECT FOR GROUP A	Petroleum	ONGC	03/2009	03/2013	N.A.	03/2013	2465.15	2378.86
34	Development of WO-16 Cluster Fields	Petroleum	ONGC	06/2010	01/2014	N.A.	01/2014	2523.00	2523.00
35	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	Petroleum	ONGC	03/2011	05/2013	N.A.	05/2013	861.79	861.79
36	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	Petroleum	ONGC	06/2010	01/2014	N.A.	01/2014	202.94	202.94
37	Construction of 6 ETps	Petroleum	ONGC	03/2009	09/2012	N.A.	09/2012	302.26	302.26
38	Mehesana Redevelopment	Petroleum	ONGC	11/2010	04/2015	N.A.	04/2015	3823.00	3823.00
39	Construction of 23 Immediate Supply Vessels (ISV)	Petroleum	ONGC	11/2010	08/2013	N.A.	08/2013	331.20	331.20
40	Ankleswar Redevelopment	Petroleum	ONGC	11/2010	12/2014	N.A.	12/2014	2189.63	2189.63
41	Development of BHE and BH-35 Area.	Petroleum	ONGC	08/2010	03/2013	N.A.	03/2013	372.11	372.11
42	Development of Cluster-7 Fields	Petroleum	ONGC	03/2010	03/2013	N.A.	03/2013	3241.03	3241.03
43	Construction of one Multipurpose Support Vessel (MSV)	Petroleum	ONGC	01/2010	03/2013	N.A.	03/2013	723.64	723.64
44	Ahmedabad Redevelopment	Petroleum	ONGC	11/2010	12/2014	N.A.	12/2014	1916.10	1916.10
45	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura	Petroleum	ONGC	07/2008	08/2012	N.A.	08/2012	288.04	288.04
46	ADDITIONAL DEV. OF D-1 FIELD	Petroleum	ONGC	01/2010	06/2012	N.A.	06/2012	2163.64	2163.64
47	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	Power	NEEPCO	01/2011	01/2014	N.A.	01/2014	913.63	913.63
48	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHON RBC	Power	PGCIL	08/2008	08/2012	N.A.	08/2012	7075.33	7075.33
49	WESTERN REGION STRENGTHENING SCHEME-X	Power	PGCIL	02/2009	02/2012	N.A.	02/2012	664.96	664.96
50	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI	Power	PGCIL	08/2010	04/2013	N.A.	04/2013	1677.57	1677.57
51	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD	Power	PGCIL	01/2012	01/2013	N.A.	01/2013	259.28	259.28
52	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	Power	PGCIL	01/2012	01/2015	N.A.	01/2015	1422.85	1422.85
53	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	1746.65	1746.65
54	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	Power	PGCIL	12/2011	02/2014	N.A.	02/2014	552.44	552.44
55	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED	Power	PGCIL	08/2011	10/2013	N.A.	10/2013	425.51	425.51

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
56	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	Power	PGCIL	09/2011	12/2013	N.A.	12/2013	1366.34	1366.34
57	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power Madras Limited LT	Power	PGCIL	09/2011	09/2014	N.A.	09/2014	1940.13	1940.13
58	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A	Power	PGCIL	10/2011	11/2013	N.A.	11/2013	558.26	558.26
59	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH	Power	PGCIL	07/2011	07/2013	N.A.	07/2013	181.93	181.93
60	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	2422.66	2422.66
61	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR TPS	Power	PGCIL	08/2010	04/2013	N.A.	04/2013	170.36	170.36
62	System Strengthening -XII of SR	Power	PGCIL	02/2010	06/2012	N.A.	06/2012	232.34	232.34
63	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A	Power	PGCIL	05/2010	01/2013	N.A.	01/2013	250.03	250.03
64	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL)	Power	PGCIL	08/2011	08/2014	N.A.	08/2014	1637.34	1637.34
65	SYTEM STRENGTHENING XIII OF SR GRID	Power	PGCIL	10/2011	06/2014	N.A.	06/2014	487.49	487.49
66	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT KALA IN UT DNH	Power	PGCIL	07/2011	07/2013	N.A.	07/2013	181.93	181.93
67	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	Power	PGCIL	08/2011	12/2013	N.A.	12/2013	1391.97	1391.97
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	Power	PGCIL	07/2010	07/2013	N.A.	07/2013	752.64	752.64
69	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM PART A	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	779.21	779.21
70	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN ORISSA-B	Power	PGCIL	12/2010	12/2013	N.A.	12/2013	2743.19	2743.19
71	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-III Gen Project	Power	PGCIL	03/2010	11/2012	N.A.	11/2012	4672.99	4672.99
72	MAUDA TRANSMISSION SYSTEM	Power	PGCIL	02/2010	10/2012	N.A.	10/2012	469.38	469.38
73	System Strengthening in NR for SASAN & MUNDRA (UMPP)	Power	PGCIL	12/2009	08/2012	N.A.	08/2012	1216.83	1216.83
74	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-III	Power	PGCIL	11/2009	05/2012	N.A.	05/2012	1075.12	1075.12

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
75	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-PART A	Power	PGCIL	09/2010	03/2013	N.A.	03/2013	2074.86	2074.86
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX	Power	PGCIL	10/2010	01/2013	N.A.	01/2013	182.68	182.68
77	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	1719.52	1719.52
78	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND BANGLADESH -INDIAN PORTION	Power	PGCIL	10/2010	10/2012	N.A.	10/2012	160.32	160.32
79	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM BHU	Power	PGCIL	04/2010	01/2015	N.A.	01/2015	4404.57	4404.57
80	System Strengthening -X of SR	Power	PGCIL	12/2009	04/2012	N.A.	04/2012	276.61	276.61
81	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B	Power	PGCIL	03/2011	11/2013	N.A.	11/2013	1585.12	1585.12
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	209.78	209.78
83	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C	Power	PGCIL	03/2011	03/2014	N.A.	03/2014	2569.25	2569.25
84	EASTERN REGION TRANSMISSION SYSTEM-III	Power	PGCIL	07/2010	11/2012	N.A.	11/2012	1272.80	1272.80
85	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	Power	PGCIL	05/2011	05/2014	N.A.	05/2014	1961.87	1961.87
86	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	Power	PGCIL	03/2010	11/2012	N.A.	11/2012	965.58	965.58
87	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID PART-II	Power	PGCIL	07/2009	06/2012	N.A.	06/2012	1736.36	1736.36
88	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC	Power	PGCIL	08/2008	08/2012	N.A.	08/2012	2360.95	2360.95
89	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	Power	PGCIL	10/2008	10/2012	N.A.	10/2012	4824.12	4824.12
90	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT	Power	PGCIL	12/2008	12/2012	N.A.	12/2012	7031.88	7031.88
91	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	07/1998	12/2012	N.A.	12/2012	248.44	1103.47
92	Tinpahar - Sahibganj (ER)	Railways	ER	04/2008	03/2012	N.A.	03/2012	167.73	167.73
93	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER)	Railways	ER	04/1999	12/2012	N.A.	12/2012	207.52	207.52
94	New Line from Dimapur to Zubza(Kohima) national project (NEFR)	Railways	NEFR	04/2006	03/2015	N.A.	03/2015	850.00	850.00
95	AGARTALA SABROOM, NL, NEFR	Railways	NEFR	04/2008	03/2014	N.A.	03/2014	813.34	1141.75
96	SEVOK RANGPO, NEFR	Railways	NEFR	04/2008	12/2015	N.A.	12/2015	1339.48	3380.57

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
97	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR)	Railways	NWR	04/2008	03/2014	N.A.	03/2014	653.19	653.19
98	Himmatnagar - Udaipur Gauge Conversion (NWR)	Railways	NWR	04/2008	03/2015	N.A.	03/2015	829.74	829.74
99	Suratpura - Hanumangarh - Sriganganagar Gauge Conversion (NWR)	Railways	NWR	04/2008	03/2014	N.A.	03/2014	516.23	516.23
100	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT	Railways	RE	02/2008	03/2012	N.A.	03/2012	171.10	171.10
101	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh.	Railways	RVNL	04/2010	03/2016	N.A.	03/2016	2619.02	2619.02
102	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP)	Railways	RVNL	04/2010	03/2016	N.A.	03/2016	3951.98	3951.98
103	Ratlam-Mhow-Khandwa-Akola (GC)	Railways	WR	04/2008	03/2012	N.A.	03/2012	603.04	603.04
104	Udhna-Jalgaon with electrification(doubling) (WR)	Railways	WR	04/2008	03/2014	N.A.	03/2014	1389.62	1389.62
105	Bhuj-Naliya(GC) with extension from naliyate vayor (WR)	Railways	WR	04/2008	03/2012	N.A.	03/2012	318.24	468.62
106	Ahmedabad-Himmatnagar-Udaipur (WR)	Railways	WR	04/2008	03/2013	N.A.	03/2013	394.13	394.14
107	Talegaon-amravati	Road Transport & Highways	NHAI	11/2009	11/2013	N.A.	11/2013	567.00	567.00
108	DEOLI-KOTA	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	953.00	593.00
109	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	11/2009	05/2012	N.A.	05/2012	795.00	795.00
110	Hyderabad-Vijaywada Km. 40 to 221.50 Km	Road Transport & Highways	NHAI	04/2010	10/2012	N.A.	10/2012	1740.00	1740.00
111	PANIPAT-ROHTAK	Road Transport & Highways	NHAI	04/2011	10/2014	N.A.	10/2014	807.00	807.00
112	MURADABAD-BAREILY	Road Transport & Highways	NHAI	04/2010	06/2013	N.A.	06/2013	1267.00	1267.00
113	PUNE-SATARA(NH-4)	Road Transport & Highways	NHAI	10/2010	03/2013	N.A.	03/2013	1724.55	1724.55
114	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	Road Transport & Highways	NHAI	09/2010	03/2013	N.A.	03/2013	852.00	852.00

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
115	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4	Road Transport & Highways	NHAI	09/2010	09/2013	N.A.	09/2013	1655.00	1655.00
116	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	06/2010	12/2012	N.A.	12/2012	792.06	792.06
117	Pune-sholapur, pkg1	Road Transport & Highways	NHAI	11/2009	05/2012	N.A.	05/2012	1110.00	1110.00
118	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	03/2005	07/2012	N.A.	07/2012	940.00	940.00
119	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	12/2009	06/2012	N.A.	06/2012	835.00	835.00
120	Indore-Jhabua-Gujrat/MP	Road Transport & Highways	NHAI	10/2010	04/2013	N.A.	04/2013	1175.00	1175.00
121	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	08/2010	01/2013	N.A.	01/2013	625.07	625.07
122	Gujarat/Maharashtra Border Surat-Hazira Port Section	Road Transport & Highways	NHAI	03/2010	09/2012	N.A.	09/2012	1509.10	1509.10
123	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	Road Transport & Highways	NHAI	11/2010	05/2013	N.A.	05/2013	1585.00	1585.00
124	2 Laning of Muzaffarpur - Sonbarsa	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	511.54	511.54
125	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	Road Transport & Highways	NHAI	06/2011	06/2013	N.A.	06/2013	600.00	600.00
126	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	Road Transport & Highways	NHAI	09/2011	12/2013	N.A.	12/2013	1250.00	1250.00
127	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	Road Transport & Highways	NHAI	06/2011	12/2013	N.A.	12/2013	535.00	535.00

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
128	GHAZIABAD-ALIGARH NH-91	Road Transport & Highways	NHAI	02/2011	08/2013	N.A.	08/2013	1141.00	1141.00
129	ROHTAK-BAWAL	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	650.00	650.00
130	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	Road Transport & Highways	NHAI	03/2011	08/2013	N.A.	08/2013	785.50	785.50
131	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	12/2010	06/2013	N.A.	06/2013	1008.50	1008.50
132	PATNA-MUZZAFFARPUR	Road Transport & Highways	NHAI	08/2010	02/2013	N.A.	02/2013	671.30	671.30
133	SAMAIKHALI - GANDHIDHAM	Road Transport & Highways	NHAI	09/2010	03/2013	N.A.	03/2013	805.39	805.39
134	Tirupati - Tiruthani - Chennai	Road Transport & Highways	NHAI	04/2011	10/2013	N.A.	10/2013	571.00	571.00
135	2 laning of Dindigul - Perigulam Theni- kumili	Road Transport & Highways	NHAI	09/2011	08/2013	N.A.	08/2013	485.00	485.00
136	Two laning of Trichy - Karaikudi and Trychi Bypass	Road Transport & Highways	NHAI	05/2010	05/2013	N.A.	05/2013	374.00	374.00
137	Kandla - Mundra port	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	953.88	953.88
138	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	Road Transport & Highways	NHAI	07/2010	07/2013	N.A.	07/2013	1813.76	1813.76
139	NASHRI CHANANI	Road Transport & Highways	NHAI	06/2010	06/2015	N.A.	06/2015	2159.00	2159.00
140	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	Road Transport & Highways	NHAI	07/2010	07/2015	N.A.	07/2015	1987.00	1987.00

SN	PROJECTS	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
141	INDORE-DEWAS(NH-3)	Road Transport & Highways	NHAI	11/2010	05/2013	N.A.	05/2013	325.00	325.00
142	4 LANING OF NAGPUR-BETUL	Road Transport & Highways	NHAI	02/2011	08/2014	N.A.	08/2014	2498.76	2498.76
143	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	Road Transport & Highways	NHAI	03/2011	09/2013	N.A.	09/2013	359.00	359.00
144	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	Road Transport & Highways	NHAI	02/2011	11/2012	N.A.	11/2012	193.45	193.45
145	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	08/2010	05/2012	N.A.	05/2012	388.00	388.00
146	Modification & Strengthening of Existing Berth No. 1 to 6	Shipping & Ports	PORT TRUST	06/2010	03/2012	N.A.	03/2012	277.00	277.00
147	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK CARRIERS	Shipping & Ports	SHIPP.	11/2007	03/2012	N.A.	03/2012	1061.96	1082.06
148	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS	Shipping & Ports	SHIPP.	08/2008	09/2012	N.A.	09/2012	1066.91	968.35
149	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy	Shipping & Ports	SHIPP.	10/2010	02/2014	N.A.	02/2014	966.46	994.82
150	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd.	Shipping & Ports	SHIPP.	10/2010	12/2013	N.A.	12/2013	1028.10	1028.10
151	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries	Shipping & Ports	SHIPP.	08/2010	12/2012	N.A.	12/2012	612.72	627.64
152	1.2 MTPA PELLET PLANT DONIMALAI	Steel	NMDC	04/2011	04/2013	N.A.	04/2013	572.00	572.00
153	7.0 MTPA KUMARASWAMY IRON ORE MINE	Steel	NMDC	02/2011	05/2013	N.A.	05/2013	898.55	898.55
154	EXPENSION OF ROURKELA STEEL PLANT	Steel	SAIL	09/2008	03/2013	N.A.	03/2013	11812.00	11812.00
155	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES	Steel	SAIL	11/2011	11/2013	N.A.	11/2013	254.55	254.55
156	EXPANSION OF DURGAPUR STEEL PLANT	Steel	SAIL	06/2009	12/2012	N.A.	12/2012	2875.00	2875.00
157	DELHI MRTS PHASE-III	Urban Development	DMRC	09/2011	03/2016	N.A.	03/2016	35242.00	35242.00
158	FARIDABAD EXTENSION	Urban Development	DMRC	09/2011	09/2014	N.A.	09/2014	2494.00	2494.00

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,410.82	09/2010 -	01/2012	16	
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	14,268.00	12/2008 -	03/2013	51	
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	860.00	12/2016 -	03/2017	3	
	Total		28,983.00 -	33,821.00	18,538.82				
<u>Civil Aviation</u>									
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,598.13	01/2011 -	02/2012	13	
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,730.76	05/2011 -	03/2012	10	
6	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	68.61	05/2012 -	08/2012	3	
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	170.82	01/2011 -	12/2012	23	
	Total		4,395.58 -	4,985.07	3,568.32				
<u>Coal</u>									
8	BARSINGSAR TPS (2 125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,868.71	1,714.72	06/2009 -	01/2012	31	
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	87.85	03/2010 -	03/2012	24	
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,361.58	06/2009 -	07/2012	37	
11	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	105.51	03/2011 03/2012	03/2013	24	
12	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 -	741.62	292.07	03/2010 -	03/2013	36	
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	229.64	03/2013 09/2012	12/2013	9	
14	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,291.82	03/2010 -	03/2014	48	
15	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,142.56	03/2010 -	03/2014	48	
16	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	19.96	03/2011 -	03/2014	36	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	33.66	03/2011 03/2012	03/2014	36	
18	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	61.24	03/2012 03/2012	03/2014	24	
19	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	93.47	03/2012 03/2013	03/2014	24	
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	141.38	03/2012	03/2015	36	
21	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48	
22	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	71.05	12/2012	03/2015	27	
23	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	248.98	03/2014	03/2016	24	
24	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	18.16	07/2012 03/2014	03/2016	44	
	Total		11,824.69	14,994.80	7,913.65				
	Fertilisers								
25	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	147.84	07/2011	03/2012	8	
26	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	159.38	07/2011	04/2012	9	
	Total		763.00	763.00	307.22				
	Steel								
27	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93	232.93	178.90	05/2011	02/2012	9	
28	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	12,663.88	12/2011	03/2012	3	
29	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	6,325.00	6,325.00	2,367.36	12/2011	03/2012	3	
30	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,130.48	10/2009 10/2012	10/2012	36	
31	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	4,575.39	03/2013	06/2013	3	
	Total		46,957.93	52,521.93	28,916.01				
	Petroleum								
32	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	149.79	03/2009 02/2012	01/2012	34	
33	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07	1,385.00	1,082.05	10/2010 12/2011	03/2012	17	

List of Delay Project w.r.t Original

Jan,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
34	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	686.69	04/2011 12/2011	03/2012	11	
35	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 898.00	898.00	804.61	09/2011 03/2012	03/2012	6	
36	HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70 -	706.70	686.67	04/2010 -	03/2012	23	
37	NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08 -	305.08	290.05	04/2011 -	03/2012	11	
38	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	934.05	09/2011 03/2012	03/2012	6	
39	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,450.37	04/2006 05/2011	05/2012	73	
40	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,335.28	05/2010 05/2012	05/2012	24	
41	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	246.28	05/2010 04/2012	05/2012	24	
42	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	715.36	09/2011 05/2012	05/2012	8	
43	KARANPUR MORADABAD-KASHIPUR- RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL, Multi State	07/2009	238.68 252.37	204.00	155.45	01/2012 -	05/2012	4	
44	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	465.50	07/2010 05/2012	07/2012	24	
45	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	-	04/2011 -	07/2012	15	
46	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,539.07	03/2012 08/2012	08/2012	5	
47	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	531.38	03/2011 05/2011	10/2012	19	
48	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.71	09/2011 -	12/2012	15	
49	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	-	12/2011 -	01/2013	13	
50	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	258.24	03/2006 03/2013	03/2013	84	
51	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	417.93	03/2010 03/2012	03/2013	36	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
52	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,808.47	05/2010 03/2013	03/2013	34	
53	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	04/2013	31	
54	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	04/2013	10	
55	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	05/2013	6	
56	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	13,027.63	11/2012 -	06/2013	7	
57	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,018.35	09/2012 -	09/2013	12	
58	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	2,393.39	08/2010 03/2012	12/2013	40	
59	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	595.83	03/2007 03/2014	03/2014	84	
60	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50	
61	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30	
62	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,413.90	03/2007 03/2017	03/2017	120	
	Total		84,314.10 -	92,699.51	43,396.50				
Power									
63	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	139.80	06/2010 06/2010	01/2012	19	
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	167.10	08/2011 -	01/2012	5	
65	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	219.00	07/2010 02/2012	01/2012	18	
66	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 -	2,283.69	2,574.64	04/2005 -	03/2012	83	
67	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	7,616.00	12/2009 -	03/2012	27	
68	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	2,084.00	1,724.30	08/2010 04/2012	03/2012	19	
69	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.66	726.70	10/2009 -	03/2012	29	
70	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,354.00	05/2011 -	03/2012	10	

List of Delay Project w.r.t Original

Jan,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
71	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	95.60	02/2012 02/2012	03/2012	1	
72	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	114.10	07/2011 -	03/2012	8	
73	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.25	718.76	02/2011 10/2012	05/2012	15	
74	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	1,794.00	1,653.86	11/2009 02/2013	06/2012	31	
75	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,779.29	1,775.08	09/2008 -	06/2012	45	
76	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 4,282.59	4,282.59	3,648.00	09/2009 -	06/2012	33	
77	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	518.50	01/2010 -	06/2012	29	
78	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,034.30	07/2010 -	06/2012	23	
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	122.40	11/2011 11/2011	06/2012	7	
80	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	307.83	07/2011 -	06/2012	11	
81	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	950.90	02/2012 -	06/2012	4	
82	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.39	1,419.95	03/2007 09/2012	09/2012	66	
83	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	685.00	11/2011 -	12/2012	13	
84	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	256.30	11/2011 -	12/2012	13	
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	306.30	11/2011 -	12/2012	13	
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	145.30	02/2012 -	12/2012	10	
87	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,666.39	10/2010 01/2013	01/2013	27	
88	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	704.32	08/2010 01/2013	01/2013	29	
89	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,087.00	04/2009 -	03/2013	47	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	387.90	09/2010 -	03/2013	30	
91	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	3,424.00	08/2012 -	03/2013	7	
92	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00 -	5,915.00	2,741.00	10/2012 -	03/2013	5	
93	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,529.00	10/2012 -	03/2013	5	
94	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,072.97	09/2009 06/2013	06/2013	45	
95	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	547.40	12/2012 -	06/2013	6	
96	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	280.37	08/2012 08/2013	08/2013	12	
97	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,493.95	01/2012 -	09/2013	20	
98	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	139.70	11/2011 -	09/2013	22	
99	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,433.00	08/2013 -	01/2014	5	
100	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,735.00	06/2011 -	04/2014	34	
101	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,307.00	03/2013 -	06/2014	15	
102	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	3,596.20	08/2013 -	09/2014	13	
103	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,431.00	12/2009 -	12/2014	60	
104	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,312.61	09/2010 08/2014	12/2015	63	
105	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	285.17	07/2010 02/2016	02/2016	67	
106	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,715.85	05/2013 06/2016	06/2016	37	
107	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	238.12	07/2014 -	09/2016	26	
108	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,131.52	01/2016 01/2016	11/2016	10	
109	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,461.64	09/2009 07/2014	12/2014	63	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		124,405.20	139,091.25	81,994.83				
			-						
	<u>Railways</u>								
110	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER, West Bengal	04/2009	259.51	259.51	72.61	12/2011 02/2012	02/2012	2	
111	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 634.13	634.13	546.82	03/1995 -	03/2012	204	
112	LANJHIGARH-JUNAGARH NL (ECOR) - [220100148]ECOR, Orissa	04/1993	100.00 142.98	227.94	190.98	03/2002 -	03/2012	120	
113	NANDYAL-YERRAGUNTALA (NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 164.36	840.32	527.52	02/2009 -	03/2012	37	
114	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	324.90	207.45	03/2010 -	03/2012	24	
115	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE, Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12	
116	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat	04/2006	196.97 -	196.97	190.24	03/2011 -	03/2012	12	
117	RANCHI-LOHARDAGA (GC), SER - [220100214]SER, Jharkhand	04/1997	194.07 -	456.45	295.54	06/2004 -	12/2012	102	
118	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 -	981.00	616.60	03/2009 12/2012	12/2012	45	
119	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47 1,389.98	1,389.98	1,134.54	10/2007 12/2012	12/2012	62	
120	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33	
121	Ghutiasharif-Canning (ER) - [N22000117]ER, West Bengal	04/2009	189.97 -	189.97	78.02	12/2011 11/2013	11/2013	23	
122	GOELKERA-MANOHARPUR, (LD) (SER) - [N22000045]SER, Jharkhand	03/1997	186.92 261.70	283.10	36.90	02/2006 -	12/2013	94	
123	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam	04/1996	1,676.31 -	4,027.93	2,903.63	03/2009 -	12/2013	57	
124	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 393.46	499.16	153.40	03/2007 03/2007	03/2014	84	
125	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00 -	1,655.80	1,076.88	12/2008 -	03/2014	63	
126	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90 -	222.92	85.29	12/2012 -	03/2014	15	
127	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00 -	819.40	114.15	03/2010 06/2014	06/2014	51	
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRT, Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	12	
129	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 662.69	723.27	387.66	06/2005 07/2011	06/2015	120	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
130	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,308.03	04/2008 03/2014	12/2015	92	
131	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	208.25	02/2010 -	12/2015	70	
132	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	1,173.79	414.38	03/2005 12/2008	03/2016	132	
133	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	592.92	03/2011 03/2014	03/2016	60	
134	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	4.01	03/2014 03/2016	03/2016	24	
135	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	8.17	03/2016 -	06/2016	3	
136	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	7,787.91	03/2001 -	12/2017	201	
	Total		22,136.80 -	52,427.15	20,566.91				
<u>Road Transport & Highways</u>									
137	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	01/2012	82	
138	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	177.69	08/2004 -	02/2012	90	
139	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	437.80	11/2007 -	02/2012	51	
140	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	436.10	09/2009 -	02/2012	29	
141	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	167.83	08/2004 07/2010	03/2012	91	
142	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	166.30	184.60	03/2008 -	03/2012	48	
143	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	155.10	03/2008 -	03/2012	48	
144	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	285.60	10/2008 -	03/2012	41	
145	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	362.10	03/2008 -	03/2012	48	
146	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	247.30	01/2009 -	03/2012	38	
147	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	264.70	06/2008 -	03/2012	45	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
148	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00 -	383.00	12/2008 -	03/2012	39	
149	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94 -	323.30	09/2008 -	03/2012	42	
150	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00 -	477.10	09/2008 -	03/2012	42	
151	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82 -	261.00	11/2008 -	03/2012	40	
152	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00 -	1,901.00	01/2011 -	03/2012	14	
153	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00 -	295.00 -	759.90	08/2010 -	03/2012	19	
154	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00 -	531.90	01/2011 -	03/2012	14	
155	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75 -	2,610.00	08/2011 -	03/2012	7	
156	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00 -	225.00 -	257.50	10/2008 -	04/2012	42	
157	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56 -	616.00	02/2012 -	04/2012	2	
158	SAGAR BY PASS, KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30 -	177.00	10/2008 -	05/2012	43	
159	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00 -	491.20	03/2008 -	05/2012	50	
160	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	263.27 -	259.07	02/2004 -	05/2012	99	
161	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00 -	930.90	02/2010 -	05/2012	27	
162	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00 -	284.00 -	349.30	05/2010 -	05/2012	24	
163	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57 -	186.00	09/2007 -	06/2012	57	
164	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	367.49 -	453.68	03/2005 -	06/2012	87	
165	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	275.00 -	300.00	09/2007 -	06/2012	57	
166	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00 -	258.80	09/2007 -	06/2012	57	
167	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66 -	100.30	09/2008 -	06/2012	45	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
168	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	170.20	10/2008 -	06/2012	44	
169	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	182.68	06/2008 -	06/2012	48	
170	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	266.44	06/2008 -	06/2012	48	
171	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	267.80	06/2008 -	06/2012	48	
172	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	188.90	06/2008 -	06/2012	48	
173	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	132.10	05/2008 -	06/2012	49	
174	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	204.70	06/2008 -	06/2012	48	
175	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2012	42	
176	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	742.00	10/2009 -	06/2012	32	
177	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	294.60	10/2009 -	06/2012	32	
178	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	470.10	12/2009 -	06/2012	30	
179	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,406.00	10/2011 -	06/2012	8	
180	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,196.00	11/2011 -	06/2012	7	
181	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	91.40	04/2004 -	07/2012	99	
182	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	182.03	02/2004 -	07/2012	101	
183	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	157.40	05/2008 -	08/2012	51	
184	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	278.50	10/2008 -	09/2012	47	
185	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	235.00	10/2008 -	09/2012	47	
186	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	185.50	06/2010 -	10/2012	28	
187	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.40	09/2009 -	10/2012	37	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
188	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16	
189	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	580.00	10/2011 -	10/2012	12	
190	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	11/2012	41	
191	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	217.70	06/2008 -	12/2012	54	
192	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	203.43	217.30	10/2008 -	12/2012	50	
193	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	287.80	10/2008 -	12/2012	50	
194	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	177.40	07/2008 -	12/2012	53	
195	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	129.50	04/2008 -	12/2012	56	
196	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	192.90	04/2008 -	12/2012	56	
197	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	235.50	04/2008 -	12/2012	56	
198	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	165.80	04/2010 -	12/2012	32	
199	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	173.60	09/2010 -	12/2012	27	
200	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	573.30	05/2010 -	12/2012	31	
201	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	244.10	02/2009 -	03/2013	49	
202	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	89.64	04/2009 -	03/2013	47	
203	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	691.90	07/2010 -	03/2013	32	
204	AGRA-BYPASS (NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	135.60	09/2007 -	06/2013	69	
205	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	846.50	11/2012 -	06/2013	7	
206	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	38.05	04/2009 -	07/2013	51	
207	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	65.49	11/2008 -	07/2013	56	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
208	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41	
209	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14	
210	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	2,047.00	11/2008	01/2014	62	
211	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	225.80	10/2011	03/2014	29	
212	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	154.70	05/2013	03/2014	10	
213	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	-	09/2007	04/2014	79	
214	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	-	07/2009	04/2014	57	
	Total		27,654.27	29,936.86	33,572.61				
	Shipping & Ports								
215	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2	
216	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.79	04/2011 06/2011	06/2012	14	
217	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	06/2012	12	
218	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8	
219	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	1,460.00	652.40	12/2010	09/2012	21	
220	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29	
221	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.16	02/2011	03/2013	25	
222	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24	
223	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009	05/2013	52	
224	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006	12/2013	93	

List of Delay Project w.r.t Original

Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		8,208.42	9,033.57	1,465.21				
			-						
	<u>Telecommunications</u>								
225	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	161.31	12/2005	03/2012	75	
			-			-			
226	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	211.36	12/2008	03/2012	39	
			-			-			
227	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	155.71	01/2009	03/2012	38	
			-			-			
228	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	03/2012	36	
			-			-			
229	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) - [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	362.62	08/2009	03/2012	31	
			-			-			
230	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) - [N26000090]BSNL,Madhya pradesh	11/2009	916.70	930.60	757.02	11/2010	03/2012	16	
			930.60			-			
231	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	21.80	10/2010	07/2012	21	
			-			03/2012			
	Total		3,457.58	3,646.98	1,834.40				
			-						
	<u>Urban Development</u>								
232	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	12/2013	24	
			-			-			
	Total		6,395.00	11,609.00	2,267.57				
			-						
	<u>Water Resources</u>								
233	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60	
			-			-			
	Total		542.90	1,187.00	35.49				
			-						
Grand Total			370,038.47	446,717.12	244,377.54				

List of Projects Without Milestones

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning	
				Original / Revised	Anticipated
1	2	3	4	7	8
<u>Atomic Energy</u>					
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	-	04/2012
			-	04/2011	
	Total		1,106.29		
			-		
<u>Civil Aviation</u>					
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
			2,015.00	-	
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011	03/2012
			-	-	
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	05/2012	08/2012
			-	-	
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011	12/2012
			-	-	
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013
			-	-	
	Total		5,021.58		
			-		
<u>Coal</u>					
7	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	03/2014	03/2014
			-	-	
8	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	04/2014	04/2014
			-	-	
9	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	03/2012	03/2015
			-	-	
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	03/2015	03/2015
			-	-	
11	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	03/2015	03/2015
			-	-	
12	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	04/2015	04/2015
			-	-	
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	03/2018	03/2018
			1,131.28	-	
	Total		4,219.75		
			-		
<u>Fertilisers</u>					
14	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	07/2011	03/2012
			-	-	
15	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	07/2011	04/2012
			-	-	
	Total		763.00		
			-		
<u>Steel</u>					

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
16	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	04/2013 -	04/2013
17	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	05/2013 -	05/2013
18	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55 -	11/2013 -	11/2013
	Total		1,725.10 -		
<u>Petroleum</u>					
19	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	12/2010 -	06/2011
20	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	09/2009 -	08/2011
21	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	03/2009 02/2012	01/2012
22	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	01/2012 -	01/2012
23	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	09/2011 03/2012	03/2012
24	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	03/2013 03/2013	03/2012
25	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	04/2010 -	03/2012
26	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	04/2011 -	03/2012
27	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	03/2012
28	WIND ENERGY - [N16000126]GAIL,Multi State	05/2011	616.00 -	- -	03/2012
29	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	04/2006 05/2011	05/2012
30	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	05/2012
31	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	05/2010 04/2012	05/2012
32	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	09/2011 05/2012	05/2012
33	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2012
34	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 09/2012	06/2012
35	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	07/2012
36	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	07/2012
37	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	07/2012 -	07/2012
38	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	08/2012
39	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2012

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
40	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	10/2012
41	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2012
42	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013
43	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	03/2013
44	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013
45	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2013
46	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	03/2013
47	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	03/2013
48	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	03/2013
49	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	- 12/2008	04/2013
50	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013
51	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	04/2013
52	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	05/2013
53	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013
54	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	08/2013
55	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013
56	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013
57	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013
58	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014
59	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014
60	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014
61	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014
62	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014
63	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014
64	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
65	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015
66	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	02/2011 08/2011	-
67	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
	Total		98,440.35 -		
Power					
68	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	06/2010 06/2010	01/2012
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	08/2011 -	01/2012
70	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	07/2010 02/2012	01/2012
71	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96 -	02/2012 -	02/2012
72	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	02/2012 02/2012	03/2012
73	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	07/2011 -	03/2012
74	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	06/2012 -	03/2012
75	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	04/2012
76	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	05/2012 -	05/2012
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	11/2011 11/2011	06/2012
78	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	07/2011 -	06/2012
79	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	02/2012 -	06/2012
80	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	06/2012 -	06/2012
81	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	06/2012 -	06/2012
82	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	08/2012 -	08/2012
83	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	08/2012 -	08/2012
84	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	08/2012 -	08/2012
85	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	10/2012 -	10/2012
86	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	10/2012 -	10/2012

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
87	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	10/2012 -	10/2012
88	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	11/2012 -	11/2012
89	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	11/2012 -	11/2012
90	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	11/2012 -	11/2012
91	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	12/2012 -	12/2012
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	11/2011 -	12/2012
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	11/2011 -	12/2012
94	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	02/2012 -	12/2012
95	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	01/2013 -	01/2013
96	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	01/2013 -	01/2013
97	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	01/2013 -	01/2013
98	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	03/2013
99	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	03/2013 -	03/2013
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	04/2013 -	04/2013
101	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	04/2013 -	04/2013
102	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	06/2013
103	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	12/2012 -	06/2013
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	07/2013 -	07/2013
105	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013
106	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	07/2013 -	07/2013
107	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	08/2013 -	08/2013
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	08/2013 -	08/2013
109	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	08/2013 -	08/2013
110	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pr.	01/2007	2,047.03 -	01/2012 -	09/2013

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
111	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	11/2011 -	09/2013
112	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	10/2013 -	10/2013
113	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	11/2013 -	11/2013
114	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26 -	11/2013 -	11/2013
115	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL,Multi State	08/2011	1,391.97 -	12/2013 -	11/2013
116	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	12/2013 -	12/2013
117	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	12/2013 -	12/2013
118	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	12/2013 -	12/2013
119	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	01/2014 -	01/2014
120	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	02/2014 -	02/2014
121	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	03/2014 -	03/2014
122	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	05/2014 -	05/2014
123	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	06/2014 -	06/2014
124	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	08/2014 -	08/2014
125	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014
126	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJEC - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	08/2014 -	08/2014
127	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	08/2013 -	09/2014
128	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	09/2014 -	09/2014
129	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	01/2015 -	01/2015
130	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	01/2015 -	01/2015
131	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	08/2014 -	-

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
	Total		94,354.56		
			-		
	<u>Railways</u>				
132	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
133	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
134	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010
135	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
136	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
137	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011
138	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	- 03/2011	03/2011
139	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
140	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
141	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	- 03/2011	03/2011
142	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
143	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	12/2011
144	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	12/2011
145	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
146	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012
147	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	- 12/2009	02/2012
148	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	12/2011 02/2012	02/2012
149	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2012
150	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	- -	03/2012
151	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2012
152	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	- 12/2011	03/2012
153	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	- 03/2012	03/2012
154	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	02/2009 -	03/2012

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
155	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	- 03/2012	03/2012
156	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
157	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	- 03/2012	03/2012
158	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	- 02/2011	03/2012
159	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012
160	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	- 03/2012	03/2012
161	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
162	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
163	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
164	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012
165	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
166	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
167	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	03/2012
168	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	03/2012 -	03/2012
169	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	03/2012 -	03/2012
170	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012
171	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	- 07/2012	07/2012
172	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	06/2004 -	12/2012
173	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 -	12/2012
174	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	- 03/2012	12/2012
175	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	- 03/2012	12/2012
176	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	03/2009 12/2012	12/2012
177	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	10/2007 12/2012	12/2012
178	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012
179	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	12/2012 -	12/2012

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
180	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013
181	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
182	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2013
183	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013
184	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	03/2013 -	03/2013
185	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	- 02/2009	04/2013
186	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	- 03/2009	04/2013
187	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTPT,Tamil Nadu	04/2006	495.74 -	- 06/2013	06/2013
188	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	12/2011 11/2013	11/2013
189	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013
190	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	02/2006 -	12/2013
191	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	03/2009 -	12/2013
192	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2014
193	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	12/2008 -	03/2014
194	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	03/2014
195	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	03/2014 -	03/2014
196	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2014
197	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	03/2014 -	03/2014
198	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	03/2014 -	03/2014
199	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014
200	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	12/2012 -	03/2014
201	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014
202	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015
203	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	- 12/2010	03/2015
204	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
205	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	03/2014 03/2015	03/2015
206	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	03/2015
207	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	03/2015 -	03/2015
208	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	03/2015 -	03/2015
209	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	06/2005 07/2011	06/2015
210	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015
211	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	12/2015
212	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015
213	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	03/2005 12/2008	03/2016
214	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	03/2011 03/2014	03/2016
215	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016
216	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016
217	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016
218	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016
219	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	03/2001 -	12/2017
220	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
221	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
222	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	- -	-
223	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	-
224	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	03/1998 -	-
225	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-
226	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
227	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	-
228	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	07/2005 -	-
229	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Antici- pated
1	2	3	4	7	8
230	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	-
231	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
232	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	-
233	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
234	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-
235	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	- -	-
236	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	- 12/2012	-
237	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-
238	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
239	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13 727.13	- -	-
240	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-
241	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
242	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
243	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI- THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-
244	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-
245	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	-
246	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-
247	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
248	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-
249	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
250	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	-
251	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
252	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,302.12	- 06/2012	-
253	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	-
254	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
255	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	-
256	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 -	- -	-
257	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, Bihar	04/2003	218.19 -	- -	-
258	HATHUA-BHATNI (N L) (NER) - [220100319]NER, Multi State	04/2005	230.03 -	- -	-
259	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER, West Bengal	04/2007	245.15 -	12/2010 03/2011	-
260	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 -	- 12/2010	-
Total			61,457.53 -		
<u>Road Transport & Highways</u>					
261	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	06/2005 -	12/2011
262	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00 -	03/2005 -	01/2012
263	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	08/2004 -	02/2012
264	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78 -	11/2007 -	02/2012
265	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	09/2009 -	02/2012
266	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00 -	- -	02/2012
267	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	08/2004 07/2010	03/2012
268	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09 -	03/2008 -	03/2012
269	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27 -	03/2008 -	03/2012
270	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	10/2008 -	03/2012
271	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	03/2008 -	03/2012
272	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	01/2009 -	03/2012
273	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	06/2008 -	03/2012
274	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	12/2008 -	03/2012
275	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	09/2008 -	03/2012
276	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	09/2008 -	03/2012
277	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	- 06/2011	03/2012

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
278	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	11/2008 -	03/2012
279	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	01/2011 -	03/2012
280	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00 -	08/2010 -	03/2012
281	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	01/2011 -	03/2012
282	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	08/2011 -	03/2012
283	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya Pradesh	12/2003	225.00 -	10/2008 -	04/2012
284	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	02/2012 -	04/2012
285	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	10/2008 -	05/2012
286	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	03/2008 -	05/2012
287	GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	02/2004 -	05/2012
288	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	02/2010 -	05/2012
289	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00 -	05/2010 -	05/2012
290	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	05/2012 -	05/2012
291	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	05/2012 -	05/2012
292	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00 -	05/2012 -	05/2012
293	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	09/2007 -	06/2012
294	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	03/2005 -	06/2012
295	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	09/2007 -	06/2012
296	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	09/2007 -	06/2012
297	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	09/2008 -	06/2012
298	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)- NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	10/2008 -	06/2012
299	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	06/2008 -	06/2012
300	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	06/2008 -	06/2012
301	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	06/2008 -	06/2012
302	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	06/2008 -	06/2012

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No Project		Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
303	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	06/2012
304	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	06/2012
305	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2012
306	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	10/2009 -	06/2012
307	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	06/2012
308	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	06/2012
309	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	06/2012
310	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	06/2012
311	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	06/2012
312	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	07/2012
313	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	07/2012
314	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	07/2012
315	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	08/2012
316	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2012
317	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	09/2012
318	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	09/2012
319	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012
320	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	10/2012
321	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012
322	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	10/2012
323	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012
324	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012
325	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012
326	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012
327	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Antici- pated
1	2	3	4	7	8
328	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012
329	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012
330	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	12/2012
331	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	12/2012
332	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2012
333	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2012
334	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	12/2012
335	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	12/2012
336	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	12/2012
337	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07 -	01/2013 -	01/2013
338	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013
339	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 -	03/2013
340	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013
341	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013
342	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013
343	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013
344	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	03/2013
345	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013
346	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013
347	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	05/2013
348	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013
349	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	06/2013
350	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013
351	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013
352	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
353	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013
354	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	07/2013
355	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	07/2013
356	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2013
357	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00 -	07/2013 -	07/2013
358	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	07/2013
359	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	07/2013
360	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013
361	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013
362	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013
363	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013
364	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	09/2013
365	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	10/2013
366	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013
367	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013
368	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013
369	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013
370	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013
371	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013
372	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	01/2014
373	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014
374	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014
375	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014
376	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014
377	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014

List of Projects Without Milestones

(Jan,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Date of Commissioning	
				Original / Revised	Anticipated
1	2	3	4	7	8
378	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	10/2014	10/2014
379	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00	06/2015	06/2015
380	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	07/2015	07/2015
	Total		67,519.63		
Shipping & Ports					
381	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
382	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	06/2006 09/2011	09/2011
383	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	12/2005 01/2008	10/2011
384	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50	09/2011	12/2011
385	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	03/2012	03/2012
386	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	01/2012	03/2012
387	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	03/2012	03/2012
388	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	04/2011 06/2011	06/2012
389	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	06/2011 01/2012	06/2012
390	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	12/2011 08/2012	08/2012
391	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	12/2010	09/2012
392	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	09/2012	09/2012
393	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	06/2010	11/2012
394	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012	12/2012
395	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	02/2011	03/2013
396	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	03/2011	03/2013
397	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	01/2009	05/2013
398	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	03/2006	12/2013

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
399	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013
400	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014
401	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	-
402	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	12/2007 01/2009	-
403	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	08/2010 -	-
404	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-
405	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-
	Total		18,221.36 -		
<u>Telecommunications</u>					
406	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	03/2009 -	02/2011
407	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010
408	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
409	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 -	08/2011
410	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 -	08/2011
411	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	09/2011 -	09/2011
412	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	12/2011
413	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	01/2010 -	12/2011
414	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 -	03/2012
415	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	03/2012
416	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	03/2012
417	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	03/2012
418	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	08/2009 -	03/2012
419	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	03/2012
420	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	07/2012
421	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-

List of Projects Without Milestones

(Jan,2012)

		Date of Commissioning			
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Antici- pated
1	2	3	4	7	8
422	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
423	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
	Total		8,443.59 -		
<u>Urban Development</u>					
424	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014
425	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016
426	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		37,850.18 -		
<u>Water Resources</u>					
427	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
Grand Total			399,665.82		

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
