

**321st FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
July, 2012**



PORT TRUST :- DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	6-8
Summary of Projects	9-21
Trend and Graphical Analysis of Projects	22-34
Sector wise analysis of projects	35-35
List of All Ongoing Projects	36-65
Sector wise Graph	66-77
ANNEXURE	78-78
Central Sector Projects	79-79
List of Projects Having Expenditure More than cost	80-85
List of Projects Ahead of Schedule	86-86
List of Projects with out Original date of Commissioning	87-89
List of Projects with out date of Commissioning	90-94
List of On schedule Projects	95-103
List of Projects without Milestones	104-120
List of Delayed Projects w.r.t Original and Revised	121-134
List of Projects Having cost overrun w.r.t original	135-144
List of Projects Having cost and time overrun w.r.t original	145-149
Abbreviations	150-151

EXECUTIVE SUMMARY

The Flash Report for July, 2012 contains information on the status of the 558 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During, July, 2012, 2 projects (1 project each in Power and Railways Sector) have reported completion.

During the reference month, out of 558 projects 251 projects are delayed and 28 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 14 months, in respect of projects relating to Road Transport and Highways, Railways, Power, Petroleum, Shipping & Ports, Steel and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest Scheduled	Additionally delayed during the month under report
1.	RAILWAYS	126	40	1
2.	ROAD TRANSPORT & HIGHWAYS	144	81	2
3.	POWER	98	43	4
4.	PETROLEUM	67	32	14
5.	COAL	51	22	0
6.	TELECOMMUNICATION	15	9	1
7.	SHIPPING & PORTS	19	6	1
8.	STEEL	16	7	5
9.	FERTILISERS	5	2	0
10.	CIVIL AVIATION	6	2	0
11.	ATOMIC ENERGY	5	5	0
12.	URBAN DEVELOPMENT	4	1	0
13.	WATER RESOURCES	1	1	0
14.	PETROCHEMICALS	1	0	0
Total		558	251	28

3. The total original cost of implementation of the 558 projects was about ₹ 7,56,601.56 Crores and their anticipated completion cost is likely to be ₹ 9,00,402.69 Crores, which reflects an overall cost overrun of ₹ 1,43,801.13 Crores (19.00 % of original cost). The expenditure incurred on these projects till July, 2012 is ₹ 4,07,443.78 Crores, which is 45.30 % of the anticipated cost of the projects.

4. Out of the 558 projects, 3 projects are ahead of schedule, 229 are on schedule and 251 projects are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 268 if delay is calculated on the basis of original scheduled of completion. Further, 44 projects have been sanctioned without any commissioning schedule/date and 30 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported. Out of 251 delayed projects, 87 projects had overall delay in the range of 1 to 12 months, 52 projects had a delay in the range of 13 to 24 months, 91 projects had a delay in the range of 25 to 60 months and 21 projects had a delay of 61 months and above.

5. The brief reasons for time overruns as reported by various projects implementing agencies are non-availability of suitable land, delay in municipal permission, delay in procurement of material, delay in award of work, ROU/ROW problem and poor mobilization by the contractor, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedule for many projects, which suggest that time/cost overrun figures are underreported.

7. The Sector-wise details of delays/additional delays are as under:-

i) In the **Shipping and Ports sector**, out of 19 projects, 6 projects are delayed. During the month 1 project namely 'Construction & Development of 2 offshore Container Berths & Terminal, Mumbai Port' has reported additional delay of 7 months. However, no specific reasons have been reported by the project authorities for delay in this project.

ii) In the **Telecommunications sector**, out of 15 projects, 9 projects are delayed. During the month 1 project namely 'GSM Equipment of 799000 Lines (2G) 101000 Lines (3G), BSNL' has reported additional delay of 3 months due to municipal permission issue and non-availability of suitable lands.

iii) In the **Petroleum Sector**, out of 67 projects, 32 projects are delayed. During the month 14 projects have reported additional delays in the range of 1-12 months. Two projects have reported additional delays of 1 month each, one project has reported additional delay of 2 months, three projects have reported additional delay of 3 months each, one project each has reported additional delay of 4 and 5 months respectively and two projects have reported additional delay of 6 months each. The project 'Up-gradation of Konaban GGS and Pipeline Grid Project, ONGC' has reported additional delay of 7 months due to ROU issue, 'Construction of 12 Offshore Supply Vessels (OSV), ONGC' has reported additional delay of 8 months due to delay in preparation of drawings and procurement of steel, 'Development of B-46 Cluster Field, ONGC' and 'Development of Cluster-7 Fields, ONGC' have reported additional delay of 10 and 12 months respectively due to delay in award of work.

iv) In the **Power Sector**, out of 98 projects, 43 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-9 months. Two projects have reported additional delays of one month each. The project 'Northern Region System Strengthening Scheme-XVIII, PGCIL' and 'Northern Region System Strengthening Scheme-XIX, PGCIL' have reported additional delay of 9 months each due to ROW problem.

v) In **Steel sector**, out of 16 projects, 7 projects are delayed. During the month 5 projects have reported additional delays in the range of 2-5 months. One project has reported additional delay of one month and two projects have reported additional delay of 3 months each. The project 'Expansion of RINL/VSP from 3 MTPY-6.3 MTPY of Liquid Steel, RINL' has reported additional delay of 5 months due to poor mobilization by the contractor. The project 'Enhancement of Production Capacity at Bolani I/O Mines, SAIL' has reported additional delay of 4 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vi) In the **Road Transport and Highways Sector**, out of 144 projects, 81 projects are delayed. During the month 2 projects of NHAI have reported additional delays in the range of 1-14 months. The project 'Harangajo to Maibang, Km 164.08-190.587 NH-54, NHAI' and 'Harangajo to Maibang (AS-23), Km.126.450 to Km.140.700, NHAI' have reported additional delay of 1 and 14 months respectively. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

viii) In the **Railways Sector**, out of 126 projects, 40 projects are delayed. During the month 1 project has reported additional delays of 6 months. The project 'Jayanagar-Darbhangha-Narkatia Ganj (GC), ECR' has reported additional delay of 6 months. However, no specific reasons have been reported by the project authorities for delay in this project. Regarding 45 projects of Railways for which either original/anticipated date of commissioning schedule is not available, M/o Railways has clarified that they have huge throwforward of ongoing projects with limited availability of resources, as a result funds are thinly spreaded prolonging period of completion. Targets are therefore, fixed on annual basis depending upon availability of resources and progress achieved on individual projects, therefore, by implication fixing of completion dates is difficult to finalize/report.

8. The status as on 01.08.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.

(T.C.A. Anant)
Secretary
Ministry of Statistics and Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	144	2
2	Railways	126	1
3	Power	98	4
4	Petroleum	67	14
5	Coal	51	0
6	Shipping & Ports	19	1
7	Steel	16	5
8	Telecommunications	15	1
9	Civil Aviation	6	0
10	Atomic Energy	5	0
11	Fertilisers	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	558	28

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April, 2012				
<u>Power</u>				
1	KOTESHWAR HEP (THDC) (TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	N.A.
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C (SHIPPING corp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH (SHIPPING corp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES (2G) AND 150K LINES (3G) (BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000 Lines (2G) 383000 lines 3 (BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May, 2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT (RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON (BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
	<u>Railways</u>			
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
	<u>Road Transport & Highways</u>			
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
	<u>Shipping & Ports</u>			
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
	June,2012			
	<u>Steel</u>			
19	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
	<u>Power</u>			
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	N.A.
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
	<u>Railways</u>			
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
	<u>Road Transport & Highways</u>			
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9
	July,2012			
	<u>Power</u>			
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
	<u>Railways</u>			
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096]	196.97	03/2011	218.66


Summary of projects in the Flash Report for the month of July, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	564
Number of Projects completed/dropped/frozen in Previous Month	9
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects Removed from system in Current Month	1
Number of Projects Added in Current Month	6
Number of Projects in Current Month	558


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 558 projects, 3 projects are ahead of schedule, 166 projects are on schedule and 268 projects are delayed. Of the balance, 84 projects do not have fixed dates of commissioning while 37 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

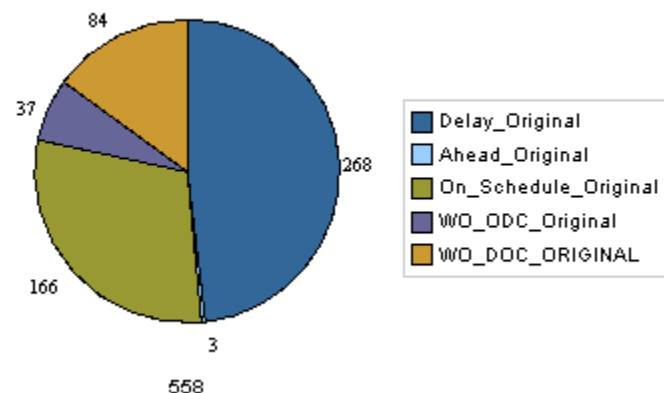

III. Investment Scenario

The Total Original cost of implementation of 558 projects when sanctioned, was of the order of Rs. 756601.56 crore but this was subsequently revised to Rs. 900402.69 crore implying a cost overrun of 19%. The expenditure incurred on these projects till July, 2012 is Rs. 407443.78 crore, which is 45.3% of the revised cost of the projects.

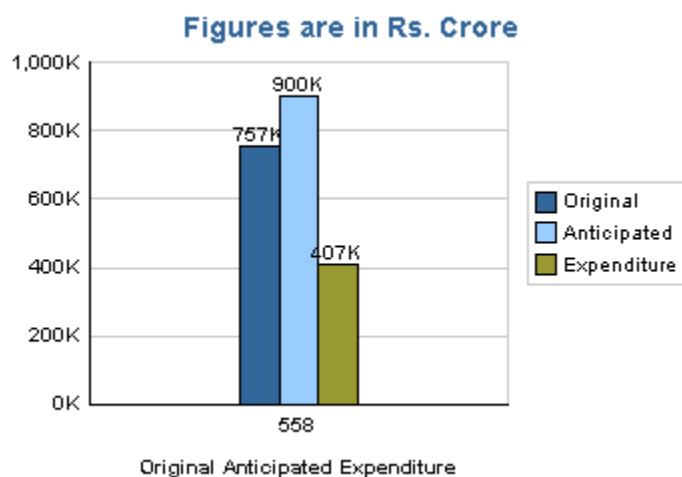

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	564
No of Projects Completed/Dropped/Frozen in Previous Month	9
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects Removed From System in Current Month	1
No of Projects added in Current Month	6
No of Projects in Current Month	558

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	268	3	166	37	84	558	48.03
Latest Approved (Date)	251	3	229	44	30	558	44.98

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	409	604,561.21	671,939.88	266,458.38	39.70	67,378.67	11.10
Latest Approved (RCE)	149	206,238.32	228,462.81	140,985.40	61.70	22,224.49	10.80
Total (RCE)	558	810,799.53	900,402.69	407,443.78	45.25	89603.16	11.05
Original Cost of All Projects							
Original Cost	558	756,601.56	900,402.69	407,443.78	45.30	143,801.13	19.00

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	268	351,403.39	432,896.93	248,353.70	57.40	81,493.54	23.20

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	30	63,837.65	86,677.27	46,671.24	53.80	22,839.62	35.80

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	33,815.1	37,312.3	10.3	12	12,779.2	16,874.1	32.0
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	16	50,110.2	71,356.8	42.4	8	32,529.9	53,806.4	65.4
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	67	157,430.3	166,078.1	5.5	16	51,356.4	68,035.0	32.5
8	Power	98	235,165.2	248,964.2	5.9	17	40,935.0	54,733.9	33.7
9	Railways	126	64,413.9	141,917.4	120.3	107	42,715.6	120,265.8	181.5
10	Road Transport & Highways	144	91,164.1	92,540.6	1.5	10	3,112.8	5,058.4	62.5
11	Shipping & Ports	19	16,242.5	17,782.5	9.5	10	8,732.5	10,579.5	21.2
12	Telecommunications	15	6,161.0	6,101.8	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		558	756,601.6	900,402.7	19.0	190	226,153.4	379,618.6	67.9

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,031.6	38,457.2	23.9	14	12,420.0	20,712.6	66.8
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	36	22,463.9	33,705.5	50.0	10	10,083.8	21,419.5	112.4
4	Bihar	29	26,796.5	31,675.7	18.2	13	12,563.5	17,442.8	38.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	10	5,496.6	7,367.2	34.0	3	1,448.2	3,318.8	129.2
8	Himachal Pr.	5	13,355.6	15,213.4	13.9	2	6,224.2	8,082.0	29.8
9	J and K	11	15,120.1	34,993.9	131.4	6	7,866.5	27,767.1	253.0
10	Karnataka	24	44,634.8	53,079.7	18.9	10	8,795.3	17,646.7	100.6
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	23	16,561.5	16,856.0	1.8	3	2,027.6	2,741.5	35.2
13	Maharashtra	53	95,829.8	111,041.9	15.9	18	31,818.4	49,505.1	55.6
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	30	57,405.4	61,398.9	7.0	13	33,147.5	37,141.0	12.0
19	Punjab	7	4,836.2	5,778.0	19.5	2	532.4	1,474.2	176.9
20	Rajasthan	14	26,544.1	26,138.3	-1.5	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	61,960.8	20.8	14	29,143.5	39,828.4	36.7
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	23	18,321.9	22,159.7	20.9	8	3,498.5	7,384.5	111.1
25	West Bengal	25	40,187.8	52,557.1	30.8	16	23,547.4	35,916.8	52.5
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	25	40,824.7	56,321.7	38.0	10	10,407.1	25,904.0	148.9
28	Jharkhandd	23	11,785.5	16,601.5	40.9	7	5,213.3	10,201.2	95.7
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	35.6
30	Multi State	103	137,052.7	142,750.9	4.2	21	6,624.0	16,517.8	149.4
Total		558	756,601.6	900,402.7	19.0	190	226,153.4	379,618.6	67.9

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	3 - 27
3	Coal	51	33,815.1	37,312.3	10.3	24	15,050.9	16,362.2	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	1	438.0	438.0	12 - 12
5	Steel	16	50,110.2	71,356.8	42.4	8	13,128.2	17,320.8	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	67	157,430.3	166,078.1	5.5	38	78,820.6	87,908.5	1 - 120
8	Power	98	235,165.2	248,964.2	5.9	48	126,828.7	140,014.6	2 - 99
9	Railways	126	64,413.9	141,917.4	120.3	40	25,960.8	66,031.1	1 - 216
10	Road Transport & Highways	144	91,164.1	92,540.6	1.5	82	33,091.2	34,800.9	2 - 101
11	Shipping & Ports	19	16,242.5	17,782.5	9.5	10	8,446.1	10,038.7	5 - 87
12	Telecommunications	15	6,161.0	6,101.8	-1.0	9	3,163.3	3,167.1	22 - 79
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		558	756,601.6	900,402.7	19.0	268	351,403.4	432,896.9	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,031.6	38,457.2	23.9	12	15,494.5	19,105.6	2 - 41
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	25 - 75
3	Assam	36	22,463.9	33,705.5	50.0	32	16,023.7	23,620.8	12 - 120
4	Bihar	29	26,796.5	31,675.7	18.2	14	20,578.4	23,672.8	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	3 - 3
6	Gujarat	22	31,111.6	31,313.5	0.6	5	13,715.4	13,885.6	9 - 24
7	Haryana	10	5,496.6	7,367.2	34.0	4	2,065.9	3,555.1	9 - 50
8	Himachal Pr.	5	13,355.6	15,213.4	13.9	5	13,355.6	15,213.4	20 - 99
9	J and K	11	15,120.1	34,993.9	131.4	7	9,707.1	29,554.1	10 - 201
10	Karnataka	24	44,634.8	53,079.7	18.9	9	22,364.3	27,444.8	3 - 96
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,674.0	5,324.0	9 - 58
12	Madhya pradesh	23	16,561.5	16,856.0	1.8	16	13,107.5	12,702.0	5 - 50
13	Maharashtra	53	95,829.8	111,041.9	15.9	25	47,453.8	58,653.6	2 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 11
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	30	57,405.4	61,398.9	7.0	9	1,798.9	2,112.2	24 - 132
19	Punjab	7	4,836.2	5,778.0	19.5	4	1,611.4	2,553.2	1 - 51
20	Rajasthan	14	26,544.1	26,138.3	-1.5	6	19,992.2	19,687.9	3 - 47
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	32	51,276.0	61,960.8	20.8	10	24,621.7	30,552.3	9 - 87
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	7 - 7
24	Uttar Pradesh	23	18,321.9	22,159.7	20.9	12	11,215.4	13,148.4	5 - 91
25	West Bengal	25	40,187.8	52,557.1	30.8	15	12,936.4	17,877.2	3 - 135
26	Delhi	3	37,985.0	37,965.4	-0.1	1	249.0	229.4	72 - 72
27	Chhatisgarh	25	40,824.7	56,321.7	38.0	6	1,743.1	2,054.4	10 - 47
28	Jharkhandd	23	11,785.5	16,601.5	40.9	9	2,442.6	3,602.4	12 - 102
29	Uttaranchal	3	5,619.2	6,559.6	16.7	3	5,619.2	6,559.6	22 - 39
30	Multi State	103	137,052.7	142,750.9	4.2	52	78,083.6	79,366.3	1 - 216
Total		558	756,601.6	900,402.7	19.0	268	351,403.4	432,896.9	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	5	41,548.3	47,832.3	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	2,278.1	2,660.6	3 - 17
3	Coal	51	33,815.1	37,312.3	10.3	22	12,952.8	14,683.6	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	2	763.0	763.0	9 - 12
5	Steel	16	50,110.2	71,356.8	42.4	7	4,436.2	5,029.8	2 - 26
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	67	157,430.3	166,078.1	5.5	32	64,927.9	70,965.1	0 - 84
8	Power	98	235,165.2	248,964.2	5.9	43	123,701.9	134,184.0	2 - 99
9	Railways	126	64,413.9	141,917.4	120.3	40	17,601.3	58,150.2	0 - 216
10	Road Transport & Highways	144	91,164.1	92,540.6	1.5	81	32,811.2	34,520.9	2 - 101
11	Shipping & Ports	19	16,242.5	17,782.5	9.5	6	7,001.8	8,242.8	9 - 34
12	Telecommunications	15	6,161.0	6,101.8	-1.0	9	3,116.1	3,120.0	17 - 79
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		558	756,601.6	900,402.7	19.0	251	318,076.4	392,948.2	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	34,781.1	37,312.3	7.3	10	10,536.1	13,067.2	24.0
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	16	55,985.5	71,356.8	27.5	5	9,099.0	24,500.3	169.3
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	67	171,256.0	166,078.1	-3.0	2	30,533.0	31,324.0	2.6
8	Power	98	238,972.3	248,964.2	4.2	11	33,945.2	43,937.1	29.4
9	Railways	126	88,855.6	141,917.4	59.7	76	37,140.2	90,206.9	142.9
10	Road Transport & Highways	144	91,330.6	92,540.6	1.3	9	2,916.3	4,695.4	61.0
11	Shipping & Ports	19	17,629.0	17,782.5	0.9	7	4,306.6	4,770.0	10.8
12	Telecommunications	15	6,164.9	6,101.8	-1.0	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		558	810,799.5	900,402.7	11.1	125	154,019.7	250,568.8	62.7

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	51	33,815.11	37,312.25	10.34	0	0.00	0.00	0- 0
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	16	50,110.22	71,356.76	42.40	2	8,987.89	12,898.17	10- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	67	157,430.30	166,078.11	5.49	12	20,971.88	35,745.22	19- 120
8	Power	98	235,165.20	248,964.17	5.87	2	2,253.45	3,986.02	0- 67
9	Railways	126	64,413.89	141,917.43	120.32	15	8,021.50	21,091.97	1- 141
10	Road Transport & Highways	144	91,164.10	92,540.59	1.51	0	0.00	0.00	0- 0
11	Shipping & Ports	19	16,242.52	17,782.49	9.48	6	6,013.42	7,487.89	5- 87
12	Telecommunications	15	6,161.00	6,101.79	-0.96	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		558	756601.56	900402.69	19.01	38	48056.14	83224.27	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	17- 17
3	Coal	51	33,815.11	37,312.25	10.34	5	7,667.52	9,576.61	19- 45
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	16	50,110.22	71,356.76	42.40	5	9,585.89	13,808.43	2- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	67	157,430.30	166,078.11	5.49	11	19,535.67	34,309.01	19- 120
8	Power	98	235,165.20	248,964.17	5.87	15	39,917.50	53,103.33	7- 99
9	Railways	126	64,413.89	141,917.43	120.32	32	13,972.11	54,047.24	1- 216
10	Road Transport & Highways	144	91,164.10	92,540.59	1.51	9	2,946.51	4,865.26	18- 99
11	Shipping & Ports	19	16,242.52	17,782.49	9.48	7	7,365.57	8,958.14	5- 87
12	Telecommunications	15	6,161.00	6,101.79	-0.96	2	1,065.85	1,089.32	22- 39
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	15- 15
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		558	756601.56	900402.69	19.01	90	124108.03	212148.34	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		Final
S.no	Project	DOA	Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>							
1	WESTERN REGION SYSTEM STRENGHTENING SCHEME-XI	02/2009	409.50	02/2012	409.50	07/2012	123.50
<u>Railways</u>							
2	RAJPIPLA-ANKELASHWAR, WR (GC)	04/2006	196.97	03/2011	196.97	07/2012	218.66

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
<u>Civil Aviation</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT	2/2011	452.00	2/2015	452.00	2/2015
<u>Petroleum</u>						
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN	8/2009	246.81	4/2012	246.81	4/2012
3	Butene-1 at Panipat	2/2012	190.00	3/2014	190.00	3/2014
<u>Power</u>						
4	KUDGI STPP STAGE 1	12/2011	15,166.19	12/2016	15,166.19	12/2016
5	MOUDA STPP STAGE 2	3/2012	7,921.47	9/2016	7,921.47	9/2016
6	SOLAPUR STPP	3/2012	9,395.18	11/2016	9,395.18	11/2016

VII. Milestones (Cumulative due & achieved)

Total	3302
Achieved up to month	1218


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay
		Original	Anticipated	Original	Last month	This month	(in months)
	<u>Steel</u>						
1	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	10/2012	10/2012	12/2012	2
2	EXPANSION OF BHILAI STEEL PLANT SAIL	5,185.00	17,265.00	N.A.	06/2013	09/2013	3
3	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2011	09/2012	12/2012	3
4	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES SAIL	254.55	254.55	N.A.	11/2013	03/2014	4
5	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,291.00	10/2009	10/2012	03/2013	5
	<u>Petroleum</u>						
6	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA ONGC	370.11	370.11	04/2011	07/2012	08/2012	1
7	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	330.47	03/2012	08/2012	09/2012	1
8	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2013	05/2013	2
9	CONSTRUCTION OF NEW PROCESS COMPLEX MHN ONGC	2,853.29	6,326.40	05/2010	07/2012	10/2012	3
10	PARADIP REFINERY PROJECT IOCL	29,777.00	30,426.00	N.A.	06/2013	09/2013	3
11	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) GAIL	540.92	400.00	07/2012	03/2013	06/2013	3
12	DEV OF G1 AND GS-15 (ONGCL) ONGC	429.82	2,735.65	04/2006	12/2012	04/2013	4
13	Development of SB-14 field ONGC	410.44	410.44	11/2012	05/2013	10/2013	5
14	Construction of 6 ETPs ONGC	302.26	240.95	09/2012	12/2012	06/2013	6
15	102 MW WIND POWER PROJECT ONGC	1,106.00	820.00	06/2012	04/2013	10/2013	6
16	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	288.04	08/2012	08/2012	03/2013	7
17	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2012	08/2013	8
18	DEVELOPMENT OF B-46 CLUSTER FIELD ONGC	1,436.21	1,436.21	07/2010	07/2012	05/2013	10
19	Development of Cluster-7 Fields ONGC	3,241.03	3,241.03	03/2013	04/2013	04/2014	12
	<u>Power</u>						
20	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIII PGCIL	317.69	317.69	11/2011	07/2012	08/2012	1
21	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	386.32	07/2011	09/2012	10/2012	1
22	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XVIII PGCIL	509.66	509.66	11/2011	03/2013	12/2013	9
23	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX PGCIL	410.29	410.29	02/2012	03/2013	12/2013	9


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Railways</u>						
24	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR ECR	233.00	1,043.56	03/2012	08/2012	02/2013	6
	<u>Road Transport & Highways</u>						
25	HARANGAJO TO MAIBANG,km 164.08- 190.587 NH-54 NHAI	212.00	212.00	09/2007	04/2014	05/2014	1
26	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	280.00	280.00	02/2009	03/2013	05/2014	14
	<u>Shipping & Ports</u>						
27	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER MUMBAI PORT TRU	1,228.00	1,460.00	12/2010	03/2013	10/2013	7
	<u>Telecommunications</u>						
28	GSM equipment of 799000Lines (2G) 101000 lines 3(G BSNL	328.13	328.12	03/2009	06/2012	09/2012	3

Trend and Graphical Analysis of All Projects

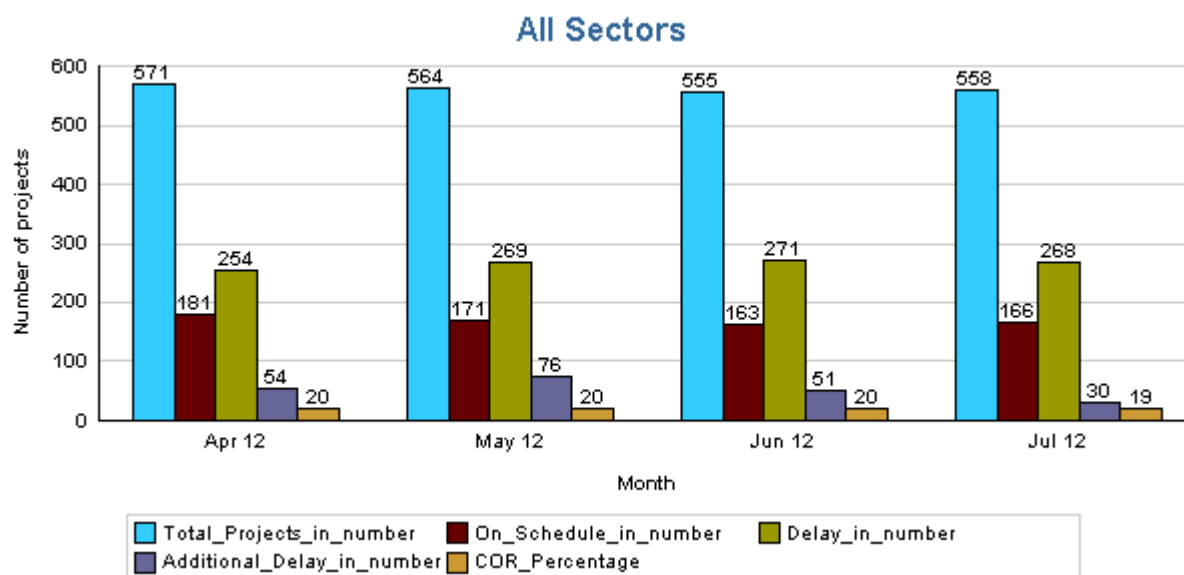


All Sectors Break-up of 268 Delayed projects in July 2012

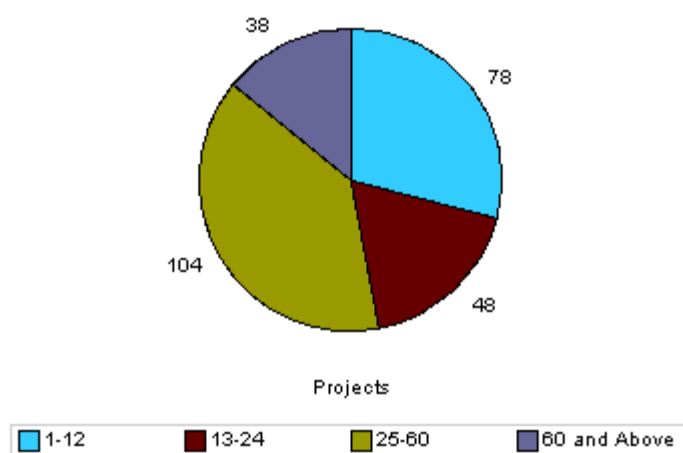


Trend and Graphical Analysis


Urban Development Sector

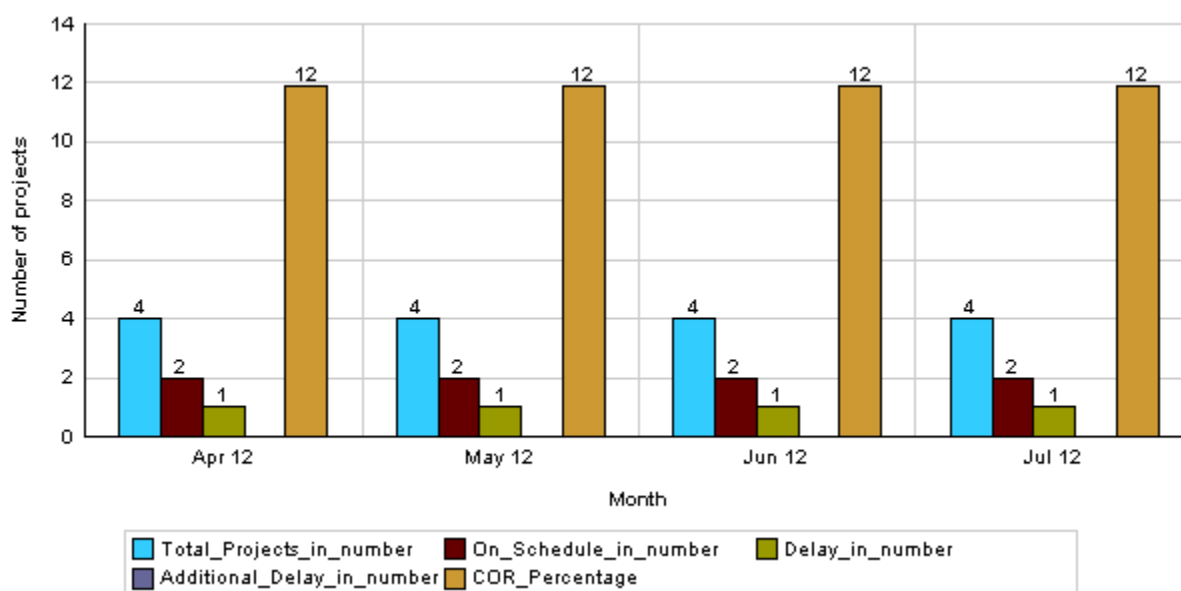


Urban Development Sector Break-up of 1 Delayed projects in July 2012

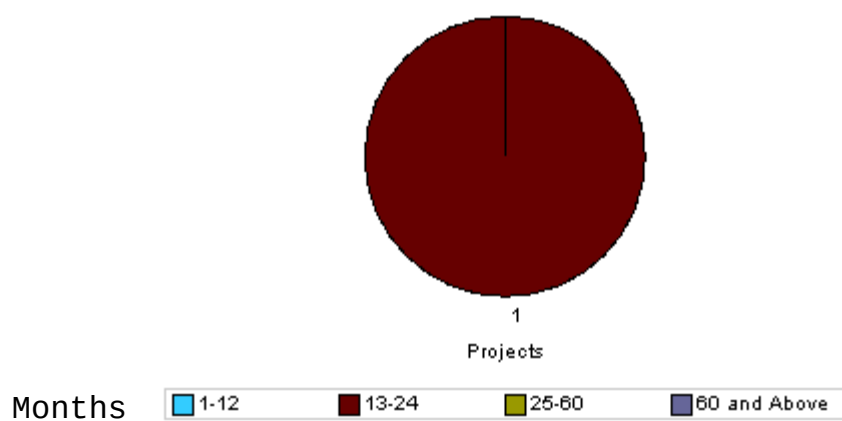


Trend and Graphical Analysis Telecommunications Sector

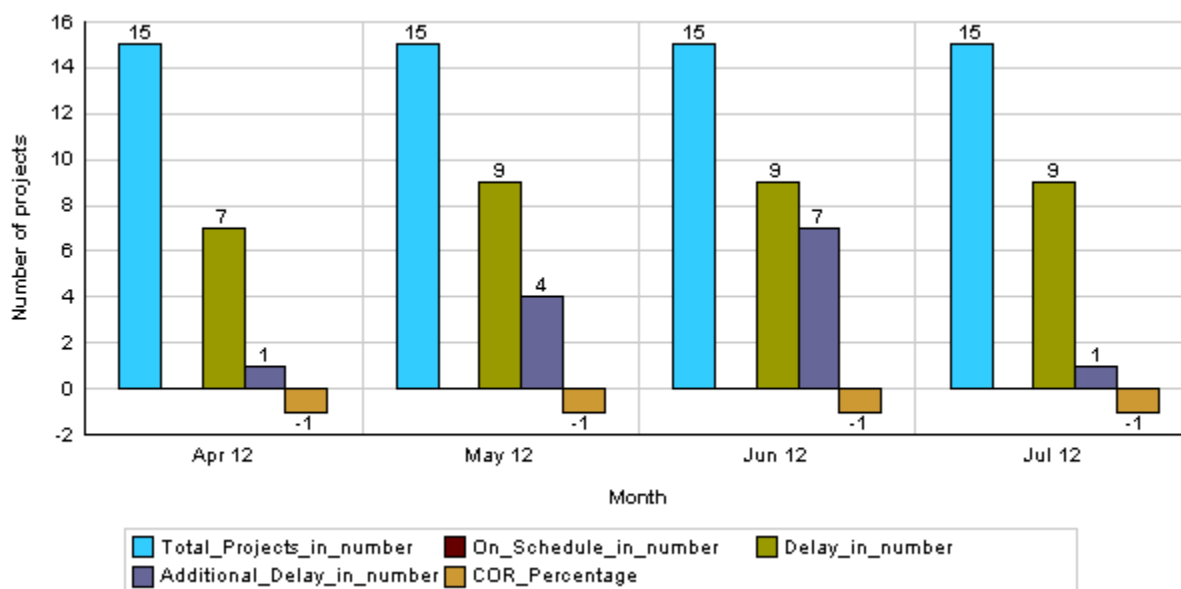


Telecommunications Sector Break-up of 9 Delayed projects in July 2012

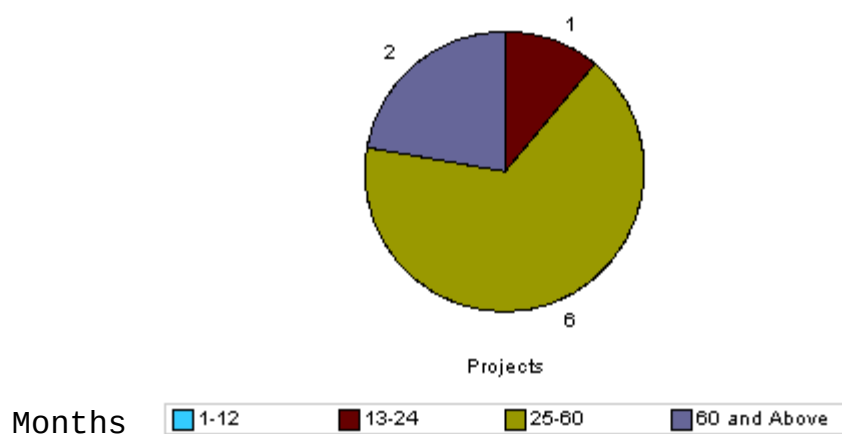


Trend and Graphical Analysis Shipping and Ports Sector

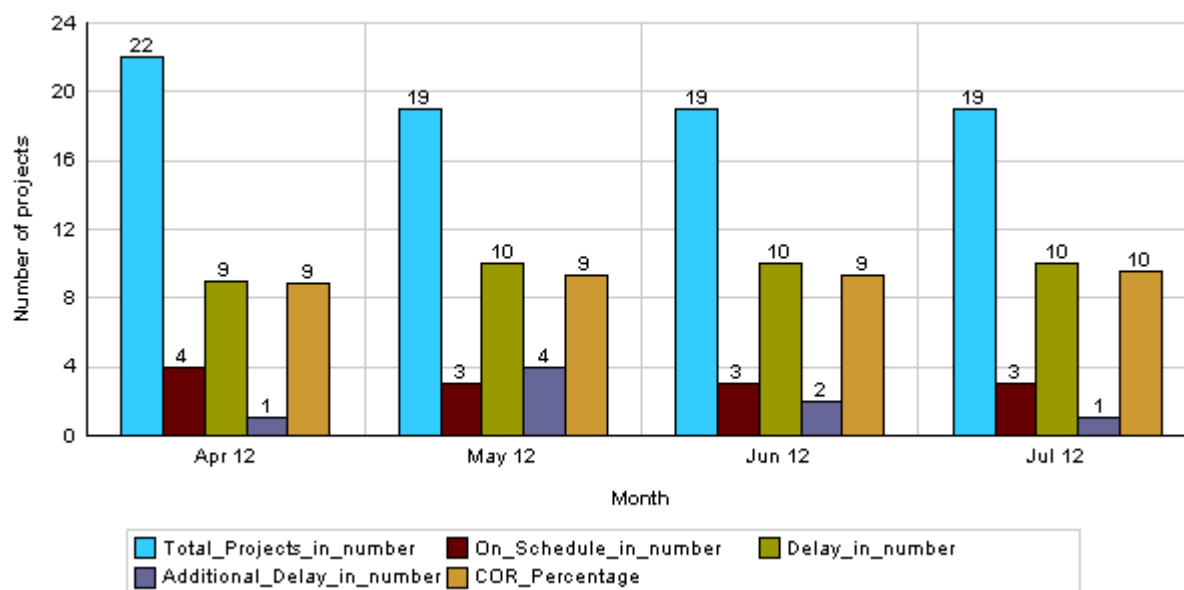


Sector Break-up of 10 Delayed projects in July 2012

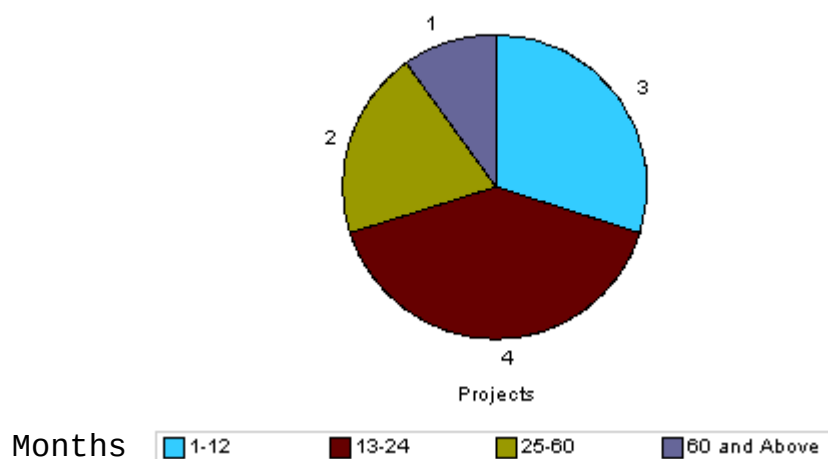

Trend and Graphical Analysis Road Transport and Highways Sector

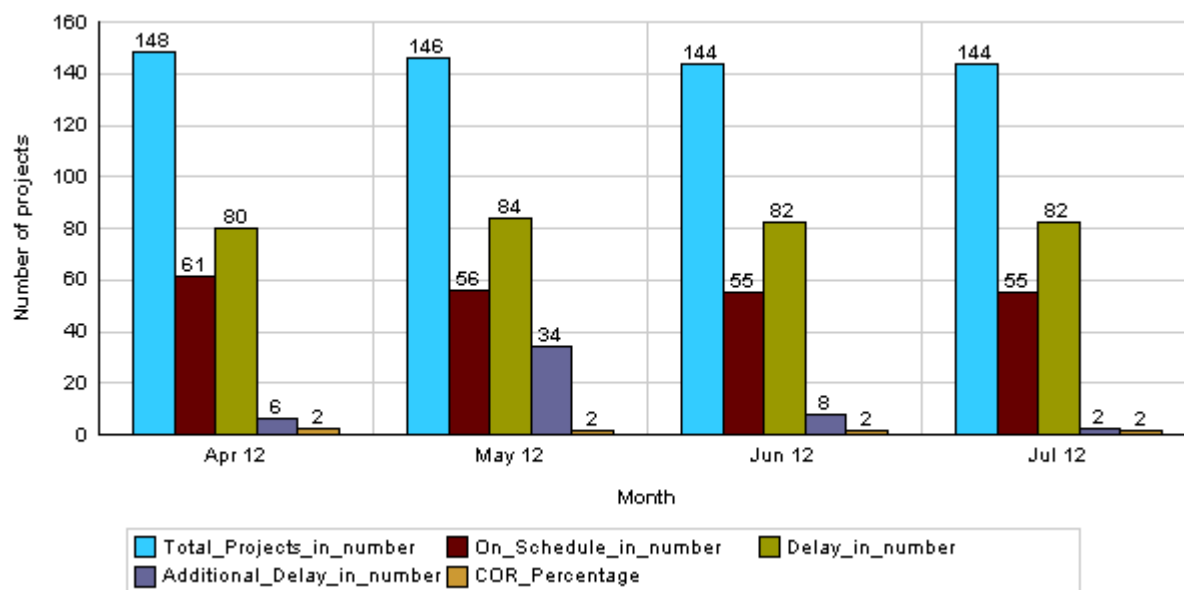


Sector Break-up of 82 Delayed projects in July 2012

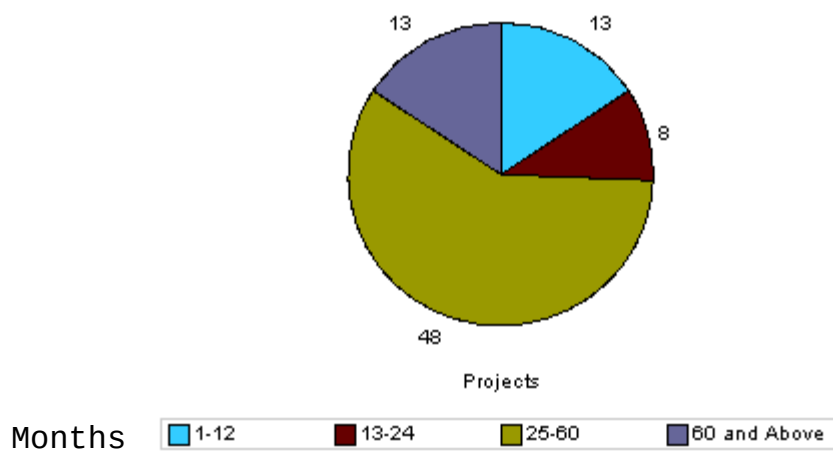


Trend and Graphical Analysis

Railways Sector

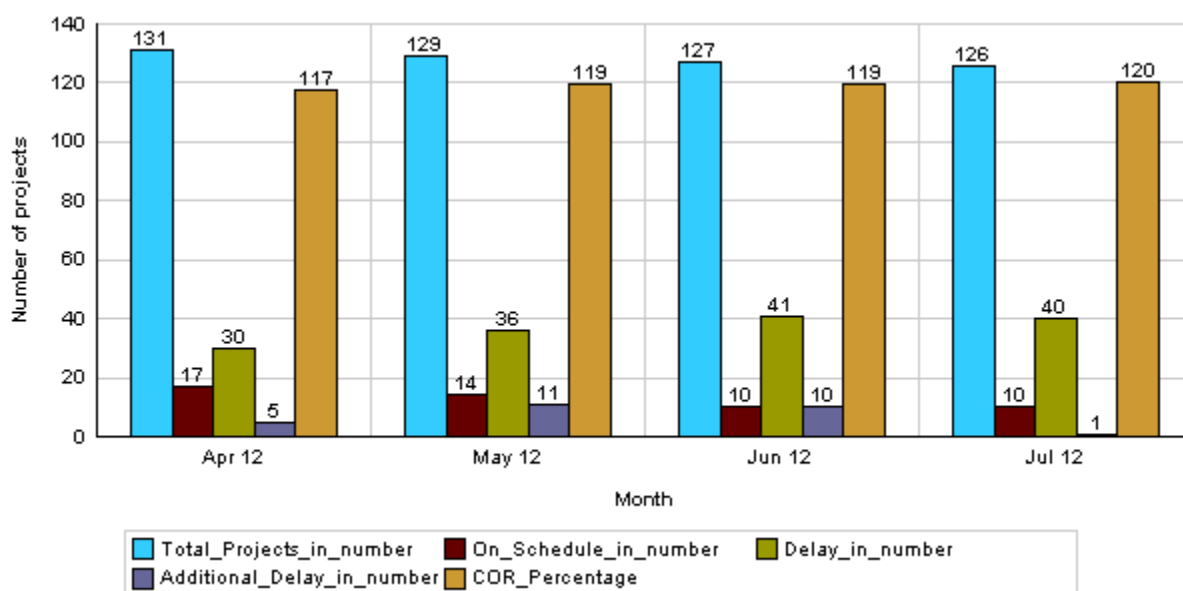


Railways Sector Sector Break-up of 40 Delayed projects in July 2012

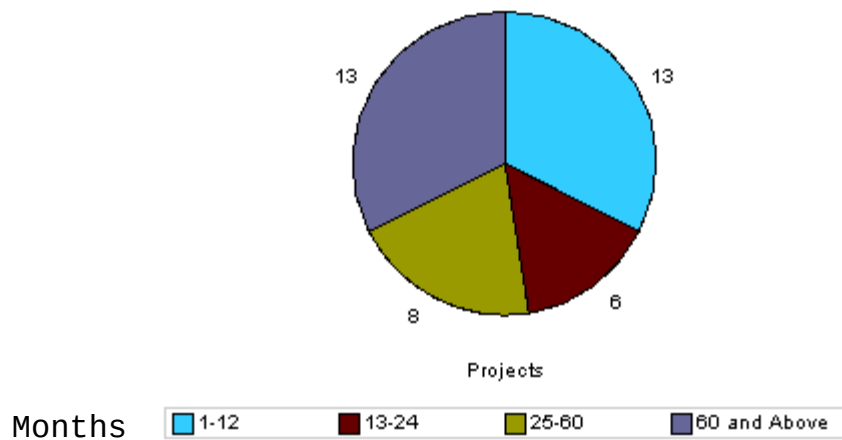


Trend and Graphical Analysis

Power Sector

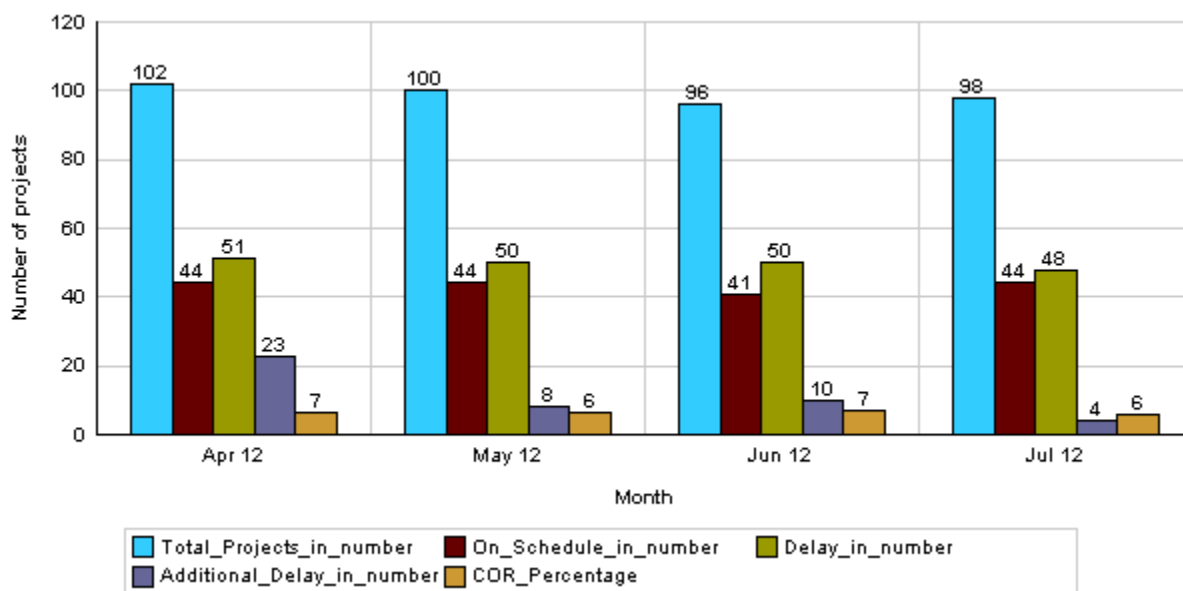


Power Sector Sector Break-up of 48 Delayed projects in July 2012

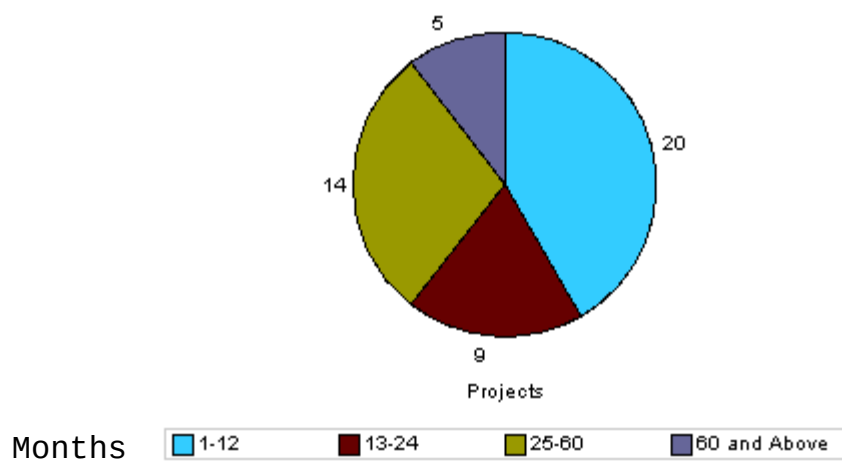


Trend and Graphical Analysis

Petroleum Sector

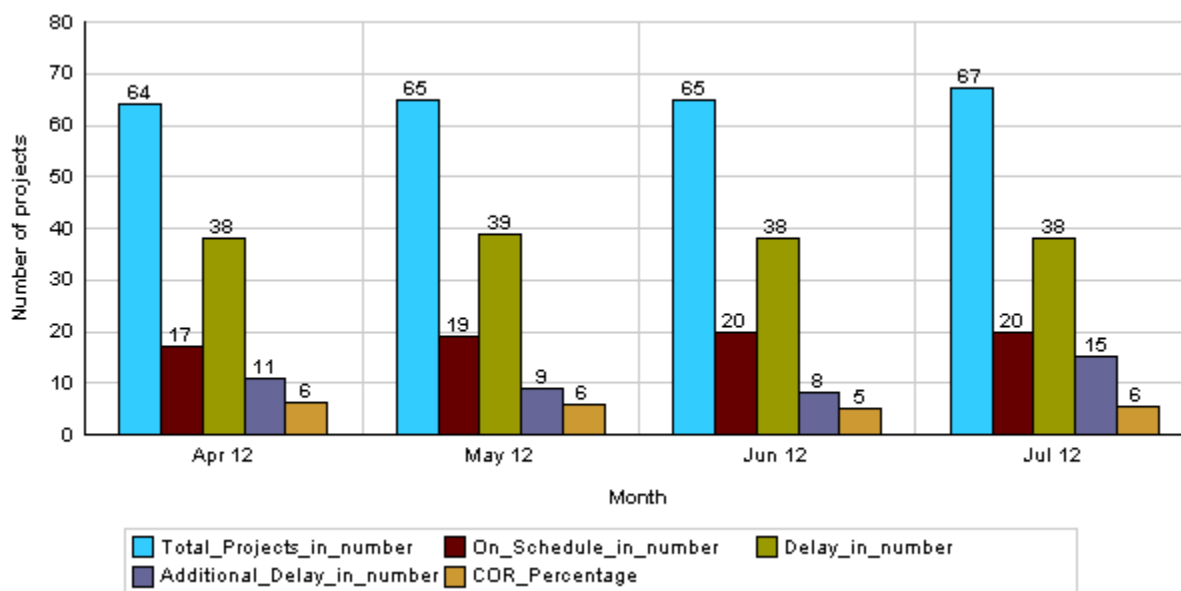


Petroleum Sector Sector Break-up of 38 Delayed projects in July 2012

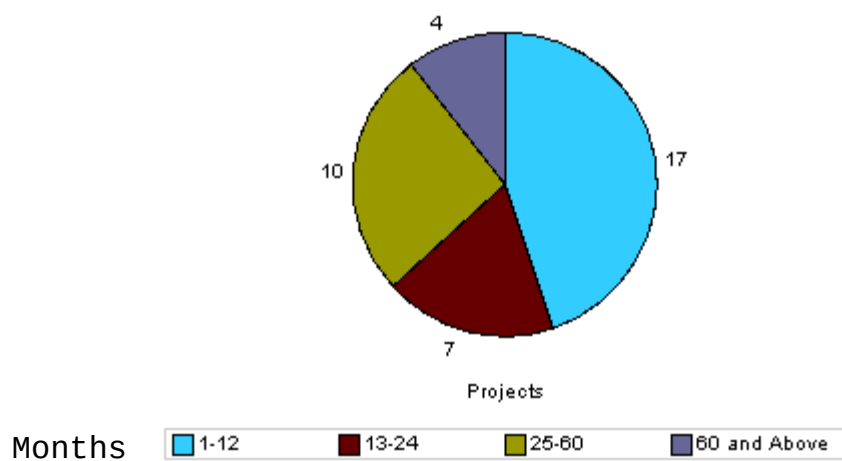


Trend and Graphical Analysis

Steel Sector

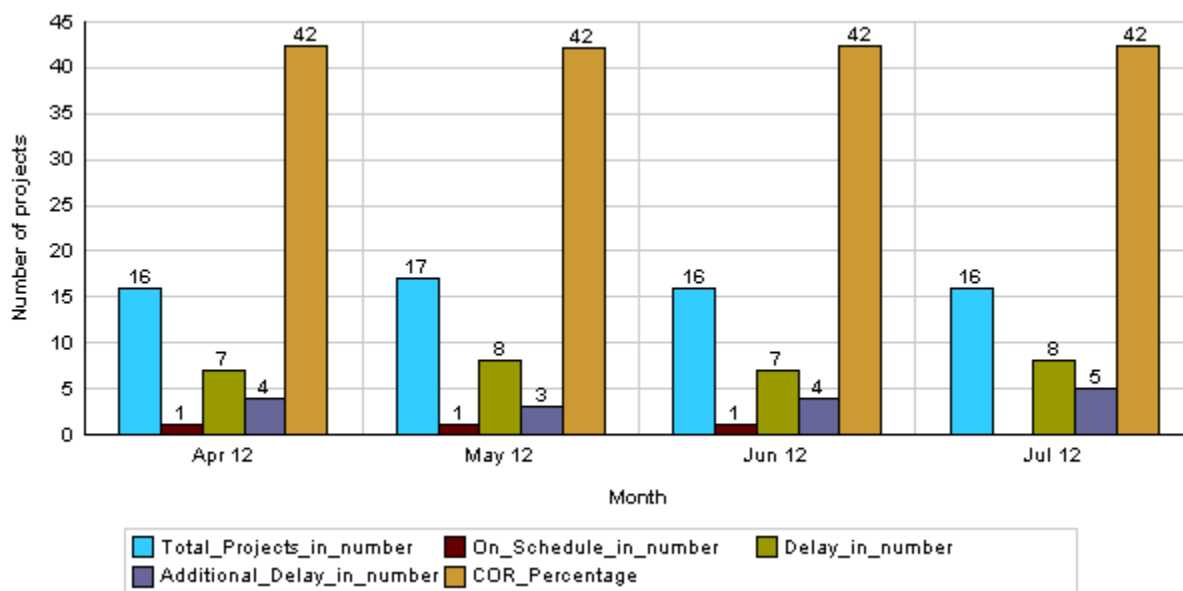


Steel Sector Sector Break-up of 8 Delayed projects in July 2012

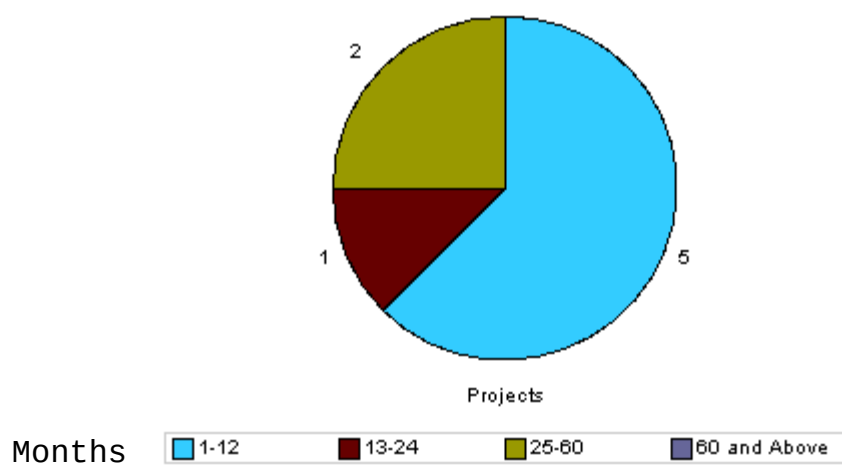


Trend and Graphical Analysis

Fertilisers Sector

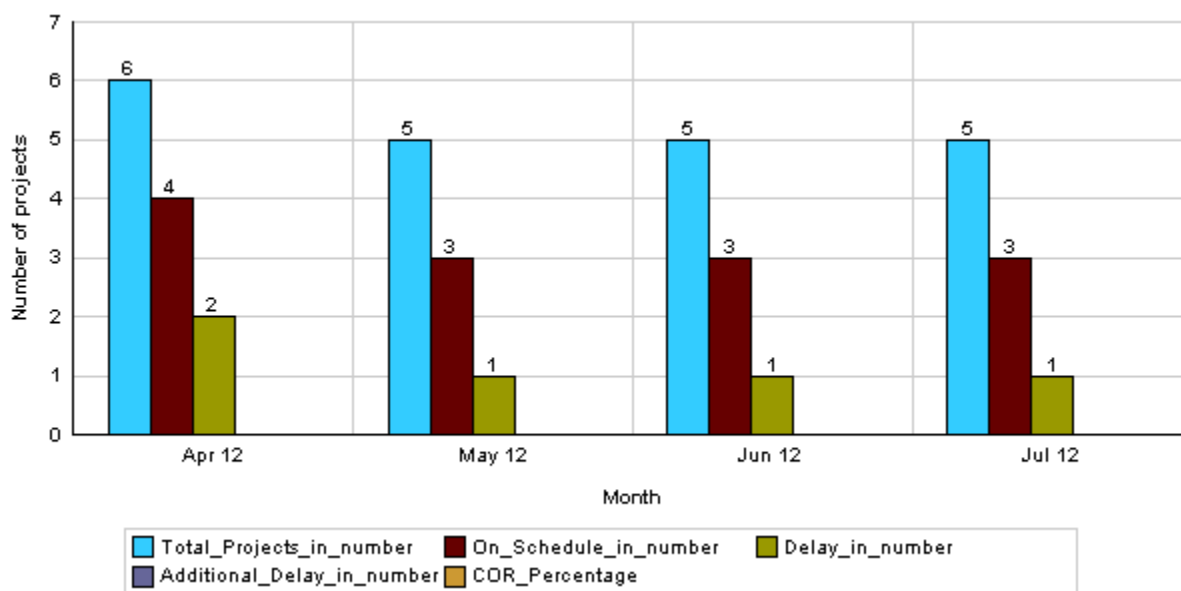


Fertilisers Sector Break-up of 1 Delayed projects in July 2012

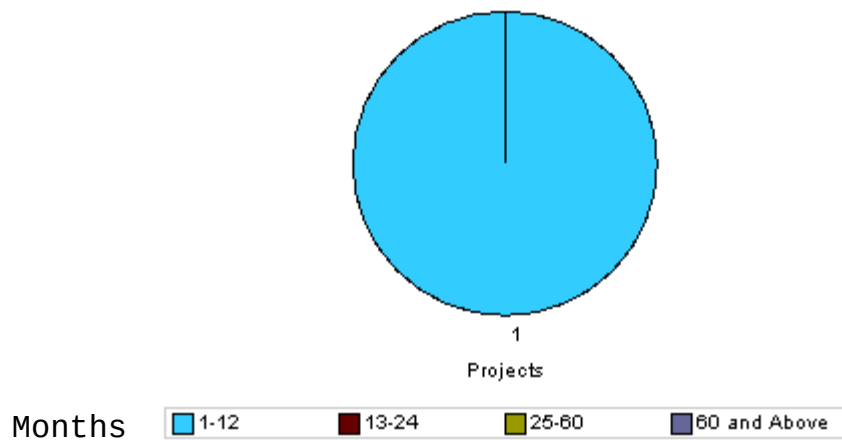


Trend and Graphical Analysis

Coal Sector

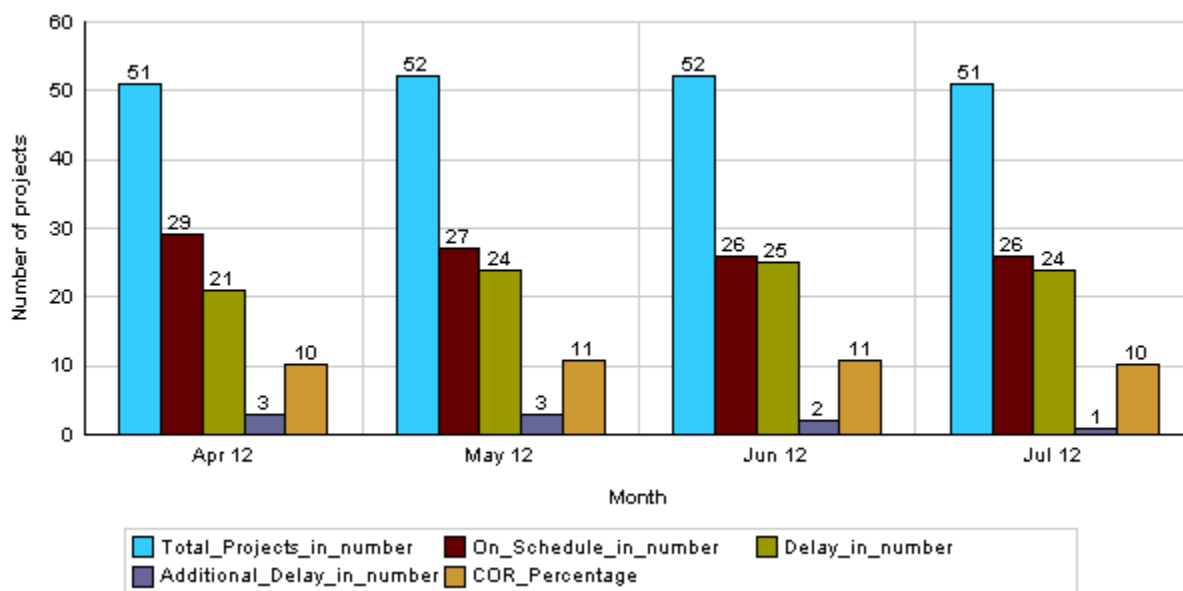


Coal Sector Sector Break-up of 24 Delayed projects in July 2012

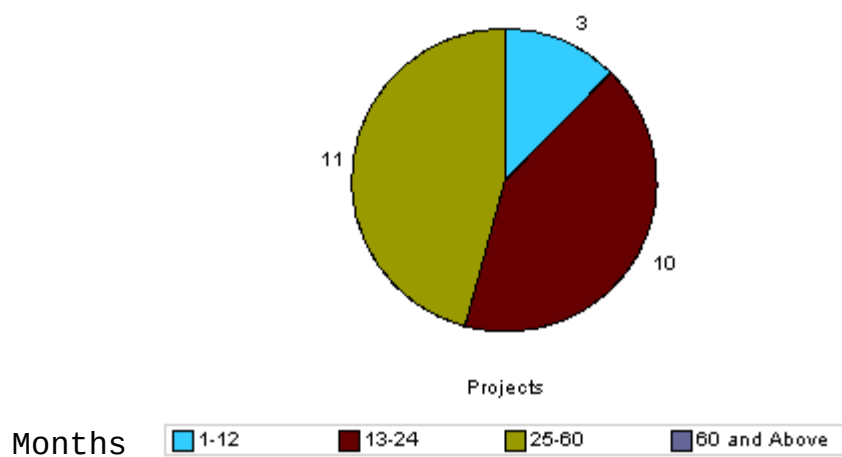


Trend and Graphical Analysis

Civil Aviation Sector

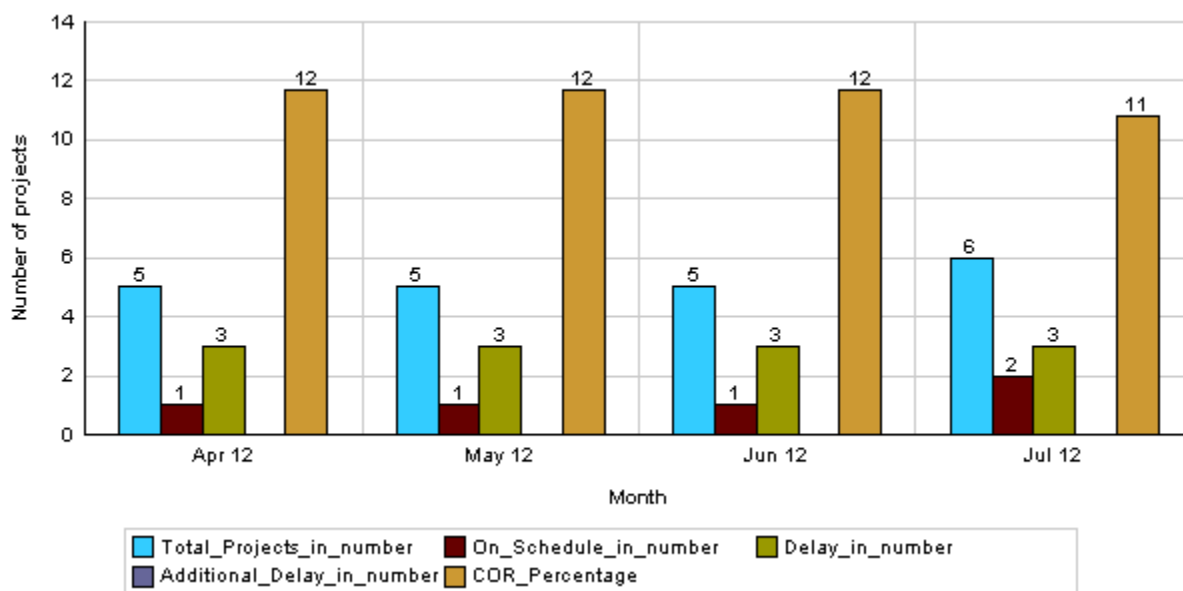


Civil Aviation Sector Sector Break-up of 3 Delayed projects in July 2012

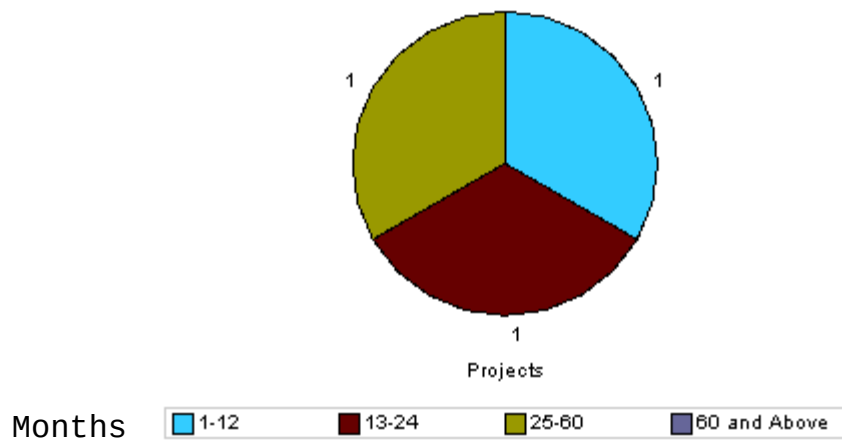


Trend and Graphical Analysis

Atomic Energy Sector

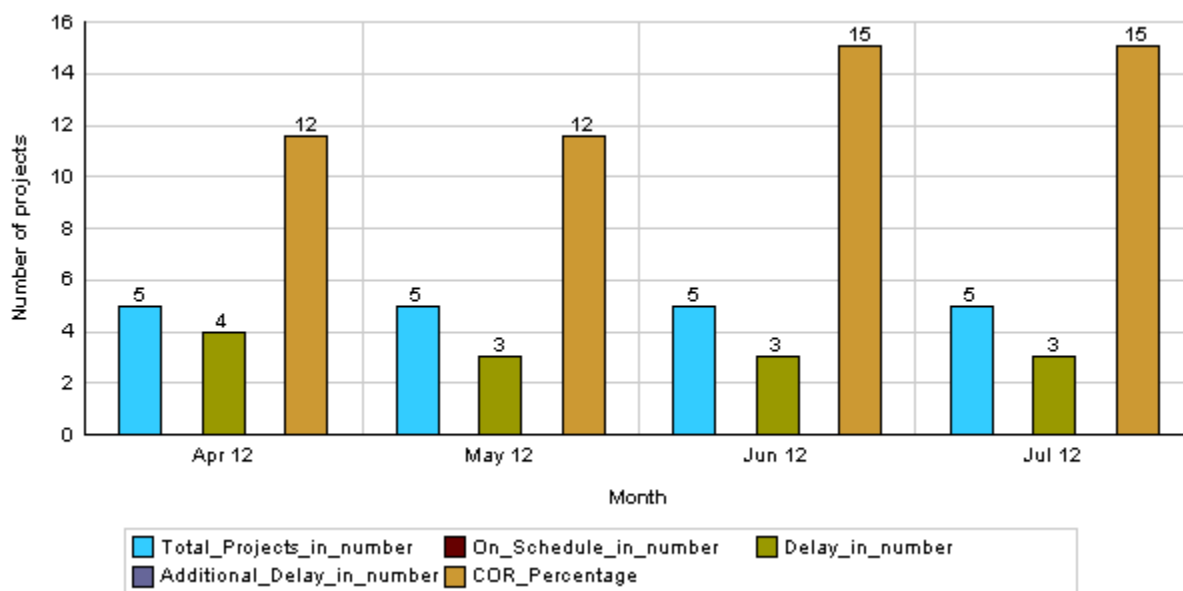

Atomic Energy Sector Sector Break-up of 3 Delayed projects in July 2012

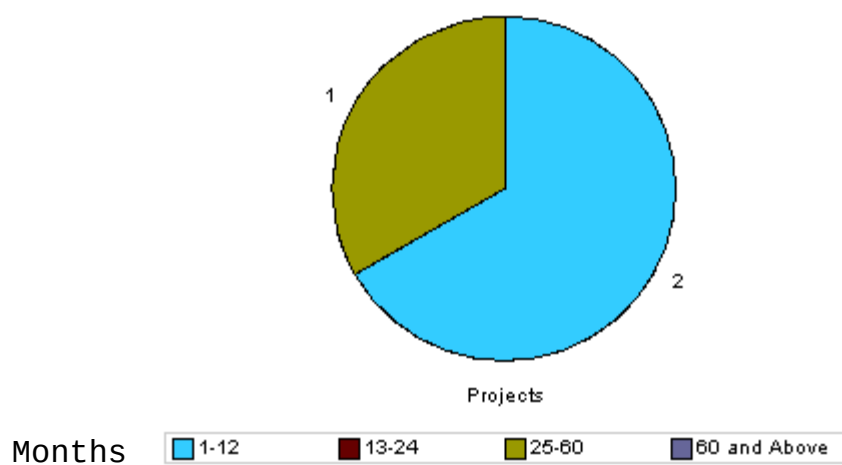

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	22,560.84
Civil Aviation	6	5,473.58	5,680.58	6,063.07	4,376.22
Coal	51	33,815.11	34,781.11	37,312.25	12,383.49
Fertilisers	5	4,828.66	4,828.66	4,828.66	2,609.90
Steel	16	50,110.22	55,985.50	71,356.76	42,373.18
Petrochemicals	1	5,460.61	8,920.00	8,920.00	5,090.47
Petroleum	67	157,430.30	171,255.95	166,078.11	75,644.41
Power	98	235,165.20	238,972.30	248,964.17	107,643.65
Railways	126	64,413.89	88,855.64	141,917.43	61,047.11
Road Transport & Highways	144	91,164.10	91,330.60	92,540.59	61,500.70
Shipping & Ports	19	16,242.52	17,629.04	17,782.49	7,642.95
Telecommunications	15	6,161.00	6,164.88	6,101.79	1,784.59
Urban Development	4	44,245.18	44,304.08	49,518.08	2,750.78
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	558	756,601.56	810,799.53	900,402.69	407,443.78

Sector Wise Details

(Jul,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,826.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	14,886.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,641.60	09/2010	01/2012	-	6/80
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,123.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011 04/2011	04/2012	-	0/0
Total			41,548.29	47,832.29	22,560.84				45/325
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,025.63	05/2011 03/2012	10/2012	17(O) 7(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	183.01	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	124.35	05/2012	08/2012	3(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,669.98	01/2011 02/2012	02/2012	-	0/0
10	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT - [N04000070]AAI,Punjab	02/2011	452.00	452.00	1.20	02/2015	02/2015	0(O)	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	372.05	06/2013	06/2013	0(O)	0/0
Total			5,473.58	6,063.07	4,376.22				0/0
<u>Coal</u>									
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	301.72	03/2013 09/2012	10/2014	19(O) 25(R)	7/22
13	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59	198.59	70.19	03/2016	03/2016	0(O)	2/6

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	338.98	03/2014 03/2016	03/2016	24(O) 0(R)	2/2
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	100.28	03/2012 -	03/2014	24(O) -	5/7
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	108.26	03/2011 -	03/2013	24(O) -	0/2
17	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	117.82	03/2010 -	03/2015	60(O) -	4/4
18	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	39.30	03/2016 -	03/2016	0(O) -	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	114.45	03/2017 -	03/2017	0(O) -	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.35	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	161.94	03/2012 03/2015	03/2015	36(O) 0(R)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	261.91	03/2014 -	03/2016	24(O) -	2/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	34.45	03/2011 -	03/2014	36(O) -	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,197.18	03/2014 -	03/2014	0(O) -	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,370.35	03/2014 -	03/2014	0(O) -	10/15
27	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	71.35	03/2015 -	03/2015	0(O) -	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	107.59	03/2013 -	03/2013	0(O) -	5/7
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48(O) -	0/1
33	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	72.66	12/2012 -	03/2015	27(O) -	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	110.35	03/2013 -	03/2013	0(O) -	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	30.89	03/2014 -	03/2014	0(O) -	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/6

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	333.97	03/2010 -	03/2013	36(O) -	2/2
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	105.28	03/2010 -	03/2014	48(O) -	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	645.16	03/2013 -	03/2013	0(O) -	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 -	706.40	19.23	07/2012 -	03/2016	44(O) -	1/2
43	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	321.50	203.55	03/2014 -	03/2014	0(O) -	1/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	38.14	03/2012 -	03/2013	12(O) -	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	21.14	12/2015 -	12/2015	0(O) -	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36(O) -	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	60.69	03/2012 -	03/2014	24(O) -	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2016	24(O) -	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	87.76	03/2013 -	03/2013	0(O) -	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	25.44	03/2011 -	03/2014	36(O) -	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	95.40	03/2012 -	03/2013	12(O) -	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.49	03/2015 -	03/2015	0(O) -	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	25.93	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	268.19	03/2016 -	03/2016	0(O) -	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	47.23	03/2012 -	03/2012	-	11/42

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	45.39	03/2016	03/2016	0(O)	1/12
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,447.14	06/2009	03/2013	45(O)	19/24
61	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,141.68	03/2012	03/2014	24(O)	0/39
62	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	104.51	03/2012	03/2013	12(O)	0/2
	Total		33,815.11	37,312.25	12,383.49				166/634
	Fertilisers								
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	697.34	01/2013	01/2013	0(O)	0/5
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	239.93	07/2011	07/2012	12(O)	0/0
65	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	185.10	07/2011	04/2012	-	0/0
66	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	769.86	01/2013 01/2013	01/2013	0(O) 0(R)	8/8
67	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	717.67	01/2013	01/2013	0(O)	0/5
	Total		4,828.66	4,828.66	2,609.90				8/18
	Steel								
68	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	149.17	-	04/2013	-	10/19
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	246.19	08/2010 08/2010	10/2012	26(O) 26(R)	0/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	248.53	02/2011 02/2011	12/2012	22(O) 22(R)	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	82.45	-	05/2013	-	8/21
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	205.20	05/2012 05/2012	02/2013	9(O) 9(R)	1/2
73	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	332.15	12/2011 03/2012	10/2012	10(O) 7(R)	16/21
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	91.83	10/2012 10/2012	12/2012	2(O) 2(R)	3/4

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
75	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55 -	254.55	6.32	- -	03/2014	- -	0/1
76	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00 -	17,265.00	6,043.92	- -	09/2013	- -	19/27
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	3,316.00 -	6,325.00	2,824.12	- -	10/2012	- -	10/16
78	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	1,027.62	12/2012 -	03/2013	3(O) -	7/12
79	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,558.10	- -	12/2012	- -	16/19
80	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,661.03	10/2009 03/2013	03/2013	41(O) 0(R)	60/64
81	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	11,812.00 11,812.00	11,812.00	7,541.34	11/2013 -	03/2013	-8(O) -	6/14
82	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL, Maharashtra	12/2011	187.33 -	187.33	-	10/2013 -	12/2013	2(O) -	0/0
83	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL, Jharkhand	10/2007	500.90 -	500.90	355.21	- -	02/2012	-	3/3
Total			50,110.22 -	71,356.76	42,373.18				161/227
<u>Petrochemicals</u>									
84	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	5,090.47	12/2013 12/2013	12/2013	0(O) 0(R)	13/29
Total			5,460.61 -	8,920.00	5,090.47				13/29
<u>Petroleum</u>									
85	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	10/2013	16(O) -	0/0
86	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	1,140.31	06/2012 -	12/2012	6(O) -	0/0
87	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	227.95	04/2011 -	08/2012	16(O) -	0/0
88	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	411.99	12/2011 -	01/2013	13(O) -	0/0
89	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	870.16	03/2013 -	03/2014	12(O) -	0/0
90	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	33.22	12/2014 -	12/2014	0(O) -	0/0
91	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	4.84	12/2014 -	12/2014	0(O) -	0/0
92	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	400.00	250.00	07/2012 07/2012	06/2013	11(O) 11(R)	0/16

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	104.66	02/2013 -	02/2013	0(O) -	34/42
94	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00 -	190.00	4.54	03/2014 -	03/2014	0(O) -	0/0
95	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	163.73	- -	09/2012	- -	33/36
96	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	719.92	04/2011 12/2011	09/2012	17(O) 9(R)	2/2
97	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	08/2013	23(O) -	0/0
98	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,553.85	05/2010 05/2012	10/2012	29(O) 5(R)	0/0
99	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	349.29	- 08/2011	-	-	0/22
100	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	0.20	01/2014 -	01/2014	0(O) -	0/0
101	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	5.73	05/2013 -	05/2013	0(O) -	0/0
102	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5(O) -	0/0
103	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	43.73	09/2012 -	06/2013	9(O) -	0/0
104	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
105	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	201.71	09/2012 09/2012	09/2012	0(O) 0(R)	0/0
106	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,775.82	03/2012 08/2012	08/2012	5(O) 0(R)	0/17
107	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	19.54	- -	-	-	0/0
108	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	04/2013	84(O) 10(R)	0/0
109	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,739.13	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
110	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,279.74	09/2010 03/2012	04/2013	31(O) 13(R)	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	865.55	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
112	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
113	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,061.76	09/2012 09/2012	09/2012	0(O) 0(R)	0/76
114	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,282.33	09/2011 03/2012	09/2012	12(O) 6(R)	0/0
115	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	59.59	03/2013 -	04/2013	1(O) -	0/0
116	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
117	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	345.62	03/2013 -	04/2014	13(O) -	0/0
118	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	46.52	11/2012 -	10/2013	11(O) -	0/0
119	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	153.52	01/2014 -	01/2014	0(O) -	0/0
120	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
121	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,923.37	- -	08/2012	- -	114/116
122	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	162.48	01/2013 -	01/2013	0(O) -	17/18
123	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	611.55	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
124	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015	0(O) -	0/0
125	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,162.58	06/2012 03/2013	06/2012	-	8/8
126	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
127	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
128	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
129	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015	0(O) -	0/0
130	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30(O) -	0/0
131	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.48	10/2010 -	12/2014	50(O) -	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
132	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 276.00	276.00	180.54	- -	09/2012	- -	0/1
133	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	987.59	12/2012 12/2012	04/2013	4(O) 4(R)	0/21
134	KOCHI-KOOTTANAD BANGLORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	194.79	03/2012 08/2012	08/2012	5(O) 0(R)	2/4
135	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,887.74	01/2012 -	09/2012	8(O) -	0/0
136	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,930.41	09/2012 -	09/2013	12(O) -	0/0
137	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,987.43	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
138	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	5.67	04/2015 -	04/2015	0(O) -	0/0
139	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19(O) 17(R)	0/0
140	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
141	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	16,808.86	- 09/2013	09/2013	- 0(R)	60/100
142	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	670.64	09/2012 -	09/2012	0(O) -	0/11
143	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	1,292.50	02/2014 -	02/2014	0(O) -	0/0
144	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	246.81	184.00	04/2012 -	04/2012	-	0/0
145	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	-	05/2014 -	05/2014	0(O) -	0/0
146	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	600.66	07/2012 -	10/2012	3(O) -	0/0
147	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	898.00	887.01	- 03/2012	08/2012	- 5(R)	0/53
148	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	656.90	05/2010 04/2012	07/2012	26(O) 3(R)	0/0
149	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012 -	03/2013	7(O) -	0/0
150	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	215.65	03/2012 -	09/2012	6(O) -	13/20

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	576.60	56.65	12/2013	12/2013	0(O) 0(R)	0/0
	Total		157,430.30	166,078.11	75,644.41				298/745
	Power								
152	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	5,196.70	08/2012	03/2013	7(O) -	0/11
153	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,047.91	02/2012	10/2012	8(O) -	0/7
154	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	624.86	05/2012	12/2012	7(O) -	0/11
155	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	952.10	06/2012	12/2012	6(O) -	0/4
156	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	4,416.00	08/2013	06/2014	10(O) -	5/19
157	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	7,201.00	12/2009 12/2014	03/2016	75(O) 15(R)	26/47
158	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,199.00	07/2011	11/2014	40(O) -	4/28
159	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	746.85	02/2011 10/2012	10/2012	20(O) 0(R)	2/4
160	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	210.06	08/2014	08/2014	0(O) -	0/20
161	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44	206.44	22.14	06/2014	06/2014	0(O) -	0/20
162	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	215.39	09/2014	09/2014	0(O) -	0/20
163	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	867.25	10/2009	12/2012	38(O) -	20/20
164	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	354.19	- -	09/2013	- -	3/11
165	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O) -	0/0
166	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	345.81	05/2014	05/2014	0(O) -	0/16

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	541.68	08/2013	08/2013	0(O)	0/14
168	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77	901.77	52.80	08/2014	08/2014	0(O)	0/21
169	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	279.01	12/2013	12/2013	0(O)	0/0
170	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	279.01	12/2013	12/2013	0(O)	0/13
171	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	45.26	10/2012	03/2013	5(O)	0/15
172	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	1,007.16	840.20	12/2007	-	-	0/10
173	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,905.06	05/2013	03/2017	46(O) 9(R)	4/22
174	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67	3,642.00	1,593.45	01/2016	11/2016	10(O) 10(R)	0/2
175	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	4,373.00	04/2009	03/2014	59(O) 0(R)	0/9
176	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19	15,166.19	939.00	12/2016	12/2016	0(O)	0/0
177	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	2,159.07	1,830.60	09/2008	12/2012	51(O)	17/37
178	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,263.00	08/2012	03/2013	7(O)	10/16
179	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47	7,921.47	296.00	09/2016	09/2016	0(O)	0/0
180	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	779.27	08/2010	01/2013	29(O) 0(R)	0/3
181	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	4,888.35	08/2013	09/2014	13(O)	0/17
182	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	183.98	11/2011	08/2012	9(O)	0/7
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	235.36	02/2012	12/2013	22(O)	0/14
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	314.26	11/2011	03/2013	16(O)	0/11
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	326.72	11/2011	12/2013	25(O)	0/14

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	46.24	01/2013 -	01/2013	0(O) -	0/7
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	182.17	07/2013 -	07/2013	0(O) -	0/12
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	469.25	04/2013 -	10/2013	6(O) -	0/12
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	63.88	08/2013 -	08/2013	0(O) -	0/16
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	40.40	11/2014 -	11/2014	0(O) -	0/0
191	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	427.61	11/2012 -	03/2013	4(O) -	0/10
192	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,877.52	10/2010 01/2013	01/2013	27(O) 0(R)	0/0
193	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,505.23	09/2009 07/2014	12/2017	99(O) 41(R)	1/20
194	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	357.17	08/2012 08/2013	09/2014	25(O) 13(R)	14/19
195	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,865.80	01/2012 -	09/2013	20(O) -	0/0
196	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,373.00	10/2012 -	03/2013	5(O) -	10/16
197	SIPAT STTP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	8,230.00	12/2009 12/2011	06/2012	-	59/60
198	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	628.00	11/2016 -	11/2016	0(O) -	0/0
199	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,703.24	09/2010 08/2014	12/2016	75(O) 28(R)	11/11
200	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	40.73	04/2013 -	04/2013	0(O) -	0/15
201	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,933.44	08/2012 -	03/2013	7(O) -	0/7
202	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	136.48	07/2011 -	08/2012	13(O) -	0/5
203	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/0
204	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	47.90	08/2014 -	08/2014	0(O) -	0/20

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
205	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	102.90	02/2015	02/2015	0(O)	0/0
206	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	1,263.26	-	11/2014	11/2014	0(O)	0/0
207	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	102.40	01/2015	01/2015	0(O)	0/19
208	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	22.17	08/2014	08/2014	0(O)	0/20
209	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	54.95	06/2014	06/2014	0(O)	0/19
210	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	134.40	04/2012	04/2012	-	0/0
211	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	109.98	06/2012	08/2012	2(O)	0/9
212	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	730.80	08/2012	12/2012	4(O)	0/11
213	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,489.00	03/2013	09/2015	30(O)	2/13
214	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,159.82	09/2009 06/2013	08/2013	47(O) 2(R)	0/0
215	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,535.59	03/2007 09/2012	12/2012	69(O) 3(R)	25/25
216	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	337.26	07/2010 02/2016	02/2016	67(O) 0(R)	1/10
217	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	259.28	14.60	01/2014	01/2014	0(O)	0/17
218	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	72.76	08/2014	08/2014	0(O)	0/0
219	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44	3,201.44	-	10/2014	10/2014	0(O)	0/21
220	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	327.05	07/2011	10/2012	15(O)	0/5
221	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,851.57	10/2012	09/2013	11(O)	0/12

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	334.28	01/2015	01/2015	0(O)	0/20
223	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25	2,569.25	526.71	03/2014	03/2014	0(O)	0/15
224	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL, Andhra Pradesh	12/2010	779.21	779.21	472.99	08/2013	08/2013	0(O)	0/14
225	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL, Andhra Pradesh	02/2012	324.33	324.33	1.64	08/2014	08/2014	0(O)	0/20
226	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL, Andhra Pradesh	02/2012	1,927.16	1,927.16	33.16	10/2014	10/2014	0(O)	0/20
227	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL, Himachal Pr.	07/2006	557.24	557.24	550.67	01/2010	02/2013	37(O)	0/22
228	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19	184.19	150.31	11/2011	03/2013	16(O)	0/7
229	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88	7,031.88	3,727.00	12/2012	12/2012	0(O)	0/11
230	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL, Gujarat	12/2011	552.44	552.44	38.53	02/2014	02/2014	0(O)	0/20
231	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya Pradesh	08/2011	425.51	425.51	75.88	10/2013	10/2013	0(O)	0/18
232	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL, Maharashtra	07/2011	181.93	181.93	48.12	07/2013	07/2013	0(O)	0/0
233	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34	1,366.34	173.04	12/2013	12/2013	0(O)	0/18
234	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL, Jharkhand	10/2011	558.26	558.26	63.06	11/2013	11/2013	0(O)	0/20
235	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL, Orissa	09/2010	2,074.86	2,074.86	619.75	03/2013	03/2013	0(O)	0/14
236	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19	2,743.19	709.60	12/2013	12/2013	0(O)	0/13
237	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL, Multi State	03/2010	4,672.99	4,672.99	1,410.14	11/2012	06/2013	7(O)	0/15

Sector Wise Details

(Jul,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total	
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
238	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	209.49	07/2014 -	07/2014	0(O) -	0/19	
239	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	322.19	- 07/2013	07/2013	- 0(R)	5/29	
240	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	338.39	07/2014 -	02/2015	7(O) -	0/16	
241	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	853.62	12/2012 -	03/2013	3(O) -	0/11	
242	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	334.81	11/2013 -	11/2013	0(O) -	0/15	
243	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	53.95	01/2013 -	01/2013	0(O) -	0/16	
244	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,083.00	1,757.40	11/2009 02/2013	02/2013	39(O) 0(R)	0/4	
245	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,614.00	10/2012 -	03/2013	5(O) -	9/15	
246	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	313.27	07/2014 -	05/2016	22(O) -	1/3	
247	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,139.11	07/2010 -	12/2012	29(O) -	20/20	
248	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	406.28	09/2010 -	-	-	0/9	
249	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	27.68	06/2015 -	06/2015	0(O) -	0/24	
Total			235,165.20 -	248,964.17	107,643.65					249/1302
Railways										
250	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	407.49	03/2014 -	03/2014	0(O) -	0/0	
251	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	03/2011	-	0/0	
252	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	165.33	- -	03/2013	- -	0/0	
253	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	453.04	392.26	03/2011 03/2011	03/2011	-	0/0	

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
254	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	523.76	06/1999 03/2011	03/2011	-	0/0
255	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
256	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 -	404.39	0.49	03/2013 -	03/2013	0(O) -	0/0
257	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
258	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	446.94	03/2005 12/2008	06/2016	135(O) 90(R)	0/0
259	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	199.16	12/2010 03/2011	03/2011	-	0/0
260	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	191.38	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
261	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	11.78	04/2014 -	03/2015	11(O) -	0/0
262	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	595.56	03/2010 -	12/2012	33(O) -	0/0
263	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	350.00	319.07	- 03/2009	03/2011	-	0/0
264	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
265	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	134.80	12/2012 -	05/2013	5(O) -	0/0
266	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	181.00	03/2011 -	03/2011	-	0/0
267	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	0.99	03/2012 -	03/2012	-	0/0
268	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
269	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	877.21	12/2012 01/2013	01/2013	1(O) 0(R)	0/0
270	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
271	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
272	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2012	06/2012	-	0/0
273	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	415.73	240.93	- -	03/2012	-	0/0
274	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	110.02	12/2012 -	-	-	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	189.42	- -	03/2013	- -	0/0
276	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	393.46	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
277	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	536.14	- -	12/2012	- -	0/0
278	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	83.30	12/2011 02/2012	02/2012	-	0/0
279	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0
280	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
281	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	155.76	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
282	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	552.50	03/1995 -	03/2013	216(O) -	0/0
283	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.18	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
284	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	47.35	02/2006 -	12/2013	94(O) -	0/0
285	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	559.17	- -	03/2012	-	0/0
286	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
287	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	320.09	- 05/2009	05/2009	-	0/0
288	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	105.94	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
289	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	179.50	- -	03/2015	- -	0/0
290	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	1,185.00	219.71	- 09/2009	12/2011	-	0/0
291	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
292	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	496.59	- -	01/2013	- -	0/0
293	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.43	- -	03/2014	- -	0/0
294	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	166.75	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
295	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.57	- -	-	-	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
296	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	5.83	03/2015 -	03/2015	0(O) -	0/0
297	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	833.20	06/2007 -	06/2007	-	0/0
298	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	651.57	03/2012 08/2012	02/2013	11(O) 6(R)	0/0
299	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	414.03	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
300	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	4,444.00	843.10	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
301	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	137.10	03/2014 -	03/2014	0(O) -	0/0
302	KADUR-CHIKMAGALUR-SAKLESHUPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	231.34	03/2012 03/2012	10/2012	7(O) 7(R)	0/0
303	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,320.26	- -	03/2012	-	0/0
304	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	491.99	- -	03/2014	- -	1/1
305	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	732.04	- -	10/2012	- -	0/0
306	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	730.92	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
307	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	91.50	- -	03/2013	- -	0/0
308	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	210.88	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
309	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	231.46	- -	03/2013	- -	0/0
310	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
311	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 371.36	452.35	410.12	- 03/2010	03/2010	-	0/0
312	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,260.07	07/2005 -	07/2005	-	0/0
313	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	119.78	- -	-	-	0/0
314	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	269.10	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
315	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.20	1,045.20	9.41	- -	-	-	0/0
316	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	341.37	- -	03/2011	-	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
317	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90 227.90	223.01	108.83	12/2012 -	03/2014	15(O) -	0/0
318	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	03/2011	-	0/0
319	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR, Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	-	0/0
320	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, Orissa	04/1993	100.00 142.98	227.94	201.83	03/2002 -	03/2013	132(O) -	0/0
321	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam	04/1996	1,676.31 1,676.31	4,255.37	3,161.45	03/2009 -	12/2013	57(O) -	0/0
322	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
323	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, Bihar	04/2003	218.19 218.19	218.19	164.00	- -	02/2013	-	0/0
324	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, Jharkhand	04/1995	184.00 900.05	900.05	554.16	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
325	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
326	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N220000002]ECR, Bihar	04/1996	114.01 332.92	477.88	388.99	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
327	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR, Tamil Nadu	09/2007	404.19 404.19	900.00	244.55	- -	-	-	0/0
328	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP, Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,334.00	06/2011 03/2012	03/2012	-	0/0
329	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	5,300.00	850.42	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
330	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	645.00	131.21	- -	03/2012	-	0/0
331	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 429.49	883.00	621.61	02/2009 -	03/2012	-	0/0
332	NANGALDAM-TALWARA(NL), NR - [220100188](NR), Multi State	03/1981	37.68 450.00	730.00	367.87	07/2012 07/2012	07/2012	0(O) 0(R)	0/0
333	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR, Bihar	09/2006	300.00 300.00	532.87	39.45	- -	-	-	0/0
334	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR, Assam	09/2006	200.00 200.00	385.20	112.60	- -	03/2014	-	0/0
335	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00 733.00	1,655.81	1,275.88	12/2008 -	03/2014	63(O) -	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	- -	0/0
337	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.44	03/2015 -	03/2015	0(O) -	0/0
338	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	2,913.51	135.97	03/2016 -	03/2016	0(O) -	0/0
339	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	27.66	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
340	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	16.68	03/2016 -	03/2016	0(O) -	0/0
341	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	22.34	03/2016 -	06/2016	3(O) -	0/0
342	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
343	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	355.00	396.62	03/2009 12/2009	03/2011	-	0/0
344	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	225.10	02/2010 -	12/2015	70(O) -	0/0
345	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,484.78	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
346	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	580.85	- -	03/2012	-	0/0
347	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	136.57	12/2010 12/2010	12/2010	-	0/0
348	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	751.22	- -	03/2013	- -	0/0
349	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	227.39	12/2007 03/2010	12/2010	-	0/0
350	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 921.00	1,115.63	756.19	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
351	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	248.66	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
352	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	232.01	- -	-	-	0/0
353	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	293.29	06/2004 -	12/2012	102(O) -	0/0
354	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,343.13	- -	03/2013	- -	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	343.10	04/2003 03/2010	-	-	0/0
356	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	530.76	486.96	02/2010 02/2011	02/2011	-	0/0
357	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	174.12	03/1998 08/2005	08/2005	-	0/0
358	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	329.78	03/2013 -	03/2014	12(O) -	0/0
359	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	96.75	03/2012 -	03/2013	12(O) -	0/0
360	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	224.35	03/2010 -	03/2012	-	0/0
361	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015	0(O) -	0/0
362	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	818.29	67.86	02/2015 -	-	-	0/0
363	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	219.56	03/2014 -	03/2014	0(O) -	0/0
364	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	112.01	- -	03/2013	-	0/0
365	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	421.08	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
366	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	522.30	- 12/2009	02/2012	-	0/0
367	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	582.83	129.43	- -	-	-	0/0
368	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 227.40	227.40	35.31	- -	-	-	0/0
369	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	548.96	500.95	- -	-	-	0/0
370	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	3,176.10	3,009.20	12/2006 08/2010	08/2010	-	0/0
371	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	44.77	03/2012 -	03/2012	-	0/0
372	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 -	20,000.00	7,947.68	03/2001 -	12/2017	201(O) -	0/0
373	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	820.40	150.01	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
374	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	296.42	03/2014 -	03/2013	-12(O) -	0/0
375	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	164.89	- 03/2010	-	-	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			64,413.89	141,917.43	61,047.11				1/1
<u>Road Transport & Highways</u>									
376	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	163.93	05/2013	03/2014	10(O)	0/0
377	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
378	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00	226.00	199.49	02/2014	02/2014	0(O)	0/0
379	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00	664.00	15.10	02/2014	04/2014	2(O)	0/0
380	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09	375.09	20.75	04/2014	04/2014	0(O)	0/0
381	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00	325.00	115.63	05/2014	05/2014	0(O)	0/0
382	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	364.02	08/2014	08/2014	0(O)	0/0
383	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	1,097.80	06/2013	06/2013	0(O)	0/0
384	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	33.22	09/2013	07/2014	10(O)	0/0
385	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	507.92	08/2013	08/2013	0(O)	0/0
386	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	575.00	366.62	07/2013	07/2013	0(O)	0/0
387	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhandd	02/2012	398.00	398.00	150.00	02/2014	02/2014	0(O)	0/0
388	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	998.79	498.45	08/2013	08/2013	0(O)	0/0
389	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	594.39	08/2013	08/2013	0(O)	0/0
390	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
391	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	162.31	09/2007	06/2013	69(O)	0/0
392	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	10/2012	91(O)	0/0
393	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,038.80	11/2012	06/2013	7(O)	0/0
394	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	-	11/2008	09/2012	46(O)	0/0
395	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	256.42	01/2009	12/2012	47(O)	0/0
396	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	07/2012	5(O)	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
397	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	188.72	02/2004	07/2012	101(O)	0/0
398	BAREILLY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	87.11	09/2013	09/2013	0(O)	0/0
399	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	155.04	06/2014	06/2014	0(O)	0/0
400	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	386.83	-	10/2013	-	2/2
401	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.77	01/2013	06/2013	5(O)	0/0
402	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	500.29	329.47	08/2013	08/2013	0(O)	0/0
403	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	243.92	06/2008	12/2012	54(O)	0/0
404	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	201.47	06/2008	03/2013	57(O)	0/0
405	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	225.24	06/2005	09/2012	87(O)	0/0
406	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	201.07	04/2010	12/2012	32(O)	0/0
407	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
408	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	634.99	03/2013	03/2013	0(O)	0/0
409	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	97.49	-	12/2013	-	0/1
410	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	05/2013	0(O)	0/0
411	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	339.37	10/2011	03/2014	29(O)	0/0
412	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	663.32	10/2011	06/2013	20(O)	0/0
413	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	278.06	06/2008	12/2012	54(O)	0/0
414	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.23	10/2008	03/2014	65(O)	0/0
415	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	578.08	05/2010	12/2012	31(O)	0/0
416	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	339.12	07/2013	07/2013	0(O)	0/0
417	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
418	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	351.33	-	06/2013	-	1/1
419	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	227.95	06/2008	03/2013	57(O)	0/0
420	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	172.56	05/2008	03/2013	58(O)	0/0
421	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	252.87	09/2010	12/2012	27(O)	0/0
422	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	56.11	08/2013	08/2013	0(O)	0/0
423	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	535.16	01/2011	12/2012	23(O)	0/0
424	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	371.68	09/2008	12/2012	51(O)	0/0
425	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
426	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	118.85	09/2008	03/2013	54(O)	0/0
427	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	265.81	02/2004	07/2012	101(O)	0/0
428	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	304.29	09/2007	09/2012	60(O)	0/0
429	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	662.22	08/2013	08/2013	0(O)	0/0
430	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	204.40	04/2008	12/2012	56(O)	0/0
431	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	145.60	04/2008	12/2012	56(O)	0/0
432	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38(O)	0/0
433	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	494.29	12/2009	12/2012	36(O)	0/0
434	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,299.10	09/2012	09/2012	0(O)	0/0
435	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,488.40	10/2011	12/2012	14(O)	0/0
436	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	273.84	09/2007	09/2012	60(O)	0/0
437	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	268.46	02/2009 05/2014	05/2014	63(O) 0(R)	0/0
438	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	196.00	55.07	07/2009	04/2014	57(O)	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
439	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	71.47	09/2007	05/2014	80(O)	0/0
440	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	184.41	08/2004	08/2012	96(O)	0/0
441	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	179.10	08/2004 07/2010	08/2012	96(O) 25(R)	0/0
442	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	779.14	01/2013	01/2013	0(O)	0/0
443	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
444	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	1,744.70	10/2012	10/2012	0(O)	0/0
445	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	506.40	05/2012	08/2012	3(O)	0/0
446	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	325.00	369.11	05/2013	02/2014	9(O)	0/0
447	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
448	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81	267.81	452.55	02/2013	02/2013	0(O)	0/0
449	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
450	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	521.77	09/2008	12/2012	51(O)	0/0
451	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	468.34	09/2009	12/2012	39(O)	0/0
452	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00	536.00	376.37	01/2014	01/2014	0(O)	0/0
453	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	1,214.20	12/2012	12/2012	0(O)	0/0
454	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	279.34	10/2008	09/2012	47(O)	0/0
455	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	285.56	10/2008	03/2013	53(O)	0/0
456	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
457	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	1,003.30	05/2012	09/2012	4(O)	0/0
458	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	185.64	06/2010	10/2012	28(O)	0/0
459	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	10/2012	37(O)	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
460	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	87.37	11/2008 -	07/2013	56(O) -	0/0
461	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	56.76	04/2009 -	07/2013	51(O) -	0/0
462	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	15.49	11/2008 -	01/2014	62(O) -	0/0
463	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	108.63	04/2009 -	03/2013	47(O) -	0/0
464	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	12/2012	6(O) -	0/0
465	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013	0(O) -	0/0
466	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	335.29	03/2013 -	03/2013	0(O) -	0/0
467	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
468	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	266.72	06/2008 -	03/2013	57(O) -	0/0
469	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	12/2012	48(O) -	0/0
470	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	262.54	04/2008 -	12/2012	56(O) -	0/0
471	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	231.87	06/2008 -	03/2013	57(O) -	0/0
472	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	273.71	06/2008 -	12/2012	54(O) -	0/0
473	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00 -	2,159.00	-	06/2015 -	06/2015	0(O) -	0/0
474	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	363.00	248.66	06/2011 06/2011	12/2012	18(O) 18(R)	0/2
475	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58(O) -	0/0
476	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00 -	586.00	259.06	01/2014 -	01/2014	0(O) -	0/0
477	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.71	09/2013 -	09/2013	0(O) -	0/0
478	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	340.68	379.89	03/2008 -	12/2012	57(O) -	0/0
479	PANIKHOLI-RIMOLI - [N24000197]NHAI, Orissa	03/2012	1,410.00 -	1,410.00	120.31	09/2014 -	09/2014	0(O) -	0/0
480	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00 -	807.00	797.01	10/2014 -	10/2014	0(O) -	0/0
481	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	205.95	05/2008 -	08/2012	51(O) -	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
482	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00	574.00	66.26	03/2014	03/2014	0(O)	0/0
483	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	671.30	580.92	02/2013	02/2013	0(O)	0/0
484	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	1,141.10	07/2012	12/2012	5(O)	0/0
485	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	874.76	03/2013	03/2013	0(O)	0/0
486	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	835.00	-	01/2014	01/2014	0(O)	0/0
487	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,459.20	11/2011	08/2013	21(O)	0/0
488	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,906.80	05/2012	10/2012	5(O)	0/0
489	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
490	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	303.96	10/2008	12/2012	50(O)	0/0
491	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	255.82	10/2008	09/2012	47(O)	0/0
492	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	734.10	11/2013	11/2013	0(O)	0/0
493	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	231.38	10/2008	12/2012	50(O)	0/0
494	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	187.27	10/2008	08/2012	46(O)	0/0
495	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	02/2013	25(O)	0/0
496	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	805.39	228.54	03/2013	03/2013	0(O)	0/0
497	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
498	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	200.06	09/2007	03/2013	66(O)	0/0
499	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	-	07/2008	12/2012	53(O)	0/0
500	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
501	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	4.93	12/2013	12/2013	0(O)	0/0
502	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
503	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2014	19(O)	0/0
504	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
505	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.21	03/2008	03/2013	60(O)	0/0
506	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	116.80	04/2004	07/2012	99(O)	0/0
507	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,649.60	08/2011	09/2012	13(O)	0/0
508	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	11/2012	41(O)	0/0
509	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	03/2013	32(O)	0/0
510	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	471.21	11/2013	11/2013	0(O)	0/0
511	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
512	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	55.89	05/2013	05/2013	0(O)	0/0
513	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	34.70	-	04/2013	-	2/2
514	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	497.30	03/2014	03/2014	0(O)	0/0
515	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09	166.30	189.15	03/2008	07/2012	52(O)	0/0
516	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	161.40	03/2008	-	-	0/0
517	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.71	11/2012	11/2012	0(O)	0/0
518	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	314.98	07/2013	07/2013	0(O)	0/0
519	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	148.11	06/2014	06/2014	0(O)	0/0
Total			91,164.10	92,540.59	61,500.70				10/14

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Shipping & Ports									
520	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18(O) 0(R)	0/0
521	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	648.62	09/2012 -	09/2012	0(O) -	0/0
522	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	187.07	12/2012 05/2013	05/2013	5(O) 0(R)	0/0
523	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8(O) 0(R)	0/0
524	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	86.46	06/2011 09/2012	09/2012	15(O) 0(R)	0/0
525	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014	0(O) -	0/0
526	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	12/2013	0(O) -	0/0
527	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	823.49	12/2010 09/2012	10/2013	34(O) 13(R)	0/0
528	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0
529	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0
530	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	10/2008	-	0/0
531	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1
532	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	110.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
533	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0
534	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
535	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0
536	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	829.37	10/2008 -	-	-	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
537	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,345.60	01/2012 09/2012	10/2012	9(O) 1(R)	0/0
538	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
	Total		16,242.52 -	17,782.49	7,642.95				0/1
Telecommunications									
539	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	09/2012	44(O) -	0/0
540	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
541	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72(O) 11(R)	0/0
542	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.27	10/2010 12/2012	12/2012	26(O) 0(R)	0/0
543	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
544	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
545	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	09/2012	39(O) -	0/0
546	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	09/2012	45(O) -	0/0
547	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) - [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	804.06	11/2010 -	09/2012	22(O) -	0/0
548	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	-	0/0
549	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	09/2012	42(O) -	0/0
550	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
551	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
552	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	07/2012	43(O) -	0/0

Sector Wise Details

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	07/2012	79(O) 52(R)	0/0
	Total		6,161.00 -	6,101.79	1,784.59				0/0
<u>Urban Development</u>									
554	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15(O) -	6/6
555	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
556	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	426.52	03/2016 -	03/2016	0(O) -	0/0
557	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	56.69	09/2014 -	09/2014	0(O) -	0/0
	Total		44,245.18 -	49,518.08	2,750.78				6/6
<u>Water Resources</u>									
558	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O) -	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			756,601.56	900,402.69	407,443.78				957/3302

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

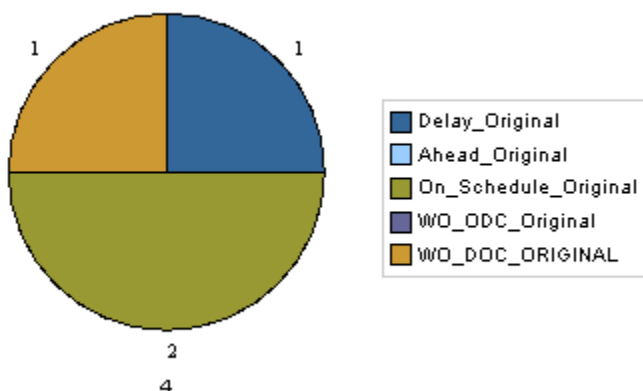

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till July, 2012 is Rs. 2750.78 crore, which is 5.6% of the revised cost of the projects.

Figures are in Rs. Crore

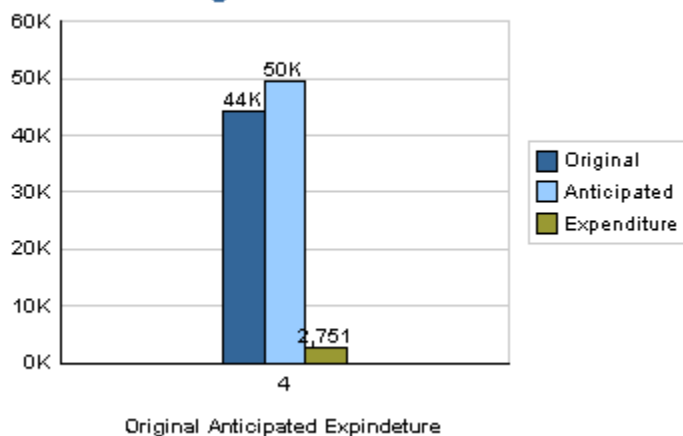

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **15**

Number of Projects Delayed **9**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 9 projects are delayed .6 projects do not have fixed dates of commissioning.

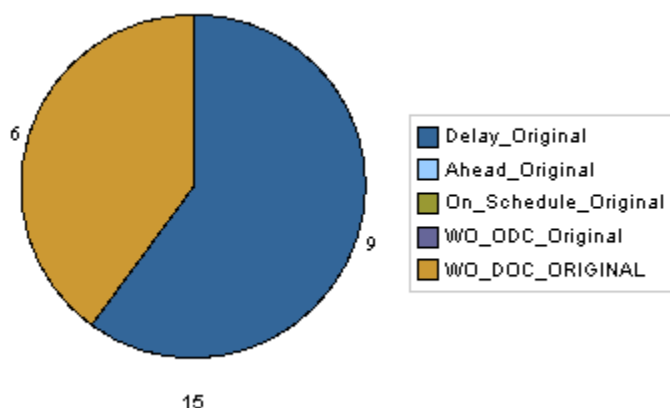

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 6161 crore but this was subsequently revised to Rs. 6101.79 crore implying a cost overrun of -1%. The expenditure incurred on these projects till July, 2012 is Rs. 1784.59 crore, which is 29.2% of the revised cost of the projects.

Figures are in Rs. Crore

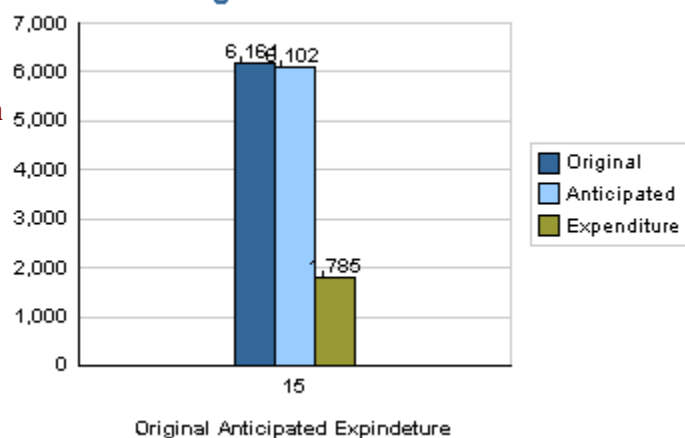

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 3 projects are on schedule and 10 projects are delayed .5 projects do not have fixed dates of commissioning.

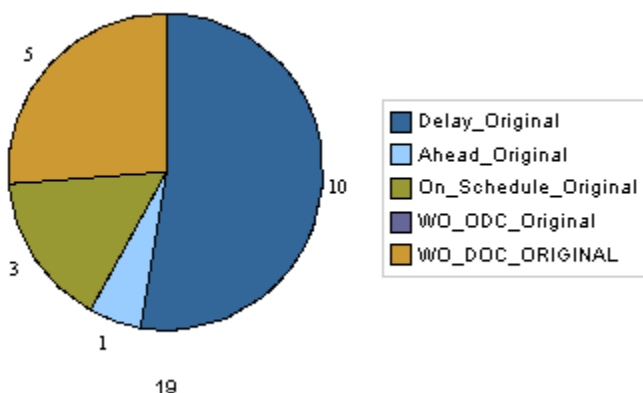

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 16242.52 crore but this was subsequently revised to Rs. 17782.49 crore implying a cost overrun of 9.5%. The expenditure incurred on these projects till July, 2012 is Rs. 7642.95 crore, which is 43% of the revised cost of the projects.

Figures are in Rs. Crore

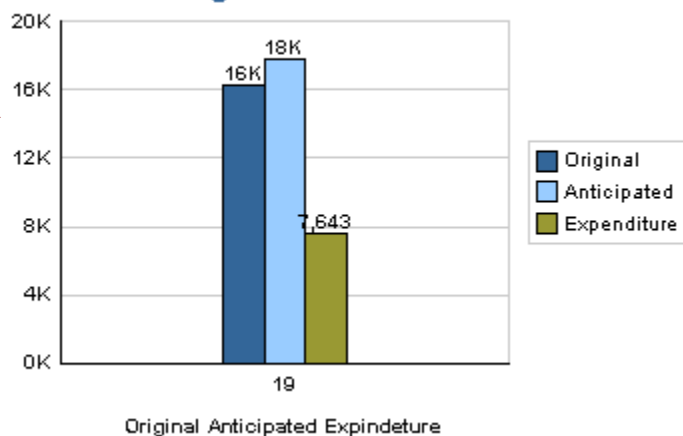

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	144
Number of Projects On Schedule	55
Number of Projects Delayed	82

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 144 projects, 55 projects are on schedule and 82 projects are delayed .1 project do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

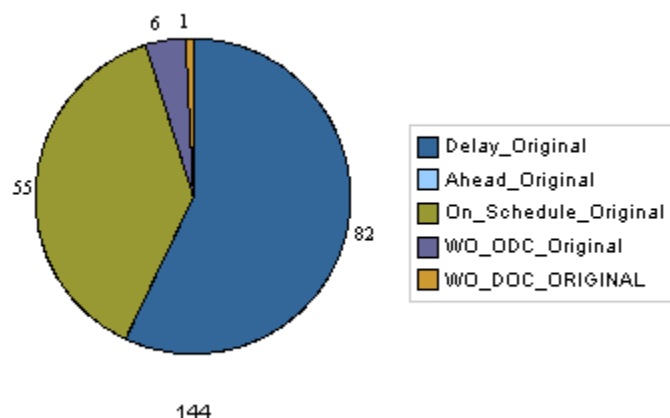

III. Investment Scenario

The Total Original cost of implementation of 144 projects when sanctioned, was of the order of Rs. 91164.1 crore but this was subsequently revised to Rs. 92540.59 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till July, 2012 is Rs. 61500.7 crore, which is 66.5% of the revised cost of the projects.

Figures are in Rs. Crore

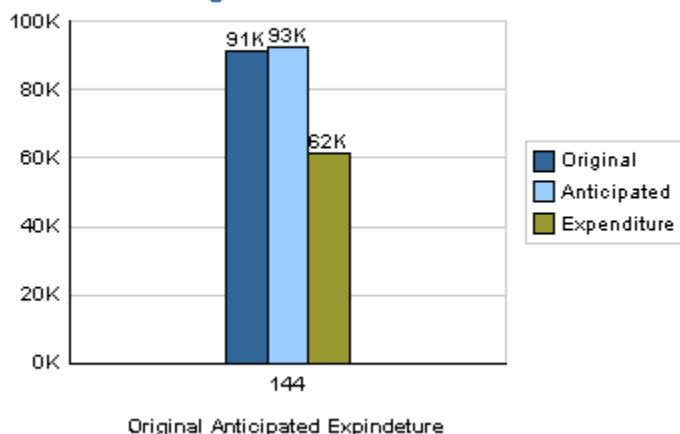

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	126
Number of Projects On Schedule	10
Number of Projects Delayed	40
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	18
Number of Projects Without Date Of Commissioning	57

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 126 projects, 1 project are ahead of schedule, 10 projects are on schedule and 40 projects are delayed .57 projects do not have fixed dates of commissioning.18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

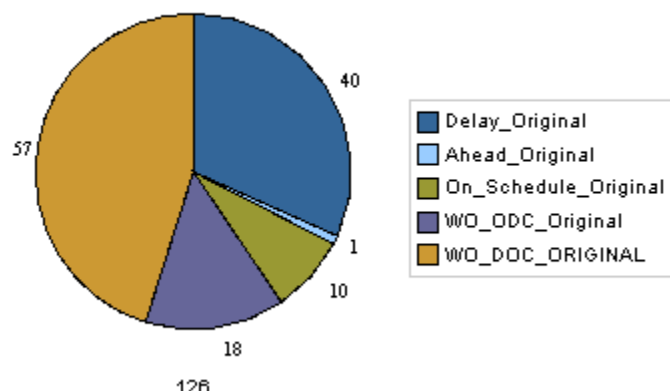

III. Investment Scenario

The Total Original cost of implementation of 126 projects when sanctioned, was of the order of Rs. 64413.89 crore but this was subsequently revised to Rs. 141917.43 crore implying a cost overrun of 120.3%. The expenditure incurred on these projects till July, 2012 is Rs. 61047.11 crore, which is 43% of the revised cost of the projects.

Figures are in Rs. Crore

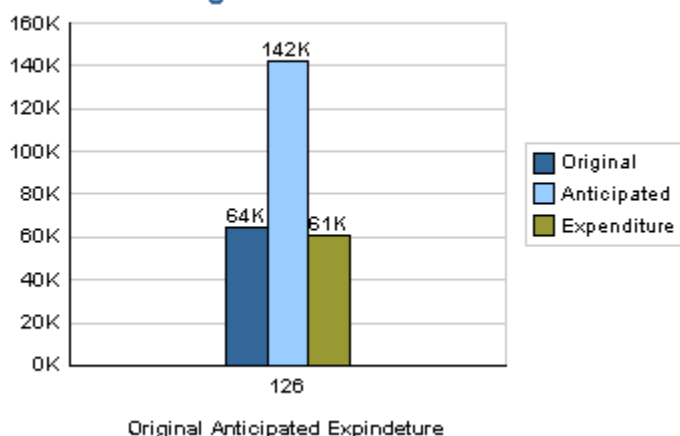

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	98
Number of Projects On Schedule	44
Number of Projects Delayed	48

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 98 projects, 44 projects are on schedule and 48 projects are delayed .4 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

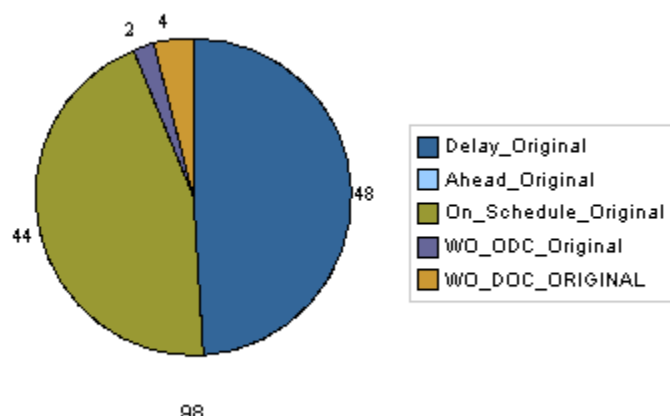

III. Investment Scenario

The Total Original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 235165.2 crore but this was subsequently revised to Rs. 248964.17 crore implying a cost overrun of 5.9%. The expenditure incurred on these projects till July, 2012 is Rs. 107643.65 crore, which is 43.2% of the revised cost of the projects.

Figures are in Rs. Crore

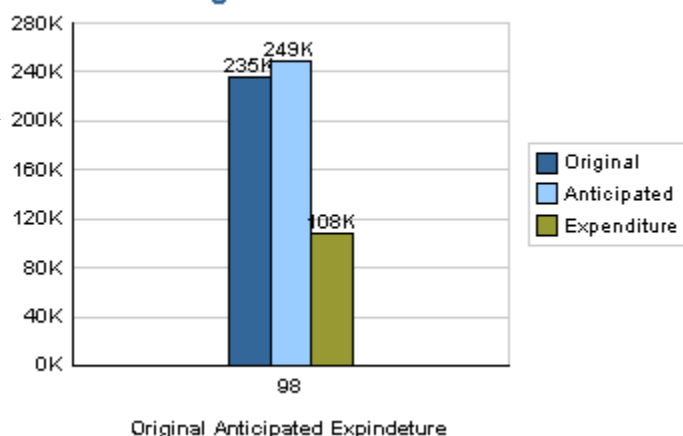

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	67
Number of Projects On Schedule	20
Number of Projects Delayed	38

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 67 projects, 20 projects are on schedule and 38 projects are delayed .4 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

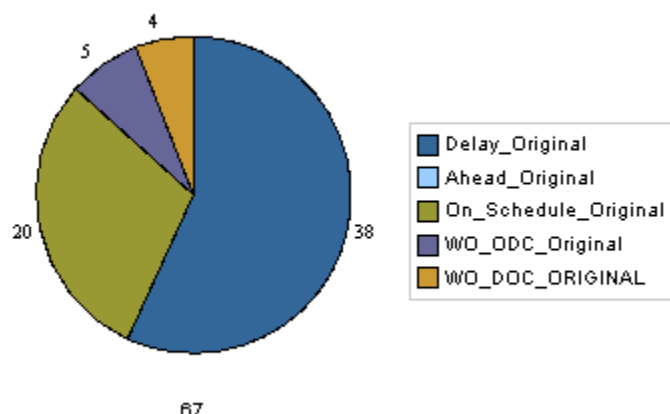

III. Investment Scenario

The Total Original cost of implementation of 67 projects when sanctioned, was of the order of Rs. 157430.3 crore but this was subsequently revised to Rs. 166078.11 crore implying a cost overrun of 5.5%. The expenditure incurred on these projects till July, 2012 is Rs. 75644.41 crore, which is 45.5% of the revised cost of the projects.

Figures are in Rs. Crore

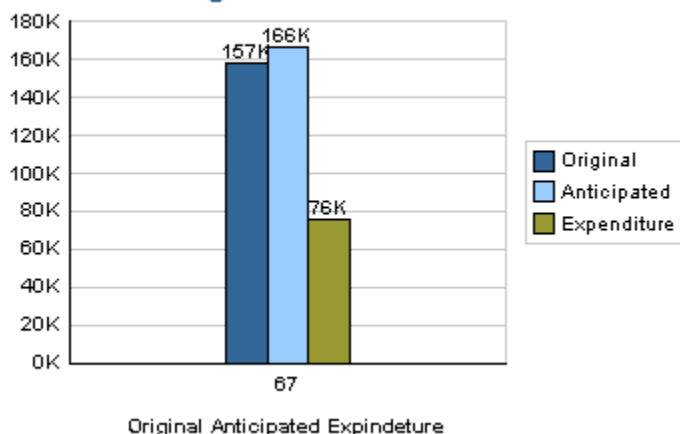

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	16
Number of Projects Delayed	8
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 1 project are ahead of schedule, 8 projects are delayed .1 project do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

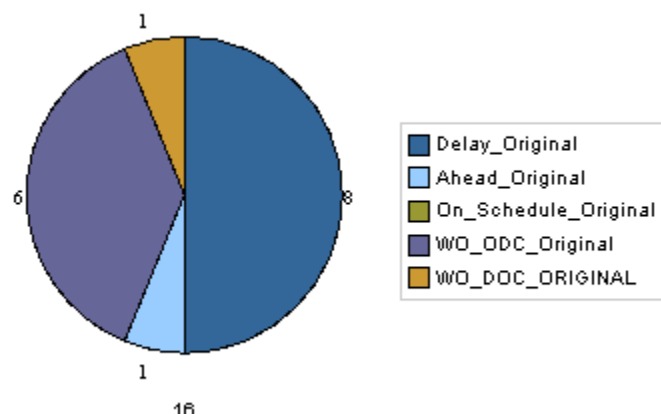

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 50110.22 crore but this was subsequently revised to Rs. 71356.76 crore implying a cost overrun of 42.4%. The expenditure incurred on these projects till July, 2012 is Rs. 42373.18 crore, which is 59.4% of the revised cost of the projects.

Figures are in Rs. Crore

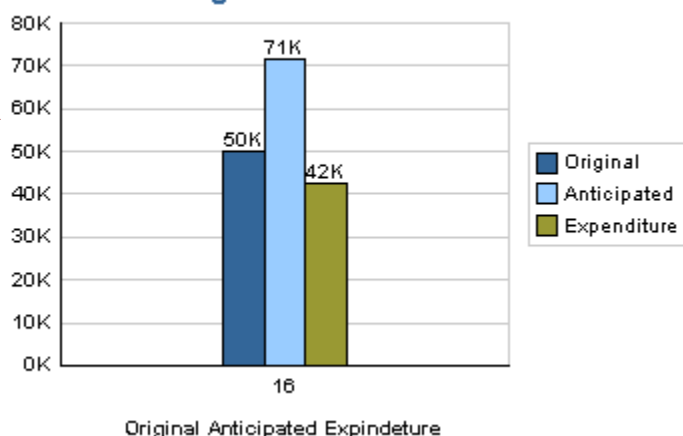

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

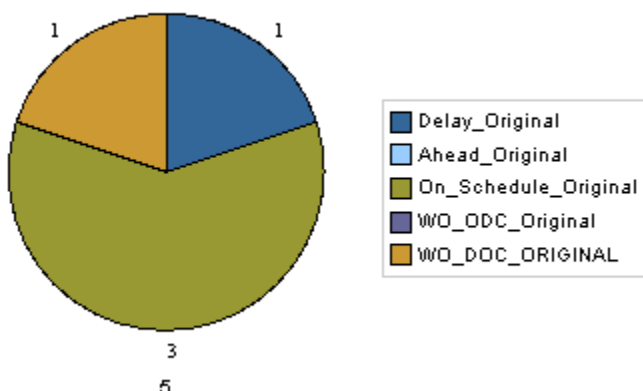

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4828.66 crore but this was subsequently revised to Rs. 4828.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till July, 2012 is Rs. 2609.9 crore, which is 54.1% of the revised cost of the projects.

Figures are in Rs. Crore

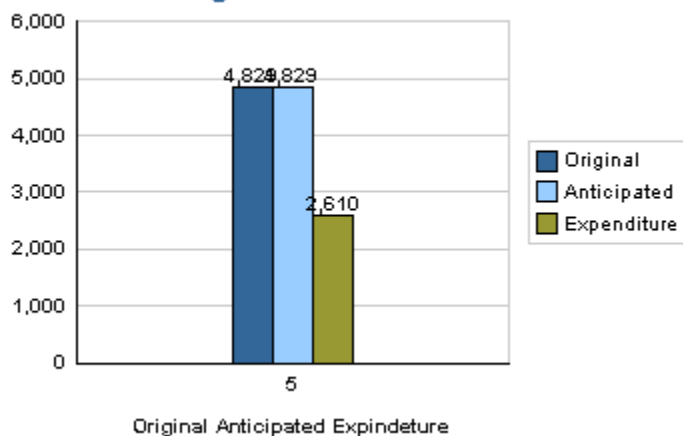

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	26
Number of Projects Delayed	24

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 26 projects are on schedule and 24 projects are delayed .1 project do not have fixed dates of commissioning.

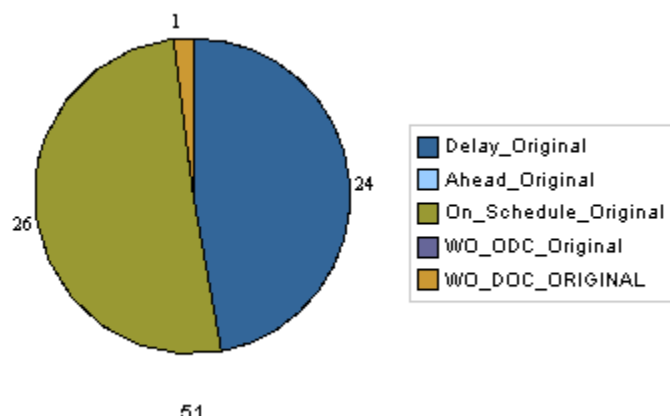

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 33815.11 crore but this was subsequently revised to Rs. 37312.25 crore implying a cost overrun of 10.3%. The expenditure incurred on these projects till July, 2012 is Rs. 12383.49 crore, which is 33.2% of the revised cost of the projects.

Figures are in Rs. Crore

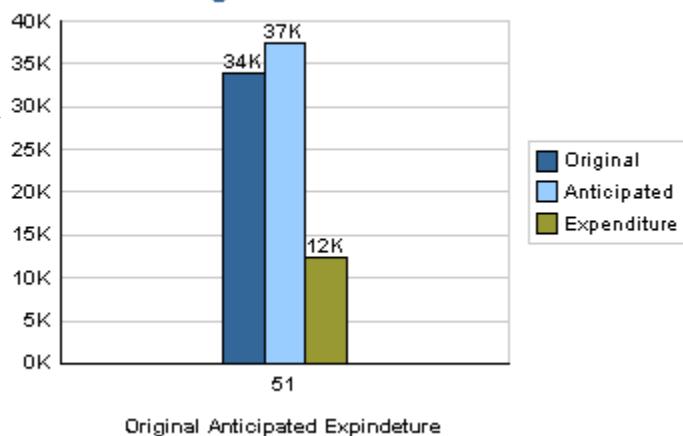

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

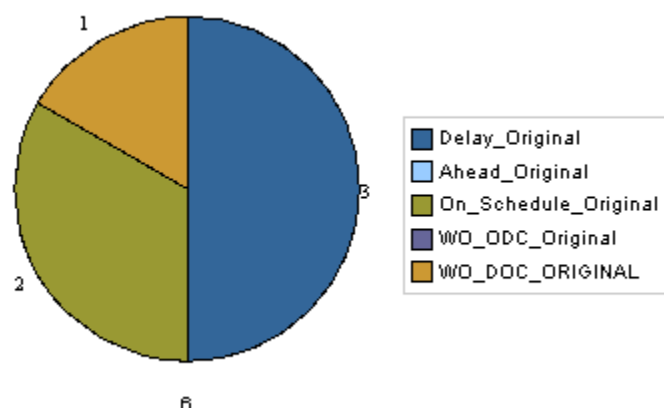

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till July, 2012 is Rs. 4376.22 crore, which is 72.2% of the revised cost of the projects.

Figures are in Rs. Crore

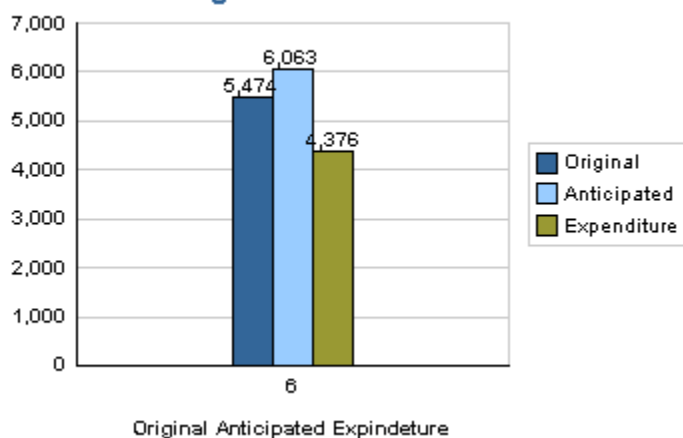

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

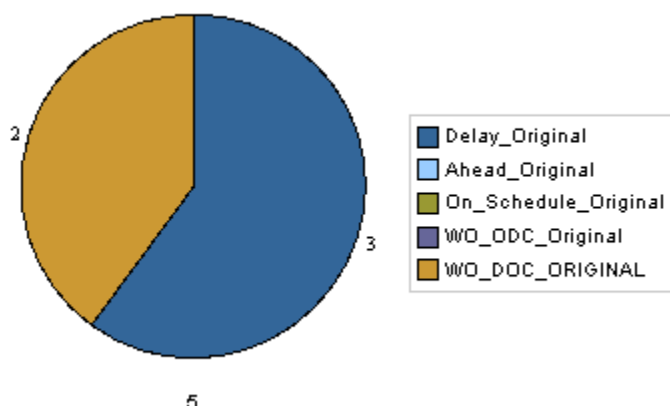

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till July, 2012 is Rs. 22560.84 crore, which is 47.2% of the revised cost of the projects.

Figures are in Rs. Crore

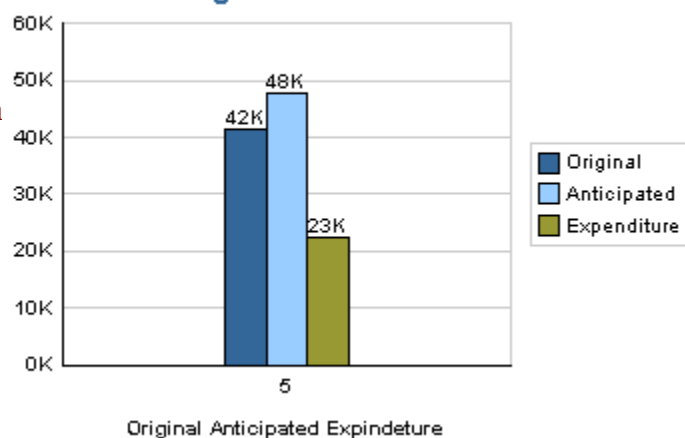

ANNEXURES

STATE WISE SUMMARY OF ONGOING PROJECTS AS ON				31.07.2012	
S.No.	State	No. Of Projects	Original Cost (In Crores)	Anticipated Cost (In Crores)	Cummulative Expenditure (In Crores)
1	Andhra Pradesh	36	31,031.62	38,457.22	21,874.62
2	Arunachal Pr.	4	9,512.22	14,153.62	8,206.40
3	Assam	36	22,463.87	33,705.52	21,831.88
4	Bihar	29	26,796.45	31,675.72	20,470.19
5	Chhatisgarh	25	40,824.67	56,321.66	21,392.70
6	Delhi	3	37,985.00	37,965.41	550.41
7	Goa	1	335.61	335.61	124.35
8	Gujarat	22	31,111.55	31,313.49	6,543.63
9	Haryana	10	5,496.60	7,367.17	7,299.73
10	Himachal Pr.	5	13,355.57	15,213.42	12,172.22
11	J and K	11	15,120.05	34,993.86	13,175.20
12	Jharkhandd	23	11,785.48	16,601.53	7,779.63
13	Karnataka	24	44,634.83	53,079.65	19,203.50
14	Kerala	5	5,469.67	6,911.22	4,854.08
15	Madhya pradesh	23	16,561.52	16,855.99	8,565.16
16	Maharashtra	53	95,829.75	111,041.89	49,568.22
17	Manipur	1	727.56	4,444.00	843.10
18	Meghalaya	2	762.00	762.00	575.86
19	Mizoram	2	1,532.97	3,307.11	350.17
20	Multi State	103	137,052.71	142,750.88	60,426.52
21	Nagaland	1	850.00	850.00	8.44
22	Orissa	30	57,405.36	61,398.87	31,211.71
23	Punjab	7	4,836.20	5,777.97	3,822.36
24	Rajasthan	14	26,544.10	26,138.31	8,436.80
25	Sikkim	2	1,648.94	3,690.04	235.64
26	Tamil Nadu	32	51,275.95	61,960.82	38,366.88
27	Tripura	3	1,522.39	2,053.23	884.05
28	Uttar Pradesh	23	18,321.94	22,159.71	11,253.85
29	Uttaranchal	3	5,619.21	6,559.64	1,878.82
30	West Bengal	25	40,187.77	52,557.13	25,537.66
Total	All States	558	756,601.56	900,402.69	407,443.78

LIST OF PROJECTS IN WHICH EXPENDITURE MORE THAN COST as on 31-07-2012

SN	PROJECTS	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2003	3492.00	0.00	3641.60
2	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	0.00	14886.00
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	08/2008	1942.51	0.00	2025.63
4	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	Petroleum	01/2008	224.00	299.00	349.29
5	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	01/2009	756.00	0.00	887.01
6	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	10/2003	768.92	0.00	1535.59
7	CHUTAK HYDRO-ELECTRIC PROJECT	Power	08/2006	621.26	0.00	746.85
8	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2006	611.01	0.00	779.27
9	URI H.E.P STAGE -II (NHPC)	Power	08/2005	1729.29	0.00	1757.40
10	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	1061.38	0.00	1159.82
11	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	07/1998	248.44	576.27	877.21
12	JIND-SONEPAT (NL),NR	Railways	01/2004	190.81	238.56	414.03
13	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	0.00	7947.68
14	REWARI-ROHTAK (NL),NR	Railways	01/2004	149.38	330.23	486.96
15	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	03/2002	409.00	625.30	833.20
16	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	523.76
17	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	201.83
18	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	03/1999	491.19	1099.20	1260.07
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	04/1997	233.00	501.69	651.57
20	PATNA GANGA BRIDGE (NL), ECR	Railways	04/2001	624.47	1389.98	1484.78
21	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	04/1996	114.01	332.92	388.99
22	KODERMA GIRIDH (NL), ECR	Railways	04/1996	371.36	371.36	410.12
23	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	04/1985	158.77	432.46	558.07
24	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	04/1999	108.00	214.09	250.82
25	KATIHAR - JOGBANI (GC)(NEFR)	Railways	09/2001	100.00	492.98	730.92
26	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	0.00	843.10
27	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	09/1996	156.00	0.00	240.93
28	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	1676.31	1676.31	3161.45
29	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	12/2006	170.00	170.00	392.26
30	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	04/2000	733.00	733.00	1275.88
31	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	01/2004	915.70	915.70	1343.13
32	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	1500.00	2408.10
33	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	03/2002	381.17	381.17	559.17

SN	PROJECTS	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
34	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	04/1999	323.40	323.40	491.99
35	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	03/1997	395.00	1062.36	1320.26
36	ELECTRIFICATION OF MORADABAD-ROZA	Railways	12/2004	129.17	0.00	227.48
37	BILASPUR-URKURA (DL)	Railways	04/1997	151.52	0.00	319.07
38	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	Railways	04/2000	133.41	207.00	210.88
39	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	04/2003	136.62	0.00	227.39
40	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	04/2005	240.00	0.00	396.62
41	RENIGUNTA-GUNTAKAL(RE)	Railways	06/2000	168.34	0.00	343.10
42	RAJATGARH-BARANG(LD),ECOR	Railways	04/1999	166.16	0.00	248.66
43	GADWAL - RAICHUR (NL), SCR	Railways	04/1998	92.63	228.09	260.18
44	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	580.85
45	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	03/1996	155.74	429.49	621.61
46	RANCHI-LOHARDAGA(GC),SER	Railways	04/1997	194.07	194.07	293.29
47	CALICUT-MANGALORE (DL) (SR)	Railways	02/1996	240.00	0.00	600.41
48	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	09/1995	100.00	100.00	500.95
49	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	09/2006	343.17	343.17	536.14
50	KARUR-SALEM(NL),SR	Railways	02/1997	155.55	229.88	732.04
51	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	341.37
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	02/1997	295.00	412.91	496.59
53	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	12/2003	240.00	0.00	285.56
54	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH 2)	Road Transport & Highways	04/2000	367.49	0.00	453.68
55	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	03/2005	220.00	0.00	273.84
56	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	12/2003	160.00	0.00	172.56
57	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	12/2003	251.03	0.00	303.96
58	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	12/2003	300.93	0.00	302.72
59	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	03/2005	168.00	0.00	457.30
60	Kishangarh-Ajmer-Beawer	Road Transport & Highways	11/2009	795.00	0.00	1003.30

SN	PROJECTS	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
61	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	12/2003	225.00	0.00	231.87
62	NALBARI T BIJNI (AS-7)	Road Transport & Highways	12/2003	208.00	0.00	262.54
63	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	12/2003	245.00	0.00	491.21
64	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	12/2003	200.00	0.00	227.95
65	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	12/2003	264.72	0.00	266.72
66	INDORE-DEWAS(NH-3)	Road Transport & Highways	11/2010	325.00	0.00	369.11
67	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	12/2003	198.16	0.00	204.40
68	Hyderabad-Vijaywada Km. 40 to 221.50 Km	Road Transport & Highways	04/2010	1740.00	0.00	1744.70
69	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	05/2009	1108.00	0.00	3459.20
70	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	12/2003	229.91	0.00	255.82
71	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	12/2003	203.43	0.00	231.38
72	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	12/2003	151.30	0.00	187.27
73	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	12/2003	355.06	0.00	468.34
74	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	12/2003	275.00	0.00	279.34
75	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	12/2003	340.68	0.00	379.89
76	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	12/2003	340.00	0.00	521.77

SN	PROJECTS	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
77	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	12/2003	195.00	0.00	201.47
78	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	12/2003	200.00	0.00	273.71
79	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	03/2005	557.00	0.00	930.92
80	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	05/2009	572.30	0.00	663.32
81	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	02/2009	1693.75	0.00	2649.60
82	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	04/2009	1673.70	0.00	2488.40
83	TRICHY - KORUR NH-67	Road Transport & Highways	03/2005	516.00	0.00	760.07
84	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	03/2005	280.00	0.00	581.49
85	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	03/2005	941.00	0.00	1901.00
86	Jaipur-Tonk-Deoli	Road Transport & Highways	06/2010	792.06	0.00	1214.20
87	AMRITSAR-PATHANKOT	Road Transport & Highways	05/2010	705.00	0.00	1038.80
88	JAIPUR-REENGUS	Road Transport & Highways	08/2010	267.81	0.00	452.55
89	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport & Highways	09/2010	671.00	0.00	737.54
90	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	12/2003	237.80	0.00	243.92
91	ROHTAK-BAWAL	Road Transport & Highways	05/2011	650.00	0.00	734.10
92	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	12/2010	1008.50	0.00	1097.80

SN	PROJECTS	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
93	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	09/2010	946.00	0.00	1394.40
94	Pune-sholapur, pkg1	Road Transport & Highways	11/2009	1110.00	0.00	1906.80
95	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	03/2005	940.00	0.00	1141.10
96	MP/Maharashtra Border-Dhula	Road Transport & Highways	12/2009	835.00	0.00	1068.70
97	Hazaribagh-Ranchi	Road Transport & Highways	08/2010	625.07	0.00	779.14
98	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	03/2005	190.00	0.00	256.42
99	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	Road Transport & Highways	01/2008	464.00	0.00	535.16
100	GANJAM-ICCHAPURUM, NH-5(NHAI)	Road Transport & Highways	04/2000	263.27	0.00	265.81
101	Armur to kadloor yellareddy	Road Transport & Highways	02/2010	390.56	0.00	631.65
102	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	08/2010	388.00	0.00	506.40
103	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	12/2003	232.45	0.00	252.87
104	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	12/2003	332.94	0.00	371.68
105	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	12/2003	225.00	0.00	278.06
106	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	04/2007	486.00	0.00	578.08
107	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	12/2003	275.00	0.00	304.29
108	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	12/2003	157.47	0.00	200.06

SN	PROJECTS	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDI TURE CUMM
109	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	03/2007	245.67	298.17	326.08
110	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	07/2007	230.00	0.00	248.53

Ahead

S.No	Project	DOA	DOC Original	DOC Revised	DOC Anticipated	COST Original	Cost Anticipated
1	Udhna-Jalgaon with electrification(doubling) (WR)	4/2008	03/2014	N.A.	03/2013	1389.62	1389.62
2	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas	2/2011	05/2013	N.A.	03/2013	830	621.53
3	EXPENSION OF ROURKELA STEEL PLANT	9/2008	11/2013	N.A.	03/2013	11812	11812

List of project Without Original Date of Commissioning

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Steel</u>									
1	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	3,316.00	6,325.00	2,824.12	-	10/2012	-	3/16
2	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00	16,408.00	13,558.10	-	12/2012	-	10/19
3	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka	04/2011	572.00	572.00	149.17	-	04/2013	-	10/19
4	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC, Karnataka	02/2011	898.55	898.55	82.45	-	05/2013	-	14/21
5	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00	17,265.00	6,043.92	-	09/2013	-	10/27
6	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55	254.55	6.32	-	03/2014	-	0/1
Total			24,669.10	41,723.10	22,664.08				47/103
<u>Petroleum</u>									
7	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00	898.00	887.01	-	03/2012	5(R3)	0/53
8	EURO-IV DHDT - [N16000109]CPCL, Tamil Nadu	09/2008	2,615.69	2,615.69	1,923.37	-	08/2012	-	116/116
9	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68	276.00	180.54	-	09/2012	-	1/1
10	CDU/VDU-II - [N16000110]CPCL, Tamil Nadu	03/2010	333.99	333.99	163.73	-	09/2012	-	33/36
11	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00	30,426.00	16,808.86	-	09/2013	0(R3)	167/100
Total			33,721.36	34,549.68	19,963.51				317/306
<u>Power</u>									
12	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01	623.44	322.19	-	07/2013	0(R3)	5/29
13	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL, Multi State	07/2010	1,272.80	1,272.80	354.19	-	09/2013	-	0/11
Total			1,693.81	1,896.24	676.38				5/40
<u>Railways</u>									
14	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55	712.00	732.04	-	10/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, Tamil Nadu	09/2006	343.17 343.17	900.00	536.14	- -	12/2012	-	0/0
16	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	496.59	- -	01/2013	-	0/0
17	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	164.00	- -	02/2013	-	0/0
18	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	165.33	- -	03/2013	-	0/0
19	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	189.42	- -	03/2013	-	0/0
20	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	91.50	- -	03/2013	-	0/0
21	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	751.22	- -	03/2013	-	0/0
22	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	231.46	- -	03/2013	-	0/0
23	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,343.13	- -	03/2013	-	0/0
24	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	112.01	- -	03/2013	-	0/0
25	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
26	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	491.99	- -	03/2014	-	0/1
27	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.43	- -	03/2014	-	0/0
28	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	112.60	- -	03/2014	-	0/0
29	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	-	0/0
30	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	179.50	- -	03/2015	-	0/0
31	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
	Total		5,654.70 -	13,748.49	6,180.50				0/1
Road Transport & Highways									
32	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
33	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
34	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	34.70	- -	04/2013	-	2/2
35	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	351.33	- -	06/2013	-	1/1
36	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	386.83	- -	10/2013	-	2/2
37	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	97.49	- -	12/2013	-	0/1
Total			4,069.00 -	4,069.00	3,002.29				10/12
Grand Total			69,807.97	95,986.51	52,486.76				379/462

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Atomic Energy</u>				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	09/2010 -	01/2012
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 04/2011	04/2012
	Total		4,598.29 -		
	<u>Civil Aviation</u>				
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
	Total		1,808.00 -		
	<u>Coal</u>				
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	03/2012
	Total		249.03 -		
	<u>Fertilisers</u>				
5	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012
	Total		325.00 -		
	<u>Steel</u>				
6	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90 -	- -	02/2012
	Total		500.90 -		
	<u>Petroleum</u>				
7	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	04/2012 -	04/2012
8	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	06/2012 03/2013	06/2012
9	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
10	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	- 08/2011	-
	Total		3,547.14 -		
	<u>Power</u>				
11	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	04/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
12	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC, Chhatisgarh	12/2003	8,323.39	12/2009	06/2012
			-	12/2011	
13	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45	12/2007	-
			1,007.16	12/2009	
14	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra	12/2007	477.69	09/2010	-
			-	-	
	Total		9,674.14		
			-		
<u>Railways</u>					
15	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19	07/2005	07/2005
			1,099.20	-	
16	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94	03/1998	08/2005
			604.04	08/2005	
17	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00	06/2007	06/2007
			625.30	-	
18	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00	07/2008	07/2008
			363.26	-	
19	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42	-	05/2009
			369.70	05/2009	
20	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36	-	03/2010
			371.36	03/2010	
21	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRT, West Bengal	03/2000	907.69	12/2006	08/2010
			3,176.10	08/2010	
22	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	12/2007	12/2010
			-	03/2010	
23	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68	12/2010	12/2010
			293.74	12/2010	
24	REWARI-ROHTAK (NL), NR - [220100279](NR), Haryana	01/2004	149.38	02/2010	02/2011
			330.23	02/2011	
25	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90	06/1999	03/2011
			284.27	03/2011	
26	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR, Karnataka	04/1995	65.94	-	03/2011
			302.23	-	
27	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00	05/2008	03/2011
			-	03/2011	
28	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00	12/2009	03/2011
			214.09	03/2011	
29	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52	-	03/2011
			-	03/2009	
30	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00	03/2009	03/2011
			-	12/2009	
31	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00	03/2011	03/2011
			170.00	03/2011	
32	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15	12/2010	03/2011
			1,106.62	03/2011	
33	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36	03/2011	03/2011
			196.95	-	
34	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR, Multi State	04/1985	158.77	03/1994	12/2011
			432.46	-	
35	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64	-	12/2011
			1,185.00	09/2009	
36	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00	-	02/2012
			-	-	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
37	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
38	Dakshin-barasal-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
39	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
40	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
41	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012
42	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	- -	03/2012
43	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
44	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 224.51	- -	03/2012
45	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	- -	03/2012
46	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
47	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR, Arunachal Pr.	09/1996	156.00 -	- -	03/2012
48	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP, Maharashtra	04/2003	3,125.20 4,501.80	06/2011 03/2012	03/2012
49	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE, Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
50	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE, Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
51	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 167.73	03/2012 -	03/2012
52	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR, Gujarat	04/2008	318.24 -	03/2012 -	03/2012
53	CHURCHGATE-VIRAR: CONV. OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233]RE, Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012
54	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	12/2012 -	-
55	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 1,038.00	03/1998 -	-
56	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	- -	-
57	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
58	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 1,045.20	- -	-
59	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-
60	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23 -	02/2015 -	-
61	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, Andhra Pradesh	04/2006	378.56 671.82	- -	-
62	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
63	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
64	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
65	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
66	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
67	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-
68	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
69	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
70	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 227.40	- -	-
71	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
	Total		19,403.94 -		
	<u>Road Transport & Highways</u>				
72	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	-
	Total		166.27 -		
	<u>Shipping & Ports</u>				
73	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008
74	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	- 01/2009	01/2009
75	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
76	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
77	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-
	Total		3,904.91 -		
	<u>Telecommunications</u>				
78	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
79	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
80	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
81	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
82	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
83	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	03/2010	-
	Total		2,997.75		
			-		
	<u>Urban Development</u>				
84	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	04/2009	-
	Total		173.08		
			114.18		
			-		
Grand Total			47,289.55		

List of On schedule Projects

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apxenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	372.05	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II [N04000070	2/2011 -	452.00 -	452.00	1.20	02/2015 -	02/2015
	Total		1,078.00 -	1,078.00	373.25		
	<u>Coal</u>						
3	Purnadih OCP - [N06000085	7/2008	210.98 -	210.98	87.76	03/2013 -	03/2013
4	KARMA OCP - [N06000088	6/2009	162.46 -	162.46	30.89	03/2014 -	03/2014
5	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
6	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
7	JALLARAM SHAFT PROJECT - [N06000025	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
8	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008	6/2006	737.65 -	1,188.31	645.16	03/2013 -	03/2013
9	Rajrappa RCE OCP - [N06000087	12/2009	510.85 -	510.85	268.19	03/2016 -	03/2016
10	MANIKPUR OC EXPANTION - [N06000081	11/2009	321.42 -	321.50	203.55	03/2014 -	03/2014
11	GOPAL PRASAD OCP - [N06000042	2/2008	395.87 -	395.87	71.35	03/2015 -	03/2015
12	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
13	Muraidih UG Turn-key Project - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
14	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094	7/2005	1,268.53 -	1,943.66	1,197.18	03/2014 -	03/2014
15	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093	7/2005	1,667.55 -	2,675.67	1,370.35	03/2014 -	03/2014
16	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	25.93	03/2015 -	03/2015
17	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.35	03/2014 03/2014	03/2014
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	475.93 -	479.63	107.59	03/2013 -	03/2013
19	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	45.39	03/2016 -	03/2016
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	39.30	03/2016 -	03/2016

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
21	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.49	03/2015 -	03/2015
22	JALAGAM VENGALA RAO OCP - [N06000094	7/2011	447.06 -	447.06	-	03/2015 -	03/2015
23	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) [N06000095	6/2011	5,907.11 -	5,907.11	21.14	12/2015 -	12/2015
24	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	114.45	03/2017 -	03/2017
25	KANIHA OCP, MCL, (10.0 Mty) - [N06000035	12/2007	457.77 -	457.77	110.35	03/2013 -	03/2013
26	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	-	03/2018 03/2018	03/2018
27	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
28	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	70.19	03/2016 -	03/2016
	Total		18,515.20 -	20,700.99	4,463.92		
Fertilisers							
29	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT - [N08000005	1/2010	1,294.19 -	1,294.19	697.34	01/2013 -	01/2013
30	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT - [N08000004	1/2010	1,292.84 -	1,292.84	717.67	01/2013 -	01/2013
31	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT [N08000006	1/2010	1,478.63 -	1,478.63	769.86	01/2013 01/2013	01/2013
	Total		4,065.66 -	4,065.66	2,184.87		
Petrochemicals							
32	Assam gas Cracker project - [N16000106	4/2006	5,460.61 -	8,920.00	5,090.47	12/2013 12/2013	12/2013
	Total		5,460.61 -	8,920.00	5,090.47		
Petroleum							
33	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY [N16000069	3/2009	3,284.00 -	2,174.00	1,061.76	09/2012 09/2012	09/2012
34	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015
35	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015
36	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	4/2008	825.00 -	1,827.00	611.55	04/2013 04/2013	04/2013

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
37	Construction of tanks and blending facility at Vadinar - [N16000115	2/2009	267.00 -	267.00	201.71	09/2012 09/2012	09/2012
38	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088	8/2009	1,793.00 -	1,793.00	670.64	09/2012 -	09/2012
39	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery - [N16000107	7/2010	1,000.00 -	1,000.00	162.48	01/2013 -	01/2013
40	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108	11/2009	341.50 -	341.50	104.66	02/2013 -	02/2013
41	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	756.65	5.73	05/2013 -	05/2013
42	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	6/2010	202.94 -	202.94	0.20	01/2014 -	01/2014
43	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	4.54	03/2014 -	03/2014
44	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	-	05/2014 -	05/2014
45	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
46	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
47	Development of WO-16 Cluster Fields - [N16000105	6/2010	2,523.00 -	2,523.00	153.52	01/2014 -	01/2014
48	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	4.84	12/2014 -	12/2014
49	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	5.67	04/2015 -	04/2015
50	Wax Project - [N16000101	6/2010	576.60 -	576.60	56.65	12/2013 12/2013	12/2013
51	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA [N16000112	8/2010	8,140.00 -	8,140.00	1,292.50	02/2014 -	02/2014
52	Ahmedabad Redevelopment - [N16000120	11/2010	1,916.10 -	1,916.10	33.22	12/2014 -	12/2014
	Total		41,341.19 -	39,997.79	4,369.67		
Power							
53	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT - [N18000046	12/2008	7,031.88 -	7,031.88	3,727.00	12/2012 -	12/2012
54	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096	3/2011	2,569.25 -	2,569.25	526.71	03/2014 -	03/2014
55	Transmission system associated with krishnapatnam- Part-A - [N18000090	12/2010	779.21 -	779.21	472.99	08/2013 -	08/2013
56	Transmission system for phase-I generation projects in orissa-part B - [N18000093	12/2010	2,743.19 -	2,743.19	709.60	12/2013 -	12/2013
57	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	9/2010	2,074.86 -	2,074.86	619.75	03/2013 -	03/2013

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX [N18000088]	10/2010	182.68 -	182.68	46.24	01/2013 -	01/2013
59	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chhattisgarh - [N18000092]	12/2010	1,719.52 -	1,719.52	541.68	08/2013 -	08/2013
60	Transm System for development of Pooling strn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	334.28	01/2015 -	01/2015
61	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]	3/2011	1,585.12 -	1,585.12	334.81	11/2013 -	11/2013
62	Northern Region system strengthening scheme-XXII - [N18000091]	12/2010	209.78 -	209.78	63.88	08/2013 -	08/2013
63	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	173.04	12/2013 -	12/2013
64	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	215.39	09/2014 -	09/2014
65	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]	10/2011	558.26 -	558.26	63.06	11/2013 -	11/2013
66	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]	7/2011	181.93 -	181.93	48.12	07/2013 -	07/2013
67	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	72.76	08/2014 -	08/2014
68	Supplementary transmission associated with vellur TPS - [N18000097]	8/2010	170.36 -	170.36	40.73	04/2013 -	04/2013
69	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A - [N18000098]	5/2010	250.03 -	250.03	53.95	01/2013 -	01/2013
70	Northern region system strengthening scheme XVI - [N18000094]	7/2010	752.64 -	752.64	182.17	07/2013 -	07/2013
71	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	345.81	05/2014 -	05/2014
72	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	-	10/2014 -	10/2014
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	40.40	11/2014 -	11/2014
74	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	52.80	08/2014 -	08/2014
75	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	33.16	10/2014 -	10/2014
76	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	1.64	08/2014 -	08/2014

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	102.90	02/2015 -	02/2015
78	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	14.60	01/2014 -	01/2014
79	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	102.40	01/2015 -	01/2015
80	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	47.90	08/2014 -	08/2014
81	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	628.00	11/2016 -	11/2016
82	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	296.00	09/2016 -	09/2016
83	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	939.00	12/2016 -	12/2016
84	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014
85	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	22.17	08/2014 -	08/2014
86	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	38.53	02/2014 -	02/2014
87	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	209.49	07/2014 -	07/2014
88	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	210.06	08/2014 -	08/2014
89	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000110]	8/2011	1,391.97 -	1,391.97	279.01	12/2013 -	12/2013
90	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	54.95	06/2014 -	06/2014
91	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	279.01	12/2013 -	12/2013
92	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	75.88	10/2013 -	10/2013
93	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	22.14	06/2014 -	06/2014
94	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	27.68	06/2015 -	06/2015
95	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
96	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
	Total		96,968.51 -	96,968.51	12,049.69		
<u>Railways</u>							
97	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02 -	2,913.51	135.97	03/2016 -	03/2016
98	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	4/2006	850.00 -	850.00	8.44	03/2015 -	03/2015
99	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	4/2008	653.19 -	653.46	137.10	03/2014 -	03/2014
100	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	813.34 -	1,141.75	407.49	03/2014 -	03/2014
101	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114]	4/2008	516.23 -	516.23	219.56	03/2014 -	03/2014
102	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	16.68	03/2016 -	03/2016
103	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	4/2008	394.14 -	404.39	0.49	03/2013 -	03/2013
104	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	37.68 -	730.00	367.87	07/2012 07/2012	07/2012
105	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]	4/2008	829.74 -	829.74	5.83	03/2015 -	03/2015
106	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
	Total		12,004.80 -	15,371.64	1,352.06		
<u>Road Transport & Highways</u>							
107	Talegaon-amravati - [N24000140]	11/2009	567.00 -	567.00	471.21	11/2013 -	11/2013
108	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]	2/2011	193.45 -	193.45	29.71	11/2012 -	11/2012
109	MURADABAD-BAREILY - [N24000154]	4/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013
110	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	874.76	03/2013 -	03/2013
111	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	05/2013
112	Hazaribagh-Ranchi - [N24000141]	8/2010	625.07 -	625.07	779.14	01/2013 -	01/2013
113	Jaipur-Tonk-Deoli - [N24000135]	6/2010	792.06 -	792.06	1,214.20	12/2012 -	12/2012
114	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
115	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	366.62	07/2013 -	07/2013
116	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	20.75	04/2014 -	04/2014
117	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	66.26	03/2014 -	03/2014
118	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
119	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	497.30	03/2014 -	03/2014
120	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	199.49	02/2014 -	02/2014
121	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	376.37	01/2014 -	01/2014
122	Kandla - Mundra port - [N24000175	1/2011	953.88 -	953.88	314.98	07/2013 -	07/2013
123	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	148.11	06/2014 -	06/2014
124	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
125	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	498.45	08/2013 -	08/2013
126	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	594.39	08/2013 -	08/2013
127	MUZAFFARNAGAR-HARIDWAR - [N24000201	9/2011	754.00 -	754.00	335.29	03/2013 -	03/2013
128	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	87.11	09/2013 -	09/2013
129	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	155.04	06/2014 -	06/2014
130	JAIPUR-REENGUS - [N24000198	8/2010	267.81 -	267.81	452.55	02/2013 -	02/2013
131	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	120.31	09/2014 -	09/2014
132	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
133	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	329.47	08/2013 -	08/2013
134	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	259.06	01/2014 -	01/2014
135	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	-	01/2014 -	01/2014
136	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	150.00	02/2014 -	02/2014
137	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	115.63	05/2014 -	05/2014
138	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
139	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
140	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.85	06/2013 -	06/2013
141	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	4.93	12/2013 -	12/2013
142	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
143	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	662.22	08/2013 -	08/2013
144	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	734.10	11/2013 -	11/2013
145	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168	3/2011	785.50 -	785.50	507.92	08/2013 -	08/2013
146	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013
147	SAMAIKHIALI - GANDHIDHAM - [N24000179	9/2010	805.39 -	805.39	228.54	03/2013 -	03/2013
148	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
149	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	56.11	08/2013 -	08/2013
150	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	55.89	05/2013 -	05/2013
151	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	580.92	02/2013 -	02/2013
152	NASHRI CHANANI - [N24000162	6/2010	2,159.00 -	2,159.00	-	06/2015 -	06/2015
153	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	-	07/2015 -	07/2015
154	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4 - [N24000139	9/2010	1,655.00 -	1,655.00	393.71	09/2013 -	09/2013
155	Indore-Jhabua-Gujrat/MP - [N24000136	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
156	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125	3/2010	1,509.10 -	1,509.10	1,299.10	09/2012 -	09/2012
157	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144	9/2010	852.00 -	852.00	634.99	03/2013 -	03/2013
158	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	364.02	08/2014 -	08/2014
159	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	797.01	10/2014 -	10/2014
160	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134	4/2010	1,740.00 -	1,740.00	1,744.70	10/2012 -	10/2012
161	DEOLI-KOTA - [N24000148	1/2011	953.00 -	593.00	339.12	07/2013 -	07/2013
	Total		53,837.59 -	53,477.59	22,410.91		

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Shipping & Ports</u>						
162	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS - [N25000031	8/2008	1,066.91 -	968.35	648.62	09/2012 -	09/2012
163	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 -	1,028.10	371.96	12/2013 -	12/2013
164	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
	Total		3,061.47 -	2,991.27	1,268.81		
	<u>Urban Development</u>						
165	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	426.52	03/2016 -	03/2016
166	FARIDABAD EXTENSION - [N28000057	9/2011	2,494.00 -	2,494.00	56.69	09/2014 -	09/2014
	Total		37,736.00 -	37,736.00	483.21		
	Grand Total		274,069.03	281,307.45	54,046.86		

List of Projects Without Milestones

(Jul,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 04/2011	04/2012	0/0
	Total		1,106.29 -			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	08/2012	0/0
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBT AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 03/2012	10/2012	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	04/2013	0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT - [N04000070]AAI,Punjab	02/2011	452.00 -	02/2015 -	02/2015	0/0
	Total		5,473.58 -			0/0
<u>Coal</u>						
8	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	03/2014 -	03/2014	0/0
9	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	04/2014 -	04/2014	0/0
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	03/2012 03/2015	03/2015	0/0
11	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	03/2016 -	03/2016	0/0
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 03/2018	03/2018	0/0
	Total		3,868.49 -			0/0
<u>Fertilisers</u>						
14	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012	0/0
15	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		763.00			0/0
			-			
	<u>Steel</u>					
16	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL,Maharashtra	12/2011	187.33	10/2013	12/2013	0/0
			-	-		
	Total		187.33			0/0
			-			
	<u>Petroleum</u>					
17	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	04/2012	04/2012	0/0
			-	-		
18	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40	05/2010	07/2012	0/0
			837.54	04/2012		
19	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	04/2011	08/2012	0/0
			-	-		
20	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	09/2011	09/2012	0/0
			2,730.00	03/2012		
21	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	01/2012	09/2012	0/0
			12,160.26	-		
22	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	09/2012	09/2012	0/0
			-	09/2012		
23	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29	05/2010	10/2012	0/0
			6,326.40	05/2012		
24	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70	03/2011	10/2012	0/0
			755.76	05/2011		
25	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	07/2012	10/2012	0/0
			-	-		
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	06/2012	12/2012	0/0
			-	-		
27	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	12/2011	01/2013	0/0
			-	-		
28	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	05/2010	03/2013	0/0
			8,813.41	03/2013		
29	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04	08/2012	03/2013	0/0
			288.04	-		
30	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	04/2006	04/2013	0/0
			2,735.65	06/2012		
31	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	12/2008	04/2013	0/0
			3,690.37	04/2013		
32	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	09/2010	04/2013	0/0
			2,920.82	03/2012		
33	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	03/2013	04/2013	0/0
			-	-		
34	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	03/2010	05/2013	0/0
			-	03/2012		
35	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21	07/2010	05/2013	0/0
			1,456.96	05/2012		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
36	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
37	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	06/2013	0/0
38	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	08/2013	0/0
39	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
40	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
41	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	10/2013	0/0
42	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
43	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
44	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
45	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
46	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
47	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0
48	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
49	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
50	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00 -	03/2014 -	03/2014	0/0
51	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	04/2014	0/0
52	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
53	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
54	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
55	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
56	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
57	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
58	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
59	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
60	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
61	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
62	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-	0/0
	Total		103,922.35	-		0/0
Power						
63	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	04/2012	0/0
64	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	10/2010 01/2013	01/2013	0/0
65	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	07/2013	07/2013	0/0
66	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	09/2009 06/2013	08/2013	0/0
67	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	01/2012	09/2013	0/0
68	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97	12/2013	12/2013	0/0
69	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	03/2014	03/2014	0/0
70	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	08/2014	08/2014	0/0
71	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	09/2014	09/2014	0/0
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63	11/2014	11/2014	0/0
73	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	11/2014	11/2014	0/0
74	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	02/2015	02/2015	0/0
75	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47	09/2016	09/2016	0/0
76	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18	11/2016	11/2016	0/0
77	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19	12/2016	12/2016	0/0
	Total		45,879.13	-		0/0
Railways						
78	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	07/2005	07/2005	0/0
79	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
80	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
81	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
82	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
83	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 371.36	- 03/2010	03/2010	0/0
84	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010	0/0
85	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
86	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
87	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
88	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
89	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
90	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
91	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
92	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
93	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
94	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
95	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
96	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011	0/0
97	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
98	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011	0/0
99	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
100	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
101	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
102	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
103	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
104	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
105	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
106	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
107	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
108	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
109	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
110	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012	0/0
111	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	06/2011 03/2012	03/2012	0/0
112	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
113	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
114	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	03/2012 -	03/2012	0/0
115	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012	0/0
116	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012	0/0
117	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 07/2012	07/2012	0/0
118	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	10/2012	0/0
119	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	10/2012	0/0
120	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
121	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
122	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 921.00	03/2009 12/2012	12/2012	0/0
123	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	10/2007 12/2012	12/2012	0/0
124	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
125	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
126	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
127	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
128	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	02/2013	0/0
129	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
130	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
131	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
132	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
133	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2013	0/0
134	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
135	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	03/2013	0/0
136	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
137	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
138	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013	0/0
139	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2013	0/0
140	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
141	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2013	0/0
142	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
143	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
144	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	03/2013	0/0
145	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 -	03/2013 -	03/2013	0/0
146	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
147	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
148	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
149	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	05/2013	0/0
150	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
151	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
152	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	02/2006 -	12/2013	0/0
153	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
154	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
155	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
156	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
157	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
158	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2014	0/0
159	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	03/2014	0/0
160	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
161	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
162	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
163	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2014	0/0
164	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014	0/0
165	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
166	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
167	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
168	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015	0/0
169	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	04/2014 -	03/2015	0/0
170	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
171	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
172	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2015	0/0
173	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
174	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	12/2015	0/0
175	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
176	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	03/2011 03/2014	03/2016	0/0
177	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
178	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
179	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
180	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	03/2016 -	03/2016	0/0
181	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
182	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
183	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
184	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 -	03/2001 -	12/2017	0/0
185	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
186	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
187	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
188	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
189	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.20	- -	-	0/0
190	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-	0/0
191	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-	0/0
192	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
193	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
195	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
196	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-	0/0
197	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
198	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-	0/0
199	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
200	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
201	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 227.40	- -	-	0/0
202	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-	0/0
Total			64,090.49 -			0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
Road Transport & Highways						
203	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	09/2007	03/2013	0/0
204	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	11/2008	09/2012	0/0
205	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	07/2008	12/2012	0/0
206	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	04/2004	07/2012	0/0
207	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09	03/2008	07/2012	0/0
208	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	02/2004	07/2012	0/0
209	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	02/2004	07/2012	0/0
210	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	02/2012	07/2012	0/0
211	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	08/2004 07/2010	08/2012	0/0
212	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	08/2004	08/2012	0/0
213	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	05/2008	08/2012	0/0
214	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	10/2008	08/2012	0/0
215	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	05/2012	08/2012	0/0
216	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	09/2007	09/2012	0/0
217	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	09/2007	09/2012	0/0
218	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	06/2005	09/2012	0/0
219	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	10/2008	09/2012	0/0
220	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91	10/2008	09/2012	0/0
221	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	09/2012	09/2012	0/0
222	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	05/2012	09/2012	0/0
223	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	08/2011	09/2012	0/0
224	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	03/2005	10/2012	0/0
225	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	06/2010	10/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
226	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17 -	09/2009 -	10/2012	0/0
227	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
228	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2012	0/0
229	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
230	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
231	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
232	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	03/2008 -	12/2012	0/0
233	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2012	0/0
234	DAKOPA TO NAGAON (NH-36) (NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	06/2008 -	12/2012	0/0
235	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2) (NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
236	FORBESGANJ TO SIMRAHI (NH-57) (NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
237	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
238	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
239	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	09/2008 -	12/2012	0/0
240	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	06/2008 -	12/2012	0/0
241	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
242	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
243	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
244	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	12/2008 -	12/2012	0/0
245	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
246	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93 -	10/2009 -	12/2012	0/0
247	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	12/2009 -	12/2012	0/0
248	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2012	0/0
249	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
250	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	01/2011 -	12/2012	0/0
251	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
252	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP- PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	12/2012	0/0
253	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	12/2012	0/0
254	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	12/2012	0/0
255	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
256	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	01/2013	0/0
257	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	02/2013	0/0
258	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
259	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
260	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
261	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2013	0/0
262	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
263	BIJNI TO ASSAM WB BORDER (NH- 31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2013	0/0
264	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	03/2013	0/0
265	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	03/2013	0/0
266	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	03/2013	0/0
267	DHARAMTUL TO SONAPUR,KM 205-183 (AS- 20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	03/2013	0/0
268	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	03/2013	0/0
269	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
270	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
271	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
272	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
273	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
274	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
275	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
276	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
277	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	09/2007 -	06/2013	0/0
278	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
279	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
280	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
281	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
282	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
283	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	01/2013 -	06/2013	0/0
284	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
285	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
286	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0
287	Kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0
288	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
289	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
290	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
291	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
292	Dindigul - Kumli - [N24000177]NHAI, Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
293	BHUBANESWAR TO PURI - [N24000195]NHAI, Orissa	03/2011	500.29 -	08/2013 -	08/2013	0/0
294	4-laning of Faraka-Raiganj - [N24000202]NHAI, Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
295	4-laning of Brahmapore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
296	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
297	New 4 Lane elevated road from Chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
298	BAREILLY-SITAPUR - [N24000200]NHAI, Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
299	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
300	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
301	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00	11/2013	11/2013	0/0
302	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	11/2013	11/2013	0/0
303	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54	11/2013	11/2013	0/0
304	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	02/2010	12/2013	0/0
305	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
306	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
307	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	11/2008	01/2014	0/0
308	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00	01/2014	01/2014	0/0
309	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00	01/2014	01/2014	0/0
310	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00	01/2014	01/2014	0/0
311	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00	05/2013	02/2014	0/0
312	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00	02/2014	02/2014	0/0
313	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00	02/2014	02/2014	0/0
314	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	10/2008	03/2014	0/0
315	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	10/2011	03/2014	0/0
316	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	08/2012	03/2014	0/0
317	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	05/2013	03/2014	0/0
318	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, Multi State	09/2011	2,848.00	03/2014	03/2014	0/0
319	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	03/2014	03/2014	0/0
320	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	07/2009	04/2014	0/0
321	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00	02/2014	04/2014	0/0
322	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09	04/2014	04/2014	0/0
323	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	02/2009 05/2014	05/2014	0/0
324	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	09/2007	05/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
325	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
326	2laning with PS Gopalganj- Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
327	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
328	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
329	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
330	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
331	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
332	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
333	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
334	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
335	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
336	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
337	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
338	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
339	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	-	0/0
	Total		86,898.60 -			0/0
Shipping & Ports						
340	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008	0/0
341	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
342	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
343	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 08/2012	08/2012	0/0
344	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 -	09/2012	0/0
345	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	06/2011 09/2012	09/2012	0/0
346	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 10/2012	10/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
347	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	10/2012	0/0
348	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
349	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
350	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
351	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0
352	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 05/2013	05/2013	0/0
353	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	03/2006 06/2013	06/2013	0/0
354	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2013	0/0
355	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013	0/0
356	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
357	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		16,087.68 -			0/0
Telecommunications						
358	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
359	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 03/2008	07/2012	0/0
360	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	12/2008 -	07/2012	0/0
361	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	09/2012	0/0
362	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	09/2012	0/0
363	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	09/2012	0/0
364	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	09/2012	0/0
365	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	09/2012	0/0
366	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 12/2012	12/2012	0/0
367	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2012	02/2013	0/0
368	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
369	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
370	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
371	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
372	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
	Total		6,161.00 -			0/0
Urban Development						
373	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
374	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
375	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
376	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			372,831.02			0/0

List of Delay Project w.r.t Original and Revised

(Jul,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	14,886.00	12/2008	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,826.00	12/2015	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,123.00	12/2016	03/2017	3	-
Total			36,950.00	41,049.00	17,835.00				
<u>Civil Aviation</u>									
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	124.35	05/2012	08/2012	3	-
5	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,025.63	05/2011 03/2012	10/2012	17	7
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	183.01	01/2011 04/2013	04/2013	27	0
Total			2,587.58	2,970.07	2,332.99				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,447.14	06/2009	03/2013	45	-
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	108.26	03/2011	03/2013	24	-
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	333.97	03/2010	03/2013	36	-
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	95.40	03/2012	03/2013	12	-
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	38.14	03/2012	03/2013	12	-
12	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	104.51	03/2012	03/2013	12	-
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	105.28	03/2010	03/2014	48	-
14	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,141.68	03/2012	03/2014	24	-
15	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08	153.82	25.44	03/2011	03/2014	36	-
16	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	100.28	03/2012	03/2014	24	-
17	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	34.45	03/2011	03/2014	36	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
18	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	60.69	03/2012	03/2014	24	-
19	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34	779.26	301.72	03/2013 09/2012	10/2014	19	25
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	161.94	03/2012 03/2015	03/2015	36	0
21	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.82	03/2011	03/2015	48	-
22	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	1.20	03/2012	03/2015	36	-
23	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	117.82	03/2010	03/2015	60	-
24	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	72.66	12/2012	03/2015	27	-
25	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	338.98	03/2014 03/2016	03/2016	24	0
26	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	19.23	07/2012	03/2016	44	-
27	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	261.91	03/2014	03/2016	24	-
28	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.82	03/2014	03/2016	24	-
29	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24	-
30	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24	-
Total			15,050.88	16,362.23	7,872.34				
			-	-					
Fertilisers									
31	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	239.93	07/2011	07/2012	12	-
Total			438.00	438.00	239.93				
			-	-					
Steel									
32	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	332.15	12/2011 03/2012	10/2012	10	7
33	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	246.19	08/2010 08/2010	10/2012	26	26
34	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	91.83	10/2012 10/2012	12/2012	2	2
35	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	248.53	02/2011 02/2011	12/2012	22	22
36	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	205.20	05/2012 05/2012	02/2013	9	9

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
37	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,661.03	10/2009 03/2013	03/2013	41	0
38	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,027.62	12/2012 -	03/2013	3	-
39	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	-	10/2013 -	12/2013	2	-
Total			13,128.22 -	17,320.76	11,812.55				
<u>Petroleum</u>									
40	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	656.90	05/2010 04/2012	07/2012	26	3
41	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	227.95	04/2011 -	08/2012	16	-
42	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	194.79	03/2012 08/2012	08/2012	5	0
43	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,775.82	03/2012 08/2012	08/2012	5	0
44	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	719.92	04/2011 12/2011	09/2012	17	9
45	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,282.33	09/2011 03/2012	09/2012	12	6
46	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	215.65	03/2012 -	09/2012	6	-
47	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,887.74	01/2012 -	09/2012	8	-
48	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,553.85	05/2010 05/2012	10/2012	29	5
49	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19	17
50	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	600.66	07/2012 -	10/2012	3	-
51	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,140.31	06/2012 -	12/2012	6	-
52	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	411.99	12/2011 -	01/2013	13	-
53	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84	0
54	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,987.43	05/2010 03/2013	03/2013	34	0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
55	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012 -	03/2013	7	-
56	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	04/2013	84	10
57	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
58	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,279.74	09/2010 03/2012	04/2013	31	13
59	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	59.59	03/2013 -	04/2013	1	-
60	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	987.59	12/2012 12/2012	04/2013	4	4
61	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38	14
62	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	865.55	07/2010 05/2012	05/2013	34	12
63	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	400.00	250.00	07/2012 07/2012	06/2013	11	11
64	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	43.73	09/2012 -	06/2013	9	-
65	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	08/2013	23	-
66	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,930.41	09/2012 -	09/2013	12	-
67	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	46.52	11/2012 -	10/2013	11	-
68	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	10/2013	16	-
69	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
70	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,739.13	08/2010 03/2012	12/2013	40	21
71	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5	-
72	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84	0
73	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	870.16	03/2013 -	03/2014	12	-
74	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	345.62	03/2013 -	04/2014	13	-
75	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.48	10/2010 -	12/2014	50	-
76	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30	-
77	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120	0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
Total			78,820.61	87,908.50	49,595.82				
<u>Power</u>									
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	183.98	11/2011	08/2012	9	-
79	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	136.48	07/2011	08/2012	13	-
80	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	109.98	06/2012	08/2012	2	-
81	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	746.85	02/2011 10/2012	10/2012	20	0
82	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	327.05	07/2011	10/2012	15	-
83	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,047.91	02/2012	10/2012	8	-
84	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,535.59	03/2007 09/2012	12/2012	69	3
85	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,830.60	09/2008	12/2012	51	-
86	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	867.25	10/2009	12/2012	38	-
87	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	5,221.23	3,139.11	07/2010	12/2012	29	-
88	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	952.10	06/2012	12/2012	6	-
89	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	624.86	05/2012	12/2012	7	-
90	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	730.80	08/2012	12/2012	4	-
91	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,716.00	1,877.52	10/2010 01/2013	01/2013	27	0
92	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	779.27	08/2010 01/2013	01/2013	29	0
93	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29	2,083.00	1,757.40	11/2009 02/2013	02/2013	39	0
94	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	557.24	550.67	01/2010	02/2013	37	-
95	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,263.00	08/2012	03/2013	7	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
96	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	314.26	11/2011 -	03/2013	16	-
97	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	150.31	11/2011 -	03/2013	16	-
98	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,933.44	08/2012 -	03/2013	7	-
99	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,196.70	08/2012 -	03/2013	7	-
100	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,614.00	10/2012 -	03/2013	5	-
101	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,373.00	10/2012 -	03/2013	5	-
102	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	853.62	12/2012 -	03/2013	3	-
103	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	427.61	11/2012 -	03/2013	4	-
104	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	45.26	10/2012 -	03/2013	5	-
105	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,410.14	11/2012 -	06/2013	7	-
106	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,159.82	09/2009 06/2013	08/2013	47	2
107	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,865.80	01/2012 -	09/2013	20	-
108	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,851.57	10/2012 -	09/2013	11	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	469.25	04/2013 -	10/2013	6	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	326.72	11/2011 -	12/2013	25	-
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	235.36	02/2012 -	12/2013	22	-
112	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,373.00	04/2009 03/2014	03/2014	59	0
113	BARH STTP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,416.00	08/2013 -	06/2014	10	-
114	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	357.17	08/2012 08/2013	09/2014	25	13

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
115	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Mult State	02/2009	11,130.19	11,130.19	4,888.35	08/2013	09/2014	13	-
116	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,199.00	07/2011	11/2014	40	-
117	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63	913.63	338.39	07/2014	02/2015	7	-
118	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,489.00	03/2013	09/2015	30	-
119	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00	2,978.86	337.26	07/2010	02/2016	67	0
120	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	7,201.00	12/2009	03/2016	75	15
121	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	3,422.44	313.27	07/2014	05/2016	22	-
122	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67	3,642.00	1,593.45	01/2016	11/2016	10	10
123	SUBANSIRI LOWER H.E.P. (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	10,667.00	5,703.24	09/2010	12/2016	75	28
124	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,905.06	05/2013	03/2017	46	9
125	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	5,366.00	3,505.23	09/2009	12/2017	99	41
Total			126,828.74	140,014.57	85,306.70				
Railways									
126	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00	262.82	231.34	03/2012	10/2012	7	7
127	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07	456.45	293.29	06/2004	12/2012	102	-
128	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81	500.00	414.03	03/2012	12/2012	9	9
129	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00	1,115.63	756.19	03/2009	12/2012	45	0
130	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47	1,389.98	1,484.78	10/2007	12/2012	62	0
131	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	595.56	03/2010	12/2012	33	-
132	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44	1,115.21	877.21	12/2012	01/2013	1	0
133	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00	1,043.56	651.57	03/2012	02/2013	11	6
134	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Mult State	04/1998	92.63	270.00	260.18	02/2011	02/2013	24	24
135	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Mult State	04/2000	138.00	607.09	393.46	12/2012	02/2013	2	2

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
136	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	552.50	03/1995 -	03/2013	216	-
137	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	201.83	03/2002 -	03/2013	132	-
138	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	554.16	12/2011 12/2011	03/2013	15	15
139	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	269.10	03/2012 03/2013	03/2013	12	0
140	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	388.99	03/2012 03/2013	03/2013	12	0
141	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	96.75	03/2012 -	03/2013	12	-
142	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	248.66	02/2009 02/2009	04/2013	50	50
143	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	210.88	03/2009 03/2009	04/2013	49	49
144	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	134.80	12/2012 -	05/2013	5	-
145	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	105.94	12/2011 11/2013	11/2013	23	0
146	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	261.70	47.35	02/2006 -	12/2013	94	-
147	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,161.45	03/2009 -	12/2013	57	-
148	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	191.38	03/2004 12/2010	03/2014	120	39
149	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,275.88	12/2008 -	03/2014	63	-
150	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	155.76	06/2013 06/2013	03/2014	9	9
151	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	329.78	03/2013 -	03/2014	12	-
152	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	108.83	12/2012 -	03/2014	15	-
153	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	820.40	150.01	03/2010 06/2014	06/2014	51	0
154	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	166.75	03/2007 03/2007	03/2015	96	96
155	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	730.92	12/2010 12/2010	03/2015	51	51
156	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	11.78	04/2014 -	03/2015	11	-
157	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92	21

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
158	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 529.23	529.23	225.10	02/2010 -	12/2015	70	-
159	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 -	4,444.00	843.10	03/2011 03/2014	03/2016	60	24
160	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	5,300.00	850.42	03/2014 03/2016	03/2016	24	0
161	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	2,069.60	27.66	03/2014 03/2016	03/2016	24	0
162	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	1,412.74	446.94	03/2005 12/2008	06/2016	135	90
163	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,086.41	421.08	06/2005 07/2011	06/2016	132	59
164	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	22.34	03/2016 -	06/2016	3	-
165	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 -	20,000.00	7,947.68	03/2001 -	12/2017	201	-
	Total		25,960.83 -	66,031.07	28,243.53				
Road Transport & Highways									
166	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	200.06	09/2007 -	03/2013	66	-
167	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	-	11/2008 -	09/2012	46	-
168	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	-	07/2008 -	12/2012	53	-
169	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00 -	241.53	116.80	04/2004 -	07/2012	99	-
170	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09 -	166.30	189.15	03/2008 -	07/2012	52	-
171	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	263.27	265.81	02/2004 -	07/2012	101	-
172	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70 -	228.70	188.72	02/2004 -	07/2012	101	-
173	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	07/2012	5	-
174	Haveri-Harihar (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	179.10	08/2004 07/2010	08/2012	96	25
175	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	184.41	08/2004 -	08/2012	96	-
176	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	205.95	05/2008 -	08/2012	51	-
177	SAGAR BY PASS, KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30	187.27	10/2008 -	08/2012	46	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
178	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	506.40	05/2012	08/2012	3	-
179	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	304.29	09/2007	09/2012	60	-
180	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	273.84	09/2007	09/2012	60	-
181	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	225.24	06/2005	09/2012	87	-
182	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.34	10/2008	09/2012	47	-
183	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	255.82	10/2008	09/2012	47	-
184	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,003.30	05/2012	09/2012	4	-
185	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,649.60	08/2011	09/2012	13	-
186	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	10/2012	91	-
187	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	185.64	06/2010	10/2012	28	-
188	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	10/2012	37	-
189	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16	-
190	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,906.80	05/2012	10/2012	5	-
191	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	11/2012	41	-
192	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	379.89	03/2008	12/2012	57	-
193	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	256.42	01/2009	12/2012	47	-
194	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	278.06	06/2008	12/2012	54	-
195	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	243.92	06/2008	12/2012	54	-
196	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	371.68	09/2008	12/2012	51	-
197	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	231.38	10/2008	12/2012	50	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
198	RAJMARG CHORHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	251.03	303.96	10/2008	12/2012	50	-
199	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	521.77	09/2008	12/2012	51	-
200	NALBARI TO BIJINI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	273.71	06/2008	12/2012	54	-
201	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	145.60	04/2008	12/2012	56	-
202	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	363.00	248.66	06/2011	12/2012	18	18
203	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	204.40	04/2008	12/2012	56	-
204	NALBARI T BIJINI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	262.54	04/2008	12/2012	56	-
205	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48	-
206	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	201.07	04/2010	12/2012	32	-
207	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38	-
208	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	494.29	12/2009	12/2012	36	-
209	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	468.34	09/2009	12/2012	39	-
210	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	252.87	09/2010	12/2012	27	-
211	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	535.16	01/2011	12/2012	23	-
212	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	578.08	05/2010	12/2012	31	-
213	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,141.10	07/2012	12/2012	5	-
214	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6	-
215	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	2,488.40	10/2011	12/2012	14	-
216	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	02/2013	25	-
217	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	201.66	118.85	09/2008	03/2013	54	-
218	KOTWA TO DEWAPUR (10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	285.56	10/2008	03/2013	53	-
219	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	108.63	04/2009	03/2013	47	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
220	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	201.47	06/2008	03/2013	57	-
221	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	266.72	06/2008	03/2013	57	-
222	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.21	03/2008	03/2013	60	-
223	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	231.87	06/2008	03/2013	57	-
224	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	172.56	05/2008	03/2013	58	-
225	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	227.95	06/2008	03/2013	57	-
226	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	03/2013	32	-
227	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	162.31	09/2007	06/2013	69	-
228	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	663.32	10/2011	06/2013	20	-
229	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,038.80	11/2012	06/2013	7	-
230	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.77	01/2013	06/2013	5	-
231	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	56.76	04/2009	07/2013	51	-
232	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	87.37	11/2008	07/2013	56	-
233	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,459.20	11/2011	08/2013	21	-
234	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46	-
235	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	15.49	11/2008	01/2014	62	-
236	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	369.11	05/2013	02/2014	9	-
237	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.23	10/2008	03/2014	65	-
238	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	339.37	10/2011	03/2014	29	-
239	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2014	19	-
240	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	163.93	05/2013	03/2014	10	-
241	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	196.00	55.07	07/2009	04/2014	57	-
242	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00	664.00	15.10	02/2014	04/2014	2	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
243	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	268.46	02/2009 05/2014	05/2014	63	0
244	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	212.00	71.47	09/2007 -	05/2014	80	-
245	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
246	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	33.22	09/2013 -	07/2014	10	-
247	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
Total			33,091.24 -	34,800.90	35,926.10				
<u>Shipping & Ports</u>									
248	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8	0
249	Acquisition of two nos. of 120 B.P BY 079&080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	86.46	06/2011 09/2012	09/2012	15	0
250	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18	0
251	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,345.60	01/2012 09/2012	10/2012	9	1
252	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
253	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
254	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
255	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	187.07	12/2012 05/2013	05/2013	5	0
256	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	110.00	03/2006 06/2013	06/2013	87	0
257	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	823.49	12/2010 09/2012	10/2013	34	13
Total			8,446.14 -	10,038.71	5,212.73				
<u>Telecommunications</u>									
258	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	07/2012	79	52
259	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	07/2012	43	-

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
260	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	232.00	12/2008	09/2012	45	-
261	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009	09/2012	39	-
262	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	157.98	01/2009	09/2012	44	-
263	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	09/2012	42	-
264	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	804.06	11/2010	09/2012	22	-
265	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	29.27	10/2010 12/2012	12/2012	26	0
266	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72	11
	Total		3,163.25	3,167.12	1,672.95				
	<u>Urban Development</u>								
267	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013	15	-
	Total		6,395.00	11,609.00	2,267.57				
	<u>Water Resources</u>								
268	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60	-
	Total		542.90	1,187.00	35.49				
Grand Total			351,403.39	432,896.93	248,353.70				

List of ongoing projects having cost overrun w.r.to original

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	3,641.60	09/2010	01/2012
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	17,270.00	14,886.00	12/2008	03/2013
	Total		16,663.00	22,947.00	18,527.60		
	<u>Civil Aviation</u>						
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00	2,015.00	1,669.98	01/2011	02/2012
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51	2,325.00	2,025.63	05/2011	10/2012
	Total		3,750.51	27,287.00	22,223.21		
	<u>Coal</u>						
5	MAGADH OC (CCL) - [N06000015]	07/2006	469.78	706.40	19.23	07/2012	03/2016
6	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	25.44	03/2011	03/2014
7	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59	198.59	70.19	03/2016	03/2016
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	3,027.59	2,447.14	06/2009	03/2013
9	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34	779.26	301.72	03/2013	10/2014
10	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	645.16	03/2013	03/2013
11	MANIKPUR OC EXPANTION - [N06000081]	11/2009	321.42	321.50	203.55	03/2014	03/2014
12	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00	490.10	114.45	03/2017	03/2017
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	475.93	479.63	107.59	03/2013	03/2013
14	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	2,675.67	1,370.35	03/2014	03/2014
15	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53	1,943.66	1,197.18	03/2014	03/2014
16	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,909.54	3,141.68	03/2012	03/2014
	Total		12,779.19	44,161.07	31,866.89		

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Petrochemicals</u>						
17	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	5,090.47	12/2013 -	12/2013
	Total		5,460.61 -	53,081.07	36,957.36		
	<u>Petroleum</u>						
18	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	04/2013
19	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00 -	299.00	349.29	- -	-
20	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	1,279.74	09/2010 03/2012	04/2013
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	6,987.43	05/2010 -	03/2013
22	North Tapti Gas Field Development - [N16000096]	07/2008	589.70 755.56	755.76	549.84	03/2011 -	10/2012
23	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00 -	898.00	887.01	- -	08/2012
24	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29 -	6,326.40	5,553.85	05/2010 -	10/2012
25	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	3,739.13	08/2010 03/2012	12/2013
26	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40 -	656.51	656.90	05/2010 -	07/2012
27	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]	07/2009	238.68 -	276.00	180.54	- -	09/2012
28	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	594.10	03/2007 -	03/2014
29	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	438.85	265.66	03/2006 -	03/2013
30	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
31	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	04/2008	825.00 -	1,827.00	611.55	04/2013 -	04/2013
32	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	1,481.56	03/2007 -	03/2017
33	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	30,426.00	16,808.86	- -	09/2013
	Total		51,356.35 -	121,116.08	81,607.73		
	<u>Power</u>						
34	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	3,505.23	09/2009 -	12/2017
35	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	5,703.24	09/2010 -	12/2016

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222]	10/2003	768.92 -	1,628.00	1,535.59	03/2007 -	12/2012
37	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	1,159.82	09/2009 -	08/2013
38	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37 -	386.32	327.05	07/2011 -	10/2012
39	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	4,263.00	08/2012 -	03/2013
40	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	1,877.52	10/2010 -	01/2013
41	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,422.44	313.27	07/2014 -	05/2016
42	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	337.26	07/2010 -	02/2016
43	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,083.00	1,757.40	11/2009 -	02/2013
44	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	779.27	08/2010 -	01/2013
45	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26 -	913.00	746.85	02/2011 -	10/2012
46	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	1,593.45	01/2016 -	11/2016
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	1,830.60	09/2008 -	12/2012
48	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	7,201.00	12/2009 -	03/2016
49	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	840.20	12/2007 -	-
50	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	322.19	- -	07/2013
	Total		40,934.96 -	175,850.01	115,700.67		
Railways							
51	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]	04/1985	158.77 274.56	540.96	558.07	03/1994 -	12/2011
52	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	552.50	03/1995 -	03/2013
53	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135]	04/1983	36.80 274.41	703.17	242.01	- -	03/2015
54	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	600.41	- -	02/2012
55	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	262.82	231.34	03/2012 -	10/2012
56	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	712.00	732.04	- -	10/2012
57	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	1,260.07	07/2005 -	07/2005

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	877.21	12/2012 -	01/2013
59	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	730.92	12/2010 -	03/2015
60	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	320.09	- 05/2009	05/2009
61	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	559.17	- -	03/2012
62	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.00	751.22	- -	03/2013
63	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
64	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,009.20	12/2006 -	08/2010
65	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	260.18	02/2011 -	02/2013
66	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	522.30	- 12/2009	02/2012
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	393.46	12/2012 12/2012	02/2013
68	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	446.94	03/2005 12/2008	06/2016
69	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	500.00	414.03	03/2012 -	12/2012
70	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.00	219.71	- 09/2009	12/2011
71	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	1,115.63	756.19	03/2009 -	12/2012
72	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	232.01	- -	-
73	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	1,717.29	1,343.13	- -	03/2013
74	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	319.07	- 03/2009	03/2011
75	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	174.12	03/1998 08/2005	08/2005
76	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
77	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	67.86	02/2015 -	-
78	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	210.88	03/2009 03/2009	04/2013
79	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	112.01	- -	03/2013
80	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	227.39	12/2007 03/2010	12/2010
81	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	47.35	02/2006 -	12/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
82	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027	04/2005	240.00 -	355.00	396.62	03/2009 12/2009	03/2011
83	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079	09/2007	404.19 -	900.00	244.55	- -	-
84	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N22000080	09/2006	343.17 -	900.00	536.14	- -	12/2012
85	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	227.40	35.31	- -	-
86	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	582.83	129.43	- -	-
87	BARDHAMAN-KATWA (GC) - [N22000091	04/2007	245.15 -	1,106.62	199.16	12/2010 -	03/2011
88	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	11.78	04/2014 -	03/2015
89	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	179.50	- -	03/2015
90	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	388.99	03/2012 -	03/2013
91	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	164.89	- 03/2010	-
92	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU [N22000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
93	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.60	0.76	- -	-
94	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-
95	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093	04/2003	3,125.20 -	4,501.80	4,334.00	06/2011 -	03/2012
96	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111	04/2010	2,619.02 -	2,913.51	135.97	03/2016 -	03/2016
97	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113	04/2008	653.19 -	653.46	137.10	03/2014 -	03/2014
98	Dakshin-barasal-lakshmikantapur - [N22000116	04/2009	259.51 -	533.38	83.30	12/2011 -	02/2012
99	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125	04/2006	117.36 196.95	196.95	181.00	03/2011 -	03/2011
100	PANSPURA-KHARAGPUR 3D LINE - [N22000076	09/2007	252.50 -	529.23	225.10	02/2010 -	12/2015
101	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	201.83	03/2002 -	03/2013
102	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,200.00	165.33	- -	03/2013
103	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	452.35	410.12	- -	03/2010
104	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	191.38	03/2004 -	03/2014
105	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	554.16	12/2011 12/2010	03/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
106	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	3,230.01	2,408.10	04/2008 12/2011	12/2015
107	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	651.57	03/2012 -	02/2013
108	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	227.42	250.82	12/2009 -	03/2011
109	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	91.50	- -	03/2013
110	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,275.88	12/2008 -	03/2014
111	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,100.00	231.46	- -	03/2013
112	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	843.10	03/2011 -	03/2016
113	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	269.10	03/2012 -	03/2013
114	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	1,389.98	1,484.78	10/2007 -	12/2012
115	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	453.04	392.26	03/2011 -	03/2011
116	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083	09/1996	156.00 -	415.73	240.93	- -	03/2012
117	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086	09/2006	200.00 -	385.20	112.60	- -	03/2014
118	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	532.87	39.45	- -	-
119	Ghutiasharif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	105.94	12/2011 -	11/2013
120	Pandabeswar-Chinpai doubling (ER) - [N22000118	04/2004	225.68 -	293.74	136.57	12/2010 -	12/2010
121	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project [N22000127	04/1996	1,676.31 -	4,255.37	3,161.45	03/2009 -	12/2013
122	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,141.75	407.49	03/2014 -	03/2014
123	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	359.86	1.22	- -	03/2015
124	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
125	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,577.46	1,320.26	- -	03/2012
126	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	491.99	- -	03/2014
127	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	189.42	- -	03/2013
128	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	730.00	367.87	07/2012 -	07/2012

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
129	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	7,947.68	03/2001 -	12/2017
130	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.76	833.20	06/2007 -	06/2007
131	REWARI-ROHTAK (NL),NR - [220100279	01/2004	149.38 -	530.76	486.96	02/2010 -	02/2011
132	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	820.40	150.01	03/2010 -	06/2014
133	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	110.02	12/2012 -	-
134	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	248.66	02/2009 02/2009	04/2013
135	RENIGUNTA-GUNTAKAL(RE) - [220100260	06/2000	168.34 -	370.00	343.10	04/2003 03/2010	-
136	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	224.35	03/2010 -	03/2012
137	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012
138	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	621.61	02/2009 -	03/2012
139	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	131.21	- -	03/2012
140	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.35	07/2008 -	07/2008
141	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
142	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	166.75	03/2007 03/2007	03/2015
143	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,086.41	421.08	06/2005 -	06/2016
144	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	293.29	06/2004 -	12/2012
145	HUBLI-ANKOLA(NL),SWR - [220100193	04/1995	227.00 -	997.58	69.57	- -	-
146	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	341.37	- -	03/2011
147	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	496.59	- -	01/2013
148	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.29	- -	-
149	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	329.78	03/2013 -	03/2014
150	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	548.96	500.95	- -	-
151	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123	04/2008	318.24 -	468.62	0.99	03/2012 -	03/2012
152	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	04/2008	394.14 -	404.39	0.49	03/2013 -	03/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
153	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
154	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	580.85	- -	03/2012
155	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	653.84 654.51	1,302.12	608.97	06/2013 -	06/2012
156	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 175.30	548.95	523.76	06/1999 -	03/2011
157	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,214.00	96.96	- -	-
	Total		42,715.64 -	296,115.82	173,088.42		
<u>Road Transport & Highways</u>							
158	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00	205.95	05/2008 -	08/2012
159	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	56.76	04/2009 -	07/2013
160	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	87.37	11/2008 -	07/2013
161	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	116.80	04/2004 -	07/2012
162	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	162.31	09/2007 -	06/2013
163	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,459.20	11/2011 -	08/2013
164	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	118.85	09/2008 -	03/2013
165	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
166	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	161.40	03/2008 -	-
167	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50 -	363.00	248.66	06/2011 -	12/2012
	Total		3,112.78 -	301,174.18	177,884.95		
<u>Shipping & Ports</u>							
168	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00 -	1,460.00	823.49	12/2010 -	10/2013
169	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]	04/2009	290.85 -	305.00	86.46	06/2011 -	09/2012
170	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
171	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
172	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	3,345.60	01/2012 -	10/2012
173	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	326.08	04/2009 -	02/2011
174	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]	08/2010	612.72 -	627.64	187.07	12/2012 -	05/2013
175	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
176	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
177	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039]	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
	Total		8,732.54 -	311,753.72	183,231.81		
<u>Steel</u>							
178	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00 -	6,325.00	2,824.12	- -	10/2012
179	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00 -	17,265.00	6,043.92	- -	09/2013
180	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	13,558.10	- -	12/2012
181	Bailadila Iron Ore Deposit- II(B)(NMDC) - [N12000018]	01/2007	295.89 -	607.17	332.15	12/2011 06/2010	10/2012
182	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	9,661.03	10/2009 -	03/2013
183	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	230.00 -	343.58	248.53	02/2011 -	12/2012
184	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	91.83	10/2012 -	12/2012
185	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	350.00	246.19	08/2010 -	10/2012
	Total		32,529.89 -	365,560.15	216,237.68		
<u>Telecommunications</u>							
186	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15 -	158.72	76.55	06/2009 -	09/2012
187	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle [N26000090]	11/2009	916.70 -	930.60	804.06	11/2010 -	09/2012
	Total		1,065.85 -	366,649.47	217,118.29		

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Urban Development</u>						
188	C/o office building for IDBI at bandra Kurla Complex, Mumbai - [N28000048	11/2006	114.18 173.08	173.08	-	04/2009 -	-
189	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013
	Total		6,509.18 -	378,431.55	219,385.86		
	<u>Water Resources</u>						
190	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012
	Total		542.90 -	379,618.55	219,421.35		
	Grand Total		226,153.40	2,843,745.67	1,713,251.82		

List of ongoing projects having time and cost overrun w.r.to original

(Jul,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apxenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	17,270.00	14,886.00	12/2008 -	03/2013
	Total		13,171.00 -	17,270.00	14,886.00		
	<u>Civil Aviation</u>						
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037	08/2008	1,942.51 -	2,325.00	2,025.63	05/2011 -	10/2012
	Total		1,942.51 -	19,595.00	16,911.63		
	<u>Coal</u>						
3	MAGADH OC (CCL) - [N06000015	07/2006	469.78 -	706.40	19.23	07/2012 -	03/2016
4	RAJMAHAL OC EXP. - [N06000056	02/2006	50.08 -	153.82	25.44	03/2011 -	03/2014
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087	10/2004	2,030.78 -	3,027.59	2,447.14	06/2009 -	03/2013
6	ADRIYALA SHAFT PROJECT - [N06000016	09/2006	212.34 -	779.26	301.72	03/2013 -	10/2014
7	TUTICORIN THERMAL POWER PROJECT - [N06000047	05/2008	4,904.54 -	4,909.54	3,141.68	03/2012 -	03/2014
	Total		7,667.52 -	29,171.61	22,846.84		
	<u>Petroleum</u>						
8	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	04/2013
9	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,279.74	09/2010 03/2012	04/2013
10	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	6,987.43	05/2010 -	03/2013
11	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	549.84	03/2011 -	10/2012
12	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,553.85	05/2010 -	10/2012
13	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	3,739.13	08/2010 03/2012	12/2013
14	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044	05/2008	333.40 -	656.51	656.90	05/2010 -	07/2012
15	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	663.69	594.10	03/2007 -	03/2014
16	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	265.66	03/2006 -	03/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
18	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,481.56	03/2007 -	03/2017
	Total		19,535.67 -	63,480.62	48,659.96		
<u>Power</u>							
19	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,505.23	09/2009 -	12/2017
20	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,703.24	09/2010 -	12/2016
21	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,535.59	03/2007 -	12/2012
22	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,159.82	09/2009 -	08/2013
23	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.32	327.05	07/2011 -	10/2012
24	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,263.00	08/2012 -	03/2013
25	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,877.52	10/2010 -	01/2013
26	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	313.27	07/2014 -	05/2016
27	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	337.26	07/2010 -	02/2016
28	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,083.00	1,757.40	11/2009 -	02/2013
29	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	779.27	08/2010 -	01/2013
30	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	746.85	02/2011 -	10/2012
31	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,593.45	01/2016 -	11/2016
32	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,830.60	09/2008 -	12/2012
33	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,201.00	12/2009 -	03/2016
	Total		39,917.50 -	116,583.95	81,590.51		
<u>Railways</u>							
34	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	552.50	03/1995 -	03/2013
35	KADUR-CHIKMAGALUR-SAKLESH PUR (NL),(SWR) - [220100190	04/1996	157.00 -	262.82	231.34	03/2012 -	10/2012
36	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	877.21	12/2012 -	01/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
37	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	730.92	12/2010 -	03/2015
38	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	260.18	02/2011 -	02/2013
39	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	393.46	12/2012 12/2012	02/2013
40	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	446.94	03/2005 12/2008	06/2016
41	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	500.00	414.03	03/2012 -	12/2012
42	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	1,115.63	756.19	03/2009 -	12/2012
43	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	210.88	03/2009 03/2009	04/2013
44	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	47.35	02/2006 -	12/2013
45	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	11.78	04/2014 -	03/2015
46	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	388.99	03/2012 -	03/2013
47	PANSPURA-KHARAGPUR 3D LINE - [N22000076	09/2007	252.50 -	529.23	225.10	02/2010 -	12/2015
48	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	201.83	03/2002 -	03/2013
49	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	191.38	03/2004 -	03/2014
50	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	554.16	12/2011 12/2010	03/2013
51	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	3,230.01	2,408.10	04/2008 12/2011	12/2015
52	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	651.57	03/2012 -	02/2013
53	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,275.88	12/2008 -	03/2014
54	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	843.10	03/2011 -	03/2016
55	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	269.10	03/2012 -	03/2013
56	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	1,389.98	1,484.78	10/2007 -	12/2012
57	Ghutiasarif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	105.94	12/2011 -	11/2013
58	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	4,255.37	3,161.45	03/2009 -	12/2013
59	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	7,947.68	03/2001 -	12/2017
60	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	820.40	150.01	03/2010 -	06/2014

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
61	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	248.66	02/2009 02/2009	04/2013
62	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	166.75	03/2007 03/2007	03/2015
63	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,086.41	421.08	06/2005 -	06/2016
64	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	293.29	06/2004 -	12/2012
65	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	329.78	03/2013 -	03/2014
	Total		13,972.11 -	170,631.19	107,841.92		
<u>Road Transport & Highways</u>							
66	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	205.95	05/2008 -	08/2012
67	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	56.76	04/2009 -	07/2013
68	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	87.37	11/2008 -	07/2013
69	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	116.80	04/2004 -	07/2012
70	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	162.31	09/2007 -	06/2013
71	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,459.20	11/2011 -	08/2013
72	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	118.85	09/2008 -	03/2013
73	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
74	NEW MANGALORE PORT NH-17 AND 48 - [N24000040	04/2000	196.50 -	363.00	248.66	06/2011 -	12/2012
	Total		2,946.51 -	175,496.45	112,477.05		
<u>Shipping & Ports</u>							
75	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	823.49	12/2010 -	10/2013
76	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042	04/2009	290.85 -	305.00	86.46	06/2011 -	09/2012
77	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013
78	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00 -	4,150.00	3,345.60	01/2012 -	10/2012
79	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051	08/2010	612.72 -	627.64	187.07	12/2012 -	05/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
80	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
81	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
	Total		7,365.57 -	184,454.59	117,249.60		
<u>Steel</u>							
82	Bailadila Iron Ore Deposit- II(B)(NMDC) - [N12000018	01/2007	295.89 -	607.17	332.15	12/2011 06/2010	10/2012
83	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	9,661.03	10/2009 -	03/2013
84	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	230.00 -	343.58	248.53	02/2011 -	12/2012
85	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68	91.83	10/2012 -	12/2012
86	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00 -	350.00	246.19	08/2010 -	10/2012
	Total		9,585.89 -	198,263.02	127,829.33		
<u>Telecommunications</u>							
87	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	76.55	06/2009 -	09/2012
88	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70 -	930.60	804.06	11/2010 -	09/2012
	Total		1,065.85 -	199,352.34	128,709.94		
<u>Urban Development</u>							
89	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013
	Total		6,395.00 -	210,961.34	130,977.51		
<u>Water Resources</u>							
90	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012
	Total		542.90 -	212,148.34	131,013.00		
	Grand Total		124,108.03	1,597,408.45	1,040,993.29		

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
