


**308th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
June, 2011**



NPCIL - Kudankulam

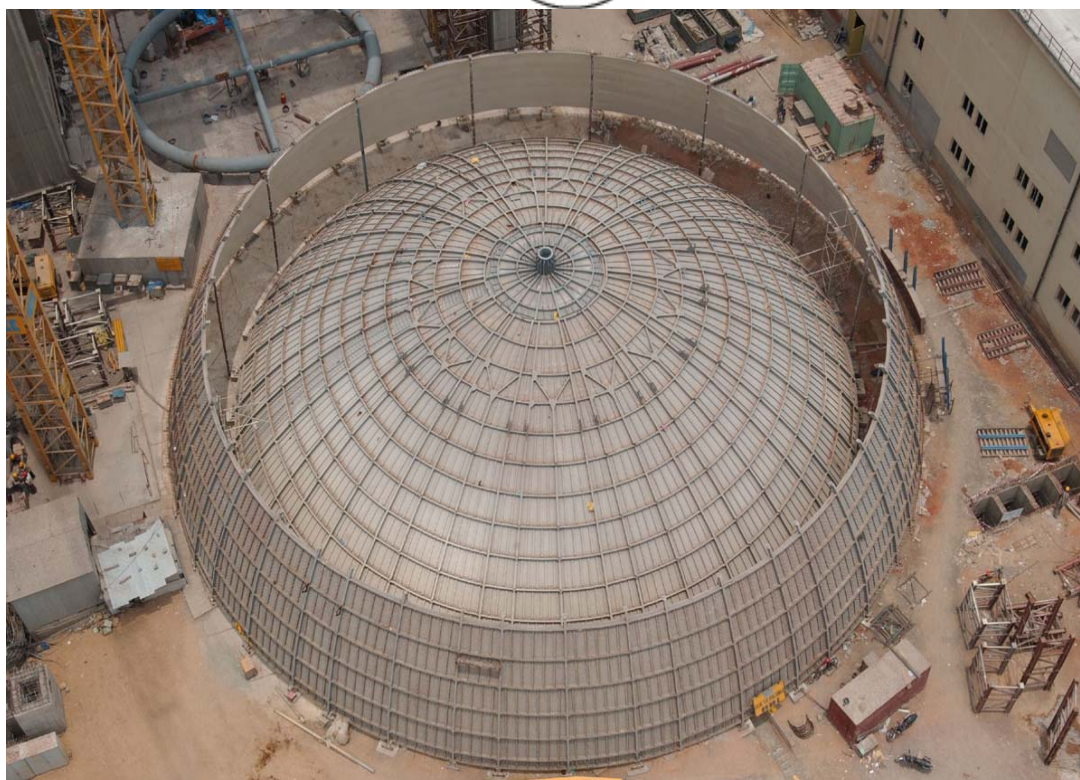

**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for June 2011 (the 308th Flash Report) contains information on the status of the 563 projects in the Central Sector costing ₹ . 150 Crores and above. During June 2011, nine projects have reported completion (which has now been dropped from the monitor of this Ministry).

The online submission of the implementation Status Report of the ongoing projects from the project authorities has improved considerably with majority of project authorities are reporting online during the current month due to the continuous effort/persuasion by this Ministry. However, NHAI, which has the largest number of projects is not reporting online in spite of repeated persuasion .During June 2011, sixty seven (67) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 18 months, in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	136	1
2.	ROAD TRANSPORT & HIGHWAYS	125	39
3.	POWER	83	10
4.	PETROLEUM	72	10
5.	COAL	45	1
6.	TELECOMMUNICATION	41	0
7.	SHIPPING & PORTS	26	0
8.	STEEL	15	3
9.	FERTILISERS	6	2
10.	CIVIL AVIATION	5	1
11.	ATOMIC ENERGY	4	0
12.	URBAN DEVELOPMENT	3	0
13.	MINES	1	0
14.	WATER RESOURCES	1	0
Total		563	67

3. The total original cost of implementation of the 563 projects was about ₹ 6,26,925.56 Crores and their anticipated completion cost is likely to be ₹ 7,52,140.93 Crores, which reflects an overall cost overrun of 20.00%. The expenditure incurred on these projects till June, 2011 is ₹ 3,36,176.40 Crores.

4. Out of the 563 projects, 8 projects are ahead of schedule, 138 are on schedule, 247 projects are delayed and 112 projects have been sanctioned without any commissioning schedule/date. Further, in case of 58 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month under reference the projects reporting delays have marginally increased to 247 from 244 in May'2011. The overall cost overrun has also increased to 20.00% from 19.90% in May 2011. Out of 247 delayed projects, at the end of June, 2011, 50 projects had overall delay in the range of 1 to 12 months, 57 projects had delay in the range of 13 to 24 months, 108 projects had delay in the range of 25 to 60 months and 32 projects had delay of 61 months and above.

The Sector-wise details of delays are as under:-

i) In the **Coal sector**, Penganga OC WCL has reported additional delay of seven months due to land acquisition problem & demand of higher compensations.

ii) In the **Steel sector**, 3 projects have reported additional delays in the range of 4-7 months. 67.5 MW TG-5 Auxiliary System Emergency Power Requirement project, RINL has reported an additional delay of 4 months (over all delay of due to delay in supply of fireclay and silica brick by the contractor). 330 TPH Boiler-6 and Auxiliary System RINL has reported an additional delay of 4 months due to delay in supply of equipments by BHEL. Expansion of RINL/Visakhapatnam Steel Plant from 3 MTPY – 6.3 MTPY of Liquid Steel has reported an additional delay of 7 months (over all delay of 36 months) due to incomplete bids along with large number of deviation with respect to NIT necessitating clarifications.

iii) In the **Petroleum Sector**, 10 projects have reported additional delays in the range of 1-16 months. Diesel Hydro Treatment Project Dhaligaon, BRPL has reported additional delay of one month (overall delay of 22 months) due to adverse weather conditions. MSQ Quality up-Gradation Project at Bongaigaon Refinery, IOCL has reported additional delay of one month (over all delay of 20 months) due to scarce technical resources availability in the region.

Karanpur Moradabad Kashipur Rudrapur Pipeline Project , GAIL has reported additional delay of one month due to farmers and land owners are demanding for re-routing the pipeline in kashipur area and also high compensation is being demanded. Construction of Tanks and Blending Facility at VAD, IOCL has reported an additional delay of two months due to slow progress of construction works. Heera Reconstruction, ONGC and Neelam Reconstruction, ONGC have reported an additional delay of 6 months each .However both the projects are nearing completion. MNW-NF Bridge Project ONGC has reported an additional delay of 9 months(over all delay of 35 months) due to revised execution methodology. Hydrocracker Revamp Setting up a New CCR at Mumbai BPCL has reported additional delay of 16 months due to poor mobilization by the main contractor. North Tapti Gas Field Development ONGC and Construction of 23 Immediate Supply Vessels (ISV), ONGC have reported an additional delay of one month and 5 months respectively, however no specific reason has been reported by the Project authorities.

iv) In the **Power Sector**, 10 projects have reported additional delays in the range of 1-12 months. Chamera Stage-III, NHPC and Mouda STPP, NTPC have reported an additional delay of one month each due to shortage of manpower. Chutak Hydro Electric Project, NHPC has reported an additional delay of two months (over all delay of 8 months) due to delay in supply of E & M by BHEL. [Sipat STPP Stage-I], NTPC has reported an additional delay of 3 months (over all delay of 27 months) due to delay in supply of equipments. Parbati H.E.P. Stage – III, NHPC has reported an additional delay of 3 months(over all delay of 17 months) due to labour related issue in NHPC. Tapovan Vishnugad Hydro Electric Project (HEP), NTPC has reported an additional delay of 4 months due to termination of contract in barrage & desilting chamber package . Nimoo Bazgo Hydro Electric Project, NHPC has reported an additional delay of 5 months(over all delay of 27 months) due to change in design of second stage river diversion. Bongaigaon Thermal Power Project, NTPC has reported an additional delay of 12 months due to delay in Turbo Generator erection slow progress by civil agency. Vishnugad Pipalkoti Hydro Electric Project, THDCL and Tehri Pumped Storage Plant, THDCL have reported an additional delay of two months and 10 months(over all delay of 22 months) respectively, however no specific reason has been reported by the project authorities.

v) In the **Road Transport and Highways Sector**, 39 projects have reported additional delay in the range of 1-18 months. 9 projects have reported additional delay of one month each due to slow progress of work by the contractor. Ayodha – Lucknow LMNHP-II, NHAI and Lalitpur to Sagar KM 132 to KM 187, NH-26 NHAI, have reported an additional delay of 2 months each due to delay in utility shifting. Thrissur to Angamali, NHAI and Nagpur –

Kondhali NH-6 ,NHAI have reported an additional delay of 2 months each due to delay in land acquisition. Jhansi to Lalitpur NH-26, NHAI has reported an additional delay of 2 months due to delay in handing over encumbrance free site. Haveri – Harihar (GQ) NH-4, NHAI, Harihar – Chitradurga (GQ)NH-4, NHAI and Haldia Port (Port Connectivity) have reported an additional delay of 3 months each due to poor performance by the contractor. Ayodhya Lucknow (LMNHP-1) NHAI has an additional delay of 3 months due to delay in cutting of trees . Sagar –Rajmarg chouraha,NH-26,NHAI has an additional delay of 3 months due to delay in finalization of design of flyover at Rajmarg Chouraha . Aurang- Raipur,NH-6,NHAI has an additional delay of 4 months due to delay in land acquisition . .Garmukteswar-Muradabad ,NHAI has an additional delay of 6 months due to delay in forest clearance .Hapur-Garmukteswar,NH-24, NHAI has an additional delay of 6 months due to delay in forest clearance .Kotwa- Deewapur,NH-28,NHAI has an additional delay of 6 months due to delay in shifting of electric poles .Gorakhpur- Ayodhya(LMNHP-5) NHAI, has an additional delay of 6 months due to delay in handing over encumbrance free site .Orai to Jhansi (UP-5),NHAI, has an additional delay of 6 months due to delay in utility shifting .UP/Bihar Border to Kasia,NHAI has an additional delay of 6 months due to delay in utility shifting .Forbesganj- to Simrahi,NHAI has an additional delay of 6 months due to delay in shifting of electric line .Lalitpur – Sagar,NH-26,NHAI has an additional delay of 6 months due to delay in forest clearance .Rajmarg chouraha – Lakhnadone,NH-26, NHAI has an additional delay of 6 months due to delay in tree cutting .Rajmarg chouraha to Lakhnadon and Sitapur – Lucknow,NHAI have an additional delay of 6 months each due to delay in tree cutting .Jhansi to Lalitpur,NH-26 and Gorakhpur Bypass,NH-28,NHAI, have an additional delay of 6 months each due to disruption by the locals at different places .Trichi-Korur ,NH-57,NHAI has an additional delay of 6 months due to delay in fixing of design consultants .Saleem-Undurpet,NH-68,NHAI has an additional delay of 6 months and Gagodhar – Garmore,NHAI has an additional delay of 2 months respectively and no any specific reasons has been reported by the project authority .Chilkaluripet- Vijaywada 6 lane,NHAI has an additional delay of 10 months ,however no any specific reasons has been reported by the project authority .Gwalior-Jhansi, NH-75, NHAI has an additional delay of 12 months due to problem in land acquisition .Ganjam- Ichhapuram, NH-5 ,NHAI has an additional delay of 18 months due to non-availability of encumbrance free site for ROB .However, NHAI is not providing any background information on projects .

vi) In the **Railway Sector**, Ratlam – Mhow – Khandwa – Akola (GC) WR has reported an additional delay of 12 months (overall delay of 12 months) due to land acquisition which is being pursued with district authorities.

vii) In the **Civil Aviation Sector**, Construction of Integrated Passenger Terminal Building NSCBI, Airport, AAI has reported an additional delay of 4 months(overall delay of 7 months), however no specific reason has been reported by the project authority.

viii) In the **Fertilisers Sector**, 2 projects have reported additional delay in the range of 4-8 months. Capacity Enhancement of Vijaipur – I Plants NFL has reported an additional delay of 4 months due to delay in supply of materials because of sudden price escalation of steel. Capacity Enhancement of Ammonia and Urea Plant VIJ, NFL has reported an additional delay of 8 months(overall delay of 8 months) . However reasons have not been specified.

The status as on 01.07.2011 in respect of completion of projects costing ₹150 Crores and above in different sectors during 2011-12 is indicated in the Report.



(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	136	1
2	Road Transport & Highways	125	39
3	Power	83	10
4	Petroleum	72	10
5	Coal	45	1
6	Telecommunications	41	0
7	Shipping & Ports	26	0
8	Steel	15	3
9	Fertilisers	6	2
10	Civil Aviation	5	1
11	Atomic Energy	4	0
12	Urban Development	3	0
13	Mines	1	0
14	Water Resources	1	0
	Total	563	67

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
	<u>Road Transport & Highways</u>			
13	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
	June,2011			
	<u>Petroleum</u>			
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
	<u>Power</u>			
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
	<u>Railways</u>			
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
	<u>Road Transport & Highways</u>			
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
	May,2011			
	<u>Civil Aviation</u>			
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97


Summary of projects in the Flash Report for the month of June, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	578
Number of Projects completed/dropped/frozen in Previous Month	11
Number of Projects completed/dropped/frozen in Current Month	9
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	4
Number of Projects Added in Current Month	1
Number of Projects in Current Month	563


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 563 projects, 8 projects are ahead of schedule, 138 projects are on schedule and 247 projects are delayed. Of the balance, 112 projects do not have fixed dates of commissioning while 58 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

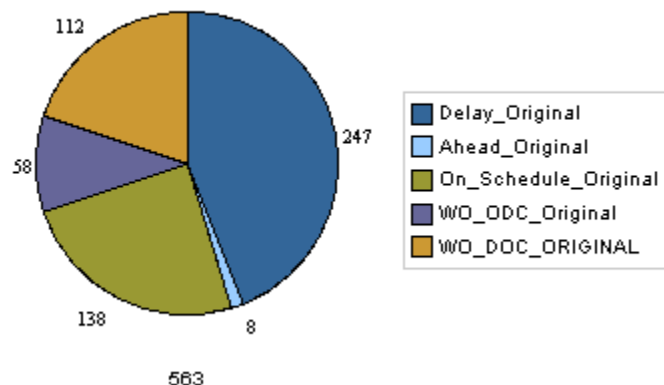

III. Investment Scenario

The Total Original cost of implementation of 563 projects when sanctioned, was of the order of Rs. 626925.56 crore but this was subsequently revised to Rs. 752140.93 crore implying a cost overrun of 20%. The expenditure incurred on these projects till June, 2011 is Rs. 336176.4 crore, which is 44.7% of the revised cost of the projects.

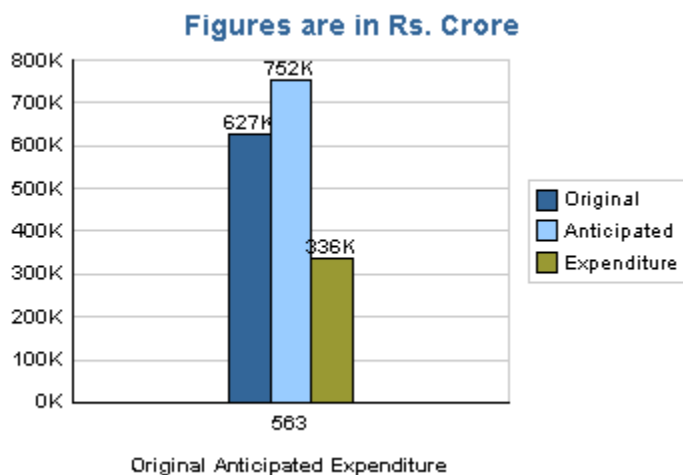

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	578
No of Projects Completed/Dropped/Frozen in Previous Month	11
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	4
No of Projects added in Current Month	1
No of Projects in Current Month	563

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	247	8	138	58	112	563	43.87
Latest Approved (Date)	271	10	180	37	64	563	48.13

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	446	489,578.43	538,416.20	217,956.13	40.50	48,837.77	10.00
Latest Approved (RCE)	117	189,390.94	213,724.73	118,220.27	55.30	24,333.79	12.80
Total (RCE)	563	678,969.37	752,140.93	336,176.40	44.70	73171.56	10.78
Original Cost of All Projects							
Original Cost	563	626,925.56	752,140.93	336,176.40	44.70	125,215.37	20.00

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	247	277,485.10	347,893.17	201,238.89	57.80	70,408.07	25.40
Latest Approved (RCE)	271	284,512.82	337,004.42	193,679.96	57.50	52,491.60	18.40

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	67	61,179.86	68,359.66	48,519.66	71.00	7,179.80	11.70

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	4,123.2	4,078.1	-1.1	0	0.0	0.0	0.0
3	Coal	45	25,504.2	28,789.6	12.9	10	12,935.0	16,916.0	30.8
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	7.6
6	Steel	15	41,398.4	68,476.4	65.4	11	39,254.2	66,332.2	69.0
7	Petroleum	72	155,657.8	164,213.0	5.5	17	25,194.5	42,422.6	68.4
8	Power	83	180,092.4	185,360.2	2.9	9	14,379.2	20,101.6	39.8
9	Railways	136	66,510.0	123,008.2	84.9	102	37,314.1	93,912.4	151.7
10	Road Transport & Highways	125	60,796.9	62,260.3	2.4	11	3,482.9	5,515.4	58.4
11	Shipping & Ports	26	18,451.4	19,434.9	5.3	11	6,524.5	7,709.1	18.2
12	Telecommunications	41	20,026.0	20,863.2	4.2	6	2,427.3	3,347.2	37.9
13	Urban Development	3	15,185.2	30,684.7	102.1	3	15,185.2	30,684.7	102.1
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		563	626,925.6	752,140.9	20.0	184	177,994.2	314,030.8	76.4

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	3	28,122.0	32,960.0	11 - 41
2	Civil Aviation	5	4,123.2	4,078.1	-1.1	3	3,524.9	3,479.8	7 - 17
3	Coal	45	25,504.2	28,789.6	12.9	20	12,840.4	15,670.0	3 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	30 - 30
6	Steel	15	41,398.4	68,476.4	65.4	4	15,498.7	24,776.7	17 - 36
7	Petroleum	72	155,657.8	164,213.0	5.5	33	46,316.0	56,797.7	3 - 120
8	Power	83	180,092.4	185,360.2	2.9	42	86,148.3	90,577.5	4 - 90
9	Railways	136	66,510.0	123,008.2	84.9	27	22,964.0	43,583.9	2 - 213
10	Road Transport & Highways	125	60,796.9	62,260.3	2.4	92	30,673.3	31,316.7	1 - 106
11	Shipping & Ports	26	18,451.4	19,434.9	5.3	14	8,954.5	9,920.7	2 - 72
12	Telecommunications	41	20,026.0	20,863.2	4.2	2	496.0	476.4	54 - 54
13	Urban Development	3	15,185.2	30,684.7	102.1	2	15,071.0	30,503.4	12 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		563	626,925.6	752,140.9	20.0	247	277,485.1	347,893.2	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	2	16,663.00	21,501.00	16- 41
2	Civil Aviation	5	4,123.24	4,078.13	-1.09	0	0.00	0.00	0- 0
3	Coal	45	25,504.15	28,789.58	12.88	7	6,813.24	10,338.47	3- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	15	41,398.40	68,476.43	65.41	2	14,825.00	24,103.00	25- 36
7	Petroleum	72	155,657.83	164,212.95	5.50	15	21,816.18	36,799.39	3- 120
8	Power	83	180,092.42	185,360.17	2.93	7	8,323.49	13,142.73	18- 90
9	Railways	136	66,510.03	123,008.24	84.95	23	11,957.56	33,482.86	11- 213
10	Road Transport & Highways	125	60,796.85	62,260.26	2.41	10	2,374.90	3,227.40	19- 90
11	Shipping & Ports	26	18,451.36	19,434.85	5.33	8	3,883.36	5,004.53	6- 72
12	Telecommunications	41	20,025.99	20,863.20	4.18	5	1,667.10	2,034.67	17- 58
13	Urban Development	3	15,185.18	30,684.66	102.07	3	15,185.18	30,684.66	12- 21
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		563	626925.56	752140.93	19.97	84	108143.42	185907.47	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
KOTESWAR TRANSMISSION SYSTEM (PGCIL)	06/2006	260.34	06/2008	241.27	06/2011	184.25
<u>Railways</u>						
VILLUPURAM-KATPADI (GC)(SR)	02/2000	175.00	N.A.	513.16	N.A.	538.69
<u>Road Transport & Highways</u>						
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31	04/2000	205.73	07/2004	205.73	06/2011	247.70
MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28	12/2003	239.00	07/2005	239.00	12/2011	317.60
<u>Power</u>						
EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME	06/2006	803.70	06/2009	803.76	06/2011	667.01
<u>Petroleum</u>						
JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	7,596.18	03/2012	6,652.22	N.A.	.80
CAPACITY EXP. CUM MODERNISATION PH-II	09/2009	2,591.80	12/2009	3,941.41	12/2010	3,265.10
<u>Power</u>						
TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE	02/2009	276.61	06/2011	276.61	06/2011	199.16
<u>Road Transport & Highways</u>						
BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4	03/2005	565.00	07/2010	565.00	06/2011	1,080.00

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Shipping & Ports</u>					
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	3/2007	245.67	4/2009	298.17	2/2011

VII. Milestones (Cumulative due & achieved)

Total	2197
Achieved up to month	890

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Civil Aviation</u>						
C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT AAI	1,942.51	1,942.51	05/2011	08/2011	12/2011	4
<u>Coal</u>						
PENGANGA OC WCL	339.77	339.77	N.A.	03/2014	10/2014	7
<u>Fertilisers</u>						
CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS NFL	325.00	325.00	07/2011	07/2011	11/2011	4
CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ NFL	438.00	438.00	07/2011	07/2011	03/2012	8
<u>Steel</u>						
67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	N.A.	08/2011	12/2011	4
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	07/2011	11/2011	4
EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,291.00	10/2009	03/2012	10/2012	7
<u>Petroleum</u>						
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON BRPL	1,431.91	1,690.13	09/2009	06/2011	07/2011	1
MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF IOCL	293.60	262.00	12/2009	07/2011	08/2011	1
KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-GAIL	238.68	200.00	N.A.	06/2011	07/2011	1
North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	05/2011	06/2011	1
CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD IOCL	267.00	267.00	09/2012	10/2011	12/2011	2
Construction of 23 Immediate Supply Vessels (ISV) ONGC	331.20	331.20	08/2013	03/2013	08/2013	5
HEERA RECONSTRUCTION ONGC	706.70	706.70	04/2010	06/2011	12/2011	6

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NEELAM RECONSTRUCTION ONGC	305.08	305.08	04/2011	06/2011	12/2011	6
MNW-NF BRIDGE PROJECT ONGC	175.21	162.12	03/2009	05/2011	02/2012	9
HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB BPCL	825.00	1,827.00	N.A.	12/2011	04/2013	16
Power						
CHAMERA, STAGE-III (NHPC) NHPC	1,405.63	1,405.63	08/2010	08/2011	09/2011	1
MOUDA STPP (NTPC) NTPC	5,459.28	6,010.89	N.A.	10/2012	11/2012	1
CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.28	621.28	02/2011	08/2011	10/2011	2
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCL	2,491.58	2,491.45	07/2014	03/2016	05/2016	2
SIPAT STPP STAGE - I (NTPC) NTPC	8,323.39	8,323.39	12/2009	12/2011	03/2012	3
PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.52	2,304.52	10/2010	12/2011	03/2012	3
TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	N.A.	02/2014	06/2014	4
NIMOO BAZGO HYDROELECTRIC PROJECT NHPC	611.02	611.02	08/2010	06/2012	11/2012	5
TEHRI PUMPED STORAGE PLANT(1000MW) THDCL	1,657.00	2,978.86	07/2010	03/2015	01/2016	10
BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	N.A.	10/2012	10/2013	12
Railways						
Rattam-Mhow-Khandwa-Akola (GC) WR	603.04	603.04	03/2012	03/2012	03/2013	12
Road Transport & Highways						
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS NHAI	210.00	210.00	04/2007	06/2011	07/2011	1
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 NHAI	359.00	359.00	03/2009	06/2011	07/2011	1
RINGBUNDS TO JHAJHANPUR (BR-6) NHAI	340.00	340.00	06/2008	06/2011	07/2011	1
KURALI-KIRATPUR, NH-21 NHAI	309.00	309.00	06/2010	06/2011	07/2011	1
TRICHY - DINDIGUL NH-45 NHAI	576.00	576.00	07/2010	06/2011	07/2011	1
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	06/2011	07/2011	1

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	07/2010	06/2011	07/2011	1
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	06/2011	07/2011	1
END OF DURG BYPASS- CHHATISGARH/MAHARASHT RA BORDER NHAI	464.00	464.00	01/2011	06/2011	07/2011	1
GAGODHAR- GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 NHAI	412.78	479.54	11/2007	06/2011	08/2011	2
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 NHAI	217.00	217.00	10/2008	06/2011	08/2011	2
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) NHAI	225.00	225.00	10/2008	07/2011	09/2011	2
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	05/2011	07/2011	2
NAGPUR-KONDHALI,NH- 6(NHAI) NHAI	168.00	168.00	12/2008	08/2011	10/2011	2
JHANSI TO LALITPUR, NH-26 NHAI	276.09	276.09	09/2009	06/2011	08/2011	2
HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	06/2011	09/2011	3
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	06/2011	09/2011	3
HALDIA PORT (PORT CONNECTIVITY) (NH-41) NHAI	273.00	522.00	03/2005	06/2011	09/2011	3
AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 NHAI	193.00	193.00	10/2008	06/2011	09/2011	3
SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) NHAI	203.43	203.43	10/2008	12/2011	03/2012	3
AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	06/2011	10/2011	4
GARHMUKTESHWAR- MURADABAD (NHAI) OTHERS KM.93-149.25, NH- 24 NHAI	275.00	275.00	09/2007	06/2011	12/2011	6
HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	06/2011	12/2011	6
KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 NHAI	240.00	240.00	10/2008	06/2011	12/2011	6

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 NHAI	227.00	227.00	10/2008	06/2011	12/2011	6
ORAI TO JHANSI (UP-5),NH- 25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	06/2011	12/2011	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) NHAI	227.00	227.00	12/2008	06/2011	12/2011	6
FORBESGANJ TO SIMRAHI (NH-57)(NHAI) NHAI	332.94	332.94	09/2008	06/2011	12/2011	6
LALITPUR TO SAGAR, NH-26 (NHAI) NHAI	198.00	198.00	11/2008	06/2011	12/2011	6
RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) NHAI	251.03	251.03	10/2008	06/2011	12/2011	6
RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA NHAI	229.91	229.91	10/2008	06/2011	12/2011	6
SITAPUR-LUCKNOW NHAI	322.00	322.00	06/2009	06/2011	12/2011	6
GORAKHPUR BYPASS, NH- 28, PHASE-II EAST-WEST CORRID NHAI	600.24	600.24	10/2009	06/2011	12/2011	6
JHANSI TO LALITPUR, NH- 25,26 NHAI	355.06	355.06	09/2009	06/2011	12/2011	6
TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	06/2011	12/2011	6
SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 NHAI	941.00	941.00	01/2011	06/2011	12/2011	6
Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) NHAI	572.30	572.30	10/2011	10/2011	08/2012	10
GWALIOR-JHANSI, NH-75 NHAI	604.00	604.00	12/2009	06/2011	06/2012	12
GANJAM-ICCHAPURUM,NH- 5(NHAI) NHAI	263.27	263.27	02/2004	06/2011	12/2012	18

Number of projects reporting additional delay = 67


Trend and Graphical Analysis of All Projects

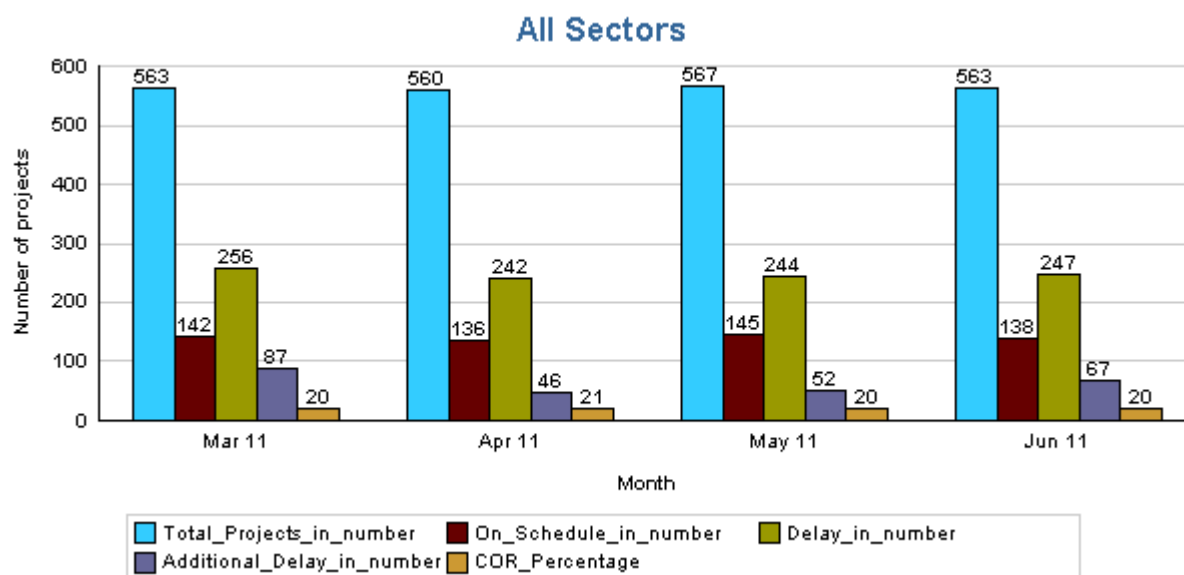


All Sectors Break-up of 247 Delayed projects in June 2011

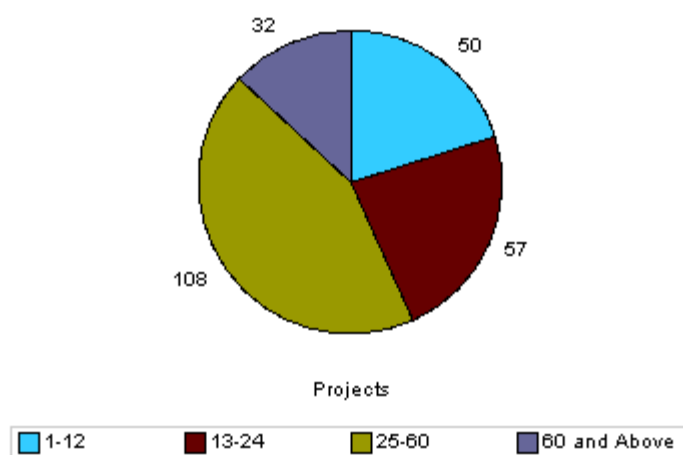


Trend and Graphical Analysis Telecommunications Sector

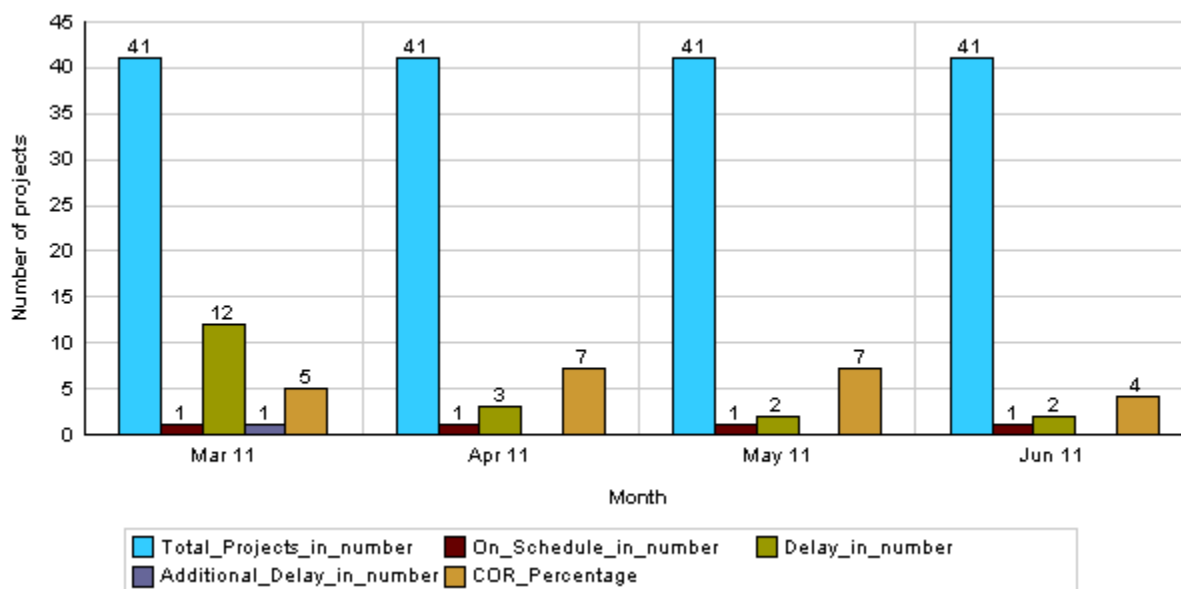


Telecommunications Sector Sector Break-up of 2 Delayed projects in June 2011




Trend and Graphical Analysis Shipping and Ports Sector

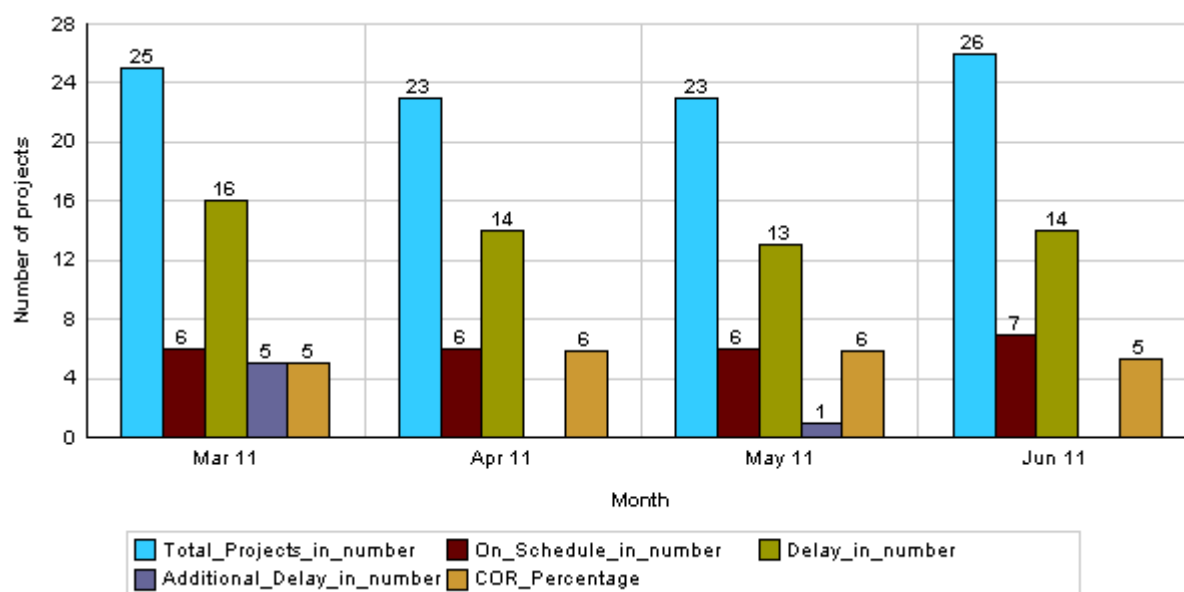


Sector Break-up of 14 Delayed projects in June 2011

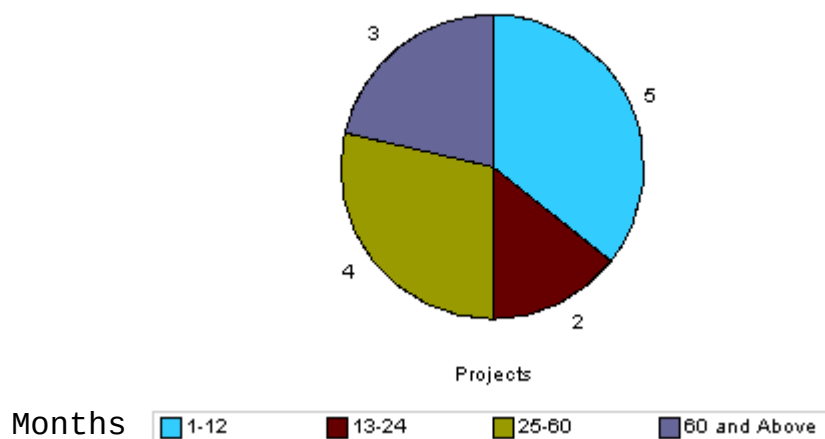

Trend and Graphical Analysis Road Transport and Highways Sector

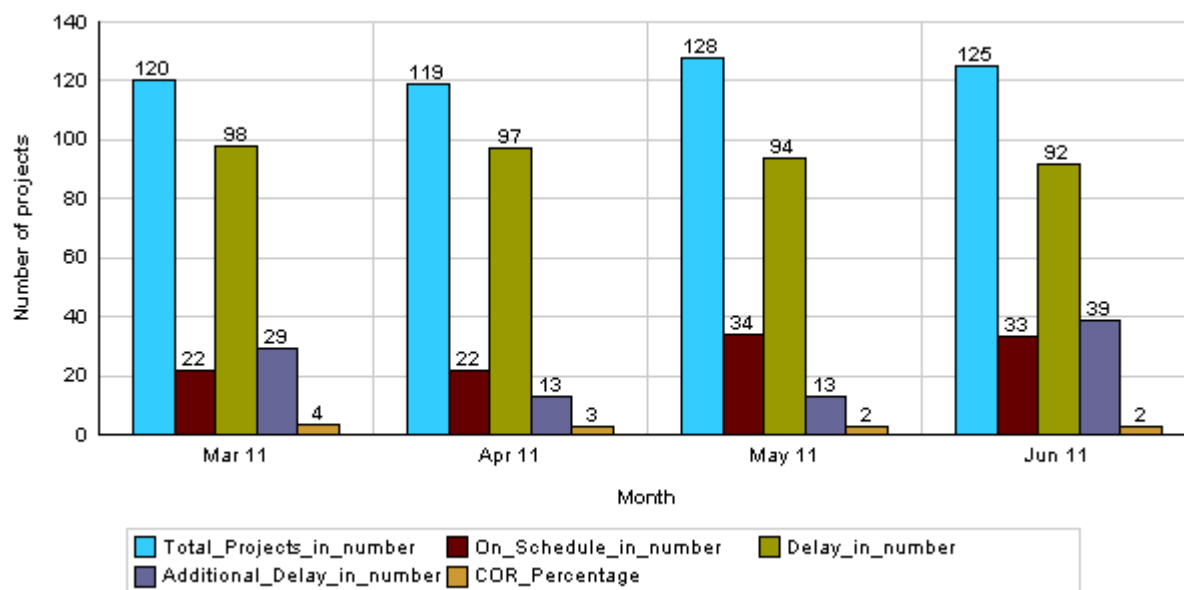


Sector Break-up of 92 Delayed projects in June 2011

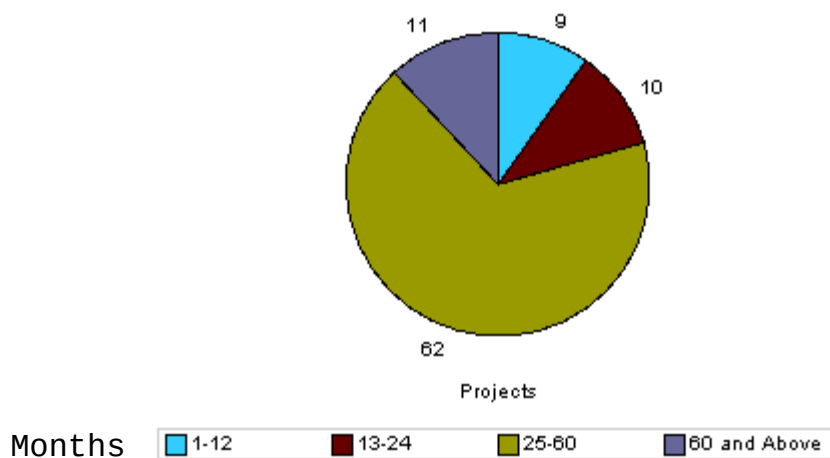


Trend and Graphical Analysis

Railways Sector

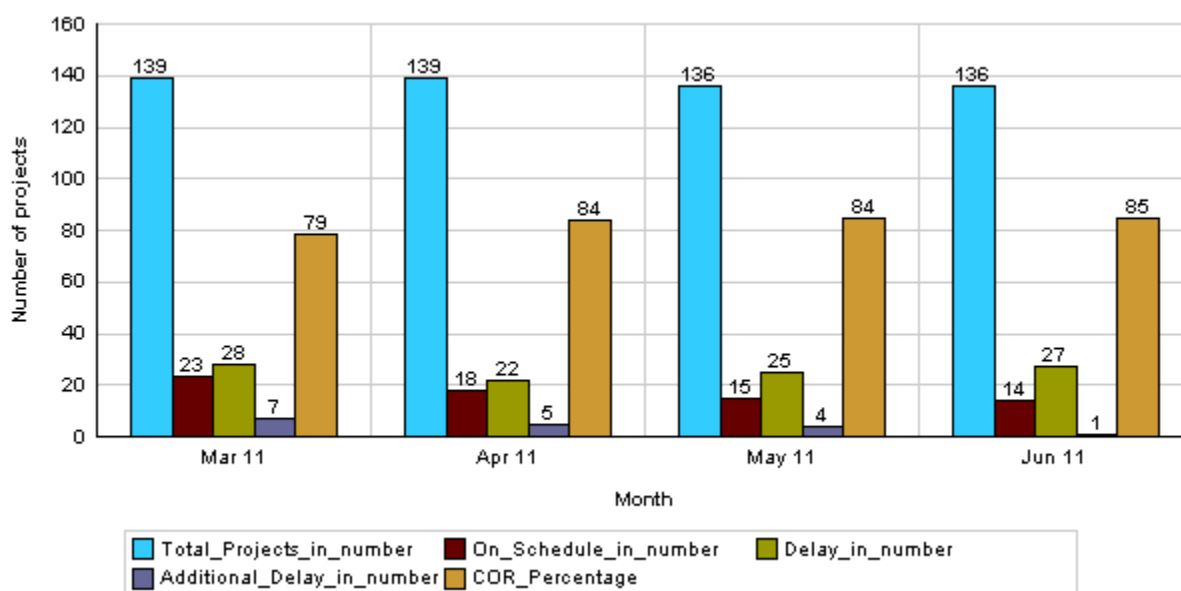


Railways Sector Sector Break-up of 27 Delayed projects in June 2011

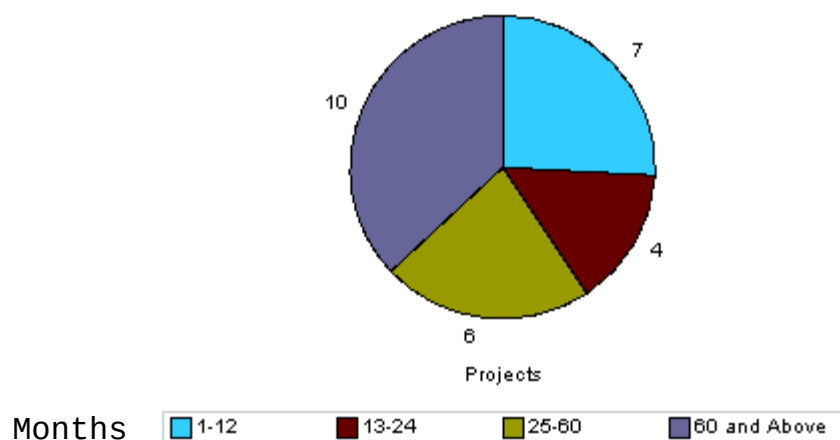


Trend and Graphical Analysis

Power Sector

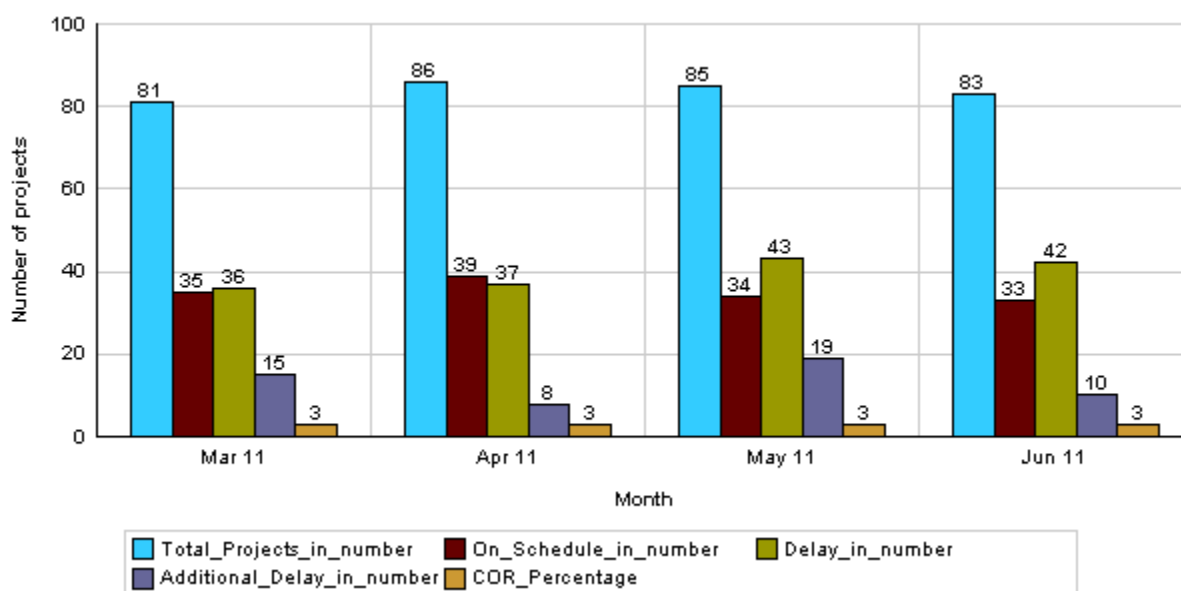


Power Sector Sector Break-up of 42 Delayed projects in June 2011

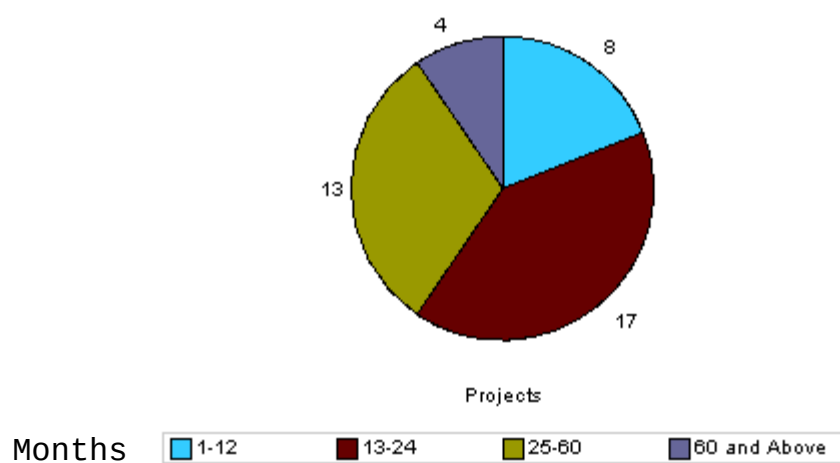


Trend and Graphical Analysis

Petroleum Sector

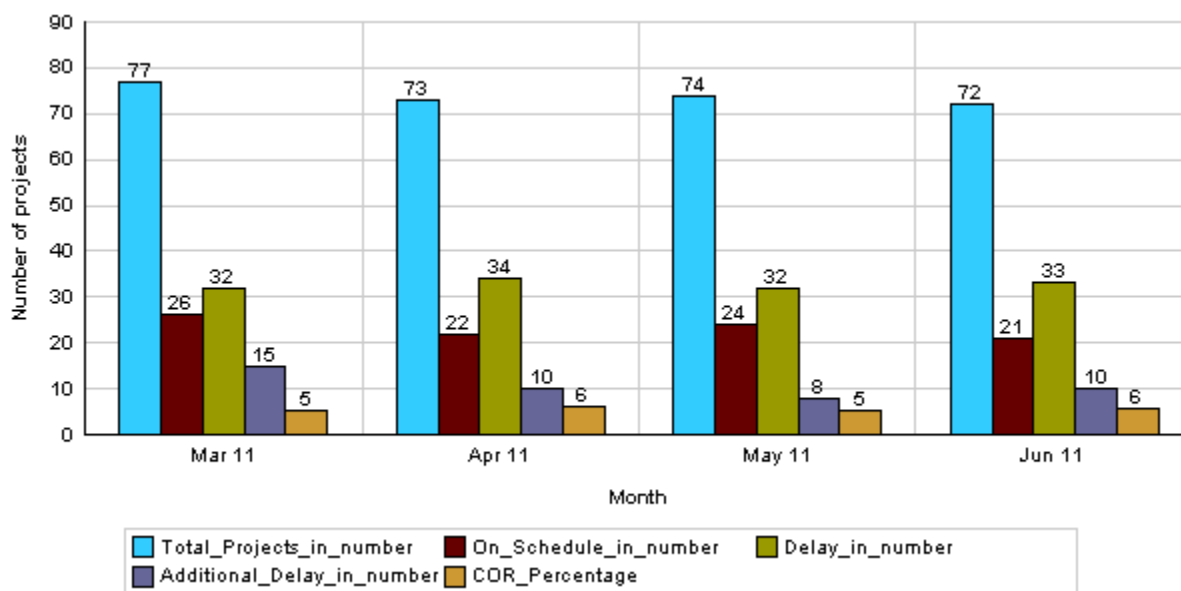


Petroleum Sector Sector Break-up of 33 Delayed projects in June 2011

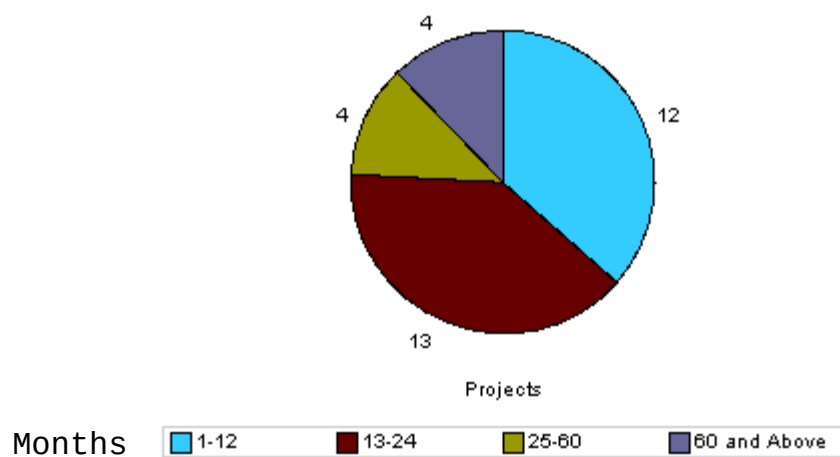


Trend and Graphical Analysis

Steel Sector

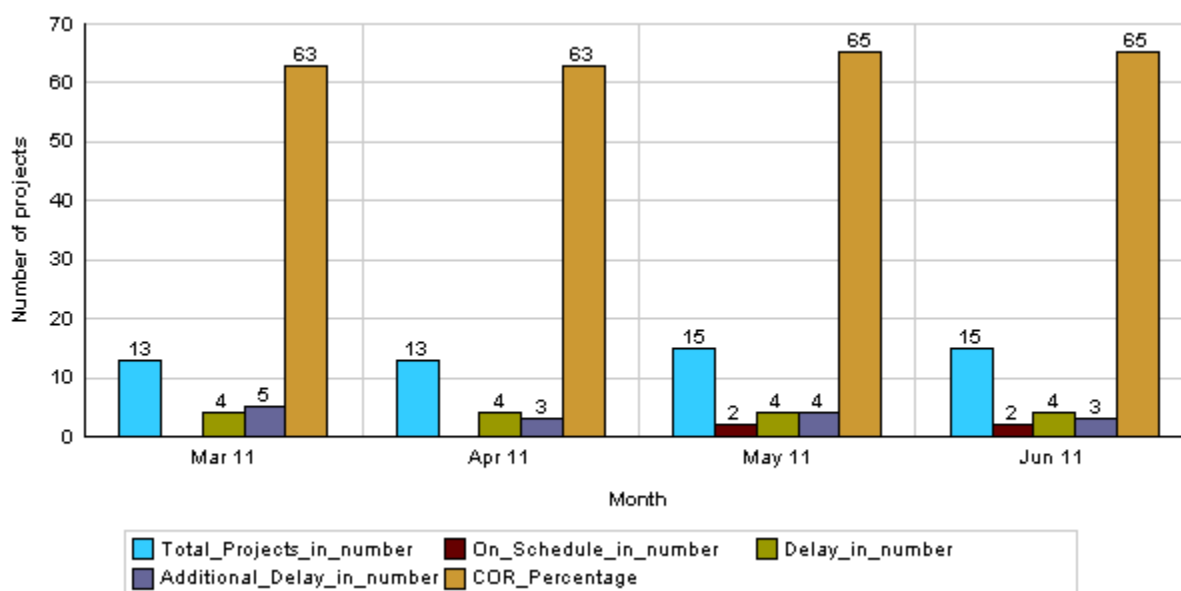


Steel Sector Sector Break-up of 4 Delayed projects in June 2011

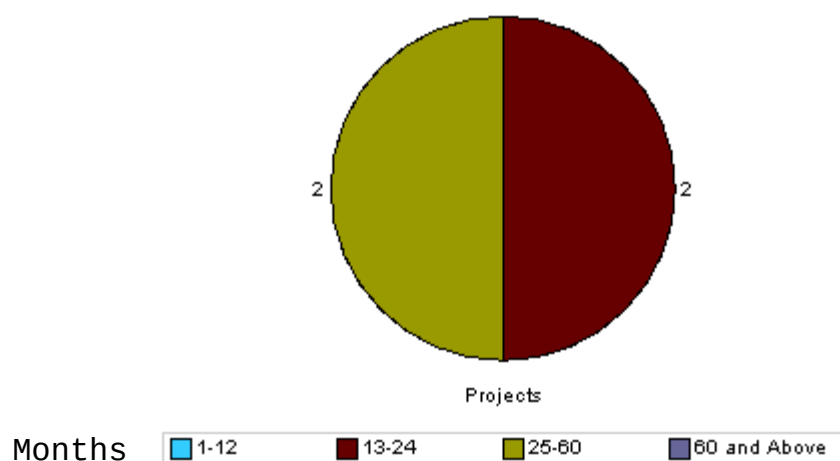


Trend and Graphical Analysis

Fertilisers Sector

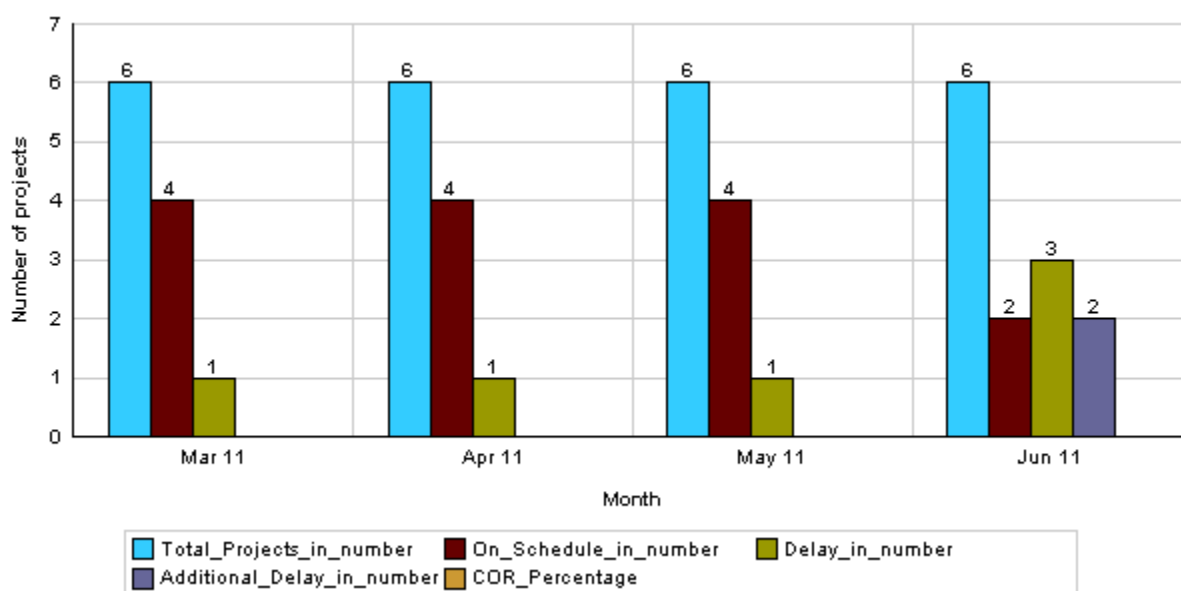


Fertilisers Sector Break-up of 3 Delayed projects in June 2011

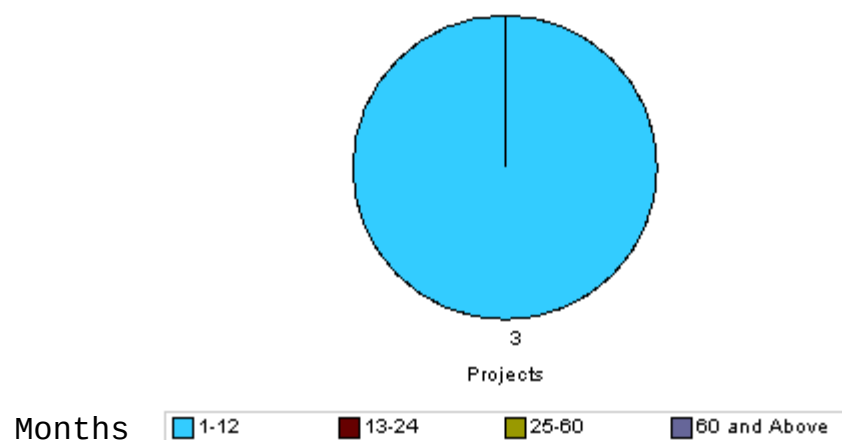


Trend and Graphical Analysis

Coal Sector

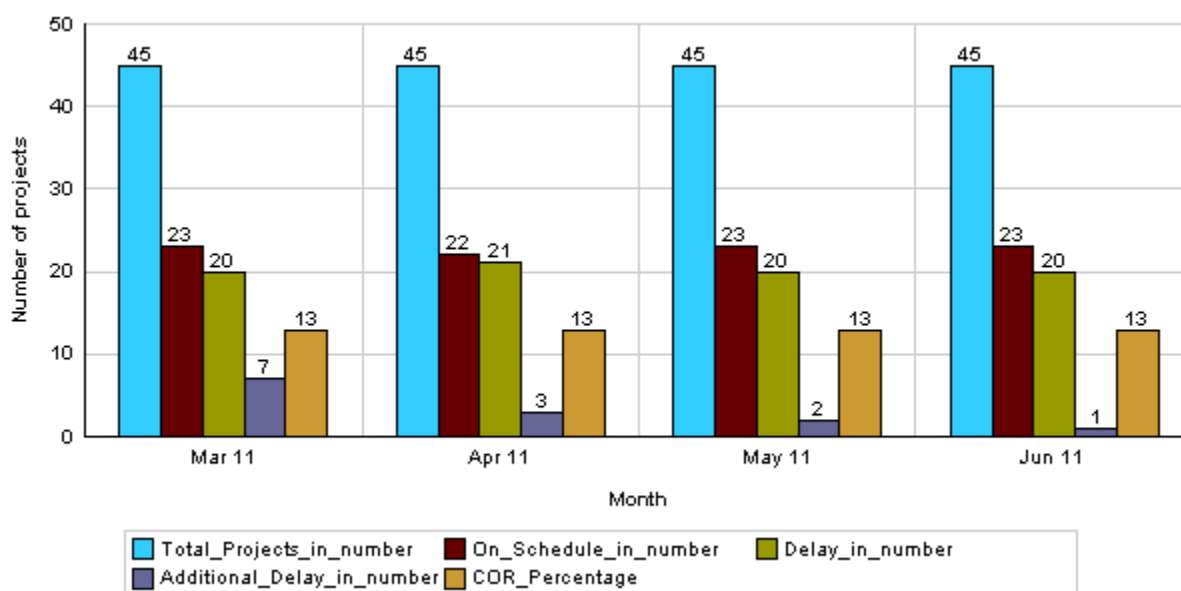


Coal Sector Sector Break-up of 20 Delayed projects in June 2011

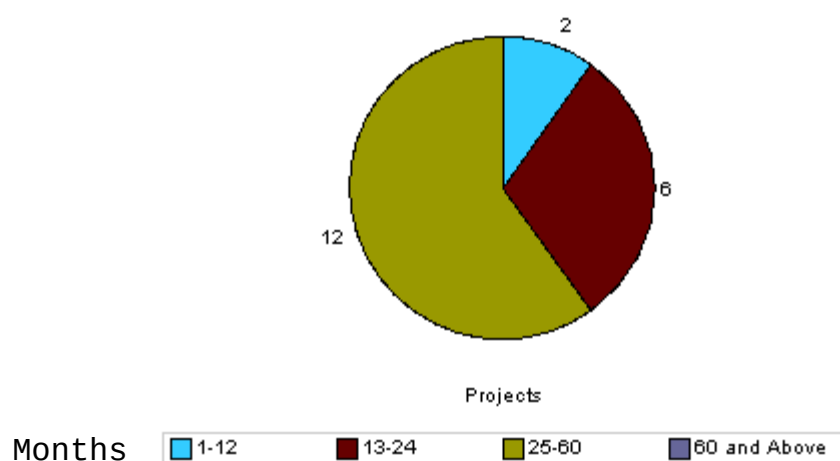


Trend and Graphical Analysis

Civil Aviation Sector

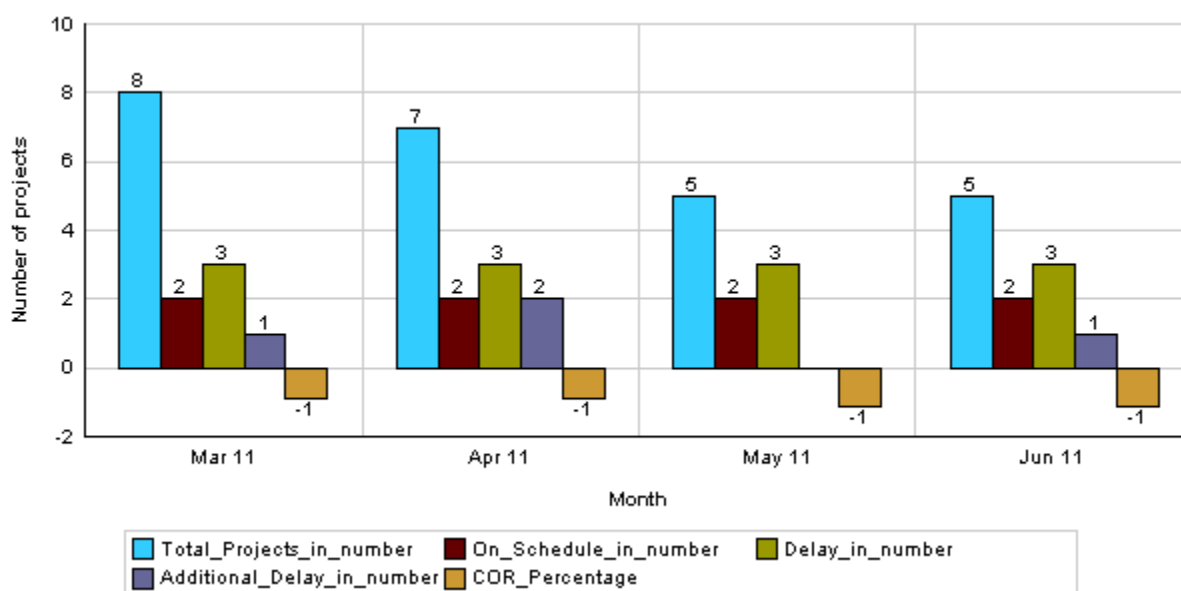


Civil Aviation Sector Break-up of 3 Delayed projects in June 2011

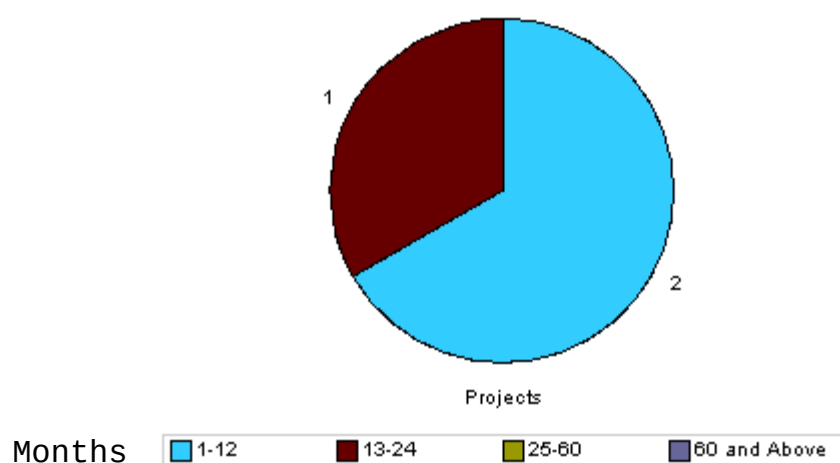


Trend and Graphical Analysis

Atomic Energy Sector

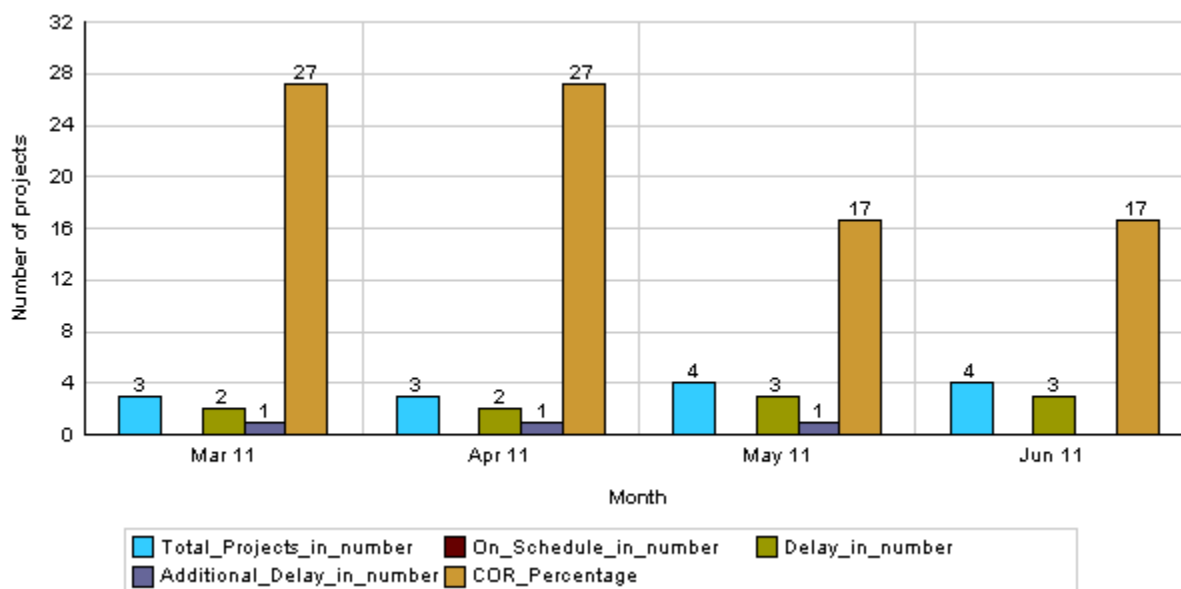

Atomic Energy Sector Sector Break-up of 3 Delayed projects in June 2011

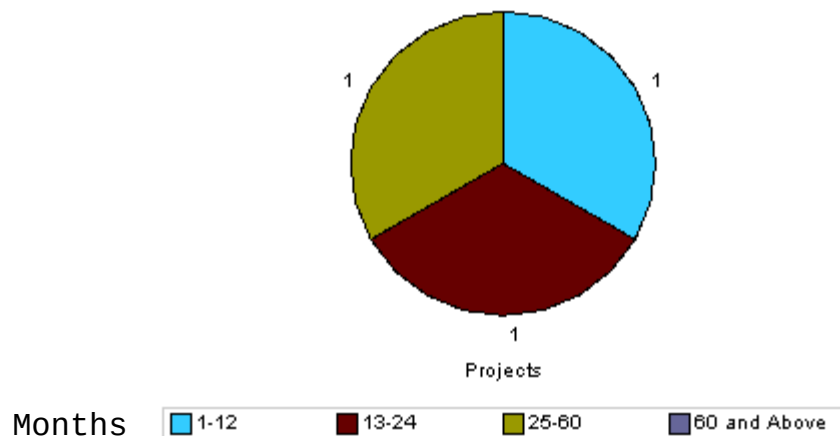

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	29,228.29	29,228.29	34,066.29
Civil Aviation	5	4,123.24	4,123.24	4,078.13
Coal	45	25,504.15	27,012.60	28,789.58
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	15	41,398.40	58,885.33	68,476.43
Petroleum	72	155,657.83	168,856.56	164,212.95
Power	83	180,092.42	181,047.91	185,360.17
Railways	136	66,510.03	84,442.39	123,008.24
Road Transport & Highways	125	60,796.85	60,796.85	62,260.26
Shipping & Ports	26	18,451.36	19,161.19	19,434.85
Telecommunications	41	20,025.99	19,979.50	20,863.20
Urban Development	3	15,185.18	15,173.44	30,684.66
Water Resources	1	542.90	542.90	1,187.00
Grand total	563	626,925.56	678,969.37	752,140.93

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,071.38	09/2010 -	01/2012	16(O)	8/80
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	978.09	- 04/2011	04/2012	12(R3)	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	13,811.00	12/2008 -	05/2012	41(O)	61/119
4	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	626.00	12/2015 05/2016	11/2016	6(R1)	0/70
	Total		29,228.29 -	34,066.29	18,486.47				69/270
<u>Civil Aviation</u>									
5	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 -	1,273.00	881.21	01/2011 -	10/2011	9(O)	0/0
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	1,256.92	05/2011 -	12/2011	7(O)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	35.99	05/2012 -	05/2012	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40 -	264.29	141.91	01/2011 -	06/2012	17(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	275.83	06/2013 -	06/2013	0(O)	0/0
	Total		4,123.24 -	4,078.13	2,591.86				0/0
<u>Coal</u>									
10	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,616.16	06/2009 -	08/2011	26(O)	59/26
11	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,215.26	06/2009 -	03/2012	33(O)	60/24
12	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	78.07	03/2010 -	03/2012	24(O)	0/4
13	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, Madhya Pradesh	10/2007	259.40 -	259.40	1.54	03/2012 -	03/2012	0(O)	0/1
14	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	115.60	03/2009 -	03/2012	36(O)	0/2
15	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	39.83	03/2012 -	03/2012	0(O)	0/0
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	74.10	03/2012 -	03/2012	0(O)	28/27

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	0.92	03/2012 -	03/2012	0(O)	10/34
18	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	1,780.64	- -	10/2012	-	0/6
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	101.90	03/2011 03/2013	03/2013	0(R3)	0/2
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 -	741.56	137.37	03/2010 -	03/2013	36(O)	0/2
21	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	631.78	03/2013 -	03/2013	0(O)	0/3
22	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	101.14	03/2013 -	03/2013	0(O)	0/2
23	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.53 -	479.63	31.59	03/2013 -	03/2013	0(O)	0/2
24	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	23.91	03/2013 -	03/2013	0(O)	0/2
25	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	174.25	03/2013 09/2012	06/2013	9(R3)	2/22
26	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,065.27	03/2010 -	03/2014	48(O)	3/2
27	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,090.71	03/2010 -	03/2014	48(O)	2/3
28	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	145.93	03/2014 -	03/2014	0(O)	1/2
29	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	256.46	03/2014 -	03/2014	0(O)	0/2
30	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	17.63	03/2011 -	03/2014	36(O)	0/3
31	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1
32	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.50 -	321.50	223.01	03/2014 -	03/2014	0(O)	0/1
33	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.63	03/2011 03/2012	03/2014	24(R3)	0/2
34	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.49	03/2012 -	03/2014	24(O)	0/2
35	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	76.08	03/2012 03/2013	03/2014	12(R3)	0/2
36	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	26.27	03/2014 -	03/2014	0(O)	0/0
37	PENGANGA OC - [N06000066]WCL,	10/2008	339.77 -	339.77	0.10	- -	10/2014	-	1/1
38	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 -	437.34	138.18	03/2012 -	03/2015	36(O)	0/2
39	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48(O)	1/5
40	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	49.16	03/2013 03/2015	03/2015	0(R3)	0/3

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
42	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	66.06	12/2012	03/2015	27(O)	11/44
43	Batura OC - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
44	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/1
45	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	16.69	03/2015	03/2015	0(O)	4/31
46	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
47	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	73.61	03/2014	03/2016	24(O)	1/2
48	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	16.25	07/2012 03/2014	03/2016	24(R3)	0/2
49	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	35.20	03/2015	03/2016	12(O)	0/2
50	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	114.02	03/2016	03/2016	0(O)	0/1
51	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	290.49	03/2016	03/2016	0(O)	0/2
52	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.10	490.10	80.33	03/2017	03/2017	0(O)	0/1
53	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	39.56	03/2012	03/2012	0(O)	13/42
54	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013	03/2013	0(O)	0/83
Total			25,504.15	28,789.58	11,057.50				196/431
Fertilisers									
55	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	121.39	- 11/2011	11/2011	0(R3)	2/22
56	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011	11/2011	4(O)	0/0
57	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011	03/2012	8(O)	0/0
58	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	155.43	01/2013	01/2013	0(O)	0/5
59	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	155.89	01/2013	01/2013	0(O)	0/5
60	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	182.71	12/2012	01/2013	1(O)	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		5,317.41	5,317.41	805.52				2/40
	<u>Mines</u>								
61	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa	10/2004	4,091.51 4,401.76	4,401.76	4,302.80	12/2008 01/2011	06/2011	5(R3)	117/110
	Total		4,091.51	4,401.76	4,302.80				117/110
	<u>Steel</u>								
62	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL, Jharkhandd	07/2008	172.78 -	172.78	131.73	01/2010 -	06/2011	17(O)	0/1
63	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Chhatisgarh	07/2007	111.28 232.93	232.93	164.50	- -	08/2011	-	0/1
64	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL, Jharkhandd	10/2007	500.90 -	500.90	174.51	04/2010 -	09/2011	17(O)	0/2
65	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	216.80	- -	11/2011	-	1/2
66	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	11,140.94	- 12/2011	12/2011	0(R3)	1/14
67	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhandd	01/2008	3,316.00 6,325.00	6,325.00	2,028.76	- 12/2011	12/2011	0(R3)	0/11
68	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	222.61	- -	12/2011	-	2/3
69	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,	01/2007	295.89 607.17	607.17	283.60	- -	03/2012	-	18/21
70	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	480.84	108.51	- 05/2012	05/2012	0(R3)	1/2
71	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	8,478.00	10/2009 -	10/2012	36(O)	46/59
72	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	42.54	- 10/2012	10/2012	0(R3)	3/4
73	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	6,133.00 -	11,812.00	1,253.17	02/2011 -	03/2013	25(O)	0/0
74	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	2,733.88	- 03/2013	03/2013	0(R3)	0/20
75	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
76	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC, Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
	Total		41,398.40	68,476.43	26,979.55				72/140
	<u>Petroleum</u>								

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
77	Pipeline Replacement project-2 - [N16000111]ONGC,Multi State	12/2007	2,553.28 3,796.21	3,796.21	3,631.29	05/2011 -	05/2011	0(O)	0/0
78	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	475.47	03/2011 05/2011	06/2011	1(R3)	0/0
79	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	649.63	12/2010 -	06/2011	6(O)	0/0
80	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92 1,493.49	976.08	774.32	05/2008 07/2010	07/2011	12(R3)	0/2
81	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,589.43	09/2009 -	07/2011	22(O)	0/0
82	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 196.25	200.00	92.80	- 06/2011	07/2011	1(R3)	1/8
83	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	237.80	12/2010 07/2011	07/2011	0(R3)	0/0
84	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam	04/2008	293.60 -	262.00	222.56	12/2009 -	08/2011	20(O)	0/0
85	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	215.41	12/2010 08/2011	08/2011	0(R3)	0/0
86	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,403.26 4,403.26	2,500.00	2,157.44	10/2011 09/2011	09/2011	0(R3)	0/2
87	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	666.63	12/2011 -	09/2011	-3(O)	0/0
88	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
89	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
90	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 1,816.07	1,400.00	856.99	- 12/2011	12/2011	0(R3)	0/1
91	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Madhya pradesh	11/2007	1,512.00 1,434.00	982.00	842.14	04/2011 12/2011	12/2011	0(R3)	0/3
92	COMPRESSOR STATIONS (KAILARAS &CHAINS) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	810.00	577.02	04/2011 12/2011	12/2011	0(R3)	0/2
93	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	185.33	03/2013 03/2013	12/2011	-15(R1)	0/0
94	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	603.92	04/2010 -	12/2011	20(O)	0/0
95	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	239.95	04/2011 -	12/2011	8(O)	0/0
96	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.29	09/2011 -	12/2011	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,570.15	05/2011	12/2011	7(O)	0/116
98	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00	267.00	160.06	09/2012	12/2011	-9(O)	0/0
99	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	12,160.26	6,140.98	01/2012	01/2012	0(O)	0/0
100	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	58.26	03/2009	02/2012	35(O)	0/0
101	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	412.78	03/2010	03/2012	0(R1)	0/0
102	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	2,730.00	471.12	09/2011	03/2012	0(R3)	0/0
103	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00	260.00	124.61	03/2012	03/2012	-9(R3)	6/12
104	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	340.00	118.90	06/2011	03/2012	0(R3)	3/9
105	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00	616.00	-	03/2012	03/2012	0(O)	0/0
106	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61	5,460.61	2,424.92	-	04/2012	-	0/30
107	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [N160100231]ONGC,Multi State	04/2003	429.82	2,218.01	-	04/2006	05/2012	12(R3)	0/0
108	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29	6,326.40	3,123.56	05/2010	05/2012	0(R3)	0/0
109	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	2,920.82	1,094.03	09/2010	05/2012	2(R3)	0/0
110	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40	656.51	12.57	05/2010	05/2012	1(R3)	0/0
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21	1,436.21	58.17	07/2010	05/2012	0(R3)	0/0
112	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	41.77	05/2012	05/2012	0(O)	6/36
113	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	5,633.44	1,222.69	08/2010	06/2012	3(R3)	0/0
114	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	2,163.64	485.72	06/2012	06/2012	0(O)	0/0
115	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33	1,492.33	664.14	-	06/2012	-	6/9
116	Wind Power Project - [N16000119]ONGC,Gujarat	07/2010	1,106.00	1,106.00	-	06/2012	06/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
117	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	58.95	04/2011 -	07/2012	15(O)	0/0
118	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	400.00	97.53	06/2011 07/2012	07/2012	0(R3)	7/9
119	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	331.24	07/2012 -	07/2012	0(O)	0/0
120	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	722.06	03/2012 08/2012	08/2012	0(R3)	11/10
121	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	79.93	08/2012 -	08/2012	0(O)	0/0
122	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,091.16	09/2012 -	09/2012	0(O)	0/0
123	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	315.60	- 09/2012	09/2012	0(R3)	0/15
124	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	15.78	09/2012 -	09/2012	0(O)	0/0
125	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	29,777.00	7,649.93	- -	11/2012	-	107/103
126	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	64.38	12/2011 -	01/2013	13(O)	0/0
127	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	12.63	- -	01/2013	-	12/18
128	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	01/2013 -	01/2013	0(O)	0/0
129	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	7.14	- -	02/2013	-	15/42
130	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	211.66	03/2006 03/2013	03/2013	0(R3)	6/6
131	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,706.08	05/2010 03/2013	03/2013	0(R3)	0/0
132	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	332.48	03/2013 -	03/2013	0(O)	0/0
133	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
134	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
135	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0
136	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	02/2008	825.00 1,827.00	1,827.00	136.24	- 04/2013	04/2013	0(R3)	0/203

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
137	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00	1,584.00	1.69	-	08/2013	-	0/0
138	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	331.20	-	08/2013	08/2013	0(O)	0/0
139	Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	9.71	02/2014	12/2013	-2(O)	0/0
140	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
141	Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	85.38	02/2014	02/2014	0(O)	0/0
142	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	573.83	03/2007 03/2014	03/2014	0(R3)	3/3
143	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
144	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
145	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
146	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,304.76	03/2007 03/2017	03/2017	0(R3)	6/6
147	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
148	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	2,174.00	384.00	09/2011 03/2012	-	-	0/0
Total			155,657.83	164,212.95	58,546.17				189/645
Power									
149	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	110.81	06/2011	06/2011	0(O)	0/0
150	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	163.60	09/2010	08/2011	11(O)	0/0
151	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,620.85	08/2010	09/2011	13(O)	0/0
152	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	210.27	05/2011 05/2011	09/2011	4(R3)	0/0
153	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	132.58	06/2010	09/2011	15(O)	0/0
154	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	653.12	02/2011	10/2011	8(O)	0/1
155	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	78.16	01/2011	10/2011	9(O)	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	459.86	01/2010	11/2011	22(O)	0/22
157	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	50.50	11/2011	11/2011	0(O)	0/0
158	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,479.33	11/2009	12/2011	25(O)	0/0
159	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,480.29	09/2009	12/2011	27(O)	15/30
160	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,908.67	07/2010	12/2011	17(O)	3/20
161	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.83	3,956.00	-	12/2011	-	0/6
162	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	289.82	07/2011	12/2011	5(O)	0/0
163	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	232.90	02/2012	02/2012	0(O)	0/0
164	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	32.53	02/2012	02/2012	0(O)	0/0
165	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	146.64	08/2011	02/2012	6(O)	0/0
166	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	205.32	07/2010 02/2012	02/2012	0(R3)	0/0
167	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	63.84	07/2011	02/2012	7(O)	0/0
168	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,433.70	04/2005	03/2012	83(O)	6/11
169	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,153.00	12/2009	03/2012	27(O)	33/56
170	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,493.52	10/2010	03/2012	17(O)	0/0
171	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,711.67	11/2008	03/2012	40(O)	25/38
172	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	683.27	10/2009	03/2012	29(O)	2/20
173	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	65.58	04/2012	04/2012	0(O)	0/0
174	TESSTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,318.78	03/2007	05/2012	62(O)	1/25
175	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	282.88	06/2012	06/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
176	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	103.63	06/2012	06/2012	0(O)	0/0
177	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	9.00	06/2012	06/2012	0(O)	0/0
178	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,641.85	08/2012	08/2012	0(O)	0/0
179	765 KV POOLING STATION & NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	3,791.31	08/2012	08/2012	0(O)	0/0
180	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	293.13	08/2012	08/2012	0(O)	0/0
181	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,803.44	10/2012	10/2012	0(O)	0/0
182	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	138.86	10/2012	10/2012	0(O)	0/0
183	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	11.32	10/2012	10/2012	0(O)	0/0
184	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	641.85	08/2010	11/2012	27(O)	0/0
185	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	2,538.00	-	11/2012	-	0/16
186	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	281.08	11/2012	11/2012	0(O)	0/0
187	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	221.30	11/2012	11/2012	0(O)	0/0
188	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	85.33	11/2012	11/2012	0(O)	0/0
189	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	970.13	09/2009	12/2012	39(O)	0/0
190	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	693.00	11/2011	12/2012	13(O)	6/34
191	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	2,340.28	12/2012	12/2012	0(O)	0/0
192	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	1,967.00	-	12/2012	-	0/15
193	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	1,848.00	-	12/2012	-	0/16
194	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	258.25	12/2012	12/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	25.54	01/2013 -	01/2013	0(O)	0/0
196	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	17.35	01/2013 -	01/2013	0(O)	0/0
197	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	3,695.00	04/2009 -	03/2013	47(O)	19/9
198	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	338.50	09/2010 -	03/2013	30(O)	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	249.15	11/2011 -	03/2013	16(O)	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	240.82	11/2011 -	03/2013	16(O)	0/0
201	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	116.00	02/2012 -	03/2013	13(O)	0/0
202	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	800.49	02/2012 -	03/2013	13(O)	0/0
203	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	224.08	05/2012 -	03/2013	10(O)	0/0
204	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	108.70	03/2013 -	03/2013	0(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	62.92	04/2013 -	04/2013	0(O)	0/0
206	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	8.71	04/2013 -	04/2013	0(O)	0/0
207	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	79.60	01/2012 -	07/2013	18(O)	0/0
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	33.39	07/2013 -	07/2013	0(O)	0/0
209	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	191.24	08/2013 08/2013	08/2013	0(R3)	8/17
210	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	59.89	08/2013 -	08/2013	0(O)	0/0
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	15.15	08/2013 -	08/2013	0(O)	0/0
212	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	125.56	08/2013 -	08/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
213	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,254.74	01/2012	09/2013	20(O)	2/10
214	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19	184.19	124.59	11/2011	09/2013	22(O)	0/0
215	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, Assam	01/2008	4,375.35	4,375.35	2,186.00	-	10/2013	-	0/29
216	BARH STPP STAGE -II - [N18000047]NTPC, Bihar	02/2008	7,341.04	7,341.04	2,255.00	-	10/2013	-	0/18
217	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL, Multi State	03/2011	1,585.12	1,585.12	55.83	11/2013	11/2013	0(O)	0/0
218	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19	2,743.19	210.01	12/2013	12/2013	0(O)	0/0
219	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72	913.63	245.77	07/2006	01/2014	0(R3)	2/5
220	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25	2,569.25	-	03/2014	03/2014	0(O)	0/0
221	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttaranchal	11/2006	2,978.48	2,978.48	1,125.00	-	06/2014	-	5/13
222	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59	3,919.59	3,211.36	09/2009	07/2014	58(O)	1/20
223	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33	6,285.33	4,970.96	09/2010	08/2014	47(O)	2/11
224	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,693.00	8,693.00	5,837.00	11/2010	09/2014	46(O)	15/51
225	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19	11,130.19	2,597.57	08/2013	09/2014	13(O)	0/0
226	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
227	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttaranchal	07/2006	1,657.00	2,978.86	261.16	07/2010	01/2016	66(O)	1/1
228	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67	3,642.04	755.56	07/2014	01/2016	18(O)	0/0
229	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,	08/2008	2,491.58	2,491.45	160.62	07/2014	05/2016	22(O)	0/7
230	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90	2,496.90	1,495.83	05/2013	06/2016	0(R3)	79/22
231	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45	947.96	820.24	12/2007	-	-	14/18
	Total		180,092.42	185,360.17	85,013.58				239/542

Railways

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
232	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 589.86	563.25	544.32	03/2004 03/2010	02/2005	-61(R3)	0/0
233	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	464.50	507.76	03/1996 08/2009	03/2008	-17(R3)	0/0
234	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	256.66	03/2008 10/2010	10/2010	0(R3)	0/0
235	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	230.33	- 02/2009	12/2010	22(R1)	0/0
236	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	184.86	- 03/2009	12/2010	21(R1)	0/0
237	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	148.47	12/2007 03/2010	12/2010	9(R1)	0/0
238	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
239	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	-	- -	12/2010	-	0/0
240	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0
241	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	255.49	03/2009 12/2009	03/2011	15(R1)	0/0
242	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	164.13	03/2011 -	03/2011	0(O)	0/0
243	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,181.81	- 12/2010	06/2011	6(R3)	0/1
244	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	592.37	- -	07/2011	-	0/0
245	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	152.68	- -	08/2011	-	0/0
246	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	181.46	03/2002 -	09/2011	114(O)	0/0
247	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	158.66	02/2010 -	11/2011	21(O)	0/0
248	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	551.30	03/1994 -	12/2011	213(O)	0/0
249	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	452.91	02/2009 -	12/2011	34(O)	0/0
250	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	195.75	- 09/2009	12/2011	27(R1)	0/0
251	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	74.88	- -	12/2011	-	0/0
252	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	212.57	03/2013 -	12/2011	-15(O)	0/0
253	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,139.38	- -	02/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
254	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	388.84	- 12/2009	02/2012	26(R1)	0/0
255	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	58.50	12/2011 -	02/2012	2(O)	0/0
256	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	539.03	03/1995 -	03/2012	204(O)	0/0
257	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	617.62	475.35	- -	03/2012	-	0/0
258	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	425.95	- 12/2011	03/2012	3(R3)	0/0
259	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	197.09	- 03/2012	03/2012	0(R3)	0/0
260	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	416.10	- -	03/2012	-	0/0
261	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	526.53	- -	03/2012	-	0/0
262	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	69.10	- -	03/2012	-	0/0
263	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	334.48	- 03/2011	03/2012	12(R3)	0/0
264	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	180.10	- -	03/2012	-	0/0
265	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	868.14	- -	03/2012	-	0/0
266	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	187.08	03/2010 -	03/2012	24(O)	0/0
267	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	165.19	- -	03/2012	-	0/0
268	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	74.98	03/2012 -	03/2012	0(O)	0/0
269	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	165.75	03/2011 -	03/2012	12(O)	0/0
270	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	372.55	06/2005 07/2011	03/2012	8(R3)	0/0
271	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	787.55	03/2011 -	03/2012	12(O)	0/0
272	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	41.89	03/2012 -	03/2012	0(O)	0/0
273	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	318.24	0.92	03/2012 -	03/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
274	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	131.08	03/2007 03/2007	06/2012	63(R1)	0/0
275	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	320.95	- 07/2012	07/2012	0(R3)	0/0
276	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	564.81	- -	12/2012	-	0/0
277	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	761.65	12/2012 -	12/2012	0(O)	0/0
278	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	379.62	03/2005 12/2008	12/2012	48(R1)	0/0
279	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	261.90	- 03/2012	12/2012	9(R3)	0/0
280	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	231.78	- -	12/2012	-	0/0
281	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	506.69	03/2009 -	12/2012	45(O)	0/0
282	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	916.18	10/2007 -	12/2012	62(O)	0/0
283	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	326.42	03/2010 -	12/2012	33(O)	0/0
284	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	98.08	12/2012 -	12/2012	0(O)	0/0
285	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	143.89	- 03/2013	03/2013	0(R3)	0/0
286	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	145.40	- -	03/2013	-	0/0
287	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	607.43	- -	03/2013	-	0/0
288	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	39.90	03/2012 -	03/2013	12(O)	0/0
289	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	350.81	0.49	03/2013 -	03/2013	0(O)	0/0
290	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	116.15	- 06/2013	06/2013	0(R3)	0/0
291	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	52.94	12/2011 -	11/2013	23(O)	0/0
292	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	159.94	- -	12/2013	-	0/0
293	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	82.41	12/2012 -	12/2013	12(O)	0/0
294	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Multi State	04/1996	1,676.31 -	4,091.33	2,698.07	03/2009 -	12/2013	57(O)	0/0
295	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,203.80	04/2008 03/2014	03/2014	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
296	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	727.51	12/2008 -	03/2014	63(O)	0/0
297	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	181.65	03/2014 -	03/2014	0(O)	0/0
298	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	3.53	04/2014 -	03/2014	-1(O)	0/0
299	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	5.87	03/2014 -	03/2014	0(O)	0/0
300	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	38.28	03/2014 -	03/2014	0(O)	0/0
301	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	156.72	03/2014 -	03/2014	0(O)	0/0
302	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	94.67	03/2010 06/2014	06/2014	0(R3)	0/0
303	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	161.74	- -	03/2015	-	0/0
304	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTTP,Maharashtra	04/2008	5,300.00 -	5,300.00	239.18	03/2014 -	03/2015	12(O)	0/0
305	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.69	12/2015 -	03/2015	-9(O)	0/0
306	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
307	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
308	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,056.85	426.90	03/2011 03/2014	03/2016	24(R3)	0/0
309	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	0.21	03/2014 -	03/2016	24(O)	0/0
310	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	1.42	03/2016 -	03/2016	0(O)	0/0
311	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	23.10	03/2016 -	03/2016	0(O)	0/0
312	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	-	03/2016 -	06/2016	3(O)	0/0
313	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001 -	12/2017	201(O)	0/0
314	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	233.91	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
315	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	968.60	87.09	12/2012 -	-	-	0/0
316	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	1,010.00	78.91	- -	-	-	0/0
317	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 -	412.91	455.06	- -	-	-	0/0
318	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
319	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 -	945.73	537.63	- -	-	-	0/0
320	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00 -	997.58	64.07	- -	-	-	0/0
321	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	497.47	84.54	- -	-	-	0/0
322	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
323	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 1,099.20	1,099.20	1,034.47	07/2005 -	-	-	0/0
324	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	369.70	132.09	- 05/2009	-	-	0/0
325	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, Bihar	04/1997	78.23 -	162.87	82.96	- -	-	-	0/0
326	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00 625.30	847.76	808.81	06/2007 -	-	-	0/0
327	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	296.20	298.46	04/2003 03/2010	-	-	0/0
328	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 -	548.96	466.66	- -	-	-	0/0
329	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 -	695.00	9.74	- -	-	-	0/0
330	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, Multi State	04/2000	138.00 519.67	607.09	298.25	- 12/2012	-	-	0/0
331	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
332	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 -	418.17	72.56	- -	-	-	0/0
333	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	206.59	- -	-	-	0/0
334	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 -	173.49	170.73	03/1998 08/2005	-	-	0/0
335	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0
336	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
337	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	261.70	17.05	02/2006 -	-	-	0/0
338	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	296.80	03/2008 06/2008	-	-	0/0
339	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	169.27	- -	-	-	0/0
340	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	386.83	- -	-	-	0/0
341	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	21.22	- -	-	-	0/0
342	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	78.89	- -	-	-	0/0
343	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	35.45	- -	-	-	0/0
344	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
345	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	437.73	06/1999 03/2011	-	-	0/0
346	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	165.26	03/2004 -	-	-	0/0
347	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	547.25	- 11/2010	-	-	0/0
348	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	322.73	- 03/2011	-	-	0/0
349	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	263.34	06/2004 04/2005	-	-	0/0
350	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	499.50	05/2008 03/2011	-	-	0/0
351	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	219.60	12/2009 03/2011	-	-	0/0
352	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	1,015.84	716.83	- 12/2010	-	-	0/0
353	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	383.68	- -	-	-	0/0
354	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	402.51	- -	-	-	0/1
355	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	668.74	- -	-	-	0/0
356	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,058.65	12/2006 08/2010	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
357	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	225.14	- 02/2011	-	-	0/0
358	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	460.27	02/2010 02/2011	-	-	0/0
359	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	347.04	- -	-	-	0/0
360	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	231.62	- 03/2011	-	-	0/0
361	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	117.60	- -	-	-	0/0
362	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	130.85	- -	-	-	0/0
363	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	360.51	- 03/2011	-	-	0/0
364	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	75.23	- -	-	-	0/0
365	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	141.04	12/2010 03/2011	-	-	0/0
366	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	126.21	- 12/2010	-	-	0/0
367	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	166.83	03/2011 03/2011	-	-	0/0
Total			66,510.03 -	123,008.24	53,223.37				0/2
<u>Road Transport & Highways</u>									
368	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	672.97	04/2007 -	07/2011	51(O)	0/0
369	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	166.30	177.03	03/2008 -	07/2011	40(O)	0/0
370	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27 -	193.10	145.14	03/2008 -	07/2011	40(O)	0/0
371	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	794.72	03/2009 -	07/2011	28(O)	0/0
372	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00 -	340.00	554.48	06/2008 -	07/2011	37(O)	0/0
373	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	598.94	03/2009 -	07/2011	28(O)	0/0
374	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	196.50	230.20	06/2008 -	07/2011	37(O)	0/0
375	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00 -	309.00	553.56	06/2010 -	07/2011	13(O)	0/0
376	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	653.51	07/2010 -	07/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
377	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	358.94	07/2010	07/2011	12(O)	0/0
378	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	875.17	07/2010	07/2011	12(O)	0/0
379	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	141.87	02/2004	07/2011	89(O)	0/0
380	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	419.88	01/2011	07/2011	6(O)	0/0
381	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	435.93	11/2007	08/2011	45(O)	0/0
382	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00	217.00	350.99	10/2008	08/2011	34(O)	0/0
383	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	910.04	11/2010	08/2011	9(O)	0/0
384	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	294.85	09/2009	08/2011	23(O)	0/0
385	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,427.10	08/2011	08/2011	0(O)	0/0
386	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	142.70	08/2004	09/2011	85(O)	0/0
387	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	154.57	08/2004	09/2011	85(O)	0/0
388	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	475.55	03/2005	09/2011	78(O)	0/0
389	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00	193.00	329.36	10/2008	09/2011	35(O)	0/0
390	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	253.25	10/2008	09/2011	35(O)	0/0
391	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	227.95	11/2008	09/2011	34(O)	0/0
392	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	62.64	04/2004	10/2011	90(O)	0/0
393	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.03	01/2009	10/2011	33(O)	0/0
394	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	246.91	06/2008	10/2011	40(O)	0/0
395	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.27	12/2008	10/2011	34(O)	0/0
396	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	171.47	10/2011	10/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
397	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	276.68	10/2008	11/2011	37(O)	0/0
398	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	170.70	10/2008	11/2011	37(O)	0/0
399	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	520.68	05/2010	11/2011	18(O)	0/0
400	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,487.00	11/2011	11/2011	0(O)	0/0
401	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
402	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	292.53	09/2007	12/2011	51(O)	0/0
403	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	220.65	09/2007	12/2011	51(O)	0/0
404	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	83.27	09/2008	12/2011	39(O)	0/0
405	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	201.89	06/2005	12/2011	78(O)	0/0
406	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	242.58	10/2008	12/2011	38(O)	0/0
407	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	383.91	10/2008	12/2011	38(O)	0/0
408	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	344.90	03/2008	12/2011	45(O)	0/0
409	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	220.52	02/2009	12/2011	34(O)	0/0
410	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	76.49	04/2009	12/2011	32(O)	0/0
411	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	167.16	06/2008	12/2011	42(O)	0/0
412	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	378.98	12/2008	12/2011	36(O)	0/0
413	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	363.15	12/2008	12/2011	36(O)	0/0
414	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	193.28	06/2008	12/2011	42(O)	0/0
415	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	261.52	09/2008	12/2011	39(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
416	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI, Madhya Pradesh	12/2003	198.00	198.00	185.80	11/2008	12/2011	37(O)	0/0
417	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	251.03	271.32	10/2008	12/2011	38(O)	0/0
418	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya Pradesh	12/2003	229.91	229.91	217.35	10/2008	12/2011	38(O)	0/0
419	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	412.36	09/2008	12/2011	39(O)	0/0
420	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	252.55	06/2008	12/2011	42(O)	0/0
421	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.66	06/2009	12/2011	30(O)	0/0
422	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	235.04	06/2008	12/2011	42(O)	0/0
423	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	462.19	03/2008	12/2011	45(O)	0/0
424	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	160.93	06/2008	12/2011	42(O)	0/0
425	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	197.17	04/2008	12/2011	44(O)	0/0
426	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	111.59	05/2008	12/2011	43(O)	0/0
427	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	183.39	06/2008	12/2011	42(O)	0/0
428	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	580.22	06/2009	12/2011	30(O)	0/0
429	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	682.83	10/2009	12/2011	26(O)	0/0
430	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	313.39	03/2010	12/2011	21(O)	0/0
431	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	294.38	09/2009	12/2011	27(O)	0/0
432	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	548.66	07/2010	12/2011	17(O)	0/0
433	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,802.80	01/2011	12/2011	11(O)	0/0
434	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	324.68	05/2010	12/2011	19(O)	0/0
435	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	622.92	08/2010	12/2011	16(O)	0/0
436	Amur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	344.24	02/2012	02/2012	0(O)	0/0
437	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	174.00	09/2007	03/2012	54(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
438	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	206.45	10/2008	03/2012	41(O)	0/0
439	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	109.34	04/2008	03/2012	47(O)	0/0
440	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	169.55	04/2008	03/2012	47(O)	0/0
441	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	126.52	04/2010	03/2012	23(O)	0/0
442	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	178.58	02/2010	03/2012	25(O)	0/0
443	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.92	02/2010	05/2012	27(O)	0/0
444	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,121.00	05/2012	05/2012	0(O)	0/0
445	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	804.29	05/2012	05/2012	0(O)	0/0
446	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	268.00	05/2012	05/2012	0(O)	0/0
447	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	156.08	10/2008	06/2012	44(O)	0/0
448	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	293.85	10/2009	06/2012	32(O)	0/0
449	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	412.09	12/2009	06/2012	30(O)	0/0
450	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	156.99	09/2010	06/2012	21(O)	0/0
451	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	388.13	06/2012	06/2012	0(O)	0/0
452	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	1,477.60	10/2011	06/2012	8(O)	0/0
453	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	314.52	07/2012	07/2012	0(O)	0/0
454	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	112.15	05/2008	08/2012	51(O)	0/0
455	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	572.30	500.02	10/2011	08/2012	10(O)	0/0
456	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.52	08/2012	08/2012	0(O)	0/0
457	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	407.60	183.69	06/2010	10/2012	28(O)	0/0
458	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	233.27	09/2009	10/2012	37(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
459	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
460	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	813.11	09/2012	10/2012	1(O)	0/0
461	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	804.62	10/2012	10/2012	0(O)	0/0
462	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	618.89	11/2012	11/2012	0(O)	0/0
463	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
464	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
465	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	175.11	07/2008	12/2012	53(O)	0/0
466	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	245.28	02/2004	12/2012	106(O)	0/0
467	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	355.11	12/2012	12/2012	0(O)	0/0
468	Hazariabagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	638.88	01/2013	01/2013	0(O)	0/0
469	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	762.20	09/2010	03/2013	30(O)	0/0
470	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
471	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	236.23	03/2013	03/2013	0(O)	0/0
472	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
473	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	97.32	03/2013	03/2013	0(O)	0/0
474	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
475	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	158.26	05/2013	05/2013	0(O)	0/0
476	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	104.94	05/2013	05/2013	0(O)	0/0
477	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
478	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	111.06	09/2007	06/2013	69(O)	0/0
479	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
480	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
481	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	29.60	04/2009	07/2013	51(O)	0/0
482	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
483	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	63.65	07/2013	07/2013	0(O)	0/0
484	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
485	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
486	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	0.99	09/2013	09/2013	0(O)	0/0
487	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0
488	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
489	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	212.00	38.61	09/2007	12/2013	75(O)	0/0
490	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	196.00	27.77	07/2009	12/2013	53(O)	0/0
491	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
492	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	299.92	10/2014	10/2014	0(O)	0/0
	Total		60,796.85	62,260.26	43,996.38				0/0
	Shipping & Ports								
493	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	298.17	293.57	04/2009	02/2011	22(O)	0/0
494	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	399.13	-	08/2010	03/2011	7(O)	0/0
495	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010	04/2011	8(O)	0/0
496	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 253.36	253.36	-	12/2007 07/2009	06/2011	23(R3)	0/0
497	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	2,190.00	12/2010	06/2011	6(O)	0/0
498	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
499	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50	241.50	48.10	09/2011	09/2011	0(O)	0/0
500	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00	165.00	117.23	12/2005 01/2008	10/2011	45(R3)	0/0
501	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
502	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
503	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	320.74	03/2012	03/2012	0(O)	0/0
504	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006	03/2012	72(O)	0/0
505	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2(O)	0/0
506	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.04	03/2012	03/2012	0(O)	0/0
507	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	55.41	12/2011 05/2012	05/2012	0(R3)	0/0
508	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	-	12/2010 09/2012	09/2012	0(R3)	0/0
509	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	221.91	09/2012	09/2012	0(O)	0/0
510	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
511	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	62.76	12/2012	12/2012	0(O)	0/0
512	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.16	02/2011	03/2013	25(O)	0/0
513	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	-	03/2011	03/2013	24(O)	0/0
514	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009	05/2013	52(O)	0/0
515	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013	12/2013	0(O)	0/0
516	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	189.92	02/2014	02/2014	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
517	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.92	10/2008 -	-	-	0/0
518	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.02	10/2008 -	-	-	0/0
Total			18,451.36 -	19,434.85	5,037.09				0/0
<u>Telecommunications</u>									
519	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	242.48	09/2009 -	02/2010	5(O)	0/0
520	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	-	12/2005 -	10/2010	58(O)	0/0
521	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
522	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	10/2010	7(O)	0/0
523	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	11/2010	8(O)	0/0
524	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86 234.24	353.00	-	02/2008 -	12/2010	34(O)	0/0
525	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	12/2010	21(O)	0/0
526	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	12/2010	9(O)	0/0
527	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	12/2010	9(O)	0/0
528	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	12/2010	9(O)	0/0
529	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	12/2010	9(O)	0/0
530	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	-	06/2009 -	01/2011	19(O)	0/0
531	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	192.48	110.99	03/2009 -	02/2011	23(O)	0/0
532	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	194.39	12/2008 -	02/2011	26(O)	0/0
533	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	377.54	308.13	03/2009 -	02/2011	23(O)	0/0
534	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	75.31	06/2009 -	02/2011	20(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
535	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81	336.81	155.71	01/2009	02/2011	25(O)	0/0
536	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL, Uttar Pradesh	02/2009	625.53	625.53	-	02/2010	02/2011	12(O)	0/0
537	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL, Bihar	10/2007	366.00	366.00	225.42	10/2008	02/2011	28(O)	0/0
538	GSM equipment of 1900000Lines (2G) 401700 lines 3(-) - [N26000091]BSNL, Tamil Nadu	01/2009	760.20	1,312.52	792.83	- 03/2011	02/2011	-1(R3)	0/1
539	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL, Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	02/2011	13(O)	0/0
540	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL, Kerala	01/2009	848.70	848.70	675.35	01/2010	02/2011	13(O)	0/0
541	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL, Tamil Nadu	01/2009	315.19	315.19	113.45	01/2010	02/2011	13(O)	0/0
542	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL, Rajasthan	06/2007	601.49	601.49	494.00	12/2008	03/2011	27(O)	0/0
543	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL, Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
544	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL, Punjab	09/2008	241.49	241.49	106.09	09/2009	03/2011	18(O)	0/0
545	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
546	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL, Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	03/2011	6(O)	0/0
547	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL, West Bengal	02/2008	584.33	584.33	398.08	02/2009	03/2011	25(O)	0/0
548	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) - [N26000089]BSNL, Gujarat	08/2008	868.00	868.00	352.89	08/2009	03/2011	19(O)	0/0
549	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) - [N26000090]BSNL, Madhya pradesh	11/2009	916.70	916.70	267.40	11/2010	03/2011	4(O)	0/0
550	GSM equipment of 1700000Lines (2G) 234100 lines 3(-) - [N26000092]BSNL, Karnataka	10/2008	677.75 719.90	719.90	395.08	10/2009	03/2011	17(O)	0/0
551	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00	384.00	-	10/2010	04/2011	6(O)	0/0
552	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007	08/2011	54(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0
554	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 389.86	389.86	3.06	09/2011 -	09/2011	0(O)	0/0
555	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
556	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	350.00	-	- -	-	-	0/0
557	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
558	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0
559	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	-	-	0/0
	Total		20,025.99 -	20,863.20	5,782.43				0/1
Urban Development									
560	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	181.30	-	04/2009 -	01/2011	21(O)	0/0
561	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00 8,605.36	18,894.36	18,050.62	06/2010 -	06/2011	12(O)	0/10
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15(O)	6/6
	Total		15,185.18 -	30,684.66	20,318.19				6/16
Water Resources									
563	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			626,925.56	752,140.93	336,176.40				890/2197

Sector wise current status of projects on the Flash Report

Telecommunications


I. Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning 38

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 41 projects, 1 project are on schedule and 2 projects are delayed .38 projects do not have fixed dates of commissioning.

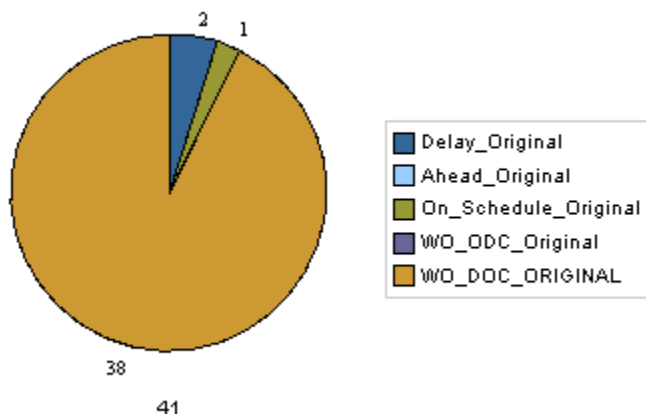

III. Investment Scenario

The Total Original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 20025.99 crore but this was subsequently revised to Rs. 20863.2 crore implying a cost overrun of 4.2%. The expenditure incurred on these projects till June, 2011 is Rs. 5782.43 crore, which is 27.7% of the revised cost of the projects.

Figures are in Rs. Crore

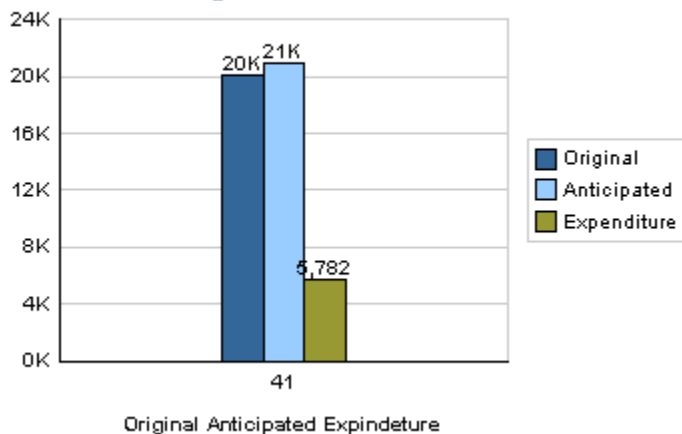

Sector wise current status of projects on the Flash Report

Shipping & Ports


I. Current Status:

Number of Projects	26
Number of Projects On Schedule	7
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning 5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 26 projects, 7 projects are on schedule and 14 projects are delayed .5 projects do not have fixed dates of commissioning.

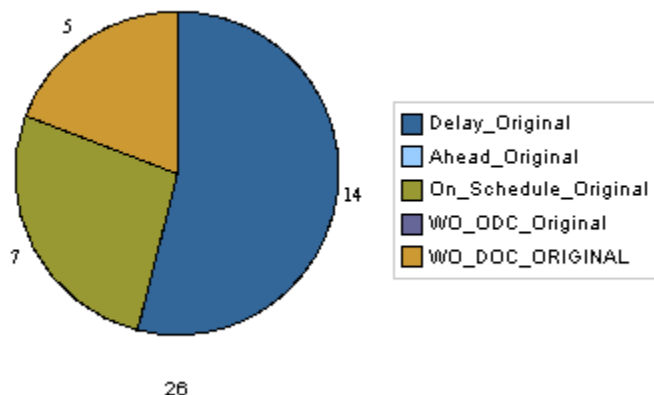

III. Investment Scenario

The Total Original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 18451.36 crore but this was subsequently revised to Rs. 19434.85 crore implying a cost overrun of 5.3%. The expenditure incurred on these projects till June, 2011 is Rs. 5037.09 crore, which is 25.9% of the revised cost of the projects.

Figures are in Rs. Crore

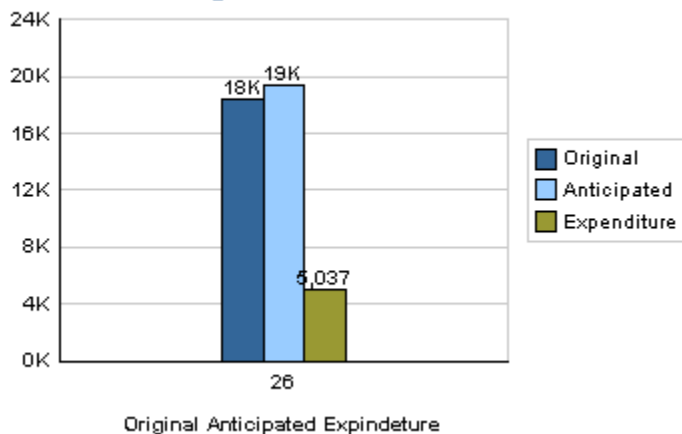

Sector wise current status of projects on the Flash Report


Road Transport & Highways

I. Current Status:

Number of Projects	125
Number of Projects On Schedule	33
Number of Projects Delayed	92

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 125 projects, 33 projects are on schedule and 92 projects are delayed.

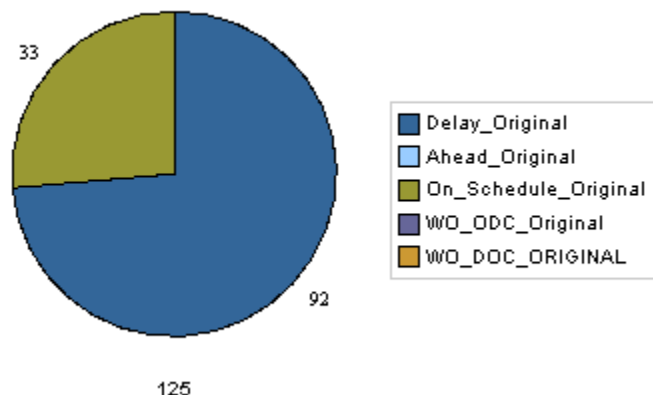

III. Investment Scenario

The Total Original cost of implementation of 125 projects when sanctioned, was of the order of Rs. 60796.85 crore but this was subsequently revised to Rs. 62260.26 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till June, 2011 is Rs. 43996.38 crore, which is 70.7% of the revised cost of the projects.

Figures are in Rs. Crore

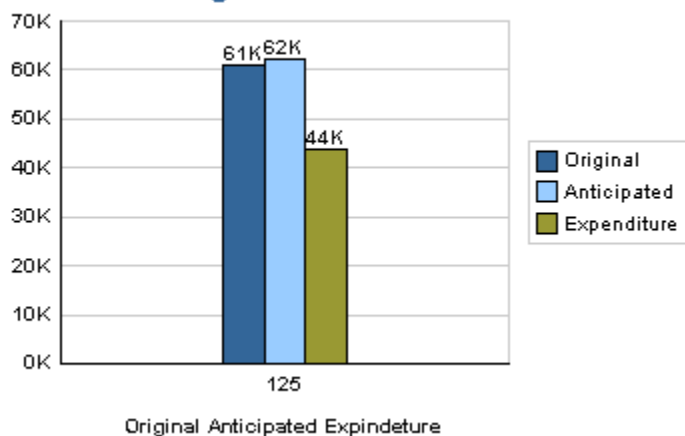

Sector wise current status of projects on the Flash Report


Railways

I. Current Status:

Number of Projects	136
Number of Projects On Schedule	14
Number of Projects Delayed	27
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	28
Number of Projects Without Date Of Commissioning	64

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 136 projects, 3 projects are ahead of schedule, 14 projects are on schedule and 27 projects are delayed .64 projects do not have fixed dates of commissioning.28 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

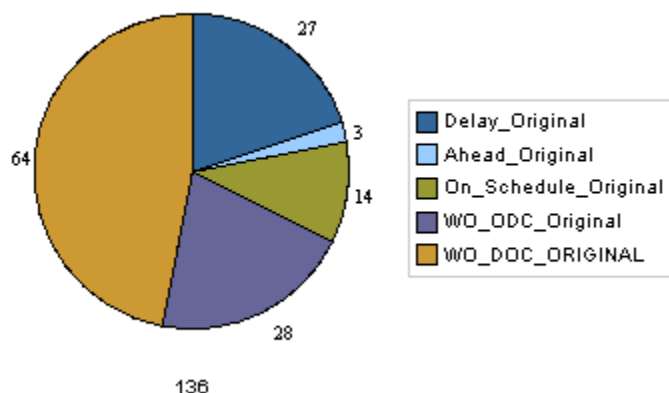

III. Investment Scenario

The Total Original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 66510.03 crore but this was subsequently revised to Rs. 123008.24 crore implying a cost overrun of 84.9%. The expenditure incurred on these projects till June, 2011 is Rs. 53223.37 crore, which is 43.3% of the revised cost of the projects.

Figures are in Rs. Crore

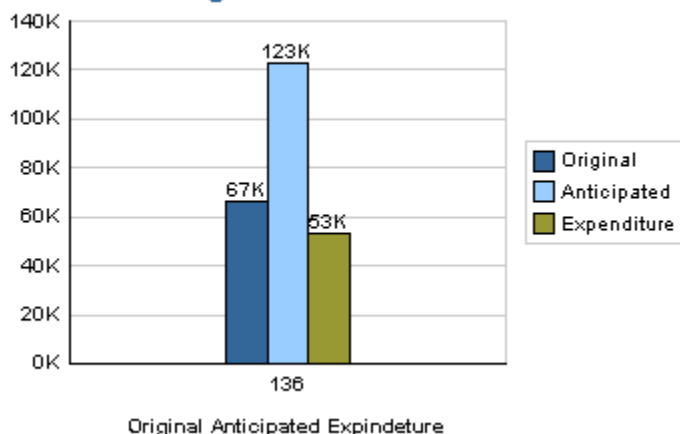

Sector wise current status of projects on the Flash Report

Power


I. Current Status:

Number of Projects	83
Number of Projects On Schedule	33
Number of Projects Delayed	42

Number of Projects Without Original Date of Commissioning	7
Number of Projects Without Date Of Commissioning	1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 83 projects, 33 projects are on schedule and 42 projects are delayed .1 project do not have fixed dates of commissioning.7 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

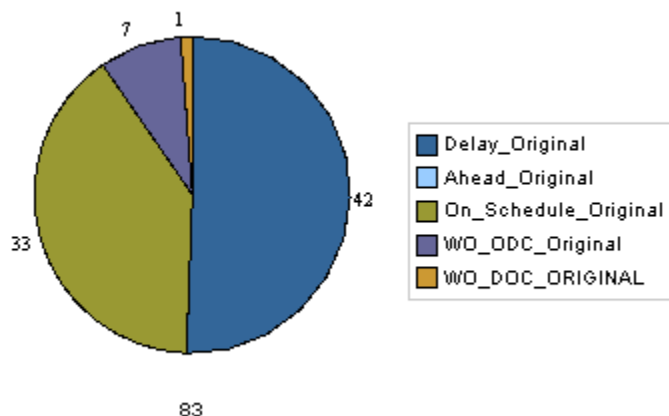

III. Investment Scenario

The Total Original cost of implementation of 83 projects when sanctioned, was of the order of Rs. 180092.42 crore but this was subsequently revised to Rs. 185360.17 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till June, 2011 is Rs. 85013.58 crore, which is 45.9% of the revised cost of the projects.

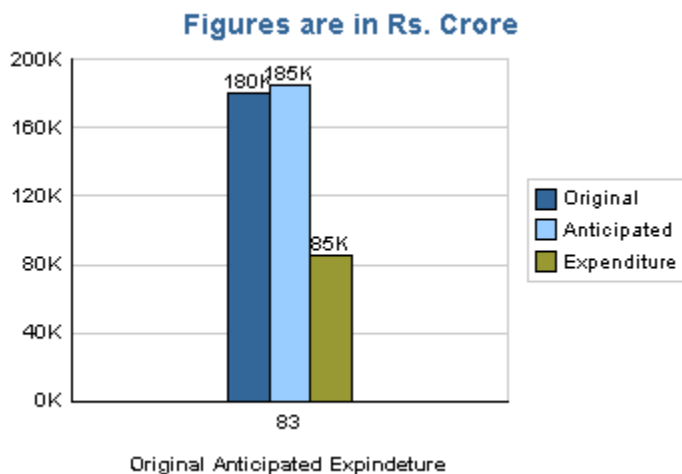

Sector wise current status of projects on the Flash Report


Petroleum

I. Current Status:

Number of Projects	72
Number of Projects On Schedule	21
Number of Projects Delayed	33
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	10
Number of Projects Without Date Of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 72 projects, 5 projects are ahead of schedule, 21 projects are on schedule and 33 projects are delayed .3 projects do not have fixed dates of commissioning.10 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

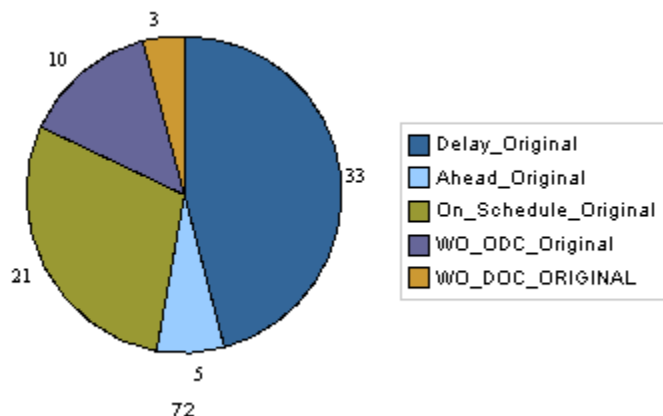

III. Investment Scenario

The Total Original cost of implementation of 72 projects when sanctioned, was of the order of Rs. 155657.83 crore but this was subsequently revised to Rs. 164212.95 crore implying a cost overrun of 5.5%. The expenditure incurred on these projects till June, 2011 is Rs. 58546.17 crore, which is 35.7% of the revised cost of the projects.

Figures are in Rs. Crore

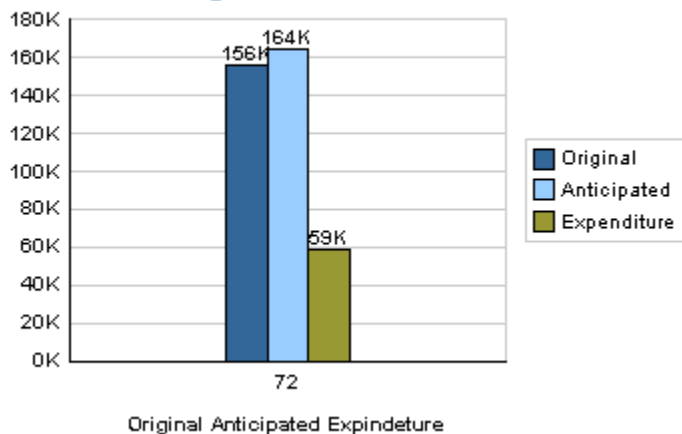

Sector wise current status of projects on the Flash Report

Steel


I. Current Status:

Number of Projects	15
Number of Projects On Schedule	2
Number of Projects Delayed	4

Number of Projects Without Original Date of Commissioning	9
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 2 projects are on schedule and 4 projects are delayed .9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

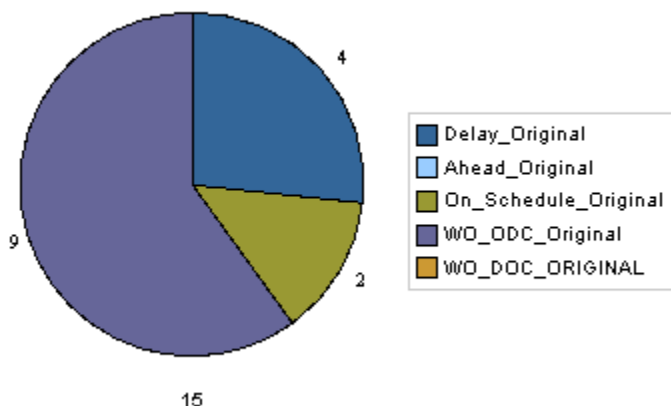

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 41398.4 crore but this was subsequently revised to Rs. 68476.43 crore implying a cost overrun of 65.4%. The expenditure incurred on these projects till June, 2011 is Rs. 26979.55 crore, which is 39.4% of the revised cost of the projects.

Figures are in Rs. Crore

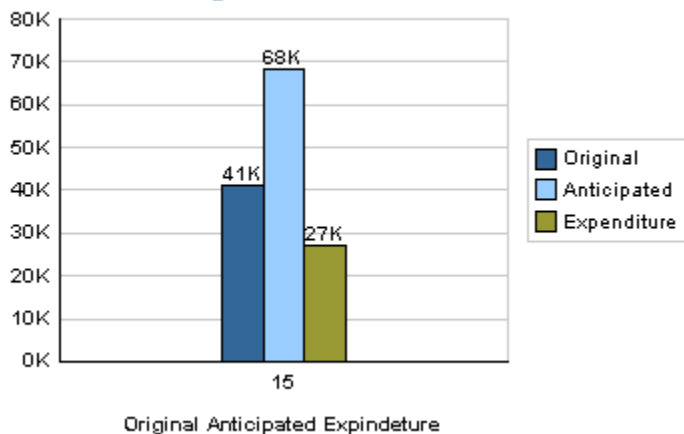

Sector wise current status of projects on the Flash Report


Fertilisers

I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

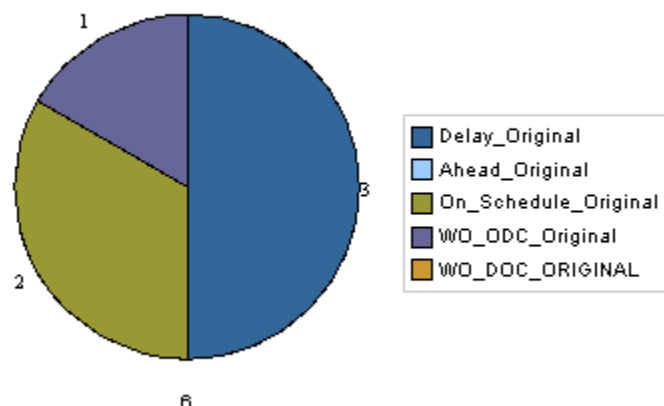

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till June, 2011 is Rs. 805.52 crore, which is 15.1% of the revised cost of the projects.

Figures are in Rs. Crore

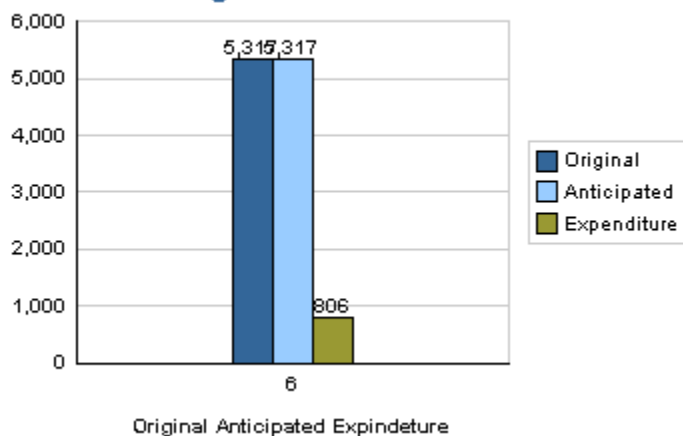

Sector wise current status of projects on the Flash Report

Coal


I. Current Status:

Number of Projects	45
Number of Projects On Schedule	23
Number of Projects Delayed	20

Number of Projects Without Original Date of Commissioning	2
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 45 projects, 23 projects are on schedule and 20 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

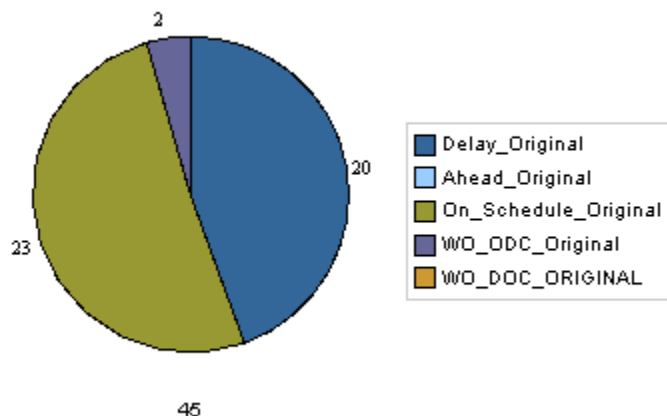

III. Investment Scenario

The Total Original cost of implementation of 45 projects when sanctioned, was of the order of Rs. 25504.15 crore but this was subsequently revised to Rs. 28789.58 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till June, 2011 is Rs. 11057.5 crore, which is 38.4% of the revised cost of the projects.

Figures are in Rs. Crore

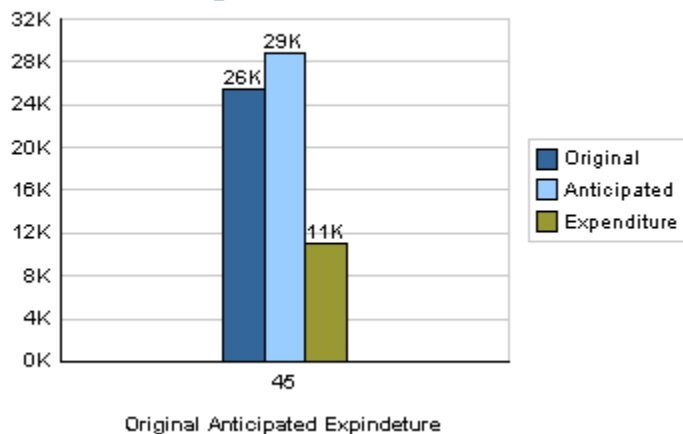

Sector wise current status of projects on the Flash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 3 projects are delayed.

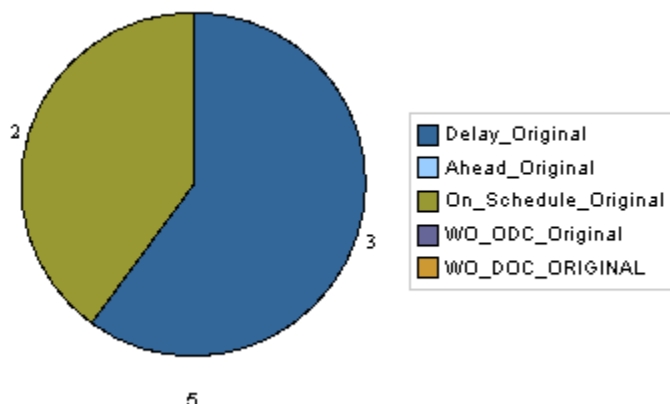

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4123.24 crore but this was subsequently revised to Rs. 4078.13 crore implying a cost overrun of -1.1%. The expenditure incurred on these projects till June, 2011 is Rs. 2591.86 crore, which is 63.6% of the revised cost of the projects.

Figures are in Rs. Crore

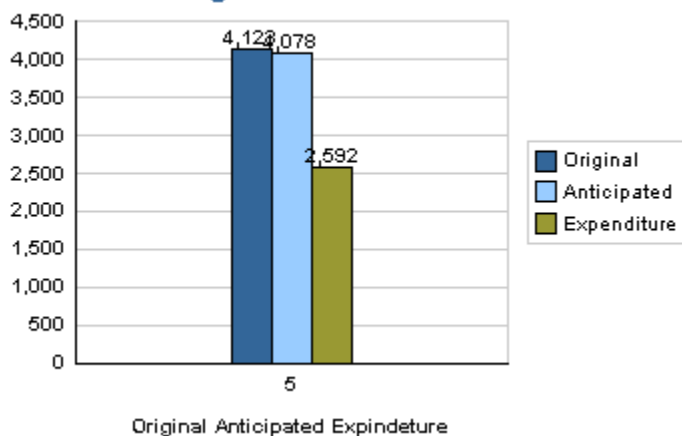

Sector wise current status of projects on the Flash Report


Atomic Energy

I. Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

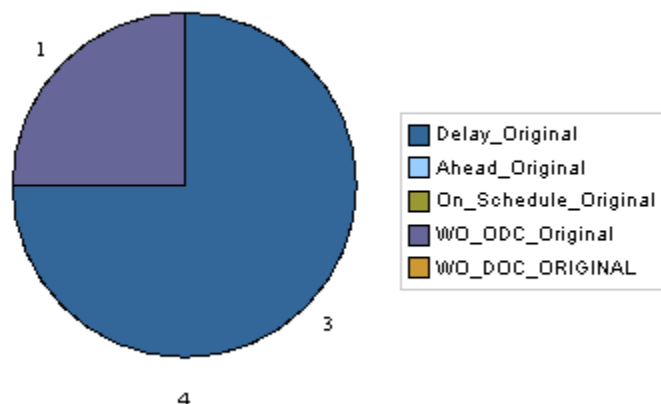

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 29228.29 crore but this was subsequently revised to Rs. 34066.29 crore implying a cost overrun of 16.6%. The expenditure incurred on these projects till June, 2011 is Rs. 18486.47 crore, which is 54.3% of the revised cost of the projects.

Figures are in Rs. Crore

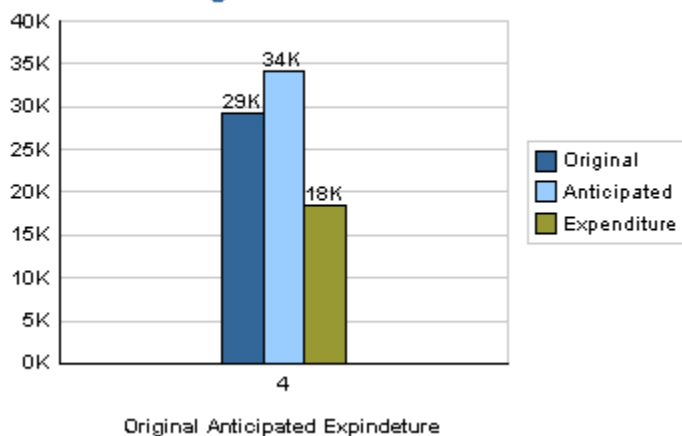

ANNEXURES

Summary of Central Sector Projects in Various States/UTs
(Status of projects as on 30.6.2011)

(Rs.Crores)					
Sr N.	State Name	No of Projects	Cost Original	Cost Anticipated	Expenditure
1	Andhra Pradesh	30	30608.05	36140.85	19497.60
2	Arunachal Pr.	4	9512.22	9610.51	6823.22
3	Assam	36	22310.13	27738.79	14872.46
4	Bihar	25	27068.60	30845.68	18869.84
5	Chhatisgarh	18	22208.97	37330.61	14479.27
6	Delhi	2	8925.00	19123.77	18116.82
7	Goa	1	204.73	204.73	35.99
8	Gujarat	26	30715.56	31681.98	5337.63
9	Haryana	10	5337.83	7054.75	4428.01
10	Himachal Pr.	7	15023.26	15105.54	11898.93
11	J & K	8	8293.37	18455.56	11230.83
12	Jharkhandd	20	9431.85	14022.85	5975.78
13	Karnataka	27	31565.39	38931.22	15972.98
14	Kerala	9	7247.37	7197.37	2770.50
15	Madhya pradesh	24	18438.11	18042.60	6472.54
16	Maharashtra	50	71427.08	85502.13	34239.34
17	Mizoram	2	988.06	3343.04	249.30
18	Multi State	106	122042.77	132759.53	44780.68
19	Nagaland	1	850.00	850.00	8.44
20	Orissa	20	49788.72	57651.17	16215.43
21	Punjab	9	5163.69	6149.65	3010.01
22	Rajasthan	16	13438.03	14167.15	8599.75
23	Sikkim	2	1648.88	3644.86	194.60
24	Tamil Nadu	33	42819.48	51851.16	34804.46
25	Tripura	3	1522.39	2053.24	341.18
26	Uttar Pradesh	31	17037.03	19172.13	10260.51
27	Uttaranchal	6	9191.07	11619.33	4604.86
28	West Bengal	27	38340.33	45801.89	21188.27
28		10	5773.89	6088.84	897.17
TOTAL		563	626921.86	752140.93	336176.4

List of Project With out Original Date of Commissioning

SN	NAME	AGENCY	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
	Atomic Energy				
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALLE	UCIL	N.A.	04/2011	04/2012
	Coal				
2	TUTICORIN THERMAL POWER PROJECT	NLC	N.A.	N.A.	10/2012
3	PENGANGA OC	WCL	N.A.	N.A.	10/2014
	Fertilisers				
4	THAL AMMONIA REVAMP PROJECT	RCF	N.A.	11/2011	11/2011
	Petroleum				
5	ASSAM GAS CRACKER PROJECT	BCPL	N.A.	N.A.	04/2012
6	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMBAI REFINERY	BPCL	N.A.	04/2013	04/2013
7	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	GAIL	N.A.	06/2011	07/2011
8	BAWANA NANGAL PIPE LINE PROJECT	GAIL	N.A.	12/2011	12/2011
9	PARADIP REFINERY PROJECT	IOCL	N.A.	N.A.	11/2012
10	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES AT PARADIP	IOCL	N.A.	N.A.	06/2012
11	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT	IOCL	N.A.	N.A.	02/2013
12	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pipeline)	IOCL	N.A.	N.A.	08/2013
13	PARADIP-RAIPUR-SAMBALPUR- RANCHI PIPELINE	IOCL	N.A.	09/2012	09/2012
14	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	IOCL	N.A.	N.A.	01/2013
	Power				
15	VINDHYACHAL STTP STAGE-IV	NTPC	N.A.	N.A.	12/2012
16	BONGAIGAON THERMAL POWER PROJECT	NTPC	N.A.	N.A.	10/2013
17	SIMHADRI STTP STAGE -II	NTPC	N.A.	N.A.	12/2011
18	Tapovan-Vishnugad HEP (4x130MW)	NTPC	N.A.	N.A.	06/2014
19	RIHAND STTP STAGE-III (2X500MW)	NTPC	N.A.	N.A.	12/2012
20	MOUDA STTP	NTPC	N.A.	N.A.	11/2012
21	BARH STTP STAGE -II	NTPC	N.A.	N.A.	10/2013
	Railways				
22	NANGALDAM-TALWARA(NL),NR	(NR)	N.A.	07/2012	07/2012
23	JIND-SONEPAT (NL),NR	(NR)	N.A.	03/2012	12/2012
24	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	N.A.	N.A.	08/2011
25	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	N.A.	N.A.	12/2011
26	KOSI BRIDGE (NL), ECR	ECR	N.A.	N.A.	12/2012
27	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	N.A.	N.A.	03/2012
28	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	N.A.	03/2011	03/2012
29	MUZAFFARPUR-SITAMARHI(NL),ECR	ECR	N.A.	N.A.	03/2012
30	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	N.A.	N.A.	03/2015
31	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	N.A.	12/2011	03/2012
32	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	N.A.	12/2009	02/2012
33	DEOGHAR - SULTANGANJ (INL), ER	ER	N.A.	12/2012	N.A.

SN	NAME	AGENCY	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
34	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTTP	N.A.	06/2013	06/2013
35	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	MRTTP	N.A.	12/2010	06/2011
36	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	NEFR	N.A.	N.A.	03/2012
37	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NEFR	N.A.	N.A.	03/2013
38	KANPUR-KASGANJ-MATHURA(GC),NER	NER	N.A.	N.A.	02/2012
39	DAUSA-GANGAPUR CITY(NL),NWR	NWR	N.A.	N.A.	03/2013
40	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	RE	N.A.	N.A.	12/2012
41	HARIDASPUR-PARADEEP(NL)	RVNL	N.A.	09/2009	12/2011
42	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	N.A.	N.A.	03/2012
43	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	N.A.	N.A.	12/2013
44	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	N.A.	N.A.	03/2012
45	CALICUT-MANGALORE (DL) (SR)	SR	N.A.	N.A.	07/2011
46	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	SWR	N.A.	03/2012	03/2012
47	VIRAMGAM-BHILDI(WR),GC	WR	N.A.	03/2013	03/2013
48	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT	WS&PU	N.A.	N.A.	03/2012
49	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU	WS&PU	N.A.	N.A.	03/2012
	Steel				
50	Bailadila Iron Ore Deposit- II(B)(NMDC)	NMDC	N.A.	N.A.	03/2012
51	330 TPH BOILER-6 AND AUXILIARY SYSTEM	RINL	N.A.	N.A.	11/2011
52	COKE OVEN BATTERY NO. 4 PHASE-II	RINL	N.A.	10/2012	10/2012
53	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	RINL	N.A.	N.A.	12/2011
54	Augmentation of Iron Ore Storage in RMHP	RINL	N.A.	05/2012	05/2012
55	INSTALLATION OF 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI	SAIL	N.A.	N.A.	08/2011
56	EXPANSION OF BOKARO STEEL PLANT	SAIL	N.A.	12/2011	12/2011
57	EXPANSION OF IISCO STEEL PLANT	SAIL	N.A.	12/2011	12/2011
58	EXPANSION OF BHILAI STEEL PLANT	SAIL	N.A.	03/2013	03/2013

List of Project With out Date of Commissioning

SN	NAME	AGENCY	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
Petroleum					
1	JHAJJAR HISSAR PIPE LINE PROJECT	GAIL	10/2010	N.A.	N.A.
2	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY	HPCL	09/2011	03/2012	05/2011
3	Pipeline Replacement project-2	ONGC	05/2011	N.A.	N.A.
Power					
4	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	12/2007	12/2009	N.A.
Railways					
5	REWARI-ROHTAK (NL),NR	(NR)	02/2010	02/2011	N.A.
6	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	(NR)	06/2007	N.A.	N.A.
7	AHMEDNAGAR-PARLI VAJNATH(NL) CR	CR	N.A.	N.A.	N.A.
8	AMRAVATI-NARKHER NL(CR)	CR	06/1999	03/2011	N.A.
9	KODERMA GIRIDH (NL), ECR	ECR	N.A.	N.A.	N.A.
10	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	N.A.	N.A.	N.A.
11	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	ECR	07/2005	N.A.	N.A.
12	KODERMA-TILAIYA (NL), ECR	ECR	N.A.	N.A.	N.A.
13	Pandabeswar-Chinpai doubling (ER)	ER	N.A.	12/2010	N.A.
14	BARDHAMAN-KATWA, ER (GC)	ER	12/2010	03/2011	N.A.
15	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	M RTP	12/2006	08/2010	N.A.
16	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/2004	N.A.	N.A.
17	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	12/2009	03/2011	N.A.
18	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	NCR	05/2008	03/2011	N.A.
19	KISHANGANJ JALALGARH, NL, NEFR	NEFR	N.A.	N.A.	N.A.
20	KATIHAR - JOGBANI (GC)(NEFR)	NEFR	N.A.	12/2010	N.A.
21	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NEFR	N.A.	N.A.	N.A.
22	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR	NEFR	N.A.	N.A.	N.A.
23	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NEFR	N.A.	03/2011	N.A.
24	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NEFR	N.A.	N.A.	N.A.
25	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	N.A.	N.A.	N.A.
26	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	NER	N.A.	N.A.	N.A.
27	MAHARAJGANJ-MASRAKH (NL) - NER	NER	N.A.	N.A.	N.A.
28	HATHUA-BHATNI (N L) (NER)	NER	N.A.	N.A.	N.A.
29	SRIGANGANAGAR-SARUPSAR (GC), NWR	NWR	N.A.	03/2011	N.A.
30	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	NWR	N.A.	11/2010	12/2010
31	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	RVNL	N.A.	N.A.	12/2010
32	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)	RVNL	03/2009	12/2008	N.A.
33	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	03/2008	06/2008	03/2011

SN	NAME	AGENCY	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
34	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	RVNL	03/2009	12/2009	12/2010
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	N.A.	03/2009	N.A.
36	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	RVNL	12/2012	N.A.	N.A.
37	RENIGUNTA-GUNTAKAL(RE)	RVNL	04/2003	03/2010	12/2010
38	RAJATGARH-BARANG(LD),ECOR	RVNL	N.A.	02/2009	N.A.
39	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	02/2015	N.A.	03/2011
40	BILASPUR-URKURA (DL)	RVNL	N.A.	03/2009	12/2010
41	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	12/2007	03/2010	N.A.
42	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	N.A.	N.A.	N.A.
43	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/2008	N.A.	N.A.
44	MUNEERABAD-MAHABOBNAGAR(NL),SCR	SCR	N.A.	N.A.	N.A.
45	GULBARGA-BIDAR,SCR(NL)	SCR	N.A.	05/2009	N.A.
46	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	N.A.	N.A.	N.A.
47	GADWAL - RAICHUR (NL), SCR	SCR	N.A.	02/2011	N.A.
48	GONDIA-JABALPUR(GC),(SECR)	SECR	03/1998	N.A.	N.A.
49	GOELKERA-MANOHARPUR,(LD)(SER)	SER	02/2006	N.A.	N.A.
50	RANCHI-LOHARDAGA(GC),SER	SER	06/2004	04/2005	N.A.
51	RUPSA-BANGRIPOSI (GC)(SER)	SER	03/1998	08/2005	N.A.
52	TIDIVANAM-NAGARI (NL)	SR	N.A.	N.A.	N.A.
53	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTHAMPALLI	SR	N.A.	N.A.	N.A.
54	KARUR-SALEM(NL),SR	SR	N.A.	N.A.	N.A.
55	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	N.A.	N.A.	N.A.
56	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	N.A.	N.A.	N.A.
57	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	N.A.	N.A.	N.A.
58	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	N.A.	N.A.	N.A.
59	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	N.A.	N.A.	N.A.
60	KOTTUR-HARIHAR(NL),(SWR)	SWR	N.A.	03/2011	N.A.
61	HUBLI-ANKOLA(NL),SWR	SWR	N.A.	N.A.	N.A.
62	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	N.A.	N.A.	N.A.
63	RAMGANJMUUNDI-BHOPAL (NL),WCR	WCR	N.A.	N.A.	10/2010
64	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	WR	03/2008	10/2010	N.A.
65	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR)	WR	03/2011	03/2011	03/2008
66	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	WR	03/1996	08/2009	02/2005
67	SURENDRANAGAR-BHAVNAGAR(GC),WR	WR	03/2004	03/2010	03/2011
68	RAJPIPLA-ANKELASHWAR, WR (GC)	WR	03/2011	N.A.	04/2011
Shipping & Ports					
69	DEVELOPMENT OF IRON ORE TERMINAL	ENNORE PORT LTD	08/2010	N.A.	03/2011

SN	NAME	AGENCY	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
70	DEVELOPMENT OF COAL TERMINAL	ENNORE PORT LTD	08/2010	N.A.	N.A.
71	SETHUSAMUDRAM SHIP CHANNEL PROJECT	PORT TRUST	10/2008	N.A.	N.A.
72	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	PORT TRUST	10/2008	N.A.	02/2011
73	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	04/2009	N.A.	02/2011
	Telecommunications				
74	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	BSNL	N.A.	03/2011	02/2011
75	GSM equipment of 945000Lines (2G) 225000lines 3(G) Bihar Phase V.1 Telecom Circle	BSNL	10/2008	N.A.	02/2011
76	GSM equipment of 1900000Lines (2G) 335500lines 3(G)kerala Phase V.1 Telecom Circle	BSNL	01/2010	N.A.	10/2010
77	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant	BSNL	03/2010	N.A.	N.A.
78	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle	BSNL	03/2009	N.A.	03/2011
79	GSM equipment of 900000Lines (2G) PunjabPhase V.2 Telecom Circle	BSNL	09/2009	N.A.	10/2010
80	PROJ.III OF NIB-II OF MESSAGING STORAGE	BSNL	12/2005	N.A.	03/2011
81	GSM equipment of 200000Lines (2G) UP(West)Phase V.2 Telecom Circle	BSNL	10/2009	N.A.	12/2010
82	Procurement of STM-16 ADM equipment	BSNL	03/2010	N.A.	03/2011
83	GSM equipment of 1867000Lines (2G) 383000 lines 3(G) GujaratPhase V.1 Telecom Circle	BSNL	08/2009	N.A.	03/2011
84	GSM equipment of 1100000Lines (2G) UP East Phase V.2 Telecom Circle	BSNL	09/2010	N.A.	02/2011
85	GSM equipment of 975000Lines (2G) 325000 lines 3(G) UP East Phase V.1 Telecom Circle	BSNL	02/2010	N.A.	11/2010
86	Procurement of DXC equipment	BSNL	03/2010	N.A.	12/2010
87	Procurement of STM-16 MADM equipment	BSNL	03/2010	N.A.	N.A.
88	Execution of telecom network requirement of defence forces	BSNL	03/2009	N.A.	N.A.
89	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06	BSNL	10/2007	N.A.	03/2011
90	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)PH-5	BSNL	12/2008	N.A.	02/2011
91	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1	BSNL	03/2009	N.A.	02/2011
92	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1	BSNL	12/2008	N.A.	02/2011
93	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	BSNL	03/2009	N.A.	03/2011
94	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN UP(W)-PH-V.I	BSNL	03/2009	N.A.	02/2011
95	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G)	BSNL	06/2009	N.A.	02/2011

SN	NAME	AGENCY	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
96	Assam Telecom Circle, Phase-V.I, 2G & 3G	BSNL	01/2009	N.A.	12/2010
97	Procurement of STM-1 SDH equipment	BSNL	03/2010	N.A.	N.A.
98	MANAGED LEASED LINE NETWORK PH-VI	BSNL	N.A.	N.A.	03/2011
99	GSM equipment of 1700000Lines (2G) 234100 lines 3(G)Karnataka Phase V.1 Telecom Circle	BSNL	10/2009	N.A.	03/2011
100	GSM equipment of 849862Lines (2G) 150138 lines 3(G) West Bengal Phase V.1 Telecom Circle	BSNL	02/2009	N.A.	02/2010
101	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3G) PH-5.1	BSNL	09/2009	N.A.	10/2010
102	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment	BSNL	03/2010	N.A.	12/2010
103	NIB-II PROJECT RURAL BROADBAND	BSNL	02/2008	N.A.	04/2011
104	ERP implementation in BSNL on Turnkey basis	BSNL	10/2010	N.A.	N.A.
105	Procurement of 10G (40 chl) DWDM equipment	BSNL	03/2009	N.A.	02/2011
106	GSM equipment of 614000Lines (2G) 150000lines 3(G) Chennai TD Phase V.1 Telecom Circle	BSNL	01/2010	N.A.	12/2010
107	Procurement of 10G 40 CHL (12 chi equipped) DWDM equipment (SDCA level)	BSNL	03/2010	N.A.	03/2011
108	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle	BSNL	11/2010	N.A.	12/2010
109	Procurement of 2.5G DWDM equipment	BSNL	03/2009	N.A.	02/2011
110	GSM equipment of 1500000Lines (2G) 264700lines 3(G)Andhra Pradesh Phase V.1 Telecom Circle	BSNL	01/2010	N.A.	01/2011
111	GSM equipment of 375000Lines (2G) 75000lines 3(G) Kolkatta Phase V.1 Telecom Circle	BSNL	06/2009	N.A.	01/2011
	Urban Development				
112	C/o office building for IDBI at bandra Kurla Complex,Mumbai	CPWD	04/2009	N.A.	

List of Projects Where in Revised cost Estimates'(s) is Required as on 01.07.2011

SN	PROJ_TITLE	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
	Atomic Energy				
1	KUDANKULAM APP (NPCIL)	NPCIL	13171.00	0.00	13811.00
	Petroleum				
2	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	HPCL	613.54	0.00	649.63
3	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	ONGC	2305.30	700.00	2416.96
	Power				
4	CHAMERA,STAGE-III (NHPC)	NHPC	1405.63	0.00	1620.85
5	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	NHPC	621.28	0.00	653.12
6	NIMOO BAZGO HYDROELECTRIC PROJECT	NHPC	611.02	0.00	641.85
7	TESSTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	NHPC	768.92	0.00	1318.78
8	KOTESHWAR HEP(THDC)	THDCL	1301.56	0.00	2433.70
	Railways				
9	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	(NR)	248.44	576.27	761.65
10	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	(NR)	409.00	625.30	808.81
11	JIND-SONEPAT (NL),NR	(NR)	190.81	238.56	261.90
12	REWARI-ROHTAK (NL),NR	(NR)	149.38	330.23	460.27
13	AMRAVATI-NARKHER NL(CR)	CR	120.90	284.27	437.73
14	LANJHIGARH-JUNAGARH NL(ECOR)	ECOR	100.00	142.90	181.46
15	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	233.00	335.77	526.53
16	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	78.23	0.00	82.96
17	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	114.01	283.95	334.48
18	MUZAFFARPUR-SITAMARHI(NL),ECR	ECR	100.00	322.29	416.10
19	PATNA GANGA BRIDGE (NL), ECR	ECR	624.47	0.00	916.18
20	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	184.00	254.07	425.95
21	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	FOIS	520.00	422.79	539.03
22	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	MRTP	3125.20	4174.40	4181.81
23	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	MRTP	907.69	1032.76	3058.65
24	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	108.00	214.09	219.60
25	GUNA-ETAWAH(NCR), NL	NCR	158.77	432.46	551.30
26	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NEFR	170.00	170.00	360.51
27	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	NEFR	156.00	0.00	165.19
28	KATIHAR - JOGBANI (GC)(NEFR)	NEFR	100.00	492.98	716.83
29	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	NEFR	1676.31	0.00	2698.07

SN	PROJ TITLE	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
30	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	NEFR	1000.00	1500.00	2203.80
31	KANPUR-KASGANJ-MATHURA(GC),NER	NER	395.00	1062.36	1139.38
32	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	323.40	0.00	402.51
33	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	NWR	262.00	456.00	547.25
34	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canvession (NWR)	NWR	643.36	0.00	787.55
35	ELECTRIFICATION OF MORADABAD-ROZA	RE	129.17	0.00	165.75
36	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	RVNL	240.00	0.00	255.49
37	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	136.62	0.00	148.47
38	RAJATGARH-BARANG(LD),ECOR	RVNL	166.16	0.00	230.33
39	RENIGUNTA-GUNTAKAL(RE)	RVNL	168.34	0.00	298.46
40	GADWAL - RAICHUR (NL), SCR	SCR	92.63	108.91	225.14
41	NANDYAL-YERRAGUNTALA(NL),SCR	SCR	155.74	164.36	452.91
42	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	124.43	407.78	475.35
43	GONDIA-JABALPUR(GC),(SECR)	SECR	386.30	0.00	524.23
44	BANKURA - DAMODAR (GC) (SER)	SER	111.90	0.00	379.62
45	RANCHI-LOHARDAGA(GC),SER	SER	194.07	0.00	263.34
46	RUPSA-BANGRIPOSI (GC)(SER)	SER	57.94	0.00	170.73
47	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	293.97	0.00	372.55
48	CALICUT-MANGALORE (DL) (SR)	SR	240.00	0.00	592.37
49	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	343.17	0.00	386.83
50	KARUR-SALEM(NL),SR	SR	155.55	0.00	537.63
51	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	280.00	0.00	668.74
52	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	100.00	0.00	466.66
53	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	295.00	0.00	455.06
54	KOTTUR-HARIHAR(NL),(SWR)	SWR	65.94	281.20	322.73
55	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	WR	148.61	0.00	256.66
56	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	WR	112.53	320.66	507.76
Road Transport & Highways					
57	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	NHAI	367.49	0.00	453.68
58	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	NHAI	221.82	0.00	227.95
59	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	NHAI	190.00	0.00	227.03
60	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	NHAI	193.00	0.00	329.36
61	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	NHAI	217.00	0.00	350.99
62	Bijapur-Hungund Section	NHAI	748.00	0.00	762.20

SN	PROJ TITLE	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
63	DAKOPA TO NAGAON (NH-36)(NHAI)	NHAI	225.00	0.00	246.91
64	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	486.00	0.00	520.68
65	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	NHAI	412.78	0.00	435.93
66	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	NHAI	275.00	0.00	292.53
67	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	NHAI	600.24	0.00	682.83
68	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	NHAI	227.00	0.00	383.91
69	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	NHAI	273.00	0.00	475.55
70	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	NHAI	220.00	0.00	220.65
71	Hazaribagh-Ranchi	NHAI	625.07	0.00	638.88
72	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	NHAI	210.00	0.00	672.97
73	JHAJHARPUR TO DARBANGA (BR-7)	NHAI	340.00	0.00	412.36
74	JHANSI TO LALITPUR, NH-26	NHAI	276.09	0.00	294.85
75	KASIA TO GORAKHPUR (NH-28)(NHAI)	NHAI	242.00	0.00	378.98
76	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	275.00	0.00	276.68
77	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	NHAI	240.00	0.00	242.58
78	KURALI-KIRATPUR, NH-21	NHAI	309.00	0.00	553.56
79	Kishangarh-Ajmer-Beawer	NHAI	795.00	0.00	804.29
80	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	NHAI	225.00	0.00	253.25
81	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	NHAI	629.00	0.00	910.04
82	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	NHAI	359.00	0.00	794.72
83	NAGPUR-KONDHALI,NH-6(NHAI)	NHAI	168.00	0.00	385.27
84	NALBARI TO BIJNI (AS-8)	NHAI	200.00	0.00	252.55
85	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	NHAI	441.00	0.00	875.17
86	NEW MANGALORE PORT NH-17 AND 48	NHAI	196.50	0.00	230.20
87	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	NHAI	557.00	0.00	930.92
88	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	NHAI	340.68	0.00	344.90
89	PATHANKOT BHOGPUR NH-1A	NHAI	229.00	0.00	324.68
90	PONDICHERY - TINDIVANAU NH-66	NHAI	285.00	0.00	358.94
91	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	NHAI	1108.00	0.00	2487.00
92	Pune-sholapur, pkg1	NHAI	1110.00	0.00	1121.00
93	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	NHAI	251.03	0.00	271.32
94	RINGBUNDS TO JHAJHANPUR (BR-6)	NHAI	340.00	0.00	554.48
95	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	NHAI	203.43	0.00	206.45

SN	PROJ_TITLE	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
96	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	NHAI	151.30	0.00	170.70
97	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	NHAI	941.00	0.00	1802.80
98	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	NHAI	157.47	0.00	174.00
99	SITAPUR-LUCKNOW	NHAI	322.00	0.00	553.66
100	SONAPUR TO GUWAHTI (AS-3)	NHAI	245.00	0.00	462.19
101	Surat- Dahisar(Six Lane) Km 263 to Km 502	NHAI	1693.75	0.00	2427.10
102	THANJAUR-TRICHY,NH-67(NHAI)	NHAI	280.00	0.00	580.22
103	THRISSUR TO ANGAMALI (NH-47)	NHAI	312.50	0.00	598.94
104	TRICHY - DINDIGUAL NH-45	NHAI	576.00	0.00	653.51
105	TRICHY - KORUR NH-67	NHAI	516.00	0.00	548.66
106	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	NHAI	227.00	0.00	363.15
107	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	NHAI	295.00	0.00	622.92
Shipping & Ports					
108	Construction & License out the OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR COAL HANDELLING	PORT TRUST	230.00	0.00	2190.00
109	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	245.67	0.00	293.57
110	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	BSNL	277.34	0.00	308.13
111	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	BSNL	760.20	0.00	792.83
Urban Development					
112	DELHI MRTS PHASE-II PROJECT	DMRC	8676.00	8605.36	18050.62

LIST OF DELAYED PROJECTS

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
	Atomic Energy							
1	KUDANKULAM APP (NPCIL)	Tamil Nadu	12/2008	05/2012	13171.00	15824.00	2653.00	41
2	KAKRAPAR ATOMIC POWER PROJECT - 3&4	Gujarat	12/2015	11/2016	11459.00	11459.00	0.00	11
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Tamil Nadu	09/2010	01/2012	3492.00	5677.00	2185.00	16
	Civil Aviation							
4	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TER BLDG(K1)	Tamil Nadu	01/2011	10/2011	1273.00	1273.00	0.00	9
5	C/o new Airport at Pakyong(Sikkim) Airport	Sikkim	01/2011	06/2012	309.40	264.29	-45.11	17
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	West Bengal	05/2011	12/2011	1942.51	1942.51	0.00	7
	Coal							
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	Tamil Nadu	06/2009	03/2012	2030.78	2453.57	422.79	33
8	BARSINGSAR TPS (2X125MW) (NLC)	Rajasthan	06/2009	08/2011	1114.18	1626.09	511.91	26
9	KULDA OCP (MAHANADI COALFIELDS LTD.)	Orissa	03/2010	03/2012	302.96	302.96	0.00	24
10	ASHOK EXPN.OCP -CCL (6.5 MTY)	Jharkhand	03/2011	03/2013	471.66	341.63	-130.03	24
11	KRISHNASHILA (NCL) (4MTY)	Madhya pradesh	03/2010	03/2013	789.88	741.56	-48.32	36
12	BLOCK-B OCP NCL (3.5 MTY)	Madhya pradesh	03/2012	03/2015	746.04	437.34	-308.70	36
13	AMLOHRI EPR (NCL) (6 MTY)	Madhya pradesh	03/2014	03/2016	1352.04	1143.54	-208.50	24
14	MAGADH OC (CCL)	Jharkhand	07/2012	03/2016	469.78	706.40	236.62	44
15	ADRIYALA SHAFT PROJECT	Andhra Pradesh	03/2013	06/2013	212.34	779.26	566.92	3
16	GOPAL PRASAD OCP	Orissa	03/2013	03/2015	395.87	395.87	0.00	24
17	TALABIRA OCP	Orissa	03/2015	03/2016	447.72	447.72	0.00	12

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
18	BALRAM OCP EXTENSION	Orissa	03/2009	03/2012	172.08	172.08	0.00	36
19	Tapin OCP	Jharkhand	03/2012	03/2014	264.68	264.68	0.00	24
20	GEVRA EXPANSION OCP (SECL) (25 MTY)	Chhatisgarh	03/2010	03/2014	1667.55	2675.67	1008.12	48
21	RAJMAHAL OC EXP.	Multi State	03/2011	03/2014	50.08	153.82	103.74	36
22	KAKATIYA LAONGWALL	Multi State	12/2012	03/2015	453.63	453.63	0.00	27
23	JHANJRA LONGWAL UG PHASE II	West Bengal	03/2011	03/2015	287.18	287.17	-0.01	48
24	Churi Benti UG	Jharkhand	03/2011	03/2014	163.51	163.51	0.00	36
25	North Urimari OCP	Jharkhand	03/2012	03/2014	179.87	179.87	0.00	24
26	DIPKA EXPANSION OCP (SECL) (20 MTY)	Chhatisgarh	03/2010	03/2014	1268.53	1943.66	675.13	48
Fertilisers								
27	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS	Madhya pradesh	07/2011	11/2011	325.00	325.00	0.00	4
28	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	Punjab	12/2012	01/2013	1478.63	1478.63	0.00	1
29	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJAIPUR-II	Madhya pradesh	07/2011	03/2012	438.00	438.00	0.00	8
Mines								
30	SECOND PHASE EXPANSION OF NALCO MINE, REFINERY, SMELTER AND CAPTIVE POWER PLANT	Orissa	12/2008	06/2011	4091.51	4401.76	310.25	30
Petroleum								
31	IOR LAKWA - LAKHMANI (ONGCL)	Assam	03/2007	03/2014	345.10	663.69	318.59	84
32	IOR GELEKI (ONGCL)	Assam	03/2007	03/2017	390.09	1674.11	1284.02	120
33	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON	Assam	09/2009	07/2011	1431.91	1690.13	258.22	22
34	DEVELOPMENT OF C-SERIES FIELDS	Maharashtra	12/2008	11/2011	3195.16	2800.00	-395.16	35

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
35	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	Maharashtra	06/2010	10/2011	2305.30	3005.30	700.00	16
36	DEVELOPMENT OF B-22 CLUSTER FIELDS	Maharashtra	09/2010	05/2012	2323.40	2920.82	597.42	20
37	DEVELOPMENT OF B-193 CLUSTER FIELDS	Maharashtra	08/2010	06/2012	3248.78	5633.44	2384.66	22
38	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	Maharashtra	05/2010	03/2013	5713.03	8813.41	3100.38	34
39	DEVELOPMENT OF B-46 CLUSTER FIELD	Maharashtra	07/2010	05/2012	1436.21	1436.21	0.00	22
40	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA	Gujarat	04/2011	07/2012	370.11	370.11	0.00	15
41	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I	Multi State	03/2012	08/2012	4543.43	2500.00	-2043.43	5
42	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	Multi State	06/2011	03/2012	463.32	340.00	-123.32	9
43	MNW-NF BRIDGE PROJECT	Maharashtra	03/2009	02/2012	175.21	162.12	-13.09	35
44	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY	Andhra Pradesh	09/2011	03/2012	3597.00	2730.00	-867.00	6
45	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REFINERY	Assam	12/2009	08/2011	293.60	262.00	-31.60	20
46	IOR, RUDRASAGAR (ONGCL)	Assam	03/2006	03/2013	113.90	438.85	324.95	84
47	North Tapti Gas Field Development	Multi State	03/2011	06/2011	589.70	755.76	166.06	3
48	REFRIGERATED LPG STORAGE AT JNPT	Maharashtra	12/2010	07/2011	304.40	304.40	0.00	7
49	ADDITIONAL GAS PROCESSING UNITS AT URAN	Maharashtra	12/2011	01/2013	1797.35	1797.35	0.00	13
50	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)	Gujarat	05/2008	07/2011	900.92	976.08	75.16	38
51	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I & II	Madhya pradesh	04/2011	12/2011	1512.00	982.00	-530.00	8

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
52	EURO-IV DHDT	Tamil Nadu	05/2011	12/2011	2615.69	2615.69	0.00	7
53	REVAMPING OF WIN PLATFORM AT MH ASSET	Maharashtra	05/2010	05/2012	333.40	656.51	323.11	24
54	HEERA RECONSTRUCTION	Maharashtra	04/2010	12/2011	706.70	706.70	0.00	20
55	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	Multi State	09/2011	12/2011	736.65	736.65	0.00	3
56	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Bihar	12/2010	06/2011	613.54	727.88	114.34	6
57	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	Tamil Nadu	12/2010	08/2011	224.00	299.00	75.00	8
58	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH	Maharashtra	03/2010	03/2012	740.02	740.02	0.00	24
59	NEELAM RECONSTRUCTION	Maharashtra	04/2011	12/2011	305.08	305.08	0.00	8
60	COMPRESSOR STATIONS (KAILARAS & CHAINSA)	Multi State	04/2011	12/2011	1167.00	810.00	-357.00	8
61	CONSTRUCTION OF NEW PROCESS COMPLEX MHN	Maharashtra	05/2010	05/2012	2853.29	6326.40	3473.11	24
62	INTEGRATED DEV OF G1 and GS-15 (ONGCL)	Multi State	04/2006	05/2012	429.82	2218.01	1788.19	73
63	BNPL SPURLINE (UTTRANCHAL & PUNJAB)	Multi State	06/2011	07/2012	540.92	400.00	-140.92	13
	Power							
64	TUIRIAL HE PROJECT(NEEPCO)	Mizoram	07/2006	01/2014	368.72	913.63	544.91	90
65	KOTESHWAR HEP(THDC)	Uttaranchal	04/2005	03/2012	1301.56	2398.39	1096.83	83
66	PARBATI HEP (NHPC) II	Himachal Pr.	09/2009	07/2014	3919.59	3919.59	0.00	58
67	SUBANSIRI LOWER H.E.P (NHPC)	Arunachal Pr.	09/2010	08/2014	6285.33	6285.33	0.00	47
68	TESSTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	West Bengal	03/2007	05/2012	768.92	768.92	0.00	62

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
69	SIPAT STPP STAGE - I (NTPC)	Chhatisgarh	12/2009	03/2012	8323.39	8323.39	0.00	27
70	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	Arunachal Pr.	05/2013	06/2016	2496.90	2496.90	0.00	37
71	CHAMERA,STAGE-III (NHPC)	Himachal Pr.	08/2010	09/2011	1405.63	1405.63	0.00	13
72	BARH STPP STAGE I (3X660MW) NTPC	Bihar	11/2010	09/2014	8693.00	8693.00	0.00	46
73	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	West Bengal	09/2009	12/2012	1061.38	1061.38	0.00	39
74	PARBATI H.E.P. STAGE -III (NHPC)	Himachal Pr.	10/2010	03/2012	2304.52	2304.52	0.00	17
75	URI H.E.P STAGE -II (NHPC)	J & K	11/2009	12/2011	1724.79	1724.79	0.00	25
76	KUDANKULAM-APP TRANS. SYSTEM (PGCIL)	Tamil Nadu	11/2008	03/2012	1779.29	1946.85	167.56	40
77	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)	Bihar	09/2009	12/2011	3779.46	3725.13	-54.33	27
78	EASTERN REGION STRENGTHENING SCHEME-I	Multi State	10/2009	03/2012	975.96	894.26	-81.70	29
79	LOHARINAG-PAL HEP(4X150MW)	Uttaranchal	11/2011	12/2012	2895.10	2895.10	0.00	13
80	NIMOO BAZGO HYDROELECTRIC PROJECT	J & K	08/2010	11/2012	611.02	611.02	0.00	27
81	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	J & K	02/2011	10/2011	621.28	621.28	0.00	8
82	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI III HEP	Himachal Pr.	01/2010	11/2011	557.24	639.52	82.28	22
83	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II	J & K	05/2011	09/2011	238.25	227.03	-11.22	4
84	RAMPUR HEP(412 MW)	Himachal Pr.	01/2012	09/2013	2047.03	2047.03	0.00	20
85	KISHANGANGA HEP	J & K	07/2014	01/2016	2238.67	3642.04	1403.37	18
86	EASTERN REGION STRENGTHENING SCHEME-II	Multi State	06/2010	09/2011	227.52	227.52	0.00	15
87	WESTERN REGION STRENGTHENING SCHEME-V	Maharashtra	09/2010	03/2013	477.69	477.69	0.00	30
88	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMERA-II HEP	Himachal Pr.	09/2010	08/2011	262.10	262.10	0.00	11

[illegible]

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
106	GUNA-ETAWAH(NCR), NL	Multi State	03/1994	12/2011	158.77	540.96	382.19	213
107	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	J & K	03/2001	12/2017	2500.00	11270.00	8770.00	201
108	LANJHIGARH-JUNAGARH NL(ECOR)	Orissa	03/2002	09/2011	100.00	170.00	70.00	114
109	NANDYAL-YERRAGUNTALA(NL),SCR	Andhra Pradesh	02/2009	12/2011	155.74	429.49	273.75	34
110	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Assam	04/2008	03/2014	1000.00	3230.01	2230.01	71
111	HOWRAH-AMTA-CHAMPADANGA NL (SER)	West Bengal	03/2007	06/2012	31.42	499.16	467.74	63
112	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Multi State	12/2008	03/2014	733.00	1655.80	922.80	63
113	BANKURA - DAMODAR (GC) (SER)	West Bengal	03/2005	12/2012	111.90	1211.22	1099.32	93
114	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Multi State	03/2011	03/2016	727.56	3056.85	2329.29	60
115	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	Bihar	03/2009	12/2012	921.00	981.00	60.00	45
116	PATNA GANGA BRIDGE (NL), ECR	Bihar	10/2007	12/2012	624.47	1389.98	765.51	62
117	SALKA ROAD -ANUPNAGAR LINE DOUBLING	Chhatisgarh	03/2010	03/2012	324.90	324.90	0.00	24
118	PANSPURA-KHARAGPUR 3D LINE	West Bengal	02/2010	11/2011	252.50	252.50	0.00	21
119	BHOPAL BINA 3D LINE DOUBLING	Madhya pradesh	03/2010	12/2012	687.20	687.20	0.00	33
120	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	Uttar Pradesh	03/2010	06/2014	325.00	369.90	44.90	51
121	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canvession (NWR)	Rajasthan	03/2011	03/2012	643.36	803.39	160.03	12
122	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbander (MTP)	West Bengal	03/2016	06/2016	2397.72	2397.72	0.00	3
123	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP)	West Bengal	03/2014	03/2016	2069.60	2069.60	0.00	24

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
124	Dakshin-barasat-lakshmikantapur (ER)	West Bengal	12/2011	02/2012	259.51	259.51	0.00	2
125	Ghutiasharif-Canning (ER)	West Bengal	12/2011	11/2013	189.97	189.97	0.00	23
126	Rattam-Mhow-Khandwa-Akola (GC)	Madhya pradesh	03/2012	03/2013	603.04	603.04	0.00	12
127	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Multi State	03/1995	03/2012	520.00	634.13	114.13	204
128	Katakhal to Bhairabi	Assam	12/2012	12/2013	227.90	223.01	-4.89	12
129	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP	Maharashtra	03/2014	03/2015	5300.00	5300.00	0.00	12
130	ELECTRIFICATION OF MORADABAD-ROZA	Uttar Pradesh	03/2011	03/2012	129.17	220.00	90.83	12
131	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Multi State	03/2009	12/2013	1676.31	4091.33	2415.02	57
132	TAMLUK DIGHA, LINE DOUBLING (SER)	West Bengal	06/2005	03/2012	293.97	723.27	429.30	81
Road Transport & Highways								
133	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4)	Karnataka	08/2004	09/2011	241.00	196.65	-44.35	85
134	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	Karnataka	08/2004	09/2011	318.00	207.56	-110.44	85
135	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)	Orissa	04/2004	10/2011	225.00	241.53	16.53	90
136	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Uttar Pradesh	03/2005	12/2011	367.49	367.49	0.00	81
137	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	West Bengal	03/2005	09/2011	273.00	522.00	249.00	78
138	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY (NHAI) OTHERS	Tamil Nadu	04/2007	07/2011	210.00	210.00	0.00	51
139	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Uttar Pradesh	09/2007	12/2011	275.00	275.00	0.00	51
140	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24	Uttar Pradesh	09/2007	12/2011	220.00	220.00	0.00	51

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
141	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Gujarat	11/2007	08/2011	412.78	479.54	66.76	45
142	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	Uttar Pradesh	09/2008	12/2011	155.00	201.66	46.66	39
143	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	Uttar Pradesh	10/2008	09/2011	193.00	193.00	0.00	35
144	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	Uttar Pradesh	10/2008	08/2011	217.00	217.00	0.00	34
145	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Assam	06/2005	12/2011	230.00	230.00	0.00	78
146	VIJAYAPUR TO PATHANKOT (J AND K) NH-1A KM.16.35 TO KM.50.00	J & K	03/2008	07/2011	193.09	166.30	-26.79	40
147	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	J & K	03/2008	07/2011	166.27	193.10	26.83	40
148	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A	Punjab	05/2008	08/2012	284.00	359.00	75.00	51
149	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Bihar	10/2008	12/2011	240.00	240.00	0.00	38
150	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	Uttar Pradesh	10/2008	12/2011	227.00	227.00	0.00	38
151	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Uttar Pradesh	03/2008	12/2011	340.68	340.68	0.00	45
152	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	Uttar Pradesh	03/2009	07/2011	359.00	359.00	0.00	28
153	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Chhatisgarh	01/2009	10/2011	190.00	190.00	0.00	33
154	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	Tamil Nadu	11/2010	08/2011	629.00	629.00	0.00	9
155	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Assam	02/2009	12/2011	280.00	280.00	0.00	34
156	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000	Assam	04/2009	07/2013	199.81	385.13	185.32	51
157	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54	Assam	11/2008	12/2013	167.64	167.64	0.00	61

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
158	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450	Assam	11/2008	07/2013	155.04	280.13	125.09	56
159	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500	Assam	04/2009	12/2011	200.00	200.00	0.00	32
160	DAKOBA TO NAGAON (NH-36)(NHAI)	Assam	06/2008	10/2011	225.00	225.00	0.00	40
161	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Assam	06/2008	12/2011	195.00	195.00	0.00	42
162	KASIA TO GORAKHPUR (NH-28)(NHAI)	Uttar Pradesh	12/2008	12/2011	242.00	242.00	0.00	36
163	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Uttar Pradesh	12/2008	12/2011	227.00	227.00	0.00	36
164	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI)	Assam	06/2008	12/2011	237.80	237.80	0.00	42
165	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Bihar	09/2008	12/2011	332.94	332.94	0.00	39
166	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Rajasthan	10/2008	11/2011	275.00	250.39	-24.61	37
167	LALITPUR TO SAGAR, NH-26 (NHAI)	Madhya pradesh	11/2008	12/2011	198.00	198.00	0.00	37
168	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Madhya pradesh	10/2008	09/2011	225.00	225.00	0.00	35
169	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Uttar Pradesh	10/2008	11/2011	151.30	151.30	0.00	37
170	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Madhya pradesh	10/2008	03/2012	203.43	203.43	0.00	41
171	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Madhya pradesh	10/2008	12/2011	251.03	251.03	0.00	38
172	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA)	Madhya pradesh	10/2008	12/2011	229.91	229.91	0.00	38
173	SILIGURI TO ISLAMPUR (WB-7)	West Bengal	07/2008	12/2012	225.00	225.00	0.00	53
174	RINGBUNDS TO JHAJHANPUR (BR-6)	Bihar	06/2008	07/2011	340.00	340.00	0.00	37
175	JHAJHARPUR TO DARBANGA (BR-7)	Bihar	09/2008	12/2011	340.00	340.00	0.00	39
176	NALBARI TO BIJNI (AS-8)	Assam	06/2008	12/2011	200.00	200.00	0.00	42
177	SITAPUR-LUCKNOW	Uttar Pradesh	06/2009	12/2011	322.00	322.00	0.00	30
178	THRISSUR TO ANGAMALI (NH-47)	Kerala	03/2009	07/2011	312.50	312.50	0.00	28

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
179	GUWHATI TO NALBARI (AS-4)	Assam	04/2008	03/2012	175.96	175.96	0.00	47
180	NEW MANGALORE PORT NH-17 AND 48	Karnataka	06/2008	07/2011	196.50	196.50	0.00	37
181	NAGAON TO DHARAMTUL (AS-2)	Assam	06/2008	12/2011	264.72	264.72	0.00	42
182	SONAPUR TO GUWAHTI (AS-3)	Assam	03/2008	12/2011	245.00	245.00	0.00	45
183	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	West Bengal	11/2008	09/2011	221.82	221.82	0.00	34
184	GUWAHATI TO NALBARI (AS-5)	Assam	04/2008	03/2012	198.16	198.16	0.00	47
185	NALBARI TO BIJNI (AS-6)	Assam	06/2008	12/2011	225.00	225.00	0.00	42
186	NALBARI T BIJNI (AS-7)	Assam	04/2008	12/2011	208.00	208.00	0.00	44
187	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Assam	05/2008	12/2011	160.00	160.00	0.00	43
188	DHARAMTUL TO SONAPUR (AS-19)	Assam	06/2008	12/2011	200.00	200.00	0.00	42
189	NAGPUR-KONDHALI,NH-6(NHAI)	Maharashtra	12/2008	10/2011	168.00	168.00	0.00	34
190	THANJAUR-TRICHY,NH-67(NHAI)	Tamil Nadu	06/2009	12/2011	280.00	280.00	0.00	30
191	GANJAM-ICCHAPURUM,NH-5(NHAI)	Orissa	02/2004	12/2012	263.27	263.27	0.00	106
192	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54	Assam	09/2007	12/2013	212.00	212.00	0.00	75
193	HARANGAJO TO MAIBANG, NH-54	Assam	07/2009	12/2013	196.00	196.00	0.00	53
194	BRAHMPUTRA BRIDGE,NH NO-31	Assam	04/2010	03/2012	217.61	217.61	0.00	23
195	CHAMBAL BRIDGE, NH-76 (RJ-5)	Rajasthan	02/2010	03/2012	275.00	281.31	6.31	25
196	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Uttar Pradesh	10/2009	12/2011	600.24	600.24	0.00	26
197	KURALI-KIRATPUR, NH-21	Punjab	06/2010	07/2011	309.00	309.00	0.00	13
198	GWALIOR BYPSS, NH-75,3	Madhya pradesh	10/2009	06/2012	300.93	300.93	0.00	32
199	GWALIOR-JHANSI, NH-75	Multi State	12/2009	06/2012	604.00	604.00	0.00	30
200	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AND AFFLUX-BOND (BR-5)	Bihar	03/2010	12/2011	418.04	418.04	0.00	21
201	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7	Madhya pradesh	06/2010	10/2012	407.60	407.60	0.00	28

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
202	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7	Madhya pradesh	09/2009	10/2012	263.17	263.17	0.00	37
203	JHANSI TO LALITPUR, NH-25,26	Uttar Pradesh	09/2009	12/2011	355.06	355.06	0.00	27
204	JHANSI TO LALITPUR, NH-26	Uttar Pradesh	09/2009	08/2011	276.09	276.09	0.00	23
205	AGRA-BYPASS(NS-1/UP-1), NH-2,3	Uttar Pradesh	09/2007	06/2013	348.16	348.16	0.00	69
206	TRICHY - DINDIGUAL NH-45	Tamil Nadu	07/2010	07/2011	576.00	576.00	0.00	12
207	PONDICHERY - TINDIVANAU NH-66	Tamil Nadu	07/2010	07/2011	285.00	285.00	0.00	12
208	TRICHY - KORUR NH-67	Tamil Nadu	07/2010	12/2011	516.00	516.00	0.00	17
209	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Tamil Nadu	01/2011	12/2011	941.00	941.00	0.00	11
210	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Karnataka	07/2010	07/2011	441.00	441.00	0.00	12
211	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Kerala	02/2010	05/2012	557.00	557.00	0.00	27
212	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Multi State	09/2010	06/2012	232.45	232.45	0.00	21
213	PATHANKOT BHOGPUR NH-1A	Punjab	05/2010	12/2011	229.00	284.00	55.00	19
214	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5	Orissa	02/2004	07/2011	228.70	228.70	0.00	89
215	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Multi State	08/2010	12/2011	295.00	295.00	0.00	16
216	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	Chhatisgarh	01/2011	07/2011	464.00	464.00	0.00	6
217	DELHI/ HARYANA BORDER TO ROHTAK	Haryana	05/2010	11/2011	486.00	486.00	0.00	18
218	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Andhra Pradesh	10/2011	08/2012	572.30	572.30	0.00	10
219	Bijapur-Hungund Section	Karnataka	09/2010	03/2013	748.00	748.00	0.00	30

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
220	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Multi State	10/2011	06/2012	1673.70	1673.70	0.00	8
221	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass	Maharashtra	06/2011	10/2012	1170.52	1170.52	0.00	16
222	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Assam	09/2007	03/2012	157.47	154.57	-2.90	54
223	Gujarat/Maharashtra Border Surat-Hazira Port Section	Gujarat	09/2012	10/2012	1509.10	1509.10	0.00	1
224	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	Bihar	10/2008	06/2012	300.00	300.00	0.00	44
Shipping & Ports								
225	DEEPENING OF CHANNEL AT PARADIP PORT	Orissa	12/2007	06/2011	154.84	253.36	98.52	42
226	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	Maharashtra	12/2010	09/2012	1228.00	1460.00	232.00	21
227	C/O Berthing and Allied Facilities off tekra near TUNA	Gujarat	02/2011	03/2013	882.00	1060.00	178.00	25
228	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH	Gujarat	12/2005	10/2011	165.00	165.00	0.00	70
229	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT COCHIN	Kerala	01/2009	05/2013	375.00	272.50	-102.50	52
230	Acquisition of two nos. of 120 B.P	Maharashtra	06/2011	01/2012	290.85	305.00	14.15	7
231	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN	Kerala	01/2012	03/2012	3500.00	3500.00	0.00	2
232	MARINE LIQUID TERMINALS	Tamil Nadu	06/2006	09/2011	196.25	196.25	0.00	63
233	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	Gujarat	03/2011	03/2013	702.00	755.50	53.50	24
234	Mechanization of coal handling facilities to 200000 DWT Vessels on DBFOT basis	Andhra Pradesh	06/2010	11/2012	444.10	444.10	0.00	29
235	Construction & License out the OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR COAL HANDELLING	Karnataka	12/2010	06/2011	230.00	272.50	42.50	6
236	Acquisition of Two nos. of 3060 DWT	Maharashtra	12/2011	05/2012	277.03	277.03	0.00	5

SN	TITLE	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TOR IN MONTHS
237	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS	Maharashtra	04/2011	11/2011	359.44	359.44	0.00	7
238	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	Tamil Nadu	03/2006	03/2012	150.00	600.00	450.00	72
	Steel							
239	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	Andhra Pradesh	10/2009	10/2012	8692.00	12291.00	3599.00	36
240	EXPENSION OF ROURKELA STEEL PLANT	Orissa	02/2011	03/2013	6133.00	11812.00	5679.00	25
241	Rebuilding of coke oven battery No.1 & 2 (Bokaro Steel Plant)	Jharkhand	04/2010	09/2011	500.90	500.90	0.00	17
242	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)	Jharkhand	01/2010	06/2011	172.78	172.78	0.00	17
	Telecommunications							
243	CONVERGENT BILLING AND CRM-MTNL(DELHI)	Delhi	02/2007	08/2011	249.00	229.41	-19.59	54
244	CONVERGENT BILLING AND CRM(MUMBAI)	Maharashtra	02/2007	08/2011	247.00	247.00	0.00	54
	Urban Development							
245	BANGALORE METRO RAIL PROJECT	Karnataka	12/2011	03/2013	6395.00	11609.00	5214.00	15
246	DELHI MRTS PHASE-II PROJECT	Delhi	06/2010	06/2011	8676.00	18894.36	10218.36	12
	Water Resources							
247	PAGLADIYA DAM PROJECT	Assam	12/2007	12/2012	542.90	1187.00	644.10	60

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Civil Aviation</u>									
5	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00	1,273.00	881.21	01/2011	10/2011	9(O)	0/0
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	1,942.51	1,256.92	05/2011	12/2011	7(O)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73	204.73	35.99	05/2012	05/2012	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40	264.29	141.91	01/2011	06/2012	17(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60	393.60	275.83	06/2013	06/2013	0(O)	0/0
<u>Coal</u>									
15	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28	207.28	39.83	03/2012	03/2012	0(O)	0/0
<u>Fertilisers</u>									
56	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011	11/2011	4(O)	0/0
57	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011	03/2012	8(O)	0/0
<u>Steel</u>									
73	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	11,812.00	1,253.17	02/2011	03/2013	25(O)	0/0
75	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	-	04/2013	04/2013	0(O)	0/0
76	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	-	05/2013	05/2013	0(O)	0/0
<u>Petroleum</u>									
77	Pipeline Replacement project-2 - [N16000111]ONGC,Multi State	12/2007	2,553.28	3,796.21	3,631.29	05/2011	05/2011	0(O)	0/0
78	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70	755.76	475.47	03/2011	06/2011	1(R3)	0/0
79	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	727.88	649.63	12/2010	06/2011	6(O)	0/0
81	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	1,690.13	1,589.43	09/2009	07/2011	22(O)	0/0
83	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	304.40	237.80	12/2010	07/2011	0(R3)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
84	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam	04/2008	293.60 -	262.00	222.56	12/2009 -	08/2011	20(O)	0/0
85	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	215.41	12/2010 08/2011	08/2011	0(R3)	0/0
87	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	666.63	12/2011 -	09/2011	-3(O)	0/0
88	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
89	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
93	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	185.33	03/2013 03/2013	12/2011	-15(R1)	0/0
94	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	603.92	04/2010 -	12/2011	20(O)	0/0
95	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	239.95	04/2011 -	12/2011	8(O)	0/0
96	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.29	09/2011 -	12/2011	3(O)	0/0
98	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	160.06	09/2012 -	12/2011	-9(O)	0/0
99	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	6,140.98	01/2012 -	01/2012	0(O)	0/0
100	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	02/2012	35(O)	0/0
101	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
102	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	471.12	09/2011 03/2012	03/2012	0(R3)	0/0
105	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
107	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	-	04/2006 05/2011	05/2012	12(R3)	0/0
108	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,123.56	05/2010 05/2012	05/2012	0(R3)	0/0
109	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,094.03	09/2010 03/2012	05/2012	2(R3)	0/0
110	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	12.57	05/2010 04/2012	05/2012	1(R3)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	58.17	07/2010 05/2012	05/2012	0(R3)	0/0
113	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,222.69	08/2010 03/2012	06/2012	3(R3)	0/0
114	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	485.72	06/2012 -	06/2012	0(O)	0/0
116	Wind Power Project - [N16000119]ONGC,Gujarat	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
117	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	58.95	04/2011 -	07/2012	15(O)	0/0
119	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	331.24	07/2012 -	07/2012	0(O)	0/0
121	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	79.93	08/2012 -	08/2012	0(O)	0/0
122	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,091.16	09/2012 -	09/2012	0(O)	0/0
124	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	15.78	09/2012 -	09/2012	0(O)	0/0
126	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	64.38	12/2011 -	01/2013	13(O)	0/0
128	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	01/2013 -	01/2013	0(O)	0/0
131	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,706.08	05/2010 03/2013	03/2013	0(R3)	0/0
132	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	332.48	03/2013 -	03/2013	0(O)	0/0
133	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
134	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
135	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0
137	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	1.69	- -	08/2013	-	0/0
138	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
139	Wax Project - [N16000101]NRL,Assam	08/2010	576.60 -	576.60	9.71	02/2014 -	12/2013	-2(O)	0/0
140	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
141	Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	85.38	02/2014 -	02/2014	0(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
143	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
144	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
145	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
147	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
148	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	2,174.00	384.00	09/2011	-	-	0/0
			2,174.00			03/2012			
Power									
149	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	110.81	06/2011	06/2011	0(O)	0/0
150	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	163.60	09/2010	08/2011	11(O)	0/0
151	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,620.85	08/2010	09/2011	13(O)	0/0
152	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	210.27	05/2011	09/2011	4(R3)	0/0
153	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	132.58	06/2010	09/2011	15(O)	0/0
157	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	50.50	11/2011	11/2011	0(O)	0/0
158	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,479.33	11/2009	12/2011	25(O)	0/0
162	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	289.82	07/2011	12/2011	5(O)	0/0
163	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	232.90	02/2012	02/2012	0(O)	0/0
164	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	32.53	02/2012	02/2012	0(O)	0/0
165	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	146.64	08/2011	02/2012	6(O)	0/0
166	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	205.32	07/2010	02/2012	0(R3)	0/0
167	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	63.84	07/2011	02/2012	7(O)	0/0
173	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	65.58	04/2012	04/2012	0(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
175	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	282.88	06/2012 -	06/2012	0(O)	0/0
176	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	215.86	103.63	06/2012 -	06/2012	0(O)	0/0
177	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	9.00	06/2012 -	06/2012	0(O)	0/0
178	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,641.85	08/2012 -	08/2012	0(O)	0/0
179	765 KV POOLING STATION & NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	3,791.31	08/2012 -	08/2012	0(O)	0/0
180	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	293.13	08/2012 -	08/2012	0(O)	0/0
181	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	1,803.44	10/2012 -	10/2012	0(O)	0/0
182	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	469.38	138.86	10/2012 -	10/2012	0(O)	0/0
183	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	11.32	10/2012 -	10/2012	0(O)	0/0
184	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02 -	611.02	641.85	08/2010 -	11/2012	27(O)	0/0
186	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	281.08	11/2012 -	11/2012	0(O)	0/0
187	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	221.30	11/2012 -	11/2012	0(O)	0/0
188	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	85.33	11/2012 -	11/2012	0(O)	0/0
189	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	970.13	09/2009 -	12/2012	39(O)	0/0
194	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	258.25	12/2012 -	12/2012	0(O)	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	25.54	01/2013 -	01/2013	0(O)	0/0
196	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	17.35	01/2013 -	01/2013	0(O)	0/0
198	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	338.50	09/2010 -	03/2013	30(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	249.15	11/2011 -	03/2013	16(O)	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	240.82	11/2011 -	03/2013	16(O)	0/0
201	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	116.00	02/2012 -	03/2013	13(O)	0/0
202	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	800.49	02/2012 -	03/2013	13(O)	0/0
203	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	224.08	05/2012 -	03/2013	10(O)	0/0
204	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	108.70	03/2013 -	03/2013	0(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	62.92	04/2013 -	04/2013	0(O)	0/0
206	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	8.71	04/2013 -	04/2013	0(O)	0/0
207	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	79.60	01/2012 -	07/2013	18(O)	0/0
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	33.39	07/2013 -	07/2013	0(O)	0/0
210	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	59.89	08/2013 -	08/2013	0(O)	0/0
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	15.15	08/2013 -	08/2013	0(O)	0/0
212	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	125.56	08/2013 -	08/2013	0(O)	0/0
214	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	124.59	11/2011 -	09/2013	22(O)	0/0
217	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	55.83	11/2013 -	11/2013	0(O)	0/0
218	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	210.01	12/2013 -	12/2013	0(O)	0/0
220	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	-	03/2014 -	03/2014	0(O)	0/0
225	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	2,597.57	08/2013 -	09/2014	13(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
226	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	-	01/2015 -	01/2015	0(O)	0/0
228	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67 -	3,642.04	755.56	07/2014 -	01/2016	18(O)	0/0
<u>Railways</u>									
232	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 589.86	563.25	544.32	03/2004 03/2010	02/2005	-61(R3)	0/0
233	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	464.50	507.76	03/1996 08/2009	03/2008	-17(R3)	0/0
234	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	256.66	03/2008 10/2010	10/2010	0(R3)	0/0
235	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	230.33	- 02/2009	12/2010	22(R1)	0/0
236	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	184.86	- 03/2009	12/2010	21(R1)	0/0
237	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	148.47	12/2007 03/2010	12/2010	9(R1)	0/0
238	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
239	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	-	- -	12/2010	-	0/0
240	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0
241	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	255.49	03/2009 12/2009	03/2011	15(R1)	0/0
242	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	164.13	03/2011 -	03/2011	0(O)	0/0
244	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	592.37	- -	07/2011	-	0/0
245	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	152.68	- -	08/2011	-	0/0
246	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	181.46	03/2002 -	09/2011	114(O)	0/0
247	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	158.66	02/2010 -	11/2011	21(O)	0/0
248	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	551.30	03/1994 -	12/2011	213(O)	0/0
249	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	452.91	02/2009 -	12/2011	34(O)	0/0
250	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	195.75	- 09/2009	12/2011	27(R1)	0/0
251	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	74.88	- -	12/2011	-	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
252	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	212.57	03/2013 -	12/2011	-15(O)	0/0
253	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,139.38	- -	02/2012	-	0/0
254	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	388.84	- 12/2009	02/2012	26(R1)	0/0
255	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	58.50	12/2011 -	02/2012	2(O)	0/0
256	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	539.03	03/1995 -	03/2012	204(O)	0/0
257	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	617.62	475.35	- -	03/2012	-	0/0
258	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	425.95	- 12/2011	03/2012	3(R3)	0/0
259	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	197.09	- 03/2012	03/2012	0(R3)	0/0
260	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	416.10	- -	03/2012	-	0/0
261	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	526.53	- -	03/2012	-	0/0
262	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	69.10	- -	03/2012	-	0/0
263	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	334.48	- 03/2011	03/2012	12(R3)	0/0
264	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	180.10	- -	03/2012	-	0/0
265	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	868.14	- -	03/2012	-	0/0
266	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	187.08	03/2010 -	03/2012	24(O)	0/0
267	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	165.19	- -	03/2012	-	0/0
268	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	74.98	03/2012 -	03/2012	0(O)	0/0
269	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	165.75	03/2011 -	03/2012	12(O)	0/0
270	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	372.55	06/2005 07/2011	03/2012	8(R3)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
271	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	787.55	03/2011 -	03/2012	12(O)	0/0
272	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	41.89	03/2012 -	03/2012	0(O)	0/0
273	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	318.24	0.92	03/2012 -	03/2012	0(O)	0/0
274	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	131.08	03/2007 03/2007	06/2012	63(R1)	0/0
275	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	320.95	- 07/2012	07/2012	0(R3)	0/0
276	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	564.81	- -	12/2012	-	0/0
277	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	761.65	12/2012 -	12/2012	0(O)	0/0
278	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	379.62	03/2005 12/2008	12/2012	48(R1)	0/0
279	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	261.90	- 03/2012	12/2012	9(R3)	0/0
280	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	231.78	- -	12/2012	-	0/0
281	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	506.69	03/2009 -	12/2012	45(O)	0/0
282	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	916.18	10/2007 -	12/2012	62(O)	0/0
283	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	326.42	03/2010 -	12/2012	33(O)	0/0
284	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	98.08	12/2012 -	12/2012	0(O)	0/0
285	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	143.89	- 03/2013	03/2013	0(R3)	0/0
286	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	145.40	- -	03/2013	-	0/0
287	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	607.43	- -	03/2013	-	0/0
288	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	39.90	03/2012 -	03/2013	12(O)	0/0
289	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	350.81	0.49	03/2013 -	03/2013	0(O)	0/0
290	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	116.15	- 06/2013	06/2013	0(R3)	0/0
291	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	52.94	12/2011 -	11/2013	23(O)	0/0
292	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	159.94	- -	12/2013	-	0/0
293	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	82.41	12/2012 -	12/2013	12(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
294	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Multi State	04/1996	1,676.31	4,091.33	2,698.07	03/2009	12/2013	57(O)	0/0
295	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,203.80	04/2008 03/2014	03/2014	0(R3)	0/0
296	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00	1,655.80	727.51	12/2008	03/2014	63(O)	0/0
297	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	1,141.76	181.65	03/2014	03/2014	0(O)	0/0
298	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	2,429.41	3.53	04/2014	03/2014	-1(O)	0/0
299	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19	653.19	5.87	03/2014	03/2014	0(O)	0/0
300	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23	516.23	38.28	03/2014	03/2014	0(O)	0/0
301	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62	1,389.62	156.72	03/2014	03/2014	0(O)	0/0
302	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00	369.90	94.67	03/2010 06/2014	06/2014	0(R3)	0/0
303	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66	324.66	161.74	-	03/2015	-	0/0
304	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00	5,300.00	239.18	03/2014	03/2015	12(O)	0/0
305	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48	3,380.57	52.69	12/2015	03/2015	-9(O)	0/0
306	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74	829.74	-	03/2015	03/2015	0(O)	0/0
307	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00	850.00	8.44	03/2015	03/2015	0(O)	0/0
308	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,056.85	426.90	03/2011 03/2014	03/2016	24(R3)	0/0
309	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60	2,069.60	0.21	03/2014	03/2016	24(O)	0/0
310	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98	3,951.98	1.42	03/2016	03/2016	0(O)	0/0
311	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02	2,619.02	23.10	03/2016	03/2016	0(O)	0/0
312	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	2,397.72	-	03/2016	06/2016	3(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
313	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001 -	12/2017	201(O)	0/0
314	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	233.91	- -	-	-	0/0
315	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	87.09	12/2012 -	-	-	0/0
316	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	78.91	- -	-	-	0/0
317	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	455.06	- -	-	-	0/0
318	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
319	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	945.73	537.63	- -	-	-	0/0
320	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	64.07	- -	-	-	0/0
321	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	84.54	- -	-	-	0/0
322	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
323	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,034.47	07/2005 -	-	-	0/0
324	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	369.70	132.09	- 05/2009	-	-	0/0
325	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	82.96	- -	-	-	0/0
326	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	808.81	06/2007 -	-	-	0/0
327	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	298.46	04/2003 03/2010	-	-	0/0
328	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	466.66	- -	-	-	0/0
329	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.74	- -	-	-	0/0
330	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	298.25	- 12/2012	-	-	0/0
331	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
332	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	72.56	- -	-	-	0/0
333	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	206.59	- -	-	-	0/0
334	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	173.49	170.73	03/1998 08/2005	-	-	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
335	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0
336	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	- -	-	-	0/0
337	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	261.70	17.05	02/2006 -	-	-	0/0
338	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	296.80	03/2008 06/2008	-	-	0/0
339	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	169.27	- -	-	-	0/0
340	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	386.83	- -	-	-	0/0
341	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	21.22	- -	-	-	0/0
342	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	78.89	- -	-	-	0/0
343	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	35.45	- -	-	-	0/0
344	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
345	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	437.73	06/1999 03/2011	-	-	0/0
346	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	165.26	03/2004 -	-	-	0/0
347	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	547.25	- 11/2010	-	-	0/0
348	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	322.73	- 03/2011	-	-	0/0
349	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	263.34	06/2004 04/2005	-	-	0/0
350	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	499.50	05/2008 03/2011	-	-	0/0
351	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	219.60	12/2009 03/2011	-	-	0/0
352	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	1,015.84	716.83	- 12/2010	-	-	0/0
353	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	383.68	- -	-	-	0/0
355	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	668.74	- -	-	-	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
356	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,058.65	12/2006 08/2010	-	-	0/0
357	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	225.14	- 02/2011	-	-	0/0
358	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	460.27	02/2010 02/2011	-	-	0/0
359	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	347.04	- -	-	-	0/0
360	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	231.62	- 03/2011	-	-	0/0
361	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	117.60	- -	-	-	0/0
362	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	130.85	- -	-	-	0/0
363	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	360.51	- 03/2011	-	-	0/0
364	NEW B.G. LINE FROM TETELIA TO BYRNihat (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	75.23	- -	-	-	0/0
365	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	141.04	12/2010 03/2011	-	-	0/0
366	Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	126.21	- 12/2010	-	-	0/0
367	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	166.83	03/2011 03/2011	-	-	0/0
Road Transport & Highways									
368	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	672.97	04/2007 -	07/2011	51(O)	0/0
369	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	166.30	177.03	03/2008 -	07/2011	40(O)	0/0
370	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27 -	193.10	145.14	03/2008 -	07/2011	40(O)	0/0
371	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	794.72	03/2009 -	07/2011	28(O)	0/0
372	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00 -	340.00	554.48	06/2008 -	07/2011	37(O)	0/0
373	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	598.94	03/2009 -	07/2011	28(O)	0/0
374	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	196.50	230.20	06/2008 -	07/2011	37(O)	0/0
375	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00 -	309.00	553.56	06/2010 -	07/2011	13(O)	0/0
376	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	653.51	07/2010 -	07/2011	12(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
377	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	285.00	358.94	07/2010	07/2011	12(O)	0/0
378	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	875.17	07/2010	07/2011	12(O)	0/0
379	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	141.87	02/2004	07/2011	89(O)	0/0
380	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	419.88	01/2011	07/2011	6(O)	0/0
381	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78	479.54	435.93	11/2007	08/2011	45(O)	0/0
382	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI, Uttar Pradesh	12/2003	217.00	217.00	350.99	10/2008	08/2011	34(O)	0/0
383	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI, Tamil Nadu	03/2005	629.00	629.00	910.04	11/2010	08/2011	9(O)	0/0
384	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09	276.09	294.85	09/2009	08/2011	23(O)	0/0
385	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,427.10	08/2011	08/2011	0(O)	0/0
386	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	142.70	08/2004	09/2011	85(O)	0/0
387	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	154.57	08/2004	09/2011	85(O)	0/0
388	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	475.55	03/2005	09/2011	78(O)	0/0
389	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI, Uttar Pradesh	12/2003	193.00	193.00	329.36	10/2008	09/2011	35(O)	0/0
390	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00	225.00	253.25	10/2008	09/2011	35(O)	0/0
391	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	227.95	11/2008	09/2011	34(O)	0/0
392	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	62.64	04/2004	10/2011	90(O)	0/0
393	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.03	01/2009	10/2011	33(O)	0/0
394	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	246.91	06/2008	10/2011	40(O)	0/0
395	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	385.27	12/2008	10/2011	34(O)	0/0
396	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	171.47	10/2011	10/2011	0(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
397	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	276.68	10/2008 -	11/2011	37(O)	0/0
398	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	170.70	10/2008 -	11/2011	37(O)	0/0
399	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	520.68	05/2010 -	11/2011	18(O)	0/0
400	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	2,487.00	11/2011 -	11/2011	0(O)	0/0
401	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	12/2011	81(O)	0/0
402	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	292.53	09/2007 -	12/2011	51(O)	0/0
403	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	220.65	09/2007 -	12/2011	51(O)	0/0
404	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	83.27	09/2008 -	12/2011	39(O)	0/0
405	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	201.89	06/2005 -	12/2011	78(O)	0/0
406	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	242.58	10/2008 -	12/2011	38(O)	0/0
407	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	383.91	10/2008 -	12/2011	38(O)	0/0
408	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	344.90	03/2008 -	12/2011	45(O)	0/0
409	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	220.52	02/2009 -	12/2011	34(O)	0/0
410	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	76.49	04/2009 -	12/2011	32(O)	0/0
411	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	167.16	06/2008 -	12/2011	42(O)	0/0
412	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00 -	242.00	378.98	12/2008 -	12/2011	36(O)	0/0
413	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	363.15	12/2008 -	12/2011	36(O)	0/0
414	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	193.28	06/2008 -	12/2011	42(O)	0/0
415	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	261.52	09/2008 -	12/2011	39(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
416	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI, Madhya Pradesh	12/2003	198.00 -	198.00	185.80	11/2008 -	12/2011	37(O)	0/0
417	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	271.32	10/2008 -	12/2011	38(O)	0/0
418	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya Pradesh	12/2003	229.91 -	229.91	217.35	10/2008 -	12/2011	38(O)	0/0
419	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00	412.36	09/2008 -	12/2011	39(O)	0/0
420	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	252.55	06/2008 -	12/2011	42(O)	0/0
421	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00 -	322.00	553.66	06/2009 -	12/2011	30(O)	0/0
422	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	235.04	06/2008 -	12/2011	42(O)	0/0
423	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	462.19	03/2008 -	12/2011	45(O)	0/0
424	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	160.93	06/2008 -	12/2011	42(O)	0/0
425	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	197.17	04/2008 -	12/2011	44(O)	0/0
426	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	111.59	05/2008 -	12/2011	43(O)	0/0
427	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	183.39	06/2008 -	12/2011	42(O)	0/0
428	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	580.22	06/2009 -	12/2011	30(O)	0/0
429	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24 -	600.24	682.83	10/2009 -	12/2011	26(O)	0/0
430	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04 -	418.04	313.39	03/2010 -	12/2011	21(O)	0/0
431	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	294.38	09/2009 -	12/2011	27(O)	0/0
432	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	548.66	07/2010 -	12/2011	17(O)	0/0
433	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,802.80	01/2011 -	12/2011	11(O)	0/0
434	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00 -	284.00	324.68	05/2010 -	12/2011	19(O)	0/0
435	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00 -	295.00	622.92	08/2010 -	12/2011	16(O)	0/0
436	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	344.24	02/2012 -	02/2012	0(O)	0/0
437	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	174.00	09/2007 -	03/2012	54(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
438	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	206.45	10/2008	03/2012	41(O)	0/0
439	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	109.34	04/2008	03/2012	47(O)	0/0
440	GUWHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	169.55	04/2008	03/2012	47(O)	0/0
441	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	126.52	04/2010	03/2012	23(O)	0/0
442	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	178.58	02/2010	03/2012	25(O)	0/0
443	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.92	02/2010	05/2012	27(O)	0/0
444	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,121.00	05/2012	05/2012	0(O)	0/0
445	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	804.29	05/2012	05/2012	0(O)	0/0
446	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	268.00	05/2012	05/2012	0(O)	0/0
447	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	156.08	10/2008	06/2012	44(O)	0/0
448	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	293.85	10/2009	06/2012	32(O)	0/0
449	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	412.09	12/2009	06/2012	30(O)	0/0
450	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	156.99	09/2010	06/2012	21(O)	0/0
451	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	388.13	06/2012	06/2012	0(O)	0/0
452	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	1,477.60	10/2011	06/2012	8(O)	0/0
453	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	314.52	07/2012	07/2012	0(O)	0/0
454	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	112.15	05/2008	08/2012	51(O)	0/0
455	Chilkaluri-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	572.30	500.02	10/2011	08/2012	10(O)	0/0
456	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.52	08/2012	08/2012	0(O)	0/0
457	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	407.60	183.69	06/2010	10/2012	28(O)	0/0
458	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	233.27	09/2009	10/2012	37(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
459	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
460	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	813.11	09/2012	10/2012	1(O)	0/0
461	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	804.62	10/2012	10/2012	0(O)	0/0
462	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	618.89	11/2012	11/2012	0(O)	0/0
463	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
464	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
465	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	175.11	07/2008	12/2012	53(O)	0/0
466	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	245.28	02/2004	12/2012	106(O)	0/0
467	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	355.11	12/2012	12/2012	0(O)	0/0
468	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07	625.07	638.88	01/2013	01/2013	0(O)	0/0
469	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00	748.00	762.20	09/2010	03/2013	30(O)	0/0
470	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
471	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	236.23	03/2013	03/2013	0(O)	0/0
472	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
473	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	97.32	03/2013	03/2013	0(O)	0/0
474	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
475	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	158.26	05/2013	05/2013	0(O)	0/0
476	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	104.94	05/2013	05/2013	0(O)	0/0
477	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
478	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	111.06	09/2007	06/2013	69(O)	0/0
479	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
480	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
481	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	29.60	04/2009 -	07/2013	51(O)	0/0
482	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	39.26	11/2008 -	07/2013	56(O)	0/0
483	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00 -	593.00	63.65	07/2013 -	07/2013	0(O)	0/0
484	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	-	08/2013 -	08/2013	0(O)	0/0
485	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	1,655.00	0.18	09/2013 -	09/2013	0(O)	0/0
486	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	0.99	09/2013 -	09/2013	0(O)	0/0
487	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	10.04	11/2013 -	11/2013	0(O)	0/0
488	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	40.71	11/2008 -	12/2013	61(O)	0/0
489	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	212.00	38.61	09/2007 -	12/2013	75(O)	0/0
490	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	196.00	27.77	07/2009 -	12/2013	53(O)	0/0
491	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	-	08/2014 -	08/2014	0(O)	0/0
492	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	299.92	10/2014 -	10/2014	0(O)	0/0
Shipping & Ports									
493	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 -	298.17	293.57	04/2009 -	02/2011	22(O)	0/0
494	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	03/2011	7(O)	0/0
495	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	04/2011	8(O)	0/0
496	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 253.36	253.36	-	12/2007 07/2009	06/2011	23(R3)	0/0
497	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	272.50	2,190.00	12/2010 -	06/2011	6(O)	0/0
498	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
499	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	241.50	48.10	09/2011 -	09/2011	0(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
500	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 -	165.00	117.23	12/2005 01/2008	10/2011	45(R3)	0/0
501	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
502	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
503	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	320.74	03/2012 -	03/2012	0(O)	0/0
504	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	03/2012	72(O)	0/0
505	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
506	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
507	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	55.41	12/2011 05/2012	05/2012	0(R3)	0/0
508	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	-	12/2010 09/2012	09/2012	0(R3)	0/0
509	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	221.91	09/2012 -	09/2012	0(O)	0/0
510	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
511	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	62.76	12/2012 -	12/2012	0(O)	0/0
512	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
513	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	-	03/2011 -	03/2013	24(O)	0/0
514	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
515	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
516	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O)	0/0
517	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.92	10/2008 -	-	-	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
518	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.02	10/2008 -	-	-	0/0
<u>Telecommunications</u>									
519	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	242.48	09/2009 -	02/2010	5(O)	0/0
520	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	-	12/2005 -	10/2010	58(O)	0/0
521	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
522	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	10/2010	7(O)	0/0
523	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	11/2010	8(O)	0/0
524	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86 234.24	353.00	-	02/2008 -	12/2010	34(O)	0/0
525	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	12/2010	21(O)	0/0
526	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	12/2010	9(O)	0/0
527	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	12/2010	9(O)	0/0
528	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	12/2010	9(O)	0/0
529	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	12/2010	9(O)	0/0
530	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	-	06/2009 -	01/2011	19(O)	0/0
531	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	192.48	110.99	03/2009 -	02/2011	23(O)	0/0
532	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	194.39	12/2008 -	02/2011	26(O)	0/0
533	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	377.54	308.13	03/2009 -	02/2011	23(O)	0/0
534	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	75.31	06/2009 -	02/2011	20(O)	0/0
535	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	02/2011	25(O)	0/0
536	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53 -	625.53	-	02/2010 -	02/2011	12(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
537	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	366.00	225.42	10/2008	02/2011	28(O)	0/0
538	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,312.52	792.83	- 03/2011	02/2011	-1(R3)	0/1
539	GSM equipment of 1500000Lines (2G) 264700lines 3(G - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	02/2011	13(O)	0/0
540	GSM equipment of 1900000Lines (2G) 335500lines 3(G - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	675.35	01/2010	02/2011	13(O)	0/0
541	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	113.45	01/2010	02/2011	13(O)	0/0
542	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	494.00	12/2008	03/2011	27(O)	0/0
543	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
544	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	106.09	09/2009	03/2011	18(O)	0/0
545	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
546	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	03/2011	6(O)	0/0
547	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	398.08	02/2009	03/2011	25(O)	0/0
548	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	352.89	08/2009	03/2011	19(O)	0/0
549	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	267.40	11/2010	03/2011	4(O)	0/0
550	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	395.08	10/2009	03/2011	17(O)	0/0
551	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	-	10/2010	04/2011	6(O)	0/0
552	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007	08/2011	54(O)	0/0
553	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
554	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0

WITOUT MILESTONES

(Jun,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
555	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
556	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	350.00	-	- -	-	-	0/0
557	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
558	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0
559	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	-	-	0/0
<u>Urban Development</u>									
560	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	181.30	-	04/2009 -	01/2011	21(O)	0/0
<u>Water Resources</u>									
563	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
