

**333rd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
July 2013**



DMRC - DELHI MRTS PHASE-III



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-29
Trend and Graphical Analysis of Projects	30-42
Sector wise analysis of projects	43-43
List of All Ongoing Projects	44-72
Sector wise Graph	73-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-104
List of On schedule Projects Original Schedule	105-112
List of Delayed Projects w.r.t Original Schedule	113-125
List of Projects Having cost overrun w.r.t original	126-136
List of Projects Having cost and time overrun w.r.t original	137-141
List of Projects without Milestones	142-162
List of Projects Ahead of Schedule w.r.t Latest Schedule	163-163
List of On schedule Projects w.r.t. Latest Schedule	164-172
List of Delayed Projects w.r.t Latest Schedule	173-185

कार्यकारी सारांश

जुलाई, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 694 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जुलाई, 2013 के दौरान 3 परियोजनाओं (विद्युत क्षेत्र की 2 तथा पेट्रोलियम क्षेत्र की 1) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 694 परियोजनाओं में से 279 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 48 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 48 परियोजनाओं में से, 19 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। परमाणु ऊर्जा, नागर विमानन, कोयला, रेलवे, पोत परिवहन तथा पत्तन, इस्पात, विद्युत, सड़क परिवहन एवं राजमार्ग तथा पेट्रोलियम क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 31 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	240	33	2	1
2.	सड़क परिवहन एवं राजमार्ग	151	91	9	1
3.	विद्युत	98	50	9	6
4.	पेट्रोलियम	82	51	19	8
5.	कोयला	55	28	1	0
6.	पोत परिवहन एवं पत्तन	19	2	2	1
7.	इस्पात	18	12	4	1
8.	दूरसंचार	13	5	0	0
9.	नागर विमानन	8	2	1	0
10.	परमाणु ऊर्जा	4	4	1	1
11.	शहरी विकास	4	1	0	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		694	279	48	19

3. 694 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ` 8,83,001.10 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ` 10,50,646.51 करोड़ रुपए होने की संभावना है जो ` 1,67,645.41 करोड़ (मूल लागत का 19.00%) की समग्र लागत वृद्धि को दर्शाता है। जुलाई, 2013 तक इन परियोजनाओं पर किया गया व्यय ` 4,90,011.19 करोड़ है जो परियोजनाओं की अनुमानित लागत का 46.60% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.07.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (` करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (31.07.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
3	सुबानश्री लोअर एचईपी (एनपीसीआईएल)	विद्युत	09/2003	6285.33	10667.00	4381.67
4	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00
5	बोगीबिल एंड लिंक लाईन पर ब्रह्मपुत्र पुल एनईएफआर	रेलवे	09/1997	1000.00	4996.65	3996.65

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 694 परियोजनाओं में से, 4 परियोजनाएं समय से पहले चल रही हैं, 163 समय पर तथा 279 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 290 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 24 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 224 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 279 विलंबित परियोजनाओं में से, 67 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 77 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 75 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 60 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.07.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
2	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएलए(एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	09/2013	138

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. समय एवं लागत वृद्धि के संबंध में गंभीर रूप से प्रभावित इन परियोजनाओं की समीक्षा में, रेल मंत्रालय ने सूचित किया है कि रेलवे परियोजनाओं हेतु परिच्यय बहुत ही कम है और वर्तमान स्फीति को निष्क्रिय करने हेतु अपर्याप्त है । इसके कारण रेलवे परियोजनाओं को पूरा करने से संबंधित लक्ष्यों को निश्चित करने की स्थिति में नहीं है । निधि की कमी ने रेलवे को वर्ष 2010-11 तथा 2011-12 में क्रमशः 2315 किमी तथा 2337 किमी की उपलब्धि के मुकाबले वर्ष 2013-14 हेतु लक्ष्य को कम करके 525 किमी करने को विवश किया है ।

7. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, उपस्कर संस्थापना में विलंब, संरचना डिजाइन में, भू वैज्ञानिक गतिविधियां, प्रौद्योगिकी का हस्तांतरण, कार्य-क्षेत्र में बदलाव, राज्य सरकार द्वारा जनोपयोगी सेवाओं को अन्यत्र ले जाने में विलंब, कार्यकारी एजेंसी के स्वामित्व में बदलाव,

स्थान की कमी, वेन्डर द्वारा संग्रहण, कार्यों को प्रदान करने में विलंब, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.07.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़)		संचयी व्यय (करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

9. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं। पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.07.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.07.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- I. कोयला क्षेत्र में 55 परियोजनाओं में से 28 परियोजनाएं विलंबित हैं । माह के दौरान, 'काकतिया लोंगवाल, एससीसीएल' परियोजना के संबंध में प्रौद्योगिकी के हस्तांतरण के कारण 12 माह के अतिरिक्त विलंब की सूचना दी गई है ।
- II. परमाणु ऊर्जा क्षेत्र में सभी 4 परियोजनाएं विलंबित हैं । माह के दौरान, "कुंदनकुलम एपीपी", एनपीसीआईएल' (मेगा परियोजना) के संबंध में उपस्करों की आपूर्ति तथा संस्थापन में विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- III. नागर विमान क्षेत्र में 8 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं । माह के दौरान, 'नए अंतर्राष्ट्रीय टर्मिनल भवन का निर्माण, एएआई' के संबंध में संरचना संबंधी डिजाइन में परिवर्तन तथा भू-वैज्ञानिक गतिविधियों के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

IV. पोत परिवहन तथा पत्तन क्षेत्र में 19 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं। माह के दौरान, दो परियोजनाओं के संबंध में 1 तथा 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से एक परियोजना मेगा परियोजना है। 'पुथु में एलएनजी रीगैसीफिकेशन टर्मिनल की स्थापना, भारतीय पत्तन न्यास' तथा 'एनोर मनाली एक्सप्रेस वे (एसपीवी का निर्माण), भारतीय पत्तन न्यास' परियोजनाओं के संबंध में 1 तथा 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारी द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

V. रेलवे क्षेत्र में 240 परियोजनाओं में से 33 परियोजनाएं विलंबित हैं। माह के दौरान, 2 परियोजनाओं के संबंध में 2-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'बारानगर से बैरकपुर तथा दक्षिणेश्वर तक मेट्रो रेल के निर्माण के लिए नए कार्य, आरवीएनएल' परियोजना में राज्य सरकार द्वारा जनोपयोगी सेवाओं के अंतरण में विलम्ब के कारण 24 माह के अतिरिक्त विलंब की सूचना दी गई है; तथा 'लांझीगढ़-जूनागढ़ न्यू लाइन, ईसीओर' परियोजना में 2 माह के अतिरिक्त विलंब की सूचना दी गई है (तथापि, इस परियोजना में विलंब के लिए परियोजना प्राधिकारी द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

VI. इस्पात क्षेत्र में 18 परियोजनाओं में से 12 परियोजनाएं विलंबित हैं। माह के दौरान 4 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 1 मेगा परियोजना है। 'तरल इस्पात का 3 एमटीपीवाई से 6.3 एमटीपीवाई तक आरआईएनएल/वीएसपी का विस्तार, आरआईएनएल'; '67.5 मेगावाट टीजी-5 आक्जीलरी सिस्टम इमरजेंसी पावर रिकवायरमेंट, आरआईएनएल' तथा '1X45 एमवीए सबमर्ज्ड आर्क फर्नेस की संस्थापना, सेल' परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना दी गई है; तथा बोलानी आयरन में उत्पादन क्षमता का विस्तार, सेल' परियोजना के संबंध में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

VII. विद्युत क्षेत्र में, 98 परियोजनाओं में से 50 परियोजनाएं विलंबित हैं। माह के दौरान, 9 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 6 मेगा परियोजनाएं हैं। 'भारत तथा बंगलादेश की विद्युत ग्रिडों के बीच इंटरकनेक्शन, पीजीसीआईएल', दक्षिण क्षेत्र का प्रणाली सुदृढीकरण-XI, पीजीसीआईएल तथा 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XX, पीजीसीआईएल' परियोजनाओं के संबंध में आरओडब्ल्यू मामलों के कारण 1, 2 तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'टेहरी पंप्ड स्टोरेज प्लांट (1000 मेवा.), टीएचडीसीएल' तथा 'मुंद्रा अल्ट्रा मेगा पावर प्रोजेक्ट से संबद्ध पारेषण प्रणाली, पीजीसीआईएल' परियोजना के संबंध में एकीकृत तथा पिसी हुई बालू हेतु आसेना में खनन कार्यकलापों की अनुमति न मिलने के कारण तथा 1200 केवी टावर संस्थापन में कठिनाई के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; '765 केवी उत्तरी ग्रिड भाग-III के केन्द्रीय

भाग हेतु प्रणाली, पीजीसीआईएल', 'पल्लातना जीबीपीपी तथा बीपीटी से संबद्ध पारेषण प्रणाली, पीजीसीआईएल' तथा 'बालूर से संबद्ध अनुपूरक पारेषण, पीजीसीआईएल' परियोजना के संबंध में कार्यान्वयन एजेंसी के स्वामित्व में परिवर्तन, वन संबंधी अनुमति में विलंब तथा भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'राजगढ़ में पूलिंग स्टेशनों की स्थापना, पीजीसीआईएल' परियोजना के संबंध में भारी वर्षा के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

VII. पट्रोलियम क्षेत्र में 82 परियोजनाओं में से 51 परियोजनाएं विलंबित हैं। माह के दौरान, 19 परियोजनाओं के संबंध में 1-31 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 8 मेगा परियोजनाएं हैं। 'फ्लूडाइज्ड कैटालाइटिक क्रैकिंग यूनिट (एफसीसीयू) रिवैम्प, आईओसीएल' परियोजना के संबंध में उपस्करों की आपूर्ति में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, "नाहरकाटिया-बरौन के कच्चा तेल पम्प स्टेशनों का उन्नयन, ओआईएल" परियोजना के संबंध में वन संबंधी स्वीकृति में विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'उरान में अतिरिक्त गैस संसाधन यूनिट, ओएनजीसी' के संबंध में निर्माण तथा स्थान की कमी के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'बीपीसीआर/एमपीसीआर से उरान एलपीजी प्लान तक एलपीजी के अंतरण हेतु पाइपलाइन, बीपीसीएल' परियोजना के संबंध में वेन्डर द्वारा संग्रहण के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'कलस्टर-7 फील्ड का विकास, ओएनजीसी' परियोजना के संबंध में कार्य प्रदान करने में विलंब के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'मेहसाणा पुनर्विकास, ओएनजीसी' परियोजना के संबंध में कार्य के क्षेत्र में परिवर्तन के कारण 23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'पानीपत में बूटाडीन एक्सट्रक्शन यूनिट, आईओसीआई' तथा 'बी-173ए फील्ड का आईओआर, ओएनजीसी' परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'पोलीप्रोपाइलीन यूनिट, मंगलौर रिफाइनरी' परियोजना के संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'एमपीआरएल फेस-III का विस्तार, मंगलौर रिफाइनरी' तथा '6 ईटीपी का निर्माण, ओएनजीसी' परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'डब्ल्यूओ-16 कलस्टर फील्ड का विकास, ओएनजीसी' एवं 'सिंगल प्वाइंट मूरिंग फैसिलिटी (एसएमपी) परियोजना, मंगलौर रिफाइनरी' के संबंध में क्रमशः 4 तथा 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'आरआईजी सागर सम्राट को मोबाइल ऑफशोर में परिवर्तन, ओएनजीसी' परियोजना के संबंध में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; '12 ऑफशोर सप्लाई वैसेल (ओएसवी) का निर्माण, ओएनजीसी' तथा एक ईटीपी तथा तीन ईटीपीएस सह जल का निर्माण, ओएनजीसी' परियोजनाओं के संबंध में प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'अहमदाबाद पुनर्विकास, ओएनजीसी' तथा अंकलेश्वर पुनर्विकास, ओएनजीसी' परियोजनाओं के संबंध में प्रत्येक में 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'एक बहुउद्देशीय सपोर्ट वैसेल का निर्माण, ओएनजीसी' परियोजना के संबंध में 31 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

IX सड़क परिवहन तथा राजमार्ग क्षेत्र में 151 परियोजनाओं में से 91 विलंबित हैं । माह के दौरान, 9 परियोजनाओं के संबंध में 2-9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 1 मेगा परियोजना है । 'तंजोर-त्रिची, एनएच-67, एनएचएआई' एवं 'देवीहल्ली-हसन एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'नलबाड़ी से बिजनी (एएस-8), एनएचएआई', 'हुंगुद-सूरतकल तथा मंगलौर-कर्नाटक/केरल सीमा, एनएचएआई' तथा 'देवली-कोटा, एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'देवली-कोटा, एनएचएआई' तथा 'हजारीबाग-रांची, एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'छपरा-हाजीपुर को 4-लेन बनाना, एनएचएआई' तथा 'नागपुर-कौंधनानी, एनएच-6, एनएचएआई' परियोजनाओं के संबंध में क्रमशः 5 और 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना कार्यान्वयन एजेंसी ने इन परियोजनाओं में विलंब के लिए किसी विशेष कारण का कोई उल्लेख नहीं किया है । तथापि, इन परियोजनाओं में विलंब के सामान्य कारण-भूमि अधिग्रहण, वन तथा पर्यावरण संबंधी अनुमति में विलंब, जनोपयोगी सुविधाओं के अंतरण में विलंब, ठेकेदारों का घटिया कार्य निष्पादन, आदि हैं ।

11. दिनांक 31.07.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ` 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
12. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for July 2013 contains information on the status of the 694 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During July 2013, 3 projects (2 projects in Power and 1 project in Petroleum Sectors) have reported completion.

2. During the reference month, out of 694 projects, 279 projects are delayed with respect to latest schedule and 48 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 48 projects, 19 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 31 months in respect of projects relating to Atomic Energy, Civil Aviation, Coal, Railways, Shipping & Ports, Steel, Power, Road Transport & Highways and Petroleum Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Railways	240	33	2	1
2.	Road Transport & Highways	151	91	9	1
3.	Power	98	50	9	6
4.	Petroleum	82	51	19	8
5.	Coal	55	28	1	0
6.	Shipping & Ports	19	2	2	1
7.	Steel	18	12	4	1
8.	Telecommunications	13	5	0	0
9.	Civil Aviation	8	2	1	0
10.	Atomic Energy	4	4	1	1
11.	Urban Development	4	1	0	0
12.	Petrochemicals	1	0	0	0
13.	Water Resources	1	0	0	0
Total		694	279	48	19

3. Total original cost of implementation of the 694 projects was about ₹ 8,83,001.10 crore and their anticipated completion cost is likely to be ₹ 10,50,646.51 crore, which reflects overall cost overruns of ₹ 1,67,645.41 crore (19.00 % of original cost). The expenditure incurred on these projects till July 2013 is ₹ 4,90,011.19 crore, which is 46.60 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-07 -2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-07-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	11609.00	5214.00
3	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
4	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00
5	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	4996.65	3996.65

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 694 projects, 4 projects are ahead of schedule, 163 are on schedule and 279 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 290 if delay is calculated on the basis of original schedule of completion. Further, 24 projects have been sanctioned without any commissioning schedule/date and for 224 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 279 delayed projects, 67 projects have overall delay in the range of 1 to 12 months, 77 projects have a delay in the range of 13 to 24 months, 75 projects have a delay in the range of 25 to 60 months and 60 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-07-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2015	240
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	141
5	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	09/2013	138

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In a review of its severely affected projects in terms of time & cost overruns, Ministry of Railways has informed that outlay for Railway projects is very low of throw forward and is insufficient even to neutralize the prevailing inflation. Due to this, Railways is not in the position to fix the targets for completion of the projects. Paucity of funds has forced Railways to scale down the targets for 2013-14 to 1525 Km against the achievement of 2315 Km and 2337 Km in 2010-11 and 2011-12 respectively.

7. The brief reasons for time overruns as reported by various other project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipment, delay in equipment erection, change in structural design, geological surprises, transfer of technology, change in scope of work, delay in shifting of utility by State Government, change of ownership of executing agency, space constraint, mobilization by vendor, delay in award of works ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-07-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ crore)		EXPENDITURE CUMMULATIVE (₹ crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-07-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.07.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

10. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Coal Sector**, out of 55 projects, 28 projects are delayed. During the month the project 'Kakatiya Longwall, SCCL' has reported additional delay of 12 months due to transfer of technology.

ii) In the **Atomic Energy Sector**, all 4 projects are delayed. During the month the project 'Kudankulam APP, NPCIL' (Mega Project) has reported additional delay of 3 months due to delay in supply and erection of equipments.

iii) In the **Civil Aviation Sector**, out of 8 projects, 2 projects are delayed. During the month the project 'Construction of New International Terminal Building, AAI' has reported additional delay of 3 months due to change in structural design and geological surprises.

iv) In the **Shipping & Ports Sector**, out of 19 projects, 2 projects are delayed. During the month 2 projects have reported additional delays of 1 and 6 months, out of which 1 is Mega project. The projects 'Setting up of LNG Regasification Terminal at Puthu, Port Trust of India' and 'Ennore Manali Express way (formation of SPV), Port Trust of India' have reported additional delay of 1 and 6 months (however, no specific reasons have been reported by the project authority for the delay in these projects).

iv) In the **Railways Sector**, out of 240 projects, 33 projects are delayed. During the month 2 projects have reported additional delays of 2-24 months. The project 'New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar, RVNL' has reported additional delay of 24 months due to delay in shifting of utilities by the State Government; and the project 'Lanjigarh-Junagarh New Line, ECOR' has reported additional delay of 2 months (however, no specific reasons have been reported by the project authority for the delay in this project).

v) In the **Steel Sector**, out of 18 projects, 12 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-12 months, out of which 1 is Mega project. The projects 'Expansion of RINL/VSP from 3 MTPY-6.3 MTPY of liquid Steel, RINL', '67.5 MW TG-5 Auxiliary System Emergency Power Requirement, RINL' and 'Installation of 1x45 MVA Submerged Arc Furnace, SAIL' have reported additional delays of 1 month each; and 'Enhancement of Production Capacity at Bolani Iron, SAIL' has reported additional delay of 12 months (however, no specific reasons have been reported by the project authorities for the delay in these projects).

vi) In the **Power Sector**, out of 98 projects, 50 projects are delayed. During the month 9 projects have reported additional delays in the range of 1-12 months, out of which 6 are Mega project. The projects 'Interconnection Between Electrical Grids of India and Bangladesh, PGCIL', 'System Strengthening -XII of Southern Region, PGCIL' and 'Northern Region System Strengthening Scheme- XXI, PGCIL' have reported additional delay of 1, 2 and 12 months respectively due to ROW issues; the projects 'Tehri Pumped Storage Plant (1000MW), THDCL' and 'Transmission System Associated with Mundra Ultra Mega Power Project, PGCIL' have reported additional delays of 3 months each due to absence of permission for mining activity at Asena for aggregate & crushed sand and difficulty in 1200 kv tower erection; the projects '765KV System for Central Part of Northern Grid Part-III, PGCIL', 'Transmission System associated with Pallatana GBPP & BPT, PGCIL' and 'Supplementary Transmission Associated with Vaallur, PGCIL' have reported additional delays of 3 months each due to change of ownership of executing agency, delay in forest clearance and delay in land acquisition; and the project 'Establishment of Pooling Stations at Rajgarh, PGCIL' has reported additional delay of 4 months due to heavy rain.

vii) In the **Petroleum Sector**, out of 82 projects, 51 projects are delayed. During the month 19 projects have reported additional delays in the range of 1-31 months, out of which 8 are Mega projects. The project 'Fluidized Catalytic Cracking Unit (FCCU) Revamp, IOCL' has reported additional delay of 1 month due to delay in supply of equipments; the project 'Upgradation of Crude Oil Pump Stations of Naharkatiya-Baraun, OIL' has reported additional delay of 3 months due to delay in forest clearance; the project 'Additional Gas Processing Units at Uran, ONGC' has reported additional delay of 4 months due to fabrication & space constraint; the project 'Pipeline for Transfer of LPG from BPCR/HPCR to Uran LPG Plan, BPCL' has reported additional delay of 6 months due to mobilization by vendor; the project 'Development of Cluster-7 Fields, ONGC' has reported additional delay of 7 months due to delay in award of works; the project 'Mehesana Redevelopment, ONGC' has reported additional delay of 23 months due to change in scope of works; the projects 'Butadiene Extraction Unit (BDEU) at Panipat, IOCL' and 'IOR of B-173A Field, ONGC' has reported additional delay of 1 month each; the project 'Polypropylene unit, Mangalore Refinery' has reported additional delay of 2 months; the projects 'MRPL Phase-III Expansion, Mangalore Refinery' and 'Construction of 6 ETPs, ONGC' have reported additional delays of 3 months each; the projects 'Development of WO-16 Cluster Fields, ONGC' and 'Single Point Mooring Facility (SMP) Project, Mangalore Refinery' have reported additional delays of 4 and 5 months respectively; the project 'Conversion of RIG Sagar Samrat to Mobile Offshore, ONGC'

has reported additional delay of 6 months; the projects 'Construction of 12 Offshore Supply Vessels (OSV), ONGC' and 'Construction of One ETP and Three ETPS cum Water, ONGC' have reported additional delays of 12 months each; the projects 'Ahmedabad Redevelopment, ONGC' and 'Ankleswar Redevelopment, ONGC' have reported additional delays of 24 months each; and the project 'Construction of One Multipurpose Support Vessel, ONGC' has reported additional delay of 31 months (however, no specific reasons have been reported by the project authorities for the delay in these projects).

viii) In the **Road Transport & Highways Sector**, out of 151 projects, 91 are delayed. During the month 9 projects have reported additional delays in the range of 2-9 months, out of which 1 is Mega project. The projects 'Thanjaur-Trichy, NH-67, NHAI' and 'Devihalli-Hassan, NHAI' have reported additional delay of 2 month each; the projects 'Nalbari to Bijni (AS-8), NHAI', 'Hungund-Surathkal and Mangalore-Knt/Kerala Border, NHAI' and 'Deoli-Kota, NHAI' have reported additional delay of 3 months each; the projects 'Deoli-Kota, NHAI' and 'Hazaribagh-Ranchi, NHAI' have reported additional delay of 4 months each; and the projects '4-Lanning of Chapra-Hajipur, NHAI' and 'Nagpur-Kondhali, NH-6, NHAI' have reported additional delay of 5 and 9 months respectively. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, delay in shifting of utility, poor performance of contractor, etc.


11. The status as on 31.07.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Railways	240	2
2	Road Transport & Highways	151	9
3	Power	98	9
4	Petroleum	82	19
5	Coal	55	1
6	Shipping & Ports	19	2
7	Steel	18	4
8	Telecommunications	13	0
9	Civil Aviation	8	1
10	Atomic Energy	4	1
11	Urban Development	4	0
12	Petrochemicals	1	0
13	Water Resources	1	0
	Total	694	48

Sectoral break up of on-going infrastructure projects.

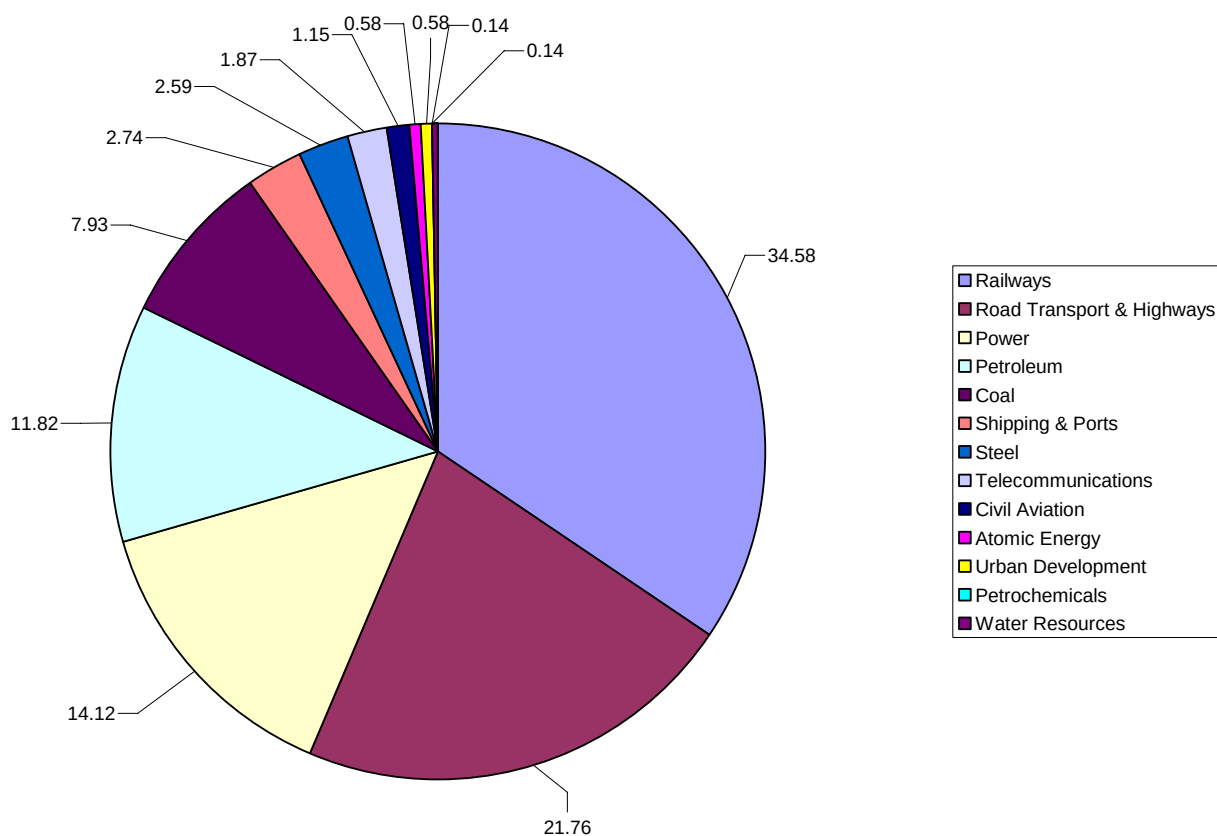

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>Power</u>			
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>Railways</u>			
2	REINGUNTA-GUNTAKAL(RE)(RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL)(RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>Fertilisers</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT(NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>Power</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>Road Transport & Highways</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56
	June,2013			
	<u>Railways</u>			
8	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000027]	240.00	03/2009	334.59
9	PANSPURA-KHARAGPUR 3D LINE(RAIL VIKAS NIGAM LTD.) - [N22000076]	252.50	02/2010	249.36
	July,2013			
	<u>Petroleum</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2013-2014

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
10	North Tapti Gas Field Development(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000096]	589.70	03/2011	912.53
	<u>Power</u>			
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100222]	768.92	03/2007	1467.53
12	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000007]	621.26	02/2011	731.93


Summary of projects in the Flash Report for the month of July, 2013

Project Implementation - Current Status:

Number of Projects in Previous Month	573
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	125
Number of Projects in Current Month	694


Brief Analysis

Project Status with respect to Original Schedule: Out of 694 projects, 3 projects are ahead of schedule, 147 projects are on schedule and 290 projects are delayed. Of the balance, 230 projects do not have fixed dates of commissioning while 24 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

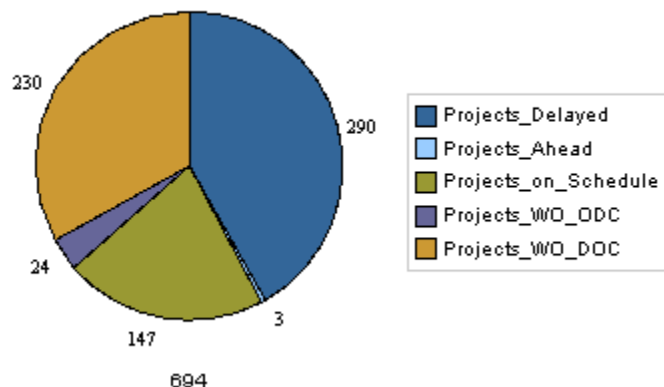

Investment Scenario

The Total Original cost of implementation of 694 projects when sanctioned, was of the order of Rs. 883001.1 crore but this was subsequently revised to Rs. 1050646.51 crore implying a cost overrun of 19%. The expenditure incurred on these projects till July, 2013 is Rs. 490011.19 crore, which is 46.6% of the revised cost of the projects.

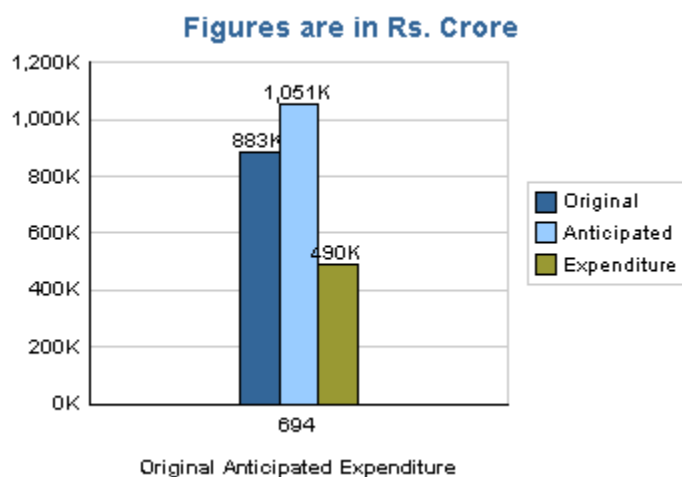

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	573
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects elevated to the status of Major Project during the current months	1
No of Projects added in Current Month	125@
No of Projects in Current Month	694

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	290	3	153	24	224	694	41.79
Latest Approved (Date)	279	4	163	24	224	694	40.20

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	542	751,430.77	797,851.62	343,874.13	43.10	46,420.85	6.20
Latest Approved (RCE)	152	195,760.21	252,794.89	146,137.06	57.80	57,034.68	29.10
Total (RCE)	694	947,190.98	1,050,646.51	490,011.19	46.64	103455.53	10.92
Original Cost of All Projects							
Original Cost	694	883,001.10	1,050,646.51	490,011.19	46.60	167,645.41	19.00

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	290	483,150.35	586,626.03	360,160.86	61.40	103,475.68	21.40
Latest Approved (RCE)	279	502,413.42	563,800.17	350,209.28	62.10	61,386.75	12.20

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	48	84,141.03	98,019.18	68,851.53	70.20	13,878.15	16.50

@ All these projects came on the monitor of this Ministry during this month; details of these projects are at page No 23

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	8	6,035.5	6,625.0	9.8	2	3,750.5	4,340.0	15.7
3	Coal	55	38,127.1	41,212.5	8.1	7	8,579.5	12,262.6	42.9
4	Steel	18	65,625.2	71,782.4	9.4	6	24,028.9	30,216.1	25.7
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	Petroleum	82	183,464.2	197,793.0	7.8	24	58,175.9	78,668.0	35.2
7	Power	98	251,918.9	270,310.2	7.3	19	49,763.6	68,154.9	37.0
8	Railways	240	121,907.6	227,295.5	86.4	136	60,009.8	165,508.1	175.8
9	Road Transport & Highways	151	103,915.6	105,854.2	1.9	11	3,324.3	5,445.2	63.8
10	Shipping & Ports	19	15,617.1	17,902.4	14.6	9	8,629.0	11,218.5	30.0
11	Telecommunications	13	5,699.2	5,520.2	-3.1	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		694	883,001.1	1,050,646.5	19.0	223	246,831.1	422,130.9	71.0

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Andhra Pradesh	38	31,729.8	39,769.6	25.3	15	13,556.4	22,463.1	65.7
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	4	9,512.2	17,330.3	82.2
3	Assam	41	24,155.5	38,430.2	59.1	14	10,762.0	25,130.7	133.5
4	Bihar	46	32,579.0	41,019.1	25.9	17	13,347.2	21,803.6	63.4
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	34	38,828.1	40,180.0	3.5	7	3,094.5	4,716.2	52.4
7	Haryana	8	4,054.4	5,737.0	41.5	2	1,298.8	2,981.4	129.5
8	Himachal Pradesh	5	13,355.6	17,318.8	29.7	4	11,308.5	15,271.8	35.0
9	Jammu and Kashmir	9	14,305.7	33,912.6	137.1	5	7,245.2	26,852.1	270.6
10	Karnataka	27	47,076.4	56,530.7	20.1	11	9,996.8	19,944.1	99.5
11	Kerala	10	21,010.6	22,804.1	8.5	3	4,295.7	6,089.2	41.8
12	Madhya pradesh	22	31,749.1	32,157.3	1.3	4	2,714.8	3,542.4	30.5
13	Maharashtra	55	95,394.7	108,795.4	14.0	17	33,052.5	48,919.9	48.0
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	512.1
15	Meghalaya	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,298.0	115.1	1	619.3	2,384.3	285.0
17	Nagaland	2	5,124.0	6,720.8	31.2	1	850.0	2,446.8	187.9
18	Odisha	31	56,321.5	63,614.3	12.9	13	32,821.5	40,114.2	22.2
19	Punjab	4	1,611.4	2,553.2	58.4	2	532.4	1,474.2	176.9
20	Rajasthan	25	25,256.6	25,208.6	-0.2	6	1,989.2	2,438.4	22.6
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	41	52,194.8	67,422.7	29.2	21	31,000.3	46,228.1	49.1
23	Tripura	5	2,669.4	4,021.1	50.6	3	2,129.4	3,515.4	65.1
24	Uttar Pradesh	27	21,281.9	25,861.1	21.5	10	3,831.0	8,458.5	120.8
25	West Bengal	33	48,249.3	59,771.3	23.9	17	24,963.9	36,486.0	46.2
26	Chandigarh	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
28	Chhatisgarh	24	58,278.3	59,362.9	1.9	5	1,396.8	2,481.4	77.6
29	Jharkhand	26	15,873.2	20,155.8	27.0	8	2,534.9	6,989.3	175.7
30	Uttarakhand	5	7,624.2	8,887.3	16.6	2	2,640.7	3,903.8	47.8
31	Multi State	158	177,008.8	197,813.4	11.8	29	19,270.0	42,331.2	119.7
Total		694	883,001.1	1,050,646.5	19.0	223	246,831.1	422,130.9	71.0

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 66
2	Civil Aviation	8	6,035.5	6,625.0	9.8	2	645.1	645.1	16 - 47
3	Coal	55	38,127.1	41,212.5	8.1	28	24,633.8	28,090.6	12 - 72
4	Steel	18	65,625.2	71,782.4	9.4	14	64,438.3	70,505.9	6 - 46
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
6	Petroleum	82	183,464.2	197,793.0	7.8	54	131,903.3	147,024.4	1 - 94
7	Power	98	251,918.9	270,310.2	7.3	50	122,216.6	139,063.3	1 - 102
8	Railways	240	121,907.6	227,295.5	86.4	35	27,508.4	76,761.6	3 - 240
9	Road Transport & Highways	151	103,915.6	105,854.2	1.9	91	54,470.8	56,366.1	2 - 108
10	Shipping & Ports	19	15,617.1	17,902.4	14.6	5	6,002.6	7,254.7	5 - 93
11	Telecommunications	13	5,699.2	5,520.2	-3.1	5	2,934.9	2,774.5	28 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		694	883,001.1	1,050,646.5	19.0	290	483,150.4	586,626.0	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Andhra Pradesh	38	31,729.8	39,769.6	25.3	10	16,303.5	20,388.9	4 - 46
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	3	9,356.2	16,923.9	25 - 87
3	Assam	41	24,155.5	38,430.2	59.1	36	22,277.8	35,723.2	3 - 105
4	Bihar	46	32,579.0	41,019.1	25.9	12	20,814.3	25,494.6	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	16 - 16
6	Gujarat	34	38,828.1	40,180.0	3.5	10	24,201.6	24,223.2	3 - 24
7	Haryana	8	4,054.4	5,737.0	41.5	4	2,216.6	3,396.6	6 - 50
8	Himachal Pradesh	5	13,355.6	17,318.8	29.7	5	13,355.6	17,318.8	26 - 102
9	Jammu and Kashmir	9	14,305.7	33,912.6	137.1	7	13,038.7	32,618.8	10 - 201
10	Karnataka	27	47,076.4	56,530.7	20.1	11	19,058.4	19,061.1	6 - 108
11	Kerala	10	21,010.6	22,804.1	8.5	5	19,581.0	20,231.0	5 - 58
12	Madhya pradesh	22	31,749.1	32,157.3	1.3	9	4,494.1	4,620.8	8 - 69
13	Maharashtra	55	95,394.7	108,795.4	14.0	25	44,363.0	51,848.1	5 - 129
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	72 - 72
15	Meghalaya	3	4,845.0	4,845.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,298.0	115.1	2	1,533.0	3,298.0	7 - 35
17	Nagaland	2	5,124.0	6,720.8	31.2	1	850.0	2,446.8	24 - 24
18	Odisha	31	56,321.5	63,614.3	12.9	15	50,676.9	54,002.3	3 - 138
19	Punjab	4	1,611.4	2,553.2	58.4	2	989.0	1,064.0	13 - 64
20	Rajasthan	25	25,256.6	25,208.6	-0.2	8	16,423.9	15,977.6	3 - 59
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 47
22	Tamil Nadu	41	52,194.8	67,422.7	29.2	15	34,552.5	43,919.7	6 - 93
23	Tripura	5	2,669.4	4,021.1	50.6	3	1,996.4	3,145.7	19 - 96
24	Uttar Pradesh	27	21,281.9	25,861.1	21.5	14	13,392.6	16,137.5	9 - 84
25	West Bengal	33	48,249.3	59,771.3	23.9	11	23,968.7	29,620.5	3 - 141
26	Chandigarh	1	452.0	452.0	0.0	0	0.0	0.0	-
27	Delhi	4	38,214.4	38,194.8	-0.1	1	2,494.0	2,494.0	8 - 8
28	Chhatisgarh	24	58,278.3	59,362.9	1.9	10	25,204.4	25,515.7	4 - 59
29	Jharkhand	26	15,873.2	20,155.8	27.0	10	9,422.6	9,529.2	9 - 60
30	Uttarakhand	5	7,624.2	8,887.3	16.6	4	6,097.2	7,360.3	5 - 54
31	Multi State	158	177,008.8	197,813.4	11.8	53	83,776.3	91,786.7	1 - 240
Total		694	883,001.1	1,050,646.5	19.0	290	483,150.4	586,626.0	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 66
2	Civil Aviation	8	6,035.5	6,625.0	9.8	2	645.1	645.1	16 - 47
3	Coal	55	38,127.1	41,212.5	8.1	28	24,633.8	28,090.6	12 - 72
4	Steel	18	65,625.2	71,782.4	9.4	12	62,967.8	69,035.3	8 - 46
5	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	Petroleum	82	183,464.2	197,793.0	7.8	51	127,927.1	137,961.3	1 - 94
7	Power	98	251,918.9	270,310.2	7.3	50	122,216.6	139,063.3	1 - 102
8	Railways	240	121,907.6	227,295.5	86.4	33	26,993.4	75,034.0	3 - 240
9	Road Transport & Highways	151	103,915.6	105,854.2	1.9	91	54,470.8	56,366.1	2 - 108
10	Shipping & Ports	19	15,617.1	17,902.4	14.6	2	4,728.0	5,610.0	19 - 39
11	Telecommunications	13	5,699.2	5,520.2	-3.1	5	2,934.9	2,774.5	28 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		694	883,001.1	1,050,646.5	19.0	279	470,453.4	563,800.2	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	44,541.0	46,726.0	4.9	1	3,492.0	5,677.0	62.6
2	Civil Aviation	8	6,242.5	6,625.0	6.1	1	1,942.5	2,325.0	19.7
3	Coal	55	40,729.4	41,212.5	1.2	5	2,211.1	2,694.1	21.8
4	Steel	18	69,847.4	71,782.4	2.8	1	14,443.0	16,408.0	13.6
5	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
6	Petroleum	82	197,694.0	197,793.0	0.1	9	32,985.2	37,291.3	13.1
7	Power	98	255,978.6	270,310.2	5.6	14	42,918.2	57,249.9	33.4
8	Railways	240	151,121.9	227,295.5	50.4	109	64,778.7	141,022.7	117.7
9	Road Transport & Highways	151	104,082.1	105,854.2	1.7	11	3,324.3	5,445.2	63.8
10	Shipping & Ports	19	17,488.0	17,902.4	2.4	5	3,157.6	3,783.5	19.8
11	Telecommunications	13	5,699.2	5,520.2	-3.1	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		694	947,191.0	1,050,646.5	10.9	161	177,584.5	286,174.2	61.1

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	8	6,035.46	6,624.95	9.77	1	1,808.00	2,015.00	13- 13
3	Coal	55	38,127.05	41,212.50	8.09	0	0.00	0.00	0- 0
4	Steel	18	65,625.22	71,782.40	9.38	2	8,987.89	12,898.17	24- 46
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	82	183,464.22	197,793.04	7.81	10	20,436.52	34,731.80	20- 94
7	Power	98	251,918.93	270,310.17	7.30	3	2,827.44	5,103.94	0- 79
8	Railways	240	121,907.58	227,295.52	86.45	15	5,839.02	22,335.92	0- 141
9	Road Transport & Highways	151	103,915.59	105,854.21	1.87	0	0.00	0.00	0- 0
10	Shipping & Ports	19	15,617.12	17,902.42	14.63	5	5,400.70	6,860.25	10- 93
11	Telecommunications	13	5,699.24	5,520.22	-3.14	0	0.00	0.00	0- 0
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		694	883001.1	1050646.51	18.99	37	50760.18	92865.08	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 66
2	Civil Aviation	8	6,035.46	6,624.95	9.77	0	0.00	0.00	0- 0
3	Coal	55	38,127.05	41,212.50	8.09	5	7,938.86	11,573.95	19- 55
4	Steel	18	65,625.22	71,782.40	9.38	5	23,768.89	29,866.43	11- 46
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	82	183,464.22	197,793.04	7.81	20	54,470.23	74,009.33	2- 94
7	Power	98	251,918.93	270,310.17	7.30	15	41,507.61	58,354.32	10- 102
8	Railways	240	121,907.58	227,295.52	86.45	31	24,179.51	73,437.57	12- 240
9	Road Transport & Highways	151	103,915.59	105,854.21	1.87	9	2,933.01	5,010.57	25- 79
10	Shipping & Ports	19	15,617.12	17,902.42	14.63	3	4,878.00	6,210.00	19- 93
11	Telecommunications	13	5,699.24	5,520.22	-3.14	2	1,065.85	1,089.32	34- 54
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		694	883001.1	1050646.51	18.99	93	182865.57	291418.49	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>Petroleum</u>						
1	North Tapti Gas Field Development	07/2008	589.70	03/2011	973.79	05/2013	912.53
	<u>Power</u>						
2	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE	10/2003	768.92	03/2007	1,628.00	05/2013	1,467.53
3	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	08/2006	621.26	02/2011	913.00	01/2013	731.93

Milestones (Cumulative due & achieved)

Total	3776
Achieved up to month	1344

List of projects added (Jul, 2013)

(All sums of money in crore of rupees)



Project Name		Original			Now anticipated	
		DOA	Cost (Rs. Crores)	DOC	Cost (Rs. Crores)	DOC
Civil Aviation						
1	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI	2/2010	344.28	3/2014	344.28	3/2014
Petroleum						
2	Pipeline Replacement Project, Ahmedabad	9/2011	202.25	7/2016	202.25	7/2016
3	Integrated Development of Bassein Field	12/2012	3513.07	2/2016	3513.07	2/2016
4	Ennore-Trichy-Madurai LPG Pipeline	5/2013	711.00	/	711.00	0/0
5	Surat Paradip Pipeline Project	10/2012	10281.00	/	10281.00	0/0
6	Reconstruction of BPA & BPB Platforms	3/2013	1138.50	4/2015	1138.50	4/2015
Power						
7	Gadarwara Super Thermal Power Project Stage-I	2/2013	11638.55	9/2017	11638.55	9/2017
Railways						
8	Bangurgram-Guriya Patch doubling	4/2012	246.08	/	246.08	0/0
9	Palanpur-Samakhayali (DL)	4/2013	1266.89	/	1266.89	0/0
10	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner & Ratangarh-De	4/2010	739.65	/	695.00	0/0
11	Mavli Jn.-Bari Sadri, MM of Ajmer-Chittsurgarh-Udaipur	4/2013	456.00	/	567.23	0/0
12	Pushkar-Merta	4/2013	323.00	/	323.00	0/0
13	Ajmer-Kota (Nasirabad-Jaundri)	4/2013	822.00	/	822.00	0/0
14	Thiyat Hamira-Sanu	4/2013	236.39	/	236.39	0/0
15	Gwalior-Seopurkala with extension to Kota (GC)	4/2011	1176.09	2/2020	3845.60	2/2020
16	Ratlam-Dungarpur via Banswara (NL)	4/2012	2082.75	/	2082.75	0/0
17	Viramgam-Surendranagar (DL)	4/2010	279.40	/	279.40	4/2014
18	Viramgam-Samakhiali (DL)	4/2011	446.00	/	685.17	0/0
19	Bihta-Aurangabad (NL)	4/2008	326.20	/	326.20	0/0
20	Gaya-Chatra (NL)	4/2008	415.67	/	415.67	0/0
21	Gaya-Daltonganj via Rafiganj (NL)	4/2008	445.25	/	445.25	0/0
22	Nawada-Laxmipur (NL)	4/2008	620.57	/	620.57	0/0
23	Ara-Bhabhua Road (NL)	4/2008	490.80	/	490.80	0/0
24	Manoharpur-Bondamunda 3rd line Doubling	4/2012	258.20	/	258.20	3/2016
25	Dangoaposi-Rajkharswan 3rd line Doubling	4/2010	309.44	12/2015	388.67	12/2015
26	Tamluk-Basulya-Sutahata Doubling	4/2010	146.95	6/2013	171.02	0/0
27	Champajharan-Bimalgarh Doubling extension	4/2010	149.90	3/2015	177.38	3/2015
28	Cuddalore-Salem via Vriddhachalam GC	4/1999	198.68	/	556.64	0/0
29	Sriperumbudur-Guduvanchery with spur to Irungattukkottai-Ava	4/2013	839.00	/	839.00	0/0
30	Chennai-Cuddalore via Mamallapuram	4/2008	523.52	/	1200.00	0/0
31	Attippattu-Puttur	4/2008	446.87	/	527.00	0/0
32	New Bongaigaon-Rangia-Kamakhya Doubling	4/2013	1798.00	/	1798.00	0/0
33	Hajipur-Ramdayalunagar Doubling	4/2013	213.01	/	213.01	0/0
34	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne	4/2009	470.00	/	470.00	0/0

List of projects added (Jul, 2013)



(All sums of money in crore of rupees)

Project Name		Original		Now anticipated		
		DOA	Cost (Rs. Crores)	DOC	Cost (Rs. Crores)	DOC
Railways						
35	Sakri-Nirmali & Jhanjharpur-Laukahabazar & Saharsa-Forbesgan	4/2004	372.14	/	355.81	0/0
36	Muzaffarpur-Darbangha (NL)	4/2008	281.30	/	281.30	0/0
37	Ernakulam-Kumbalam	4/2010	189.24	/	189.24	0/0
38	Chengannur-Chingavanam	4/2006	191.72	/	191.72	0/0
39	Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch	4/2007	247.00	/	951.24	0/0
40	Madurai-Bodinayakanur	4/2008	164.41	/	260.72	0/0
41	Madurai-Rameswaram-GC	4/1999	240.00	/	441.69	0/0
42	Erode-Palani	4/2008	288.57	/	603.22	0/0
43	New Coochbehar-Gumanihat Patch Doubling project	4/2012	283.55	/	283.55	3/2015
44	New Coochbehar to Samuktala	4/2011	209.77	/	209.77	3/2015
45	Dimapur-Tizit NL	4/2013	4274.00	/	4274.00	0/0
46	Bandel-Boinchi 3rd line	4/2011	288.35	/	288.35	0/0
47	Plassey-Jiaganj Doubling	4/2011	248.07	3/2015	248.07	3/2015
48	Pirpainti-Jasidih	4/2013	915.98	/	915.98	0/0
49	Hansnabad-Hingalgaon New BG line	4/2010	172.03	/	172.03	0/0
50	Sultanganj-Katuria via Asarganj, Tarapur & Belhar	4/2007	450.00	/	450.00	0/0
51	Lakshmikanthapur-Namkhana subsequently MM for Namkhana-Chandr	4/1999	406.99	/	406.99	0/0
52	Madurai-Tuticorin via Aruppukkottai	4/2011	601.43	/	800.00	0/0
53	Running of 12 car trains on Harbour Line	4/2012	714.10	/	714.10	0/0
54	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Pha	4/2012	632.68	4/2012	816.55	0/0
55	Boinchi-Shaktigarh 3rd line	4/2011	175.80	/	175.80	0/0
56	Sainthia-Tarapith 3rd line	4/2011	193.44	/	193.44	0/0
57	Hansdiha-Godda NL	4/2011	267.09	/	267.09	0/0
58	Tarakeswar-Magra New BG line	4/2010	365.17	/	365.17	0/0
59	Bariarpur-Mananpurvia Kharagpuer, Lachimpur-Barahat	4/2007	450.55	/	450.55	0/0
60	Kalyan-Kasara 3rd line	4/2011	277.70	/	277.70	0/0
61	Pen-Roha doubling	4/2007	98.74	/	0.00	0/0
62	Wardha-Nanded Maharashtra	4/2008	697.00	/	1604.00	0/0
63	Howrah Division- Platform shelter (40 C Category stations)	4/2010	157.94	/	157.94	0/0
64	Panvel-Pen Doubling	4/2006	96.16	/	190.00	0/0
65	Wardha-Sewagram NGP 3rd line	4/2012	297.85	/	297.85	0/0
66	Howrah-Development of station including segregation of aariv	4/2011	166.89	/	166.89	0/0
67	Santoshpur-Remount Road via Garden Reach- Metiabruze	4/2010	268.52	/	268.52	0/0
68	3rd line between Bhusawal-Jalgaon	4/2011	182.06	/	182.06	0/0
69	Nabadwipdham-Patuli doubling	4/2010	169.82	/	169.82	0/0
70	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC	4/2010	423.66	3/2017	423.66	3/2017
71	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S	4/2009	257.42	3/2014	257.42	3/2014
72	Magrahat-Diamond Harbour with MM Sangrampur-Krishnachandpur	4/2009	493.96	/	493.96	0/0
73	Chandpara-Bangaon doubling with exension to Chandbazar & new	4/2003	337.96	/	337.96	0/0
74	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat	4/2000	297.47	/	297.47	0/0
75	New Alipur to Akra, MM for Budge Budge-Pujali NL, Pujali-Ulu	4/2010	494.54	/	494.54	0/0
76	Princepghat-Majerhat Doubling of	4/2011	299.60	3/2017	299.60	3/2017

List of projects added (Jul, 2013)

(All sums of money in crore of rupees)



Project Name		Original		Now anticipated		
		DOA	Cost (Rs. Crores)	DOC	Cost (Rs. Crores)	DOC
Railways						
	Circular Railway					
77	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh	4/2010	296.44	/	296.44	0/0
78	Sondalia-Champapukur doubling with new MM for Bira-Chakia NL	4/2010	277.28	/	277.28	0/0
79	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D	4/2010	174.56	/	174.56	0/0
80	Krishnanagar-Bethua Dahri doubling	4/2009	151.65	3/2015	151.65	3/2015
81	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S	4/2005	595.91	/	595.91	0/0
82	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar	4/2001	923.52	/	923.52	0/0
83	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL	4/2000	157.17	/	157.17	0/0
84	Pirpainti-Bhagalpur	4/2011	261.38	/	261.38	0/0
85	Circular Railway including Remount Road to Santoshpur	4/2009	573.78	/	573.78	0/0
86	Lumding-Hojai Patch Doubling Project	4/2012	246.07	/	246.07	0/0
87	Ambari Falakata to New Maynaguri	4/2011	312.12	/	312.12	0/0
88	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line &	4/1999	523.17	/	1393.44	0/0
89	Murkongselek-Pasighat NL	4/2011	165.82	/	165.82	0/0
90	New BG line from Jagbani to Biratnagar	4/2010	241.52	/	238.83	0/0
91	New BG line from Balurghat to Hilly NFR	4/2010	242.22	/	242.22	0/0
92	New BG line from Byrnihat to Shillong	4/2010	4083.02	/	4083.02	0/0
93	Agartala-Akhaura NL	4/2012	252.00	/	252.00	0/0
94	Construction of NL from Kumarghat-Agartala	4/1999	895.00	3/2007	1151.00	3/2015
95	New BG line from Kaliyaganj to Buniadpur	4/2010	221.42	/	221.47	0/0
96	New BG line from Dudhnoi-Mendipatar	4/1999	175.43	/	175.43	3/2014
97	Kumbalam-Turavur	4/2011	252.96	/	252.96	0/0
98	Kuruppanthara-Chingavanam	4/2007	270.14	/	270.14	0/0
99	Villupuram-Dindigul with Electrification	4/2008	822.39	/	1280.83	0/0
100	Chennai Beach-Tambaram-Chengalpattu Suburban GC	4/1999	271.24	/	520.00	0/0
101	Kursela-Bihariganj (NL)	4/2008	192.56	/	192.56	0/0
102	Araria-Supaul (NL)	4/2008	304.41	/	304.41	0/0
103	Muzaffarpur-Katra-Orai-Janakpur Road (NL)	4/2008	228.05	/	228.05	0/0
104	Sitamarhi-Jaynagar-Nirmali via Sursand (NL)	4/2008	678.62	/	678.62	0/0
105	Motihari-Sitamarhi (NL)	4/2006	211.00	/	211.00	0/0
106	Darbangha-Kusheshwarsthan (NL)	4/2005	366.73	/	366.73	0/0
107	Chhapra-Muzaffarpur (NL)	4/2006	285.07	/	378.56	0/0
108	Sakri-Hasanpur Road (NL)	4/1999	175.69	/	325.00	0/0
109	Bhadutola-Jhargram via Lalgah (NL)	4/2011	289.64	/	289.64	0/0
110	Digha-Jaleswar including MM for Digha-Egra	4/2010	553.63	/	651.17	0/0
111	Bowaichandi-Arambagh	4/2010	267.37	/	267.37	0/0
112	Dholpur-Sirmuttra with extension to Gangapurcity & Mohari-Ta	4/2010	622.41	2/2019	2030.50	2/2019
113	Alwar-Bandikui doubling	4/2013	242.09	/	242.09	0/0
114	Rani-Marwar Jn. Patch doubling	4/2012	288.97	/	288.97	0/0
115	Ajmer-Bangurgram	4/2011	213.39	/	251.99	0/0

List of projects added (Jul, 2013)

(All sums of money in crore of rupees)



Project Name		Original			Now anticipated	
		DOA	Cost (Rs. Crores)	DOC	Cost (Rs. Crores)	DOC
Railways						
116	Guriya-Marwar & Karjoda-Palanpur	4/2011	239.73	/	274.34	0/0
117	Rajkot-Veraval,Wansjalia to Jatahsar with new MM for Shapur-	4/1994	320.66	/	320.66	0/0
118	Chottaudepur-Dhar(NL)	4/2007	1347.26	/	1347.26	0/0
119	Ahmedabad-Botad (GC)	4/2012	567.18	/	567.18	0/0
120	Dhasa-Jetalsar (GC)	4/2012	376.59	/	376.59	0/0
121	Miyagam-Karjan-Dabhoi-Samlaya (GC)	4/2011	439.88	/	439.88	0/0
122	Dahod-Indore via Sardarpur, Jhabua & Dhar	4/2007	1640.04	/	1640.04	0/0
Road Transport & Highways						
123	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	3/2012	828.00	9/2014	828.00	9/2014
124	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC	10/2011	1565.00	10/2014	1565.00	10/2014
125	REENGUS SIKAR	3/2012	333.51	9/2014	333.51	9/2014

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	03/2014	06/2014	3
	<u>Civil Aviation</u>						
2	Construction of New International Terminal Building AAI	335.61	335.61	05/2012	06/2013	09/2013	3
	<u>Coal</u>						
3	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
	<u>Steel</u>						
4	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,291.00	10/2009	07/2013	08/2013	1
5	67.5 MW TG-5 AUX. SYSTEM EMERGENCY POWER REQUIREMENT RINL	230.00	343.58	02/2011	07/2013	08/2013	1
6	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT SAIL	187.33	187.33	10/2013	05/2014	06/2014	1
7	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON SAIL	254.55	254.55	11/2013	06/2014	06/2015	12
	<u>Petroleum</u>						
8	Fluidized catalytic cracking unit(FCCU) revamp IOCL	1,000.00	1,000.00	01/2013	09/2013	10/2013	1
9	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT IOCL	341.50	341.50	02/2013	07/2013	08/2013	1
10	IOR of B-173A Field ONGC	352.49	352.49	03/2014	04/2014	05/2014	1
11	Polypropylene unit Mangalore Refin	1,803.78	1,803.78	07/2012	10/2013	12/2013	2
12	MRPL Phase-III Expansion Mangalore Refin	12,412.00	12,160.26	01/2012	07/2013	10/2013	3
13	Construction of 6 ETPs ONGC	302.26	240.95	09/2012	09/2013	12/2013	3
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN OIL	871.35	871.35	03/2015	03/2015	06/2015	3
15	ADDITIONAL GAS PROCESSING UNITS AT URAN ONGC	1,797.35	977.00	12/2011	07/2013	11/2013	4
16	Development of WO-16 Cluster Fields ONGC	2,523.00	2,523.00	01/2014	01/2014	05/2014	4
17	SINGLE POINT MOORING FACILITY(SMP) PROJECT Mangalore Refin	1,043.57	957.10	04/2012	07/2013	12/2013	5
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE ONGC	861.79	761.68	05/2013	11/2013	05/2014	6
19	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN BPCL	246.81	276.83	04/2012	06/2013	12/2013	6
20	Development of Cluster-7 Fields ONGC	3,241.03	6,638.94	03/2013	04/2014	11/2014	7

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
21	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2013	12/2014	12
22	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER ONGC	202.94	202.94	01/2014	01/2014	01/2015	12
23	Mehesana Redevelopment ONGC	3,823.00	3,823.00	04/2015	04/2015	03/2017	23
24	Ahmedabad Redevelopment ONGC	1,916.10	1,916.10	12/2014	12/2014	12/2016	24
25	Ankleswar Redevelopment ONGC	2,189.63	2,189.63	12/2014	12/2014	12/2016	24
26	Construction of one Multipurpose Support Vessel ONGC	723.64	723.64	03/2013	11/2013	06/2016	31
	<u>Power</u>						
27	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B PGCIL	160.32	160.32	10/2012	07/2013	08/2013	1
28	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	07/2013	09/2013	2
29	TEHRI PUMPED STORAGE PLANT(1000MW) THDCL	1,657.00	2,978.86	07/2010	11/2016	02/2017	3
30	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	03/2014	06/2014	3
31	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR PGCIL	1,075.12	1,075.12	05/2012	09/2013	12/2013	3
32	Trans. System associated with PALLATANA GBPP & BPT PGCIL	2,144.00	2,144.00	12/2012	03/2014	06/2014	3
33	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR PGCIL	170.36	170.36	04/2013	09/2013	12/2013	3
34	Establishment of pooling stations at Rajgarh PGCIL	1,719.52	1,719.52	08/2013	08/2013	12/2013	4
35	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI PGCIL	1,677.57	1,677.57	04/2013	03/2014	03/2015	12
	<u>Railways</u>						
36	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	07/2013	09/2013	2
37	New Work for Construction of Metro railway from Ba RVNL	2,069.60	2,298.42	03/2014	03/2014	03/2016	24
	<u>Road Transport & Highways</u>						
38	THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	07/2013	09/2013	2
39	DEVIHALLI-HASSAN NHAI	453.00	453.00	N.A.	07/2013	09/2013	2
40	NALBARI TO BIJNI (AS-8) NHAI	200.00	200.00	06/2008	09/2013	12/2013	3
41	Hungund-Surathkal and Mangalore-Knt/Kerala Border NHAI	946.00	946.00	N.A.	07/2013	10/2013	3
42	DEOLI-KOTA NHAI	593.00	593.00	07/2013	07/2013	10/2013	3
43	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) NHAI	1,108.00	2,288.00	11/2011	08/2013	12/2013	4
44	Hazaribagh-Ranchi NHAI	625.07	625.07	01/2013	06/2013	10/2013	4
45	4-LANNING OF CHAPRA-HAJIPUR NHAI	575.00	575.00	07/2013	07/2013	12/2013	5
46	NAGPUR-KONDHALI,NH-6(NHAI) NHAI	168.00	168.00	12/2008	06/2013	03/2014	9

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Shipping & Ports</u>						
47	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	07/2013	08/2013	1
48	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICULAR PORT TRUST	150.00	600.00	03/2006	06/2013	12/2013	6
	48						

Graphical Presentation of All Projects w.r.t. Original Schedule

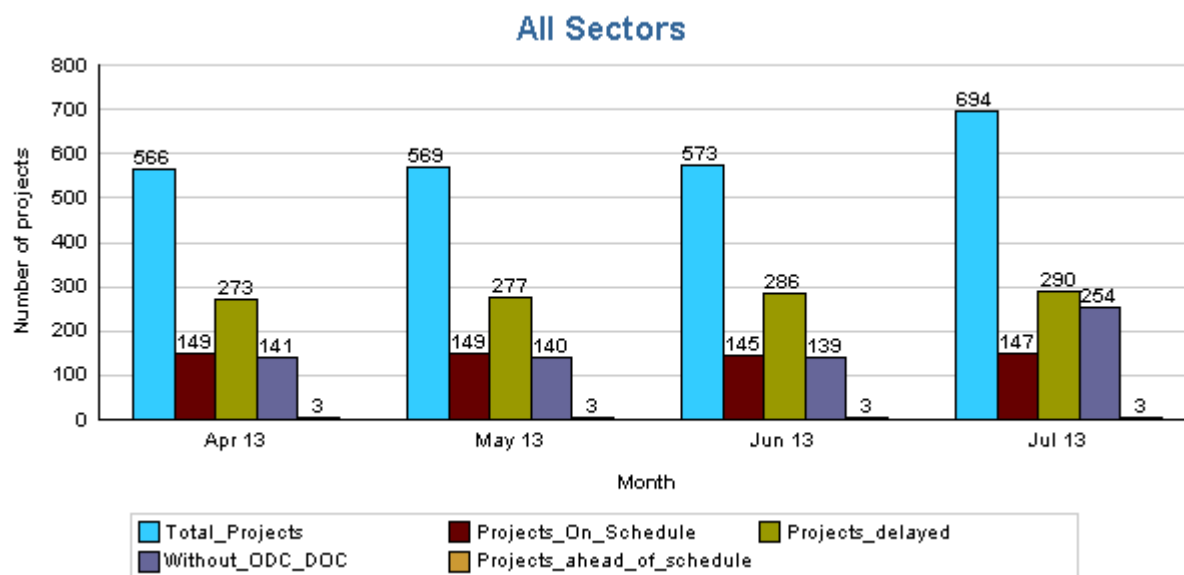


Break-up of 290 Delayed projects in July 2013

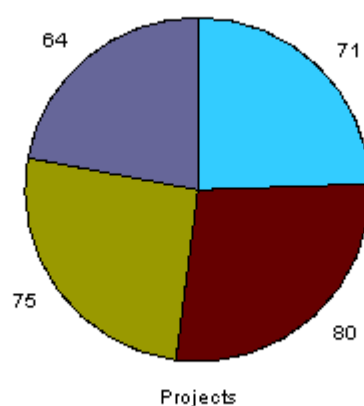


Delay in Months



Graphical Presentation of All Projects w.r.t. Revised Schedule

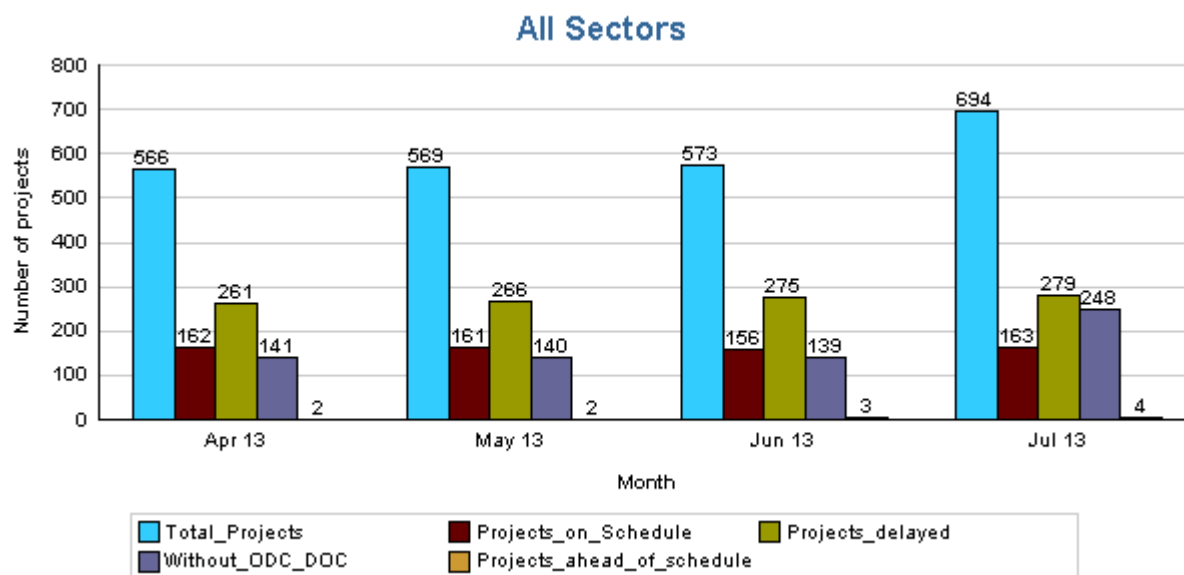


Break-up of 279 Delayed projects in July 2013

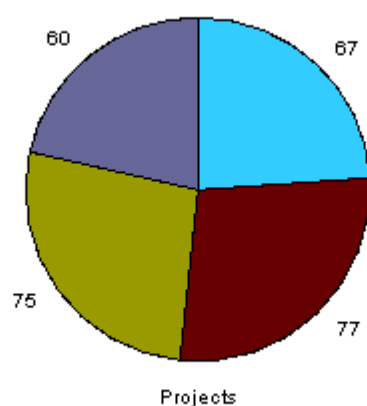


Delay in Months



Graphical Presentation of Urban Development Sector

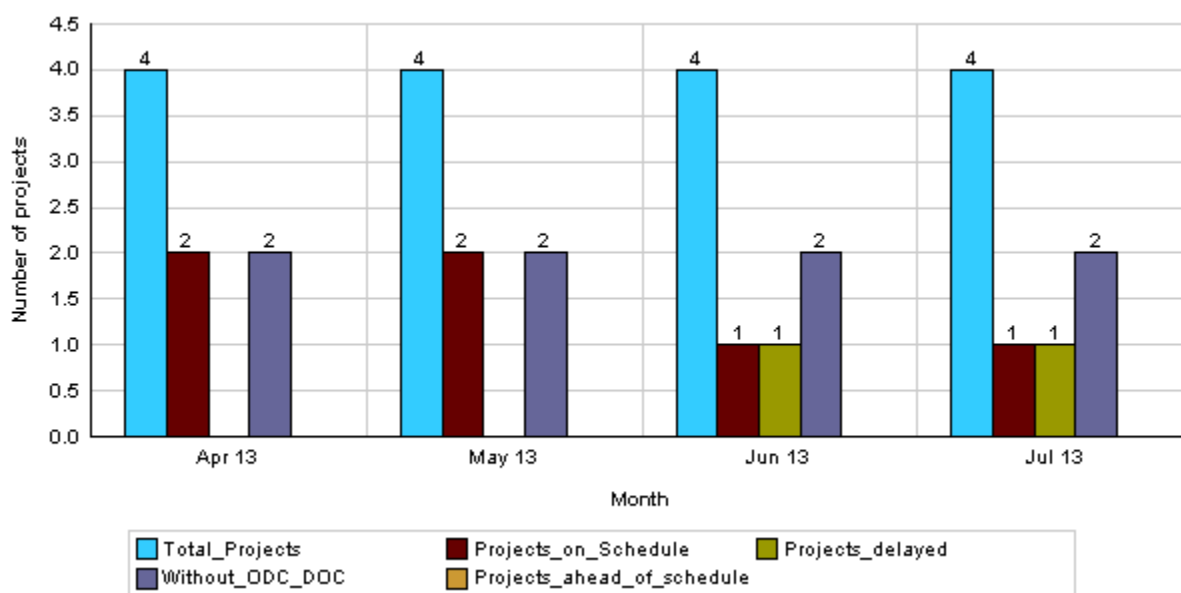


Break-up of 1 Delayed projects in July 2013




Delay in Months



Graphical Presentation of Telecommunications Sector

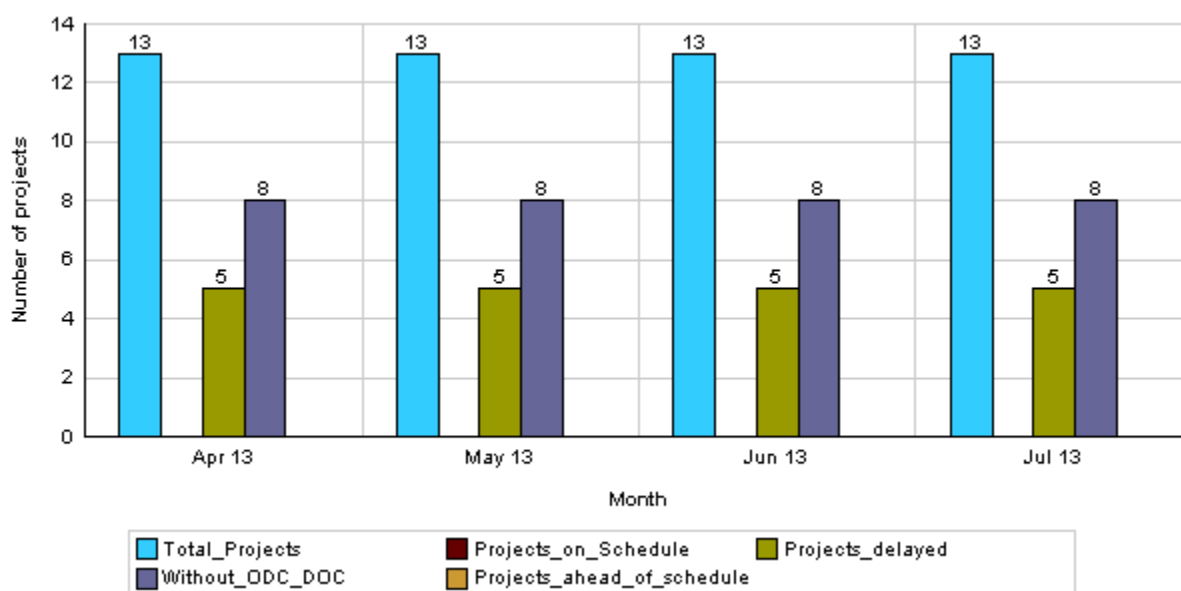


Break-up of 5 Delayed projects in July 2013

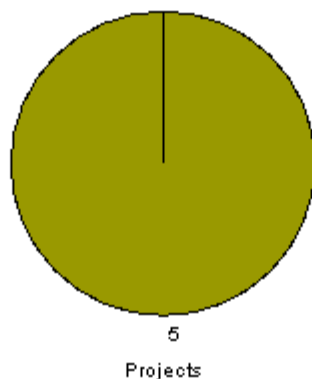


Delay in Months



Graphical Presentation of Shipping & Ports Sector

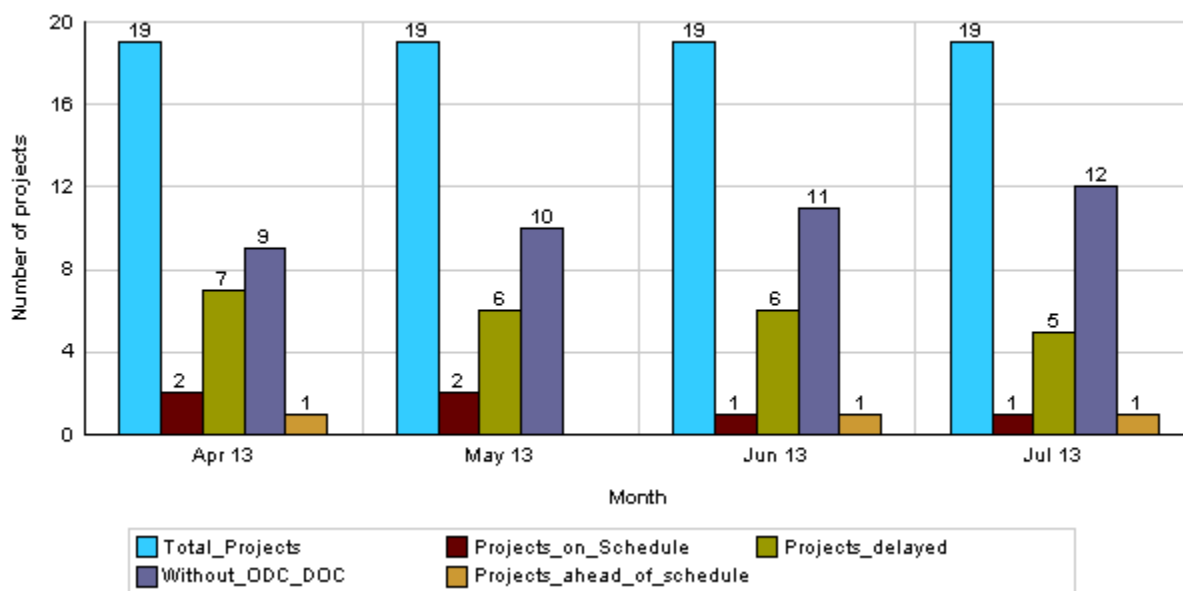


Break-up of 5 Delayed projects in July 2013

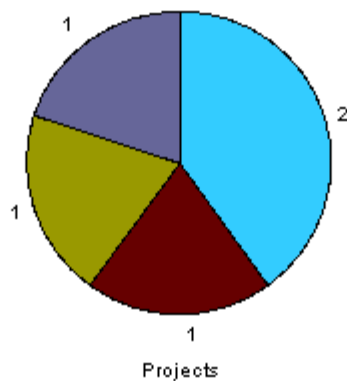


Delay in Months



Graphical Presentation of Road Transport & Highways Sector

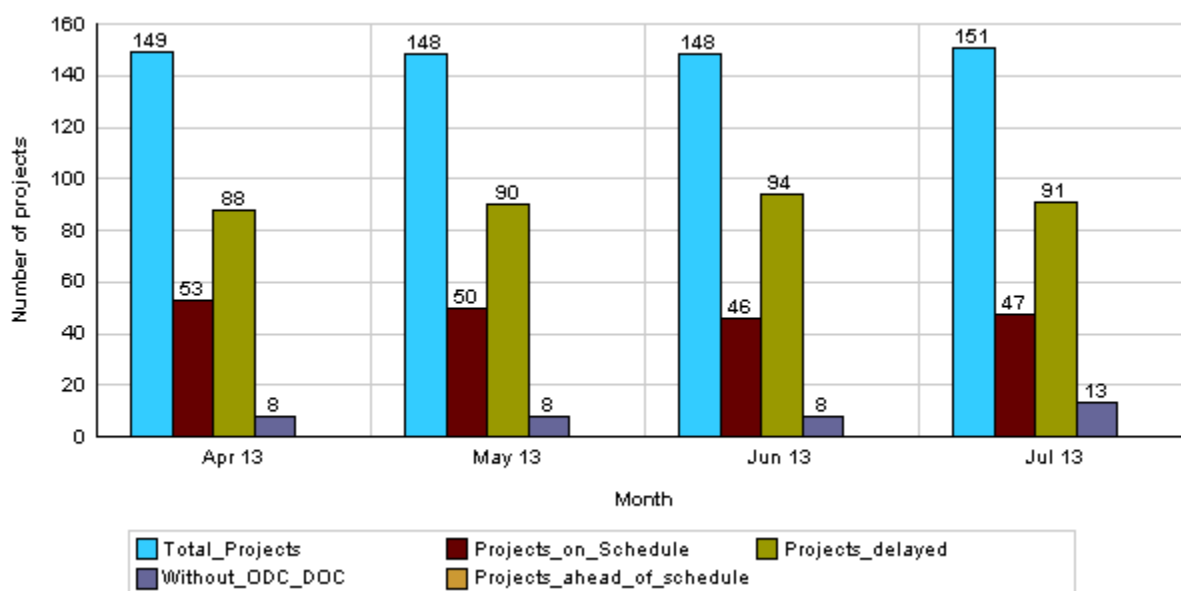


Break-up of 91 Delayed projects in July 2013

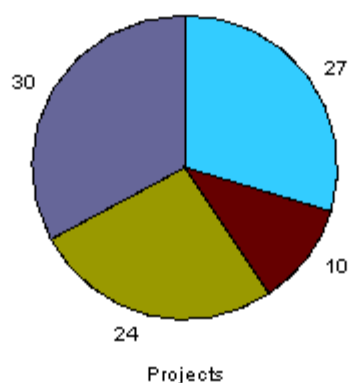


Delay in Months



Graphical Presentation of Railways Sector

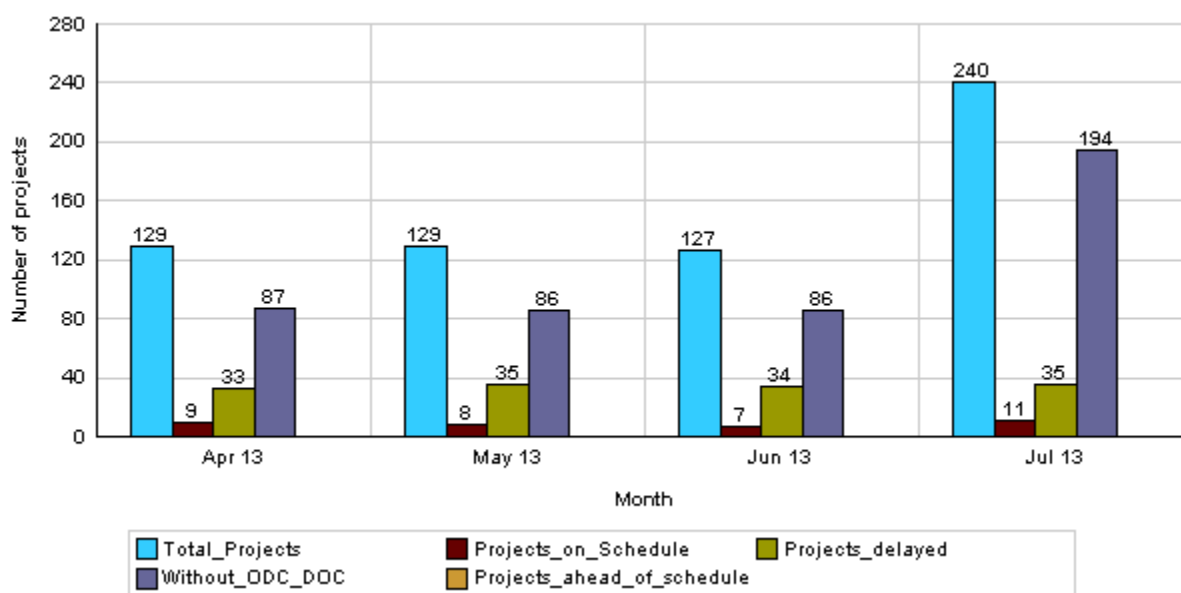


Break-up of 35 Delayed projects in July 2013

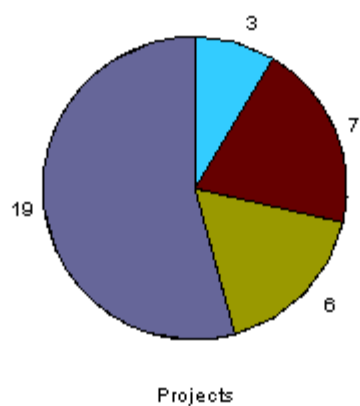


Delay in Months



Graphical Presentation of Power Sector

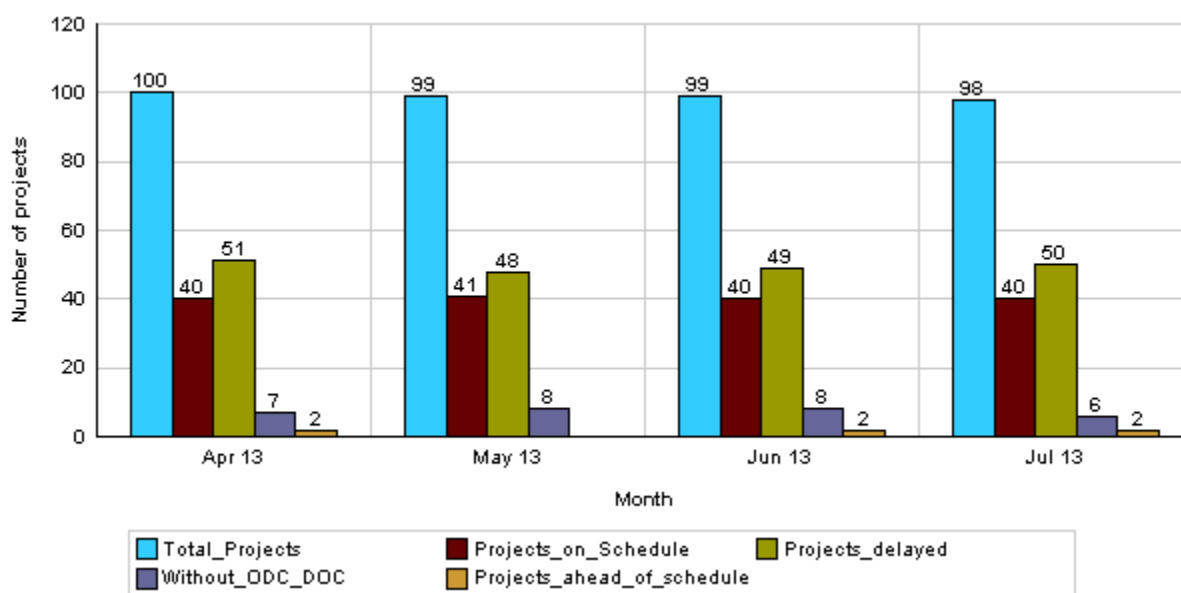


Break-up of 50 Delayed projects in July 2013

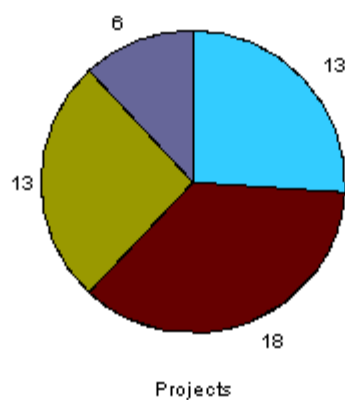


Delay in Months



Graphical Presentation of Petroleum Sector

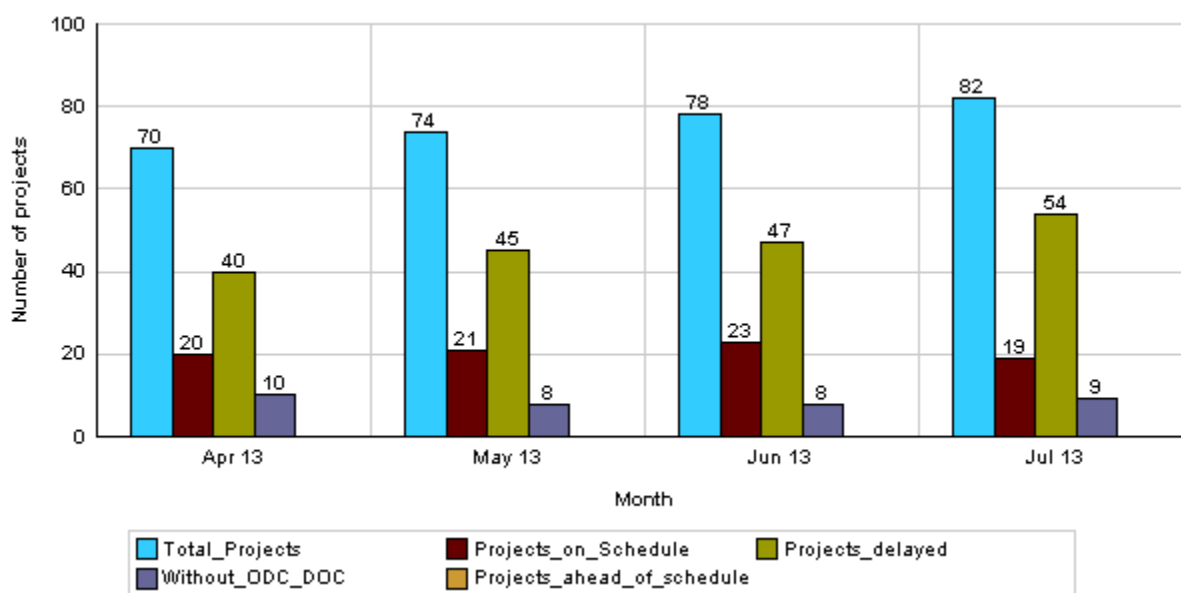


Break-up of 54 Delayed projects in July 2013

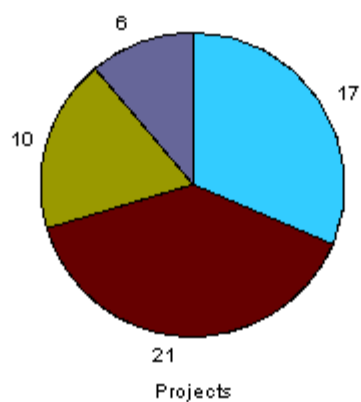


Delay in Months



Graphical Presentation of Steel Sector

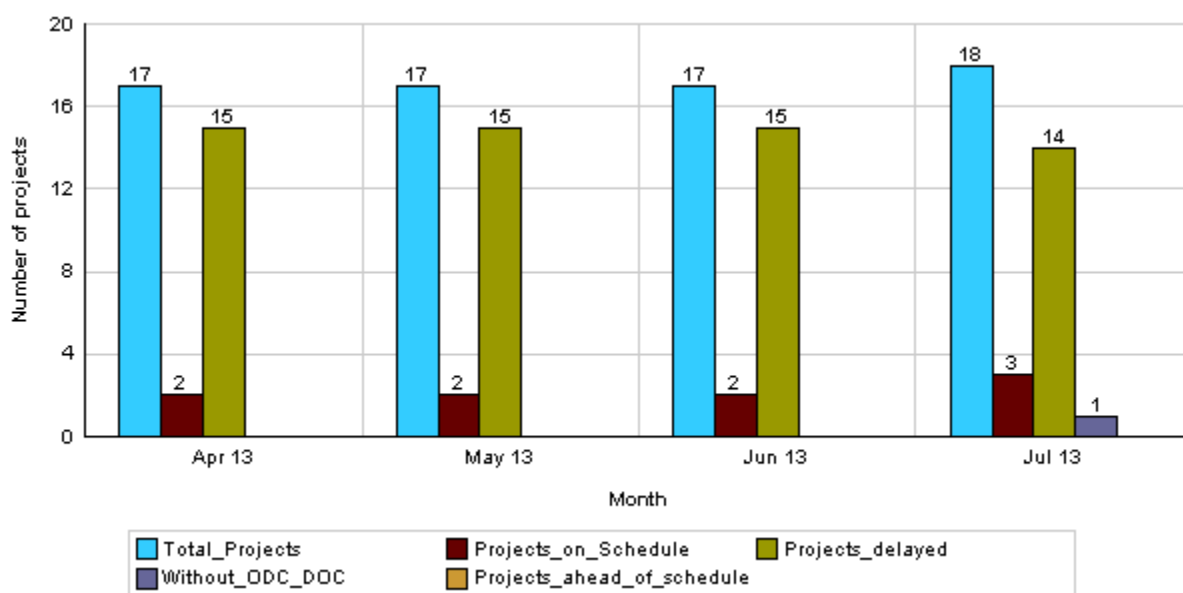


Break-up of 14 Delayed projects in July 2013

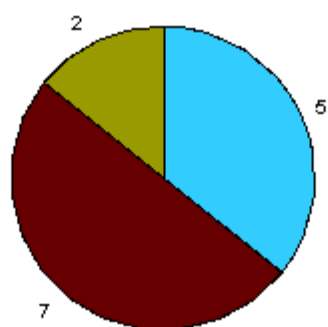


Delay in Months



Graphical Presentation of Coal Sector

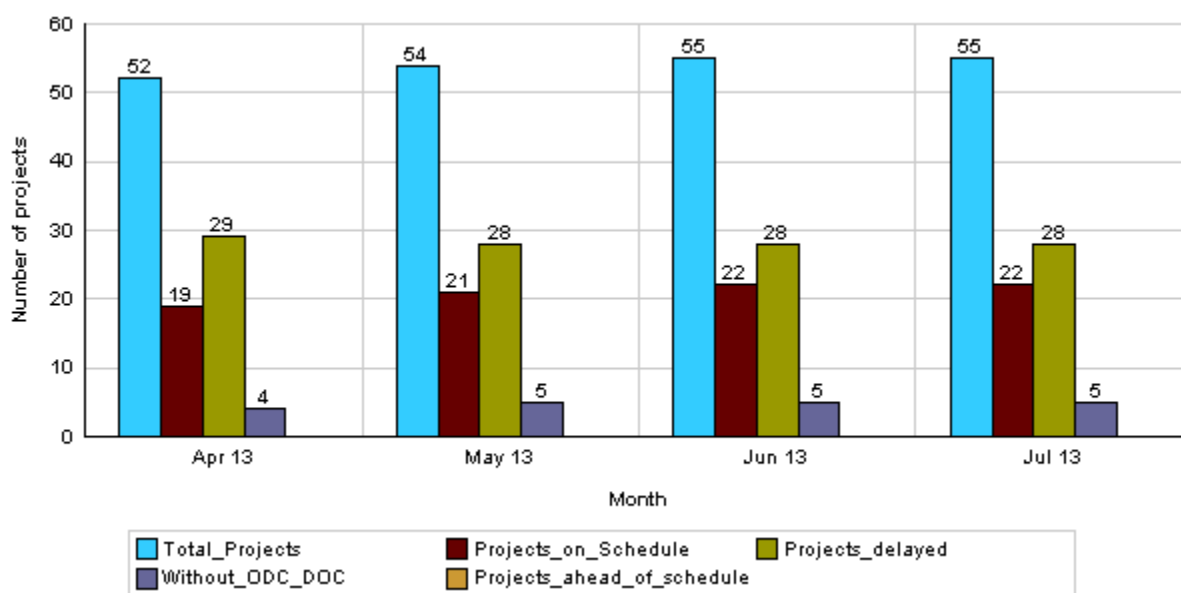


Break-up of 28 Delayed projects in July 2013

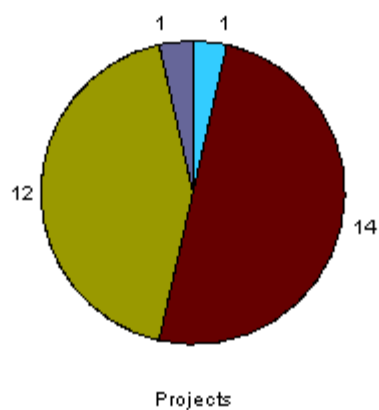


Delay in Months



Graphical Presentation of Civil Aviation Sector

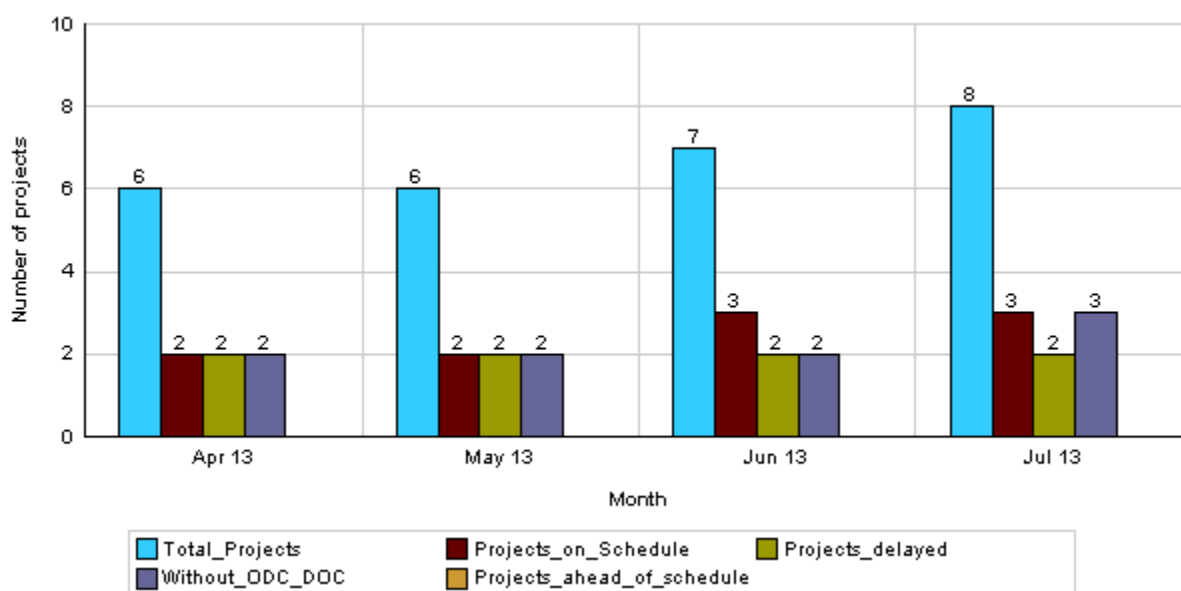


Break-up of 2 Delayed projects in July 2013

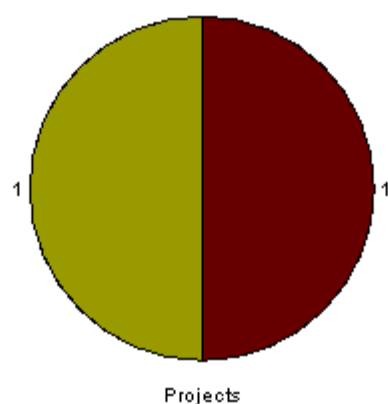


Delay in Months



Graphical Presentation of Atomic Energy Sector

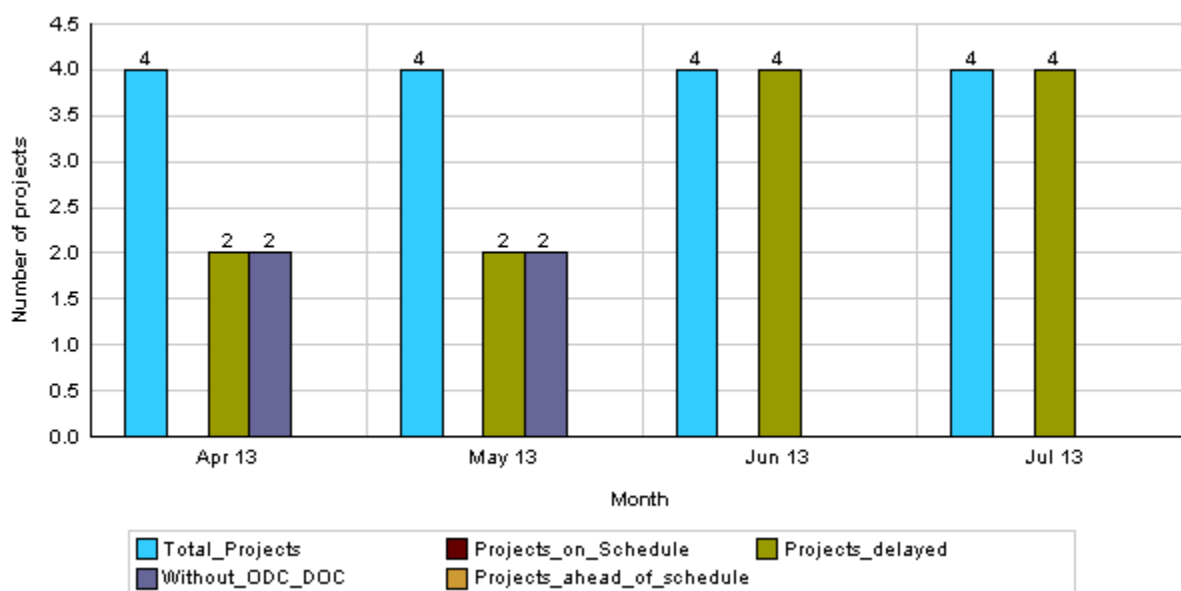

Break-up of 4 Delayed projects in July 2013

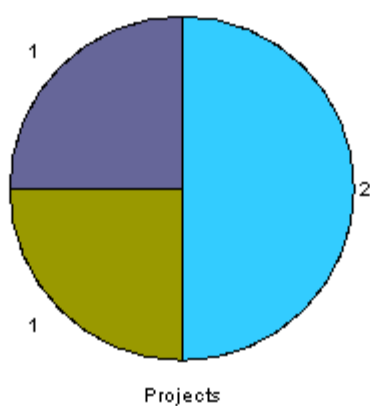

Delay in Months



Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
Atomic Energy	4	40,442.00	44,541.00	46,726.00	26,100.60
Civil Aviation	8	6,035.46	6,242.46	6,624.95	5,404.81
Coal	55	38,127.05	40,729.44	41,212.50	15,215.76
Steel	18	65,625.22	69,847.40	71,782.40	52,362.23
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	82	183,464.22	197,693.96	197,793.04	92,271.22
Power	98	251,918.93	255,978.58	270,310.17	122,996.17
Railways	240	121,907.58	151,121.88	227,295.52	72,903.41
Road Transport & Highways	151	103,915.59	104,082.09	105,854.21	81,038.79
Shipping & Ports	19	15,617.12	17,487.95	17,902.42	8,607.77
Telecommunications	13	5,699.24	5,699.24	5,520.22	1,970.84
Urban Development	4	44,245.18	44,304.08	49,518.08	6,593.59
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	694	883,001.10	947,190.98	1,050,646.51	490,011.19

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(Jul,2013)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,991.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,354.00	12/2008 -	06/2014	66(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,681.60	09/2010 -	03/2015	54(O) -	8/82
4	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,074.00	12/2016 -	03/2017	3(O) -	0/69
	Total		40,442.00 -	46,726.00	26,100.60				47/327
	<u>Civil Aviation</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,472.45	05/2011 -	03/2013	-	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.80	01/2011 04/2013	12/2014	47(O) 20(R)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	228.60	05/2012 -	09/2013	16(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,904.73	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Chandigarh	02/2011	452.00 -	452.00	117.24	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI - [N04000072]AAI,Multi State	02/2010	344.28 -	344.28	-	03/2014 -	03/2014	0(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	449.97	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,624.95	5,404.81				0/0
	<u>Coal</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	721.74	03/2013 09/2012	10/2014	19(O) 25(R)	18/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	88.71	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	446.32	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC - [N06000103]CCL,Jharkhand	02/2012	858.11 -	858.11	49.30	03/2020 -	03/2020	0(O) -	0/3
17	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	112.35	03/2012 -	03/2014	24(O) -	5/6

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.36	03/2011 -	03/2014	36(O) -	0/2
19	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.44	03/2010 -	03/2015	60(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	52.44	03/2016 -	03/2016	0(O) -	0/6
21	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00 -	490.10	149.76	03/2017 -	03/2017	0(O) -	4/12
22	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	45.02	03/2014 03/2014	03/2014	0(O) 0(R)	0/2
23	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	535.10	160.76	03/2015 03/2015	03/2015	0(O) 0(R)	0/3
24	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	265.66	03/2014 -	03/2016	24(O) -	2/8
26	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,253.35	03/2014 -	03/2016	24(O) -	6/12
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,415.57	03/2014 -	03/2016	24(O) -	10/15
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87 -	395.87	72.34	03/2015 -	03/2015	0(O) -	1/13
30	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	114.33	03/2013 -	03/2015	24(O) -	3/8
31	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	14.02	03/2015 -	03/2015	0(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72(O) -	0/2
35	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	87.20	12/2012 -	03/2016	39(O) -	9/44
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,Andhra Pradesh	07/2012	417.33 -	417.33	0.06	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.62	03/2013 -	03/2015	24(O) -	5/10
38	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46 -	162.46	38.66	03/2014 -	03/2014	0(O) -	0/2
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
40	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	4.88	03/2018 03/2018	03/2018	0(O) 0(R)	0/4
41	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.85	03/2013 -	03/2014	12(O) -	0/2
42	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.27	03/2010 -	03/2014	48(O) -	9/10
43	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	703.34	03/2013 -	03/2013	-	0/9

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
44	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
45	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016	44(O) -	0/3
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24(O) -	1/6
47	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.48	03/2012 -	03/2015	36(O) -	11/20
48	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
49	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
50	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	32.00	12/2015 -	02/2018	26(O) -	1/33
51	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.66	03/2012 -	03/2015	36(O) -	0/2
52	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60(O) -	0/2
53	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
54	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.01	03/2014 -	03/2016	24(O) -	0/1
55	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.24	03/2013 -	03/2015	24(O) -	0/3
56	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24(O) -	0/2
57	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	235.20	03/2012 -	-	-	24/27
58	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
59	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	58.85	- -	03/2016	- -	4/48
60	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,Andhra Pradesh	06/2012	365.01 -	365.01	-	06/2015 -	06/2015	0(O) -	2/51
61	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	49.93	03/2015 -	03/2015	0(O) -	8/31
62	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85 -	510.85	264.37	03/2016 -	03/2016	0(O) -	0/2
63	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	55.56	03/2012 -	-	-	16/42
64	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72 -	447.72	45.17	03/2016 -	03/2016	0(O) -	0/12
65	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,747.67	06/2009 -	01/2014	55(O) -	19/23
66	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,478.68	03/2012 -	03/2014	24(O) -	20/39
67	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	128.14	03/2012 -	03/2016	48(O) -	0/2
	Total		38,127.05 -	41,212.50	15,215.76				204/792

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Steel</u>								
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	316.17	04/2013 12/2013	12/2013	8(O) 0(R)	17/19
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 349.64	349.64	253.79	08/2010 08/2010	06/2013	-	1/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 343.58	343.58	260.62	02/2011 02/2011	08/2013	30(O) 30(R)	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	209.28	05/2013 11/2013	11/2013	6(O) 0(R)	12/21
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	276.50	05/2012 05/2012	09/2013	16(O) 16(R)	2/2
73	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	352.58	12/2011 03/2012	12/2013	24(O) 21(R)	16/21
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 216.68	216.68	147.26	10/2012 10/2012	09/2013	11(O) 11(R)	3/4
75	Coke Oven Battery-5 - [N12000080]SAIL,West Bengal	03/2012	339.35 -	339.35	9.05	06/2015 -	06/2015	0(O) -	0/0
76	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	332.65	64.42	08/2014 -	08/2014	0(O) -	0/0
77	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	68.64	11/2013 -	06/2015	19(O) -	1/1
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	9,923.03	03/2013 -	09/2014	18(O) -	22/27
79	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,662.34	12/2011 -	12/2013	24(O) -	16/16
80	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,691.38	12/2012 -	03/2014	15(O) -	10/12
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	14,889.86	12/2011 -	12/2013	24(O) -	19/19
82	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,478.48	10/2009 10/2012	08/2013	46(O) 10(R)	66/67
83	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,679.32	03/2013 -	12/2013	9(O) -	11/14
84	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	76.05	10/2013 -	06/2014	8(O) -	0/1
85	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	254.90	3.46	12/2014 -	12/2014	0(O) -	0/0
	Total		65,625.22 -	71,782.40	52,362.23				198/228
	<u>Petrochemicals</u>								
86	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20(O) 0(R)	19/29
	Total		5,460.61 -	8,920.00	4,510.51				19/29
	<u>Petroleum</u>								
87	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	28.10	06/2012 -	03/2014	21(O) -	0/4
88	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23(O) -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
89	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	726.73	12/2011 -	11/2013	23(O) -	0/5
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,494.55	03/2013 -	03/2014	12(O) -	0/5
91	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,Multi State	08/2011	586.00 -	586.00	17.03	07/2015 -	08/2015	1(O) -	0/0
92	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24(O) -	0/0
93	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24(O) -	0/0
94	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	540.92	287.28	07/2012 07/2012	-	-	0/17
95	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]OCL,Haryana	11/2009	341.50 -	341.50	189.49	02/2013 -	08/2013	6(O) -	38/42
96	Butene-1 at Panipat - [N16000139]OCL,Haryana	02/2012	190.00 -	190.00	67.27	03/2014 -	03/2014	0(O) -	0/24
97	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	128.88	06/2012 -	09/2013	15(O) -	0/0
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	360.28	09/2011 -	12/2014	39(O) -	0/0
99	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	57.73	06/2012 -	09/2013	15(O) -	0/0
100	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	312.61	- -	03/2013	-	18/19
101	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	4.12	01/2014 -	01/2015	12(O) -	0/5
102	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	276.67	05/2013 -	05/2014	12(O) -	0/5
103	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	152.89	115.74	06/2013 -	-	-	0/0
104	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	62.49	08/2013 -	01/2014	5(O) -	0/5
105	Construction of 6 ETps - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	98.45	09/2012 -	12/2013	15(O) -	0/0
106	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]ONGC,Gujarat	10/2011	200.69 -	200.69	2.96	07/2014 -	07/2014	0(O) -	0/5
107	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
108	Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12(O) -	0/5
109	Construction of three ETps, Mehsana - [N16000135]ONGC,Gujarat	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2014	0(O) -	0/5
110	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	486.00	54.56	09/2013 -	09/2013	0(O) -	0/0
111	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00 -	1,584.00	409.88	- -	-	-	0/0
112	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94(O) 20(R)	0/0
113	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,107.72	08/2010 03/2012	05/2014	45(O) 26(R)	0/10
114	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63(O) 45(R)	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
115	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	02/2014	43(O) 21(R)	0/0
116	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63(O) 11(R)	0/0
117	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24(O) 16(R)	6/76
118	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	23(O) 17(R)	56/59
119	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	240.31	03/2013 -	12/2013	9(O) -	0/5
120	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	11.10	05/2014 -	05/2014	0(O) -	0/9
121	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
122	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	228.26	11/2012 -	10/2013	11(O) -	0/9
123	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	957.44	01/2014 -	05/2014	4(O) -	0/9
124	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	80.56	12/2014 -	12/2014	0(O) -	0/8
125	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu	05/2013	711.00 -	711.00	0.59	- -	-	-	0/0
126	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	624.66	01/2013 -	10/2013	9(O) -	18/18
127	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	156.85	10/2011 -	07/2013	21(O) -	0/9
128	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,469.11	04/2013 -	09/2013	5(O) -	0/167
129	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	1,116.82	05/2015 -	05/2015	0(O) -	0/17
130	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,727.24	03/2007 03/2017	12/2013	81(O) -39(R)	6/6
131	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	750.00	729.07	03/2007 03/2014	12/2013	81(O) -3(R)	3/3
132	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	4.00	03/2014 -	05/2014	2(O) -	0/5
133	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93(O) 9(R)	6/6
134	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	453.95	12/2015 -	05/2016	5(O) -	0/0
135	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 2,665.65	2,665.65	188.07	03/2015 -	03/2015	0(O) -	0/12
136	Integrated Development of Bassein Field - [N16000160]ONGC,Maharashtra	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0
137	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,496.18	13.30	01/2013 -	12/2015	35(O) -	0/0
138	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50(O) -	0/0
139	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	18(O) -	0/1

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
140	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	1,229.00	12/2012 -	-	-	0/21
141	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015	0(O) -	0/0
142	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,458.39	01/2012 -	10/2013	21(O) -	0/108
143	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	09/2013	12(O) -	0/0
144	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46(O) 12(R)	0/0
145	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	03/2017	23(O) -	0/0
146	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	279.00	-	12/2014 -	12/2014	0(O) -	0/0
147	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	729.24	03/2010 03/2012	12/2013	45(O) 21(R)	0/0
148	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	913.00	32.13	07/2015 -	07/2015	0(O) -	0/0
149	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	22,593.00	11/2012 -	04/2014	17(O) -	60/100
150	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	845.71	09/2012 -	-	-	5/11
151	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	4,978.58	02/2014 -	02/2014	0(O) -	0/0
152	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	228.47	04/2012 -	12/2013	20(O) -	0/0
153	Pipeline Replacement Project, Ahmedabad - [N16000159]ONGC,Gujarat	09/2011	202.25 -	202.25	-	07/2016 -	07/2016	0(O) -	0/5
154	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	435.83	05/2014 -	05/2014	0(O) -	0/5
155	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	725.28	07/2012 -	12/2013	17(O) -	0/31
156	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	- -	08/2013	- -	52/53
157	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64 -	1,210.64	72.54	11/2015 -	11/2015	0(O) -	6/25
158	Reconstruction of BPA & BPB Platforms - [N16000161]ONGC,Maharashtra	03/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015	0(O) -	0/0
159	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	97.03	12/2014 -	12/2014	0(O) -	0/0
160	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	651.11	04/2012 -	12/2013	20(O) -	0/0
161	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26(O) -	0/0
162	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26(O) -	0/0
163	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	10,281.00	0.04	- -	-	-	0/0
164	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3(O) -	0/5

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
165	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014	2(O) -	0/0
166	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	187.62	08/2012 -	03/2014	19(O) -	0/5
167	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	260.22	03/2012 -	12/2013	21(O) -	13/20
168	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	225.00	12/2013 -	12/2013	0(O) -	0/0
	Total		183,464.22 -	197,793.04	92,271.22				287/974
	Power								
169	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,835.42	08/2012 -	03/2014	19(O) -	0/11
170	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	830.37	05/2012 -	12/2013	19(O) -	0/8
171	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	0/7
172	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,163.00	08/2013 -	09/2014	13(O) -	10/19
173	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,514.00	12/2009 -	02/2017	86(O) -	27/47
174	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,938.00	07/2011 -	10/2015	51(O) -	5/28
175	COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015	0(O) -	0/20
176	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	1,909.24	144.20	06/2015 -	06/2015	0(O) -	0/0
177	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	824.57	08/2014 -	08/2014	0(O) -	7/20
178	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	40.12	06/2014 -	06/2014	0(O) -	0/20
179	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
180	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	182.80	3.60	10/2014 -	10/2014	0(O) -	0/0
181	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	955.49	09/2014 -	09/2014	0(O) -	7/20
182	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	884.62	10/2009 -	12/2013	50(O) -	5/15
183	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	688.73	11/2012 -	09/2014	22(O) -	2/13
184	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
185	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	1,034.60	05/2014 -	05/2014	0(O) -	1/11
186	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,217.64	08/2013 -	12/2013	4(O) -	1/12

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
187	Gadarwara Super Thermal Power Project Stage-I - [N18000151]NTPC,Madhya pradesh	02/2013	11,638.55 -	11,638.55	-	09/2017 -	09/2017	0(O) -	0/40
188	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	306.40	08/2014 -	08/2014	0(O) -	1/16
189	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	1,025.01	12/2013 -	12/2013	0(O) -	1/12
190	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	84.66	10/2012 -	08/2013	10(O) -	4/14
191	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	904.18	12/2007 12/2009	-	-	2/11
192	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,417.91	05/2013 05/2013	03/2017	46(O) 46(R)	7/22
193	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,706.11	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
194	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,031.00	04/2009 -	09/2014	65(O) -	0/9
195	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,700.00	12/2016 -	12/2016	0(O) -	12/15
196	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,870.68	09/2008 -	03/2013	-	15/23
197	LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00 -	11,846.00	1,082.00	05/2017 -	05/2017	0(O) -	5/39
198	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017	0(O) -	0/15
199	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
200	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	1,074.00	09/2016 -	09/2016	0(O) -	14/14
201	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	752.82	08/2010 01/2013	10/2013	38(O) 9(R)	0/3
202	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,315.50	08/2013 -	06/2015	22(O) -	0/17
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.57	02/2012 -	12/2013	22(O) -	1/13
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	355.89	11/2011 -	07/2014	32(O) -	0/11
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	372.89	11/2011 -	12/2013	25(O) -	1/14
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	131.59	01/2013 -	09/2013	8(O) -	1/6
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	308.88	07/2013 -	03/2014	8(O) -	1/11
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	869.10	04/2013 -	03/2015	23(O) -	0/11
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	174.41	11/2014 -	11/2014	0(O) -	1/12
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	91.41	03/2015 -	03/2015	0(O) -	0/15
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	35.47	04/2015 -	05/2015	1(O) -	0/16

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
212	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, Multi State	03/2010	965.58 -	965.58	595.85	11/2012 -	03/2014	16(O) -	0/11
213	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC, Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,833.75	10/2010 01/2013	03/2014	41(O) 14(R)	0/6
214	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,505.44	09/2009 07/2014	03/2018	102(O) 44(R)	1/20
215	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO, Arunachal Pradesh	12/2008	573.99 1,117.92	1,117.92	646.69	08/2012 08/2013	09/2014	25(O) 13(R)	17/22
216	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,607.63	01/2012 -	03/2014	26(O) -	0/27
217	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,420.00	10/2012 -	11/2013	13(O) -	14/16
218	SOLAPUR STPP - [N18000133]NTPC, Maharashtra	03/2012	9,395.18 -	9,395.18	1,558.00	11/2016 -	11/2016	0(O) -	15/15
219	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,317.03	09/2010 08/2014	12/2017	87(O) 40(R)	11/11
220	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL, Multi State	08/2010	170.36 -	170.36	88.08	04/2013 -	12/2013	8(O) -	4/15
221	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL, Multi State	08/2008	2,360.95 -	2,580.90	2,054.21	08/2012 -	03/2014	19(O) -	0/5
222	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL, Multi State	09/2012	1,508.74 -	1,508.74	75.55	06/2016 -	04/2015	-14(O) -	0/20
223	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL, Multi State	09/2012	1,935.35 -	1,935.35	209.13	12/2014 -	11/2014	-1(O) -	0/0
224	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL, Madhya Pradesh	03/2012	213.78 -	213.78	12.44	03/2014 -	03/2014	0(O) -	0/7
225	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL, Chhatisgarh	12/2011	1,746.65 -	1,746.65	97.42	08/2014 -	08/2014	0(O) -	2/19
226	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL, Maharashtra	02/2012	1,310.85 -	1,310.85	391.06	02/2015 -	02/2015	0(O) -	0/14
227	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL, Multi State	06/2012	1,263.26 -	1,263.26	224.31	11/2014 -	11/2014	0(O) -	0/16
228	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL, Chhatisgarh	01/2012	1,422.85 -	1,422.85	351.54	01/2015 -	01/2015	0(O) -	3/19
229	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, Multi State	12/2011	297.33 -	297.33	116.91	08/2014 -	08/2014	0(O) -	7/20
230	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, Multi State	10/2011	487.49 -	487.49	181.21	06/2014 -	06/2014	0(O) -	7/20
231	System Strengthening -XII of SR - [N18000085]PGCIL, Multi State	02/2010	232.34 -	232.34	150.53	06/2012 -	09/2013	15(O) -	0/3
232	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL, Multi State	12/2009	1,216.83 -	1,216.83	895.00	08/2012 -	06/2014	22(O) -	0/11
233	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttarakhand	11/2006	2,978.48 -	2,978.48	1,857.00	03/2013 -	03/2016	36(O) -	2/15
234	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38 -	1,501.75	1,156.83	09/2009 06/2013	11/2014	62(O) 17(R)	0/0
235	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	497.79	07/2010 02/2016	02/2017	79(O) 12(R)	1/10

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
236	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	105.28	01/2014 -	01/2014	0(O) -	3/18
237	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	411.38	08/2014 -	08/2014	0(O) -	2/19
238	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	823.01	10/2014 -	10/2014	0(O) -	2/18
239	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,467.53	10/2012 -	06/2014	20(O) -	0/11
240	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	387.19	01/2015 -	01/2015	0(O) -	0/20
241	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,718.22	03/2014 -	03/2014	0(O) -	4/15
242	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	40.34	08/2014 -	08/2014	0(O) -	7/20
243	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	357.08	10/2014 -	10/2014	0(O) -	3/16
244	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	775.25	644.73	01/2010 -	07/2013	42(O) -	2/11
245	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	156.80	11/2011 -	09/2013	22(O) -	0/4
246	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,540.95	12/2012 -	12/2013	12(O) -	0/9
247	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	305.43	02/2014 -	02/2014	0(O) -	3/17
248	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	309.32	10/2013 -	10/2013	0(O) -	2/13
249	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	131.55	07/2013 -	12/2013	5(O) -	0/13
250	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	722.79	12/2013 -	12/2013	0(O) -	2/13
251	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	151.90	11/2013 -	09/2014	10(O) -	7/20
252	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,113.89	03/2013 -	03/2014	12(O) -	4/15
253	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,646.55	12/2013 -	03/2014	3(O) -	0/13
254	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,593.11	11/2012 -	03/2015	28(O) -	0/15
255	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	976.32	07/2014 -	07/2014	0(O) -	2/14
256	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	609.36	-	07/2013	-	10/29
257	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	442.17	07/2014 -	02/2015	7(O) -	1/16
258	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,326.81	12/2012 -	06/2014	18(O) -	0/11

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
259	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	950.74	11/2013 -	12/2014	13(O) -	5/16
260	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.74	01/2013 -	12/2014	23(O) -	5/18
261	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,762.78	11/2009 02/2013	10/2013	47(O) 8(R)	0/4
262	VINDHYACHAL STTP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	368.00	08/2015 -	08/2015	0(O) -	11/12
263	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
264	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	358.03	07/2014 -	05/2016	22(O) -	1/1
265	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	444.80	09/2010 -	-	-	0/5
266	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	750.21	06/2015 -	06/2015	0(O) -	3/28
	Total		251,918.93 -	270,310.17	122,996.17				325/1401
	<u>Railways</u>								
267	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	182.06	0.75	- -	-	-	0/0
268	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	488.37	03/2014 -	12/2015	21(O) -	0/0
269	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	392.93	12/2009 03/2011	10/2013	46(O) 31(R)	0/0
270	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,820.00	123.56	- -	-	-	0/0
271	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	408.87	03/2011 03/2011	03/2011	-	0/0
272	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	725.00	557.32	06/1999 03/2011	03/2011	-	0/0
273	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	307.00	-	- -	-	-	0/0
274	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	1,566.00	119.70	- -	-	-	0/0
275	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	199.75	30.57	- -	-	-	0/0
276	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	252.00	-	- -	-	-	0/0
277	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	567.18	0.17	- -	-	-	0/0
278	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	1,215.30	30.68	03/2013 -	03/2013	-	0/0
279	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	251.99	16.28	- -	-	-	0/0
280	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	822.00	-	- -	-	-	0/0
281	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	242.09	-	- -	-	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
282	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12 -	312.12	28.94	- -	-	-	0/0
283	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
284	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
285	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	527.00	2.73	- -	-	-	0/0
286	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.42	- -	-	-	0/0
287	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	477.57	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
288	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	225.41	12/2010 03/2011	03/2011	-	0/0
289	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	244.66	03/2004 12/2010	12/2014	129(O) 48(R)	0/0
290	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	91.38	04/2014 -	03/2017	35(O) -	0/0
291	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	195.64	67.64	- -	-	-	0/0
292	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015	69(O) -	0/0
293	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,798.00	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
294	Bandel-Boinchi 3rd line - [N22000221]ER,Multi State	04/2011	288.35 -	288.35	3.92	- -	-	-	0/0
295	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	176.62	12/2012 -	12/2013	12(O) -	0/0
296	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	246.08	-	- -	-	-	0/0
297	Bariaipuri-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State	04/2007	450.55 -	450.55	9.16	- -	-	-	0/0
298	Bhadutola-Jhargram via Lalgath (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	289.64	0.04	- -	-	-	0/0
299	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	192.39	03/2011 -	-	-	0/0
300	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	485.65	1.76	03/2012 -	-	-	0/0
301	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	326.20	1.67	- -	-	-	0/0
302	Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State	04/2011	175.80 -	175.80	0.82	- -	-	-	0/0
303	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	267.37	33.58	- -	-	-	0/0
304	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
305	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	966.97	12/2012 01/2013	04/2013	-	0/0
306	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	295.00	0.06	- -	-	-	0/0
307	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
308	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
309	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	243.78	27.24	- -	-	-	0/0
310	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	350.55	- -	12/2013	-	0/0
311	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	177.38	36.46	03/2015 -	03/2015	0(O) -	0/0
312	Chandpara-Bangaon doubling with extension to Chandbazar & new - [N22000242]ER,Multi State	04/2003	337.96 -	337.96	58.74	- -	-	-	0/0
313	Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	951.24	504.64	- -	-	-	0/0
314	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	191.72	80.62	- -	-	-	0/0
315	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	520.00	457.75	- -	-	-	0/0
316	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	1,200.00	1.62	- -	-	-	0/0
317	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	378.56	104.54	- -	-	-	0/0
318	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER,Multi State	04/2005	595.91 -	595.91	88.57	- -	-	-	0/0
319	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	1,347.26	136.46	- -	-	-	0/0
320	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
321	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,151.00	944.66	03/2007 -	03/2015	96(O) -	0/0
322	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	556.64	266.21	- -	-	-	0/0
323	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	126.84	12/2012 -	-	-	0/0
324	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	102.28	- -	-	-	0/0
325	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	221.69	- -	03/2014	- -	0/0
326	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	496.64	12/2012 12/2012	02/2013	-	0/0
327	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	914.98	653.96	- -	12/2012	-	0/0
328	Dahod-Indore via Sardarpur, Jhabua & Dhar - [N22000139]WR,Multi State	04/2007	1,640.04 -	1,640.04	150.57	- -	-	-	0/0
329	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	99.25	12/2011 02/2012	02/2012	-	0/0
330	Dangoaposi-Rajkharwan 3rd line Doubling - [N22000164]SER,Jharkhand	04/2010	309.44 -	388.67	39.53	12/2015 -	12/2015	0(O) -	0/0
331	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER,Multi State	04/2010	296.44 -	296.44	2.80	- -	-	-	0/0
332	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	366.73	3.67	- -	-	-	0/0
333	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	376.59	0.17	- -	-	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
334	Dholpur-Sirmuttra with extension to Gangapurcity & Mohari-Ta - [N22000158]NCR,Multi State	04/2010	622.41 -	2,030.50	1.20	02/2019 -	02/2019	0(O) -	0/0
335	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	651.17	7.07	- -	-	-	0/0
336	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
337	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
338	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
339	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	230.03	12/2008 -	09/2014	69(O) -	0/0
340	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	248.49	06/2013 06/2013	12/2014	18(O) 18(R)	0/0
341	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	189.24	1.88	- -	-	-	0/0
342	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	603.22	1.31	- -	-	-	0/0
343	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240(O) -	0/0
344	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	279.16	02/2011 02/2011	03/2013	-	0/0
345	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	280.00	127.13	02/2006 -	-	-	0/0
346	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	719.19	- -	03/2012	-	0/0
347	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
348	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	832.00	343.53	- 05/2009	05/2009	-	0/0
349	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL,(NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	578.57	03/1994 -	10/2013	235(O) -	0/0
350	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	415.67	12.91	- -	-	-	0/0
351	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	445.25	0.94	- -	-	-	0/0
352	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	128.61	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
353	Guriya-Marwar & Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	274.34	2.50	- -	-	-	0/0
354	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State	04/2011	1,176.09 -	3,845.60	1.52	02/2020 -	02/2020	0(O) -	0/0
355	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	189.04	- -	-	-	0/0
356	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	1,185.64	195.65	- 09/2009	-	-	0/0
357	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
358	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	412.91	672.78	- -	01/2013	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
359	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	149.24	- -	03/2014	- -	0/0
360	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.01	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
361	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	101.17	- -	-	-	0/0
362	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State	04/2000	157.17 -	157.17	75.78	- -	-	-	0/0
363	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	213.01	-	- -	-	-	0/0
364	Hansdiha-Godda NL - [N22000236]ER,Multi State	04/2011	267.09 -	267.09	0.10	- -	-	-	0/0
365	Hansnabad-Hingalgaon New BG line - [N22000218]ER,Multi State	04/2010	172.03 -	172.03	2.27	- -	-	-	0/0
366	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	27.24	03/2015 -	03/2015	0(O) -	0/0
367	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State	04/2010	157.94 -	157.94	37.46	- -	-	-	0/0
368	Howrah-Development of station including segregation of aariv - [N22000249]ER,Multi State	04/2011	166.89 -	166.89	-	- -	-	-	0/0
369	Hyderabad/Secunderabad Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP,Andhra Pradesh	04/2012	632.68 -	816.55	0.36	04/2012 -	-	-	0/0
370	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	836.10	06/2007 -	06/2007	-	0/0
371	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	709.54	03/2012 08/2012	-	-	0/0
372	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	693.39	469.21	03/2012 03/2012	12/2012	-	0/0
373	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,529.74	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
374	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	245.66	03/2014 -	03/2014	0(O) -	0/0
375	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar	04/2009	470.00 -	470.00	34.32	- -	-	-	0/0
376	KADUR-CHIKMAGALUR-SAKLISHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	308.25	03/2012 03/2012	03/2013	-	0/0
377	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,475.25	- -	03/2013	-	0/0
378	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	643.00	-	- -	-	-	0/0
379	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	744.71	513.75	- -	03/2014	- -	1/1
380	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	775.36	758.00	- -	10/2012	-	0/0
381	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	743.88	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
382	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	121.33	- -	-	-	0/0
383	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65(O) 65(R)	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
384	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	259.43	- -	03/2014	- -	0/0
385	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
386	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	488.66	- 03/2010	03/2010	-	0/0
387	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,580.66	07/2005 -	-	-	0/0
388	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	161.85	- -	-	-	0/0
389	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	288.78	03/2012 03/2013	03/2013	-	0/0
390	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
391	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	354.49	- -	12/2012	-	0/0
392	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER,Multi State	04/2001	923.52 -	923.52	231.21	- -	-	-	0/0
393	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER,Multi State	04/2010	174.56 -	174.56	44.71	- -	-	-	0/0
394	Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra	04/2011	277.70 -	277.70	1.64	- -	-	-	0/0
395	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	124.52	12/2012 -	03/2015	27(O) -	0/0
396	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State	04/2010	423.66 -	423.66	130.65	03/2017 -	03/2017	0(O) -	0/0
397	Krishnanagar-Bethua Dahri doubling - [N22000226]ER,Multi State	04/2009	151.65 -	151.65	-	03/2015 -	03/2015	0(O) -	0/0
398	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
399	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
400	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	270.14	6.69	- -	-	-	0/0
401	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	388.03	05/2008 03/2011	-	-	0/0
402	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	226.51	03/2002 -	09/2013	138(O) -	0/0
403	Lakshmikantapur-Namkhana subsequently MM for Namkhana-Chandr - [N22000216]ER,Multi State	04/1999	406.99 -	406.99	137.68	- -	-	-	0/0
404	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244]ER,Multi State	04/2009	257.42 -	257.42	32.29	03/2014 -	03/2014	0(O) -	0/0
405	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam	04/2012	246.07 -	246.07	0.11	- -	-	-	0/0
406	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,604.73	03/2009 -	03/2014	60(O) -	0/0
407	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.33	07/2008 -	07/2008	-	0/0
408	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	472.00	177.85	- -	02/2013	-	0/0
409	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	717.63	12/2011 12/2011	03/2013	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
410	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0
411	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	434.81	03/2012 03/2013	03/2013	-	0/0
412	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	1,383.45	335.09	- -	-	-	0/0
413	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,209.40	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
414	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	243.54	- -	03/2012	-	0/0
415	Madurai-Bodinayakkanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	260.72	10.20	- -	-	-	0/0
416	Madurai-Rameswaram-GC - [N22000200]SR,Tamil Nadu	04/1999	240.00 -	441.69	367.01	- -	-	-	0/0
417	Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State	04/2011	601.43 -	800.00	0.13	- -	-	-	0/0
418	Magrahat-Diamond Harbour with MM Sangrampur-Krishnachandpur - [N22000243]ER,Multi State	04/2009	493.96 -	493.96	114.81	- -	-	-	0/0
419	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20 -	258.20	-	- -	03/2016	- -	0/0
420	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittisgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	567.23	557.12	- -	-	-	0/0
421	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	439.88	0.63	- -	-	-	0/0
422	Motihari-Sitamrhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
423	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	165.82	0.25	- -	-	-	0/0
424	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	281.30	0.49	- -	-	-	0/0
425	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	228.05	0.13	- -	-	-	0/0
426	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	656.92	02/2009 -	03/2012	-	0/0
427	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	357.74	07/2012 -	-	-	0/0
428	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	40.88	- -	-	-	0/0
429	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	139.81	- -	03/2015	- -	0/0
430	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,473.98	12/2008 -	03/2015	75(O) -	0/0
431	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	169.82	31.40	- -	-	-	0/0
432	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	620.57	-	- -	-	-	0/0
433	New Alipur to Akra, MM for Budge Budge-Pujali NL, Pujali-Ulu - [N22000240]ER,Multi State	04/2010	494.54 -	494.54	31.92	- -	-	-	0/0
434	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.40	- -	03/2015	- -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
435	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	242.22	39.04	- -	-	-	0/0
436	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	4,083.02	2.57	- -	-	-	0/0
437	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	175.43	145.19	- -	03/2014	-	0/0
438	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	238.83	98.33	- -	-	-	0/0
439	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	221.47	21.40	- -	-	-	0/0
440	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
441	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	209.77	18.76	- -	03/2015	-	0/0
442	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	283.55	0.40	- -	03/2015	-	0/0
443	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line & - [N22000209]NEFR,Multi State	04/1999	523.17 -	1,393.44	1,032.44	- -	-	-	0/0
444	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,446.81	8.94	03/2015 -	03/2017	24(O) -	0/0
445	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,913.51	314.60	03/2016 -	03/2016	0(O) -	0/0
446	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	24.59	03/2014 -	03/2016	24(O) -	0/0
447	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	173.31	03/2016 -	03/2016	0(O) -	0/0
448	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	50.61	03/2016 -	06/2016	3(O) -	0/0
449	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	437.69	03/2008 06/2008	-	-	0/0
450	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,828.20	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
451	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	618.81	- -	03/2012	-	0/0
452	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
453	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	139.10	12/2010 12/2010	12/2010	-	0/0
454	Pirpainti-Bhagalpur - [N22000222]ER,Multi State	04/2011	261.38 -	261.38	13.99	- -	-	-	0/0
455	Pirpainti-Jasidih - [N22000219]ER,Multi State	04/2013	915.98 -	915.98	-	- -	-	-	0/0
456	Plassey-Jiaganj Doubling - [N22000220]ER,Multi State	04/2011	248.07 -	248.07	8.13	03/2015 -	03/2015	0(O) -	0/0
457	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER,Multi State	04/2011	299.60 -	299.60	1.09	03/2017 -	03/2017	0(O) -	0/0
458	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	323.00	-	- -	-	-	0/0
459	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.92	812.76	- -	03/2013	-	0/6
460	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	289.93	257.91	12/2007 03/2010	-	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
461	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,104.99	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
462	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
463	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.90	227.27	- -	-	-	0/0
464	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.00	329.21	06/2004 -	12/2012	-	0/0
465	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	3,000.00	2,121.06	- -	03/2014	- -	0/0
466	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	639.97	175.75	03/1998 08/2005	08/2005	-	0/0
467	Rajkot-Veraval,Wansjalia to Jataisar with new MM for Shapur - [N22000143]WR,Gujarat	04/1994	320.66 -	320.66	-	- -	-	-	0/0
468	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	486.44	03/2013 -	03/2014	12(O) -	0/0
469	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	288.97	-	- -	-	-	0/0
470	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner & Ratangarh-De - [N22000153]NWR,Rajasthan	04/2010	739.65 -	695.00	788.75	- -	-	-	0/0
471	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	2,082.75	9.54	- -	-	-	0/0
472	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	249.55	03/2012 -	-	-	0/0
473	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	714.10	2.42	- 12/2017	-	-	0/0
474	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	233.73	03/2010 -	-	-	0/0
475	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15(O) -	0/0
476	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	818.29	84.10	02/2015 -	02/2015	0(O) -	0/0
477	Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State	04/2011	193.44 -	193.44	10.40	- -	-	-	0/0
478	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	325.00	229.07	- -	-	-	0/0
479	Sakri-Nirmali & Jhanjharpur-Laukahabazar & Saharsa-Forbesgan - [N22000180]ECR,Bihar	04/2004	372.14 -	355.81	352.65	- -	-	-	0/0
480	Santoshpur-Remount Road via Garden Reach-Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	268.52	77.34	- -	-	-	0/0
481	Sitamrhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	678.62	14.17	- -	-	-	0/0
482	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State	04/2000	297.47 -	297.47	51.70	- -	-	-	0/0
483	Sondalia-Champapukur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State	04/2010	277.28 -	277.28	32.99	- -	-	-	0/0
484	Sriperumbudur-Guduvanchery with spur to Irungattukottai-Ava - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	839.00	-	- -	-	-	0/0
485	Sultanganj-Katuria via Asarganj, Tarapur & Belhar - [N22000217]ER,Multi State	04/2007	450.00 -	450.00	7.61	- -	-	-	0/0
486	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	388.06	03/2014 -	03/2014	0(O) -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
487	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	127.07	- -	-	-	0/0
488	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	445.45	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
489	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	632.20	- 12/2009	02/2012	-	0/0
490	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	187.48	- -	-	-	0/0
491	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	57.93	- -	-	-	0/0
492	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	800.00	549.73	- -	-	-	0/0
493	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,440.96	12/2006 08/2010	08/2010	-	0/0
494	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	171.02	76.58	06/2013 -	-	-	0/0
495	Tarakeshwar-Magra New BG line - [N22000235]ER,Multi State	04/2010	365.17 -	365.17	1.39	- -	-	-	0/0
496	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.39 -	236.39	-	- -	-	-	0/0
497	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	47.10	03/2012 -	02/2013	-	0/0
498	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201(O) -	0/0
499	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	1,116.53	216.92	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
500	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	642.18	03/2014 -	03/2014	0(O) -	0/0
501	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	589.43	199.37	- 03/2010	-	-	0/0
502	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
503	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	685.17	11.51	- -	-	-	0/0
504	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	279.40	85.57	- -	04/2014	- -	0/0
505	Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra	04/2008	697.00 -	1,604.00	16.10	- -	-	-	0/0
506	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	297.85	0.98	- -	-	-	0/0
	Total		121,907.58 -	227,295.52	72,903.41				1/7
	<u>Road Transport & Highways</u>								
507	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	250.50	131.37	10/2014 -	10/2014	0(O) -	0/0
508	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	373.47	38.90	07/2014 -	07/2014	0(O) -	0/0
509	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	393.14	05/2013 -	03/2014	10(O) -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
510	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	626.59	11/2013 -	11/2013	0(O) -	0/0
511	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	624.00	243.51	04/2014 -	04/2014	0(O) -	0/0
512	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,Madhya pradesh	10/2011	1,565.00 -	1,565.00	-	10/2014 -	10/2014	0(O) -	0/0
513	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
514	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	81.70	01/2014 -	01/2014	0(O) -	0/0
515	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	288.77	02/2014 -	02/2014	0(O) -	0/0
516	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	525.57	02/2014 -	04/2014	2(O) -	0/0
517	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	174.37	04/2014 -	04/2014	0(O) -	0/0
518	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	161.02	05/2014 -	05/2014	0(O) -	0/0
519	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,Gujarat	03/2012	828.00 -	828.00	463.63	09/2014 -	09/2014	0(O) -	0/0
520	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,731.30	08/2014 -	07/2015	11(O) -	0/0
521	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,341.40	06/2013 -	09/2013	3(O) -	0/0
522	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.15	09/2013 -	07/2014	10(O) -	0/0
523	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	817.69	08/2013 -	08/2013	0(O) -	0/0
524	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.21	07/2013 -	12/2013	5(O) -	0/0
525	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	398.00	435.68	02/2014 -	02/2014	0(O) -	0/0
526	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,172.60	08/2013 -	08/2013	0(O) -	0/0
527	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,198.20	08/2013 -	08/2013	0(O) -	0/0
528	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	257.54	08/2013 -	08/2013	0(O) -	0/0
529	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	1,396.18	1,005.50	09/2014 -	09/2014	0(O) -	0/0
530	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	233.02	09/2007 -	03/2014	78(O) -	0/0
531	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	2,125.24	30.80	12/2015 -	12/2015	0(O) -	0/0
532	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,123.30	11/2012 -	12/2013	13(O) -	0/0
533	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.53	01/2009 -	12/2013	59(O) -	0/0
534	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
535	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	06/2013	-	0/0
536	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	346.82	09/2013 -	09/2013	0(O) -	0/0
537	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	2,388.00	1,255.70	06/2014 -	06/2014	0(O) -	0/0
538	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	558.91	-	10/2013	-	2/2
539	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9(O) -	0/0
540	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	505.64	08/2013 -	08/2013	0(O) -	0/0
541	BIJNI TO ASSAM WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	285.21	06/2008 -	03/2014	69(O) -	0/0
542	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	247.36	06/2008 -	03/2014	69(O) -	0/0
543	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	238.88	06/2005 -	03/2014	105(O) -	0/0
544	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	284.89	04/2010 -	11/2014	55(O) -	0/0
545	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53(O) -	0/0
546	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	811.61	03/2013 -	12/2013	9(O) -	0/0
547	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	559.73	-	12/2013	-	0/1
548	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	09/2013	4(O) -	0/0
549	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	410.02	10/2011 -	03/2014	29(O) -	0/0
550	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	814.19	10/2011 -	06/2014	32(O) -	0/0
551	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68(O) -	0/0
552	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	1,928.22	302.56	04/2015 -	04/2015	0(O) -	0/0
553	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	652.98	05/2010 -	10/2013	41(O) -	0/0
554	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	550.72	07/2013 -	10/2013	3(O) -	0/0
555	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6(O) -	0/0
556	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	708.02	-	09/2013	-	1/1
557	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	252.67	06/2008 -	12/2013	66(O) -	0/0
558	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	206.40	05/2008 -	12/2013	67(O) -	0/0
559	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	302.85	09/2010 -	08/2014	47(O) -	0/0
560	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	315.83	08/2013 -	02/2015	18(O) -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
561	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	1,573.00	13.50	09/2015 -	09/2015	0(O) -	0/0
562	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	461.55	09/2008 -	12/2013	63(O) -	0/0
563	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	1,232.00	148.12	08/2015 -	08/2015	0(O) -	0/0
564	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	118.72	10/2013 -	11/2015	25(O) -	0/0
565	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30(O) -	0/0
566	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	142.58	09/2008 -	03/2014	66(O) -	0/0
567	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.26	02/2004 -	06/2013	-	0/0
568	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,260.10	08/2013 -	08/2013	0(O) -	0/0
569	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	265.28	04/2008 -	03/2014	71(O) -	0/0
570	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	204.62	04/2008 -	03/2014	71(O) -	0/0
571	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	06/2013	-	0/0
572	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.37	12/2009 -	12/2014	60(O) -	0/0
573	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,024.30	09/2012 -	12/2013	15(O) -	0/0
574	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,838.80	10/2011 -	12/2013	26(O) -	0/0
575	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.24	09/2007 -	11/2013	74(O) -	0/0
576	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	318.28	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
577	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	150.29	07/2009 -	05/2014	58(O) -	0/0
578	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	67.44	09/2007 -	04/2014	79(O) -	0/0
579	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	259.70	10/2013 -	03/2014	5(O) -	0/0
580	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	195.15	08/2004 -	08/2013	108(O) -	0/0
581	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	195.52	08/2004 07/2010	08/2013	108(O) 37(R)	0/0
582	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	947.24	01/2013 -	10/2013	9(O) -	0/0
583	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,721.50	- -	10/2013	- -	3/3
584	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	507.47	05/2013 -	02/2014	9(O) -	0/0
585	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	12/2013	8(O) -	0/0
586	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	645.56	02/2013 -	09/2013	7(O) -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
587	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11(O) -	0/0
588	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.19	09/2009 -	12/2013	51(O) -	0/0
589	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	536.00	511.33	01/2014 -	01/2014	0(O) -	0/0
590	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,968.50	12/2012 -	08/2013	8(O) -	0/0
591	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.92	10/2008 -	09/2013	59(O) -	0/0
592	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.91	10/2008 -	12/2013	62(O) -	0/0
593	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	702.16	463.54	07/2014 -	07/2014	0(O) -	0/0
594	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	925.49	-	06/2014	-	2/3
595	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,126.80	05/2012 -	09/2013	16(O) -	0/0
596	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.51	06/2010 -	12/2013	42(O) -	0/0
597	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60(O) -	0/0
598	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	181.53	07/2012 -	07/2014	24(O) -	0/0
599	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	119.93	11/2008 -	06/2014	67(O) -	0/0
600	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	90.10	04/2009 -	12/2014	68(O) -	0/0
601	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	59.83	11/2008 -	12/2014	73(O) -	0/0
602	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	159.85	04/2009 -	12/2014	68(O) -	0/0
603	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,828.90	06/2013 -	03/2014	9(O) -	0/0
604	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	270.58	03/2013 -	03/2014	12(O) -	0/0
605	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
606	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	300.84	06/2008 -	12/2013	66(O) -	0/0
607	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63(O) -	0/0
608	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	484.19	282.58	10/2014 -	10/2014	0(O) -	0/0
609	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	302.87	04/2008 -	05/2014	73(O) -	0/0
610	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	262.59	06/2008 -	09/2013	63(O) -	0/0
611	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	285.56	06/2008 -	12/2013	66(O) -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
612	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
613	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	284.35	06/2011 06/2011	08/2013	26(O) 26(R)	0/2
614	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,128.20	02/2010 -	12/2014	58(O) -	0/0
615	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.55	01/2014 -	12/2014	11(O) -	0/0
616	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013	0(O) -	0/0
617	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.79	09/2014 -	10/2015	13(O) -	0/0
618	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	1,284.70	10/2014 -	10/2014	0(O) -	0/0
619	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	942.69	190.43	06/2014 -	06/2014	0(O) -	0/0
620	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	309.90	05/2008 -	09/2013	64(O) -	0/0
621	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	574.00	637.40	03/2014 -	03/2014	0(O) -	0/0
622	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.37	02/2013 -	10/2013	8(O) -	0/0
623	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,319.40	07/2012 -	08/2013	13(O) -	0/0
624	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.30	03/2013 -	04/2014	13(O) -	0/0
625	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	835.00	122.65	01/2014 -	01/2014	0(O) -	0/0
626	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	12/2013	25(O) -	0/0
627	Pune-sholapur,pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17(O) -	0/0
628	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	922.41	07/2015 -	06/2016	11(O) -	0/0
629	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	337.60	10/2008 -	03/2014	65(O) -	0/0
630	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	1,479.00	189.14	06/2015 -	06/2015	0(O) -	0/0
631	REENGUS SIKAR - [N24000227]NHAI,Rajasthan	03/2012	333.51 -	333.51	-	09/2014 -	09/2014	0(O) -	0/0
632	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	1,086.30	11/2013 -	11/2013	0(O) -	0/0
633	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31(O) -	0/0
634	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	612.91	03/2013 -	12/2013	9(O) -	0/0
635	SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39 -	805.39	543.70	12/2013 -	12/2013	0(O) -	0/0
636	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	909.00	941.91	05/2014 -	05/2014	0(O) -	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
637	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	239.49	09/2007 -	03/2014	78(O) -	0/0
638	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	191.25	07/2008 -	03/2013	-	0/0
639	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0
640	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013	0(O) -	0/0
641	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	1,535.00	1,162.30	05/2014 -	05/2014	0(O) -	0/0
642	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31(O) -	0/0
643	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0
644	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	08/2013	65(O) -	0/0
645	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013	-	0/0
646	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,700.30	08/2011 -	12/2013	28(O) -	0/0
647	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	09/2013	51(O) -	0/0
648	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	857.99	07/2010 -	03/2014	44(O) -	0/0
649	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	1,131.20	11/2013 -	11/2013	0(O) -	0/0
650	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	571.00	-	10/2013 -	10/2013	0(O) -	0/0
651	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	114.73	05/2013 -	12/2013	7(O) -	0/0
652	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	-	04/2013	-	2/2
653	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	864.87	03/2014 -	03/2014	0(O) -	0/0
654	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	193.10	197.57	03/2008 -	02/2008	-	0/0
655	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	53.97	11/2012 -	03/2014	16(O) -	0/0
656	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	651.32	07/2013 -	06/2014	11(O) -	0/0
657	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	201.93	06/2014 -	06/2014	0(O) -	0/0
	Total		103,915.59 -	105,854.21	81,038.79				10/14
	<u>Shipping & Ports</u>								
658	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 09/2011	09/2011	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
659	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	-	0/0
660	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
661	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	418.64	12/2012 10/2013	10/2013	10(O) 0(R)	0/0
662	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
663	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014	0(O) -	0/0
664	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-1(O) 0(R)	0/0
665	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	963.01	12/2010 09/2012	03/2014	39(O) 18(R)	0/0
666	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
667	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
668	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	08/2012	-	0/0
669	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
670	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	137.00	03/2006 12/2013	12/2013	93(O) 0(R)	0/0
671	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
672	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
673	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
674	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	832.04	10/2008 11/2010	-	-	0/0
675	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	19(O) 11(R)	0/0
676	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	17,902.42	8,607.77				0/1
	<u>Telecommunications</u>								
677	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59(O) -	0/0
678	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
679	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	67.20	02/2007 03/2012	02/2013	-	0/0
680	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	229.41	67.21	03/2012 02/2013	-	-	0/0

Sector Wise Details

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
681	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38(O) 21(R)	0/0
682	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	168.30	86.11	10/2007 -	-	-	0/0
683	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013	54(O) -	0/0
684	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
685	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34(O) 9(R)	0/0
686	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
687	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
688	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
689	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28(O) -	0/0
	Total		5,699.24 -	5,520.22	1,970.84				0/0
	<u>Urban Development</u>								
690	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,482.18	06/2011 -	03/2013	-	3/3
691	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
692	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	3,853.30	03/2016 -	03/2016	0(O) -	0/0
693	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	258.11	09/2014 -	05/2015	8(O) -	0/0
	Total		44,245.18 -	49,518.08	6,593.59				3/3
	<u>Water Resources</u>								
694	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		883,001.10	1,050,646.51	490,011.19				1094/3776

Sector wise current status of projects on the Flash Report

Urban Development


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

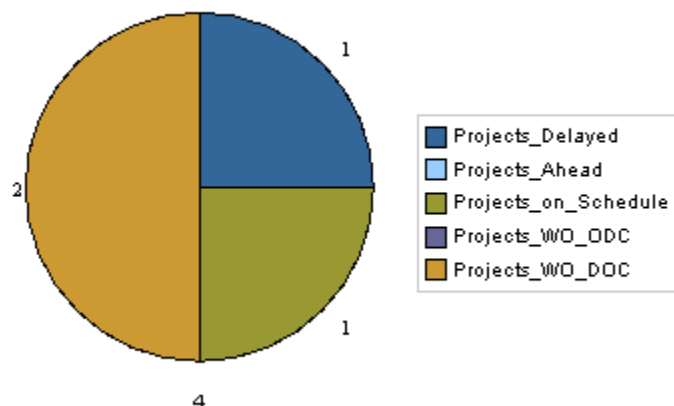

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till July, 2013 is Rs. 6593.59 crore, which is 13.3% of the revised cost of the projects.

Figures are in Rs. Crore

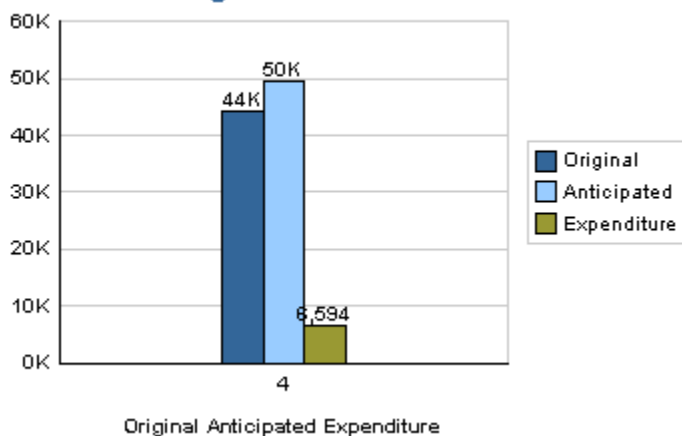

Sector wise current status of projects on the Flash Report

Telecommunications

Current Status:


Number of Projects **13**

Number of Projects Delayed **5**

Number of Projects Without Date Of Commissioning **8**

Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 5 projects are delayed .8 projects do not have fixed dates of commissioning.

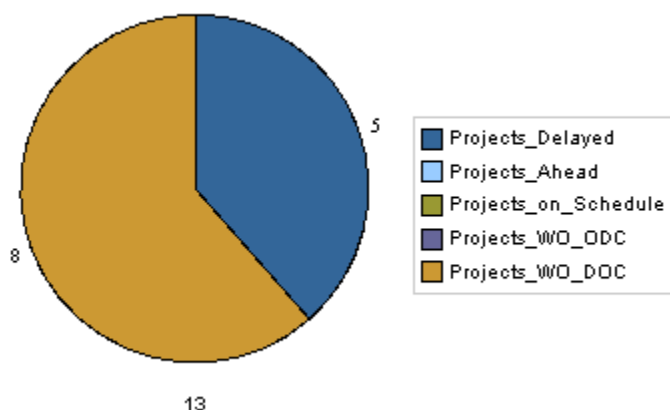

Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5699.24 crore but this was subsequently revised to Rs. 5520.22 crore implying a cost overrun of -3.1%. The expenditure incurred on these projects till July, 2013 is Rs. 1970.84 crore, which is 35.7% of the revised cost of the projects.

Figures are in Rs. Crore

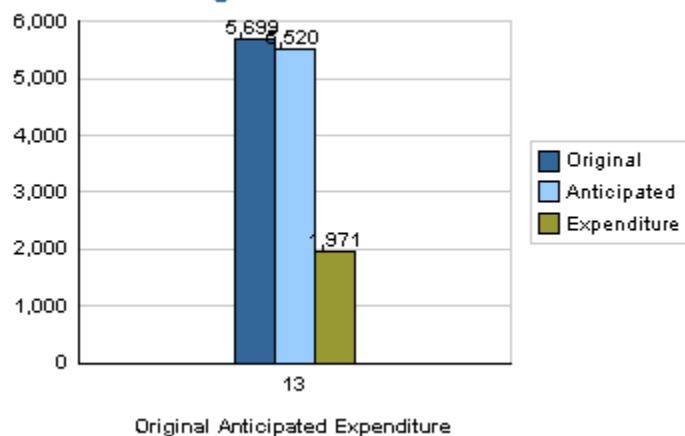

Sector wise current status of projects on the Flash Report


Shipping & Ports

Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	5
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	12

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 1 project are on schedule and 5 projects are delayed .12 projects do not have fixed dates of commissioning.

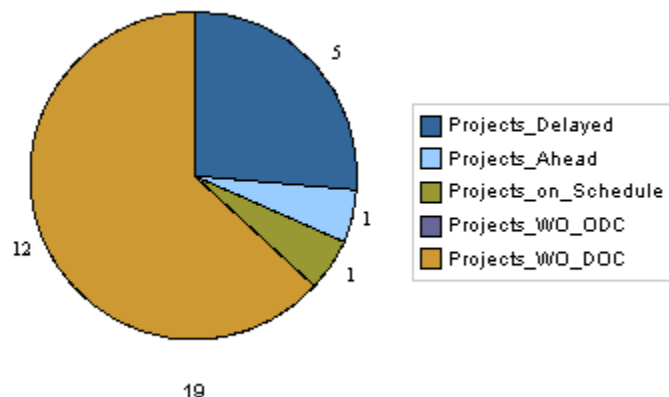

Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17902.42 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till July, 2013 is Rs. 8607.77 crore, which is 48.1% of the revised cost of the projects.

Figures are in Rs. Crore

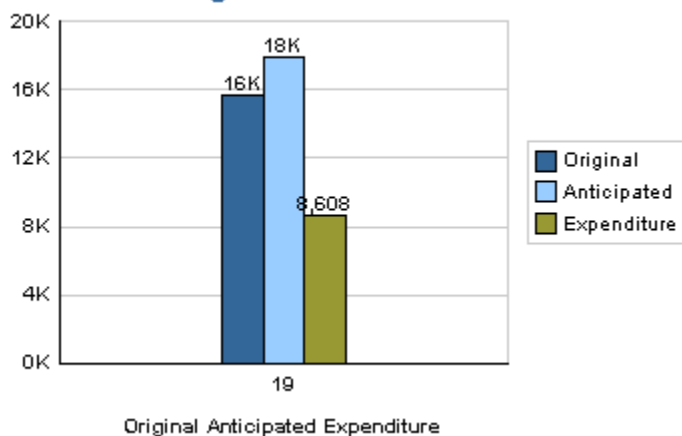

Sector wise current status of projects on the Flash Report

Road Transport & Highways


Current Status:

Number of Projects	151
Number of Projects On Schedule	47
Number of Projects Delayed	91

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	8

Brief Analysis


Project Status with respect to Original Schedule: Out of 151 projects, 47 projects are on schedule and 91 projects are delayed .8 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

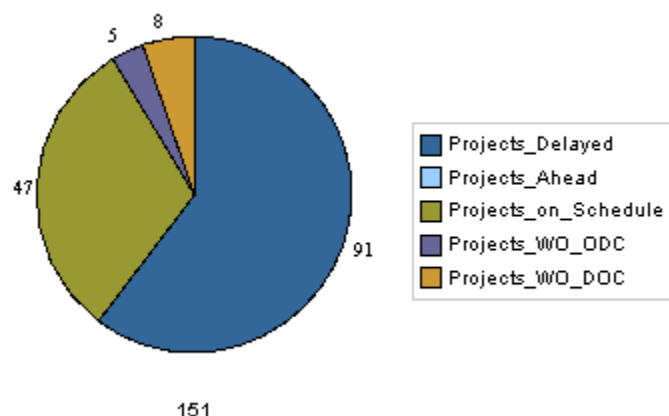

Investment Scenario

The Total Original cost of implementation of 151 projects when sanctioned, was of the order of Rs. 103915.59 crore but this was subsequently revised to Rs. 105854.21 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till July, 2013 is Rs. 81038.79 crore, which is 76.6% of the revised cost of the projects.

Figures are in Rs. Crore

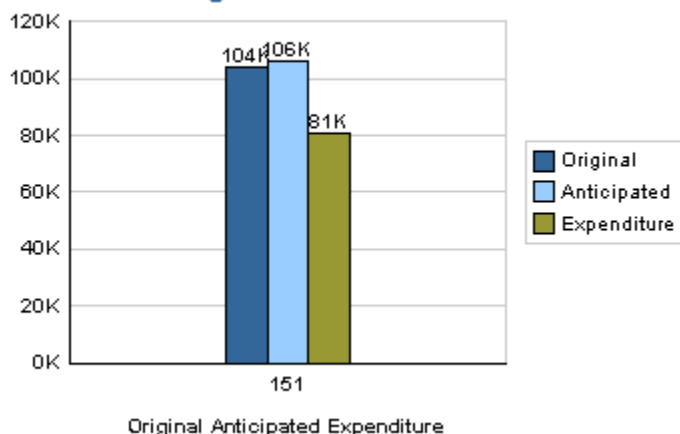

Sector wise current status of projects on the Flash Report

Railways


Current Status:

Number of Projects	240
Number of Projects On Schedule	11
Number of Projects Delayed	35

Number of Projects Without Original Date of Commissioning	16
Number of Projects Without Date Of Commissioning	178


Brief Analysis

Project Status with respect to Original Schedule: Out of 240 projects, 11 projects are on schedule and 35 projects are delayed .178 projects do not have fixed dates of commissioning.16 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

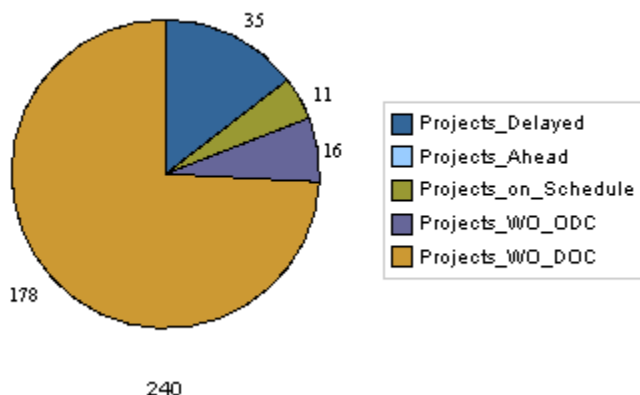

Investment Scenario

The Total Original cost of implementation of 240 projects when sanctioned, was of the order of Rs. 121907.58 crore but this was subsequently revised to Rs. 227295.52 crore implying a cost overrun of 86.4%. The expenditure incurred on these projects till July, 2013 is Rs. 72903.41 crore, which is 32.1% of the revised cost of the projects.

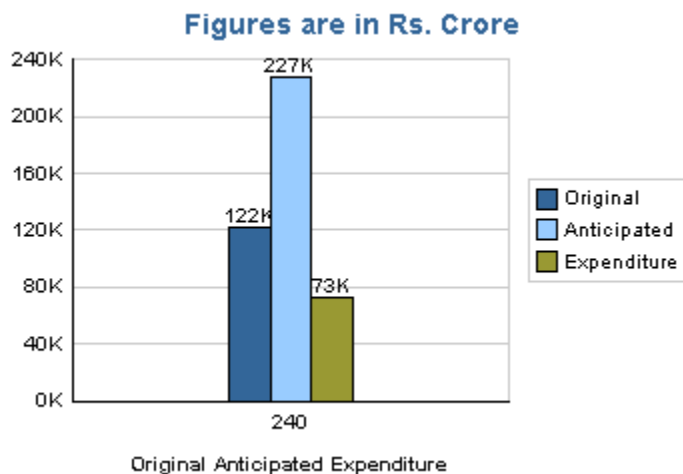

Sector wise current status of projects on the Flash Report


Power

Current Status:

Number of Projects	98
Number of Projects On Schedule	40
Number of Projects Delayed	50
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5

Brief Analysis


Project Status with respect to Original Schedule: Out of 98 projects, 2 projects are ahead of schedule, 40 projects are on schedule and 50 projects are delayed .5 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

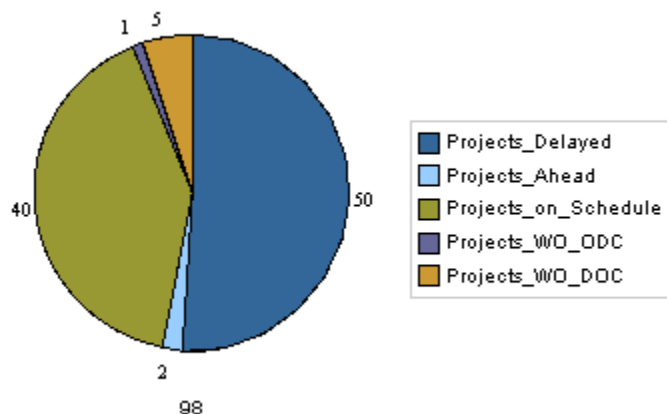

Investment Scenario

The Total Original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 251918.93 crore but this was subsequently revised to Rs. 270310.17 crore implying a cost overrun of 7.3%. The expenditure incurred on these projects till July, 2013 is Rs. 122996.17 crore, which is 45.5% of the revised cost of the projects.

Figures are in Rs. Crore

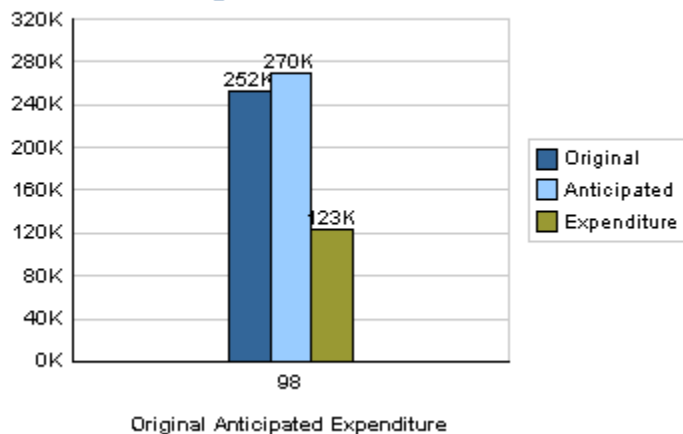

Sector wise current status of projects on the Flash Report

Petroleum


Current Status:

Number of Projects	82
Number of Projects On Schedule	19
Number of Projects Delayed	54

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8

Brief Analysis


Project Status with respect to Original Schedule: Out of 82 projects, 19 projects are on schedule and 54 projects are delayed .8 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

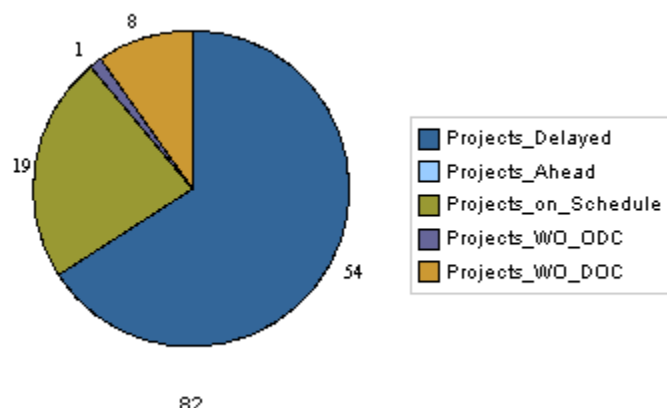

Investment Scenario

The Total Original cost of implementation of 82 projects when sanctioned, was of the order of Rs. 183464.22 crore but this was subsequently revised to Rs. 197793.04 crore implying a cost overrun of 7.8%. The expenditure incurred on these projects till July, 2013 is Rs. 92271.22 crore, which is 46.7% of the revised cost of the projects.

Figures are in Rs. Crore

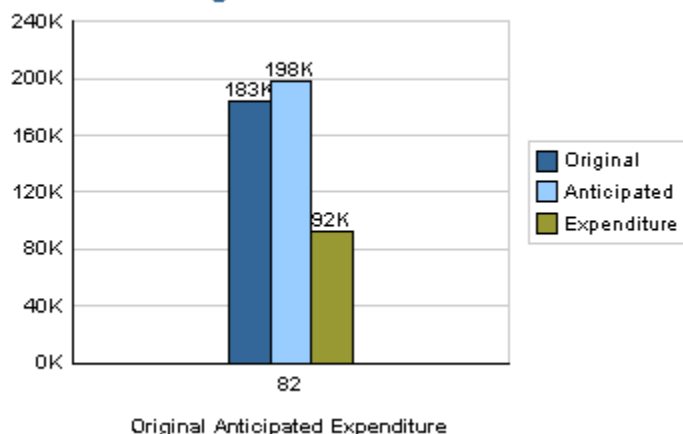

Sector wise current status of projects on the Flash Report

Steel


Current Status:

Number of Projects	18
Number of Projects On Schedule	3
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 18 projects, 3 projects are on schedule and 14 projects are delayed .1 project do not have fixed dates of commissioning.

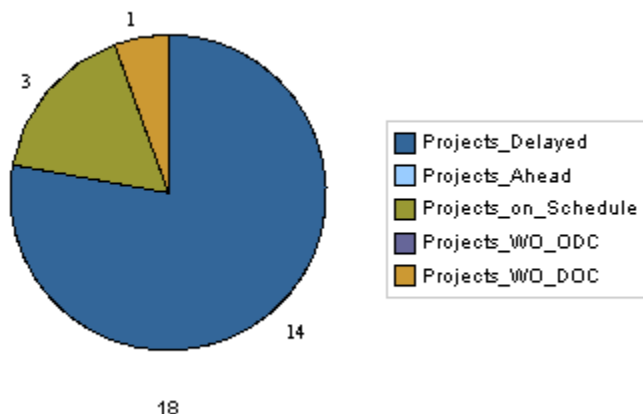

Investment Scenario

The Total Original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 65625.22 crore but this was subsequently revised to Rs. 71782.4 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till July, 2013 is Rs. 52362.23 crore, which is 72.9% of the revised cost of the projects.

Figures are in Rs. Crore

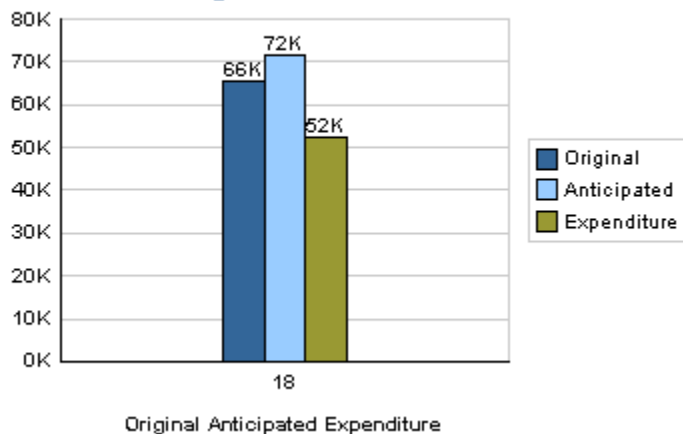

Sector wise current status of projects on the Flash Report

Coal


Current Status:

Number of Projects	55
Number of Projects On Schedule	22
Number of Projects Delayed	28

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 55 projects, 22 projects are on schedule and 28 projects are delayed .4 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

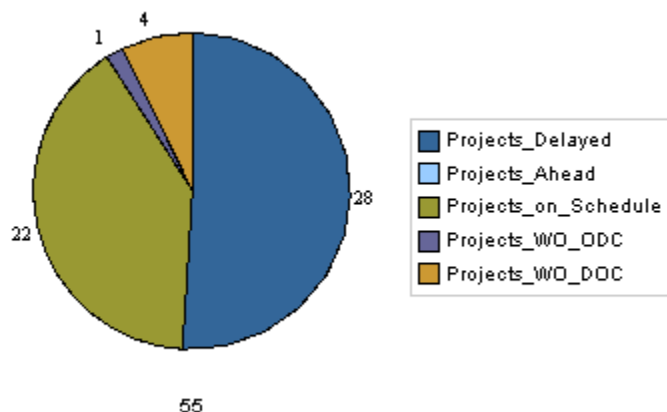

Investment Scenario

The Total Original cost of implementation of 55 projects when sanctioned, was of the order of Rs. 38127.05 crore but this was subsequently revised to Rs. 41212.5 crore implying a cost overrun of 8.1%. The expenditure incurred on these projects till July, 2013 is Rs. 15215.76 crore, which is 36.9% of the revised cost of the projects.

Figures are in Rs. Crore

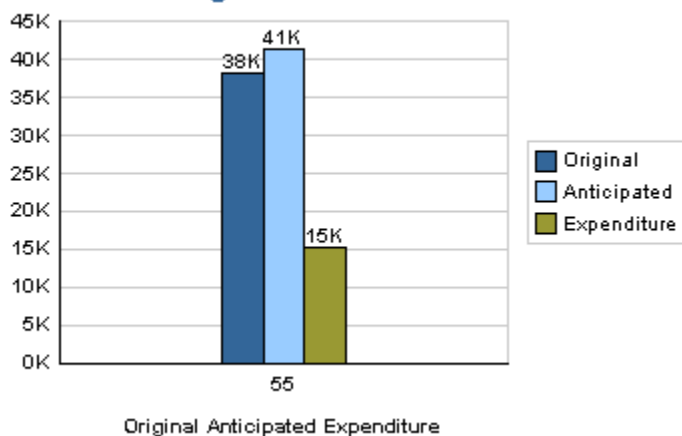

Sector wise current status of projects on the Flash Report

Civil Aviation


Current Status:

Number of Projects	8
Number of Projects On Schedule	3
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule and 2 projects are delayed .3 projects do not have fixed dates of commissioning.

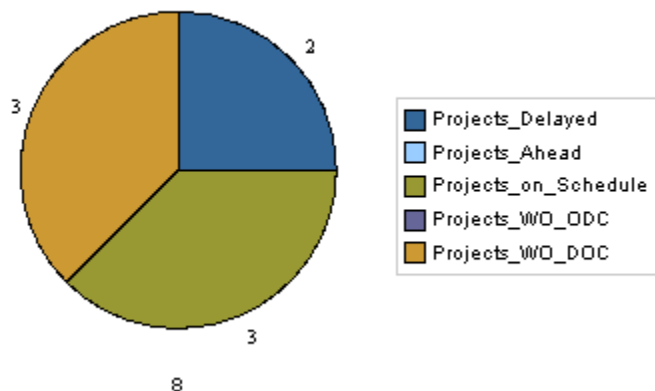

Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6624.95 crore implying a cost overrun of 9.8%. The expenditure incurred on these projects till July, 2013 is Rs. 5404.81 crore, which is 81.6% of the revised cost of the projects.

Figures are in Rs. Crore

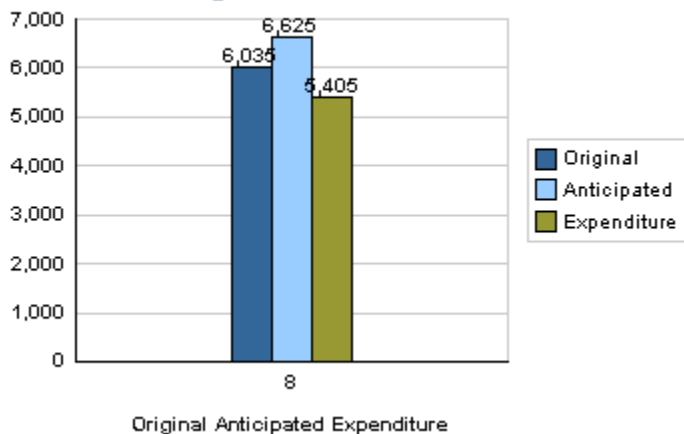

Sector wise current status of projects on the Flash Report


Atomic Energy

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

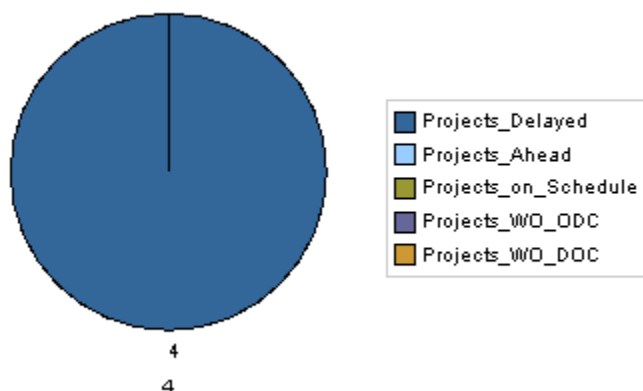

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till July, 2013 is Rs. 26100.6 crore, which is 55.9% of the revised cost of the projects.

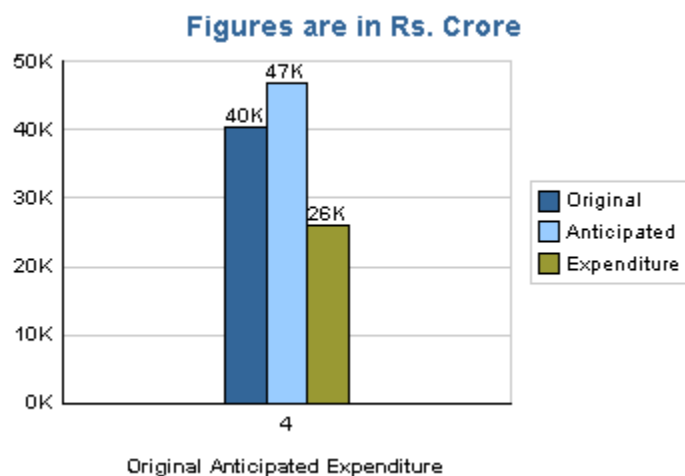

ANNEXURES

LIST OF CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	38	31729.81	39769.55	22118.18
2	Arunachal Pradesh	4	9512.22	17330.32	9732.18
3	Assam	41	24155.49	38430.19	25135.80
4	Bihar	46	32579.04	41019.11	27563.13
5	Chandigarh	1	452.00	452.00	117.24
6	Chhatisgarh	24	58278.32	59362.92	21488.81
7	Delhi	4	38214.41	38194.82	4245.82
8	Goa	1	335.61	335.61	228.60
9	Gujarat	34	38828.13	40180.04	13796.14
10	Haryana	8	4054.38	5736.96	7219.26
11	Himachal Pradesh	5	13355.57	17318.84	13622.55
12	Jammu and Kashmir	9	14305.70	33912.56	14164.19
13	Jharkhand	26	15873.15	20155.82	9671.45
14	Karnataka	27	47076.40	56530.71	24918.05
15	Kerala	10	21010.59	22804.14	6092.20
16	Madhya pradesh	22	31749.13	32157.30	8665.34
17	Maharashtra	55	95394.73	108795.37	49168.16
18	Manipur	1	727.56	4453.50	1529.74
19	Meghalaya	3	4845.02	4845.02	802.67
20	Mizoram	2	1532.97	3297.97	533.55
21	Multi State	158	177008.81	197813.37	82157.14
22	Nagaland	2	5124.00	6720.81	8.94
23	Odisha	31	56321.53	63614.31	40020.79
24	Punjab	4	1611.38	2553.15	3627.75
25	Rajasthan	25	25256.57	25208.59	10471.57
26	Sikkim	2	1648.94	3690.04	290.59
27	Tamil Nadu	41	52194.84	67422.67	44189.59
28	Tripura	5	2669.39	4021.10	2230.01
29	Uttar Pradesh	27	21281.92	25861.13	14238.11
30	Uttarakhand	5	7624.21	8887.28	2622.38
31	West Bengal	33	48249.28	59771.31	29341.26
TOTAL		694	883001.10	1050646.51	490011.19

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2003	3492.00	0.00	4681.60
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	08/2008	1942.51	0.00	2472.45
3	IOR LAKWA - LAKHMANI (ONGCL)	Petroleum	09/2001	345.10	663.69	729.07
4	IOR GELEKI (ONGCL)	Petroleum	09/2001	390.09	1674.11	1727.24
5	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	01/2009	756.00	898.00	913.72
6	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	Petroleum	07/2009	238.68	0.00	293.12
7	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	04/2008	825.00	0.00	1469.11
8	KOLDAM HEP (NTPC)	Power	10/2002	4527.15	0.00	5031.00
9	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	0.00	6317.03
10	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	1061.38	0.00	1156.83
11	URI H.E.P STAGE -II (NHPC)	Power	08/2005	1729.29	0.00	1762.78
12	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2006	611.01	0.00	752.82
13	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	Power	07/2006	557.24	0.00	644.73
14	RAMPUR HEP(412 MW)	Power	01/2007	2047.03	0.00	2607.63
15	TRIPURA GAS BASED POWER PROJECT	Power	07/2009	421.01	0.00	609.36
16	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	618.81
17	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8822.50
18	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	226.51
19	CALICUT-MANGALORE (DL) (SR)	Railways	02/1996	240.00	0.00	599.40
20	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	02/1997	295.00	412.91	672.78
21	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	Railways	04/1996	157.00	262.82	308.25
22	KARUR-SALEM(NL),SR	Railways	02/1997	155.55	155.00	758.00
23	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	03/1996	155.74	429.49	656.92
24	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	1500.00	2798.00
25	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	354.49
26	RANCHI-LOHARDAGA(GC),SER	Railways	04/1997	194.07	194.07	329.21
27	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	04/1997	233.00	501.69	709.54
28	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	07/1998	248.44	576.27	966.97
29	KATIHAR - JOGBANI (GC)(NEFR)	Railways	09/2001	100.00	492.98	743.88
30	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER)	Railways	04/1999	323.40	323.40	513.75
31	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	03/2002	409.00	625.30	836.10
32	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	09/1995	100.00	100.00	549.73
33	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	04/2000	733.00	733.00	1473.98
34	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	03/2000	907.69	3156.32	3440.96

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
35	GADWAL - RAICHUR (NL), SCR	Railways	04/1998	92.63	228.09	279.16
36	JIND-SONEPAT (NL),NR	Railways	01/2004	190.81	238.56	469.21
37	RAJATGARH-BARANG(LD),ECOR	Railways	04/1999	166.16	0.00	271.99
38	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	727.53	1529.74
39	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	01/2004	915.70	915.70	2121.06
40	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	04/2003	136.62	0.00	257.91
41	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	04/1996	114.01	332.92	434.81
42	BHOPAL BINA 3D LINE DOUBLING	Railways	09/2007	687.20	0.00	718.89
43	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	09/2006	343.17	343.17	653.96
44	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	12/2006	170.00	170.00	408.87
45	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	09/1996	156.00	156.00	350.55
46	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)	Railways	04/2007	482.00	482.70	486.44
47	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	1676.31	1676.31	3604.73
48	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur	Railways	04/2013	456.00	0.00	557.12
49	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner & Ratangarh-Degana GC)	Railways	04/2010	739.65	0.00	788.75
50	Sakri-Hasanpur Road (NL)	Railways	04/1999	175.69	0.00	229.07
51	Cuddalore-Salem via Vriddhachalam GC	Railways	04/1999	198.68	0.00	266.21
52	Chennai Beach-Tambaram-Chengalpattu Suburban GC	Railways	04/1999	271.24	0.00	457.75
53	Construction of NL from Kumarghat-Agartala	Railways	04/1999	895.00	0.00	944.66
54	Madurai-Rameswaram-GC	Railways	04/1999	240.00	0.00	367.01
55	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif	Railways	04/2007	247.00	0.00	504.64
56	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line & MM for Chalsa-Naxal& Rajabhatkhowa-Jaint	Railways	04/1999	523.17	0.00	1032.44
57	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport And Highways	12/2003	157.47	0.00	239.49
58	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport And Highways	03/2005	220.00	0.00	284.24
59	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Road Transport And Highways	12/2003	230.00	0.00	238.88
60	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	Road Transport And Highways	12/2003	166.27	0.00	197.57
61	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A	Road Transport And Highways	12/2003	284.00	0.00	309.90

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
62	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport And Highways	12/2003	240.00	0.00	294.91
63	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport And Highways	03/2005	190.00	0.00	264.53
64	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport And Highways	12/2003	280.00	0.00	318.28
65	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport And Highways	12/2003	195.00	0.00	247.36
66	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport And Highways	12/2003	237.80	0.00	285.21
67	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport And Highways	12/2003	332.94	0.00	461.55
68	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport And Highways	12/2003	275.00	0.00	279.92
69	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport And Highways	12/2003	251.03	0.00	337.60
70	NALBARI TO BIJNI (AS-8)	Road Transport And Highways	12/2003	200.00	0.00	285.56
71	GUWHATI TO NALBARI (AS-4)	Road Transport And Highways	12/2003	175.96	0.00	204.62
72	NAGAON TO DHARAMTUL (AS-2)	Road Transport And Highways	12/2003	264.72	0.00	300.84
73	SONAPUR TO GUWAHTI (AS-3)	Road Transport And Highways	12/2003	245.00	0.00	491.21
74	GUWAHATI TO NALBARI (AS-5)	Road Transport And Highways	12/2003	198.16	0.00	265.28
75	NALBARI TO BIJNI (AS-6)	Road Transport And Highways	12/2003	225.00	0.00	262.59
76	NALBARI T BIJNI (AS-7)	Road Transport And Highways	12/2003	208.00	0.00	302.87
77	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport And Highways	12/2003	160.00	0.00	206.40
78	DHARAMTUL TO SONAPUR (AS-19)	Road Transport And Highways	12/2003	200.00	0.00	252.67

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
79	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport And Highways	03/2005	168.00	0.00	457.30
80	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport And Highways	03/2005	280.00	0.00	581.49
81	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport And Highways	04/2000	263.27	0.00	276.26
82	BRAHMPUTRA BRIDGE,NH NO-31	Road Transport And Highways	12/2003	217.61	0.00	284.89
83	GWALIOR BYPASS, NH-75,3	Road Transport And Highways	12/2003	300.93	0.00	303.02
84	JHANSI TO LALITPUR, NH-25,26	Road Transport And Highways	12/2003	355.06	0.00	507.19
85	TRICHY - KORUR NH-67	Road Transport And Highways	03/2005	516.00	0.00	857.99
86	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport And Highways	03/2005	941.00	0.00	1901.00
87	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport And Highways	03/2005	557.00	0.00	1128.20
88	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport And Highways	12/2003	232.45	0.00	302.85
89	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport And Highways	04/2007	486.00	0.00	652.98
90	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport And Highways	03/2005	940.00	0.00	1319.40
91	Gujarat/Maharashtra Border Surat-Hazira Port Section	Road Transport And Highways	03/2010	1509.10	0.00	2024.30
92	Pune-sholapur, pkg1	Road Transport And Highways	11/2009	1110.00	0.00	1802.10
93	Kishangarh-Ajmer-Beawer	Road Transport And Highways	11/2009	795.00	0.00	1126.80
94	Chennai-Tada(Six lane)	Road Transport And Highways	04/2009	353.37	0.00	410.02
95	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport And Highways	04/2009	1673.70	0.00	2838.80

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
96	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport And Highways	02/2009	1693.75	0.00	2700.30
97	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport And Highways	05/2009	572.30	0.00	814.19
98	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport And Highways	05/2009	1108.00	0.00	3465.90
99	Jaipur-Tonk-Deoli	Road Transport And Highways	06/2010	792.06	0.00	1968.50
100	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport And Highways	09/2010	946.00	0.00	1721.50
101	Talegaon-amravati	Road Transport And Highways	11/2009	567.00	0.00	1131.20
102	Hazaribagh-Ranchi	Road Transport And Highways	08/2010	625.07	0.00	947.24
103	Armur to kadloor yellareddy	Road Transport And Highways	02/2010	390.56	0.00	772.40
104	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport And Highways	09/2010	671.00	0.00	925.49
105	AMRITSAR-PATHANKOT	Road Transport And Highways	05/2010	705.00	0.00	2123.30
106	PANIPAT-ROHTAK	Road Transport And Highways	04/2011	807.00	0.00	1284.70
107	DEVIHALLI-HASSAN	Road Transport And Highways	12/2010	453.00	0.00	708.02
108	MURADABAD-BAREILY	Road Transport And Highways	04/2010	1267.00	0.00	1828.90
109	BELGAUM-DHARWAD(NH-4)	Road Transport And Highways	12/2010	480.00	0.00	558.91
110	INDORE-DEWAS(NH-3)	Road Transport And Highways	11/2010	325.00	0.00	507.47
111	2 LANNING OF MOKAMA-MUNGER	Road Transport And Highways	05/2011	351.54	0.00	393.14
112	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport And Highways	12/2010	1008.50	0.00	1341.40

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
113	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	Road Transport And Highways	03/2011	785.50	0.00	817.69
114	ROHTAK-BAWAL	Road Transport And Highways	05/2011	650.00	0.00	1086.30
115	GHAZIABAD-ALIGARH NH-91	Road Transport And Highways	02/2011	1141.00	0.00	1260.10
116	2-LANNING OF SHILONG BYPASS	Road Transport And Highways	02/2011	226.00	0.00	288.77
117	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	Road Transport And Highways	09/2011	574.00	0.00	637.40
118	4-LANNING OF CHAPRA-HAJIPUR	Road Transport And Highways	01/2011	575.00	0.00	714.21
119	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport And Highways	05/2011	511.54	0.00	626.59
120	4-laning of Barhi-Hazaribagh	Road Transport And Highways	02/2012	398.00	0.00	435.68
121	BHUBANESWAR TO PURI	Road Transport And Highways	03/2011	500.29	0.00	505.64
122	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	Road Transport And Highways	11/2011	909.00	0.00	941.91
123	JAIPUR-REENGUS	Road Transport And Highways	08/2010	267.81	0.00	645.56
124	4-laning of Faraka-Raiganj	Road Transport And Highways	02/2011	1078.84	0.00	1198.20
125	4-laning of Brahampore-Faraka	Road Transport And Highways	02/2011	998.79	0.00	1172.60
126	Acquisition of Two nos. of 3060 DWT	Shipping And Ports	04/2009	277.03	280.00	294.87
127	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping And Ports	03/2007	245.67	298.17	371.18
128	EXPANSION OF IISCO STEEL PLANT	Steel	02/2008	14443.00	0.00	14889.86

List of Projects Ahead of Schedule w.r.t. Original Schedule

						(Jul,2013)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Power</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	75.55	06/2016 -	04/2015
2	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	209.13	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	284.68		
	<u>Shipping & Ports</u>						
3	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013
	Total		1,028.10 -	1,012.23	554.60		
	Grand Total		4,472.19	4,456.32	839.28		

List of projects without Original Date of Commissioning

(Jul,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Coal</u>								
1	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	58.85	- -	03/2016	-	4/48
	Total		430.14 -	430.14	58.85				4/48
	<u>Petroleum</u>								
2	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	- -	08/2013	-	52/53
	Total		756.00 -	898.00	913.72				52/53
	<u>Power</u>								
3	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	609.36	- -	07/2013	-	10/29
	Total		421.01 -	623.44	609.36				10/29
	<u>Railways</u>								
4	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
5	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	350.55	- -	12/2013	-	0/0
6	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	221.69	- -	03/2014	-	0/0
7	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	744.71	513.75	- -	03/2014	-	0/1
8	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	259.43	- -	03/2014	-	0/0
9	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	3,000.00	2,121.06	- -	03/2014	-	0/0
10	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	149.24	- -	03/2014	-	0/0
11	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	175.43	145.19	- -	03/2014	-	0/0
12	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	279.40	85.57	- -	04/2014	-	0/0
13	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.40	- -	03/2015	-	0/0
14	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	139.81	- -	03/2015	-	0/0

(Jul,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Antici pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
16	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	209.77	18.76	- -	03/2015	-	0/0
17	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	283.55	0.40	- -	03/2015	-	0/0
18	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20 -	258.20	-	- -	03/2016	-	0/0
19	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	714.10	2.42	- 12/2017	-	-	0/0
	Total		4,956.31 -	10,741.08	4,454.40				0/1
	<u>Road Transport & Highways</u>								
20	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	708.02	- -	09/2013	-	1/1
21	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,721.50	- -	10/2013	-	3/3
22	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	558.91	- -	10/2013	-	2/2
23	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	559.73	- -	12/2013	-	0/1
24	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	925.49	- -	06/2014	-	2/3
	Total		3,389.00 -	3,389.00	4,473.65				8/10
	Grand Total		9,952.46	16,081.66	10,509.98				74/141

List of projects without Date of Commissioning

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Civil Aviation</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013
	Total		4,376.51 -		
	<u>Coal</u>				
4	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	03/2013 -	03/2013
5	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	-
6	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	03/2013 -	-
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	03/2012 -	-
	Total		2,324.09 -		
	<u>Steel</u>				
8	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 349.64	08/2010 08/2010	06/2013
	Total		260.00 -		
	<u>Petroleum</u>				
9	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	- -	03/2013
10	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	09/2012 -	-
11	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
12	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	07/2012 07/2012	-
13	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	12/2012 -	-
14	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	-
15	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu	05/2013	711.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	- -	-
	Total		18,201.81 -		
	<u>Power</u>				
17	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
18	MOUDA STTP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	08/2012 -	03/2013
19	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhy Pradesh	01/2009	5,915.00 -	10/2012 -	03/2013
20	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	-
21	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		14,227.71 -		
	<u>Railways</u>				
22	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005
23	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
24	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
25	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
26	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
27	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
28	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
29	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011
30	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
31	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
32	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
33	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
34	Dakshin-barasal-Iakshmikanapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
35	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
36	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
37	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
38	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	03/2012
39	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
40	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
41	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
42	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
43	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012
44	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
46	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013
47	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013
48	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013
49	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013
50	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013
51	KADUR-CHIKMAGALUR-SAKLLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013
52	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013
53	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
54	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013
55	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013
57	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013
58	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013
59	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
60	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
61	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
62	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-
63	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
64	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
65	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	-
66	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
67	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
68	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-
69	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-
70	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-
71	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-
72	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-
73	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-
74	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	- -	-
75	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	- -	-
76	Dahod-Indore via Sardarpur, Jhabua & Dhar - [N22000139]WR,Multi State	04/2007	1,640.04 -	- -	-
77	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	- -	-
78	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	- -	-
79	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	- -	-
80	Rajkot-Veraval,Wansjalia to Jataisar with new MM for Shapur- - [N22000143]WR,Gujarat	04/1994	320.66 -	- -	-
81	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	- -	-
82	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	- -	-
83	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	- -	-
84	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.39 -	- -	-
85	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	- -	-
86	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittisgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	- -	-
88	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner & Ratangarh-De - [N22000153]NWR,Rajasthan	04/2010	739.65 -	- -	-
89	Guriya-Marwar & Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	- -	-
90	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	- -	-
91	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	- -	-
92	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	- -	-
93	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	- -	-
94	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	- -	-
95	Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	- -	-
96	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	06/2013 -	-
97	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	- -	-
98	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	- -	-
99	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	- -	-
100	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	- -	-
101	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	- -	-
102	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	- -	-
103	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	- -	-
104	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	- -	-
105	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	- -	-
106	Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	- -	-
107	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	- -	-
108	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	- -	-
109	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	- -	-
110	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	- -	-
111	Sakri-Nirmali & Jhanjharpur-Laukahabazar & Saharsa-Forbesgan - [N22000180]ECR,Bihar	04/2004	372.14 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
112	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar	04/2009	470.00 -	- -	-
113	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	- -	-
114	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	- -	-
115	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	- -	-
116	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	- -	-
117	Sriperumbudur-Guduvanchery with spur to Irungattukkottai-Ava - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	- -	-
118	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	- -	-
119	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	- -	-
120	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	- -	-
121	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	- -	-
122	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	- -	-
123	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	- -	-
124	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	- -	-
125	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	- -	-
126	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	- -	-
127	Madurai-Rameswaram-GC - [N22000200]SR,Tamil Nadu	04/1999	240.00 -	- -	-
128	Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	- -	-
129	Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	- -	-
130	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	- -	-
131	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	- -	-
132	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	- -	-
133	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	- -	-
134	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	- -	-
135	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	- -	-
136	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line & - [N22000209]NEFR,Multi State	04/1999	523.17 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
137	Ambari Falakata to New Maynaguri - [N22000210]NEFR, Assam	04/2011	312.12 -	- -	-
138	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR, Assam	04/2012	246.07 -	- -	-
139	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP, West Bengal	04/2009	573.78 -	- -	-
140	Hyderabad/Secunderabad Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP, Andhra Pradesh	04/2012	632.68 -	04/2012 -	-
141	Madurai-Tuticorin via Aruppukkottai - [N22000215]SR, Multi State	04/2011	601.43 -	- -	-
142	Lakshmikantapur-Namkhana subsequently MM for Namkhana-Chandr - [N22000216]ER, Multi State	04/1999	406.99 -	- -	-
143	Sultanganj-Katuria via Asarganj, Tarapur & Belhar - [N22000217]ER, Multi State	04/2007	450.00 -	- -	-
144	Hansnabad-Hingalgarj New BG line - [N22000218]ER, Multi State	04/2010	172.03 -	- -	-
145	Pirpainti-Jasidih - [N22000219]ER, Multi State	04/2013	915.98 -	- -	-
146	Bandel-Boinchi 3rd line - [N22000221]ER, Multi State	04/2011	288.35 -	- -	-
147	Pirpainti-Bhagalpur - [N22000222]ER, Multi State	04/2011	261.38 -	- -	-
148	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER, Multi State	04/2000	157.17 -	- -	-
149	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER, Multi State	04/2001	923.52 -	- -	-
150	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER, Multi State	04/2005	595.91 -	- -	-
151	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER, Multi State	04/2010	174.56 -	- -	-
152	Sondalia-Champakpur doubling with new MM for Bira-Chakia NL - [N22000228]ER, Multi State	04/2010	277.28 -	- -	-
153	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER, Multi State	04/2010	296.44 -	- -	-
154	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER, Multi State	04/2010	157.94 -	- -	-
155	Wardha-Nanded Maharashtra - [N22000231]CR, Maharashtra	04/2008	697.00 -	- -	-
156	Kalyan-Kasara 3rd line - [N22000233]CR, Maharashtra	04/2011	277.70 -	- -	-
157	Bariarpur-Mananpur via Kharagpur, Lachimpur-Barahat - [N22000234]ER, Multi State	04/2007	450.55 -	- -	-
158	Tarakeshwar-Magra New BG line - [N22000235]ER, Multi State	04/2010	365.17 -	- -	-
159	Hansdiha-Godda NL - [N22000236]ER, Multi State	04/2011	267.09 -	- -	-
160	Sainthia-Tarapith 3rd line - [N22000237]ER, Multi State	04/2011	193.44 -	- -	-
161	Boinchi-Shaktigarh 3rd line - [N22000238]ER, Multi State	04/2011	175.80 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
162	New Alipur to Akra, MM for Budge Budge-Pujali NL, Pujali-Ulu - [N22000240]ER,Multi State	04/2010	494.54 -	- -	-
163	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State	04/2000	297.47 -	- -	-
164	Chandpara-Bangaon doubling with exension to Chandbazar & new - [N22000242]ER,Multi State	04/2003	337.96 -	- -	-
165	Magrahat-Diamond Harbour with MM Sangrampur-Krishanchandpur - [N22000243]ER,Multi State	04/2009	493.96 -	- -	-
166	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	- -	-
167	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	- -	-
168	Santoshpur-Remount Road via Garden Reach- Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	- -	-
169	Howrah-Development of station including segragation of aariv - [N22000249]ER,Multi State	04/2011	166.89 -	- -	-
170	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	- -	-
171	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
172	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-
173	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
174	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
175	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
176	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
177	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
178	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
179	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
180	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
181	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
182	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
183	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
184	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
185	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-
186	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
187	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
188	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
189	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
190	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
191	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-
192	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
193	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		70,787.05 -		
	<u>Road Transport & Highways</u>				
194	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008
195	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013
196	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	- -	04/2013
197	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	06/2013
198	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	06/2013
199	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	06/2013
200	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	02/2004 -	06/2013
201	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2013
	Total		2,479.73 -		
	<u>Shipping & Ports</u>				
202	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	- 01/2009	12/2010
203	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
204	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 09/2011	09/2011
205	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
206	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
207	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
208	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
209	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013
210	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013
211	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013
212	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
213	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	08/2012
	Total		7,619.97 -		
	<u>Telecommunications</u>				
214	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012
215	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013
216	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013
217	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
218	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
219	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
220	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
221	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 02/2013	-
	Total		2,764.39 -		
	<u>Urban Development</u>				
222	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	06/2011 -	03/2013
223	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>Water Resources</u>				
224	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		130,093.34		

List of on schedule Projects w.r.t. Original Schedule

(Jul,2013)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	117.24	03/2015 -	03/2015
2	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]	2/2010	344.28 -	344.28	-	03/2014 -	03/2014
	Total		1,013.88 -	1,013.88	117.26		
	<u>Coal</u>						
4	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	160.76	03/2015 03/2015	03/2015
5	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	149.76	03/2017 -	03/2017
6	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	45.17	03/2016 -	03/2016
7	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	88.71	03/2016 -	03/2016
9	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	38.66	03/2014 -	03/2014
10	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.06	07/2016 -	07/2016
11	RAMAGUNDUM OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	-	06/2015 -	06/2015
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	52.44	03/2016 -	03/2016
13	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
14	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
15	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	14.02	03/2015 -	03/2015
16	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
17	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.88	03/2018 03/2018	03/2018
18	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.30	03/2020 -	03/2020
20	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	264.37	03/2016 -	03/2016

(Jul,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	49.93	03/2015 -	03/2015
22	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
23	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	72.34	03/2015 -	03/2015
24	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	45.02	03/2014 03/2014	03/2014
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	446.32	03/2016 03/2016	03/2016
	Total		10,739.01 -	10,367.67	1,484.22		
	<u>Petroleum</u>						
26	Wax Project - [N16000101]	6/2010	576.60 -	576.60	225.00	12/2013 -	12/2013
27	Reconstruction of BPA & BPB Platforms - [N16000161]	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
28	Integrated Development of Bassein Field - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
29	Pipeline Replacement Project, Ahmedabad - [N16000159]	9/2011	202.25 -	202.25	-	07/2016 -	07/2016
30	Mounded Bullet Project at CPCL - [N16000154]	12/2012	279.00 -	279.00	-	12/2014 -	12/2014
31	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	32.13	07/2015 -	07/2015
32	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]	6/2009	486.00 -	486.00	54.56	09/2013 -	09/2013
33	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
34	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	72.54	11/2015 -	11/2015
35	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	97.03	12/2014 -	12/2014
36	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	67.27	03/2014 -	03/2014
37	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	435.83	05/2014 -	05/2014
38	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	80.56	12/2014 -	12/2014
39	Construction of three ETPs, Mehsana - [N16000135]	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
40	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]	10/2011	200.69 -	200.69	2.96	07/2014 -	07/2014
41	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	11.10	05/2014 -	05/2014
42	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	4,978.58	02/2014 -	02/2014
43	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,116.82	05/2015 -	05/2015

(Jul,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,665.65	188.07	03/2015 -	03/2015
	Total		32,603.12 -	32,113.88	7,379.53		
	Power						
45	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	387.19	01/2015 -	01/2015
46	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]	3/2011	2,569.25 -	2,569.25	1,718.22	03/2014 -	03/2014
47	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	955.49	09/2014 -	09/2014
48	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	309.32	10/2013 -	10/2013
49	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	181.21	06/2014 -	06/2014
50	Gadarwara Super Thermal Power Project Stage-I - [N18000151]	2/2013	11,638.55 -	11,638.55	-	09/2017 -	09/2017
51	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	144.20	06/2015 -	06/2015
52	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
53	COMMON TR. SYS. ASSOCIATED WITH EAST COAST & NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
54	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017
55	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,082.00	05/2017 -	05/2017
56	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	391.06	02/2015 -	02/2015
57	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	105.28	01/2014 -	01/2014
58	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	351.54	01/2015 -	01/2015
59	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	97.42	08/2014 -	08/2014
60	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	116.91	08/2014 -	08/2014
61	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	305.43	02/2014 -	02/2014
62	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	411.38	08/2014 -	08/2014
63	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	976.32	07/2014 -	07/2014

(Jul,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
64	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	824.57	08/2014 -	08/2014
65	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
66	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
67	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	91.41	03/2015 -	03/2015
68	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	368.00	08/2015 -	08/2015
69	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,558.00	11/2016 -	11/2016
70	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,074.00	09/2016 -	09/2016
71	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	1,700.00	12/2016 -	12/2016
72	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	224.31	11/2014 -	11/2014
73	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	823.01	10/2014 -	10/2014
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	174.41	11/2014 -	11/2014
75	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	306.40	08/2014 -	08/2014
76	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	40.12	06/2014 -	06/2014
77	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	750.21	06/2015 -	06/2015
78	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	12.44	03/2014 -	03/2014
79	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
80	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATTNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	357.08	10/2014 -	10/2014
81	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATTNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	40.34	08/2014 -	08/2014
82	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	1,025.01	12/2013 -	12/2013
83	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	722.79	12/2013 -	12/2013
84	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	1,034.60	05/2014 -	05/2014
	Total		111,609.53 -	111,609.53	18,729.19		
	<u>Railways</u>						

(Jul,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N220100325]	4/1998	183.23 -	818.29	84.10	02/2015 -	02/2015
86	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02 -	2,913.51	314.60	03/2016 -	03/2016
87	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	4/2008	653.19 -	653.46	245.66	03/2014 -	03/2014
88	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	642.18	03/2014 -	03/2014
89	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.52	02/2020 -	02/2020
90	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]	4/2010	423.66 -	423.66	130.65	03/2017 -	03/2017
91	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura Sharif NL - [N22000244]	4/2009	257.42 -	257.42	32.29	03/2014 -	03/2014
92	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]	4/2011	299.60 -	299.60	1.09	03/2017 -	03/2017
93	Krishnanagar-Bethua Dahri doubling - [N22000226]	4/2009	151.65 -	151.65	-	03/2015 -	03/2015
94	Plassey-Jiaganj Doubling - [N22000220]	4/2011	248.07 -	248.07	8.13	03/2015 -	03/2015
95	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]	4/2010	309.44 -	388.67	39.53	12/2015 -	12/2015
96	Champajharan-Bimalgarh Doubling extension - [N22000162]	4/2010	149.90 -	177.38	36.46	03/2015 -	03/2015
97	Dholpur-Sirmuttra with extension to Gangapurcity & Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]	4/2010	622.41 -	2,030.50	1.20	02/2019 -	02/2019
98	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
99	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114]	4/2008	516.23 -	516.23	388.06	03/2014 -	03/2014
100	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]	4/2008	829.74 -	829.74	27.24	03/2015 -	03/2015
101	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	173.31	03/2016 -	03/2016
	Total		18,655.83 -	23,769.96	2,126.02		
	<u>Road Transport & Highways</u>						
102	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139]	9/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013
103	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]	3/2011	785.50 -	785.50	817.69	08/2013 -	08/2013
104	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,260.10	08/2013 -	08/2013
105	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
106	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
107	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	282.58	10/2014 -	10/2014

(Jul,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	463.54	07/2014 -	07/2014
109	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	81.70	01/2014 -	01/2014
110	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,005.50	09/2014 -	09/2014
111	Six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]	12/2011	1,047.00 -	1,047.00	201.93	06/2014 -	06/2014
112	4-laning of Raiganj-Dalkola - [N24000204]	2/2011	580.43 -	580.43	257.54	08/2013 -	08/2013
113	4-laning of Brahampore-Faraka - [N24000203]	2/2011	998.79 -	998.79	1,172.60	08/2013 -	08/2013
114	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	626.59	11/2013 -	11/2013
115	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	-	09/2014 -	09/2014
116	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	-	10/2014 -	10/2014
117	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	463.63	09/2014 -	09/2014
118	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	302.56	04/2015 -	04/2015
119	SAMAIKHALI GANDHIDHAM - [N24000223]	9/2010	805.39 -	805.39	543.70	12/2013 -	12/2013
120	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	30.80	12/2015 -	12/2015
121	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	38.90	07/2014 -	07/2014
122	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	131.37	10/2014 -	10/2014
123	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	13.50	09/2015 -	09/2015
124	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	148.12	08/2015 -	08/2015
125	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	190.43	06/2014 -	06/2014
126	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	189.14	06/2015 -	06/2015
127	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	243.51	04/2014 -	04/2014
128	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.37	04/2014 -	04/2014
129	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	637.40	03/2014 -	03/2014
130	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,162.30	05/2014 -	05/2014
131	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	864.87	03/2014 -	03/2014
132	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	288.77	02/2014 -	02/2014

(Jul,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
133	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	511.33	01/2014 -	01/2014
134	Tirupati - Tiruthani - Chennai - [N24000178]	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
135	2 Laning of Muzaffarpur - Sonbarsa - [N24000174]	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
136	4-laning of Faraka-Raiganj - [N24000202]	2/2011	1,078.84 -	1,078.84	1,198.20	08/2013 -	08/2013
137	BAREILY-SITAPUR - [N24000200]	3/2011	1,046.00 -	1,046.00	346.82	09/2013 -	09/2013
138	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	1,255.70	06/2014 -	06/2014
139	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	941.91	05/2014 -	05/2014
140	BHUBANESWAR TO PURI - [N24000195]	3/2011	500.29 -	500.29	505.64	08/2013 -	08/2013
141	PUNE-SHOLAPUR,Pkg-II - [N24000193]	9/2011	835.00 -	835.00	122.65	01/2014 -	01/2014
142	4-laning of Barhi-Hazaribagh - [N24000191]	2/2012	398.00 -	398.00	435.68	02/2014 -	02/2014
143	2laning with PS Gopalganj-Chappra - [N24000190]	12/2011	325.00 -	325.00	161.02	05/2014 -	05/2014
144	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
145	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
146	ROHTAK-BAWAL - [N24000169]	5/2011	650.00 -	650.00	1,086.30	11/2013 -	11/2013
147	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,284.70	10/2014 -	10/2014
148	Talegaon-amravati - [N24000140]	11/2009	567.00 -	567.00	1,131.20	11/2013 -	11/2013
	Total		43,576.03 -	43,576.03	21,049.92		
	<u>Shipping & Ports</u>						
149	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
	Total		966.46 -	994.82	363.20		
	<u>Steel</u>						
150	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078]	7/2012	332.65 -	332.65	64.42	08/2014 -	08/2014
151	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]	1/2012	254.90 -	254.90	3.46	12/2014 -	12/2014
152	Rebuilding of Battery Block 5A and Re-construction of Battery Block 5B - [N12000080]	3/2012	339.35 -	339.35	9.05	06/2015 -	06/2015
	Total		926.90 -	926.90	76.93		

(Jul,2013)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Urban Development</u>						
153	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	3,853.30	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	3,853.30		
	Grand Total		255,332.76	259,614.67	55,179.57		

List of Delayed Projects w.r.t. Original Schedule

(Jul,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,354.00	12/2008 -	06/2014	66	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,681.60	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,991.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,074.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,100.60				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	228.60	05/2012 -	09/2013	16	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.80	01/2011 04/2013	12/2014	47	20
	Total		645.07 -	645.07	460.40				
	<u>Coal</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,747.67	06/2009 -	01/2014	55	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.27	03/2010 -	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.36	03/2011 -	03/2014	36	-
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.85	03/2013 -	03/2014	12	-
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,478.68	03/2012 -	03/2014	24	-
12	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	112.35	03/2012 -	03/2014	24	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	721.74	03/2013 09/2012	10/2014	19	25
14	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.66	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.62	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.44	03/2010 -	03/2015	60	-
17	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	114.33	03/2013 -	03/2015	24	-
18	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.48	03/2012 -	03/2015	36	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.24	03/2013 -	03/2015	24	-
20	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,415.57	03/2014 -	03/2016	24	-
21	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,253.35	03/2014 -	03/2016	24	-
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016	44	-
23	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	265.66	03/2014 -	03/2016	24	-
24	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	87.20	12/2012 -	03/2016	39	-
25	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24	-
26	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.01	03/2014 -	03/2016	24	-
27	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
28	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24	-
29	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
30	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	128.14	03/2012 -	03/2016	48	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72	-
32	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
33	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60	-
34	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	32.00	12/2015 -	02/2018	26	-
	Total		24,633.81 -	28,090.60	12,666.28				
	<u>Steel</u>								
35	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,478.48	10/2009 10/2012	08/2013	46	10
36	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 343.58	343.58	260.62	02/2011 02/2011	08/2013	30	30
37	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 216.68	216.68	147.26	10/2012 10/2012	09/2013	11	11
38	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	276.50	05/2012 05/2012	09/2013	16	16
39	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	209.28	05/2013 11/2013	11/2013	6	0
40	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	352.58	12/2011 03/2012	12/2013	24	21
41	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	14,889.86	12/2011 -	12/2013	24	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,662.34	12/2011 -	12/2013	24	-
43	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,679.32	03/2013 -	12/2013	9	-
44	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	316.17	04/2013 12/2013	12/2013	8	0
45	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,691.38	12/2012 -	03/2014	15	-
46	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	76.05	10/2013 -	06/2014	8	-
47	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	9,923.03	03/2013 -	09/2014	18	-
48	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	68.64	11/2013 -	06/2015	19	-
	Total		64,438.32 -	70,505.86	52,031.51				
	<u>Petrochemicals</u>								
49	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	4,510.51				
	<u>Petroleum</u>								
50	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	18	-
51	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	156.85	10/2011 -	07/2013	21	-
52	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	23	17
53	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	189.49	02/2013 -	08/2013	6	-
54	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	09/2013	12	-
55	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24	16
56	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,469.11	04/2013 -	09/2013	5	-
57	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12	-
58	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	128.88	06/2012 -	09/2013	15	-
59	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	57.73	06/2012 -	09/2013	15	-
60	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	624.66	01/2013 -	10/2013	9	-
61	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,458.39	01/2012 -	10/2013	21	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	228.26	11/2012 -	10/2013	11	-
63	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	726.73	12/2011 -	11/2013	23	-
64	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	750.00	729.07	03/2007 03/2014	12/2013	81	-3
65	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,727.24	03/2007 03/2017	12/2013	81	-39
66	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93	9
67	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	729.24	03/2010 03/2012	12/2013	45	21
68	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	260.22	03/2012 -	12/2013	21	-
69	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	725.28	07/2012 -	12/2013	17	-
70	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	98.45	09/2012 -	12/2013	15	-
71	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	240.31	03/2013 -	12/2013	9	-
72	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	228.47	04/2012 -	12/2013	20	-
73	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	651.11	04/2012 -	12/2013	20	-
74	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26	-
75	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26	-
76	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	62.49	08/2013 -	01/2014	5	-
77	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
78	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	02/2014	43	21
79	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
80	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
81	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,494.55	03/2013 -	03/2014	12	-
82	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	187.62	08/2012 -	03/2014	19	-
83	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	28.10	06/2012 -	03/2014	21	-
84	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	22,593.00	11/2012 -	04/2014	17	-
85	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,107.72	08/2010 03/2012	05/2014	45	26
86	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	957.44	01/2014 -	05/2014	4	-
88	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	276.67	05/2013 -	05/2014	12	-
89	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	4.00	03/2014 -	05/2014	2	-
90	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014	2	-
91	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20	0
92	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50	-
93	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	360.28	09/2011 -	12/2014	39	-
94	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	4.12	01/2014 -	01/2015	12	-
95	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3	-
96	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,Multi State	08/2011	586.00 -	586.00	17.03	07/2015 -	08/2015	1	-
97	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
98	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,496.18	13.30	01/2013 -	12/2015	35	-
99	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	453.95	12/2015 -	05/2016	5	-
100	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
101	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24	-
102	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24	-
103	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	03/2017	23	-
	Total		131,903.29 -	147,024.35	80,777.12				
	Power								
104	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	775.25	644.73	01/2010 -	07/2013	42	-
105	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	84.66	10/2012 -	08/2013	10	-
106	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	156.80	11/2011 -	09/2013	22	-
107	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	150.53	06/2012 -	09/2013	15	-
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	131.59	01/2013 -	09/2013	8	-
109	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,762.78	11/2009 02/2013	10/2013	47	8

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
110	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	752.82	08/2010 01/2013	10/2013	38	9
111	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,420.00	10/2012 -	11/2013	13	-
112	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	884.62	10/2009 -	12/2013	50	-
113	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,540.95	12/2012 -	12/2013	12	-
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	372.89	11/2011 -	12/2013	25	-
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.57	02/2012 -	12/2013	22	-
116	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	830.37	05/2012 -	12/2013	19	-
117	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,217.64	08/2013 -	12/2013	4	-
118	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	88.08	04/2013 -	12/2013	8	-
119	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	131.55	07/2013 -	12/2013	5	-
120	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,833.75	10/2010 01/2013	03/2014	41	14
121	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,607.63	01/2012 -	03/2014	26	-
122	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,580.90	2,054.21	08/2012 -	03/2014	19	-
123	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,835.42	08/2012 -	03/2014	19	-
124	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	595.85	11/2012 -	03/2014	16	-
125	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,113.89	03/2013 -	03/2014	12	-
126	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,646.55	12/2013 -	03/2014	3	-
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	308.88	07/2013 -	03/2014	8	-
128	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,467.53	10/2012 -	06/2014	20	-
129	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,326.81	12/2012 -	06/2014	18	-
130	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	895.00	08/2012 -	06/2014	22	-
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	355.89	11/2011 -	07/2014	32	-
132	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,031.00	04/2009 -	09/2014	65	-
133	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 1,117.92	1,117.92	646.69	08/2012 08/2013	09/2014	25	13
134	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,163.00	08/2013 -	09/2014	13	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
135	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	688.73	11/2012 -	09/2014	22	-
136	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	151.90	11/2013 -	09/2014	10	-
137	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,156.83	09/2009 06/2013	11/2014	62	17
138	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.74	01/2013 -	12/2014	23	-
139	Transmission system for transfer of power from Gen- PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	950.74	11/2013 -	12/2014	13	-
140	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	442.17	07/2014 -	02/2015	7	-
141	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,593.11	11/2012 -	03/2015	28	-
142	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	869.10	04/2013 -	03/2015	23	-
143	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	35.47	04/2015 -	05/2015	1	-
144	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,315.50	08/2013 -	06/2015	22	-
145	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,938.00	07/2011 -	10/2015	51	-
146	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,857.00	03/2013 -	03/2016	36	-
147	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	358.03	07/2014 -	05/2016	22	-
148	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,706.11	01/2016 01/2016	11/2016	10	10
149	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,514.00	12/2009 -	02/2017	86	-
150	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	497.79	07/2010 02/2016	02/2017	79	12
151	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,417.91	05/2013 05/2013	03/2017	46	46
152	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,317.03	09/2010 08/2014	12/2017	87	40
153	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,505.44	09/2009 07/2014	03/2018	102	44
	Total		122,216.59 -	139,063.30	92,696.28				
	<u>Railways</u>								
154	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	226.51	03/2002 -	09/2013	138	-
155	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	578.57	03/1994 -	10/2013	235	-
156	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	392.93	12/2009 03/2011	10/2013	46	31
157	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	128.61	12/2011 11/2013	11/2013	23	0

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
158	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52 207.52	207.52	176.62	12/2012 -	12/2013	12	-
159	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE, Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
160	Ramanagaram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	486.44	03/2013 -	03/2014	12	-
161	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam	04/1996	1,676.31 1,676.31	5,000.00	3,604.73	03/2009 -	03/2014	60	-
162	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, Odisha	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014	66	66
163	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Odisha	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65	65
164	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, Uttar Pradesh	09/2001	129.70 245.39	245.39	230.03	12/2008 -	09/2014	69	-
165	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, Maharashtra	03/1996	401.81 495.44	1,512.86	244.66	03/2004 12/2010	12/2014	129	48
166	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 2,363.00	2,363.00	1,104.99	03/2009 12/2012	12/2014	69	24
167	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, Tamil Nadu	04/2006	495.74 -	495.74	248.49	06/2013 06/2013	12/2014	18	18
168	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
169	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 393.46	535.40	177.01	03/2007 03/2007	03/2015	96	96
170	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR, Bihar	09/2001	100.00 492.98	1,041.79	743.88	12/2010 12/2010	03/2015	51	51
171	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00 733.00	2,350.00	1,473.98	12/2008 -	03/2015	75	-
172	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90 227.90	223.01	124.52	12/2012 -	03/2015	27	-
173	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR, Tripura	04/1999	895.00 -	1,151.00	944.66	03/2007 -	03/2015	96	-
174	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	4,996.65	2,798.00	04/2008 03/2014	12/2015	92	21
175	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47 2,921.00	2,921.00	1,828.20	10/2007 12/2012	12/2015	98	36
176	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015	69	-
177	AGARTALA SABROOM, NL, NEFR - [N220000099]NEFR, Tripura	04/2008	813.34 813.34	1,741.00	488.37	03/2014 -	12/2015	21	-
178	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	2,298.42	24.59	03/2014 -	03/2016	24	-
179	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,074.47	445.45	06/2005 07/2011	06/2016	132	59
180	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	50.61	03/2016 -	06/2016	3	-
181	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	1,423.98	477.57	03/2005 12/2008	12/2016	141	96
182	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,209.40	03/2014 03/2016	12/2016	33	9

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
183	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	4,453.50	1,529.74	03/2011 03/2014	03/2017	72	36
184	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, Uttar Pradesh	04/2006	325.00 325.00	1,116.53	216.92	03/2010 03/2017	03/2017	84	0
185	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 -	2,384.34	91.38	04/2014 -	03/2017	35	-
186	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15	-
187	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	2,446.81	8.94	03/2015 -	03/2017	24	-
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201	-
	Total		27,508.39 -	76,761.56	30,671.70				
	<u>Road Transport & Highways</u>								
189	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	195.52	08/2004 07/2010	08/2013	108	37
190	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	195.15	08/2004 -	08/2013	108	-
191	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	284.35	06/2011 06/2011	08/2013	26	26
192	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	08/2013	65	-
193	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31	-
194	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	1,319.40	07/2012 -	08/2013	13	-
195	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	792.06	1,968.50	12/2012 -	08/2013	8	-
196	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	309.90	05/2008 -	09/2013	64	-
197	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	250.39	279.92	10/2008 -	09/2013	59	-
198	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	262.59	06/2008 -	09/2013	63	-
199	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	09/2013	51	-
200	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	795.00	1,126.80	05/2012 -	09/2013	16	-
201	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	09/2013	4	-
202	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	1,008.50	1,341.40	06/2013 -	09/2013	3	-
203	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81 -	267.81	645.56	02/2013 -	09/2013	7	-
204	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	652.98	05/2010 -	10/2013	41	-
205	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
206	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	947.24	01/2013 -	10/2013	9	-
207	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	550.72	07/2013 -	10/2013	3	-
208	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.37	02/2013 -	10/2013	8	-
209	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9	-
210	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.24	09/2007 -	11/2013	74	-
211	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.91	10/2008 -	12/2013	62	-
212	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.53	01/2009 -	12/2013	59	-
213	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	461.55	09/2008 -	12/2013	63	-
214	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	285.56	06/2008 -	12/2013	66	-
215	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	300.84	06/2008 -	12/2013	66	-
216	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	206.40	05/2008 -	12/2013	67	-
217	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	252.67	06/2008 -	12/2013	66	-
218	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.51	06/2010 -	12/2013	42	-
219	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.19	09/2009 -	12/2013	51	-
220	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
221	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,024.30	09/2012 -	12/2013	15	-
222	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,838.80	10/2011 -	12/2013	26	-
223	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,700.30	08/2011 -	12/2013	28	-
224	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	12/2013	25	-
225	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	12/2013	8	-
226	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	811.61	03/2013 -	12/2013	9	-
227	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,123.30	11/2012 -	12/2013	13	-
228	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
229	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	114.73	05/2013 -	12/2013	7	-
230	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	612.91	03/2013 -	12/2013	9	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
231	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.21	07/2013 -	12/2013	5	-
232	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	507.47	05/2013 -	02/2014	9	-
233	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	239.49	09/2007 -	03/2014	78	-
234	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	142.58	09/2008 -	03/2014	66	-
235	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	238.88	06/2005 -	03/2014	105	-
236	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	247.36	06/2008 -	03/2014	69	-
237	BIJNI TO ASSAM /WB. BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	285.21	06/2008 -	03/2014	69	-
238	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	337.60	10/2008 -	03/2014	65	-
239	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	204.62	04/2008 -	03/2014	71	-
240	GUWHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	265.28	04/2008 -	03/2014	71	-
241	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63	-
242	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	233.02	09/2007 -	03/2014	78	-
243	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	857.99	07/2010 -	03/2014	44	-
244	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	410.02	10/2011 -	03/2014	29	-
245	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	193.45	53.97	11/2012 -	03/2014	16	-
246	MURADABAD-BAREILY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,828.90	06/2013 -	03/2014	9	-
247	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	393.14	05/2013 -	03/2014	10	-
248	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	270.58	03/2013 -	03/2014	12	-
249	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, Uttarakhand	11/2011	478.00 -	478.00	259.70	10/2013 -	03/2014	5	-
250	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	67.44	09/2007 -	04/2014	79	-
251	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.30	03/2013 -	04/2014	13	-
252	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	525.57	02/2014 -	04/2014	2	-
253	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	318.28	02/2009 03/2014	05/2014	63	2
254	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	302.87	04/2008 -	05/2014	73	-
255	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	150.29	07/2009 -	05/2014	58	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
256	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68	-
257	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	119.93	11/2008 -	06/2014	67	-
258	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	814.19	10/2011 -	06/2014	32	-
259	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
260	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	651.32	07/2013 -	06/2014	11	-
261	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53	-
262	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.15	09/2013 -	07/2014	10	-
263	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	181.53	07/2012 -	07/2014	24	-
264	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	302.85	09/2010 -	08/2014	47	-
265	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
266	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	284.89	04/2010 -	11/2014	55	-
267	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	90.10	04/2009 -	12/2014	68	-
268	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	59.83	11/2008 -	12/2014	73	-
269	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	159.85	04/2009 -	12/2014	68	-
270	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.37	12/2009 -	12/2014	60	-
271	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,128.20	02/2010 -	12/2014	58	-
272	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.55	01/2014 -	12/2014	11	-
273	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	315.83	08/2013 -	02/2015	18	-
274	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31	-
275	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,731.30	08/2014 -	07/2015	11	-
276	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.79	09/2014 -	10/2015	13	-
277	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	118.72	10/2013 -	11/2015	25	-
278	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
279	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	922.41	07/2015 -	06/2016	11	-
	Total		54,470.83 -	56,366.09	53,418.76				

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Shipping & Ports</u>								
280	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	19	11
281	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	418.64	12/2012 10/2013	10/2013	10	0
282	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	137.00	03/2006 12/2013	12/2013	93	0
283	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	963.01	12/2010 09/2012	03/2014	39	18
284	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
	Total		6,002.59 -	7,254.70	5,287.32				
	<u>Telecommunications</u>								
285	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34	9
286	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28	-
287	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013	54	-
288	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
289	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
	Total		2,934.85 -	2,774.50	1,282.27				
	<u>Urban Development</u>								
290	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	258.11	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	258.11				
	Grand Total		483,150.35	586,626.03	360,160.86				

List of ongoing projects having cost overrun w.r.t. to original schedule

(Jul,2013)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	05/2011 -	03/2013	19.69
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
	Total		3,750.51 -	27,287.00			
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	01/2014	49.09
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	03/2013 -	10/2014	360.36
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	03/2012 -	03/2014	33.36
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		8,579.45 -	39,549.64			
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	12/2013	63.35
	Total		5,460.61 -	48,469.64			
	<u>Petroleum</u>						

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	750.00	03/2007 -	12/2013	117.33
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	03/2007 -	12/2013	329.16
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	03/2006 -	12/2013	285.29
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	04/2006 -	02/2014	536.46
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40
20	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27
21	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057	01/2009	756.00 -	898.00	- -	08/2013	18.78
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	04/2014	9.85
23	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066	01/2008	224.00 -	394.00	- -	03/2013	75.89
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	04/2013 -	09/2013	121.45
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76
27	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29
28	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
29	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
30	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	12/2013	12.16
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	08/2014 -	10/2014	0.00
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	12/2013	54.46
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	12/2013	67.62
35	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	06/2012 -	09/2013	41.85

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
36	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	09/2013	26.44
	Total		58,175.86 -	127,137.62			
	<u>Power</u>						
37	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	03/2018	36.90
38	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69
39	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	12/2017	69.71
40	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	05/2013 05/2013	03/2017	105.82
41	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	02/2017	0.00
42	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	11/2014	41.49
43	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
44	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85
45	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	10/2013	20.34
46	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
47	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	08/2010 -	10/2013	53.19
48	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
49	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]	07/2006	557.24 -	775.25	01/2010 -	07/2013	39.12
50	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69
51	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	05/2016	50.31
52	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	08/2012 -	09/2014	94.76
53	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
54	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32
55	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	- -	07/2013	48.08
	Total		49,763.64 -	195,292.50			

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Railways</u>						
56	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	03/1994 -	10/2013	265.83
57	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
58	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	589.43	- 03/2010	-	278.67
59	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	03/2012	643.63
60	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
61	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	03/2001 -	12/2017	700.00
62	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
63	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	09/2013	127.94
64	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
65	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
66	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	03/2004 -	12/2014	276.51
67	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
68	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
69	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	412.91	- -	01/2013	39.97
70	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	- -	03/2014	170.07
71	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
72	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
73	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	03/2012 -	03/2013	112.42
74	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	775.36	- -	10/2012	398.46
75	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
76	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
77	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
78	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.65	04/2008 12/2011	12/2015	399.67

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
79	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2012	195.55
80	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01
81	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	- -	12/2012	358.34
82	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.00	06/2004 -	12/2012	207.11
83	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
84	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05
85	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
86	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
87	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	12/2012 -	04/2013	348.89
88	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	10/2013	300.67
89	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	12/2010 -	03/2015	941.79
90	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
91	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
92	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47
93	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28
94	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	- -	-	108.19
95	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
96	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	800.00	- -	-	700.00
97	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,029.92	- -	03/2013	267.83
98	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73
99	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,350.00	12/2008 -	03/2015	220.60
100	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
101	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
102	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67
103	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92
104	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	- -	-	553.35
105	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
106	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	693.39	03/2012 -	12/2012	263.39
107	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	03/2014	461.44
108	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
109	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
110	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,453.50	03/2011 -	03/2017	512.11
111	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	- -	-	62.83
112	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
113	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04
114	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
115	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
116	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
117	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
118	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,000.00	- -	03/2014	227.62
119	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
120	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	12/2008 -	09/2014	89.20
121	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	03/1998 08/2005	08/2005	1,004.54
122	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
123	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
124	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
125	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
126	RAICHUR-GUNTAKAL(DL)(SCR) - [N220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
127	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
128	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11
129	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	280.00	02/2006 -	-	49.80
130	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
131	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU - [N22000052	04/2003	98.74 -	337.30	- -	03/2012	241.60
132	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
133	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
134	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
135	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	1,383.45	- -	-	242.28
136	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	914.98	- -	12/2012	166.63
137	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	435.87	03/2011 -	03/2011	156.39
138	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083	09/1996	156.00 -	406.40	- -	12/2013	160.51
139	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	227.40	- -	-	81.92
140	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	582.83	- -	-	27.81
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	385.20	- -	03/2015	92.60
142	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	532.87	- -	-	77.62
143	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
144	BARDHAMAN-KATWA (GC) - [N22000091	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
145	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36
146	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
147	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50
148	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,741.00	03/2014 -	12/2015	114.06

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
149	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,384.34 -	04/2014 -	03/2017	284.98
150	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86 -	- -	03/2015	27.20
151	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58 -	12/2015 -	03/2017	152.38
152	Ramanagram-Mysore doubling with electrification of Kengesii-Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70 -	03/2013 -	03/2014	0.15
153	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]	04/2010	2,069.60 -	2,298.42 -	03/2014 -	03/2016	11.06
154	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51 -	03/2016 -	03/2016	11.24
155	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46 -	03/2014 -	03/2014	0.04
156	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38 -	12/2011 -	02/2012	105.53
157	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03 -	12/2011 -	11/2013	221.65
158	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74 -	12/2010 -	12/2010	30.16
159	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	1,215.30 -	03/2013 -	03/2013	208.34
160	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]	04/2008	318.24 -	485.65 -	03/2012 -	-	52.61
161	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	04/2006	850.00 -	2,446.81 -	03/2015 -	03/2017	187.86
162	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]	04/2006	117.36 196.95	196.95 -	03/2011 -	-	67.82
163	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	5,000.00 -	03/2009 -	03/2014	198.27
164	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75 -	- -	-	24.15
165	Virangam-Samakhiali (DL) - [N22000145]	04/2011	446.00 -	685.17 -	- -	-	53.63
166	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60 -	02/2020 -	02/2020	226.98
167	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur - [N22000152]	04/2013	456.00 -	567.23 -	- -	-	24.39
168	Guriya-Marwar & Karjoda-Palanpur - [N22000154]	04/2011	239.73 -	274.34 -	- -	-	14.44
169	Ajmer-Bangurgram - [N22000155]	04/2011	213.39 -	251.99 -	- -	-	18.09
170	Dholpur-Sirmuttra with extension to Gangapucity & Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]	04/2010	622.41 -	2,030.50 -	02/2019 -	02/2019	226.23
171	Digha-Jaleswar including MM for Digha-Egra - [N22000160]	04/2010	553.63 -	651.17 -	- -	-	17.62
172	Champajharan-Bimalgarh Doubling extension - [N22000162]	04/2010	149.90 -	177.38 -	03/2015 -	03/2015	18.33

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	Tamluk-Basulya-Sutahata Doubling - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	-	16.38
174	Dangoaposi-Rajkharwan 3rd line Doubling - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	12/2015	25.60
175	Sakri-Hasanpur Road (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
176	Chhapra-Muzaffarpur (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
177	Attippattu-Puttur - [N22000184]	04/2008	446.87 -	527.00	- -	-	17.93
178	Chennai-Cuddalore via Mamallapuram - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
179	Cuddalore-Salem via Vriddhachalam GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
180	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
181	Villupuram-Dindigul with Electrification - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
182	New BG line from Kaliyaganj to Buniadpur - [N22000193]	04/2010	221.42 -	221.47	- -	-	0.02
183	Construction of NL from Kumarghat-Agartala - [N22000194]	04/1999	895.00 -	1,151.00	03/2007 -	03/2015	28.60
184	Erode-Palani - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
185	Madurai-Rameswaram-GC - [N22000200]	04/1999	240.00 -	441.69	- -	-	84.04
186	Madurai-Bodinayakanur - [N22000201]	04/2008	164.41 -	260.72	- -	-	58.58
187	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC along with electrification - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
188	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line & MM for Chalsa-Naxal & Rajabhatkhowa-Jaintia - [N22000209]	04/1999	523.17 -	1,393.44	- -	-	166.35
189	Hyderabad/Secunderabad Multi Modal Transport System(MMTS) Phase-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	-	29.06
190	Madurai-Tuticorin via Aruppukkottai - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
191	Wardha-Nanded Maharashtra - [N22000231]	04/2008	697.00 -	1,604.00	- -	-	130.13
	Total		60,009.84 -	360,800.58			
	<u>Road Transport & Highways</u>						
192	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	04/2004 -	06/2013	7.35
193	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2014	30.10

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
194	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	03/2008 -	02/2008	16.14
195	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	05/2008 -	09/2013	26.41
196	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75
197	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68
198	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2014	82.12
199	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	05/2014	85.58
200	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	07/2014	2.29
201	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	03/2014	33.70
202	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2013	106.50
	Total		3,324.28 -	366,245.78			
	<u>Shipping & Ports</u>						
203	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
204	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
205	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	03/2014	18.89
206	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2013	300.00
207	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
208	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
209	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
210	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	02/2014 -	02/2014	2.93
211	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	377,464.28			
	<u>Steel</u>						

(Jul,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
212	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00 -	10/2009 -	08/2013	41.41
213	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17 -	12/2011 06/2010	12/2013	105.20
214	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68 -	10/2012 -	09/2013	100.63
215	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00 -	12/2011 -	12/2013	13.61
216	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068	07/2007	230.00 -	343.58 -	02/2011 -	08/2013	49.38
217	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00 -	349.64 -	08/2010 -	06/2013	34.48
	Total		24,028.89 -	407,680.35 -			
	<u>Telecommunications</u>						
218	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL [N26000058	01/2009	149.15 -	158.72 -	06/2009 -	12/2013	6.42
219	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088	03/2008	328.13 -	392.13 -	03/2009 -	01/2013	19.50
220	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70 -	930.60 -	11/2010 -	09/2013	1.52
	Total		1,393.98 -	409,161.80 -			
	<u>Urban Development</u>						
221	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00 -	06/2011 -	03/2013	81.53
222	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048	11/2006	114.18 173.08	173.08 -	04/2009 -	-	51.59
	Total		6,509.18 -	420,943.88 -			
	<u>Water Resources</u>						
223	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00 -	12/2007 -	12/2012	118.64
	Total		542.90 -	422,130.88 -			
	Grand Total		246,831.11	3,225,110.95			

List of ongoing projects having time and cost overrun w.r.t original schedule

(Jul,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	16,354.00	12/2008 -	06/2014
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	4,681.60	09/2010 -	03/2015
	Total		16,663.00 -	22,947.00	21,035.60		
	<u>Coal</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,747.67	06/2009 -	01/2014
4	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	721.74	03/2013 -	10/2014
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	4,478.68	03/2012 -	03/2014
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016
	Total		7,938.86 -	34,520.95	29,217.88		
	<u>Petrochemicals</u>						
8	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	4,510.51	04/2012 -	12/2013
	Total		5,460.61 -	43,440.95	33,728.39		
	<u>Petroleum</u>						
9	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	750.00	729.07	03/2007 -	12/2013
10	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	1,727.24	03/2007 -	12/2013
11	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	438.85	432.22	03/2006 -	12/2013
12	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	02/2014
13	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	03/2014
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	1,902.72	09/2010 03/2012	12/2015
15	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	5,107.72	08/2010 03/2012	05/2014
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	7,204.61	05/2010 -	03/2014

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
17	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	22,593.00	11/2012 -	04/2014
18	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070]	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013
19	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081]	04/2008	825.00 -	1,827.00	1,469.11	04/2013 -	09/2013
20	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,331.62	1,557.08	06/2012 -	05/2014
21	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099]	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013
22	Development of Cluster-7 Fields - [N16000104]	03/2010	3,241.03 -	6,638.94	1,451.42	03/2013 -	11/2014
23	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	228.47	04/2012 -	12/2013
24	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	-	10/2011 -	12/2013
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157]	01/2006	732.00 -	1,227.00	-	10/2011 -	12/2013
27	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	128.88	06/2012 -	09/2013
28	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	57.73	06/2012 -	09/2013
	Total		54,470.23 -	117,450.28	83,461.28		
	<u>Power</u>						
29	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	3,505.44	09/2009 -	03/2018
30	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	5,031.00	04/2009 -	09/2014
31	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	6,317.03	09/2010 -	12/2017
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	2,417.91	05/2013 05/2013	03/2017
33	BARH STPP(3X660MW) NTPC [180100242]	12/2003	8,692.97 -	8,693.00	8,514.00	12/2009 -	02/2017
34	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	1,156.83	09/2009 -	11/2014
35	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	1,833.75	10/2010 -	03/2014
36	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	1,762.78	11/2009 -	10/2013
37	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	752.82	08/2010 -	10/2013

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
38	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	497.79	07/2010 -	02/2017
39	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018]	07/2006	557.24 -	775.25	644.73	01/2010 -	07/2013
40	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	1,706.11	01/2016 -	11/2016
41	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,745.08	358.03	07/2014 -	05/2016
42	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	646.69	08/2012 -	09/2014
43	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	2,054.21	08/2012 -	03/2014
	Total		41,507.61 -	175,804.60	120,660.40		
	<u>Railways</u>						
44	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	580.83	578.57	03/1994 -	10/2013
45	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	602.18	03/1995 -	03/2015
46	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	8,822.50	03/2001 -	12/2017
47	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 119.29	227.94	226.51	03/2002 -	09/2013
48	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,512.86	244.66	03/2004 -	12/2014
49	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	09/1997	1,000.00 -	4,996.65	2,798.00	04/2008 12/2011	12/2015
50	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	535.40	177.01	03/2007 03/2007	03/2015
51	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	392.93	12/2009 -	10/2013
52	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	1,041.79	743.88	12/2010 -	03/2015
53	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,350.00	1,473.98	12/2008 -	03/2015
54	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	477.57	03/2005 12/2008	12/2016
55	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014
56	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	4,453.50	1,529.74	03/2011 -	03/2017
57	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	1,104.99	03/2009 -	12/2014
58	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	1,828.20	10/2007 -	12/2015

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
59	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	230.03	12/2008 -	09/2014
60	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014
61	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015
62	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	216.92	03/2010 -	03/2017
63	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,220.15	1,209.40	03/2014 -	12/2016
64	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR & G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	141.55	03/2012 -	03/2014
65	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.47	445.45	06/2005 -	06/2016
66	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,741.00	488.37	03/2014 -	12/2015
67	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,384.34	91.38	04/2014 -	03/2017
68	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017
69	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	486.44	03/2013 -	03/2014
70	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109	04/2010	2,069.60 -	2,298.42	24.59	03/2014 -	03/2016
71	Ghutiasharif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	128.61	12/2011 -	11/2013
72	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124	04/2006	850.00 -	2,446.81	8.94	03/2015 -	03/2017
73	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	5,000.00	3,604.73	03/2009 -	03/2014
74	Construction of NL from Kumarghat-Agartala - [N22000194	04/1999	895.00 -	1,151.00	944.66	03/2007 -	03/2015
	Total		24,179.51 -	249,242.17	150,731.86		
	<u>Road Transport & Highways</u>						
75	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	142.58	09/2008 -	03/2014
76	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	309.90	05/2008 -	09/2013
77	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	90.10	04/2009 -	12/2014
78	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	119.93	11/2008 -	06/2014
79	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	67.44	09/2007 -	04/2014

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
80	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	150.29	07/2009 -	05/2014
81	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
82	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	233.02	09/2007 -	03/2014
83	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	12/2013
	Total		2,933.01 -	254,252.74	155,490.25		
	<u>Shipping & Ports</u>						
84	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00 -	1,460.00	963.01	12/2010 -	03/2014
85	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	137.00	03/2006 -	12/2013
86	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	3,661.95	01/2012 -	08/2013
	Total		4,878.00 -	260,462.74	160,252.21		
	<u>Steel</u>						
87	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10,478.48	10/2009 -	08/2013
88	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	352.58	12/2011 06/2010	12/2013
89	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	147.26	10/2012 -	09/2013
90	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	14,889.86	12/2011 -	12/2013
91	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	230.00 -	343.58	260.62	02/2011 -	08/2013
	Total		23,768.89 -	290,329.17	186,381.01		
	<u>Telecommunications</u>						
92	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013
93	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle [N26000090]	11/2009	916.70 -	930.60	828.80	11/2010 -	09/2013
	Total		1,065.85 -	291,418.49	187,291.54		
	Grand Total		182,865.57	1,739,869.09	1,128,250.42		

List of Projects without Milestones w.r.t. Original Schedule

				(Jul,2013)		
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Civil Aviation</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	09/2013	0/0
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI - [N04000072]AAI,Multi State	02/2010	344.28 -	03/2014 -	03/2014	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	12/2014	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Chandigarh	02/2011	452.00 -	03/2015 -	03/2015	0/0
8	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60 -	03/2015 -	03/2015	0/0
	Total		6,035.46 -			0/0
	<u>Coal</u>					
9	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	04/2014 -	04/2014	0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
	Total		1,570.15 -			0/0
	<u>Steel</u>					
11	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhatisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	08/2014 -	08/2014	0/0
12	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	12/2014 -	12/2014	0/0
13	Coke Oven Battery-5 - [N12000080]SAIL,West Bengal	03/2012	339.35 -	06/2015 -	06/2015	0/0
	Total		926.90 -			0/0
	<u>Petroleum</u>					
14	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00	09/2013	09/2013	0/0
16	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02	06/2012	09/2013	0/0
17	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18	06/2012	09/2013	0/0
18	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	03/2010 03/2012	12/2013	0/0
19	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	12/2013	12/2013	0/0
20	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	09/2012	12/2013	0/0
21	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	04/2012	12/2013	0/0
22	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57	04/2012	12/2013	0/0
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	10/2011	12/2013	0/0
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	10/2011	12/2013	0/0
25	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	02/2014	0/0
26	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	02/2014	0/0
27	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	02/2014	02/2014	0/0
28	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	03/2014	0/0
29	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2014	0/0
30	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	06/2012	05/2014	0/0
31	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81	08/2014	10/2014	0/0
32	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	10/2010	12/2014	0/0
33	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	09/2011	12/2014	0/0
34	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00	12/2014	12/2014	0/0
35	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00	12/2014	12/2014	0/0
36	Reconstruction of BPA & BPB Platforms - [N16000161]ONGC,Maharashtra	03/2013	1,138.50	04/2015	04/2015	0/0
37	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00	07/2015	07/2015	0/0
38	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00	07/2015	08/2015	0/0
39	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00	11/2015	11/2015	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
41	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
42	Integrated Development of Bassein Field - [N16000160]ONGC,Maharashtra	12/2012	3,513.07 -	02/2016 -	02/2016	0/0
43	IROP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
44	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	06/2016	0/0
45	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2016	0/0
46	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2016	0/0
47	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	03/2017	0/0
48	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
49	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	-	0/0
50	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu	05/2013	711.00 -	- -	-	0/0
51	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	- -	-	0/0
	Total		88,648.65 -			0/0
	<u>Power</u>					
52	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
53	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
54	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	11/2014	0/0
55	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	11/2014	0/0
56	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	06/2015 -	06/2015	0/0
57	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
	Total		5,801.60 -			0/0
	<u>Railways</u>					
58	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
59	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
60	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
61	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
62	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
63	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
64	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
65	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011	0/0
66	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
67	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
68	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
69	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
70	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
71	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
72	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
73	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
74	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	03/2012	0/0
75	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
76	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
77	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
78	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
79	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
80	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
81	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
82	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
83	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
84	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
85	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
86	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
87	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
88	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
89	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
90	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
91	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
92	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
93	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013	0/0
94	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	09/2013	0/0
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
96	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
97	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
98	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
99	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	12/2013	0/0
100	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
101	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2014	0/0
102	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
103	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
104	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
105	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
106	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
107	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
108	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
109	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
110	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	03/2014	0/0
111	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	- -	03/2014	0/0
112	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244]ER,Multi State	04/2009	257.42 -	03/2014 -	03/2014	0/0
113	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	- -	04/2014	0/0
114	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
115	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
116	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
117	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
118	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
119	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	12/2014	0/0
120	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	02/2015	0/0
121	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
122	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
123	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
124	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
125	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2015	0/0
126	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2015	0/0
127	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
128	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
129	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0
130	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	03/2015 -	03/2015	0/0
131	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	03/2007 -	03/2015	0/0
132	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	- -	03/2015	0/0
133	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	- -	03/2015	0/0
134	Plassey-Jiaganj Doubling - [N22000220]ER,Multi State	04/2011	248.07 -	03/2015 -	03/2015	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
135	Krishnanagar-Bethua Dahri doubling - [N22000226]ER,Multi State	04/2009	151.65 -	03/2015 -	03/2015	0/0
136	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
137	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
138	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2015	0/0
139	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
140	Dangoaposi-Rajkharwan 3rd line Doubling - [N22000164]SER,Jharkhand	04/2010	309.44 -	12/2015 -	12/2015	0/0
141	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 -	03/2016	0/0
142	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
143	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
144	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
145	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20 -	- -	03/2016	0/0
146	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
147	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
148	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	12/2016	0/0
149	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
150	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
151	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
152	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2017	0/0
153	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
154	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
155	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER,Multi State	04/2011	299.60 -	03/2017 -	03/2017	0/0
156	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State	04/2010	423.66 -	03/2017 -	03/2017	0/0
157	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
158	Dholpur-Sirmuttra with extension to Gangapurcity & Mohari-Ta - [N22000158]NCR,Multi State	04/2010	622.41 -	02/2019 -	02/2019	0/0
159	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State	04/2011	1,176.09 -	02/2020 -	02/2020	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
160	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
161	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
162	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	- -	-	0/0
163	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-	0/0
164	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
165	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
166	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	-	0/0
167	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
168	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
169	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-	0/0
170	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-	0/0
171	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-	0/0
172	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-	0/0
173	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-	0/0
174	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-	0/0
175	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	- -	-	0/0
176	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	- -	-	0/0
177	Dahod-Indore via Sardarpur, Jhabua & Dhar - [N22000139]WR,Multi State	04/2007	1,640.04 -	- -	-	0/0
178	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	- -	-	0/0
179	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	- -	-	0/0
180	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	- -	-	0/0
181	Rajkot-Veraval,Wansjalvia to Jatalasr with new MM for Shapur- - [N22000143]WR,Gujarat	04/1994	320.66 -	- -	-	0/0
182	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	- -	-	0/0
183	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	- -	-	0/0
184	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	- -	-	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
185	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.39 -	- -	-	0/0
186	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	- -	-	0/0
187	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	- -	-	0/0
188	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittisurgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	- -	-	0/0
189	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner & Ratangarh-De - [N22000153]NWR,Rajasthan	04/2010	739.65 -	- -	-	0/0
190	Guriya-Marwar & Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	- -	-	0/0
191	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	- -	-	0/0
192	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	- -	-	0/0
193	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	- -	-	0/0
194	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	- -	-	0/0
195	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	- -	-	0/0
196	Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	- -	-	0/0
197	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	06/2013 -	-	0/0
198	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	- -	-	0/0
199	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	- -	-	0/0
200	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	- -	-	0/0
201	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	- -	-	0/0
202	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	- -	-	0/0
203	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	- -	-	0/0
204	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	- -	-	0/0
205	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	- -	-	0/0
206	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	- -	-	0/0
207	Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	- -	-	0/0
208	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	- -	-	0/0
209	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	- -	-	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
210	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	- -	-	0/0
211	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	- -	-	0/0
212	Sakri-Nirmali & Jhanjharpur-Laukahabazar & Saharsa-Forbesgan - [N22000180]ECR,Bihar	04/2004	372.14 -	- -	-	0/0
213	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar	04/2009	470.00 -	- -	-	0/0
214	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	- -	-	0/0
215	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	- -	-	0/0
216	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	- -	-	0/0
217	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	- -	-	0/0
218	Sriperumbudur-Guduvanchery with spur to Irungattukottai-Ava - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	- -	-	0/0
219	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	- -	-	0/0
220	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	- -	-	0/0
221	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	- -	-	0/0
222	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	- -	-	0/0
223	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	- -	-	0/0
224	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	- -	-	0/0
225	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	- -	-	0/0
226	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	- -	-	0/0
227	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	- -	-	0/0
228	Madurai-Rameswaram-GC - [N22000200]SR,Tamil Nadu	04/1999	240.00 -	- -	-	0/0
229	Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	- -	-	0/0
230	Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	- -	-	0/0
231	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	- -	-	0/0
232	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	- -	-	0/0
233	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	- -	-	0/0
234	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	- -	-	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
235	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	- -	-	0/0
236	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	- -	-	0/0
237	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line & - [N22000209]NEFR,Multi State	04/1999	523.17 -	- -	-	0/0
238	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12 -	- -	-	0/0
239	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam	04/2012	246.07 -	- -	-	0/0
240	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal	04/2009	573.78 -	- -	-	0/0
241	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP,Andhra Pradesh	04/2012	632.68 -	04/2012 -	-	0/0
242	Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State	04/2011	601.43 -	- -	-	0/0
243	Lakshmikantapur-Namkhana subsequently MM for Namkhana-Chandr - [N22000216]ER,Multi State	04/1999	406.99 -	- -	-	0/0
244	Sultanganj-Katuria via Asarganj, Tarapur & Belhar - [N22000217]ER,Multi State	04/2007	450.00 -	- -	-	0/0
245	Hansnabad-Hingalgaon New BG line - [N22000218]ER,Multi State	04/2010	172.03 -	- -	-	0/0
246	Pirpainti-Jasidih - [N22000219]ER,Multi State	04/2013	915.98 -	- -	-	0/0
247	Bandel-Boinchi 3rd line - [N22000221]ER,Multi State	04/2011	288.35 -	- -	-	0/0
248	Pirpainti-Bhagalpur - [N22000222]ER,Multi State	04/2011	261.38 -	- -	-	0/0
249	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State	04/2000	157.17 -	- -	-	0/0
250	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER,Multi State	04/2001	923.52 -	- -	-	0/0
251	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER,Multi State	04/2005	595.91 -	- -	-	0/0
252	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER,Multi State	04/2010	174.56 -	- -	-	0/0
253	Sondalia-Champapukur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State	04/2010	277.28 -	- -	-	0/0
254	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER,Multi State	04/2010	296.44 -	- -	-	0/0
255	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State	04/2010	157.94 -	- -	-	0/0
256	Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra	04/2008	697.00 -	- -	-	0/0
257	Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra	04/2011	277.70 -	- -	-	0/0
258	Bariarpur-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State	04/2007	450.55 -	- -	-	0/0
259	Tarakeswar-Magra New BG line - [N22000235]ER,Multi State	04/2010	365.17 -	- -	-	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
260	Hansdiha-Godda NL - [N22000236]ER,Multi State	04/2011	267.09 -	- -	-	0/0
261	Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State	04/2011	193.44 -	- -	-	0/0
262	Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State	04/2011	175.80 -	- -	-	0/0
263	New Alipur to Akra, MM for Budge Budge-Pujali NL, Pujali-Ulu - [N22000240]ER,Multi State	04/2010	494.54 -	- -	-	0/0
264	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State	04/2000	297.47 -	- -	-	0/0
265	Chandpara-Bangaon doubling with extension to Chandbazar & new - [N22000242]ER,Multi State	04/2003	337.96 -	- -	-	0/0
266	Magrahat-Diamond Harbour with MM Sangrampur-Krishanchandpur - [N22000243]ER,Multi State	04/2009	493.96 -	- -	-	0/0
267	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	- -	-	0/0
268	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	- -	-	0/0
269	Santoshpur-Remount Road via Garden Reach- Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	- -	-	0/0
270	Howrah-Development of station including segregation of aariv - [N22000249]ER,Multi State	04/2011	166.89 -	- -	-	0/0
271	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	- -	-	0/0
272	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	- 12/2017	-	0/0
273	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
274	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-	0/0
275	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
276	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
277	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
278	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
279	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
280	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
281	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
282	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
283	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
284	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
285	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
286	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
287	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-	0/0
288	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
289	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
290	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
291	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
292	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
293	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
294	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
295	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		121,304.18 -			0/0
	<u>Road Transport & Highways</u>					
296	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008	0/0
297	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
298	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	06/2013	0/0
299	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	06/2013	0/0
300	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	06/2013	0/0
301	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	02/2004 -	06/2013	0/0
302	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2013	0/0
303	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	08/2013	0/0
304	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	08/2013	0/0
305	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	08/2013	0/0
306	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	08/2013	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
307	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	07/2012	08/2013	0/0
308	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	12/2012	08/2013	0/0
309	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	08/2013	08/2013	0/0
310	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
311	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29	08/2013	08/2013	0/0
312	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
313	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	08/2013	08/2013	0/0
314	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	08/2013	08/2013	0/0
315	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	05/2008	09/2013	0/0
316	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	10/2008	09/2013	0/0
317	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	06/2008	09/2013	0/0
318	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	06/2009	09/2013	0/0
319	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	05/2012	09/2013	0/0
320	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
321	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	05/2013	09/2013	0/0
322	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	06/2013	09/2013	0/0
323	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	02/2013	09/2013	0/0
324	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
325	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	05/2010	10/2013	0/0
326	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	05/2012	10/2013	0/0
327	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	01/2013	10/2013	0/0
328	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00	07/2013	10/2013	0/0
329	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	02/2013	10/2013	0/0
330	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
331	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	01/2013	10/2013	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
332	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	11/2013	0/0
333	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
334	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
335	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
336	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
337	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	12/2013	0/0
338	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2013	0/0
339	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2013	0/0
340	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2013	0/0
341	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	12/2013	0/0
342	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	12/2013	0/0
343	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2013	0/0
344	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	12/2013	0/0
345	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2013	0/0
346	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	12/2013	0/0
347	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	12/2013	0/0
348	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	12/2013	0/0
349	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	12/2013	0/0
350	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	12/2013	0/0
351	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	12/2013	0/0
352	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	12/2013	0/0
353	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	12/2013	0/0
354	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
355	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
356	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	12/2013	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
357	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	12/2013	0/0
358	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	12/2013	0/0
359	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	12/2013	0/0
360	SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39 -	12/2013 -	12/2013	0/0
361	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
362	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
363	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
364	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
365	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
366	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
367	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2014	0/0
368	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2014	0/0
369	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
370	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
371	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
372	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	03/2014	0/0
373	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
374	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
375	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	03/2014	0/0
376	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
377	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2014	0/0
378	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
379	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
380	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	03/2014	0/0
381	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
382	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
383	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
384	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
385	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
386	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
387	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
388	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
389	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
390	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
391	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
392	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
393	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
394	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
395	2laning with PS Gopalganj-Chhapra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
396	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
397	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
398	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
399	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2014	0/0
400	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
401	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
402	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
403	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
404	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
405	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
406	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2014	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
407	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
408	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
409	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
410	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
411	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	07/2014 -	07/2014	0/0
412	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	08/2014	0/0
413	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
414	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
415	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,Gujarat	03/2012	828.00 -	09/2014 -	09/2014	0/0
416	REENGUS SIKAR - [N24000227]NHAI,Rajasthan	03/2012	333.51 -	09/2014 -	09/2014	0/0
417	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
418	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
419	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	10/2014 -	10/2014	0/0
420	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,Madhya pradesh	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
421	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	11/2014	0/0
422	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
423	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
424	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
425	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2014	0/0
426	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
427	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	01/2014 -	12/2014	0/0
428	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	02/2015	0/0
429	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
430	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
431	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
432	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
433	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
434	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
435	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
436	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	11/2015	0/0
437	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	12/2015 -	12/2015	0/0
438	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
439	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		99,650.09 -			0/0
	<u>Shipping & Ports</u>					
440	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
441	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 09/2011	09/2011	0/0
442	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
443	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
444	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
445	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
446	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
447	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013	0/0
448	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
449	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
450	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 10/2013	10/2013	0/0
451	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
452	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 12/2013	12/2013	0/0
453	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
454	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	03/2014	0/0
455	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
456	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
457	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	08/2012	0/0
	Total		15,462.28 -			0/0
	<u>Telecommunications</u>					
458	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
459	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
460	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
461	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
462	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	09/2013	0/0
463	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	12/2013	0/0
464	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	12/2013	0/0
465	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	12/2013	0/0
466	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
467	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
468	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
469	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
470	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 02/2013	-	0/0
	Total		5,699.24 -			0/0
	<u>Urban Development</u>					
471	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
472	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
473	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0

			(Jul,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		37,850.18 -			0/0
	<u>Water Resources</u>					
474	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		383,491.63			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(Jul,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Petroleum</u>						
1	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	9/2001	345.10 663.69	750.00	729.07	03/2007 03/2014	12/2013
2	IOR GELEKI (ONGCL) - [160100216	9/2001	390.09 1,674.11	1,674.11	1,727.24	03/2007 03/2017	12/2013
	Total		735.19 -	2,424.11	2,456.31		
	<u>Power</u>						
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	75.55	06/2016 -	04/2015
4	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	209.13	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	284.68		
	Grand Total		4,179.28	5,868.20	2,740.99		

List of Projects on schedule w.r.t. Latest Schedule

(Jul,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	117.24	03/2015 -	03/2015
2	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]	2/2010	344.28 -	344.28	-	03/2014 -	03/2014
	Total		1,013.88 -	1,013.88	117.26		
	<u>Coal</u>						
4	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	160.76	03/2015 03/2015	03/2015
5	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	149.76	03/2017 -	03/2017
6	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	45.17	03/2016 -	03/2016
7	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	88.71	03/2016 -	03/2016
9	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	38.66	03/2014 -	03/2014
10	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.06	07/2016 -	07/2016
11	RAMAGUNDUM OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	-	06/2015 -	06/2015
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	52.44	03/2016 -	03/2016
13	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
14	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
15	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	14.02	03/2015 -	03/2015
16	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
17	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.88	03/2018 03/2018	03/2018

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.30	03/2020 -	03/2020
20	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	264.37	03/2016 -	03/2016
21	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	49.93	03/2015 -	03/2015
22	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
23	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	72.34	03/2015 -	03/2015
24	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	45.02	03/2014 03/2014	03/2014
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	446.32	03/2016 03/2016	03/2016
	Total		10,739.01 -	10,367.67	1,484.22		
	<u>Petrochemicals</u>						
26	Assam gas Cracker project - [N16000106]	4/2006	5,460.61 -	8,920.00	4,510.51	04/2012 12/2013	12/2013
	Total		5,460.61 -	8,920.00	4,510.51		
	<u>Petroleum</u>						
27	Wax Project - [N16000101]	6/2010	576.60 -	576.60	225.00	12/2013 -	12/2013
28	Reconstruction of BPA & BPB Platforms - [N16000161]	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
29	Integrated Development of Bassein Field - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
30	Pipeline Replacement Project, Ahmedabad - [N16000159]	9/2011	202.25 -	202.25	-	07/2016 -	07/2016
31	Mounded Bullet Project at CPCL - [N16000154]	12/2012	279.00 -	279.00	-	12/2014 -	12/2014
32	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	32.13	07/2015 -	07/2015
33	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]	6/2009	486.00 -	486.00	54.56	09/2013 -	09/2013
34	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
35	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	72.54	11/2015 -	11/2015
36	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	97.03	12/2014 -	12/2014
37	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	67.27	03/2014 -	03/2014

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
38	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	435.83	05/2014 -	05/2014
39	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	80.56	12/2014 -	12/2014
40	Construction of three ETPs, Mehsana - [N16000135]	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
41	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]	10/2011	200.69 -	200.69	2.96	07/2014 -	07/2014
42	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	11.10	05/2014 -	05/2014
43	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,116.82	05/2015 -	05/2015
44	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,665.65	188.07	03/2015 -	03/2015
45	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	4,978.58	02/2014 -	02/2014
46	Development of Cluster-7 Fields - [N16000104]	3/2010	3,241.03 -	6,638.94	1,451.42	03/2013 11/2014	11/2014
	Total		35,844.15 -	38,752.82	8,830.95		
	<u>Power</u>						
47	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	387.19	01/2015 -	01/2015
48	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	955.49	09/2014 -	09/2014
49	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	722.79	12/2013 -	12/2013
50	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	1,034.60	05/2014 -	05/2014
51	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]	3/2011	2,569.25 -	2,569.25	1,718.22	03/2014 -	03/2014
52	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	309.32	10/2013 -	10/2013
53	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	181.21	06/2014 -	06/2014
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV [N18000128]	11/2011	723.63 -	723.63	174.41	11/2014 -	11/2014
55	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	306.40	08/2014 -	08/2014
56	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	40.12	06/2014 -	06/2014

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	750.21	06/2015 -	06/2015
58	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	12.44	03/2014 -	03/2014
59	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
60	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	357.08	10/2014 -	10/2014
61	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	40.34	08/2014 -	08/2014
62	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	391.06	02/2015 -	02/2015
63	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
64	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	91.41	03/2015 -	03/2015
66	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	368.00	08/2015 -	08/2015
67	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,558.00	11/2016 -	11/2016
68	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,074.00	09/2016 -	09/2016
69	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	1,700.00	12/2016 -	12/2016
70	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	224.31	11/2014 -	11/2014
71	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	823.01	10/2014 -	10/2014
72	Gadarwara Super Thermal Power Project Stage-I - [N18000151]	2/2013	11,638.55 -	11,638.55	-	09/2017 -	09/2017
73	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	144.20	06/2015 -	06/2015
74	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
75	COMMON TR. SYS. ASSOCIATED WITH EAST COAST & NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017
77	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,082.00	05/2017 -	05/2017
78	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	105.28	01/2014 -	01/2014
79	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	351.54	01/2015 -	01/2015
80	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	97.42	08/2014 -	08/2014
81	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	116.91	08/2014 -	08/2014
82	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	305.43	02/2014 -	02/2014
83	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	411.38	08/2014 -	08/2014
84	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	976.32	07/2014 -	07/2014
85	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	824.57	08/2014 -	08/2014
86	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	1,025.01	12/2013 -	12/2013
	Total		111,609.53 -	111,609.53	18,729.19		
	<u>Railways</u>						
87	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	84.10	02/2015 -	02/2015
88	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02 -	2,913.51	314.60	03/2016 -	03/2016
89	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	173.31	03/2016 -	03/2016
90	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088]	4/2006	325.00 -	1,116.53	216.92	03/2010 03/2017	03/2017
91	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]	4/2008	829.74 -	829.74	27.24	03/2015 -	03/2015
92	Suratpura - Hanumangarh - Sriganganagar Gauge Conversion (NWR) - [N22000114]	4/2008	516.23 -	516.23	388.06	03/2014 -	03/2014
93	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	642.18	03/2014 -	03/2014
94	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura Sharif NL - [N22000244]	4/2009	257.42 -	257.42	32.29	03/2014 -	03/2014

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
95	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]	4/2011	299.60 -	299.60	1.09	03/2017 -	03/2017
96	Krishnanagar-Bethua Dahri doubling - [N22000226]	4/2009	151.65 -	151.65	-	03/2015 -	03/2015
97	Plassey-Jiaganj Doubling - [N22000220]	4/2011	248.07 -	248.07	8.13	03/2015 -	03/2015
98	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]	4/2010	309.44 -	388.67	39.53	12/2015 -	12/2015
99	Champajharan-Bimalgarh Doubling extension - [N22000162]	4/2010	149.90 -	177.38	36.46	03/2015 -	03/2015
100	Dholpur-Sirmuttra with extension to Gangapurcity & Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]	4/2010	622.41 -	2,030.50	1.20	02/2019 -	02/2019
101	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.52	02/2020 -	02/2020
102	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
103	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]	4/2010	423.66 -	423.66	130.65	03/2017 -	03/2017
104	Ghutiasharif-Canning (ER) - [N22000117]	4/2009	189.97 -	611.03	128.61	12/2011 11/2013	11/2013
105	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	4/2008	653.19 -	653.46	245.66	03/2014 -	03/2014
	Total		19,170.80 -	25,497.52	2,471.55		
	<u>Road Transport & Highways</u>						
106	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139]	9/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013
107	Talegaon-amravati - [N24000140]	11/2009	567.00 -	567.00	1,131.20	11/2013 -	11/2013
108	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,284.70	10/2014 -	10/2014
109	ROHTAK-BAWAL - [N24000169]	5/2011	650.00 -	650.00	1,086.30	11/2013 -	11/2013
110	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
111	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	38.90	07/2014 -	07/2014
112	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	131.37	10/2014 -	10/2014
113	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	13.50	09/2015 -	09/2015
114	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	148.12	08/2015 -	08/2015
115	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	190.43	06/2014 -	06/2014
116	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	189.14	06/2015 -	06/2015

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
117	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	243.51	04/2014 -	04/2014
118	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI [N24000211]	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
119	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	282.58	10/2014 -	10/2014
120	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	-	09/2014 -	09/2014
121	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC [N24000226]	10/2011	1,565.00 -	1,565.00	-	10/2014 -	10/2014
122	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	463.63	09/2014 -	09/2014
123	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	302.56	04/2015 -	04/2015
124	SAMAIKHIALI GANDHIDHAM - [N24000223]	9/2010	805.39 -	805.39	543.70	12/2013 -	12/2013
125	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	30.80	12/2015 -	12/2015
126	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	463.54	07/2014 -	07/2014
127	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	81.70	01/2014 -	01/2014
128	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,005.50	09/2014 -	09/2014
129	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]	12/2011	1,047.00 -	1,047.00	201.93	06/2014 -	06/2014
130	4-laning of Raiganj-Dalkola - [N24000204]	2/2011	580.43 -	580.43	257.54	08/2013 -	08/2013
131	4-laning of Brahampore-Faraka - [N24000203]	2/2011	998.79 -	998.79	1,172.60	08/2013 -	08/2013
132	4-laning of Faraka-Raiganj - [N24000202]	2/2011	1,078.84 -	1,078.84	1,198.20	08/2013 -	08/2013
133	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.37	04/2014 -	04/2014
134	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	637.40	03/2014 -	03/2014
135	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 [N24000183]	11/2011	1,535.00 -	1,535.00	1,162.30	05/2014 -	05/2014
136	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	864.87	03/2014 -	03/2014
137	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	288.77	02/2014 -	02/2014
138	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	511.33	01/2014 -	01/2014
139	Tirupati - Tiruthani - Chennai - [N24000178]	4/2011	571.00 -	571.00	-	10/2013 -	10/2013

(Jul,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
140	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
141	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 [N24000172	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
142	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	346.82	09/2013 -	09/2013
143	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,255.70	06/2014 -	06/2014
144	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	941.91	05/2014 -	05/2014
145	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	505.64	08/2013 -	08/2013
146	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	122.65	01/2014 -	01/2014
147	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	435.68	02/2014 -	02/2014
148	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	161.02	05/2014 -	05/2014
149	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
150	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	626.59	11/2013 -	11/2013
151	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,260.10	08/2013 -	08/2013
152	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168	3/2011	785.50 -	785.50	817.69	08/2013 -	08/2013
	Total		43,576.03 -	43,576.03	21,049.92		
	<u>Shipping & Ports</u>						
153	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	137.00	03/2006 12/2013	12/2013
154	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051	8/2010	612.72 -	532.83	418.64	12/2012 10/2013	10/2013
155	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 -	1,012.23	554.60	12/2013 11/2013	11/2013
156	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
157	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		3,269.15 -	3,651.75	1,580.16		
	<u>Steel</u>						
158	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072	4/2011	572.00 -	572.00	316.17	04/2013 12/2013	12/2013

(Jul,2013)

						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
159	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]	2/2011	898.55 -	898.55	209.28	05/2013 11/2013	11/2013
160	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh - [N12000078]	7/2012	332.65 -	332.65	64.42	08/2014 -	08/2014
161	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]	1/2012	254.90 -	254.90	3.46	12/2014 -	12/2014
162	Rebuilding of Battery Block 5A and Re-construction of Battery Block 5B - [N12000080]	3/2012	339.35 -	339.35	9.05	06/2015 -	06/2015
	Total		2,397.45 -	2,397.45	602.38		
	<u>Urban Development</u>						
163	DELHI MRTS PHASE-III - [N28000056]	9/2011	35,242.00 -	35,242.00	3,853.30	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	3,853.30		
	Grand Total		268,322.61	281,028.65	63,229.44		

List of Delayed Projects w.r.t. Latest Schedule

(Jul,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,354.00	12/2008 -	06/2014	66	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,681.60	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,991.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,074.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,100.60				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	228.60	05/2012 -	09/2013	16	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.80	01/2011 04/2013	12/2014	47	20
	Total		645.07 -	645.07	460.40				
	<u>Coal</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,747.67	06/2009 -	01/2014	55	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.27	03/2010 -	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.36	03/2011 -	03/2014	36	-
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.85	03/2013 -	03/2014	12	-
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,478.68	03/2012 -	03/2014	24	-
12	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	112.35	03/2012 -	03/2014	24	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	721.74	03/2013 09/2012	10/2014	19	25
14	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.66	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.62	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.44	03/2010 -	03/2015	60	-
17	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	114.33	03/2013 -	03/2015	24	-
18	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.48	03/2012 -	03/2015	36	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.24	03/2013 -	03/2015	24	-
20	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,415.57	03/2014 -	03/2016	24	-
21	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,253.35	03/2014 -	03/2016	24	-
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016	44	-
23	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	265.66	03/2014 -	03/2016	24	-
24	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	87.20	12/2012 -	03/2016	39	-
25	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24	-
26	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.01	03/2014 -	03/2016	24	-
27	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
28	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24	-
29	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
30	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	128.14	03/2012 -	03/2016	48	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72	-
32	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
33	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60	-
34	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	32.00	12/2015 -	02/2018	26	-
	Total		24,633.81 -	28,090.60	12,666.28				
	<u>Steel</u>								
35	EXPANSION OF RINLVSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,478.48	10/2009 10/2012	08/2013	46	10
36	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 343.58	343.58	260.62	02/2011 02/2011	08/2013	30	30
37	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 216.68	216.68	147.26	10/2012 10/2012	09/2013	11	11
38	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	276.50	05/2012 05/2012	09/2013	16	16
39	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	352.58	12/2011 03/2012	12/2013	24	21
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	14,889.86	12/2011 -	12/2013	24	-
41	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,662.34	12/2011 -	12/2013	24	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,679.32	03/2013 -	12/2013	9	-
43	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,691.38	12/2012 -	03/2014	15	-
44	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	76.05	10/2013 -	06/2014	8	-
45	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	9,923.03	03/2013 -	09/2014	18	-
46	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	68.64	11/2013 -	06/2015	19	-
	Total		62,967.77 -	69,035.31	51,506.06				
	<u>Petroleum</u>								
47	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - - [N16000070]GAIL,Multi State	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	18	-
48	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	156.85	10/2011 -	07/2013	21	-
49	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	23	17
50	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	189.49	02/2013 -	08/2013	6	-
51	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	09/2013	12	-
52	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24	16
53	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,469.11	04/2013 -	09/2013	5	-
54	Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12	-
55	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	128.88	06/2012 -	09/2013	15	-
56	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	57.73	06/2012 -	09/2013	15	-
57	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	624.66	01/2013 -	10/2013	9	-
58	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,458.39	01/2012 -	10/2013	21	-
59	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	228.26	11/2012 -	10/2013	11	-
60	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	726.73	12/2011 -	11/2013	23	-
61	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93	9
62	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	729.24	03/2010 03/2012	12/2013	45	21
63	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	260.22	03/2012 -	12/2013	21	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
64	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	725.28	07/2012 -	12/2013	17	-
65	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	98.45	09/2012 -	12/2013	15	-
66	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	240.31	03/2013 -	12/2013	9	-
67	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	228.47	04/2012 -	12/2013	20	-
68	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	651.11	04/2012 -	12/2013	20	-
69	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPR,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26	-
70	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPR,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26	-
71	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	62.49	08/2013 -	01/2014	5	-
72	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
73	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	02/2014	43	21
74	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
75	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
76	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,494.55	03/2013 -	03/2014	12	-
77	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	187.62	08/2012 -	03/2014	19	-
78	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	28.10	06/2012 -	03/2014	21	-
79	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	22,593.00	11/2012 -	04/2014	17	-
80	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,107.72	08/2010 03/2012	05/2014	45	26
81	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
82	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	957.44	01/2014 -	05/2014	4	-
83	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	276.67	05/2013 -	05/2014	12	-
84	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	4.00	03/2014 -	05/2014	2	-
85	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014	2	-
86	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50	-
87	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	360.28	09/2011 -	12/2014	39	-
88	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	4.12	01/2014 -	01/2015	12	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
89	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL, Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3	-
90	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00 -	586.00	17.03	07/2015 -	08/2015	1	-
91	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
92	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18 -	7,496.18	13.30	01/2013 -	12/2015	35	-
93	IREP - [N16000143]BPCL, Kerala	01/1999	14,225.00 -	14,225.00	453.95	12/2015 -	05/2016	5	-
94	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
95	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24	-
96	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24	-
97	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	03/2017	23	-
	Total		127,927.07 -	137,961.30	76,869.39				
	<u>Power</u>								
98	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATHI-III HEP - [N18000018]PGCIL, Himachal Pradesh	07/2006	557.24 -	775.25	644.73	01/2010 -	07/2013	42	-
99	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL, Multi State	10/2010	160.32 -	160.32	84.66	10/2012 -	08/2013	10	-
100	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19 -	184.19	156.80	11/2011 -	09/2013	22	-
101	System Strengthening -XII of SR - [N18000085]PGCIL, Multi State	02/2010	232.34 -	232.34	150.53	06/2012 -	09/2013	15	-
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL, Multi State	10/2010	182.68 -	182.68	131.59	01/2013 -	09/2013	8	-
103	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC, Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,762.78	11/2009 02/2013	10/2013	47	8
104	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC, Jammu and Kashmir	08/2006	611.01 -	936.00	752.82	08/2010 01/2013	10/2013	38	9
105	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,420.00	10/2012 -	11/2013	13	-
106	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL, Multi State	10/2006	975.96 -	975.96	884.62	10/2009 -	12/2013	50	-
107	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88 -	7,031.88	4,540.95	12/2012 -	12/2013	12	-
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State	02/2009	509.66 -	509.66	372.89	11/2011 -	12/2013	25	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, Multi State	02/2009	410.29 -	410.29	266.57	02/2012 -	12/2013	22	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
110	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	830.37	05/2012 -	12/2013	19	-
111	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,217.64	08/2013 -	12/2013	4	-
112	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	88.08	04/2013 -	12/2013	8	-
113	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	131.55	07/2013 -	12/2013	5	-
114	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,833.75	10/2010 01/2013	03/2014	41	14
115	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,607.63	01/2012 -	03/2014	26	-
116	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,580.90	2,054.21	08/2012 -	03/2014	19	-
117	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,835.42	08/2012 -	03/2014	19	-
118	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	595.85	11/2012 -	03/2014	16	-
119	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,113.89	03/2013 -	03/2014	12	-
120	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,646.55	12/2013 -	03/2014	3	-
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	308.88	07/2013 -	03/2014	8	-
122	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,467.53	10/2012 -	06/2014	20	-
123	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,326.81	12/2012 -	06/2014	18	-
124	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	895.00	08/2012 -	06/2014	22	-
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	355.89	11/2011 -	07/2014	32	-
126	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,031.00	04/2009 -	09/2014	65	-
127	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 1,117.92	1,117.92	646.69	08/2012 08/2013	09/2014	25	13
128	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,163.00	08/2013 -	09/2014	13	-
129	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	688.73	11/2012 -	09/2014	22	-
130	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	151.90	11/2013 -	09/2014	10	-
131	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,156.83	09/2009 06/2013	11/2014	62	17
132	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.74	01/2013 -	12/2014	23	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
133	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	950.74	11/2013 -	12/2014	13	-
134	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	442.17	07/2014 -	02/2015	7	-
135	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,593.11	11/2012 -	03/2015	28	-
136	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	869.10	04/2013 -	03/2015	23	-
137	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	35.47	04/2015 -	05/2015	1	-
138	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,315.50	08/2013 -	06/2015	22	-
139	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,938.00	07/2011 -	10/2015	51	-
140	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,857.00	03/2013 -	03/2016	36	-
141	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	358.03	07/2014 -	05/2016	22	-
142	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,706.11	01/2016 01/2016	11/2016	10	10
143	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,514.00	12/2009 -	02/2017	86	-
144	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	497.79	07/2010 02/2016	02/2017	79	12
145	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,417.91	05/2013 05/2013	03/2017	46	46
146	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,317.03	09/2010 08/2014	12/2017	87	40
147	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,505.44	09/2009 07/2014	03/2018	102	44
	Total		122,216.59 -	139,063.30	92,696.28				
	<u>Railways</u>								
148	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	226.51	03/2002 -	09/2013	138	-
149	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	578.57	03/1994 -	10/2013	235	-
150	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	392.93	12/2009 03/2011	10/2013	46	31
151	Bandel-Naihati new rail bridge in replacement of j - [N22000119]JR,West Bengal	04/1999	207.52 207.52	207.52	176.62	12/2012 -	12/2013	12	-
152	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
153	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	486.44	03/2013 -	03/2014	12	-
154	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,604.73	03/2009 -	03/2014	60	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
155	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014	66	66
156	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65	65
157	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	230.03	12/2008 -	09/2014	69	-
158	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	244.66	03/2004 12/2010	12/2014	129	48
159	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,104.99	03/2009 12/2012	12/2014	69	24
160	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	248.49	06/2013 06/2013	12/2014	18	18
161	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
162	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.01	03/2007 03/2007	03/2015	96	96
163	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	743.88	12/2010 12/2010	03/2015	51	51
164	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,473.98	12/2008 -	03/2015	75	-
165	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	124.52	12/2012 -	03/2015	27	-
166	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,151.00	944.66	03/2007 -	03/2015	96	-
167	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,798.00	04/2008 03/2014	12/2015	92	21
168	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,828.20	10/2007 12/2012	12/2015	98	36
169	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015	69	-
170	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	488.37	03/2014 -	12/2015	21	-
171	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	24.59	03/2014 -	03/2016	24	-
172	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	445.45	06/2005 07/2011	06/2016	132	59
173	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	50.61	03/2016 -	06/2016	3	-
174	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	477.57	03/2005 12/2008	12/2016	141	96
175	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,209.40	03/2014 03/2016	12/2016	33	9
176	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,529.74	03/2011 03/2014	03/2017	72	36
177	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	91.38	04/2014 -	03/2017	35	-
178	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15	-
179	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,446.81	8.94	03/2015 -	03/2017	24	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
180	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201	-
	Total		26,993.42 -	75,034.00	30,326.17				
	<u>Road Transport & Highways</u>								
181	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	195.52	08/2004 07/2010	08/2013	108	37
182	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	195.15	08/2004 -	08/2013	108	-
183	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	284.35	06/2011 06/2011	08/2013	26	26
184	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	08/2013	65	-
185	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31	-
186	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,319.40	07/2012 -	08/2013	13	-
187	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,968.50	12/2012 -	08/2013	8	-
188	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	309.90	05/2008 -	09/2013	64	-
189	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.92	10/2008 -	09/2013	59	-
190	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	262.59	06/2008 -	09/2013	63	-
191	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	09/2013	51	-
192	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,126.80	05/2012 -	09/2013	16	-
193	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	09/2013	4	-
194	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,341.40	06/2013 -	09/2013	3	-
195	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	645.56	02/2013 -	09/2013	7	-
196	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	652.98	05/2010 -	10/2013	41	-
197	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-
198	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	947.24	01/2013 -	10/2013	9	-
199	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	550.72	07/2013 -	10/2013	3	-
200	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.37	02/2013 -	10/2013	8	-
201	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9	-
202	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.24	09/2007 -	11/2013	74	-
203	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.91	10/2008 -	12/2013	62	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
204	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.53	01/2009 -	12/2013	59	-
205	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	461.55	09/2008 -	12/2013	63	-
206	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	285.56	06/2008 -	12/2013	66	-
207	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	300.84	06/2008 -	12/2013	66	-
208	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	206.40	05/2008 -	12/2013	67	-
209	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	252.67	06/2008 -	12/2013	66	-
210	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.51	06/2010 -	12/2013	42	-
211	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.19	09/2009 -	12/2013	51	-
212	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
213	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,024.30	09/2012 -	12/2013	15	-
214	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,838.80	10/2011 -	12/2013	26	-
215	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,700.30	08/2011 -	12/2013	28	-
216	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	12/2013	25	-
217	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	12/2013	8	-
218	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	811.61	03/2013 -	12/2013	9	-
219	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,123.30	11/2012 -	12/2013	13	-
220	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
221	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	114.73	05/2013 -	12/2013	7	-
222	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	612.91	03/2013 -	12/2013	9	-
223	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.21	07/2013 -	12/2013	5	-
224	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	507.47	05/2013 -	02/2014	9	-
225	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	239.49	09/2007 -	03/2014	78	-
226	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	142.58	09/2008 -	03/2014	66	-
227	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	238.88	06/2005 -	03/2014	105	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
228	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	247.36	06/2008 -	03/2014	69	-
229	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	285.21	06/2008 -	03/2014	69	-
230	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	337.60	10/2008 -	03/2014	65	-
231	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	204.62	04/2008 -	03/2014	71	-
232	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	265.28	04/2008 -	03/2014	71	-
233	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63	-
234	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	233.02	09/2007 -	03/2014	78	-
235	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	857.99	07/2010 -	03/2014	44	-
236	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	410.02	10/2011 -	03/2014	29	-
237	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	53.97	11/2012 -	03/2014	16	-
238	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,828.90	06/2013 -	03/2014	9	-
239	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	393.14	05/2013 -	03/2014	10	-
240	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	270.58	03/2013 -	03/2014	12	-
241	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	259.70	10/2013 -	03/2014	5	-
242	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	67.44	09/2007 -	04/2014	79	-
243	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.30	03/2013 -	04/2014	13	-
244	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	525.57	02/2014 -	04/2014	2	-
245	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	318.28	02/2009 03/2014	05/2014	63	2
246	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	302.87	04/2008 -	05/2014	73	-
247	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	150.29	07/2009 -	05/2014	58	-
248	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68	-
249	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	119.93	11/2008 -	06/2014	67	-
250	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	814.19	10/2011 -	06/2014	32	-
251	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
252	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	651.32	07/2013 -	06/2014	11	-
253	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53	-

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
254	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.15	09/2013 -	07/2014	10	-
255	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	181.53	07/2012 -	07/2014	24	-
256	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	302.85	09/2010 -	08/2014	47	-
257	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
258	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	284.89	04/2010 -	11/2014	55	-
259	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	90.10	04/2009 -	12/2014	68	-
260	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	59.83	11/2008 -	12/2014	73	-
261	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	159.85	04/2009 -	12/2014	68	-
262	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.37	12/2009 -	12/2014	60	-
263	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,128.20	02/2010 -	12/2014	58	-
264	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.55	01/2014 -	12/2014	11	-
265	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	315.83	08/2013 -	02/2015	18	-
266	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31	-
267	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,731.30	08/2014 -	07/2015	11	-
268	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.79	09/2014 -	10/2015	13	-
269	FOUR LANNING OF WALAYAR-VADAKKANANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	118.72	10/2013 -	11/2015	25	-
270	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
271	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	922.41	07/2015 -	06/2016	11	-
	Total		54,470.83 -	56,366.09	53,418.76				
	<u>Shipping & Ports</u>								
272	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	19	11
273	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	963.01	12/2010 09/2012	03/2014	39	18
	Total		4,728.00 -	5,610.00	4,624.96				
	<u>Telecommunications</u>								

(Jul,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
274	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL, Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34	9
275	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL, Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28	-
276	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttarakhand	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013	54	-
277	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
278	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
	Total		2,934.85 -	2,774.50	1,282.27				
	<u>Urban Development</u>								
279	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	2,494.00	258.11	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	258.11				
	Grand Total		470,453.41	563,800.17	350,209.28				
