

**305th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
March, 2011**



Secondary Runway Tamil nadu



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for March 2011 (the 305th Flash Report) contains information on the status of the 562 projects in the Central Sector costing ` 150 Crores and above. During March 2011, 17 projects have reported completion (which have now been dropped from the monitor of this Ministry). Sixteen new projects have been added during the month under reference.

The online submission of the implementation Status Report of the ongoing projects from the project authorities has improved considerably with all projects reporting online during the current month. This has been mainly due to the continuous effort/persuasion by this Ministry. During March 2011, eighty seven (87) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 36 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Telecommunications, Shipping & Ports, Civil Aviation, Mines and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	120	29
2.	RAILWAYS	138	7
3.	POWER	81	15
4.	PETROLEUM	77	15
5.	COAL	45	7
6.	TELECOMMUNICATION	41	1
7.	STEEL	13	5
8.	SHIPPING & PORTS	25	5
9.	CIVIL AVIATION	8	1
10.	FERTILISERS	6	0
11.	ATOMIC ENERGY	3	1
12.	URBAN DEVELOPMENT	3	0
13.	MINES	1	1
14.	WATER RESOURCES	1	0
Total		562	87

3. The total original cost of implementation of the 562 projects was about ` 6,13,026.37 Crores and their anticipated completion cost is likely to be ` 7,33,653.52 Crores, which reflects an overall cost overrun of 19.70%. The expenditure incurred on these projects till March, 2011 is ` 3,21,943.80 Crores.

4. Out of the 562 projects, 11 projects are ahead of schedule, 147 are on schedule and 266 projects are delayed and 90 projects have been sanctioned without any commissioning schedule/date. Further in case of 48 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently date of completion have been finalised. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month the project reporting delays have marginally decreased to 266 from 278 in February'2011. The overall cost overrun has also increased to 19.70% from 19% in February 2011. Out of 266 delayed projects, at the end of March, 2011, 62 projects had overall delay in the range of 1 to 12 months, 60 projects had delay in the range of 13 to 24 months, 108 projects had delay in the range of 25 to 60 months and 36 projects had delay of 61 months and above.

The Sector-wise details of delays are as under:-

i) In the **Coal sector**, 7 projects have reported additional delays in the range of 3-36 months. TPS-II Expansion (1470MW To 1970MW) NLC Project has reported additional delay of three months due to delay in equipments erection and inadequate mobilization by the contractor. Barsingsar TPS (2X125MW) NLC has reported additional delay of 3 months due to slow progress by the contractor. Ashok Expn. OCP-CCL (5 MTY) CCL has reported an additional delay of 12 months due to delay in land acquisition of forest land . North Urimari OCP CCL, Tapin OCP CCL, Magadh OC CCL have reported additional delays of 24 months, 24 months and 36 months respectively as clearance of forest land is still awaited. Churi Benti UG CCL has reported an additional delay of 36 months; however no specific reason has been reported by the project authority.

ii) In the **Steel sector**, 5 projects have reported additional delays in the range of 1-3 months. Rebuilding of Coke Oven Battery No-1 & 2 (Bokaro Steel Plant) SAIL, Rebuilding of Coke Oven Battery No-6 (Bokaro Steel Plant) SAIL has reported an additional delay of one month

and 2 months due to delay in supply of fireclay & silica brick by the contractor. 330 TPH Boiler-6 and Auxiliary System, RINL has reported an additional delay of one month due to increased cost of labour charge. 700TPD AIR Separation Unit-4 at Oxygen Plant-II, Bhilai, SAIL has reported an additional delay of 2 months due to termination of contract as the contractor demanded changes in terms and conditions. Expansion of IISCO Steel plant SAIL has reported an additional delay of 3 months due to delay in approval for commencement of work at Railway yards.

iii) In the **Petroleum Sector**, 15 projects have reported additional delays in the range of 1-8 months. Sultanpur Neemrana Pipeline Project (Superline to CJPL) GAIL has reported additional delay of one month as acquiring ROU has become difficult. Bawana Nangal Pipe Line Project GAIL has reported an additional delay of 2 months due to problems in acquiring ROU for construction of pipeline. BNPL Superlines (Uttanchal & Punjab) of GAIL has reported additional delay of 2 months due to delay pending Court cases for laying pipeline in Raja ji National Park. Dahej -Vijaypur Pipe Line Project (Phase-II) GAIL has reported an additional delay of 3 months as GAIL is filing case against the award of Rs. 41.27 Crore. MSQ Improvement Project IOCL has reported delay of 4 months due to delay in supply of accessories of recycle GAS compressor by 8 months. Construction of New Terminal at ENNORE, Chennai HPCL has reported an additional delay of 6 months due to heavy rain, cyclone in the past months and also due local problems. Diesel Hydrotreator Project at Mumbai Refinery HPCL has reported an additional delay of 6 months due to slow progress by the contractors. Hydrocracker Revamp & Setting BPCL, Compressor Stations (Vijaypur and Jhabua) Phase -1 GAIL, CDU/VDU-II CPCL, Diesel Hydro Treatment Project Dhaligaon BRPL, Integrated Sugar Ethanol Cogen Power plant at Sugauli HPCL, Diesel Hydrotreator Project at Visakh Refinery HPCL, Heera and South Heera Re-development Project ONGC, Development of C-Series Fields ONGC have reported an additional delay of one month, 2 months, 2 months, 3 months, 5 months, 6 months, 7 months and 8 months respectively, However no specific reason has been reported by the Project authorities.

iv) In the **Power Sector**, 15 projects have reported additional delays in the range of 1-9 months. Mouda STPP NTPC has reported an additional delay of 1 month due to shortage of manpower. Stage IV NHPC, Teesta Low Dam-III Hydroelectric Power Project NHPC have reported an additional delay of 2 months and 3 months due to strike by “Gorkha Janmukti

Morcha” (GJMM). Transmission System Associated with Uri-II HEP PGCIL has reported an additional delay of 2 months due to law & order problem. Koteswar Transmission System PGCIL, Est. of 400/220 KV GIS Pooling Station Near Chamer PGCIL have reported an additional delay of 3 months and 5 months respectively due to delay in generation project. East-West Transmission Corridor Strengthening Scheme PGCIL, Eastern Region Strengthening Scheme-I PGCIL, Eastern Region Strengthening Scheme-II PGCIL and Kudankulam-APP Trans. System PGCIL have reported an additional delay of 3 months, 3 months and 9 months due to ROW problem in Jharkhand, West Bengal and Kerala respectively. Western Region Strengthening Scheme-IX PGCIL has reported an additional delay of 3 months due to heavy rain. Transmission System Associated with Parbati-III HEP PGCIL has reported an additional delay of 5 months due to delay in civil work. Western Region Strengthening Scheme-II PGCIL has reported an additional delay of 6 months due to ROW problem and forest clearance. Transmission System for Startup Power to DVC & Maithon RB G PGCIL and Transmission System Associated with Chamara III HEP PGCIL have reported an additional delay of one month and 4 months respectively, However no specific reason has been reported by the project authorities.

v) In the **Road Transport and Highways Sector**, 29 projects have reported additional delay in the range of 1-12 months. 9 projects have reported additional delay of one month each due to slow progress of work by the contractor. Gonde-Vadape (Thane) NHAI, Garhmukteshwar-Muradabad NHAI, Lalitpur to Sagar KM 132 to KM 187 NHAI have reported additional delay of 2 months, 3 months and 4 months respectively due to delay in forest & environment clearance. Jhansi to Lalitpur NHAI has reported additional delay of 2 months due to delay in handing over encumbrance free site. Haveri-Harihar (GQ) NHAI and Harihar-Chitradurga NHAI have reported additional delay of 3 months each due to re-awarding of balance work. Kotwa to Dewapur NHAI has reported additional delay of 3 months due to delay in shifting of electric lines. Orai to Jhansi NHAI, Gwalior Bypass, NH-75, 3 NHAI and Neelamangalar Junction on NH-4 Smith NH-48 to Devi NHAI have reported an additional delay of 3 months each due to slow progress of work by the contractor. Meerut- Muzaffarnagar NHAI has reported an additional delay of 3 months due to delay in providing proof checking/Drawings for major bridge at river saryu. Lalitpur to Sagar NH-26 NHAI has reported an additional delay of 3 months due to delay in utility shifting. Ringbunds to Jhajhanpur NHAI has reported an additional delay of 3 months due to slow mobilization of

contractor. Sitapur –Lucknow NHAI has reported an additional delay of 3 months due to delay in providing proof checked/Drawings for major bridge. Jhansi to Lalitpur NHAI and Nalbari to Bijni NHAI have reported an additional delay of 3 months and 9 months due to delay in tree cutting by the state forest department and shifting of electric poles. Bangalore-Hoskote Mudbogal Section NH-4 NHAI has reported an additional delay of 3 months as the Hon'ble High court has put a stay on acquisition of some portion of land. New Mangalore Port, NHAI has reported an additional delay of 4 months due to delay in shifting of a religious structure. Thanjaur-Trichy NHAI has reported an additional delay of 9 months; however no specific reason has been given by the project authority. Silchar-Udarband NHAI has reported an additional delay of 12 months due to tree cutting and delay in utility shifting.

vi) In the Mines Sector, Second Phase Expansion of Captive Aluminium, Smelter and Power NALCO has reported an additional delay of two months due to slow progress by the contractor.

vii) In the Railway Sector, 7 projects have reported additional delay in the range of 5-15 months. Khurda Road-Bolangir (NL) ECOR, Lanjigarh-Junagarh NL ECOR, Talcher-Bimalagarh (NL) ECOR and Ext. of MRTS from Velachery to Saint. Thomas MTP, MRTP have reported an additional delay of 5 months, 6 months, 10 months and 15 months respectively due to delay in land acquisition and forest clearance. Electrification of Moradabad- Roza RE has reported an additional delay of 12 months due to delay in Route Relay Interlocking (RRI) of Muradabad and Roza. Electrification of Khurja-Meerut – Saharanpur & G'BA RE and Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves NWR have reported an additional delay of 12 months each. However no specific reason has not been given by the project authority.

viii) In the Telecommunication Sector, convergent Billing and CRM (Mumbai of MTNL) has reported additional delay of 5 months due to slow progress by the contractor.

ix) In the Shipping & Ports Sector, 5 projects have reported additional delay in the range of 1-7 months. Acquisition of 4 nos. of 80655 DWT Panamax Bulk CA Shipp, Acquisition of Two nos. of 3060 DWT Port Trust and Acquisition of Two nos. of 120 B.P Port Trust have reported additional delay of one month, 5 months and 7 months due to slow progress by the contractor. Deepening of Channel at Paradip Port Trust has reported additional delay of 3

months due to delay in tendering process. Establishment of Vessel Traffic Services in Gulf of Kutch Shipp has reported additional delay of 7 months. However no specific reason has been reported by the Project authority.

x) In the **Atomic Energy Sector**, Uranium ORE Mine & Processing Plant at Tummalapall UCIL has an additional delay of 8 months due to political disturbance due to Telangana issue.

xi) In the **Civil Aviation Sector**, Construction of New Airport at Pakyong (Sikkim) Airport, AAI has reported an additional delay of 17 months, however no specific reason has been reported by the Project authority.

The status as on 01.04.2011 in respect of completion of projects costing ` 150 Crores and above in different sectors during 2010-11 is indicated in the Report.



(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	138	7
2	Road Transport & Highways	120	29
3	Power	81	15
4	Petroleum	77	15
5	Coal	45	7
6	Telecommunications	41	1
7	Shipping & Ports	25	5
8	Steel	13	5
9	Civil Aviation	8	1
10	Fertilisers	6	0
11	Atomic Energy	3	1
12	Urban Development	3	0
13	Mines	1	1
14	Water Resources	1	0
	Total	562	87

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	168.33	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93
September,2010				
<u>Coal</u>				
8	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)(NEYVELI LIGNITE CORPORATION) - [060100090]	254.07	06/2009	1,687.78
<u>Steel</u>				
9	REBUILDING OF COKE OVEN BATTERY-10(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000016]	416.50	09/2009	305.14
<u>Petroleum</u>				
10	PANIPAT NAPHTHA CRACKER PROJECT(INDIAN OIL CORPORATION LIMITED) - [160100292]	12,138.00	09/2009	12,054.37

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	DADRI- PANIPAT R-LNG SPUR PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000018]	250.66	06/2008	350.96
12	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000026]	638.90	04/2009	796.21
13	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE(INDIAN OIL CORPORATION LIMITED) - [N16000034]	348.00	12/2009	186.58
14	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000035]	1,131.00	12/2009	750.71
15	CHAINSA-JHAJJAR PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000047]	967.77	09/2009	416.90
16	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000067]	643.46	-	726.45
17	Construction of Tank and Blending Facility at Vadi(INDIAN OIL CORPORATION LIMITED) - [N16000075]	267.00	-	72.99
18	BINA DESPATCH TERMINAL(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000078]	490.71	12/2009	590.52
<u>Railways</u>				
19	HOSPET-GUNTAKAL(LD),SCR(RAIL VIKAS NIGAM LTD.) - [220100195]	105.22	12/1999	283.49
20	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100224]	536.85	03/2003	1,005.50
21	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)(RAIL VIKAS NIGAM LTD.) - [220100244]	223.00	-	586.85
22	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000033]	352.00	03/2008	616.44
23	ABOHAR- FAZILKA, NR, NL(NORTHERN RAILWAY) - [N22000055]	86.44	03/2009	201.79
<u>Road Transport & Highways</u>				
24	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100203]	440.93	12/2006	641.40
25	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100204]	534.39	05/2007	716.15
26	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101178]	372.40	07/2004	406.05
27	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101181]	467.93	03/2005	453.64
28	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101187]	399.75	03/2005	424.96
29	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106227]	276.00	04/2008	360.00
30	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106228]	310.00	04/2008	392.26
31	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106241]	507.49	03/2008	342.80
32	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106257]	556.00	03/2009	568.50
33	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106273]	469.80	12/2008	665.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
34	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106285]	261.00	08/2008	286.30
35	TOVARAMKURCHI-MADURAI, NH45B (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000054]	263.00	08/2008	317.74
36	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000060]	402.80	03/2009	453.70
37	PADALUR-TRICHY, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000083]	320.00	05/2009	636.10
38	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000093]	360.42	11/2009	478.40
39	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000105]	450.00	07/2008	876.61
40	ISLAM NAGAR TO KADTAL(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000109]	546.83	03/2010	667.80
41	WAINGANGA BRIDGE -CHHATISGARH-MAHARASHTRA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000120]	424.00	09/2010	298.40
<u>Shipping & Ports</u>				
42	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS(SHIPPING crp. of india) - [N25000013]	411.32	03/2010	406.28
43	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA(PORT TRUST) - [N25000046]	2,118.00	11/2004	.00
<u>Telecommunications</u>				
44	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I(DEPARTMENT OF TELECOMMUNICATION) - [260100051]	279.97	12/2004	136.24
45	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA(BHARAT SANCHAR NIGAM LIMITED) - [260100095]	1,174.75	03/2006	371.41
46	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000026]	741.77	10/2007	151.37
47	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-(BHARAT SANCHAR NIGAM LIMITED) - [N26000028]	364.52	-	51.44
48	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000042]	409.21	12/2008	470.24
49	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000061]	180.53	12/2009	25.97
October,2010				
<u>Health & Family Welfare</u>				
50	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS(HEALTH & FAMILY WELFARE) - [210100001]	71.18	03/1999	547.78
<u>Railways</u>				
51	DHARMAVARAM-PAKALA (GC), SCR(SOUTH CENTRAL RAILWAY) - [220100282]	200.00	-	567.49
<u>Road Transport & Highways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
52	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106268]	263.00	02/2009	420.80
53	AMRITSAR-WAGHA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000121]	205.88	06/2010	214.90
<u>Shipping & Ports</u>				
54	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE(SHIPPING crp. of india) - [N25000029]	1,658.59	07/2010	1,657.45
<u>Telecommunications</u>				
55	GSM BASED NETWORK EXPANSION PLAN PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000034]	239.19	04/2008	96.97
56	Provision of data network for CWG delhi(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000076]	488.76	10/2010	198.65
57	Expn of existing 2G & 3G GSM N/W by 750k(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000077]	180.53	06/2010	40.92
58	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph(BHARAT SANCHAR NIGAM LIMITED) - [N26000079]	577.35	09/2010	40.76
November,2010				
<u>Petroleum</u>				
59	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL)(INDIAN OIL CORPORATION LIMITED) - [160100289]	1,876.00	04/2009	2,747.34
60	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA(INDIAN OIL CORPORATION LIMITED) - [N16000017]	806.00	03/2008	840.06
<u>Power</u>				
61	SEWA- II H.E.P (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100220]	665.46	09/2007	982.76
62	NORTHERN REGION SYSTEM STRENGTHENING-XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000034]	417.76	12/2010	266.87
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000036]	408.36	12/2010	304.83
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000039]	261.55	11/2010	143.36
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000055]	525.14	07/2011	354.99
<u>Railways</u>				
66	RAJGIR-TILAIYA (NL), ECR(EAST CENTRAL RAILWAYS) - [220100312]	180.82	03/2006	272.46
<u>Road Transport & Highways</u>				
67	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000079]	205.92	08/2009	204.50

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
68	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000080]	243.64	08/2009	256.40
	<u>Telecommunications</u>			
69	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M(BHARAT SANCHAR NIGAM LIMITED) - [N26000051]	908.30	08/2009	211.83
70	CENTRALISED TRANSMISSION NMS(BHARAT SANCHAR NIGAM LIMITED) - [N26000064]	300.00	-	.00
	December,2010			
	<u>Petroleum</u>			
71	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000036]	372.00	-	229.04
72	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000037]	356.00	-	222.69
73	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000038]	1,492.00	04/2010	1,113.09
	<u>Road Transport & Highways</u>			
74	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106302]	206.96	10/2008	281.90
75	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000078]	243.38	09/2008	286.40
76	BANGALORE-NEELAMANGAL NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000104]	445.00	07/2010	803.40
	<u>Shipping & Ports</u>			
77	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS(SHIPPING corp. of india) - [N25000030]	586.58	11/2010	634.09
	<u>Telecommunications</u>			
78	KOLKATA TELECOM DISTRICT PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000036]	208.50	09/2008	146.00
	January,2011			
	<u>Atomic Energy</u>			
79	KAIGA 3 and 4 UNITS (NPCIL)(NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100041]	4,213.00	10/2009	2,610.00
	<u>Steel</u>			
80	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000025]	302.70	06/2009	244.97
81	REBUILDING OF BLAST FURNACE NO.2(BOKARO STEEL PL(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000035]	892.32	-	616.57

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
82	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000036]	197.66	11/2009	130.32
83	POWER PLANT-I(RASTRIYA ISPAT NIGAM LIMITED) - [N12000039]	462.00	12/2009	84.40
84	EXPANSION OF SALEM STEEL PLANT(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000050]	1,902.00	06/2011	1,754.78
<u>Petroleum</u>				
85	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000048]	5,595.31	11/2009	3,326.01
<u>Power</u>				
86	KORBA STPP STAGE-III(NATIONAL THERMAL POWER CORPORATION) - [N18000011]	2,448.50	02/2010	2,119.00
87	National Capital Thermal Power Project Stage-II(NATIONAL THERMAL POWER CORPORATION) - [N18000013]	5,135.33	10/2010	4,062.00
88	WESTERN REGION STRENGTHENING SCHEME-VI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000038]	340.72	11/2010	164.37
<u>Railways</u>				
89	HOTGI-GADAG(GC),SWR(SOUTH WESTERN RAILWAY) - [220100125]	180.00	03/1999	360.21
90	BHILDI-SAMDARI (GC)(RAIL VIKAS NIGAM LTD.) - [220100291]	244.74	-	476.85
91	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN(GAUGE CONVERSION) - [N22000103]	100.41	12/2009	911.24
<u>Road Transport & Highways</u>				
92	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100206]	106.00	08/2006	141.70
93	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106202]	480.00	11/2007	846.20
94	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000076]	208.46	08/2009	197.80
95	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000077]	239.19	09/2009	224.80
96	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000081]	194.80	08/2009	179.70
February, 2011				
<u>Civil Aviation</u>				
97	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000017]	290.92	01/2011	266.53
<u>Railways</u>				
98	MIRAJ-LATUR ROAD(GC),CR(CENTRAL RAILWAYS) - [220100162]	225.00	03/2001	845.26
<u>Road Transport & Highways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
99	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106245]	239.00	10/2008	396.30
100	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106249]	451.97	04/2008	533.70
101	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106296]	291.80	06/2008	455.00
Shipping & Ports				
102	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM(PORT TRUST) - [N25000015]	245.67	04/2009	304.01
March,2011				
Steel				
103	AIR SEPARATION PLANT (ASU-4)(RASTRIYA ISPAT NIGAM LIMITED) - [N12000060]	96.00	06/2010	74.39
Petroleum				
104	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT(INDIAN OIL CORPORATION LIMITED) - [N16000021]	5,693.00	-	6,054.67
105	INSTALLATION OF FCCV AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000056]	900.47	09/2009	900.00
Power				
106	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000044]	328.97	09/2011	181.39
Railways				
107	AMBALA-MORADABAD(RE)(RAILWAY ELECTRIFICATION) - [220100131]	152.21	03/1998	272.32
108	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR)(SOUTHERN RAILWAY) - [220100249]	178.76	-	190.49
109	PURNA-AKOLA (G.C), SCR(SOUTH CENTRAL RAILWAY) - [220100253]	228.00	-	518.08
110	GULBARGA-BIDAR,SCR(NL)(SOUTH CENTRAL RAILWAY) - [220100254]	242.42	-	169.69
111	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR)(SOUTH CENTRAL RAILWAY) - [220100267]	304.50	-	341.81
112	VALLAPARPADM-IDAPALLY,(NL)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000048]	246.50	03/2009	337.10
Road Transport & Highways				
113	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106220]	158.06	08/2005	163.50
114	MUZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106224]	275.00	07/2005	334.70

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
115	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106247]	205.00	10/2008	351.30
116	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106248]	212.00	10/2008	388.50
117	LANKA TO DABOKA (NH-54)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106286]	225.00	06/2008	220.50
118	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106295]	305.00	06/2008	497.20
119	BARA TO ORAI, NH-2, 25(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000069]	465.00	04/2009	607.80


Summary of projects in the Flash Report for the month of March, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	572
Number of Projects completed/dropped/frozen in Previous Month	9
Number of Projects completed/dropped/frozen in Current Month	17
Number of Projects Added in Current Month	16
Number of Projects in Current Month	562

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 562 projects, 11 projects are ahead of schedule, 147 projects are on schedule and 266 projects are delayed. Of the balance, 90 projects do not have fixed dates of commissioning while 48 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

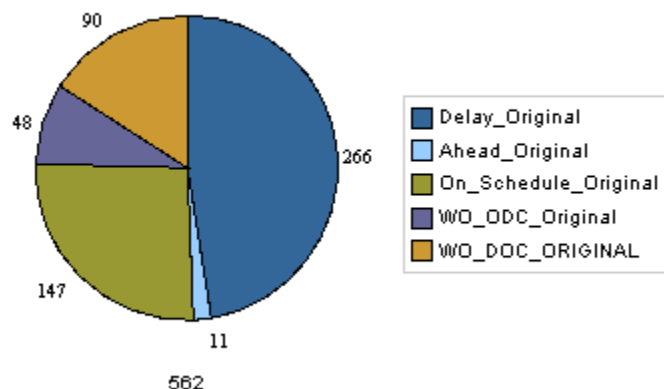

III. Investment Scenario

The Total Original cost of implementation of 562 projects when sanctioned, was of the order of Rs. 613026.37 crore but this was subsequently revised to Rs. 733653.52 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till March, 2011 is Rs. 321943.8 crore, which is 43.9% of the revised cost of the projects.

Figures are in Rs. Crore

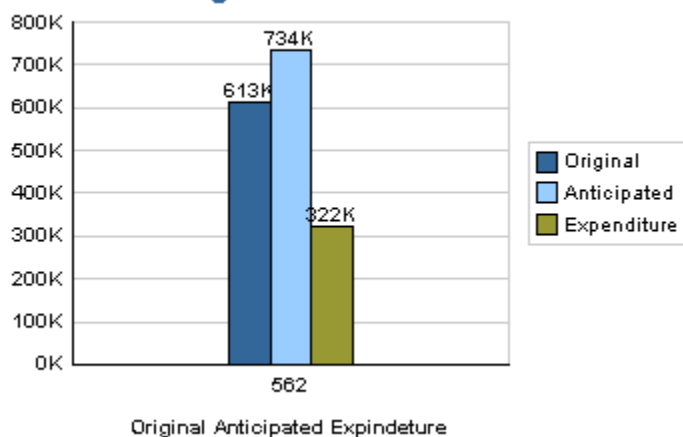

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	572
No of Projects Completed/Dropped/Frozen in Previous Month	9
No of Projects Completed/Dropped/Frozen in Current Month	17
No of Projects added in Current Month	16
No of Projects in Current Month	562

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	266	11	147	48	90	562	47.33
Latest Approved (Date)	271	12	197	30	53	562	48.22

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	453	520,428.87	567,741.88	231,648.74	40.80	47,313.01	9.10
Latest Approved (RCE)	109	145,207.44	165,911.64	90,295.06	54.40	20,704.20	14.30
Total (RCE)	562	665,636.31	733,653.52	321,943.80	43.88	68017.21	10.22
Original Cost of All Projects							
Original Cost	562	613,026.37	733,653.52	321,943.80	43.90	120,627.15	19.70

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	266	305,079.65	379,009.33	221,974.32	58.60	73,929.68	24.20
Latest Approved (RCE)	271	314,412.67	361,804.97	214,855.68	59.40	47,392.30	15.10

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	87	82,615.71	82,296.88	57,626.50	70.00	-318.83	-.40

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Railways</u>						
AMBALA-MORADABAD(RE)	03/1993	152.21	03/1998	283.00	N.A.	272.32
KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR)	03/2001	178.76	N.A.	219.94	N.A.	190.49
PURNA-AKOLA (G.C), SCR	02/2000	228.00	N.A.	518.08	N.A.	518.08
GULBARGA-BIDAR,SCR(NL)	02/1998	242.42	N.A.	369.70	N.A.	169.69
GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR)	05/2002	304.50	N.A.	306.00	03/2011	341.81
<u>Road Transport & Highways</u>						
JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25	12/2003	158.06	08/2005	158.06	03/2011	163.50
MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28	12/2003	275.00	07/2005	275.00	03/2011	334.70
GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00	12/2003	205.00	10/2008	205.00	03/2011	351.30
AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075	12/2003	212.00	10/2008	212.00	03/2011	388.50
LANKA TO DABOKA (NH-54)(NHAI)	12/2003	225.00	06/2008	225.00	03/2011	220.50
<u>Steel</u>						
AIR SEPARATION PLANT (ASU-4)	03/2008	96.00	06/2010	170.00	10/2010	74.39
<u>Petroleum</u>						
INSTALLATION OF FCCV AT MUMBAI REFINERY	03/2007	900.47	09/2009	900.47	12/2010	900.00
<u>Power</u>						
SYSTEM STRENGHTENING IN NR GRID FOR KARCHAM WANGTO	12/2008	328.97	09/2011	328.97	03/2011	181.39
<u>Railways</u>						
VALLAPARPADM-IDAPALLY,(NL)(RVNL)	07/2006	246.50	03/2009	246.50	N.A.	337.10
<u>Road Transport & Highways</u>						
BARA TO ORAI, NH-2, 25	12/2003	465.00	04/2009	465.00	03/2011	607.80
<u>Petroleum</u>						
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT	01/2007	5,693.00	N.A.	6,825.00	03/2011	6,054.67
<u>Road Transport & Highways</u>						
DARBHANGA-MUZZAFFARPUR, NH-57	12/2003	305.00	06/2008	305.00	11/2011	497.20

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
(NHAI)						

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Road Transport & Highways</u>					
CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	1,585.00	5/2013	1,585.00	5/2013
<u>Petroleum</u>					
Construction of 6 ETPs	3/2009	302.26	9/2012	302.26	9/2012
Development of BHE and BH-35 Area.	8/2010	372.11	3/2013	372.11	3/2013
<u>Road Transport & Highways</u>					
KUNDUPUR-SURATHKAL & MANGLORE	9/2010	671.00	3/2013	671.00	3/2013
<u>Petroleum</u>					
Ahmedabad Redevelopment	11/2010	1,916.10	12/2014	1,916.10	12/2014
Wind Power Project	7/2010	1,106.00	6/2012	1,106.00	6/2012
Development of BHE & BH-35 Area	8/2010	372.11	3/2013	372.11	3/2013
Construction of tanks and blending facility at vadinar	2/2009	267.00	9/2012	267.00	10/2011
Ankleswar Redevelopment	11/2010	2,189.63	12/2014	2,189.63	12/2014
<u>Road Transport & Highways</u>					
AMRITSAR-PATHANKOT	5/2010	705.00	11/2012	705.00	11/2012
DEOLI-KOTA	1/2011	953.00	7/2013	953.00	7/2013
CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	9/2010	852.00	3/2013	852.00	3/2013
<u>Petroleum</u>					
Development of SB-14 Field	1/2011	410.44	12/2012	410.44	12/2012
Mehesana Redevelopment	11/2010	3,823.00	4/2015	3,823.00	4/2015
Construction of 23 Immediate Supply Vessels (ISV)	11/2010	331.20	8/2013	331.20	3/2013
Development of SB-14 field	1/2011	410.44	1/2013	410.44	1/2013

VII. Milestones (Cumulative due & achieved)

Total	1984
Achieved up to month	802

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL UCIL	1,106.29	1,106.29	N.A.	04/2011	12/2011	8
<u>Civil Aviation</u>						
C/o new Airport at Pakyong(Sikkim) Airport AAI	264.29	264.29	01/2011	01/2011	06/2012	17
<u>Coal</u>						
TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	2,453.57	06/2009	12/2011	03/2012	3
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	03/2011	06/2011	3
ASHOK EXPN.OCP -CCL (5 MTY) CCL	471.66	341.63	03/2011	03/2012	03/2013	12
North Urimari OCP CCL	179.87	179.87	03/2012	03/2012	03/2014	24
Tapin OCP CCL	264.68	264.68	03/2012	03/2012	03/2014	24
MAGADH OC (CCL) CCL	469.78	706.40	07/2012	03/2013	03/2016	36
Churi Benti UG CCL	163.51	163.51	03/2011	03/2011	03/2014	36
<u>Mines</u>						
SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE NALCO	4,091.51	4,401.76	12/2008	03/2011	05/2011	2
<u>Steel</u>						
Rebuilding of coke oven battery No.1 & 2 (Bokaro S SAIL	500.90	500.90	04/2010	08/2011	09/2011	1
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	06/2011	07/2011	1
700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI SAIL	111.28	232.93	N.A.	05/2011	07/2011	2
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) SAIL	172.78	172.78	01/2010	04/2011	06/2011	2
EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	14,443.00	09/2010	12/2011	03/2012	3
<u>Petroleum</u>						
SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) GAIL	396.13	266.00	10/2009	03/2011	04/2011	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
HYDROCRACKER REVAMP & SETTING BPCL	825.00	825.00	N.A.	12/2011	01/2012	1
BAWANA NANGAL PIPE LINE PROJECT GAIL	1,816.07	1,200.00	N.A.	10/2011	12/2011	2
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I GAIL	1,512.00	975.00	04/2011	10/2011	12/2011	2
BNPL SPURLINE (UTTRANCHAL & PUNJAB) GAIL	540.92	375.00	06/2011	11/2011	01/2012	2
CDU/VDU-II CPCL	333.99	333.99	05/2012	03/2012	05/2012	2
DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON BRPL	1,431.91	1,690.13	09/2009	03/2011	06/2011	3
DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) GAIL	4,403.26	2,500.00	10/2011	06/2011	09/2011	3
MSQ IMPROVMENT PROJECT IOCL	293.60	294.00	12/2009	03/2011	07/2011	4
Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli HPCL	613.54	727.88	12/2010	01/2011	06/2011	5
CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI HPCL	224.00	299.00	12/2010	02/2011	08/2011	6
DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	3,597.00	09/2011	09/2011	03/2012	6
DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY HPCL	3,284.00	3,284.00	09/2011	09/2011	03/2012	6
HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT ONGC	2,305.30	2,305.30	06/2010	03/2011	10/2011	7
DEVELOPMENT OF C-SERIES FIELDS ONGC	3,195.16	3,195.16	12/2008	03/2011	11/2011	8
Power						
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G PGCIL	290.49	299.08	04/2010	03/2011	04/2011	1
MOUDA STPP (NTPC) NTPC	5,459.28	6,010.89	08/2012	10/2012	11/2012	1
TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,061.38	09/2009	10/2012	12/2012	2
Transmission system associated with Uri-II HEP PGCIL	238.25	227.03	05/2011	05/2011	07/2011	2
TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT NHPC	768.92	768.92	03/2007	02/2012	05/2012	3
KOTESWAR TRANSMISSION SYSTEM (PGCIL) PGCIL	260.34	241.27	06/2008	03/2011	06/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME PGCIL	803.70	803.76	06/2009	03/2011	06/2011	3
EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	894.26	10/2009	03/2011	06/2011	3
EASTERN REGION STRENGTHENING SCHEME- II PGCIL	227.52	227.52	06/2010	03/2011	06/2011	3
WESTERN REGION STRENGTHENING SCHEME- IX PGCIL	230.89	230.89	01/2011	03/2011	06/2011	3
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	297.37	07/2011	03/2011	07/2011	4
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE PGCIL	557.24	639.52	01/2010	06/2011	11/2011	5
EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER PGCIL	262.10	262.10	09/2010	03/2011	08/2011	5
WESTERN REGION STRENGTHENING SCHEME- II PGCIL	5,221.23	4,978.56	07/2010	06/2011	12/2011	6
KUDANKULAM-APP TRANS. SYSTEM (PGCIL) PGCIL	1,779.29	1,946.85	11/2008	06/2011	03/2012	9
<u>Railways</u>						
KHURDA ROAD- BOLANGIR(NL)ECOR ECOR	355.38	700.00	N.A.	03/2011	08/2011	5
LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	170.00	03/2002	03/2011	09/2011	6
TALCHER- BIMALAGARH(NL)(ECOR) ECOR	726.96	810.78	N.A.	02/2011	12/2011	10
ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR & G'BA RE	171.10	171.10	03/2012	03/2011	03/2012	12
ELECTRIFICATION OF MORADABAD-ROZA RE	129.17	220.00	03/2011	03/2011	03/2012	12
Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves NWR	643.36	803.39	03/2011	03/2011	03/2012	12
EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP MRTF	495.74	495.74	N.A.	03/2012	06/2013	15
<u>Road Transport & Highways</u>						
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 NHAI	205.73	205.73	07/2004	03/2011	04/2011	1

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS NHAI	210.00	210.00	04/2007	03/2011	04/2011	1
MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 NHAI	239.00	239.00	07/2005	03/2011	04/2011	1
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 NHAI	323.36	323.36	03/2008	03/2011	04/2011	1
MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	03/2011	04/2011	1
KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	03/2011	04/2011	1
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	03/2011	04/2011	1
KURALI-KIRATPUR, NH-21 NHAI	309.00	309.00	06/2010	03/2011	04/2011	1
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	03/2011	04/2011	1
GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 NHAI	579.00	579.00	04/2009	03/2011	05/2011	2
JHANSI TO LALITPUR, NH-26 NHAI	276.09	276.09	09/2009	03/2011	05/2011	2
HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	03/2011	06/2011	3
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	03/2011	06/2011	3
GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 NHAI	275.00	275.00	09/2007	03/2011	06/2011	3
KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 NHAI	240.00	240.00	10/2008	03/2011	06/2011	3
ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	03/2011	06/2011	3
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 NHAI	359.00	359.00	03/2009	03/2011	06/2011	3
LALITPUR TO SAGAR, NH-26 (NHAI) NHAI	198.00	198.00	11/2008	03/2011	06/2011	3
RINGBUNDS TO JHAJHANPUR (BR-6) NHAI	340.00	340.00	06/2008	03/2011	06/2011	3
SITAPUR-LUCKNOW NHAI	322.00	322.00	06/2009	03/2011	06/2011	3
GWALIOR BYPASS, NH-75,3 NHAI	300.93	300.93	10/2009	03/2011	06/2011	3

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
JHANSI TO LALITPUR, NH-25,26 NHAI	355.06	355.06	09/2009	03/2011	06/2011	3
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	07/2010	03/2011	06/2011	3
BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 NHAI	565.00	565.00	07/2010	03/2011	06/2011	3
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) NHAI	225.00	225.00	10/2008	03/2011	07/2011	4
NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2008	03/2011	07/2011	4
NALBARI TO BIJNI (AS-8) NHAI	200.00	200.00	06/2008	03/2011	12/2011	9
THANJAUR-TRICHY, NH-67(NHAI) NHAI	280.00	280.00	06/2009	03/2011	12/2011	9
SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 NHAI	157.47	154.57	09/2007	03/2011	03/2012	12
Shipping & Ports						
ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA SHIPP.	1,066.91	968.35	09/2012	08/2012	09/2012	1
DEEPENING OF CHANNEL AT PARADIP PORT TRUST	154.84	253.36	12/2007	03/2011	06/2011	3
Acquisition of Two nos. of 3060 DWT PORT TRUST	277.03	277.03	12/2011	12/2011	05/2012	5
ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH SHIPP.	165.00	165.00	12/2005	03/2011	10/2011	7
Acquisition of two nos. of 120 B.P PORT TRUST	290.85	290.85	06/2011	06/2011	01/2012	7
Telecommunications						
CONVERGENT BILLING AND CRM(MUMBAI) MTNL	247.00	247.00	02/2007	03/2011	08/2011	5

Number of projects reporting additional delay = 87


Trend and Graphical Analysis of All Projects

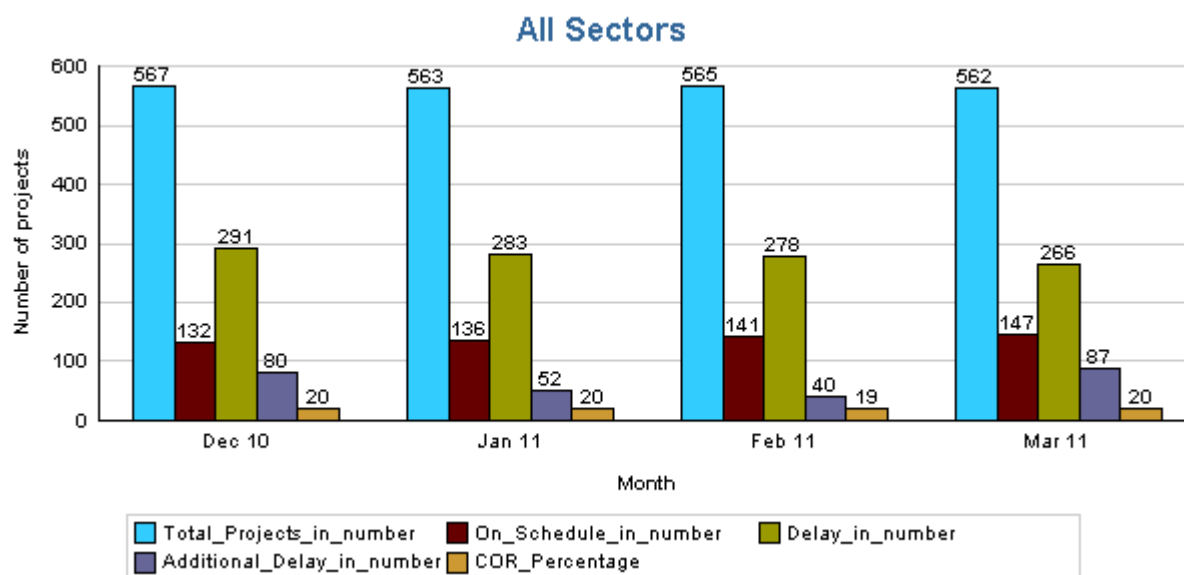


All Sectors Break-up of 266 Delayed projects in March 2011

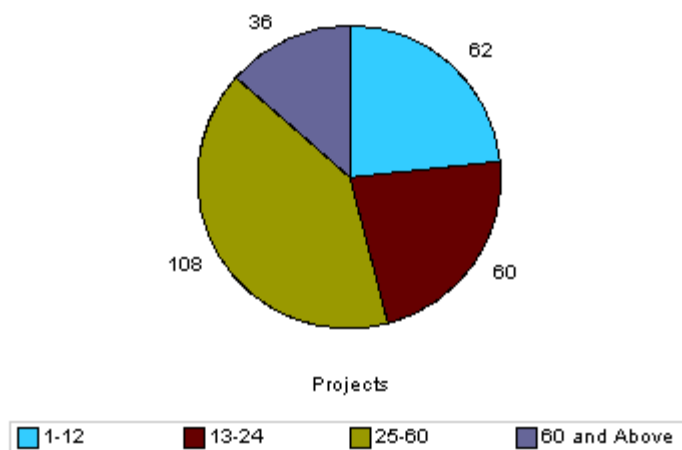


Trend and Graphical Analysis of Urban Development Sector

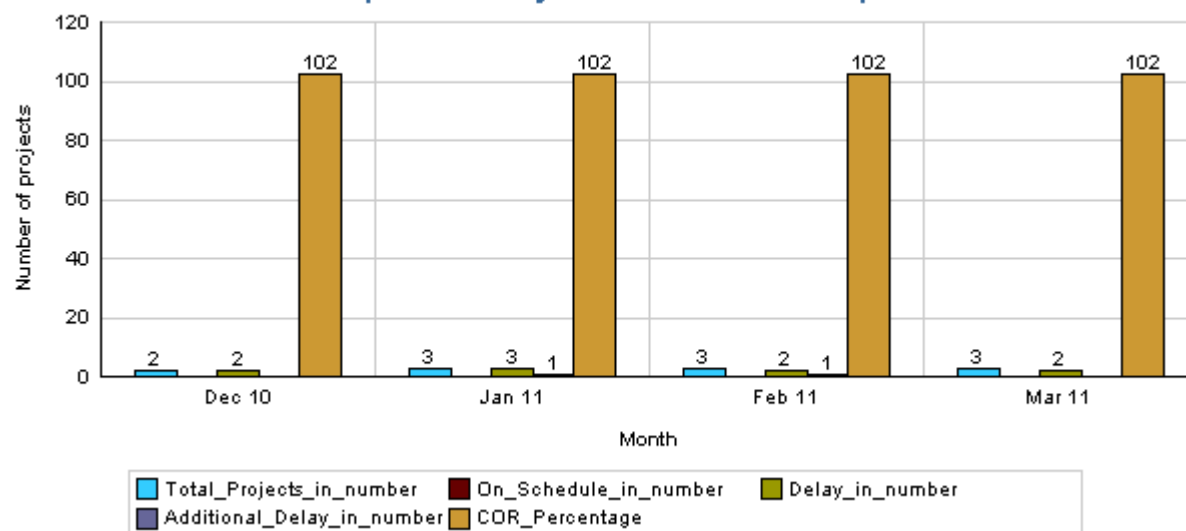


Urban Development Sector Break-up of 2 Delayed projects in March 2011

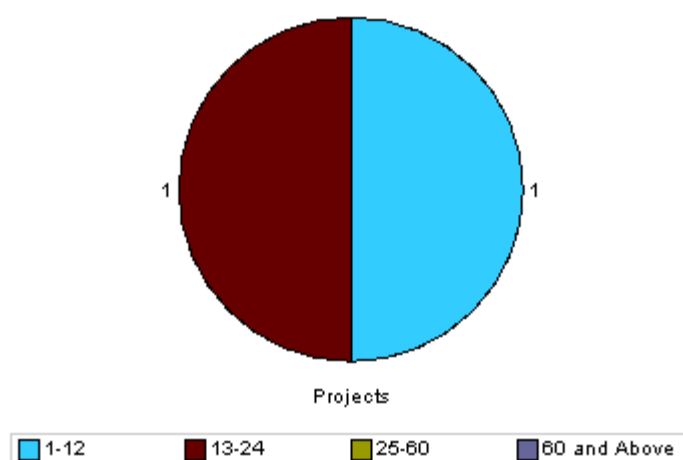


Trend and Graphical Analysis of Telecommunications Sector

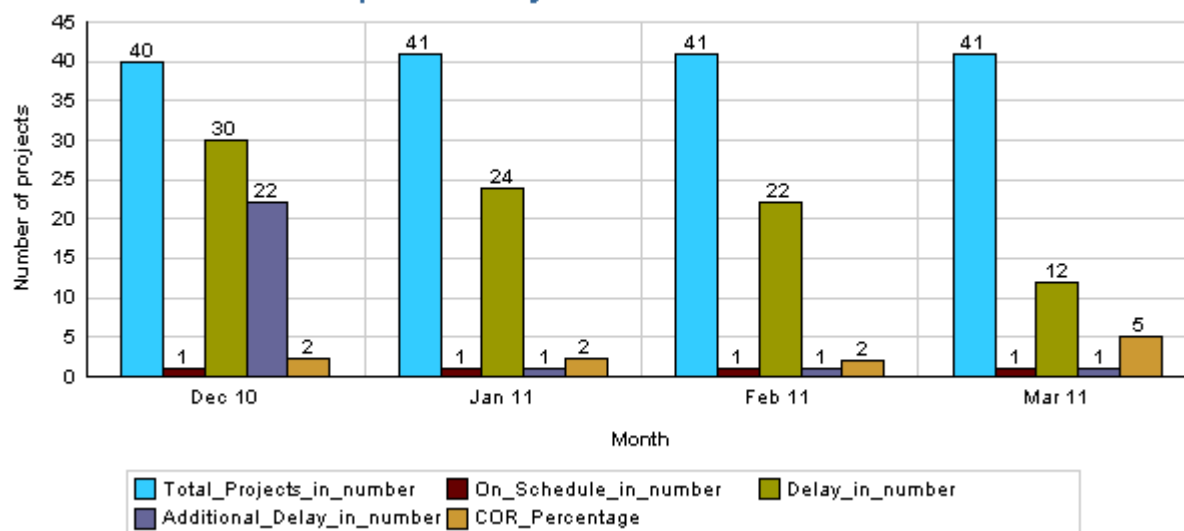


Telecommunications Sector Break-up of 12 Delayed projects in March 2011

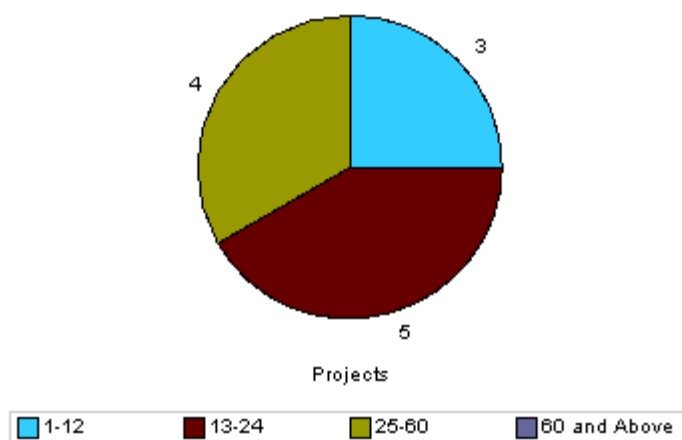

Trend and Graphical Analysis of Steel Sector

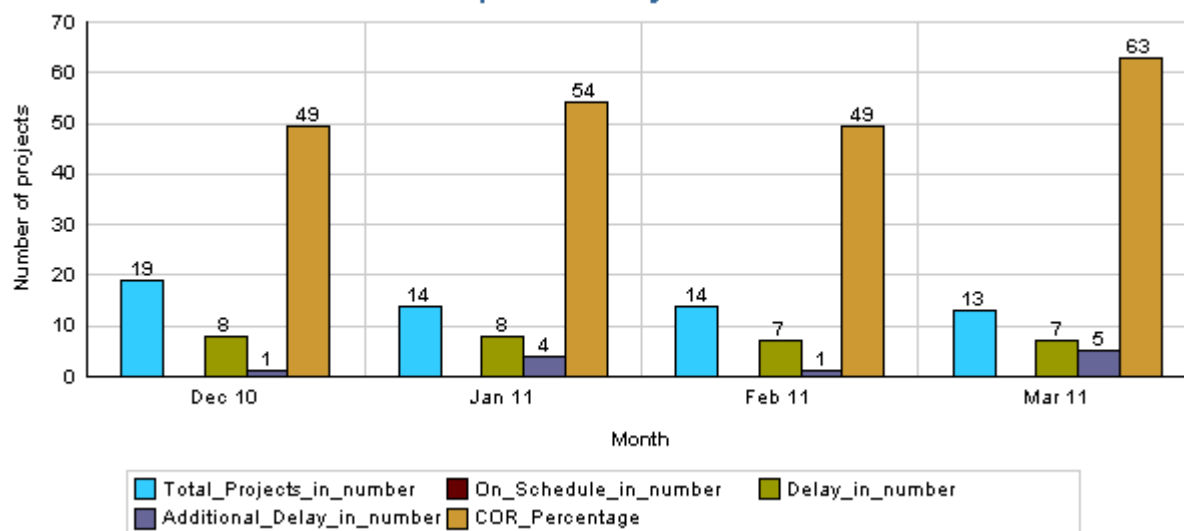


Steel Sector Break-up of 7 Delayed projects in March 2011

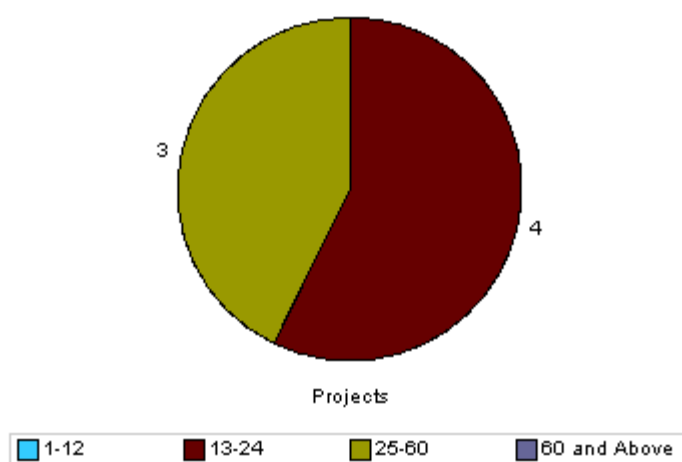


Trend and Graphical Analysis


Shipping and Ports Sector

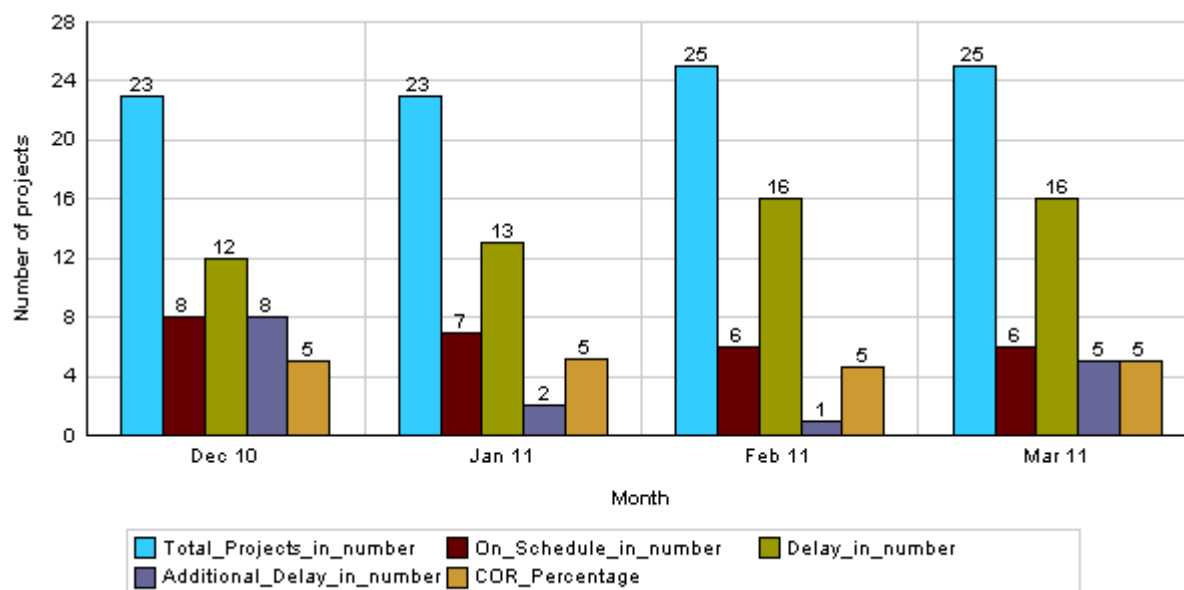


Sector Break-up of 16 Delayed projects in March 2011

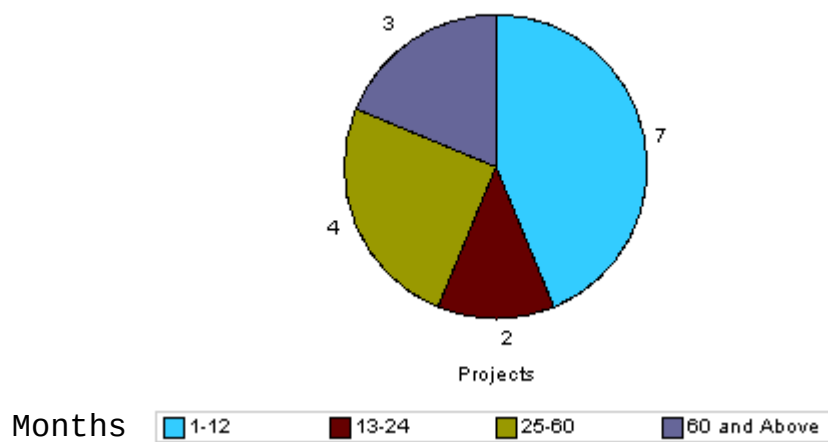


Trend and Graphical Analysis of Road Transport and Highways Sector

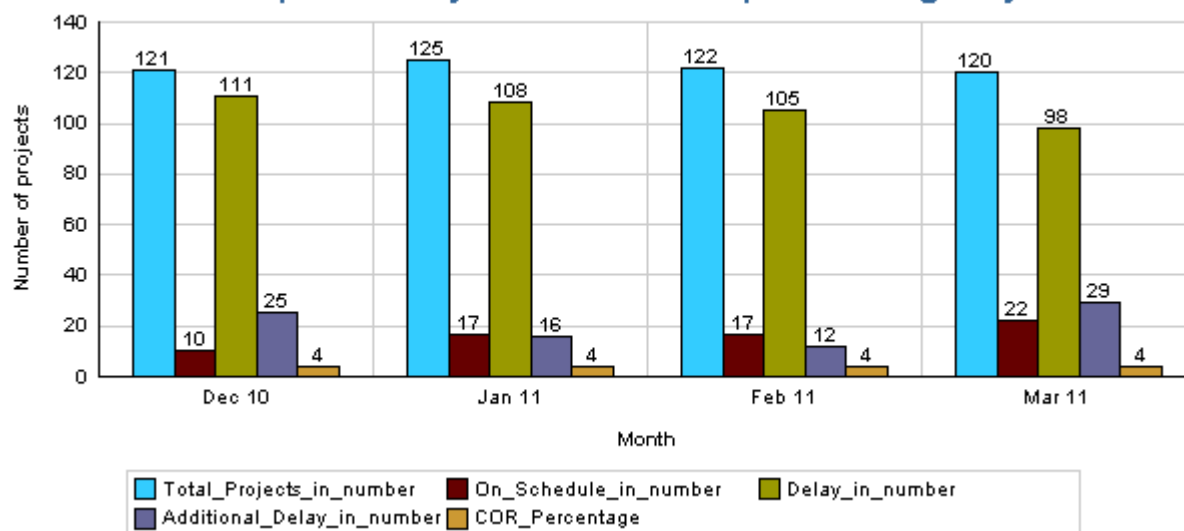


Sector Break-up of 98 Delayed projects in March 2011

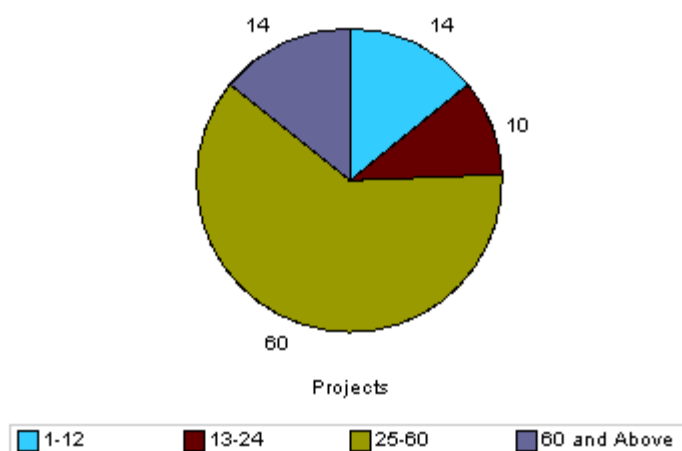


Trend and Graphical Analysis of Railways Sector

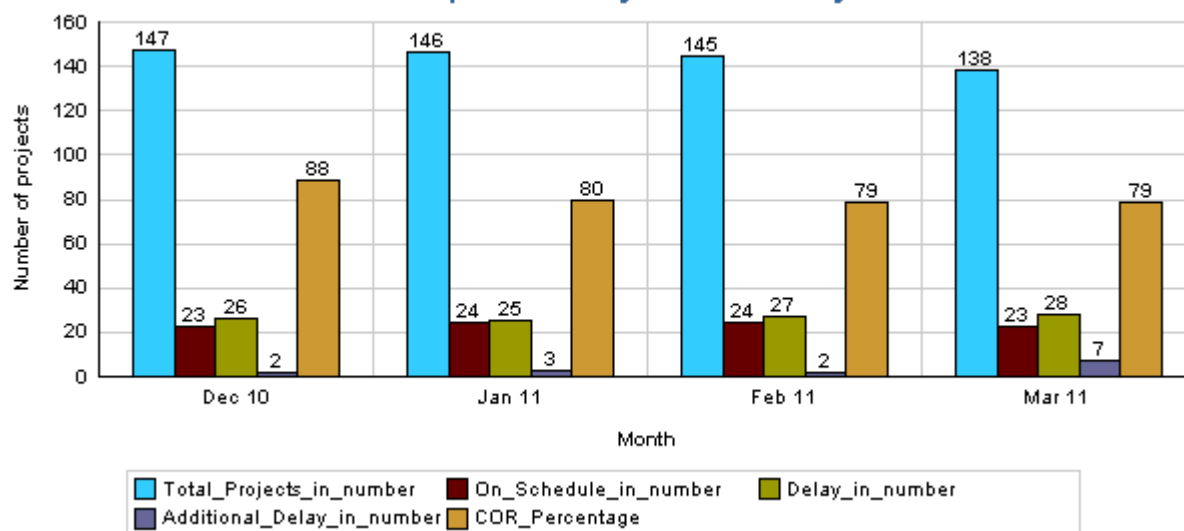


Railways Sector Break-up of 28 Delayed projects in March 2011

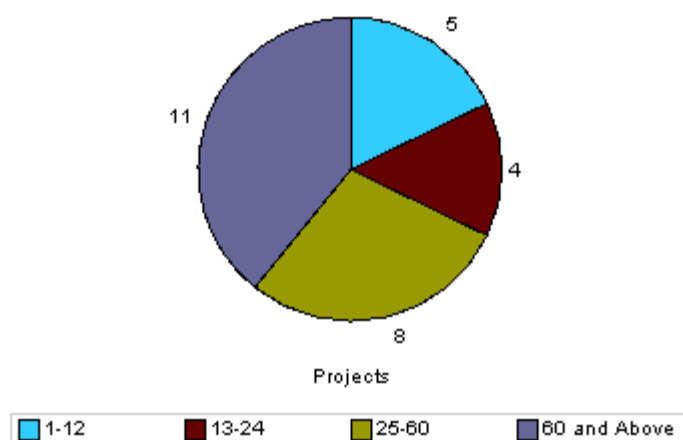


Trend and Graphical Analysis of Power Sector

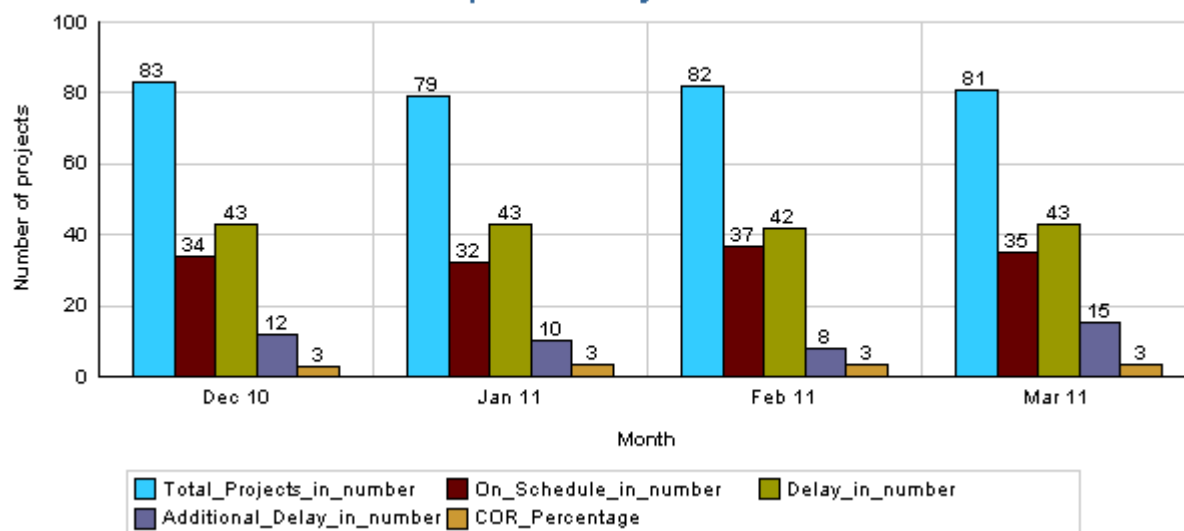


Power Sector Break-up of 43 Delayed projects in March 2011

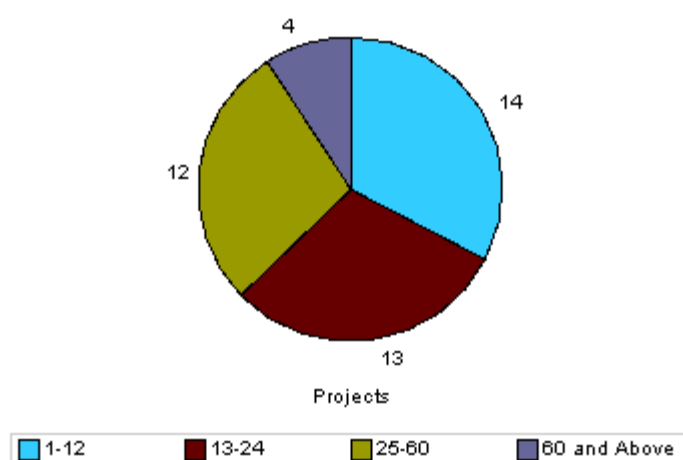


Trend and Graphical Analysis of Petroleum Sector

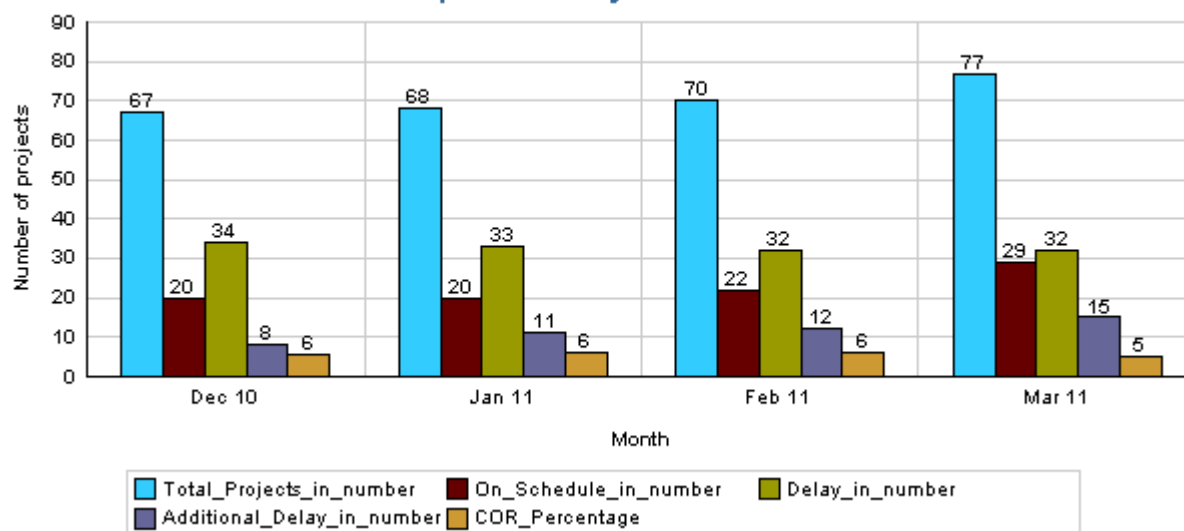


Petroleum Sector Break-up of 32 Delayed projects in March 2011

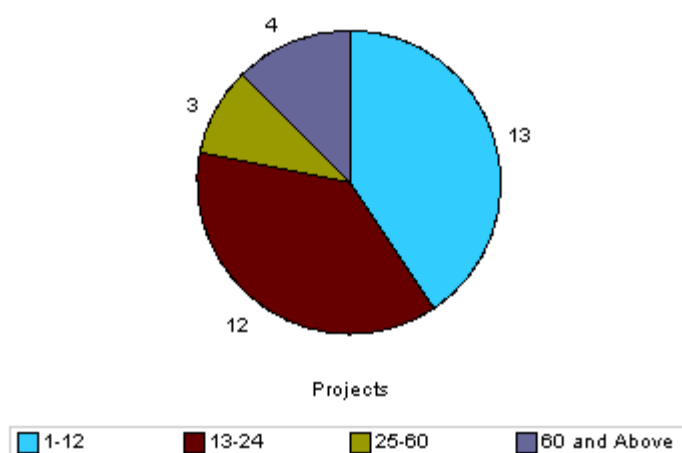


Trend and Graphical Analysis of Fertilisers Sector

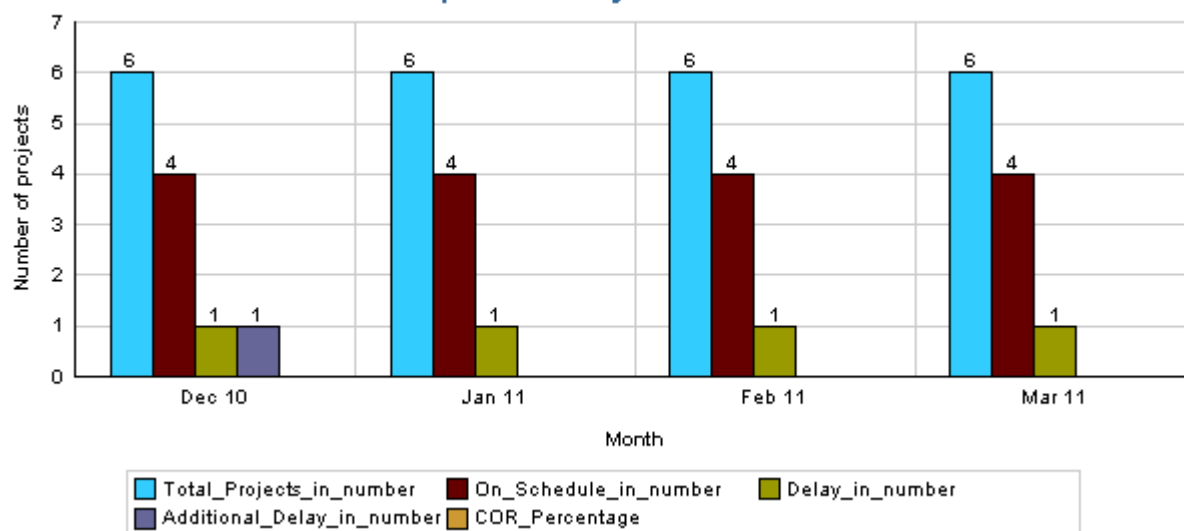


Fertilisers Sector Break-up of 1 Delayed projects in March 2011

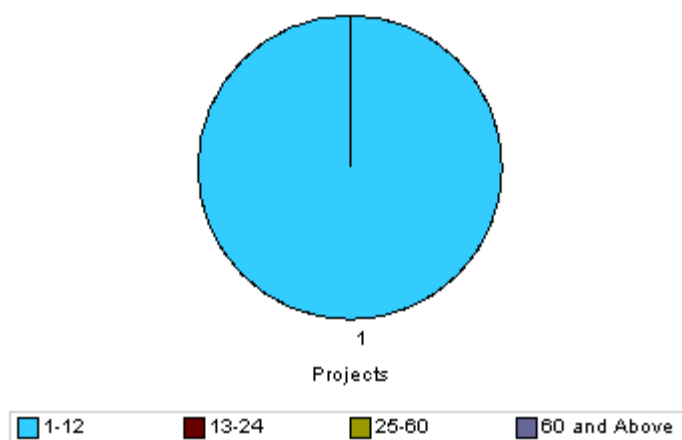


Trend and Graphical Analysis of Coal Sector

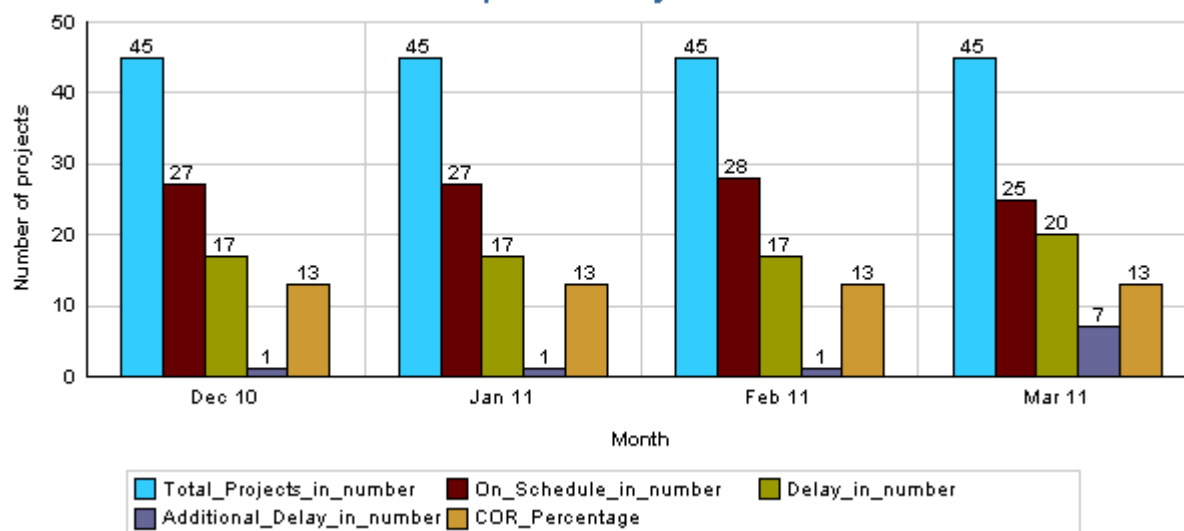


Coal Sector Break-up of 20 Delayed projects in March 2011

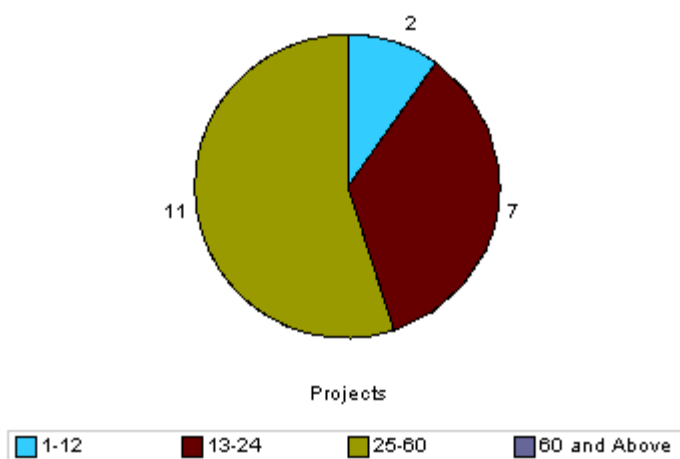


Trend and Graphical Analysis of Civil Aviation Sector

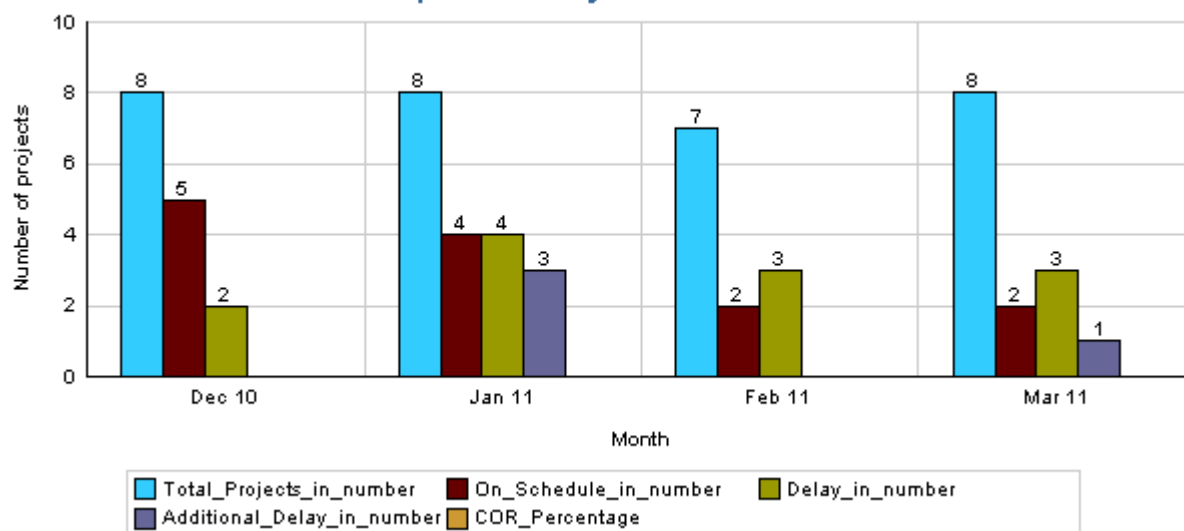


Civil Aviation Sector Break-up of 3 Delayed projects in March 2011

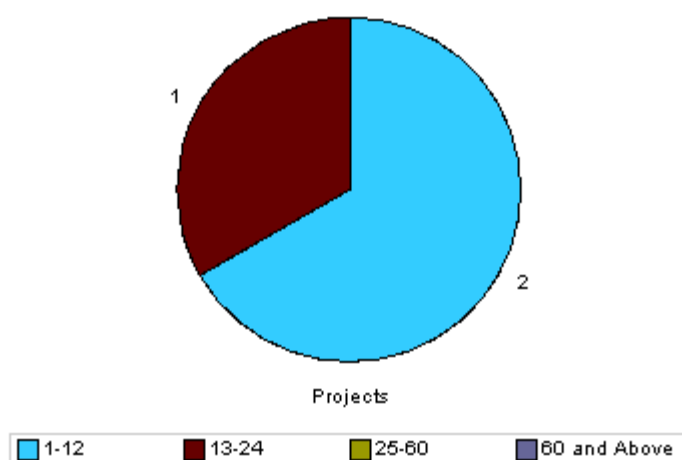

Trend and Graphical Analysis of Atomic Energy Sector

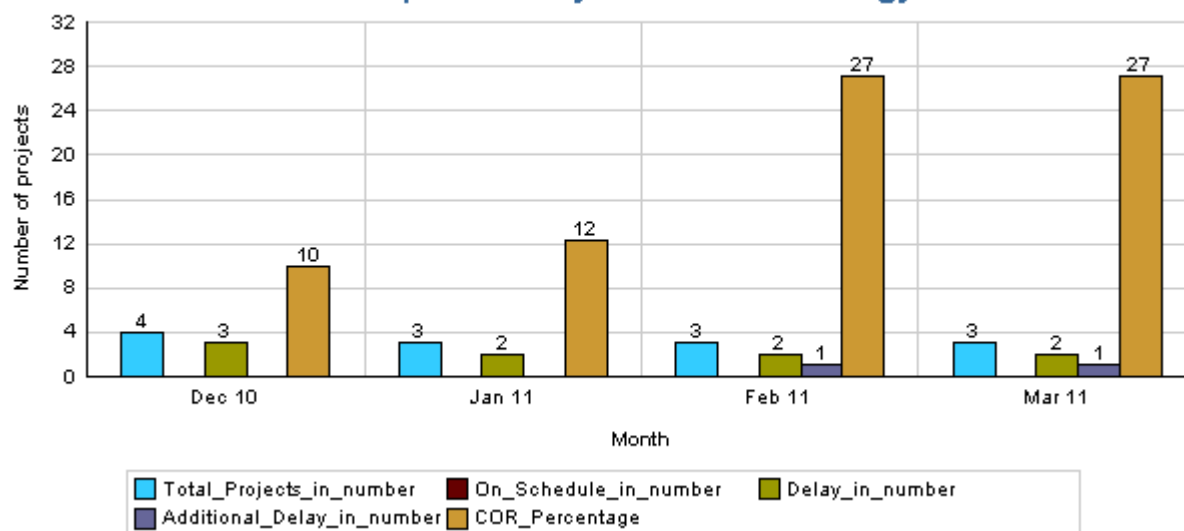

Atomic Energy Sector Break-up of 2 Delayed projects in March 2011

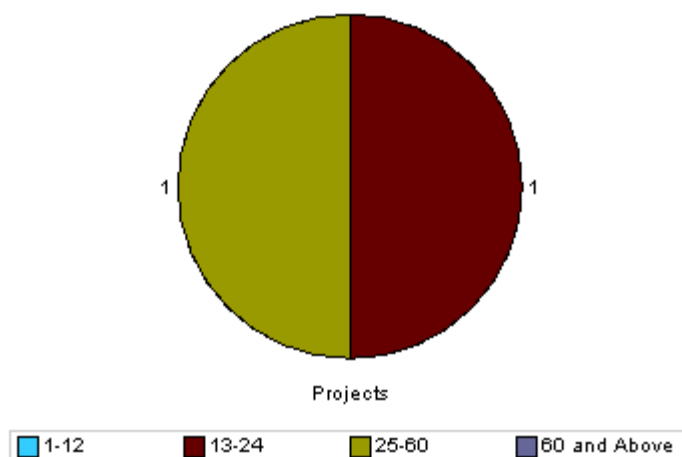

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	3	17,769.29	17,769.29	22,607.29
Civil Aviation	8	5,056.48	4,839.48	5,056.48
Coal	45	25,504.15	28,784.49	28,789.48
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	13	39,927.85	55,138.50	65,040.88
Petroleum	77	167,009.99	181,158.42	175,658.75
Power	81	173,209.28	174,164.90	178,736.68
Railways	138	67,069.85	85,371.71	119,977.99
Road Transport & Highways	120	53,244.18	53,244.18	55,142.59
Shipping & Ports	25	19,072.31	19,750.33	20,026.03
Telecommunications	41	20,025.99	19,979.50	21,026.52
Urban Development	3	15,185.18	15,173.44	30,684.66
Water Resources	1	542.90	542.90	1,187.00
Grand total	562	613,026.37	665,636.31	733,653.52

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	925.69	- 04/2011	12/2011	8(R3)	0/1
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	2,944.81	09/2010 -	01/2012	16(O)	8/80
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	13,561.00	12/2008 -	03/2012	39(O)	61/119
	Total		17,769.29 -	22,607.29	17,431.50				69/200
	<u>Civil Aviation</u>								
4	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35 -	213.35	227.95	09/2010 -	03/2011	6(O)	0/0
5	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 -	1,273.00	714.65	01/2011 -	01/2011	0(O)	0/0
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	-	05/2011 -	08/2011	3(O)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	25.64	05/2012 -	05/2012	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29 -	264.29	105.01	01/2011 -	06/2012	17(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	262.69	06/2013 -	06/2013	0(O)	0/0
10	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]AAI,Tamil Nadu	01/2008	535.00 -	535.00	143.97	06/2010 -	-	-	0/0
11	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00 13.00	230.00	232.82	01/2011 -	-	-	0/0
	Total		5,056.48 -	5,056.48	1,712.73				0/0
	<u>Coal</u>								
12	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,576.46	06/2009 -	06/2011	24(O)	59/26
13	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,453.57	06/2009 -	03/2012	33(O)	59/24
14	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	75.95	03/2010 03/2012	03/2012	0(R3)	0/4
15	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	38.37	03/2012 -	03/2012	0(O)	12/42
16	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.49	03/2012 -	03/2012	0(O)	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	109.64	03/2009 03/2010	03/2012	24(R3)	0/2
18	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	55.95	03/2012 -	03/2012	0(O)	0/0
19	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,	12/2009	418.97 -	418.97	71.60	03/2012 -	03/2012	0(O)	18/27
20	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,	03/2010	181.19 -	181.19	0.90	03/2012 -	03/2012	0(O)	6/34
21	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	1,609.59	08/2012 -	08/2012	0(O)	0/3
22	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	101.16	03/2011 03/2013	03/2013	0(R3)	0/2
23	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.56	741.56	137.36	03/2010 -	03/2013	36(O)	0/2
24	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,	06/2006	737.65 1,188.31	1,188.31	556.97	03/2013 -	03/2013	0(O)	0/3
25	JALLARAM SHAFT PROJECT - [N06000025]SCCL,	03/2013	467.78 -	467.78	11.73	03/2013 -	03/2013	0(O)	0/83
26	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	69.11	03/2013 -	03/2013	0(O)	0/2
27	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.53 -	479.53	205.31	03/2013 -	03/2013	0(O)	0/2
28	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	23.01	03/2013 -	03/2013	0(O)	0/2
29	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	154.25	03/2013 09/2012	06/2013	9(R3)	2/22
30	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 2,675.67	2,675.67	1,049.83	03/2010 03/2014	03/2014	0(R3)	3/2
31	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 1,943.66	1,943.66	949.45	03/2010 03/2014	03/2014	0(R3)	2/3
32	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	145.92	03/2014 -	03/2014	0(O)	1/2
33	CHURCHA UG - [N06000046]SECL,	06/2008	462.35 -	462.35	255.90	03/2014 -	03/2014	0(O)	0/2
34	RAJMAHAL OC EXP. - [N06000056]ECL,	02/2006	50.08 153.82	153.82	17.11	03/2011 03/2014	03/2014	0(R3)	0/3
35	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77 -	339.77	0.10	03/2014 -	03/2014	0(O)	1/2
36	KARTALI (EAST) OC - [N06000076]SECL,	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1
37	MANIKPUR OC EXPANTION - [N06000081]SECL,	11/2009	321.50 -	321.50	213.92	03/2014 -	03/2014	0(O)	0/1
38	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.54	03/2011 03/2012	03/2014	24(R3)	0/2
39	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.43	03/2012 -	03/2014	24(O)	0/2
40	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	76.00	03/2012 03/2013	03/2014	12(R3)	0/2
41	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	25.13	03/2014 -	03/2014	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 437.34	437.34	137.59	03/2012 03/2015	03/2015	0(R3)	0/2
43	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,	11/2006	287.18 -	287.17	-	03/2011 03/2015	03/2015	0(R3)	1/5
44	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	23.97	03/2013 03/2015	03/2015	0(R3)	0/3
45	PELMA OC - [N06000045]SECL,	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O)	0/1
46	KAKATIYA LAONGWALL - [N06000048]SCCL,	12/2008	453.63 -	453.63	60.20	12/2012 -	03/2015	27(O)	11/44
47	Batura OC - [N06000049]SECL,	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O)	0/1
48	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2015	0(O)	0/1
49	RKP OCP PHASE-I - [N06000079]SCCL,	03/2010	209.78 -	209.78	15.88	03/2015 -	03/2015	0(O)	4/31
50	Kistaram OCP - [N06000089]SCCL,	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O)	0/28
51	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	66.42	03/2014 03/2016	03/2016	0(R3)	1/2
52	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.19	07/2012 03/2014	03/2016	24(R3)	0/2
53	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72 -	447.72	35.20	03/2015 03/2016	03/2016	0(R3)	0/2
54	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,	11/2009	198.59 -	198.59	108.57	03/2016 -	03/2016	0(O)	0/1
55	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	289.64	03/2016 -	03/2016	0(O)	0/2
56	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.10 -	490.10	72.77	03/2017 -	03/2017	0(O)	0/1
Total			25,504.15 -	28,789.48	10,912.18				180/429
Fertilisers									
57	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	-	07/2011 -	07/2011	0(O)	0/0
58	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	-	07/2011 -	07/2011	0(O)	0/0
59	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	488.75	74.79	- 11/2011	11/2011	0(R3)	2/22
60	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	109.54	01/2013 -	01/2013	0(O)	0/5
61	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	97.13	01/2013 -	01/2013	0(O)	0/5
62	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	108.64	12/2012 -	01/2013	1(O)	0/8
Total			5,317.41 -	5,317.41	390.10				2/40

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Mines</u>									
63	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa	10/2004	4,091.51 4,401.76	4,401.76	3,957.31	12/2008 01/2011	05/2011	4(R3)	117/110
	Total		4,091.51 -	4,401.76	3,957.31				117/110
<u>Steel</u>									
64	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL, Jharkhand	07/2008	172.78 -	172.78	125.72	01/2010 -	06/2011	17(O)	0/1
65	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Chhatisgarh	07/2007	111.28 232.93	232.93	133.41	- -	07/2011	-	0/1
66	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	208.61	- -	07/2011	-	0/1
67	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	216.15	02/2010 -	08/2011	18(O)	0/0
68	Rebuilding of coke oven battery No.1 & 2 (Bokaro S) - [N12000033]SAIL, Jharkhand	10/2007	500.90 -	500.90	268.63	04/2010 -	09/2011	17(O)	0/2
69	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC, Chhatisgarh	01/2003	295.89 -	607.17	261.72	- -	10/2011	-	2/21
70	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	3,316.00 6,325.00	6,325.00	1,873.68	- 12/2011	12/2011	0(R3)	0/7
71	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	8,156.00	10/2009 -	03/2012	29(O)	5/25
72	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 -	14,443.00	10,618.26	09/2010 12/2011	03/2012	3(R3)	0/6
73	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,	05/2008	480.00 -	480.84	80.19	- -	05/2012	-	0/1
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	32.54	10/2009 -	10/2012	36(O)	0/0
75	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	6,133.00 -	11,812.00	1,253.17	02/2011 -	03/2013	25(O)	0/0
76	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	2,448.23	- 03/2013	03/2013	0(R3)	0/8
	Total		39,927.85 -	65,040.88	25,676.31				7/73
<u>Petroleum</u>									
77	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL, Punjab	01/2009	605.40 605.40	510.00	394.35	12/2010 12/2010	12/2010	0(R3)	17/17
78	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL, Kerala	09/2009	2,591.80 3,941.41	3,941.41	3,274.25	12/2009 -	12/2010	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
79	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92 1,493.49	976.08	766.67	05/2008 07/2010	02/2011	7(R3)	0/2
80	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	211.91	12/2010 -	03/2011	3(O)	0/0
81	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL,Multi State	11/2007	396.13 -	266.00	188.54	10/2009 -	04/2011	18(O)	0/0
82	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	551.47	04/2010 -	04/2011	12(O)	0/0
83	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	182.22	04/2011 -	04/2011	0(O)	0/0
84	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	948.49	04/2006 05/2011	05/2011	0(R3)	0/0
85	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	175.21	58.26	03/2009 -	05/2011	26(O)	0/0
86	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	287.89	03/2011 05/2011	05/2011	0(R3)	0/0
87	Pipeline Replacement project-2 - [N16000111]ONGC,Multi State	12/2007	2,553.28 3,796.21	3,796.21	3,459.59	05/2011 -	05/2011	0(O)	0/0
88	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,568.98	09/2009 -	06/2011	21(O)	0/0
89	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	261.36	12/2010 -	06/2011	6(O)	0/0
90	MSQ IMPROVMENT PROJECT - [N16000040]IOCL,Assam	04/2008	293.60 -	294.00	217.86	12/2009 -	07/2011	19(O)	0/0
91	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	334.50	12/2011 -	08/2011	-4(O)	0/0
92	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 -	299.00	131.46	12/2010 02/2011	08/2011	6(R3)	0/0
93	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,403.26 4,403.26	2,500.00	1,357.26	10/2011 09/2011	09/2011	0(R3)	0/2
94	COMPRESSOR STATIONS (KAILARAS &CHAINS) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	810.00	280.39	04/2011 04/2011	09/2011	5(R3)	0/2
95	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 -	2,305.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
96	Construction of tanks and blending facility at vadinar - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	156.40	09/2012 -	10/2011	-11(O)	0/0
97	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	3,195.16	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
98	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 1,816.07	1,200.00	677.71	- 04/2011	12/2011	8(R3)	0/1
99	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Madhya pradesh	11/2007	1,512.00 1,434.00	975.00	773.60	04/2011 -	12/2011	8(O)	0/3

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
100	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 -	250.00	158.07	03/2013 -	12/2011	-15(O)	0/0
101	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Multi State	06/2009	348.00 348.00	260.00	100.24	03/2012 -	12/2011	-3(O)	6/12
102	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.29	09/2011 -	12/2011	3(O)	0/0
103	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	375.00	58.03	06/2011 -	12/2011	6(O)	3/9
104	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,498.47	05/2011 -	12/2011	7(O)	0/116
105	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL,Maharashtra	02/2008	825.00 -	825.00	99.58	- 12/2011	01/2012	1(R3)	0/203
106	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	375.00	21.89	06/2011 07/2012	01/2012	-6(R3)	7/9
107	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.00	5,100.00	01/2012 -	01/2012	0(O)	0/0
108	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	411.64	03/2010 03/2012	03/2012	0(R1)	0/0
109	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 -	3,597.00	354.02	09/2011 -	03/2012	6(O)	0/0
110	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	227.38	09/2011 -	03/2012	6(O)	0/0
111	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	390.05	03/2012 -	03/2012	0(O)	11/10
112	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	608.56	09/2010 03/2012	04/2012	1(R3)	0/0
113	Assam gas Cracker project - [N16000106]BCPL,	04/2006	5,460.61 -	5,460.61	-	- -	04/2012	-	0/30
114	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	2,445.44	05/2010 05/2012	05/2012	0(R3)	0/0
115	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	3.34	05/2010 04/2012	05/2012	1(R3)	0/0
116	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,456.96	-	07/2010 05/2012	05/2012	0(R3)	0/0
117	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	27.26	05/2012 08/2010	05/2012	21(R3)	5/36
118	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	594.29	08/2010 03/2012	06/2012	3(R3)	0/0
119	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	397.69	06/2012 -	06/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
120	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Orissa	12/2009	1,492.33	1,492.33	614.18	06/2012	06/2012	0(O)	0/0
121	Wind Power Project - [N16000119]ONGC,Gujarat	07/2010	1,106.00	1,106.00	-	06/2012	06/2012	0(O)	0/0
122	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	46.00	04/2011	07/2012	15(O)	0/0
123	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	150.84	07/2012	07/2012	0(O)	0/0
124	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04	253.66	45.06	08/2012	08/2012	0(O)	0/0
125	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	7,133.39	1,659.23	09/2012	09/2012	0(O)	0/0
126	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	212.14	-	09/2012	-	0/15
127	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78	234.78	15.78	09/2012	09/2012	0(O)	0/0
128	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	302.26	15.78	09/2012	09/2012	0(O)	0/0
129	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	29,777.00	6,404.95	-	11/2012	-	107/103
130	Development of SB-14 Field - [N16000125]ONGC,Multi State	01/2011	410.44	410.44	-	12/2012	12/2012	0(O)	0/0
131	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	890.37	49.86	12/2011	01/2013	13(O)	0/0
132	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	8.93	01/2013	01/2013	0(O)	0/0
133	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	-	01/2013	01/2013	0(O)	0/0
134	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	2.68	02/2013	02/2013	0(O)	0/0
135	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90	438.85	218.08	03/2006	03/2013	0(R3)	6/6
136	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	8,813.41	6,212.68	05/2010	03/2013	0(R3)	0/0
137	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	281.62	03/2013	03/2013	0(O)	0/0
138	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
139	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
140	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	-	03/2013	03/2013	0(O)	0/0
141	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	331.20	-	08/2013	03/2013	-5(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
142	Development of BHE & BH-35 Area - [N16000124]ONGC,Multi State	08/2010	372.11	372.11	-	03/2013	03/2013	0(O)	0/0
143	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	1.69	-	08/2013	-	0/0
144	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
145	Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	8.18	02/2014	02/2014	0(O)	0/0
146	Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	62.33	02/2014	02/2014	0(O)	0/0
147	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	559.61	03/2007 03/2014	03/2014	0(R3)	3/3
148	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
149	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
150	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
151	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,184.06	03/2007 03/2017	03/2017	0(R3)	6/6
152	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
153	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	0.65	03/2012	03/2012	0(O)	0/0
Total			167,009.99	175,658.75	51,484.89				171/585
Power									
154	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44	2,570.44	1,896.00	08/2010	03/2011	7(O)	13/26
155	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49	299.08	333.30	04/2010	04/2011	12(O)	0/0
156	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34	241.27	164.36	06/2008	06/2011	36(O)	9/20
157	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70	803.76	644.31	06/2009	06/2011	24(O)	1/20
158	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	638.75	10/2009	06/2011	20(O)	2/20
159	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	126.68	06/2010	06/2011	12(O)	0/0
160	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	102.35	06/2011	06/2011	0(O)	0/0
161	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	71.85	01/2011	06/2011	5(O)	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
162	TRANSMISSION SYSTEM ASSOCIATED WITH CORBA III GENE - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	190.98	06/2011	06/2011	0(O)	0/0
163	Transmission system associated with Uri-II HEP - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	206.10	05/2011 05/2011	07/2011	2(R3)	0/0
164	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	278.23	07/2011	07/2011	0(O)	0/0
165	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	51.42	07/2011	07/2011	0(O)	0/0
166	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,554.83	08/2010	08/2011	12(O)	0/0
167	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	622.08	02/2011	08/2011	6(O)	0/1
168	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	154.67	09/2010	08/2011	11(O)	0/0
169	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	134.49	08/2011	08/2011	0(O)	0/0
170	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC,J & K	08/2006	611.02	611.02	622.61	08/2010	09/2011	13(O)	0/0
171	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,436.48	09/2009	10/2011	25(O)	15/30
172	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,401.40	11/2009	11/2011	24(O)	0/0
173	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	426.11	01/2010	11/2011	22(O)	0/22
174	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	226.05	11/2011	11/2011	0(O)	0/0
175	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	219.02	11/2011	11/2011	0(O)	0/0
176	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	48.11	11/2011	11/2011	0(O)	0/0
177	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	113.15	11/2011	11/2011	0(O)	0/0
178	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,402.45	10/2010	12/2011	14(O)	0/0
179	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,774.05	07/2010	12/2011	17(O)	3/20
180	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.53	3,675.00	05/2011	12/2011	7(O)	0/0
181	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	208.92	02/2012	02/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
182	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	23.62	02/2012	02/2012	0(O)	0/0
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	109.14	02/2012	02/2012	0(O)	0/0
184	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	199.46	07/2010 02/2012	02/2012	0(R3)	0/0
185	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	695.17	02/2012	02/2012	0(O)	0/0
186	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,306.88	04/2005	03/2012	83(O)	2/1
187	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	6,916.00	12/2009	03/2012	27(O)	33/56
188	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,672.40	11/2008	03/2012	40(O)	25/38
189	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	33.05	04/2012	03/2012	-1(O)	0/0
190	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,273.57	03/2007	05/2012	62(O)	1/25
191	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	168.45	05/2012	05/2012	0(O)	0/0
192	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	186.47	06/2012	06/2012	0(O)	0/0
193	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	74.98	06/2012	06/2012	0(O)	0/0
194	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	6.30	06/2012	06/2012	0(O)	0/0
195	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,537.64	08/2012	08/2012	0(O)	0/0
196	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	3,298.25	08/2012	08/2012	0(O)	0/0
197	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	207.00	08/2012	08/2012	0(O)	0/0
198	TRANSMISSION SYSTEM ASSOCIATED WITH MUNDRA ULTRA M - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,379.93	10/2012	10/2012	0(O)	0/0
199	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	63.02	10/2012	10/2012	0(O)	0/0
200	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF I - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	3.72	10/2012	10/2012	0(O)	0/0
201	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	2,069.00	08/2012	11/2012	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
202	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	75.20	11/2012 -	11/2012	0(O)	0/0
203	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	133.28	11/2012 -	11/2012	0(O)	0/0
204	Transmission system associated with krishnapatnam-part-A - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	3.71	08/2013 -	11/2012	-9(O)	0/0
205	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	928.52	09/2009 -	12/2012	39(O)	0/0
206	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42 -	358.42	14.74	12/2008 09/2010	12/2012	27(R1)	0/15
207	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	1,974.24	12/2012 -	12/2012	0(O)	0/0
208	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	1,564.00	10/2012 -	12/2012	2(O)	0/0
209	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	1,445.00	10/2012 -	12/2012	2(O)	0/0
210	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	151.85	12/2012 -	12/2012	0(O)	0/0
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	-	01/2013 -	01/2013	0(O)	0/0
212	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	3,507.00	04/2009 -	03/2013	47(O)	19/41
213	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	333.53	09/2010 -	03/2013	30(O)	0/0
214	Transmission System for phase-1 generation project - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	48.01	03/2013 -	03/2013	0(O)	0/0
215	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	1,831.00	07/2011 -	04/2013	21(O)	0/0
216	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	63.59	01/2012 -	07/2013	18(O)	0/0
217	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	182.47	08/2013 08/2013	08/2013	0(R3)	8/17
218	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	2,072.84	08/2013 -	08/2013	0(O)	0/0
219	Northern Region system strengthening scheme-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	10.35	08/2013 -	08/2013	0(O)	0/0
220	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	32.91	08/2013 -	08/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,127.52	01/2012	09/2013	20(O)	2/10
222	BARH STPP STAGE -II (NTPC) - [N18000047]NTPC, Bihar	02/2008	7,341.04	7,341.04	1,755.00	08/2013	10/2013	2(O)	0/0
223	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33	6,285.33	4,844.54	09/2010	12/2013	39(O)	2/11
224	Transmission system for phase-I generation project - [N18000093]PGCIL, Orissa	12/2010	2,743.19	2,743.19	30.63	12/2013	12/2013	0(O)	0/0
225	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72	913.63	226.09	07/2006	01/2014	0(R3)	2/5
226	Tapovan-Vishnugad HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttarakhand	11/2006	2,978.48	2,978.48	1,018.00	03/2013	02/2014	11(O)	5/31
227	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59	3,919.59	3,084.87	09/2009	07/2014	58(O)	1/20
228	BARH STPP(3x660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,693.00	8,692.97	5,361.00	11/2010	09/2014	46(O)	15/51
229	Transm System for development of Pooling stn. in N - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
230	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttarakhand	07/2006	1,657.00	2,978.86	252.14	07/2010	03/2015	56(O)	0/0
231	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67	3,642.04	688.64	07/2014	01/2016	18(O)	0/0
232	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttarakhand	08/2008	2,221.31	2,491.58	146.49	07/2014	03/2016	20(O)	0/8
233	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90	2,496.90	1,410.14	12/2009	06/2016	0(R3)	78/21
234	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45	947.96	801.35	12/2007	-	-	14/18
	Total		173,209.28	178,736.68	79,066.45	12/2009			250/528

Railways

235	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, Orissa	04/1999	166.16	243.40	227.21	-	12/2010	22(R1)	0/0
236	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41	211.90	-	02/2009	12/2010	21(R1)	0/0
237	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	221.90	139.10	03/2009	12/2010	9(R1)	0/0
238	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73	399.50	289.67	12/2008	12/2010	24(R1)	0/0
239	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL, Gujarat	09/2005	200.80	200.80	214.20	-	12/2010	-	0/0
240	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00	925.00	493.70	05/2008	03/2011	34(O)	0/0
241	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhattisgarh	04/1997	151.52	273.00	268.07	03/2009	03/2011	24(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
242	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	275.40	03/2009 12/2009	03/2011	15(R1)	0/0
243	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	272.11	349.61	- -	03/2011	-	0/0
244	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	156.82	03/2011 -	03/2011	0(O)	0/0
245	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,087.96	- 12/2010	06/2011	6(R3)	0/1
246	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	415.41	361.97	06/2005 07/2011	07/2011	0(R3)	0/0
247	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	143.87	- -	08/2011	-	0/0
248	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	178.20	03/2002 -	09/2011	114(O)	0/0
249	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	147.13	02/2010 -	11/2011	21(O)	0/0
250	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	512.70	03/1994 -	12/2011	213(O)	0/0
251	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	401.33	02/2009 -	12/2011	34(O)	0/0
252	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	191.04	- 09/2009	12/2011	27(R1)	0/0
253	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	72.14	- -	12/2011	-	0/0
254	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	50.71	12/2011 -	12/2011	0(O)	0/0
255	Ghutarisharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	43.98	12/2011 -	12/2011	0(O)	0/0
256	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,117.17	- -	02/2012	-	0/0
257	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	617.63	465.67	- -	03/2012	-	0/0
258	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	179.88	- 03/2012	03/2012	0(R3)	0/0
259	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	322.29	393.94	- -	03/2012	-	0/0
260	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	727.52	509.74	- -	03/2012	-	0/0
261	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	205.57	- -	03/2012	-	0/0
262	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	348.78	326.45	- 03/2011	03/2012	12(R3)	0/0
263	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	175.15	- -	03/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
264	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	813.57	- -	03/2012	-	0/0
265	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	165.10	03/2010 -	03/2012	24(O)	0/0
266	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	160.48	160.50	- -	03/2012	-	0/0
267	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	124.80	03/2012 -	03/2012	0(O)	0/0
268	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	203.22	03/2011 -	03/2012	12(O)	0/0
269	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	749.10	03/2011 -	03/2012	12(O)	0/0
270	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	34.30	03/2012 -	03/2012	0(O)	0/0
271	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	27.28	03/2012 -	03/2012	0(O)	0/0
272	Bhuj-Naliya(GC) with extension from naliya te vayar - [N22000123]WR,Gujarat	04/2008	318.24 -	318.24	0.10	03/2012 -	03/2012	0(O)	0/0
273	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	157.94	- -	06/2012	-	0/0
274	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	313.10	- 07/2012	07/2012	0(R3)	0/0
275	DALLIRAJDHARA - RAOGHAT(PART OF DALLIRAJHARA-JAGDALPUR),NL,R - [220100149]RVNL,Chhatisgarh	04/1995	304.00 631.78	631.78	82.83	12/2012 -	12/2012	0(O)	0/0
276	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,404.00	537.68	- -	12/2012	-	0/0
277	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,103.47	722.07	12/2012 -	12/2012	0(O)	0/0
278	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	325.17	368.83	03/2005 12/2008	12/2012	48(R1)	0/0
279	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	234.45	214.58	- 03/2012	12/2012	9(R3)	0/0
280	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	436.45	03/2009 -	12/2012	45(O)	0/0
281	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.00	891.63	10/2007 -	12/2012	62(O)	0/0
282	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	294.26	03/2010 -	12/2012	33(O)	0/0
283	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	97.17	12/2012 -	12/2012	0(O)	0/0
284	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	227.90	80.72	12/2012 -	12/2012	0(O)	0/0
285	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	139.18	- 03/2013	03/2013	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
286	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	136.89	- -	03/2013	-	0/0
287	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	653.18	- -	03/2013	-	0/0
288	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	915.70 912.70	1,556.23	565.31	- -	03/2013	-	0/0
289	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	350.81	-	03/2013 -	03/2013	0(O)	0/0
290	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]M RTP,Tamil Nadu	04/2006	495.74 495.74	495.74	108.50	- 06/2013	06/2013	0(R3)	0/0
291	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.00	174.55	03/2013 -	12/2013	9(O)	0/0
292	Lumding-silchar jiribam, badarpur-baraigram kumarghat - [N22000127]NEFR,Multi State	04/1996	1,676.31 -	3,909.49	2,629.95	03/2009 -	12/2013	57(O)	0/0
293	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,162.02	04/2008 03/2014	03/2014	0(R3)	0/0
294	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	672.73	12/2008 -	03/2014	63(O)	0/0
295	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	165.64	03/2014 -	03/2014	0(O)	0/0
296	BHAIRABI SAIRONG, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	2.89	04/2014 -	03/2014	-1(O)	0/0
297	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	0.21	03/2014 -	03/2014	0(O)	0/0
298	Jaipur - Ringus - Churu and Sikar - Lohatu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	3.13	03/2014 -	03/2014	0(O)	0/0
299	Suratpura - Hanumangarh - Sriganganagar Guage Canv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	7.92	03/2014 -	03/2014	0(O)	0/0
300	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	116.09	03/2014 -	03/2014	0(O)	0/0
301	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	92.32	03/2010 06/2014	06/2014	0(R3)	0/0
302	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	154.91	- -	03/2015	-	0/0
303	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]M RTP,Maharashtra	04/2008	5,300.00 -	5,300.00	171.00	03/2014 -	03/2015	12(O)	0/0
304	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.94	12/2015 -	03/2015	-9(O)	0/0
305	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	0.09	03/2015 -	03/2015	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
306	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00	850.00	7.98	03/2015	03/2015	0(O)	0/0
307	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,056.85	396.69	03/2011 03/2014	03/2016	24(R3)	0/0
308	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	2,397.72	-	03/2016	03/2016	0(O)	0/0
309	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98	3,951.98	1.42	03/2016	03/2016	0(O)	0/0
310	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02	2,619.02	19.40	03/2016	03/2016	0(O)	0/0
311	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,166.01	03/2001	12/2017	201(O)	0/0
312	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	534.28	03/1995	-	-	0/0
313	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	464.50	504.20	03/1996 07/2002	-	-	0/0
314	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	285.93	233.02	-	-	-	0/0
315	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	589.87	-	-	-	0/0
316	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	93.97	-	-	-	0/0
317	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00	412.91	449.87	-	-	-	0/0
318	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30	1,038.00	520.42	03/1998	-	-	0/0
319	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55	712.00	522.06	-	-	-	0/0
320	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00	997.58	58.20	-	-	-	0/0
321	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	78.27	-	-	-	0/0
322	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	154.30	128.54	03/2007 03/2007	-	-	0/0
323	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00	363.26	0.27	07/2008	-	-	0/0
324	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	988.38	07/2005	-	-	0/0
325	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00	513.16	535.83	-	-	-	0/0
326	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	550.00	68.13	-	-	-	0/0
327	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23	162.87	86.25	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
328	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	639.54	804.25	06/2007 -	-	-	0/0
329	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	-	04/2003 03/2010	-	-	0/0
330	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	454.48	- -	-	-	0/0
331	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
332	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	293.52	- 12/2012	-	-	0/0
333	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
334	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	68.62	- -	-	-	0/0
335	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	201.05	- -	-	-	0/0
336	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0
337	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
338	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	- -	-	-	0/0
339	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	274.28	03/2008 06/2008	-	-	0/0
340	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	145.38	- -	-	-	0/0
341	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	359.30	- -	-	-	0/0
342	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	20.40	- -	-	-	0/0
343	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	70.01	- -	-	-	0/0
344	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	31.12	- -	-	-	0/0
345	KISHANGANJ JALALGARH, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	333.76	0.71	- -	-	-	0/0
346	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	429.58	06/1999 03/2011	03/2011	0(R3)	0/0
347	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	162.68	03/2004 -	-	-	0/0
348	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	409.17	- 12/2011	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
349	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	547.31	- 11/2010	-	-	0/0
350	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 589.86	563.25	540.93	03/2004 03/2010	-	-	0/0
351	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	281.20	323.10	- 03/2011	03/2011	0(R3)	0/0
352	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	264.11	06/2004 04/2005	03/2011	71(R3)	0/0
353	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	214.09	177.70	12/2009 03/2011	03/2011	0(R3)	0/0
354	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	724.31	707.50	- 12/2010	-	-	0/0
355	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	257.38	- -	03/2013	-	0/0
356	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	374.95	- -	03/2011	-	0/1
357	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]ER,Jharkhandd	02/1999	180.73 -	358.00	347.43	12/2006 02/2011	02/2011	0(R3)	0/0
358	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	2,812.07	2,690.75	12/2006 08/2010	03/2011	7(R3)	0/0
359	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	219.30	- 02/2011	02/2011	0(R3)	0/0
360	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	358.14	- 12/2009	-	-	0/0
361	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.16	449.82	02/2010 02/2011	02/2011	0(R3)	0/0
362	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	330.81	- -	-	-	0/0
363	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	223.19	- 03/2011	03/2011	0(R3)	0/0
364	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	97.32	- -	03/2011	-	0/0
365	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	133.60	- -	03/2011	-	0/0
366	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	255.30	03/2008 10/2010	-	-	0/0
367	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	283.10	1.86	02/2006 02/2006	01/2012	71(R3)	0/0
368	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056]SWR,Karnataka	12/1992	46.00 218.00	218.00	246.36	- 02/2011	02/2011	0(R3)	0/0
369	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	46.05	- -	-	-	0/0
370	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	130.15	12/2010 03/2011	03/2011	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
371	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97	196.97	142.14	03/2011	03/2011	0(O)	0/0
372	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68	225.68	121.83	-	-	-	0/0
			-	-	-	12/2010	-	-	0/0
	Total		67,069.85	119,977.99	52,723.66				0/2
			-	-	-				
Road Transport & Highways									
373	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73	205.73	247.70	07/2004	04/2011	81(O)	0/0
			-	-	-	-	-	-	0/0
374	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00	210.00	670.40	04/2007	04/2011	48(O)	0/0
			-	-	-	-	-	-	0/0
375	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00	239.00	317.62	07/2005	04/2011	69(O)	0/0
			-	-	-	-	-	-	0/0
376	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36	323.36	200.98	03/2008	04/2011	37(O)	0/0
			-	-	-	-	-	-	0/0
377	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	910.04	11/2010	04/2011	5(O)	0/0
			-	-	-	-	-	-	0/0
378	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam	12/2003	230.00	230.00	312.00	06/2008	04/2011	34(O)	0/0
			-	-	-	-	-	-	0/0
379	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	275.30	10/2008	04/2011	30(O)	0/0
			-	-	-	-	-	-	0/0
380	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	592.10	03/2009	04/2011	25(O)	0/0
			-	-	-	-	-	-	0/0
381	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	242.21	02/2004	04/2011	86(O)	0/0
			-	-	-	-	-	-	0/0
382	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00	309.00	553.56	06/2010	04/2011	10(O)	0/0
			-	-	-	-	-	-	0/0
383	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	613.96	07/2010	04/2011	9(O)	0/0
			-	-	-	-	-	-	0/0
384	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	355.83	07/2010	04/2011	9(O)	0/0
			-	-	-	-	-	-	0/0
385	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	132.29	02/2004	04/2011	86(O)	0/0
			-	-	-	-	-	-	0/0
386	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	418.40	01/2011	04/2011	3(O)	0/0
			-	-	-	-	-	-	0/0
387	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra	03/2005	579.00	579.00	765.86	04/2009	05/2011	25(O)	0/0
			-	-	-	-	-	-	0/0
388	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	348.34	12/2008	05/2011	29(O)	0/0
			-	-	-	-	-	-	0/0
389	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	294.85	09/2009	05/2011	20(O)	0/0
			-	-	-	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
390	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	622.81	08/2010	05/2011	9(O)	0/0
391	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI, Madhya pradesh	11/2008	549.00	549.00	792.50	05/2010	05/2011	12(O)	0/0
392	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	491.96	05/2010	05/2011	12(O)	0/0
393	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	135.40	08/2004	06/2011	82(O)	0/0
394	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	145.22	08/2004	06/2011	82(O)	0/0
395	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	379.17	03/2005	06/2011	75(O)	0/0
396	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	275.00	288.00	09/2007	06/2011	45(O)	0/0
397	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	200.90	09/2007	06/2011	45(O)	0/0
398	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78	479.54	435.53	11/2007	06/2011	43(O)	0/0
399	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI, Uttar Pradesh	12/2003	193.00	193.00	321.11	10/2008	06/2011	32(O)	0/0
400	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI, Uttar Pradesh	12/2003	217.00	217.00	345.41	10/2008	06/2011	32(O)	0/0
401	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K	12/2003	193.09	166.30	167.60	03/2008	06/2011	39(O)	0/0
402	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K	12/2003	166.27	193.10	136.88	03/2008	06/2011	39(O)	0/0
403	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	240.86	10/2008	06/2011	32(O)	0/0
404	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00	227.00	341.38	10/2008	06/2011	32(O)	0/0
405	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	333.65	03/2008	06/2011	39(O)	0/0
406	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI, Uttar Pradesh	03/2005	359.00	359.00	772.84	03/2009	06/2011	27(O)	0/0
407	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	06/2011	29(O)	0/0
408	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	333.08	12/2008	06/2011	30(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
409	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	248.75	09/2008	06/2011	33(O)	0/0
410	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	170.14	11/2008	06/2011	31(O)	0/0
411	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	247.23	10/2008	06/2011	32(O)	0/0
412	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	197.60	10/2008	06/2011	32(O)	0/0
413	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	534.99	06/2008	06/2011	36(O)	0/0
414	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	06/2011	24(O)	0/0
415	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	636.52	10/2009	06/2011	20(O)	0/0
416	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	293.85	10/2009	06/2011	20(O)	0/0
417	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	411.85	12/2009	06/2011	18(O)	0/0
418	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	294.38	09/2009	06/2011	21(O)	0/0
419	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	548.66	07/2010	06/2011	11(O)	0/0
420	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,803.00	01/2011	06/2011	5(O)	0/0
421	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	785.70	07/2010	06/2011	11(O)	0/0
422	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka	03/2005	565.00	565.00	1,035.00	07/2010	06/2011	11(O)	0/0
423	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	236.43	10/2008	07/2011	33(O)	0/0
424	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	221.20	06/2008	07/2011	37(O)	0/0
425	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.27	12/2008	08/2011	32(O)	0/0
426	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,102.00	08/2011	08/2011	0(O)	0/0
427	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	209.72	11/2008	09/2011	34(O)	0/0
428	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	60.74	04/2004	10/2011	90(O)	0/0
429	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	238.86	06/2008	10/2011	40(O)	0/0
430	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	171.50	10/2011	10/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
431	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	444.70	10/2011	10/2011	0(O)	0/0
432	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	158.49	10/2008	11/2011	37(O)	0/0
433	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,137.00	11/2011	11/2011	0(O)	0/0
434	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
435	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	76.56	09/2008	12/2011	39(O)	0/0
436	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	192.00	06/2005	12/2011	78(O)	0/0
437	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	209.60	02/2009	12/2011	34(O)	0/0
438	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	73.55	04/2009	12/2011	32(O)	0/0
439	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	159.80	06/2008	12/2011	42(O)	0/0
440	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	184.70	06/2008	12/2011	42(O)	0/0
441	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	181.43	10/2008	12/2011	38(O)	0/0
442	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	410.70	09/2008	12/2011	39(O)	0/0
443	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	244.42	06/2008	12/2011	42(O)	0/0
444	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	229.40	06/2008	12/2011	42(O)	0/0
445	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	458.58	03/2008	12/2011	45(O)	0/0
446	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	160.90	06/2008	12/2011	42(O)	0/0
447	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	173.60	04/2008	12/2011	44(O)	0/0
448	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	98.01	05/2008	12/2011	43(O)	0/0
449	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	175.30	06/2008	12/2011	42(O)	0/0
450	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	579.25	06/2009	12/2011	30(O)	0/0
451	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04	418.04	279.40	03/2010	12/2011	21(O)	0/0
452	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	278.20	02/2012	02/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
453	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	166.90	09/2007 -	03/2012	54(O)	0/0
454	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	101.65	04/2008 -	03/2012	47(O)	0/0
455	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	157.22	04/2008 -	03/2012	47(O)	0/0
456	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	113.47	04/2010 -	03/2012	23(O)	0/0
457	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	178.40	02/2010 -	03/2012	25(O)	0/0
458	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	926.06	02/2010 -	05/2012	27(O)	0/0
459	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	501.80	05/2012 -	05/2012	0(O)	0/0
460	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	559.40	05/2012 -	05/2012	0(O)	0/0
461	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	388.00	246.60	05/2012 -	05/2012	0(O)	0/0
462	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	151.14	10/2008 -	06/2012	44(O)	0/0
463	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	157.00	09/2010 -	06/2012	21(O)	0/0
464	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	835.00	289.90	06/2012 -	06/2012	0(O)	0/0
465	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	1,478.00	10/2011 -	06/2012	8(O)	0/0
466	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	298.60	07/2012 -	07/2012	0(O)	0/0
467	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	93.38	05/2008 -	08/2012	51(O)	0/0
468	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00 -	359.00	93.38	05/2010 -	08/2012	27(O)	0/0
469	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	183.27	06/2010 -	10/2012	28(O)	0/0
470	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	232.70	09/2009 -	10/2012	37(O)	0/0
471	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16(O)	0/0
472	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	608.80	09/2012 -	10/2012	1(O)	0/0
473	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	1,740.00	527.00	10/2012 -	10/2012	0(O)	0/0
474	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	518.79	11/2012 -	11/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
475	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	173.08	07/2008	12/2012	53(O)	0/0
476	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	355.10	12/2012	12/2012	0(O)	0/0
477	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	528.90	01/2013	01/2013	0(O)	0/0
478	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	620.60	09/2010	03/2013	30(O)	0/0
479	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
480	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	29.53	03/2013	03/2013	0(O)	0/0
481	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
482	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
483	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	68.17	05/2013	05/2013	0(O)	0/0
484	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	109.80	09/2007	06/2013	69(O)	0/0
485	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	953.00	1.43	07/2013	07/2013	0(O)	0/0
486	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
487	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0
488	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	29.60	04/2009	12/2013	56(O)	0/0
489	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
490	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	29.12	11/2008	12/2013	61(O)	0/0
491	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	38.58	09/2007	12/2013	75(O)	0/0
492	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	27.64	07/2009	12/2013	53(O)	0/0
Total			53,244.18	55,142.59	42,671.35				0/0
Shipping & Ports									
493	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40	2,427.40	820.50	10/2008	11/2010	25(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
494	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra	08/2008	1,108.12	1,238.88	1,238.88	04/2011 03/2011	03/2011	0(R3)	0/0
495	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	399.13	335.00	08/2010 -	03/2011	7(O)	0/0
496	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	356.12	08/2010 -	04/2011	8(O)	0/0
497	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 253.36	253.36	223.60	12/2007 07/2009	06/2011	23(R3)	0/0
498	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	06/2011	0(R3)	0/0
499	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	230.00	219.00	12/2010 -	06/2011	6(O)	0/0
500	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
501	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00	165.00	117.11	12/2005 01/2008	10/2011	45(R3)	0/0
502	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	290.85	290.85	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
503	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96	1,061.96	240.52	03/2012 -	03/2012	0(O)	0/0
504	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	03/2012	72(O)	0/0
505	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,512.00	1,778.00	01/2012 03/2012	03/2012	0(R3)	0/0
506	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.20	03/2012 -	03/2012	0(O)	0/0
507	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03	277.03	55.41	12/2011 05/2012	05/2012	0(R3)	0/0
508	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	463.69	12/2010 09/2012	09/2012	0(R3)	0/0
509	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
510	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010 -	11/2012	29(O)	0/0
511	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	612.72	61.31	12/2012 -	12/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
512	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.27	02/2011 -	03/2013	25(O)	0/0
513	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	0.73	03/2011 -	03/2013	24(O)	0/0
514	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
515	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 -	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
516	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	966.46	189.92	02/2014 -	02/2014	0(O)	0/0
517	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
Total			19,072.31 -	20,026.03	7,039.23				0/0
Telecommunications									
518	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	225.78	09/2009 -	02/2010	5(O)	0/0
519	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	109.31	12/2005 -	10/2010	58(O)	0/0
520	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
521	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	10/2010	7(O)	0/0
522	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	11/2010	8(O)	0/0
523	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86 234.24	353.00	234.24	02/2008 -	12/2010	34(O)	0/0
524	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	12/2010	21(O)	0/0
525	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	12/2010	9(O)	0/0
526	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	12/2010	9(O)	0/0
527	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	12/2010	9(O)	0/0
528	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	12/2010	9(O)	0/0
529	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	127.42	06/2009 -	01/2011	19(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
530	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	01/2011	22(O)	0/0
531	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.97	03/2009	02/2011	23(O)	0/0
532	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	179.26	12/2008	02/2011	26(O)	0/0
533	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	308.13	03/2009	02/2011	23(O)	0/0
534	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	88.17	06/2009	02/2011	20(O)	0/0
535	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	136.76	01/2009	02/2011	25(O)	0/0
536	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	02/2011	12(O)	0/0
537	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	225.42	10/2008	02/2011	28(O)	0/0
538	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,	01/2009	760.20	1,312.52	759.33	- 03/2011	02/2011	-1(R3)	0/1
539	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.88	01/2010	02/2011	13(O)	0/0
540	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	513.15	01/2010	02/2011	13(O)	0/0
541	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	113.45	01/2010	02/2011	13(O)	0/0
542	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	480.57	12/2008	03/2011	27(O)	0/0
543	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	169.43	03/2009	03/2011	24(O)	0/0
544	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	94.98	09/2009	03/2011	18(O)	0/0
545	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	31.26	10/2009	03/2011	17(O)	0/0
546	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	74.65	09/2010	03/2011	6(O)	0/0
547	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	398.08	02/2009	03/2011	25(O)	0/0
548	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	345.63	08/2009	03/2011	19(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
549	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	232.83	11/2010 -	03/2011	4(O)	0/0
550	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	395.06	10/2009 -	03/2011	17(O)	0/0
551	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	138.65	10/2010 -	04/2011	6(O)	0/0
552	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 -	08/2011	54(O)	0/0
553	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0
554	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	389.86	3.06	09/2011 -	09/2011	0(O)	0/0
555	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	94.13	10/2007 -	-	-	0/0
556	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	350.00	-	- -	-	-	0/0
557	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	841.00	03/2009 -	-	-	0/0
558	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0
	Total		20,025.99 -	21,026.52	7,326.83				0/1
<u>Urban Development</u>									
559	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	181.30	93.80	04/2009 -	01/2011	21(O)	0/0
560	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00 8,605.36	18,894.36	17,467.38	06/2010 -	06/2011	12(O)	0/10
561	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	3,954.59	12/2011 -	03/2013	15(O)	6/6
	Total		15,185.18 -	30,684.66	21,515.77				6/16
<u>Water Resources</u>									
562	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			613,026.37	733653.52	321,943.80				802/1984

Sector wise current status of projects on theFlash Report


Urban Development

I. Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed .1 project do not have fixed dates of commissioning.

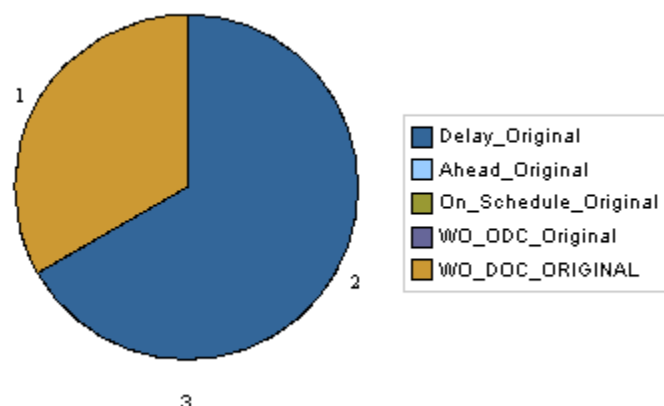

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15185.18 crore but this was subsequently revised to Rs. 30684.66 crore implying a cost overrun of 102.1%. The expenditure incurred on these projects till March, 2011 is Rs. 21515.77 crore, which is 70.1% of the revised cost of the projects.

Figures are in Rs. Crore

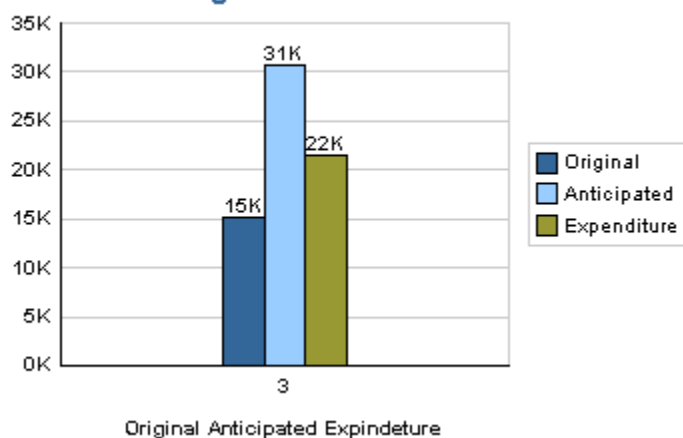

Sector wise current status of projects on theFlash Report

Telecommunications


I. Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning 28

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 41 projects, 1 project are on schedule and 12 projects are delayed .28 projects do not have fixed dates of commissioning.

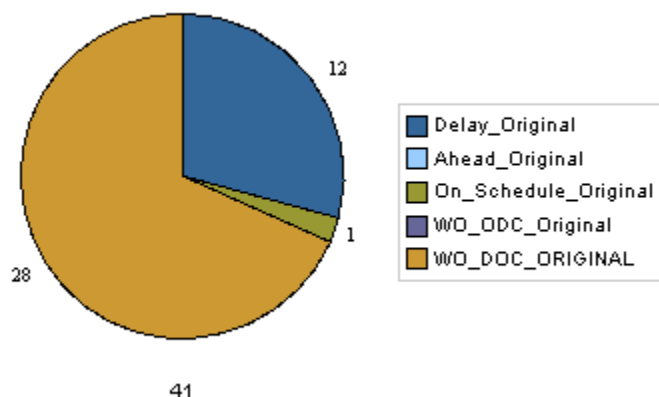

III. Investment Scenario

The Total Original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 20025.99 crore but this was subsequently revised to Rs. 21026.52 crore implying a cost overrun of 5%. The expenditure incurred on these projects till March, 2011 is Rs. 7326.83 crore, which is 34.8% of the revised cost of the projects.

Figures are in Rs. Crore

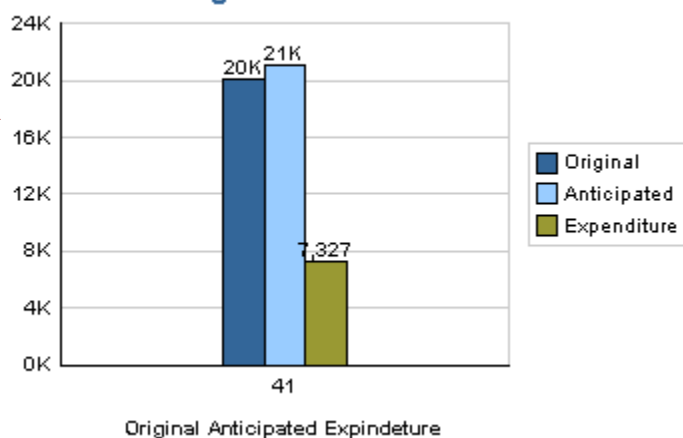

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	13
Number of Projects Delayed	7
Number of Projects Without Original Date of Commissioning	6

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 7 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

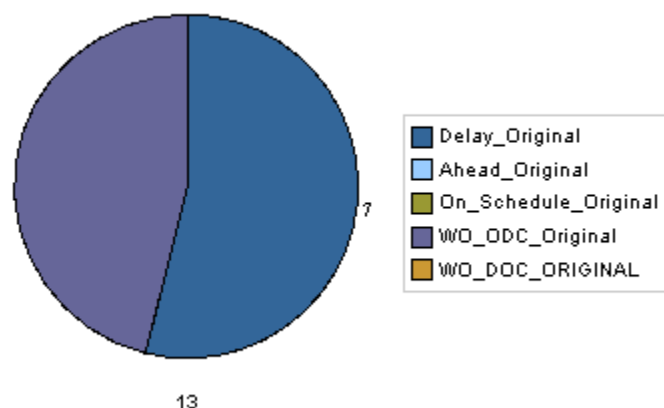

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 39927.85 crore but this was subsequently revised to Rs. 65040.88 crore implying a cost overrun of 62.9%. The expenditure incurred on these projects till March, 2011 is Rs. 25676.31 crore, which is 39.5% of the revised cost of the projects.

Figures are in Rs. Crore

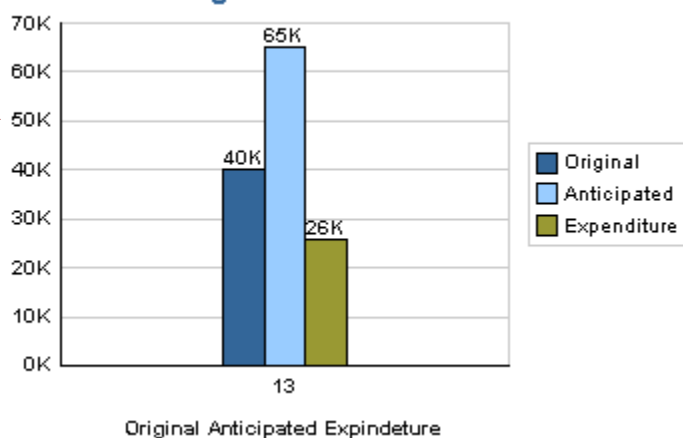

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	25
Number of Projects On Schedule	6
Number of Projects Delayed	16
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 1 project are ahead of schedule, 6 projects are on schedule and 16 projects are delayed .2 projects do not have fixed dates of commissioning.

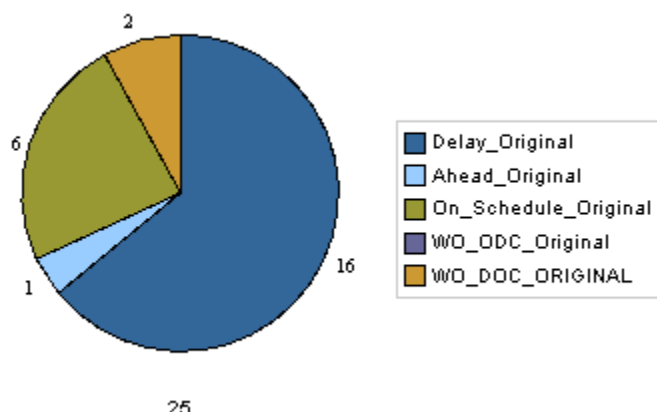

III. Investment Scenario

The Total Original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 19072.31 crore but this was subsequently revised to Rs. 20026.03 crore implying a cost overrun of 5%. The expenditure incurred on these projects till March, 2011 is Rs. 7039.23 crore, which is 35.2% of the revised cost of the projects.

Figures are in Rs. Crore

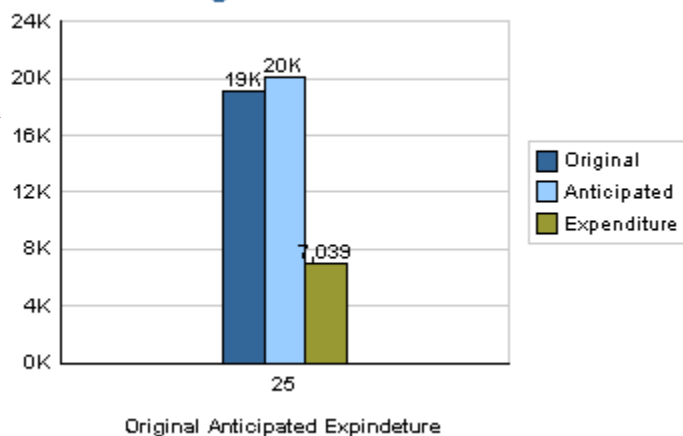

Sector wise current status of projects on theFlash Report


Road Transport & Highways

I. Current Status:

Number of Projects	120
Number of Projects On Schedule	22
Number of Projects Delayed	98

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 120 projects, 22 projects are on schedule and 98 projects are delayed .

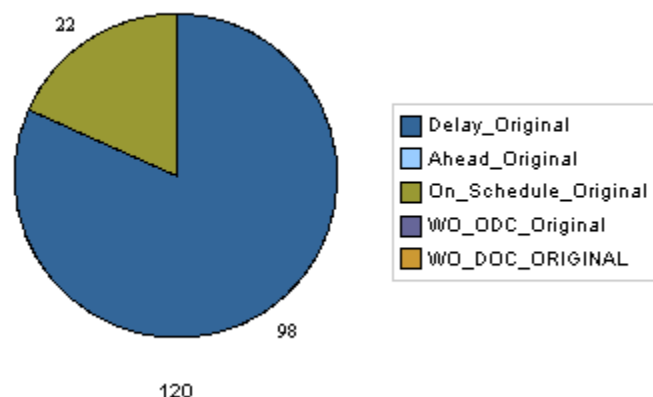

III. Investment Scenario

The Total Original cost of implementation of 120 projects when sanctioned, was of the order of Rs. 53244.18 crore but this was subsequently revised to Rs. 55142.59 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till March, 2011 is Rs. 42671.35 crore, which is 77.4% of the revised cost of the projects.

Figures are in Rs. Crore

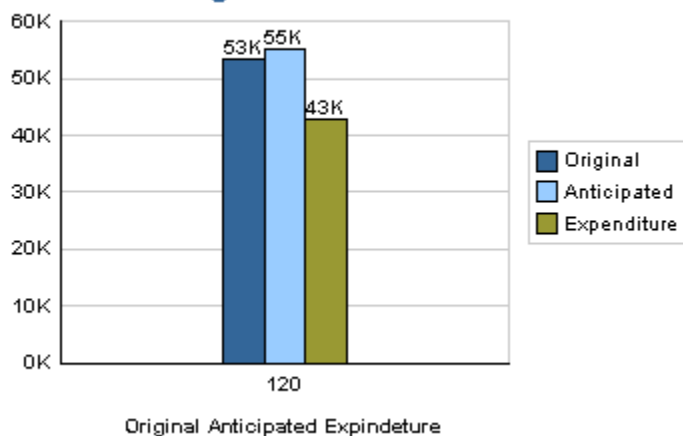

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	138
Number of Projects On Schedule	23
Number of Projects Delayed	28
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	34
Number of Projects Without Date Of Commissioning	51

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 138 projects, 2 projects are ahead of schedule, 23 projects are on schedule and 28 projects are delayed. 51 projects do not have fixed dates of commissioning. 34 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

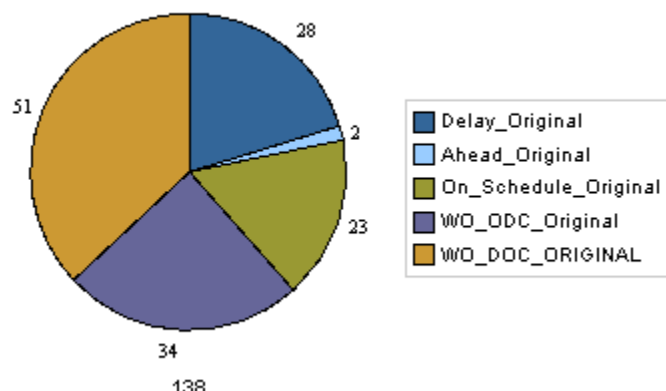

III. Investment Scenario

The Total Original cost of implementation of 138 projects when sanctioned, was of the order of Rs. 67069.85 crore but this was subsequently revised to Rs. 119977.99 crore implying a cost overrun of 78.9%. The expenditure incurred on these projects till March, 2011 is Rs. 52723.66 crore, which is 43.9% of the revised cost of the projects.

Figures are in Rs. Crore

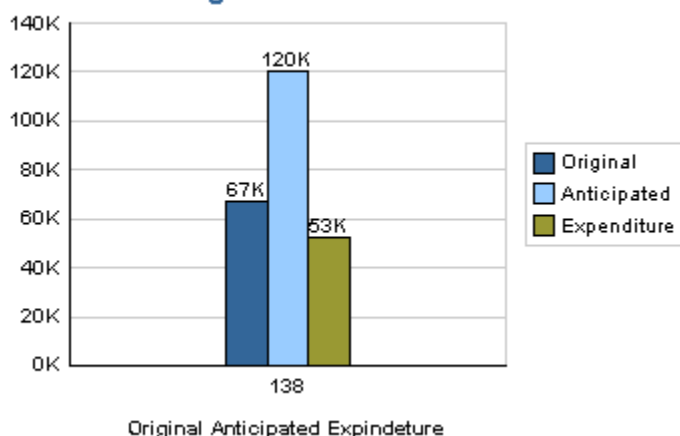

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	81
Number of Projects On Schedule	35
Number of Projects Delayed	43
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 81 projects, 2 projects are ahead of schedule, 35 projects are on schedule and 43 projects are delayed. 1 project do not have fixed dates of commissioning.

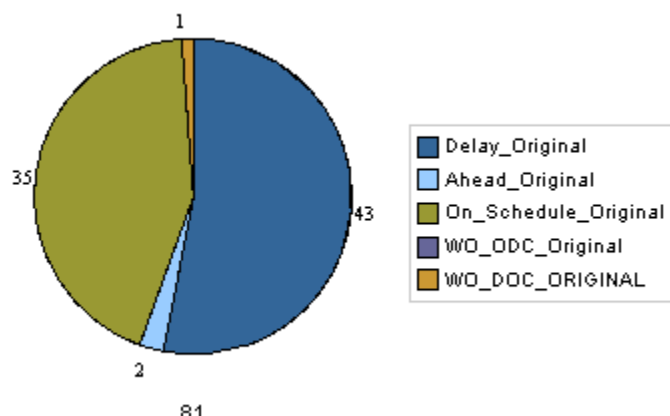

III. Investment Scenario

The Total Original cost of implementation of 81 projects when sanctioned, was of the order of Rs. 173209.28 crore but this was subsequently revised to Rs. 178736.68 crore implying a cost overrun of 3.2%. The expenditure incurred on these projects till March, 2011 is Rs. 79066.45 crore, which is 44.2% of the revised cost of the projects.

Figures are in Rs. Crore

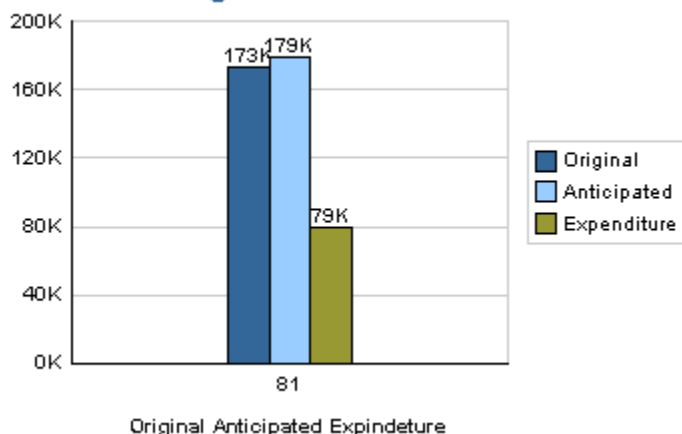

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	77
Number of Projects On Schedule	29
Number of Projects Delayed	32
Number of Projects Ahead	6
Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 77 projects, 6 projects are ahead of schedule, 29 projects are on schedule and 32 projects are delayed. 4 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

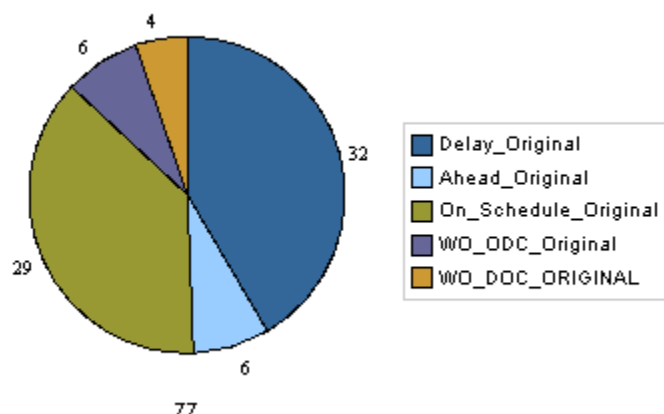

III. Investment Scenario

The Total Original cost of implementation of 77 projects when sanctioned, was of the order of Rs. 167009.99 crore but this was subsequently revised to Rs. 175658.75 crore implying a cost overrun of 5.2%. The expenditure incurred on these projects till March, 2011 is Rs. 51484.89 crore, which is 29.3% of the revised cost of the projects.

Figures are in Rs. Crore

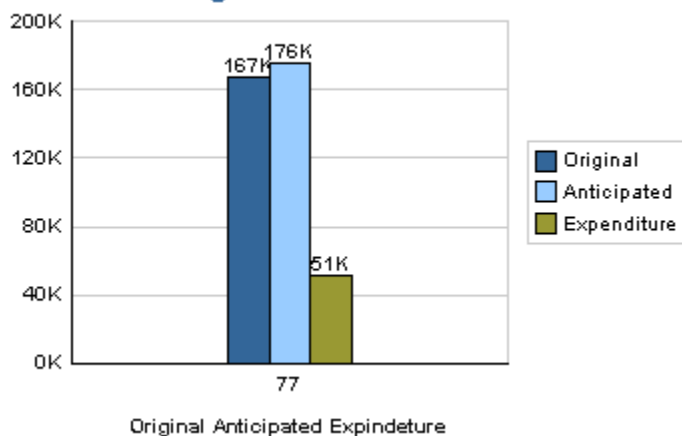

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	1

Number of Projects Without Original Date of Commissioning	1
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule and 1 project are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

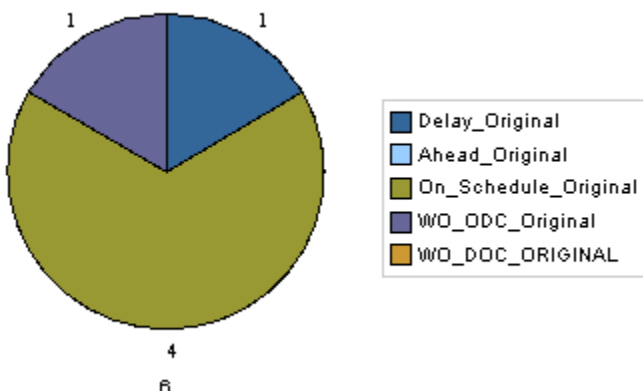

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till March, 2011 is Rs. 390.1 crore, which is 7.3% of the revised cost of the projects.

Figures are in Rs. Crore

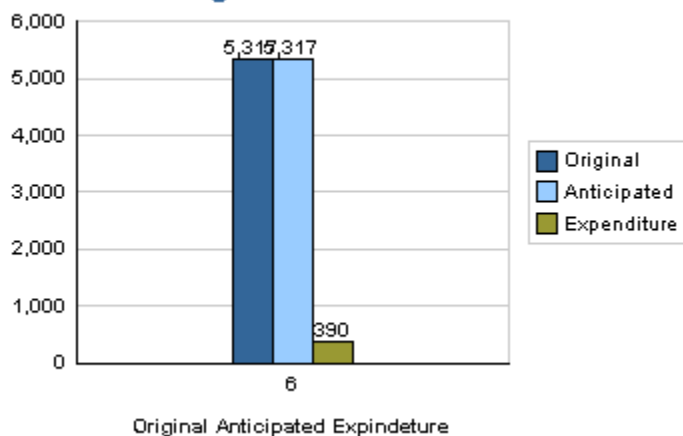

Sector wise current status of projects on theFlash Report


Coal

I. Current Status:

Number of Projects	45
Number of Projects On Schedule	25
Number of Projects Delayed	20

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 45 projects, 25 projects are on schedule and 20 projects are delayed .

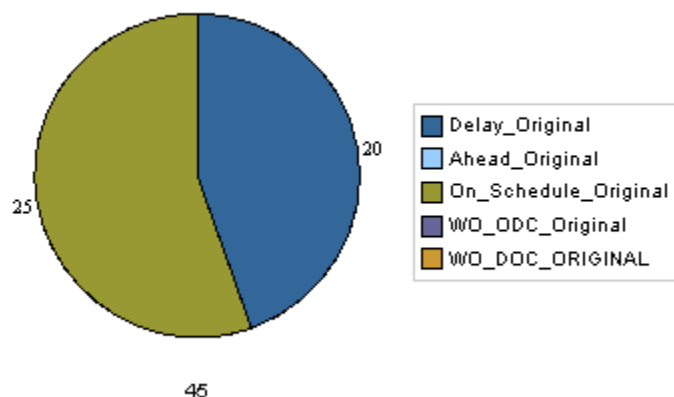

III. Investment Scenario

The Total Original cost of implementation of 45 projects when sanctioned, was of the order of Rs. 25504.15 crore but this was subsequently revised to Rs. 28789.48 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till March, 2011 is Rs. 10912.18 crore, which is 37.9% of the revised cost of the projects.

Figures are in Rs. Crore

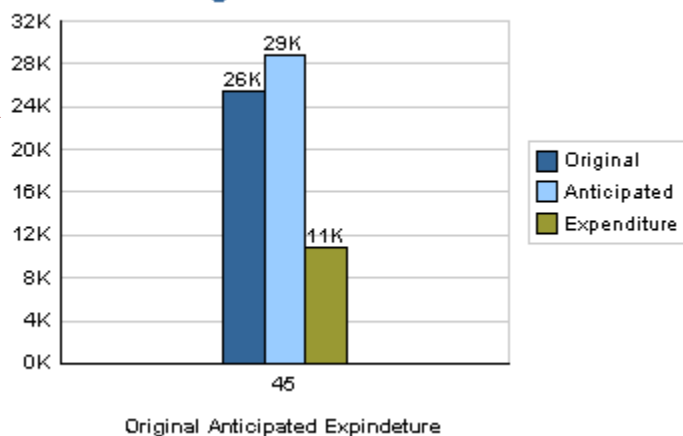

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	3
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule and 3 projects are delayed .3 projects do not have fixed dates of commissioning.

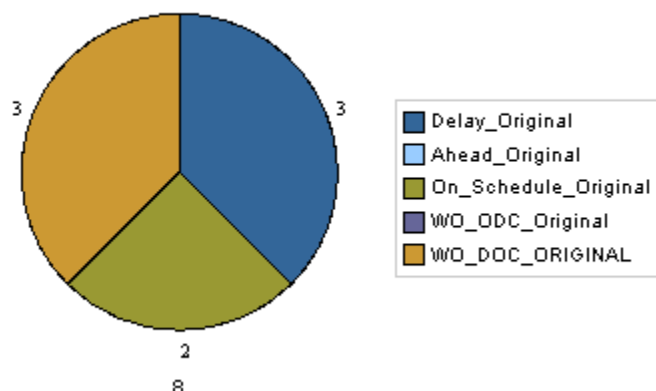

III. Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 5056.48 crore but this was subsequently revised to Rs. 5056.48 crore implying a cost overrun of 0%. The expenditure incurred on these projects till March, 2011 is Rs. 1712.73 crore, which is 33.9% of the revised cost of the projects.

Figures are in Rs. Crore

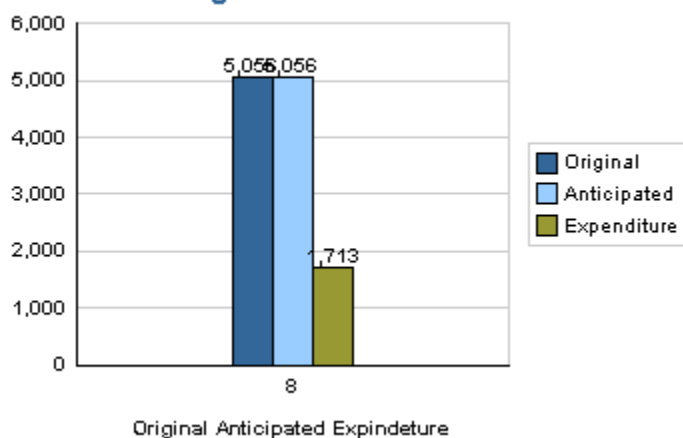

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

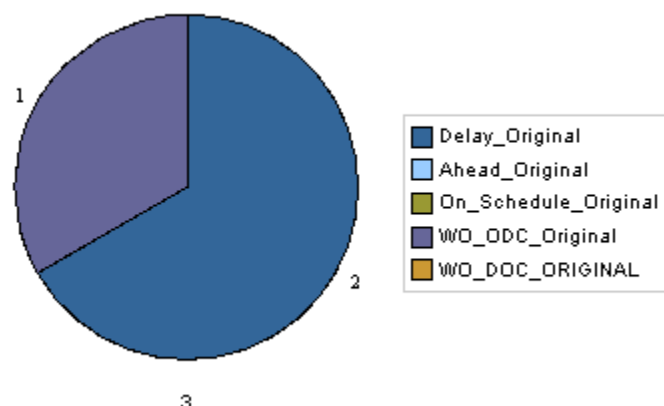

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 17769.29 crore but this was subsequently revised to Rs. 22607.29 crore implying a cost overrun of 27.2%. The expenditure incurred on these projects till March, 2011 is Rs. 17431.5 crore, which is 77.1% of the revised cost of the projects.

Figures are in Rs. Crore

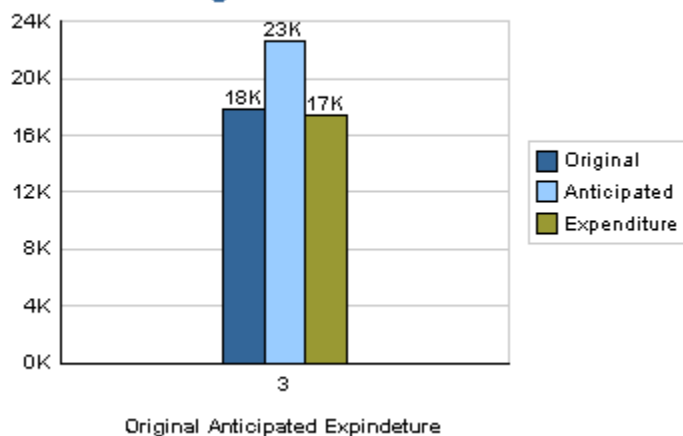

ANNEXURES

SUMMARY OF STATE WISE PROJECTS AS ON 01.04.2011

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	EXPENDITURE CUMM
1	Andhra Pradesh	33	31886.27	38401.29	18021.23
2	Arunachal Pr.	4	9512.22	9516.70	6597.65
3	Assam	37	22540.13	28005.68	11946.04
4	Bihar	27	27513.33	31082.54	17668.21
5	Chhatisgarh	19	22504.86	37600.96	14088.31
6	Delhi	2	8925.00	19123.77	17533.58
7	Goa	1	204.73	204.73	25.64
8	Gujarat	26	19491.34	20457.76	4596.75
9	Haryana	10	4821.32	6379.33	3927.93
10	Himachal Pr.	8	15381.68	15463.96	11272.19
11	J & K	8	8293.37	18455.56	11011.32
12	Jharkhandd	21	9612.58	14402.25	6037.29
13	Karnataka	21	27652.42	34998.48	15169.41
14	Kerala	7	8735.00	9994.11	7151.69
15	Madhya pradesh	25	18938.72	18536.21	6458.65
16	Maharashtra	50	71196.20	84633.84	32074.08
17	Mizoram	2	988.06	3343.04	228.98
18	Multi State	101	119967.89	128452.05	41555.38
19	Nagaland	1	850.00	850.00	7.98
20	Orissa	25	51923.36	59670.26	14666.47
21	Punjab	10	5769.09	6733.72	2855.54
22	Rajasthan	16	13438.03	14527.15	8002.83
23	Sikkim	2	1603.77	3644.86	157.95
24	Tamil Nadu	38	44296.19	53432.30	35768.64
25	Tripura	3	1522.39	2018.86	274.29
26	Uttar Pradesh	30	15770.03	17891.80	10096.78
27	Uttaranchal	7	8777.62	11457.08	3991.92
28	West Bengal	28	40910.77	44375.23	20757.07
TOTA		562	613026.37	733653.52	321943.80

List of Projects Without Original Date of Commissioning as on 01.04.2011

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
	Atomic Energy			
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALLE	N.A.	04/2011	12/2011
	Fertilisers			
2	THAL AMMONIA REVAMP PROJECT	N.A.	11/2011	11/2011
	Petroleum			
3	Assam gas Cracker project	N.A.	N.A.	04/2012
4	BAWANA NANGAL PIPE LINE PROJECT	N.A.	04/2011	12/2011
5	De-bottlenecking of SMPL	N.A.	N.A.	08/2013
6	HYDROCRACKER REVAMP & SETTING	N.A.	12/2011	01/2012
7	PARADIP REFINERY PROJECT	N.A.	N.A.	11/2012
8	Paradip-Sambalpur-Raipur-Ranchi Pipeline	N.A.	N.A.	09/2012
	Railways			
9	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR	N.A.	N.A.	03/2011
10	BILASPUR-URKURA (DL)	N.A.	03/2009	03/2011
11	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT	N.A.	N.A.	03/2012
12	CHHINDWARA - NAGPUR (GC)(SECR)	N.A.	N.A.	06/2012
13	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	N.A.	N.A.	03/2012
14	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	N.A.	N.A.	12/2012
15	DAUSA-GANGAPUR CITY(NL),NWR	N.A.	N.A.	03/2013
16	DEOGHAR - SULTANGANJ (INL), ER	N.A.	12/2012	N.A.
17	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	N.A.	06/2013	06/2013
18	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	N.A.	N.A.	03/2013
19	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	N.A.	N.A.	03/2015
20	HARIDASPUR-PARADEEP(NL)	N.A.	09/2009	12/2011
21	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU	N.A.	N.A.	03/2012
22	HATHUA-BHATNI (N L) (NER)	N.A.	N.A.	03/2011
23	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	N.A.	N.A.	03/2012
24	JIND-SONEPAT (NL),NR	N.A.	03/2012	12/2012
25	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	N.A.	03/2012	03/2012
26	KANPUR-KASGANJ-MATHURA(GC),NER	N.A.	N.A.	02/2012
27	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	N.A.	N.A.	03/2011
28	KHURDA ROAD-BOLANGIR(NL)ECOR	N.A.	N.A.	08/2011
29	KOSI BRIDGE (NL), ECR	N.A.	N.A.	03/2012
30	KOTTUR-HARIHAR(NL),(SWR)	N.A.	03/2011	03/2011
31	MAHARAJGANJ-MASRAKH (NL) - NER	N.A.	N.A.	03/2011
32	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	N.A.	12/2011	N.A.
33	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	N.A.	03/2011	03/2012
34	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	N.A.	12/2010	06/2011
35	MUZAFFARPUR-SITAMARHI(NL),ECR	N.A.	N.A.	03/2012
36	NANGALDAM-TALWARA(NL),NR	N.A.	07/2012	07/2012
37	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	N.A.	N.A.	03/2012
38	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	N.A.	N.A.	03/2013
39	RANGIA-MURKONGSELEK, (GC) NEFR	N.A.	N.A.	03/2013

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
40	SRIGANGANAGAR-SARUPSAR (GC), NWR	N.A.	03/2011	03/2011
41	TALCHER-BIMALAGARH(NL)(ECOR)	N.A.	N.A.	12/2011
42	VIRAMGAM-BHILDI(WR),GC	N.A.	03/2013	03/2013
	Steel			
43	330 TPH BOILER-6 AND AUXILIARY SYSTEM	N.A.	N.A.	07/2011
44	Augmentation of Iron Ore Storage in RMHP	N.A.	N.A.	05/2012
45	Bailadila Iron Ore Deposit- II(B)(NMDC)	N.A.	N.A.	10/2011
46	EXPANSION OF BHILAI STEEL PLANT	N.A.	03/2013	03/2013
47	EXPANSION OF BOKARO STEEL PLANT	N.A.	12/2011	12/2011
48	INSTALLATION OF 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI	N.A.	N.A.	07/2011

List of Projects Without Date of commissioning as on 01.04.2011

SN	PROJECTS NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
Civil Aviation				
1	Extension of Secondary Runway, Construction of Taxi tracks at chennai Airport(K2)	01/2011	N.A.	N.A.
2	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNAI AIRPORT	06/2010	N.A.	N.A.
3	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TER BLDG(K1)	01/2011	N.A.	01/2011
Petroleum				
4	CAPACITY EXP. CUM MODERNISATION PH-II	12/2009	N.A.	12/2010
5	JHAJJAR HISSAR PIPE LINE PROJECT	10/2010	N.A.	N.A.
6	Guru Govind Singh Refinery Products Evacuation Project	12/2010	12/2010	12/2010
7	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)	05/2008	07/2010	02/2011
Power				
8	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	12/2007	12/2009	N.A.
Railways				
9	REWARI-ROHTAK (NL),NR	02/2010	02/2011	02/2011
10	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	06/2007	N.A.	N.A.
11	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	N.A.	N.A.	N.A.
12	KODERMA GIRIDH (NL), ECR	N.A.	N.A.	N.A.
13	KODERMA-TILAIYA (NL), ECR	N.A.	N.A.	N.A.
14	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR	07/2005	N.A.	N.A.
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	N.A.	N.A.	N.A.
16	Pandabeswar-Chinpai doubling (ER)	N.A.	12/2010	N.A.
17	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	N.A.	12/2009	N.A.
18	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	12/2006	02/2011	02/2011
19	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	03/1995	N.A.	N.A.
20	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP)	03/2004	N.A.	N.A.
21	KISHANGANJ JALALGARH, NEFR	N.A.	N.A.	N.A.
22	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	N.A.	N.A.	N.A.
23	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR	N.A.	N.A.	N.A.
24	KATIHAR - JOGBANI (GC)(NEFR)	N.A.	12/2010	N.A.
25	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	N.A.	N.A.	N.A.
26	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	N.A.	11/2010	N.A.
27	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	N.A.	N.A.	12/2010
28	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	03/2008	06/2008	N.A.
29	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)	03/2009	12/2008	12/2010
30	RAICHUR-GUNTAKAL(DL)(SCR)	12/2007	03/2010	12/2010
31	SUKINDA ROAD - ANGUL (NL)(ECOR)	02/2015	N.A.	N.A.
32	RAJATGARH-BARANG(LD),ECOR	N.A.	02/2009	12/2010
33	RENIGUNTA-GUNTAKAL(RE)	04/2003	03/2010	N.A.
34	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	N.A.	03/2009	12/2010
35	MANOHARABAD-KOTHPALL NEW LINE(SCR)	N.A.	N.A.	N.A.
36	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)	N.A.	N.A.	N.A.

SN	PROJECTS NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
37	GADWAL - RAICHUR (NL), SCR	N.A.	02/2011	02/2011
38	MACHERLA-NALGONDA(NL)(SCR)	07/2008	N.A.	N.A.
39	MUNEERABAD-MAHABOBNAGAR(NL),SCR	N.A.	N.A.	N.A.
40	KOTLPALLI-NARASAPUR (NL) (SCR)	N.A.	N.A.	N.A.
41	GONDIA-JABALPUR(GC),(SECR)	03/1998	N.A.	N.A.
42	HOWRAH-AMTA-CHAMPADANGA NL (SER)	03/2007	03/2007	N.A.
43	TIDIVANAM-NAGARI (NL)	N.A.	N.A.	N.A.
44	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	N.A.	N.A.	N.A.
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	N.A.	N.A.	N.A.
46	CALICUT-MANGALORE (DL) (SR)	N.A.	N.A.	N.A.
47	KARUR-SALEM(NL),SR	N.A.	N.A.	N.A.
48	VILLUPURAM-KATPADI (GC)(SR)	N.A.	N.A.	N.A.
49	ANGAMALI-SABARIMALA (N.L.)(SR)	N.A.	N.A.	N.A.
50	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	N.A.	N.A.	N.A.
51	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTHAMPALLI	N.A.	N.A.	N.A.
52	SHIMOGA-TALAGUPPA (SWR), GC	N.A.	02/2011	02/2011
53	BANGLORE - SATYAMANGALAM (NL)(SWR)	N.A.	N.A.	N.A.
54	HUBLI-ANKOLA(NL),SWR	N.A.	N.A.	N.A.
55	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	N.A.	N.A.	N.A.
56	RAMGANJMUUNDI-BHOPAL (NL),WCR	N.A.	N.A.	N.A.
57	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	03/2008	10/2010	N.A.
58	SURENDRANAGAR-BHAVNAGAR(GC),WR	03/2004	03/2010	N.A.
59	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	03/1996	07/2002	N.A.
Shipping & Ports				
60	SETHUSAMUDRAM SHIP CHANNEL PROJECT	10/2008	N.A.	11/2010
61	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2008	N.A.	N.A.
Telecommunications				
62	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	N.A.	03/2011	02/2011
63	GSM equipment of 1900000Lines (2G) 335500lines 3(G)kerala Phase V.1 Telecom Circle	01/2010	N.A.	02/2011
64	Procurement of STM-16 ADM equipment	03/2010	N.A.	12/2010
65	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle	03/2009	N.A.	01/2011
66	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3G) PH-5.1	09/2009	N.A.	02/2010
67	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment	03/2010	N.A.	10/2010
68	GSM equipment of 614000Lines (2G) 150000lines 3(G) Chennai TD Phase V.1 Telecom Circle	01/2010	N.A.	02/2011
69	NIB-II PROJECT RURAL BROADBAND	02/2008	N.A.	12/2010
70	Procurement of 10G (40 chl) DWDM equipment	03/2009	N.A.	N.A.
71	PROJ.III OF NIB-II OF MESSAGING STORAGE	12/2005	N.A.	10/2010
72	Procurement of 10G 40 CHL (12 chl equipped) DWDM equipment (SDCA level)	03/2010	N.A.	12/2010

SN	PROJECTS NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
73	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant	03/2010	N.A.	10/2010
74	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06	10/2007	N.A.	N.A.
75	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1	03/2009	N.A.	02/2011
76	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1	12/2008	N.A.	02/2011
77	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	03/2009	N.A.	02/2011
78	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G)	06/2009	N.A.	02/2011
79	Assam Telecom Circle, Phase-V.I, 2G & 3G	01/2009	N.A.	02/2011
80	Procurement of STM-1 SDH equipment	03/2010	N.A.	12/2010
81	MANAGED LEASED LINE NETWORK PH-VI	N.A.	N.A.	N.A.
82	Procurement of STM-16 MADM equipment	03/2010	N.A.	12/2010
83	Execution of telecom network requirement of defence forces	03/2009	N.A.	N.A.
84	Procurement of 2.5G DWDM equipment	03/2009	N.A.	12/2010
85	GSM equipment of 975000Lines (2G) 325000 lines 3(G) UP East Phase V.1 Telecom Circle	02/2010	N.A.	02/2011
86	GSM equipment of 1500000Lines (2G) 264700lines 3(G)Andhra Pradesh Phase V.1 Telecom Circle	01/2010	N.A.	02/2011
87	Procurement of DXC equipment	03/2010	N.A.	11/2010
88	GSM equipment of 945000Lines (2G) 225000lines 3(G) Bihar Phase V.1 Telecom Circle	10/2008	N.A.	02/2011
89	GSM equipment of 375000Lines (2G) 75000lines 3(G) Kolkatta Phase V.1 Telecom Circle	06/2009	N.A.	01/2011
	Urban Development			
90	C/o office building for IDBI at bandra Kurla Complex,Mumbai	04/2009	N.A.	01/2011

List of Projects where in Revised cost Estimates'(s) is required

SN	PROJ_TITLE	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
cost (Rs. Crore)					
	Atomic Energy				
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	0.00	13561.00
	Civil Aviation				
2	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE ACROSS THE ADYAR AT CHENNAI AIRPORT(k3)	06/2009	213.35	0.00	227.95
3	Extension of Secondary Runway, Construction of Taxi tracks at chennai Airport(K2)	08/2008	230.00	13.00	232.82
	Petroleum				
4	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	09/2006	2305.30	0.00	2416.96
5	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	10/2007	5713.03	0.00	6212.68
	Power				
6	CHAMERA,STAGE-III (NHPC)	08/2005	1405.63	0.00	1554.83
7	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	08/2006	621.28	0.00	622.08
8	KOTESHWAR HEP(THDC)	04/2000	1301.56	0.00	2306.88
9	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC)	08/2006	611.02	0.00	622.61
10	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT (NHPC)	10/2003	768.92	0.00	1273.57
11	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.	04/2008	290.49	0.00	333.30
	Railways				
12	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	09/1996	262.00	456.00	547.31
13	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR	12/2006	170.00	170.00	349.61
14	AMRAVATI-NARKHER NL(CR)	06/1994	120.90	284.27	429.58
15	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	0.00	368.83
16	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	09/2005	200.80	0.00	214.20
17	BILASPUR-URKURA (DL)	04/1997	151.52	0.00	268.07
18	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	0.00	589.87
19	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	07/1998	248.44	576.27	722.07
20	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	09/1996	156.00	0.00	160.50
21	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	02/1999	180.73	0.00	347.43
22	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	09/2006	343.17	0.00	359.30
23	ELECTRIFICATION OF MORADABAD-ROZA	12/2004	129.17	0.00	203.22
24	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	03/1984	520.00	422.79	534.28
25	GADWAL - RAICHUR (NL), SCR	04/1998	92.63	108.91	219.30
26	GONDIA-JABALPUR(GC),(SECR)	02/1997	386.30	0.00	520.42
27	GUNA-ETAWAH(NCR), NL	04/1985	158.77	432.46	512.70
28	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)	04/1992	458.45	0.00	555.49

SN	PROJ_TITLE	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
cost (Rs. Crore)					
29	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	02/1997	295.00	0.00	449.87
30	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	03/2002	409.00	625.30	804.25
31	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	04/1997	233.00	335.77	509.74
32	KANPUR-KASGANJ-MATHURA(GC),NER	03/1997	395.00	1062.36	1117.17
33	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	04/1999	323.40	0.00	374.95
34	KARUR-SALEM(NL),SR	02/1997	155.55	0.00	522.06
35	KATIHAR - JOGBANI (GC)(NEFR)	09/2001	100.00	492.98	707.50
36	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	04/1997	78.23	0.00	86.25
37	KOTTUR-HARIHAR(NL),(SWR)	04/1995	65.94	281.20	323.10
38	LANJHIGARH-JUNAGARH NL(ECOR)	04/1993	100.00	142.90	178.20
39	Lumding-silchar jiribam, badarpur-baraigram kumarghat national project	04/1996	1676.31	0.00	2629.95
40	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	04/1995	184.00	254.07	409.17
41	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	04/1996	114.01	283.95	326.45
42	MUZAFFARPUR-SITAMARHI(NL),ECR	04/1997	100.00	322.29	393.94
43	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	155.74	164.36	401.33
44	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	04/2005	240.00	0.00	275.40
45	PATNA GANGA BRIDGE (NL), ECR	04/2001	624.47	0.00	891.63
46	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	407.78	465.67
47	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	04/2005	148.61	0.00	255.30
48	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	03/1998	280.00	0.00	653.18
49	RAICHUR-GUNTAKAL(DL)(SCR)	04/2003	136.62	0.00	139.10
50	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	09/1997	1000.00	1500.00	2162.02
51	RAJATGARH-BARANG(LD),ECOR	04/1999	166.16	0.00	227.21
52	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	04/1992	112.53	320.66	504.20
53	RANCHI-LOHARDAGA(GC),SER	04/1997	194.07	0.00	264.11
54	REWARI-ROHTAK (NL),NR	01/2004	149.38	330.23	449.82
55	SHIMOGA-TALAGUPPA (SWR), GC	12/1992	46.00	218.00	246.36
56	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canvession (NWR)	04/2007	643.36	0.00	749.10
57	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	0.00	361.97
58	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	0.00	454.48
59	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara and Naopara-NSCB Airport(MTP)	03/2000	907.69	1032.76	2690.75
60	VILLUPURAM-KATPADI (GC)(SR)	02/2000	175.00	0.00	535.83
Road Transport & Highways					
61	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	04/2000	367.49	0.00	453.68
62	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	03/2005	190.00	0.00	227.00

SN	PROJ_TITLE	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
cost (Rs. Crore)					
63	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	12/2003	193.00	0.00	321.11
64	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	12/2003	217.00	0.00	345.41
65	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4	03/2005	565.00	0.00	1035.00
66	DAKOBA TO NAGAON (NH-36)(NHAI)	12/2003	225.00	0.00	238.86
67	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	486.00	0.00	491.96
68	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	12/2003	412.78	0.00	435.53
69	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	12/2003	275.00	0.00	288.00
70	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500	03/2005	579.00	0.00	765.86
71	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	12/2003	600.24	0.00	636.52
72	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	12/2003	227.00	0.00	341.38
73	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	04/2000	273.00	0.00	379.17
74	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	12/2003	210.00	0.00	670.40
75	JHAJHARPUR TO DARBANGA (BR-7)	12/2003	340.00	0.00	410.70
76	JHANSI TO LALITPUR, NH-26	12/2003	276.09	0.00	294.85
77	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70	11/2008	549.00	0.00	792.50
78	KASIA TO GORAKHPUR (NH-28)(NHAI)	12/2003	242.00	0.00	348.34
79	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12/2003	275.00	0.00	275.30
80	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	12/2003	240.00	0.00	240.86
81	KURALI-KIRATPUR, NH-21	03/2005	309.00	0.00	553.56
82	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	12/2003	225.00	0.00	236.43
83	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	03/2005	629.00	0.00	910.04
84	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	03/2005	359.00	0.00	772.84
85	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28	12/2003	239.00	0.00	317.62
86	NAGAON BYPASS (NH-37)(NHAI)	12/2003	230.00	0.00	312.00
87	NAGPUR-KONDHALI,NH-6(NHAI)	03/2005	168.00	0.00	385.27
88	NALBARI TO BIJNI (AS-8)	12/2003	200.00	0.00	244.42
89	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	03/2005	441.00	0.00	785.70
90	NEW MANGALORE PORT NH-17 AND 48	04/2000	196.50	0.00	221.20
91	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	03/2005	557.00	0.00	926.06
92	PONDICHERY - TINDIVANAU NH-66	03/2005	285.00	0.00	355.83

SN	PROJ_TITLE	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
cost (Rs. Crore)					
93	PURNEA-GOYAKOTA SEC.(EW) (NS AND EW-PH-I) KM.419-KM.447, NH-31	04/2000	205.73	0.00	247.70
94	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	05/2009	1108.00	0.00	2137.00
95	RINGBUNDS TO JHAJHANPUR (BR-6)	12/2003	340.00	0.00	534.99
96	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	12/2003	151.30	0.00	158.49
97	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	03/2005	941.00	0.00	1803.00
98	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	12/2003	157.47	0.00	166.90
99	SITAPUR-LUCKNOW	03/2005	322.00	0.00	553.70
100	SONAPUR TO GUWAHTI (AS-3)	12/2003	245.00	0.00	458.58
101	Surat- Dahisar(Six Lane) Km 263 to Km 502	02/2009	1693.75	0.00	2102.00
102	THANJAUR-TRICHY,NH-67(NHAI)	03/2005	280.00	0.00	579.25
103	THRISSUR TO ANGAMALI (NH-47)	12/2003	312.50	0.00	592.10
104	TRICHY - DINDIGUAL NH-45	03/2005	576.00	0.00	613.96
105	TRICHY - KORUR NH-67	03/2005	516.00	0.00	548.66
106	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	12/2003	227.00	0.00	333.08
107	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	02/2008	295.00	0.00	622.81
Shipping & Ports					
108	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARRIERS	08/2008	1108.12	0.00	1238.88
Telecommunications					
109	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	11/2007	277.34	0.00	308.13
Urban Development					
110	DELHI MRTS PHASE-II PROJECT	08/2005	8676.00	8605.36	17467.38

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
