

**319th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
May, 2012**



DMRC Phase -III



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -6
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	7-8
Summary of Projects	9-24
Trend and Graphical Analysis of Mega Projects	25-37
Sector wise analysis of projects	38-38
List of All Ongoing Projects	39-69
Sector wise Graph	70-81
ANNEXURE	82-82
Central Sector Projects	83-83
List of Projects Having Expenditure More than cost	84-87
List of Projects Ahead of Schedule	88-88
List of Projects with out Original date of Commissioning	89-93
List of Projects with out date of Commissioning	94-98
List of On schedule Projects	99-104
List of Delayed Projects w.r.t Original and Revised	105-124
List of Projects without Milestones	125-143
Abbreviations	144-145

EXECUTIVE SUMMARY

The Flash Report for May, 2012 contains information on the status of the 564 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During, May, 2012, 10 projects (3 projects of Shipping & Port, 2 projects each of Road Transport & Highways and Road Transport & Highways and one project each of Fertiliser, Petroleum and Power Sectors) have reported completion.

During the reference month, 76 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 41 months, in respect of projects relating to Road Transport and Highways, Railways, Power, Petroleum, Coal, Shipping & Ports, Steel, and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	129	11
2.	ROAD TRANSPORT & HIGHWAYS	146	34
3.	POWER	100	08
4.	PETROLEUM	65	09
5.	COAL	52	3
6.	TELECOMMUNICATION	15	4
7.	SHIPPING & PORTS	19	4
8.	STEEL	17	3
9.	FERTILISERS	5	0
10.	CIVIL AVIATION	5	0
11.	ATOMIC ENERGY	5	0
12.	URBAN DEVELOPMENT	4	0
13.	WATER RESOURCES	1	0
14.	PETROCHEMICALS	1	0
Total		564	76

3. The total original cost of implementation of the 564 projects was about ₹ 7,32,115.53 Crores and their anticipated completion cost is likely to be ₹ 8, 75,158.5 Crores, which reflects an overall cost overrun of ₹ 1,43,042.97 Crores (19.5 % of original cost). The expenditure incurred on these projects till May, 2012 is ₹ 3,96,282.70 Crores, which is 45.3 % of the anticipated cost of the projects.

4. Out of the 564 projects, 3 projects are ahead of schedule, 133 are on schedule, 251 projects are delayed, and 85 projects have been sanctioned without any commissioning schedule/date. Further, in case of 92 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. Out of 251 delayed projects, 68 projects had overall delay in the range of 1 to 12 months, 44 projects had a delay in the range of 13 to 24 months, 105 projects had a delay in the range of 25 to 60 months and 34 projects had a delay of 61 months and above.

5. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

6. The brief reasons for time overruns as reported by various projects implementing agencies are Court cases, delay in land acquisitions, revision of scope of work, delay in supply of equipment, ROU problem, termination of contracts, geological surprises, frequent strike, fund constraint , delay in equipment erection and forest and environment clearances, etc

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

8. The Sector-wise details of additional delays are as under:-

i) In the **Shipping and Ports sector**, 4 projects have reported additional delays in the range of 3-25 months. The project 'Sethusamudram Ship Channel Project, Port Trust' has reported additional delay of 25 months due to delay in court case, 'Acquisition of Two Nos. of 120 B.P BY 079 & 080, Shipping & Ports', 'Acquisition of 4 No. of Anchor Handling Cum Supply, Shipping & Ports' and 'Acquisition of 4 Nos of 82000 DWT Kamsavmax Bulk Carriers, Shipping & Ports' have reported additional delay of 3, 4 and 5 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

ii) In the **Telecommunications sector**, 4 projects have reported additional delays in the range of 1-11 months. The project 'Project-III of NIB-II of Messaging Storage, BSNL' and 'NIB Project Capacity Expansion, BSNL' have reported additional delay of 1 month each due to delay in supplies and non implementation of DR functionalities. The project 'GSM Equipment of 1625000 Lines (2G) 325000 lines (3G), BSNL' has reported additional delay of 3 months due to delay in permission to lay optical fiber cable from local bodies and 'Convergent Billing And CRM-MTNL (Delhi), MTNL' has reported additional delay of 11 months due to delay by vendor.

iii) In the **Petroleum Sector**, 9 projects have reported additional delays in the range of 1-12 months. The project 'Revamping of Win Platform At MH Asset, ONGC' has reported additional delay of 1 month due to high quoted price of tender, 'Construction of New Process Complex MHN, ONGC' and 'Offshore Grid Interconnectivity project in Mumbai High, ONGC' have reported additional delay of 2 months each due to delay in high quoted price leading to cancellation of tender and termination of contract respectively, 'Polypropylene unit Mangalore Refinery' has reported additional delays of 3 months due to delay in non availability of land, 'Upgradation of Konaban GGS and Pipeline Grid Project, ONGC' has reported additional delay of 4 months due to ROU issues, 'Development of G-1 and GS-15, ONGC' has reported additional delay of 6 months due to termination of contract and court proceeding, 'Construction of 12 Offshore Supply Vessels (OSV), ONGC' has reported additional delay of 8 months due to delay in preparation of drawing & procurement of steel by PSL and shortage of skilled manpower, 'Assam Renewal Project for Group-A, ONGC' has reported additional delay of 12

months due to Court cases and ROU issues etc. 'Construction of 6 ETPs, ONGC has reported additional delay of 3 months. However, no specific reason has been reported by the project authorities for delay in this project.

iv) In the **Power Sector**, 8 projects have reported additional delays in the range of 5-41 months. The project 'Barh STTP, Stage-II, NTPC' has reported additional delay of 5 months due to delay in supply of equipment by BHEL, 'Bongaigaon Thermal Power Project, NTPC' has reported additional delay of 7 months due to delay in TG erection start, 'Koldam HEP, NTPC' and 'Subansiri Lower H.E.P (NHPC), NHPC' have reported additional delay of 12 months each due to geological occurrences and frequent strikes respectively, 'PARBATI HEP II, NHPC' has reported additional delay of 41 months due to contract terminated & retendering is in progress, 'Barh STPP, Stage-I, NTPC' and 'Tapovan Visnugad HEP, NTPC' have reported additional delay of 15 months each due to quality increased in TG area civil works and contract terminated due to non performance of the agency respectively and 'Tuirial Hydro Electric Project (60MW), NEEPCO' has reported additional delay of 13 months. However, no specific reasons has been reported by the project authorities for delay in this project.

v) In **Steel sector**, 3 projects have reported additional delays in the range of 2-3 months. The project 'Augmentation of Iron Ore Storage in RMHP, RINL' has reported additional delay of 2 months due to delay in deviations in techno-commercial issues, '67.5 MW TG-5 System Emergency Power Requirement, RINL' and 330 TPH Boiler-6 and Auxiliary System, RINL' have reported additional delay of 3 months each due to delay in supply of equipment and delay in erection activities respectively

vi) In the **Road Transport and Highways Sector**, 34 projects of NHAI have reported additional delays in the range of 1-31 months. Two projects have reported additional delays of one month each, four projects have reported additional delay of 2 months each, three projects have reported additional delay of 3 months each, two projects have reported additional delay of 4 months each, three projects have reported additional delay of 5 months each, eight projects have reported additional delay of 6 months each and nine projects have reported additional delay of 9 months each. The project 'Sonapur to Guwahti (AS-3), NHAI', 'Deewapur To UP/Bihar Border (LMNHP-9)-NH-28, KM.402-360.915, NHAI' and 'NH Connectivity to ICTT Vallarpadaeu NH – SH, NHAI' have

reported additional delay of 10, 15 and 31 respectively. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

vii) In the **Coal Sector**, 3 projects have been reported additional delays in the range of 2-24 months. The project 'Kakatiya Laongwall, SCCL' has reported additional delay of 2 months due to delay in selection of technology provider cum operator (TPO), 'Churcha Roug (1.35MTY), SECL' has reported additional delay of 24 months due to delay in forest clearance and 'Jagannathpur OCP (3.00 MTY), SECL' has reported additional delay of 24 months due to delay in start of project.

viii) In the **Railways Sector**, 11 projects have been reported additional delays in the range of 1-24 months. One project has additional delay of 1 month and two projects have additional delay of 3 months each. The project 'Kadur-Chikmagalur-Sakleshpur (NL), SWR' and 'Ahmednagar-Parli Vaijnath (NL), CR' have reported additional delay of 7 and 9 months respectively, 'Mansi-Purnia (Extension Of Mansi-Saharsa) GAN, ECR' and 'Bhairabi Sairong, NL, NEFR' have reported additional delay of 12 months each, 'Ramanagram-Mysore doubling with Electrification of SWR, SWR' has reported additional delay of 24 months. The project authority has reported reason of delay as fund constrains for these projects. The project 'Extention. of MRTS from Velachery to Station Thomas, MTP, MRTP', 'Mumbai Urban Transport Project Phase-I, MRTP' and 'Mumbai Urban Transport Project Phase-II, MRTP' have reported additional delay of 9, 9 and 12 months respectively. However, no specific reasons have been reported by the project authorities for delay in this project.

9. The status as on 01.06.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.

(Pankaj Jain)
Special Secretary
Min. of Statistics and Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	146	34
2	Railways	129	11
3	Power	100	8
4	Petroleum	65	9
5	Coal	52	3
6	Shipping & Ports	19	4
7	Steel	17	3
8	Telecommunications	15	4
9	Atomic Energy	5	0
10	Civil Aviation	5	0
11	Fertilisers	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	564	76

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2,635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.10
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.10
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	.00
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1,284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.80
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1,596.80
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.60
	<u>Railways</u>			
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
	<u>Road Transport & Highways</u>			
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
	<u>Shipping & Ports</u>			
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61


Summary of projects in the Flash Report for the month of May, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	579
Number of Projects completed/dropped/frozen in Previous Month	8
Number of Projects completed/dropped/frozen in Current Month	10
Number of Projects Added in Current Month	3
Number of Projects in Current Month	564


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 564 projects, 3 projects are ahead of schedule, 133 projects are on schedule and 251 projects are delayed. Of the balance, 92 projects do not have fixed dates of commissioning while 85 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

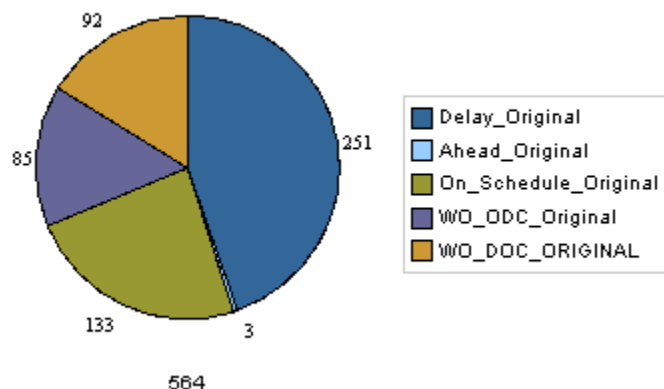

III. Investment Scenario

The Total Original cost of implementation of 564 projects when sanctioned, was of the order of Rs. 732115.53 crore but this was subsequently revised to Rs. 875158.5 crore implying a cost overrun of 19.5%. The expenditure incurred on these projects till May, 2012 is Rs. 396282.7 crore, which is 45.3% of the revised cost of the projects.

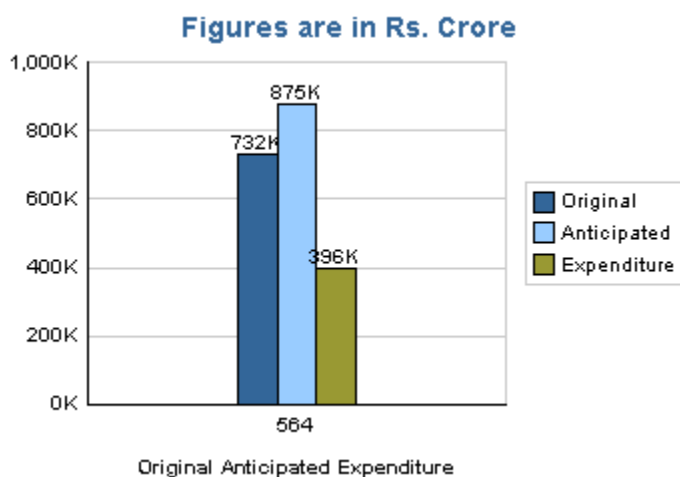

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	579
No of Projects Completed/Dropped/Frozen in Previous Month	8
No of Projects Completed/Dropped/Frozen in Current Month	10
No of Projects added in Current Month	3
No of Projects in Current Month	564

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original (Date)	251	3	133	85	92	564	44.50
Latest Approved (Date)	245	2	194	92	31	564	43.44

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	444	596,028.22	673,186.01	272,580.01	40.50	77,157.79	12.90
Latest Approved (RCE)	120	190,036.75	201,972.49	123,702.69	61.20	11,935.74	6.30
Total (RCE)	564	786,064.97	875,158.50	396,282.70	45.28	89093.53	11.33
Original Cost of All Projects							
Original Cost	564	732,115.53	875,158.50	396,282.70	45.30	143,042.97	19.50

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	251	346,419.79	426,380.29	242,545.06	56.90	79,960.50	23.10
Latest Approved (RCE)	245	330,078.27	385,037.39	215,491.66	56.00	54,959.12	16.70

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	76	81,281.02	101,851.95	70,978.19	69.70	20,570.93	25.30

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	52	33,950.7	37,570.7	10.7	13	12,914.8	17,132.5	32.7
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	50,343.2	71,589.7	42.2	8	32,529.9	53,806.4	65.4
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	65	156,993.5	166,236.2	5.9	15	51,117.7	67,759.0	32.6
8	Power	100	210,306.6	223,892.5	6.5	17	40,561.3	54,148.1	33.5
9	Railways	129	64,854.8	142,224.6	119.3	107	42,240.8	119,657.2	183.3
10	Road Transport & Highways	146	91,616.1	93,334.4	1.9	12	3,520.8	5,808.2	65.0
11	Shipping & Ports	19	16,242.5	17,757.5	9.3	10	8,732.5	10,579.5	21.2
12	Telecommunications	15	6,161.0	6,101.8	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		564	732,115.5	875,158.5	19.5	192	225,609.8	377,710.4	67.4

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	14	12,420.0	20,714.4	66.8
2	Arunachal Pr.	4	9,512.2	14,152.7	48.8	2	6,441.3	11,082.7	72.1
3	Assam	36	22,463.9	33,865.5	50.8	12	10,491.8	21,987.5	109.6
4	Bihar	32	30,891.8	35,951.1	16.4	13	12,338.8	17,398.2	41.0
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	23	31,308.5	31,536.5	0.7	4	2,019.6	2,481.1	22.8
7	Haryana	9	5,306.6	7,177.2	35.2	3	1,448.2	3,318.8	129.2
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	3	7,629.8	10,324.0	35.3
9	J and K	11	15,120.1	34,413.1	127.6	6	7,866.5	27,186.4	245.6
10	Karnataka	23	29,468.6	37,913.5	28.7	10	8,795.3	17,646.7	100.6
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	25	16,968.5	17,262.9	1.7	3	2,027.6	2,741.5	35.2
13	Maharashtra	50	78,266.3	93,478.4	19.4	18	31,818.4	49,505.1	55.6
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	30	57,405.4	61,206.4	6.6	13	33,147.5	37,140.9	12.0
19	Punjab	6	4,384.2	5,326.0	21.5	2	532.4	1,474.2	176.9
20	Rajasthan	15	26,688.0	26,417.9	-1.0	4	1,224.0	1,624.4	32.7
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	60,135.0	17.3	13	27,364.2	36,223.3	32.4
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	24	18,548.9	22,386.7	20.7	8	3,498.5	7,384.5	111.1
25	West Bengal	25	40,187.8	52,298.3	30.1	16	23,547.4	35,657.9	51.4
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	27	41,193.2	56,813.2	37.9	11	10,542.6	26,162.6	148.2
28	Jharkhandd	23	11,785.5	16,601.5	40.9	7	5,213.3	10,201.2	95.7
29	Uttaranchal	4	8,514.3	9,454.7	11.0	2	2,640.7	3,581.2	35.6
30	Multi State	103	136,199.0	142,534.7	4.7	20	6,385.4	16,153.4	153.0
Total		564	732,115.5	875,158.5	19.5	192	225,609.8	377,710.4	67.4

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	3	36,950.0	39,603.0	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	3	2,587.6	2,970.1	3 - 27
3	Coal	52	33,950.7	37,570.7	10.7	26	17,944.1	21,061.7	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	1	438.0	438.0	12 - 12
5	Steel	17	50,343.2	71,589.7	42.2	8	13,253.2	17,337.0	2 - 36
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	65	156,993.5	166,236.2	5.9	41	111,428.5	121,252.7	1 - 120
8	Power	100	210,306.6	223,892.5	6.5	28	86,681.8	99,654.1	5 - 99
9	Railways	129	64,854.8	142,224.6	119.3	36	25,088.9	62,483.1	1 - 216
10	Road Transport & Highways	146	91,616.1	93,334.4	1.9	84	33,500.5	35,578.8	1 - 101
11	Shipping & Ports	19	16,242.5	17,757.5	9.3	10	8,446.1	10,038.7	5 - 93
12	Telecommunications	15	6,161.0	6,101.8	-1.0	9	3,163.3	3,167.1	19 - 78
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		564	732,115.5	875,158.5	19.5	251	346,419.8	426,380.3	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	11	15,386.5	18,889.0	1 - 36
2	Arunachal Pr.	4	9,512.2	14,152.7	48.8	3	9,356.2	13,737.0	25 - 75
3	Assam	36	22,463.9	33,865.5	50.8	31	11,648.4	19,405.4	12 - 120
4	Bihar	32	30,891.8	35,951.1	16.4	15	17,116.8	20,595.3	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	3 - 3
6	Gujarat	23	31,308.5	31,536.5	0.7	6	13,912.3	14,143.8	3 - 24
7	Haryana	9	5,306.6	7,177.2	35.2	4	2,065.9	3,555.1	9 - 50
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	6	14,761.2	17,455.4	20 - 99
9	J and K	11	15,120.1	34,413.1	127.6	8	9,873.4	29,166.4	10 - 201
10	Karnataka	23	29,468.6	37,913.5	28.7	9	22,364.3	27,444.8	3 - 96
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,674.0	5,324.0	8 - 58
12	Madhya pradesh	25	16,968.5	17,262.9	1.7	16	13,123.5	12,718.0	5 - 50
13	Maharashtra	50	78,266.3	93,478.4	19.4	25	49,644.1	59,732.9	2 - 52
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	11 - 13
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	30	57,405.4	61,206.4	6.6	9	31,475.9	32,310.2	7 - 101
19	Punjab	6	4,384.2	5,326.0	21.5	4	1,611.4	2,553.2	1 - 51
20	Rajasthan	15	26,688.0	26,417.9	-1.0	6	19,992.2	19,687.9	3 - 47
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	32	51,276.0	60,135.0	17.3	9	22,842.4	26,947.2	9 - 93
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	4 - 4
24	Uttar Pradesh	24	18,548.9	22,386.7	20.7	13	11,442.4	13,375.4	5 - 91
25	West Bengal	25	40,187.8	52,298.3	30.1	14	12,683.9	17,348.3	3 - 132
26	Delhi	3	37,985.0	37,965.4	-0.1	1	249.0	229.4	72 - 72
27	Chhatisgarh	27	41,193.2	56,813.2	37.9	10	13,192.7	15,310.2	10 - 48
28	Jharkhandd	23	11,785.5	16,601.5	40.9	8	2,258.6	2,702.4	24 - 102
29	Uttaranchal	4	8,514.3	9,454.7	11.0	4	8,514.3	9,454.7	13 - 36
30	Multi State	103	136,199.0	142,534.7	4.7	30	35,036.9	35,610.1	1 - 216
Total		564	732,115.5	875,158.5	19.5	251	346,419.8	426,380.3	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	5	41,548.3	46,386.3	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	2,278.1	2,660.6	3 - 17
3	Coal	52	33,950.7	37,570.7	10.7	24	15,846.0	19,383.0	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	2	763.0	763.0	9 - 12
5	Steel	17	50,343.2	71,589.7	42.2	7	4,561.2	5,046.0	2 - 24
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	65	156,993.5	166,236.2	5.9	34	96,779.8	103,411.3	1 - 80
8	Power	100	210,306.6	223,892.5	6.5	27	80,311.3	91,961.6	0 - 99
9	Railways	129	64,854.8	142,224.6	119.3	39	17,125.4	55,226.7	0 - 216
10	Road Transport & Highways	146	91,616.1	93,334.4	1.9	84	33,500.5	35,578.8	1 - 101
11	Shipping & Ports	19	16,242.5	17,757.5	9.3	7	6,079.2	7,120.2	22 - 93
12	Telecommunications	15	6,161.0	6,101.8	-1.0	12	4,700.0	4,703.8	7 - 78
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		564	732,115.5	875,158.5	19.5	245	310,430.5	385,037.4	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	52	35,153.3	37,570.7	6.9	10	10,201.9	12,619.3	23.7
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	56,218.4	71,589.7	27.3	5	9,099.0	24,500.3	169.3
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	65	170,795.5	166,236.2	-2.7	2	30,533.0	31,324.0	2.6
8	Power	100	213,645.0	223,892.5	4.8	13	35,648.2	45,896.7	28.7
9	Railways	129	89,328.7	142,224.6	59.2	81	39,431.1	92,535.8	134.7
10	Road Transport & Highways	146	91,782.6	93,334.4	1.7	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	17,604.0	17,757.5	0.9	7	4,306.6	4,770.0	10.8
12	Telecommunications	15	6,164.9	6,101.8	-1.0	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		564	786,065.0	875,158.5	11.3	134	158,087.4	253,713.2	60.5

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,808.00	2,015.00	13- 13
3	Coal	52	33,950.69	37,570.71	10.66	1	469.78	706.40	44- 44
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	50,343.15	71,589.69	42.20	2	8,987.89	12,898.17	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	65	156,993.49	166,236.24	5.89	13	21,195.88	36,044.22	6- 120
8	Power	100	210,306.58	223,892.50	6.46	2	2,253.45	3,986.02	24- 67
9	Railways	129	64,854.78	142,224.55	119.30	15	8,021.50	21,092.01	1- 141
10	Road Transport & Highways	146	91,616.10	93,334.43	1.88	0	0.00	0.00	0- 0
11	Shipping & Ports	19	16,242.52	17,757.49	9.33	4	4,635.42	5,427.89	5- 22
12	Telecommunications	15	6,161.00	6,101.79	-0.96	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		564	732115.53	875158.5	19.54	38	47371.92	82169.71	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	1	13,171.00	15,824.00	51- 51
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,942.51	2,325.00	17- 17
3	Coal	52	33,950.69	37,570.71	10.66	8	10,739.18	14,454.50	12- 48
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	50,343.15	71,589.69	42.20	4	9,477.89	13,591.75	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	65	156,993.49	166,236.24	5.89	12	49,312.67	64,735.01	7- 120
8	Power	100	210,306.58	223,892.50	6.46	14	39,246.47	52,219.61	7- 99
9	Railways	129	64,854.78	142,224.55	119.30	27	12,903.17	50,302.30	1- 216
10	Road Transport & Highways	146	91,616.10	93,334.43	1.88	12	3,520.78	5,808.20	18- 99
11	Shipping & Ports	19	16,242.52	17,757.49	9.33	7	7,365.57	8,958.14	5- 93
12	Telecommunications	15	6,161.00	6,101.79	-0.96	2	1,065.85	1,089.32	19- 36
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	15- 15
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		564	732115.53	875158.5	19.54	90	155682.99	242103.83	

V. List of projects completed/dropped/Frozen current month

(All Cost
/Expenditure in
Rs. crore)

S.no	Project	DOA	Original		Now anticipated		Final
			Cost	DOC	Cost	DOC	Expenditure
<u>Fertilisers</u>							
1	THAL AMMONIA REVAMP PROJECT	01/2009	488.75	04/2012	488.75	04/2012	307.89
<u>Petroleum</u>							
2	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON	06/2006	1,431.91	09/2009	1,690.13	08/2011	1,596.80
<u>Power</u>							
3	MAUDA TRANSMISSION SYSTEM	02/2010	469.38	10/2012	469.38	05/2012	224.60
<u>Railways</u>							
4	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)	04/2003	230.73	03/2009	399.47	05/2012	328.83
5	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	09/2005	200.80	N.A.	333.79	05/2012	323.35
<u>Road Transport & Highways</u>							
6	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	04/2000	273.00	03/2005	522.00	05/2012	475.55
7	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI	03/2005	441.00	N.A.	441.00	05/2012	958.09
<u>Shipping & Ports</u>							
8	DEVELOPMENT OF COAL TERMINAL	09/2006	399.13	08/2010	399.13	05/2012	351.08
9	DEVELOPMENT OF IRON ORE TERMINAL	09/2006	370.00	08/2010	370.00	05/2012	351.61
10	MARINE LIQUID TERMINALS	10/2004	196.25	06/2006	196.25	05/2012	250.77

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	<u>Petroleum</u>					
1	Development of Western Periphery of MH South Field	4/2012	600.17	12/2014	600.17	12/2014
2	Pipeline Replacement Project-3	4/2012	2,547.26	5/2014	2,547.26	5/2014
	<u>Steel</u>					
3	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P	12/2011	187.33	10/2013	187.33	12/2013

VII. Milestones (Cumulative due & achieved)

Total	3321
Achieved up to month	1124

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
<u>Coal</u>							
1	KAKATIYA LAONGWALL SCCL	453.63	453.63	12/2012	01/2015	03/2015	2
2	CHURCHA ROUG (1.35MTY) SECL	462.35	462.35	03/2014	03/2014	03/2016	24
3	JAGANNATHPUR OCP(3.00 MTY) SECL	152.43	152.43	03/2015	03/2015	03/2017	24
<u>Steel</u>							
4	Augmentation of Iron Ore Storage in RMHP RINL	480.00	450.00	05/2012	12/2012	02/2013	2
5	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2011	06/2012	09/2012	3
6	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	05/2012	08/2012	3
<u>Petroleum</u>							
7	REVAMPING OF WIN PLATFORM AT MH ASSET ONGC	333.40	656.51	05/2010	05/2012	06/2012	1
8	CONSTRUCTION OF NEW PROCESS COMPLEX MHN ONGC	2,853.29	6,326.40	05/2010	05/2012	07/2012	2
9	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2013	05/2013	2
10	Polypropylene unit Mangalore Refin	1,803.78	1,803.78	07/2012	07/2012	10/2012	3
11	Construction of 6 ETPs ONGC	302.26	302.26	09/2012	09/2012	12/2012	3
12	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	288.04	08/2012	08/2012	12/2012	4
13	DEV OF G1 AND GS-15 (ONGCL) ONGC	429.82	2,735.65	04/2006	06/2012	12/2012	6
14	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2012	08/2013	8
15	ASSAM RENEWAL PROJECT FOR GROUP A ONGC	2,465.15	2,378.86	03/2013	03/2013	03/2014	12
<u>Power</u>							
16	BARH STPP STAGE -II NTPC	7,341.04	7,341.04	N.A.	01/2014	06/2014	5
17	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	N.A.	04/2014	11/2014	7
18	KOLDAM HEP (NTPC) NTPC	4,527.15	4,527.15	04/2009	03/2013	03/2014	12
19	SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	10,667.00	09/2010	12/2015	12/2016	12
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) NEEPCO	913.63	913.63	01/2014	01/2014	02/2015	13
21	BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	12/2014	03/2016	15
22	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	03/2013	06/2014	09/2015	15
23	PARBATI HEP (NHPC) II NHPC	3,919.59	5,524.00	09/2009	07/2014	12/2017	41
<u>Railways</u>							

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
24	CHANDIGARH-LUDHIANA(NEW BG LINE),NR (NR)	248.44	1,115.21	12/2012	12/2012	01/2013	1
25	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR ECR	233.00	1,043.60	03/2012	03/2012	06/2012	3
26	KOSI BRIDGE (NL), ECR ECR	323.41	341.41	03/2012	12/2012	03/2013	3
27	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) SWR	157.00	262.82	03/2012	03/2012	10/2012	7
28	AHMEDNAGAR-PARLI VAIJNATH(NL) CR CR	353.08	2,200.00	N.A.	06/2012	03/2013	9
29	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP MRTP	495.74	495.74	06/2013	06/2013	03/2014	9
30	MUMBAI URBAN TRANSPORT PROJECT PHASE-I MRTP	3,125.20	4,501.80	06/2011	06/2011	03/2012	9
31	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR ECR	114.01	477.88	03/2012	03/2012	03/2013	12
32	MUMBAI URBAN TRANSPORT PROJECT PHASE-II MRTP	5,300.00	5,300.00	03/2014	03/2015	03/2016	12
33	BHAIRABI SAIRONG, NL, NEFR NEFR	619.34	2,393.48	04/2014	03/2014	03/2015	12
34	Ramanagram-Mysore doubling with electrification of SWR	482.00	482.70	03/2013	03/2013	03/2015	24
<u>Road Transport & Highways</u>							
35	Hyderabad-yadgiri N.H no-202 NHAI	388.00	388.00	05/2012	05/2012	06/2012	1
36	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	06/2012	07/2012	1
37	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	06/2012	08/2012	2
38	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	06/2012	08/2012	2
39	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 NHAI	193.09	166.30	03/2008	05/2012	07/2012	2
40	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) NHAI	1,108.00	2,288.00	11/2011	06/2013	08/2013	2
41	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 NHAI	275.00	275.00	09/2007	06/2012	09/2012	3
42	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	06/2012	09/2012	3
43	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) NHAI	151.30	151.30	10/2008	05/2012	08/2012	3
44	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) NHAI	367.49	367.49	03/2005	06/2012	10/2012	4
45	Kishangarh-Ajmer-Beawer NHAI	795.00	795.00	05/2012	05/2012	09/2012	4
46	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) NHAI	940.00	940.00	07/2012	07/2012	12/2012	5
47	Pune-sholapur, pkg1 NHAI	1,110.00	1,110.00	05/2012	05/2012	10/2012	5
48	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION NHAI	617.00	617.00	08/2012	10/2013	03/2014	5
49	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	06/2012	12/2012	6
50	DAKOPA TO NAGAON (NH-36)(NHAI) NHAI	225.00	225.00	06/2008	06/2012	12/2012	6


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
51	JHAJHARPUR TO DARBANGA (BR-7) NHAI	340.00	340.00	09/2008	06/2012	12/2012	6
52	NALBARI TO BIJNI (AS-8) NHAI	200.00	200.00	06/2008	06/2012	12/2012	6
53	NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	363.00	06/2011	06/2012	12/2012	6
54	NAGPUR-KONDHALI,NH-6(NHAI) NHAI	168.00	168.00	12/2008	06/2012	12/2012	6
55	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER NHAI	464.00	464.00	01/2011	06/2012	12/2012	6
56	MP/Maharashtra Border-Dhula NHAI	835.00	835.00	06/2012	06/2012	12/2012	6
57	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 NHAI	157.47	154.57	09/2007	06/2012	03/2013	9
58	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHAI	155.00	201.66	09/2008	06/2012	03/2013	9
59	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 NHAI	240.00	240.00	10/2008	06/2012	03/2013	9
60	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) NHAI	195.00	195.00	06/2008	06/2012	03/2013	9
61	NAGAON TO DHARAMTUL (AS-2) NHAI	264.72	264.72	06/2008	06/2012	03/2013	9
62	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	06/2012	03/2013	9
63	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	06/2012	03/2013	9
64	DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	06/2012	03/2013	9
65	SALEM - U / UNDRUPET(BOT -1/TN-06) NH - 68 NHAI	941.00	941.00	01/2011	05/2012	02/2013	9
66	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	05/2012	03/2013	10
67	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 NHAI	300.00	300.00	10/2008	12/2012	03/2014	15
68	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH NHAI	557.00	557.00	02/2010	05/2012	12/2014	31
Shipping & Ports							
69	Acquisition of two nos. of 120 B.P BY 079& 080 SHIPP.	290.85	305.00	06/2011	06/2012	09/2012	3
70	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY SHIPP.	359.44	359.44	04/2011	06/2012	10/2012	4
71	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers SHIPP.	612.72	627.64	12/2012	12/2012	05/2013	5
72	SETHUSAMUDRAM SHIP CHANNEL PROJECT PORT TRUST	2,427.40	2,427.40	10/2008	10/2008	11/2010	25
Telecommunications							
73	PROJ.III OF NIB-II OF MESSAGING STORAGE BSNL	250.00	250.00	12/2005	05/2012	06/2012	1
74	NIB Project Capacity Expansion BSNL	175.52	175.52	12/2008	05/2012	06/2012	1
75	GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	930.60	11/2010	03/2012	06/2012	3
76	CONVERGENT BILLING AND CRM-MTNL(DELHI) MTNL	249.00	229.41	02/2007	03/2012	02/2013	11


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
76							

Trend and Graphical Analysis of All Projects

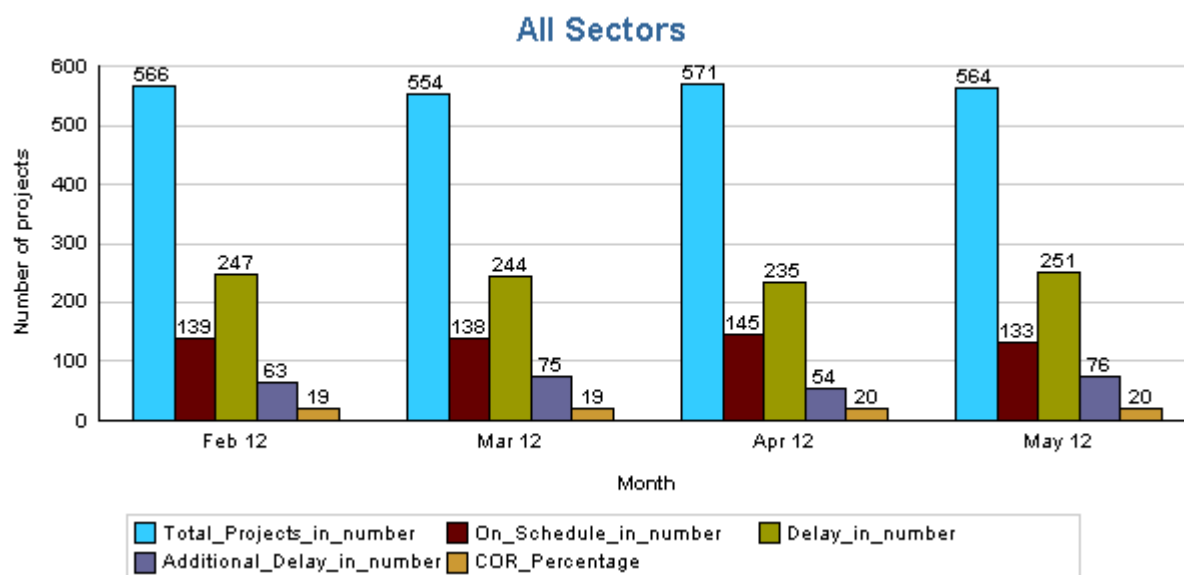


All Sectors Break-up of 251 Delayed projects in May 2012

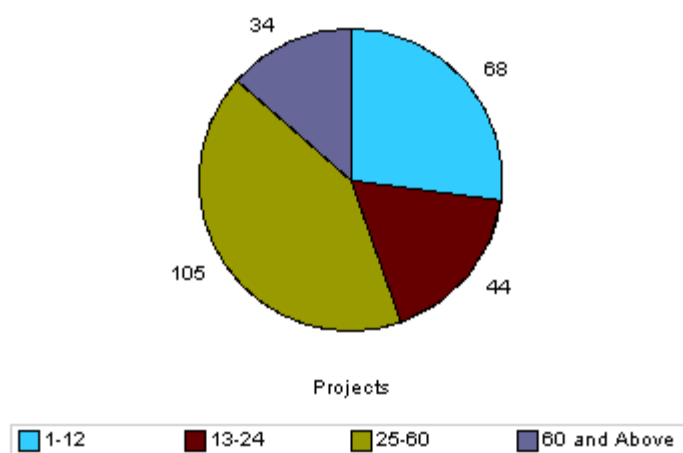


Trend and Graphical Analysis


Urban Development Sector

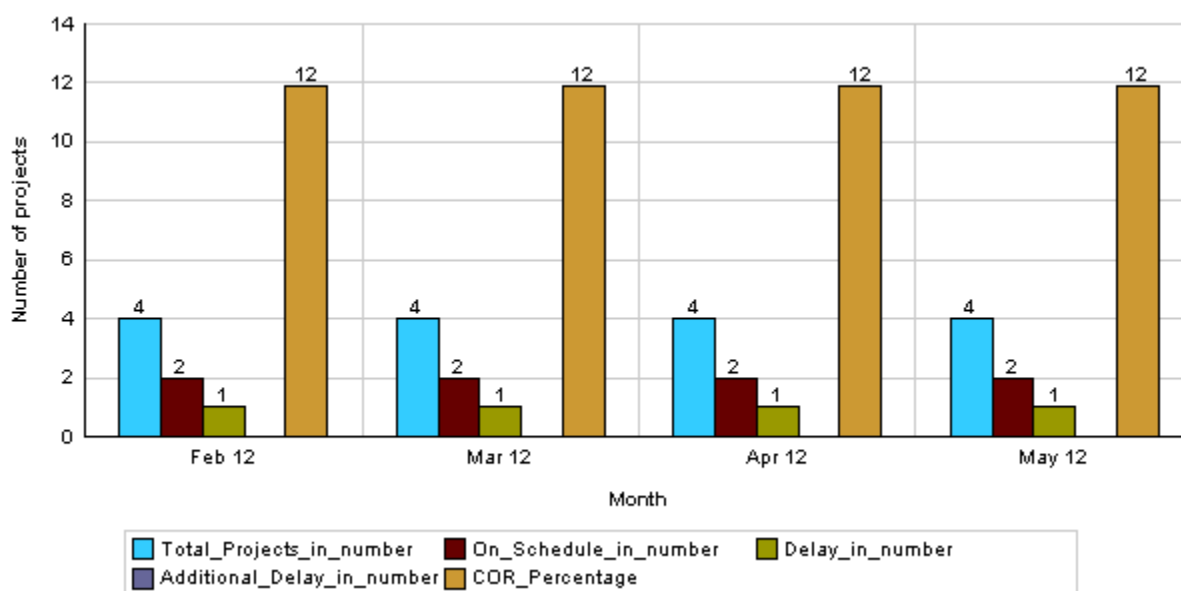


Urban Development Sector Sector Break-up of 1 Delayed projects in May 2012

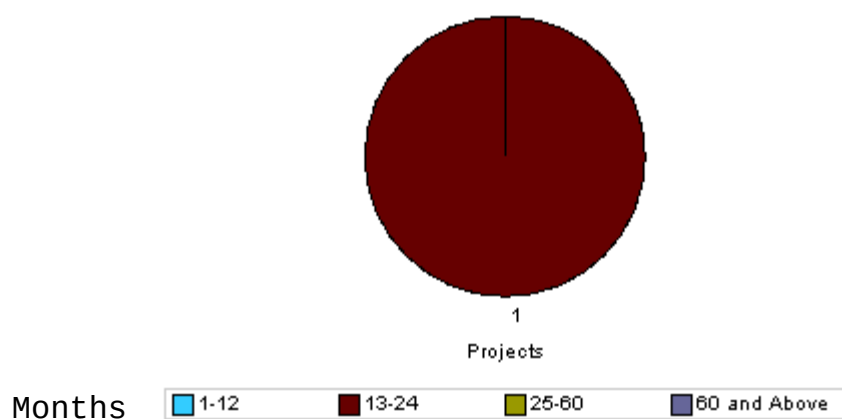


Trend and Graphical Analysis Telecommunications Sector

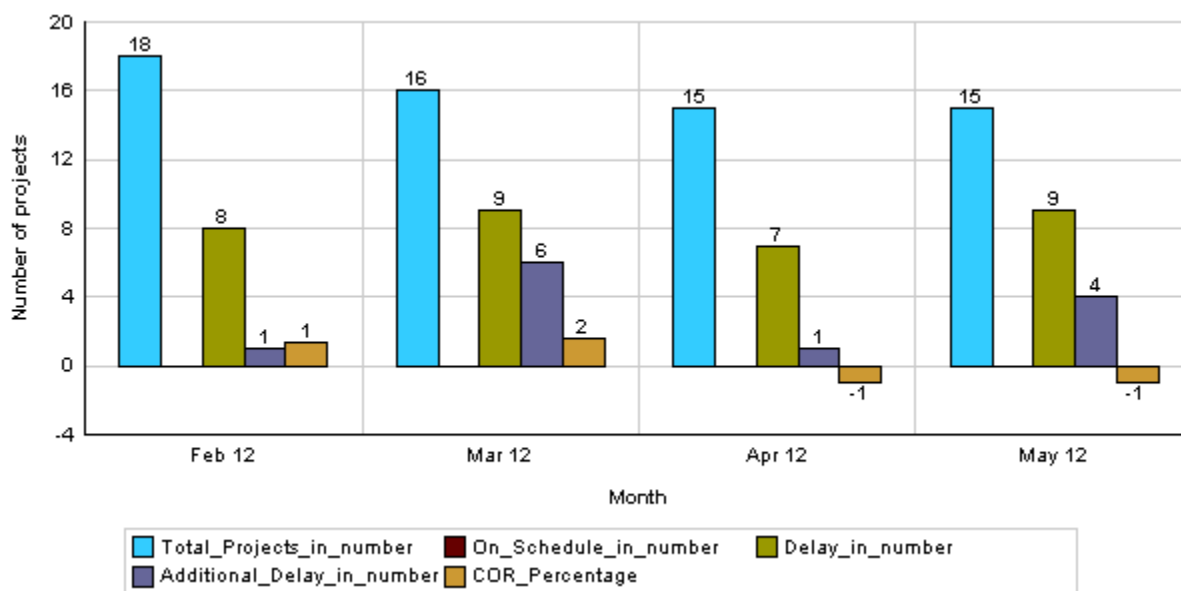


Telecommunications Sector Sector Break-up of 9 Delayed projects in May 2012

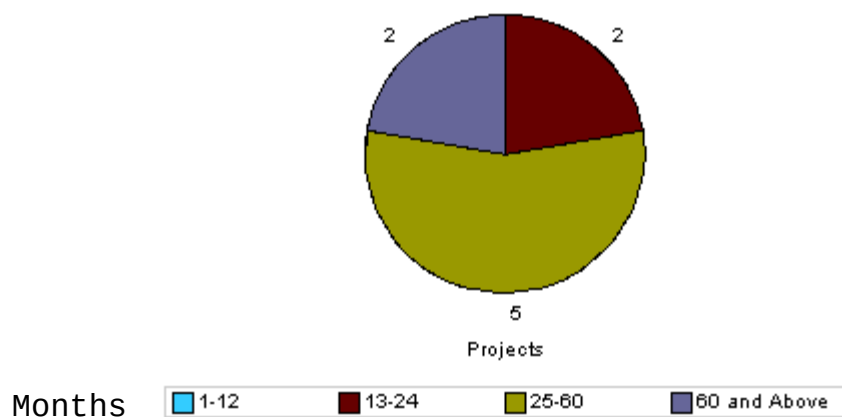

Trend and Graphical Analysis Shipping and Ports Sector

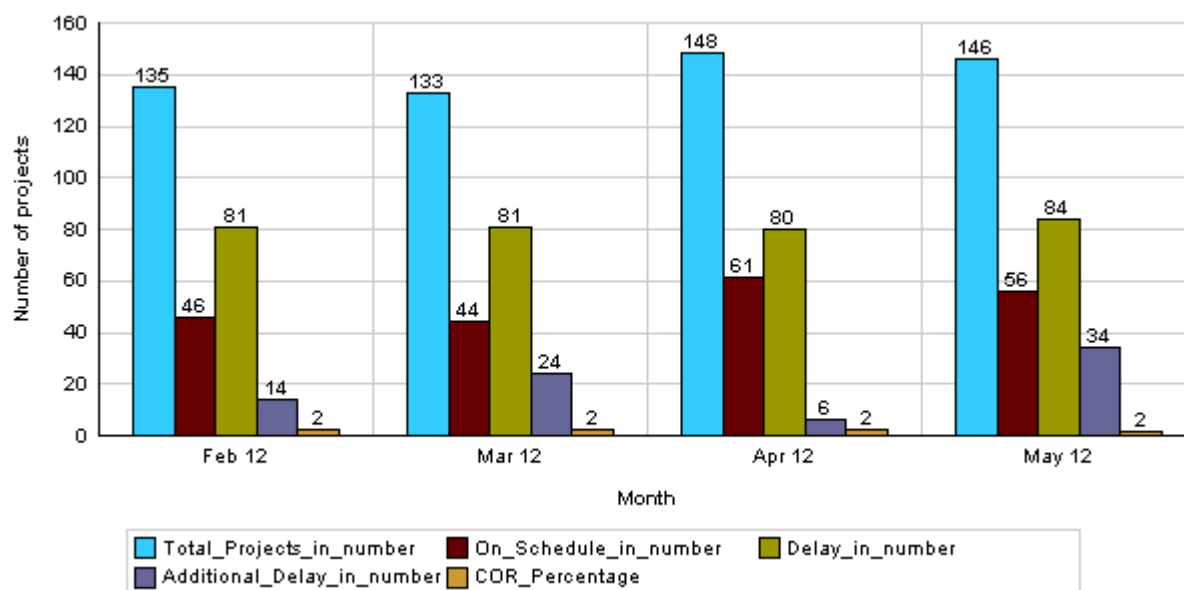


Sector Break-up of 84 Delayed projects in May 2012

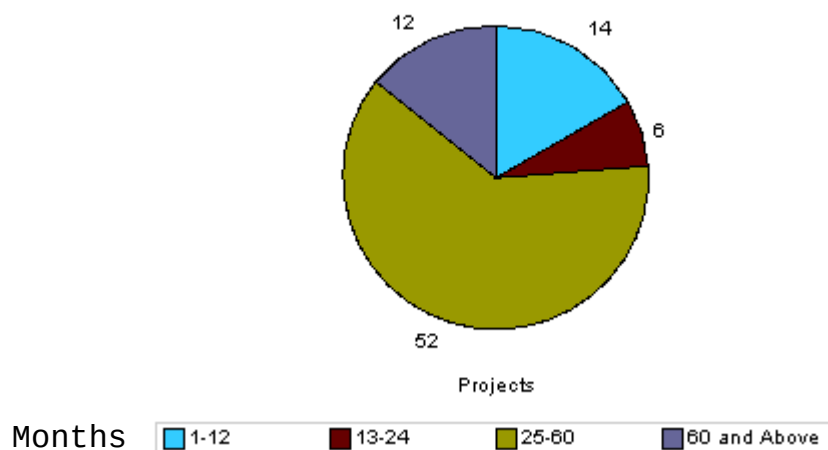


Trend and Graphical Analysis

Road Transport and Highways Sector

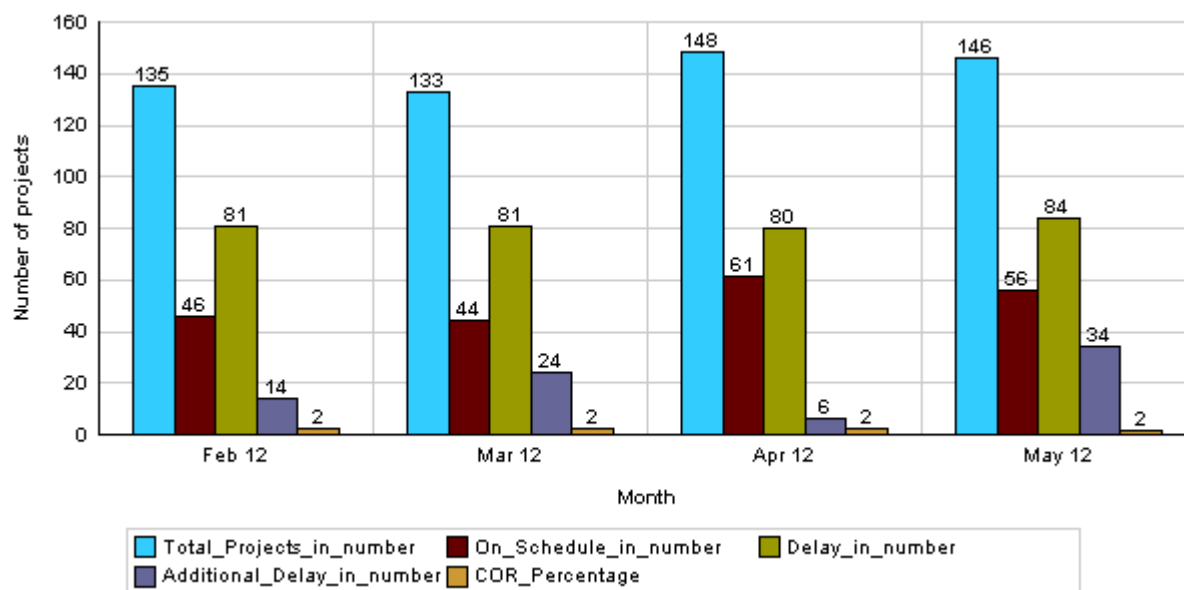


Sector Break-up of 84 Delayed projects in May 2012

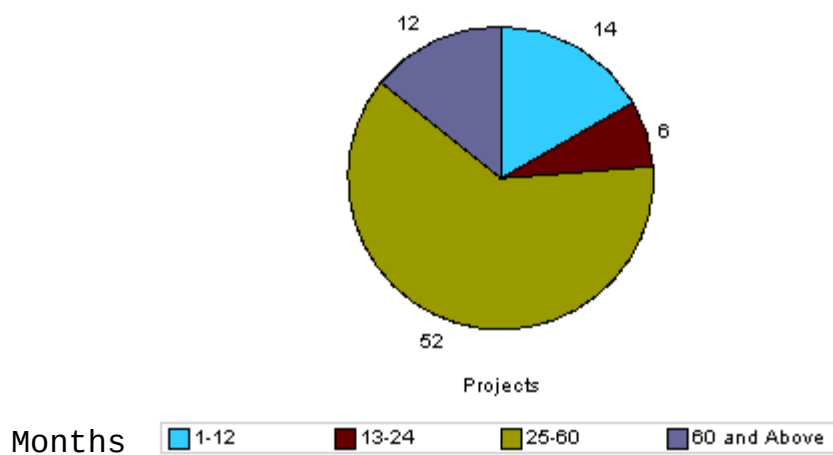


Trend and Graphical Analysis

Railways Sector

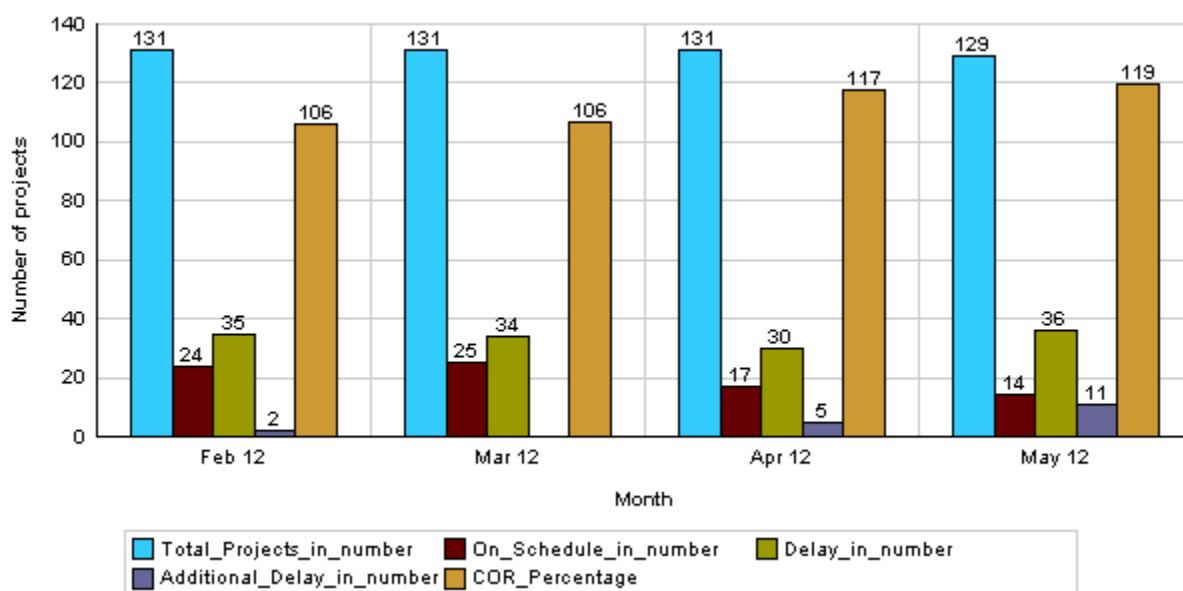


Railways Sector Sector Break-up of 36 Delayed projects in May 2012

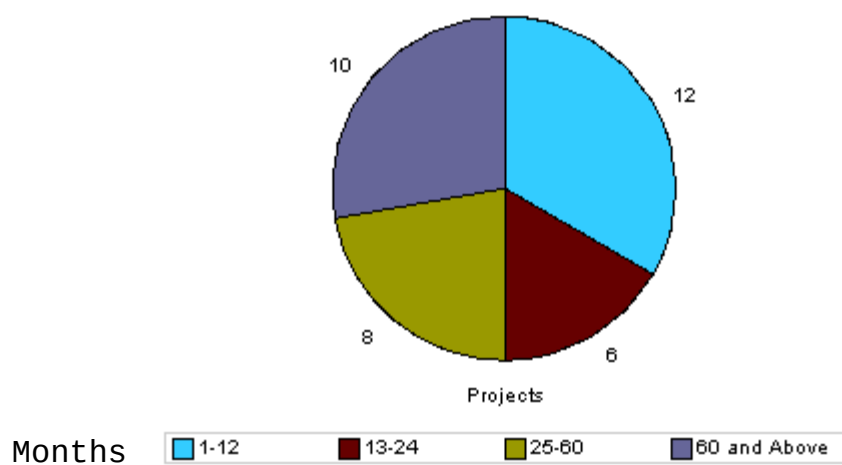


Trend and Graphical Analysis

Power Sector

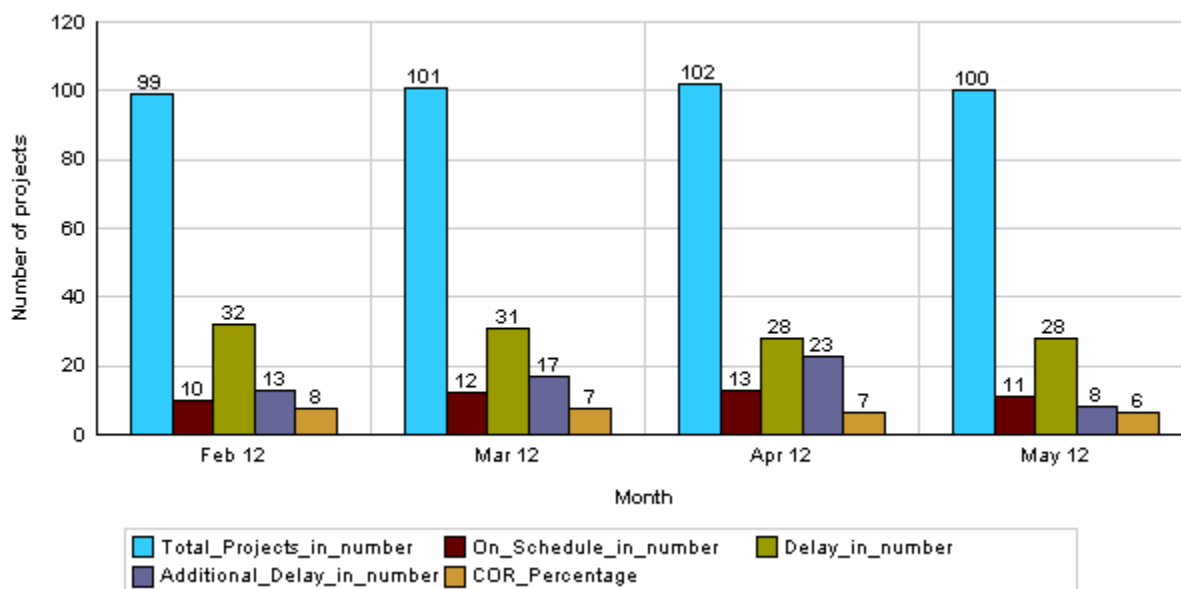


Power Sector Sector Break-up of 28 Delayed projects in May 2012

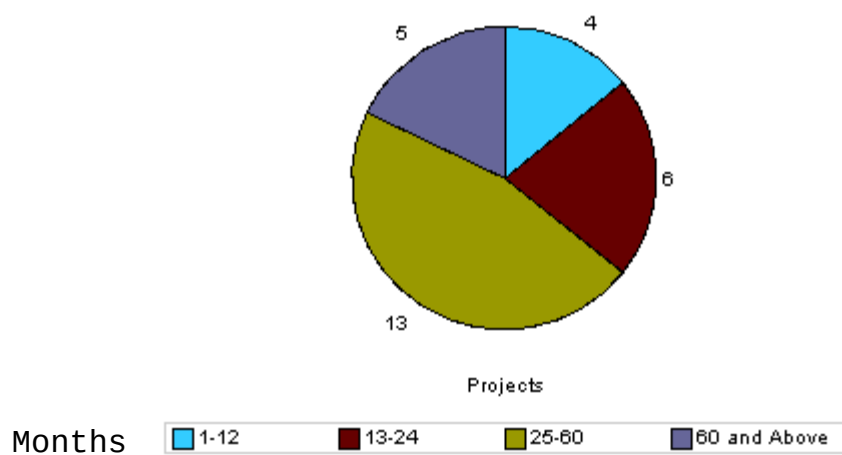


Trend and Graphical Analysis

Petroleum Sector

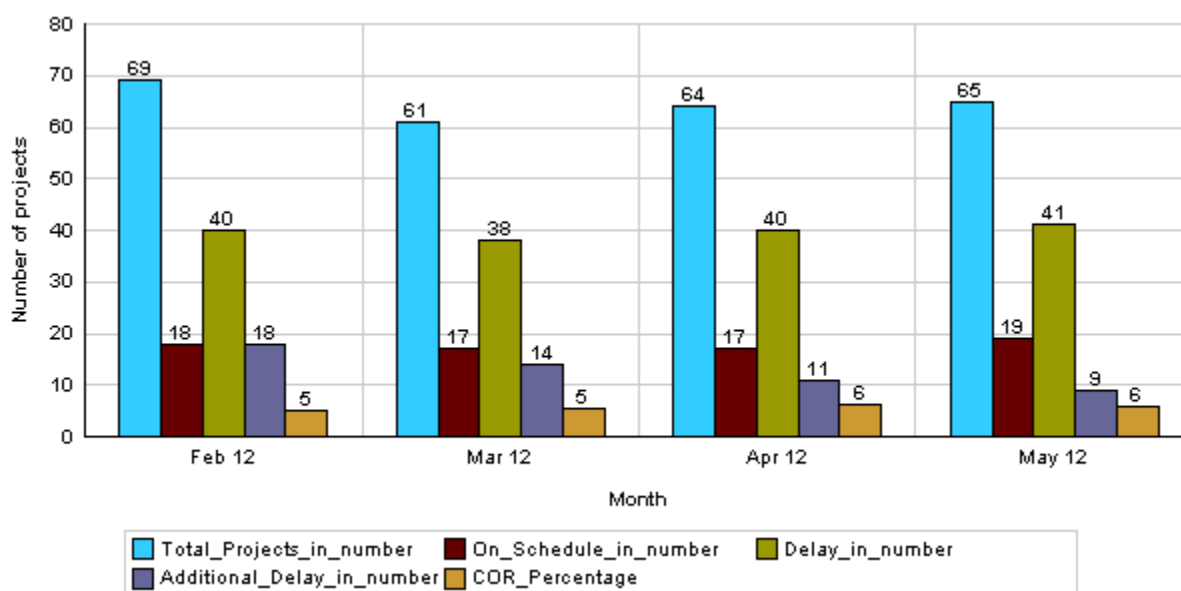


Petroleum Sector Sector Break-up of 41 Delayed projects in May 2012

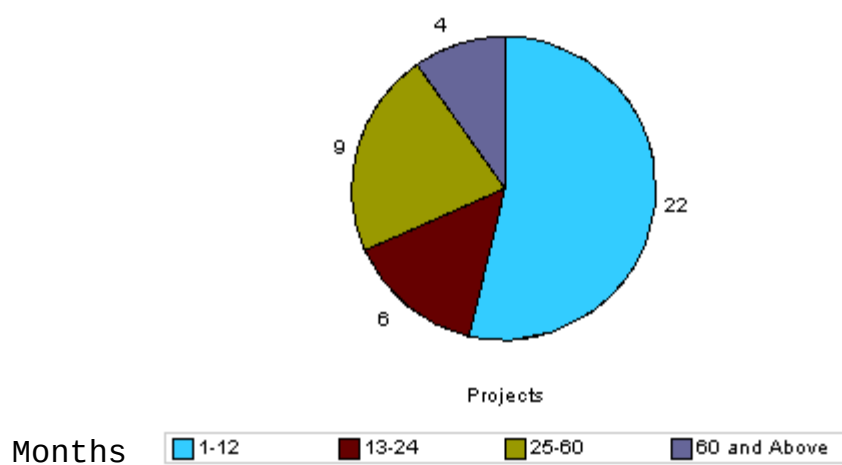


Trend and Graphical Analysis

Steel Sector

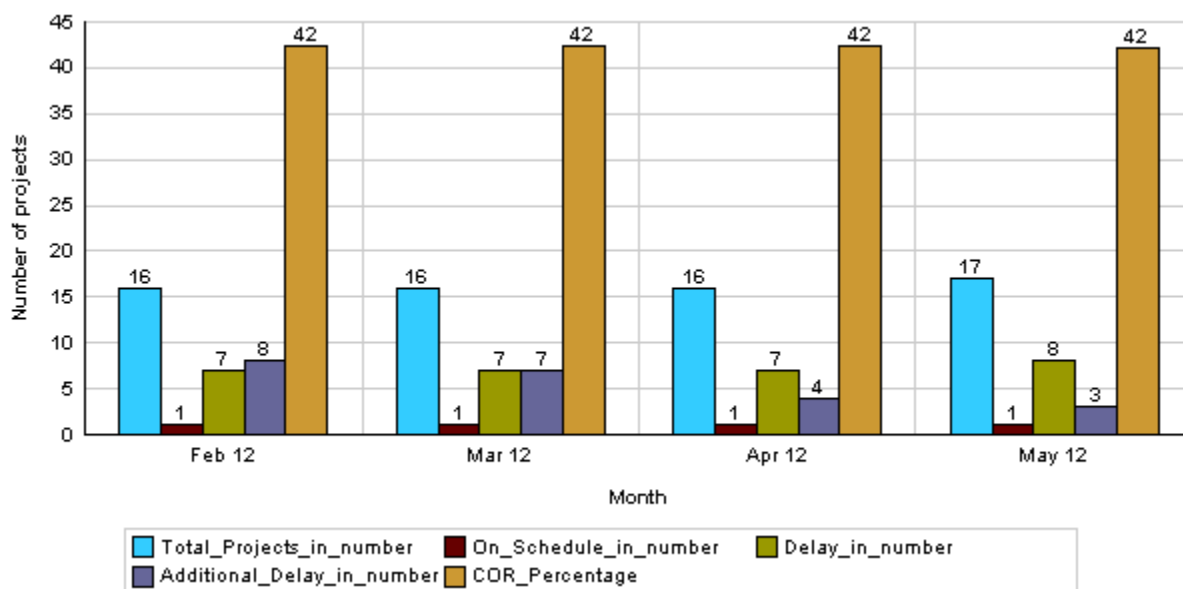


Steel Sector Break-up of 8 Delayed projects in May 2012

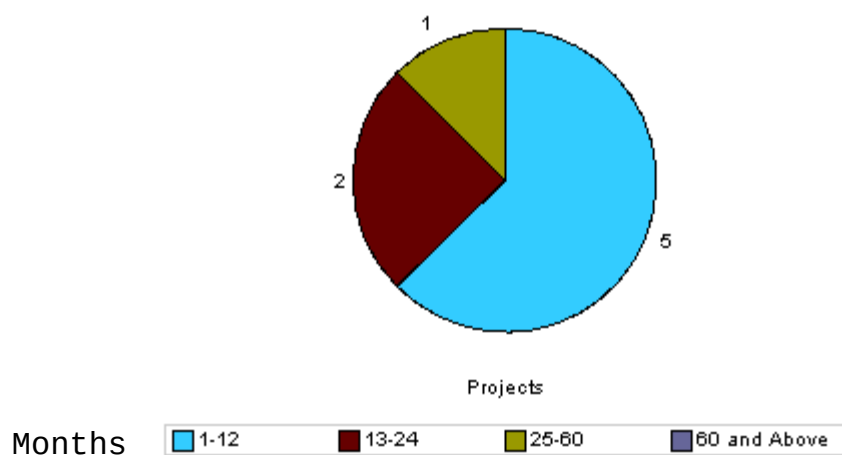


Trend and Graphical Analysis

Fertilisers Sector

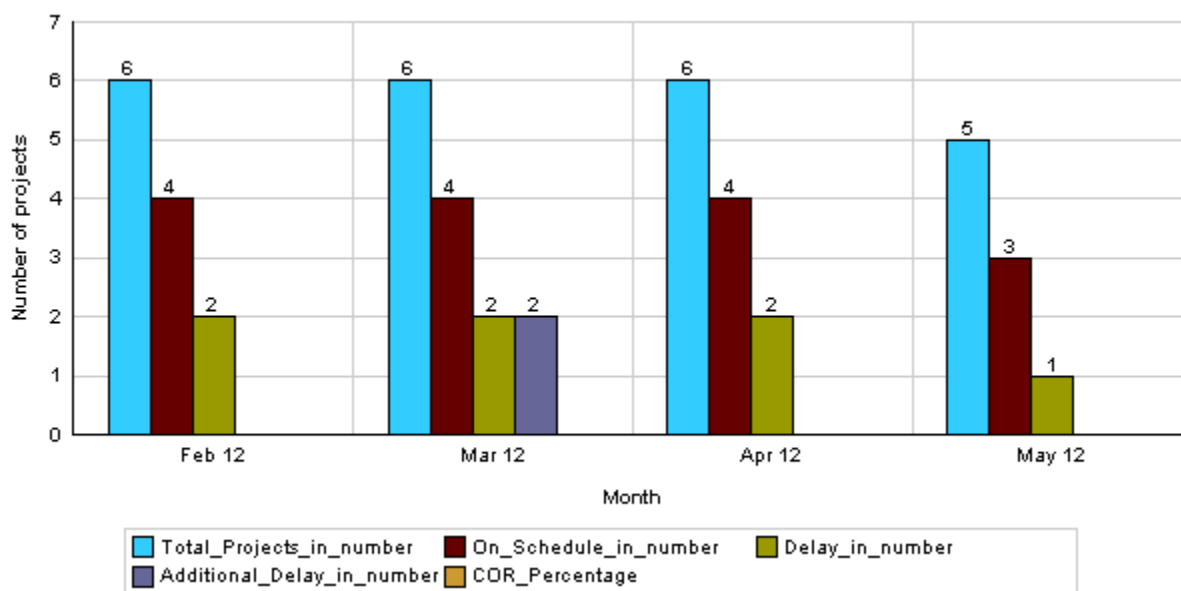


Fertilisers Sector Break-up of 1 Delayed projects in May 2012

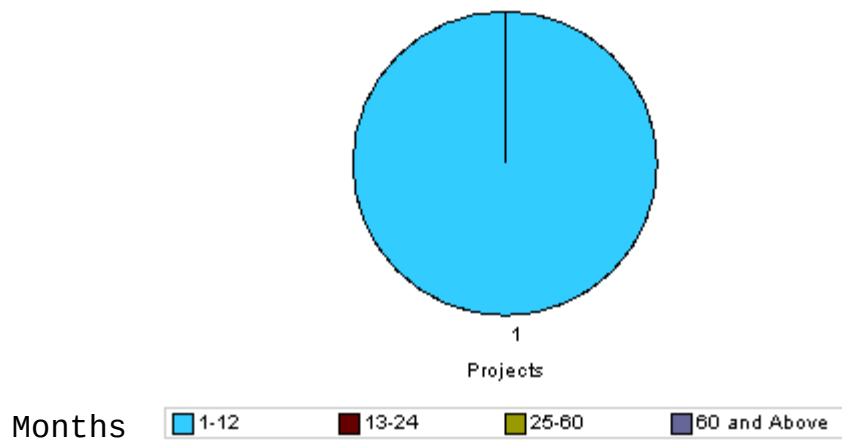


Trend and Graphical Analysis

Coal Sector

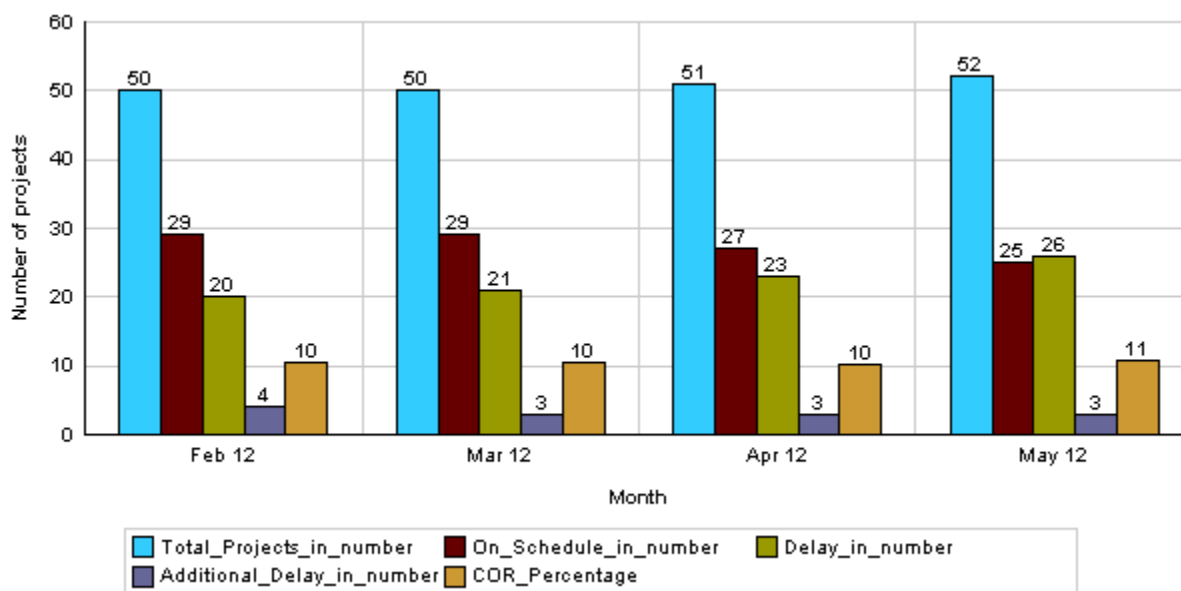


Coal Sector Sector Break-up of 26 Delayed projects in May 2012

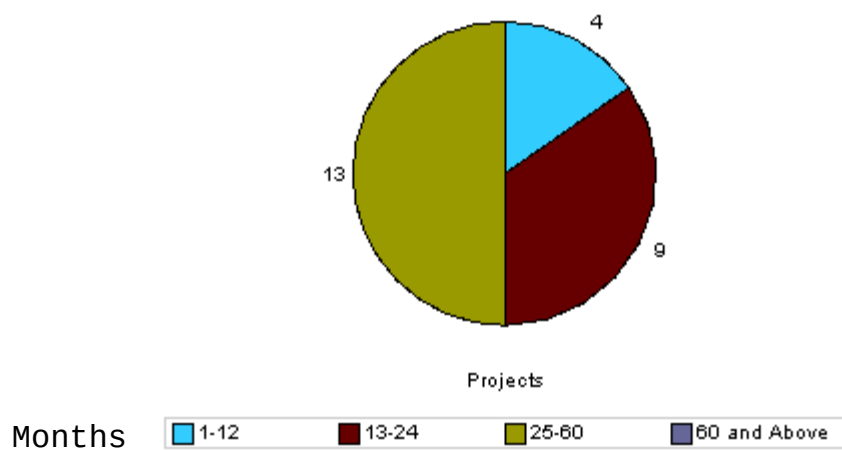


Trend and Graphical Analysis

Civil Aviation Sector

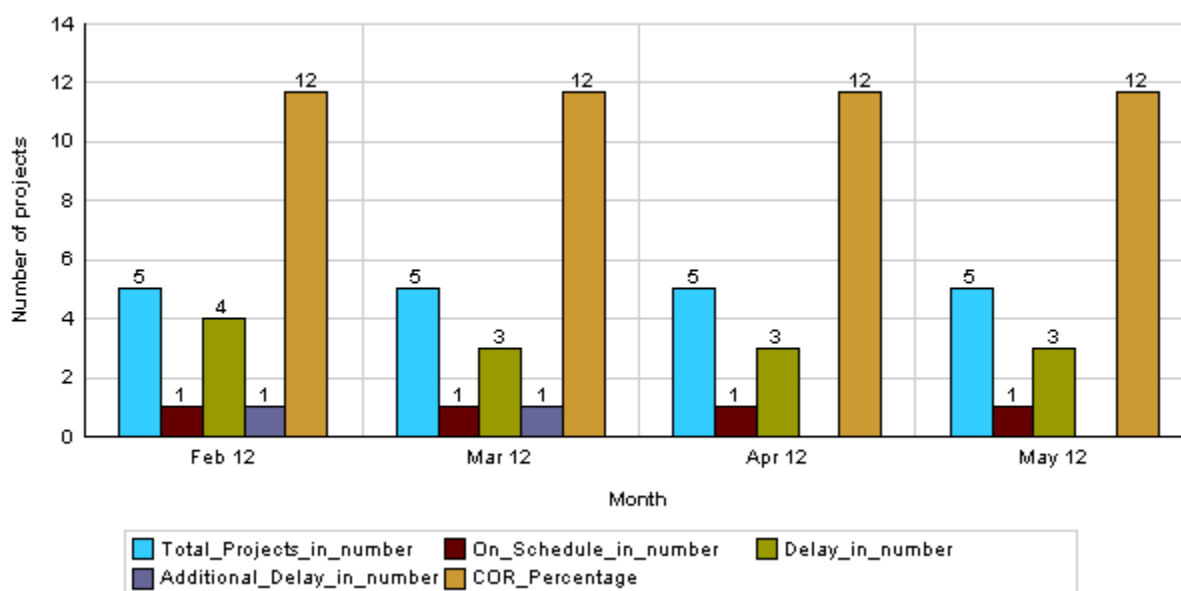


Civil Aviation Sector Sector Break-up of 3 Delayed projects in May 2012

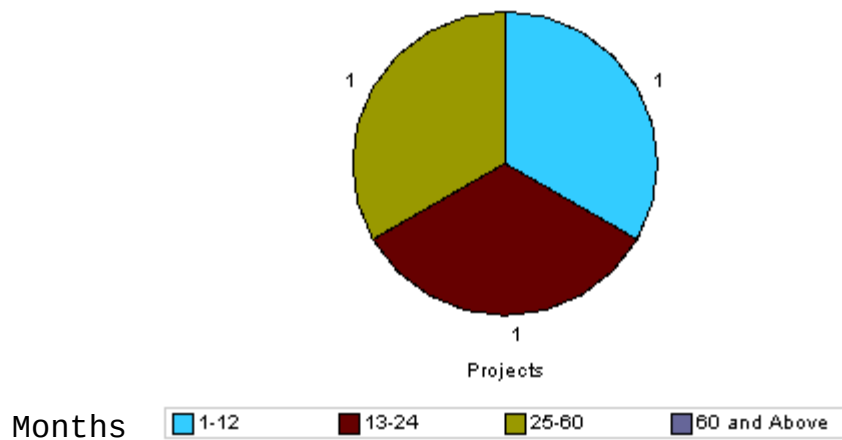


Trend and Graphical Analysis

Atomic Energy Sector

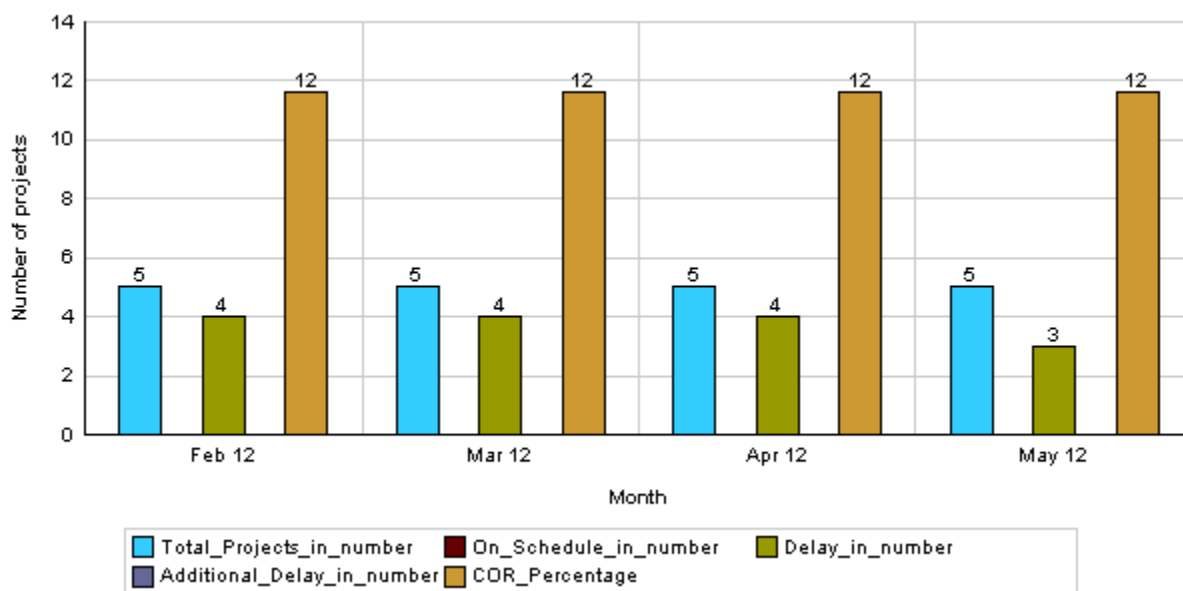

Atomic Energy Sector Sector Break-up of 3 Delayed projects in May 2012

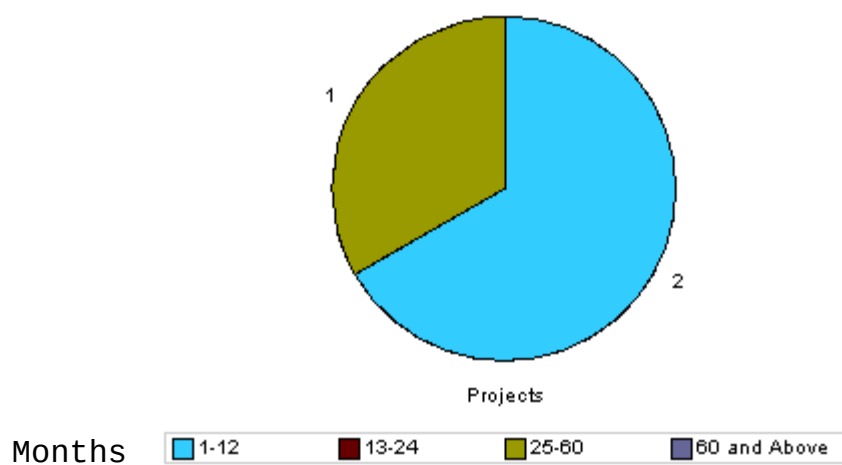

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	46,386.29	22,212.84
Civil Aviation	5	5,021.58	5,228.58	5,611.07	4,298.52
Coal	52	33,950.69	35,153.31	37,570.71	11,975.21
Fertilisers	5	4,828.66	4,828.66	4,828.66	2,265.48
Steel	17	50,343.15	56,218.43	71,589.69	40,797.20
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,657.21
Petroleum	65	156,993.49	170,795.51	166,236.24	71,570.25
Power	100	210,306.58	213,644.95	223,892.50	107,720.47
Railways	129	64,854.78	89,328.74	142,224.55	60,751.33
Road Transport & Highways	146	91,616.10	91,782.60	93,334.43	58,472.90
Shipping & Ports	19	16,242.52	17,604.04	17,757.49	7,189.62
Telecommunications	15	6,161.00	6,164.88	6,101.79	1,774.29
Urban Development	4	44,245.18	44,304.08	49,518.08	2,561.89
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	564	732,115.53	786,064.97	875,158.50	396,282.70

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,714.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,755.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,641.60	09/2010	01/2012	16(O)	6/80
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,018.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011	04/2012	12(O) 12(R)	0/0
Total			41,548.29	46,386.29	22,212.84				45/325
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,966.18	05/2011 03/2012	10/2012	17(O) 7(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	182.98	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	111.25	05/2012	08/2012	3(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,688.78	01/2011 02/2012	02/2012	13(O) 0(R)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	349.33	06/2013	06/2013	0(O)	0/0
Total			5,021.58	5,611.07	4,298.52				0/0
<u>Coal</u>									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	281.16	03/2013 09/2012	10/2014	19(O) 25(R)	7/22
12	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59	198.59	70.00	03/2016	03/2016	0(O)	0/6
13	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	328.96	03/2014 03/2016	03/2016	24(O) 0(R)	2/2

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	100.06	03/2012	03/2014	24(O)	5/7
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66	341.63	108.58	03/2011	03/2013	24(O)	0/2
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	101.88	03/2010	03/2015	60(O)	4/4
17	BAROUD OC EXPANSION - [N06000065]SECL,Chhatisgarh	07/2008	135.58	258.56	38.92	03/2015	03/2016	12(O)	0/0
18	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	258.56	32.29	03/2016	03/2016	0(O)	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	109.50	03/2017	03/2017	0(O)	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.35	03/2014	03/2014	0(O)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	161.80	03/2012	03/2015	36(O)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	260.92	03/2014	03/2016	24(O)	0/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	34.45	03/2011	03/2014	36(O)	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	1,163.51	03/2010	03/2014	48(O)	0/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,365.35	03/2010	03/2014	48(O)	0/15
27	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	59.64	03/2015	03/2015	0(O)	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.53	96.69	03/2013	03/2013	0(O)	5/7
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24(O)	0/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015	03/2015	0(O)	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013	03/2013	0(O)	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	0/1
33	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	72.38	12/2012	03/2015	27(O)	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	119.28	03/2013	03/2013	0(O)	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	30.89	03/2014	03/2014	0(O)	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/6

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	331.78	03/2010 -	03/2013	36(O) -	2/2
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	92.54	03/2010 -	03/2014	48(O) -	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	639.75	03/2013 03/2013	03/2013	0(O) 0(R)	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	19.23	07/2012 03/2014	03/2016	44(O) 24(R)	1/2
43	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	321.50	203.46	03/2014 03/2014	03/2014	0(O) 0(R)	0/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	36.96	03/2012 -	03/2013	12(O) -	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	18.39	12/2015 -	12/2015	0(O) -	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36(O) -	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	60.66	03/2012 03/2012	03/2014	24(O) 24(R)	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	0/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2015	12(O) -	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	86.80	03/2013 -	03/2013	0(O) -	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	23.72	03/2011 -	03/2014	36(O) -	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	89.45	03/2012 -	03/2013	12(O) -	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.49	03/2015 -	03/2015	0(O) -	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	22.74	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	266.79	03/2016 -	03/2016	0(O) -	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	45.80	03/2012 -	03/2012	0(O) -	11/42

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	46.63	03/2016	03/2016	0(O)	1/12
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,412.12	06/2009	03/2013	45(O)	19/24
61	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	2,883.23	03/2012	03/2014	24(O)	0/39
62	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	101.73	03/2012 03/2013	03/2014	24(O) 12(R)	0/2
	Total		33,950.69	37,570.71	11,975.21				141/634
	Fertilisers								
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	589.51	01/2013	01/2013	0(O)	0/5
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	239.87	07/2011	07/2012	12(O)	0/0
65	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	185.10	07/2011	04/2012	9(O)	0/0
66	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	637.00	01/2013 01/2013	01/2013	0(O) 0(R)	8/8
67	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	614.00	01/2013	01/2013	0(O)	0/5
	Total		4,828.66	4,828.66	2,265.48				8/18
	Steel								
68	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	-	-	04/2013	-	0/19
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	242.28	08/2010 08/2010	08/2012	24(O) 24(R)	0/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	247.41	02/2011 02/2011	09/2012	19(O) 19(R)	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	-	-	05/2013	-	0/21
72	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93	232.93	191.83	05/2011	05/2012	12(O)	1/1
73	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	196.32	05/2012 05/2012	02/2013	9(O) 9(R)	1/2
74	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	330.20	12/2011 03/2012	10/2012	10(O) 7(R)	16/21

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N1200038]RINL,Andhra Pradesh	08/2007	108.00	216.68	89.82	10/2012 10/2012	10/2012	0(O) 0(R)	3/4
76	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N1200075]SAIL,Orissa	11/2011	254.55	254.55	6.12	- -	11/2013	- -	0/1
77	EXPANSION OF BHILAI STEEL PLANT - [N1200057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	5,634.23	- -	09/2013	- -	18/27
78	EXPANSION OF BOKARO STEEL PLANT - [N1200055]SAIL,Jharkhand	01/2008	3,316.00	6,325.00	2,716.78	- -	10/2012	- -	10/16
79	EXPANSION OF DURGAPUR STEEL PLANT - [N1200074]SAIL,West Bengal	06/2009	2,875.00	2,875.00	866.76	12/2012	03/2013	3(O)	6/12
80	EXPANSION OF IISCO STEEL PLANT - [N1200051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,293.51	- -	12/2012	- -	13/19
81	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,545.71	10/2009 10/2012	10/2012	36(O) 0(R)	59/64
82	EXPANSION OF ROURKELA STEEL PLANT - [N1200056]SAIL,Orissa	09/2008	11,812.00 11,812.00	11,812.00	7,081.02	11/2013 -	03/2013	-8(O) -	6/14
83	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N1200076]SAIL,Maharashtra	12/2011	187.33	187.33	-	10/2013 -	12/2013	2(O) -	0/0
84	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N1200033]SAIL,Jharkhand	10/2007	500.90	500.90	355.21	- -	02/2012	- -	3/3
Total			50,343.15	71,589.69	40,797.20				138/228
<u>Petrochemicals</u>									
85	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,657.21	12/2013 12/2013	12/2013	0(O) 0(R)	10/30
Total			5,460.61	8,920.00	4,657.21				10/30
<u>Petroleum</u>									
86	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	820.00	-	06/2012 -	04/2013	10(O) -	0/0
87	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	2,163.64	1,017.31	06/2012 -	12/2012	6(O) -	0/0
88	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	211.24	04/2011 -	07/2012	15(O) -	0/0
89	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	977.00	327.30	12/2011 -	01/2013	13(O) -	0/0
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	761.10	03/2013 -	03/2014	12(O) -	0/0
91	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	5.57	12/2014 -	12/2014	0(O) -	0/0
92	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	4.84	12/2014 -	12/2014	0(O) -	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	231.69	07/2012 07/2012	03/2013	8(O) 8(R)	0/16
94	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	66.44	02/2013 -	02/2013	0(O) -	34/42
95	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	132.00	- -	09/2012	- -	25/36
96	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	714.11	04/2011 12/2011	09/2012	17(O) 9(R)	2/2
97	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	08/2013	23(O) -	0/0
98	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,467.35	05/2010 05/2012	07/2012	26(O) 2(R)	0/0
99	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	328.43	02/2011 08/2011	08/2011	6(O) 0(R)	0/0
100	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	0.20	01/2014 -	01/2014	0(O) -	0/0
101	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	5.73	05/2013 -	05/2013	0(O) -	0/0
102	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5(O) -	0/0
103	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	19.21	09/2012 -	12/2012	3(O) -	0/0
104	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
105	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	196.35	09/2012 09/2012	09/2012	0(O) 0(R)	0/0
106	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,733.00	03/2012 08/2012	08/2012	5(O) 0(R)	0/17
107	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	14.46	- -	-	- -	0/0
108	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	12/2012	80(O) 6(R)	0/0
109	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,531.71	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
110	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,278.73	09/2010 03/2012	04/2013	31(O) 13(R)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	829.98	07/2010 05/2012	07/2012	24(O) 2(R)	0/0
112	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
113	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	933.91	09/2012 09/2012	09/2012	0(O) 0(R)	0/76
114	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,156.52	09/2011 03/2012	09/2012	12(O) 6(R)	0/0
115	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	40.52	03/2013 -	04/2013	1(O) -	0/0
116	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	03/2015	10(O) -	0/0
117	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	219.80	03/2013 -	04/2013	1(O) -	0/0
118	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	7.33	11/2012 -	05/2013	6(O) -	0/0
119	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	47.45	01/2014 -	01/2014	0(O) -	0/0
120	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
121	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,902.02	- -	-	-	114/116
122	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	113.23	01/2013 -	01/2013	0(O) -	15/18
123	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	528.47	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
124	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015	0(O) -	0/0
125	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,300.00	1,113.63	06/2012 06/2012	06/2012	0(O) 0(R)	6/8
126	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
127	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
128	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
129	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015	0(O) -	0/0
130	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30(O) -	0/0
131	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50(O) -	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
132	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 252.37	204.00	169.73	01/2012 -	07/2012	6(O) -	3/8
133	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	927.98	12/2012 12/2012	04/2013	4(O) 4(R)	0/21
134	KOCHI-KOOTANAD BANGLORE-MANGLORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	193.68	03/2012 08/2012	08/2012	5(O) 0(R)	2/4
135	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,653.57	01/2012 -	09/2012	8(O) -	0/0
136	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,456.81	09/2012 -	09/2013	12(O) -	0/0
137	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,939.45	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
138	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	5.67	04/2015 -	04/2015	0(O) -	0/0
139	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19(O) 17(R)	0/0
140	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
141	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	15,728.00	11/2012 -	06/2013	7(O) -	57/100
142	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,400.00	606.13	09/2012 09/2012	09/2012	0(O) 0(R)	0/11
143	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	1,149.01	02/2014 -	02/2014	0(O) -	0/0
144	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	2,547.26	-	05/2014 -	05/2014	0(O) -	0/0
145	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	570.26	07/2012 -	10/2012	3(O) -	0/0
146	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	898.00	847.00	09/2011 -	-	- -	0/0
147	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	625.59	05/2010 04/2012	06/2012	25(O) 2(R)	0/0
148	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	144.02	08/2012 -	12/2012	4(O) -	0/0
149	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	210.72	03/2012 03/2012	06/2012	3(O) 3(R)	0/20
150	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	35.00	12/2013 12/2013	12/2013	0(O) 0(R)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			156,993.49	166,236.24	71,570.25				273/677
<u>Power</u>									
151	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	5,174.00	-	03/2013	-	0/11
152	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,035.00	-	10/2012	-	0/7
153	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	592.50	-	12/2012	-	0/11
154	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	943.80	-	12/2012	-	0/4
155	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	4,253.00	-	06/2014	-	5/19
156	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	7,004.00	12/2009 12/2014	03/2016	75(O) 15(R)	26/47
157	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,109.00	-	11/2014	-	4/28
158	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	2,084.00	1,824.71	08/2010 08/2011	06/2012	22(O) 10(R)	0/2
159	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	621.28	737.92	02/2011	10/2012	20(O)	2/4
160	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	176.70	-	08/2014	-	0/20
161	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44	206.44	21.90	-	06/2014	-	0/20
162	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	197.90	-	09/2014	-	0/20
163	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	832.00	10/2009	12/2012	38(O)	20/20
164	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	299.20	-	09/2013	-	0/13
165	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O)	0/0
166	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	278.10	-	05/2014	-	0/16

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	455.50	-	08/2013	-	0/14
168	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	179.30	-	06/2012	-	0/9
169	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77	901.77	52.80	-	08/2014	-	0/21
170	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	182.10	12/2013	12/2013	0(O)	0/0
171	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	185.70	-	12/2013	-	0/13
172	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	39.00	-	03/2013	-	0/15
173	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	1,007.16	831.60	12/2007	12/2009	24(O) 0(R)	0/10
174	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.00	1,859.60	05/2013	03/2017	46(O) 9(R)	4/22
175	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67	3,642.00	1,462.21	01/2016	11/2016	10(O) 10(R)	0/2
176	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	4,281.00	04/2009	03/2014	59(O) 0(R)	0/9
177	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,779.29	1,828.98	09/2008	-	-	3/37
178	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/0
179	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	690.00	11/2011	12/2012	13(O)	6/34
180	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,116.00	08/2012	03/2013	7(O)	10/16
181	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	751.75	08/2010	01/2013	29(O) 16(R)	0/3
182	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	4,537.10	-	09/2014	-	0/17
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	182.50	-	06/2012	-	0/7
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	226.20	-	03/2013	-	0/14
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	305.70	-	03/2013	-	0/11

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	324.10	- -	03/2013	- -	0/14
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	42.50	- -	01/2013	- -	0/7
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	167.40	- -	07/2013	- -	0/12
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	399.50	- -	06/2013	- -	0/12
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	52.80	- -	08/2013	- -	0/16
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	40.40	11/2014 -	11/2014	0(O) -	0/0
192	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	390.20	- -	03/2013	- -	0/10
193	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,816.32	10/2010 12/2011	01/2013	27(O) 13(R)	0/1
194	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,445.63	09/2009 07/2014	12/2017	99(O) 41(R)	1/20
195	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	331.39	08/2012 08/2013	09/2014	25(O) 13(R)	11/19
196	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,658.86	01/2012 -	09/2013	20(O) -	0/0
197	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,200.00	10/2012 -	03/2013	5(O) -	10/16
198	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	8,230.00	12/2009 12/2011	05/2012	29(O) 5(R)	59/60
199	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,666.41	09/2010 08/2014	12/2016	75(O) 28(R)	11/11
200	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	36.10	- -	04/2013	- -	0/15
201	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,917.20	- -	12/2012	- -	0/7
202	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	132.80	- -	06/2012	- -	0/5
203	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	47.90	- -	08/2014	- -	0/20

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
204	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	93.00	02/2015	02/2015	0(O)	0/0
205	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	95.10	-	01/2015	-	0/19
206	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	21.80	-	08/2014	-	0/20
207	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	51.50	-	06/2014	-	0/19
208	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	134.40	04/2012	04/2012	0(O)	0/0
209	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	94.98	-	06/2012	-	0/9
210	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	717.10	-	08/2012	-	0/11
211	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,467.00	03/2013	09/2015	30(O)	2/13
212	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,134.42	09/2009	06/2013	45(O)	0/0
213	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.39	1,488.49	03/2007	09/2012	66(O)	25/25
214	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00	2,978.86	325.98	07/2010	02/2016	67(O) 0(R)	1/10
215	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93	181.93	45.30	-	07/2013	-	0/20
216	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	259.28	14.60	-	01/2014	-	0/17
217	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	72.40	08/2014	08/2014	0(O)	0/0
218	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44	3,201.44	-	-	10/2014	-	0/21
219	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.91	326.43	-	09/2012	-	0/5
220	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,701.10	-	09/2013	-	0/12

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	254.50	01/2015	01/2015	0(O)	0/20
222	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25	2,569.25	440.70	-	03/2014	-	0/15
223	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL, Bihar	12/2005	3,779.46	3,779.46	3,681.30	09/2009	06/2012	33(O)	11/30
224	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL, Andhra Pradesh	12/2010	779.21	779.21	371.00	-	08/2013	-	0/14
225	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL, Andhra Pradesh	02/2012	324.33	324.33	1.30	-	08/2014	-	0/20
226	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL, Andhra Pradesh	02/2012	1,927.16	1,927.16	17.30	-	10/2014	-	0/20
227	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL, Himachal Pr.	07/2006	557.24	557.24	549.10	01/2010	02/2013	37(O)	0/22
228	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19	184.19	149.00	-	03/2013	-	0/7
229	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88	7,031.88	3,618.90	-	12/2012	-	0/11
230	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL, Gujarat	12/2011	552.44	552.44	38.40	-	02/2014	-	0/20
231	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya pradesh	08/2011	425.51	425.51	49.50	-	10/2013	-	0/18
232	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL, Maharashtra	07/2011	181.93	181.93	45.30	07/2013	07/2013	0(O)	0/0
233	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34	1,366.34	137.50	-	12/2013	-	0/18
234	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL, Jharkhand	10/2011	558.26	558.26	62.80	-	11/2013	-	0/20
235	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL, Orissa	09/2010	2,074.86	2,074.86	545.80	-	03/2013	-	0/14
236	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19	2,743.19	587.20	-	12/2013	-	0/13

Sector Wise Details

(May,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
237	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,222.50	- -	03/2013	- -	0/15
238	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	183.10	- -	07/2014	- -	0/19
239	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	250.55	- 07/2013	07/2013	- 0(R)	3/29
240	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	313.71	01/2014 02/2015	02/2015	13(O) 0(R)	0/0
241	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	759.10	- -	03/2013	- -	0/11
242	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	273.70	- -	11/2013	- -	0/15
243	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	50.50	- -	01/2013	- -	0/16
244	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	1,794.00	1,729.07	11/2009 11/2011	02/2013	39(O) 15(R)	0/4
245	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,421.00	10/2012 -	03/2013	5(O) -	8/15
246	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	306.16	07/2014 -	05/2016	22(O) -	1/3
247	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,125.70	07/2010 -	12/2012	29(O) -	20/20
248	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	84.00	- -	-	- -	0/9
249	WESTERN REGION SYSTEM STRENGHTENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	103.30	- 02/2012	06/2012	- 4(R)	0/3
250	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	18.60	- -	06/2015	- -	0/24
Total			210,306.58 -	223,892.50	107,720.47	243/1387			
Railways									
251	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.75	356.57	03/2014 -	03/2014	0(O) -	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
252	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	03/2011	15(O) 0(R)	0/0
253	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	156.15	- -	03/2013	- -	0/0
254	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	453.04	391.98	03/2011 03/2011	03/2011	0(O) 0(R)	0/0
255	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	518.18	06/1999 03/2011	03/2011	141(O) 0(R)	0/0
256	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	- -	0/0
257	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 -	394.14	0.49	03/2013 -	03/2013	0(O) -	0/0
258	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	- -	0/0
259	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	433.94	03/2005 12/2008	12/2015	129(O) 84(R)	0/0
260	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	198.70	12/2010 03/2011	03/2011	3(O) 0(R)	0/0
261	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	187.88	03/2004 12/2010	12/2010	81(O) 0(R)	0/0
262	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.48	4.57	04/2014 -	03/2015	11(O) -	0/0
263	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	595.56	03/2010 -	12/2012	33(O) -	0/0
264	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	350.00	315.39	- 03/2009	03/2011	- 24(R)	0/0
265	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
266	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	126.13	12/2012 -	05/2013	5(O) -	0/0
267	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	178.20	03/2011 -	03/2011	0(O) -	0/0
268	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	0.99	03/2012 -	03/2012	0(O) -	0/0
269	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	- -	0/0
270	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	873.69	12/2012 01/2013	01/2013	1(O) 0(R)	0/0
271	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	- -	0/0
272	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
273	CHURCHGATE-VIRAR: CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2012	06/2012	-12(O) 0(R)	0/0
274	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	415.73	240.93	- -	03/2012	- -	0/0
275	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	968.60	110.02	12/2012 -	12/2012	0(O) -	0/0
276	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	181.81	- -	03/2013	- -	0/0
277	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	376.26	12/2012 12/2012	12/2012	0(O) 0(R)	0/0
278	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	505.61	- -	-	- -	0/0
279	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	80.26	12/2011 02/2012	02/2012	2(O) 0(R)	0/0
280	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	0(O) -	0/0
281	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12(O) -	0/0
282	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	152.82	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
283	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	551.09	03/1995 -	03/2013	216(O) -	0/0
284	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	258.80	02/2011 02/2011	03/2012	13(O) 13(R)	0/0
285	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	39.12	02/2006 -	12/2013	94(O) -	0/0
286	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	863.23	509.13	- -	-	- -	0/0
287	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	- -	0/0
288	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	314.62	- 05/2009	05/2009	- 0(R)	0/0
289	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	89.65	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
290	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	178.53	- -	03/2015	- -	0/0
291	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	1,185.00	211.91	- 09/2009	12/2011	- 27(R)	0/0
292	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	- -	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
293	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	492.12	- -	01/2013	- -	0/0
294	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	137.83	- -	-	- -	0/0
295	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	163.52	03/2007 03/2007	03/2014	84(O) 84(R)	0/0
296	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.45	- -	-	- -	0/0
297	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	4.11	03/2015 -	03/2015	0(O) -	0/0
298	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	830.87	06/2007 -	06/2007	0(O) -	0/0
299	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.60	636.03	03/2012 06/2012	06/2012	3(O) 0(R)	0/0
300	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	409.77	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
301	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	4,444.00	797.35	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
302	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.46	105.44	03/2014 -	03/2014	0(O) -	0/0
303	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	229.99	03/2012 03/2012	10/2012	7(O) 7(R)	0/0
304	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,255.66	- -	02/2012	- -	0/0
305	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	750.89	474.97	- -	-	- -	1/1
306	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	713.06	- -	-	- -	0/0
307	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	728.94	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
308	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	90.41	- -	03/2013	- -	0/0
309	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	206.01	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
310	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	206.43	- -	03/2012	- -	0/0
311	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.22	- -	03/2015	- -	0/0
312	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	407.41	- 03/2010	03/2010	- 0(R)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
313	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,238.11	07/2005 -	07/2005	0(O) -	0/0
314	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, Jharkhandd	04/2002	459.91 418.17	418.17	117.55	- -	-	- -	0/0
315	KOSI BRIDGE (NL), ECR - [220100304] ECR, Bihar	04/2002	323.41 -	341.41	263.53	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
316	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265] SCR, Andhra Pradesh	12/2001	330.00 1,045.20	1,047.00	9.41	- -	-	- -	0/0
317	KOTTUR-HARIHAR (NL), (SWR) - [220100212] SWR, Karnataka	04/1995	65.94 302.23	302.23	335.67	- -	03/2011	- -	0/0
318	Katakhal to Bhairabi - [N22000126] NEFR, Assam	04/1998	227.90 -	223.01	105.81	12/2012 -	03/2014	15(O) -	0/0
319	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] NCR, Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	03/2011	34(O) 0(R)	0/0
320	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007] NCR, Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O) -	0/0
321	LANJHIGARH-JUNAGARH NL (ECOR) - [220100148] ECOR, Orissa	04/1993	100.00 142.98	227.94	200.21	03/2002 -	03/2012	120(O) -	0/0
322	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127] NEFR, Assam	04/1996	1,676.31 -	4,073.53	3,083.48	03/2009 -	12/2013	57(O) -	0/0
323	MACHERLA-NALGONDA (NL) (SCR) - [220100220] SCR, Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	0(O) -	0/0
324	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316] NER, Bihar	04/2003	218.19 -	218.19	153.90	- -	-	- -	0/0
325	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168] ER, Jharkhandd	04/1995	184.00 900.05	900.05	519.54	12/2011 12/2011	03/2012	3(O) 3(R)	0/0
326	MANOHARABAD-KOTHPALL NEW LINE (SCR) - [N22000032] SCR, Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	- -	0/0
327	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002] ECR, Bihar	04/1996	114.01 332.92	477.88	382.09	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
328	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079] SR, Tamil Nadu	09/2007	404.19 -	900.00	239.07	- -	-	- -	0/0
329	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N220000093] MRT, Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,334.00	06/2011 03/2012	03/2012	9(O) 0(R)	0/0
330	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092] MRT, Maharashtra	04/2008	5,300.00 -	5,300.00	698.48	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
331	MUNEERABAD-MAHABOBNAGAR (NL), SCR - [220100205] SCR, Multi State	04/1997	218.24 377.32	645.00	123.29	- -	03/2012	- -	0/0
332	MUZAFFARPUR-SITAMARHI (NL), ECR - [220100194] ECR, Bihar	04/1997	100.00 483.62	484.03	456.36	03/2012 03/2012	06/2012	3(O) 3(R)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
333	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	583.67	02/2009 -	03/2012	37(O) -	0/0
334	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	367.87	07/2012 07/2012	07/2012	0(O) 0(R)	0/0
335	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	532.87	39.45	- -	-	-	0/0
336	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	385.20	100.31	- -	03/2014	-	0/0
337	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.81	1,141.55	12/2008 -	03/2014	63(O) -	0/0
338	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	-	0/0
339	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O) -	0/0
340	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	2,913.51	101.35	03/2016 -	03/2016	0(O) -	0/0
341	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	24.60	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
342	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	16.66	03/2016 -	03/2016	0(O) -	0/0
343	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	21.98	03/2016 -	06/2016	3(O) -	0/0
344	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	386.60	03/2008 06/2008	-	-	0/0
345	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	355.00	386.79	03/2009 12/2009	03/2011	24(O) 15(R)	0/0
346	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	270.00	230.70	02/2010 -	11/2011	21(O) -	0/0
347	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,284.98	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
348	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	561.57	- -	03/2012	-	0/0
349	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	135.90	12/2010 12/2010	12/2010	0(O) 0(R)	0/0
350	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	733.51	- -	03/2013	-	0/0
351	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	221.21	12/2007 03/2010	12/2010	36(O) 9(R)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
352	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	1,115.63	711.40	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
353	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	248.52	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
354	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	216.85	03/2011 -	06/2012	15(O) -	0/0
355	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	225.35	- -	-	- -	0/0
356	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	292.01	06/2004 -	12/2012	102(O) -	0/0
357	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	1,190.08	- -	03/2013	- -	0/0
358	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	338.03	04/2003 03/2010	-	- -	0/0
359	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	530.76	486.33	02/2010 02/2011	02/2011	12(O) 0(R)	0/0
360	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	173.67	03/1998 08/2005	08/2005	89(O) 0(R)	0/0
361	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	329.78	03/2013 -	03/2015	24(O) -	0/0
362	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	64.13	03/2012 -	03/2013	12(O) -	0/0
363	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	222.07	03/2010 -	03/2012	24(O) -	0/0
364	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015	0(O) -	0/0
365	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	279.59	234.26	03/2011 03/2011	03/2011	0(O) 0(R)	0/0
366	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	818.29	-	02/2015 -	02/2015	0(O) -	0/0
367	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	196.61	03/2014 -	03/2014	0(O) -	0/0
368	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	109.94	- -	03/2013	- -	0/0
369	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	408.72	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
370	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	485.56	- 12/2009	02/2012	- 26(R)	0/0
371	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	582.83	112.89	- -	-	- -	0/0
372	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	34.89	- -	-	- -	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
373	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00	548.96	495.87	-	-	-	0/0
374	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69	3,176.10	3,183.24	12/2006	08/2010	44(O) 0(R)	0/0
375	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73	167.73	41.63	03/2012	03/2012	0(O)	0/0
376	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00	20,000.00	7,939.79	03/2001	12/2017	201(O)	0/0
377	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00	820.40	146.21	03/2010	06/2014	51(O) 0(R)	0/0
378	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62	1,389.62	283.11	03/2014	03/2014	0(O)	0/0
379	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66	356.87	161.67	-	-	-	0/0
	Total		64,854.78	142,224.55	60,751.33				1/1
Road Transport & Highways									
380	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	351.54	163.93	05/2013	03/2014	10(O)	0/0
381	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
382	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00	226.00	194.20	02/2014	02/2014	0(O)	0/0
383	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00	664.00	15.15	02/2014	04/2014	2(O)	0/0
384	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09	375.09	20.75	04/2014	04/2014	0(O)	0/0
385	2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar	12/2011	325.00	325.00	111.04	05/2014	05/2014	0(O)	0/0
386	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	196.58	08/2014	08/2014	0(O)	0/0
387	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50	1,008.50	1,079.10	06/2013	06/2013	0(O)	0/0
388	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	-	09/2013	07/2014	10(O)	0/0
389	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	785.50	472.11	08/2013	08/2013	0(O)	0/0
390	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00	575.00	343.02	07/2013	07/2013	0(O)	0/0
391	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00	398.00	-	02/2014	02/2014	0(O)	0/0
392	4-laning of Brahampore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79	998.79	498.45	08/2013	08/2013	0(O)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
393	4-laning of Faraka-Raiganj - [N24000202]NHAI, Multi State	02/2011	1,078.84	1,078.84	528.00	08/2013	08/2013	0(O)	0/0
394	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
395	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	465.50	151.69	09/2007	06/2013	69(O)	0/0
396	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	10/2012	91(O)	0/0
397	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	996.43	11/2012	06/2013	7(O)	0/0
398	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	278.86	11/2008	06/2012	43(O)	0/0
399	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	256.19	01/2009	06/2012	41(O)	0/0
400	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	07/2012	5(O)	0/0
401	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	188.72	02/2004	07/2012	101(O)	0/0
402	BAREILY-SITAPUR - [N24000200]NHAI, Uttar Pradesh	03/2011	1,046.00	1,046.00	79.65	09/2013	09/2013	0(O)	0/0
403	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, Rajasthan	12/2011	2,388.00	2,388.00	154.33	06/2014	06/2014	0(O)	0/0
404	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	331.15	-	10/2013	-	2/2
405	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00	209.00	3.77	01/2013	01/2013	0(O)	0/0
406	BHUBANESWAR TO PURI - [N24000195]NHAI, Orissa	03/2011	500.29	500.29	329.47	08/2013	08/2013	0(O)	0/0
407	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80	237.80	240.61	06/2008	12/2012	54(O)	0/0
408	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00	195.00	199.07	06/2008	03/2013	57(O)	0/0
409	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	225.24	06/2005	09/2012	87(O)	0/0
410	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	189.55	04/2010	12/2012	32(O)	0/0
411	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
412	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	610.20	03/2013	03/2013	0(O)	0/0
413	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	91.32	-	12/2013	-	0/1

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
414	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	914.62	05/2013	05/2013	0(O)	0/0
415	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	242.93	10/2011	03/2014	29(O)	0/0
416	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	663.32	10/2011	06/2013	20(O)	0/0
417	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	275.76	06/2008	12/2012	54(O)	0/0
418	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.23	10/2008	03/2014	65(O)	0/0
419	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	579.90	05/2010	12/2012	31(O)	0/0
420	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	324.26	07/2013	07/2013	0(O)	0/0
421	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
422	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	262.43	-	06/2013	-	1/1
423	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	223.78	06/2008	03/2013	57(O)	0/0
424	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	164.42	05/2008	03/2013	58(O)	0/0
425	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	251.79	09/2010	12/2012	27(O)	0/0
426	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	52.09	08/2013	08/2013	0(O)	0/0
427	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	535.00	01/2011	12/2012	23(O)	0/0
428	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	371.31	09/2008	12/2012	51(O)	0/0
429	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
430	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	118.85	09/2008	03/2013	54(O)	0/0
431	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	265.81	02/2004	06/2012	100(O)	0/0
432	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	304.26	09/2007	09/2012	60(O)	0/0
433	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	661.84	08/2013	08/2013	0(O)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
434	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	203.08	04/2008	12/2012	56(O)	0/0
435	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	142.77	04/2008	12/2012	56(O)	0/0
436	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38(O)	0/0
437	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	494.29	12/2009	12/2012	36(O)	0/0
438	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	1,299.10	09/2012	09/2012	0(O)	0/0
439	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	2,480.90	10/2011	06/2012	8(O)	0/0
440	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	273.02	09/2007	09/2012	60(O)	0/0
441	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	263.00	02/2009	03/2013	49(O)	0/0
442	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	35.95	07/2009	04/2014	57(O)	0/0
443	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	21.81	09/2007	04/2014	79(O)	0/0
444	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	182.88	08/2004	08/2012	96(O)	0/0
445	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	177.04	08/2004 07/2010	08/2012	96(O) 25(R)	0/0
446	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	768.35	01/2013	01/2013	0(O)	0/0
447	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	-	03/2013	-	3/3
448	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	1,679.30	10/2012	10/2012	0(O)	0/0
449	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	506.40	05/2012	06/2012	1(O)	0/0
450	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00	325.00	344.12	05/2013	02/2014	9(O)	0/0
451	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
452	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81	267.81	452.55	02/2013	02/2013	0(O)	0/0
453	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
454	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	500.97	09/2008	12/2012	51(O)	0/0
455	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	467.78	09/2009	12/2012	39(O)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
456	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00	536.00	366.19	01/2014	01/2014	0(O)	0/0
457	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	1,079.80	12/2012	12/2012	0(O)	0/0
458	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	279.31	10/2008	09/2012	47(O)	0/0
459	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	285.56	10/2008	03/2013	53(O)	0/0
460	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	-	-	03/2013	-	2/3
461	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	966.77	05/2012	09/2012	4(O)	0/0
462	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	185.52	06/2010	10/2012	28(O)	0/0
463	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	10/2012	37(O)	0/0
464	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00	225.00	261.98	10/2008	05/2012	43(O)	0/0
465	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	85.39	11/2008	07/2013	56(O)	0/0
466	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	54.25	04/2009	07/2013	51(O)	0/0
467	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	10.00	11/2008	01/2014	62(O)	0/0
468	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	106.74	04/2009	03/2013	47(O)	0/0
469	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6(O)	0/0
470	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	1,263.20	06/2013	06/2013	0(O)	0/0
471	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00	754.00	315.49	03/2013	03/2013	0(O)	0/0
472	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
473	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	281.81	06/2008	03/2013	57(O)	0/0
474	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48(O)	0/0
475	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	259.16	04/2008	12/2012	56(O)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
476	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	226.70	06/2008	03/2013	57(O)	0/0
477	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	273.65	06/2008	12/2012	54(O)	0/0
478	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
479	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	363.00	248.66	06/2011 06/2011	12/2012	18(O) 18(R)	0/2
480	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.92	02/2010	12/2014	58(O)	0/0
481	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00	586.00	154.47	01/2014	01/2014	0(O)	0/0
482	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	393.71	09/2013	09/2013	0(O)	0/0
483	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	377.71	03/2008	12/2012	57(O)	0/0
484	PANIKHOLI-RIMOLI - [N24000197]NHAI, Orissa	03/2012	1,410.00	1,410.00	120.31	09/2014	09/2014	0(O)	0/0
485	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	797.01	10/2014	10/2014	0(O)	0/0
486	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	197.27	05/2008	08/2012	51(O)	0/0
487	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	574.00	59.69	03/2014	03/2014	0(O)	0/0
488	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	501.32	02/2013	02/2013	0(O)	0/0
489	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,141.10	07/2012	12/2012	5(O)	0/0
490	PUNE-SATARA (NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	747.77	03/2013	03/2013	0(O)	0/0
491	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00	835.00	-	01/2014	01/2014	0(O)	0/0
492	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	3,458.50	11/2011	08/2013	21(O)	0/0
493	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2012	5(O)	0/0
494	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
495	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHA) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	302.00	10/2008	12/2012	50(O)	0/0
496	RAJMARG CHORAH TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91	229.91	253.74	10/2008	09/2012	47(O)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
497	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	639.25	11/2013	11/2013	0(O)	0/0
498	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	229.13	10/2008	12/2012	50(O)	0/0
499	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	180.94	10/2008	08/2012	46(O)	0/0
500	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	02/2013	25(O)	0/0
501	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	805.39	227.33	03/2013	03/2013	0(O)	0/0
502	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
503	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	196.85	09/2007	03/2013	66(O)	0/0
504	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	180.10	07/2008	12/2012	53(O)	0/0
505	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
506	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	4.93	12/2013	12/2013	0(O)	0/0
507	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00	1,535.00	808.88	05/2014	05/2014	0(O)	0/0
508	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2014	19(O)	0/0
509	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
510	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.21	03/2008	03/2013	60(O)	0/0
511	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	116.80	04/2004	07/2012	99(O)	0/0
512	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,648.00	08/2011	06/2012	10(O)	0/0
513	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	11/2012	41(O)	0/0
514	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	733.12	07/2010	03/2013	32(O)	0/0
515	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	468.64	11/2013	11/2013	0(O)	0/0
516	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
517	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	374.00	55.89	05/2013	05/2013	0(O)	0/0
518	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	-	-	04/2013	-	2/2
519	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	383.29	12/2008	05/2012	41(O)	0/0
520	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, Multi State	09/2011	2,848.00	2,848.00	494.52	03/2014	03/2014	0(O)	0/0
521	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09	166.30	185.05	03/2008	07/2012	52(O)	0/0
522	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27	193.10	161.44	03/2008	05/2012	50(O)	0/0
523	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	29.71	11/2012	11/2012	0(O)	0/0
524	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88	953.88	300.33	07/2013	07/2013	0(O)	0/0
525	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI, Multi State	12/2011	1,047.00	1,047.00	148.11	06/2014	06/2014	0(O)	0/0
Total			91,616.10	93,334.43	58,472.90				10/14
Shipping & Ports									
526	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	359.44	358.78	04/2011 10/2012	10/2012	18(O) 0(R)	0/0
527	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP., Maharashtra	08/2008	1,066.91	968.35	447.38	09/2012	09/2012	0(O)	0/0
528	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP., Maharashtra	08/2010	612.72 627.64	627.64	187.07	12/2012 05/2013	05/2013	5(O) 0(R)	0/0
529	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP., Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8(O) 0(R)	0/0
530	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP., Maharashtra	04/2009	290.85	305.00	86.46	06/2011 09/2012	09/2012	15(O) 0(R)	0/0
531	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP., Maharashtra	10/2010	966.46	994.82	189.92	02/2014	02/2014	0(O)	0/0
532	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP., Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013	12/2013	0(O)	0/0

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total	
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
533	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	772.87	12/2010 -	12/2012	24(O) -	0/0	
534	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0	
535	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0	
536	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	10/2008	0(O) -	0/0	
537	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	- 0(R)	0/1	
538	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O) -	0/0	
539	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0	
540	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	252.00	0.21	03/2012 -	03/2012	0(O) -	0/0	
541	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	22(O) 15(R)	0/0	
542	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	829.21	10/2008 -	11/2010	25(O) -	0/0	
543	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,245.60	01/2012 09/2012	09/2012	8(O) 0(R)	0/0	
544	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0	
Total			16,242.52 -	17,757.49	7,189.62					0/1
<u>Telecommunications</u>										
545	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2012	41(O) -	0/0	
546	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	08/2011	54(O) 8(R)	0/0	
547	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72(O) 11(R)	0/0	

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
548	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	21.93	10/2010 03/2012	07/2012	21(O) 4(R)	0/0
549	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	- -	0/0
550	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	- -	0/0
551	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	06/2012	36(O) -	0/0
552	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94 -	373.94	229.04	12/2008 -	06/2012	42(O) -	0/0
553	GSM equipment of 1625000 Lines (2G) 325000 lines 3(G) - [N26000090]BSNL, Madhya pradesh	11/2009	916.70 930.60	930.60	804.06	11/2010 -	06/2012	19(O) -	0/0
554	GSM equipment of 200000 Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	17(O) -	0/0
555	GSM equipment of 799000 Lines (2G) 101000 lines 3(G) - [N26000088]BSNL, Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	06/2012	39(O) -	0/0
556	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL, Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	- -	0/0
557	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O) -	0/0
558	NIB Project Capacity Expansion - [N26000098]BSNL, Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	06/2012	42(O) -	0/0
559	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL, Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	06/2012	78(O) 51(R)	0/0
	Total		6,161.00 -	6,101.79	1,774.29				0/0
Urban Development									
560	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15(O) -	6/6
561	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	- -	0/0
562	DELHI MRTS PHASE-III - [N28000056]DMRC, Delhi	09/2011	35,242.00 -	35,242.00	279.92	03/2016 -	03/2016	0(O) -	0/0
563	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	2,494.00	14.40	09/2014 -	09/2014	0(O) -	0/0
	Total		44,245.18 -	49,518.08	2,561.89				6/6

Sector Wise Details

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Water Resources</u>								
564	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
	Grand Total		732,115.53	875,158.50	396,282.70				875/3321

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

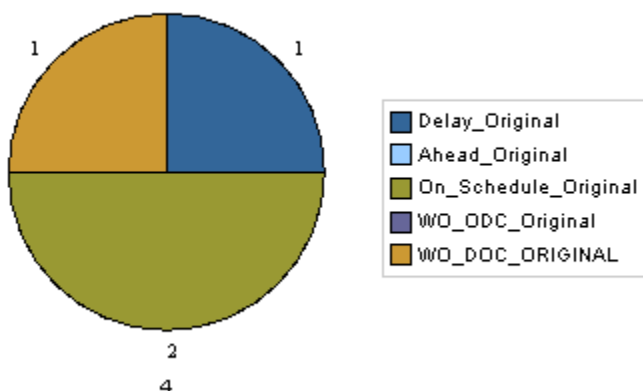

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till May, 2012 is Rs. 2561.89 crore, which is 5.2% of the revised cost of the projects.

Figures are in Rs. Crore

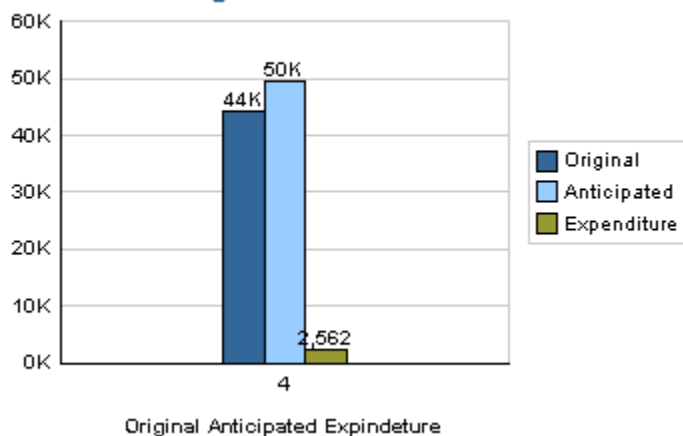

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **15**

Number of Projects Delayed **9**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 9 projects are delayed .6 projects do not have fixed dates of commissioning.

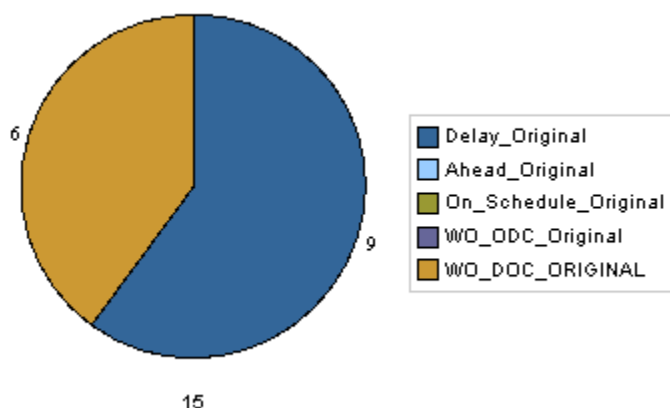

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 6161 crore but this was subsequently revised to Rs. 6101.79 crore implying a cost overrun of -1%. The expenditure incurred on these projects till May, 2012 is Rs. 1774.29 crore, which is 29.1% of the revised cost of the projects.

Figures are in Rs. Crore

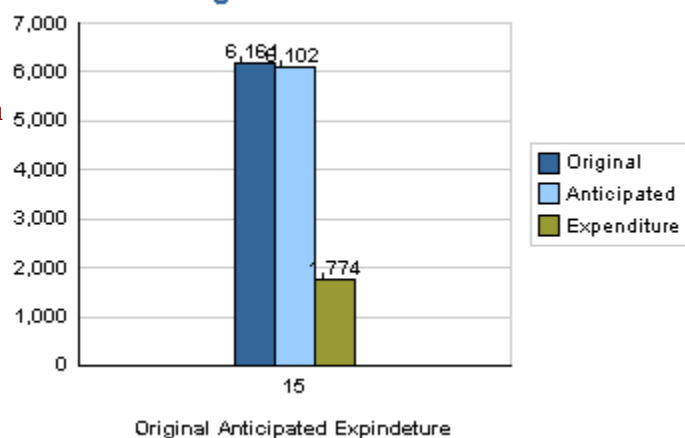

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 3 projects are on schedule and 10 projects are delayed .5 projects do not have fixed dates of commissioning.

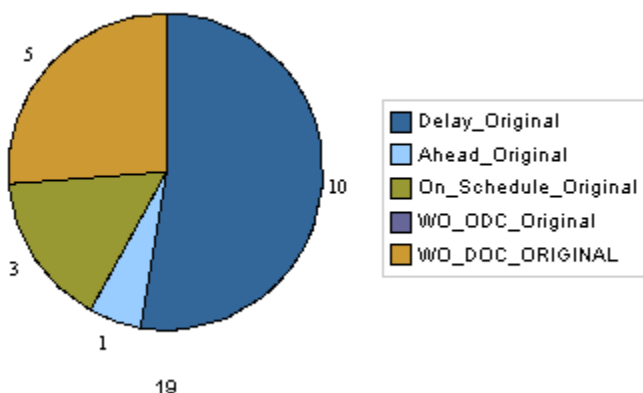

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 16242.52 crore but this was subsequently revised to Rs. 17757.49 crore implying a cost overrun of 9.3%. The expenditure incurred on these projects till May, 2012 is Rs. 7189.62 crore, which is 40.5% of the revised cost of the projects.

Figures are in Rs. Crore

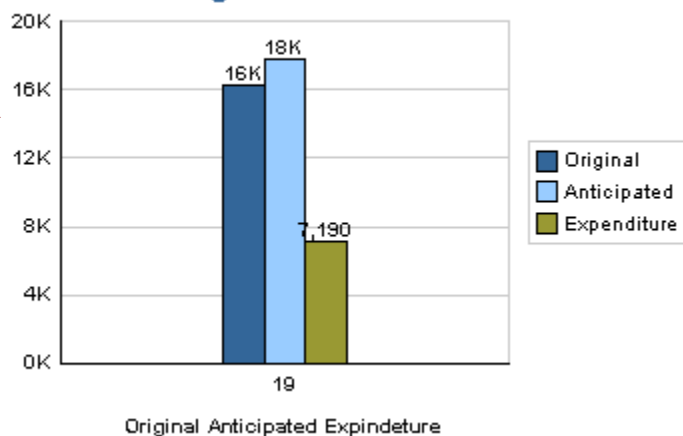

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	146
Number of Projects On Schedule	56
Number of Projects Delayed	84

Number of Projects Without Original Date of Commissioning	6
---	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 146 projects, 56 projects are on schedule and 84 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

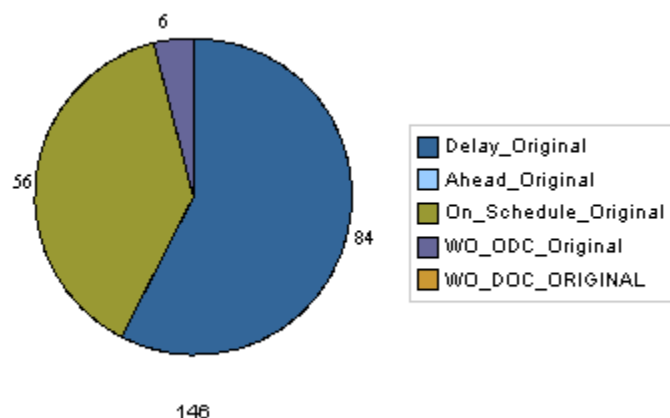

III. Investment Scenario

The Total Original cost of implementation of 146 projects when sanctioned, was of the order of Rs. 91616.1 crore but this was subsequently revised to Rs. 93334.43 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till May, 2012 is Rs. 58472.9 crore, which is 62.6% of the revised cost of the projects.

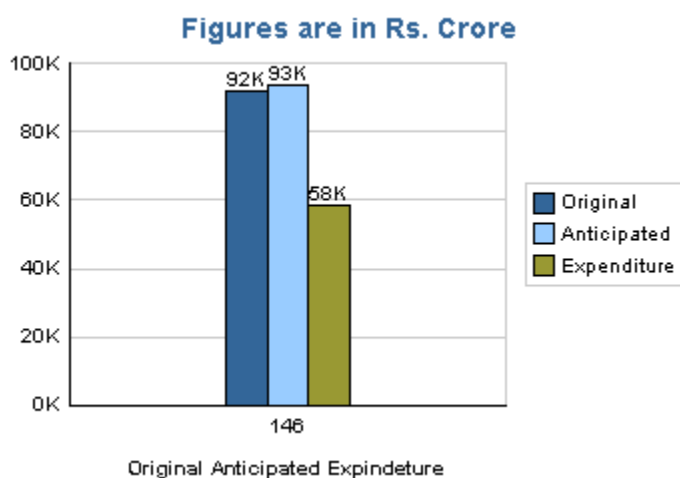

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	129
Number of Projects On Schedule	14
Number of Projects Delayed	36
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	12
Number of Projects Without Date Of Commissioning	66

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 129 projects, 1 project are ahead of schedule, 14 projects are on schedule and 36 projects are delayed .66 projects do not have fixed dates of commissioning.12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

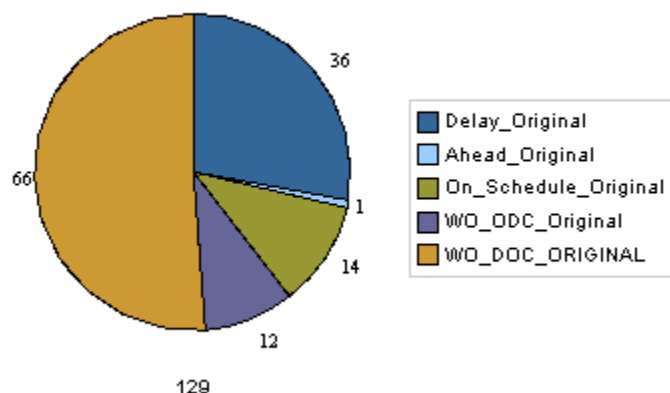

III. Investment Scenario

The Total Original cost of implementation of 129 projects when sanctioned, was of the order of Rs. 64854.78 crore but this was subsequently revised to Rs. 142224.55 crore implying a cost overrun of 119.3%. The expenditure incurred on these projects till May, 2012 is Rs. 60751.33 crore, which is 42.7% of the revised cost of the projects.

Figures are in Rs. Crore

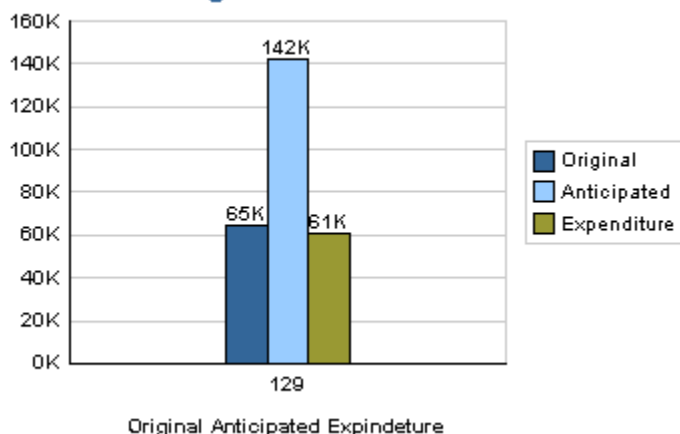

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	100
Number of Projects On Schedule	9
Number of Projects Delayed	28

Number of Projects Without Original Date of Commissioning	59
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 100 projects, 9 projects are on schedule and 28 projects are delayed .4 projects do not have fixed dates of commissioning.59 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

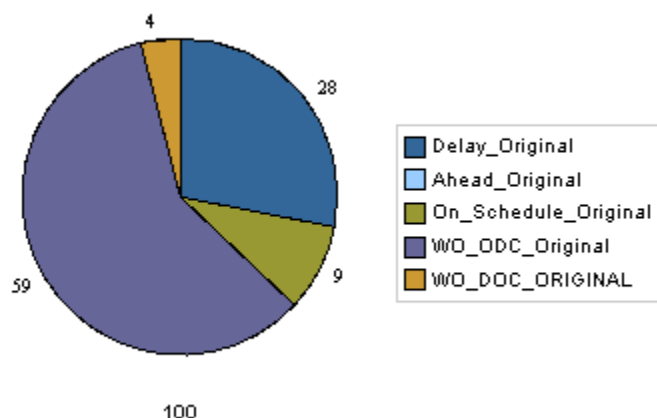

III. Investment Scenario

The Total Original cost of implementation of 100 projects when sanctioned, was of the order of Rs. 210306.58 crore but this was subsequently revised to Rs. 223892.5 crore implying a cost overrun of 6.5%. The expenditure incurred on these projects till May, 2012 is Rs. 107720.47 crore, which is 48.1% of the revised cost of the projects.

Figures are in Rs. Crore

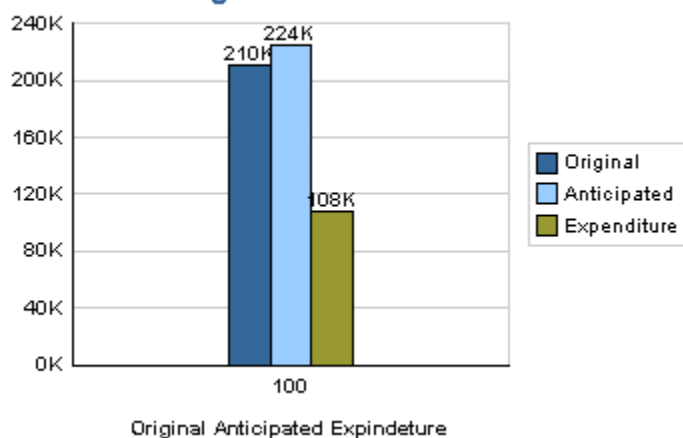

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	65
Number of Projects On Schedule	19
Number of Projects Delayed	41

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 65 projects, 19 projects are on schedule and 41 projects are delayed .4 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

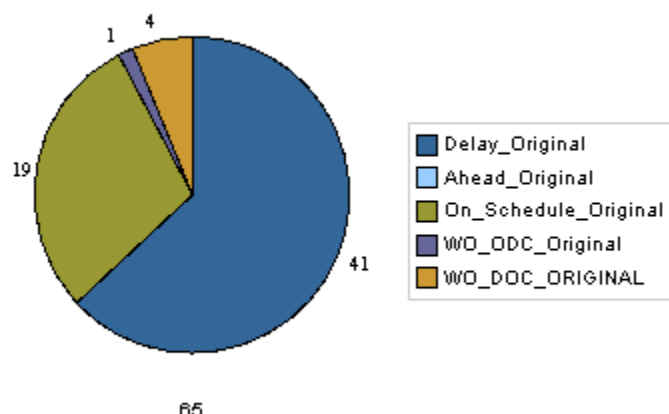

III. Investment Scenario

The Total Original cost of implementation of 65 projects when sanctioned, was of the order of Rs. 156993.49 crore but this was subsequently revised to Rs. 166236.24 crore implying a cost overrun of 5.9%. The expenditure incurred on these projects till May, 2012 is Rs. 71570.25 crore, which is 43.1% of the revised cost of the projects.

Figures are in Rs. Crore

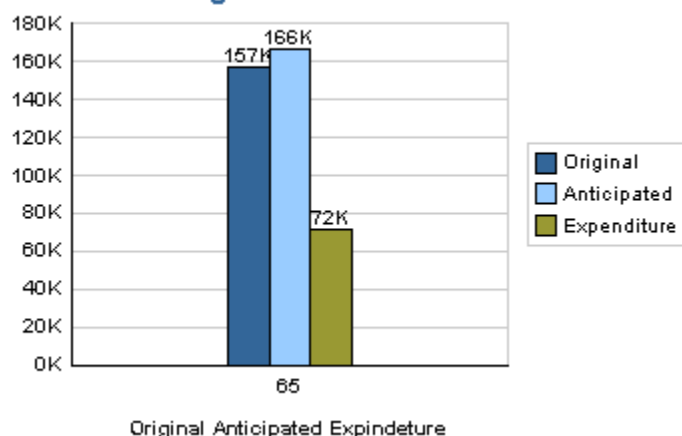

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	1
Number of Projects Delayed	8
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 1 project are ahead of schedule, 1 project are on schedule and 8 projects are delayed .1 project do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

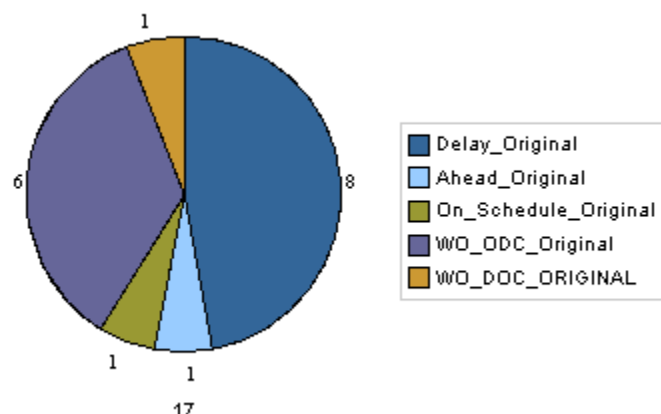

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 50343.15 crore but this was subsequently revised to Rs. 71589.69 crore implying a cost overrun of 42.2%. The expenditure incurred on these projects till May, 2012 is Rs. 40797.2 crore, which is 57% of the revised cost of the projects.

Figures are in Rs. Crore

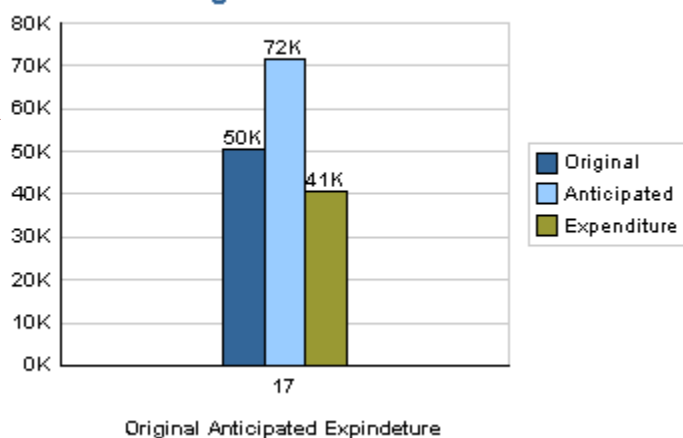

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

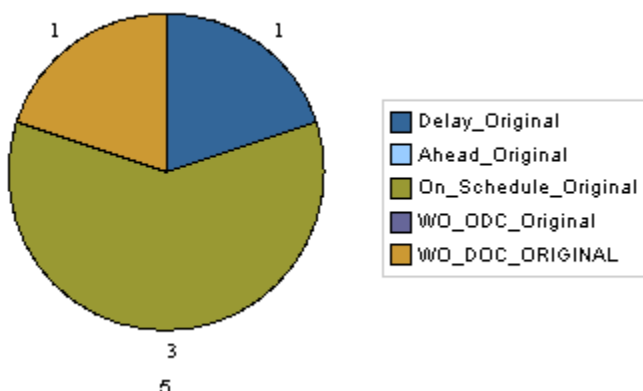

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4828.66 crore but this was subsequently revised to Rs. 4828.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till May, 2012 is Rs. 2265.48 crore, which is 46.9% of the revised cost of the projects.

Figures are in Rs. Crore

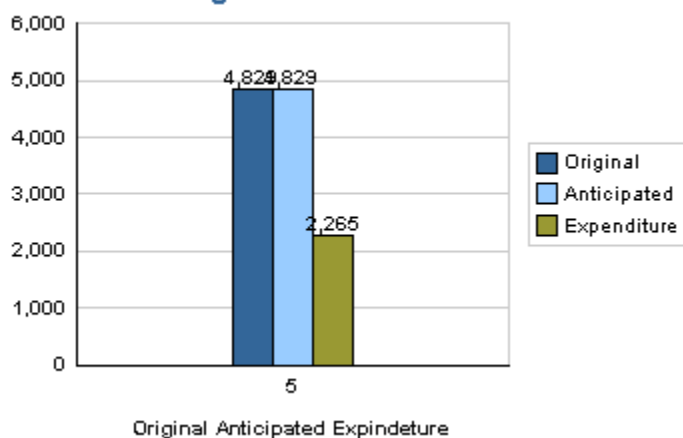

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	52
Number of Projects On Schedule	25
Number of Projects Delayed	26

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 52 projects, 25 projects are on schedule and 26 projects are delayed .1 project do not have fixed dates of commissioning.

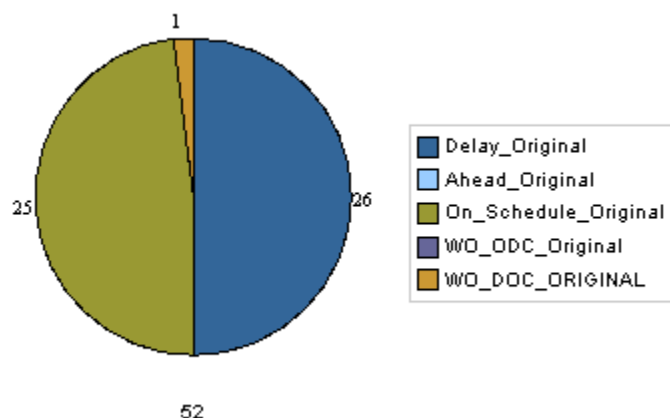

III. Investment Scenario

The Total Original cost of implementation of 52 projects when sanctioned, was of the order of Rs. 33950.69 crore but this was subsequently revised to Rs. 37570.71 crore implying a cost overrun of 10.7%. The expenditure incurred on these projects till May, 2012 is Rs. 11975.21 crore, which is 31.9% of the revised cost of the projects.

Figures are in Rs. Crore

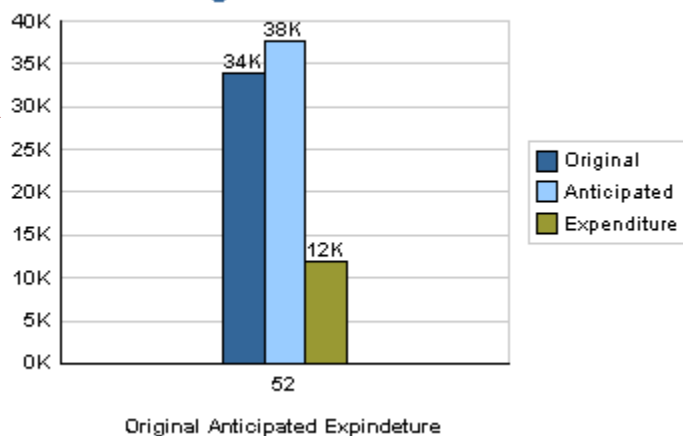

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

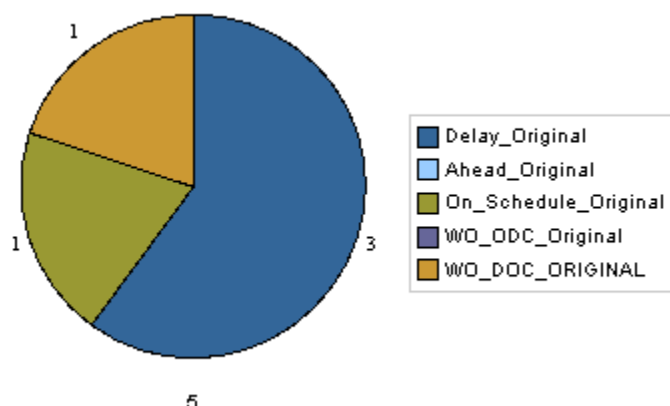

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till May, 2012 is Rs. 4298.52 crore, which is 76.6% of the revised cost of the projects.

Figures are in Rs. Crore

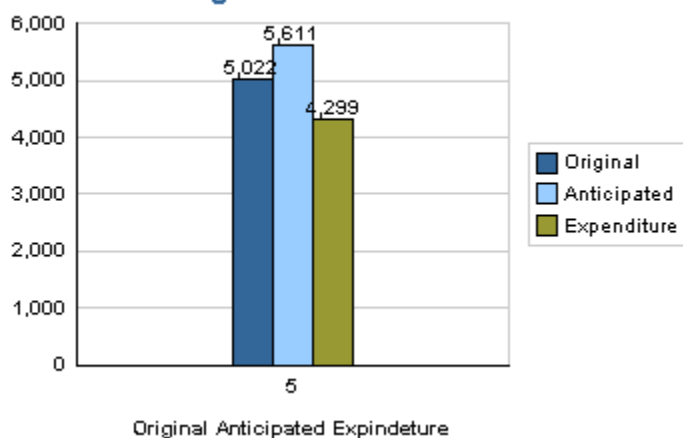

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

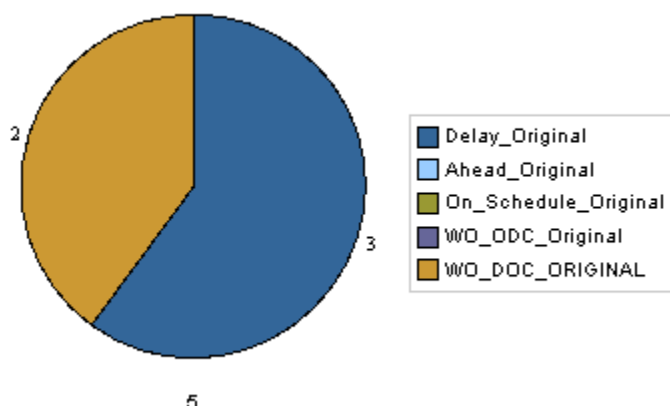

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 46386.29 crore implying a cost overrun of 11.6%. The expenditure incurred on these projects till May, 2012 is Rs. 22212.84 crore, which is 47.9% of the revised cost of the projects.

Figures are in Rs. Crore

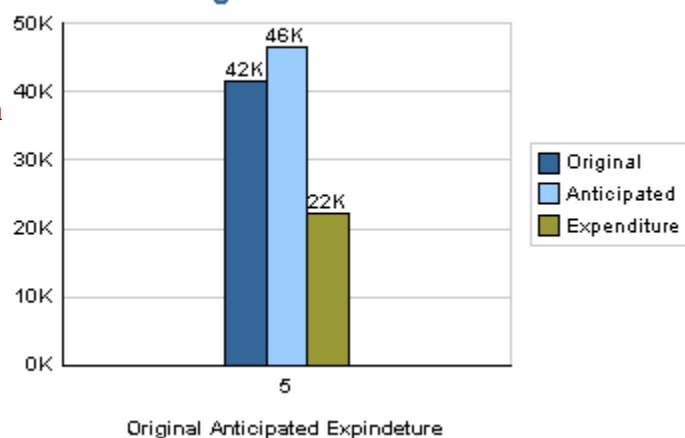

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	36	31031.62	38459.02	21597.86
2	Arunachal Pr.	4	9512.22	14152.72	8098.33
3	Assam	36	22463.87	33865.52	20965.80
4	Bihar	32	30891.77	35951.12	24004.93
5	Chhatisgarh	27	41193.18	56813.15	20863.13
6	Delhi	3	37985.00	37965.41	361.52
7	Goa	1	335.61	335.61	111.25
8	Gujarat	23	31308.52	31536.52	6487.63
9	Haryana	9	5306.60	7177.17	7054.61
10	Himachal Pr.	6	14761.20	17455.42	13575.62
11	J and K	11	15120.05	34413.14	12967.23
12	Jharkhandd	23	11785.48	16601.53	7432.22
13	Karnataka	23	29468.64	37913.46	15388.40
14	Kerala	5	5469.67	6911.22	4754.08
15	Madhya pradesh	25	16968.45	17262.92	8572.16
16	Maharashtra	51	78453.62	93665.76	46079.50
17	Manipur	1	727.56	4444.00	797.35
18	Meghalaya	2	762.00	762.00	560.39
19	Mizoram	2	1532.97	3307.11	318.28
20	Multi State	103	136198.95	142534.67	57518.76
21	Nagaland	1	850.00	850.00	8.44
22	Orissa	30	57405.36	61206.44	29164.31
23	Punjab	6	4384.20	5325.97	3522.94
24	Rajasthan	15	26688.02	26417.90	8302.18
25	Sikkim	2	1648.94	3690.04	235.61
26	Tamil Nadu	32	51275.95	60135.04	37590.08
27	Tripura	3	1522.39	2053.23	751.14
28	Uttar Pradesh	24	18548.94	22386.71	11253.50
29	Uttaranchal	4	8514.31	9454.74	2539.71
30	West Bengal	25	40187.77	52298.29	25405.74
TOTAL		565	732302.86	875345.83	396282.70

LIST OF PROJECTS IN WHICH EXPENDITURE MORE THAN COST

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	BHAVNI	3492.00	0.00	3641.60
2	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	14755.00
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	AAI	1942.51	0.00	1966.18
4	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	Petroleum	HPCL	224.00	299.00	328.43
5	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATTNAM	Petroleum	HPCL	756.00	0.00	847.00
6	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1488.49
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	NHPC	1061.38	0.00	1134.42
8	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	PGCIL	297.37	0.00	326.43
9	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.01	0.00	751.75
10	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	Power	PGCIL	1779.29	0.00	1828.98
11	CHUTAK HYDRO-ELECTRIC PROJECT	Power	NHPC	621.26	0.00	737.92
12	CHAMERA,STAGE-III (NHPC)	Power	NHPC	1405.63	0.00	1824.71
13	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	NCR	158.77	432.46	558.07
14	CALICUT-MANGALORE (DL) (SR)	Railways	SR	240.00	0.00	600.41
15	KARUR-SALEM(NL),SR	Railways	SR	155.55	229.88	713.06
16	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	ECR	491.19	1099.20	1238.11
17	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	248.44	576.27	873.69
18	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	NEFR	915.70	0.00	1190.08
19	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	RVNL	136.62	0.00	221.21
20	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	NEFR	733.00	0.00	1141.55
21	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	250.82
22	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	233.00	501.69	636.03
23	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	NEFR	1000.00	1500.00	2408.10
24	KODERMA GIRIDH (NL), ECR	Railways	ECR	371.36	0.00	407.41
25	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	100.00	142.98	200.21
26	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	114.01	332.92	382.09
27	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	505.61
28	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	RVNL	240.00	0.00	386.79
29	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	486.33
30	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	(NR)	409.00	625.30	830.87

31	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	(NR)	2500.00	0.00	7939.79
32	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	474.97
33	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	NER	395.00	1062.36	1255.66
34	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	3083.48
35	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	240.93
36	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	0.00	391.98
37	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	NEFR	727.56	0.00	797.35
38	RAJPIPLA-ANKELASHWAR, WR (GC)	Railways	WR	196.97	0.00	216.85
39	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	518.18
40	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	495.68	561.57
41	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	SR	100.00	0.00	495.87
42	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	SWR	295.00	412.91	492.12
43	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	302.23	335.67
44	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	292.01
45	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	429.49	583.67
46	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	227.48
47	RENIGUNTA-GUNTAKAL(RE)	Railways	RVNL	168.34	0.00	338.03
48	RAJATGARH-BARANG(LD),ECOR	Railways	RVNL	166.16	0.00	248.52
49	BILASPUR-URKURA (DL)	Railways	RVNL	151.52	0.00	315.39
50	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	728.94
51	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	NER	381.17	0.00	509.13
52	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	M RTP	907.69	3176.10	3183.24
53	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	228.09	258.80
54	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	409.77
55	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	285.56
56	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	196.85
57	JAIPUR-REENGUS	Road Transport & Highways	NHAI	267.81	0.00	452.55
58	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	835.00	0.00	1068.70
59	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	768.35
60	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	256.19
61	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	Road Transport & Highways	NHAI	464.00	0.00	535.00
62	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	NHAI	263.27	0.00	265.81
63	Armur to kadloor yellareddy	Road Transport & Highways	NHAI	390.56	0.00	631.65
64	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	NHAI	229.91	0.00	253.74

65	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	229.13
66	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	180.94
67	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	NHAI	237.80	0.00	240.61
68	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	1008.50	0.00	1079.10
69	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.92
70	Chilkaluri pet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	NHAI	572.30	0.00	663.32
71	Surat- Dahisar (Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2648.00
72	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	NHAI	1673.70	0.00	2480.90
73	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	733.12
74	THANJAUR-TRICHY, NH-67 (NHAI)	Road Transport & Highways	NHAI	280.00	0.00	581.49
75	SALEM - U / UNDRUPET (BOT -1/TN-06) NH 68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
76	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	792.06	0.00	1079.80
77	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	996.43
78	Pune-sholapur, pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1802.10
79	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP PHASE-III)	Road Transport & Highways	NHAI	940.00	0.00	1141.10
80	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	NHAI	225.00	0.00	261.98
81	JHANSI TO LALITPUR, NH-25, 26	Road Transport & Highways	NHAI	355.06	0.00	467.78
82	KOTA BYPASS, RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	279.31
83	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	377.71
84	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	500.97
85	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	278.86
86	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	NHAI	195.00	0.00	199.07
87	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	NHAI	198.16	0.00	203.08
88	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	3458.50
89	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	966.77
90	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	388.00	0.00	506.40
91	NAGPUR-KONDHALI, NH-6 (NHAI)	Road Transport & Highways	NHAI	168.00	0.00	457.30
92	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	NHAI	232.45	0.00	251.79
93	GWALIOR BYPASS, NH-75, 3	Road Transport & Highways	NHAI	300.93	0.00	302.72

94	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	NHAI	332.94	0.00	371.31
95	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	302.00
96	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	273.65
97	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	NHAI	225.00	0.00	226.70
98	NALBARI T BIJNI (AS-7)	Road Transport & Highways	NHAI	208.00	0.00	259.16
99	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	491.21
100	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	NHAI	200.00	0.00	223.78
101	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	NHAI	264.72	0.00	281.81
102	INDORE-DEWAS(NH-3)	Road Transport & Highways	NHAI	325.00	0.00	344.12
103	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	NHAI	227.00	0.00	383.29
104	DAKOPA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	275.76
105	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	NHAI	160.00	0.00	164.42
106	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	579.90
107	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
108	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	304.26
109	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	273.02
110	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	RVNL	245.67	298.17	326.08
111	EXPANSION OF BHILAI STEEL PLANT	Steel	SAIL	5185.00	0.00	5634.23
112	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	RINL	230.00	0.00	247.41

Ahead

S.No	Project	DOA	DOC Original	DOC Revised	DOC Anticipated	COST Original	Cost Anticipated
1	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas	2/2011	05/2013	N.A.	03/2013	830	621.53
2	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	7/1996	06/2013	06/2012	06/2012	653.84	1302.12
3	EXPENSION OF ROURKELA STEEL PLANT	9/2008	11/2013	N.A.	03/2013	11812	11812

List of project Without Original Date of Commissioning

(May,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Steel</u>									
1	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00	6,325.00	2,716.78	-	10/2012	-	3/16
2	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,293.51	-	12/2012	-	7/19
3	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	-	-	04/2013	-	0/19
4	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	-	-	05/2013	-	0/21
5	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	5,634.23	-	09/2013	-	9/27
6	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55	254.55	6.12	-	11/2013	-	0/1
Total			24,669.10	41,723.10	21,650.64				19/103
<u>Petroleum</u>									
7	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	132.00	-	09/2012	-	25/36
Total			333.99	333.99	132.00				25/36
<u>Power</u>									
8	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	103.30	- 02/2012	06/2012	4(R3)	0/3
9	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	182.50	- 11/2011	06/2012	7(R3)	0/7
10	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	132.80	-	06/2012	-	0/5
11	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	179.30	-	06/2012	-	0/9
12	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	94.98	-	06/2012	-	0/9
13	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	717.10	-	08/2012	-	0/11
14	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.91	326.43	-	09/2012	-	0/5
15	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,035.00	-	10/2012	-	0/7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	3,618.90	-	12/2012	-	0/11
17	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,917.20	-	12/2012	-	0/7
18	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	943.80	-	12/2012	-	0/4
19	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	592.50	-	12/2012	-	0/11
20	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	42.50	-	01/2013	-	0/7
21	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	50.50	-	01/2013	-	0/16
22	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	305.70	-	03/2013	-	0/11
23	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	324.10	-	03/2013	-	0/14
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	226.20	-	03/2013	-	0/14
25	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	149.00	-	03/2013	-	0/7
26	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	5,174.00	-	03/2013	-	0/11
27	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	1,222.50	-	03/2013	-	0/15
28	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	759.10	-	03/2013	-	0/11
29	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	390.20	-	03/2013	-	0/10
30	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	545.80	-	03/2013	-	0/14
31	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	39.00	-	03/2013	-	0/15
32	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	36.10	-	04/2013	-	0/15
33	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	399.50	-	06/2013	-	0/12

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
34	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01 623.44	623.44	250.55	- 07/2013	07/2013	0(R3)	3/29
35	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, Multi State	07/2010	752.64 -	752.64	167.40	- -	07/2013	-	0/12
36	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL, Madhya Pradesh	07/2011	181.93 -	181.93	45.30	- -	07/2013	-	0/20
37	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL, Andhra Pradesh	12/2010	779.21 -	779.21	371.00	- -	08/2013	-	0/14
38	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL, Multi State	12/2010	209.78 -	209.78	52.80	- -	08/2013	-	0/16
39	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL, Chhatisgarh	12/2010	1,719.52 -	1,719.52	455.50	- -	08/2013	-	0/14
40	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, Multi State	10/2008	4,824.12 -	4,824.12	2,701.10	- -	09/2013	-	0/12
41	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL, Multi State	07/2010	1,272.80 -	1,272.80	299.20	- -	09/2013	-	0/13
42	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya Pradesh	08/2011	425.51 -	425.51	49.50	- -	10/2013	-	0/18
43	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL, Multi State	03/2011	1,585.12 -	1,585.12	273.70	- -	11/2013	-	0/15
44	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL, Jharkhand	10/2011	558.26 -	558.26	62.80	- -	11/2013	-	0/20
45	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19 -	2,743.19	587.20	- -	12/2013	-	0/13
46	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34 -	1,366.34	137.50	- -	12/2013	-	0/18
47	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL, Chhatisgarh	08/2011	1,391.97 -	1,391.97	185.70	- -	12/2013	-	0/13
48	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL, Gujarat	01/2012	259.28 -	259.28	14.60	- -	01/2014	-	0/17
49	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL, Gujarat	12/2011	552.44 -	552.44	38.40	- -	02/2014	-	0/20
50	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25 -	2,569.25	440.70	- -	03/2014	-	0/15

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
51	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	278.10	- -	05/2014	-	0/16
52	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,253.00	- -	06/2014	-	5/19
53	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	183.10	- -	07/2014	-	0/19
54	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	176.70	- -	08/2014	-	0/20
55	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	47.90	- -	08/2014	-	0/20
56	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	52.80	- -	08/2014	-	0/21
57	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	4,537.10	- -	09/2014	-	0/17
58	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	197.90	- -	09/2014	-	0/20
59	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	17.30	- -	10/2014	-	0/20
60	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	-	- -	10/2014	-	0/21
61	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,109.00	- -	11/2014	-	4/28
62	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	95.10	- -	01/2015	-	0/19
63	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	18.60	- -	06/2015	-	0/24
Total			108,331.09 -	108,534.06	38,607.56				12/804
<u>Railways</u>									
64	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	492.12	- -	01/2013	-	0/0
65	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	156.15	- -	03/2013	-	0/0
66	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	181.81	- -	03/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
67	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	90.41	- -	03/2013	-	0/0
68	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	733.51	- -	03/2013	-	0/0
69	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	1,190.08	- -	03/2013	-	0/0
70	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	109.94	- -	03/2013	-	0/0
71	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
72	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	385.20	100.31	- -	03/2014	-	0/0
73	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	-	0/0
74	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	178.53	- -	03/2015	-	0/0
75	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.22	- -	03/2015	-	0/0
	Total		4,028.98 -	9,633.39	3,671.00				0/0
Road Transport & Highways									
76	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	-	- -	03/2013	-	3/3
77	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	-	- -	03/2013	-	2/3
78	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	-	2/2
79	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	262.43	- -	06/2013	-	1/1
80	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	331.15	- -	10/2013	-	2/2
81	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	91.32	- -	12/2013	-	0/1
	Total		4,069.00 -	4,069.00	684.90				10/12
Grand Total			141,432.16	164,293.54	64,746.10				66/955

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	09/2010	01/2012
			-	-	
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	04/2012
			-	04/2011	
	Total		4,598.29		
			-		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
			2,015.00	02/2012	
	Total		1,808.00		
			-		
<u>Coal</u>					
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	03/2012
			-	-	
	Total		249.03		
			-		
<u>Fertilisers</u>					
5	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	07/2011	04/2012
			-	-	
	Total		325.00		
			-		
<u>Steel</u>					
6	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	-	02/2012
			-	-	
	Total		500.90		
			-		
<u>Petroleum</u>					
7	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	02/2011	08/2011
			299.00	08/2011	
8	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	09/2011	-
			-	-	
9	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
			-	-	
10	EURO-IV DHD T - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	-	-
			-	-	
	Total		5,179.69		
			-		
<u>Power</u>					
11	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	04/2012
			-	-	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
12	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	12/2009
13	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	09/2008 -	-
14	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	- -	-
	Total		3,130.04 -		
<u>Railways</u>					
15	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	07/2005 -	07/2005
16	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
17	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
18	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
19	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
20	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	- 03/2010	03/2010
21	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010
22	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2010
23	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
24	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
25	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
26	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
27	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011
28	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
29	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
30	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	03/2011 03/2011	03/2011
31	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
32	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
33	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011
34	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
35	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011
36	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	02/2010 -	11/2011

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
37	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
38	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011
39	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
40	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012
41	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
42	Dakshin-barasa-Hakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
43	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
44	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2012
45	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2012
46	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
47	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
48	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2012
49	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012
50	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
51	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
52	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
53	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012
54	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	06/2011 03/2012	03/2012
55	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
56	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
57	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	03/2012 -	03/2012
58	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012
59	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
60	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
61	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-
62	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
63	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
64	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
65	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-
66	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.20	- -	-
67	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-
68	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
69	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13 727.13	- -	-
70	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
71	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
72	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-
73	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-
74	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-
75	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
76	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-
77	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-
78	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	- -	-
79	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-
80	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-
Total			21,063.45 -		
<u>Shipping & Ports</u>					
81	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008
82	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	- 01/2009	01/2009
83	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	11/2010
84	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
85	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	03/2012 -	03/2012
Total			3,904.91 -		
<u>Telecommunications</u>					

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
86	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
87	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
88	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
89	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
90	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	08/2011
91	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010
	Total		2,997.75 -		
	<u>Urban Development</u>				
92	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
	Grand Total			43,871.24	

List of On Schedule

S.No	Project	DOA	DOC Original	DOC Revised	DOC Anticipated	COST Original	Cost Anticipated
1	DEOGHAR - SULTANGANJ (INL), ER	4/2000	12/2012	12/2012	12/2012	138	607.09
2	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	02/2015	N.A.	02/2015	183.23	818.29
3	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY	3/2009	09/2012	09/2012	09/2012	3284	2174
4	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJECT	1/2010	01/2013	N.A.	01/2013	1294.19	1294.19
5	Talegaon-amravati	11/2009	11/2013	N.A.	11/2013	567	567
6	Purnadih OCP	7/2008	03/2013	N.A.	03/2013	210.98	210.98
7	KARMA OCP	6/2009	03/2014	N.A.	03/2014	162.46	162.46
8	Hyderabad-Vijaywada Km. 40 to 221.50 Km	4/2010	10/2012	N.A.	10/2012	1740	1740
9	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh.	4/2010	03/2016	N.A.	03/2016	2619.02	2913.51
10	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR)	4/2008	03/2014	N.A.	03/2014	653.19	653.46
11	Ahmedabad Redevelopment	11/2010	12/2014	N.A.	12/2014	1916.1	1916.1
12	DEOLI-KOTA	1/2011	07/2013	N.A.	07/2013	953	593
13	JALLARAM SHAFT PROJECT	3/2013	03/2013	N.A.	03/2013	467.78	467.78
14	Batura OCP (2.0 MTY)	9/2008	03/2015	N.A.	03/2015	203.82	203.82
15	Kistaram OCP	11/2010	03/2015	N.A.	03/2015	242.29	242.29
16	PELMA OCP(10.00MTY)	7/2008	03/2015	N.A.	03/2015	448.32	448.32
17	KARTALI (EAST) OC	7/2008	03/2014	N.A.	03/2014	178.44	178.44
18	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	03/2016	N.A.	03/2016	150.59	198.59
19	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU	4/2010	01/2015	N.A.	01/2015	4404.57	4404.57
20	Development of WO-16 Cluster Fields	6/2010	01/2014	N.A.	01/2014	2523	2523
21	Ankleswar Redevelopment	11/2010	12/2014	N.A.	12/2014	2189.63	2189.63
22	Mehesana Redevelopment	11/2010	04/2015	N.A.	04/2015	3823	3823
23	PETROCHEMICAL COMPLEX-II AT VIJAYPUR	8/2010	02/2014	N.A.	02/2014	8140	8140

	AND PATA						
24	New Line from Dimapur to Zubza(Kohima) national project (NEFR)	4/2006	03/2015	N.A.	03/2015	850	850
25	AGARTALA SABROOM, NL, NEFR	4/2008	03/2014	N.A.	03/2014	813.34	1141.75
26	SEVOK RANGPO, NEFR	4/2008	12/2015	N.A.	12/2015	1339.48	3380.58
27	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR)	4/2008	03/2014	N.A.	03/2014	516.23	516.23
28	NANGALDAM-TALWARA(NL),NR	3/1981	07/2012	07/2012	07/2012	37.68	730
29	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	4/1995	12/2012	N.A.	12/2012	304	968.6
30	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP)	4/2010	03/2016	N.A.	03/2016	3951.98	3951.98
31	Udhna-Jalgaon with electrification(doubling) (WR)	4/2008	03/2014	N.A.	03/2014	1389.62	1389.62
32	Ahmedabad-Himmatnagar-Udaipur (WR)	4/2008	03/2013	N.A.	03/2013	394.14	394.14
33	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	2/2011	11/2012	N.A.	11/2012	193.45	193.45
34	PANIPAT-ROHTAK	4/2011	10/2014	N.A.	10/2014	807	807
35	MURADABAD-BAREILY	4/2010	06/2013	N.A.	06/2013	1267	1267
36	4 LANING OF NAGPUR-BETUL	2/2011	08/2014	N.A.	08/2014	2498.76	2498.76
37	PUNE-SATARA(NH-4)	10/2010	03/2013	N.A.	03/2013	1724.55	1724.55
38	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	9/2010	03/2013	N.A.	03/2013	852	852
39	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	05/2013	N.A.	05/2013	1585	1585
40	Gujarat/Maharashtra BorderSurat-Hazira Port Section	3/2010	09/2012	N.A.	09/2012	1509.1	1509.1
41	Hazaribagh-Ranchi	8/2010	01/2013	N.A.	01/2013	625.07	625.07
42	Indore-Jhabua-Gujrat/MP	10/2010	04/2013	N.A.	04/2013	1175	1175
43	Jaipur-Tonk-Deoli	6/2010	12/2012	N.A.	12/2012	792.06	792.06
44	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4	9/2010	09/2013	N.A.	09/2013	1655	1655
45	Wax Project	6/2010	12/2013	12/2013	12/2013	576.6	576.6
46	KUSMUNDA EXPN.OCP(SECL)(10MTY)	6/2006	03/2013	03/2013	03/2013	737.65	1188.31

47	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	1/2010	01/2013	N.A.	01/2013	1292.84	1292.84
48	DELHI MRTS PHASE-III	9/2011	03/2016	N.A.	03/2016	35242	35242
49	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS	8/2008	09/2012	N.A.	09/2012	1066.91	968.35
50	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy	10/2010	02/2014	N.A.	02/2014	966.46	994.82
51	Acquistion of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd.	10/2010	12/2013	N.A.	12/2013	1028.1	1028.1
52	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	6/2011	03/2018	03/2018	03/2018	1131.28	1131.28
53	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A	12/2011	08/2014	N.A.	08/2014	2422.66	2422.66
54	Rajrappa RCE OCP	12/2009	03/2016	N.A.	03/2016	510.85	510.85
55	Himmatnagar - Udaipur Gauge Canvession (NWR)	4/2008	03/2015	N.A.	03/2015	829.74	829.74
56	KANIHA OCP, MCL, (10.0 Mty)	12/2007	03/2013	N.A.	03/2013	457.77	457.77
57	MANIKPUR OC EXPANTION	11/2009	03/2014	03/2014	03/2014	321.42	321.5
58	BHUBANESWARI OCP, MCL (20.0 Mty)	12/2007	03/2017	03/2017	03/2017	490	490.1
59	GOPAL PRASAD OCP	2/2008	03/2015	N.A.	03/2015	395.87	395.87
60	TALABIRA OCP	3/2008	03/2016	N.A.	03/2016	447.72	447.72
61	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	03/2013	N.A.	03/2013	475.93	479.53
62	BINA EXTN. PROJ(6.0 Mtpa)	11/2006	03/2014	03/2014	03/2014	168.97	168.97
63	RKP OCP PHASE-I	3/2010	03/2015	N.A.	03/2015	209.78	209.78
64	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH	7/2011	07/2013	N.A.	07/2013	181.93	181.93
65	GAGAN PROJECT	9/2008	06/2013	N.A.	06/2013	626	626
66	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	01/2014	N.A.	01/2014	202.94	202.94
67	CONVERSION OF RIG	3/2011	05/2013	N.A.	05/2013	861.79	756.65

	SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)						
68	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	07/2015	N.A.	07/2015	1987	1987
69	NASHRI CHANANI	6/2010	06/2015	N.A.	06/2015	2159	2159
70	PATNA-MUZZAFFARPUR	8/2010	02/2013	N.A.	02/2013	671.3	671.3
71	4 LANNING OF AHMEDABAD TO GODHARA	12/2010	06/2013	N.A.	06/2013	1008.5	1008.5
72	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	3/2011	08/2013	N.A.	08/2013	785.5	785.5
73	ROHTAK-BAWAL	5/2011	11/2013	N.A.	11/2013	650	650
74	GHAZIABAD-ALIGARH NH- 91	2/2011	08/2013	N.A.	08/2013	1141	1141
75	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	6/2011	12/2013	N.A.	12/2013	535	535
76	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013	N.A.	12/2013	1250	1250
77	DEVELOPMENT OF ADIQUE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	06/2013	N.A.	06/2013	600	600
78	FARIDABAD EXTENSION	9/2011	09/2014	N.A.	09/2014	2494	2494
79	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	8/2011	12/2013	N.A.	12/2013	1391.97	1391.97
80	2 Laning of Muzaffarpur - Sonbarsa	5/2011	11/2013	N.A.	11/2013	511.54	511.54
81	Kandla - Mundra port	1/2011	07/2013	N.A.	07/2013	953.88	953.88
82	Two laning of Trichy - Karaikudi and Trychi Bypass	5/2010	05/2013	N.A.	05/2013	374	374
83	2 laning of Dindigul - Perigulam Theni- kumili	9/2011	08/2013	N.A.	08/2013	485	485
84	Tirupati - Tiruthani - Chennai	4/2011	10/2013	N.A.	10/2013	571	571
85	SAMAIKHALI - GANDHIDHAM	9/2010	03/2013	N.A.	03/2013	805.39	805.39
86	Muraidih UG Turn-key Project	2/2011	04/2014	N.A.	04/2014	339.88	339.88
87	Moonidih XV Seam UG	8/2011	04/2015	N.A.	04/2015	1230.27	1230.27
88	Assam gas Cracker project	4/2006	12/2013	12/2013	12/2013	5460.61	8920
89	Butadiene Extraction Unit(BDEU) at Panipat	11/2009	02/2013	N.A.	02/2013	341.5	341.5

90	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	7/2010	01/2013	N.A.	01/2013	1000	1000
91	PARADIP-RAIPUR-SAMBALPUR- RANCHI PIPELINE	8/2009	09/2012	09/2012	09/2012	1793	1400
92	Construction of tanks and blending facility at Vadinar	2/2009	09/2012	09/2012	09/2012	267	267
93	COKE OVEN BATTERY NO. 4 PHASE-II	8/2007	10/2012	10/2012	10/2012	108	216.68
94	Integrated crude Oil handling facilities at Paradip(2nd SPM)	12/2009	06/2012	06/2012	06/2012	1492.33	1300
95	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	4/2008	04/2013	04/2013	04/2013	825	1827
96	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW)	6/2011	12/2015	N.A.	12/2015	5907.11	5907.11
97	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	1/2010	01/2013	01/2013	01/2013	1478.63	1478.63
98	JALAGAM VENGALA RAO OCP	7/2011	03/2015	N.A.	03/2015	447.06	447.06
99	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH	2/2012	02/2015	N.A.	02/2015	1310.85	1310.85
100	JORBAT - BARAPANI	1/2011	01/2014	N.A.	01/2014	536	536
101	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	03/2015	N.A.	03/2015	162.76	162.76
102	2-LANNING OF SHILONG BYPASS	2/2011	02/2014	N.A.	02/2014	226	226
103	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	03/2014	N.A.	03/2014	2848	2848
104	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	05/2014	N.A.	05/2014	1535	1535
105	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	03/2014	N.A.	03/2014	574	574
106	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	04/2014	N.A.	04/2014	375.09	375.09
107	4-LANNING OF CHAPRA-HAJIPUR	1/2011	07/2013	N.A.	07/2013	575	575
108	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	N.A.	11/2013	511.54	511.54
109	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN	3/2012	09/2014	N.A.	09/2014	198.63	198.63

	REGION						
110	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS ASSOCIATED WITH SYSTEM STRENGTHENING COMMO	3/2012	03/2014	N.A.	03/2014	213.78	213.78
111	Integrated Development of B-127 fields	12/2011	03/2015	N.A.	03/2015	2059.63	2059.63
112	Heera and South Heera Redevelopment Ph-II	3/2012	05/2015	N.A.	05/2015	5608.4	5608.4
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	11/2011	11/2014	N.A.	11/2014	723.63	723.63
114	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	03/2016	N.A.	03/2016	258.56	258.56
115	SRINAGAR TO BANIHAL	6/2011	06/2014	N.A.	06/2014	1100.7	1100.7
116	2laning with PS Gopalganj-Chappra	12/2011	05/2014	N.A.	05/2014	325	325
117	4-laning of Barhi-Hazaribagh	2/2012	02/2014	N.A.	02/2014	398	398
118	BHOPAL-SANCHI	10/2011	01/2013	N.A.	01/2013	209	209
119	PUNE-SHOLAPUR,Pkg-II	9/2011	01/2014	N.A.	01/2014	835	835
120	NIROLI-ROXY-RAJAMUNDA	7/2011	01/2014	N.A.	01/2014	586	586
121	BHUBANESWAR TO PURI	3/2011	08/2013	N.A.	08/2013	500.29	500.29
122	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	11/2011	05/2014	N.A.	05/2014	909	909
123	PANIKHOLI-RIMOLI	3/2012	09/2014	N.A.	09/2014	1410	1410
124	JAIPUR-REENGUS	8/2010	02/2013	N.A.	02/2013	267.81	267.81
125	BEAWAR-PALI-PINDWARA	12/2011	06/2014	N.A.	06/2014	2388	2388
126	BAREILY-SITAPUR	3/2011	09/2013	N.A.	09/2013	1046	1046
127	MUZAFFARNAGAR-HARIDWAR	9/2011	03/2013	N.A.	03/2013	754	754
128	4-laning of Faraka-Raiganj	2/2011	08/2013	N.A.	08/2013	1078.84	1078.84
129	4-laning of Brahampore-Faraka	2/2011	08/2013	N.A.	08/2013	998.79	998.79
130	4-laning of Raiganj-Dalkola	2/2011	08/2013	N.A.	08/2013	580.43	580.43
131	six laning of Chandikhol-Jagatpur-Bhubaneswar	12/2011	06/2014	N.A.	06/2014	1047	1047
132	Development of Western Periphery of MH South Field	4/2012	12/2014	N.A.	12/2014	600.17	600.17
133	Pipeline Replacement Project-3	4/2012	05/2014	N.A.	05/2014	2547.26	2547.26

List of Delay Project

(May, 2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, Tamil Nadu	12/2001	13,171.00	15,824.00	14,755.00	12/2008	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL, Gujarat	10/2009	11,459.00	11,459.00	1,714.00	12/2015	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL, Rajasthan	10/2009	12,320.00	12,320.00	1,018.00	12/2016	03/2017	3	-
Total			36,950.00	39,603.00	17,487.00				
<u>Civil Aviation</u>									
4	Construction of New International Terminal Building - [N04000069]AAI, Goa	05/2010	335.61	335.61	111.25	05/2012	08/2012	3	-
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI, West Bengal	08/2008	1,942.51	2,325.00	1,966.18	05/2011 03/2012	10/2012	17	7
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI, Sikkim	01/2009	309.46	309.46	182.98	01/2011 04/2013	04/2013	27	0
Total			2,587.58	2,970.07	2,260.41				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,412.12	06/2009	03/2013	45	-
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL, Jharkhand	04/2006	471.66 341.63	341.63	108.58	03/2011 03/2012	03/2013	24	12
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, Uttar Pradesh	05/2006	789.88 741.62	741.62	331.78	03/2010	03/2013	36	-
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, Andhra Pradesh	12/2009	418.97	418.97	89.45	03/2012	03/2013	12	-

List of Delay Project

(May, 2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, Andhra Pradesh	03/2010	181.19 -	181.19	36.96	03/2012 -	03/2013	12	-
12	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, Orissa	01/2005	302.96 -	302.96	92.54	03/2010 -	03/2014	48	-
13	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,365.35	03/2010 -	03/2014	48	-
14	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL, Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,163.51	03/2010 -	03/2014	48	-
15	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC, Tamil Nadu	05/2008	4,904.54 -	4,909.54	2,883.23	03/2012 -	03/2014	24	-
16	RAJMAHAL OC EXP. - [N06000056]ECL, Multi State	02/2006	50.08 -	153.82	23.72	03/2011 -	03/2014	36	-
17	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL, Orissa	08/2008	207.28 -	207.28	100.06	03/2012 -	03/2014	24	-
18	Churi Benti UG - [N06000083]CCL, Jharkhand	06/2007	163.51 -	163.51	34.45	03/2011 03/2012	03/2014	36	24
19	North Urimari OCP - [N06000084]CCL, Jharkhand	12/2007	179.87 -	179.87	60.66	03/2012 03/2012	03/2014	24	24
20	Tapin OCP - [N06000086]CCL, Jharkhand	08/2008	264.68 -	264.68	101.73	03/2012 03/2013	03/2014	24	12
21	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, Andhra Pradesh	09/2006	212.34 779.26	779.26	281.16	03/2013 09/2012	10/2014	19	25
22	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, Madhya Pradesh	06/2006	746.04 535.10	535.10	161.80	03/2012 03/2015	03/2015	36	0
23	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48	-
24	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, Madhya Pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36	-
25	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL, Orissa	12/2007	172.08 -	172.08	101.88	03/2010 -	03/2015	60	-

List of Delay Project

(May, 2012)

		Date of Commissioning						Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
26	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	72.38	12/2012 -	03/2015	27	-
27	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2015	12	-
28	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	328.96	03/2014 03/2016	03/2016	24	0
29	MAGADH OC (CCL) - [N06000015]JCL,Jharkhand	07/2006	469.78 706.40	706.40	19.23	07/2012 03/2014	03/2016	44	24
30	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	260.92	03/2014 03/2014	03/2016	24	24
31	BAROUD OC EXPANSION - [N06000065]SECL,Chhatisgarh	07/2008	135.58 -	258.56	38.92	03/2015 -	03/2016	12	-
32	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
Total			17,944.10 -	21,061.68	10,071.41				
Fertilisers									
33	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	239.87	07/2011 -	07/2012	12	-
Total			438.00 -	438.00	239.87				
Steel									
34	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 -	232.93	191.83	05/2011 -	05/2012	12	-
35	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	242.28	08/2010 08/2010	08/2012	24	24
36	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	247.41	02/2011 02/2011	09/2012	19	19

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
37	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,545.71	10/2009 10/2012	10/2012	36	0
38	Bailadila Iron Ore Deposit-IIB(NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	330.20	12/2011 03/2012	10/2012	10	7
39	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	450.00	196.32	05/2012 05/2012	02/2013	9	9
40	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	866.76	12/2012 -	03/2013	3	-
41	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL, Maharashtra	12/2011	187.33 -	187.33	-	10/2013 -	12/2013	2	-
Total			13,253.15	17,337.01	11,620.51				
<u>Petroleum</u>									
42	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	625.59	05/2010 04/2012	06/2012	25	2
43	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	210.72	03/2012 03/2012	06/2012	3	3
44	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,467.35	05/2010 05/2012	07/2012	26	2
45	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	829.98	07/2010 05/2012	07/2012	24	2
46	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	211.24	04/2011 -	07/2012	15	-
47	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 252.37	204.00	169.73	01/2012 -	07/2012	6	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
48	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL, Multi State	06/2009	348.00 -	261.00	193.68	03/2012 08/2012	08/2012	5	0
49	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,733.00	03/2012 08/2012	08/2012	5	0
50	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	714.11	04/2011 12/2011	09/2012	17	9
51	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,156.52	09/2011 03/2012	09/2012	12	6
52	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,653.57	01/2012 -	09/2012	8	-
53	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19	17
54	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	1,803.78	570.26	07/2012 -	10/2012	3	-
55	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	12/2012	80	6
56	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	1,017.31	06/2012 -	12/2012	6	-
57	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	288.04	144.02	08/2012 -	12/2012	4	-
58	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	302.26	19.21	09/2012 -	12/2012	3	-
59	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	327.30	12/2011 -	01/2013	13	-
60	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84	0
61	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,939.45	05/2010 03/2013	03/2013	34	0

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	8
62	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	460.70	231.69	07/2012 07/2012	03/2013	8	8
63	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
64	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,278.73	09/2010 03/2012	04/2013	31	13
65	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03 -	3,241.03	219.80	03/2013 -	04/2013	1	-
66	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	372.11	40.52	03/2013 -	04/2013	1	-
67	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	04/2013	10	-
68	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	2,915.00	927.98	12/2012 12/2012	04/2013	4	4
69	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38	14
70	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	410.44	7.33	11/2012 -	05/2013	6	-
71	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00 -	30,426.00	15,728.00	11/2012 -	06/2013	7	-
72	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	08/2013	23	-
73	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	6,855.93	3,456.81	09/2012 -	09/2013	12	-
74	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-

List of Delay Project

(May, 2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
75	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,531.71	08/2010 03/2012	12/2013	40	21
76	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5	-
77	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC, Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84	0
78	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	761.10	03/2013 -	03/2014	12	-
79	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50	-
80	Development of C-26 Cluster Fields - [N16000133]ONGC, Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	03/2015	10	-
81	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30	-
82	IOR GELEKI (ONGCL) - [160100216]ONGC, Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120	0
	Total		111,428.46	121,252.68	63,534.71				
	Power								
83	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC, Chhatisgarh	12/2003	8,323.39 -	8,323.39	8,230.00	12/2009 12/2011	05/2012	29	5
84	CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.	08/2005	1,405.63 -	2,084.00	1,824.71	08/2010 08/2011	06/2012	22	10
85	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT (P.G.R.) - [180100260]PGCIL, Bihar	12/2005	3,779.46 -	3,779.46	3,681.30	09/2009 -	06/2012	33	-
86	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC, West Bengal	10/2003	768.92 -	1,628.39	1,488.49	03/2007 -	09/2012	66	-
87	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC, J and K	08/2006	621.26 -	621.28	737.92	02/2011 -	10/2012	20	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
88	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL, Multi State	10/2006	975.96 -	975.96	832.00	10/2009 -	12/2012	38	-
89	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC, Uttarakhal	06/2006	2,895.10 -	2,895.10	690.00	11/2011 -	12/2012	13	-
90	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL, Rajasthan	07/2006	5,221.23 -	5,221.23	3,125.70	07/2010 -	12/2012	29	-
91	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC, Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,816.32	10/2010 12/2011	01/2013	27	13
92	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC, J and K	08/2006	611.01 -	936.00	751.75	08/2010 09/2011	01/2013	29	16
93	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC, J and K	08/2005	1,729.29 -	1,794.00	1,729.07	11/2009 11/2011	02/2013	39	15
94	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL, Himachal Pr.	07/2006	557.24 -	557.24	549.10	01/2010 -	02/2013	37	-
95	MOUDA STPP (NTPC) - [N18000048]NTPC, Maharashtra	11/2008	5,459.28 -	6,010.89	4,116.00	08/2012 -	03/2013	7	-
96	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC, Madhya Pradesh	01/2009	5,915.00 -	5,915.00	3,421.00	10/2012 -	03/2013	5	-
97	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,200.00	10/2012 -	03/2013	5	-
98	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38 -	1,501.75	1,134.42	09/2009 -	06/2013	45	-
99	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,658.86	01/2012 -	09/2013	20	-
100	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,281.00	04/2009 03/2014	03/2014	59	0
101	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO, Arunachal Pr.	12/2008	573.99 -	573.99	331.39	08/2012 08/2013	09/2014	25	13

List of Delay Project

(May, 2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
102	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, Mizoram	01/2011	913.63 -	913.63	313.71	01/2014 02/2015	02/2015	13	0
103	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttarakhal	11/2006	2,978.48 -	2,978.48	1,467.00	03/2013 -	09/2015	30	-
104	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	325.98	07/2010 02/2016	02/2016	67	0
105	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97 -	8,693.00	7,004.00	12/2009 12/2014	03/2016	75	15
106	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttarakhal	08/2008	2,491.58 2,491.58	3,422.44	306.16	07/2014 -	05/2016	22	-
107	KISHANGANGA HEP - [N18000031]NHPC, J and K	07/2007	2,238.67 3,642.04	3,642.00	1,462.21	01/2016 01/2016	11/2016	10	10
108	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,666.41	09/2010 08/2014	12/2016	75	28
109	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90 -	2,496.00	1,859.60	05/2013 06/2016	03/2017	46	9
110	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,445.63	09/2009 07/2014	12/2017	99	41
Total			86,681.84 -	99,654.08	65,449.73				
<u>Railways</u>									
111	MUZAFFARPUR-SITAMARHI(NL), ECR - [220100194]ECR, Bihar	04/1997	100.00 483.62	484.03	456.36	03/2012 03/2012	06/2012	3	3
112	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 501.69	1,043.60	636.03	03/2012 06/2012	06/2012	3	0
113	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat	04/2006	196.97 -	196.97	216.85	03/2011 -	06/2012	15	-
114	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR, Karnataka	04/1996	157.00 262.82	262.82	229.99	03/2012 03/2012	10/2012	7	7

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
115	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	292.01	06/2004 -	12/2012	102	-
116	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	409.77	03/2012 03/2012	12/2012	9	9
117	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	1,115.63	711.40	03/2009 12/2012	12/2012	45	0
118	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,284.98	10/2007 12/2012	12/2012	62	0
119	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20 -	687.20	595.56	03/2010 -	12/2012	33	-
120	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	873.69	12/2012 01/2013	01/2013	1	0
121	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	551.09	03/1995 -	03/2013	216	-
122	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	263.53	03/2012 03/2013	03/2013	12	0
123	MANSI-PURNA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	382.09	03/2012 03/2013	03/2013	12	0
124	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh	04/2008	603.04 -	603.04	64.13	03/2012 -	03/2013	12	-
125	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, Orissa	04/1999	166.16 -	243.40	248.52	02/2009 02/2009	04/2013	50	50
126	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41 207.00	225.00	206.01	03/2009 03/2009	04/2013	49	49
127	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52 -	207.52	126.13	12/2012 -	05/2013	5	-
128	Ghutiasharif-Canning (ER) - [N22000117]ER, West Bengal	04/2009	189.97 611.03	611.03	89.65	12/2011 11/2013	11/2013	23	0
129	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	39.12	02/2006 -	12/2013	94	-
130	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam	04/1996	1,676.31 -	4,073.53	3,083.48	03/2009 -	12/2013	57	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
131	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 393.46	499.16	163.52	03/2007 03/2007	03/2014	84	84
132	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00 -	1,655.81	1,141.55	12/2008 -	03/2014	63	-
133	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, Tamil Nadu	04/2006	495.74 -	495.74	152.82	06/2013 06/2013	03/2014	9	9
134	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90 -	223.01	105.81	12/2012 -	03/2014	15	-
135	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00 -	820.40	146.21	03/2010 06/2014	06/2014	51	0
136	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR, Bihar	09/2001	100.00 492.98	1,041.79	728.94	12/2010 12/2010	03/2015	51	51
137	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 -	2,393.48	4.57	04/2014 -	03/2015	11	-
138	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	329.78	03/2013 -	03/2015	24	-
139	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92	21
140	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	1,412.74	433.94	03/2005 12/2008	12/2015	129	84
141	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 -	4,444.00	797.35	03/2011 03/2014	03/2016	60	24
142	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	5,300.00	698.48	03/2014 03/2016	03/2016	24	0
143	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	2,069.60	24.60	03/2014 03/2016	03/2016	24	0
144	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,086.41	408.72	06/2005 07/2011	06/2016	132	59

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
145	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	21.98	03/2016 -	06/2016	3	-
146	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 -	20,000.00	7,939.79	03/2001 -	12/2017	201	-
Total			25,088.86 -	62,483.10	26,266.55				
<u>Road Transport & Highways</u>									
147	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27 -	193.10	161.44	03/2008 -	05/2012	50	-
148	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00	383.29	12/2008 -	05/2012	41	-
149	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya Pradesh	12/2003	225.00 -	225.00	261.98	10/2008 -	05/2012	43	-
150	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	190.00	256.19	01/2009 -	06/2012	41	-
151	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	278.86	11/2008 -	06/2012	43	-
152	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	263.27	265.81	02/2004 -	06/2012	100	-
153	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,480.90	10/2011 -	06/2012	8	-
154	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,648.00	08/2011 -	06/2012	10	-
155	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00 -	388.00	506.40	05/2012 -	06/2012	1	-
156	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00 -	241.53	116.80	04/2004 -	07/2012	99	-

List of Delay Project

(May,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
157	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	166.30	185.05	03/2008 -	07/2012	52	-
158	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	188.72	02/2004 -	07/2012	101	-
159	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	07/2012	5	-
160	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	177.04	08/2004 07/2010	08/2012	96	25
161	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	182.88	08/2004 -	08/2012	96	-
162	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	197.27	05/2008 -	08/2012	51	-
163	SAGAR BY PASS,KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	180.94	10/2008 -	08/2012	46	-
164	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	304.26	09/2007 -	09/2012	60	-
165	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	273.02	09/2007 -	09/2012	60	-
166	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	225.24	06/2005 -	09/2012	87	-
167	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.31	10/2008 -	09/2012	47	-
168	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	253.74	10/2008 -	09/2012	47	-
169	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	966.77	05/2012 -	09/2012	4	-
170	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	10/2012	91	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
171	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60 -	407.60	185.52	06/2010 -	10/2012	28	-
172	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	10/2012	37	-
173	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16	-
174	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2012	5	-
175	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	11/2012	41	-
176	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	340.68	377.71	03/2008 -	12/2012	57	-
177	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	225.00	275.76	06/2008 -	12/2012	54	-
178	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	240.61	06/2008 -	12/2012	54	-
179	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	371.31	09/2008 -	12/2012	51	-
180	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	203.43	229.13	10/2008 -	12/2012	50	-
181	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	302.00	10/2008 -	12/2012	50	-
182	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	180.10	07/2008 -	12/2012	53	-
183	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00	500.97	09/2008 -	12/2012	51	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
184	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	273.65	06/2008 -	12/2012	54	-
185	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	142.77	04/2008 -	12/2012	56	-
186	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	363.00	248.66	06/2011 06/2011	12/2012	18	18
187	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	203.08	04/2008 -	12/2012	56	-
188	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	259.16	04/2008 -	12/2012	56	-
189	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	12/2012	48	-
190	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	189.55	04/2010 -	12/2012	32	-
191	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93 -	300.93	302.72	10/2009 -	12/2012	38	-
192	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	494.29	12/2009 -	12/2012	36	-
193	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	467.78	09/2009 -	12/2012	39	-
194	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	251.79	09/2010 -	12/2012	27	-
195	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	535.00	01/2011 -	12/2012	23	-
196	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	579.90	05/2010 -	12/2012	31	-
197	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	1,141.10	07/2012 -	12/2012	5	-
198	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	12/2012	6	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
199	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25	-
200	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	196.85	09/2007 -	03/2013	66	-
201	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	118.85	09/2008 -	03/2013	54	-
202	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	240.00	285.56	10/2008 -	03/2013	53	-
203	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	263.00	02/2009 -	03/2013	49	-
204	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	106.74	04/2009 -	03/2013	47	-
205	BIJNI TO ASSAM WB BORDER (NH- 31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	199.07	06/2008 -	03/2013	57	-
206	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	281.81	06/2008 -	03/2013	57	-
207	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60	-
208	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	226.70	06/2008 -	03/2013	57	-
209	DHARAMTUL TO SONAPUR, KM 205-183 (AS- 20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	164.42	05/2008 -	03/2013	58	-
210	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	223.78	06/2008 -	03/2013	57	-
211	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	733.12	07/2010 -	03/2013	32	-
212	AGRA-BYPASS(NS-1/UP- 1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	151.69	09/2007 -	06/2013	69	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
213	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	663.32	10/2011 -	06/2013	20	-
214	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	996.43	11/2012 -	06/2013	7	-
215	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	54.25	04/2009 -	07/2013	51	-
216	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	85.39	11/2008 -	07/2013	56	-
217	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,458.50	11/2011 -	08/2013	21	-
218	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-
219	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	10.00	11/2008 -	01/2014	62	-
220	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	344.12	05/2013 -	02/2014	9	-
221	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	170.23	10/2008 -	03/2014	65	-
222	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	242.93	10/2011 -	03/2014	29	-
223	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19	-
224	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	163.93	05/2013 -	03/2014	10	-
225	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	21.81	09/2007 -	04/2014	79	-
226	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	35.95	07/2009 -	04/2014	57	-
227	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	15.15	02/2014 -	04/2014	2	-
228	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-

List of Delay Project

(May, 2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
229	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	-	09/2013 -	07/2014	10	-
230	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
Total			33,500.51 -	35,578.84	36,630.05				
<u>Shipping & Ports</u>									
231	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Mahara shtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8	0
232	Acquisition of two nos. of 120 B. P BY 079& 080 - [N25000042]SHIPP.,Mahara shtra	04/2009	290.85 -	305.00	86.46	06/2011 09/2012	09/2012	15	0
233	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,245.60	01/2012 09/2012	09/2012	8	0
234	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Mahara shtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18	0
235	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
236	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	772.87	12/2010 -	12/2012	24	-
237	Construction of berthing and allied facilities off - [N25000037]PORT TRUST, Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
238	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
239	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Mahara shtra	08/2010	612.72 627.64	627.64	187.07	12/2012 05/2013	05/2013	5	0

List of Delay Project

(May,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
240	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93	-
	Total		8,446.14	10,038.71	5,019.11				
			-						
	<u>Telecommunications</u>								
241	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	06/2012	78	51
242	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	229.04	12/2008 -	06/2012	42	-
243	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	06/2012	36	-
244	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2012	41	-
245	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	06/2012	39	-
246	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	804.06	11/2010 -	06/2012	19	-
247	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	06/2012	42	-
248	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.93	10/2010 03/2012	07/2012	21	4
249	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72	11
	Total		3,163.25	3,167.12	1,662.65				
			-						
	<u>Urban Development</u>								
250	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15	-

List of Delay Project

(May, 2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
Total			6,395.00	11,609.00	2,267.57				
<u>Water Resources</u>									
251	PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60	-
Total			542.90	1,187.00	35.49				
Grand Total			346,419.79	426,380.29	242,545.06				

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 04/2011	04/2012	0/0
	Total		1,106.29 -			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	08/2012	0/0
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 03/2012	10/2012	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	04/2013	0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
	Total		5,021.58 -			0/0
<u>Coal</u>						
7	KARMA OCP - [N06000088]JCL,Jharkhandd	06/2009	162.46 -	03/2014 -	03/2014	0/0
8	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	04/2014 -	04/2014	0/0
9	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	03/2012 03/2015	03/2015	0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
11	BAROUD OC EXPANSION - [N06000065]SECL,Chhatisgarh	07/2008	135.58 -	03/2015 -	03/2016	0/0
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	03/2016 -	03/2016	0/0
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 03/2018	03/2018	0/0
	Total		4,004.07 -			0/0
<u>Fertilisers</u>						
14	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012	0/0
15	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
Total			763.00			0/0
			-			
<u>Steel</u>						
16	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL,Maharashtra	12/2011	187.33	10/2013	12/2013	0/0
			-	-		
17	INSTALLATION OF 45MVA SAF AT CHANDRAPUR FERRO PLANT(CFP) - [N12000077]SAIL,Maharashtra	12/2011	187.33	10/2013	12/2013	0/0
			-	-		
Total			374.66			0/0
			-			
<u>Petroleum</u>						
18	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	02/2011	08/2011	0/0
			299.00	08/2011		
19	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40	05/2010	06/2012	0/0
			837.54	04/2012		
20	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29	05/2010	07/2012	0/0
			6,326.40	05/2012		
21	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21	07/2010	07/2012	0/0
			1,456.96	05/2012		
22	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	04/2011	07/2012	0/0
			-	-		
23	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	09/2011	09/2012	0/0
			2,730.00	03/2012		
24	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	01/2012	09/2012	0/0
			12,160.26	-		
25	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	09/2012	09/2012	0/0
			-	09/2012		
26	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70	03/2011	10/2012	0/0
			755.76	05/2011		
27	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	07/2012	10/2012	0/0
			-	-		
28	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	04/2006	12/2012	0/0
			2,735.65	06/2012		
29	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	06/2012	12/2012	0/0
			-	-		
30	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04	08/2012	12/2012	0/0
			288.04	-		
31	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	09/2012	12/2012	0/0
			-	-		
32	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	12/2011	01/2013	0/0
			-	-		
33	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	05/2010	03/2013	0/0
			8,813.41	03/2013		

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
34	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
35	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
36	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	04/2013	0/0
37	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
38	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	04/2013	0/0
39	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
40	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	05/2013	0/0
41	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
42	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	08/2013	0/0
43	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
44	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
45	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
46	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
47	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
48	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
49	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0
50	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
51	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
52	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
53	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
54	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
55	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
56	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
57	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
58	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	03/2015	0/0
59	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
60	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
61	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0
62	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	09/2011 -	-	0/0
63	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
	Total		104,465.54 -			0/0
Power						
64	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	04/2012	0/0
65	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 -	06/2013	0/0
66	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
67	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	01/2012 -	09/2013	0/0
68	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97 -	12/2013 -	12/2013	0/0
69	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
70	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	06/2014 -	06/2014	0/0
71	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	06/2014 -	06/2014	0/0
72	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
73	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	08/2014 -	08/2014	0/0
74	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	08/2014 -	08/2014	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
75	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
77	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	01/2014 02/2015	02/2015	0/0
78	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
Total			12,057.69 -			0/0
<u>Railways</u>						
79	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	02/2015	0/0
80	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	12/2012	0/0
81	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	07/2005 -	07/2005	0/0
82	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
83	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
84	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
85	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
86	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	- 03/2010	03/2010	0/0
87	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010	0/0
88	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2010	0/0
89	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
90	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
91	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
92	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
93	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
94	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
95	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
96	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	03/2011 03/2011	03/2011	0/0
97	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
98	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
99	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011	0/0
100	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
101	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011	0/0
102	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	02/2010 -	11/2011	0/0
103	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
104	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011	0/0
105	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
106	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012	0/0
107	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
108	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
109	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
110	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2012	0/0
111	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2012	0/0
112	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
113	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
114	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2012	0/0
115	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012	0/0
116	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
117	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
118	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
119	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012	0/0
120	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	06/2011 03/2012	03/2012	0/0
121	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
122	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
123	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	03/2012 -	03/2012	0/0
124	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012	0/0
125	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	03/2012 03/2012	06/2012	0/0
126	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012	0/0
127	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 06/2012	06/2012	0/0
128	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	06/2012	0/0
129	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 07/2012	07/2012	0/0
130	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	10/2012	0/0
131	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	06/2004 -	12/2012	0/0
132	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	12/2012 12/2012	12/2012	0/0
133	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
134	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	03/2009 12/2012	12/2012	0/0
135	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	10/2007 12/2012	12/2012	0/0
136	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
137	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
138	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0
139	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
140	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	03/2013	0/0
141	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
142	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
143	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013	0/0
144	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	03/2012 03/2013	03/2013	0/0
145	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2013	0/0
146	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
147	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
148	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	03/2012 -	03/2013	0/0
149	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 -	03/2013 -	03/2013	0/0
150	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
151	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
152	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	12/2012 -	05/2013	0/0
153	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
154	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
155	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	02/2006 -	12/2013	0/0
156	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	03/2009 -	12/2013	0/0
157	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2014	0/0
158	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	12/2008 -	03/2014	0/0
159	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
160	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	03/2014	0/0
161	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	03/2014 -	03/2014	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
162	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	03/2014 -	03/2014	0/0
163	Suratpura - Hanumangarh - Sriganaganagar Gauge Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	03/2014 -	03/2014	0/0
164	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
165	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	12/2012 -	03/2014	0/0
166	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014	0/0
167	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
168	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
169	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015	0/0
170	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2015	0/0
171	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	03/2015	0/0
172	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2015	0/0
173	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	03/2015 -	03/2015	0/0
174	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	03/2015 -	03/2015	0/0
175	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
176	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	12/2015	0/0
177	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
178	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	03/2011 03/2014	03/2016	0/0
179	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
180	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
181	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
182	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	03/2016 -	03/2016	0/0
183	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
184	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
185	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 -	03/2001 -	12/2017	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
186	VIRAMGAM-BHILD(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
187	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
188	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-	0/0
189	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-	0/0
190	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
191	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
192	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-	0/0
193	KOTLPALI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.20	- -	-	0/0
194	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-	0/0
195	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
196	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
197	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
198	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
199	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-	0/0
200	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-	0/0
201	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-	0/0
202	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-	0/0
203	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-	0/0
204	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-	0/0
205	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-	0/0
206	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-	0/0
Total			64,531.38 -			0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Road Transport & Highways</u>						
207	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	05/2012	0/0
208	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	12/2008 -	05/2012	0/0
209	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	10/2008 -	05/2012	0/0
210	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	06/2012	0/0
211	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	06/2012	0/0
212	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	06/2012	0/0
213	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	06/2012	0/0
214	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	06/2012	0/0
215	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	05/2012 -	06/2012	0/0
216	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	07/2012	0/0
217	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	03/2008 -	07/2012	0/0
218	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	07/2012	0/0
219	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	07/2012	0/0
220	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	08/2012	0/0
221	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	08/2012	0/0
222	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	08/2012	0/0
223	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	10/2008 -	08/2012	0/0
224	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	09/2007 -	09/2012	0/0
225	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	09/2012	0/0
226	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	09/2012	0/0
227	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2012	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
228	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	09/2012	0/0
229	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	09/2012	0/0
230	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	09/2012	0/0
231	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	10/2012	0/0
232	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012	0/0
233	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	10/2012	0/0
234	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
235	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2012	0/0
236	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
237	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
238	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
239	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	12/2012	0/0
240	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	06/2008 -	12/2012	0/0
241	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
242	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
243	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
244	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
245	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0
246	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	12/2012	0/0
247	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2012	0/0
248	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
249	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
250	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
251	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	12/2012	0/0
252	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
253	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	12/2012	0/0
254	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2012	0/0
255	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2012	0/0
256	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0
257	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	01/2011 -	12/2012	0/0
258	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
259	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	12/2012	0/0
260	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	12/2012	0/0
261	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
262	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07 -	01/2013 -	01/2013	0/0
263	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	01/2013 -	01/2013	0/0
264	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	02/2013	0/0
265	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
266	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
267	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2013	0/0
268	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
269	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2013	0/0
270	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 -	03/2013	0/0
271	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
272	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	06/2008 -	03/2013	0/0
273	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	06/2008 -	03/2013	0/0
274	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	03/2008 -	03/2013	0/0
275	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	06/2008 -	03/2013	0/0
276	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	05/2008 -	03/2013	0/0
277	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	06/2008 -	03/2013	0/0
278	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
279	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
280	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
281	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
282	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	03/2013 -	03/2013	0/0
283	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
284	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
285	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
286	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	09/2007 -	06/2013	0/0
287	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
288	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
289	MURADABAD-BAREILY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
290	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
291	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
292	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
293	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
294	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
295	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	07/2013	07/2013	0/0
296	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	07/2013	07/2013	0/0
297	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	11/2011	08/2013	0/0
298	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	08/2013	08/2013	0/0
299	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
300	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	08/2013	08/2013	0/0
301	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	08/2013	08/2013	0/0
302	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
303	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	08/2013	08/2013	0/0
304	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	08/2013	08/2013	0/0
305	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
306	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
307	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
308	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
309	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
310	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
311	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
312	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	02/2010	12/2013	0/0
313	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
314	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
315	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	11/2008	01/2014	0/0
316	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	01/2014	01/2014	0/0
317	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	01/2014	01/2014	0/0
318	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00	01/2014	01/2014	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
319	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
320	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
321	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
322	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	03/2014	0/0
323	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
324	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2014	0/0
325	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
326	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
327	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
328	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
329	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
330	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
331	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
332	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
333	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
334	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
335	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
336	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
337	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
338	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
339	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
340	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
341	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
342	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
343	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
344	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
345	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
	Total		87,350.60 -			0/0
<u>Shipping & Ports</u>						
346	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008	0/0
347	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	11/2010	0/0
348	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
349	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	03/2012 -	03/2012	0/0
350	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 08/2012	08/2012	0/0
351	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 -	09/2012	0/0
352	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	06/2011 09/2012	09/2012	0/0
353	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	09/2012	0/0
354	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 10/2012	10/2012	0/0
355	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
356	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 -	12/2012	0/0
357	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
358	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
359	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0

List of Projects Without Milestones

(May,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
360	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 05/2013	05/2013	0/0
361	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	03/2006 -	12/2013	0/0
362	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013	0/0
363	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
	Total		16,087.68 -			0/0
Telecommunications						
364	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
365	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 03/2008	06/2012	0/0
366	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	06/2012	0/0
367	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	06/2012	0/0
368	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2012	0/0
369	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	06/2012	0/0
370	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	06/2012	0/0
371	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	12/2008 -	06/2012	0/0
372	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	07/2012	0/0
373	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2012	02/2013	0/0
374	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
375	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
376	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
377	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	08/2011	0/0

List of Projects Without Milestones

(May, 2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
378	Implementation of FTTH, the state of the art access, upon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -	03/2010 -	10/2010	0/0
	Total		6,161.00 -			0/0
<u>Urban Development</u>						
379	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
380	DELHI MRTS PHASE-III - [N28000056]DMRC, Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
381	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
<u>Water Resources</u>						
382	PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			340,316.57			0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
