

**295th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 Crores and above)
MAY, 2010**



Atomic Reactor



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-6
Summary of Projects	7-15
Graph	16-25
Sector wise analysis of projects	26-53

EXECUTIVE SUMMARY

The 295th Flash Report for May' 2010, that contains information on the status of 578 projects in the Central Sector, each costing Rs. 150 Crores and above. Since April' 2010, Flash report is prepared for the central sector projects costing Rs 150 Crores and above. During May' 2010, one project have reported completion and have been dropped from the monitor of this Ministry. During May' 2010, five projects , one project each of Coal, Petroleum, and Road Transport & Highways and two projects of Railways have shown improvement over the completion schedule reported earlier. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	135
2.	RAILWAYS	135
3.	POWER	84
4.	PETROLEUM	79
5.	COAL	39
6.	TELECOMMUNICATION	39
7.	STEEL	22
8.	SHIPPING & PORTS	22
9.	CIVIL AVIATION	8
10.	FERTILISERS	6
11.	ATOMIC ENERGY	4
12.	URBAN DEVELOPMENT	2
13.	MINES	1
14.	HEALTH & FW	1
15.	WATER RESOURCES	1
Total		578

2. One hundred eleven (111) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1 to 30 months in respect of projects relating to Atomic Energy, Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports and Telecommunications sectors.
3. In the **Atomic Energy sector**, Kaiga Units 3 and 4, Project (NPCIL) has shown additional delay of 2 months due to the continued problem of non availability of fuel. Kudankulam APP (NPCIL) has reported additional delay of 3 months due to slippage in commitment by M/s Atom Stroy Export (ASE), Russia.

4. In the **Coal sector**, 3 projects have reported additional delays in the range of 12-24 months whereas Kakatiya Longwal project has reported considerable improvement over the completion schedule reported earlier. Balram OCP Extension and Gevra Expansion OCP 25 MTY (SECL) have reported additional delay of 3 months and 24 months respectively due to delay in land acquisition. Manikpur OC expansion project has reported additional delay of 12 months, however no specific reason has been reported by the project authorities.
5. In the **Steel Sector**, Development of Bailadila Iron Ore Deposit-II (B) (NMDC) project has reported additional delay of 8 months due to problem between the main contractor & their sub-contractor and also due to change in scope of work.
6. In the **Petroleum Sector**, 21 projects have reported additional delays in the range of 1-23 months whereas Construction of new Terminal at Ennore, Chennai has reported improvement over the completion schedule reported earlier. Expansion of Panipat Refinery from 12 MMTPA to 15 MMTPA has suffered delay of 2 months due to delay in shutdown of various units like Crude Distillation Unit (CDU), Vacuum Distillation Unit (VDU) and Delayed Cracker Unit (DCU) for providing furnits. Additional Gas Processing Facility at Hazira has reported additional delay of 1 months due to late issue of Notice inviting tenders (NIT). Additional Gas processing units at (ONGC) Uran, Mumbai has reported additional delay of 2 months due to delay in tender process. MNW – NF Bridge Project at Hazira (ONGC) has reported additional delays of 5 months due to adverse weather conditions. Sultanpur Neemrana Pipe line project (Spurline to CJPL) and Development of C-Series Fields have reported additional delays of 4 months and 5 months respectively due to slow progress of work by the contractor. Installation of FCCV at Mumbai Refinery has reported additional delays of 6 months due to difficulties in execution of FCCU revamp. MSQ Improvement project and Heera Reconstruction has reported additional delay of 1 month and 11 months respectively due to delay in supply of equipments. Mumbai High South redevelopment PH-2 has reported additional delay of 23 months due to detailed engineering and delay in procurement activities. The specific reason of delay in respect of remaining projects, have not been reported by the concerned authorities.
7. In the **Power Sector**, 10 projects have reported additional delays in the range of 1-19 months. SEWA-II HEP (NHPC) has reported additional delay of 1 month due to delay in work of excavation because of poor geology & formation of cavities. SIPAT STPP Stage –I has been delayed by 2 months due to delay in supply of boilers. Koldam HEP of (NTPC) has reported additional delay of 3 months due to seepage in main dam and delay in supply of major items. Farakka STPP Stage-III (NTPC) has reported additional delay of 3 months due to delay in erection schedule by M/s BHEL. Bongaigaon Thermal Power Project (NTPC) has reported additional delay of 3 months due to delay in slow progress by civil agency. KORBA STPP Stage-III has reported additional delay of 2 months, due to slow progress of work and delay in supply of equipments. BARH STPP, 3x660 MW has reported additional delay of 6 months due to delay in supply of material by M/s Power Machine, Russia. Kunadankulam-APP Transmission system (PGCIL) has reported additional delay of 18 months due to stiff resistance from locals and pending court cases. MOUDA STPP (3x660 MW) of NTPC and transmission system associated with

- Tuticorin JV TPS have reported additional delay of 2 months and 19 months, however, no specific reasons have been given by the concerned project authorities.
8. In the **Road Transport and Highways Sector**, 46 projects have reported additional delay in the range of 1-24 months. The major reasons of delay in meeting the completion schedule include delay in land acquisition, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such delays.
 9. In the **Railway Sector**, 7 projects have shown additional delays in the range of 3-30 months whereas Muzzaffarpur- Sitamari NL, ECR and Bhairabi Sairong rail project has shown marginal improvement over the completion schedule reported earlier. Raichur-Guntakal of SCR has reported additional delay of 5 months due to delay in approval of Engineers Supports Partnership (ESP) and land acquisition. Bardhaman-Katwa (GC) has reported additional delay of 3 months as the State Government has not deposited its share of funds. Rajatgarh- Barrang (LD) ECOR, Khurda Road- Barang 3rd Line (LD) ECOR have shown delays of 6 months and 9 months respectively due to slow progress of work by the contractor. Bharuch – Samini- Dahej (GC), and Conversion of 1500 Volts DC Traction to 25 KV AC WR have reported additional delay of 3 months, 9 months and 30 months respectively, however, no specific reasons have been given by the project authorities.
 10. In the **Shipping & Ports Sector**, 2 projects have shown additional delay of 3-10 months Rail connectivity to ICTT at Vallarpadam project has shown additional delay of 3 months due to slow progress by the contractor and Establishment of Vessel Traffic Services in Gulf of Kutch has shown additional delay of 10 months due to slow progress in civil works.
 11. In the **Urban Development Sector**, 2 Projects have reported additional delay of 1 – 6 months. Delhi MRTS Phase-II Project has reported additional delay of 1 month due to slow process of land acquisition. Bangalore Metro Rail Project has reported additional delays of 6 months but no specific reason has been reported by the concerned project authority.
 12. In the **Telecommunications**, 15 projects have reported additional delay in the range of 1-9 months. GSM equipment of 700K Lines (2G) and 150K Lines (3G) has reported additional delay of 8 months due to delay in supply of 3 phase supply and delay in land acquisition. Expansion of existing 750K GSM Network project has reported additional delay of 4 months due to delay in supply of equipments by M/s ITI Ltd. The project authorities have not mentioned any specific reason for such delays in respect of other projects.
 13. Status as on 01.06.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the following tables.

(Pankaj Jain)

**Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation**

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	135	9
2	Road Transport & Highways	135	46
3	Power	84	10
4	Petroleum	79	22
5	Coal	39	4
6	Telecommunications	39	15
7	Steel	22	1
8	Shipping & Ports	22	2
9	Civil Aviation	8	0
10	Fertilisers	6	0
11	Atomic Energy	4	2
12	Urban Development	2	0
13	Mines	1	0
14	Health & Family Welfare	1	0
15	Water Resources	1	0
	Total	578	111

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
	May,2010			
	<u>Petroleum</u>			
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43


Summary of projects on the Flash Report for the month of May, 2010

I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 150 Cr. & above) Previous Month	578
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Previous Month	0
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Current month	1
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	1
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	578

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 578 projects, 13 projects are ahead of schedule, 109 projects are on schedule and 279 projects are delayed. Of the balance, 119 projects do not have fixed dates of commissioning while 58 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

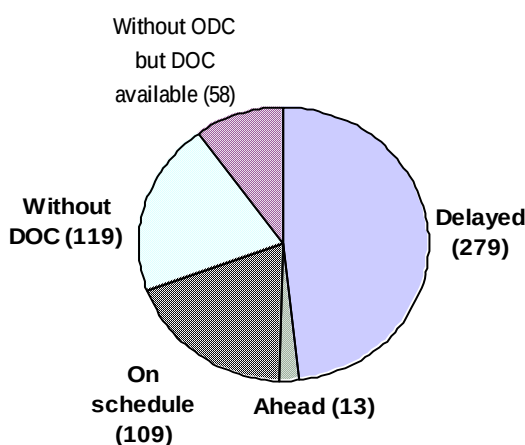

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 578 projects when sanctioned, was of the order of Rs. 620010.03 crore but this was subsequently revised to Rs. 683427.40 crore implying a cost overrun of 10.23%. The expenditure incurred on these projects till May, 2010 is Rs. 300335.32 crore, which is 43.95% of the revised cost of the projects.

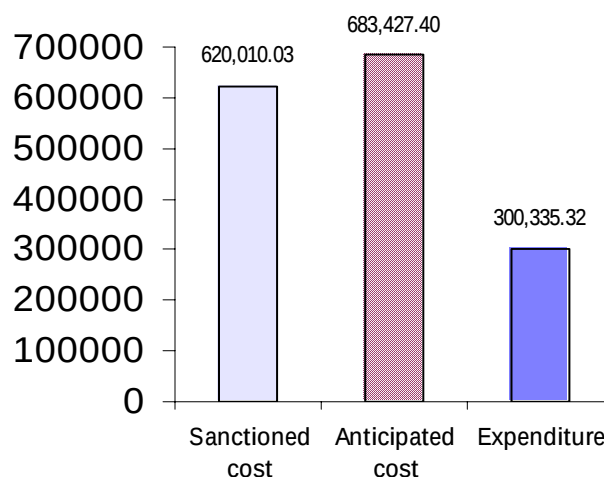

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	578
No of Projects Completed/Dropped/Frozen in Previous Month	0
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	1
No of Projects in Current Month	578

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original	279	13	109	58	119	578	48.27
Latest Approved	321	19	120	54	69	578	55.54

III. (A) Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Original	478	509,439.29	551,159.34	231,877.78	42.10	41,720.05	8.20
Latest Approved	100	110,570.74	132,268.06	68,457.54	51.80	21,697.32	19.60
Total	578	620,010.03	683,427.40	300,335.32	43.95	63417.37	10.23

III. (B) Delayed Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Original	279	310,057.03	369,156.86	196,510.47	53.20	59,099.83	19.10
Latest Approved	321	58,029.57	380,214.82	212,824.00	56.00	322,185.25	555.20
Total	600	368,086.60	749,371.68	409,334.47	54.62	381285.08	103.59

IV. Additional Delayed Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Latest Approved	111	128,604.96	141,759.02	91,937.60	64.90	13,154.06	10.20
Total	111	128,604.96	141,759.02	91,937.60	64.85	13154.06	10.23

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Petroleum</u>						
SHORT TERM LOW COST MUMBAI REFINERY	12/2006	390.00	01/2010	390.00	01/2010	188.43

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Coal</u>					
AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY)	11/2009	158.59	3/2016	158.59	3/2016

VII. Milestones (Cumulative due & achieved)

Total	1990
Achieved up to month	775

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	06/2010	08/2010	2
KUDANKULAM APP (NPCIL)	13,171.00	13,171.00	12/2008	03/2011	06/2011	3
<u>Coal</u>						
KAKATIYA LAONGWALL	453.63	453.63	N.A.	03/2013	12/2012	-3
BALRAM OCP EXTENSION	172.08	172.08	03/2009	03/2010	03/2011	12
MANIKPUR OC EXPANTION	321.42	321.50	03/2013	03/2013	03/2014	12
GEVRA EXPANSION OCP (SECL) (25 MTY)	1,667.55	1,667.55	03/2010	03/2010	03/2012	24
<u>Steel</u>						
Deve. of Bailadila Iron Ore Deposit- II(B)(NMDC)	295.89	607.17	10/2009	10/2009	06/2010	8
<u>Petroleum</u>						
CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	224.00	224.00	12/2010	02/2011	12/2010	-2
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON	1,431.91	1,675.72	09/2009	06/2010	07/2010	1
DADRI- PANIPAT R-LNG SPUR PIPELINE	250.66	389.00	06/2008	04/2010	05/2010	1
LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY	638.90	1,030.00	04/2009	05/2010	06/2010	1
DEVELOPMENT OF B-22 CLUSTER FIELDS	1,552.63	2,920.82	02/2009	04/2012	05/2012	1
MSQ UPGRADATION PROJECT AT BARAUNI REFINERY	1,492.00	1,492.00	04/2010	06/2010	07/2010	1
ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA	370.11	370.11	04/2011	06/2012	07/2012	1
VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI	463.32	463.32	N.A.	05/2011	06/2011	1
PANIPAT NAPHTA CRACKER PROJECT	14,439.00	15,292.00	11/2009	03/2010	05/2010	2
EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA	1,007.83	1,007.83	12/2009	08/2010	10/2010	2
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT	5,693.00	6,898.00	01/2010	06/2010	08/2010	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
ADDITIONAL GAS PROCESSING UNITS AT URAN	1,797.35	1,797.35	12/2011	09/2012	11/2012	2
SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)	396.13	396.13	10/2009	03/2010	07/2010	4
DEVELOPMENT OF C-SERIES FIELDS	3,195.16	2,800.00	12/2008	10/2010	03/2011	5
MNW-NF BRIDGE PROJECT	175.21	162.12	03/2009	12/2010	05/2011	5
BAWANA NANGAL PIPE LINE PROJECT	1,816.07	1,816.07	10/2010	10/2010	04/2011	6
DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)	4,429.38	2,800.00	10/2010	10/2010	04/2011	6
INSTALLATION OF FCCV AT MUMBAI REFINERY	900.47	900.47	09/2009	06/2010	12/2010	6
CAPACITY EXP. CUM MODERNISATION PH-II	2,591.80	3,941.41	12/2009	02/2010	09/2010	7
HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	2,305.30	2,305.30	06/2010	06/2010	03/2011	9
HEERA RECONSTRUCTION	706.70	706.70	04/2010	05/2010	04/2011	11
MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	1,252.75	8,813.41	06/2009	04/2011	03/2013	23
Power						
SEWA- II H.E.P (NHPC)	665.46	1,016.74	09/2007	04/2010	05/2010	1
BONGAIGAON THERMAL POWER PROJECT	4,375.35	4,375.35	07/2011	02/2012	03/2012	1
SIPAT STPP STAGE - I (NTPC)	8,323.39	8,323.39	12/2009	10/2011	12/2011	2
KORBA STPP STAGE-III	2,448.50	2,448.49	02/2010	08/2010	10/2010	2
MOUDA STPP	5,459.28	6,010.89	02/2012	08/2012	10/2012	2
KOLDAM HEP (NTPC)	4,527.15	4,527.15	04/2009	12/2011	03/2012	3
Farakka STPP Stage-III	2,570.44	2,570.44	08/2010	11/2010	02/2011	3
BARH STPP(3X660MW) NTPC	8,692.97	8,692.97	11/2010	10/2013	04/2014	6
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	1,779.29	1,896.65	11/2008	03/2010	09/2011	18
TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS	353.57	353.57	07/2010	07/2010	02/2012	19
Railways						
MUZAFFARPUR-SITAMARHI(NL), ECR	100.00	332.75	N.A.	03/2011	02/2011	-1
BHAIRABI SAIRONG	619.34	619.34	04/2014	04/2014	03/2014	-1
BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	200.80	200.80	N.A.	09/2010	12/2010	3
BARDHAMAN-KATWA (GC)	245.15	245.15	12/2010	12/2010	03/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
BILASPUR-URKURA (DL)	151.52	273.00	N.A.	11/2010	03/2011	4
RAICHUR- GUNTAKAL(DL)(SCR)	136.62	221.90	12/2007	07/2010	12/2010	5
RAJATGARH- BARANG(LD),ECOR	166.16	243.40	N.A.	06/2010	12/2010	6
KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	133.41	211.90	N.A.	03/2010	12/2010	9
CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	273.67	1,160.52	N.A.	06/2010	12/2012	30
<u>Road Transport & Highways</u>						
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH- 7,KM.80 TO KM.120	323.36	323.36	03/2008	09/2010	06/2010	-3
GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500	579.00	579.00	04/2009	05/2010	06/2010	1
COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358	106.00	193.00	08/2006	04/2010	06/2010	2
FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)	372.40	372.40	07/2004	04/2010	06/2010	2
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5	480.00	480.00	11/2007	06/2010	08/2010	2
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	507.49	507.49	03/2008	04/2010	06/2010	2
JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1	263.00	263.00	02/2009	04/2010	06/2010	2
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	225.00	225.00	10/2008	10/2010	12/2010	2
NAGPUR-KONDHALI,NH- 6(NHAI)	168.00	168.00	12/2008	04/2010	06/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293	208.46	208.46	08/2009	04/2010	06/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418	205.92	205.92	08/2009	04/2010	06/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463	243.64	243.64	08/2009	04/2010	06/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251	194.80	194.80	08/2009	04/2010	06/2010	2
MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS- 2/BOT/AP-6),NH-7	360.42	360.42	11/2009	03/2010	05/2010	2
BANGALORE- NEELAMANGALALA NH-4	445.00	445.00	07/2010	04/2010	06/2010	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	318.00	207.56	08/2004	06/2010	09/2010	3
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	193.09	193.09	03/2008	07/2010	10/2010	3
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80	166.27	166.27	03/2008	07/2010	10/2010	3
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	227.00	227.00	10/2008	12/2010	03/2011	3
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	629.00	629.00	11/2010	06/2010	09/2010	3
HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	280.00	280.00	02/2009	12/2010	03/2011	3
KOTA BYPASS,RJ-4, NH-76 (NHAI)	275.00	250.39	10/2008	06/2010	09/2010	3
SONAPUR TO GUWAHTI (AS-3)	245.00	245.00	03/2008	12/2010	03/2011	3
NALBARI TO BIJNI (AS-6)	225.00	225.00	06/2008	12/2010	03/2011	3
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS- 1/BOT/MP-2),NH7	407.60	407.60	06/2010	06/2010	09/2010	3
MAIBANG TO LUNDING (AS- 27), KM.40.000 TO KM.60.500	200.00	200.00	04/2009	12/2010	04/2011	4
THANJAUR-TRICHY,NH- 67(NHAI)	280.00	280.00	06/2009	06/2010	10/2010	4
ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH)	295.00	295.00	08/2010	08/2010	12/2010	4
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31	205.73	205.73	07/2004	06/2010	12/2010	6
SILIGURI TO ISLAMPUR (WB-7)	225.00	225.00	07/2008	06/2010	12/2010	6
NALBARI TO BIJNI (AS-8)	200.00	200.00	06/2008	07/2010	01/2011	6
THRISSUR TO ANGAMALI (NH-47)	312.50	312.50	03/2009	06/2010	12/2010	6
ASSAM/WB BORDER TO GAIRKATTA (WB-1)	221.82	221.82	11/2008	06/2010	12/2010	6
DHARAMTUL TO SONAPUR,KM 205-183 (AS- 20)	160.00	160.00	05/2008	12/2010	06/2011	6
AURANG-RAIPUR, NH-6, KM.232 TO KM.281	190.00	190.00	01/2009	05/2010	12/2010	7
DELHI/ HARYANA BORDER TO ROHTAK	486.00	486.00	05/2010	05/2010	12/2010	7
DAKOBA TO NAGAON (NH- 36)(NHAI)	225.00	225.00	06/2008	12/2010	10/2011	10

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	195.00	195.00	06/2008	12/2010	12/2011	12
NAGAON TO DHARAMTUL (AS-2)	264.72	264.72	06/2008	12/2010	12/2011	12
NALBARI T BIJNI (AS-7)	208.00	208.00	04/2008	12/2010	12/2011	12
DHARAMTUL TO SONAPUR (AS-19)	200.00	200.00	06/2008	12/2010	12/2011	12
GUWAHATI TO NALBARI (AS-5)	198.16	198.16	04/2008	12/2010	03/2012	15
CHAMBAL BRIDGE, NH-76 (RJ-5)	275.00	281.31	02/2010	12/2010	03/2012	15
MAIBANG TO LUNDING (AS- 24), KM.111.000 TO KM.126.450	155.04	155.04	11/2008	12/2010	12/2012	24
HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54	212.00	212.00	09/2007	12/2010	12/2012	24
BRAHMPUTRA BRIDGE, NH NO-31	217.61	217.61	04/2010	12/2010	12/2012	24
<u>Shipping & Ports</u>						
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	245.67	298.17	04/2009	03/2010	06/2010	3
ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH	165.00	165.00	12/2005	03/2010	01/2011	10
<u>Telecommunications</u>						
GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3	1,799.94	1,799.94	09/2009	06/2010	08/2010	2
GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M	908.30	916.70	08/2009	06/2010	08/2010	2
CONVERGENT BILLING AND CRM-MTNL(DELHI)	249.00	229.41	02/2007	12/2010	03/2011	3
GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5	409.21	483.54	12/2008	12/2009	03/2010	3
DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES	463.61	488.76	12/2009	03/2010	06/2010	3
EXPANSION OF EXISTING 2G&3G GSM NW BY 750 KPE NO	180.53	180.53	12/2009	06/2010	09/2010	3
EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992	231.38	168.30	10/2007	03/2010	07/2010	4
GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G)	373.94	373.94	12/2008	01/2010	08/2010	7

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN	335.91	335.91	03/2009	01/2010	08/2010	7
Assam Telecom Circle, Phase- V.I, 2G & 3G	336.81	336.81	01/2009	01/2010	08/2010	7
GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)	601.49	601.49	12/2008	12/2009	08/2010	8
GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1	192.48	192.48	03/2009	12/2009	08/2010	8
GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)	277.34	277.34	03/2009	12/2009	08/2010	8
BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G	366.00	529.32	09/2009	12/2009	08/2010	8
CONVERGENT BILLING AND CRM(MUMBAI)	247.00	247.00	02/2007	03/2010	12/2010	9

Number of projects reporting additional delay = 111

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	23,236.29
Civil Aviation	8	5,142.67	5,081.67	5,142.67
Coal	39	24,242.02	25,048.62	26,255.92
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,091.51	4,091.51
Steel	22	44,741.86	44,741.86	52,147.80
Petroleum	79	155,953.74	169,541.28	176,846.51
Power	84	178,816.28	180,630.36	188,077.57
Health & Family Welfare	1	71.18	422.60	443.15
Railways	135	51,007.64	62,798.24	101,416.46
Road Transport & Highways	135	41,863.55	41,863.55	42,136.98
Shipping & Ports	22	24,047.63	24,047.63	24,630.99
Telecommunications	39	17,315.28	17,136.75	17,426.14
Urban Development	2	15,071.00	16,763.36	15,071.00
Water Resources	1	542.90	542.90	1,187.00
Grand total	578	590,206.96	620,010.03	683,427.40


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

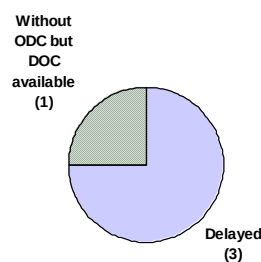

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 18465.25 Crores.

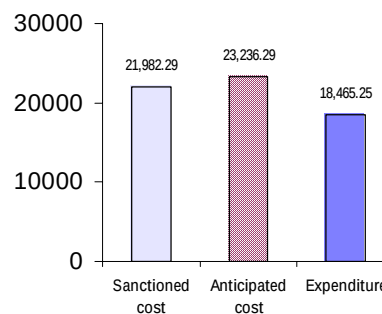


2. Sector: - Civil Aviation

Number of Projects	8
Number of Projects on schedule	3
Number of Projects Delayed	2
Number of Projects Wo_Doc_Original	2
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule, 2 projects are delayed and 2 projects are original date of commissioning and 1 projects are Wo_Odc_original.

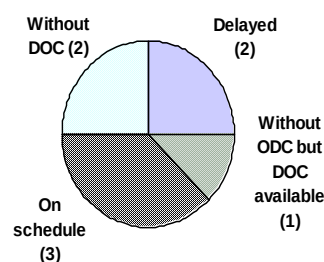

Investment Scenario

The total cost of implementation of 8 projects when sanctioned, was of the order of Rs. 5142.67 Crores but this was subsequently revised to Rs. 5142.67 Crores. The expenditure incurred on these projects till May, 2010 is Rs 1688.49 Crores.

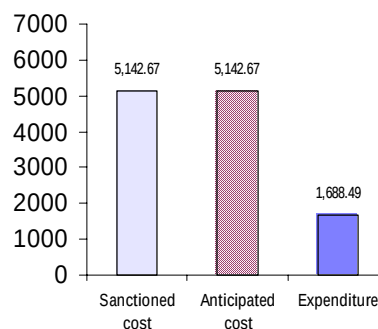


3. Sector: - Coal

Number of Projects	39
Number of Projects on schedule	9
Number of Projects Delayed	22
Number of Projects Ahead	3
Number of Projects Wo_ODC_Original	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 39 projects, 9 projects are on schedule, 22 projects are delayed and 3 projects are ahead and 5 Project W_Odc_Original .



Investment Scenario

The total cost of implementation of 42 projects when sanctioned, was of the order of Rs. 24242.02 Crores but this was subsequently revised to Rs. 26555.92 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 9364.84 Crores

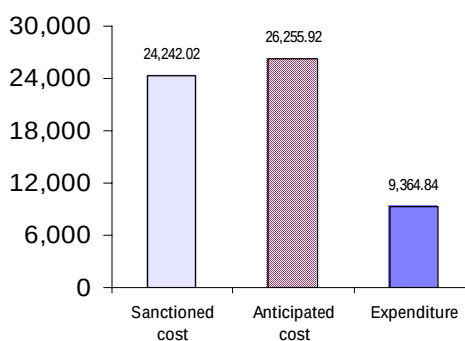


4. Sector: - Petroleum

Number of Projects	79
Number of Projects on schedule	22
Number of Projects Delayed	42
Number of Projects Ahead	4
Number of Projects Wo_Doc_Original	2
Number of Projects Without original date of commissioning	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 79 projects, 22 projects are on schedule, 42 projects are delayed and 4 projects are ahead and 2 projects are without date of commissioning and 9 Project is Without original date of commissioning.

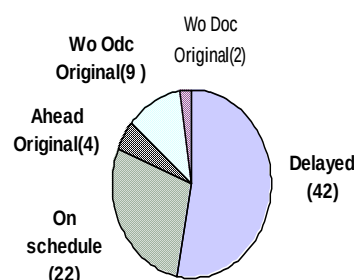

Investment Scenario

The total cost of implementation of 79 projects when sanctioned, was of the order of Rs. 15953.74 Crores but this was subsequently revised to Rs. 176846.49 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 5763.49 Crores.

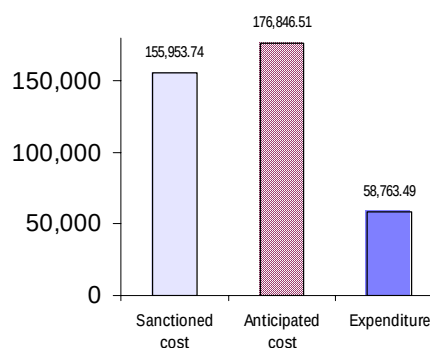


5. Sector: - Power


Number of Projects	84
Number of Projects on schedule	46
Number of Projects Delayed	33
Number of Projects Wo_Doc_Original	4
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 84 projects, 46 projects are on schedule, 33 projects are delayed, 4 projects is without date of commissioning and 1 projects is with out original date of commissioning

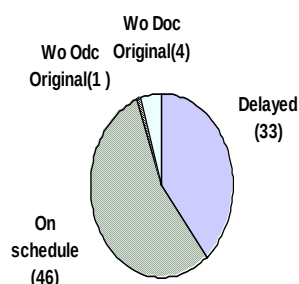

Investment Scenario

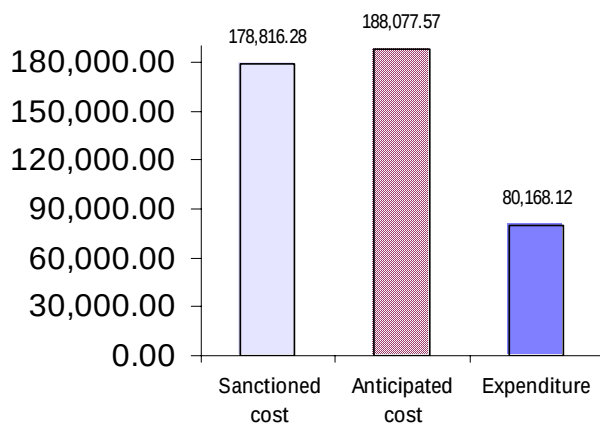


The total cost of implementation of 84 projects when sanctioned, was of the order of Rs. 178816.24 Crores but this was subsequently revised to Rs. 188077.57 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 80168.12 Crores.

6. Sector: - Railways

Number of Projects	135
Number of Projects on schedule	6
Number of Projects Delayed	36
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	51
Number of Projects Wo_Odc_Original	40


Brief Analysis

Project Status with out respect Original Schedule: Out of 135 projects, 6 projects are on schedule, 36 projects are delayed, 2 projects is ahead. 51 projects are Without date of commissioning and 40 projects are without original date of commissioning.

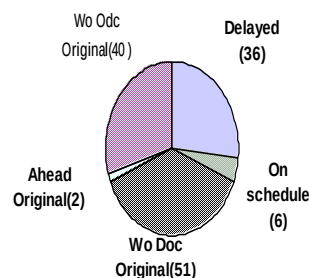

Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs. 51007.64 Crores but this was subsequently revised to Rs. 101416.46 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 43074.21 Crores.

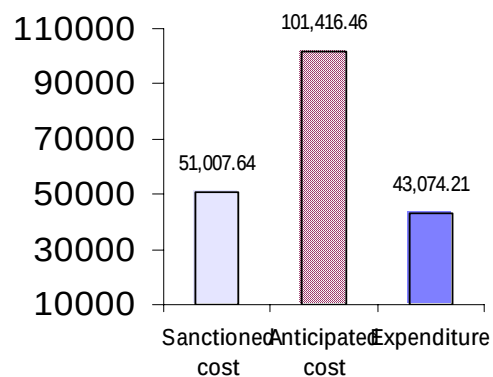


7. Sector: - Road Transport and Highways

Number of Projects	135
Number of Projects on schedule	9
Number of Projects Delayed	119
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 135 projects, 9 projects are on schedule, 119 projects are delayed, 2 projects are ahead and 5 projects is with out date of commissioning .



Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs 41863.55 Crores but this was subsequently revised to Rs. 42136.98 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 34831.42 Crores.

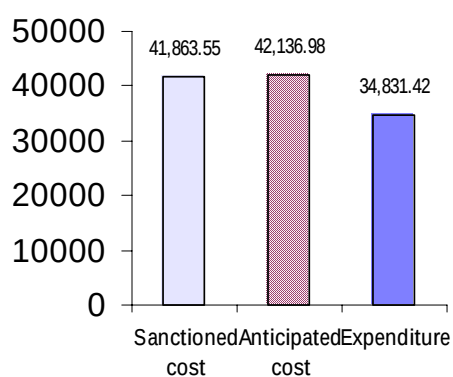


8. Sector: - Shipping and Ports

Number of Projects	22
Number of Projects on schedule	9
Number of Projects Delayed	8
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 9 projects are on schedule, 8 projects are delayed, 2 projects are ahead and 3 projects are without date of commissioning.



Investment Scenario

The total cost of implementation of 22 projects when sanctioned, was of the order of Rs.24047.63 Crores but this was subsequently revised to Rs. 24630.99 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 4783.27 Crores.

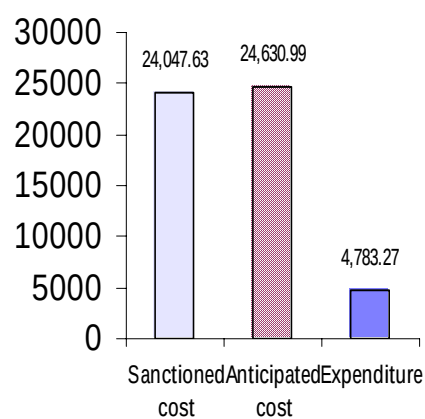


9. Sector: - Steel

Number of Projects	22
Number of Projects on schedule	1
Number of Projects Delayed	11
Number of Projects Wo_Odc_Original	10


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 1 projects are on schedule, 11 projects are delayed and 10 projects are Wo_Odc_Original.

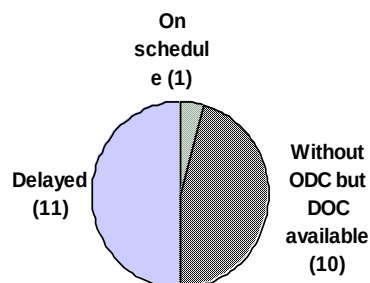

Investment Scenario

The total cost of implementation of 22 projects when sanctioned, was of the order of Rs.44741.86 Crores but this was subsequently revised to Rs. 52147.80 Crores. The expenditure incurred on these projects till May, 2010 is Rs. 22671.71 Crores.

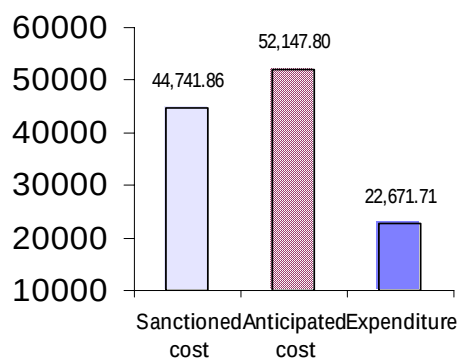


10. Sector: - Telecommunications

Number of Projects	39
Number of Projects Delayed	30
Number of Projects Wo_Doc_Original	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 39 projects, 30 projects are delayed and 9 projects are with our date of commissioning.

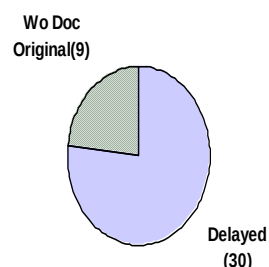

Investment Scenario

The total cost of implementation of 39 projects when sanctioned, was of the order of Rs 17315.28 Crores but this was subsequently revised to Rs. 17426.14 Crores. The expenditure incurred on these projects till May, 2010 is Rs 5700.37 Crores.

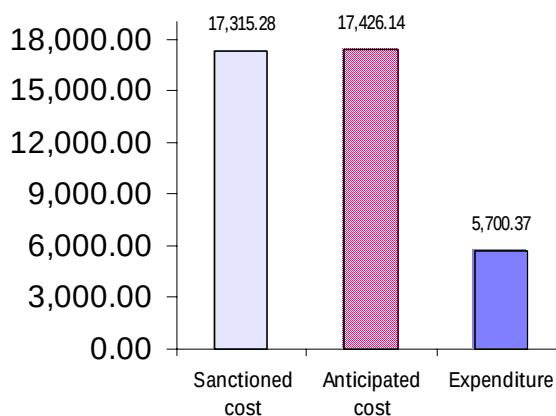

(May,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,536.00	10/2009 09/2007	08/2010	35(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	486.37	-	04/2011	-	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	13,002.00	12/2008	06/2011	30(O)	61/119
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,440.88	09/2010	09/2011	12(O)	8/80
Total			21,982.29	23,236.29	18,465.25				140/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	239.59	-	06/2010	-	1/24
6	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	143.97	06/2010	06/2010	0(O)	0/0
7	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]	06/2009	213.35	213.35	112.00	09/2010	11/2010	2(O)	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]	08/2008	1,273.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0
9	Extension of Secondary Runway(K2) - [N04000056]	08/2008	230.00	230.00	188.12	01/2011	01/2011	0(O)	0/0
10	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	579.26	05/2011	08/2011	3(O)	0/0
11	C/o new Airport-SH: E/W in cutting and filling geogrid - [N04000050]	01/2009	264.29	264.29	10.02	01/2011	-	-	0/0
12	GAGAN PROJECT - [N04000065]	09/2008	393.60	393.60	160.29	06/2013	-	-	0/0
Total			5,142.67	5,142.67	1,688.49				1/24
<u>Coal</u>									
13	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07	254.60	215.84	06/2009	05/2010	11(O)	36/21
14	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,433.21	06/2009	09/2010	15(O)	59/26
15	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	473.97	03/2009	03/2011	24(O)	0/0
16	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,970.33	06/2009	06/2011	24(O)	41/24
17	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	57.90	03/2010	03/2012	24(O)	0/4

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	1,008.38	03/2010	03/2012	24(O)	3/7
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66	341.63	101.25	03/2011	03/2012	12(O)	0/0
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	249.03	37.44	03/2012	03/2012	0(O)	0/42
21	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	0.40	03/2012	03/2012	0(O)	0/0
22	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	249.85	03/2012	03/2012	0(O)	0/0
23	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.57	418.57	64.85	-	03/2012	-	0/27
24	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]	03/2010	181.91	181.19	-	-	03/2012	-	0/34
25	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	779.31	08/2012	08/2012	0(O)	0/0
26	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34	779.26	98.19	03/2013	09/2012	-6(O)	2/22
27	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63	453.63	48.40	-	12/2012	-	0/44
28	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88	741.56	135.17	03/2010	03/2013	36(O)	0/1
29	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	583.33	03/2011 03/2013	03/2013	0(R3)	0/4
30	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04	437.34	135.65	03/2012	03/2013	12(O)	0/1
31	MAGADH OC (CCL) - [N06000015]	07/2006	469.78	706.40	16.17	07/2012	03/2013	8(O)	0/1
32	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78	467.78	11.42	-	03/2013	-	0/83
33	KANIHA OCP - [N06000035]	12/2007	457.77	457.77	48.96	03/2012	03/2013	12(O)	0/0
34	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93	479.53	175.35	03/2013	03/2013	0(O)	0/0
35	BINA EXTN. PROJ - [N06000019]	11/2006	168.97	168.97	240.37	03/2014	11/2013	-4(O)	1/1
36	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53	1,943.66	789.87	03/2010	03/2014	48(O)	2/6
37	CHURCHA UG - [N06000046]	06/2008	462.35	462.35	270.94	06/2014	03/2014	-3(O)	0/0
38	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	-	03/2010	03/2014	48(O)	0/0
39	PENGANGA OC - [N06000066]	10/2008	339.77	339.77	-	-	03/2014	-	0/1
40	KARTALI (EAST) OC - [N06000076]	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
41	MANIKPUR OC EXPANTION - [N06000081]	11/2009	321.42	321.50	206.71	03/2013	03/2014	12(O)	0/0
42	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18	287.17	-	11/2009 01/2012	03/2015	38(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87	395.87	22.73	03/2013	03/2015	24(O)	0/0
44	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0
45	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
46	JAGANNATHPOR OC - [N06000075]	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
47	RKP OCP PHASE-I - [N06000079]	03/2010	201.58	209.78	0.18	-	03/2015	-	0/31
48	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04	1,143.54	27.17	03/2014	03/2016	24(O)	1/1
49	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	56.52	03/2014	03/2016	24(O)	0/0
50	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	5.32	03/2015	03/2016	12(O)	0/0
51	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]	11/2009	158.59	158.59	99.66	03/2016	03/2016	0(O)	0/0
Total			24,242.02	26,255.92	9,364.84				145/381
<u>Fertilisers</u>									
52	THAL AMMONIA REVAMP PROJECT - [N08000003]	01/2009	488.75	488.75	-	03/2011	03/2011	0(O)	0/0
53	CAPACITY ENHANCEMENT OF VIJAIPUR-I - [N08000007]	09/2008	325.00	325.00	-	07/2011	07/2011	0(O)	0/0
54	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]	09/2008	438.00	438.00	-	07/2011	07/2011	0(O)	0/0
55	PANIPATH - AMMONIA PLANT FEEDSTOCK PLANT - [N08000004]	01/2010	1,292.84	1,292.84	-	10/2012	10/2012	0(O)	0/0
56	BATHINDA - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000005]	01/2010	1,294.19	1,294.19	-	10/2012	10/2012	0(O)	0/0
57	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]	01/2010	1,478.63	1,478.63	-	10/2012	10/2012	0(O)	0/0
Total			5,317.41	5,317.41	.00				0/0
<u>Mines</u>									
58	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	18/111
Total			4,091.51	4,091.51	3,316.00				18/111
<u>Steel</u>									
59	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	164.48	08/2009	02/2010	6(O)	0/0
60	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	118.16	-	03/2010	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	583.78	-	04/2010	-	2/1
62	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	278.89	-	06/2010	-	1/1
63	BILADILLA IRON ORE DEPOSITE-11B - [N12000017]	01/2009	295.89	295.89	213.74	10/2009	06/2010	8(O)	0/0
64	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89	607.17	213.89	10/2009	06/2010	8(O)	2/21
65	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,543.37	-	06/2010	-	2/6
66	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	93.35	-	06/2010	-	0/1
67	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	42.02	06/2010	06/2010	0(O)	0/0
68	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	232.51	06/2009	07/2010	13(O)	0/0
69	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	84.40	12/2009	08/2010	8(O)	0/0
70	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	80.00	02/2010	08/2010	6(O)	0/0
71	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	114.32	02/2010	01/2011	11(O)	0/0
72	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	182.63	-	04/2011	-	0/2
73	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	111.28	232.93	52.37	-	05/2011	-	0/1
74	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	6,203.00	10/2009	06/2011	20(O)	0/126
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	12.00	10/2009	06/2011	20(O)	0/0
76	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	7,703.14	-	06/2011	-	0/6
77	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	4.04	09/2010	12/2011	15(O)	0/0
78	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,534.00	1,114.89	-	12/2011	-	0/7
79	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	8,128.00	2,506.34	02/2011	03/2013	25(O)	0/0
80	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	6,146.00	1,130.39	-	03/2013	-	0/8
	Total		44,741.86	52,147.80	22,671.71				7/180
Petroleum									
81	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	43(O)	29/45

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
82	CRUDE OIL RECEIPT FACILITIES,KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.00	09/2009	12/2009	3(O)	0/0
83	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	750.71	12/2009	01/2010	1(O)	0/0
84	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00 2,869.00	3,127.00	2,688.58	04/2009 12/2009	02/2010	2(R1)	36/36
85	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	186.58	12/2009	02/2010	2(O)	0/0
86	CHAINSANGHARAJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77 571.64	565.00	405.34	09/2009 03/2010	03/2010	0(R3)	0/0
87	BINA DESPATCH TERMINAL - [N16000078]	05/2007	490.71 639.11	639.11	576.17	12/2009 03/2010	03/2010	0(R3)	0/0
88	BINA KOTA PIPE LINE PROJECT - [N16000079]	07/2007	405.82	405.82	349.82	12/2009 03/2010	03/2010	0(R3)	0/0
89	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	3,114.04	11/2009 04/2010	04/2010	0(R3)	0/0
90	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	14,439.00	15,292.00	12,054.37	11/2009 11/2009	05/2010	6(R1)	61/101
91	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66 350.00	389.00	484.73	06/2008	05/2010	23(O)	0/0
92	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	198.16	05/2010	05/2010	0(O)	0/0
93	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	434.38	-	05/2010	-	0/2
94	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY - [N16000026]	10/2006	638.90 1,030.00	1,030.00	715.97	04/2009	06/2010	14(O)	0/0
95	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92	1,493.49	673.81	06/2006 05/2008	07/2010	26(R1)	0/2
96	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]	06/2006	1,431.91	1,675.72	1,370.28	09/2009	07/2010	10(O)	0/0
97	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00	372.00	201.11	02/2010	07/2010	5(O)	0/0
98	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00	356.00	185.13	02/2010	07/2010	5(O)	0/0
99	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00	1,492.00	854.73	04/2010	07/2010	3(O)	0/0
100	MSQ IMPROVEMENT PROJECT - [N16000040]	04/2008	293.60	293.60	164.38	12/2009	07/2010	7(O)	0/0
101	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]	11/2007	396.13	396.13	170.82	10/2009 06/2010	07/2010	1(R3)	0/0
102	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00 6,898.00	6,898.00	5,330.21	01/2010 06/2010	08/2010	2(R3)	0/0
103	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]	09/2009	2,591.80 3,941.41	3,941.41	2,688.84	12/2009	09/2010	9(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
104	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA - [N16000017]	06/2005	1,007.83	1,007.83	684.18	12/2009 12/2009	10/2010	10(R1)	18/49
105	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	1.13	10/2010 -	10/2010	0(O)	0/0
106	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00 1,434.00	1,434.00	216.33	10/2011 04/2011	10/2010	-6(R3)	0/0
107	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	592.37	09/2009 -	12/2010	15(O)	0/0
108	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00	224.00	74.49	12/2010 -	12/2010	0(O)	0/0
109	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]	01/2009	605.40 605.40	605.40	201.74	12/2010 12/2010	12/2010	0(R3)	12/17
110	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]	06/2008	304.40	304.40	101.07	12/2010 -	12/2010	0(O)	0/0
111	CAPACITY AUGMENTATION OF AGRA& FERROZABAD REGION - [N16000074]	07/2009	199.57	199.57	0.74	- -	01/2011	-	8/5
112	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10	600.00	523.08	03/2007 -	03/2011	48(O)	3/3
113	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09	1,200.00	988.06	03/2007 -	03/2011	48(O)	6/6
114	IOR, RUHRASAGAR (ONGCL) - [160100217]	09/2001	113.90	371.05	145.95	03/2006 -	03/2011	60(O)	6/6
115	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16	2,800.00	2,681.28	12/2008 12/2008	03/2011	27(R3)	0/0
116	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30	2,305.30	1,971.48	06/2010 06/2010	03/2011	9(R3)	0/0
117	NORTH TAPTI GAS FIELD DEV. - [N16000085]	07/2008	589.70	755.76	-	03/2011 -	03/2011	0(O)	0/0
118	North Tapti Gas Field Development - [N16000096]	01/2010	589.70 755.56	755.56	-	03/2011 -	03/2011	0(O)	0/0
119	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07	1,816.07	182.56	10/2010 04/2011	04/2011	0(R3)	0/0
120	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]	11/2007	4,429.38 4,403.00	2,800.00	892.47	10/2010 04/2011	04/2011	0(R3)	0/0
121	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93 1,167.00	1,167.00	17.76	11/2011 04/2011	04/2011	0(R3)	0/0
122	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70	706.70	257.48	04/2010 -	04/2011	12(O)	0/0
123	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08	305.08	42.56	04/2011 -	04/2011	0(O)	0/0
124	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82	1,262.93	1,234.69	03/2005 -	05/2011	74(O)	0/0
125	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	330.40	0.35	05/2010 -	05/2011	12(O)	0/0
126	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	58.19	03/2009 -	05/2011	26(O)	0/0
127	BNPL superlines(Uttaranchal & Punjab) - [N16000091]	12/2009	540.92	540.92	-	05/2011 -	05/2011	0(O)	0/0
128	VKPL Upgradation and Laying of Superlines - [N16000092]	12/2009	463.32	463.32	-	05/2011 -	05/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
129	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]	12/2009	540.92	540.92	-	-	05/2011	-	6/5
130	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]	12/2009	463.32	463.32	-	-	06/2011	-	3/3
131	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00	267.00	127.16	-	08/2011	-	0/1
132	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00	3,597.00	57.14	09/2011	09/2011	0(O)	0/0
133	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00	3,284.00	47.31	09/2011	09/2011	0(O)	0/0
134	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00	820.00	592.37	12/2011	12/2011	0(O)	0/0
135	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00	349.00	16.18	08/2011	12/2011	4(O)	0/0
136	HYDROCRACKER REVAMP & SETTING - [N16000081]	02/2008	825.00	825.00	62.26	12/2011	12/2011	0(O)	0/0
137	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	06/2007	736.65	736.65	154.37	12/2011	12/2011	0(O)	0/0
138	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64	2,163.64	-	12/2011	12/2011	0(O)	0/0
139	Additional Development of D-1 Field - [N16000097]	01/2010	2,163.64	2,163.64	-	12/2011	12/2011	0(O)	0/0
140	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- [N16000070]	07/2009	238.68	238.68	-	-	01/2012	-	7/7
141	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	298.68	03/2010 03/2012	03/2012	0(R1)	0/0
142	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	07/2009	7,596.18	6,652.22	0.50	01/2013	03/2012	-10(O)	0/0
143	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]	12/2009	1,492.33	1,492.33	37.50	06/2012	03/2012	-3(O)	0/0
144	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78	5,633.44	0.61	03/2010 08/2010	04/2012	20(R1)	0/0
145	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29	6,326.40	599.85	05/2010	05/2012	24(O)	0/0
146	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63 2,920.82	2,920.82	5.24	02/2009 09/2010	05/2012	20(R1)	0/0
147	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2012	22(O)	0/0
148	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11	370.11	8.53	04/2011	07/2012	15(O)	0/0
149	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]	07/2008	288.04 288.04	288.04	-	08/2012	08/2012	0(O)	0/0
150	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	536.22	09/2012	09/2012	0(O)	0/0
151	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]	08/2009	1,793.00	1,793.00	14.24	09/2012	09/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
152	Construction of six Effluent Treatment Plants (ETP) - [N16000099]	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
153	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	29,777.00	3,413.38	03/2012 -	11/2012	8(O)	0/0
154	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35 -	1,797.35	9.77	12/2011 -	11/2012	11(O)	0/0
155	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]	06/2009	3,032.00 3,263.00	3,263.00	5.58	- -	12/2012	-	5/7
156	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]	06/2009	4,543.43 5,014.25	5,014.25	5.74	- -	12/2012	-	8/7
157	De-bottlenecking of SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	2.51	- -	12/2012	-	0/0
158	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75 8,813.41	8,813.41	4,304.35	06/2009 03/2013	03/2013	0(R3)	0/0
159	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15 -	2,378.86	109.52	03/2013 -	03/2013	0(O)	0/0
Total			155,953.74 -	176,846.51	58,763.49				208/302
Power									
160	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72 -	877.06	231.01	07/2006 -	03/2010	44(O)	2/5
161	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46 -	1,016.74	968.72	09/2007 -	05/2010	32(O)	8/36
162	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 1,007.16	1,007.16	756.45	12/2007 -	06/2010	30(O)	7/18
163	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52 -	227.52	150.34	06/2010 -	06/2010	0(O)	0/0
164	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34 -	241.27	142.26	06/2008 -	08/2010	26(O)	8/20
165	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	477.69	446.63	09/2010 -	09/2010	0(O)	0/0
166	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49 -	290.49	386.05	04/2010 -	09/2010	5(O)	0/0
167	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10 -	262.10	235.38	09/2010 -	09/2010	0(O)	0/0
168	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50 -	2,448.49	1,973.00	02/2010 -	10/2010	8(O)	5/24
169	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33 -	5,135.33	4,000.00	10/2010 -	10/2010	0(O)	11/40
170	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72 -	340.72	197.82	11/2010 -	11/2010	0(O)	0/0
171	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55 -	261.55	202.10	11/2010 -	11/2010	0(O)	0/0
172	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63 -	1,405.63	1,188.22	08/2010 -	12/2010	4(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
173	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]	12/2005	3,779.46	3,779.46	4,167.87	09/2009	12/2010	15(O)	15/30
174	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96	975.96	875.80	10/2009	12/2010	14(O)	2/20
175	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01	611.02	470.70	08/2010	12/2010	4(O)	0/0
176	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23	5,221.23	3,585.41	07/2010	12/2010	5(O)	3/20
177	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76	417.76	393.94	12/2010	12/2010	0(O)	0/0
178	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36	408.36	404.39	12/2010	12/2010	0(O)	0/0
179	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89	230.89	41.38	01/2011	01/2011	0(O)	0/0
180	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92	768.92	1,129.81	03/2007	02/2011	47(O)	1/25
181	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29	1,724.79	1,122.66	11/2009	02/2011	15(O)	0/0
182	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26	621.28	435.60	02/2011	02/2011	0(O)	0/1
183	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44	2,570.44	1,728.00	08/2010	02/2011	6(O)	13/26
184	URI-II - [N18000023]	10/2006	238.25	1,724.79	1,122.66	-	05/2011	-	0/0
185	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	3,002.00	05/2011	05/2011	0(O)	0/0
186	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,304.52	1,036.44	10/2010	06/2011	8(O)	0/0
187	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24	557.25	540.79	01/2010	06/2011	17(O)	0/22
188	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	123.81	06/2011	06/2011	0(O)	0/0
189	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	195.49	06/2011	06/2011	0(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	635.70	07/2011	07/2011	0(O)	0/0
191	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	336.21	07/2011	07/2011	0(O)	0/0
192	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	26.85	07/2011	07/2011	0(O)	0/0
193	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,061.38	31.17	09/2009	08/2011	23(O)	0/0
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	99.85	08/2011	08/2011	0(O)	0/0
195	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	1,896.65	1,843.49	11/2008	09/2011	34(O)	25/38

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
196	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97	328.97	168.12	09/2011	09/2011	0(O)	0/0
197	KOTESHWAR HEP (THDC) - [180100184]	04/2000	1,301.56	1,301.56	1,847.87	04/2005	10/2011	78(O)	2/22
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48	520.48	283.88	11/2011	11/2011	0(O)	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66	509.66	73.43	11/2011	11/2011	0(O)	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69	317.69	15.53	11/2011	11/2011	0(O)	0/0
201	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19	184.19	53.47	11/2011	11/2011	0(O)	0/0
202	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39	8,323.39	6,745.00	12/2009	12/2011	24(O)	33/56
203	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01	623.44	17.32	01/2012	01/2012	0(O)	0/0
204	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96	664.96	78.85	02/2012	02/2012	0(O)	0/0
205	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50	409.50	4.07	02/2012	02/2012	0(O)	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29	410.29	103.09	02/2012	02/2012	0(O)	0/0
207	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57	353.57	158.11	07/2010	02/2012	19(O)	0/0
208	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32	1,347.32	447.96	02/2012	02/2012	0(O)	0/0
209	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15	4,527.15	3,183.00	04/2009	03/2012	35(O)	19/41
210	RAMPUR HEP (412 MW) - [N18000024]	01/2007	2,047.03	2,047.03	825.72	01/2012	03/2012	2(O)	2/10
211	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35	4,375.35	1,119.00	07/2011	03/2012	8(O)	0/0
212	System Strengthening -X of SR - [N18000086]	12/2009	276.61	276.61	-	04/2012	04/2012	0(O)	0/0
213	765KV System for central part of Northern Region Grid - [N18000079]	11/2009	1,075.12	1,075.12	-	05/2012	05/2012	0(O)	0/0
214	765KV System for Central part of Northern Region G - [N18000078]	07/2009	1,736.36	1,736.36	-	06/2012	06/2012	0(O)	0/0
215	System Strengthening -XII of SR - [N18000085]	02/2010	232.34	232.34	-	06/2012	06/2012	0(O)	0/0
216	PARE HYDRO ELECTRIC PROJECT (110 MW) - [N18000045]	12/2008	573.99	573.99	104.88	08/2012	08/2012	0(O)	0/10
217	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95	2,360.95	1,868.14	08/2012	08/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
218	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33	7,075.33	3,723.73	08/2012	08/2012	0(O)	0/0
219	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]	12/2009	1,216.83	1,216.83	-	08/2012	08/2012	0(O)	0/0
220	MOUDA STPP - [N18000048]	11/2007	5,459.28	6,010.89	1,074.00	02/2012	10/2012	8(O)	0/0
221	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12	4,824.12	933.07	10/2012	10/2012	0(O)	0/0
222	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00	5,915.00	737.00	11/2012	11/2012	0(O)	0/0
223	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81	6,230.81	617.00	11/2012	11/2012	0(O)	0/0
224	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]	03/2010	4,672.99	4,672.99	11.89	11/2012	11/2012	0(O)	0/0
225	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33	6,285.33	4,056.06	09/2010	12/2012	27(O)	2/11
226	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	3,919.59	2,784.76	12/2008 09/2010	12/2012	27(R1)	0/15
227	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
228	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	1,412.25	12/2012	12/2012	0(O)	0/0
229	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]	02/2010	2,144.00	2,144.00	62.94	12/2012	12/2012	0(O)	0/0
230	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,919.59	2,784.76	09/2009	03/2013	42(O)	1/20
231	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	870.00	03/2013	03/2013	0(O)	5/31
232	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	1,161.14	05/2013	05/2013	0(O)	63/36
233	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	976.00	08/2013	08/2013	0(O)	0/0
234	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	1,708.02	08/2013	08/2013	0(O)	0/0
235	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,680.00	11/2010	04/2014	41(O)	15/51
236	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	245.74	07/2010	12/2014	53(O)	0/0
237	Transm System for development of Pooling str. in N - [N18000077]	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
238	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	108.00	07/2014	03/2015	8(O)	0/4
239	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	315.66	07/2014	01/2016	18(O)	0/0
240	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
241	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]	02/2010	215.86 -	215.86	-	06/2012 -	-	-	0/0
242	Northern Region Transmission Strengthening Scheme - [N18000083]	03/2012	965.58 -	965.58	-	11/2012 -	-	-	0/0
243	MAUDA Transmission System - [N18000084]	02/2010	469.38 -	469.38	-	10/2012 -	-	-	0/0
Total			178,816.28 -	188,077.57	80,168.12				248/666
<u>Health & Family Welfare</u>									
244	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	477.33	03/1999 03/2005	-	-	7/16
Total			71.18 -	443.15	477.33				7/16
<u>Railways</u>									
245	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50 246.50	246.50	314.80	03/2009 03/2009	11/2009	8(R3)	0/0
246	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74 -	224.51	41.39	- -	12/2009	-	0/0
247	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44 -	209.57	188.22	03/2009 -	02/2010	11(O)	0/0
248	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	556.48	03/1995 -	03/2010	180(O)	0/0
249	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21 157.76	265.00	265.33	03/1998 -	03/2010	144(O)	0/0
250	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 459.55	579.37	574.82	- -	03/2010	-	0/0
251	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	766.68	03/2001 -	03/2010	108(O)	0/0
252	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	548.92	03/2004 03/2005	03/2010	60(R1)	0/0
253	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 124.13	325.00	292.47	- -	03/2010	-	0/0
254	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 -	1,010.00	1,002.04	03/2003 -	03/2010	84(O)	0/0
255	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 -	665.00	586.85	- 11/2008	03/2010	16(R1)	0/0
256	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	503.16	482.13	- -	03/2010	-	0/0
257	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	746.02	06/2007 -	03/2010	33(O)	0/0
258	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	228.09	198.33	- -	03/2010	-	0/0
259	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 546.49	610.07	724.45	- 02/2009	03/2010	13(R1)	0/0
260	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	466.94	- 03/2009	03/2010	12(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
261	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [N220100322]	04/2005	148.61 -	227.52	223.97	03/2008 03/2009	03/2010	12(R1)	0/0
262	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	213.66	03/2008 06/2008	03/2010	21(R3)	0/0
263	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	405.60	404.70	- -	03/2010	-	0/0
264	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	296.20	253.51	04/2003 03/2010	06/2010	3(R1)	0/0
265	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	824.18	12/2006 -	06/2010	42(O)	0/0
266	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
267	DEOGHAR-DUMKA NEW BG LINE (DOUBL.) (ER) - [220100264]	02/1999	180.73 320.66	358.00	309.87	12/2006 12/2008	11/2010	23(R3)	0/0
268	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	-	02/2015 -	11/2010	-51(O)	0/0
269	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	133.05	03/2004 -	12/2010	81(O)	0/0
270	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	724.31	681.08	- -	12/2010	-	0/0
271	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 479.20	762.33	244.42	- 12/2009	12/2010	12(R1)	0/0
272	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	243.40	195.64	- 02/2009	12/2010	22(R1)	0/0
273	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	211.90	143.61	- 03/2009	12/2010	21(R1)	0/0
274	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	221.90	112.72	12/2007 03/2010	12/2010	9(R1)	0/0
275	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 716.64	718.30	616.44	03/2008 08/2008	12/2010	28(R1)	0/0
276	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
277	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]	09/2005	200.80 200.80	200.80	148.98	- -	12/2010	-	0/0
278	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,103.20	3,727.00	- -	12/2010	-	0/1
279	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	-110.66	- -	02/2011	-	0/0
280	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	346.51	02/2010 -	02/2011	12(O)	0/0
281	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 -	810.78	50.97	- 03/2011	02/2011	-1(R3)	0/0
282	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	375.21	114.88	- 03/2010	03/2011	12(R1)	0/0
283	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 284.27	488.76	280.58	06/1999 -	03/2011	141(O)	0/0
284	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	456.45	247.29	06/2004 -	03/2011	81(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
285	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	436.60	05/2008 -	03/2011	34(O)	0/0
286	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00 214.09	214.09	158.52	12/2009 -	03/2011	15(O)	0/0
287	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	341.81	- 06/2009	03/2011	21(R3)	0/0
288	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	452.35	263.12	- -	03/2011	-	0/0
289	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	70.43	- -	03/2011	-	0/0
290	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 -	273.00	257.88	- 03/2009	03/2011	24(R1)	0/0
291	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	348.78	-139.95	- -	03/2011	-	0/0
292	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	329.70	256.90	03/2009 12/2009	03/2011	15(R1)	0/0
293	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	245.15	34.57	12/2010 -	03/2011	3(O)	0/0
294	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
295	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.38	03/2011 -	03/2011	0(O)	0/0
296	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97 -	196.97	81.15	03/2011 -	03/2011	0(O)	0/0
297	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 252.50	252.50	67.61	02/2010 -	11/2011	21(O)	0/0
298	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44 576.27	1,103.47	659.43	- -	12/2011	-	0/0
299	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	735.10	175.76	- 09/2009	12/2011	27(R1)	0/0
300	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	496.03	27.08	03/2010 -	12/2011	21(O)	0/0
301	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	727.52	442.51	- -	03/2012	-	0/0
302	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 238.56	234.45	144.11	- -	03/2012	-	0/0
303	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	341.41	163.15	- -	03/2012	-	0/0
304	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59 -	495.74	61.86	- -	03/2012	-	0/0
305	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	324.90	103.73	03/2010 -	03/2012	24(O)	0/0
306	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69 -	501.69	45.90	03/2010 -	03/2012	24(O)	0/0
307	TAMLUK DIGHA - [N22000097]	03/1984	293.97 -	293.97	311.22	06/2005 -	04/2012	82(O)	0/0
308	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77 274.56	540.96	474.40	03/1994 -	12/2012	225(O)	0/0
309	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 654.51	1,160.52	484.07	- -	12/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
310	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	981.00	333.51	03/2009 -	12/2012	45(O)	0/0
311	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	1,480.71	445.84	10/2007 -	12/2012	62(O)	0/0
312	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	687.20	125.24	03/2010 -	12/2012	33(O)	0/0
313	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84 -	410.08	101.53	- -	03/2013	-	0/0
314	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 280.00	1,029.00	557.47	- -	03/2013	-	0/0
315	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70 915.70	1,556.23	248.09	- -	03/2013	-	0/0
316	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00 1,500.00	3,230.01	1,875.59	04/2008 12/2011	03/2014	27(R1)	0/0
317	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00 733.00	1,655.80	502.03	12/2008 -	03/2014	63(O)	0/0
318	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00 156.00	160.48	89.18	- -	03/2014	-	0/0
319	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00 200.00	390.00	0.78	- -	03/2014	-	0/0
320	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	5,300.00	98.20	03/2014 -	03/2014	0(O)	0/0
321	AGARTALA SABROOM - [N22000099]	04/2008	813.34 -	813.34	79.68	03/2014 -	03/2014	0(O)	0/0
322	BHAIRABI SAIRONG - [N22000100]	04/2008	619.34 -	619.34	0.71	04/2014 -	03/2014	-1(O)	0/0
323	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	324.66	129.28	- -	03/2015	-	0/0
324	SEVOK RANGPO - [N22000102]	04/2008	1,339.48 -	1,339.48	1.42	12/2015 -	12/2015	0(O)	0/0
325	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 727.53	3,123.52	194.37	03/2011 -	03/2016	60(O)	0/0
326	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 8,000.00	16,000.00	6,748.81	03/2001 -	12/2017	201(O)	0/0
327	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 407.78	617.63	386.41	- -	-	-	0/0
328	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53 320.66	464.50	490.13	03/1996 06/2009	-	-	0/0
329	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
330	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	232.15	- -	-	-	0/0
331	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 142.98	170.00	111.69	03/2002 03/2011	-	-	0/0
332	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
333	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	312.72	- -	-	-	0/0
334	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
335	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
336	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 450.00	730.00	274.41	- -	-	-	0/0
337	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	465.00	104.45	- -	-	-	0/0
338	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	712.00	363.60	- -	-	-	0/0
339	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	363.58	02/2009 -	-	-	0/0
340	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	337.82	49.69	- -	-	-	0/0
341	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 -	268.00	-	12/1999 03/2008	-	-	0/0
342	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0
343	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	82.45	- -	-	-	0/0
344	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	101.86	03/2007 03/2007	-	-	0/0
345	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
346	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	686.07	07/2005 -	-	-	0/0
347	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	- -	-	-	0/0
348	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	63.26	- -	-	-	0/0
349	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
350	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	151.69	- 05/2009	-	-	0/0
351	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15 -	381.17	80.12	- -	-	-	0/0
352	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
353	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	72.06	- -	-	-	0/0
354	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	396.22	- -	-	-	0/0
355	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
356	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00	1,300.00	-	-	-	-	0/0
357	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90	325.17	311.98	03/2005	-	-	0/0
358	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38	700.00	97.09	12/2008	-	-	0/0
359	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91	459.91	52.53	03/2011	-	-	0/0
360	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82	180.82	261.57	-	-	-	0/0
361	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13	1,225.00	120.45	-	-	-	0/0
362	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67	165.67	0.15	-	-	-	0/0
363	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73	230.03	45.76	-	-	-	0/0
364	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	585.93	102.78	-	-	-	0/0
365	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45	573.12	555.49	-	-	-	0/0
366	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56	671.82	1.05	-	-	-	0/0
367	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92	261.70	0.08	02/2006	-	-	0/0
368	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]	09/2007	404.19	900.00	47.91	-	-	-	0/0
369	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17	900.00	199.95	-	-	-	0/0
370	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00	255.96	129.45	-	-	-	0/0
371	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00	227.40	13.30	-	-	-	0/0
372	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00	582.83	28.22	-	-	-	0/0
373	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00	529.88	24.40	-	-	-	0/0
374	BHAKURA DAMODAR - [N22000098]	03/1998	282.70	325.17	24.32	07/2008	-	-	0/0
375	KISHANGANJ JALALGARH - [N22000101]	04/2008	282.92	333.76	0.71	-	-	-	0/0
376	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]	04/1993	100.41	949.22	15.65	12/2009	-	-	0/0
377	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00	675.00	315.61	-	-	-	0/0
378	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08	1,010.00	64.75	12/2011	-	-	0/0
379	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00	607.09	194.84	12/2012	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		51,007.64	101,416.46	43,074.21				0/1
	<u>Road Transport & Highways</u>								
380	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	-	03/2009	03/2010	12(O)	0/0
381	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00	276.00	-	04/2008	04/2010	24(O)	0/0
382	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00	310.00	392.26	04/2008	04/2010	24(O)	0/0
383	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	-	12/2008	04/2010	16(O)	0/0
384	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	-	10/2008	04/2010	18(O)	0/0
385	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93	440.93	641.40	12/2006	12/2009	36(O)	0/0
386	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39	534.39	716.15	05/2007	12/2009	31(O)	0/0
387	TOVARAMKURCHI-MADURAI, NH45B (NHAI) - [N24000054]	04/2000	263.00	263.00	317.74	08/2008	12/2009	16(O)	0/0
388	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80	402.80	453.70	03/2009	12/2009	9(O)	0/0
389	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00	450.00	876.61	07/2008	01/2010	18(O)	0/0
390	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00	261.00	286.30	08/2008	03/2010	19(O)	0/0
391	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	164.23	06/2008	03/2010	21(O)	0/0
392	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	636.10	05/2009	04/2010	11(O)	0/0
393	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]	12/2003	360.42	360.42	-	11/2009	05/2010	6(O)	0/0
394	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	134.60	08/2006	06/2010	46(O)	0/0
395	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40	372.40	399.29	07/2004	06/2010	71(O)	0/0
396	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	452.07	03/2005	06/2010	63(O)	0/0
397	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	407.18	03/2005	06/2010	63(O)	0/0
398	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	423.50	11/2007	06/2010	31(O)	0/0
399	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	150.03	08/2005	06/2010	58(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
400	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.90	03/2008	06/2010	27(O)	0/0
401	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	342.80	03/2008	06/2010	27(O)	0/0
402	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	560.71	03/2009	06/2010	15(O)	0/0
403	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	677.94	04/2009	06/2010	14(O)	0/0
404	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	383.30	02/2009	06/2010	16(O)	0/0
405	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	414.30	06/2008	06/2010	24(O)	0/0
406	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	376.40	06/2008	06/2010	24(O)	0/0
407	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	447.60	06/2008	06/2010	24(O)	0/0
408	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	132.44	06/2008	06/2010	24(O)	0/0
409	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]	03/2005	168.00	168.00	-	12/2008	06/2010	18(O)	0/0
410	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	212.00	02/2004	06/2010	76(O)	0/0
411	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	30.89	04/2009	06/2010	14(O)	0/0
412	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	184.00	08/2009	06/2010	10(O)	0/0
413	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	211.10	09/2009	06/2010	9(O)	0/0
414	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	237.70	09/2008	06/2010	21(O)	0/0
415	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	191.10	08/2009	06/2010	10(O)	0/0
416	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	247.80	08/2009	06/2010	10(O)	0/0
417	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	164.60	08/2009	06/2010	10(O)	0/0
418	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	441.60	06/2010	06/2010	0(O)	0/0
419	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]	03/2005	445.00	445.00	793.20	07/2010	06/2010	-1(O)	0/0
420	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	205.20	06/2010	06/2010	0(O)	0/0
421	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	67.03	08/2004	07/2010	71(O)	0/0
422	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.55	07/2010	07/2010	0(O)	0/0
423	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	513.50	07/2010	07/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
424	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	831.21	07/2010	07/2010	0(O)	0/0
425	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	667.70	03/2010	07/2010	4(O)	0/0
426	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	782.86	11/2007	08/2010	33(O)	0/0
427	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	187.60	06/2008	08/2010	26(O)	0/0
428	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	71.35	08/2004	09/2010	73(O)	0/0
429	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	314.00	03/2005	09/2010	66(O)	0/0
430	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	838.90	11/2010	09/2010	-2(O)	0/0
431	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	223.40	10/2008	09/2010	23(O)	0/0
432	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]	12/2003	407.60	407.60	232.40	06/2010	09/2010	3(O)	0/0
433	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	232.40	09/2009	09/2010	12(O)	0/0
434	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	242.40	09/2009	09/2010	12(O)	0/0
435	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	184.60	09/2009	09/2010	12(O)	0/0
436	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	298.40	09/2010	09/2010	0(O)	0/0
437	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	262.60	10/2008	10/2010	24(O)	0/0
438	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	287.70	10/2008	10/2010	24(O)	0/0
439	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	122.70	03/2008	10/2010	31(O)	0/0
440	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	93.21	03/2008	10/2010	31(O)	0/0
441	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	355.90	10/2008	10/2010	24(O)	0/0
442	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	282.00	10/2008	10/2010	24(O)	0/0
443	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	292.12	10/2008	10/2010	24(O)	0/0
444	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	449.20	04/2008	10/2010	30(O)	0/0
445	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	550.82	06/2009	10/2010	16(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
446	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	232.00	10/2009	10/2010	12(O)	0/0
447	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	422.12	03/2005	12/2010	69(O)	0/0
448	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	244.30	07/2004	12/2010	77(O)	0/0
449	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	622.20	04/2007	12/2010	44(O)	0/0
450	GARHMUKTRESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00	275.00	277.35	09/2007	12/2010	39(O)	0/0
451	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	291.00	05/2008	12/2010	31(O)	0/0
452	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68	340.68	259.50	03/2008	12/2010	33(O)	0/0
453	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	204.68	01/2009	12/2010	23(O)	0/0
454	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81	199.81	28.10	04/2009	12/2010	20(O)	0/0
455	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64	167.64	39.49	11/2008	12/2010	25(O)	0/0
456	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00	242.00	306.20	12/2008	12/2010	24(O)	0/0
457	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00	227.00	289.30	12/2008	12/2010	24(O)	0/0
458	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	178.00	10/2008	12/2010	26(O)	0/0
459	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30	151.30	104.00	10/2008	12/2010	26(O)	0/0
460	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43	203.43	108.10	10/2008	12/2010	26(O)	0/0
461	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	162.80	07/2008	12/2010	29(O)	0/0
462	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	254.30	06/2009	12/2010	18(O)	0/0
463	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	12/2010	21(O)	0/0
464	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	175.50	11/2008	12/2010	25(O)	0/0
465	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	253.60	12/2009	12/2010	12(O)	0/0
466	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	12/2010	5(O)	0/0
467	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]	03/2005	557.00	557.00	505.00	02/2010	12/2010	10(O)	0/0
468	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	0.41	02/2004	12/2010	82(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
469	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	444.84	08/2010	12/2010	4(O)	0/0
470	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	287.00	05/2010	12/2010	7(O)	0/0
471	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	173.20	06/2008	01/2011	31(O)	0/0
472	TRICHY - DINDIGUAL NH-45 - [N24000099]	03/2005	576.00	576.00	254.40	07/2010	01/2011	6(O)	0/0
473	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	526.99	01/2011	01/2011	0(O)	0/0
474	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	334.80	01/2011	01/2011	0(O)	0/0
475	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	108.30	09/2007	02/2011	41(O)	0/0
476	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	135.90	09/2007	03/2011	42(O)	0/0
477	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	195.53	07/2005	03/2011	68(O)	0/0
478	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	229.19	07/2005	03/2011	68(O)	0/0
479	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	166.62	10/2008	03/2011	29(O)	0/0
480	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00	227.00	231.70	10/2008	03/2011	29(O)	0/0
481	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	280.00	131.90	02/2009	03/2011	25(O)	0/0
482	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94	332.94	147.14	09/2008	03/2011	30(O)	0/0
483	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]	12/2003	198.00	198.00	110.90	11/2008	03/2011	28(O)	0/0
484	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	244.40	03/2008	03/2011	36(O)	0/0
485	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	131.40	06/2008	03/2011	33(O)	0/0
486	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	482.50	10/2009	03/2011	17(O)	0/0
487	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	118.00	09/2010	03/2011	6(O)	0/0
488	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00	200.00	61.40	04/2009	04/2011	24(O)	0/0
489	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	517.38	05/2010	05/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
490	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	145.60	09/2007	06/2011	45(O)	0/0
491	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	53.32	09/2008	06/2011	33(O)	0/0
492	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHA) - [240106304]	12/2003	251.03	251.03	205.60	10/2008	06/2011	32(O)	0/0
493	RAJMARG CHORAH TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91	229.91	150.30	10/2008	06/2011	32(O)	0/0
494	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	70.60	05/2008	06/2011	37(O)	0/0
495	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	240.70	03/2010	06/2011	15(O)	0/0
496	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	-	04/2004	10/2011	90(O)	0/0
497	DAKOPA TO NAGAON (NH-36)(NHA) - [240106288]	12/2003	225.00	225.00	183.80	06/2008	10/2011	40(O)	0/0
498	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	107.60	06/2005	12/2011	78(O)	0/0
499	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHA) - [240106290]	12/2003	195.00	195.00	91.36	06/2008	12/2011	42(O)	0/0
500	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHA) - [240106293]	12/2003	237.80	237.80	106.80	06/2008	12/2011	42(O)	0/0
501	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	291.20	09/2008	12/2011	39(O)	0/0
502	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	171.60	06/2008	12/2011	42(O)	0/0
503	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	140.20	04/2008	12/2011	44(O)	0/0
504	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	139.70	06/2008	12/2011	42(O)	0/0
505	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	93.82	04/2008	03/2012	47(O)	0/0
506	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	126.60	04/2008	03/2012	47(O)	0/0
507	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	177.32	02/2010	03/2012	25(O)	0/0
508	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
509	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	8.72	05/2010	08/2012	27(O)	0/0
510	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	155.04	28.05	11/2008	12/2012	49(O)	0/0
511	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	34.47	09/2007	12/2012	63(O)	0/0
512	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	24.06	07/2009	12/2012	41(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
513	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	73.64	04/2010	12/2012	32(O)	0/0
514	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]	12/2003	300.00	300.00	-	10/2008	-	-	0/0
	Total		41,863.55	42,136.98	34,831.42				0/0
			-						
	<u>Shipping & Ports</u>								
515	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	406.28	03/2010	03/2010	0(O)	0/0
516	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	193.47	06/2007 01/2009	06/2010	17(R1)	0/0
517	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	297.76	04/2009	06/2010	14(O)	0/0
518	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	374.37	07/2010	07/2010	0(O)	0/0
519	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA - [N25000046]	11/2004	2,118.00	2,118.00	-	11/2004	08/2010	69(O)	0/0
520	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	815.90	10/2008	11/2010	25(O)	0/0
521	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	307.02	11/2010	11/2010	0(O)	0/0
522	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
523	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
524	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	99.84	12/2005	01/2011	61(O)	0/0
525	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	1,140.00	0.16	02/2011	02/2011	0(O)	0/0
526	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	755.50	0.73	03/2011	03/2011	0(O)	0/0
527	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	211.21	04/2011	04/2011	0(O)	0/0
528	Acquisition of two nos. of 120 B.P - [N25000042]	04/2009	2,908.48	2,908.48	58.18	03/2011	06/2011	3(O)	0/0
529	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	438.02	04/2011	12/2011	8(O)	0/0
530	Acquisition of Two nos. of 3060 DWT - [N25000043]	04/2009	2,770.32	2,770.42	1,108.12	09/2011	12/2011	3(O)	0/0
531	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
532	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]	03/2009	3,500.00	3,500.00	-	01/2012	01/2012	0(O)	0/0
533	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
534	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.63	10/2008	-	-	0/0
535	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
536	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]	03/2008	375.00	375.00	-	01/2009	-	-	0/0
	Total		24,047.63	24,630.99	4,783.27				0/0
Telecommunications									
537	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	-	04/2008	12/2009	20(O)	0/0
538	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	10/2009	46(O)	0/0
539	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	34(O)	0/0
540	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	15(O)	0/0
541	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	0.00	278.16	175.77	12/2008 12/2009	01/2010	1(R3)	0/0
542	NATIONAL RADIO SPECTRUM MANAGEMENT and MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.24	12/2004	02/2010	62(O)	0/0
543	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	483.54	475.59	12/2008	03/2010	15(O)	0/0
544	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	161.35	02/2008	05/2010	27(O)	0/0
545	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	488.76	106.13	12/2009	06/2010	6(O)	0/0
546	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	94.14	10/2007 12/2009	07/2010	7(R3)	0/0
547	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	558.30	12/2008	08/2010	20(O)	0/0
548	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	144.63	03/2009	08/2010	17(O)	0/0
549	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	172.03	12/2008	08/2010	20(O)	0/0
550	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	54.65	09/2009	08/2010	11(O)	0/0
551	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	455.01	03/2009	08/2010	17(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
552	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	150.12	03/2009	08/2010	17(O)	0/0
553	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	165.56	08/2009	08/2010	12(O)	0/0
554	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	529.32	213.42	09/2009	08/2010	11(O)	0/0
555	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	336.81	105.16	01/2009	08/2010	19(O)	0/0
556	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]	06/2006	803.70	803.76	595.62	06/2009	09/2010	15(O)	1/20
557	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53	180.53	30.30	12/2009	09/2010	9(O)	0/0
558	Execution of telecom network requirement of defence - [N26000065]	05/2006	1,077.00	1,077.00	841.00	03/2009	09/2010	18(O)	0/0
559	Implementation of FTTH, the state of the art access, gpon eq - [N26000072]	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
560	Implementation of FTTH, the state of the art Acces - [N26000073]	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
561	Procurement of DXC equipment - [N26000074]	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
562	Procurement of 24 F OF cable. - [N26000075]	02/2008	199.00	199.00	-	03/2010	11/2010	8(O)	0/0
563	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007 12/2009	12/2010	12(R3)	0/0
564	Procurement of 2.5G DWDM equipment - [N26000066]	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
565	Procurement of 10G (40 chl) DWDM equipment - [N26000067]	08/2006	590.10	590.10	-	03/2009	12/2010	21(O)	0/0
566	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
567	Procurement of STM-1 SDH equipment - [N26000069]	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
568	Procurement of STM-16 ADM equipment - [N26000070]	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
569	Procurement of STM-16 ADM equipment - [N26000071]	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
570	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	64.30	02/2007	03/2011	49(O)	0/0
571	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
572	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	160.00	92.45	06/2006	-	-	0/0
573	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
574	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]	11/2008	350.00	350.00	-	-	-	-	0/0
575	CENTRALISED TRANSMISSION NMS - [N26000064]	08/2009	300.00	300.00	-	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		17,315.28	17,426.14	5,700.37				1/20
	<u>Urban Development</u>								
576	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,676.00 8,605.36	8,676.00	14,727.76	06/2010 -	11/2010	5(O)	0/8
577	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 8,158.00	6,395.00	2,267.57	12/2011 09/2012	06/2012	-3(R3)	0/6
	Total		15,071.00	15,071.00	16,995.33				0/14
	<u>Water Resources</u>								
578	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
	Grand Total		590,206.96	683,427.40	300,335.32				775/1990
