

289th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.100 Crores and above)
NOVEMBER, 2009

Ministry of Statistics & Programme Implementation
Sardar Patel Bhawan, New Delhi
Website:- www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 100 Crore and Above During 2009-2010	6-10
Summary of Projects	1-18
Sector wise analysis of projects	19-54

EXECUTIVE SUMMARY

The 289th Flash Report for November' 2009, that contains information on the status of 589 projects in the Central Sector, each costing Rs. 100 crores and above. During November' 2009, four projects reported completion and have been dropped from the monitor of this Ministry. During the month under reference, two new projects have been added. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	152
2.	RAILWAYS	150
3.	POWER	85
4.	PETROLEUM	64
5.	COAL	43
6.	TELECOMMUNICATION	29
7.	STEEL	28
8.	SHIPPING & PORTS	18
9.	CIVIL AVIATION	9
10.	ATOMIC ENERGY	5
11.	URBAN DEVELOPMENT	3
12.	MINES	1
13.	HEALTH & FW	1
14.	WATER RESOURCES	1
Total		589

2. Sixty one (61) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1-36 months in respect of projects relating to Atomic Energy, Civil Aviation, Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways and Shipping & Port sectors.

3. In the **Atomic Energy Sector**, 4 projects have reported additional delays as compared to the position in the previous month. Kaiga Atomic Power Project units 3&4, completed last year, has reported further delay of 2 months due to non supply of fuel. Rajasthan Atomic Power Project units 5&6 (NPCIL) has reported additional delay of 1 month as the project is in the critical stage and likely to be completed during February, 2010. Kudankulam APP (NPCIL) has reported additional delay of 3 months due to slippage of commitment of M/s Atom Stroy Export (ASE), Russia. Prototype Fast Breeder Reactor Kalpakkam, Tamilnadu has reported additional delay of 12 months, however, no specific reasons have been provided by the project authorities.

4. In the **Civil Aviation Sector**, 4 projects have shown additional delays of 1-11 months. Construction of New Expandable Modular Integrated Building, Raipur has reported additional delay of 3 months, due to change in location of service block being overlapped with the existing residential quarters. Construction of Expandable Modular Terminal Building, Indore, Construction of Expandable Modular Integrated Terminal Building, Bhopal, and Construction of Integrated Cargo Complex (Ph-III) at Chennai have shown additional delays of 1 month, 3 months and 11 months respectively, however no specific reasons have been provided by the project authorities.

5. In the **Coal sector**, 5 projects have reported additional delays in the range of 1-36 months. Barsingsar Lignite Mine, NLC, has reported additional delay of 1 month due to delay in preparation of tender documents and inadequate mobilization by the contractor. The TPS-II Expansion (1470 MW to 1970 MW) project of National Lignite Corporation, (NLC), has reported additional delay of 3 months due to delay in equipment erection and inadequate mobilization by the contractor. Batura of South Eastern Coalfields Ltd (SECL) has reported additional delay of 24 months due to delay in acquisition of land. Another project titled PELMA opencast belonging to SECL has reported additional delay of 36 months due to delay in acquisition of land. The Jhanjra Continuous Miner (2nd Set) project of Eastern Coalfields Limited has reported additional delay of 36 months but no specific reasons have been provided by the project authorities for the delay.

6. In the **Steel Sector**, 4 projects have reported additional delays in the range of 1-2 months. Rebuilding of coke oven battery No.4 has reported additional delay of one month due to delay in supply of equipments and their erection by M/s Mecon. Installation of 700 Tones per Day Oxygen Plant, Rourkela, Orissa, has reported additional delay of 1 month due to termination of

contract. Simultaneous Blowing of Blast Furnace Converter of SMS-II, Orissa has reported additional delays of 2 months due to delay in civil work and supply of other equipment. Rebuilding of coke oven battery No. 1 & 2, Bokaro has reported additional delays of 2 months however, no specific reason has been provided by the project authorities.

7. In the **Petroleum Sector**, 5 projects have reported additional delays in the range of 1-14 months. Jhajjar Hissar Pipe Line Project has reported additional delay of 14 months. Delayed, as the basic design of the project is under review. Panipat Naphta Cracker Project has reported additional delay of 1 month due to delay in completion of Captive Power Plant by L&T. Inst. Of FCC Gasoline Desulphun Unit at Mathura Refinery has reported additional delay of 1 month, delayed due to continuous delay in supply of compressor's piping and instrumentation items by BPCL. Chainsa-Jhajjar Pipeline Project has reported additional delay of 2 months, due to delay in land acquisition. LPG Processing & Compression has reported additional delay of 4 months, however no specific reason has been given by the project authorities.

8. In the **Power Sector**, 11 projects have reported additional delays in the range of 1-14 months. SIPAT-II Supplementary Transmission System (PGCIL) project and Koldam HEP Transmission Line (PGCIL) due to delay in commissioning of Generation Project. System Strengthening in South West Part of NR has reported additional delay of 1 month due to non-availability of forest clearance. Enhancement of transmission capacity in East West has reported additional delay of 2 months due to delay in shutdown in switch yard. Farakka STPP Stage-III has reported additional delay of 3 months due to delay in finalization of erection agency by M/s BHEL. Northern Region System Strengthening Scheme-V has reported additional delay of 3 months due to court cases. Chamera, Stage III (NHPC) has reported additional delay of 4 months due to court stay on crushing plant at leading to huge shortage of aggregate for concrete work. NIMOO Bazgo HEP has reported additional delay of 4 months due to delay in award of civil works and delay in supply of equipment and machinery by M/s BHEL. Korba STPP Stage III has reported additional delay of 6 months due to delay in various civil and structural works by M/s SPML. SIPAT STPP Stage-I has reported additional delay of 7 months due to delay in supply of equipment by Power Machine Ltd, Russia. Parbati HEP stage III has reported additional delay of 7 months due to delay in land acquisition for Sainj bypass and due to delay in decision from GOI regarding participation of Chinese companies.

9. In the Road Transport and Highways Sector, 25 projects have reported additional delays in the range of 1-22 months. The concerned project authorities have not indicated any specific reason for such delays.

10. In the Shipping & Ports Sector, Rail Connectivity to Integrated Container Terminal at Vallarpadam has reported additional delays of 12 months due to rescheduling of the projects.

11. In the Railway Sector, 2 projects have shown additional delays in the range of 1-3 months. Tollyganj-Garia (MTP) project has reported additional delays of 3 months to complete the ancillary works. Mansi-Purnia (Extension of Mansi-Saharsa) project has reported additional delay of 3 months due to slow progress in the bridge works.

12. In the Telecommunication Sector, 3 projects have reported additional delays in the range of 1-2 months. GSM based network Expansion Plan, Phase-IV, Chhattisgarh has reported additional delay of 2 months due to delay in execution of work by M/s ITI Ltd. Assam Telecom Circle, Phase-V.I, 2G & 3G have reported additional delay of 1 month due to delay in supply of equipment. Kolkata Telecom District, Phase-IV has reported additional delay of 2 months due to revision of works.

Status as on 01.12.2009 in respect of completion of projects costing Rs.100 crore and above in different sectors during 2009-10 is indicated in the following tables.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Delayed
1	Road Transport & Highways	152	25
2	Railways	150	2
3	Power	85	11
4	Petroleum	64	5
5	Coal	43	5
6	Steel	29	4
7	Telecommunications	28	0
8	Shipping & Ports	18	1
9	Civil Aviation	9	4
10	Atomic Energy	5	4
11	Urban Development	3	0
12	Mines	1	0
13	Health & Family Welfare	1	0
14	Water Resources	1	0
	Total	589	61

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 100 Crore and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2009				
<u>Steel</u>				
1	COKE OVEN BATTERY NO. 4(PHASE-1) (RINL)(RASTRIYA ISPAT NIGAM LIMITED) - [120100061]	286.63	12/2006	301.25
May,2009				
<u>Petroleum</u>				
2	AUGMENTATION OF MUNDRA-PANIPAT CRUDE OIL PIPELINE(INDIAN OIL CORPORATION LIMITED) - [160100291]	205.00	03/2008	140.55
<u>Road Transport & Highways</u>				
3	JHANSI-SHIVPURI ,NH-25,NH-25 KM-91-50(NHDP,P) - [240106251]	220.31	05/2008	149.02
4	BHARATPUR MAHAVA, NH-11, KM.63 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106259]	250.00	01/2010	341.10
5	AMBALA-ZIRAKPUR, NH-21AND22, KM.5/735 TO KM.39/961(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106261]	298.00	11/2010	364.62
6	KONDHALI-TELEGAON(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000041]	212.00	03/2010	331.87
<u>Telecommunications</u>				
7	GSM BASED NETWORK EXPANSION PH-IV (BSNL) (U.P. WEST)(BHARAT SANCHAR NIGAM LIMITED) - [260100081]	359.07	06/2009	36.19
8	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(PUNJAB)(BHARAT SANCHAR NIGAM LIMITED) - [260100089]	508.63	06/2010	365.16
9	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(RAJASTHAN)(BHARAT SANCHAR NIGAM LIMITED) - [260100090]	448.91	06/2009	154.52
10	GSM BASED NETWORK(PH-IV)(BSNL) ORISSA(BHARAT SANCHAR NIGAM LIMITED) - [260100093]	164.06	12/2009	89.29
11	GSM-NETWORK EXPANSION(PH-IV) (BSNL) W. BENGAL(BHARAT SANCHAR NIGAM LIMITED) - [260100094]	428.00	06/2009	200.00
June,2009				
<u>Petroleum</u>				
12	GREEN FUELS & EMISSION CONTROL (HPCL) MUMBAI REF.(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100236]	1,152.00	06/2009	1,551.79
<u>Railways</u>				
13	THANE-TURBHE-NERUL-VASHI(MTP)(METROPOLITAN TRANSPORT PROJECTS) - [220100159]	403.39	03/2000	400.60

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
14	PARADIP PORT, NH-5A (PORT CONNECTIVITY) KM 0 - KM 77(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100202]	428.00	02/2007	459.38
15	SWAROOPGANJ TO BAKARIA (RJ-1) PH.II, KM.29-KM.0 (NH-76)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106229]	220.00	04/2010	244.47
16	RAJASTHAN/MP BORDER TO KOTA(RJ-10), KM.509- 449.15, NH-76(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106254]	378.22	04/2008	365.05
17	RJ/MP BORDER TO KOTA(RJ-9) NH-76, KM.449.15 TO KM.406(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106255]	297.72	04/2008	289.88
18	AGRA-BHARATPUR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000027]	195.00	03/2009	192.10
19	PALANPUR TO SWAROOPGANJ, NH-14(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000067]	498.00	03/2009	82.09
July, 2009				
<u>Power</u>				
20	KAHAL GAON STPP STAGE - II (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100230]	5,868.31	05/2007	4,881.17
<u>Road Transport & Highways</u>				
21	GARAMORE TO BAMANBORE (PACK.-III) PH.-II, KM.254-KM.182.60(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106215]	360.70	11/2007	334.72
22	TINDIVANAM-UIUNDURPET, KM 121-192.25 NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000082]	480.00	03/2009	1,130.80
<u>Telecommunications</u>				
23	COMM. OF GSM EQU. OF 600K LINES(PH-4)(BHARAT SANCHAR NIGAM LIMITED) - [N26000032]	214.00	01/2007	120.48
24	PROJECT NIB-II BROADBAND MULTIPLY(BHARAT SANCHAR NIGAM LIMITED) - [N26000047]	1,008.00	03/2009	337.50
August, 2009				
<u>Power</u>				
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000025]	220.69	04/2009	131.26
<u>Railways</u>				
26	MADURAI-DINDIGUL,(LD)(SR)(SR) - [N22000047]	73.19	-	181.81
<u>Road Transport & Highways</u>				
27	TIRUNELVELI-PANAGUDI, KM 160-203(T.N)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106242]	423.54	03/2008	220.40

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
28	SALEM TO KARUR (NS-21 OF TN-2), KM.207.050-KM.248.625, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106270]	253.50	01/2009	333.34
29	SALEM TO KARUR, KM.258-645 TO KM.292.6(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106271]	205.60	08/2008	323.94
30	SALEM TO KERALA BORDER SEC. (TN-7), KM.53 TO KM.100, NH-47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106274]	379.80	12/2008	453.20
September,2009				
31	MADURAI-KANNIAKUMARI, KM.42 TO KM.80, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106238]	474.21	03/2008	246.20
32	MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106239]	567.38	03/2008	382.50
33	MAHUA-JAIPUR, NH-11, KM.120 TO KM.228(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106258]	483.00	03/2009	578.30
34	KARUR TO MADURAI (TN-5), KM.373.275 TO KM.426.6, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106275]	283.50	12/2008	448.30
35	INDORE-KALAGHAT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000034]	472.00	09/2009	663.90
36	Bharuch-Surat Package BOT-II(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000070]	492.00	07/2009	448.87
37	Vadodara-Bharuch Package BOT-I(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000071]	660.00	07/2009	789.84
38	UIUWDURPET-PADALUR,NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000084]	460.00	06/2009	799.19
Shipping & Ports				
39	ACQUISITION OF 2-300,000 DWT VERY LARGE CRUDE CARRIERS(SHIPPING) - [250100174]	1,136.08	09/2009	1,196.24
October,2009				
Petroleum				
40	DEVELOPMENT OF BASSEIN EAST (ONGCL)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100232]	985.17	03/2006	1,568.46
Railways				
41	2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR)(RAIL VIKAS NIGAM LTD.) - [220100221]	93.10	-	126.11
Telecommunications				
42	GSM EQUIPMENT OF 1015K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000044]	350.84	11/2008	182.06
43	ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM(BHARAT SANCHAR NIGAM LIMITED) - [N26000059]	567.40	06/2009	241.85
November,2009				

Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
44	KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106272]	327.20	01/2009	457.60
45	HYDERABAD BANGALORE SECTION(NH-7)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106284]	611.44	03/2009	834.20
46	KADAL TO ARMUR, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000092]	271.73	11/2009	303.80
<u>Telecommunications</u>				
47	GSM BASED NETWORK PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000033]	174.36	11/2007	71.50

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 100 Crore and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2009				
<u>Telecommunications</u>				
1	500K BROAD BAND ACCESS N/W PH-III(MAHANAGAR TELEPHONE NIGAM LIMITED) - [120100061]	134.25	10/2009	31.95

Summary of projects on the Flash Report for the month of November, 2009


I. Project Implementation – Current Status:

Number of Projects Previous Month	595
Number of Projects Completed/Dropped/Frozen in Previous Month	4
Number of Projects Completed/Dropped/Frozen in Current month	4
Number of Projects Added in Current month	2
Number of Projects in Current Month	589

II. Brief Analysis

a) Project Status w.r.t


Original Schedule: Out of 589 projects, 13 projects are ahead of schedule, 131 projects are on schedule and 321 projects are delayed. Of the balance, 81 projects do not have fixed dates of commissioning while 43 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

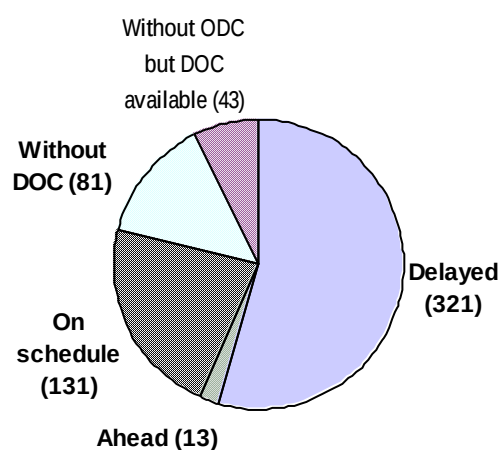

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 589 projects when sanctioned, was of the order of Rs. 554113.81 crore but this was subsequently revised to Rs. 605937.65 crore implying a cost overrun of 9.35%. The expenditure incurred on these projects till November, 2009 is Rs. 231696.19 crore, which is 38.24% of the revised cost of the projects.

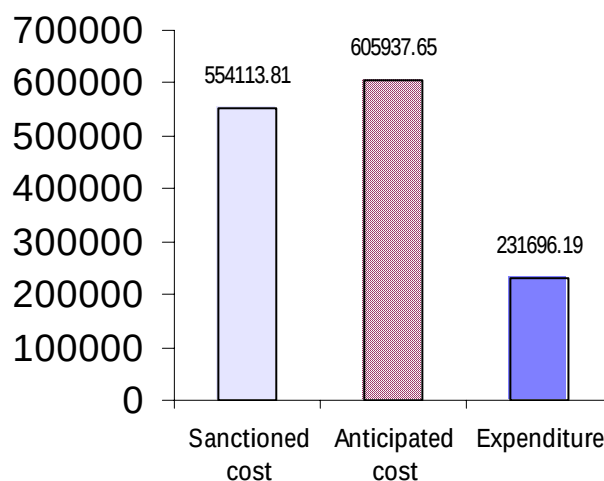

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	595
No of Projects Completed/Dropped/Frozen in Previous Month	4
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	2
No of Projects in Current Month	589

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original	321	13	131	43	81	589	54.50
Latest Approved	339	15	135	30	70	589	57.56

III. Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	492	498,125.66	536,487.46	195,209.98	36.40	38,361.80	7.70
Latest Approved	97	55,988.15	70,314.19	38,132.77	54.20	14,326.04	25.60
Total	589	554,113.81	606,801.65	233,342.75	38.45	52687.84	9.51

IV. List of projects completed/dropped current month

IV. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Road Transport & Highways</u>						
KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7	12/2003	327.20	01/2009	327.20	11/2009	457.60
HYDERABAD BANGALORE SECTION(NH-7)(NHAI)	12/2003	611.44	03/2009	592.00	11/2009	834.20
KADAL TO ARMUR, NH-7	12/2003	271.73	11/2009	271.73	11/2009	303.80
<u>Telecommunications</u>						
GSM BASED NETWORK PH-4	11/2007	174.36	11/2007	174.36	11/2009	71.50

V. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Power</u>					
VINDHYACHAL STTP STAGE-IV	1/2009	5,915.00	11/2012	5,915.00	11/2012
RIHAND STTP STAGE-III (2X500MW)	1/2009	6,230.81	11/2012	6,230.81	11/2012

VI. Milestones (Cumulative due & achieved)

Total	1993
Achieved up to month	739

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL)	3,072.00	3,072.00	02/2008	01/2010	02/2010	1
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	01/2010	03/2010	2
KUDANKULAM APP (NPCIL)	13,171.00	13,171.00	12/2008	12/2010	03/2011	3
PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	3,492.00	5,677.00	09/2010	09/2010	09/2011	12
<u>Civil Aviation</u>						
C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE	135.60	135.60	10/2009	02/2010	03/2010	1
C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR	129.65	129.65	09/2009	12/2009	03/2010	3
C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA	135.04	135.04	09/2009	12/2009	03/2010	3
C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A	144.94	144.94	04/2010	01/2010	12/2010	11
<u>Coal</u>						
BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)	254.07	254.60	06/2009	11/2009	12/2009	1
TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	2,030.78	2,453.57	06/2009	11/2010	02/2011	3
Batura OC	203.82	203.82	03/2013	03/2013	03/2015	24
PELMA OC	448.32	448.32	03/2012	03/2012	03/2015	36
JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II	122.35	122.35	03/2010	03/2010	03/2013	36
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO.-4	248.94	248.94	08/2009	12/2009	01/2010	1
INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA	302.70	302.70	06/2009	12/2009	01/2010	1
Rebuilding of coke oven battery No.1 & 2 (Bokaro S	500.90	500.90	04/2010	10/2010	12/2010	2
SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II	197.66	197.66	10/2009	11/2009	01/2010	2

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Petroleum</u>						
JHAJJAR HISSAR PIPE LINE PROJECT	281.07	281.07	10/2010	12/2011	10/2010	-14
PANIPAT NAPHTA CRACKER PROJECT	12,138.00	14,439.00	09/2009	02/2010	03/2010	1
INST. OF FCC GASOLINE DESULPHUN UNIT AT MATHURA RE	348.00	348.00	12/2009	12/2009	01/2010	1
CHAINSA-JHAJJAR PIPE LINE PROJECT	967.77	571.64	09/2009	12/2009	02/2010	2
LPG PROCESSING & COMPRESSION	142.00	139.07	10/2009	12/2009	04/2010	4
<u>Power</u>						
SIPAT-II SUPP. TRANS. SYSTEM (PGCIL)	813.67	820.45	06/2008	11/2009	12/2009	1
KOLDAM HEP TRANSMISSION LINE (PGCIL)	464.91	464.91	09/2008	11/2009	12/2009	1
SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN	150.26	153.24	10/2009	12/2009	01/2010	1
ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST	103.80	103.80	06/2009	12/2009	02/2010	2
Farakka STPP Stage-III	2,570.44	2,570.44	08/2010	08/2010	11/2010	3
NORTHERN REGION SYSTEM STRENGHTENING SCHEME-V	721.25	721.25	06/2009	12/2009	03/2010	3
CHAMERA,STAGE-III (NHPC)	1,405.63	1,405.63	08/2010	08/2010	12/2010	4
NIMOO BAZGO HYDROELECTRIC PROJECT	611.01	611.02	08/2010	08/2010	12/2010	4
KORBA STPP STAGE-III	2,448.50	2,448.49	02/2010	02/2010	08/2010	6
SIPAT STPP STAGE - I (NTPC)	8,323.39	8,323.39	12/2009	03/2011	10/2011	7
PARBATI H.E.P. STAGE -III (NHPC)	2,304.56	2,304.52	10/2010	11/2010	06/2011	7
<u>Railways</u>						
TOLLYGANJ-GARIA(MTP)	907.69	1,032.76	12/2006	03/2010	06/2010	3
MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN	114.01	322.87	N.A.	12/2009	03/2010	3
<u>Road Transport & Highways</u>						
VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)	467.93	467.93	03/2005	12/2009	01/2010	1
TOVARAMKURCHI-MADURAI,NH45B (NHAI)	263.00	263.00	08/2008	11/2009	12/2009	1

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
AP/KARNATKA BORDER- NANDI HILL CROSSING AND DEVANHA	402.80	402.80	03/2009	11/2009	12/2009	1
PADALUR-TRICHY, NH-45	320.00	320.00	05/2009	11/2009	12/2009	1
SIX LANING OF BANGLORE- HOSUR SECTION OF NH-7, PHAS	110.00	110.00	07/2008	11/2009	12/2009	1
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH- 7,KM.80 TO KM.120	323.36	323.36	03/2008	11/2009	01/2010	2
SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47	469.80	469.80	12/2008	11/2009	01/2010	2
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	507.49	507.49	03/2008	11/2009	02/2010	3
ORAI TO JHANSI (UP-4),NH- 25, KM.170.0 TO KM.104.0	451.97	451.97	04/2008	03/2010	06/2010	3
THANJAUR-TRICHY,NH- 67(NHAI)	280.00	280.00	06/2009	03/2010	06/2010	3
JHANSI TO LALITPUR, NH-26	276.09	276.09	09/2009	06/2010	09/2010	3
TRICHY BYPASS END TO TOVARAMKURCHI (NH- 45B)(NHAI)	261.00	261.00	08/2008	11/2009	03/2010	4
ORAI TO JHANSI (UP-5),NH- 25, KM.220.0 TO KM.170.0	340.68	340.68	03/2008	06/2010	12/2010	6
KASIA TO GORAKHPUR (NH- 28)(NHAI)	242.00	242.00	12/2008	06/2010	12/2010	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	227.00	227.00	12/2008	06/2010	12/2010	6
THRISSUR TO ANGAMALI (NH-47)	312.50	312.50	03/2009	12/2009	06/2010	6
NALBARI TO BIJNI (AS-9)	142.00	142.00	06/2008	06/2010	12/2010	6
TRICHY - DINDIGUAL NH-45	576.00	576.00	07/2010	07/2010	01/2011	6
GAGODHAR- GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	412.78	479.54	11/2007	11/2009	06/2010	7
KUNJWANI-VIJAYPUR(NS- 15) (NS & EW-PH-I) KM.80- KM.97.20,NH-1A	110.00	110.00	12/2004	03/2010	12/2010	9
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	210.00	210.00	04/2007	12/2009	12/2010	12
GARHMUKTESHWAR- MURADABAD (NHAI) OTHERS KM.93-149.25, NH- 24	275.00	275.00	09/2007	12/2009	12/2010	12
HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	220.00	220.00	09/2007	12/2009	12/2010	12

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A	284.00	284.00	05/2008	12/2009	12/2010	12
SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)	225.00	241.53	04/2004	12/2009	10/2011	22
<u>Shipping & Ports</u>						
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	245.67	298.17	04/2009	11/2009	11/2010	12
Number of projects reporting additional delay = 61						

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	25,054.29	25,054.29	26,308.29
Civil Aviation	9	4,832.24	4,826.73	4,832.24
Coal	43	26,110.40	26,216.99	27,522.73
Mines	1	4,091.51	4,091.51	4,091.51
Steel	29	45,596.58	45,596.58	49,353.10
Petroleum	64	136,018.51	136,018.51	145,750.52
Power	85	165,980.96	167,384.33	170,229.80
Health & Family Welfare	1	71.18	422.60	443.15
Railways	150	50,032.77	59,029.60	93,825.28
Road Transport & Highways	152	44,015.85	44,015.85	44,257.13
Shipping & Ports	18	12,475.83	12,475.83	12,747.59
Telecommunications	28	11,591.06	11,591.06	11,047.28
Urban Development	3	14,596.67	16,847.03	15,206.03
Water Resources	1	542.90	542.90	1,187.00
Grand total	589	541,010.75	554,113.81	606,801.65


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	5
Number of Projects on schedule	1
Number of Projects Delayed	4

Brief Analysis


Project Status w.r.t Original Schedule: Out of 5 projects, 1 projects are on schedule and 4 projects are delayed.



Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 5 projects when sanctioned, was of the order of Rs. 25054.29 Crores but this was subsequently revised to Rs. 26308.29 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 19398.61 Crores.

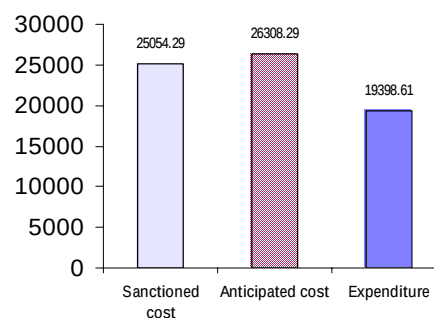


2. Sector: - Civil Aviation

Number of Projects	9
Number of Projects on schedule	3
Number of Projects Delayed	6


Brief Analysis

Project Status w.r.t Original Schedule: Out of 9 projects, 3 projects are on schedule, 6 projects are delayed.



Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 4832.24 Crores but this was subsequently revised to Rs. 4832.24 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 1057.08 Crores.

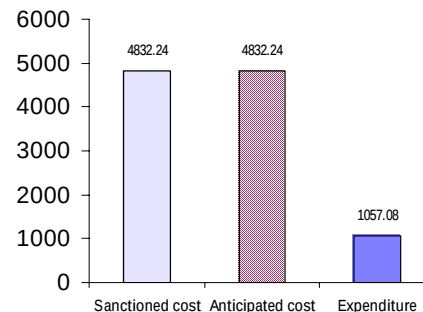


3. Sector: - Coal


Number of Projects	43
Number of Projects on schedule	18
Number of Projects Delayed	21
Number of Projects Ahead	4
Number of Projects Wo_Doc_Original	1

Brief Analysis

Project Status w.r.t Original Schedule: Out of 43 projects, 18 projects are on schedule, 20 projects are delayed and 4 projects are ahead and 1 projects Wo_Doc_Original



Investment Scenario

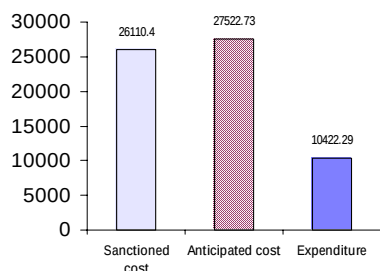


The total cost of implementation of 43 projects when sanctioned, was of the order of Rs. 26110.4 Crores but this was subsequently revised to Rs. 27522.73 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 10422.29 Crores

4. Sector: - Petroleum


Number of Projects	64
Number of Projects on schedule	28
Number of Projects Delayed	33
Number of Projects Ahead	3

Brief Analysis

Project Status w.r.t Original Schedule: Out of 64 projects, 28 projects are on schedule, 33 projects are delayed and 3 projects are ahead .



Investment Scenario

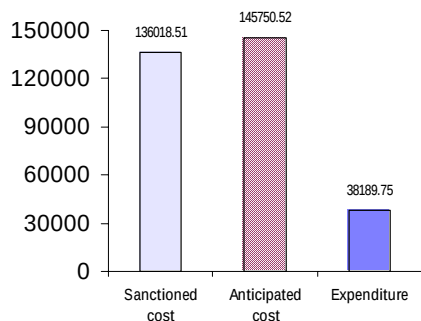


The total cost of implementation of 64 projects when sanctioned, was of the order of Rs. 136018.51 Crores but this was subsequently revised to Rs. 145750.52 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 38189.75 Crores.

5. Sector: - Power


Number of Projects	85
Number of Projects on schedule	44
Number of Projects Delayed	39
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status w.r.t Original Schedule:
Out of 85 projects, 44 projects are on schedule, 39 projects are delayed, 1 projects is Wo_Doc_Original and 1 projects is Wo_Odc_Original



Investment Scenario

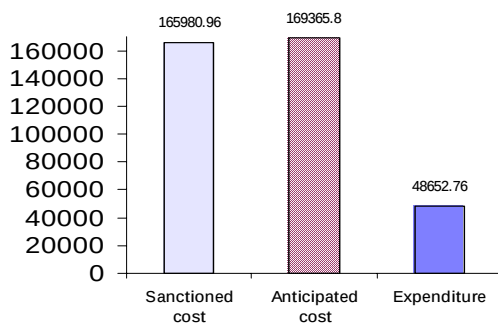


The total cost of implementation of 85 projects when sanctioned, was of the order of Rs. 165980.96 Crores but this was subsequently revised to Rs. 169365.80 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 48652.76 Crores.

6. Sector: - Railways

Number of Projects	150
Number of Projects on schedule	8
Number of Projects Delayed	39
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	59
Number of Projects Wo_Odc_Original	43


Brief Analysis

Project Status w.r.t Original Schedule: Out of 150 projects, 8 projects are on schedule, 39 projects are delayed, 1 projects is ahead. 59 projects are Wo_Doc_Original and 43 projects are Wo_Odc_Original



Investment Scenario

The total cost of implementation of 150 projects when sanctioned, was of the order of Rs. 50032.77 Crores but this was subsequently revised to Rs. 93825.28 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 41119.69 Crores.

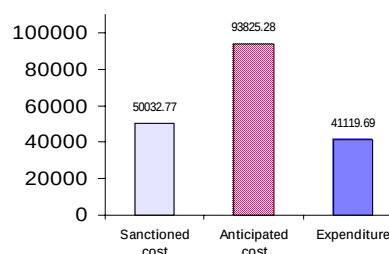


7. Sector: - Road Transport and Highways

Number of Projects	152
Number of Projects on schedule	14
Number of Projects Delayed	134
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 152 projects, 14 projects are on schedule, 134 projects are delayed, 3 projects are ahead and 1 projects is Wo_Doc_Original .



Investment Scenario

The total cost of implementation of 152 projects when sanctioned, was of the order of Rs. 44015.85 Crores but this was subsequently revised to Rs. 44257.13 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 41119.69 Crores.

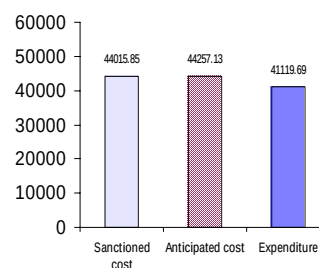


8. Sector: - Shipping and Ports

Number of Projects	18
Number of Projects on schedule	9
Number of Projects Delayed	5
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	2


Brief Analysis

Project Status w.r.t Original Schedule: Out of 18 projects, 9 projects are on schedule, 5 projects are delayed, 2 projects are ahead and 2 projects are Wo_Doc_Original.



Investment Scenario

The total cost of implementation of 18 projects when sanctioned, was of the order of Rs.12475.83 Crores but this was subsequently revised to Rs. 12747.59 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 3247.05 Crores.

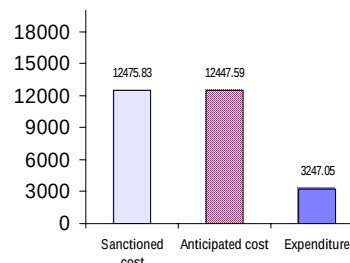


9. Sector: - Steel


Number of Projects	29
Number of Projects on schedule	4
Number of Projects Delayed	23
Number of Projects Wo_Doc_Original	2

Brief Analysis

Project Status w.r.t Original Schedule:
Out of 29 projects, 4 projects are on schedule, 23 projects are delayed and 2 projects are Wo_Doc_Original .



Investment Scenario

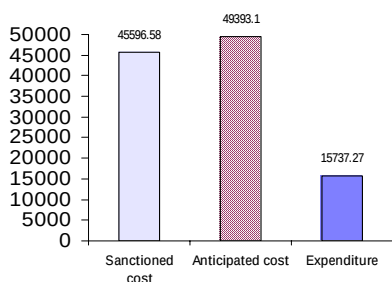


The total cost of implementation of 29 projects when sanctioned, was of the order of Rs. 45596.58 Crores but this was subsequently revised to Rs. 49353.10 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 15737.55 Crores.

10. Sector: - Telecommunications

Number of Projects	28
Number of Projects on schedule	2
Number of Projects Delayed	23
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status w.r.t Original Schedule:
Out of 28 projects, 2 projects are on schedule, 23 projects are delayed and 3 projects are Wo_Doc_Original .



Investment Scenario

The total cost of implementation of 28 projects when sanctioned, was of the order of Rs. 11591.06 Crores but this was subsequently revised to Rs. 11047.28 Crores. The expenditure incurred on these projects till November, 2009 is Rs. 3606.30 Crores.

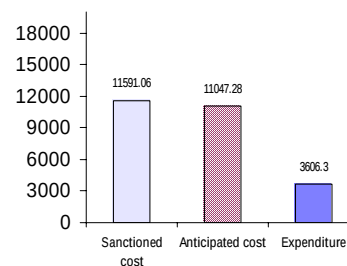

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL) - [020100042]	04/2002	3,072.00 -	3,072.00	2,070.00	02/2008 -	02/2010	24(O)	73/75
2	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00 -	3,282.00	2,476.00	10/2009 09/2007	03/2010	30(R1)	71/75
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	13,171.00	12,446.00	12/2008 -	03/2011	27(O)	61/119
4	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29 -	1,106.29	356.94	04/2011 -	04/2011	0(O)	0/0
5	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	2,049.67	09/2010 -	09/2011	12(O)	8/80
Total			25,054.29 -	26,308.29	19,398.61				213/349
<u>Civil Aviation</u>									
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92 -	290.92	146.12	02/2009 -	10/2009	8(O)	1/24
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING - [N04000016]	10/2006	245.58 295.00	245.58	216.62	12/2008 -	12/2009	12(O)	1/28
8	C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR - [N04000034]	03/2008	129.65 135.72	129.65	29.50	09/2009 -	03/2010	6(O)	0/0
9	C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA - [N04000035]	03/2008	135.04 -	135.04	43.42	09/2009 -	03/2010	6(O)	0/0
10	C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE - [N04000036]	02/2008	135.60 -	135.60	38.05	10/2009 -	03/2010	5(O)	0/0
11	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00 -	535.00	116.05	06/2010 -	06/2010	0(O)	0/0
12	C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A - [N04000039]	08/2008	144.94 -	144.94	20.56	04/2010 -	12/2010	8(O)	0/1
13	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE - [N04000038]	08/2008	1,273.00 1,212.00	1,273.00	221.24	01/2011 -	01/2011	0(O)	0/0
14	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51 -	1,942.51	225.52	05/2011 -	05/2011	0(O)	0/0
Total			4,832.24 -	4,832.24	1,057.08				2/53
<u>Coal</u>									
15	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07 -	254.60	206.93	06/2009 -	12/2009	6(O)	14/21

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC) - [060100088]	10/2004	2,161.28	2,295.93	1,694.77	06/2009	02/2010	8(O)	27/23
17	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,318.57	06/2009	03/2010	9(O)	27/26
18	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	858.28	03/2010	03/2010	0(O)	3/7
19	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53	1,268.53	751.34	03/2010	03/2010	0(O)	2/6
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88	789.88	134.44	03/2010	03/2010	0(O)	0/1
21	BHARATPUR OC EXPANSION PHASE-III PROJECT - [N06000030]	02/2007	131.39	131.39	358.84	03/2010	03/2010	0(O)	0/0
22	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	471.91	03/2009	03/2010	12(O)	0/0
23	KTK OC Sector-I - [N06000077]	01/2008	91.50	128.16	128.16	09/2010	03/2010	-6(O)	0/0
24	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,831.44	06/2009	02/2011	20(O)	20/24
25	LAKHANPUR OC EXP. PROJECT PH-II - [N06000069]	03/2004	98.74	116.54	245.70	03/2007	03/2011	48(O)	0/0
26	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	55.66	03/2010	03/2012	24(O)	0/4
27	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66	471.66	100.37	03/2011	03/2012	12(O)	0/0
28	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04	746.04	134.20	03/2012	03/2012	0(O)	0/1
29	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	249.03	28.42	03/2012	03/2012	0(O)	0/0
30	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18	287.17	-	11/2009	03/2012	28(O)	0/0
31	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	-	03/2012	03/2012	0(O)	0/0
32	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	244.40	03/2012	03/2012	0(O)	0/0
33	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34	212.34	17.34	03/2013	09/2012	-6(O)	2/11
34	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	459.73	08/2012	09/2012	1(O)	0/0
35	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63	453.63	40.54	12/2012	12/2012	0(O)	0/0
36	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	590.59	03/2011 03/2013	03/2013	0(R3)	0/4
37	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 706.40	469.78	12.12	07/2012	03/2013	8(O)	0/1
38	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78	467.78	10.37	03/2013	03/2013	0(O)	0/7
39	KANIHA OCP - [N06000035]	12/2007	457.77	457.77	48.96	03/2012	03/2013	12(O)	0/0
40	JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II - [N06000057]	02/2009	122.35	122.35	-	03/2010	03/2013	36(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	NARAYANKURI UG - [N06000059]	02/2009	149.06	149.06	-	03/2013	03/2013	0(O)	0/0
42	CHITRA EAST OCP - [N06000060]	08/2007	112.69	112.69	-	11/2010	03/2013	28(O)	0/0
43	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93	479.53	171.63	03/2013	03/2013	0(O)	0/0
44	BINA EXTN. PROJ - [N06000019]	11/2006	168.97	168.97	109.90	03/2014	11/2013	-4(O)	1/1
45	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04	1,352.04	27.00	03/2014	03/2014	0(O)	1/1
46	CHURCHA UG - [N06000046]	06/2008	462.35	462.35	235.91	06/2014	03/2014	-3(O)	0/0
47	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	2.76	03/2010	03/2014	48(O)	0/0
48	PENGANGA OC - [N06000066]	10/2008	339.77	339.77	-	03/2014	03/2014	0(O)	0/0
49	KARTALI (EAST) OC - [N06000076]	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
50	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87	395.87	23.23	03/2013	03/2015	24(O)	0/0
51	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0
52	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
53	BAROUD OC EXPANSION - [N06000065]	07/2008	135.58	135.58	23.26	03/2015	03/2015	0(O)	0/0
54	JAGANNATHPOR OC - [N06000075]	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
55	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	54.70	03/2014	03/2016	24(O)	0/0
56	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	5.32	03/2015	03/2016	12(O)	0/0
57	AUGMENTATION OF PRODUCTION AT SAPRI UG MINE - [N06000058]	09/1987	147.86	147.86	25.50	03/2012	-	-	0/0
Total			26,110.40	27,522.73	10,422.29				97/138
<u>Mines</u>									
58	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	18/111
Total			4,091.51	4,091.51	3,316.00				18/111
<u>Steel</u>									
59	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89	607.17	196.14	10/2009	10/2009	0(O)	2/21
60	INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA - [N12000024]	07/2007	123.22	123.22	77.09	06/2009	12/2009	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	157.01	08/2009	01/2010	5(O)	0/0
62	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	209.54	06/2009	01/2010	7(O)	0/0
63	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	88.50	10/2009	01/2010	3(O)	0/0
64	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	53.94	01/2010	01/2010	0(O)	0/0
65	ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE - [N12000049]	06/2008	124.88	119.88	38.18	12/2009	02/2010	2(O)	0/0
66	COAL DUST INJECTION IN BF-2 and 3 - [120100069]	04/2006	132.73	133.92	84.77	05/2008	03/2010	22(O)	0/2
67	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	221.36	09/2009	03/2010	6(O)	0/0
68	REBUILDING OF BLAST FURNACE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	477.12	08/2009	03/2010	7(O)	0/0
69	Pulverised coal injection system for bf-1&2 - [N12000037]	11/2007	125.00	130.00	32.75	09/2009	03/2010	6(O)	0/0
70	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,133.65	03/2010	06/2010	3(O)	0/0
71	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	40.52	06/2010	06/2010	0(O)	0/0
72	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	79.91	02/2010	08/2010	6(O)	0/0
73	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	113.17	04/2010	12/2010	8(O)	0/0
74	Air Separation Plant(ASU-5) - [N12000052]	06/2008	129.50	129.50	3.32	12/2010	12/2010	0(O)	0/0
75	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	81.97	12/2009	01/2011	13(O)	0/0
76	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	96.14	02/2010	01/2011	11(O)	0/0
77	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	244.30	232.93	45.23	07/2009	05/2011	22(O)	0/0
78	INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S - [N12000034]	10/2007	105.33	116.33	9.68	08/2009	05/2011	21(O)	0/0
79	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	4,620.00	10/2009	06/2011	20(O)	0/126
80	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	11.69	10/2009	06/2011	20(O)	0/0
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	4,981.28	07/2010	06/2011	11(O)	0/0
82	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,316.00	584.49	12/2010	10/2011	10(O)	0/0
83	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	-	09/2010	12/2011	15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
84	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	6,171.00	884.34	02/2011	03/2012	13(O)	0/0
85	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	4,792.00	1,207.54	05/2011	09/2012	16(O)	0/0
86	COKING COAL FACILITIES IN COAL HANDLING PLANT - [N12000010]	09/2006	133.91	134.32	103.45	03/2008	-	-	0/3
87	INSTALLATION OF MSDS-V AND TRANSMISSION NETWORK F - [N12000022]	05/2007	143.02	143.02	104.49	11/2008	-	-	0/0
Total			45,596.58	49,353.10	15,737.27				2/152
<u>Petroleum</u>									
88	CLEAN FUELS PROJECT AT VISAKH REFINERY (HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	43(O)	29/45
89	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00	2,869.00	2,355.31	04/2009 12/2009	12/2009	0(R1)	31/36
90	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66	350.00	304.78	06/2008	12/2009	18(O)	0/0
91	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16	1,800.00	1,518.89	12/2008	12/2009	12(O)	0/0
92	CRUDE OIL RECEIPT FACILITIES, KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.09	09/2009	12/2009	3(O)	0/0
93	CHENNAI-BANGALORE PIPELINE - [N16000029]	07/2007	232.11	273.00	205.75	07/2009	12/2009	5(O)	0/0
94	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	666.97	12/2009	12/2009	0(O)	0/0
95	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00	6,898.00	4,299.29	01/2010	01/2010	0(O)	0/0
96	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	165.00	12/2009	01/2010	1(O)	0/0
97	CHAINSAR-JHAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77	571.64	328.56	09/2009	02/2010	5(O)	0/0
98	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10	429.38	483.40	03/2007	03/2010	36(O)	3/3
99	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90	219.22	134.54	03/2006	03/2010	48(O)	6/6
100	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	12,138.00	14,439.00	10,484.79	09/2009 11/2009	03/2010	4(R1)	61/101
101	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13	396.13	44.14	10/2009	03/2010	5(O)	0/0
102	LPG PROCESSING & COMPRESSION - [N16000041]	08/2007	142.00	139.07	40.51	10/2009	04/2010	6(O)	0/0
103	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	2,913.44	11/2009	04/2010	5(O)	0/0
104	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70	706.70	77.64	04/2010	04/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
105	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90	1,030.00	422.98	04/2009	05/2010	13(O)	0/0
106	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	333.40	-	05/2010	05/2010	0(O)	0/0
107	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	9.51	03/2009	05/2010	14(O)	0/0
108	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2010	-2(O)	0/0
109	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	47.60	05/2010	05/2010	0(O)	0/0
110	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	396.73	09/2009	05/2010	8(O)	0/0
111	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	96.17	05/2010	05/2010	0(O)	0/0
112	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]	06/2006	1,431.91	1,646.39	1,169.53	09/2009	06/2010	9(O)	0/0
113	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30	1,339.25	1,135.36	06/2010 06/2010	06/2010	0(R1)	0/0
114	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00	372.00	102.31	02/2010	06/2010	4(O)	0/0
115	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00	356.00	101.42	02/2010	06/2010	4(O)	0/0
116	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00	1,492.00	389.60	04/2010	06/2010	2(O)	0/0
117	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60	293.60	96.63	12/2009	06/2010	6(O)	0/0
118	TWO PIPELINE REPLACEMENT PROJECT AT AHMEDABAD MEHS - [N16000042]	03/2008	188.18	143.84	45.68	06/2010	06/2010	0(O)	0/0
119	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92	1,493.49	595.22	06/2006 05/2008	07/2010	26(R1)	0/2
120	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA - [N16000017]	06/2005	806.00	1,007.83	503.16	03/2008 12/2009	08/2010	8(R1)	18/48
121	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07	1,816.07	5.70	10/2010	10/2010	0(O)	0/0
122	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	0.64	10/2010	10/2010	0(O)	0/0
123	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38	3,000.00	47.00	10/2010	10/2010	0(O)	0/0
124	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00	1,212.85	15.01	10/2011	10/2010	-12(O)	0/0
125	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00	224.00	32.76	12/2010	12/2010	0(O)	0/0
126	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40	605.40	-	12/2010	12/2010	0(O)	0/0
127	CAPACITY AUGMENTATION OF AGRA& FERAZABAD REGION - [N16000074]	07/2009	199.57	199.57	-	01/2011	01/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
128	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09	834.90	929.54	03/2007	03/2011	48(O)	6/6
129	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75	8,061.42	380.20	06/2009	04/2011	22(O)	0/0
130	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93	1,061.78	3.48	11/2011	04/2011	-7(O)	0/0
131	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08	305.08	33.52	04/2011	04/2011	0(O)	0/0
132	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82	1,262.93	1,080.22	03/2005	05/2011	74(O)	0/0
133	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00	349.00	2.40	08/2011	08/2011	0(O)	0/0
134	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00	349.00	5.37	08/2011	08/2011	0(O)	0/0
135	Construction of Tanks and Blending Facility at Vad - [N16000077]	02/2009	267.00	349.00	-	08/2011	08/2011	0(O)	0/0
136	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00	3,597.00	47.79	09/2011	09/2011	0(O)	0/0
137	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00	3,284.00	36.58	09/2011	09/2011	0(O)	0/0
138	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00	756.00	90.33	12/2011	12/2011	0(O)	0/0
139	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35	1,797.35	-	12/2011	12/2011	0(O)	0/0
140	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11	370.11	-	04/2011	12/2011	8(O)	0/0
141	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT - [N16000070]	07/2009	238.68	238.68	-	01/2012	01/2012	0(O)	0/0
142	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	104.64	03/2010 03/2012	03/2012	0(R1)	0/0
143	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78	2,710.10	0.61	03/2010 08/2010	03/2012	19(R1)	0/0
144	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63	1,849.50	5.24	02/2009 09/2010	04/2012	19(R1)	0/0
145	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29	2,853.29	0.54	05/2010	05/2012	24(O)	0/0
146	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	0.54	09/2012	09/2012	0(O)	0/0
147	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	29,777.00	2,344.01	03/2012	11/2012	8(O)	0/0
148	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00	3,032.00	-	12/2012	12/2012	0(O)	0/0
149	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43	4,543.43	-	12/2012	12/2012	0(O)	0/0
150	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18	7,596.18	0.27	01/2013	01/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	-	03/2013	03/2013	0(O)	0/0
	Total		136,018.51	145,750.52	38,189.75				154/247
			-						
	Power								
152	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,018.98	874.82	09/2007	12/2009	27(O)	8/36
			-			-			
153	SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL) - [180100253]	05/2005	279.30	340.14	280.87	07/2009	12/2009	5(O)	5/18
			-			-			
154	SIPAT-II SUPP. TRANS. SYSTEM (PGCIL) - [180100257]	06/2005	813.67	820.45	778.74	06/2008	12/2009	18(O)	9/22
			-			-			
155	KOLDAM HEP TRANSMISSION LINE (PGCIL) - [180100263]	09/2005	464.91	464.91	159.31	09/2008	12/2009	15(R1)	9/22
			-			09/2008			
156	SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN - [N18000020]	10/2006	150.26	153.24	107.32	10/2009	01/2010	3(O)	5/20
			-			-			
157	NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL) - [180100247]	01/2005	691.83	913.33	703.18	12/2007	02/2010	26(O)	13/20
			-			-			
158	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	1,896.65	1,459.58	11/2008	02/2010	15(O)	20/38
			-			-			
159	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI - [N18000021]	01/2007	186.95	186.95	137.10	07/2009	02/2010	7(O)	2/21
			-			-			
160	ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST - [N18000026]	10/2006	103.80	103.80	67.61	06/2009	02/2010	8(O)	0/0
			-			-			
161	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72	836.14	318.70	07/2006	03/2010	44(O)	2/5
			-			-			
162	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45	1,007.16	702.92	12/2007	03/2010	27(O)	7/18
			-			-			
163	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34	266.61	124.54	06/2008	03/2010	21(O)	6/20
			-			-			
164	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]	12/2005	3,779.46	3,779.46	3,164.67	09/2009	03/2010	6(O)	11/30
			-			-			
165	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]	06/2006	803.70	803.76	516.22	06/2009	03/2010	9(O)	0/20
			-			-			
166	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96	975.96	490.72	10/2009	03/2010	5(O)	2/20
			-			-			
167	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-V - [N18000017]	06/2006	721.25	721.25	549.91	06/2009	03/2010	9(O)	4/19
			-			-			
168	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49	290.49	200.99	04/2010	04/2010	0(O)	0/0
			-			-			
169	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52	227.52	84.57	06/2010	06/2010	0(O)	0/0
			-			-			
170	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23	5,221.23	1,775.80	07/2010	07/2010	0(O)	2/20
			-			-			

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
171	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57	353.57	19.81	07/2010	07/2010	0(O)	0/0
172	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50	2,448.49	1,735.90	02/2010	08/2010	6(O)	2/24
173	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69	477.69	179.42	09/2010	09/2010	0(O)	0/0
174	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10	262.10	125.03	09/2010	09/2010	0(O)	0/0
175	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33	5,135.33	3,519.77	10/2010	10/2010	0(O)	8/40
176	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44	2,570.44	1,465.78	08/2010	11/2010	3(O)	10/26
177	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24	557.25	235.51	01/2010	11/2010	10(O)	0/22
178	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72	340.72	81.76	11/2010	11/2010	0(O)	0/0
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55	261.55	59.86	11/2010	11/2010	0(O)	0/0
180	SYSTEM STRAIGHTENING SCHEME-VIII OF SOUTHERN REGION - [N18000070]	02/2008	105.84	105.84	38.94	11/2010	11/2010	0(O)	0/0
181	KOTESHWAR HEP(THDC) - [180100184]	04/2000	1,301.56	1,301.56	1,487.95	04/2005	12/2010	68(O)	0/0
182	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63	1,405.63	259.18	08/2010	12/2010	4(O)	0/0
183	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01	611.02	113.37	08/2010	12/2010	4(O)	0/0
184	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76	417.76	197.65	12/2010	12/2010	0(O)	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36	408.36	208.38	12/2010	12/2010	0(O)	0/0
186	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89	230.89	4.94	01/2011	01/2011	0(O)	0/0
187	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92	1,279.40	1,009.68	03/2007	02/2011	47(O)	1/25
188	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29	1,724.79	229.41	11/2009	02/2011	15(O)	0/0
189	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26	621.28	93.96	02/2011	02/2011	0(O)	0/0
190	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]	10/2006	238.25	238.25	157.16	-	05/2011	-	0/0
191	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	2,242.87	05/2011	05/2011	0(O)	0/0
192	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,304.52	150.84	10/2010	06/2011	8(O)	0/0
193	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	25.13	06/2011	06/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
194	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	35.35	06/2011	06/2011	0(O)	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	249.28	07/2011	07/2011	0(O)	0/0
196	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	112.39	07/2011	07/2011	0(O)	0/0
197	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	3.58	07/2011	07/2011	0(O)	0/0
198	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,061.38	144.60	09/2009	08/2011	23(O)	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIV - [N18000057]	02/2009	132.19	132.19	9.62	08/2011	08/2011	0(O)	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	-	08/2011	08/2011	0(O)	0/0
201	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97	328.97	32.36	09/2011	09/2011	0(O)	0/0
202	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39	8,323.39	6,502.01	12/2009	10/2011	22(O)	33/56
203	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35	4,375.35	727.42	07/2011	11/2011	4(O)	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48	520.48	86.14	11/2011	11/2011	0(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66	509.66	5.33	11/2011	11/2011	0(O)	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69	317.69	2.51	11/2011	11/2011	0(O)	0/0
207	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19	184.19	11.86	11/2011	11/2011	0(O)	0/0
208	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15	4,527.15	2,943.39	04/2009	12/2011	32(O)	19/41
209	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01	421.01	64.24	01/2012	01/2012	0(O)	0/0
210	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96	664.96	18.55	02/2012	02/2012	0(O)	0/0
211	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50	409.50	-	02/2012	02/2012	0(O)	0/0
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29	410.29	13.59	02/2012	02/2012	0(O)	0/0
213	SYSTEM STRENGTHENING SCHEME-IX OF SOUTHERN REGION - [N18000060]	02/2009	120.62	120.62	3.25	02/2012	02/2012	0(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
214	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32	1,347.32	72.38	02/2012	02/2012	0(O)	0/0
215	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03	2,047.03	710.65	01/2012	03/2012	2(O)	2/10
216	PARA HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99	573.99	62.11	08/2012	08/2012	0(O)	0/0
217	MOUDA STPP - [N18000048]	11/2007	5,459.28	5,459.28	660.94	02/2012	08/2012	6(O)	0/0
218	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95	2,360.95	542.28	08/2012	08/2012	0(O)	0/0
219	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33	7,075.33	1,185.60	08/2012	08/2012	0(O)	0/0
220	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12	4,824.12	179.83	10/2012	10/2012	0(O)	0/0
221	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00	5,915.00	411.80	11/2012	11/2012	0(O)	0/0
222	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81	6,230.81	364.92	11/2012	11/2012	0(O)	0/0
223	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33	6,285.33	512.55	09/2010	12/2012	27(O)	2/11
224	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	358.42	6.09	12/2008 09/2010	12/2012	27(R1)	0/15
225	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10	2,895.10	507.06	11/2011	12/2012	13(O)	6/34
226	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	248.91	12/2012	12/2012	0(O)	0/0
227	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,919.59	245.56	09/2009	03/2013	42(O)	1/20
228	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	686.19	03/2013	03/2013	0(O)	5/31
229	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	252.91	07/2010	04/2013	33(O)	0/0
230	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	1,010.74	12/2009 03/2011	05/2013	26(R3)	37/165
231	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	75.96	06/2013	06/2013	0(O)	0/0
232	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	619.47	08/2013	08/2013	0(O)	0/0
233	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	294.33	08/2013	08/2013	0(O)	0/0
234	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,500.68	11/2010	10/2013	35(O)	15/51
235	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	14.69	07/2014	01/2016	18(O)	0/0
236	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			165,980.96	170,229.80	50,299.32				246/920
<u>Health & Family Welfare</u>									
237	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	381.31	03/1999 03/2005	-	-	7/16
Total			71.18	443.15	381.31				7/16
<u>Railways</u>									
238	HAPUR-KANKATHER (LD),NR - [220100278]	04/2003	106.64 117.31	106.64	138.89	03/2007 -	05/2008	14(O)	0/0
239	AMROHA-KANKATHER,NR - [N22000058]	04/2000	57.00 107.29	103.57	106.47	03/2005 09/2008	05/2009	8(R3)	0/0
240	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50 246.50	246.50	296.25	03/2009 03/2009	11/2009	8(R3)	0/0
241	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00 214.09	214.09	112.90	12/2009 -	12/2009	0(O)	0/0
242	KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR - [220100300]	04/1995	49.84 102.90	136.45	114.25	03/2002 -	12/2009	93(O)	0/0
243	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70 129.70	142.48	98.84	12/2008 -	12/2009	12(O)	0/0
244	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74 -	224.51	41.39	- -	12/2009	-	0/0
245	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44 -	209.57	153.00	03/2009 -	02/2010	11(O)	0/0
246	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	430.25	03/1995 -	03/2010	180(O)	0/0
247	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21 157.76	265.00	265.33	03/1998 -	03/2010	144(O)	0/0
248	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 142.98	170.00	93.24	03/2002 -	03/2010	96(O)	0/0
249	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 459.55	571.55	563.79	- -	03/2010	-	0/0
250	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	671.85	03/2001 -	03/2010	108(O)	0/0
251	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 -	281.20	254.62	- -	03/2010	-	0/0
252	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 523.17	960.48	968.52	03/2003 -	03/2010	84(O)	0/0
253	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	501.69	278.12	- -	03/2010	-	0/0
254	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 356.90	425.90	122.08	- 11/2008	03/2010	16(R3)	0/0
255	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	502.14	445.48	- -	03/2010	-	0/0
256	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	743.05	06/2007 -	03/2010	33(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
257	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]	02/1999	180.73 320.66	335.00	297.49	12/2006 12/2008	03/2010	15(R3)	0/0
258	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	219.00	107.83	- -	03/2010	-	0/0
259	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 294.99	546.49	505.55	- 02/2009	03/2010	13(R1)	0/0
260	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 243.20	243.40	185.29	- 02/2009	03/2010	13(R3)	0/0
261	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	452.36	- 03/2009	03/2010	12(R3)	0/0
262	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	4.77	- -	03/2010	-	0/0
263	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 227.52	227.52	218.05	03/2008 03/2009	03/2010	12(R3)	0/0
264	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 137.56	137.57	134.52	03/1998 08/2005	03/2010	55(R3)	0/0
265	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 211.90	211.90	132.13	- 03/2009	03/2010	12(R3)	0/0
266	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	322.87	33.00	- -	03/2010	-	0/0
267	PODAPAHAR-BANSPANI,(LD)(SER) - [N22000046]	04/2006	129.74 129.74	129.74	126.50	03/2006 -	03/2010	48(O)	0/0
268	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	148.27	03/2008 06/2008	03/2010	21(R3)	0/0
269	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	158.95	204.77	- -	03/2010	-	0/0
270	NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I - [N22000078]	09/2007	99.84 99.84	110.94	64.08	03/2010 -	03/2010	0(O)	0/0
271	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 648.76	1,160.52	495.02	- 12/2009	06/2010	6(R3)	0/0
272	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 296.20	296.20	213.63	04/2003 03/2010	06/2010	3(R1)	0/0
273	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	875.14	12/2006 -	06/2010	42(O)	0/0
274	BARAMATI - LONAND (NL), CR - [220100271]	03/1998	75.00 138.48	138.48	35.66	- -	06/2010	-	0/0
275	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 135.10	135.00	116.06	- -	06/2010	-	0/0
276	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	329.70	214.58	03/2009 12/2009	06/2010	6(R1)	0/0
277	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 221.90	221.90	85.60	12/2007 03/2010	07/2010	4(R1)	0/0
278	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
279	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	78.48	- -	09/2010	-	0/0
280	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 273.00	273.00	256.26	- 03/2009	11/2010	20(R1)	0/0
281	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	0.81	02/2015 -	11/2010	-51(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
282	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	130.52	03/2004 -	12/2010	81(O)	0/0
283	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 492.98	672.38	639.30	- -	12/2010	-	0/0
284	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 479.20	567.00	169.98	- 12/2009	12/2010	12(R1)	0/0
285	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 718.30	718.30	608.38	03/2008 03/2009	12/2010	21(R3)	0/0
286	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	251.71	03/2009 12/2009	12/2010	12(R3)	0/0
287	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	245.15	-	12/2010 -	12/2010	0(O)	0/0
288	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,174.00	2,953.68	12/2010 -	12/2010	0(O)	0/0
289	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	311.60	02/2010 -	02/2011	12(O)	0/0
290	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38 -	1,000.00	79.07	- -	02/2011	-	0/0
291	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 810.78	810.78	32.36	- -	02/2011	-	0/0
292	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	356.87	179.71	- 03/2010	03/2011	12(R1)	0/0
293	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 284.27	284.27	251.43	06/1999 -	03/2011	141(O)	0/0
294	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	43.72	- -	03/2011	-	0/0
295	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	456.45	240.05	06/2004 -	03/2011	81(O)	0/0
296	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	334.52	- 06/2009	03/2011	21(R3)	0/0
297	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	371.36	234.34	- -	03/2011	-	0/0
298	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
299	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.30	03/2011 -	03/2011	0(O)	0/0
300	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97 -	196.97	16.78	03/2011 -	03/2011	0(O)	0/0
301	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	22.26	- -	06/2011	-	0/0
302	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69 -	501.69	312.32	03/2010 -	06/2011	15(O)	0/0
303	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 252.50	252.50	23.86	02/2010 -	11/2011	21(O)	0/0
304	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44 576.27	587.08	622.00	- -	12/2011	-	0/0
305	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 735.10	735.10	178.73	- 09/2009	12/2011	27(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
306	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00	496.03	26.64	03/2010	12/2011	21(O)	0/0
307	LUMDING-SILCHAR(GC),NEFR - [220100170]	04/1996	648.00 1,676.31	4,074.10	1,882.64	03/2009	03/2012	36(O)	0/0
308	DLW GM 4000 / 3000 HP DIESEL LOCOS - [220100226]	04/1999	155.54	141.40	103.18	03/2003	03/2012	108(O)	0/0
309	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 238.56	234.45	56.22	-	03/2012	-	0/0
310	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41	322.95	32.59	-	03/2012	-	0/0
311	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59	495.74	50.09	-	03/2012	-	0/0
312	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 324.90	324.90	57.58	03/2010	03/2012	24(O)	0/0
313	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	11,270.00	5,790.47	03/2001	12/2012	141(O)	0/0
314	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08 353.08	462.67	44.03	-	12/2012	-	0/0
315	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00	921.00	236.87	03/2009	12/2012	45(O)	0/0
316	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47	1,480.71	445.84	10/2007	12/2012	62(O)	0/0
317	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20	687.20	39.77	03/2010	12/2012	33(O)	0/0
318	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84	410.08	88.28	-	03/2013	-	0/0
319	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 280.00	899.42	525.58	-	03/2013	-	0/0
320	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70 915.70	1,556.23	106.46	-	03/2013	-	0/0
321	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00 1,500.00	3,087.44	1,610.14	04/2008 12/2011	03/2014	27(R1)	0/0
322	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00 733.00	1,502.29	403.60	12/2008	03/2014	63(O)	0/0
323	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00 156.00	160.48	61.69	-	03/2014	-	0/0
324	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00 200.00	546.47	0.48	-	03/2014	-	0/0
325	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00	5,300.00	60.00	03/2014	03/2014	0(O)	0/0
326	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 727.53	2,492.53	117.67	03/2011	03/2016	60(O)	0/0
327	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77 274.56	432.46	427.70	03/1994	-	-	0/0
328	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 408.43	517.63	309.34	-	-	-	0/0
329	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53 193.61	564.50	461.59	03/1996 06/2009	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
330	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
331	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	231.58	- -	-	-	0/0
332	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0
333	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	310.72	- -	-	-	0/0
334	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
335	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
336	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	518.92	03/2004 03/2005	-	-	0/0
337	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 450.00	730.00	212.91	- -	-	-	0/0
338	KADUR-CHIKMAGALUR-SAKLESHUPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	274.29	71.76	- -	-	-	0/0
339	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.11	281.25	- -	-	-	0/0
340	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	235.94	02/2009 -	-	-	0/0
341	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	103.72	44.83	- -	-	-	0/0
342	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 268.00	268.00	275.41	12/1999 03/2008	-	-	0/0
343	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0
344	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	55.09	- -	-	-	0/0
345	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	89.61	03/2007 03/2007	-	-	0/0
346	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	366.54	0.27	07/2008 -	-	-	0/0
347	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	540.09	07/2005 -	-	-	0/0
348	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	311.43	05/2008 -	-	-	0/0
349	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	- -	-	-	0/0
350	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	61.00	- -	-	-	0/0
351	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
352	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	123.21	- 05/2009	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
353	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15 -	381.17	80.12	- -	-	-	0/0
354	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
355	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	57.38	- -	-	-	0/0
356	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	364.06	- -	-	-	0/0
357	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 329.05	695.00	9.41	- -	-	-	0/0
358	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	901.62	0.28	- -	-	-	0/0
359	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	111.90	278.36	03/2005 12/2008	-	-	0/0
360	SURAT-KOSAMBA (LD),WR - [220100281]	04/2000	133.00 -	133.00	-	- -	-	-	0/0
361	TANUR (KUTTIPURAM) GURUVAYUR (NL) (SR) - [220100283]	04/1995	40.00 -	137.71	8.97	- -	-	-	0/0
362	REWARI-SADULPUR-HISSAR (GC),NWR - [220100290]	04/1997	198.96 364.19	410.00	377.20	- -	-	-	0/0
363	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	459.91	36.40	- -	-	-	0/0
364	BARBIGHA - SHEKHPURA + NEORA-DANIAWAN (NL), ECR - [220100309]	04/2002	120.23 -	120.23	220.17	- -	-	-	0/0
365	BIHARSHARIFF-BARBIGHA (NL), ECR - [220100310]	04/2001	103.86 -	103.86	28.93	- -	-	-	0/0
366	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	104.79	34.13	- -	-	-	0/0
367	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	230.44	03/2006 -	-	-	0/0
368	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	726.05	105.14	- -	-	-	0/0
369	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	104.10 -	113.75	40.35	- -	-	-	0/0
370	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
371	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73 -	230.03	45.76	- -	-	-	0/0
372	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	102.78	- -	-	-	0/0
373	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
374	BHATNI-JIRADEI PATCH DOUBLING (NER) - [N22000029]	04/2006	100.27 -	100.27	0.01	- -	-	-	0/0
375	MUNDERWA-BABHNAN PATCH DOUBLING(NER) - [N22000030]	04/2006	102.10 -	102.10	22.75	- -	-	-	0/0
376	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	670.00	0.74	- -	-	-	0/0
377	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92 261.70	283.10	1.86	02/2006 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
378	SETTING UP EAST COAST RLY.ZN. (SER) - [N22000054]	04/1997	41.67 -	129.78	90.84	- -	-	-	0/0
379	PATTABIRAM-ARAKKONAM,SR - [N22000057]	04/2002	71.94 -	124.00	151.76	03/2004 07/2008	-	-	0/0
380	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]	09/2007	404.19 404.19	711.15	33.01	- -	-	-	0/0
381	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 343.17	639.00	154.10	- -	-	-	0/0
382	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00 170.00	255.96	54.67	- -	-	-	0/0
383	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 125.00	227.40	10.71	- -	-	-	0/0
384	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 456.00	582.83	20.54	- -	-	-	0/0
385	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00 300.00	529.88	18.34	- -	-	-	0/0
386	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 254.07	676.00	272.38	- 12/2011	06/2011	-6(R3)	0/0
387	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	127.51	- 12/2012	12/2012	0(R1)	0/0
Total			50,032.77 -	93,825.28	41,119.69				0/0
<u>Road Transport & Highways</u>									
388	CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213 - [240106232]	03/2005	133.03 -	133.03	244.00	08/2005 -	10/2009	50(O)	0/0
389	JAWAHARLAL NEHRU PORT PHASE-II,SH-54 - [N24000039]	04/2000	143.00 -	143.00	120.30	05/2007 -	10/2009	29(O)	0/0
390	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93 -	440.93	595.57	12/2006 -	12/2009	36(O)	0/0
391	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39 -	534.39	643.69	05/2007 -	12/2009	31(O)	0/0
392	BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5) - [240101151]	04/2000	140.85 -	140.85	148.01	01/2004 -	12/2009	71(O)	0/0
393	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49 -	367.49	416.56	03/2005 -	12/2009	57(O)	0/0
394	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40 -	372.40	380.72	07/2004 -	12/2009	65(O)	0/0
395	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00 -	480.00	742.90	11/2007 -	12/2009	25(O)	0/0
396	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06 -	158.06	137.40	08/2005 -	12/2009	52(O)	0/0
397	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00 -	276.00	309.30	04/2008 -	12/2009	20(O)	0/0
398	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00 -	310.00	321.00	04/2008 -	12/2009	20(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
399	GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73 - [240106231]	12/2003	266.00	288.06	312.80	08/2007	12/2009	28(O)	0/0
400	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	448.30	03/2009	12/2009	9(O)	0/0
401	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	568.50	03/2009	12/2009	9(O)	0/0
402	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	12/2009	14(O)	0/0
403	SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4) - [N24000029]	12/2003	100.50	100.50	145.90	04/2008	12/2009	20(O)	0/0
404	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	132.40	06/2008	12/2009	18(O)	0/0
405	TOVARAMKURCHI-MADURAI, NH45B (NHAI) - [N24000054]	04/2000	263.00	263.00	311.44	08/2008	12/2009	16(O)	0/0
406	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]	03/2005	168.00	168.00	227.70	12/2008	12/2009	12(O)	0/0
407	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80	402.80	453.70	03/2009	12/2009	9(O)	0/0
408	PANIPAT TO PANCHI GUJRAN, NH-1 - [N24000066]	12/2003	109.00	109.00	131.00	10/2008	12/2009	14(O)	0/0
409	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	23.82	04/2009	12/2009	8(O)	0/0
410	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	636.10	05/2009	12/2009	7(O)	0/0
411	SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS - [N24000086]	03/2005	110.00	110.00	107.90	07/2008	12/2009	17(O)	0/0
412	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00	450.00	868.21	07/2008	12/2009	17(O)	0/0
413	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	-	05/2010	12/2009	-5(O)	0/0
414	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	447.13	03/2005	01/2010	58(O)	0/0
415	MADURAI -KANIYAKUMARI SECTION (NS-41/TN) NH-7, KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.80	03/2008	01/2010	22(O)	0/0
416	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	665.80	12/2008	01/2010	13(O)	0/0
417	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	749.60	11/2010	01/2010	-10(O)	0/0
418	MADURAI -KANNIYAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	283.90	03/2008	02/2010	23(O)	0/0
419	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	197.10	01/2009	02/2010	13(O)	0/0
420	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]	03/2005	557.00	557.00	737.90	02/2010	02/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
421	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	388.44	03/2005	03/2010	60(O)	0/0
422	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	240.90	07/2004	03/2010	68(O)	0/0
423	DEVDHARI-KELAPUR - [240106207]	12/2003	144.00	144.00	95.12	07/2005	03/2010	56(O)	0/0
424	BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7 - [240106210]	12/2003	110.00	110.00	105.70	06/2005	03/2010	57(O)	0/0
425	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	339.71	02/2009	03/2010	13(O)	0/0
426	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00	261.00	282.30	08/2008	03/2010	19(O)	0/0
427	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	137.10	06/2008	03/2010	21(O)	0/0
428	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]	12/2003	360.42	360.42	308.90	11/2009	03/2010	4(O)	0/0
429	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]	03/2005	445.00	445.00	664.82	07/2010	03/2010	-4(O)	0/0
430	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	85.61	08/2006	04/2010	44(O)	0/0
431	KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7 - [240102202]	01/2004	120.00	120.00	84.51	09/2006	04/2010	43(O)	0/0
432	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	79.54	03/2008	04/2010	25(O)	0/0
433	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	151.20	08/2009	04/2010	8(O)	0/0
434	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	154.20	08/2009	04/2010	8(O)	0/0
435	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	197.60	08/2009	04/2010	8(O)	0/0
436	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	133.50	08/2009	04/2010	8(O)	0/0
437	CHITRADURGA BY PASS (GQ) KM.207-KM.189 (NH-4) - [240101134]	04/2000	104.00	104.00	143.28	08/2004	05/2010	69(O)	0/0
438	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	104.20	03/2008	05/2010	26(O)	0/0
439	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	480.20	04/2009	05/2010	13(O)	0/0
440	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	123.50	10/2008	05/2010	19(O)	0/0
441	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	64.42	05/2010	05/2010	0(O)	0/0
442	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	114.60	09/2007	06/2010	33(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
443	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	40.30	08/2004	06/2010	70(O)	0/0
444	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	405.80	11/2007	06/2010	31(O)	0/0
445	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	246.79	10/2008	06/2010	20(O)	0/0
446	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	277.42	10/2008	06/2010	20(O)	0/0
447	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	294.60	10/2008	06/2010	20(O)	0/0
448	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	224.20	10/2008	06/2010	20(O)	0/0
449	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	271.01	10/2008	06/2010	20(O)	0/0
450	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	383.00	04/2008	06/2010	26(O)	0/0
451	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	321.80	06/2008	06/2010	24(O)	0/0
452	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	334.20	06/2008	06/2010	24(O)	0/0
453	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	163.90	10/2008	06/2010	20(O)	0/0
454	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	136.70	07/2008	06/2010	23(O)	0/0
455	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	375.80	06/2008	06/2010	24(O)	0/0
456	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	140.00	06/2008	06/2010	24(O)	0/0
457	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	171.20	06/2009	06/2010	12(O)	0/0
458	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	06/2010	15(O)	0/0
459	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	146.90	11/2008	06/2010	19(O)	0/0
460	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	533.50	06/2009	06/2010	12(O)	0/0
461	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	184.77	02/2004	06/2010	76(O)	0/0
462	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	175.70	09/2009	06/2010	9(O)	0/0
463	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	172.40	09/2008	06/2010	21(O)	0/0
464	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	237.53	06/2010	06/2010	0(O)	0/0
465	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	223.00	03/2010	06/2010	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
466	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]	12/2003	407.60	407.60	177.60	06/2010	06/2010	0(O)	0/0
467	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	238.40	09/2009	06/2010	9(O)	0/0
468	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	127.10	06/2010	06/2010	0(O)	0/0
469	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	38.82	08/2004	07/2010	71(O)	0/0
470	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.60	07/2010	07/2010	0(O)	0/0
471	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	07/2010	0(O)	0/0
472	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	321.10	07/2010	07/2010	0(O)	0/0
473	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	563.64	07/2010	07/2010	0(O)	0/0
474	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	666.20	03/2010	07/2010	4(O)	0/0
475	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	99.85	06/2008	08/2010	26(O)	0/0
476	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	245.20	08/2010	08/2010	0(O)	0/0
477	LUCKNOW-BYPASS (EW) (NS & EW-PH-I) NH-25 & NH-28 VIA NH-56 - [240103192]	04/2000	182.52	111.78	0.59	06/2004	09/2010	75(O)	0/0
478	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	230.40	03/2005	09/2010	66(O)	0/0
479	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]	12/2003	198.00	198.00	66.84	11/2008	09/2010	22(O)	0/0
480	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	214.80	09/2009	09/2010	12(O)	0/0
481	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	183.20	09/2009	09/2010	12(O)	0/0
482	LUMDING TO DABOKA - [N24000110]	12/2003	130.00	130.00	23.87	08/2010	09/2010	1(O)	0/0
483	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	275.60	09/2010	09/2010	0(O)	0/0
484	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	170.80	10/2009	10/2010	12(O)	0/0
485	KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20,NH-1A - [240102193]	04/2000	110.00	110.00	139.20	12/2004	12/2010	72(O)	0/0
486	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	576.60	04/2007	12/2010	44(O)	0/0
487	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00	275.00	267.50	09/2007	12/2010	39(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
488	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	117.10	09/2007	12/2010	39(O)	0/0
489	JAM-WADNER - [240106209]	12/2003	145.00	145.00	68.18	07/2005	12/2010	65(O)	0/0
490	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	89.65	06/2005	12/2010	66(O)	0/0
491	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	276.40	05/2008	12/2010	31(O)	0/0
492	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00	227.00	189.82	10/2008	12/2010	26(O)	0/0
493	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68	340.68	201.10	03/2008	12/2010	33(O)	0/0
494	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	280.00	106.60	02/2009	12/2010	22(O)	0/0
495	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81	199.81	27.54	04/2009	12/2010	20(O)	0/0
496	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64	167.64	39.49	11/2008	12/2010	25(O)	0/0
497	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	155.04	27.96	11/2008	12/2010	25(O)	0/0
498	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00	200.00	36.15	04/2009	12/2010	20(O)	0/0
499	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00	225.00	86.47	06/2008	12/2010	30(O)	0/0
500	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]	12/2003	195.00	195.00	84.06	06/2008	12/2010	30(O)	0/0
501	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00	242.00	268.90	12/2008	12/2010	24(O)	0/0
502	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00	227.00	238.70	12/2008	12/2010	24(O)	0/0
503	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]	12/2003	237.80	237.80	81.15	06/2008	12/2010	30(O)	0/0
504	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94	332.94	124.40	09/2008	12/2010	27(O)	0/0
505	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30	151.30	83.78	10/2008	12/2010	26(O)	0/0
506	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43	203.43	63.28	10/2008	12/2010	26(O)	0/0
507	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]	12/2003	251.03	251.03	62.13	10/2008	12/2010	26(O)	0/0
508	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91	229.91	29.18	10/2008	12/2010	26(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
509	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	48.88	04/2008	12/2010	32(O)	0/0
510	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	75.54	06/2008	12/2010	30(O)	0/0
511	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	186.20	03/2008	12/2010	33(O)	0/0
512	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	76.14	04/2008	12/2010	32(O)	0/0
513	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	108.20	06/2008	12/2010	30(O)	0/0
514	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	59.45	04/2008	12/2010	32(O)	0/0
515	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	51.60	05/2008	12/2010	31(O)	0/0
516	NALBARI TO BIJNI (AS-9) - [N24000050]	12/2003	142.00	142.00	105.90	06/2008	12/2010	30(O)	0/0
517	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	78.52	06/2008	12/2010	30(O)	0/0
518	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	33.80	09/2007	12/2010	39(O)	0/0
519	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.32	07/2009	12/2010	17(O)	0/0
520	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	60.80	04/2010	12/2010	8(O)	0/0
521	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	165.70	02/2010	12/2010	10(O)	0/0
522	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	368.34	10/2009	12/2010	14(O)	0/0
523	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	188.30	12/2009	12/2010	12(O)	0/0
524	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	-	02/2004	12/2010	82(O)	0/0
525	TRICHY - DINDIGUAL NH-45 - [N24000099]	03/2005	576.00	576.00	170.40	07/2010	01/2011	6(O)	0/0
526	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	266.60	01/2011	01/2011	0(O)	0/0
527	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	169.30	01/2011	01/2011	0(O)	0/0
528	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	102.10	09/2007	02/2011	41(O)	0/0
529	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	179.10	07/2005	03/2011	68(O)	0/0
530	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	188.40	07/2005	03/2011	68(O)	0/0
531	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	139.70	10/2008	03/2011	29(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
532	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	192.30	09/2008	03/2011	30(O)	0/0
533	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	78.70	09/2010	03/2011	6(O)	0/0
534	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	363.70	05/2010	05/2011	12(O)	0/0
535	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	38.29	09/2008	06/2011	33(O)	0/0
536	KELARPUR-PIMPALKATTI-KM 153 TO KM 175 - [240106283]	12/2003	117.40	117.40	29.83	11/2008	06/2011	31(O)	0/0
537	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	241.53	-	04/2004	10/2011	90(O)	0/0
538	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
539	DEVDHARI-WADNER - [240106208]	12/2003	145.00	145.00	24.71	07/2005	-	-	0/0
	Total		44,015.85	44,257.13	33,088.51				0/0
Shipping & Ports									
540	CONSTRUCTION OF CAR /CLEAN CARGO TERMINAL - [N25000034]	01/2009	100.00	100.00	0.50	01/2010	01/2010	0(O)	0/0
541	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	65.60	12/2005	03/2010	51(O)	0/0
542	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	129.44	06/2007 01/2009	03/2010	14(R1)	0/0
543	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	342.92	03/2010	03/2010	0(O)	0/0
544	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	368.23	07/2010	07/2010	0(O)	0/0
545	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	809.61	10/2008	11/2010	25(O)	0/0
546	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	274.01	04/2009	11/2010	19(O)	0/0
547	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	241.64	11/2010	11/2010	0(O)	0/0
548	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
549	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
550	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	882.00	0.16	02/2011	02/2011	0(O)	0/0
551	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	702.00	0.73	03/2011	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
552	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	200.91	04/2011	04/2011	0(O)	0/0
553	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	341.48	04/2011	12/2011	8(O)	0/0
554	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
555	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
556	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.24	10/2008	-	-	0/0
557	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
	Total		12,475.83	12,747.59	3,247.05				0/0
Telecommunications									
558	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	10/2009	46(O)	0/0
559	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	34(O)	0/0
560	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	119.28	02/2008	10/2009	20(O)	0/0
561	500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB - [N26000038]	04/2007	134.25	133.75	34.05	06/2008	10/2009	16(O)	0/0
562	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	278.16	278.16	157.32	12/2008	10/2009	10(O)	0/0
563	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007	11/2009	33(O)	0/0
564	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]	06/2007	336.81	174.36	64.50	01/2009	11/2009	10(O)	0/0
565	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007	12/2009	34(O)	0/0
566	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	92.61	10/2007	12/2009	26(O)	0/0
567	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	12/2009	20(O)	0/0
568	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	15(O)	0/0
569	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	399.77	12/2008	12/2009	12(O)	0/0
570	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	81.36	03/2009	12/2009	9(O)	0/0
571	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	155.56	12/2008	12/2009	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
572	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	483.54	470.24	12/2008	12/2009	12(O)	0/0
573	GSM EQUIPMENT OF 1162K LINES PH-4.5 - [N26000045]	03/2008	325.00	325.00	233.23	12/2008	12/2009	12(O)	0/0
574	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	177.49	03/2009	12/2009	9(O)	0/0
575	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	10.96	03/2009	12/2009	9(O)	0/0
576	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	463.61	66.50	12/2009	12/2009	0(O)	0/0
577	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]	01/2009	149.15	149.15	40.87	06/2009	12/2009	6(O)	0/0
578	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	366.00	-	09/2009	12/2009	3(O)	0/0
579	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53	180.53	9.86	12/2009	12/2009	0(O)	0/0
580	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.16	12/2004	02/2010	62(O)	0/0
581	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	29.32	09/2009	06/2010	9(O)	0/0
582	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	06/2010	10(O)	0/0
583	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
584	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	135.00	94.77	06/2006	-	-	0/0
585	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
Total			11,591.06	11,047.28	3,606.30				0/0
<u>Urban Development</u>									
586	C/O GENERAL POOL OFFICE COMPLEX AT INA - [N28000016]	10/2004	83.67	135.03	-	02/2010	02/2010	0(O)	0/0
587	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00	8,676.00	11,807.84	06/2010	10/2010	4(O)	0/7
588	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	6,395.00	1,636.24	12/2011	12/2011	-9(R3)	0/0
Total			14,596.67	15,206.03	13,444.08				0/7
<u>Water Resources</u>									
589	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
Total			542.90	1,187.00	35.49				0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Grand Total			541,010.75	606,801.65	233,342.75				739/1993
