

**301th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
November, 2010**



Madurai Airport



**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary	1 -7
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	8-12
List of Delete Projects	13-13
Summary of Projects	14-22
Sector wise Trend and Graphicalf Analysis	23-31
Sector wise analysis of projects	32-61
Graph	62-72
List of All Ongoing Projects	73-73
List of Abbreviations	74-75

EXECUTIVE SUMMARY

The 301th Flash Report for November' 2010, that contains information on the status of 572 projects in the Central Sector, each costing ` 150 Crores and above. Since April' 2010, Flash report is prepared for the central sector projects costing `150 Crores and above. During November' 2010, 12 projects reported completion and have been dropped from the monitor of this Ministry. In addition 1 project has been deleted due to merger with other packages of the same project. Twenty new projects have been added during the month under reference.

The online submission of the implementation Status Report of the ongoing projects has been improved as in November, 2010 nearly 89% projects are reported online. Out of 572 ongoing projects on the monitor of this Ministry, 505 projects were updated online by the concerned project agencies. Sector-wise number of ongoing projects along with status of online reporting is given below:

S. No.	Sector	Projects on monitor	Reported Online	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	123	117	30
2.	RAILWAYS	147	117	3
3.	POWER	83	75	20
4.	PETROLEUM	70	59	17
5.	COAL	44	44	7
6.	TELECOMMUNICATION	42	42	1
7.	STEEL	19	12	5
8.	SHIPPING & PORTS	22	21	-
9.	CIVIL AVIATION	8	8	1
10.	FERTILISERS	6	5	1
11.	ATOMIC ENERGY	4	2	1
12.	URBAN DEVELOPMENT	2	2	1
13.	MINES	1	1	-
15.	WATER RESOURCES	1	-	-
Total		572	505	87

2. Eighty seven (87) projects have reported additional delays compared to the completion dates in the previous month during November' 2010.

3. The additional delays are in the range of 1 to 28 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Telecommunications, Civil Aviation, Atomic Energy, Fertilizers and Urban Development Sectors.

4. Out of 572 projects, 9 projects are ahead of schedule, 133 are on schedule and 291 projects are delayed. Of the balance, 78 projects do not have fixed dates of commissioning i.e. either the year of commissioning or the tentative gestation period of the projects have been reported. A large number of projects (61) were sanctioned without any commissioning schedule/date.

5. The total original cost of implementation of 572 projects ` 592196.97 Crores and their anticipated completion cost is ` 714501.64 Crores implying a cost overrun of 20.70%. The expenditure incurred on these projects till November, 2010 is ` 304331.57 Crores which is 42.60% of the revised cost of the projects.

6. Out of 572 projects, presently on the monitor at the end of November 2010, 133 projects were on schedule (23%), excluding 78 projects without date of commissioning and those have not reported during the month, 291 projects were delayed (51%). During the month, 87 projects have reported additional delays in the range of 1-28 months. The analysis of pictorial presentation shows that since July, 2010 the marginal decrease in projects reporting delays have been noticed. The overall cost overrun has somewhat constant since July 2010. It may be seen that out of 291 delayed projects, at the end of November, 2010, 71 projects had overall delay in the range of 1 to 12 months, 77 projects had delay in the range of 13 to 24 months, 114 projects had delay in the range of 25 to 60 months and 29 projects had time overrun of 61 months and above. To present a concise picture of the status of on-going projects costing ₹ 150 Crores and above, a pictorial presentation is given in the report.

7. In the **Coal sector**, 7 projects have shown additional delays in the range of 2-27 months Churi Benti UG CCL, Ashok expansion OCP and North Urimari OCP CCL have shown considerable improvement of 24 months, 9 months and 9 months without reporting any reason. Barsingsar TPS has reported additional delay of 2 month due to slow progress by the contractor. Adriyala Shaft Project SCCL has reported additional delay of 9 months due to delay in diverges. Kakatiya Longowall SCCL has reported addition delay of 27 months due to delay in selection of TPO. TPS-II Expansion, NLC have reported additional delays of 4 months, however, no specific reason has been given by the project authority.

8. In the **Steel Sector**, 5 projects have reported additional delay of 1-9 months. Expansions of Salem Steel Plant Sail have reported considerable improvement of 1 month over the completion schedule

reported earlier. Installation of Rebuilding of coke oven battery No. 1 & 2 have reported additional delays of 1 month however, no specific reason has been given by the project authority. STEM Emergency Power Requirement RINL have reported additional delay of 7 months due to delay in supply of BHEL. Expansion of IISCO Steel Plant SAIL has reported additional delay of 6 months due to delay in supply of equipments. Expansion of RINL/Vishakhapatnam Steel Plant has reported delay of 9 months due to Poor mobilization by Contractors and due to lack of erection equipments.

9. In the **Petroleum Sector**, 17 projects have reported additional delays in the range of 1-12 months. Kochi- Kanjirkod Bangalore-Mangalore Pipeline Project Phase-I (GAIL) and Dhabol-Bangalore Pipeline Project Phase –I (GAIL) have reported considerable improvement of 12 months and 9 months over the completion schedule reported earlier. MSQ Improvement project (IOCL) has reported additional delay of 5 months delay, however no specific reasons have been reported by project authority. MSQ Upgradation Project at Guwahati Refinery and MSQ Upgradation Project at Digboi Refinery have reported additional delay of 7 months and 1 month due to poor response to consultancy bids, frequent bands and insufficient transportation of material/equipment. MSQ Upgradation Project at Barauni Refinery has reported additional delay of 1 month due to backing out of reputed PSU consultants in last moment and slow progress by M/S BHEL in power plant. BNPL Spurline (Uttaranchal & Punjab) & Diesel Hydro Treatment Project (BRPL) project have reported additional delay of 1 month and 3 months due to slow progress by the contractor. North Tapti Gas Field Dev. ONGC project, C2-C3 and LPG Recovery from LNG, Dahej (ONGC), Refrigerated LPG Storage at JNPT BPCL, Integrated Offshore crude Oil handling facilities at Paradip and Additional Development of D-1 Field ONGC projects have reported additional delays of 2 months, 4 months, 3 months, 3 months and 6 months, however no specific reasons have been given by the project authorities. Vijaypur Dadri-Bawana Pipe line Project (GAIL) has reported additional delay of 3 months due to resistance from farmers demanding high compensation. Jagdishpur Haldia Pipeline Project Phase-I (GAIL) has reported additional delay of 10 months due to synchronize action with the revival of Fertilizer Plants reroute and availability of Gas at Haldia Landball point. Revamping of Win Platform at MH Asset ONGC has reported additional delays of 12 months, however, no specific reason has been given.

10. In the **Power Sector**, 20 projects have reported additional delays in the range of 1-18 months. Kundankulam-Atomic Power Plant Transmission System (PGCIL) has reported considerable improvement of 6 months over the completion schedule reported earlier. Transmission System

Associated with Barh Generation Project, Power Grid Corporation of India Ltd has reported additional delay of 3 months to match the requirement of linked Generation project. BARH STPP, 3x660 MW, and Chamara Hydro Electric Project Stage III (NHPC) have reported additional delay of 5 months and 8 months respectively, however, no specific reasons have been given by the project authorities. Nimoo Bazoo Hydro Electric Project has reported additional delay of 9 months due to highly inclement weather condition. Western Region Transmission Strengthening Scheme has reported additional delay of 4 months to match with the linked generation project. Western Region Strengthening Scheme VI have reported additional delay of 4 months however, no specific reason has been given. Eastern Region Strengthening Scheme -1 PGCIL project has reported additional delay of 3 months due to ROW problems in Jharkhand and West Bengal and delay in permission of forest clearance by Orissa Government. Parbati HEP Stage-III (NHPC) project has reported additional delay of 16 months due to poor geological conditions at tunnel boring machine (TBM) of the project. Parbati HEP Stage-II (NHPC) project has reported additional delay of 6 months, due to copiously leakage of mountain water. Chutak Hydro Electric Project and URI HEP Stage-II (NHPC) have reported additional delay of 6 months and 9 months respectively, due to civil disturbance in Kashmir Valley and indefinite bandhs /strikes. Bongaigaon Thermal Power Project (NTPC) has report additional delay of 7 months due to slow progress by civil agency. Lower Subansiri HEP (NHPC) has reported additional delay of 12 months due to damaged bridge at NH-52, anti dam activities and delay in signing of MOU by State Government. Koteswar HEP (THDC) has reported additional delay of 15 months, however, no specific reason has been given by the project authority. Koldam HEP (NTPC) has reported additional delay of 12 months; however, no specific reason has been given by the project authority. Rampur HEP (412 MW) SJVNL has reported additional delay of 18 months, due to major factors of natural surprises which have extensively effected the progress of excavation of HRT.

11. In the **Road Transport and Highways Sector**, 30 projects (Table VIII may be referred) have reported additional delay in the range of 1-28 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, utility shifting, Termination of contracts due to poor performance and delay in getting the forest clearance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such additional delays.

12. In the **Fertilizer Sector**, Thal Ammonia Revamp Project RCF has reported additional delay of 8 months due to difficulties in finalization of specifications of turbines of BFW Pump and Cooling water pump, Benfield Absorber modification and primary reformer Burner modification.

13. In the **Railway Sector**, 3 projects have shown additional delays in the range of 1-6 months. Muzaffarpur-Sitamarhi (NL), Deoghar –Dumka New BG Line (Double) and Mumbai Urban Transport Project Phase-I have reported additional delay of 1 month, 3 months and 6 months, however, the project authorities have not mentioned any specific reason for such additional delays.

14. In the **Telecommunication Sector**, ERP Implementation in BSNL on Turkey basis has shown additional delays of 5 months, however, no specific reasons have been given by the project authorities.

15. In the **Urban Development Sector**, Delhi MRTS Phase-II Project has reported additional delay of 2 months due to delay in releasing of funds.

16. In the **Civil Aviation Sector**, Construction of RCC/PRE Stressed Concrete Bridge K3 AAI has shown additional delays of 3 months due to slow progress by Contractors.

17. In the **Atomic Energy Sector**, Kudankulam APP (NPCIL) has shown additional delays of 6 months due to slow progress by Contractors.

Status as on 01.12.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the Report.



(Pankaj Jain)

Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	147	3
2	Road Transport & Highways	123	30
3	Power	83	20
4	Petroleum	70	17
5	Coal	44	7
6	Telecommunications	42	1
7	Shipping & Ports	22	0
8	Steel	19	5
9	Civil Aviation	8	1
10	Fertilisers	6	1
11	Atomic Energy	4	1
12	Urban Development	2	1
13	Mines	1	0
14	Water Resources	1	0
	Total	572	87

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	168.33	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93
September,2010				
<u>Coal</u>				
8	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)(NEYVELI LIGNITE CORPORATION) - [060100090]	254.07	06/2009	1,687.78
<u>Steel</u>				
9	REBUILDING OF COKE OVEN BATTERY-10(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000016]	416.50	09/2009	305.14
<u>Petroleum</u>				
10	PANIPAT NAPHTHA CRACKER PROJECT(INDIAN OIL CORPORATION LIMITED) - [160100292]	12,138.00	09/2009	12,054.37

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	DADRI- PANIPAT R-LNG SPUR PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000018]	250.66	06/2008	350.96
12	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000026]	638.90	04/2009	796.21
13	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE(INDIAN OIL CORPORATION LIMITED) - [N16000034]	348.00	12/2009	186.58
14	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000035]	1,131.00	12/2009	750.71
15	CHAINSAR-JHAJJAR PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000047]	967.77	09/2009	416.90
16	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000067]	643.46	-	726.45
17	Construction of Tank and Blending Facility at Vadi(INDIAN OIL CORPORATION LIMITED) - [N16000075]	267.00	-	72.99
18	BINA DESPATCH TERMINAL(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000078]	490.71	12/2009	590.52
<u>Railways</u>				
19	HOSPET-GUNTAKAL(LD),SCR(RAIL VIKAS NIGAM LTD.) - [220100195]	105.22	12/1999	283.49
20	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100224]	536.85	03/2003	1,005.50
21	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)(RAIL VIKAS NIGAM LTD.) - [220100244]	223.00	-	586.85
22	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000033]	352.00	03/2008	616.44
23	ABOHAR- FAZILKA, NR, NL(NORTHERN RAILWAY) - [N22000055]	86.44	03/2009	201.79
<u>Road Transport & Highways</u>				
24	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100203]	440.93	12/2006	641.40
25	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100204]	534.39	05/2007	716.15
26	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101178]	372.40	07/2004	406.05
27	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101181]	467.93	03/2005	453.64
28	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101187]	399.75	03/2005	424.96
29	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106227]	276.00	04/2008	360.00
30	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106228]	310.00	04/2008	392.26
31	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106241]	507.49	03/2008	342.80
32	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106257]	556.00	03/2009	568.50
33	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106273]	469.80	12/2008	665.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
34	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106285]	261.00	08/2008	286.30
35	TOVARAMKURCHI-MADURAI, NH45B (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000054]	263.00	08/2008	317.74
36	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000060]	402.80	03/2009	453.70
37	PADALUR-TRICHY, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000083]	320.00	05/2009	636.10
38	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000093]	360.42	11/2009	478.40
39	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000105]	450.00	07/2008	876.61
40	ISLAM NAGAR TO KADTAL(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000109]	546.83	03/2010	667.80
41	WAINGANGA BRIDGE -CHHATISGARH-MAHARASHTRA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000120]	424.00	09/2010	298.40
<u>Shipping & Ports</u>				
42	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS(SHIPPING crp. of india) - [N25000013]	411.32	03/2010	406.28
43	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA(PORT TRUST) - [N25000046]	2,118.00	11/2004	.00
<u>Telecommunications</u>				
44	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I(DEPARTMENT OF TELECOMMUNICATION) - [260100051]	279.97	12/2004	136.24
45	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA(BHARAT SANCHAR NIGAM LIMITED) - [260100095]	1,174.75	03/2006	371.41
46	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000026]	741.77	10/2007	151.37
47	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-(BHARAT SANCHAR NIGAM LIMITED) - [N26000028]	364.52	-	51.44
48	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000042]	409.21	12/2008	470.24
49	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000061]	180.53	12/2009	25.97
October,2010				
<u>Health & Family Welfare</u>				
50	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS(HEALTH & FAMILY WELFARE) - [210100001]	71.18	03/1999	547.78
<u>Railways</u>				
51	DHARMAVARAM-PAKALA (GC), SCR(SOUTH CENTRAL RAILWAY) - [220100282]	200.00	-	567.49
<u>Road Transport & Highways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
52	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106268]	263.00	02/2009	420.80
53	AMRITSAR-WAGHA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000121]	205.88	06/2010	214.90
<u>Shipping & Ports</u>				
54	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE(SHIPPING crp. of india) - [N25000029]	1,658.59	07/2010	1,657.45
<u>Telecommunications</u>				
55	GSM BASED NETWORK EXPANSION PLAN PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000034]	239.19	04/2008	96.97
56	Provision of data network for CWG delhi(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000076]	488.76	10/2010	198.65
57	Expn of existing 2G & 3G GSM N/W by 750k(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000077]	180.53	06/2010	40.92
58	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph(BHARAT SANCHAR NIGAM LIMITED) - [N26000079]	577.35	09/2010	40.76
November,2010				
<u>Petroleum</u>				
59	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL)(INDIAN OIL CORPORATION LIMITED) - [160100289]	1,876.00	04/2009	2,747.34
60	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA(INDIAN OIL CORPORATION LIMITED) - [N16000017]	806.00	03/2008	840.06
<u>Power</u>				
61	SEWA- II H.E.P (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100220]	665.46	09/2007	982.76
62	NORTHERN REGION SYSTEM STRENGTHENING-XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000034]	417.76	12/2010	266.42
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000036]	408.36	12/2010	304.83
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000039]	261.55	11/2010	143.36
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000055]	525.14	07/2011	354.9971
<u>Railways</u>				
66	RAJGIR-TILAIYA (NL), ECR(EAST CENTRAL RAILWAYS) - [220100312]	180.82	03/2006	272.46
<u>Road Transport & Highways</u>				
67	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000079]	205.92	08/2009	204.50

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
68	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000080]	243.64	08/2009	256.40
	<u>Telecommunications</u>			
69	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M(BHARAT SANCHAR NIGAM LIMITED) - [N26000051]	908.30	08/2009	211.83
70	CENTRALISED TRANSMISSION NMS(BHARAT SANCHAR NIGAM LIMITED) - [N26000064]	300.00	-	.00

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
September,2010				
<u>Road Transport & Highways</u>				
1	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N16000082]	300.00	10/2008	.00
November,2010				
<u>Civil Aviation</u>				
2	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N12000021]	535.00	06/2010	331.80


Summary of projects on the Flash Report for the month of Nov, 2010

I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 150 Cr. & above) Previous Month	568
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Previous Month	9
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Current month	13
No. of projects with Anticipated greater than Rs. 150 Cr in Current Month	6
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	20
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	572

II. Brief Analysis


a) Project Status w.r.t Original Schedule: Out of 572 projects, 9 projects are ahead of schedule, 133 projects are on schedule and 291 projects are delayed. Of the balance, 78 projects do not have fixed dates of commissioning while 61 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

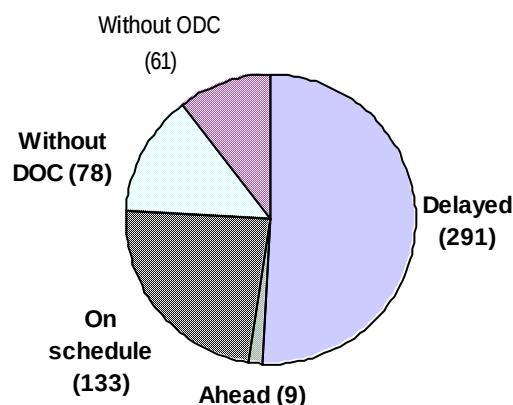

III. Investment Scenario

Figures are in Rs. Crore

The total Original cost of implementation of 572 projects when sanctioned, was of the order of Rs. 592196.97 crore but this was subsequently revised to Rs. 714501.64 crore implying a cost overrun of 20.70%. The expenditure incurred on these projects till Nov, 2010 is Rs. 304331.57 crore, which is 42.60% of the revised cost of the projects.

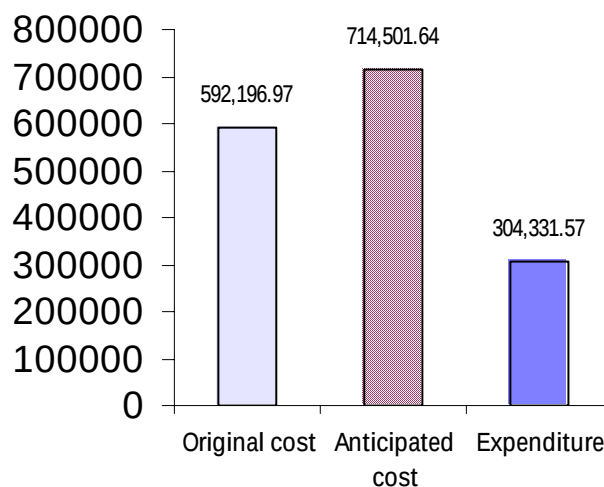

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	568
No of Projects Completed/Dropped/Frozen in Previous Month	9
No of Projects Completed/Dropped/Frozen in Current Month	13
No. of projects with Anticipated grater then Rs. 150 Cr in Current Mont	6
No of Projects added in Current Month	20
No of Projects in Current Month	572

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	291	9	133	61	78	572	50.87
Latest Approved (Date)	296	12	154	43	69	572	51.75

III. (A) Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	486	499,323.68	541,895.04	219,571.98	40.50	42,571.36	8.50
Latest Approved (RCE)	86	135,778.23	172,606.60	84,759.59	49.10	36,828.37	27.10
Total (RCE)	572	635,101.91	714,501.64	304,331.57	42.59	79399.73	12.50
Original Cost of All Projects							
Original Cost	572	592,196.97	714,501.64	304,331.57	42.60	122,304.67	20.70

III. (B) Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	291	302,994.35	375,819.38	211,754.58	56.30	72,825.03	24.00
Latest Approved (RCE)	296	299,631.23	354,029.54	203,709.99	57.50	54,398.31	18.20

IV. Additional Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	87	156,763.59	171,623.05	114,611.78	66.80	14,859.46	9.50

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Railways</u>						
RAJGIR-TILAIYA (NL), ECR	04/2001	180.82	03/2006	180.82	N.A.	272.46
<u>Power</u>						
NORTHERN REGION SYSTEM STRENGTHENING-XI	12/2007	417.76	12/2010	417.76	10/2010	266.42
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X	12/2007	408.36	12/2010	408.36	10/2010	304.83
NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XII	02/2008	261.55	11/2010	261.55	09/2010	143.36
<u>Road Transport & Highways</u>						
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418	12/2003	205.92	08/2009	205.92	11/2010	204.50
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463	12/2003	243.64	08/2009	243.64	11/2010	256.40
<u>Telecommunications</u>						
GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M	06/2008	908.30	08/2009	916.70	11/2010	211.83
<u>Civil Aviation</u>						
D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA	01/2008	535.00	06/2010	535.00	12/2010	331.80
<u>Power</u>						
NORTHERN REGION SYSTEM STRENGHTENING SCHEME-IX	07/2008	525.14	07/2011	525.14	10/2010	351.71
<u>Telecommunications</u>						
CENTRALISED TRANSMISSION NMS	08/2009	300.00	N.A.	300.00	N.A.	.00
<u>Power</u>						
SEWA- II H.E.P (NHPC)	09/2003	665.46	09/2007	665.46	07/2010	982.76
<u>Petroleum</u>						
INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL)	11/2005	1,876.00	04/2009	3,155.00	02/2010	2,747.34
EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA	06/2005	806.00	03/2008	1,100.00	11/2010	840.06

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Railways</u>					
Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves	4/2007	643.36	3/2011	803.39	3/2011
Ramanagram-Musore doubling with deiltification of	4/2007	482.00	3/2013	482.00	3/2013
New Work for Construction of Metro railway from No	4/2010	3,447.41	3/2016	5,573.83	3/2016
New Work for Construction of Metro railway from Bu	4/2010	2,069.60	3/2014	2,069.60	3/2014
New Work for Construction of Metro railway from NS	4/2010	3,951.98	3/2016	3,951.98	3/2016
New Work for Construction of Metro railway	4/2010	2,619.02	3/2016	2,619.02	3/2016
Himmatnagar - Udaipur Gauge Canvession (NWR)	4/2008	829.74	3/2015	829.74	3/2015
Jaipur - Ringus - Churu and Sikar - Lohatu Guage C	4/2008	653.19	3/2014	653.19	3/2014
Suratpura - Hanumangarh - Sriganganagar Guage Canv	4/2008	516.23	3/2014	516.23	3/2014
Tinpahar - Sahibganj (ER)	4/2008	167.73	3/2012	167.73	3/2012
Dakshin-barasat-lakshmikantapur (ER)	4/2009	259.51	12/2011	259.51	12/2011
Ghutiarisharif-Canning (ER)	4/2009	189.97	12/2011	189.97	12/2011
Pandabeswar-Chinpai doubling (ER)	4/2004	225.68	12/2010	225.68	12/2010
Rattam-Mhow-Khandwa-Akola (GC)	4/2008	603.04	3/2012	603.04	3/2012
Ahmedabad-Himmatnagar-Udaipur (WR)	4/2008	394.13	3/2013	394.13	3/2013
Udhna-Jalgaon with electrification(doubling) (WR)	4/2008	1,389.62	3/2014	1,389.62	3/2014
Bhuj-Naliya(GC) with extension from naliyate vaylor	4/2008	318.24	3/2012	318.24	3/2012
New Line from Dimapur to Zubza(Kohima) national pr	4/2006	850.00	3/2015	850.00	3/2015
Bhavnagar-workshop facilities for 50 BG coaches PO	4/2006	117.36	3/2011	196.95	3/2011
Bandel-Naihati new rail bridge in replacement of j	4/1999	207.52	12/2012	207.52	12/2012

VII. Milestones (Cumulative due & achieved)

Total	2107
Achieved up to month	853

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	13,171.00	12/2008	06/2011	12/2011	6
<u>Civil Aviation</u>						
CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 AAI	213.35	213.35	09/2010	11/2010	02/2011	3
<u>Coal</u>						
Churi Benti UG CCL	163.51	163.51	03/2011	03/2013	03/2011	-24
ASHOK EXPN.OCP -CCL (5 MTY) CCL	471.66	341.63	03/2011	12/2012	03/2012	-9
North Urimari OCP CCL	179.87	179.87	03/2012	12/2012	03/2012	-9
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	10/2010	12/2010	2
TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	2,453.57	06/2009	06/2011	10/2011	4
ADRIYALA SHAFT PROJECT SCCL	212.34	779.26	03/2013	09/2012	06/2013	9
KAKATIYA LAONGWALL SCCL	453.63	453.63	N.A.	12/2012	03/2015	27
<u>Fertilisers</u>						
THAL AMMONIA REVAMP PROJECT RCF	488.75	488.75	N.A.	03/2011	11/2011	8
<u>Steel</u>						
EXPANSION OF SALEM STEEL PLANT SAIL	1,902.00	1,902.00	06/2011	10/2010	09/2010	-1
Rebuilding of coke oven battery No.1 & 2 (Bokaro S SAIL	500.90	500.90	04/2010	07/2011	08/2011	1
EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	14,443.00	06/2011	06/2011	12/2011	6
67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2010	01/2011	08/2011	7
EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,499.00	10/2009	06/2011	03/2012	9
<u>Petroleum</u>						

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I GAIL	348.00	348.00	03/2012	12/2012	12/2011	-12
DHABOL-BANGALORE PIPELINE PROJECT PHASE-I GAIL	4,543.43	2,600.00	03/2012	12/2012	03/2012	-9
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY IOCL	356.00	251.00	N.A.	11/2010	12/2010	1
MSQ UPGRADATION PROJECT AT BARAUNI REFINERY IOCL	1,492.00	1,525.00	04/2010	11/2010	12/2010	1
BNPL SPURLINE (UTTRANCHAL & PUNJAB) GAIL	540.92	540.92	06/2011	05/2011	06/2011	1
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT IOCL	5,693.00	6,898.00	N.A.	11/2010	01/2011	2
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY IOCL	372.00	276.00	N.A.	10/2010	12/2010	2
North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	03/2011	05/2011	2
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON BRPL	1,431.91	1,676.00	09/2009	12/2010	03/2011	3
VIJAPUR DADRI-BAWANA PIPE LINE PROJECT GAIL	5,595.31	3,700.00	11/2009	10/2010	01/2011	3
REFRIGERATED LPG STORAGE AT JNPT BPCL	304.40	304.40	12/2010	12/2010	03/2011	3
Integrated offshore crude Oil handling facilities at Paradip IOCL	1,492.33	1,492.33	06/2012	03/2012	06/2012	3
C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) ONGC	900.92	976.08	06/2006	10/2010	02/2011	4
MSQ IMPROVMENT PROJECT IOCL	293.60	294.00	12/2009	10/2010	03/2011	5
Additional Development of D-1 Field ONGC	2,163.64	2,163.64	12/2011	12/2011	06/2012	6
JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I GAIL	7,596.18	6,652.22	01/2013	03/2012	01/2013	10
REVAMPING OF WIN PLATFORM AT MH ASSET ONGC	333.40	330.40	05/2010	05/2011	05/2012	12
Power						
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) PGCIL	1,779.29	1,946.85	11/2008	09/2011	03/2011	-6

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G PGCIL	290.49	299.08	04/2010	12/2010	01/2011	1
EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME PGCIL	803.70	803.76	06/2009	12/2010	02/2011	2
BARH STPP STAGE -II (NTPC) NTPC	7,341.04	7,341.04	08/2013	08/2013	10/2013	2
WESTERN REGION STRENGTHENING SCHEME- IX PGCIL	230.89	230.89	01/2011	01/2011	03/2011	2
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) PGCIL	3,779.46	3,725.13	09/2009	12/2010	03/2011	3
EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	894.26	10/2009	12/2010	03/2011	3
WESTERN REGION STRENGTHENING SCHEME-VI PGCIL	340.72	340.72	11/2010	11/2010	03/2011	4
BARH STPP(3X660MW) NTPC NTPC	8,692.97	8,693.00	11/2010	04/2014	09/2014	5
PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.56	2,304.52	10/2010	06/2011	12/2011	6
CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.26	621.28	02/2011	02/2011	08/2011	6
BONGAIGAON THERMAL POWER PROJECT (NTPC) NTPC	4,375.35	4,375.35	07/2011	03/2012	10/2012	7
CHAMERA,STAGE-III (NHPC) NHPC	1,405.63	1,405.63	08/2010	12/2010	08/2011	8
URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	1,724.79	11/2009	02/2011	11/2011	9
NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) NHPC	611.01	611.02	08/2010	12/2010	09/2011	9
KOLDAM HEP (NTPC) NTPC	4,527.15	4,527.15	04/2009	03/2012	03/2013	12
LOWER SUBANSIRI H.E.P (NHPC) NHPC	6,285.33	6,285.33	09/2010	12/2012	12/2013	12
KOTESHWAR HEP(THDC) THDCL	1,301.56	2,398.39	04/2005	12/2010	03/2012	15
PARBATI HEP (NHPC) II NHPC	3,919.59	3,919.59	09/2009	03/2013	07/2014	16
RAMPUR HEP(412 MW) SJVNL	2,047.03	2,047.03	01/2012	03/2012	09/2013	18
Railways						
MUZAFFARPUR- SITAMARHI(NL),ECR ECR	100.00	322.29	N.A.	02/2011	03/2011	1
DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) ER	180.73	358.00	12/2006	11/2010	02/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP MRTPT	3,125.20	4,103.20	N.A.	12/2010	06/2011	6
Road Transport & Highways						
BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	217.61	04/2010	12/2012	03/2012	-9
HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	11/2011	06/2011	-5
AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) NHAI	367.49	367.49	03/2005	04/2011	03/2011	-1
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 NHAI	480.00	480.00	11/2007	11/2010	12/2010	1
Gujarat/Maharashtra BorderSurat-Hazira Port Section NHAI	1,509.10	1,509.10	09/2012	09/2012	10/2012	1
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 NHAI	227.00	227.00	10/2008	03/2011	06/2011	3
ORAI TO JHANSI (UP-5),NH- 25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	12/2010	03/2011	3
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 NHAI	359.00	359.00	03/2009	12/2010	03/2011	3
RINGBUNDS TO JHAJHANPUR (BR-6) NHAI	340.00	340.00	06/2008	12/2010	03/2011	3
SITAPUR-LUCKNOW NHAI	322.00	322.00	06/2009	12/2010	03/2011	3
BARA TO ORAI, NH-2, 25 NHAI	465.00	465.00	04/2009	12/2010	03/2011	3
GORAKHPUR BYPASS, NH- 28, PHASE-II EAST-WEST CORRID NHAI	600.24	600.24	10/2009	03/2011	06/2011	3
GWALIOR-JHANSI, NH-75 NHAI	604.00	604.00	12/2009	03/2011	06/2011	3
Four Lanning from MP/Maharashtra Border to nagpur NHAI	1,170.52	1,170.52	06/2011	06/2011	10/2011	4
KASIA TO GORAKHPUR (NH- 28)(NHAI) NHAI	242.00	242.00	12/2008	12/2010	05/2011	5
SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 NHAI	941.00	941.00	01/2011	01/2011	06/2011	5
ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) NHAI	295.00	295.00	08/2010	12/2010	05/2011	5
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 NHAI	166.27	193.10	03/2008	12/2010	06/2011	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) NHAI	227.00	227.00	12/2008	12/2010	06/2011	6



VIII. List of projects reporting additional delays



Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	06/2011	12/2011	6
TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	12/2010	06/2011	6
NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH NHAI	557.00	557.00	02/2010	10/2011	05/2012	7
MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 NHAI	200.00	200.00	04/2009	04/2011	12/2011	8
HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	280.00	280.00	02/2009	03/2011	12/2011	9
SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	03/2011	12/2011	9
NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	03/2011	12/2011	9
DARBHANGA- MUZAFFARPUR, NH-57 (NHAI) NHAI	305.00	305.00	06/2008	12/2010	11/2011	11
PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A NHAI	284.00	359.00	05/2008	12/2010	08/2012	20
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 NHAI	407.60	407.60	06/2010	12/2010	09/2012	21
AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 NHAI	348.16	348.16	09/2007	02/2011	06/2013	28
<u>Telecommunications</u>						
ERP implementation in BSNL on Turnkey basis BSNL	384.00	384.00	10/2010	11/2010	04/2011	5
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT DMRC	8,676.00	18,894.36	06/2010	10/2010	12/2010	2



Number of projects reporting additional delay = 87



Sector wise Trend and Graphical Analysis



(10, Aug'10, Sep'10, Oct'10, Nov'10)

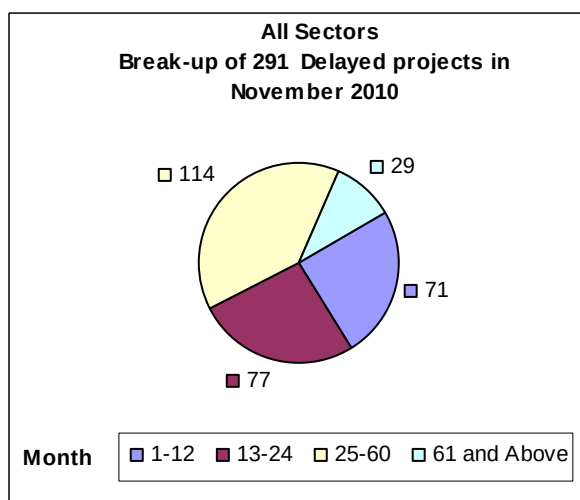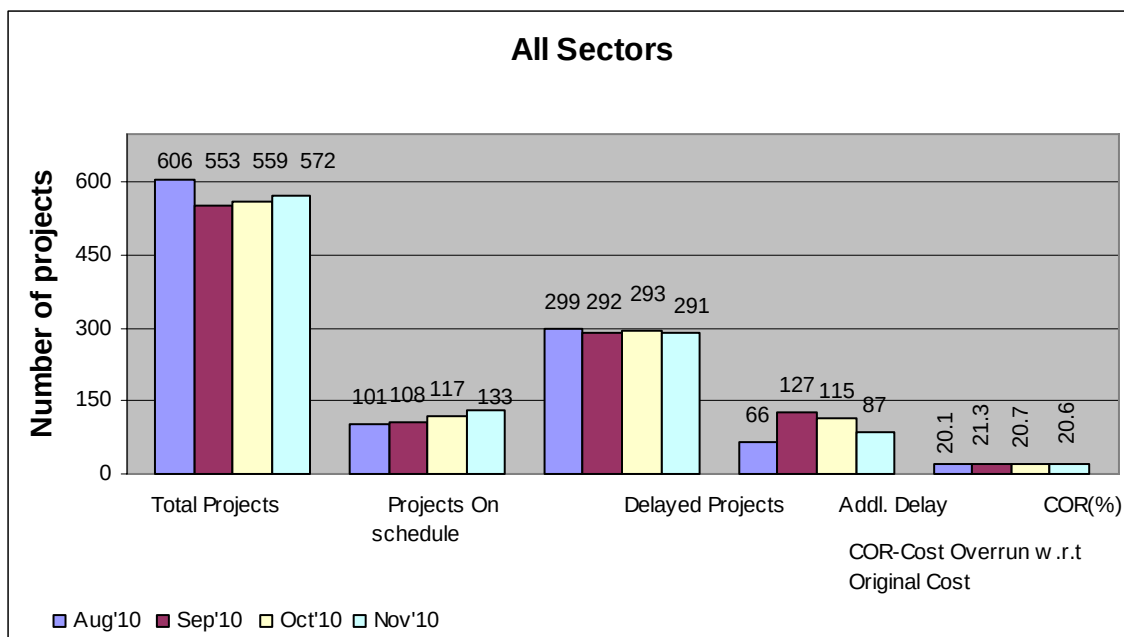

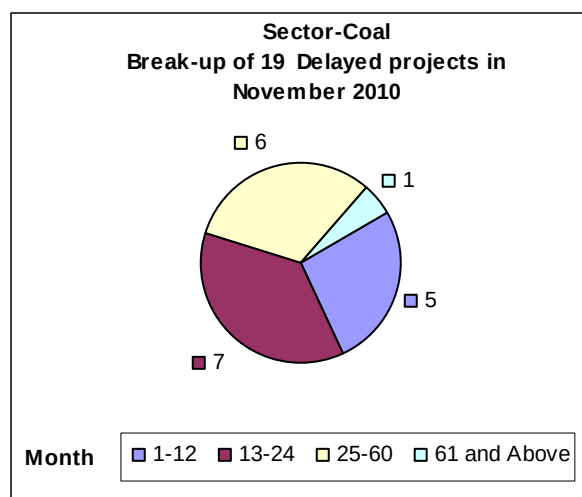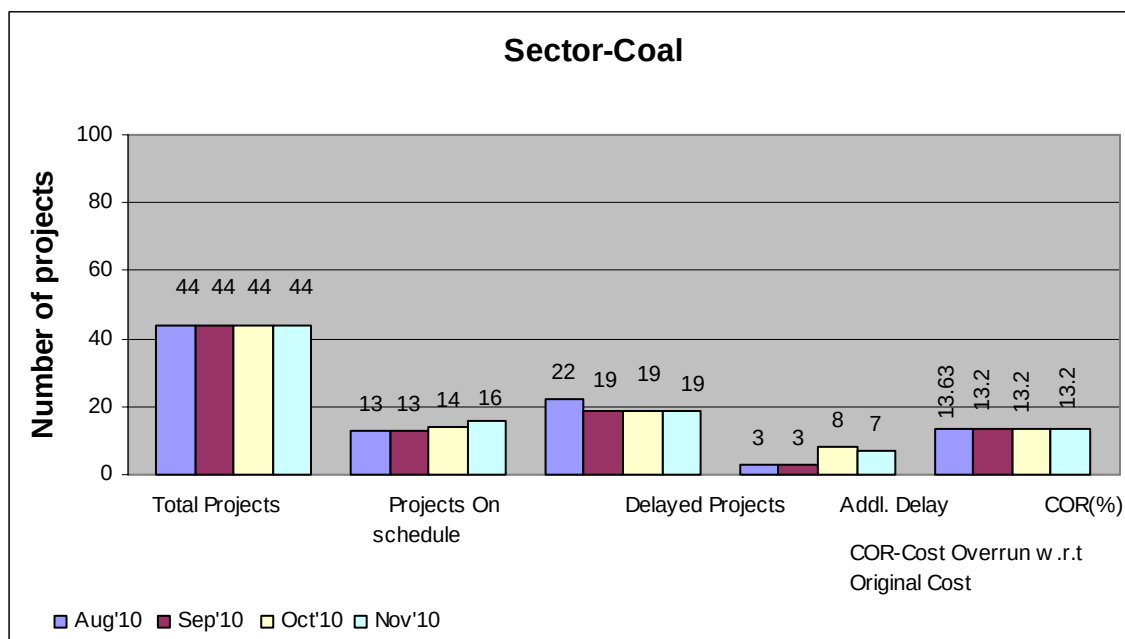


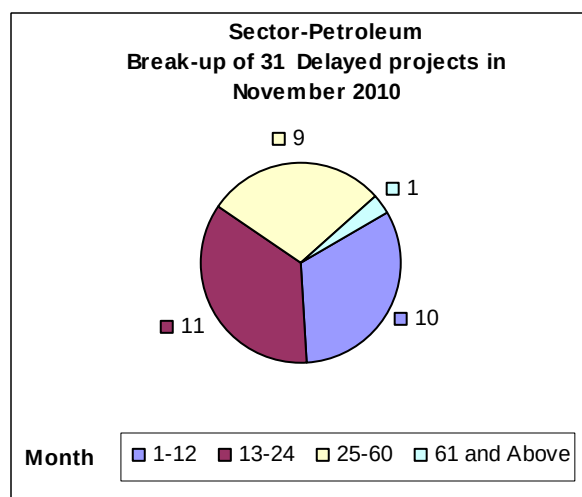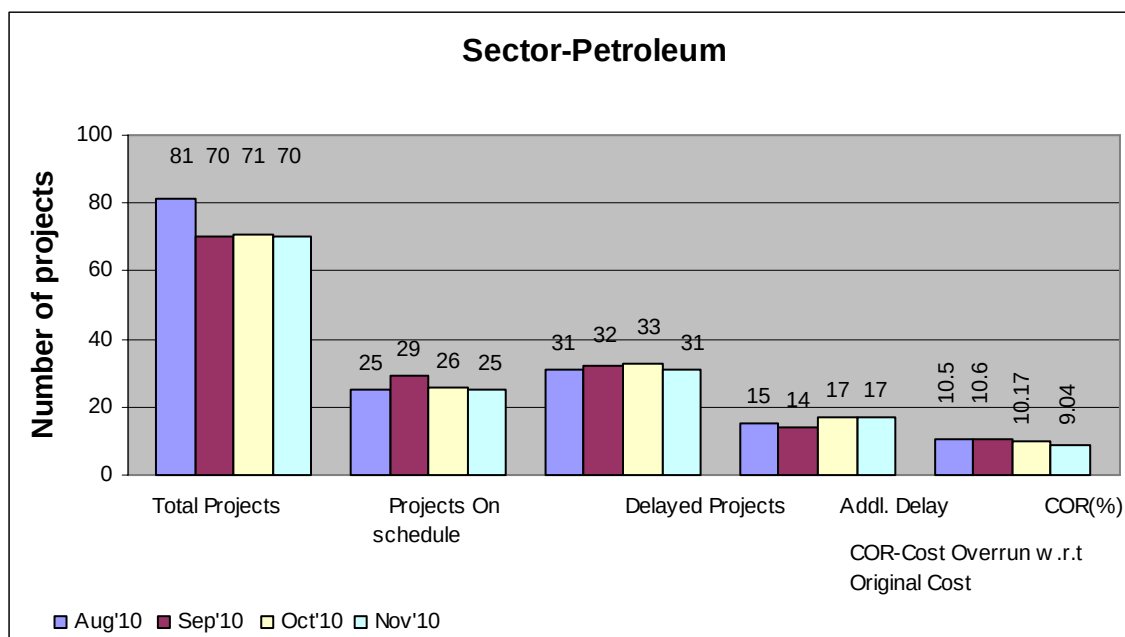

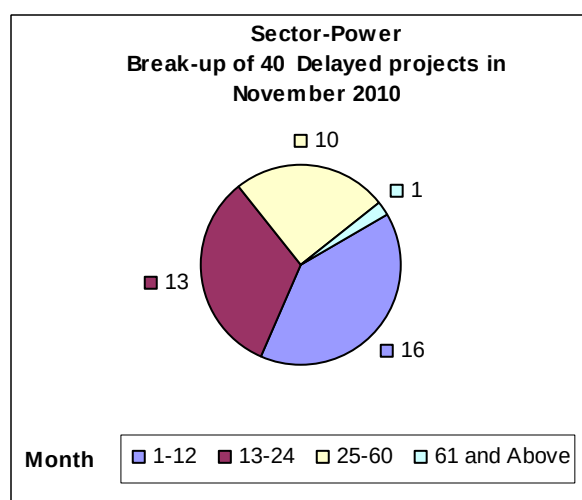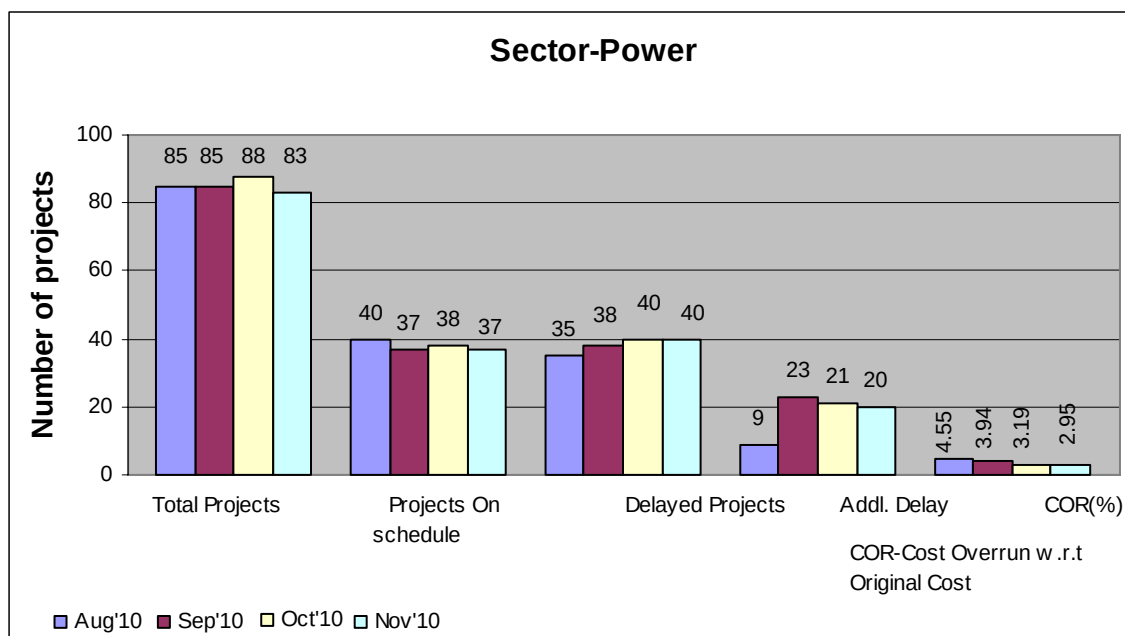


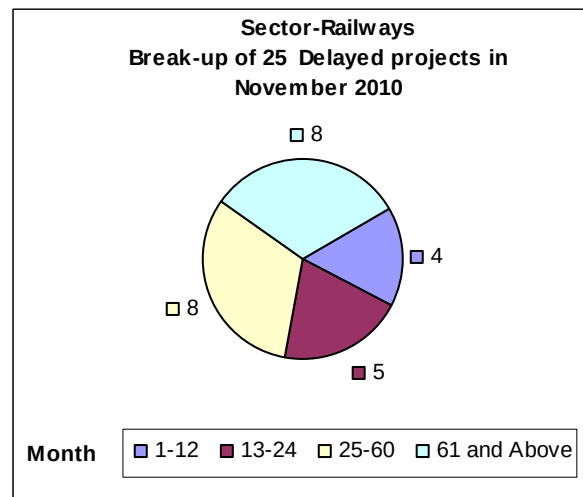
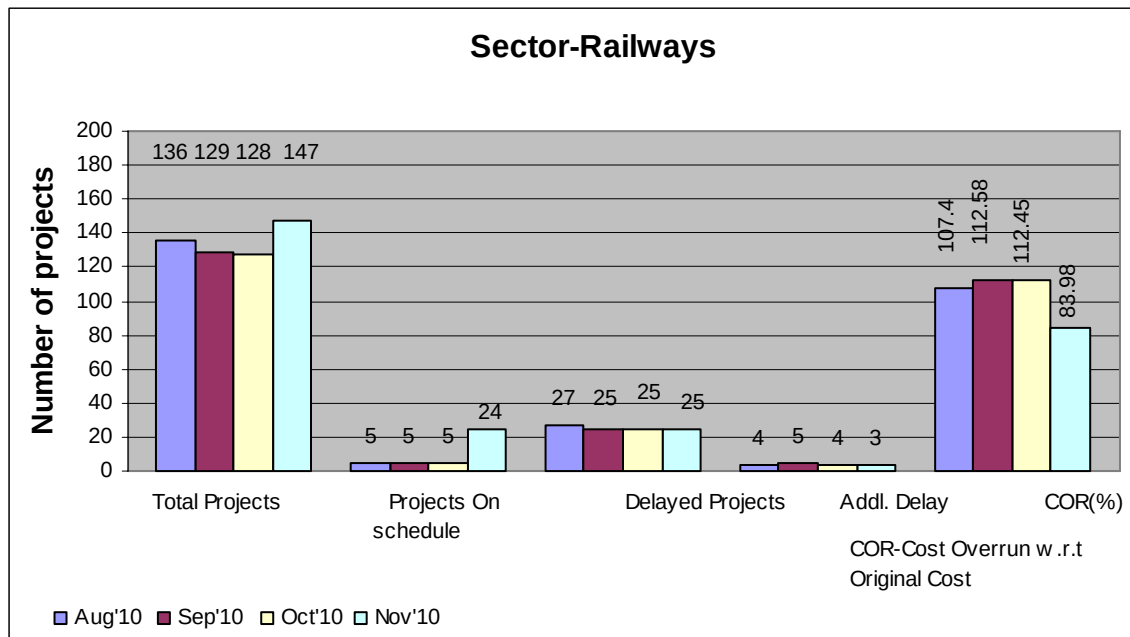




Sector-Road Transport & Highways


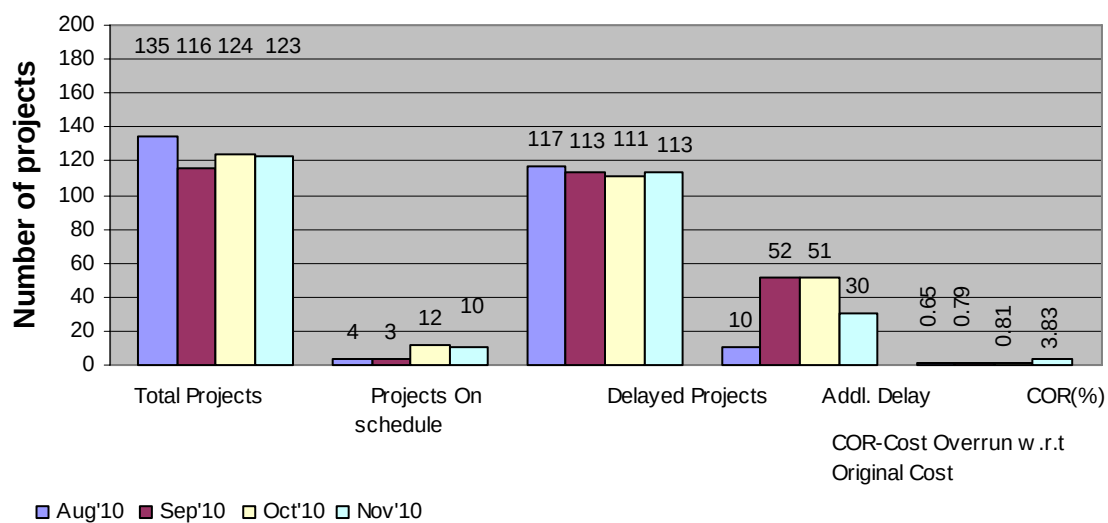


Sector-Road Transport & Highways Break-up of 113 Delayed projects in November 2010

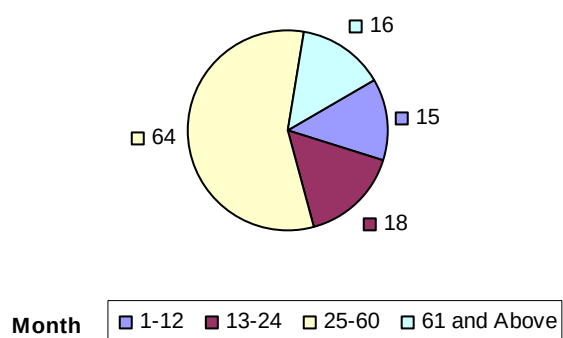

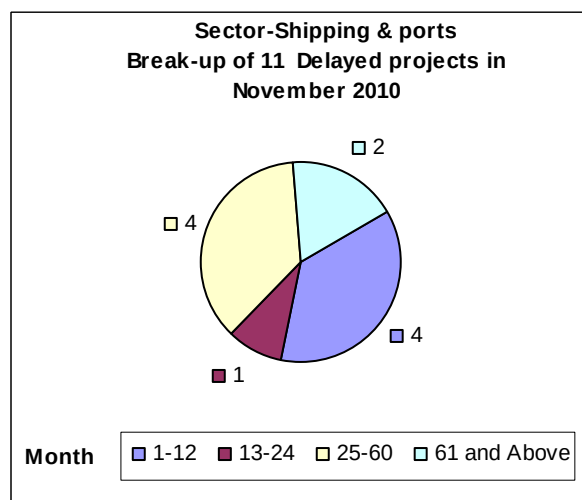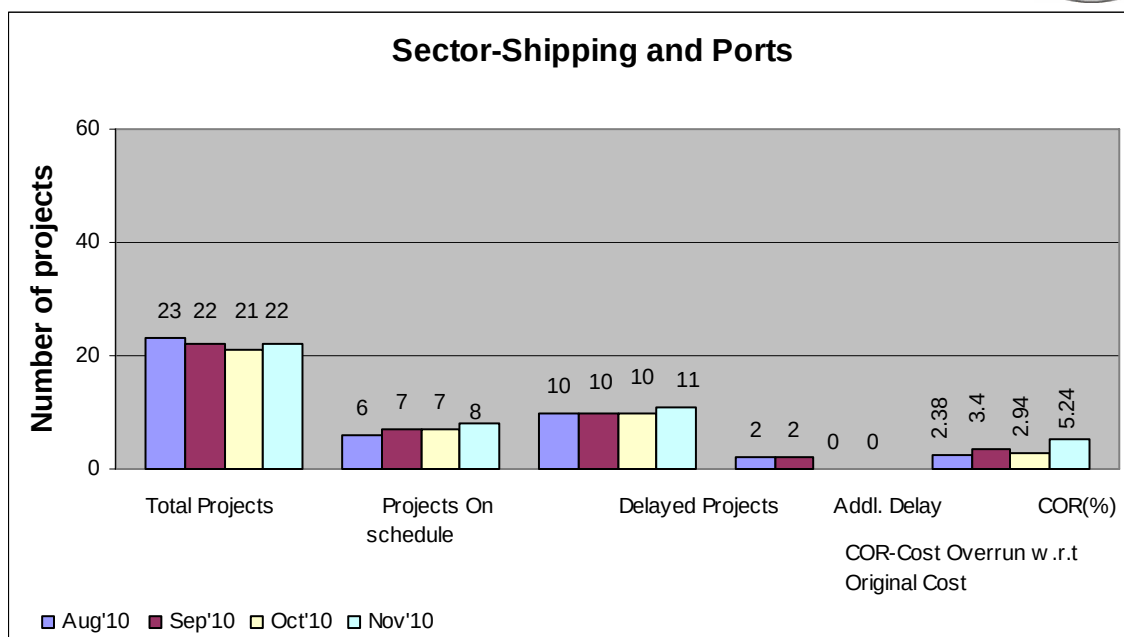

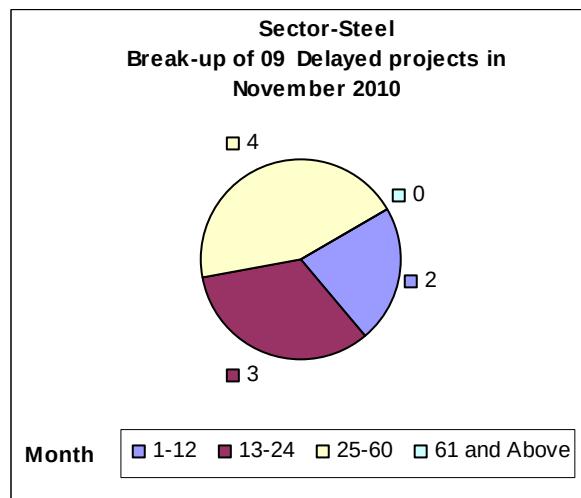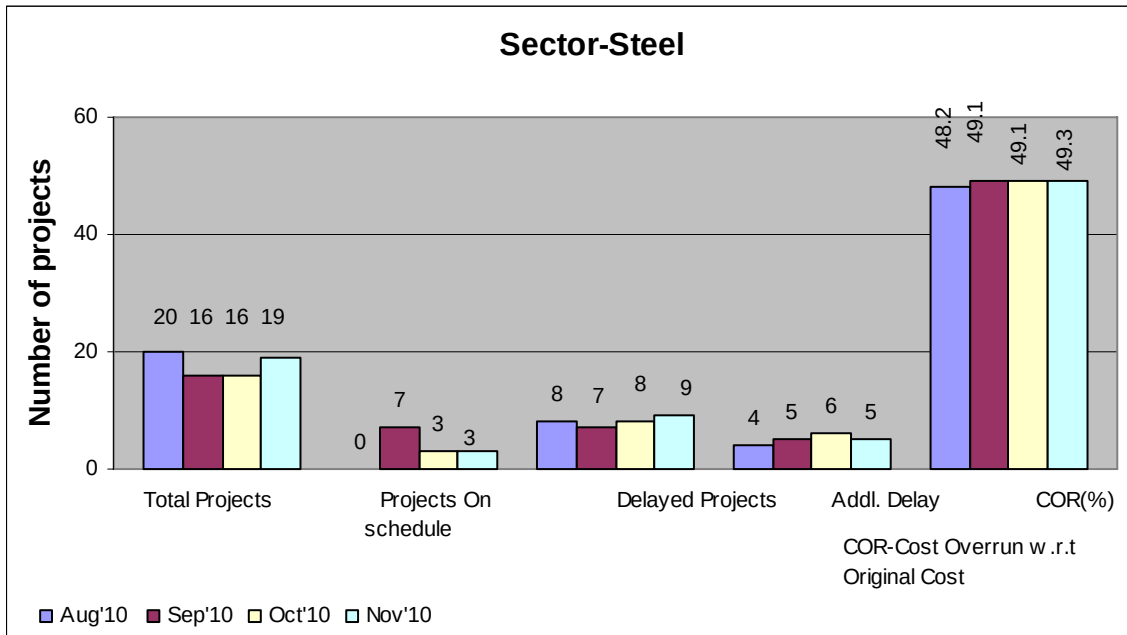

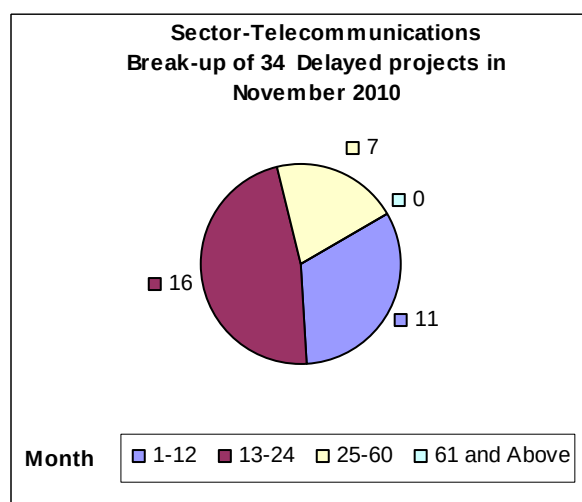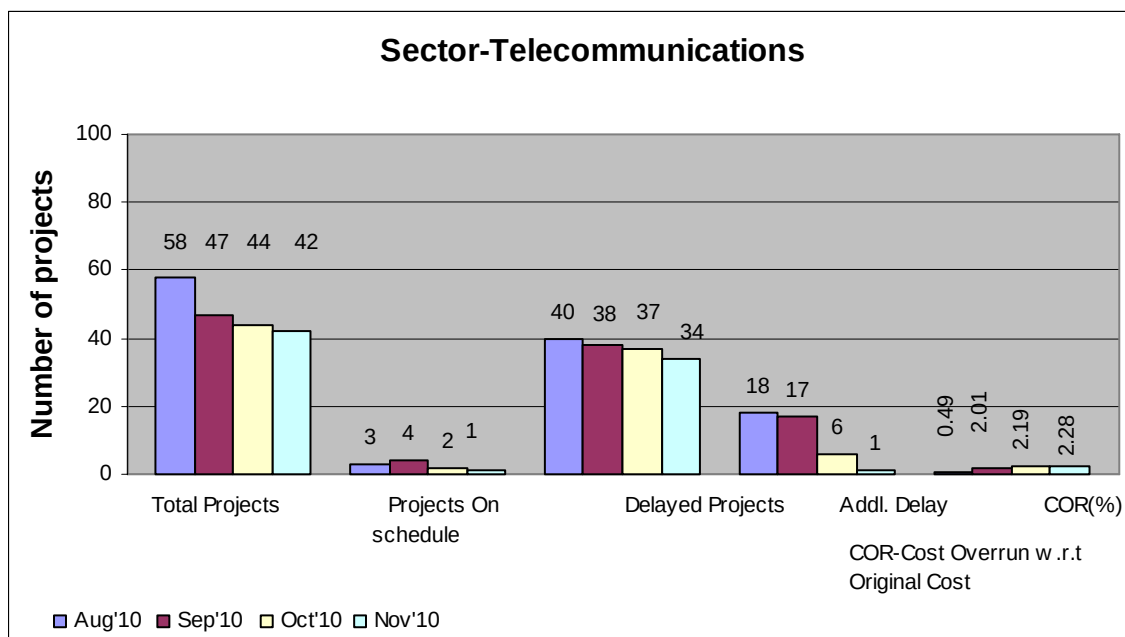

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	24,167.29
Civil Aviation	8	4,812.40	4,812.40	4,812.40
Coal	44	25,210.20	26,673.93	28,547.29
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	19	43,780.53	59,104.76	65,379.56
Petroleum	70	142,330.59	161,564.51	155,206.10
Power	83	179,759.57	180,170.28	185,077.10
Railways	147	68,578.35	80,564.86	126,174.41
Road Transport & Highways	123	44,403.11	44,403.11	46,104.91
Shipping & Ports	22	16,082.62	16,683.64	16,926.26
Telecommunications	42	20,234.49	20,271.70	20,696.79
Urban Development	2	15,071.00	8,608.36	30,503.36
Water Resources	1	542.90	542.90	1,187.00
Grand total	572	592,196.97	635,101.91	714,501.64

(Nov,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]NPCIL,Karnataka	05/2001	4,213.00	4,213.00	2,593.00	10/2009 09/2007	12/2010	39(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	486.37	-	04/2011	-	0/1
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	2,592.29	09/2010	09/2011	12(O)	8/80
4	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	13,171.00	13,293.00	12/2008	12/2011	36(O)	61/119
Total			21,982.29	24,167.29	18,964.66				140/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]AAI,Gujarat	02/2007	290.92	290.92	198.32	-	01/2011	-	1/24
6	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00	1,273.00	657.78	01/2011	01/2011	0(O)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29	264.29	79.17	01/2011	01/2011	0(O)	0/0
8	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00	230.00	207.69	01/2011	01/2011	0(O)	0/0
9	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35	213.35	182.35	09/2010	02/2011	5(O)	0/0
10	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	1,942.51	832.54	05/2011	08/2011	3(O)	0/0
11	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73	204.73	16.04	05/2012	05/2012	0(O)	0/0
12	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60	393.60	205.95	06/2013	-	-	0/0
Total			4,812.40	4,812.40	2,379.84				1/24
<u>Coal</u>									
13	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18	1,626.09	1,512.91	06/2009	12/2010	18(O)	59/26
14	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08	172.08	156.09	03/2009	03/2011	24(O)	0/0
15	Churi Benti UG - [N06000083]JCL,Jharkhandd	06/2007	163.51	163.51	33.46	03/2011	03/2011	0(O)	0/2
16	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78	2,453.57	2,048.60	06/2009	10/2011	28(O)	41/24
17	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96	302.96	65.08	03/2010	03/2012	24(O)	0/4

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	102.68	03/2011 03/2012	03/2012	0(R3)	0/2
19	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	38.85	03/2012 -	03/2012	0(O)	8/42
20	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	0.96	03/2012 03/2012	03/2012	0(R3)	0/1
21	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	58.66	03/2012 -	03/2012	0(O)	0/0
22	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.57 418.97	418.97	69.69	- -	03/2012	-	7/7
23	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.91 -	181.19	0.90	- -	03/2012	-	2/8
24	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	68.37	03/2012 -	03/2012	0(O)	0/2
25	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	78.66	03/2012 -	03/2012	0(O)	0/2
26	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	1,190.95	08/2012 -	08/2012	0(O)	0/0
27	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.56	741.56	136.68	03/2010 03/2013	03/2013	0(R3)	0/2
28	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	555.92	03/2011 -	03/2013	24(O)	0/4
29	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.23	07/2012 03/2013	03/2013	0(R3)	0/2
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	11.42	03/2013 -	03/2013	0(O)	0/83
31	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	52.04	- -	03/2013	-	0/2
32	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	24.66	03/2013 -	03/2013	0(O)	0/0
33	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	20.05	03/2013 -	03/2013	0(O)	0/2
34	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	133.86	03/2013 07/2012	06/2013	11(R3)	2/22
35	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,019.05	03/2010 -	03/2014	48(O)	3/7
36	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	907.54	03/2010 -	03/2014	48(O)	2/6
37	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	140.51	03/2014 03/2014	03/2014	0(R3)	1/1
38	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	254.18	06/2014 -	03/2014	-3(O)	0/0
39	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	02/2006	50.08 153.82	153.82	14.77	- 03/2014	03/2014	0(R3)	0/1
40	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77 -	339.77	0.05	03/2014 -	03/2014	0(O)	0/1
41	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	213.57	03/2013	03/2014	12(O)	0/0
43	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	437.34	137.16	03/2012 03/2015	03/2015	0(R3)	0/1
44	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	11/2009	03/2015	64(O)	0/0
45	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	24.33	03/2013	03/2015	24(O)	0/0
46	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2012 03/2015	03/2015	0(R3)	0/0
47	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	53.30	- 12/2012	03/2015	27(R3)	7/44
48	Batura OC - [N06000049]BCCL,Madhya pradesh	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
49	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
50	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	201.58 209.78	209.78	14.89	- -	03/2015	-	0/8
51	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	32.29	03/2014 03/2016	03/2016	0(R3)	1/2
52	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	6.04	03/2015	03/2016	12(O)	0/0
53	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	158.59	198.59	92.09	03/2016	03/2016	0(O)	0/0
54	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	290.99	03/2016	03/2016	0(O)	0/2
55	BHUBANESWARI OCP - [N06000034]MCL,	12/2007	490.00	490.10	59.35	-	03/2017	-	0/1
56	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	-	-	-	-	0/0
Total			25,210.20	28,547.29	9,636.83				133/311
Fertilisers									
57	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	15.86	07/2011	07/2011	0(O)	0/0
58	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	29.06	07/2011	07/2011	0(O)	0/0
59	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	29.87	- 11/2011	11/2011	0(R3)	2/22
60	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	43.41	12/2012	12/2012	0(O)	0/8
61	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	71.49	01/2013	01/2013	0(O)	0/5
62	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	61.56	01/2013	01/2013	0(O)	0/5
Total			5,317.41	5,317.41	251.25				2/40

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Mines</u>									
63	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa	10/2004	4,091.51 4,401.76	4,401.76	3,893.98	12/2008 01/2011	03/2011	2(R3)	116/110
Total			4,091.51	4,401.76	3,893.98				116/110
<u>Steel</u>									
64	EXPANSION OF SALEM STEEL PLANT - [N12000050]SAIL, Tamil Nadu	01/2008	1,902.00 -	1,902.00	1,754.78	06/2011 -	09/2010	-9(O)	2/6
65	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]SAIL, Orissa	07/2007	302.70 -	302.70	244.97	06/2009 -	10/2010	16(O)	0/0
66	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]SAIL, Orissa	01/2008	197.66 -	197.66	130.32	11/2009 -	10/2010	11(O)	0/0
67	AIR SEPARATION PLANT (ASU-4) - [N12000060]RINL, Andhra Pradesh	03/2008	96.00 -	170.00	73.03	06/2010 -	12/2010	6(O)	0/0
68	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL, Jharkhand	07/2008	172.78 -	172.78	118.69	01/2010 -	02/2011	13(O)	0/1
69	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Madhya Pradesh	07/2007	111.28 232.93	232.93	92.07	05/2011 -	05/2011	0(O)	0/1
70	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC,	01/2003	295.89 -	607.17	237.14	- -	06/2011	-	2/21
71	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	190.59	- 08/2010	06/2011	10(R3)	0/1
72	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL, Jharkhand	10/2007	500.90 -	500.90	227.82	04/2010 -	08/2011	16(O)	0/2
73	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 343.58	343.58	193.10	02/2010 02/2011	08/2011	6(R3)	0/0
74	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 -	14,443.00	9,520.22	06/2011 12/2011	12/2011	0(R3)	0/6
75	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	3,316.00 6,325.00	6,325.00	1,501.74	12/2011 12/2011	12/2011	0(R3)	0/7
76	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,499.00	7,446.00	10/2009 -	03/2012	29(O)	4/16
77	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Andhra Pradesh	05/2008	480.00 -	480.84	52.58	09/2010 -	05/2012	20(O)	0/0
78	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	25.19	10/2009 -	10/2012	36(O)	0/0
79	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	6,133.00 -	8,128.00	2,506.34	02/2011 -	03/2013	25(O)	0/0
80	EXPANSION OF BHILLAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	1,711.17	03/2013 03/2013	03/2013	0(R3)	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
81	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]SAIL,Jharkhandd	10/2007	892.32 -	892.32	616.57	08/2009 -	-	-	2/1
82	POWER PLANT-I - [N12000039]RINL,Andhra Pradesh	09/2007	462.00 -	350.00	84.40	12/2009 -	-	-	0/0
	Total		43,780.53 -	65,379.56	26,726.72				10/70
Petroleum									
83	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL,Maharashtra	03/2007	900.47 -	900.47	1,332.68	09/2009 -	11/2010	14(O)	0/0
84	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]IOCL,	04/2008	372.00 -	276.00	227.16	- -	12/2010	-	0/28
85	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]IOCL,Assam	04/2008	356.00 -	251.00	218.45	- -	12/2010	-	0/27
86	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]IOCL,Bihar	04/2008	1,492.00 -	1,525.00	1,098.99	04/2010 -	12/2010	8(O)	0/0
87	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL,Punjab	01/2009	605.40 605.40	510.00	311.58	12/2010 12/2010	12/2010	0(R3)	17/17
88	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80 3,941.41	3,941.41	3,179.63	12/2009 -	12/2010	12(O)	0/0
89	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	315.52	12/2010 -	12/2010	0(O)	0/0
90	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL,Gujarat	01/2007	5,693.00 6,898.00	6,898.00	5,822.64	- 06/2010	01/2011	7(R3)	57/42
91	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]GAIL,Multi State	11/2007	5,595.31 4,316.00	3,700.00	3,307.01	11/2009 04/2010	01/2011	9(R3)	0/0
92	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL,Multi State	11/2007	396.13 -	396.13	185.56	10/2009 06/2010	01/2011	7(R3)	0/0
93	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92 1,493.49	976.08	735.45	06/2006 07/2010	02/2011	7(R3)	0/2
94	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 -	224.00	136.12	12/2010 02/2011	02/2011	0(R3)	0/0
95	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 -	600.00	552.27	03/2007 -	03/2011	48(O)	3/3
96	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 834.90	1,200.00	1,138.77	03/2007 03/2011	03/2011	0(R3)	6/6
97	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 219.22	219.22	198.22	03/2006 -	03/2011	60(O)	6/6
98	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,676.00	1,463.68	09/2009 -	03/2011	18(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
99	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.63	12/2008 12/2008	03/2011	27(R3)	0/0
100	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 -	2,305.30	2,061.15	06/2010 06/2010	03/2011	9(R3)	0/0
101	MSQ IMPROVMENT PROJECT - [N16000040]IOCL,Assam	04/2008	293.60 -	294.00	196.15	12/2009 -	03/2011	15(O)	0/0
102	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	169.86	12/2010 -	03/2011	3(O)	0/0
103	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	07/2011	1,816.07 1,816.07	1,400.00	482.68	- 04/2011	04/2011	0(R3)	0/1
104	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38 4,403.00	2,800.00	1,844.64	10/2011 04/2011	04/2011	0(R3)	0/2
105	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,	11/2007	1,512.00 1,434.00	1,434.00	728.24	- 04/2011	04/2011	0(R3)	0/3
106	COMPRESSOR STATIONS (KAILARAS &CHAINS) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	810.00	46.71	04/2011 04/2011	04/2011	0(R3)	0/2
107	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	474.75	04/2010 -	04/2011	12(O)	0/0
108	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	88.25	04/2011 -	04/2011	0(O)	0/0
109	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,234.69	03/2005 05/2011	05/2011	0(R3)	0/0
110	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	05/2011	26(O)	0/0
111	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	01/2010	589.70 755.76	755.76	78.13	03/2011 05/2011	05/2011	0(R3)	0/0
112	BNPL superlines(Uttranchal & Punjab) - [N16000091]GAIL,Multi State	12/2009	540.92 -	540.92	0.96	05/2011 -	06/2011	1(O)	0/0
113	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	463.32	0.13	06/2011 -	06/2011	0(O)	3/9
114	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	540.92	1.35	06/2011 -	06/2011	0(O)	7/9
115	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 -	3,597.00	146.54	09/2011 -	09/2011	0(O)	0/0
116	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	108.33	09/2011 -	09/2011	0(O)	0/0
117	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	492.96	12/2011 -	12/2011	0(O)	0/0
118	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	349.00 -	349.00	123.86	08/2011 -	12/2011	4(O)	0/0
119	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Multi State	06/2009	348.00 -	348.00	8.70	03/2012 -	12/2011	-3(O)	6/12

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
120	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL,Maharashtra	02/2008	825.00 -	825.00	85.27	- -	12/2011	-	0/203
121	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	154.37	12/2011 -	12/2011	0(O)	0/0
122	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	110.39	12/2011 -	12/2011	0(O)	0/0
123	EURO-IV DHDT - [N16000109]CPCL,	09/2008	2,615.69 -	2,615.69	1,253.31	- -	12/2011	-	0/116
124	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	411.41	03/2010 03/2012	03/2012	0(R1)	0/0
125	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,600.00	37.73	03/2012 -	03/2012	0(O)	11/10
126	CDU/VDU-II - [N16000110]CPCL,	03/2010	333.99 -	333.99	15.69	- -	03/2012	-	4/36
127	Assam gas Cracker project - [N16000106]BCPL,Assam	04/2006	5,460.61 -	5,460.61	1,246.69	- -	04/2012	-	0/2
128	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	1,683.89	05/2010 05/2012	05/2012	0(R3)	0/0
129	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	1,552.63 2,920.82	2,920.82	165.00	02/2009 03/2012	05/2012	2(R3)	0/0
130	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 -	330.40	2.45	05/2010 -	05/2012	24(O)	0/0
131	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	-	07/2010 05/2012	05/2012	0(R3)	0/0
132	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	89.83	03/2010 03/2012	06/2012	3(R3)	0/0
133	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	154.65	06/2012 -	06/2012	0(O)	0/0
134	Additional Development of D-1 Field - [N16000097]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	213.44	12/2011 06/2012	06/2012	0(R3)	0/0
135	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	17.75	04/2011 -	07/2012	15(O)	0/0
136	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	10.50	08/2012 -	08/2012	0(O)	0/0
137	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	6,855.93 -	6,855.93	1,077.44	09/2012 -	09/2012	0(O)	0/0
138	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	21.05	09/2012 -	09/2012	0(O)	0/0
139	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
140	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	29,777.00	4,794.53	-	11/2012	-	58/103
141	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	1,797.35	9.78	12/2011	01/2013	13(O)	0/0
142	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	0.65	01/2013	01/2013	0(O)	0/0
143	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	7.93	01/2013	01/2013	0(O)	0/0
144	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	-	02/2013	02/2013	0(O)	0/0
145	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	06/2007	1,252.75	8,813.41	5,434.52	06/2009 03/2013	03/2013	0(R3)	0/0
146	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	211.94	03/2013	03/2013	0(O)	0/0
147	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
148	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
149	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
150	Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	6.48	02/2014	02/2014	0(O)	0/0
151	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	2.13	10/2010	-	-	0/0
152	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	-	-	12/2012	-	0/0
Total			142,330.59	155,206.10	48,309.52				178/639
Power									
153	KORBA STPP STAGE-III - [N18000011]NTPC,Madhya pradesh	08/2006	2,448.50	2,448.49	2,103.00	02/2010	12/2010	10(O)	5/24
154	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	142.59	09/2010	12/2010	3(O)	0/0
155	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	246.39	07/2011	12/2010	-7(O)	0/0
156	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	117.46	06/2010	01/2011	7(O)	0/0
157	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49	299.08	309.36	04/2010	01/2011	9(O)	0/0
158	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70	803.76	622.67	06/2009	02/2011	20(O)	1/20

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
159	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44	2,570.44	1,812.00	08/2010	02/2011	6(O)	13/26
160	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,626.71	11/2008	03/2011	28(O)	25/38
161	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,422.62	09/2009	03/2011	18(O)	15/30
162	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Uttar Pradesh	10/2006	975.96	894.26	626.81	10/2009	03/2011	17(O)	2/20
163	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,656.48	07/2010	03/2011	8(O)	3/20
164	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	325.00	09/2010	03/2011	6(O)	0/0
165	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]PGCIL,Gujarat	02/2008	340.72	340.72	154.32	11/2010	03/2011	4(O)	0/0
166	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	54.57	01/2011	03/2011	2(O)	0/0
167	Transmission system associated with Uri-II HEP - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	196.33	-	05/2011	-	0/0
168	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,103.39	3,394.00	05/2011	05/2011	0(O)	0/0
169	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	409.85	01/2010	06/2011	17(O)	0/22
170	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	92.45	06/2011	06/2011	0(O)	0/0
171	TRANSMISSION SYSTEM ASSOCIATED WITH CORBA III GENE - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	163.39	06/2011	06/2011	0(O)	0/0
172	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	26.53	07/2011	07/2011	0(O)	0/0
173	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,347.01	08/2010	08/2011	12(O)	0/0
174	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.26	621.28	555.49	02/2011	08/2011	6(O)	0/1
175	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	99.65	08/2011	08/2011	0(O)	0/0
176	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC,J & K	08/2006	611.01	611.02	549.54	08/2010	09/2011	13(O)	0/0
177	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL,Multi State	12/2008	328.97	328.97	161.47	09/2011	09/2011	0(O)	0/0
178	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,729.29	1,724.79	1,264.90	11/2009	11/2011	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	203.79	11/2011 -	11/2011	0(O)	0/0
180	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	145.88	11/2011 -	11/2011	0(O)	0/0
181	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	15.18	11/2011 -	11/2011	0(O)	0/0
182	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	82.81	11/2011 -	11/2011	0(O)	0/0
183	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT - [180100222]NHPC,West Bengal	10/2003	768.92 -	768.92	1,226.24	03/2007 -	12/2011	57(O)	1/25
184	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	6,633.00	12/2009 -	12/2011	24(O)	33/56
185	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,304.52	1,206.78	10/2010 -	12/2011	14(O)	0/0
186	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34 -	241.27	157.81	06/2008 -	12/2011	42(O)	8/20
187	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	58.82	01/2012 -	01/2012	0(O)	0/0
188	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96 -	664.96	70.35	02/2012 -	02/2012	0(O)	0/0
189	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	12.78	02/2012 -	02/2012	0(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	106.55	02/2012 -	02/2012	0(O)	0/0
191	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	156.28	07/2010 -	02/2012	19(O)	0/0
192	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	492.24	02/2012 -	02/2012	0(O)	0/0
193	KOTESHWAR HEP (THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 -	2,398.39	2,109.43	04/2005 -	03/2012	83(O)	2/1
194	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	16.40	04/2012 -	04/2012	0(O)	0/0
195	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	107.25	05/2012 -	05/2012	0(O)	0/0
196	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	-	06/2012 -	06/2012	0(O)	0/0
197	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	215.86	34.02	06/2012 -	06/2012	0(O)	0/0
198	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	4.80	06/2012 -	06/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
199	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38	1,061.38	833.27	09/2009	08/2012	35(O)	0/0
200	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	135.81	08/2012	08/2012	0(O)	4/13
201	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,389.88	08/2012	08/2012	0(O)	0/0
202	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	2,716.55	08/2012	08/2012	0(O)	0/0
203	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	112.82	08/2012	08/2012	0(O)	0/0
204	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	1,539.00	07/2011	10/2012	15(O)	0/0
205	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	1,577.00	02/2012 08/2012	10/2012	2(R3)	0/0
206	TRANSMISSION SYSTEM ASSOCIATED WITH MUNDRA ULTRA M - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,064.44	10/2012	10/2012	0(O)	0/0
207	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	17.82	10/2012	10/2012	0(O)	0/0
208	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF I - [N18000089]PGCIL,Multi State	10/2012	160.32	160.32	-	10/2012	10/2012	0(O)	0/0
209	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	11.89	11/2012	11/2012	0(O)	0/0
210	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2012	965.58	965.58	82.29	11/2012	11/2012	0(O)	0/0
211	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42	358.42	6.57	12/2008 09/2010	12/2012	27(R1)	0/15
212	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
213	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	1,449.39	12/2012	12/2012	0(O)	0/0
214	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	1,206.00	11/2012	12/2012	1(O)	0/0
215	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	1,066.00	11/2012	12/2012	1(O)	0/0
216	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	93.50	12/2012	12/2012	0(O)	0/0
217	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	-	01/2013	01/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
218	Transmission System for phase-1 generation project - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	-	02/2013	02/2013	0(O)	0/0
219	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,370.00	04/2009	03/2013	47(O)	19/41
220	Tapovan-Vishnugad HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	937.00	03/2013	03/2013	0(O)	5/31
221	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,305.26	05/2013	05/2013	0(R3)	77/22
222	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	1,533.48	08/2013	08/2013	0(O)	0/0
223	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,001.38	01/2012	09/2013	20(O)	2/10
224	BARH STPP STAGE -II (NTPC) - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	1,304.00	08/2013	10/2013	2(O)	0/0
225	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	6,285.33	4,306.42	09/2010	12/2013	39(O)	2/11
226	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	2,979.70	09/2009	07/2014	58(O)	1/20
227	BARH STPP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	5,123.00	11/2010	09/2014	46(O)	15/51
228	Transm System for development of Pooling stn. in N - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
229	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00	2,978.86	249.73	07/2010	03/2015	56(O)	0/0
230	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	2,491.58	134.95	07/2014	03/2015	8(O)	0/8
231	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	515.57	07/2014	01/2016	18(O)	0/0
232	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,Manipur	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
233	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72	913.63	217.71	07/2006	-	-	2/5
234	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	947.96	777.39	12/2007	-	-	14/18
235	National Capital Thermal Power Project Stage-II - [N18000013]NTPC,Uttar Pradesh	10/2006	5,135.33	5,135.33	4,000.00	10/2010	-	-	12/40
Total			179,759.57	185,077.10	76,959.48				267/622
<u>Railways</u>									
236	BHILDI-SAMDARI (GC) - [220100291]RVNL,Gujarat	04/1999	244.74	479.00	-	-	03/2010	12(R1)	0/0
237	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	-	03/2008	03/2010	21(R1)	0/0
238	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	24.70	02/2015	11/2010	-51(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
239	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]RVNL,Kerala	07/2006	246.50 246.50	246.50	-	03/2009 03/2009	11/2009	8(R3)	0/0
240	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 -	281.20	312.68	- -	09/2010	-	0/0
241	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	245.92	03/2008 03/2009	10/2010	19(R1)	0/0
242	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	546.55	- 03/2000	11/2010	128(R1)	0/0
243	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	724.31	695.80	- -	12/2010	-	0/0
244	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	- 02/2009	12/2010	22(R1)	0/0
245	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	159.30	- 03/2009	12/2010	21(R1)	0/0
246	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	-	12/2007 03/2010	12/2010	9(R1)	0/0
247	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
248	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	187.21	- -	12/2010	-	0/0
249	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,	04/2004	225.68 -	225.68	112.81	12/2010 -	12/2010	0(O)	0/0
250	DEOGHAR-DUMKA NEW BG LINE (DOUBL.) (ER) - [220100264]ER,Jharkhandd	02/1999	180.73 -	358.00	330.78	12/2006 12/2008	02/2011	26(R1)	0/0
251	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.16	418.48	02/2010 -	02/2011	12(O)	0/0
252	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 -	810.78	39.55	- -	02/2011	-	0/0
253	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056]SWR,Karnataka	12/1992	46.00 -	218.00	227.16	- -	02/2011	-	0/0
254	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	352.17	06/1999 -	03/2011	141(O)	0/0
255	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	03/1997	100.00 -	322.29	378.47	- -	03/2011	-	0/0
256	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	193.78 -	456.45	247.29	06/2004 -	03/2011	81(O)	0/0
257	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	476.70	05/2008 -	03/2011	34(O)	0/0
258	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 -	214.09	152.40	12/2009 -	03/2011	15(O)	0/0
259	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]SCR,Andhra Pradesh	05/2002	304.50 -	306.00	341.81	- -	03/2011	-	0/0
260	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	5,573.82	2,935.94	12/2006 08/2010	03/2011	7(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
261	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/1997	143.92	258.60	152.39	-	03/2011	-	0/0
262	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	200.73	230.03	130.77	-	03/2011	-	0/0
263	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	273.00	-	03/2009	03/2011	24(R1)	0/0
264	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	348.78	318.31	-	03/2011	-	0/0
265	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
266	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 255.96	272.11	202.03	-	03/2011	-	0/0
267	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15	245.15	77.36	12/2010	03/2011	3(O)	0/0
268	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10	171.10	43.83	03/2011	03/2011	0(O)	0/0
269	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	03/2006	258.35	258.35	9.38	03/2011	03/2011	0(O)	0/0
270	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97	196.97	127.14	03/2011	03/2011	0(O)	0/0
271	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36	803.39	716.11	03/2011	03/2011	0(O)	0/0
272	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	144.37	03/2011	03/2011	0(O)	0/0
273	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20	4,103.20	4,036.58	12/2010	06/2011	6(R3)	0/1
274	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50	252.50	-	02/2010	11/2011	21(O)	0/0
275	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64	735.10	-	09/2009	12/2011	27(R1)	0/0
276	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51	259.51	32.47	12/2011	12/2011	0(O)	0/0
277	Ghutarisharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97	189.97	32.69	12/2011	12/2011	0(O)	0/0
278	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	727.52	483.94	-	03/2012	-	0/0
279	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41	341.41	188.10	-	03/2012	-	0/0
280	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	415.59	495.74	93.88	-	03/2012	-	0/0
281	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	324.90	118.69	03/2010	03/2012	24(O)	0/0
282	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00	160.48	104.77	-	03/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
283	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	27.38	03/2012 -	03/2012	0(O)	0/0
284	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya pradesh	04/2008	603.04 -	603.04	22.04	03/2012 -	03/2012	0(O)	0/0
285	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]ER,Gujarat	04/2008	318.24 -	318.24	-	03/2012 -	03/2012	0(O)	0/0
286	TAMLUK DIGHA - [N22000097]LD, West Bengal	03/1984	293.97 -	293.97	313.13	06/2005 -	04/2012	82(O)	0/0
287	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	290.23	- -	07/2012	-	0/0
288	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	489.10	03/1994 -	12/2012	225(O)	0/0
289	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	2,100.00	519.88	- -	12/2012	-	0/0
290	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1997	248.44 576.27	1,103.47	709.36	- -	12/2012	-	0/0
291	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	383.15 -	863.23	335.28	- -	12/2012	-	0/0
292	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	234.45	163.01	- 03/2012	12/2012	9(R3)	0/0
293	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	420.77	03/2009 -	12/2012	45(O)	0/0
294	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.00	738.72	10/2007 -	12/2012	62(O)	0/0
295	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya pradesh	09/2007	687.20 -	687.20	224.54	03/2010 -	12/2012	33(O)	0/0
296	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	88.25	03/2010 -	12/2012	33(O)	0/0
297	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52 -	207.52	93.22	12/2012 -	12/2012	0(O)	0/0
298	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 -	410.08	114.62	- -	03/2013	-	0/0
299	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	608.40	- -	03/2013	-	0/0
300	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	912.70 912.70	1,556.23	337.10	- -	03/2013	-	0/0
301	Ramanagram-Musore doubling with deiltification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.00	139.15	03/2013 -	03/2013	0(O)	0/0
302	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.13	0.03	03/2013 -	03/2013	0(O)	0/0
303	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya pradesh	04/2005	383.79 -	585.93	139.81	- -	12/2013	-	0/0
304	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR, Assam	04/1996	1,000.00 1,500.00	3,230.02	1,958.06	04/2008 12/2011	03/2014	27(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
305	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	02/2000	733.00	1,655.80	574.72	12/2008	03/2014	63(O)	0/0
306	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	813.34	111.38	03/2014	03/2014	0(O)	0/0
307	BHAIRABI SAIRONG, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	2,429.41	1.61	04/2014	03/2014	-1(O)	0/0
308	New Work for Construction of Metro railway from Bu - [N22000109]RVNL,West Bengal	04/2010	2,069.60	2,069.60	-	03/2014	03/2014	0(O)	0/0
309	Jaipur - Ringus - Churu and Sikar - Lohatu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19	653.19	1.89	03/2014	03/2014	0(O)	0/0
310	Suratpura - Hanumangarh - Sriganganagar Guage Canv - [N22000114]NWR,Rajasthan	04/2008	516.23	516.23	1.70	03/2014	03/2014	0(O)	0/0
311	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62	1,389.62	60.11	03/2014	03/2014	0(O)	0/0
312	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66	324.66	137.31	-	03/2015	-	0/0
313	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTD,Maharashtra	04/2008	5,300.00	5,300.00	148.59	03/2014	03/2015	12(O)	0/0
314	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48	3,380.57	52.90	12/2015	03/2015	-9(O)	0/0
315	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74	829.74	-	03/2015	03/2015	0(O)	0/0
316	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00	850.00	5.16	03/2015	03/2015	0(O)	0/0
317	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,123.52	255.39	03/2011	03/2016	60(O)	0/0
318	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	3,447.41	5,573.83	-	03/2016	03/2016	0(O)	0/0
319	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98	3,951.98	-	03/2016	03/2016	0(O)	0/0
320	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02	2,619.02	-	03/2016	03/2016	0(O)	0/0
321	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	6,624.21	03/2001	12/2017	201(O)	0/0
322	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	526.02	03/1995 03/2010	-	-	0/0
323	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43	617.63	386.41	-	-	-	0/0
324	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	464.50	498.52	03/1996 06/2009	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
325	HOTGI-GADAG(GC),SWR - [220100125]SWR,Multi State	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
326	AMBALA-MORADABAD(RE) - [220100131]RE,Multi State	03/1993	152.21 157.76	265.00	265.33	03/1998 -	-	-	0/0
327	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	01/1986	36.80 274.41	285.93	232.31	- -	-	-	0/0
328	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECR,Orissa	04/1993	100.00 119.29	170.00	111.69	03/2002 -	-	-	0/0
329	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]SECR,Chhatisgarh	04/1995	369.00 968.60	1,317.24	50.08	- -	-	-	0/0
330	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	581.69	- -	-	-	0/0
331	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 -	675.00	361.41	- 12/2011	-	-	0/0
332	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	67.32	- -	-	-	0/0
333	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	473.63	- -	-	-	0/0
334	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	356.00 -	1,038.00	491.58	03/1998 -	-	-	0/0
335	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 -	157.00	119.88	- 03/2012	-	-	0/0
336	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	712.00	432.80	- -	-	-	0/0
337	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1997	155.74 164.36	429.49	363.58	02/2009 -	-	-	0/0
338	HUBLI-AKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	54.94	- -	-	-	0/0
339	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,548.95	1,117.42	- -	-	-	0/0
340	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1996	377.32 236.41	497.47	82.45	- -	-	-	0/0
341	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	154.30	106.79	03/2007 03/2007	-	-	0/0
342	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
343	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 -	1,099.20	846.72	07/2005 -	-	-	0/0
344	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR,Kerala	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0
345	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00 -	513.16	520.42	- -	-	-	0/0
346	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	65.39	- -	-	-	0/0
347	PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
348	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1999	242.42 369.70	369.70	151.69	- 05/2009	-	-	0/0
349	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	09/2001	320.10 -	522.56	306.05	- -	-	-	0/1
350	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	03/1997	78.23 -	162.87	79.22	- -	-	-	0/0
351	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 408.76	639.54	783.08	06/2007 -	-	-	0/0
352	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	272.46	04/2003 03/2010	-	-	0/0
353	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	432.28	- -	-	-	0/0
354	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
355	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 -	228.09	198.33	- -	-	-	0/0
356	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 240.59	607.09	253.60	- 12/2012	-	-	0/0
357	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
358	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	325.17	311.98	03/2005 12/2008	-	-	0/0
359	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECR,Orissa	04/1994	355.38 -	700.00	97.09	- -	-	-	0/0
360	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	61.34	- -	-	-	0/0
361	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	152.79	- -	-	-	0/0
362	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	104.10 -	218.19	74.11	- -	-	-	0/0
363	KICHHA-KHATIMA (NL) - NER - [220100317]NER,Uttaranchal	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
364	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
365	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 -	671.82	1.05	- -	-	-	0/0
366	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1998	186.92 -	261.70	0.08	02/2006 -	-	-	0/0
367	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 -	224.51	41.39	- -	-	-	0/0
368	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 -	881.19	86.35	- -	-	-	0/0
369	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	98.25	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
370	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	284.20	-	-	-	0/0
371	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	17.44	-	-	-	0/0
372	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	42.02	-	-	-	0/0
373	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	529.88	27.33	-	-	-	0/0
374	KISHANGANJ JALALGARH, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	333.76	0.71	-	-	-	0/0
375	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]GC,Assam	04/1993	100.41	949.22	15.65	12/2009	-	-	0/0
376	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	131.60	-	03/2011	-24(R3)	0/0
377	MIRAJ-LATUR ROAD(GC),CR - [220100162]CR,Maharashtra	04/1993	225.00	816.40	827.29	03/2001	-	-	0/0
378	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81	495.44	156.46	03/2004	12/2010	81(O)	0/0
379	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40	563.25	540.90	03/2004	-	-	0/0
380	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96	762.33	313.01	-	12/2010	12(R1)	0/0
381	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36	452.35	295.09	-	03/2011	-	0/0
382	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00	390.00	0.93	-	03/2014	-	0/0
Total			68,578.35	126,174.41	46,401.58				0/2
Road Transport & Highways									
383	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]NHAI,Kerala	04/2000	106.00	193.00	141.70	08/2006	12/2010	52(O)	0/0
384	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	102.51	08/2004	12/2010	76(O)	0/0
385	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	112.45	08/2004	12/2010	76(O)	0/0
386	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73	205.73	244.90	07/2004	12/2010	77(O)	0/0
387	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]NHAI,Tamil Nadu	12/2003	480.00	480.00	844.20	11/2007	12/2010	37(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
388	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	658.50	04/2007 -	12/2010	44(O)	0/0
389	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	286.70	09/2007 -	12/2010	39(O)	0/0
390	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	424.80	11/2007 -	12/2010	37(O)	0/0
391	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	307.10	10/2008 -	12/2010	26(O)	0/0
392	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00 -	217.00	333.80	10/2008 -	12/2010	26(O)	0/0
393	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	193.10	105.30	03/2008 -	12/2010	33(O)	0/0
394	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36 -	323.36	189.90	03/2008 -	12/2010	33(O)	0/0
395	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]NHAI,Uttar Pradesh	12/2003	239.00 -	239.00	395.70	10/2008 -	12/2010	26(O)	0/0
396	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI,Uttar Pradesh	12/2003	205.00 -	205.00	324.40	10/2008 -	12/2010	26(O)	0/0
397	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI,Uttar Pradesh	12/2003	212.00 -	212.00	367.60	10/2008 -	12/2010	26(O)	0/0
398	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	12/2010	23(O)	0/0
399	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	905.80	11/2010 -	12/2010	1(O)	0/0
400	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam	12/2003	230.00 -	230.00	291.80	06/2008 -	12/2010	30(O)	0/0
401	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]NHAI,Bihar	12/2003	291.80 -	291.80	436.10	06/2008 -	12/2010	30(O)	0/0
402	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	261.20	10/2008 -	12/2010	26(O)	0/0
403	SAGAR - RAJMARG CHORAHA,KM 255-297, NH-26 (NHAI) - [240106302]NHAI,Madhya pradesh	12/2003	206.96 -	206.96	281.90	10/2008 -	12/2010	26(O)	0/0
404	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	172.80	07/2008 -	12/2010	29(O)	0/0
405	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	571.10	03/2009 -	12/2010	21(O)	0/0
406	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	196.50	202.70	06/2008 -	12/2010	30(O)	0/0
407	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	189.30	11/2008 -	12/2010	25(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
408	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	305.40	12/2008	12/2010	24(O)	0/0
409	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	574.40	06/2009	12/2010	18(O)	0/0
410	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]NHAI, Andhra Pradesh	12/2003	208.46	208.46	197.80	08/2009	12/2010	16(O)	0/0
411	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]NHAI, Andhra Pradesh	12/2003	239.19	239.19	224.80	09/2009	12/2010	15(O)	0/0
412	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]NHAI, Andhra Pradesh	12/2003	243.38	243.38	286.40	09/2008	12/2010	27(O)	0/0
413	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]NHAI, Andhra Pradesh	12/2003	194.80	194.80	179.70	08/2009	12/2010	16(O)	0/0
414	BANGALORE-NEELAMANGALALA NH-4 - [N24000104]NHAI, Karnataka	03/2005	445.00	445.00	803.40	07/2010	12/2010	5(O)	0/0
415	BANGALORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI, Karnataka	03/2005	565.00	565.00	919.20	07/2010	12/2010	5(O)	0/0
416	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	112.07	02/2004	12/2010	82(O)	0/0
417	GONDE-VADAPE (THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI, Maharashtra	03/2005	579.00	579.00	693.50	04/2009	01/2011	21(O)	0/0
418	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	197.20	06/2008	01/2011	31(O)	0/0
419	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	340.00	07/2010	01/2011	6(O)	0/0
420	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	285.00	241.40	07/2010	01/2011	6(O)	0/0
421	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	411.40	01/2011	01/2011	0(O)	0/0
422	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	140.10	09/2007	03/2011	42(O)	0/0
423	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	03/2011	72(O)	0/0
424	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	342.60	03/2005	03/2011	72(O)	0/0
425	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]NHAI, Uttar Pradesh	12/2003	158.06	158.06	158.30	08/2005	03/2011	67(O)	0/0
426	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI, Bihar	12/2003	239.00	239.00	280.10	07/2005	03/2011	68(O)	0/0
427	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]NHAI, Bihar	12/2003	275.00	275.00	307.20	07/2005	03/2011	68(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
428	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	213.00	10/2008	03/2011	29(O)	0/0
429	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]NHAI,Uttar Pradesh	12/2003	451.97	451.97	518.80	04/2008	03/2011	35(O)	0/0
430	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	310.80	03/2008	03/2011	36(O)	0/0
431	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00	359.00	632.80	03/2009	03/2011	24(O)	0/0
432	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI,Assam	12/2003	225.00	225.00	204.40	06/2008	03/2011	33(O)	0/0
433	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	146.30	11/2008	03/2011	28(O)	0/0
434	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	215.00	10/2008	03/2011	29(O)	0/0
435	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	496.90	06/2008	03/2011	33(O)	0/0
436	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	275.40	06/2009	03/2011	21(O)	0/0
437	BARA TO ORAI, NH-2, 25 - [N24000069]NHAI,Uttar Pradesh	12/2003	465.00	465.00	36.22	04/2009	03/2011	23(O)	0/0
438	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00	309.00	538.30	06/2010	03/2011	9(O)	0/0
439	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	232.10	10/2009	03/2011	17(O)	0/0
440	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	244.50	09/2009	03/2011	18(O)	0/0
441	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	184.60	09/2009	03/2011	18(O)	0/0
442	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	655.20	07/2010	03/2011	8(O)	0/0
443	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	133.20	09/2010	03/2011	6(O)	0/0
444	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	230.18	02/2004	04/2011	86(O)	0/0
445	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	332.10	12/2008	05/2011	29(O)	0/0
446	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	589.30	08/2010	05/2011	9(O)	0/0
447	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI,Madhya pradesh	11/2008	549.00	549.00	674.40	05/2010	05/2011	12(O)	0/0
448	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	437.90	05/2010	05/2011	12(O)	0/0
449	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	175.10	09/2007	06/2011	45(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
450	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	69.92	09/2008	06/2011	33(O)	0/0
451	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	115.70	03/2008	06/2011	39(O)	0/0
452	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	288.70	10/2008	06/2011	32(O)	0/0
453	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	320.50	12/2008	06/2011	30(O)	0/0
454	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	226.70	09/2008	06/2011	33(O)	0/0
455	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	205.60	10/2008	06/2011	32(O)	0/0
456	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	150.30	10/2008	06/2011	32(O)	0/0
457	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	538.00	10/2009	06/2011	20(O)	0/0
458	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	257.90	12/2009	06/2011	18(O)	0/0
459	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04	418.04	255.60	03/2010	06/2011	15(O)	0/0
460	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	502.50	07/2010	06/2011	11(O)	0/0
461	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	598.50	01/2011	06/2011	5(O)	0/0
462	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	1,547.00	08/2011	08/2011	0(O)	0/0
463	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	28.94	04/2004	10/2011	90(O)	0/0
464	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	207.60	06/2008	10/2011	40(O)	0/0
465	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2011	4(O)	0/0
466	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	70.68	10/2011	10/2011	0(O)	0/0
467	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	972.00	10/2011	10/2011	0(O)	0/0
468	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	10.92	10/2011	10/2011	0(O)	0/0
469	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI,Bihar	12/2003	305.00	305.00	468.80	06/2008	11/2011	41(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
470	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	137.30	10/2008 -	11/2011	37(O)	0/0
471	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	1,409.00	11/2011 -	11/2011	0(O)	0/0
472	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	137.90	06/2005 -	12/2011	78(O)	0/0
473	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	174.70	02/2009 -	12/2011	34(O)	0/0
474	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	64.29	04/2009 -	12/2011	32(O)	0/0
475	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	126.30	06/2008 -	12/2011	42(O)	0/0
476	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	126.40	06/2008 -	12/2011	42(O)	0/0
477	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	154.60	10/2008 -	12/2011	38(O)	0/0
478	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	358.80	09/2008 -	12/2011	39(O)	0/0
479	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	193.80	06/2008 -	12/2011	42(O)	0/0
480	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	254.50	03/2008 -	12/2011	45(O)	0/0
481	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	151.40	06/2008 -	12/2011	42(O)	0/0
482	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	168.60	04/2008 -	12/2011	44(O)	0/0
483	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	87.38	05/2008 -	12/2011	43(O)	0/0
484	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	152.50	06/2008 -	12/2011	42(O)	0/0
485	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	96.64	04/2008 -	03/2012	47(O)	0/0
486	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	144.40	04/2008 -	03/2012	47(O)	0/0
487	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	76.93	04/2010 -	03/2012	23(O)	0/0
488	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	177.50	02/2010 -	03/2012	25(O)	0/0
489	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	926.10	02/2010 -	05/2012	27(O)	0/0
490	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	339.80	05/2012 -	05/2012	0(O)	0/0
491	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	431.70	05/2012 -	05/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
492	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	133.50	10/2008 -	06/2012	44(O)	0/0
493	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	835.00	67.60	06/2012 -	06/2012	0(O)	0/0
494	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	95.50	07/2012 -	07/2012	0(O)	0/0
495	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	52.44	05/2008 -	08/2012	51(O)	0/0
496	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00 -	359.00	58.55	05/2010 -	08/2012	27(O)	0/0
497	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60 -	407.60	182.20	06/2010 -	09/2012	27(O)	0/0
498	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17 -	263.17	232.50	09/2009 -	09/2012	36(O)	0/0
499	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	1,509.10	467.90	09/2012 -	10/2012	1(O)	0/0
500	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	348.16	108.90	09/2007 -	06/2013	69(O)	0/0
501	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	199.81	28.52	04/2009 -	12/2013	56(O)	0/0
502	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	39.52	11/2008 -	12/2013	61(O)	0/0
503	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	155.04	28.37	11/2008 -	12/2013	61(O)	0/0
504	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	212.00	37.62	09/2007 -	12/2013	75(O)	0/0
505	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	196.00	25.33	07/2009 -	12/2013	53(O)	0/0
	Total		44,403.11 -	46,104.91	37,313.67				0/0
Shipping & Ports									
506	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40 -	2,427.40	819.36	10/2008 -	11/2010	25(O)	0/0
507	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]PORT TRUST, Kerala	03/2007	245.67 298.17	395.05	297.76	04/2009 11/2009	12/2010	13(R3)	0/0
508	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	366.00 -	366.00	1.43	12/2010 -	12/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
509	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	230.00	-	12/2010 -	12/2010	0(O)	0/0
510	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 -	165.00	107.58	12/2005 -	01/2011	61(O)	0/0
511	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,140.00	0.38	02/2011 -	02/2011	0(O)	0/0
512	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 253.36	253.36	222.07	06/2007 07/2009	03/2011	20(R3)	0/0
513	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]SHIPP.,Maharashtra	08/2007	586.58 -	586.58	634.09	11/2010 -	03/2011	4(O)	0/0
514	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	0.73	03/2011 -	03/2011	0(O)	0/0
515	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	324.50	04/2011 -	04/2011	0(O)	0/0
516	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	290.85 -	290.85	72.59	03/2011 -	06/2011	3(O)	0/0
517	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra	08/2008	1,108.12 -	1,168.42	760.34	04/2011 -	12/2011	8(O)	0/0
518	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 -	277.03	55.40	09/2011 -	12/2011	3(O)	0/0
519	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 -	1,061.96	219.98	03/2012 -	01/2012	-2(O)	0/0
520	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	2,948.00	01/2012 -	01/2012	0(O)	0/0
521	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	10.00	09/2005 -	03/2012	78(O)	0/0
522	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	252.00	-	03/2012 -	03/2012	0(O)	0/0
523	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	08/2012	-1(O)	0/0
524	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
525	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 -	612.72	61.31	12/2012 -	12/2012	0(O)	0/0
526	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 -	272.50	-	01/2009 -	05/2013	52(O)	0/0
527	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.22	10/2008 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			16,082.62	16,926.26	6,763.65				0/0
<u>Telecommunications</u>									
528	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	216.14	09/2009	02/2010	5(O)	0/0
529	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	109.31	12/2005	10/2010	58(O)	0/0
530	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
531	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
532	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
533	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	73.73	02/2007 03/2010	12/2010	9(R3)	0/0
534	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86 234.24	353.00	234.24	02/2008	12/2010	34(O)	0/0
535	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
536	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	12/2010	21(O)	0/0
537	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
538	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
539	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
540	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
541	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	01/2011	24(O)	0/0
542	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	75.25	09/2010	01/2011	4(O)	0/0
543	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	127.46	06/2009	01/2011	19(O)	0/0
544	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	219.08	10/2008	01/2011	27(O)	0/0
545	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 392.44	392.44	164.58	03/2009	01/2011	22(O)	0/0
546	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	266.06	01/2010	01/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
547	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	107.88	01/2010	01/2011	12(O)	0/0
548	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]BSNL,West Bengal	09/2006	208.50	208.50	146.00	09/2008	02/2011	29(O)	0/0
549	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	477.08	12/2008	02/2011	26(O)	0/0
550	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.88	03/2009	02/2011	23(O)	0/0
551	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	176.33	12/2008	02/2011	26(O)	0/0
552	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	307.00	03/2009	02/2011	23(O)	0/0
553	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	169.43	03/2009	02/2011	23(O)	0/0
554	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	88.17	06/2009	02/2011	20(O)	0/0
555	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	90.50	09/2009	02/2011	17(O)	0/0
556	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	31.15	10/2009	02/2011	16(O)	0/0
557	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	02/2011	12(O)	0/0
558	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	378.85	02/2009	02/2011	24(O)	0/0
559	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	274.30	08/2009	02/2011	18(O)	0/0
560	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	211.83	11/2010	02/2011	3(O)	0/0
561	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	810.37	748.30	01/2010	02/2011	13(O)	0/0
562	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.70	719.70	308.06	10/2009	02/2011	16(O)	0/0
563	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	441.28	01/2010	02/2011	13(O)	0/0
564	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007 11/2009	03/2011	16(R3)	0/0
565	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	12.72	10/2010	04/2011	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
566	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	09/2011	389.86	389.86	2.13	09/2011	09/2011	0(O)	0/0
567	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
568	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
569	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	-	-	0/0
	Total		20,234.49	20,696.79	6,916.79				0/0
	Urban Development								
570	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00	18,894.36	16,254.46	06/2010	12/2010	6(O)	0/8
571	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	3,523.65	12/2011	03/2013	15(O)	6/6
	Total		15,071.00	30,503.36	19,778.11				6/14
	Water Resources								
572	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			592,196.97	714,501.64	304,331.57				853/2107


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

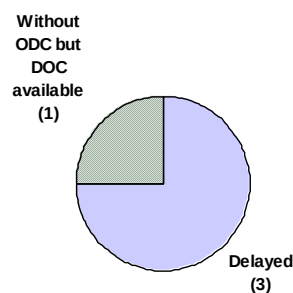

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs. 18964.66 Crores.

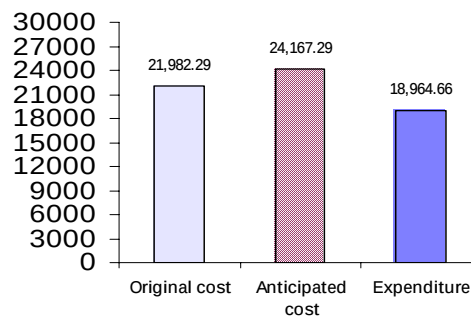


2. Sector: - Civil Aviation

Number of Projects	8
Number of Projects on schedule	4
Number of Projects Delayed	2
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule, 2 projects are delayed and 1 projects are original date of commissioning and 1 projects are Wo_Odc_Original.

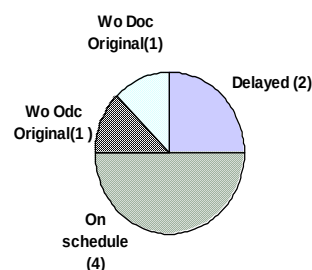

Investment Scenario

The total cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4812.40 Crores but this was subsequently revised to Rs. 4812.40 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs 2379.84 Crores.

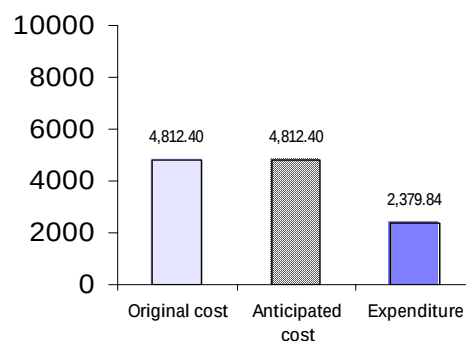


3. Sector: - Coal

Number of Projects	44
Number of Projects on schedule	16
Number of Projects Delayed	19
Number of Projects Ahead	1
Number of Projects Wo_ODC_Original	7
Number of Projects Wo_DOC_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 44 projects, 16 projects are on schedule, 19 projects are delayed and 1 projects are ahead and 7 Project W_Odc_Original and 1 Project W_Odc_Original .



Investment Scenario

The total cost of implementation of 44 projects when sanctioned, was of the order of Rs. 25210.30 Crores but this was subsequently revised to Rs. 28542.29 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs 9636.83 Crores

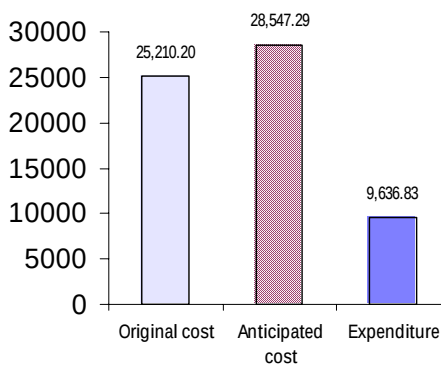


4. Sector: - Petroleum

Number of Projects	70
Number of Projects on schedule	25
Number of Projects Delayed	31
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	1
Number of Projects Without original date of commissioning	11


Brief Analysis

Project Status with respect to Original Schedule: Out of 70 projects, 25 projects are on schedule, 31 projects are delayed and 2 projects are ahead and 1 projects is without date of commissioning and 11 Project is Without original date of commissioning.

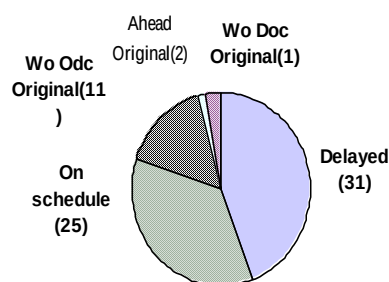

Investment Scenario

The total cost of implementation of 70 projects when sanctioned, was of the order of Rs. 142330.59 Crores but this was subsequently revised to Rs. 155206.10 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs. 48309.52 Crores.

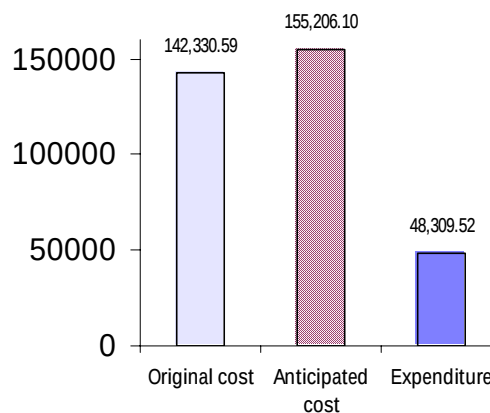


5. Sector: - Power


Number of Projects	83
Number of Projects on schedule	37
Number of Projects Delayed	40
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	4
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 83 projects, 37 projects are on schedule, 40 projects are delayed, and 1 Projects are Ahead, 4 projects are without date of commissioning and 1 projects is without original date of commissioning

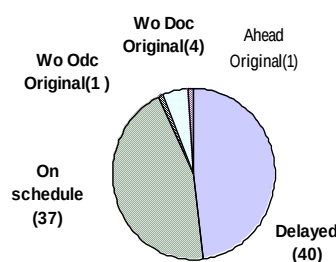

Investment Scenario

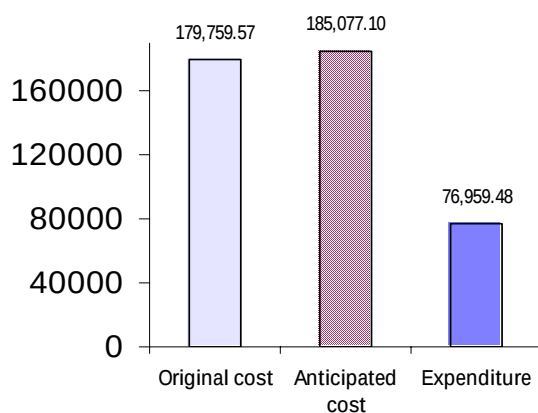


The total cost of implementation of 83 projects when sanctioned, was of the order of Rs. 179759.57 Crores but this was subsequently revised to Rs. 185077.10 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs. 76969.48 Crores.

6. Sector: - Railways

Number of Projects	147
Number of Projects on schedule	24
Number of Projects Delayed	25
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	58
Number of Projects Wo_Odc_Original	37


Brief Analysis

Project Status with out respect Original Schedule: Out of 147 projects, 24 projects are on schedule, 25 projects are delayed, 3 projects is ahead. 58 projects are Without date of commissioning and 37 projects are without original date of commissioning.

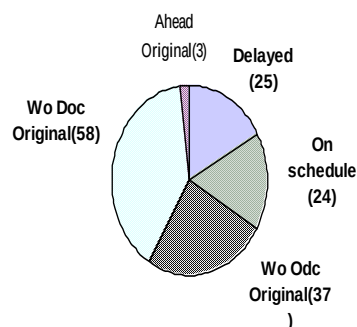

Investment Scenario

The total cost of implementation of 147 projects when sanctioned, was of the order of Rs. 68578.35 Crores but this was subsequently revised to Rs. 126174.41 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs. 46401.58 Crores.

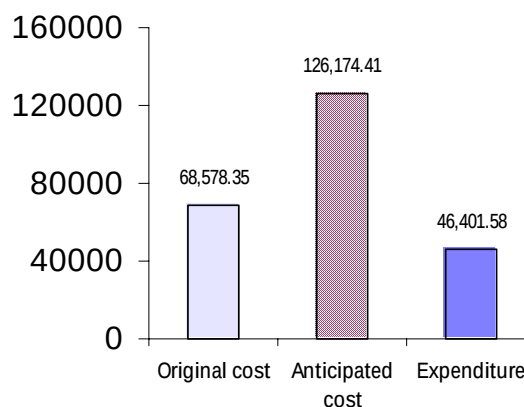


7. Sector: - Road Transport and Highways

Number of Projects	123
Number of Projects on schedule	10
Number of Projects Delayed	113


Brief Analysis

Project Status with respect to Original Schedule: Out of 123 projects, 10 projects are on schedule, 113 projects are delayed 1 projects are Without date of commissioning



Investment Scenario

The total cost of implementation of 123 projects when sanctioned, was of the order of Rs 44403.11 Crores but this was subsequently revised to Rs. 46104.91 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs. 37313.67 Crores.

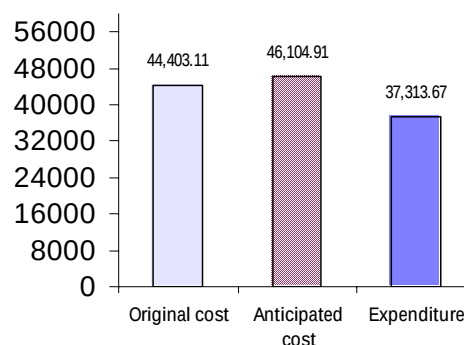


8. Sector: - Shipping and Ports

Number of Projects	22
Number of Projects on schedule	8
Number of Projects Delayed	11
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 8 projects are on schedule, 11 projects are delayed, 2 projects are ahead and 1 projects are without date of commissioning.

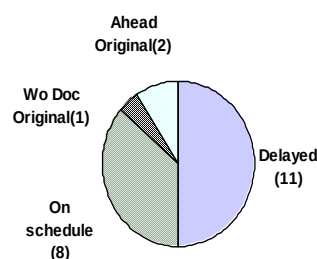

Investment Scenario

The total cost of implementation of 22 projects when sanctioned, was of the order of Rs.16082.62 Crores but this was subsequently revised to Rs. 16926.26 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs. 6763.65 Crores.

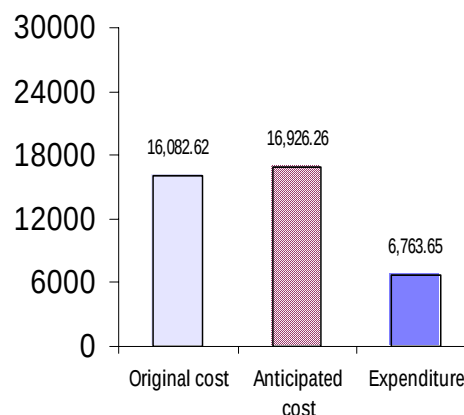


9. Sector: - Steel

Number of Projects	19
Number of Projects On schedule	3
Number of Projects Delayed	9
Number of Projects Wo_Doc_Original	5
Number of Projects Wo_Odc_Original	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 9 projects are delayed and 3 projects are on Schedule and 5 projects are Wo_Doc_Original and 2 Project is Wo_Odc_Original.

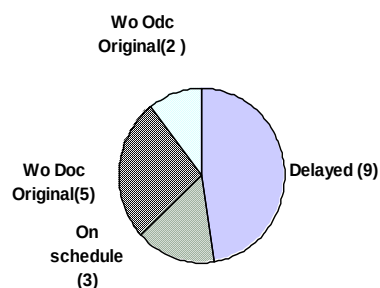

Investment Scenario

The total cost of implementation of 19 projects when sanctioned, was of the order of Rs.43780.53 Crores but this was subsequently revised to Rs. 65379.16 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs. 26726.72 Crores.

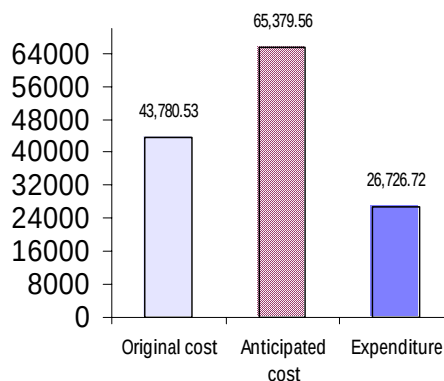


10. Sector: - Telecommunications

Number of Projects	42
Number of Projects Delayed	34
Number of Projects on Schedule	1
Number of Projects Wo_Doc_Original	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 42 projects, 34 projects are delayed and 7 projects are with out date of commissioning, and 1 projects are on schedule.

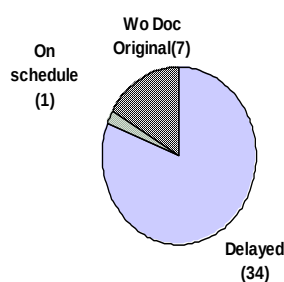

Investment Scenario

The total cost of implementation of 42 projects when sanctioned, was of the order of Rs 20234.49 Crores but this was subsequently revised to Rs. 20696.79 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs 6916.79 Crores.

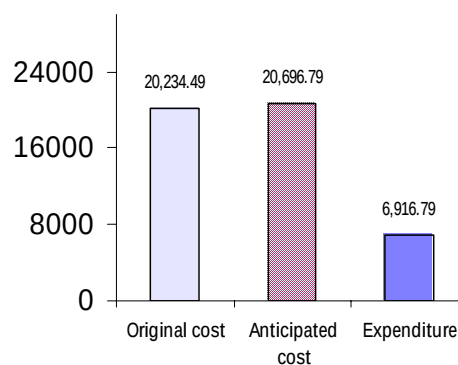


11. Sector: - Fertilisers

Number of Projects	6
Number of Projects on Schedule	5
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 1 projects are Wo_Odc_Original, and 5 projects are on schedule.



Investment Scenario

The total cost of implementation of 6 projects when sanctioned, was of the order of Rs 5317.41 Crores but this was subsequently revised to Rs. 5317.41 Crores. The expenditure incurred on these projects till Nov, 2010 is Rs 251.25 Crores.

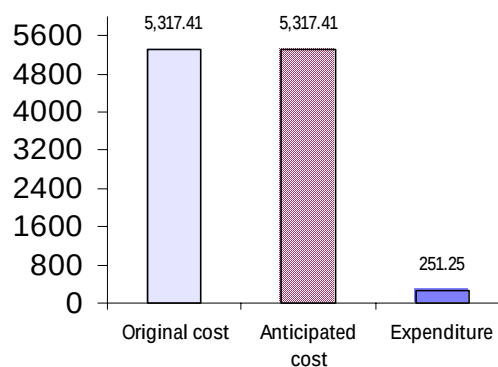

STATE WISE SUMMARY AS ON 30.11.2010

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	EXPENDITURE CUMM
1	Andhra Pradesh	34	28509.86	35141.14	15935.69
2	Arunachal Pr.	4	9512.22	9516.70	5852.26
3	Assam	40	23365.64	28403.00	12270.30
4	Bihar	31	29763.01	32829.80	17913.56
5	Chhatisgarh	17	20698.98	36333.97	12430.83
6	Delhi	2	8925.00	19123.77	16320.66
7	Goa	1	204.73	204.73	16.04
8	Gujarat	24	16555.73	19059.73	10132.23
9	Haryana	10	4821.32	6379.33	2952.12
10	Himachal Pr.	8	15381.72	15463.96	10463.88
11	J & K	8	8297.84	18482.36	9927.04
12	Jharkhandd	22	9929.62	14866.24	5424.70
13	Karnataka	19	15972.06	23591.38	11476.98
14	Kerala	11	9511.93	11036.60	8761.45
15	Madhya pradesh	27	20530.46	20708.59	7870.62
16	Maharashtra	50	64090.00	83699.41	28528.86
17	Manipur	1	578.62	578.62	28.33
18	Mizoram	2	988.06	3343.04	219.32
19	Multi State	96	113546.53	117908.42	32220.70
20	Nagaland	1	850.00	850.00	5.16
21	Orissa	26	49676.83	53643.33	13451.59
22	Punjab	9	5064.09	6028.72	2042.03
23	Rajasthan	14	11692.97	12782.09	7149.78
24	Sikkim	2	1603.77	3644.86	132.07
25	Tamil Nadu	34	42590.66	48788.99	33491.98
26	Tripura	3	1522.39	1724.82	180.70
27	Uttar Pradesh	38	23743.51	25662.26	14766.61
28	Uttaranchal	9	12100.46	14517.85	4244.46
29	West Bengal	29	42168.96	50400.15	20142.99
TOTAL		572	592196.97	714713.86	304352.94

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
