


**325th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
November, 2012**



PORT TRUST - DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A

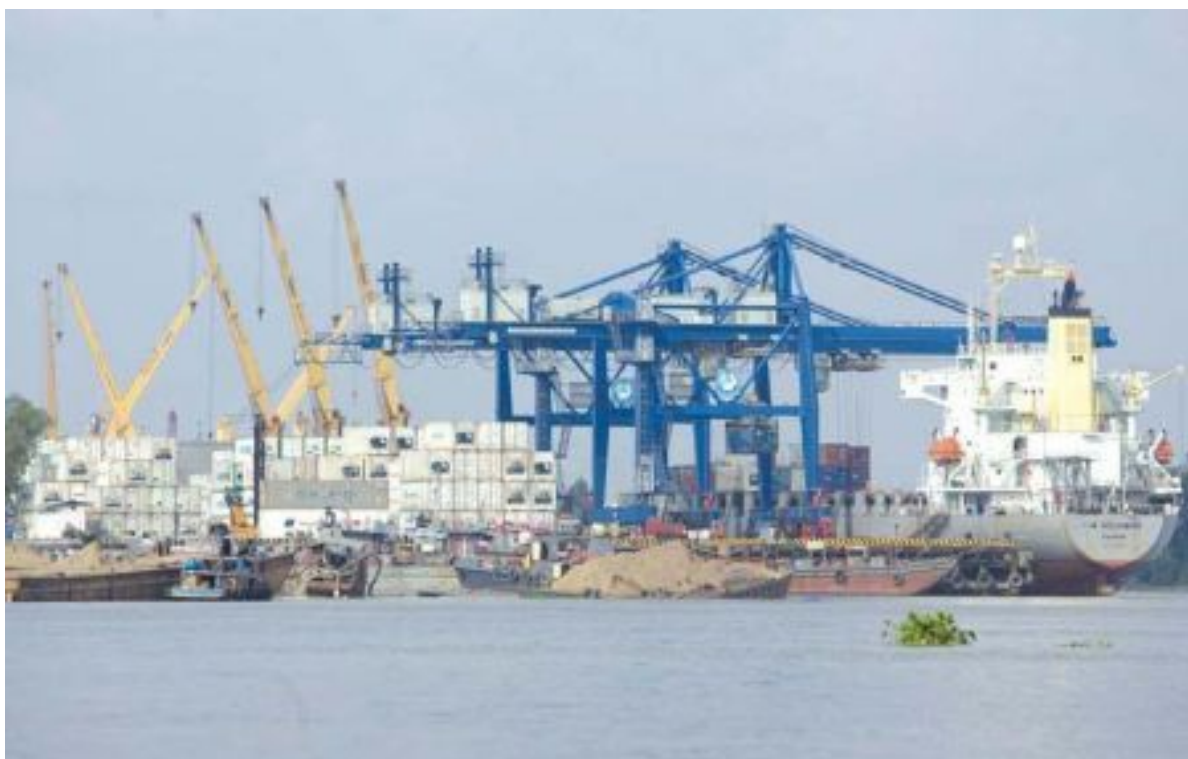

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

नवंबर, 2012 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 566 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। नवंबर, 2012 के दौरान पेट्रोलियम क्षेत्र की 2 परियोजनाओं के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 566 परियोजनाओं में से 249 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 30 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 30 परियोजनाओं में से, 12 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। ऊर्वरक, इस्पात, रेलवे, पोत परिवहन तथा पत्तन, पेट्रोलियम, विद्युत तथा सड़क परिवहन एवं राजमार्ग क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 13 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	127	30	1	0
2.	सड़क परिवहन एवं राजमार्ग	146	86	10	2
3.	विद्युत	99	51	9	5
4.	पेट्रोलियम	72	34	6	3
5.	कोयला	51	20	0	0
6.	दूरसंचार	13	7	0	0
7.	पोत परिवहन एवं पत्तन	19	5	2	1
8.	इस्पात	17	10	1	1
9.	ऊर्वरक	5	1	1	0
10.	नागर विमानन	6	0	0	0
11.	परमाणु ऊर्जा	5	3	0	0
12.	शहरी विकास	4	1	0	0
13.	जल संसाधन	1	1	0	0
14.	पेट्रोरसायन	1	0	0	0
कुल		566	249	30	12

3. 566 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,93,285.10 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,33,569.56 करोड़ रुपए होने की संभावना है जो 1,40,284.46 करोड़ रुपए (मूल लागत का 17.70%) की समग्र लागत वृद्धि को दर्शाता है। नवंबर, 2012 तक इन परियोजनाओं पर किया गया व्यय 4,33,732.24 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 46.50% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (30.11.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	499.16	1488.67
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1412.74	1162.50
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. 566 परियोजनाओं में से, 4 परियोजनाएं समय से पहले चल रही हैं, 195 समय पर तथा 249 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या 270 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है। इसके अलावा, 30 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 88 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया गया है। 249 विलंबित परियोजनाओं में से, 72 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 52 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 94 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 31 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (30.11.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2013	216
2	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
3	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	06/2016	135
4	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	06/2005	06/2016	132
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	01/2013	132

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की समीक्षा करेंगे ।

5. विभिन्न परियोजना कार्यान्वयनकर्ता एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, वन संबंधी स्वीकृति में विलंब, मेसर्स बीएचईएल द्वारा सामग्री की आपूर्ति में विलंब, ठेकेदार द्वारा धीमी प्रगति, आरओयू समस्या, बोलीदाता द्वारा एनआईटी को उत्तर नहीं दिया जाना, सीपेज समस्या, भूगर्भीय आकस्मिकताएं, कानून और व्यवस्था की समस्या आदि शामिल हैं ।

6. मंत्रालय की ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाओं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दिए गए हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (30.11.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	499.16	169.68	03/2007	03/2015	0
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	730	352.01	07/2012	ऊ.न.	0
3	इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.8	703.17	242.39	ऊ.न.	03/2015	0
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520	634.13	555.27	03/1995	03/2013	0
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1086.41	427.98	06/2005	06/2016	0

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

7. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (30.11.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)
				मूल	अनुमानित	
1	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	रेलवे	04/1985	158.77	432.46	558.07
2	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	205.16
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	538.10
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	590.02
5	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8521.82

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (30.11.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	उ.न.	उ.न.
2	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	रेलवे	04/1985	03/1994	उ.न.	12/2011
3	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	उ.न.	03/2010	उ.न.
4	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
5	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल		12/1994	उ.न.	उ.न.	03/2012

	(एससीआर)	रेलवे				
--	----------	-------	--	--	--	--

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

8. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है :-

(i) **उर्वरक क्षेत्र में**, 05 परियोजनाओं में से 01 परियोजना विलंबित है । माह के दौरान 'नांगल-अमोनिया प्लांट फीडस्टॉक परियोजना, एनएफएल में 3 महीने अतिरिक्त विलंब की सूचना प्राप्त हुई है । तथापि, परियोजना प्राधिकारियों द्वारा इस परियोजना में विलंब के लिए किसी विशेष कारण की सूचना नहीं दी गई है ।

(ii) **इस्पात क्षेत्र में**, 17 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं । माह के दौरान 'कोक ओवेन बैटरी सं.4 चरण-II, आरआईएनएल' नामक मेगा परियोजना ने एनआईटी को बोलीदाताओं द्वारा किसी प्रत्युत्तर के नहीं प्राप्त होने के कारण 3 महीने अतिरिक्त विलंब की सूचना दी है ।

(iii) **रेलवे क्षेत्र में**, 127 परियोजनाओं में से 30 परियोजनाएं विलंबित हैं । माह के दौरान 'लांझीगढ़-जूनागढ़ एनएल, इसीओआर' परियोजना ने कार्य की धीमी प्रगति के कारण 2 महीने अतिरिक्त विलंब की सूचना दी है ।

(iv) **पोत परिवहन तथा पत्तन क्षेत्र में**, 19 परियोजनाओं में से 5 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से एक मेगा परियोजना है । 'एंकर हैंडलिंग कम सप्लाई शिपिंग संख्या 4 के पुथु पोर्ट ट्रस्ट पर एलएनजी रिगेसिफिकेशन टर्मिनल की स्थापना' परियोजना के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना दी गई है । तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है ।

(v) **पेट्रोलियम क्षेत्र में**, 72 परियोजनाओं में से 34 परियोजनाएं विलंबित हैं । माह के दौरान, 6 परियोजनाओं के संबंध में 1-3 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 4 बड़ी परियोजनाएं हैं । इन 6 परियोजनाओं में से, 4 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'कम्प्रेसर स्टेशन्स (कैलारास तथा चेन्सा) गेल' परियोजना ने ठेकेदार द्वारा धीमी प्रगति के कारण 2 महीने अतिरिक्त विलंब की सूचना दी है । 'कोची-कूटांड बंगलोर मंगलोर पाइप लाइन परियोजना गेल' ने आरओयू समस्या के कारण 3 महीने अतिरिक्त विलंब की सूचना दी है ।

(vi) **विद्युत क्षेत्र में**, 99 परियोजनाओं में से 51 परियोजनाएं विलंबित हैं । माह के दौरान 9 परियोजनाओं के संबंध में 1-6 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 5 परियोजनाएं बड़ी परियोजनाएं

हैं। इन 9 परियोजनाओं में से 3 परियोजना के संबंध में क्रमशः प्रत्येक में 1 माह के विलंब की सूचना प्राप्त हुई है तथा 3 परियोजनाओं के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। '765 केवी सिस्टम फॉर सेंट्रल पार्ट ऑफ नार्दर्न ग्रिड पार, पीजीसीआईएल' परियोजना ने आरओयू समस्या के कारण 3 महीने अतिरिक्त विलंब की सूचना दी है। डीवीसी, पीजीसीआईएल से संबद्ध पूरक पारेषण तथा कोलडैम एचईपी,एनटीपीसी' परियोजनाओं ने क्रमशः वन संबंधी स्वीकृति तथा मुख्य बांध में सीपेज समस्या के कारण प्रत्येक में अतिरिक्त 6 महीने विलंब की सूचना दी है।

(vi) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 146 परियोजनाओं में से 86 परियोजनाएं विलंबित हैं। माह के दौरान 10 परियोजनाओं के संबंध में 1-13 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 3 परियोजनाएं बड़ी परियोजनाएं हैं। इन 10 परियोजनाओं में से 8 परियोजनाओं के संबंध में प्रत्येक में एक माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। राजमार्ग चौराहा से लखनानन्दन (297 से 351 कि.मी.), एनएच 26, एनएचएआई तथा वाडनेर-देवधारी (एनएस-60/एमएच) (94-123 कि.मी.), एनएचएआई' ने क्रमशः 6 तथा 13 महीने अतिरिक्त विलंब की सूचना दी है। परियोजना कार्यान्वयनकर्ता एजेंसी ने इन परियोजनाओं के विलंब के लिए किसी विशेष कारण का उल्लेख नहीं किया है। तथापि, इन परियोजनाओं में विलंब के कारणों में भूमि अधिग्रहण, वन तथा पर्यावरण संबंधी अनुमति में विलंब, जनसुविधा स्थानांतरित करने की समस्या, ठेकेदार का खराब कार्य निष्पादन आदि शामिल हैं।

9. दिनांक 30.11.2012 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपये तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

10. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for November 2012 contains information on the status of the 566 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During November 2012, 1 project of Petroleum Sector has reported completion.

2. During the reference month, out of 566 projects, 249 projects are delayed with respect to latest schedule and 30 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 30 projects, 12 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 13 months in respect of projects relating to Fertilizers, Steel, Railways, Shipping & Ports, Petroleum, Power and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	127	30	1	0
2.	ROAD TRANSPORT & HIGHWAYS	146	86	10	2
3.	POWER	99	51	9	5
4.	PETROLEUM	72	34	6	3
5.	COAL	51	20	0	0
6.	TELECOMMUNICATION	13	7	0	0
7.	SHIPPING & PORTS	19	5	2	1
8.	STEEL	17	10	1	1
9.	FERTILISERS	5	1	1	0
10.	CIVIL AVIATION	6	0	0	0
11.	ATOMIC ENERGY	5	3	0	0
12.	URBAN DEVELOPMENT	4	1	0	0
13.	WATER RESOURCES	1	1	0	0
14.	PETROCHEMICALS	1	0	0	0
Total		566	249	30	12

3. The total original cost of implementation of the 566 projects was about ₹ 7,93,285.10 crore and their anticipated completion cost is likely to be ₹ 9,33,569.56 crore, which reflects an overall cost overrun of ₹ 1,40,284.46 crore (17.70 % of original cost). The expenditure incurred on these projects till November 2012 is ₹ 4,33,732.24 crore, which is 46.50 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 30-11-2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	499.16	1488.67
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1412.74	1162.50
5	RUPSA-BANGRIPOSI (GC)(SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. Out of the 566 projects, 4 projects are ahead of schedule, 195 are on schedule and 249 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 270 if delay is calculated on the basis of original schedule of completion. Further, 30 projects have been sanctioned without any commissioning schedule/date and for 88 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 249 delayed projects, 72 projects have overall delay in the range of 1 to 12 months, 52 projects have a delay in the range of 13 to 24 months, 94 projects have a delay in the range of 25 to 60 months and 31 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 30-11-2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
3	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
4	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	06/2005	06/2016	132
5	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

5. The brief reasons for time overruns as reported by various project implementing agencies are land acquisition, delay in forest clearance, delay in supply of material by M/S BHEL, slow progress by the contractor, ROU problem, no response to the NIT by the bidder, seepage problem, geological surprises, law & order problem, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 30.11.2012)

S N	PROJECT	SECTOR	DATE OF APPROV AL	COST OF PROJECT (₹ : crore)		EXPENDI TURE CUMMUL ATIVE (₹ : crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGIN AL	ANTICIPAT ED		ORIGINA L	ANTICIPA TED	
1	HOWRAH- AMTA- CHAMPADAN GA NL (SER)	Railways	04/1974	31.42	499.16	169.68	03/2007	03/2015	0
2	NANGALDAM TALWARA (NL), NR	Railways	03/1981	37.68	730.00	352.01	07/2012	N.A.	0
3	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUD	Railways	04/1983	36.80	703.17	242.39	N.A.	03/2015	0
4	FREIGHT OPERATIONS INFORMATIO N SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	0
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1086.41	427.98	06/2005	06/2016	0

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

7. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 30.11.2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	04/1985	158.77	432.46	558.07
2	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	205.16
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	538.10
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	590.02
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8521.82

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 30.11.2012)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.A.	N.A.
2	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	04/1985	03/1994	N.A.	12/2011
3	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.A.	03/2010	N.A.
4	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
5	PEDAPALLI-KARIMNAGAR-	Railways	12/1994	N.A.	N.A.	03/2012

	NIZAMABAD NL(SCR)					
--	-------------------	--	--	--	--	--

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

8. The Sector-wise details of delays/additional delays are as under:-

i) In the **Fertilizers Sector**, out of 05 projects, 01 project is delayed. During the month the project 'Nangal-Ammonia Plant Feedstock Project, NFL' has reported additional delay of 3 months. However, no specific reasons have been reported by the project authorities for delay in this project.

ii) In the **Steel Sector**, out of 17 projects, 10 projects are delayed. During the month a Mega project 'Coke Oven Battery No. 4 Phase-II, RINL' has reported additional delay of 3 months due to no response to the NIT by bidders.

iii) In the **Railways Sector**, out of 127 projects, 30 projects are delayed. During the month the project 'Lanjigarh-Junagarh NL, ECOR' has reported additional delay of 2 months due to slow progress of work.

iv) In the **Shipping & Ports Sector**, out of 19 projects, 5 projects are delayed. During the month 2 projects have reported additional delays of 1 month each, out of which 1 is a Mega project. The projects 'Acquisition of 4 No. of Anchor Handling cum Supply, Shipping' and 'Setting up of LNG Regasification Terminal at Puthu, Port Trust' have reported additional delay of 1 month each. However, no specific reasons have been reported by the project authorities for delay in these projects.

v) In the **Petroleum Sector**, out of 72 projects, 34 projects are delayed. During the month 6 projects have reported additional delays in the range of 1-3 months, out of which 3 are Mega projects. Of these 6 projects, 4 projects have reported additional delay of 1 month each. The project 'Compressor Stations (Kailaras and Chainsa), GAIL' has reported additional delay of 2 months due to slow progress by contractor. The project 'Kochi-

Kootanad Bangalore Mangalore Pipeline Project, GAIL' has reported additional delay of 3 months due to ROU problem.

vi) In the **Power Sector**, out of 99 projects, 51 projects are delayed. During the month 9 projects have reported additional delays in the range of 1-6 months, out of which 5 are Mega projects. Of these 9 projects, 3 projects have reported additional delay of 1 month each and 3 projects have reported additional delay of 2 months each. The project '765KV System for Central Part of Northern Grid Par, PGCIL' has reported additional delay of 3 months due to ROU problem. The projects 'Supplementary Transmission Associated with DVC, PGCIL' and 'Koldam HEP, NTPC' have reported additional delay of 6 months each due to delay in forest clearance and due to seepage problem in main dam respectively.

vii) In the **Road Transport & Highways Sector**, out of 146 projects, 86 are delayed. During the month 10 projects have reported additional delays in the range of 1-13 months, out of which 2 are Mega Projects. Of these 10 projects, 8 projects have reported additional delays of 1 month each. The projects 'Rajmarg Choraha to Lakhnandon, (Km 297 to Km 351), NH-26, NHAI' and 'Wadner-Devdhari (NS-60/MH) (Km 94-123 Km), NHAI' have reported additional delay of 6 and 13 months respectively. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

9. The status as on 30.11.2012 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

10. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	146	10
2	Railways	127	1
3	Power	99	14
4	Petroleum	72	6
5	Coal	51	0
6	Shipping & Ports	19	2
7	Steel	17	1
8	Telecommunications	13	0
9	Civil Aviation	6	0
10	Atomic Energy	5	0
11	Fertilisers	5	1
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	566	35

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	1438
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
	<u>Railways</u>			
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
	<u>Road Transport & Highways</u>			
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
	<u>Shipping & Ports</u>			
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
	June,2012			
	<u>Steel</u>			
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
	<u>Power</u>			
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	3779.46
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
	<u>Railways</u>			
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
	<u>Road Transport & Highways</u>			
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9
	July,2012			
	<u>Power</u>			
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
	<u>Railways</u>			
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096]	196.97	03/2011	218.66
	August,2012			
	<u>Steel</u>			
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
	<u>Power</u>			
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
	<u>Road Transport & Highways</u>			
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235]	193.09	03/2008	189.15
	September,2012			
	<u>Petroleum</u>			
34	REVAMPING OF WIN PLATFORM AT MH ASSET(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000044]	333.40	05/2010	680.85
	<u>Telecommunications</u>			
35	PROJ.III OF NIB-II OF MESSAGING STORAGE(BHARAT SANCHAR NIGAM LIMITED) - [260100099]	250.00	12/2005	80.47
36	NIB Project Capacity Expansion(BHARAT SANCHAR NIGAM LIMITED) - [N26000098]	175.52	12/2008	60.84

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
October,2012				
<u>Road Transport & Highways</u>				
37	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106204]	275.00	09/2007	306.65
38	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106301]	151.30	10/2008	190.61
November,2012				
<u>Petroleum</u>				
39	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC(GAS AUTHORITY OF INDIA LIMITED) - [N16000071]	348.00	03/2012	203.31


Summary of projects in the Flash Report for the month of November, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	565
Number of Projects completed/dropped/frozen in Previous Month	2
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects are Duplicate in Current Month	1
Number of Projects Added in Current Month	5
Number of Projects in Current Month	566


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 566 projects, 4 projects are ahead of schedule, 174 projects are on schedule and 270 projects are delayed. Of the balance, 88 projects do not have fixed dates of commissioning while 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

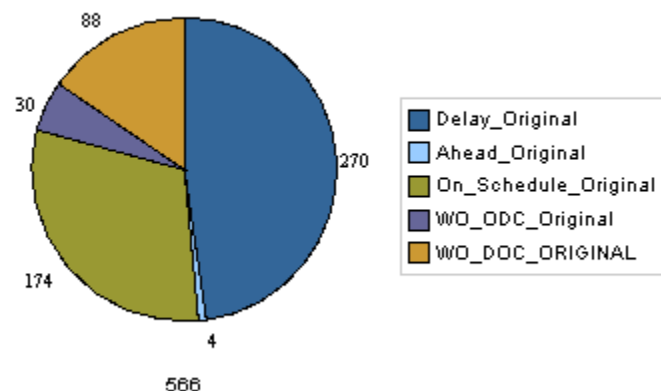

III. Investment Scenario

The Total Original cost of implementation of 566 projects when sanctioned, was of the order of Rs. 793285.1 crore but this was subsequently revised to Rs. 933569.56 crore implying a cost overrun of 17.7%. The expenditure incurred on these projects till November, 2012 is Rs. 433732.24 crore, which is 46.5% of the revised cost of the projects.

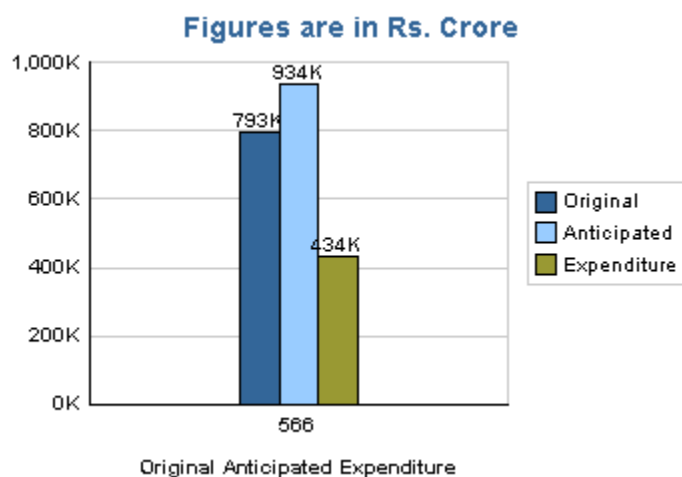

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	565
No of Projects Completed/Dropped/Frozen in Previous Month	2
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects Duplicate in Current Month	1
No of Projects added in Current Month	5
No of Projects in Current Month	566

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	270	4	174	30	88	566	47.70
Latest Approved (Date)	249	4	195	30	88	566	43.99

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	414	648,087.29	683,004.12	286,115.53	41.90	34,916.83	5.40
Latest Approved (RCE)	152	204,002.01	250,565.44	147,616.71	58.90	46,563.43	22.80
Total (RCE)	566	852,089.30	933,569.56	433,732.24	46.46	81480.26	9.56
Original Cost of All Projects							
Original Cost	566	793,285.10	933,569.56	433,732.24	46.50	140,284.46	17.70

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	270	443,860.97	539,008.11	319,329.83	59.20	95,147.14	21.40
Latest Approved (RCE)	249	438,792.98	494,891.46	293,789.62	59.40	56,098.48	12.80

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	35	63,859.13	70,305.86	55,297.36	78.70	6,446.73	10.10

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	5,549.7	1.4	1	1,808.0	2,015.0	11.4
3	Coal	51	36,056.5	37,510.5	4.0	7	8,579.5	10,631.3	23.9
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	72	176,404.1	187,683.1	6.4	16	54,264.0	73,426.2	35.3
8	Power	99	232,888.3	248,718.5	6.8	19	46,019.4	61,849.6	34.4
9	Railways	127	64,518.7	150,659.2	133.5	109	45,490.4	131,677.5	189.5
10	Road Transport & Highways	146	94,054.5	95,488.7	1.5	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	11	9,532.5	12,151.1	27.5
12	Telecommunications	13	5,735.5	5,676.3	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	793,285.1	933,569.6	17.7	188	223,288.4	373,337.7	67.2

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	37	31,485.3	39,109.1	24.2	14	12,420.0	20,910.9	68.4
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	35	22,260.9	33,844.4	52.0	12	10,491.8	22,169.3	111.3
4	Bihar	30	26,901.2	34,657.0	28.8	13	12,343.6	20,099.4	62.8
5	Goa	1	335.6	204.7	-39.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	10	5,496.6	7,439.1	35.3	3	1,448.2	3,390.7	134.1
8	Himachal Pr.	5	13,355.6	17,246.7	29.1	4	11,308.5	15,199.7	34.4
9	J and K	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	25	45,300.8	54,787.3	20.9	9	8,598.8	18,491.8	115.1
11	Kerala	6	19,694.7	21,136.2	7.3	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	24	19,741.9	19,892.0	0.8	3	2,027.6	2,741.5	35.2
13	Maharashtra	54	97,399.5	113,680.2	16.7	18	32,285.0	51,040.2	58.1
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	31	57,664.0	62,099.1	7.7	12	32,671.6	37,106.7	13.6
19	Punjab	7	4,836.2	5,778.0	19.5	2	532.4	1,474.2	176.9
20	Rajasthan	14	26,544.1	26,138.3	-1.5	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	23	18,822.9	22,659.7	20.4	8	3,498.5	7,383.5	111.0
25	West Bengal	27	42,286.1	54,501.8	28.9	16	23,674.5	35,890.2	51.6
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	25	47,047.8	48,330.9	2.7	6	1,548.3	2,831.4	82.9
28	Jharkhandd	23	14,447.4	18,429.0	27.6	6	1,897.3	6,050.7	218.9
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	35.6
30	Multi State	104	142,189.7	151,656.2	6.7	22	10,740.0	24,254.3	125.8
Total		566	793,285.1	933,569.6	17.7	188	223,288.4	373,337.7	67.2

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	5,549.7	1.4	1	309.5	309.5	27 - 27
3	Coal	51	36,056.5	37,510.5	4.0	20	17,557.6	19,431.2	16 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	1	1,478.6	1,478.6	2 - 2
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	3 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	72	176,404.1	187,683.1	6.4	40	110,647.2	122,957.6	1 - 120
8	Power	99	232,888.3	248,718.5	6.8	51	135,624.0	150,841.1	2 - 99
9	Railways	127	64,518.7	150,659.2	133.5	39	25,689.1	68,484.7	1 - 216
10	Road Transport & Highways	146	94,054.5	95,488.7	1.5	87	41,616.6	43,410.8	2 - 106
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	8	7,878.3	9,456.7	5 - 87
12	Telecommunications	13	5,735.5	5,676.3	-1.0	7	2,737.7	2,741.6	25 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	793,285.1	933,569.6	17.7	270	443,861.0	539,008.1	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	37	31,485.3	39,109.1	24.2	14	17,688.1	21,497.5	2 - 41
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	25 - 78
3	Assam	35	22,260.9	33,844.4	52.0	33	21,484.3	32,882.6	12 - 120
4	Bihar	30	26,901.2	34,657.0	28.8	14	20,578.4	26,451.2	2 - 75
5	Goa	1	335.6	204.7	-39.0	0	0.0	0.0	-
6	Gujarat	22	31,111.6	31,313.5	0.6	6	15,224.5	15,394.7	6 - 24
7	Haryana	10	5,496.6	7,439.1	35.3	4	2,065.9	3,555.0	9 - 50
8	Himachal Pr.	5	13,355.6	17,246.7	29.1	5	13,355.6	17,246.7	20 - 99
9	J and K	10	14,927.0	34,825.6	133.3	9	13,826.3	33,724.9	10 - 201
10	Karnataka	25	45,300.8	54,787.3	20.9	9	22,364.3	27,349.0	10 - 100
11	Kerala	6	19,694.7	21,136.2	7.3	3	4,674.0	5,324.0	12 - 58
12	Madhya pradesh	24	19,741.9	19,892.0	0.8	13	10,571.4	10,440.9	5 - 60
13	Maharashtra	54	97,399.5	113,680.2	16.7	23	47,036.3	57,898.9	5 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 11
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	31	57,664.0	62,099.1	7.7	11	33,068.2	34,030.5	9 - 132
19	Punjab	7	4,836.2	5,778.0	19.5	5	3,090.0	4,031.8	1 - 58
20	Rajasthan	14	26,544.1	26,138.3	-1.5	6	19,992.2	19,687.9	3 - 52
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	11	30,528.8	36,459.4	9 - 87
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	7 - 7
24	Uttar Pradesh	23	18,822.9	22,659.7	20.4	11	11,635.1	13,615.4	5 - 93
25	West Bengal	27	42,286.1	54,501.8	28.9	14	25,184.4	31,659.7	3 - 135
26	Delhi	3	37,985.0	37,965.4	-0.1	1	249.0	229.4	72 - 72
27	Chhatisgarh	25	47,047.8	48,330.9	2.7	6	18,545.8	18,857.0	6 - 47
28	Jharkhandd	23	14,447.4	18,429.0	27.6	10	8,748.4	9,833.4	11 - 102
29	Uttaranchal	3	5,619.2	6,559.6	16.7	3	5,619.2	6,559.6	22 - 45
30	Multi State	104	142,189.7	151,656.2	6.7	51	86,116.6	90,192.2	1 - 216
Total		566	793,285.1	933,569.6	17.7	270	443,861.0	539,008.1	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	5,549.7	1.4	0	0.0	0.0	-
3	Coal	51	36,056.5	37,510.5	4.0	20	17,557.6	19,431.2	16 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	1	1,478.6	1,478.6	2 - 2
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	3 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	72	176,404.1	187,683.1	6.4	34	99,397.6	106,184.9	1 - 86
8	Power	99	232,888.3	248,718.5	6.8	51	135,624.0	150,841.1	2 - 99
9	Railways	127	64,518.7	150,659.2	133.5	30	15,573.2	52,237.3	2 - 216
10	Road Transport & Highways	146	94,054.5	95,488.7	1.5	86	41,336.6	43,130.8	2 - 106
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	5	6,756.1	7,869.6	12 - 34
12	Telecommunications	13	5,735.5	5,676.3	-1.0	7	2,737.7	2,741.6	25 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	793,285.1	933,569.6	17.7	249	415,323.2	494,891.5	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	5,549.7	-2.3	0	0.0	0.0	0.0
3	Coal	51	37,022.5	37,510.5	1.3	6	7,115.6	7,603.7	6.9
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	72	192,532.2	187,683.1	-2.5	2	30,533.0	31,324.0	2.6
8	Power	99	236,695.4	248,718.5	5.1	13	39,029.6	51,052.7	30.8
9	Railways	127	94,382.6	150,659.2	59.6	83	51,086.9	107,574.2	110.6
10	Road Transport & Highways	146	94,221.0	95,488.7	1.3	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	18,109.6	18,554.1	2.5	8	4,615.6	5,370.0	16.3
12	Telecommunications	13	5,739.4	5,676.3	-1.1	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	852,089.3	933,569.6	9.6	131	168,595.8	257,314.1	52.6

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	5,549.70	1.39	1	1,808.00	2,015.00	13- 13
3	Coal	51	36,056.46	37,510.52	4.03	0	0.00	0.00	0- 0
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	13- 13
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	72	176,404.09	187,683.11	6.39	11	20,638.48	35,088.71	24- 120
8	Power	99	232,888.28	248,718.52	6.80	2	2,253.45	3,986.02	0- 76
9	Railways	127	64,518.68	150,659.22	133.51	16	8,942.50	25,058.02	1- 141
10	Road Transport & Highways	146	94,054.50	95,488.69	1.52	0	0.00	0.00	0- 0
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	6	6,013.42	7,487.89	5- 87
12	Telecommunications	13	5,735.48	5,676.27	-1.03	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		566	793285.1	933569.56	17.68	38	45412.35	83162.81	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	5,549.70	1.39	0	0.00	0.00	0- 0
3	Coal	51	36,056.46	37,510.52	4.03	4	7,617.44	9,621.06	16- 45
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	5- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	72	176,404.09	187,683.11	6.39	13	52,458.98	70,307.15	10- 120
8	Power	99	232,888.28	248,718.52	6.80	17	45,001.89	60,218.99	7- 99
9	Railways	127	64,518.68	150,659.22	133.51	31	15,602.29	58,402.71	1- 216
10	Road Transport & Highways	146	94,054.50	95,488.69	1.52	11	3,324.28	5,445.20	21- 104
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	6	7,074.72	8,653.14	5- 87
12	Telecommunications	13	5,735.48	5,676.27	-1.03	2	1,065.85	1,089.32	25- 45
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	21- 21
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		566	793285.1	933569.56	17.68	94	181743.85	282940	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		Final
S.no	Project	DOA	Cost	DOC	Cost	DOC	Expenditure
<u>Petroleum</u>							
1	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC	06/2009	348.00	03/2012	261.00	11/2012	203.31

VI. List of projects added

(All Cost in Rs. crore)

			Original		Anticipated	
S.no	Project	DOA	Cost	DOC	Cost	DOC
	<u>Petroleum</u>					
1	REWARI KANPUR PIPELINE PROJECT	3/2012	1,210.64	3/2015	1,210.64	3/2015
2	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	11/2012	666.00	11/2015	666.00	11/2015
3	DBPL-II	6/2009	486.00	9/2013	486.00	9/2013
4	PARADIP HALDIA DURGAPUR LPG PIPELINE	2/2011	913.00	7/2015	913.00	7/2015
5	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	8/2011	586.00	7/2015	586.00	7/2015

VII. Milestones (Cumulative due & achieved)

Total	3419
Achieved up to month	1244


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Fertilisers</u>						
1	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT NFL	1,478.63	1,478.63	01/2013	12/2012	03/2013	3
	<u>Steel</u>						
2	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	10/2012	12/2012	03/2013	3
	<u>Petroleum</u>						
3	CONSTRUCTION OF NEW PROCESS COMPLEX MHN ONGC	2,853.29	6,326.40	05/2010	11/2012	12/2012	1
4	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-GAIL	238.68	312.00	01/2012	12/2012	01/2013	1
5	EURO-IV DHDT CPCL	2,615.69	2,615.69	N.A.	11/2012	12/2012	1
6	CDU/VDU-II CPCL	333.99	333.99	N.A.	09/2012	10/2012	1
7	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) GAIL	1,167.00	798.00	04/2011	10/2012	12/2012	2
8	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC GAIL	2,915.00	2,915.00	12/2012	12/2013	03/2014	3
	<u>Power</u>						
9	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.26	913.00	02/2011	11/2012	12/2012	1
10	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	386.32	07/2011	11/2012	12/2012	1
11	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G PGCIL	1,736.36	1,736.36	06/2012	11/2012	12/2012	1
12	NIMOO BAZGO HYDROELECTRIC PROJECT NHPC	611.01	936.00	08/2010	01/2013	03/2013	2
13	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA PGCIL	1,347.32	1,347.32	02/2012	11/2012	01/2013	2
14	RIHAND STTP STAGE-III (2X500MW) (NTPC) NTPC	6,230.81	6,230.81	10/2012	03/2013	05/2013	2
15	System Strengthening -X of SR PGCIL	276.61	276.61	04/2012	10/2012	12/2012	2
16	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR PGCIL	1,075.12	1,075.12	05/2012	12/2012	03/2013	3
17	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND PGCIL	2,360.95	2,360.95	08/2012	03/2013	09/2013	6
18	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	07/2011	04/2014	11/2014	7
19	BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	01/2014	09/2014	8
20	BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	12/2014	03/2016	15
21	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	03/2013	06/2014	09/2015	15


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
22	KOLDAM HEP (NTPC) NTPC	4,527.15	6,358.91	04/2009	03/2013	09/2014	18
	<u>Railways</u>						
23	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	01/2013	03/2013	2
	<u>Road Transport & Highways</u>						
24	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	11/2012	12/2012	1
25	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	11/2012	12/2012	1
26	ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	11/2012	12/2012	1
27	THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	11/2012	12/2012	1
28	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	11/2012	12/2012	1
29	Hyderabad-Vijaywada Km. 40 to 221.50 Km NHAI	1,740.00	1,740.00	10/2012	11/2012	12/2012	1
30	Hyderabad-yadgiri N.H no-202 NHAI	388.00	388.00	05/2012	11/2012	12/2012	1
31	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	11/2012	12/2012	1
32	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) NHAI	251.03	251.03	10/2008	12/2012	06/2013	6
33	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) NHAI	193.45	193.45	11/2012	11/2012	12/2013	13
	<u>Shipping & Ports</u>						
34	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY SHIPP.	359.44	359.44	04/2011	10/2012	11/2012	1
35	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	12/2012	01/2013	1

Trend and Graphical Analysis of All Projects

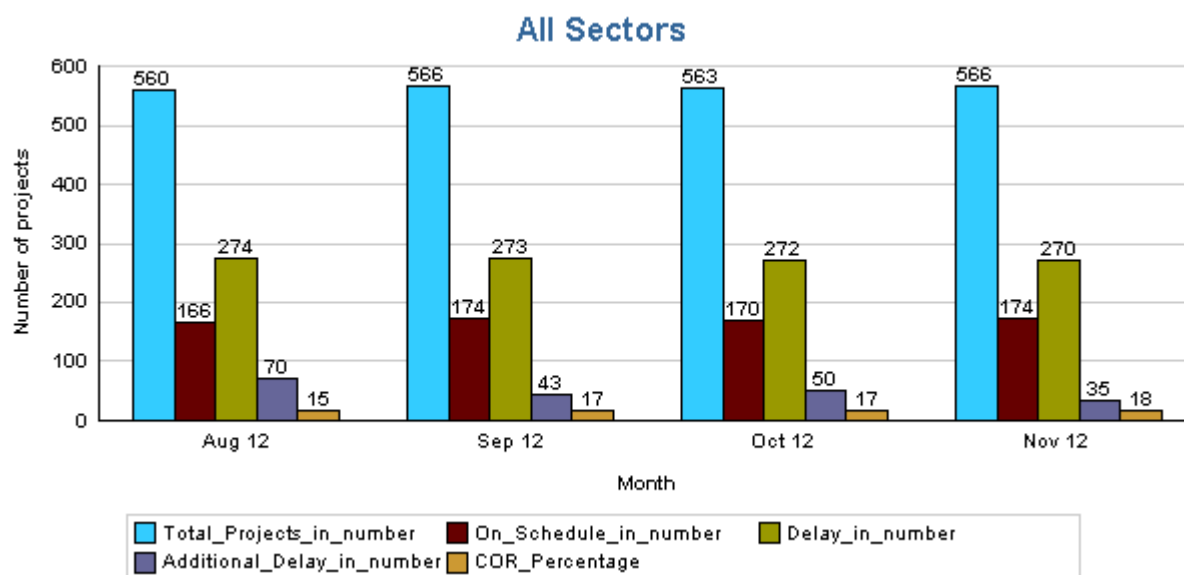


All Sectors Break-up of 270 Delayed projects in November 2012

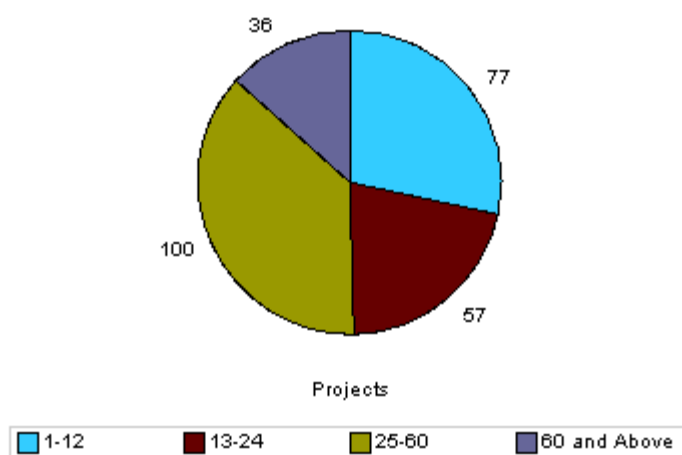


Trend and Graphical Analysis

Urban Development Sector

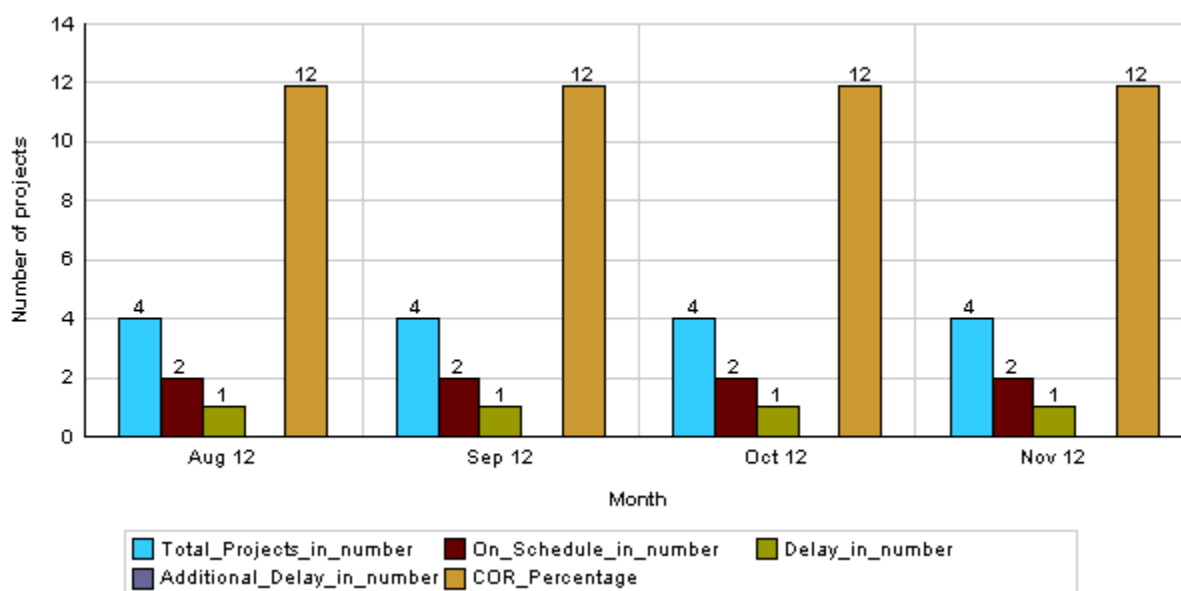


Urban Development Sector Break-up of 1 Delayed projects in November 2012

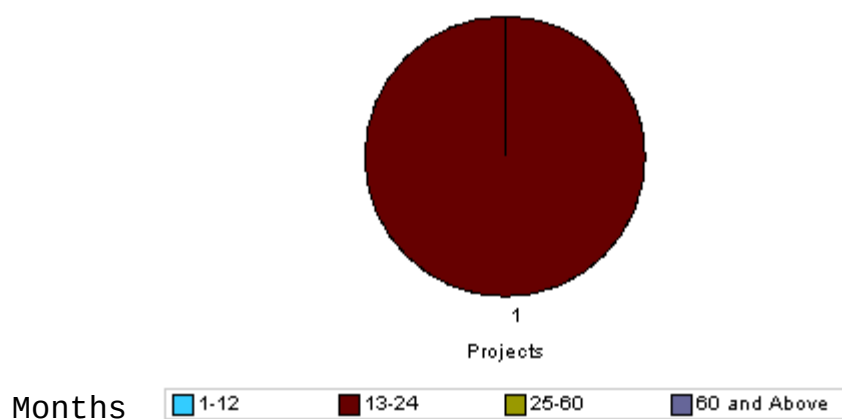


Trend and Graphical Analysis


Telecommunications Sector

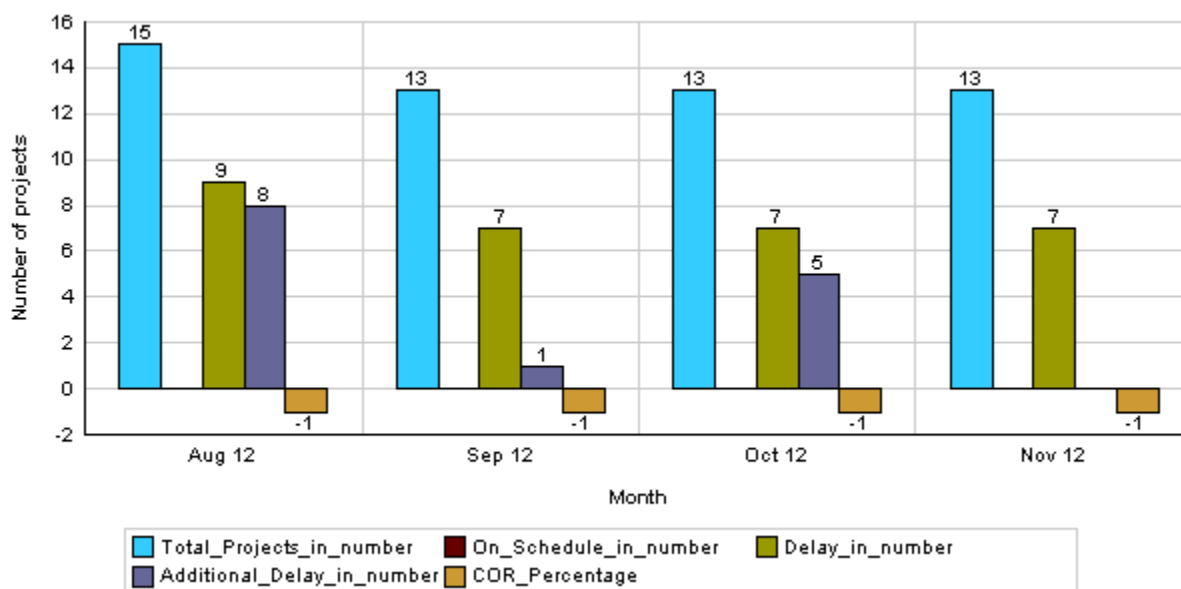


Telecommunications Sector Break-up of 7 Delayed projects in November 2012

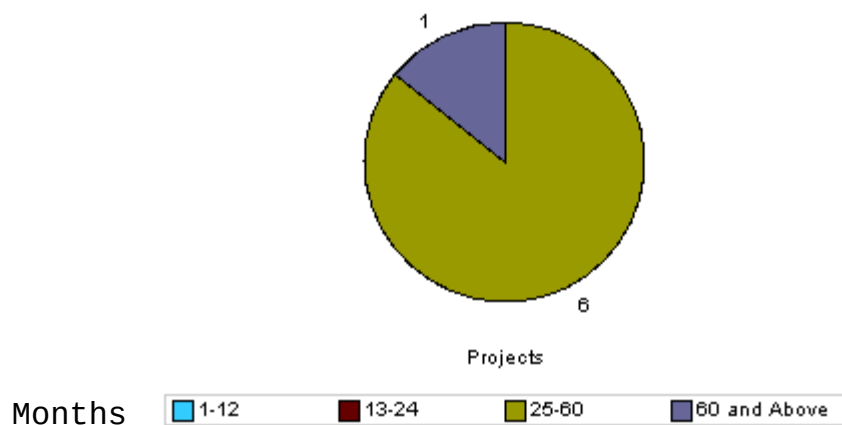


Trend and Graphical Analysis Shipping and Ports Sector

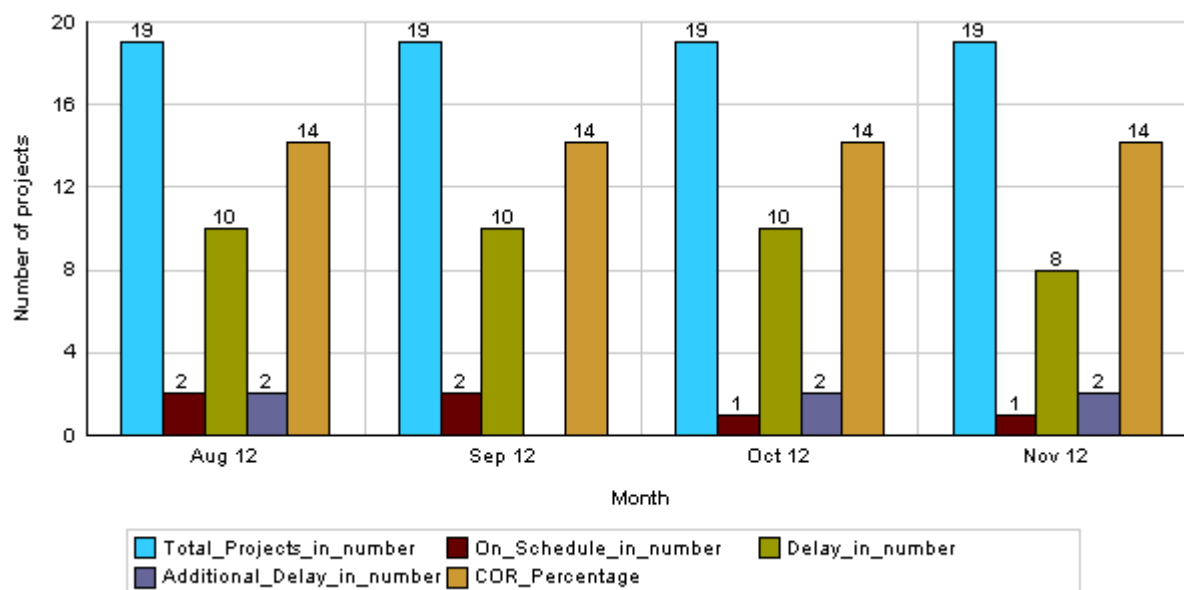


Sector Break-up of 8 Delayed projects in November 2012

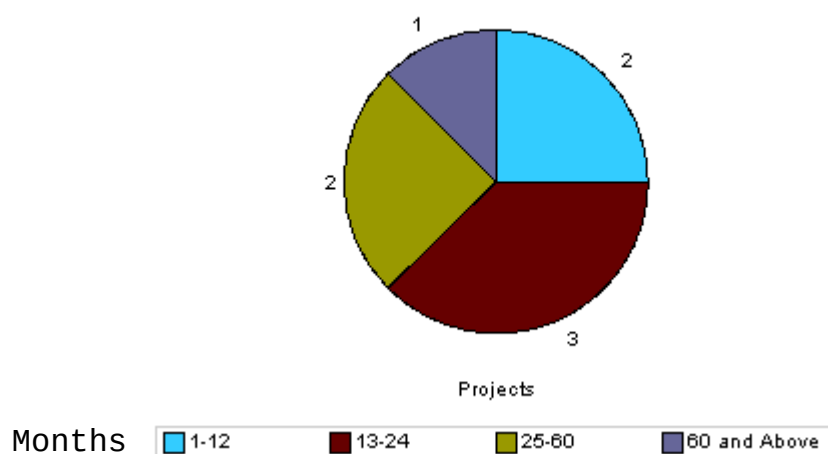

Trend and Graphical Analysis Road Transport and Highways Sector

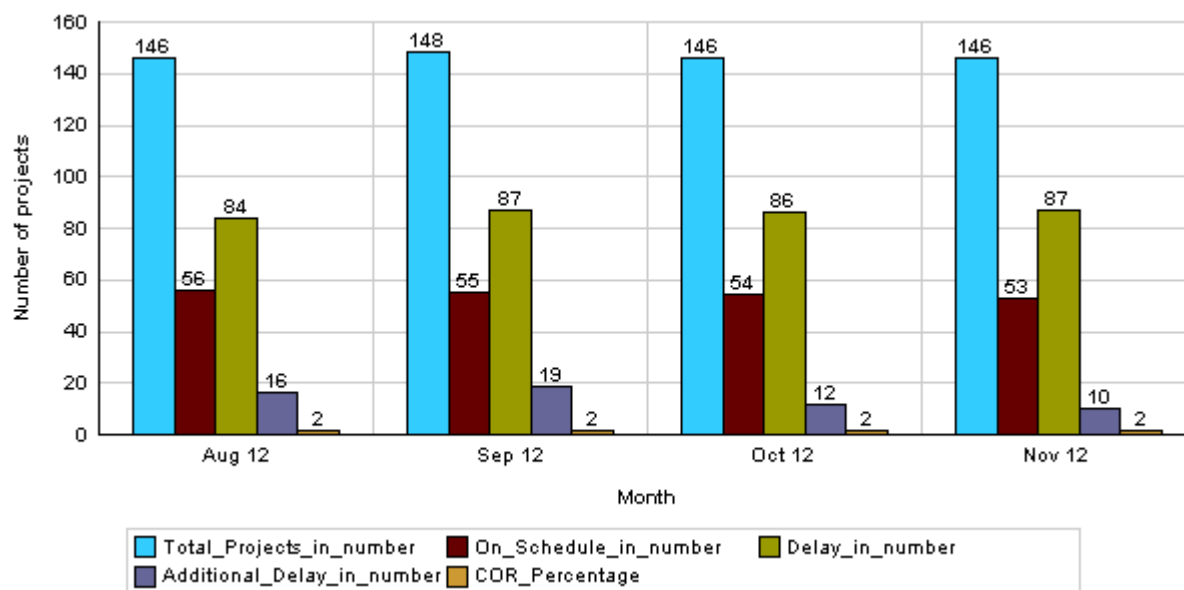


Sector Break-up of 87 Delayed projects in November 2012

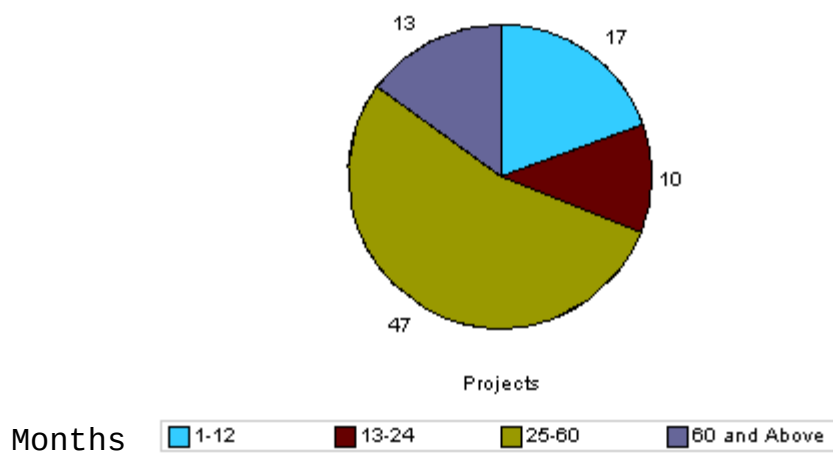


Trend and Graphical Analysis

Railways Sector

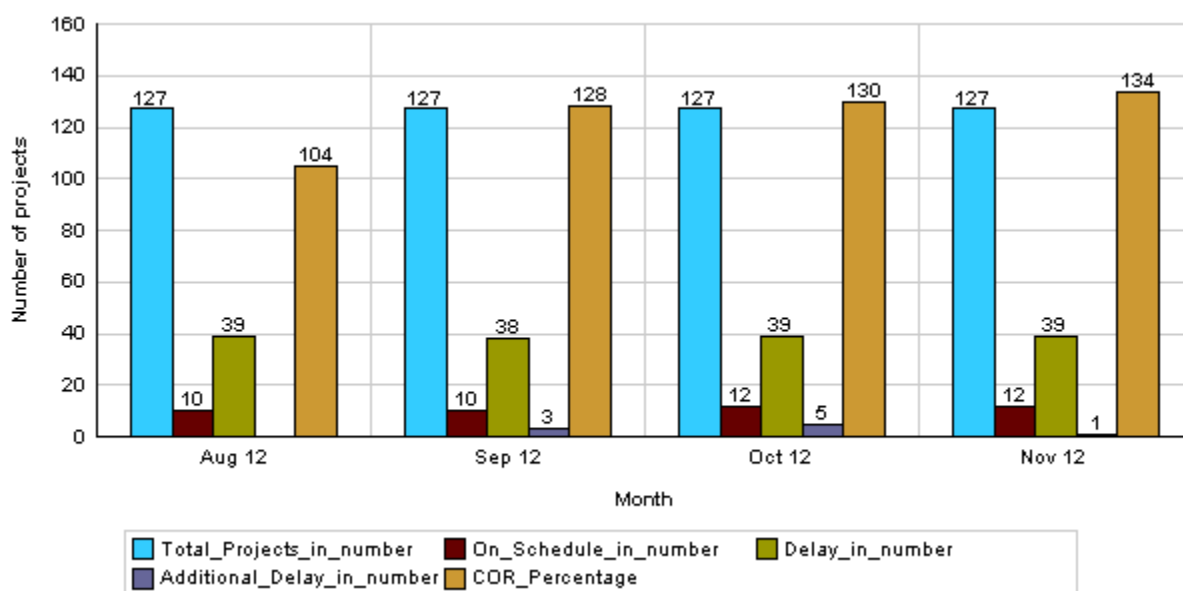


Railways Sector Sector Break-up of 39 Delayed projects in November 2012

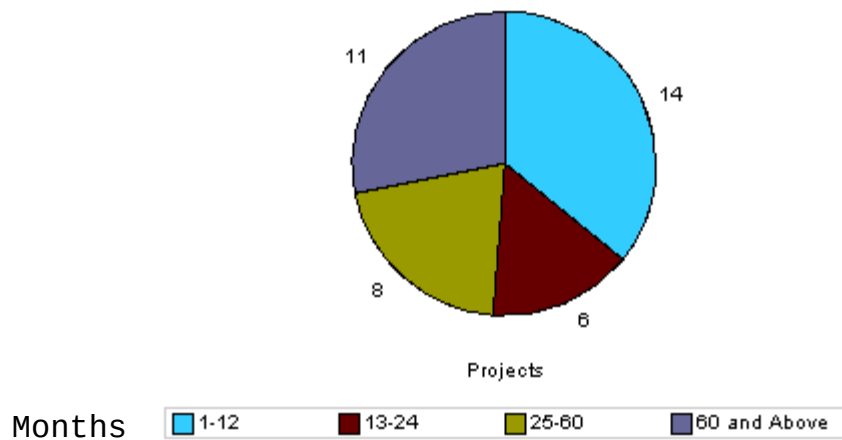


Trend and Graphical Analysis

Power Sector

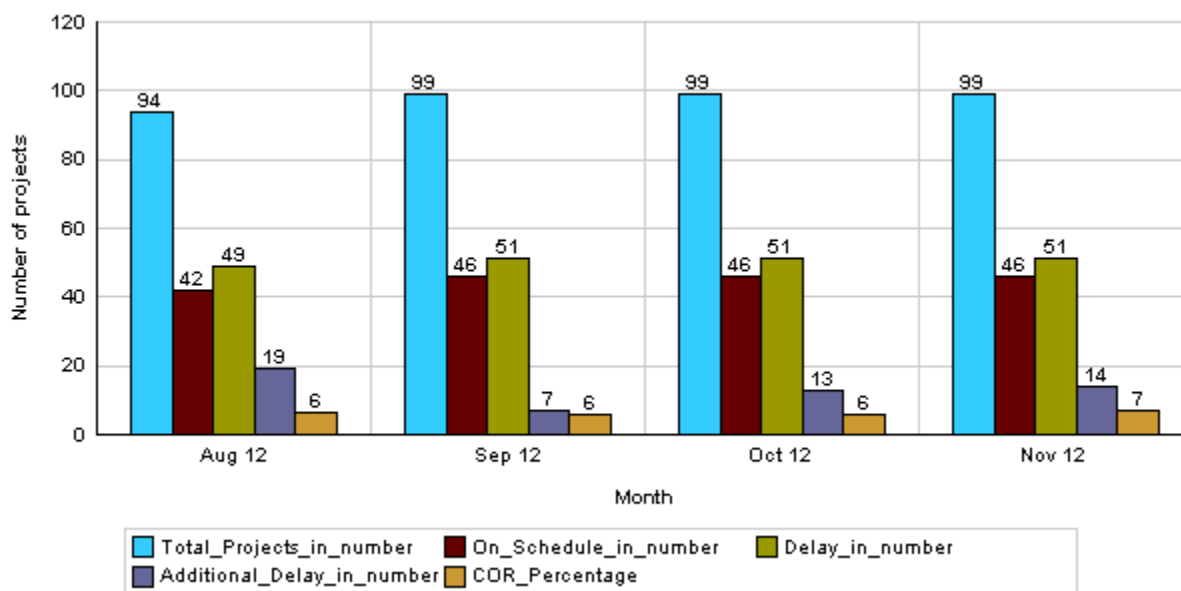


Power Sector Sector Break-up of 51 Delayed projects in November 2012

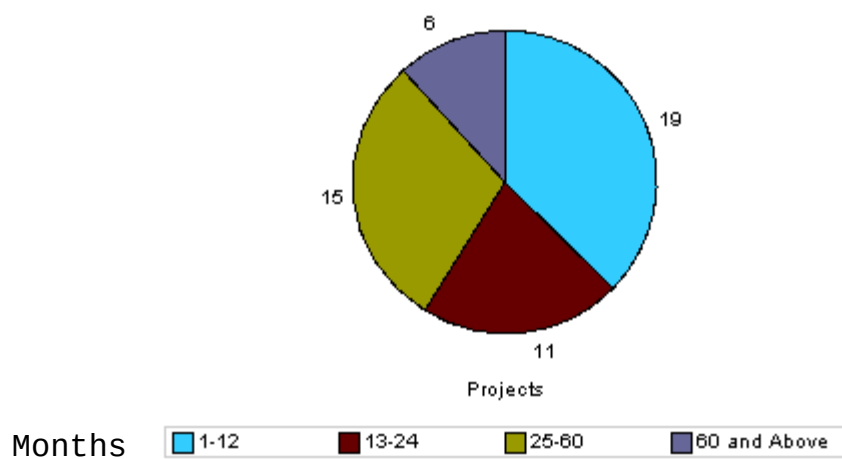


Trend and Graphical Analysis

Petroleum Sector

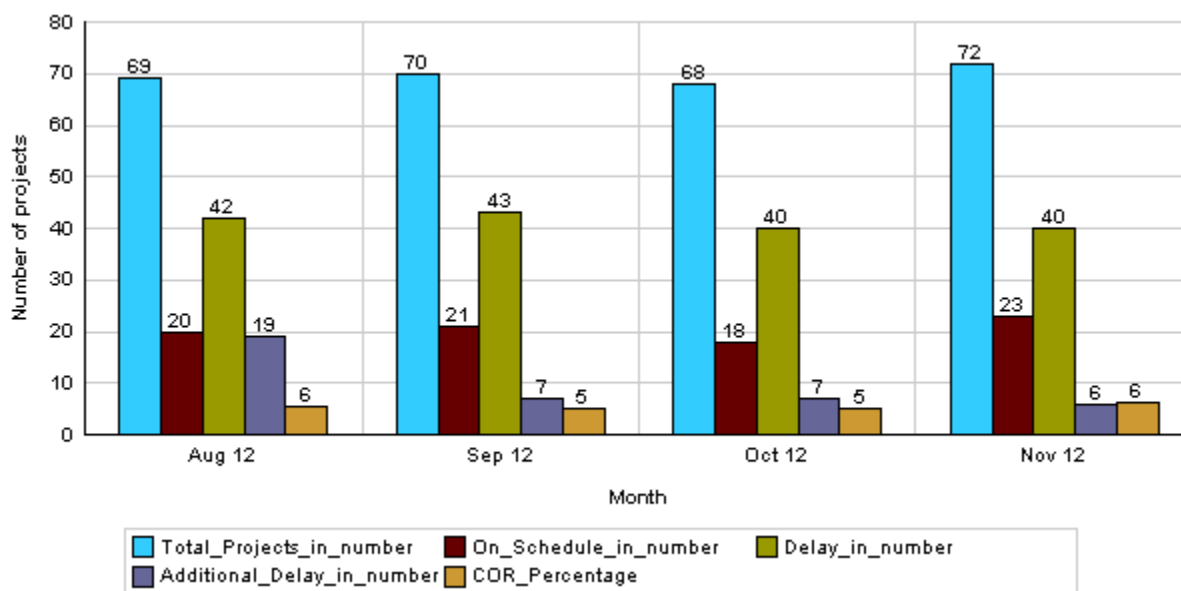


Petroleum Sector Sector Break-up of 40 Delayed projects in November 2012

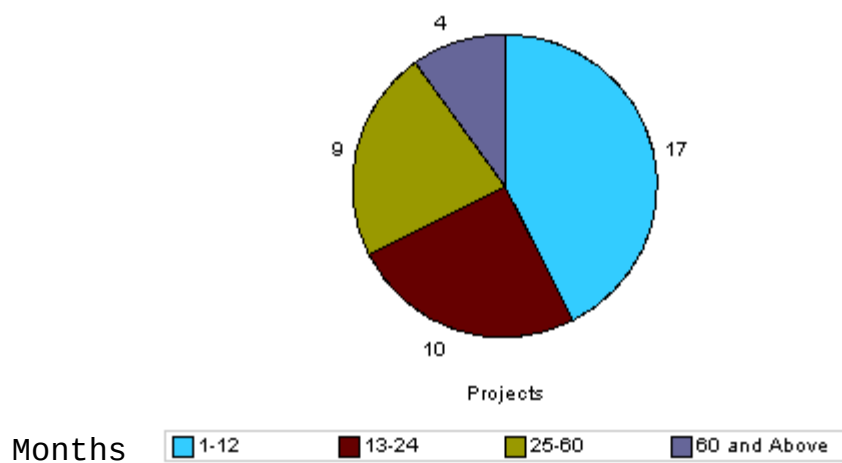


Trend and Graphical Analysis

Steel Sector

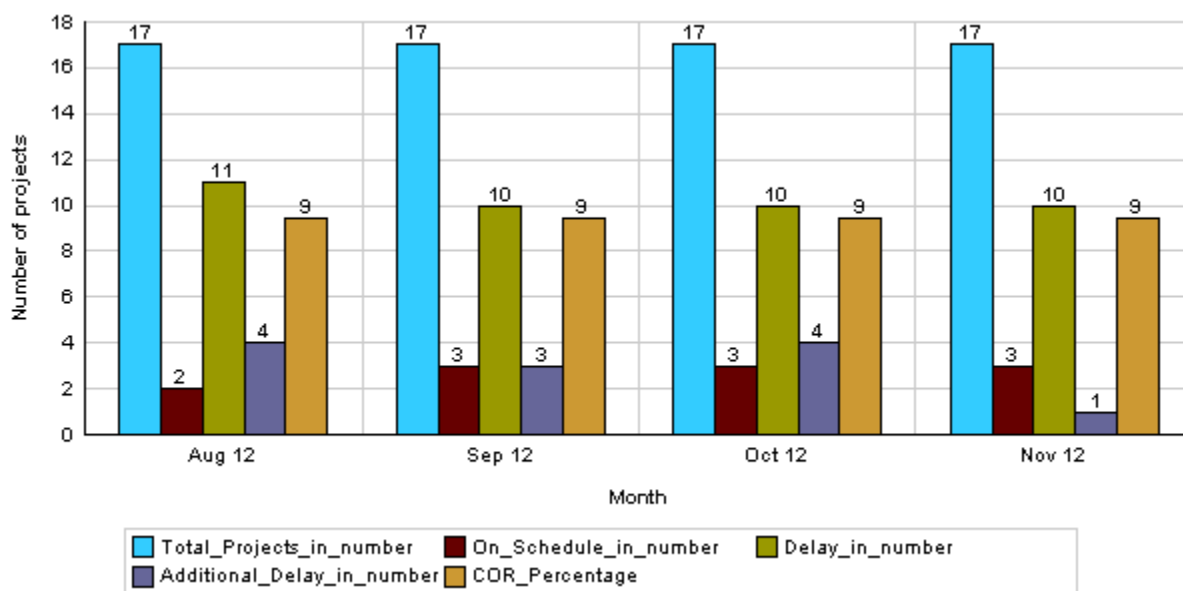


Steel Sector Sector Break-up of 10 Delayed projects in November 2012

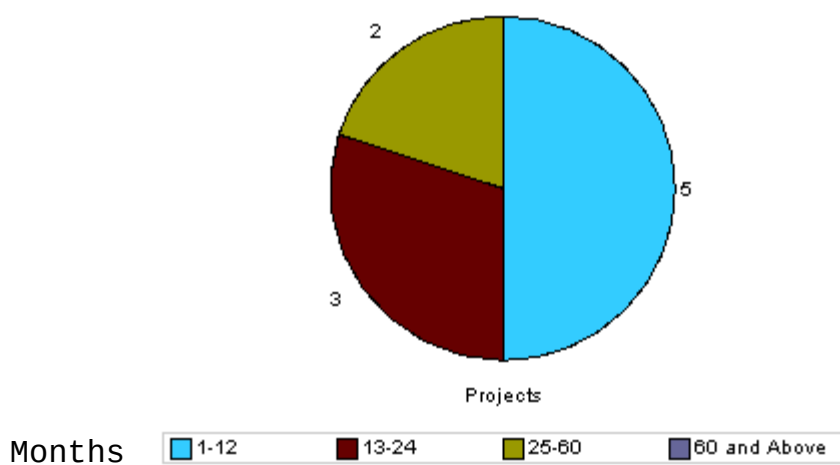


Trend and Graphical Analysis

Fertilisers Sector

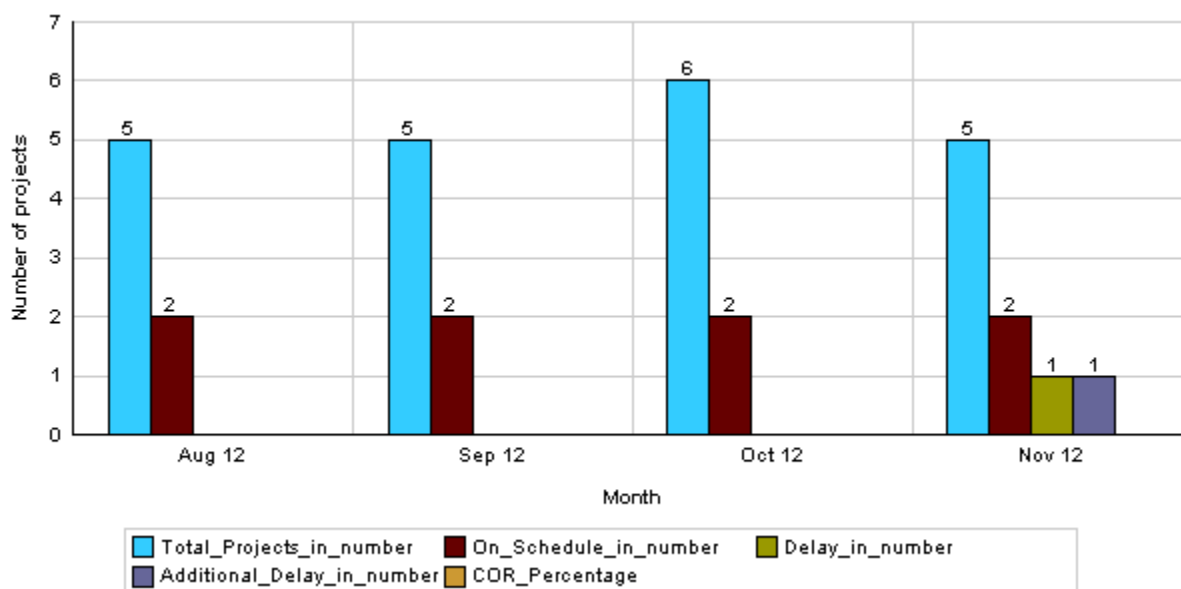


Fertilisers Sector Sector Break-up of 1 Delayed projects in November 2012

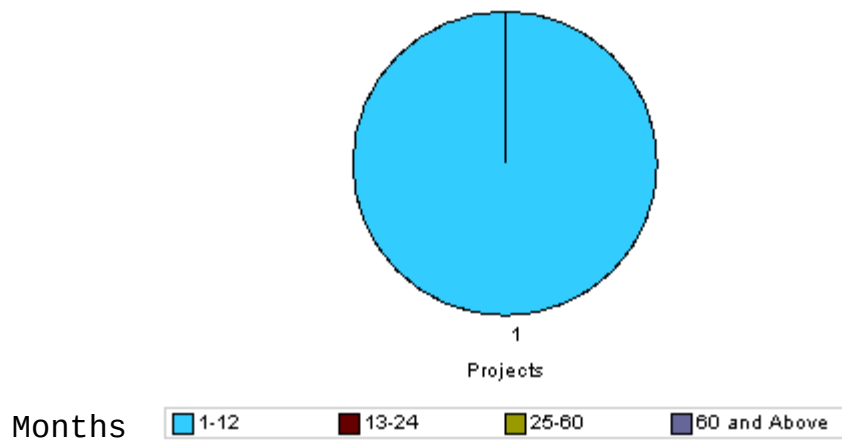


Trend and Graphical Analysis

Coal Sector

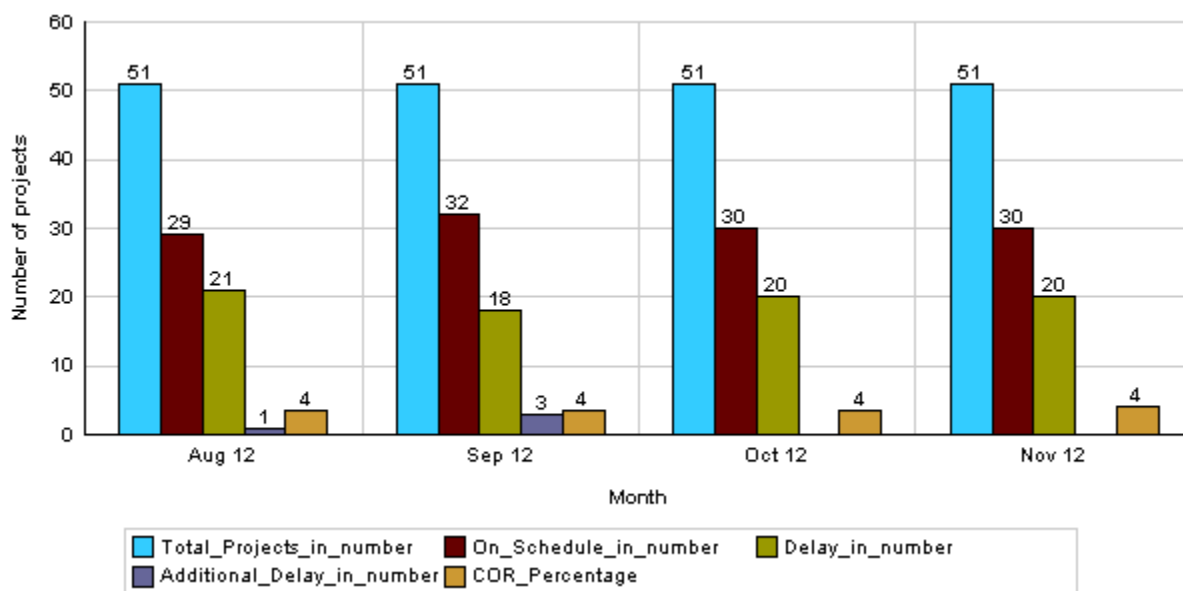


Coal Sector Sector Break-up of 20 Delayed projects in November 2012

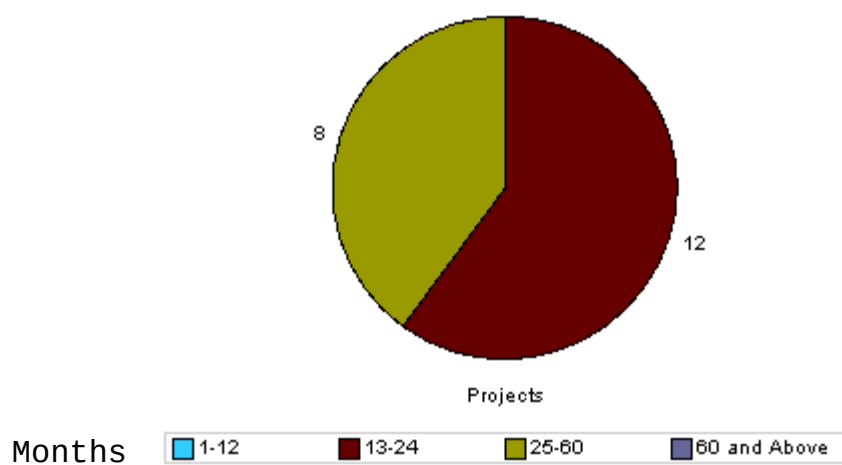


Trend and Graphical Analysis

Civil Aviation Sector

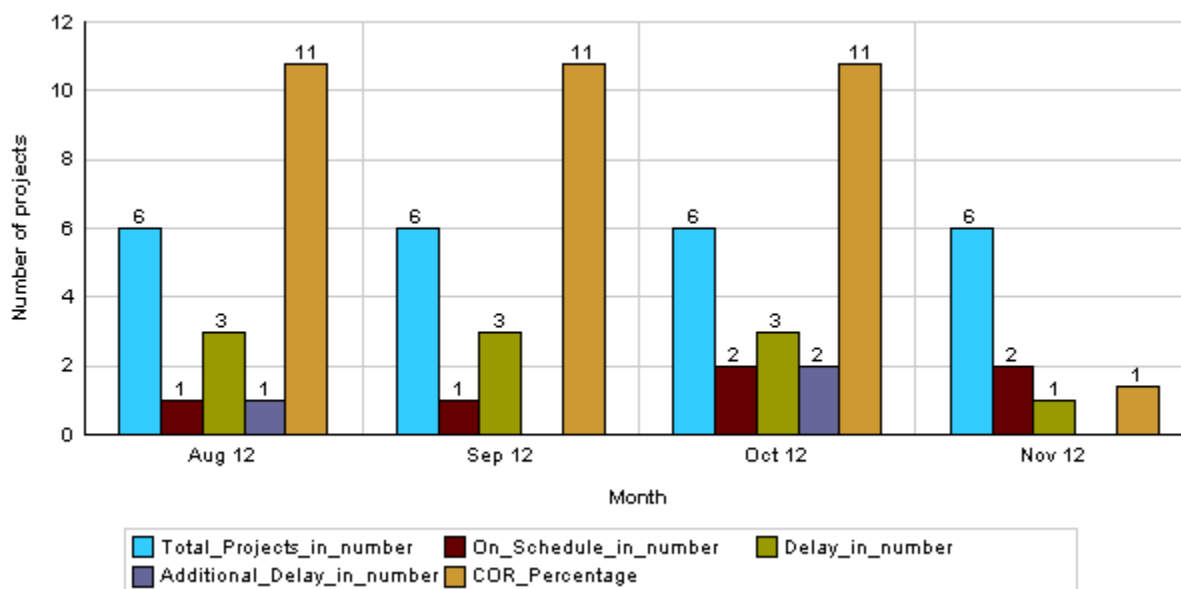


Civil Aviation Sector Break-up of 1 Delayed projects in November 2012

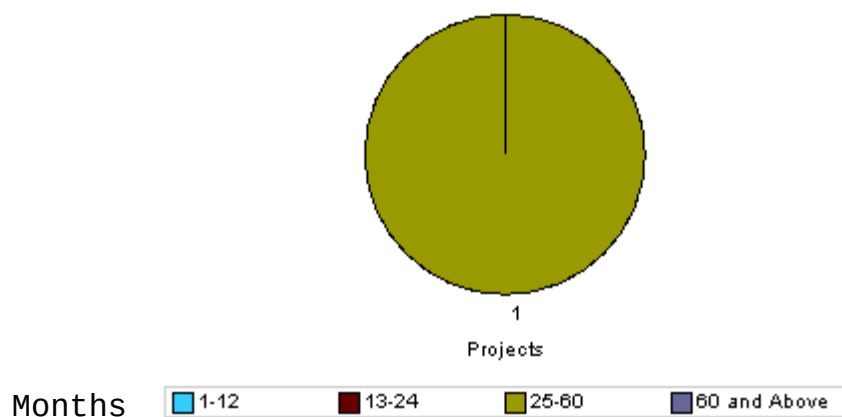


Trend and Graphical Analysis

Atomic Energy Sector

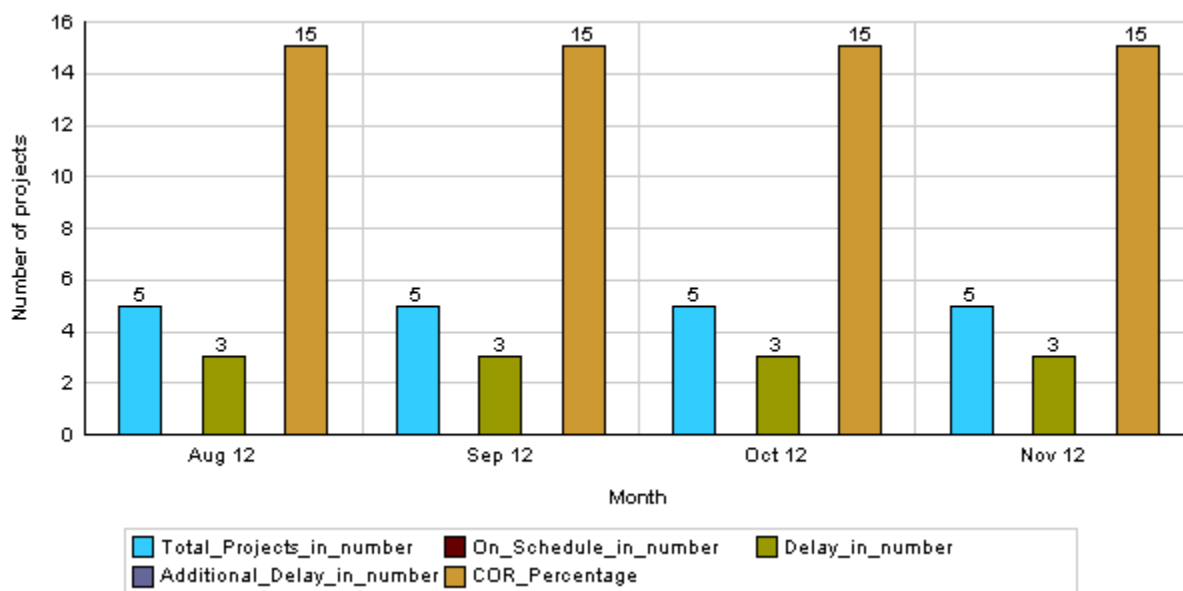

Atomic Energy Sector Sector Break-up of 3 Delayed projects in November 2012

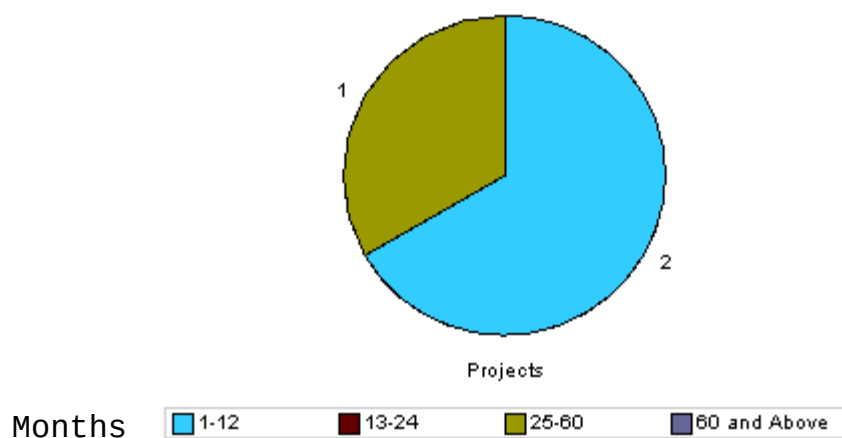

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	23,455.84
Civil Aviation	6	5,473.58	5,680.58	5,549.70	2,319.52
Coal	51	36,056.46	37,022.46	37,510.52	13,273.49
Fertilisers	5	4,828.66	4,828.66	4,828.66	3,234.03
Steel	17	65,285.87	67,562.15	71,443.41	44,907.61
Petrochemicals	1	5,460.61	8,920.00	8,920.00	5,775.44
Petroleum	72	176,404.09	192,532.22	187,683.11	84,103.88
Power	99	232,888.28	236,695.38	248,718.52	109,362.53
Railways	127	64,518.68	94,382.58	150,659.22	64,648.56
Road Transport & Highways	146	94,054.50	94,221.00	95,488.69	69,013.72
Shipping & Ports	19	16,242.52	18,109.64	18,554.09	8,500.80
Telecommunications	13	5,735.48	5,739.36	5,676.27	1,660.99
Urban Development	4	44,245.18	44,304.08	49,518.08	3,440.34
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	566	793,285.10	852,089.30	933,569.56	433,732.24

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Atomic Energy									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	2,169.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,161.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,577.60	09/2010	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,464.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011	-	-	0/0
Total			41,548.29	47,832.29	23,455.84				47/327
Civil Aviation									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	1,942.51	-	05/2011	-	-	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	188.47	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	204.73	-	05/2012	-	-	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,724.62	01/2011 02/2012	02/2012	-	0/0
10	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	452.00	33.36	03/2015	03/2015	0(O)	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	373.07	06/2013	06/2013	0(O)	0/0
Total			5,473.58	5,549.70	2,319.52				0/0
Coal									
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	430.95	03/2013 09/2012	07/2014	16(O) 22(R)	7/22
13	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59	198.59	92.53	03/2016	03/2016	0(O)	2/6
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	374.26	03/2016 03/2016	03/2016	0(O) 0(R)	2/2
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	100.19	03/2012	03/2014	24(O)	5/7

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	12/2007	471.66 341.63	341.63	143.61	03/2011 -	03/2013	24(O) -	0/2
17	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	119.04	03/2010 -	03/2015	60(O) -	4/4
18	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	39.81	03/2016 -	03/2016	0(O) -	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	117.19	03/2017 -	03/2017	0(O) -	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.35	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	535.10	162.06	03/2015 03/2015	03/2015	0(O) 0(R)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	264.15	03/2014 -	03/2014	0(O) -	2/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	08/2007	163.51 -	163.51	34.58	03/2011 -	03/2014	36(O) -	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,236.96	03/2014 -	03/2014	0(O) -	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,394.48	03/2014 -	03/2014	0(O) -	10/15
27	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	71.33	03/2015 -	03/2015	0(O) -	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.63 -	479.63	112.88	03/2013 -	03/2013	0(O) -	5/7
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48(O) -	0/1
33	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	81.72	12/2012 -	03/2015	27(O) -	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	112.76	03/2013 -	03/2013	0(O) -	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	30.89	03/2014 -	03/2014	0(O) -	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/6
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	1.51	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	334.67	03/2013 -	03/2013	0(O) -	2/2

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	106.03	03/2010	03/2014	48(O)	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31	1,188.31	675.53	03/2013	03/2013	0(O)	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	08/2008	469.78	706.40	19.23	07/2012	03/2016	44(O)	1/2
43	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42	321.50	204.77	03/2014	03/2014	0(O)	1/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	39.31	03/2012	03/2014	24(O)	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	1,230.27	-	04/2015	04/2015	0(O)	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	339.88	-	04/2014	04/2014	0(O)	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	24.62	12/2015	08/2017	20(O)	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	1.73	03/2012	03/2015	36(O)	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	60.74	03/2012	03/2014	24(O)	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.88	03/2014	03/2016	24(O)	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98	210.98	87.89	03/2013	03/2013	0(O)	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	09/2009	153.82	153.82	24.39	03/2014	03/2014	0(O)	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	117.70	03/2012	03/2014	24(O)	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	2.48	03/2015	03/2015	0(O)	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78	209.78	29.06	03/2015	03/2015	0(O)	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	269.00	03/2016	03/2016	0(O)	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	49.02	03/2012	-	-	11/42
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	44.23	03/2016	03/2016	0(O)	1/12
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,522.47	06/2009	03/2013	45(O)	19/24

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,578.69	03/2012	03/2014	24(O)	0/39
62	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	106.67	03/2012	03/2014	24(O)	0/2
	Total		36,056.46	37,510.52	13,273.49				166/634
	Fertilisers								
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	925.00	01/2013	01/2013	0(O)	0/5
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	239.93	07/2011	07/2012	-	0/0
65	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	185.10	07/2011	04/2012	-	0/0
66	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	982.00	01/2013 12/2012	03/2013	2(O) 3(R)	8/8
67	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	902.00	01/2013	01/2013	0(O)	0/5
	Total		4,828.66	4,828.66	3,234.03				8/18
	Steel								
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	204.36	-	04/2013	-	13/19
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	250.08	08/2010	12/2012	28(O)	0/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	253.31	02/2011	01/2013	23(O)	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	141.86	-	11/2013	-	11/21
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	221.95	05/2012	06/2013	13(O)	1/2
73	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	343.37	12/2011 03/2012	01/2013	13(O) 10(R)	16/21
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	117.84	10/2012	03/2013	5(O)	3/4
75	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	332.65	-	08/2014	08/2014	0(O)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
76	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL, Orissa	11/2011	254.55	254.55	11.86	11/2013	11/2013	0(O)	1/1
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00	17,265.00	7,038.48	03/2013	09/2013	6(O)	22/27
78	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00	6,325.00	3,106.01	12/2011	12/2012	12(O)	11/16
79	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00	2,875.00	1,222.04	12/2012	03/2013	3(O)	10/12
80	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00	16,408.00	13,926.54	12/2011	12/2012	12(O)	19/19
81	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00	12,291.00	9,885.02	10/2009	03/2013	41(O)	62/64
82	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Orissa	09/2008	11,812.00	11,812.00	8,173.33	11/2013	03/2013	-8(O)	8/14
83	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL, Maharashtra	12/2011	187.33	187.33	11.30	-	12/2013	-	0/1
84	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL, Orissa	01/2012	254.90	254.90	0.26	12/2014	12/2014	0(O)	0/0
Total			65,285.87	71,443.41	44,907.61				179/225
<u>Petrochemicals</u>									
85	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61	8,920.00	5,775.44	04/2012	12/2013	20(O)	13/29
Total			5,460.61	8,920.00	5,775.44	12/2013		0(R)	13/29
<u>Petroleum</u>									
86	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00	820.00	-	06/2012	10/2013	16(O)	0/0
87	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64	2,163.64	1,147.97	06/2012	06/2013	12(O)	0/0
88	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11	370.11	271.67	04/2011	11/2012	19(O)	0/0
89	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35	977.00	586.34	12/2011	01/2013	13(O)	0/0
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	1,099.96	03/2013	03/2014	12(O)	0/0
91	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00	586.00	4.26	07/2015	07/2015	0(O)	0/0
92	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	711.28	12/2014	12/2014	0(O)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
94	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	460.70	260.34	07/2012 07/2012	06/2013	11(O) 11(R)	0/17
95	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]OCL,Haryana	11/2009	341.50	341.50	141.87	02/2013	02/2013	0(O)	38/42
96	Butene-1 at Panipat - [N16000139]OCL,Haryana	02/2012	190.00	190.00	15.87	03/2014	03/2014	0(O)	0/0
97	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	218.27	-	10/2012	-	36/36
98	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	798.00	748.84	04/2011 12/2011	12/2012	20(O) 12(R)	2/2
99	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	344.37	09/2011	08/2013	23(O)	0/0
100	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,583.08	05/2010 05/2012	12/2012	31(O) 7(R)	0/0
101	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	365.36	- 08/2011	-	-	0/22
102	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	756.65	77.45	05/2013	05/2013	0(O)	0/0
103	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	27.13	08/2013	01/2014	5(O)	0/0
104	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	240.95	47.51	09/2012	09/2013	12(O)	0/0
105	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
106	Construction of tanks and blending facility at Vad - [N16000115]OCL,Gujarat	02/2009	267.00	267.00	215.39	09/2012	09/2012	-	0/0
107	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,950.54	03/2012 08/2012	12/2012	9(O) 4(R)	0/21
108	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00	486.00	34.88	09/2013	09/2013	0(O)	0/0
109	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00	1,584.00	83.67	-	-	-	0/0
110	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86(O) 12(R)	0/0
111	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,917.83	08/2010 03/2012	12/2013	40(O) 21(R)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
112	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
113	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
114	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
115	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,203.81	09/2011 09/2012	09/2012	-	0/76
116	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,391.33	09/2011 03/2012	03/2013	18(O) 12(R)	0/0
117	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	96.08	03/2013 -	04/2013	1(O) -	0/0
118	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
119	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	559.68	03/2013 -	04/2014	13(O) -	0/0
120	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	66.34	11/2012 -	10/2013	11(O) -	0/0
121	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	359.20	01/2014 -	01/2014	0(O) -	0/0
122	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
123	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,970.91	- -	12/2012	- -	115/116
124	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	322.92	01/2013 -	06/2013	5(O) -	18/18
125	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	611.55	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
126	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	26.42	05/2015 -	05/2015	0(O) -	0/0
127	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,165.42	06/2012 03/2013	03/2013	9(O) 0(R)	8/8
128	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.00	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
129	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	634.47	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
130	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	03/2014	0(O) -	0/0
131	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	277.79	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
132	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	9.21	12/2015 -	12/2015	0(O) -	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
133	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	2,059.63	-	03/2015	03/2015	0(O)	0/0
134	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.54	01/2013	07/2015	30(O)	0/0
135	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	4.49	10/2010	12/2014	50(O)	0/0
136	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 312.00	312.00	273.34	01/2012 01/2012	01/2013	12(O) 12(R)	0/1
137	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	1,091.35	12/2012 12/2012	03/2014	15(O) 15(R)	0/21
138	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00	666.00	-	11/2015	11/2015	0(O)	0/0
139	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	9,540.15	01/2012	03/2013	14(O)	0/108
140	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	4,258.26	09/2012	09/2013	12(O)	0/0
141	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.54	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
142	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	701.81	04/2015	04/2015	0(O)	0/0
143	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24(O) 22(R)	0/0
144	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	556.60	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
145	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00	913.00	21.50	07/2015	07/2015	0(O)	0/0
146	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	19,099.00	11/2012	09/2013	10(O)	60/100
147	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	706.64	09/2012	09/2012	-	0/11
148	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	2,303.59	02/2014	02/2014	0(O)	0/0
149	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	246.81	184.00	04/2012	-	-	0/0
150	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	1,417.00	30.09	05/2014	05/2014	0(O)	0/0
151	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	636.50	07/2012	06/2013	11(O)	0/31

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
152	RESITEMENT OF MARKETING INSTALLATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	898.00	907.45	- 03/2012	08/2012	-	51/53
153	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	03/2012	1,210.64 -	1,210.64	-	03/2015 -	03/2015	0(O) -	0/0
154	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014	0(O) -	0/0
155	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	165.66	08/2012 -	03/2013	7(O) -	0/0
156	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	226.47	03/2012 -	03/2013	12(O) -	13/20
157	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	89.68	12/2013 -	12/2013	0(O) -	0/0
Total			176,404.09 -	187,683.11	84,103.88				356/885
Power									
158	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,501.40	08/2012 -	03/2013	7(O) -	0/11
159	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,138.40	02/2012 -	01/2013	11(O) -	0/7
160	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	681.20	05/2012 -	03/2013	10(O) -	0/11
161	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,075.40	06/2012 -	12/2012	6(O) -	0/4
162	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,808.00	08/2013 -	09/2014	13(O) -	7/19
163	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,614.00	12/2009 -	03/2016	75(O) -	26/47
164	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,451.00	07/2011 -	11/2014	40(O) -	4/28
165	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.00	767.36	02/2011 10/2012	12/2012	22(O) 2(R)	2/4
166	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	337.40	08/2014 -	08/2014	0(O) -	0/20
167	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	33.70	06/2014 -	06/2014	0(O) -	0/20

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
168	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	407.40	09/2014 -	09/2014	0(O) -	8/19
169	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	866.00	10/2009 -	03/2013	41(O) -	20/20
170	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	464.60	11/2012 -	03/2014	16(O) -	3/11
171	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
172	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	492.70	05/2014 -	05/2014	0(O) -	0/16
173	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	735.60	08/2013 -	08/2013	0(O) -	0/14
174	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	72.90	08/2014 -	08/2014	0(O) -	0/21
175	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	577.30	12/2013 -	12/2013	0(O) -	0/13
176	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	57.50	10/2012 -	03/2013	5(O) -	0/15
177	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	863.03	12/2007 12/2009	-	-	0/10
178	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	2,034.59	05/2013 06/2016	03/2017	46(O) 9(R)	5/22
179	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,751.05	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
180	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	6,358.91	4,633.00	04/2009 -	09/2014	65(O) -	0/9
181	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,036.00	12/2016 -	12/2016	0(O) -	0/5
182	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,842.31	09/2008 -	03/2013	54(O) -	17/37
183	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,573.00	08/2012 -	03/2013	7(O) -	11/16
184	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	597.00	09/2016 -	09/2016	0(O) -	0/12
185	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	807.36	08/2010 01/2013	03/2013	31(O) 2(R)	0/3
186	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,257.90	08/2013 -	09/2014	13(O) -	0/17

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	248.10	02/2012 -	12/2013	22(O) -	0/14
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	332.10	11/2011 -	12/2013	25(O) -	0/11
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	347.70	11/2011 -	12/2013	25(O) -	0/14
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	67.50	01/2013 -	01/2013	0(O) -	0/7
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	219.50	07/2013 -	07/2013	0(O) -	0/12
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	614.60	04/2013 -	10/2013	6(O) -	0/12
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	102.60	08/2013 -	08/2013	0(O) -	0/16
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	54.00	11/2014 -	11/2014	0(O) -	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	-	03/2015 -	03/2015	0(O) -	0/0
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	-	04/2015 -	04/2015	0(O) -	0/0
197	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	469.10	11/2012 -	03/2013	4(O) -	0/10
198	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,974.99	10/2010 01/2013	09/2013	35(O) 8(R)	0/6
199	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,659.80	09/2009 07/2014	12/2017	99(O) 41(R)	1/20
200	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	410.24	08/2012 08/2013	09/2014	25(O) 13(R)	15/21
201	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03 -	2,047.03	2,056.66	01/2012 -	09/2013	20(O) -	0/0
202	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,742.00	10/2012 -	05/2013	7(O) -	11/16
203	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	896.00	11/2016 -	11/2016	0(O) -	0/11
204	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,858.69	09/2010 08/2014	03/2017	78(O) 31(R)	11/11
205	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	54.70	04/2013 -	04/2013	0(O) -	0/15

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
206	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,987.20	08/2012	09/2013	13(O)	0/7
207	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	1,508.74	-	06/2016	06/2016	0(O)	0/0
208	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	1,935.35	-	12/2014	12/2014	0(O)	0/0
209	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/0
210	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	50.40	08/2014	08/2014	0(O)	0/20
211	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	115.90	02/2015	02/2015	0(O)	0/0
212	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	1,263.26	53.40	11/2014	11/2014	0(O)	0/0
213	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	126.70	01/2015	01/2015	0(O)	0/19
214	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	33.20	08/2014	08/2014	0(O)	0/20
215	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	67.40	06/2014	06/2014	0(O)	0/19
216	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	167.30	04/2012	12/2012	8(O)	0/0
217	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	128.58	06/2012	12/2012	6(O)	0/9
218	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	791.40	08/2012	12/2013	16(O)	0/11
219	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,613.00	03/2013	09/2015	30(O)	2/14
220	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,233.36	09/2009 06/2013	12/2013	51(O) 6(R)	0/0
221	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,622.90	03/2007 09/2012	02/2013	71(O) 5(R)	25/25
222	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	388.96	07/2010 02/2016	11/2016	76(O) 9(R)	1/10

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
223	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	35.50	01/2014 -	01/2014	0(O) -	0/17
224	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	104.10	08/2014 -	08/2014	0(O) -	0/0
225	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	95.00	10/2014 -	10/2014	0(O) -	0/21
226	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	333.83	07/2011 -	12/2012	17(O) -	0/5
227	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,091.50	10/2012 -	09/2013	11(O) -	0/12
228	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	337.00	01/2015 -	01/2015	0(O) -	0/20
229	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	857.50	03/2014 -	03/2014	0(O) -	0/15
230	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	643.00	08/2013 -	08/2013	0(O) -	0/14
231	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	2.20	08/2014 -	08/2014	0(O) -	0/20
232	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	42.80	10/2014 -	10/2014	0(O) -	0/20
233	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013	37(O) -	0/22
234	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	154.10	11/2011 -	09/2013	22(O) -	0/7
235	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,110.90	12/2012 -	02/2013	2(O) -	0/11
236	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	105.60	02/2014 -	02/2014	0(O) -	0/20
237	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	136.60	10/2013 -	10/2013	0(O) -	0/18
238	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	53.80	07/2013 -	07/2013	0(O) -	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
239	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	311.40	12/2013 -	12/2013	0(O) -	0/18
240	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhandd	10/2011	558.26 -	558.26	74.50	11/2013 -	11/2013	0(O) -	0/20
241	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	746.80	03/2013 -	03/2013	0(O) -	0/14
242	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	989.40	12/2013 -	12/2013	0(O) -	0/13
243	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,759.60	11/2012 -	06/2013	7(O) -	0/15
244	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	281.10	07/2014 -	07/2014	0(O) -	0/19
245	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	400.03	- -	07/2013	- -	6/29
246	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	368.59	07/2014 -	02/2015	7(O) -	0/16
247	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	995.50	12/2012 -	12/2013	12(O) -	0/11
248	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	550.10	11/2013 -	11/2013	0(O) -	0/15
249	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	58.40	01/2013 -	11/2013	10(O) -	0/16
250	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,081.00	1,843.25	11/2009 02/2013	03/2013	40(O) 1(R)	0/4
251	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	150.00	08/2015 -	08/2015	0(O) -	0/5
252	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,990.00	10/2012 -	03/2013	5(O) -	11/15
253	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 -	3,422.44	328.35	07/2014 -	05/2016	22(O) -	1/3
254	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,170.10	07/2010 -	12/2012	29(O) -	20/20
255	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	420.80	09/2010 -	03/2013	30(O) -	0/9

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
256	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, Chhatisgarh	03/2012	9,569.76	9,569.76	261.10	06/2015	06/2015	0(O)	0/24
	Total		232,888.28	248,718.52	109,362.53				207/1273
Railways									
257	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura	04/2008	813.34	1,141.75	426.35	03/2014	03/2014	0(O)	0/0
			813.34			-		-	
258	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00	227.42	250.82	12/2009	03/2011	-	0/0
			214.09			03/2011			
259	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08	2,820.00	174.97	-	03/2013	-	0/0
			1,010.00			-		-	
260	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00	453.04	392.85	03/2011	03/2011	-	0/0
			170.00			03/2011			
261	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90	548.95	543.14	06/1999	03/2011	-	0/0
			284.27			03/2011			
262	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00	1,214.00	96.96	-	-	-	0/0
			-			-			
263	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR, Gujarat	04/2008	394.14	404.39	3.77	03/2013	03/2013	0(O)	0/0
			385.60			-		-	
264	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
			901.62			-			
265	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90	1,412.74	459.54	03/2005	06/2016	135(O)	0/0
			1,028.05			12/2008		90(R)	
266	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15	1,106.62	208.26	12/2010	03/2011	-	0/0
			1,106.62			03/2011			
267	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, Maharashtra	03/1996	401.81	1,512.86	204.74	03/2004	03/2014	120(O)	0/0
			495.44			12/2010		39(R)	
268	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34	2,393.48	12.87	04/2014	03/2015	11(O)	0/0
			619.34			-		-	
269	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20	687.20	668.82	03/2010	12/2012	33(O)	0/0
			-			-		-	
270	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52	350.00	327.08	-	03/2011	-	0/0
			-			03/2009			
271	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00	3,230.02	2,501.02	04/2008	12/2015	92(O)	0/0
			1,500.00			03/2014		21(R)	
272	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52	207.52	149.23	12/2012	12/2013	12(O)	0/0
			207.52			-		-	
273	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36	196.95	193.55	03/2011	-	-	0/0
			196.95			-			
274	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR, Gujarat	04/2008	318.24	468.62	1.00	03/2012	-	-	0/0
			-			-			

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
276	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	904.73	12/2012 01/2013	01/2013	1(O) 0(R)	0/0
277	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
278	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
279	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2013	06/2013	0(O) 0(R)	0/0
280	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	415.73	279.98	- -	12/2012	- -	0/0
281	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	122.02	12/2012 -	12/2012	0(O) -	0/0
282	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	84.24	- -	-	-	0/0
283	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	203.62	- -	03/2013	- -	0/0
284	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	452.22	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
285	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	564.99	- -	12/2012	- -	0/0
286	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	93.16	12/2011 02/2012	02/2012	-	0/0
287	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0
288	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
289	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	175.20	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
290	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
291	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	261.02	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
292	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	62.07	02/2006 -	-	-	0/0
293	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	603.58	- -	03/2012	-	0/0
294	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
295	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	320.09	- 05/2009	05/2009	-	0/0
296	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	117.44	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
297	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	182.57	- -	-	-	0/0
298	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	221.60	- 09/2009	-	-	0/0
299	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
300	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	551.49	- -	01/2013	- -	0/0
301	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	146.32	- -	03/2014	- -	0/0
302	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	171.83	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
303	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	70.22	- -	-	-	0/0
304	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	7.97	03/2015 -	03/2015	0(O) -	0/0
305	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	835.57	06/2007 -	06/2007	-	0/0
306	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	662.52	03/2012 08/2012	02/2013	11(O) 6(R)	0/0
307	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	499.90	437.79	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
308	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	937.59	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
309	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	206.41	03/2014 -	03/2014	0(O) -	0/0
310	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	256.66	03/2012 03/2012	03/2013	12(O) 12(R)	0/0
311	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,389.02	- -	03/2013	- -	0/0
312	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	506.14	- -	03/2014	- -	1/1
313	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	751.86	- -	10/2012	-	0/0
314	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	732.83	12/2010 12/2010	03/2015	51(O) 51(R)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
315	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	99.56	- -	03/2013	- -	0/0
316	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
317	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,995.25	239.07	- -	03/2013	- -	0/0
318	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
319	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	768.87	440.16	- 03/2010	03/2010	-	0/0
320	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	2,957.21	1,336.45	07/2005 -	-	-	0/0
321	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	126.53	- -	-	-	0/0
322	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	276.82	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
323	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
324	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	334.77	- -	12/2012	- -	0/0
325	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	114.08	12/2012 -	03/2014	15(O) -	0/0
326	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	324.06	05/2008 03/2011	03/2011	-	0/0
327	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	-	0/0
328	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	206.16	03/2002 -	03/2013	132(O) -	0/0
329	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,195.95	03/2009 -	12/2013	57(O) -	0/0
330	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
331	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.46	- -	02/2013	- -	0/0
332	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	633.10	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
333	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
334	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	404.60	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
335	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	900.00	301.11	- -	-	-	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,334.00	06/2011 03/2012	03/2012	-	0/0
337	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	920.70	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
338	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	141.45	- -	03/2012	-	0/0
339	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	634.24	02/2009 -	03/2012	-	0/0
340	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	352.10	07/2012 -	-	-	0/0
341	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	39.45	- -	-	-	0/0
342	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	114.85	- -	03/2014	- -	0/0
343	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,298.65	12/2008 -	03/2014	63(O) -	0/0
344	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.39	- -	03/2015	- -	0/0
345	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2015	0(O) -	0/0
346	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,913.51	198.56	03/2016 -	03/2016	0(O) -	0/0
347	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	36.71	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
348	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	42.65	03/2016 -	03/2016	0(O) -	0/0
349	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	32.66	03/2016 -	06/2016	3(O) -	0/0
350	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	448.67	03/2008 06/2008	-	-	0/0
351	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	355.00	413.37	03/2009 12/2009	03/2011	-	0/0
352	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	243.77	02/2010 -	-	-	0/0
353	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,580.27	10/2007 12/2012	12/2012	62(O) 0(R)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
354	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	925.30	587.51	- -	03/2012	-	0/0
355	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	293.74	132.87	12/2010 12/2010	12/2010	-	0/0
356	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 842.35	1,029.00	775.39	- -	03/2013	-	0/6
357	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	221.90	236.81	12/2007 03/2010	12/2010	-	0/0
358	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 2,363.00	2,363.00	881.70	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
359	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
360	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	224.49	- -	-	-	0/0
361	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, Jharkhand	04/1997	194.07 194.07	456.45	309.09	06/2004 -	12/2012	102(O) -	0/0
362	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70 915.70	1,717.29	1,476.55	- -	03/2013	-	0/0
363	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	370.00	358.98	04/2003 03/2010	-	-	0/0
364	REWARI-ROHTAK (NL), NR - [220100279]NR, Haryana	01/2004	149.38 330.23	602.78	503.47	02/2010 02/2011	02/2011	-	0/0
365	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 604.04	639.97	174.95	03/1998 08/2005	08/2005	-	0/0
366	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	409.29	03/2013 -	03/2014	12(O) -	0/0
367	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh	04/2008	603.04 603.04	603.04	111.83	03/2012 -	03/2013	12(O) -	0/0
368	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhattisgarh	09/2006	324.90 -	385.54	228.77	03/2010 -	03/2012	-	0/0
369	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015	0(O) -	0/0
370	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23 -	818.29	75.05	02/2015 -	02/2015	0(O) -	0/0
371	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR, Rajasthan	04/2008	516.23 516.23	516.23	300.84	03/2014 -	03/2014	0(O) -	0/0
372	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, Orissa	04/2005	726.96 810.78	810.78	137.87	- -	03/2013	-	0/0
373	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,086.41	431.18	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
374	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	1,188.91	566.80	- 12/2009	02/2012	-	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
375	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	137.04	- -	-	-	0/0
376	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	40.30	- -	-	-	0/0
377	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	548.96	521.61	- -	-	-	0/0
378	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,235.94	12/2006 08/2010	08/2010	-	0/0
379	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	62.11	03/2012 -	02/2013	11(O) -	0/0
380	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,J and K	03/1995	2,500.00 2,500.00	20,000.00	8,525.30	03/2001 -	12/2017	201(O) -	0/0
381	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	819.40	170.80	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
382	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	402.64	03/2014 -	03/2013	-12(O) -	0/0
383	VIRAMGAM-BHILD(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	174.00	- 03/2010	-	-	0/0
Total			64,518.68	150,659.22	64,648.56				1/7
Road Transport & Highways									
384	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	390.56	05/2013 -	03/2014	10(O) -	0/0
385	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	269.32	11/2013 -	11/2013	0(O) -	0/0
386	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	11.19	01/2014 -	01/2014	0(O) -	0/0
387	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	256.79	02/2014 -	02/2014	0(O) -	0/0
388	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	262.23	02/2014 -	04/2014	2(O) -	0/0
389	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014	0(O) -	0/0
390	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	131.46	05/2014 -	05/2014	0(O) -	0/0
391	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	976.72	08/2014 -	08/2014	0(O) -	0/0
392	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013	0(O) -	0/0
393	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	34.69	09/2013 -	07/2014	10(O) -	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
394	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	616.04	08/2013	08/2013	0(O)	0/0
395	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	575.00	479.87	07/2013	07/2013	0(O)	0/0
396	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00	398.00	297.32	02/2014	02/2014	0(O)	0/0
397	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	998.79	580.59	08/2013	08/2013	0(O)	0/0
398	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	218.49	08/2013	08/2013	0(O)	0/0
399	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
400	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18	1,396.18	529.67	09/2014	09/2014	0(O)	0/0
401	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	190.08	09/2007	03/2014	78(O)	0/0
402	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2012	93(O)	0/0
403	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,163.70	11/2012	06/2013	7(O)	0/0
404	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	294.04	11/2008	12/2012	49(O)	0/0
405	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	260.19	01/2009	12/2012	47(O)	0/0
406	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	12/2012	10(O)	0/0
407	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	194.51	02/2004	12/2012	106(O)	0/0
408	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	201.26	09/2013	09/2013	0(O)	0/0
409	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	535.37	06/2014	06/2014	0(O)	0/0
410	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	419.65	-	10/2013	-	2/2
411	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.82	01/2013	10/2013	9(O)	0/0
412	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	500.29	449.35	08/2013	08/2013	0(O)	0/0
413	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	253.69	06/2008	12/2012	54(O)	0/0
414	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	212.33	06/2008	03/2013	57(O)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	228.65	06/2005 -	03/2013	93(O) -	0/0
416	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	225.26	04/2010 -	12/2012	32(O) -	0/0
417	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46(O) -	0/0
418	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	852.00	743.61	03/2013 -	03/2013	0(O) -	0/0
419	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00 -	839.00	433.49	- -	12/2013	- -	0/1
420	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.75	05/2013 -	05/2013	0(O) -	0/0
421	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	379.97	10/2011 -	03/2014	29(O) -	0/0
422	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	718.83	10/2011 -	06/2013	20(O) -	0/0
423	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	225.00	285.20	06/2008 -	12/2012	54(O) -	0/0
424	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	175.59	10/2008 -	01/2014	63(O) -	0/0
425	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	636.27	05/2010 -	12/2012	31(O) -	0/0
426	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00 -	593.00	422.82	07/2013 -	07/2013	0(O) -	0/0
427	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	06/2013	0(O) -	0/0
428	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00 -	453.00	355.66	- -	06/2013	- -	1/1
429	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	231.18	06/2008 -	03/2013	57(O) -	0/0
430	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	187.69	05/2008 -	03/2013	58(O) -	0/0
431	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	274.33	09/2010 -	12/2012	27(O) -	0/0
432	Dindigul - Kumli - [N24000177]NHAI, Tamil Nadu	09/2011	485.00 -	485.00	85.41	08/2013 -	08/2013	0(O) -	0/0
433	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	535.62	01/2011 -	12/2012	23(O) -	0/0
434	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	406.18	09/2008 -	12/2012	51(O) -	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
435	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	12/2013	30(O)	0/0
436	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	201.66	135.13	09/2008	03/2013	54(O)	0/0
437	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	271.66	02/2004	12/2012	106(O)	0/0
438	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00	1,141.00	710.17	08/2013	08/2013	0(O)	0/0
439	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	211.16	04/2008	12/2012	56(O)	0/0
440	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	152.14	04/2008	12/2012	56(O)	0/0
441	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38(O)	0/0
442	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	495.27	12/2009	07/2013	43(O)	0/0
443	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	1,427.90	09/2012	03/2013	6(O)	0/0
444	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	2,731.90	10/2011	12/2012	14(O)	0/0
445	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	279.46	09/2007	12/2012	63(O)	0/0
446	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	279.78	02/2009 03/2014	03/2013	49(O) -12(R)	0/0
447	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	67.36	07/2009	04/2014	57(O)	0/0
448	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	28.21	09/2007	04/2014	79(O)	0/0
449	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	187.79	08/2004	12/2012	100(O)	0/0
450	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	183.76	08/2004 07/2010	12/2012	100(O) 29(R)	0/0
451	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	876.51	01/2013	01/2013	0(O)	0/0
452	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
453	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	1,923.80	10/2012	12/2012	2(O)	0/0
454	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	537.91	05/2012	12/2012	7(O)	0/0
455	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	325.00	387.71	05/2013	02/2014	9(O)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
456	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
457	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81	267.81	549.27	02/2013	02/2013	0(O)	0/0
458	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
459	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	575.32	09/2008	12/2012	51(O)	0/0
460	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	499.80	09/2009	03/2013	42(O)	0/0
461	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00	536.00	413.95	01/2014	01/2014	0(O)	0/0
462	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	1,553.70	12/2012	12/2012	0(O)	0/0
463	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	279.46	10/2008	02/2013	52(O)	0/0
464	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	294.29	10/2008	03/2013	53(O)	0/0
465	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, West Bengal	02/2012	702.16	702.16	192.51	07/2014	07/2014	0(O)	0/0
466	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
467	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	1,055.70	05/2012	12/2012	7(O)	0/0
468	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	263.17	233.77	06/2010	09/2014	51(O)	0/0
469	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
470	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24(O)	0/0
471	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	97.61	11/2008	07/2013	56(O)	0/0
472	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	64.82	04/2009	07/2013	51(O)	0/0
473	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	24.44	11/2008	01/2014	62(O)	0/0
474	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	122.13	04/2009	03/2013	47(O)	0/0
475	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6(O)	0/0
476	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	1,264.30	06/2013	06/2013	0(O)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
477	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00	754.00	465.47	03/2013	03/2014	12(O)	0/0
478	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	269.32	11/2013	11/2013	0(O)	0/0
479	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	289.79	06/2008	03/2013	57(O)	0/0
480	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48(O)	0/0
481	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19	484.19	25.36	10/2014	10/2014	0(O)	0/0
482	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	270.92	04/2008	12/2012	56(O)	0/0
483	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	148.90	06/2008	03/2013	57(O)	0/0
484	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	277.10	06/2008	12/2012	54(O)	0/0
485	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
486	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	257.43	06/2011 06/2011	12/2012	18(O) 18(R)	0/2
487	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.92	02/2010	12/2014	58(O)	0/0
488	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00	586.00	237.55	01/2014	01/2014	0(O)	0/0
489	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	456.32	09/2013	09/2013	0(O)	0/0
490	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	391.02	03/2008	03/2013	60(O)	0/0
491	PANIKHOLI-RIMOLI - [N24000197]NHAI, Orissa	03/2012	1,410.00	1,410.00	152.77	09/2014	09/2014	0(O)	0/0
492	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	960.09	10/2014	10/2014	0(O)	0/0
493	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	239.66	05/2008	03/2013	58(O)	0/0
494	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	574.00	426.20	03/2014	03/2014	0(O)	0/0
495	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	588.91	02/2013	02/2013	0(O)	0/0
496	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,198.70	07/2012	12/2012	5(O)	0/0
497	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	1,035.70	03/2013	03/2013	0(O)	0/0
498	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00	835.00	104.67	01/2014	01/2014	0(O)	0/0
499	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	3,565.00	11/2011	08/2013	21(O)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
500	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17(O)	0/0
501	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00	1,987.00	-	07/2015	06/2016	11(O)	0/0
502	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	251.03	314.73	10/2008	06/2013	56(O)	0/0
503	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya Pradesh	12/2003	229.91	229.91	275.64	10/2008	12/2012	50(O)	0/0
504	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00	650.00	768.75	11/2013	11/2013	0(O)	0/0
505	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	241.70	10/2008	12/2012	50(O)	0/0
506	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	02/2013	25(O)	0/0
507	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	362.46	03/2013	03/2013	0(O)	0/0
508	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Orissa	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
509	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	209.43	09/2007	03/2013	66(O)	0/0
510	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	187.10	07/2008	12/2012	53(O)	0/0
511	SIX LANNING OF HOSUR-KRISHNAGIRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
512	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	12.48	12/2013	12/2013	0(O)	0/0
513	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
514	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2014	19(O)	0/0
515	SNG toBANL - [N24000189]NHAI, J and K	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
516	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	491.21	03/2008	03/2013	60(O)	0/0
517	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	148.22	04/2004	12/2012	104(O)	0/0
518	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,675.10	08/2011	12/2012	16(O)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
519	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	12/2012	42(O)	0/0
520	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	03/2013	32(O)	0/0
521	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	777.98	11/2013	11/2013	0(O)	0/0
522	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
523	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	78.28	05/2013	05/2013	0(O)	0/0
524	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	172.90	-	04/2013	-	2/2
525	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	692.68	03/2014	03/2014	0(O)	0/0
526	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	163.43	03/2008	12/2012	57(O)	0/0
527	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	33.97	11/2012	12/2013	13(O)	0/0
528	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	440.83	07/2013	07/2013	0(O)	0/0
529	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	149.40	06/2014	06/2014	0(O)	0/0
Total			94,054.50	95,488.69	69,013.72				10/14
Shipping & Ports									
530	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011 11/2012	11/2012	19(O) 0(R)	0/0
531	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	777.97	09/2012 10/2012	10/2012	-	0/0
532	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	294.84	12/2012 05/2013	05/2013	5(O) 0(R)	0/0
533	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
534	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	305.00	194.14	06/2011 09/2012	09/2012	-	0/0
535	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	248.23	02/2014	02/2014	0(O)	0/0
536	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 10/2013	10/2013	-2(O) 0(R)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
537	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	904.13	12/2010 09/2012	10/2013	34(O) 13(R)	0/0
538	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0
539	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0
540	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	10/2008	-	0/0
541	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1
542	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
543	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0
544	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
545	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0
546	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	830.41	10/2008 11/2010	-	-	0/0
547	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,563.50	01/2012 09/2012	01/2013	12(O) 4(R)	0/0
548	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
Total			16,242.52 -	18,554.09	8,500.80				0/1
<u>Telecommunications</u>									
549	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53(O) -	0/0
550	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
551	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72(O) 11(R)	0/0

Sector Wise Details

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
552	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	06/2013	32(O) 15(R)	0/0
553	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
554	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
555	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttaranchal	01/2009	149.15 158.72	158.72	80.05	06/2009 -	03/2013	45(O) -	0/0
556	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	03/2013	51(O) -	0/0
557	GSM equipment of 1625000 Lines (2G) 325000 lines 3(-) - [N26000090]BSNL, Madhya pradesh	11/2009	916.70 930.60	930.60	818.09	11/2010 -	12/2012	25(O) -	0/0
558	GSM equipment of 200000 Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	-	0/0
559	GSM equipment of 799000 Lines (2G) 101000 lines 3(G) - [N26000088]BSNL, Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	03/2013	48(O) -	0/0
560	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL, Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
561	Implementation of FTTH, the state of the art access, upon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
Total			5,735.48 -	5,676.27	1,660.99				0/0
<u>Urban Development</u>									
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21(O) -	6/6
563	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
564	DELHI MRTS PHASE-III - [N28000056]DMRC, Delhi	09/2011	35,242.00 -	35,242.00	1,057.48	03/2016 -	03/2016	0(O) -	0/0
565	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	2,494.00	115.29	09/2014 -	09/2014	0(O) -	0/0
Total			44,245.18 -	49,518.08	3,440.34				6/6
<u>Water Resources</u>									
566	PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O) -	0/0

Sector Wise Details

(Nov,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			542.90	1,187.00	35.49				0/0
Grand Total			793,285.10	933,569.56	433,732.24				993/3419

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

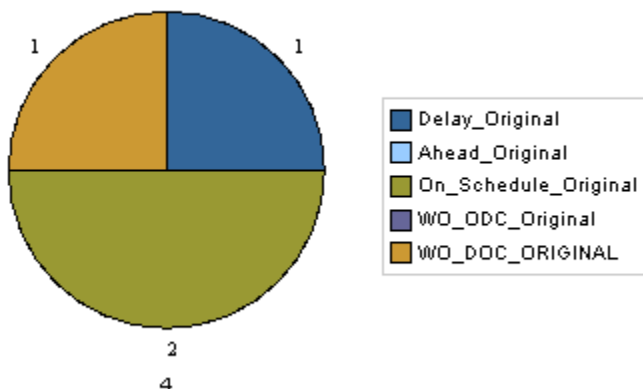

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till November, 2012 is Rs. 3440.34 crore, which is 6.9% of the revised cost of the projects.

Figures are in Rs. Crore

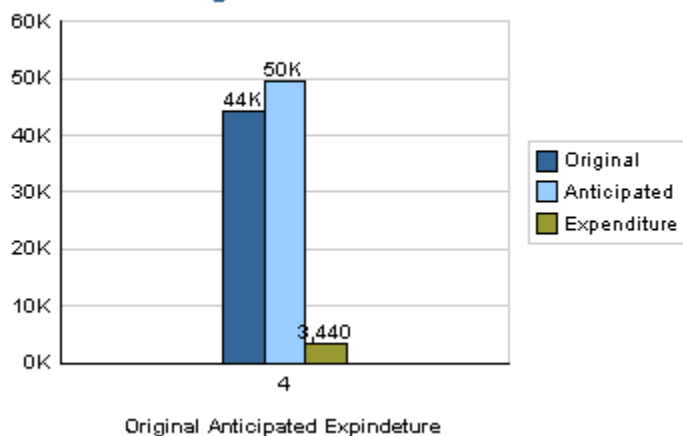

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **13**

Number of Projects Delayed **7**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 7 projects are delayed .6 projects do not have fixed dates of commissioning.

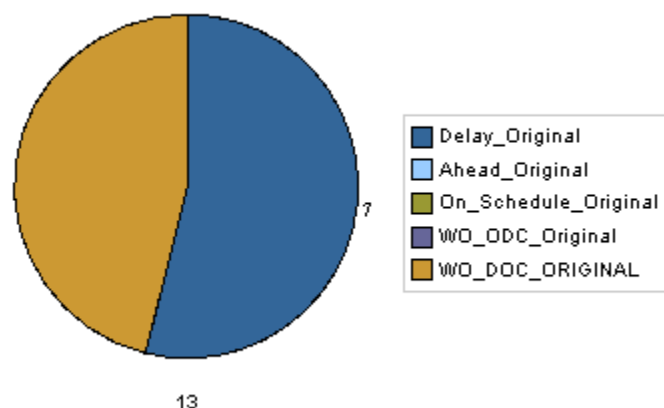

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5735.48 crore but this was subsequently revised to Rs. 5676.27 crore implying a cost overrun of -1%. The expenditure incurred on these projects till November, 2012 is Rs. 1660.99 crore, which is 29.3% of the revised cost of the projects.

Figures are in Rs. Crore

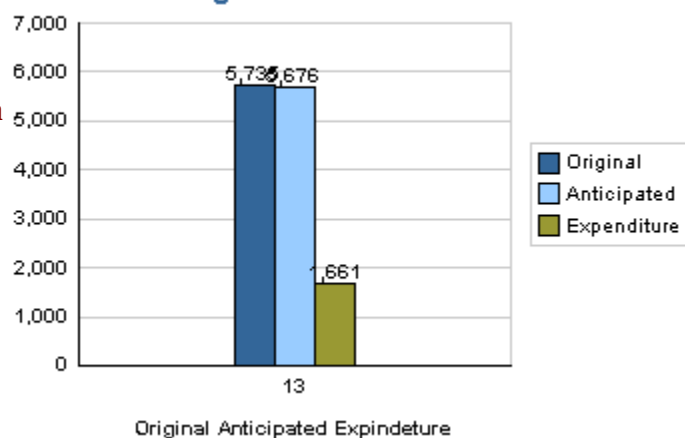

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	8
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	8

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 2 projects are ahead of schedule, 1 project are on schedule and 8 projects are delayed .8 projects do not have fixed dates of commissioning.

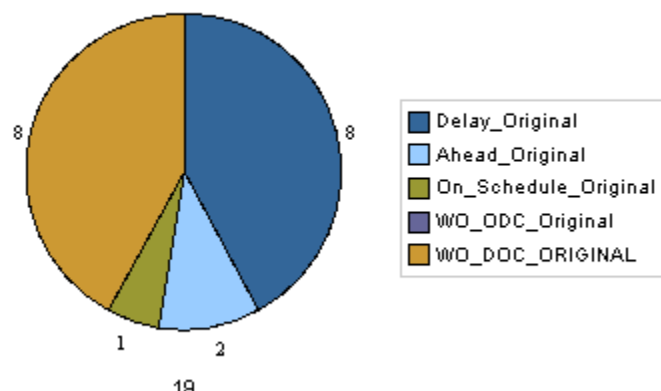

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 16242.52 crore but this was subsequently revised to Rs. 18554.09 crore implying a cost overrun of 14.2%. The expenditure incurred on these projects till November, 2012 is Rs. 8500.8 crore, which is 45.8% of the revised cost of the projects.

Figures are in Rs. Crore

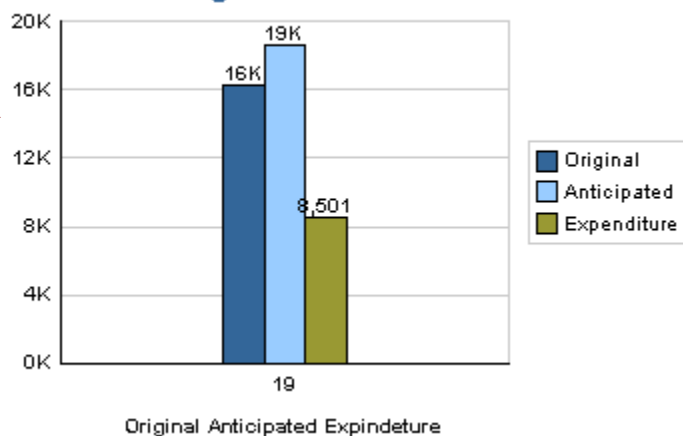

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	146
Number of Projects On Schedule	53
Number of Projects Delayed	87

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 146 projects, 53 projects are on schedule and 87 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

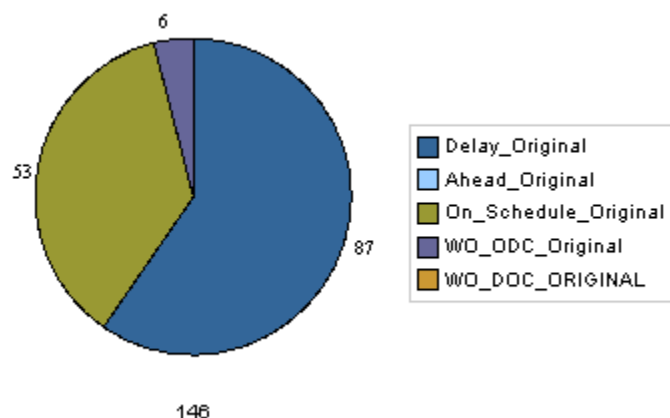

III. Investment Scenario

The Total Original cost of implementation of 146 projects when sanctioned, was of the order of Rs. 94054.5 crore but this was subsequently revised to Rs. 95488.69 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till November, 2012 is Rs. 69013.72 crore, which is 72.3% of the revised cost of the projects.

Figures are in Rs. Crore

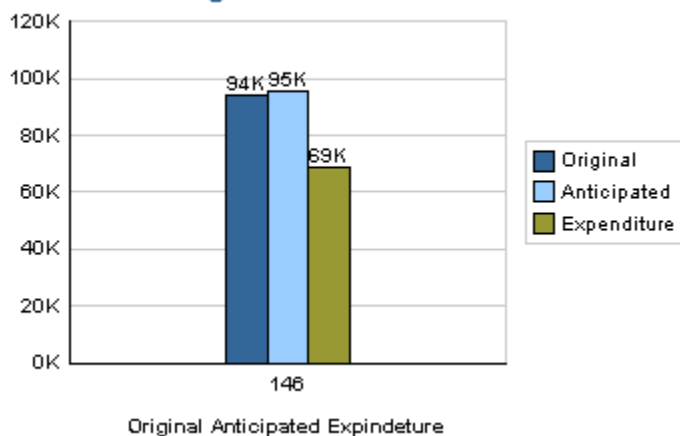

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	127
Number of Projects On Schedule	12
Number of Projects Delayed	39
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	19
Number of Projects Without Date Of Commissioning	56

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 127 projects, 1 project are ahead of schedule, 12 projects are on schedule and 39 projects are delayed .56 projects do not have fixed dates of commissioning.19 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

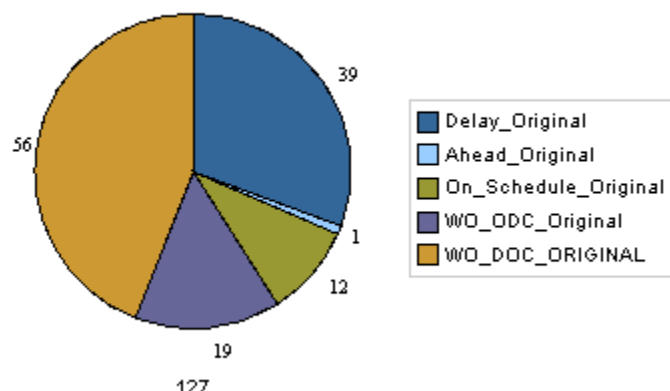

III. Investment Scenario

The Total Original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 64518.68 crore but this was subsequently revised to Rs. 150659.22 crore implying a cost overrun of 133.5%. The expenditure incurred on these projects till November, 2012 is Rs. 64648.56 crore, which is 42.9% of the revised cost of the projects.

Figures are in Rs. Crore

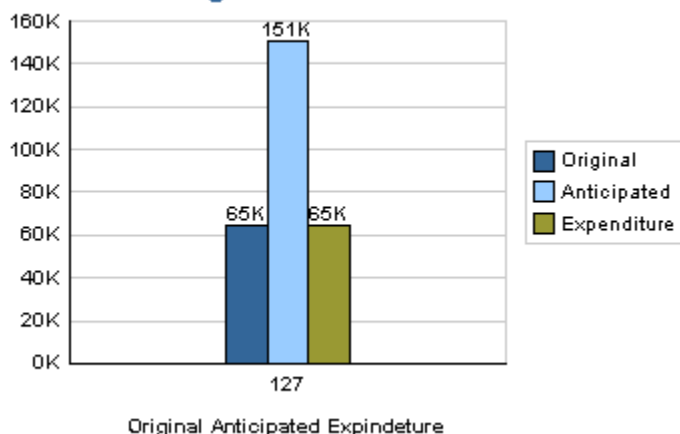

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	99
Number of Projects On Schedule	46
Number of Projects Delayed	51

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 99 projects, 46 projects are on schedule and 51 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

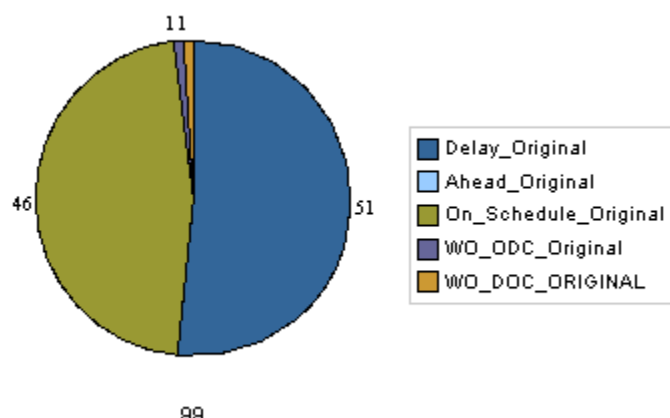

III. Investment Scenario

The Total Original cost of implementation of 99 projects when sanctioned, was of the order of Rs. 232888.28 crore but this was subsequently revised to Rs. 248718.52 crore implying a cost overrun of 6.8%. The expenditure incurred on these projects till November, 2012 is Rs. 109362.53 crore, which is 44% of the revised cost of the projects.

Figures are in Rs. Crore

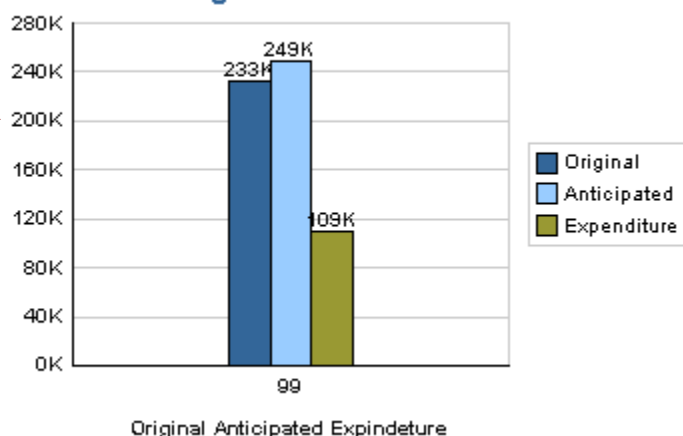

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	72
Number of Projects On Schedule	23
Number of Projects Delayed	40

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 72 projects, 23 projects are on schedule and 40 projects are delayed .8 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

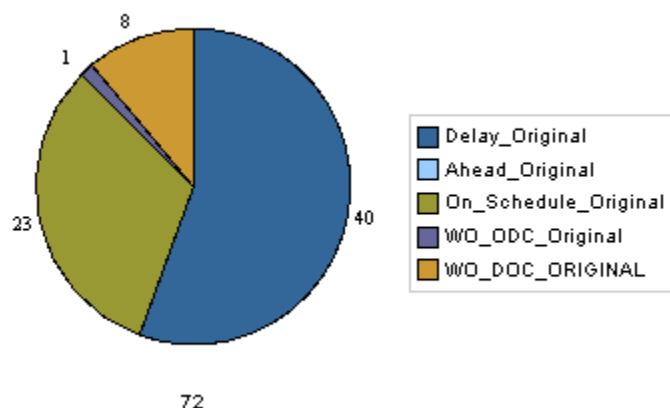

III. Investment Scenario

The Total Original cost of implementation of 72 projects when sanctioned, was of the order of Rs. 176404.09 crore but this was subsequently revised to Rs. 187683.11 crore implying a cost overrun of 6.4%. The expenditure incurred on these projects till November, 2012 is Rs. 84103.88 crore, which is 44.8% of the revised cost of the projects.

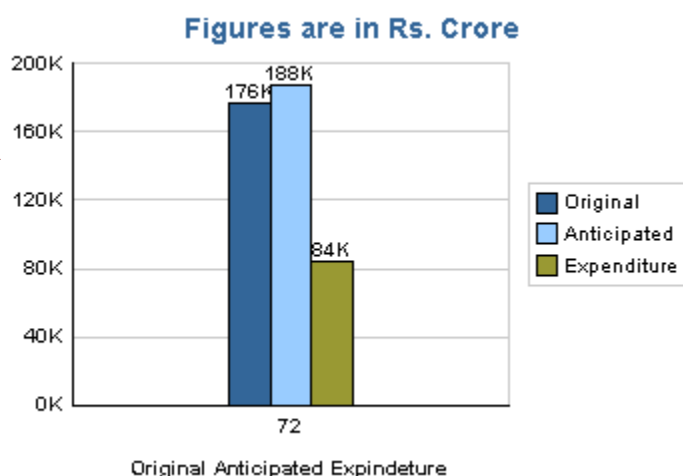

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 1 project are ahead of schedule, 3 projects are on schedule and 10 projects are delayed .3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

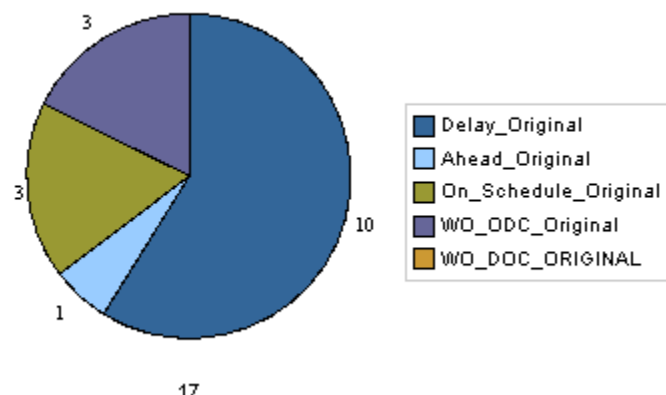

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till November, 2012 is Rs. 44907.61 crore, which is 62.9% of the revised cost of the projects.

Figures are in Rs. Crore

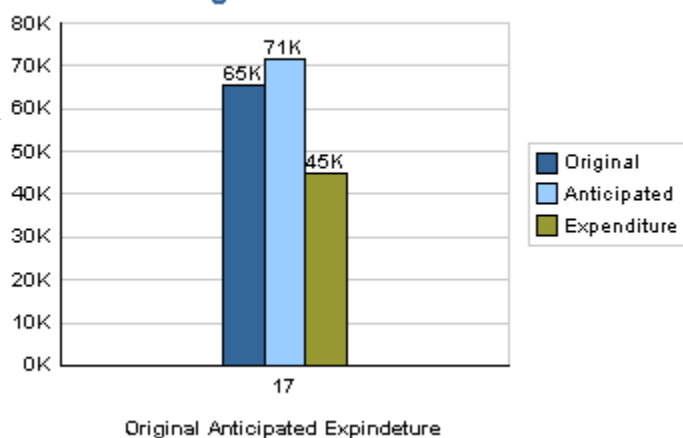

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

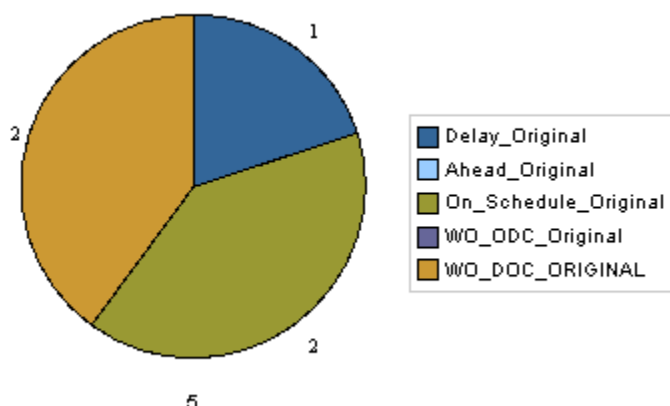

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4828.66 crore but this was subsequently revised to Rs. 4828.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till November, 2012 is Rs. 3234.03 crore, which is 67% of the revised cost of the projects.

Figures are in Rs. Crore

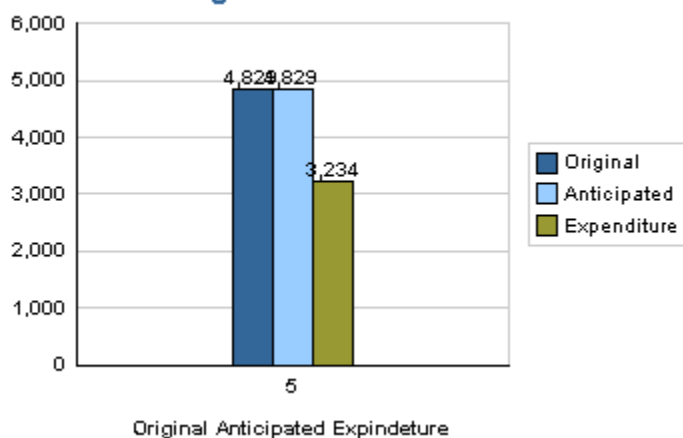

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	30
Number of Projects Delayed	20

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 30 projects are on schedule and 20 projects are delayed .1 project do not have fixed dates of commissioning.

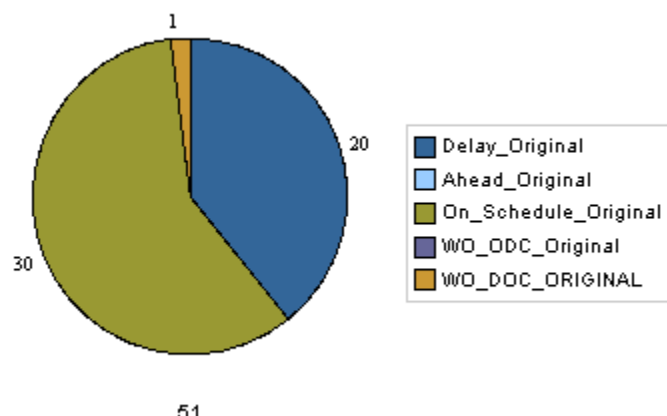

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37510.52 crore implying a cost overrun of 4%. The expenditure incurred on these projects till November, 2012 is Rs. 13273.49 crore, which is 35.4% of the revised cost of the projects.

Figures are in Rs. Crore

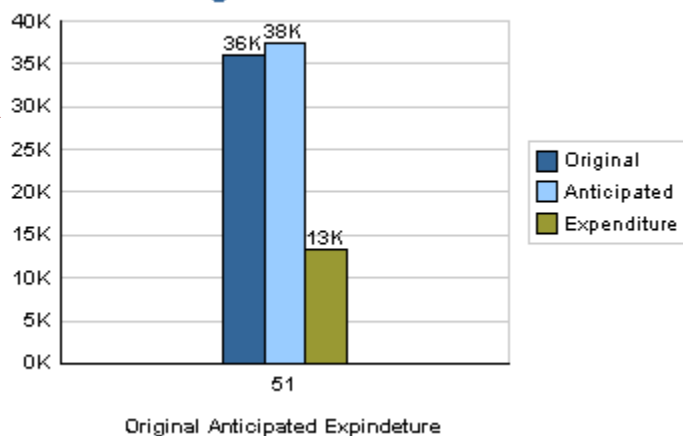

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	3
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 1 project are delayed .3 projects do not have fixed dates of commissioning.

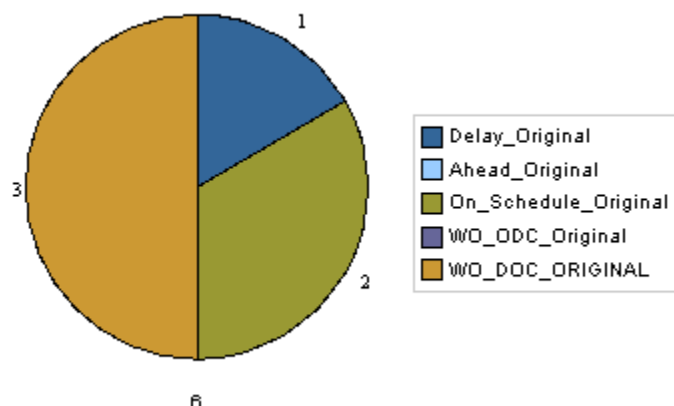

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 5549.7 crore implying a cost overrun of 1.4%. The expenditure incurred on these projects till November, 2012 is Rs. 2319.52 crore, which is 41.8% of the revised cost of the projects.

Figures are in Rs. Crore

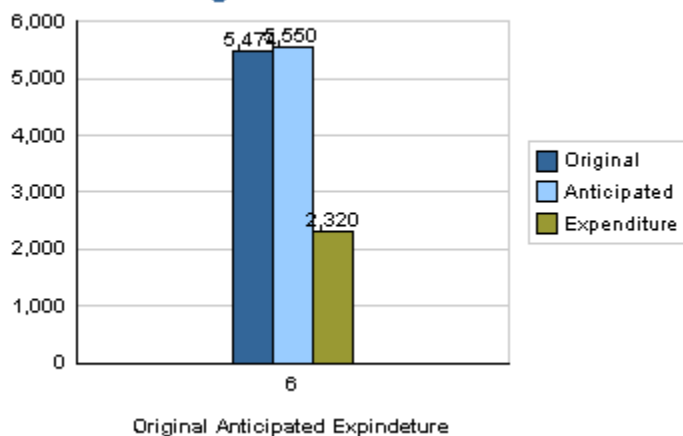

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

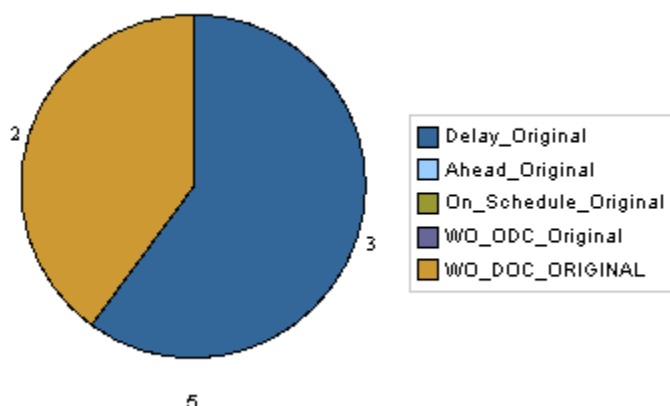

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till November, 2012 is Rs. 23455.84 crore, which is 49% of the revised cost of the projects.

Figures are in Rs. Crore

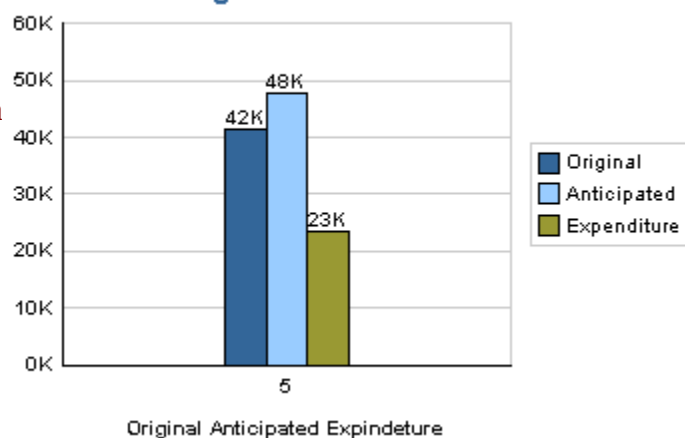

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	37	31485.25	39109.12	23580.54
2	Arunachal Pr.	4	9512.22	14153.62	8583.50
3	Assam	35	22260.93	33844.43	23362.71
4	Bihar	30	26901.24	34657.04	23148.66
5	Chhatisgarh	25	47047.84	48330.92	15288.66
6	Delhi	3	37985.00	37965.41	1239.97
7	Goa	1	335.61	204.73	0.00
8	Gujarat	22	31111.55	31313.49	9023.89
9	Haryana	10	5496.60	7439.09	7935.60
10	Himachal Pr.	5	13355.57	17246.69	12919.45
11	J and K	10	14926.96	34825.56	13857.75
12	Jharkhandd	23	14447.40	18428.98	8265.43
13	Karnataka	25	45300.83	54787.25	20809.59
14	Kerala	6	19694.67	21136.22	5081.19
15	Madhya pradesh	24	19741.92	19891.96	9390.35
16	Maharashtra	54	97399.54	113680.17	52917.42
17	Manipur	1	727.56	4444.00	937.59
18	Meghalaya	2	762.00	762.00	670.74
19	Mizoram	2	1532.97	3307.11	381.46
20	Multi State	104	142189.68	151656.17	66316.81
21	Nagaland	1	850.00	850.00	8.45
22	Orissa	31	57663.96	62099.12	34794.63
23	Punjab	7	4836.20	5777.97	4480.45
24	Rajasthan	14	26544.10	26138.31	9928.49
25	Sikkim	2	1648.94	3690.04	241.10
26	Tamil Nadu	32	51275.95	62055.82	39900.25
27	Tripura	3	1522.39	2053.23	992.04
28	Uttar Pradesh	23	18822.90	22659.67	11745.15
29	Uttaranchal	3	5619.21	6559.64	2021.40
30	West Bengal	27	42286.11	54501.80	25908.97
TOTAL		566	793285.10	933569.56	433732.24

LIST OF PROJECTS MORE THAN COST AS ON 01.12.2012

SN	PROJECT	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	Atomic Energy	09/2003	3492.00	0.00	3577.60
2	KUDANKULAM APP (NPCIL)	NPCIL	Atomic Energy	12/2001	13171.00	0.00	15161.00
3	RESITMENT OF MARKETING INSTALATION AT VISAKH	HPCL	Petroleum	01/2009	756.00	0.00	907.45
4	CHUTAK HYDRO-ELECTRIC PROJECT	NHPC	Power	08/2006	621.26	0.00	767.36
5	URI H.E.P STAGE -II (NHPC)	NHPC	Power	08/2005	1729.29	0.00	1843.25
6	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	NHPC	Power	10/2003	768.92	0.00	1622.90
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	NHPC	Power	09/2005	1061.38	0.00	1233.36
8	NIMOO BAZGO HYDROELECTRIC PROJECT	NHPC	Power	08/2006	611.01	0.00	807.36
9	KOLDAM HEP (NTPC)	NTPC	Power	10/2002	4527.15	0.00	4633.00
10	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	PGCIL	Power	07/2006	557.24	0.00	595.00
11	RAMPUR HEP(412 MW)	SJVNL	Power	01/2007	2047.03	0.00	2056.66
12	JIND-SONEPAT (NL),NR	(NR)	Railways	01/2004	190.81	238.56	437.79
13	REWARI-ROHTAK (NL),NR	(NR)	Railways	01/2004	149.38	330.23	503.47
14	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	(NR)	Railways	03/1995	2500.00	2500.00	8525.30
15	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	(NR)	Railways	07/1998	248.44	576.27	904.73
16	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	(NR)	Railways	03/2002	409.00	625.30	835.57
17	AMRAVATI-NARKHER NL(CR)	CR	Railways	06/1994	120.90	284.27	543.14
18	LANJHIGARH-JUNAGARH NL(ECOR)	ECOR	Railways	04/1993	100.00	142.98	206.16
19	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	Railways	04/1996	114.01	332.92	404.60
20	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	Railways	04/1997	233.00	501.69	662.52
21	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	MRTTP	Railways	04/2003	3125.20	4174.40	4334.00
22	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	MRTTP	Railways	03/2000	907.69	3156.32	3235.94
23	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	Railways	04/1999	108.00	214.09	250.82
24	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	NCR	Railways	04/1985	158.77	432.46	558.07
25	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	NEFR	Railways	09/1996	156.00	156.00	279.98
26	KATI HAR - JOGBANI (GC)(NEFR)	NEFR	Railways	09/2001	100.00	492.98	732.83
27	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	NEFR	Railways	04/1996	1676.31	1676.31	3195.95
28	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NEFR	Railways	04/2000	733.00	733.00	1298.65
29	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NEFR	Railways	01/2004	915.70	915.70	1476.55

SN	PROJECT	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDI TURE CUMM
30	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NEFR	Railways	12/2006	170.00	170.00	392.85
31	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NEFR	Railways	04/2003	727.56	727.53	937.59
32	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	NEFR	Railways	09/1997	1000.00	1500.00	2501.02
33	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	NER	Railways	03/2002	381.17	381.17	603.58
34	KANPUR-KASGANJ-MATHURA(GC),NER	NER	Railways	03/1997	395.00	1062.36	1389.02
35	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	Railways	04/1999	323.40	323.40	506.14
36	ELECTRIFICATION OF MORADABAD-ROZA	RE	Railways	12/2004	129.17	0.00	227.48
37	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	Railways	04/2003	136.62	0.00	236.81
38	RENIGUNTA-GUNTAKAL(RE)	RVNL	Railways	06/2000	168.34	0.00	358.98
39	RAJATGARH-BARANG(LD),ECOR	RVNL	Railways	04/1999	166.16	0.00	253.88
40	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	RVNL	Railways	04/2005	240.00	0.00	413.37
41	BILASPUR-URKURA (DL)	RVNL	Railways	04/1997	151.52	0.00	327.08
42	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	Railways	04/2000	133.41	207.00	218.22
43	NANDYAL-YERRAGUNTALA(NL),SCR	SCR	Railways	03/1996	155.74	429.49	634.24
44	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	Railways	12/1994	124.43	495.68	587.51
45	GADWAL - RAICHUR (NL), SCR	SCR	Railways	04/1998	92.63	228.09	261.02
46	RANCHI-LOHARDAGA(GC),SER	SER	Railways	04/1997	194.07	194.07	309.09
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	Railways	09/2006	343.17	343.17	564.99
48	CALICUT-MANGALORE (DL) (SR)	SR	Railways	02/1996	240.00	0.00	600.41
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	Railways	09/1995	100.00	100.00	521.61
50	KARUR-SALEM(NL),SR	SR	Railways	02/1997	155.55	155.00	751.86
51	KOTTUR-HARIHAR(NL),(SWR)	SWR	Railways	04/1995	65.94	302.23	334.77
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	Railways	02/1997	295.00	412.91	551.49
53	Armur to kadloor yellareddy	NHAI	Road Transport & Highways	02/2010	390.56	0.00	631.65
54	Hyderabad-yadgiri N.H no-202	NHAI	Road Transport & Highways	08/2010	388.00	0.00	537.91
55	DHARAMTUL TO SONAPUR (AS-19)	NHAI	Road Transport & Highways	12/2003	200.00	0.00	231.18
56	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	Road Transport & Highways	12/2003	217.61	0.00	225.26

SN	PROJECT	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	Hyderabad-Vijaywada Km. 40 to 221.50 Km	NHAI	Road Transport & Highways	04/2010	1740.00	0.00	1923.80
58	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	NHAI	Road Transport & Highways	05/2009	572.30	0.00	718.83
59	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	NHAI	Road Transport & Highways	12/2003	160.00	0.00	187.69
60	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	NHAI	Road Transport & Highways	12/2003	157.47	0.00	209.43
61	DAKOBA TO NAGAON (NH-36)(NHAI)	NHAI	Road Transport & Highways	12/2003	225.00	0.00	285.20
62	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	NHAI	Road Transport & Highways	12/2003	195.00	0.00	212.33
63	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	Road Transport & Highways	12/2003	237.80	0.00	253.69
64	NALBARI TO BIJNI (AS-8)	NHAI	Road Transport & Highways	12/2003	200.00	0.00	277.10
65	NAGAON TO DHARAMTUL (AS-2)	NHAI	Road Transport & Highways	12/2003	264.72	0.00	289.79
66	SONAPUR TO GUWAHTI (AS-3)	NHAI	Road Transport & Highways	12/2003	245.00	0.00	491.21
67	GUWAHATI TO NALBARI (AS-5)	NHAI	Road Transport & Highways	12/2003	198.16	0.00	211.16
68	NALBARI T BIJNI (AS-7)	NHAI	Road Transport & Highways	12/2003	208.00	0.00	270.92
69	Hungund-Surathkal and Mangalore-Knt/Kerala Border	NHAI	Road Transport & Highways	09/2010	946.00	0.00	1394.40

SN	PROJECT	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
70	KUNDUPUR-SURATHKAL & MANGLORE	NHAI	Road Transport & Highways	09/2010	671.00	0.00	737.54
71	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	Road Transport & Highways	04/2007	486.00	0.00	636.27
72	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	NHAI	Road Transport & Highways	05/2009	1108.00	0.00	3565.00
73	PANIPAT-ROHTAK	NHAI	Road Transport & Highways	04/2011	807.00	0.00	960.09
74	ROHTAK-BAWAL	NHAI	Road Transport & Highways	05/2011	650.00	0.00	768.75
75	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	Road Transport & Highways	12/2010	1008.50	0.00	1097.80
76	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	NHAI	Road Transport & Highways	12/2003	240.00	0.00	294.29
77	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	NHAI	Road Transport & Highways	12/2003	332.94	0.00	406.18
78	JHAJHARPUR TO DARBANGA (BR-7)	NHAI	Road Transport & Highways	12/2003	340.00	0.00	575.32
79	2 LANNING OF MOKAMA-MUNGER	NHAI	Road Transport & Highways	05/2011	351.54	0.00	390.56
80	HAPUR-GARH Mukteswar (Others) KM.58-93, NH-24	NHAI	Road Transport & Highways	03/2005	220.00	0.00	279.46
81	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	NHAI	Road Transport & Highways	12/2003	340.68	0.00	391.02
82	JHANSI TO LALITPUR, NH-25,26	NHAI	Road Transport & Highways	12/2003	355.06	0.00	499.80

SN	PROJECT	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
83	THANJAUR-TRICHY,NH-67(NHAI)	NHAI	Road Transport & Highways	03/2005	280.00	0.00	581.49
84	TRICHY - KORUR NH-67	NHAI	Road Transport & Highways	03/2005	516.00	0.00	760.07
85	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	NHAI	Road Transport & Highways	03/2005	941.00	0.00	1901.00
86	Chennai-Tada(Six lane)	NHAI	Road Transport & Highways	04/2009	353.37	0.00	379.97
87	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	Road Transport & Highways	12/2003	275.00	0.00	279.46
88	Kishangarh-Ajmer-Beawer	NHAI	Road Transport & Highways	11/2009	795.00	0.00	1055.70
89	Hazaribagh-Ranchi	NHAI	Road Transport & Highways	08/2010	625.07	0.00	876.51
90	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	NHAI	Road Transport & Highways	03/2005	190.00	0.00	260.19
91	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	NHAI	Road Transport & Highways	01/2008	464.00	0.00	535.62
92	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	Road Transport & Highways	12/2003	232.45	0.00	274.33
93	Gurgaon-Kotputli Km 42.70 to 54.4 Km	NHAI	Road Transport & Highways	04/2009	1673.70	0.00	2731.90
94	Surat- Dahisar(Six Lane) Km 263 to Km 502	NHAI	Road Transport & Highways	02/2009	1693.75	0.00	2675.10
95	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	NHAI	Road Transport & Highways	12/2003	221.82	0.00	294.04

SN	PROJECT	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
96	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	NHAI	Road Transport & Highways	04/2000	367.49	0.00	453.68
97	Jaipur-Tonk-Deoli	NHAI	Road Transport & Highways	06/2010	792.06	0.00	1553.70
98	JAIPUR-REENGUS	NHAI	Road Transport & Highways	08/2010	267.81	0.00	549.27
99	AMRITSAR-PATHANKOT	NHAI	Road Transport & Highways	05/2010	705.00	0.00	1163.70
100	GANJAM-ICCHAPURUM,NH-5(NHAI)	NHAI	Road Transport & Highways	04/2000	263.27	0.00	271.66
101	2-LANNING OF SHILONG BYPASS	NHAI	Road Transport & Highways	02/2011	226.00	0.00	256.79
102	NAGPUR-KONDHALI,NH-6(NHAI)	NHAI	Road Transport & Highways	03/2005	168.00	0.00	457.30
103	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	Road Transport & Highways	03/2005	940.00	0.00	1198.70
104	MP/Maharashtra Border-Dhula	NHAI	Road Transport & Highways	12/2009	835.00	0.00	1068.70
105	Pune-sholapur,pkg1	NHAI	Road Transport & Highways	11/2009	1110.00	0.00	1802.10
106	Talegaon-amravati	NHAI	Road Transport & Highways	11/2009	567.00	0.00	777.98
107	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	NHAI	Road Transport & Highways	12/2003	203.43	0.00	241.70
108	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	NHAI	Road Transport & Highways	12/2003	251.03	0.00	314.73

SN	PROJECT	AGENCY	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
109	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	NHAI	Road Transport & Highways	12/2003	229.91	0.00	275.64
110	GWALIOR BYPASS, NH-75,3	NHAI	Road Transport & Highways	12/2003	300.93	0.00	302.72
111	INDORE-DEWAS(NH-3)	NHAI	Road Transport & Highways	11/2010	325.00	0.00	387.71
112	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	NHAI	Road Transport & Highways	03/2005	557.00	0.00	930.92
113	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	Shipping & Ports	03/2007	245.67	298.17	326.08
114	Acquisition of Two nos. of 3060 DWT	SHIPP.	Shipping & Ports	04/2009	277.03	280.00	294.87
115	67.5 MW TG-5 AUX. SYSTEM EMERGENCY POWER REQUIREMENT EXP. UNIT	RINL	Steel	07/2007	230.00	0.00	253.31
116	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	Steel	10/2005	8692.00	0.00	9885.02
117	COKE OVEN BATTERY NO. 4 PHASE-II	RINL	Steel	08/2007	108.00	0.00	117.84

Sectorwise Summary of Project Without Original Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Petroleum	1	2,615.69	.00	2,615.69	1,970.91
Power	1	421.01	623.44	623.44	400.03
Railways	19	5,791.43	8,427.61	16,318.51	7,598.57
Road Transport & Highways	6	4,069.00	.00	4,069.00	3,513.64
Steel	3	1,657.88	.00	1,657.88	357.52
Grand total	30	14,555.01	9,051.05	25,284.52	13,840.67

List of project Without Original Date of Commissioning

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Steel</u>								
1	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	204.36	-	04/2013	-	13/19
2	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	141.86	-	11/2013	-	17/21
3	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33	187.33	11.30	-	12/2013	-	0/1
	Total		1,657.88	1,657.88	357.52				30/41
	<u>Petroleum</u>								
4	EURO-IV DHD T - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,970.91	-	12/2012	-	117/116
	Total		2,615.69	2,615.69	1,970.91				117/116
	<u>Power</u>								
5	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	400.03	-	07/2013	-	6/29
	Total		421.01	623.44	400.03				6/29
	<u>Railways</u>								
6	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	334.77	-	12/2012	-	0/0
7	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	564.99	-	12/2012	-	0/0
8	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	415.73	279.98	-	12/2012	-	0/0
9	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	551.49	-	01/2013	-	0/0
10	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.46	-	02/2013	-	0/0
11	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,820.00	174.97	-	03/2013	-	0/0
12	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	203.62	-	03/2013	-	0/0
13	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,389.02	-	03/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	99.56	- -	03/2013	-	0/0
15	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	775.39	- -	03/2013	-	0/6
16	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,995.25	239.07	- -	03/2013	-	0/0
17	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,476.55	- -	03/2013	-	0/0
18	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	137.87	- -	03/2013	-	0/0
19	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
20	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	506.14	- -	03/2014	-	0/1
21	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	146.32	- -	03/2014	-	0/0
22	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	114.85	- -	03/2014	-	0/0
23	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.39	- -	03/2015	-	0/0
24	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
Total			5,791.43 -	16,318.51	7,598.57				0/7
Road Transport & Highways									
25	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
26	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3
27	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	172.90	- -	04/2013	-	2/2
28	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	355.66	- -	06/2013	-	1/1
29	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	419.65	- -	10/2013	-	2/2
30	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	433.49	- -	12/2013	-	0/1
Total			4,069.00 -	4,069.00	3,513.64				10/12
Grand Total			14,555.01	25,284.52	13,840.67				163/205

Sectorwise Summary Without Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	2	4,598.29	.00	6,783.29	4,661.84
Civil Aviation	3	4,086.12	2,015.00	4,162.24	1,724.62
Coal	1	249.03	.00	249.03	49.02
Fertilisers	2	763.00	.00	763.00	425.03
Petroleum	8	8,488.80	2,568.00	7,690.80	3,884.59
Power	1	596.45	1,007.16	1,007.16	863.03
Railways	56	18,540.30	30,563.85	46,735.77	24,859.26
Shipping & Ports	8	5,539.70	2,149.77	6,452.96	2,429.43
Telecommunications	6	2,997.75	.00	2,934.67	111.64
Urban Development	1	114.18	173.08	173.08	0.00
Grand total	88	45,973.62	38,476.86	76,952.00	39,008.46

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00 -	09/2010 -	-
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 -	-
	Total		4,598.29 -		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI, West Bengal	08/2008	1,942.51 -	05/2011 -	-
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	-
	Total		4,086.12 -		
<u>Coal</u>					
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	-
	Total		249.03 -		
<u>Fertilisers</u>					
7	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012
8	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012
	Total		763.00 -		
<u>Petroleum</u>					
9	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	- 03/2012	08/2012
10	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	09/2011 09/2012	09/2012
11	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	09/2012 -	09/2012
12	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 -	09/2012
13	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	- -	10/2012
14	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
15	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	04/2012 -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
16	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 394.00	- 08/2011	-
	Total		8,488.80 -		
<u>Power</u>					
17	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		596.45 -		
<u>Railways</u>					
18	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
19	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
20	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
21	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
22	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
23	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRT, West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
24	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
25	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
26	REWARI-ROHTAK (NL), NR - [220100279]NR, Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
27	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
28	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
29	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
30	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhattisgarh	04/1997	151.52 -	- 03/2009	03/2011
31	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
32	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
33	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
34	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR, Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
35	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012
36	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
37	Dakshin-barasal-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
38	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
39	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
40	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
41	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
42	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
43	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
44	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
45	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012
46	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
47	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
48	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
49	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
50	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
51	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
52	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	-
53	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
54	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	02/2006 -	-
55	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
56	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	-
57	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
58	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
59	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
60	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	-
61	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
62	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
63	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
64	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
65	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79	-	-
			-	-	
66	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13	-	-
			727.13	-	
67	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56	-	-
			671.82	-	
68	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	-	-
			404.19	-	
69	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	-	-
			125.00	-	
70	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	-	-
			456.00	-	
71	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	-	-
			300.00	-	
72	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24	03/2012	-
			-	-	
73	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36	03/2011	-
			196.95	-	
	Total		18,540.30		
			-		
Shipping & Ports					
74	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	10/2008	10/2008
			1,571.60	-	
75	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	-	01/2009
			-	01/2009	
76	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	04/2009	02/2011
			298.17	11/2009	
77	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	03/2012	03/2012
			-	-	
78	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	06/2011	09/2012
			-	09/2012	
79	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	09/2012	10/2012
			-	10/2012	
80	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03	12/2011	10/2012
			280.00	10/2012	
81	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	10/2008	-
			-	11/2010	
	Total		5,539.70		
			-		
Telecommunications					
82	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	10/2009	03/2011
			-	-	
83	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	10/2007	-
			-	-	
84	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	03/2009	-
			-	-	
85	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	03/2010	-
			-	-	
86	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	02/2007	-
			-	12/2010	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
87	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	03/2010	-
	Total		2,997.75		
			-		
	<u>Urban Development</u>				
88	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	04/2009	-
	Total		173.08		
			114.18		
			-		
Grand Total			45,973.62		

List of Projects Ahead of Schedule

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Steel</u>						
1	Expansion of Rourkela Steel Plant - [N12000056	9/2008	11,812.00 11,812.00	11,812.00	8,173.33	11/2013 -	03/2013
	Total		11,812.00 -	11,812.00	8,173.33		
	<u>Railways</u>						
2	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	402.64	03/2014 -	03/2013
	Total		1,389.62 -	1,389.62	402.64		
	<u>Shipping & Ports</u>						
3	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 10/2013	10/2013
4	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060	2/2011	830.00 -	621.53	-	05/2013 -	03/2013
	Total		1,858.10 -	1,649.63	371.96		
	Grand Total		15,059.72	14,851.25	8,947.93		

List of Delay Project W.R.T. Original and Revised

(Nov,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,161.00	12/2008	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	2,169.00	12/2015	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,464.00	12/2016	03/2017	3	-
Total			36,950.00	41,049.00	18,794.00				
<u>Civil Aviation</u>									
4	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	188.47	01/2011 04/2013	04/2013	27	0
Total			309.46	309.46	188.47				
<u>Coal</u>									
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,522.47	06/2009	03/2013	45	-
6	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	143.61	03/2011	03/2013	24	-
7	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	106.03	03/2010	03/2014	48	-
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,578.69	03/2012	03/2014	24	-
9	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	100.19	03/2012	03/2014	24	-
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	117.70	03/2012	03/2014	24	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	39.31	03/2012	03/2014	24	-
12	Churi Benti UG - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.58	03/2011	03/2014	36	-
13	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87	179.87	60.74	03/2012	03/2014	24	-
14	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	106.67	03/2012	03/2014	24	-
15	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	430.95	03/2013 09/2012	07/2014	16	22
16	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.82	03/2011	03/2015	48	-
17	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	1.73	03/2012	03/2015	36	-
18	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	119.04	03/2010	03/2015	60	-
19	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63	453.63	81.72	12/2012	03/2015	27	-
20	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78	706.40	19.23	07/2012	03/2016	44	-
21	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.88	03/2014	03/2016	24	-
22	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24	-
23	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24	-
24	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	24.62	12/2015	08/2017	20	-
Total			17,557.60	19,431.18	7,488.98				

Fertilisers

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
25	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	982.00	01/2013 12/2012	03/2013	2	3
	Total		1,478.63 -	1,478.63	982.00				
<u>Steel</u>									
26	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,926.54	12/2011 -	12/2012	12	-
27	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,106.01	12/2011 -	12/2012	12	-
28	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	250.08	08/2010 -	12/2012	28	-
29	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	343.37	12/2011 03/2012	01/2013	13	10
30	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	253.31	02/2011 -	01/2013	23	-
31	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 -	12,291.00	9,885.02	10/2009 -	03/2013	41	-
32	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	117.84	10/2012 -	03/2013	5	-
33	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,222.04	12/2012 -	03/2013	3	-
34	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	221.95	05/2012 -	06/2013	13	-
35	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	7,038.48	03/2013 -	09/2013	6	-
	Total		50,973.89 -	57,131.43	36,364.64				

Petrochemicals

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	5,775.44	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	5,775.44				
Petroleum									
37	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	271.67	04/2011 -	11/2012	19	-
38	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,583.08	05/2010 05/2012	12/2012	31	7
39	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	748.84	04/2011 12/2011	12/2012	20	12
40	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,950.54	03/2012 08/2012	12/2012	9	4
41	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	586.34	12/2011 -	01/2013	13	-
42	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 312.00	312.00	273.34	01/2012 01/2012	01/2013	12	12
43	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	277.79	03/2006 03/2013	03/2013	84	0
44	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.54	05/2010 03/2013	03/2013	34	0
45	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,391.33	09/2011 03/2012	03/2013	18	12
46	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,165.42	06/2012 03/2013	03/2013	9	0
47	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	226.47	03/2012 -	03/2013	12	-

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
48	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24	22
49	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	165.66	08/2012 -	03/2013	7	-
50	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	9,540.15	01/2012 -	03/2013	14	-
51	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
52	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
53	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	96.08	03/2013 -	04/2013	1	-
54	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	556.60	03/2010 03/2012	05/2013	38	14
55	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34	12
56	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86	12
57	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,147.97	06/2012 -	06/2013	12	-
58	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	260.34	07/2012 07/2012	06/2013	11	11
59	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	322.92	01/2013 -	06/2013	5	-
60	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	636.50	07/2012 -	06/2013	11	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
61	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.37	09/2011 -	08/2013	23	-
62	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	19,099.00	11/2012 -	09/2013	10	-
63	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	4,258.26	09/2012 -	09/2013	12	-
64	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	47.51	09/2012 -	09/2013	12	-
65	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	66.34	11/2012 -	10/2013	11	-
66	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	10/2013	16	-
67	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
68	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,917.83	08/2010 03/2012	12/2013	40	21
69	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	27.13	08/2013 -	01/2014	5	-
70	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	634.47	03/2007 03/2014	03/2014	84	0
71	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,099.96	03/2013 -	03/2014	12	-
72	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	1,091.35	12/2012 12/2012	03/2014	15	15
73	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	559.68	03/2013 -	04/2014	13	-
74	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.49	10/2010 -	12/2014	50	-
75	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.54	01/2013 -	07/2015	30	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	0
76	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.00	03/2007 03/2017	03/2017	120	0
	Total		110,647.22	122,957.64	73,108.65				
			-						
	<u>Power</u>								
77	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.00	767.36	02/2011 10/2012	12/2012	22	2
78	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,170.10	07/2010 -	12/2012	29	-
79	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	333.83	07/2011 -	12/2012	17	-
80	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,075.40	06/2012 -	12/2012	6	-
81	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	128.58	06/2012 -	12/2012	6	-
82	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	167.30	04/2012 -	12/2012	8	-
83	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,138.40	02/2012 -	01/2013	11	-
84	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,622.90	03/2007 09/2012	02/2013	71	5
85	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013	37	-
86	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,110.90	12/2012 -	02/2013	2	-
87	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,081.00	1,843.25	11/2009 02/2013	03/2013	40	1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
88	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,842.31	09/2008 -	03/2013	54	-
89	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	866.00	10/2009 -	03/2013	41	-
90	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	807.36	08/2010 01/2013	03/2013	31	2
91	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	420.80	09/2010 -	03/2013	30	-
92	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,573.00	08/2012 -	03/2013	7	-
93	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,501.40	08/2012 -	03/2013	7	-
94	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,990.00	10/2012 -	03/2013	5	-
95	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	681.20	05/2012 -	03/2013	10	-
96	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	469.10	11/2012 -	03/2013	4	-
97	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	57.50	10/2012 -	03/2013	5	-
98	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,742.00	10/2012 -	05/2013	7	-
99	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,759.60	11/2012 -	06/2013	7	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	8
100	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,974.99	10/2010 01/2013	09/2013	35	8
101	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pr.	01/2007	2,047.03 -	2,047.03	2,056.66	01/2012 -	09/2013	20	-
102	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,091.50	10/2012 -	09/2013	11	-
103	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	154.10	11/2011 -	09/2013	22	-
104	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,987.20	08/2012 -	09/2013	13	-
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	614.60	04/2013 -	10/2013	6	-
106	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	58.40	01/2013 -	11/2013	10	-
107	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,233.36	09/2009 06/2013	12/2013	51	6
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	332.10	11/2011 -	12/2013	25	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	347.70	11/2011 -	12/2013	25	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	248.10	02/2012 -	12/2013	22	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
111	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	995.50	12/2012 -	12/2013	12	-
112	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	791.40	08/2012 -	12/2013	16	-
113	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	464.60	11/2012 -	03/2014	16	-
114	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	6,358.91	4,633.00	04/2009 -	09/2014	65	-
115	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Aruna chal Pr.	12/2008	573.99 -	573.99	410.24	08/2012 08/2013	09/2014	25	13
116	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,808.00	08/2013 -	09/2014	13	-
117	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,257.90	08/2013 -	09/2014	13	-
118	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,451.00	07/2011 -	11/2014	40	-
119	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizor am	01/2011	913.63 -	913.63	368.59	07/2014 -	02/2015	7	-
120	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranc hal	11/2006	2,978.48 -	2,978.48	1,613.00	03/2013 -	09/2015	30	-
121	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,614.00	12/2009 -	03/2016	75	-
122	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaran chal	08/2008	2,491.58 -	3,422.44	328.35	07/2014 -	05/2016	22	-
123	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	388.96	07/2010 02/2016	11/2016	76	9
124	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,751.05	01/2016 01/2016	11/2016	10	10

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Antici- pated Cost	Cumm. Expendi- ture	Original / Revised	Antici- pated		
1	2	3	4	5	6	7	8	9	
125	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,858.69	09/2010 08/2014	03/2017	78	31
126	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	2,034.59	05/2013 06/2016	03/2017	46	9
127	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,659.80	09/2009 07/2014	12/2017	99	41
Total			135,623.96 -	150,841.06	96,190.67				
<u>Railways</u>									
128	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	309.09	06/2004 -	12/2012	102	-
129	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	499.90	437.79	03/2012 03/2012	12/2012	9	9
130	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	881.70	03/2009 12/2012	12/2012	45	0
131	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,580.27	10/2007 12/2012	12/2012	62	0
132	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya Pradesh	09/2007	687.20 -	687.20	668.82	03/2010 -	12/2012	33	-
133	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	904.73	12/2012 01/2013	01/2013	1	0
134	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	662.52	03/2012 08/2012	02/2013	11	6
135	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	261.02	02/2011 02/2011	02/2013	24	24
136	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	452.22	12/2012 12/2012	02/2013	2	2
137	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	62.11	03/2012 -	02/2013	11	-
138	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
139	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	206.16	03/2002 -	03/2013	132	-	
140	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	633.10	12/2011 12/2011	03/2013	15	15	
141	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	256.66	03/2012 03/2012	03/2013	12	12	
142	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	276.82	03/2012 03/2013	03/2013	12	0	
143	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	404.60	03/2012 03/2013	03/2013	12	0	
144	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	111.83	03/2012 -	03/2013	12	-	
145	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013	50	50	
146	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013	49	49	
147	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	117.44	12/2011 11/2013	11/2013	23	0	
148	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	149.23	12/2012 -	12/2013	12	-	
149	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,195.95	03/2009 -	12/2013	57	-	
150	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	204.74	03/2004 12/2010	03/2014	120	39	
151	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,298.65	12/2008 -	03/2014	63	-	
152	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	175.20	06/2013 06/2013	03/2014	9	9	
153	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	409.29	03/2013 -	03/2014	12	-	

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
154	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	114.08	12/2012 -	03/2014	15	-	
155	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 325.00	819.40	170.80	03/2010 06/2014	06/2014	51	0	
156	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	171.83	03/2007 03/2007	03/2015	96	96	
157	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	732.83	12/2010 12/2010	03/2015	51	51	
158	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	12.87	04/2014 -	03/2015	11	-	
159	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.02	2,501.02	04/2008 03/2014	12/2015	92	21	
160	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	937.59	03/2011 03/2014	03/2016	60	24	
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	920.70	03/2014 03/2016	03/2016	24	0	
162	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	36.71	03/2014 03/2016	03/2016	24	0	
163	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	459.54	03/2005 12/2008	06/2016	135	90	
164	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	431.18	06/2005 07/2011	06/2016	132	59	
165	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	32.66	03/2016 -	06/2016	3	-	
166	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 2,500.00	20,000.00	8,525.30	03/2001 -	12/2017	201	-	
Total			25,689.14 -	68,484.67	29,734.42					

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
167	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	183.76	08/2004 07/2010	12/2012	100	29
168	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	187.79	08/2004 -	12/2012	100	-
169	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	148.22	04/2004 -	12/2012	104	-
170	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	12/2012	93	-
171	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	279.46	09/2007 -	12/2012	63	-
172	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	163.43	03/2008 -	12/2012	57	-
173	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	260.19	01/2009 -	12/2012	47	-
174	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	285.20	06/2008 -	12/2012	54	-
175	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	253.69	06/2008 -	12/2012	54	-
176	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	406.18	09/2008 -	12/2012	51	-
177	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	241.70	10/2008 -	12/2012	50	-
178	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	275.64	10/2008 -	12/2012	50	-
179	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	187.10	07/2008 -	12/2012	53	-
180	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	575.32	09/2008 -	12/2012	51	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
181	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	277.10	06/2008 -	12/2012	54	-
182	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	152.14	04/2008 -	12/2012	56	-
183	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	257.43	06/2011 06/2011	12/2012	18	18
184	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	294.04	11/2008 -	12/2012	49	-
185	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	211.16	04/2008 -	12/2012	56	-
186	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	270.92	04/2008 -	12/2012	56	-
187	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	12/2012	48	-
188	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	12/2012	42	-
189	GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	263.27	271.66	02/2004 -	12/2012	106	-
190	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	225.26	04/2010 -	12/2012	32	-
191	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93 -	300.93	302.72	10/2009 -	12/2012	38	-
192	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	274.33	09/2010 -	12/2012	27	-
193	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70 -	228.70	194.51	02/2004 -	12/2012	106	-
194	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	535.62	01/2011 -	12/2012	23	-
195	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	636.27	05/2010 -	12/2012	31	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
196	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	1,198.70	07/2012 -	12/2012	5	-
197	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	12/2012	6	-
198	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	795.00	1,055.70	05/2012 -	12/2012	7	-
199	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,731.90	10/2011 -	12/2012	14	-
200	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,675.10	08/2011 -	12/2012	16	-
201	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,923.80	10/2012 -	12/2012	2	-
202	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00 -	388.00	537.91	05/2012 -	12/2012	7	-
203	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	12/2012	10	-
204	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	250.39	279.46	10/2008 -	02/2013	52	-
205	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25	-
206	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	209.43	09/2007 -	03/2013	66	-
207	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	135.13	09/2008 -	03/2013	54	-
208	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	228.65	06/2005 -	03/2013	93	-
209	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	239.66	05/2008 -	03/2013	58	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
210	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.29	10/2008 -	03/2013	53	-
211	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	391.02	03/2008 -	03/2013	60	-
212	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	279.78	02/2009 03/2014	03/2013	49	-12
213	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	122.13	04/2009 -	03/2013	47	-
214	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	212.33	06/2008 -	03/2013	57	-
215	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	289.79	06/2008 -	03/2013	57	-
216	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60	-
217	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	148.90	06/2008 -	03/2013	57	-
218	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	187.69	05/2008 -	03/2013	58	-
219	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	231.18	06/2008 -	03/2013	57	-
220	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	499.80	09/2009 -	03/2013	42	-
221	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32	-
222	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,427.90	09/2012 -	03/2013	6	-
223	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	314.73	10/2008 -	06/2013	56	-

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
224	Chilkaluri-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	718.83	10/2011 -	06/2013	20	-	
225	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	1,163.70	11/2012 -	06/2013	7	-	
226	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	64.82	04/2009 -	07/2013	51	-	
227	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	97.61	11/2008 -	07/2013	56	-	
228	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	495.27	12/2009 -	07/2013	43	-	
229	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,565.00	11/2011 -	08/2013	21	-	
230	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-	
231	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	209.00	3.82	01/2013 -	10/2013	9	-	
232	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-	
233	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-	
234	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	193.45	33.97	11/2012 -	12/2013	13	-	
235	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	175.59	10/2008 -	01/2014	63	-	
236	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	24.44	11/2008 -	01/2014	62	-	
237	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	387.71	05/2013 -	02/2014	9	-	
238	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	190.08	09/2007 -	03/2014	78	-	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
239	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	379.97	10/2011 -	03/2014	29	-
240	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19	-
241	2 LANNING OF MOKAMAMUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	390.56	05/2013 -	03/2014	10	-
242	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	465.47	03/2013 -	03/2014	12	-
243	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014	79	-
244	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	67.36	07/2009 -	04/2014	57	-
245	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	262.23	02/2014 -	04/2014	2	-
246	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
247	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	34.69	09/2013 -	07/2014	10	-
248	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90 -	635.90	-	07/2012 -	07/2014	24	-
249	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60 -	263.17	233.77	06/2010 -	09/2014	51	-
250	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
251	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
252	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
253	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
Total			41,616.57	43,410.76	41,398.97				

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
Shipping & Ports									
254	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Mahara shtra	10/2007	359.44 -	359.44	358.78	04/2011 11/2012	11/2012	19	0
255	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
256	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
257	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,563.50	01/2012 09/2012	01/2013	12	4
258	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
259	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Mahara shtra	08/2010	612.72 627.64	627.64	294.84	12/2012 05/2013	05/2013	5	0
260	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87	0
261	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	904.13	12/2010 09/2012	10/2013	34	13
Total			7,878.26 -	9,456.68	5,451.18				
Telecommunications									
262	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	818.09	11/2010 -	12/2012	25	-
263	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72	11

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expendi- ture	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Antici- pated		
1	2	3	4	5	6	7	8	9	
264	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	03/2013	51	-
265	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	80.05	06/2009 -	03/2013	45	-
266	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	03/2013	48	-
267	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53	-
268	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	06/2013	32	15
Total			2,737.73 -	2,741.60	1,549.35				
<u>Urban Development</u>									
269	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21	-
Total			6,395.00 -	11,609.00	2,267.57				
<u>Water Resources</u>									
270	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-
Total			542.90 -	1,187.00	35.49				
Grand Total			443,860.97	539,008.11	319,329.83				

Sectorwise Summary On Schedule

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Civil Aviation	2	1,078.00	.00	1,078.00	406.43
Coal	30	18,249.83	.00	17,830.31	5,735.49
Fertilisers	2	2,587.03	.00	2,587.03	1,827.00
Petroleum	23	54,652.38	.00	54,418.98	5,139.73
Power	46	96,246.86	.00	96,246.86	11,908.80
Railways	12	13,108.19	654.51	17,730.65	2,053.67
Road Transport & Highways	53	48,368.93	.00	48,008.93	24,101.11
Shipping & Ports	1	966.46	.00	994.82	248.23
Steel	3	842.10	.00	842.10	12.12
Urban Development	2	37,736.00	.00	37,736.00	1,172.77
Grand total	174	273,835.78	654.51	277,473.68	52,605.35

List of On schedule Projects

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	373.07	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070	2/2011	452.00 -	452.00	33.36	03/2015 -	03/2015
	Total		1,078.00 -	1,078.00	406.43		
	<u>Coal</u>						
3	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093	6/2010	2,675.67 -	2,675.67	1,394.48	03/2014 -	03/2014
4	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094	12/2009	1,943.66 -	1,943.66	1,236.96	03/2014 -	03/2014
5	KRISHNASHILA (NCL) (4MTY) - [N06000007	6/2011	789.88 -	741.62	334.67	03/2013 -	03/2013
6	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	162.06	03/2015 03/2015	03/2015
7	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.35	03/2014 03/2014	03/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	117.19	03/2017 -	03/2017
9	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	71.33	03/2015 -	03/2015
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	92.53	03/2016 -	03/2016
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	204.77	03/2014 -	03/2014
12	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	29.06	03/2015 -	03/2015
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.63 -	479.63	112.88	03/2013 -	03/2013
14	RAJMAHAL OC EXP. - [N06000056	9/2009	153.82 -	153.82	24.39	03/2014 -	03/2014
15	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
16	CHURCHA UG - [N06000046	6/2008	462.35 -	462.35	264.15	03/2014 -	03/2014
17	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
18	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	44.23	03/2016 -	03/2016
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	39.81	03/2016 -	03/2016
20	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
21	Muraidih UG Turn-key Project - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
22	JALAGAM VENGALA RAO OCP - [N06000094	7/2011	447.06 -	447.06	-	03/2015 -	03/2015
23	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
24	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	1.51	03/2018 03/2018	03/2018
25	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
26	KARMA OCP - [N06000088	6/2009	162.46 -	162.46	30.89	03/2014 -	03/2014
27	Rajrappa RCE OCP - [N06000087	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016
28	Purnadih OCP - [N06000085	7/2008	210.98 -	210.98	87.89	03/2013 -	03/2013
29	KANIHA OCP, MCL, (10.0 Mty) - [N06000035	12/2007	457.77 -	457.77	112.76	03/2013 -	03/2013
30	JALLARAM SHAFT PROJECT - [N06000025	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
31	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	374.26	03/2016 03/2016	03/2016
32	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008	6/2008	1,188.31 -	1,188.31	675.53	03/2013 -	03/2013
	Total		18,249.83 -	17,830.31	5,735.49		
<u>Fertilisers</u>							
33	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJECT - [N08000004	1/2010	1,292.84 -	1,292.84	902.00	01/2013 -	01/2013
34	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJECT - [N08000005	1/2010	1,294.19 -	1,294.19	925.00	01/2013 -	01/2013
	Total		2,587.03 -	2,587.03	1,827.00		
<u>Petroleum</u>							
35	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	4/2008	825.00 -	1,827.00	611.55	04/2013 04/2013	04/2013
36	Development of WO-16 Cluster Fields - [N16000105	6/2010	2,523.00 -	2,523.00	359.20	01/2014 -	01/2014
37	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE [N16000149	8/2011	586.00 -	586.00	4.26	07/2015 -	07/2015
38	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	913.00	21.50	07/2015 -	07/2015
39	DABHOL BANGALORE PIPELINE PROJECT PHASE-II [N16000147	6/2009	486.00 -	486.00	34.88	09/2013 -	09/2013

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
41	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	26.42	05/2015 -	05/2015
42	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015
43	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	756.65	77.45	05/2013 -	05/2013
44	Ankleswar Redevelopment - [N16000122]	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014
45	Mehesana Redevelopment - [N16000121]	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
46	Ahmedabad Redevelopment - [N16000120]	11/2010	1,916.10 -	1,916.10	711.28	12/2014 -	12/2014
47	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	2,303.59	02/2014 -	02/2014
48	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]	11/2009	341.50 -	341.50	141.87	02/2013 -	02/2013
49	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	666.00	-	11/2015 -	11/2015
50	REWARI KANPUR PIPELINE PROJECT - [N16000145]	3/2012	1,210.64 -	1,210.64	-	03/2015 -	03/2015
51	Integrated Refinery Expansion Project - [N16000143]	1/1999	14,225.00 -	14,225.00	9.21	12/2015 -	12/2015
52	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014
53	IOR of B-173A Field - [N16000140]	1/2012	352.49 -	352.49	-	03/2014 -	03/2014
54	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	15.87	03/2014 -	03/2014
55	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	30.09	05/2014 -	05/2014
56	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
57	Wax Project - [N16000101]	6/2010	576.60 -	576.60	89.68	12/2013 -	12/2013
	Total		54,652.38 -	54,418.98	5,139.73		
<u>Power</u>							
58	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016
59	Transm System for development of Pooling strn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	337.00	01/2015 -	01/2015
60	Transmission system associated with krishnapatnam- Part-A - [N18000090]	12/2010	779.21 -	779.21	643.00	08/2013 -	08/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
61	Northern Region system strengthening scheme-XXII - [N18000091	12/2010	209.78 -	209.78	102.60	08/2013 -	08/2013
62	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX - [N18000088	10/2010	182.68 -	182.68	67.50	01/2013 -	01/2013
63	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	9/2010	2,074.86 -	2,074.86	746.80	03/2013 -	03/2013
64	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	735.60	08/2013 -	08/2013
65	Northern region system strengthening scheme XVI - [N18000094	7/2010	752.64 -	752.64	219.50	07/2013 -	07/2013
66	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	1,746.65	50.40	08/2014 -	08/2014
67	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	297.33	33.20	08/2014 -	08/2014
68	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	105.60	02/2014 -	02/2014
69	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2 - [N18000113	12/2011	2,422.66 -	2,422.66	104.10	08/2014 -	08/2014
70	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112	11/2011	2,127.51 -	2,127.51	281.10	07/2014 -	07/2014
71	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111	8/2011	1,637.34 -	1,637.34	337.40	08/2014 -	08/2014
72	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	67.40	06/2014 -	06/2014
73	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107	8/2011	1,391.97 -	1,391.97	577.30	12/2013 -	12/2013
74	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106	8/2011	425.51 -	425.51	136.60	10/2013 -	10/2013
75	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126	3/2012	206.44 -	206.44	33.70	06/2014 -	06/2014
76	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	261.10	06/2015 -	06/2015
77	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
78	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
79	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122	2/2012	1,927.16 -	1,927.16	42.80	10/2014 -	10/2014

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
80	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121	2/2012	324.33 -	324.33	2.20	08/2014 -	08/2014
81	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120	2/2012	1,310.85 -	1,310.85	115.90	02/2015 -	02/2015
82	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118	1/2012	259.28 -	259.28	35.50	01/2014 -	01/2014
83	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117	1/2012	1,422.85 -	1,422.85	126.70	01/2015 -	01/2015
84	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID [N18000137	9/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI [N18000136	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII [N18000135	9/2012	524.40 -	524.40	-	04/2015 -	04/2015
87	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	150.00	08/2015 -	08/2015
88	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	896.00	11/2016 -	11/2016
89	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	597.00	09/2016 -	09/2016
90	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	1,036.00	12/2016 -	12/2016
91	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID [N18000130	6/2012	1,263.26 -	1,263.26	53.40	11/2014 -	11/2014
92	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B [N18000129	2/2012	3,201.44 -	3,201.44	95.00	10/2014 -	10/2014
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV [N18000128	11/2011	723.63 -	723.63	54.00	11/2014 -	11/2014
94	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	901.77	72.90	08/2014 -	08/2014
95	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	311.40	12/2013 -	12/2013
96	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104	10/2011	558.26 -	558.26	74.50	11/2013 -	11/2013
97	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103	9/2011	1,940.13 -	1,940.13	407.40	09/2014 -	09/2014
98	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102	7/2011	181.93 -	181.93	53.80	07/2013 -	07/2013

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	492.70	05/2014 -	05/2014
100	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099	3/2011	1,585.12 -	1,585.12	550.10	11/2013 -	11/2013
101	Supplementary transmission associated with vellur TPS - [N18000097	8/2010	170.36 -	170.36	54.70	04/2013 -	04/2013
102	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096	3/2011	2,569.25 -	2,569.25	857.50	03/2014 -	03/2014
103	Transmission system for phase-I generation projects in orissa-part B - [N18000093	12/2010	2,743.19 -	2,743.19	989.40	12/2013 -	12/2013
	Total		96,246.86 -	96,246.86	11,908.80		
<u>Railways</u>							
104	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	4/1995	304.00 -	968.60	122.02	12/2012 -	12/2012
105	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	7/1996	653.84 654.51	1,302.12	608.97	06/2013 06/2013	06/2013
106	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29	75.05	02/2015 -	02/2015
107	SEVOK RANGPO, NEFR - [N22000102	4/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
108	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111	4/2010	2,619.02 -	2,913.51	198.56	03/2016 -	03/2016
109	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113	4/2008	653.19 -	653.46	206.41	03/2014 -	03/2014
110	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	4/2008	394.14 -	404.39	3.77	03/2013 -	03/2013
111	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124	4/2006	850.00 -	850.00	8.45	03/2015 -	03/2015
112	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114	4/2008	516.23 -	516.23	300.84	03/2014 -	03/2014
113	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112	4/2008	829.74 -	829.74	7.97	03/2015 -	03/2015
114	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	42.65	03/2016 -	03/2016
115	AGARTALA SABROOM, NL, NEFR - [N22000099	4/2008	813.34 -	1,141.75	426.35	03/2014 -	03/2014
	Total		13,108.19 -	17,730.65	2,053.67		
<u>Road Transport & Highways</u>							
116	Jaipur-Tonk-Deoli - [N24000135	6/2010	792.06 -	792.06	1,553.70	12/2012 -	12/2012

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
117	Hazaribagh-Ranchi - [N24000141	8/2010	625.07 -	625.07	876.51	01/2013 -	01/2013
118	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM [N24000145	11/2010	1,585.00 -	1,585.00	957.75	05/2013 -	05/2013
119	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	149.40	06/2014 -	06/2014
120	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
121	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	580.59	08/2013 -	08/2013
122	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	218.49	08/2013 -	08/2013
123	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	201.26	09/2013 -	09/2013
124	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	535.37	06/2014 -	06/2014
125	JAIPUR-REENGUS - [N24000198	8/2010	267.81 -	267.81	549.27	02/2013 -	02/2013
126	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	152.77	09/2014 -	09/2014
127	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
128	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	25.36	10/2014 -	10/2014
129	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	192.51	07/2014 -	07/2014
130	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	11.19	01/2014 -	01/2014
131	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	529.67	09/2014 -	09/2014
132	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	449.35	08/2013 -	08/2013
133	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.55	01/2014 -	01/2014
134	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	104.67	01/2014 -	01/2014
135	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	297.32	02/2014 -	02/2014
136	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	131.46	05/2014 -	05/2014
137	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
138	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
139	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	768.75	11/2013 -	11/2013
140	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	616.04	08/2013 -	08/2013

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013
142	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	588.91	02/2013 -	02/2013
143	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	1,035.70	03/2013 -	03/2013
144	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	976.72	08/2014 -	08/2014
145	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013
146	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	960.09	10/2014 -	10/2014
147	DEOLI-KOTA - [N24000148	1/2011	953.00 -	593.00	422.82	07/2013 -	07/2013
148	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	479.87	07/2013 -	07/2013
149	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014
150	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	426.20	03/2014 -	03/2014
151	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
152	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	692.68	03/2014 -	03/2014
153	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	256.79	02/2014 -	02/2014
154	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	413.95	01/2014 -	01/2014
155	SAMAIKHALI - GANDHIDHAM - [N24000179	9/2010	805.39 -	805.39	362.46	03/2013 -	03/2013
156	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
157	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	85.41	08/2013 -	08/2013
158	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	78.28	05/2013 -	05/2013
159	Kandla - Mundra port - [N24000175	1/2011	953.88 -	953.88	440.83	07/2013 -	07/2013
160	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
161	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.85	06/2013 -	06/2013
162	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013
163	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
164	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	710.17	08/2013 -	08/2013

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
165	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]	9/2010	852.00 -	852.00	743.61	03/2013 -	03/2013
166	Talegaon-amravati - [N24000140]	11/2009	567.00 -	567.00	777.98	11/2013 -	11/2013
167	Indore-Jhabua-Gujrat/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
168	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139]	9/2010	1,655.00 -	1,655.00	456.32	09/2013 -	09/2013
	Total		48,368.93 -	48,008.93	24,101.11		
<u>Shipping & Ports</u>							
169	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
	Total		966.46 -	994.82	248.23		
<u>Steel</u>							
170	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]	11/2011	254.55 -	254.55	11.86	11/2013 -	11/2013
171	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078]	7/2012	332.65 -	332.65	-	08/2014 -	08/2014
172	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]	1/2012	254.90 -	254.90	0.26	12/2014 -	12/2014
	Total		842.10 -	842.10	12.12		
<u>Urban Development</u>							
173	DELHI MRTS PHASE-III - [N28000056]	9/2011	35,242.00 -	35,242.00	1,057.48	03/2016 -	03/2016
174	FARIDABAD EXTENSION - [N28000057]	9/2011	2,494.00 -	2,494.00	115.29	09/2014 -	09/2014
	Total		37,736.00 -	37,736.00	1,172.77		
	Grand Total		273,835.78	277,473.68	52,605.35		

Sectorwise Summary of Project Without Milestone

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	1	1,106.29	.00	1,106.29	1,084.24
Civil Aviation	6	5,473.58	2,015.00	5,549.70	2,319.52
Coal	6	3,868.49	1,666.38	3,657.55	234.27
Fertilisers	3	1,088.00	.00	1,088.00	425.03
Petroleum	50	109,028.36	41,267.50	120,530.74	40,194.89
Power	19	52,439.39	.00	53,291.20	8,492.51
Railways	125	63,915.28	67,424.97	148,879.33	63,367.03
Road Transport & Highways	139	89,789.00	.00	91,223.19	65,242.65
Shipping & Ports	18	16,087.68	9,708.64	18,300.73	8,500.80
Steel	2	587.55	.00	587.55	0.26
Telecommunications	13	5,735.48	1,318.73	5,676.27	1,660.99
Urban Development	3	37,850.18	173.08	37,909.08	1,172.77
Water Resources	1	542.90	.00	1,187.00	35.49
Grand total	386	387,512.18	123,574.30	488,986.63	192,730.45

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	-	0/0
			-	-		
	Total		1,106.29			0/0
			-			
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012	0/0
			2,015.00	02/2012		
3	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011	04/2013	0/0
			-	04/2013		
4	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013	0/0
			-	-		
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	03/2015	03/2015	0/0
			-	-		
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011	-	0/0
			-	-		
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	05/2012	-	0/0
			-	-		
	Total		5,473.58			0/0
			-			
<u>Coal</u>						
8	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	03/2014	03/2014	0/0
			-	-		
9	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	04/2014	04/2014	0/0
			-	-		
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04	03/2015	03/2015	0/0
			535.10	03/2015		
11	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	04/2015	04/2015	0/0
			-	-		
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	03/2016	03/2016	0/0
			-	-		
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	03/2018	03/2018	0/0
			1,131.28	03/2018		
	Total		3,868.49			0/0
			-			
<u>Fertilisers</u>						
14	DUMMY PROJECT FOR FERTILISERS - [N08000002]RCF,Multi State	04/2007	325.00	11/2009	10/2011	0/0
			-	-		
15	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	07/2011	04/2012	0/0
			-	-		
16	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	07/2011	07/2012	0/0
			-	-		
	Total		1,088.00			0/0
			-			

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Steel</u>					
17	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh - [N12000078]SAIL, Delhi	07/2012	332.65 -	08/2014 -	08/2014	0/0
18	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]SAIL, Delhi	01/2012	254.90 -	12/2014 -	12/2014	0/0
	Total		587.55 -			0/0
	<u>Petroleum</u>					
19	Construction of tanks and blending facility at Vad - [N16000115]IOCL, Gujarat	02/2009	267.00 -	09/2012 -	09/2012	0/0
20	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	04/2011 -	11/2012	0/0
21	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	12/2012	0/0
22	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
23	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
24	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	03/2013	0/0
25	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	03/2011 05/2011	03/2013	0/0
26	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	08/2012 -	03/2013	0/0
27	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
28	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
29	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
30	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
31	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
32	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
33	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
34	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	09/2011 -	08/2013	0/0
36	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
37	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
38	DBPL-II - [N16000147]GAIL, Multi State	06/2009	486.00 -	09/2013 -	09/2013	0/0
39	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	06/2012	10/2013	0/0
			-	-		
41	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	03/2013	11/2013	0/0
			-	-		
42	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	08/2010	12/2013	0/0
			5,633.44	03/2012		
43	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	12/2013	12/2013	0/0
			-	-		
44	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	01/2014	01/2014	0/0
			-	-		
45	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	08/2013	01/2014	0/0
			-	-		
46	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	02/2014	02/2014	0/0
			-	-		
47	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	03/2013	03/2014	0/0
			-	-		
48	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00	03/2014	03/2014	0/0
			-	-		
49	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49	03/2014	03/2014	0/0
			-	-		
50	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	03/2013	04/2014	0/0
			5,916.65	-		
51	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17	05/2014	05/2014	0/0
			-	-		
52	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	05/2014	05/2014	0/0
			-	-		
53	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	10/2010	12/2014	0/0
			-	-		
54	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	12/2014	12/2014	0/0
			-	-		
55	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	12/2014	12/2014	0/0
			-	-		
56	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17	12/2014	12/2014	0/0
			-	-		
57	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00	12/2014	12/2014	0/0
			-	-		
58	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	03/2015	03/2015	0/0
			-	-		
59	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	03/2012	1,210.64	03/2015	03/2015	0/0
			-	-		
60	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	04/2015	04/2015	0/0
			-	-		
61	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40	05/2015	05/2015	0/0
			-	-		
62	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	01/2013	07/2015	0/0
			-	-		
63	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00	07/2015	07/2015	0/0
			-	-		
64	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00	07/2015	07/2015	0/0
			-	-		
65	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00	11/2015	11/2015	0/0
			-	-		

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
66	I REP - [N16000143]BPCL,Kerala	01/1999	14,225.00	12/2015	12/2015	0/0
			-	-		
67	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00	-	-	0/0
			-	-		
68	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	04/2012	-	0/0
			-	-		
	Total		109,028.36			0/0
			-			
Power						
69	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	12/2012	0/0
			-	-		
70	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	07/2013	07/2013	0/0
			-	-		
71	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	10/2010	09/2013	0/0
			-	01/2013		
72	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	01/2012	09/2013	0/0
			-	-		
73	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	09/2009	12/2013	0/0
			-	06/2013		
74	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	03/2014	03/2014	0/0
			-	-		
75	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	08/2014	08/2014	0/0
			-	-		
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	09/2014	09/2014	0/0
			-	-		
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63	11/2014	11/2014	0/0
			-	-		
78	SYSTEM STRENGTHENING-XXVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	11/2014	11/2014	0/0
			-	-		
79	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	12/2014	12/2014	0/0
			-	-		
80	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	02/2015	02/2015	0/0
			-	-		
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34	03/2015	03/2015	0/0
			-	-		
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40	04/2015	04/2015	0/0
			-	-		
83	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40	08/2015	08/2015	0/0
			-	-		
84	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	06/2016	06/2016	0/0
			-	-		
85	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47	09/2016	09/2016	0/0
			-	-		
86	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18	11/2016	11/2016	0/0
			-	-		
87	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19	12/2016	12/2016	0/0
			-	-		
	Total		52,439.39			0/0
			-			

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Railways</u>						
88	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
89	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
90	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
91	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
92	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
93	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
94	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
95	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
96	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
97	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
98	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
99	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
100	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
101	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
102	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
103	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
104	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
105	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
106	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
107	Dakshin-barasa-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
108	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
109	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
110	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
111	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
112	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
113	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
114	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
115	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012	0/0
116	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
117	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
118	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
119	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	12/2012	0/0
120	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
121	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
122	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
123	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2012	0/0
124	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2012	0/0
125	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
126	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
127	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	- -	12/2012	0/0
128	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
129	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0
130	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	02/2013	0/0
131	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
132	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
133	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
134	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
135	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
136	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2013	0/0
137	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
138	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	03/2013	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
139	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
140	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
141	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2013	0/0
142	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
143	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2013	0/0
144	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
145	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2013	0/0
146	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
147	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
148	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	03/2013	0/0
149	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
150	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
151	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
152	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
153	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2013	06/2013	0/0
154	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
155	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
156	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
157	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2013	0/0
158	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
159	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
160	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
161	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
162	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2014	0/0
163	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	03/2014	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
164	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
165	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
166	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
167	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2014	0/0
168	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 325.00	03/2010 06/2014	06/2014	0/0
169	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	02/2015	0/0
170	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
171	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
172	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
173	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	04/2014 -	03/2015	0/0
174	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
175	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
176	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2015	0/0
177	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
178	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
179	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2016	0/0
180	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
181	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
182	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
183	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
184	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
185	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
186	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
187	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
188	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
189	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
190	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
191	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	-	0/0
192	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-	0/0
193	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	02/2006 -	-	0/0
194	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
195	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	-	0/0
196	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
197	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
198	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
199	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	-	0/0
200	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
201	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
202	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
203	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
204	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
205	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
206	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
207	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
208	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
209	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
210	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
211	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
212	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
Total			63,915.28 -			0/0
Road Transport & Highways						
213	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	12/2012	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
214	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	08/2004	12/2012	0/0
215	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	04/2004	12/2012	0/0
216	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	03/2005	12/2012	0/0
217	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	09/2007	12/2012	0/0
218	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	03/2008	12/2012	0/0
219	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	01/2009	12/2012	0/0
220	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	06/2008	12/2012	0/0
221	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	06/2008	12/2012	0/0
222	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	09/2008	12/2012	0/0
223	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	10/2008	12/2012	0/0
224	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	10/2008	12/2012	0/0
225	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	07/2008	12/2012	0/0
226	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	09/2008	12/2012	0/0
227	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	06/2008	12/2012	0/0
228	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	04/2008	12/2012	0/0
229	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	11/2008	12/2012	0/0
230	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	04/2008	12/2012	0/0
231	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	04/2008	12/2012	0/0
232	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	12/2008	12/2012	0/0
233	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	06/2009	12/2012	0/0
234	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	02/2004	12/2012	0/0
235	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	04/2010	12/2012	0/0
236	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	10/2009	12/2012	0/0
237	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	09/2010	12/2012	0/0
238	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	02/2004	12/2012	0/0
239	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	01/2011	12/2012	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
240	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	05/2010	12/2012	0/0
241	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	07/2012	12/2012	0/0
242	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	06/2012	12/2012	0/0
243	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	05/2012	12/2012	0/0
244	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	10/2011	12/2012	0/0
245	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	08/2011	12/2012	0/0
246	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	10/2012	12/2012	0/0
247	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	12/2012	12/2012	0/0
248	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	05/2012	12/2012	0/0
249	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	02/2012	12/2012	0/0
250	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07	01/2013	01/2013	0/0
251	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	10/2008	02/2013	0/0
252	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	01/2011	02/2013	0/0
253	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	02/2013	02/2013	0/0
254	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	02/2013	02/2013	0/0
255	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	09/2007	03/2013	0/0
256	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	09/2008	03/2013	0/0
257	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	06/2005	03/2013	0/0
258	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	05/2008	03/2013	0/0
259	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	10/2008	03/2013	0/0
260	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	03/2008	03/2013	0/0
261	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	02/2009 03/2014	03/2013	0/0
262	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	04/2009	03/2013	0/0
263	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	06/2008	03/2013	0/0
264	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	06/2008	03/2013	0/0
265	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	03/2008	03/2013	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
266	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	06/2008	03/2013	0/0
267	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	05/2008	03/2013	0/0
268	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	06/2008	03/2013	0/0
269	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	09/2009	03/2013	0/0
270	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	07/2010	03/2013	0/0
271	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	09/2012	03/2013	0/0
272	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	03/2013	03/2013	0/0
273	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	03/2013	03/2013	0/0
274	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	03/2013	03/2013	0/0
275	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	04/2013	04/2013	0/0
276	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	05/2013	05/2013	0/0
277	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	05/2013	05/2013	0/0
278	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	10/2008	06/2013	0/0
279	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	10/2011	06/2013	0/0
280	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	11/2012	06/2013	0/0
281	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	06/2013	06/2013	0/0
282	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	06/2013	06/2013	0/0
283	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	06/2013	06/2013	0/0
284	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	04/2009	07/2013	0/0
285	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	11/2008	07/2013	0/0
286	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	12/2009	07/2013	0/0
287	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	07/2013	07/2013	0/0
288	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	07/2013	07/2013	0/0
289	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	07/2013	07/2013	0/0
290	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	11/2011	08/2013	0/0
291	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	08/2013	08/2013	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
292	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
293	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	08/2013	08/2013	0/0
294	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	08/2013	08/2013	0/0
295	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
296	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	08/2013	08/2013	0/0
297	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	08/2013	08/2013	0/0
298	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
299	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
300	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	05/2012	10/2013	0/0
301	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
302	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	01/2013	10/2013	0/0
303	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
304	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
305	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
306	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
307	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	02/2010	12/2013	0/0
308	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	06/2011	12/2013	0/0
309	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	11/2012	12/2013	0/0
310	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
311	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
312	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	10/2008	01/2014	0/0
313	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	11/2008	01/2014	0/0
314	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	01/2014	01/2014	0/0
315	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	01/2014	01/2014	0/0
316	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00	01/2014	01/2014	0/0
317	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36	01/2014	01/2014	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
318	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00	05/2013	02/2014	0/0
319	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00	02/2014	02/2014	0/0
320	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00	02/2014	02/2014	0/0
321	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	09/2007	03/2014	0/0
322	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	10/2011	03/2014	0/0
323	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	08/2012	03/2014	0/0
324	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	05/2013	03/2014	0/0
325	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, Multi State	09/2011	2,848.00	03/2014	03/2014	0/0
326	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	03/2014	03/2014	0/0
327	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00	03/2013	03/2014	0/0
328	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	09/2007	04/2014	0/0
329	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	07/2009	04/2014	0/0
330	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00	02/2014	04/2014	0/0
331	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09	04/2014	04/2014	0/0
332	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00	05/2014	05/2014	0/0
333	2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar	12/2011	325.00	05/2014	05/2014	0/0
334	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Orissa	11/2011	909.00	05/2014	05/2014	0/0
335	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76	07/2013	06/2014	0/0
336	SNG toBANL - [N24000189]NHAI, J and K	06/2011	1,100.70	06/2014	06/2014	0/0
337	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, Rajasthan	12/2011	2,388.00	06/2014	06/2014	0/0
338	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI, Multi State	12/2011	1,047.00	06/2014	06/2014	0/0
339	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	09/2013	07/2014	0/0
340	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90	07/2012	07/2014	0/0
341	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, West Bengal	02/2012	702.16	07/2014	07/2014	0/0
342	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	08/2014	08/2014	0/0
343	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	06/2010	09/2014	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
344	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	09/2009	09/2014	0/0
345	PANIKHOLI-RIMOLI - [N24000197]NHAI, Orissa	03/2012	1,410.00	09/2014	09/2014	0/0
346	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, West Bengal	04/2012	1,396.18	09/2014	09/2014	0/0
347	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	10/2014	10/2014	0/0
348	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19	10/2014	10/2014	0/0
349	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	02/2010	12/2014	0/0
350	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	06/2015	05/2016	0/0
351	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00	07/2015	06/2016	0/0
	Total		89,789.00			0/0
Shipping & Ports						
352	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST, Maharashtra	10/2005	800.00	10/2008	10/2008	0/0
353	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67	04/2009	02/2011	0/0
354	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat	06/2010	277.00	03/2012	03/2012	0/0
355	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP., Maharashtra	04/2009	290.85	06/2011	09/2012	0/0
356	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP., Maharashtra	08/2008	1,066.91	09/2012	10/2012	0/0
357	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP., Maharashtra	04/2009	277.03	12/2011	10/2012	0/0
358	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	04/2011	11/2012	0/0
359	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh	02/2010	444.10	06/2010	11/2012	0/0
360	Construction of berthing and allied facilities off - [N25000037]PORT TRUST, Gujarat	04/2005	882.00	02/2011	12/2012	0/0
361	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00	01/2012	01/2013	0/0
362	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat	12/2005	702.00	03/2011	03/2013	0/0
363	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST, Gujarat	02/2011	830.00	05/2013	03/2013	0/0
364	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP., Maharashtra	08/2010	612.72	12/2012	05/2013	0/0
365	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00	03/2006	06/2013	0/0
366	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00	12/2010	10/2013	0/0
367	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP., Maharashtra	10/2010	1,028.10	12/2013	10/2013	0/0

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
368	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	02/2014	02/2014	0/0
			-	-		
369	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	10/2008	-	0/0
			-	11/2010		
	Total		16,087.68			0/0
			-			
Telecommunications						
370	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	10/2009	03/2011	0/0
			-	-		
371	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	11/2010	12/2012	0/0
			930.60	-		
372	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	02/2007	02/2013	0/0
			229.41	03/2012		
373	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	12/2008	03/2013	0/0
			-	-		
374	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15	06/2009	03/2013	0/0
			158.72	-		
375	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13	03/2009	03/2013	0/0
			-	-		
376	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	01/2009	06/2013	0/0
			-	-		
377	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	10/2010	06/2013	0/0
			-	03/2012		
378	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	10/2007	-	0/0
			-	-		
379	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	03/2009	-	0/0
			-	-		
380	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	03/2010	-	0/0
			-	-		
381	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	02/2007	-	0/0
			-	12/2010		
382	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	03/2010	-	0/0
			-	-		
	Total		5,735.48			0/0
			-			
Urban Development						
383	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	09/2014	09/2014	0/0
			-	-		
384	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	03/2016	03/2016	0/0
			-	-		
385	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	04/2009	-	0/0
			173.08	-		
	Total		37,850.18			0/0
			-			
Water Resources						
386	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	12/2007	12/2012	0/0
			-	-		

List of Projects Without Milestones

(Nov,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		542.90			0/0
			-			
	Grand Total		387,512.18			0/0

List of ongoing projects having cost overrun w.r.to original

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apxenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	17,270.00	15,161.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	5,677.00	3,577.60	09/2010 -	-
	Total		16,663.00 -	22,947.00	18,738.60		
	<u>Civil Aviation</u>						
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) [N04000038	08/2008	1,808.00 -	2,015.00	1,724.62	01/2011 -	02/2012
	Total		1,808.00 -	24,962.00	20,463.22		
	<u>Coal</u>						
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087	10/2004	2,030.78 -	3,027.59	2,522.47	06/2009 -	03/2013
5	MAGADH OC (CCL) - [N06000015	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
6	ADRIYALA SHAFT PROJECT - [N06000016	12/2009	212.34 -	977.53	430.95	03/2013 -	07/2014
7	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	117.19	03/2017 -	03/2017
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047	05/2008	4,904.54 -	4,909.54	3,578.69	03/2012 -	03/2014
9	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	204.77	03/2014 -	03/2014
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	92.53	03/2016 -	03/2016
	Total		8,579.45 -	35,593.25	27,429.05		
	<u>Petrochemicals</u>						
11	Assam gas Cracker project - [N16000106	04/2006	5,460.61 -	8,920.00	5,775.44	04/2012 -	12/2013
	Total		5,460.61 -	44,513.25	33,204.49		
	<u>Petroleum</u>						
12	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	663.69	634.47	03/2007 -	03/2014
13	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.00	03/2007 -	03/2017

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	277.79	03/2006 -	03/2013
15	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
16	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
17	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,583.08	05/2010 -	12/2012
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	3,917.83	08/2010 03/2012	12/2013
20	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,084.54	05/2010 -	03/2013
21	RESITMENT OF MARKETING INSTALATION AT VISAKH [N16000057	01/2009	756.00 -	898.00	907.45	- -	08/2012
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	19,099.00	11/2012 -	09/2013
23	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI [N16000066	01/2008	224.00 -	394.00	365.36	- -	-
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	273.34	01/2012 -	01/2013
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	611.55	04/2013 -	04/2013
26	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
27	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	559.68	03/2013 -	04/2014
	Total		54,263.98 -	117,939.40	81,315.90		
Power							
28	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,659.80	09/2009 -	12/2017
29	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,633.00	04/2009 -	09/2014
30	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,858.69	09/2010 -	03/2017
31	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,622.90	03/2007 -	02/2013
32	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,614.00	12/2009 -	03/2016
33	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,233.36	09/2009 -	12/2013
34	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	863.03	12/2007 -	-

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,974.99	10/2010 -	09/2013
36	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,843.25	11/2009 -	03/2013
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,842.31	09/2008 -	03/2013
38	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	807.36	08/2010 -	03/2013
39	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	767.36	02/2011 -	12/2012
40	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	388.96	07/2010 -	11/2016
41	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013
42	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,751.05	01/2016 -	11/2016
43	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	328.35	07/2014 -	05/2016
44	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,573.00	08/2012 -	03/2013
45	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.32	333.83	07/2011 -	12/2012
46	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	400.03	- -	07/2013
	Total		46,019.35 -	179,788.99	122,406.17		
<u>Railways</u>							
47	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007	04/1985	158.77 274.56	540.96	558.07	03/1994 -	12/2011
48	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
49	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	174.00	- 03/2010	-
50	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	587.51	- -	03/2012
51	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	548.95	543.14	06/1999 -	03/2011
52	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,525.30	03/2001 -	12/2017
53	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	242.39	- -	03/2015
54	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	206.16	03/2002 -	03/2013
55	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	122.02	12/2012 -	12/2012
56	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	600.41	- -	02/2012

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	204.74	03/2004 -	03/2014
58	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	633.10	12/2011 12/2010	03/2013
59	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	174.97	- -	03/2013
60	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	551.49	- -	01/2013
61	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	203.62	- -	03/2013
62	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
63	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	352.10	07/2012 -	-
64	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	256.66	03/2012 -	03/2013
65	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	712.00	751.86	- -	10/2012
66	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	634.24	02/2009 -	03/2012
67	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	70.22	- -	-
68	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,577.46	1,389.02	- -	03/2013
69	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	3,230.02	2,501.02	04/2008 12/2011	12/2015
70	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	141.45	- -	03/2012
71	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	171.83	03/2007 03/2007	03/2015
72	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	334.77	- -	12/2012
73	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	309.09	06/2004 -	12/2012
74	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.35	07/2008 -	07/2008
75	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,336.45	07/2005 -	-
76	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	324.06	05/2008 -	03/2011
77	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	07/1996	653.84 654.51	1,302.12	608.97	06/2013 -	06/2013
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	662.52	03/2012 -	02/2013
79	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	904.73	12/2012 -	01/2013
80	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	227.42	250.82	12/2009 -	03/2011

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	732.83	12/2010 -	03/2015
82	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,214.00	96.96	- -	-
83	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	320.09	- 05/2009	05/2009
84	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	603.58	- -	03/2012
85	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	506.14	- -	03/2014
86	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	99.56	- -	03/2013
87	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	835.57	06/2007 -	06/2007
88	RENIGUNTA-GUNTAKAL(RE) - [220100260	06/2000	168.34 -	370.00	358.98	04/2003 03/2010	-
89	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	548.96	521.61	- -	-
90	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.00	775.39	- -	03/2013
91	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
92	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,298.65	12/2008 -	03/2014
93	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,235.94	12/2006 -	08/2010
94	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	261.02	02/2011 -	02/2013
95	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	566.80	- 12/2009	02/2012
96	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	452.22	12/2012 12/2012	02/2013
97	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.29	- -	-
98	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	459.54	03/2005 12/2008	06/2016
99	REWARI-ROHTAK (NL),NR - [220100279	01/2004	149.38 -	602.78	503.47	02/2010 -	02/2011
100	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	499.90	437.79	03/2012 -	12/2012
101	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	239.07	- -	03/2013
102	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	735.10	221.60	- 09/2009	-
103	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013
104	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	937.59	03/2011 -	03/2016

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	276.82	03/2012 -	03/2013
106	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	440.16	- -	03/2010
107	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	881.70	03/2009 -	12/2012
108	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,580.27	10/2007 -	12/2012
109	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	84.24	- -	-
110	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	224.49	- -	-
111	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	1,717.29	1,476.55	- -	03/2013
112	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	327.08	- 03/2009	03/2011
113	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	174.95	03/1998 08/2005	08/2005
114	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
115	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	75.05	02/2015 -	02/2015
116	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013
117	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	137.87	- -	03/2013
118	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	236.81	12/2007 03/2010	12/2010
119	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	404.60	03/2012 -	03/2013
120	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027	04/2005	240.00 -	355.00	413.37	03/2009 12/2009	03/2011
121	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.60	0.76	- -	-
122	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	62.07	02/2006 -	-
123	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	448.67	03/2008 06/2008	-
124	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU [N22000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
125	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
126	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	228.77	03/2010 -	03/2012
127	PANSPURA-KHARAGPUR 3D LINE - [N22000076	09/2007	252.50 -	529.23	243.77	02/2010 -	-

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
128	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	900.00	301.11	- -	-
129	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N22000080]	09/2006	343.17 -	900.00	564.99	- -	12/2012
130	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	453.04	392.85	03/2011 -	03/2011
131	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	415.73	279.98	- -	12/2012
132	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	227.40	40.30	- -	-
133	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	582.83	137.04	- -	-
134	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	200.00 -	385.20	114.85	- -	03/2014
135	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	39.45	- -	-
136	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	819.40	170.80	03/2010 -	06/2014
137	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	208.26	12/2010 -	03/2011
138	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,501.80	4,334.00	06/2011 -	03/2012
139	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012
140	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,086.41	431.18	06/2005 -	06/2016
141	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	426.35	03/2014 -	03/2014
142	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	12.87	04/2014 -	03/2015
143	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
144	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
145	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	409.29	03/2013 -	03/2014
146	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) [N22000109]	04/2010	2,069.60 -	2,298.42	36.71	03/2014 -	03/2016
147	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51	198.56	03/2016 -	03/2016
148	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46	206.41	03/2014 -	03/2014
149	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	93.16	12/2011 -	02/2012
150	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	117.44	12/2011 -	11/2013

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
151	Pandabeswar-Chinpai doubling (ER) - [N22000118	04/2004	225.68 -	293.74	132.87	12/2010 -	12/2010
152	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	04/2008	394.14 -	404.39	3.77	03/2013 -	03/2013
153	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123	04/2008	318.24 -	468.62	1.00	03/2012 -	-
154	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125	04/2006	117.36 196.95	196.95	193.55	03/2011 -	-
155	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project [N22000127	04/1996	1,676.31 -	4,255.37	3,195.95	03/2009 -	12/2013
	Total		45,490.37 -	311,466.53	183,295.12		
Road Transport & Highways							
156	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	148.22	04/2004 -	12/2012
157	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221	12/2003	155.00 -	201.66	135.13	09/2008 -	03/2013
158	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.43	03/2008 -	12/2012
159	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	239.66	05/2008 -	03/2013
160	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	64.82	04/2009 -	07/2013
161	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	97.61	11/2008 -	07/2013
162	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014
163	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	67.36	07/2009 -	04/2014
164	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
165	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	190.08	09/2007 -	03/2014
166	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,565.00	11/2011 -	08/2013
	Total		3,324.28 -	316,911.73	188,173.87		
Shipping & Ports							
167	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,571.60	5.75	10/2008 -	10/2008
168	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
169	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	1,460.00	904.13	12/2010 -	10/2013

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
170	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013
171	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
172	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039]	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
173	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]	04/2009	290.85 -	305.00	194.14	06/2011 -	09/2012
174	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	3,563.50	01/2012 -	01/2013
175	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]	08/2010	612.72 -	627.64	294.84	12/2012 -	05/2013
176	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
177	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	326.08	04/2009 -	02/2011
	Total		9,532.54 -	329,062.87	194,040.47		
<u>Steel</u>							
178	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	9,885.02	10/2009 -	03/2013
179	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	343.37	12/2011 06/2010	01/2013
180	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	117.84	10/2012 -	03/2013
181	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	13,926.54	12/2011 -	12/2012
182	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	230.00 -	343.58	253.31	02/2011 -	01/2013
183	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	350.00	250.08	08/2010 -	12/2012
	Total		24,028.89 -	359,279.30	218,816.63		
<u>Telecommunications</u>							
184	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013
185	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle [N26000090]	11/2009	916.70 -	930.60	818.09	11/2010 -	12/2012
	Total		1,065.85 -	360,368.62	219,714.77		

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Urban Development</u>						
186	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013
187	C/o office building for IDBI at bandra Kurla Complex, Mumbai [N28000048	11/2006	114.18 173.08	173.08	-	04/2009 -	-
	Total		6,509.18 -	372,150.70	221,982.34		
	<u>Water Resources</u>						
188	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012
	Total		542.90 -	373,337.70	222,017.83		
	Grand Total		223,288.40	2,848,321. 34	1,751,598.46		

List of ongoing projects having time and cost overrun w.r.to original

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL)	12/2001	13,171.00	17,270.00	15,161.00	12/2008	03/2013
	- [020100040		-			-	
	Total		13,171.00	17,270.00	15,161.00		
			-				
	<u>Coal</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2,030.78	3,027.59	2,522.47	06/2009	03/2013
	- [060100087		-			-	
3	MAGADH OC (CCL)	08/2008	469.78	706.40	19.23	07/2012	03/2016
	- [N06000015		-			-	
4	ADRIYALA SHAFT PROJECT	12/2009	212.34	977.53	430.95	03/2013	07/2014
	- [N06000016		-			-	
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4,904.54	4,909.54	3,578.69	03/2012	03/2014
	- [N06000047		-			-	
	Total		7,617.44	26,891.06	21,712.34		
			-				
	<u>Petrochemicals</u>						
6	Assam gas Cracker project	04/2006	5,460.61	8,920.00	5,775.44	04/2012	12/2013
	- [N16000106		-			-	
	Total		5,460.61	35,811.06	27,487.78		
			-				
	<u>Petroleum</u>						
7	IOR LAKWA - LAKHMANI (ONGCL)	09/2001	345.10	663.69	634.47	03/2007	03/2014
	- [160100215		-			-	
8	IOR GELEKI (ONGCL)	09/2001	390.09	1,674.11	1,556.00	03/2007	03/2017
	- [160100216		-			-	
9	IOR, RUDRASAGAR (ONGCL)	09/2001	113.90	438.85	277.79	03/2006	03/2013
	- [160100217		-			-	
10	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	2,735.65	2,184.00	04/2006	06/2013
	- [160100231		-			-	
11	DEVELOPMENT OF C-SERIES FIELDS	08/2006	3,195.16	3,690.37	2,520.91	12/2008	04/2013
	- [N16000023		-			-	
12	CONSTRUCTION OF NEW PROCESS COMPLEX MHN	01/2007	2,853.29	6,326.40	5,583.08	05/2010	12/2012
	- [N16000030		-			-	
13	DEVELOPMENT OF B-22 CLUSTER FIELDS	01/2007	2,323.40	2,920.82	1,858.42	09/2010	04/2013
	- [N16000032		-			03/2012	
14	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3,248.78	5,633.44	3,917.83	08/2010	12/2013
	- [N16000033		-			03/2012	
15	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	10/2007	5,713.03	8,813.41	7,084.54	05/2010	03/2013
	- [N16000039		-			-	
16	PARADIP REFINERY PROJECT	02/2009	29,777.00	30,426.00	19,099.00	11/2012	09/2013
	- [N16000058		-			-	

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
17	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070]	07/2009	238.68 -	312.00	273.34	01/2012 -	01/2013
18	North Tapti Gas Field Development - [N16000096]	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
19	Development of Cluster-7 Fields - [N16000104]	03/2010	3,241.03 -	5,916.65	559.68	03/2013 -	04/2014
	Total		52,458.98 -	106,118.21	73,714.83		
Power							
20	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	3,659.80	09/2009 -	12/2017
21	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,358.91	4,633.00	04/2009 -	09/2014
22	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	5,858.69	09/2010 -	03/2017
23	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222]	10/2003	768.92 -	1,628.00	1,622.90	03/2007 -	02/2013
24	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	7,614.00	12/2009 -	03/2016
25	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	1,233.36	09/2009 -	12/2013
26	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	1,974.99	10/2010 -	09/2013
27	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	1,843.25	11/2009 -	03/2013
28	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	1,842.31	09/2008 -	03/2013
29	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	807.36	08/2010 -	03/2013
30	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26 -	913.00	767.36	02/2011 -	12/2012
31	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	388.96	07/2010 -	11/2016
32	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018]	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013
33	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	1,751.05	01/2016 -	11/2016
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,422.44	328.35	07/2014 -	05/2016
35	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	4,573.00	08/2012 -	03/2013
36	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37 -	386.32	333.83	07/2011 -	12/2012
	Total		45,001.89 -	166,337.20	113,542.04		

(Nov,2012)


Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Railways</u>						
37	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
38	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,525.30	03/2001 -	12/2017
39	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	206.16	03/2002 -	03/2013
40	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	204.74	03/2004 -	03/2014
41	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	633.10	12/2011 12/2010	03/2013
42	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	256.66	03/2012 -	03/2013
43	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	3,230.02	2,501.02	04/2008 12/2011	12/2015
44	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	171.83	03/2007 03/2007	03/2015
45	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	309.09	06/2004 -	12/2012
46	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	662.52	03/2012 -	02/2013
47	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	904.73	12/2012 -	01/2013
48	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	732.83	12/2010 -	03/2015
49	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,298.65	12/2008 -	03/2014
50	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	261.02	02/2011 -	02/2013
51	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	452.22	12/2012 12/2012	02/2013
52	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	459.54	03/2005 12/2008	06/2016
53	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	499.90	437.79	03/2012 -	12/2012
54	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	937.59	03/2011 -	03/2016
56	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	276.82	03/2012 -	03/2013
57	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	881.70	03/2009 -	12/2012
58	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,580.27	10/2007 -	12/2012
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	404.60	03/2012 -	03/2013

(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
61	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	819.40	170.80	03/2010 -	06/2014
62	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,086.41	431.18	06/2005 -	06/2016
63	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	12.87	04/2014 -	03/2015
64	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	409.29	03/2013 -	03/2014
65	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109	04/2010	2,069.60 -	2,298.42	36.71	03/2014 -	03/2016
66	Ghutiasharif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	117.44	12/2011 -	11/2013
67	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	4,255.37	3,195.95	03/2009 -	12/2013
	Total		15,602.29 -	224,739.91	141,041.83		
<u>Road Transport & Highways</u>							
68	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	148.22	04/2004 -	12/2012
69	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	135.13	09/2008 -	03/2013
70	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.43	03/2008 -	12/2012
71	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	239.66	05/2008 -	03/2013
72	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	64.82	04/2009 -	07/2013
73	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	97.61	11/2008 -	07/2013
74	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014
75	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	67.36	07/2009 -	04/2014
76	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
77	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	190.08	09/2007 -	03/2014
78	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,565.00	11/2011 -	08/2013
	Total		3,324.28 -	230,185.11	145,920.58		
<u>Shipping & Ports</u>							
79	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	904.13	12/2010 -	10/2013



Date of

Water Resources



(Nov,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
94	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012
	Total		542.90 -	282,940.00	178,990.34		
	Grand Total		181,743.85	2,150,082. 48	1,400,014.99		

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
