

**300th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
October, 2010**



PUMP SLAB

HPCL – Mumbai Refinery



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-9
List of Delete Projects	10-10
Summary of Projects	11-21
Sector wise Trend and Graphicalf Analysis	22-31
Sector wise analysis of projects	32-61
Graph	67-71
List of All Ongoing Projects	72-72
List of Abbreviations	73-74

EXECUTIVE SUMMARY

The 300th Flash Report for October' 2010, that contains information on the status of 559 projects in the Central Sector, each costing ` 150 Crores and above. Since April' 2010, Flash report is prepared for the central sector projects costing `150 Crores and above. During October' 2010, 9 projects reported completion and have been dropped from the monitor of this Ministry. 12 projects have been added during the month under reference..

The online submission of the implementation Status Report of the ongoing projects has significantly improved as in October, 2010 nearly 85% projects reported online. Out of 559 ongoing projects on the monitor of this Ministry, 474 projects were updated either by the concerned project agencies online or the data has been entered locally by the staff of this Ministry. Sector-wise number of ongoing projects along with status of online reporting is given below:

S. No.	Sector	Projects on monitor	Reported Online	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	124	124	51
2.	RAILWAYS	128	64	4
3.	POWER	88	83	20
4.	PETROLEUM	71	68	16
5.	COAL	44	44	6
6.	TELECOMMUNICATION	44	44	6
7.	STEEL	16	13	6
8.	SHIPPING & PORTS	21	18	-
9.	CIVIL AVIATION	9	9	-
10.	FERTILISERS	6	3	4
11.	ATOMIC ENERGY	4	2	1
12.	URBAN DEVELOPMENT	2	1	1
13.	MINES	1	1	-
15.	WATER RESOURCES	1	-	-
Total		559	474	115

2. One hundred fifteen (115) projects have reported additional delays compared to the completion dates in the previous month. During October' 2010, two projects in Road Transport and Highways sector have shown considerable improvement over the completion schedule reported earlier.

3. The additional delays are in the range of 1 to 36 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Tele communications, Fertilizers and Urban Development Sectors.

4. Out of 559 projects, 14 projects are ahead of schedule, 117 are on schedule and 293 projects are delayed. Of the balance, 80 projects do not have fixed dates of commissioning i.e. either the year of commissioning or the tentative gestation period of the projects have been reported. A large number of projects (55) were sanctioned without any commissioning schedule/date.

5. The total original cost of implementation of 559 projects ` 578217.92 Crores and their anticipated completion cost is ` 698067.04 Crores implying a cost overrun of 20.70%. The expenditure incurred on these projects till October, 2010 is ` 300519.72 Crores which is 43.10% of the revised cost of the projects.

6. To present a concise picture of the status of on-going projects costing ₹ 150 Crores and above, a pictorial presentation is given in the report. Out of 559 projects, presently on the monitor at the end of October 2010, 117 projects were on schedule (20%), excluding 80 projects without date of commissioning and those have not reported during the month, 293 projects were delayed (52%). During the month, 115 projects have reported additional delays in the range of 1-36 months. The analysis of pictorial presentation shows that since July, 2010 the marginal decrease in projects reporting delays have been noticed. The overall cost overrun has somewhat constant since July 2010. It may be seen that out of 293 delayed projects, at the end of October, 2010, 76 projects had overall delay in the range of 1 to 12 months, 80 projects had delay in the range of 13 to 24 months, 109 projects had delay in the range of 25 to 60 months and 28 projects had time overrun of 61 months and above.

7. In the **Coal sector**, 6 projects have reported additional delays in the range of 1-27 months. Adriyala Shaft Project SCCL have reported considerable improvement of 2 months over the completion schedule reported earlier. Barsingsar TPS has reported additional delay of 1 month due to slow progress by the contractor. Bhubaneswari OCP has reported additional delay of 12 months due to delay in environment clearances. Gevera Expansion OCP (SECL) has reported additional delay of 24 months due to delay in finalization of tender process. Kakatiya Longowall SCCL has reported addition delay of 27 months due to delay in acquisition of private land. TPS-II Expansion, NLC has reported additional delay of 4 months, however, no specific reason has been given by the project authority.

8. In the **Steel Sector**, 6 projects have reported additional delay of 1-6 months. Installation of 700 TPD Oxygen Plant, Rourkela, 67.5 MW TG-5 Aux. STEM Emergency Power Requirement RINL and Simultaneous Blowing of BOF Converter of SMS-II have reported additional delays of 1 month, 2 months and 1 month respectively due to delay in supply of equipment. Rebuilding of Coke Oven Battery No. 1 & 2 and Rebuilding of Coke Oven Battery No - 6 have reported additional delay of 3 months each due to delay in supply of fireclay bricks. Expansion of IISCO Steel Plant SAIL has reported additional delay of 6 months due to delay in supply of equipments.

9. In the **Petroleum Sector**, 16 projects have reported additional delays in the range of 1-6 months. Installation of FCCV at Mumbai refinery has reported improvement of 1 month due to non availability of raw material. MSQ Improvement project (IOCL) has reported additional delay of 5 months due to delay in installation and drilling work by the contractor. MSQ Upgradation Project at Guwahati Refinery and MSQ Upgradation Project at Digboi Refinery have reported additional delay of 1 month each due to poor response to consultancy bids,

frequent bands and insufficient transportation of material/equipment. MSQ Upgradation Project at Barauni Refinery has reported additional delay of 1 month due to backing out of reputed PSU consultants in last moment and slow progress by M/S BHEL in power plant. BNPL Spurline (Uttaranchal & Punjab) project has reported additional delay of 1 month due to slow progress because of problems in North East. Diesel Hydro Treatment Project, BRPL Dhauligaon project has reported addition delay of 2 months due to local constraints like scares technical resources in this region. Sultanpur Neemrana Pipe Line Project has reported additional delay of 2 months; however, no specific reason has been given by the project authority. Compressor Stations (Vijaypur and Jhabua) Phase-1 project has report additional delay of 6 months due to delay in supply of equipments & bad weather. Expansion of Panipat Refinery from 12 to 15 MMTPA IOCL, North Tapti Gas Field Dev. ONGC project, C2-C3 and LPG Recovery from LNG, Dahej (ONGC), Refrigerated LPG Storage at JNPT BPCL, Integrated Offshore crude Oil handling facilities at Paradip and Additional Development of D-1 Field ONGC projects have reported additional delays of 6 months, however no specific reasons have been given by the project authorities.

10. In the **Power Sector**, 20 projects have reported additional delays in the range of 1-18 months over the completion schedule reported earlier. Transmission System Associated with Barh Generation Project, Power Grid Corporation of India Ltd has reported additional delay of 3 months to match the requirement of linked Generation project. BARH STPP, 3x660 MW has reported additional delay of 5 months due to continued delay in supply of material by M/s Power Machine, Russia. Chamera Hydro Electric Project Stage III (NHPC) has reported additional delay of 8 months due to violence among contractor's laborers and court stay on crushing Plant leading to huge shortage of aggregate for concrete work. Nimoo Bazo Hydro Electric Project has reported additional delay of 9 months due to highly inclement weather condition, delay in award of E&M works due to poor participation, delay in HM works due to abnormal high price bid and retendering thereof. Western Region Transmission Strengthening Scheme has reported additional delay of 1 month to match with the linked generation project. KORBA STPP Stage-III has reported additional delay of 1 month, due to slow progress of work and delay in supply of equipments. Western Region Strengthening Scheme VI have reported additional delay of 4 months due to severe ROW problems. Northern Region System Strengthening-IX PGCIL and Northern Region System Strengthening-X PGCIL and Northern Region System Strengthening-XI PGCIL projects have reported additional delays of 1 month each, however, no specific reasons have been given by the project authorities. Eastern Region Strengthening Scheme -1 PGCIL project has reported additional delay of 3 months due to ROW problems in Jharkhand and West Bengal and forest clearance awaited for Orissa. Parbati HEP Stage-II (NHPC) project has reported additional delay of 6 months due to delay in award of E&M package on account of delay in receipt of decision from Govt. of India regarding participation of Chinese companies. Chutak Hydro Electric Project (NHPC) has reported additional delay of 6 months due to delay in civil disturbance in Kashmir Valley and indefinite bandhs /strikes. Bongaigaon Thermal Power Project (NTPC) has report additional delay of 7 months due to slow progress by civil agency. URI HEP Stage-II (NHPC) has reported additional delay of 8 months due to civil disturbance in Kashmir Valley further deteriorated in September, 2010. Lower Subansiri HEP (NHPC) has reported additional delay of 12 months due to damaged bridge at NH-52, anti dam activities and delay in signing of MOU by State Government. Koteswar HEP (THDC) has reported additional delay of 15 months, however, no specific reason has been given by the project authority. Parbati HEP (NHPC) Stage-II has reported additional delay of 16 months due to widening of HPPWD roads. Rampur HEP (412 MW) SJVNL has reported additional delay of 18 months, however no specific reasons have been given by the project authorities.

11. In the **Road Transport and Highways Sector**, 51 projects (Table VIII may be referred) have reported additional delay in the range of 1-36 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, utility shifting, Termination of contracts due to poor performance and delay in getting the forest clearance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such additional delays.

12. In the **Fertilizer Sector**, 4 projects (Table VIII may be referred) have reported additional delay in the range of 2-8 months. However, the project authorities have not mentioned any specific reason for such additional delays.

13. In the **Railway Sector**, 4 projects have shown additional delays in the range of 1-13 months. Muzaffarpur-Sitamarhi (NL) has reported additional delay of 1 month. Deoghar – Dumka New BG Line (Double) has reported additional delay of 3 months. Pratapnagar-Chota Udaipur (GC) and Talcher-Bimlagarh (NL) has reported additional delays of 7 months and 13 months respectively, however, the project authorities have not mentioned any specific reason for such additional delays.

14. In the **Atomic Energy Sector, Kudankulam APP (NPCIL)** project has reported additional delay of 6 months due to delay in supply/erection of equipment.

15. In the **Telecommunication Sector**, 6 projects have shown additional delays of 1 – 3 months. GSM equipment of 975000 Lines (2G) 325000 Line (3G) BSNL has reported additional delay of 1 month due to delay in acquisition of site/land. GSM Equipment of 1625 K Lines (2G) & 325 K Lines in M BSNL has reported additional delay of 2 months due to installation by M/s ALTL. GSM Equipment of 900000 Lines (2G) Punjab Phase V.2 BSNL has reported additional delay of 2 months due to (W&P). GSM Equipment of 1900000 Lines (2G) 335500 lines (3G) BSNL has reported additional delay of 2 months due to vendor's/ site acquisition. GSM Equipment of 1867000 Lines (2G) 38300 lines (3G) BSNL has reported additional delay of 3 months due to delay in supply of equipment by ALTL/ITT. GSM Equipment of 1700000 Lines (2G) 234100 lines (3G) BSNL has reported additional delay of 3 months due to slow progress by the contractor and delay in supply of equipment.

16. In the **Urban Development Sector**, Delhi MRTS Phase-II Project has reported additional delay of 1 month due to delay in releasing of funds.

Status as on 01.10.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the Report.

(Pankaj Jain)

**Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation**

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	128	4
2	Road Transport & Highways	124	51
3	Power	88	20
4	Petroleum	71	16
5	Coal	44	6
6	Telecommunications	44	6
7	Shipping & Ports	21	0
8	Steel	16	6
9	Civil Aviation	9	0
10	Fertilisers	6	4
11	Atomic Energy	4	1
12	Urban Development	2	1
13	Mines	1	0
14	Water Resources	1	0
	Total	559	115

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	168.33	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93
September,2010				
<u>Coal</u>				
8	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)(NEYVELI LIGNITE CORPORATION) - [060100090]	254.07	06/2009	1,687.78
<u>Steel</u>				
9	REBUILDING OF COKE OVEN BATTERY-10(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000016]	416.50	09/2009	305.14
<u>Petroleum</u>				
10	PANIPAT NAPHTHA CRACKER PROJECT(INDIAN OIL CORPORATION LIMITED) - [160100292]	12,138.00	09/2009	12,054.37

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	DADRI- PANIPAT R-LNG SPUR PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000018]	250.66	06/2008	350.96
12	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000026]	638.90	04/2009	796.21
13	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE(INDIAN OIL CORPORATION LIMITED) - [N16000034]	348.00	12/2009	186.58
14	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000035]	1,131.00	12/2009	750.71
15	CHAINSA-JHAJJAR PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000047]	967.77	09/2009	416.90
16	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000067]	643.46	-	726.45
17	Construction of Tank and Blending Facility at Vadi(INDIAN OIL CORPORATION LIMITED) - [N16000075]	267.00	-	72.99
18	BINA DESPATCH TERMINAL(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000078]	490.71	12/2009	590.52
<u>Railways</u>				
19	HOSPET-GUNTAKAL(LD),SCR(RAIL VIKAS NIGAM LTD.) - [220100195]	105.22	12/1999	283.49
20	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100224]	536.85	03/2003	1,005.50
21	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)(RAIL VIKAS NIGAM LTD.) - [220100244]	223.00	-	586.85
22	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000033]	352.00	03/2008	616.44
23	ABOHAR- FAZILKA, NR, NL(NEW LINE) - [N22000055]	86.44	03/2009	201.79
<u>Road Transport & Highways</u>				
24	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100203]	440.93	12/2006	641.40
25	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100204]	534.39	05/2007	716.15
26	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101178]	372.40	07/2004	406.05
27	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101181]	467.93	03/2005	453.64
28	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101187]	399.75	03/2005	424.96
29	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106227]	276.00	04/2008	360.00
30	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106228]	310.00	04/2008	392.26
31	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106241]	507.49	03/2008	342.80
32	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106257]	556.00	03/2009	568.50
33	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106273]	469.80	12/2008	665.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
34	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106285]	261.00	08/2008	286.30
35	TOVARAMKURCHI-MADURAI, NH45B (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000054]	263.00	08/2008	317.74
36	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000060]	402.80	03/2009	453.70
37	PADALUR-TRICHY, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000083]	320.00	05/2009	636.10
38	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000093]	360.42	11/2009	478.40
39	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000105]	450.00	07/2008	876.61
40	ISLAM NAGAR TO KADTAL(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000109]	546.83	03/2010	667.80
41	WAINGANGA BRIDGE -CHHATISGARH-MAHARASHTRA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000120]	424.00	09/2010	298.40
<u>Shipping & Ports</u>				
42	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS(SHIPPING crp. of india) - [N25000013]	411.32	03/2010	406.28
43	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA(PORT TRUST) - [N25000046]	2,118.00	11/2004	.00
<u>Telecommunications</u>				
44	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I(DEPARTMENT OF TELECOMMUNICATION) - [260100051]	279.97	12/2004	136.24
45	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA(BHARAT SANCHAR NIGAM LIMITED) - [260100095]	1,174.75	03/2006	371.41
46	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000026]	741.77	10/2007	151.37
47	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-(BHARAT SANCHAR NIGAM LIMITED) - [N26000028]	364.52	-	51.44
48	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000042]	409.21	12/2008	470.24
49	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000061]	180.53	12/2009	25.97
October,2010				
<u>Health & Family Welfare</u>				
50	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS(HEALTH & FAMILY WELFARE) - [210100001]	71.18	03/1999	547.78
<u>Railways</u>				
51	DHARMAVARAM-PAKALA (GC), SCR(SOUTH CENTRAL RAILWAY) - [220100282]	200.00	-	567.49

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
52	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106268]	263.00	02/2009	420.80
53	AMRITSAR-WAGHA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000121]	205.88	06/2010	214.90
<u>Shipping & Ports</u>				
54	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE(SHIPPING corp. of india) - [N25000029]	1,658.59	07/2010	1,657.45
<u>Telecommunications</u>				
55	GSM BASED NETWORK EXPANSION PLAN PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000034]	239.19	04/2008	96.97
56	Provision of data network for CWG delhi(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000076]	488.76	10/2010	198.65
57	Expn of existing 2G & 3G GSM N/W by 750k(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000077]	180.53	06/2010	40.92
58	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph(BHARAT SANCHAR NIGAM LIMITED) - [N26000079]	577.35	09/2010	40.76

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
September, 2010				
<u>Road Transport & Highways</u>				
1	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N16000082]	300.00	10/2008	.00


Summary of projects on the Flash Report for the month of Oct, 2010

I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 150 Cr. & above) Previous Month	599
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Previous Month	46
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Current month	9
No. of projects with Anticipated greater than Rs. 150 Cr in Current Month	3
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	12
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	559

II. Brief Analysis


a) Project Status w.r.t Original Schedule: Out of 559 projects, 14 projects are ahead of schedule, 117 projects are on schedule and 293 projects are delayed. Of the balance, 80 projects do not have fixed dates of commissioning while 55 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

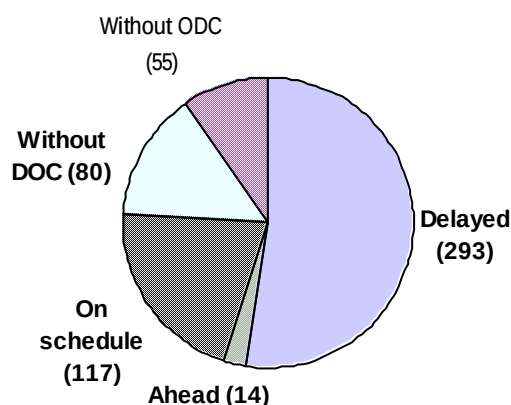

III. Investment Scenario

Figures are in Rs. Crore

The total Original cost of implementation of 559 projects when sanctioned, was of the order of Rs. 578217.92 crore but this was subsequently revised to Rs. 698067.04 crore implying a cost overrun of 20.70%. The expenditure incurred on these projects till Oct, 2010 is Rs. 300519.72 crore, which is 43.10% of the revised cost of the projects.

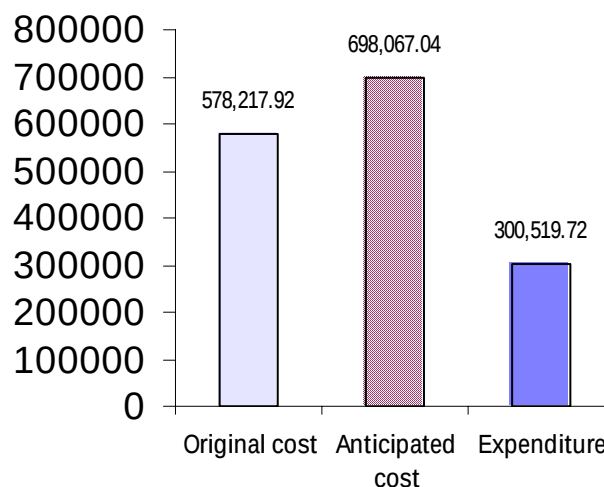

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	599
No of Projects Completed/Dropped/Frozen in Previous Month	46
No of Projects Completed/Dropped/Frozen in Current Month	9
No. of projects with Anticipated grater then Rs. 150 Cr in Current Mont	3
No of Projects added in Current Month	12
No of Projects in Current Month	559

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	293	13	118	55	80	559	52.42
Latest Approved (Date)	283	16	149	43	70	559	50.63

III. (A) Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	461	478,262.49	520,924.59	216,368.55	41.50	42,662.10	8.90
Latest Approved (RCE)	98	148,588.33	177,142.45	84,151.17	47.50	28,554.12	19.20
Total (RCE)	559	626,850.82	698,067.04	300,519.72	43.05	71216.22	11.36
Original Cost of All Projects							
Original Cost	559	578,217.92	698,067.04	300,519.72	43.10	119,849.12	20.70

III. (B) Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	293	304,151.07	372,212.02	203,949.80	54.80	68,060.95	22.40
Latest Approved (RCE)	283	297,186.88	343,310.52	196,332.10	57.20	46,123.64	15.50

IV. Additional Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	115	133,151.18	148,476.50	100,557.18	67.70	15,325.32	11.50

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Railways</u>						
DHARMAVARAM-PAKALA (GC), SCR	04/1997	200.00	N.A.	610.07	03/2010	567.49
<u>Road Transport & Highways</u>						
JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1	03/2005	263.00	02/2009	263.00	10/2010	420.80
AMRITSAR-WAGHA BORDER	06/2008	205.88	06/2010	205.88	10/2010	214.90
<u>Shipping & Ports</u>						
ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE	10/2006	1,658.59	07/2010	1,658.59	10/2010	1,657.45
<u>Telecommunications</u>						
GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph	09/2009	577.35	09/2010	577.35	12/2010	40.76
Expn of existing 2G & 3G GSM N/W by 750k	10/2008	180.53	06/2010	180.53	12/2010	40.92
<u>Health & Family Welfare</u>						
NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS	05/1986	71.18	03/1999	443.15	10/2010	547.78
<u>Telecommunications</u>						
GSM BASED NETWORK EXPANSION PLAN PH-4	02/2007	239.19	04/2008	239.19	N.A.	96.97
Provision of data network for CWG delhi	11/2009	488.76	10/2010	488.76	10/2010	198.65

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Road Transport & Highways</u>					
Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1)	5/2009	572.30	10/2011	572.30	10/2011
MP/Maharashtra Border-Dhula	12/2009	835.00	6/2012	835.00	6/2012
Surat- Dahisar(Six Lane) Km 263 to Km 502	2/2009	1,693.75	8/2011	1,693.75	8/2011
Gurgaon-Kotputli Km 42.70 to 54.4 Km	4/2009	1,673.70	10/2011	1,673.70	10/2011
Four Lanning from MP/Maharashtra Border to nagpur	4/2010	1,170.52	6/2011	1,170.52	6/2011
Pune-sholapur, pkg1	11/2009	1,110.00	5/2012	1,110.00	5/2012
Chennai-Tada(Six lane)	4/2009	353.37	10/2011	353.37	10/2011
<u>Power</u>					
INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF I	10/2012	160.32	10/2012	160.32	10/2012
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX	10/2010	182.68	1/2013	182.68	1/2013
<u>Road Transport & Highways</u>					
Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	5/2009	1,108.00	11/2011	1,108.00	11/2011
Kishangarh-Ajmer-Beawer	11/2009	795.00	5/2012	795.00	5/2012
Gujarat/Maharashtra BorderSurat-Hazira Port Section	3/2010	1,509.10	9/2012	1,509.10	9/2012

VII. Milestones (Cumulative due & achieved)

Total	2045
Achieved up to month	797

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	13,171.00	12/2008	06/2011	12/2011	6
<u>Coal</u>						
ADRIYALA SHAFT PROJECT SCCL	212.34	779.26	03/2013	09/2012	07/2012	-2
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	10/2010	11/2010	1
TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	2,453.57	06/2009	06/2011	10/2011	4
BHUBANESWARI OCP MCL	490.10	490.10	03/2014	03/2016	03/2017	12
GEVRA EXPANSION OCP (SECL) (25 MTY) SECL	1,667.55	2,675.67	03/2010	03/2012	03/2014	24
KAKATIYA LAONGWALL SCCL	453.63	453.63	N.A.	12/2012	03/2015	27
<u>Fertilisers</u>						
NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT NFL	1,478.63	1,478.63	12/2012	10/2012	12/2012	2
PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE NFL	1,292.84	1,292.84	01/2013	10/2012	01/2013	3
BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ NFL	1,294.19	1,294.19	01/2013	10/2012	01/2013	3
THAL AMMONIA REVAMP PROJECT RCF	488.75	488.75	N.A.	03/2011	11/2011	8
<u>Steel</u>						
INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA SAIL	302.70	302.70	06/2009	09/2010	10/2010	1
SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II SAIL	197.66	197.66	11/2009	09/2010	10/2010	1
67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	358.00	02/2010	01/2011	03/2011	2
Rebuilding of coke oven battery No.1 & 2 (Bokaro S SAIL	500.90	500.90	04/2010	04/2011	07/2011	3
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) SAIL	172.78	172.78	01/2010	11/2010	02/2011	3
EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	14,443.00	06/2011	06/2011	12/2011	6

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Petroleum</u>						
EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA IOCL	806.00	1,100.00	03/2008	10/2010	11/2010	1
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY IOCL	372.00	276.00	N.A.	10/2010	11/2010	1
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY IOCL	356.00	251.00	N.A.	10/2010	11/2010	1
MSQ UPGRADATION PROJECT AT BARAUNI REFINERY IOCL	1,492.00	1,505.57	04/2010	10/2010	11/2010	1
INSTALLATION OF FCCV AT MUMBAI REFINERY HPCL	900.47	900.47	09/2009	10/2010	11/2010	1
BNPL SPURLINE (UTTRANCHAL & PUNJAB) GAIL	540.92	540.92	06/2011	05/2011	06/2011	1
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON BRPL	1,431.91	1,676.00	09/2009	10/2010	12/2010	2
SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) GAIL	396.13	396.13	10/2009	09/2010	11/2010	2
NORTH TAPTI GAS FIELD DEV. ONGC	589.70	589.70	03/2011	03/2011	05/2011	2
North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	03/2011	05/2011	2
C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) ONGC	900.92	976.08	06/2006	10/2010	01/2011	3
REFRIGERAPED LPG STORAGE AT JNPT BPCL	304.40	304.40	12/2010	12/2010	03/2011	3
Integrated offshore crude Oil handling facilities at Paradip IOCL	1,492.33	1,492.33	06/2012	03/2012	06/2012	3
MSQ IMPROVMENT PROJECT IOCL	293.60	293.60	12/2009	10/2010	03/2011	5
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I GAIL	1,512.00	1,434.00	04/2011	10/2010	04/2011	6
Additional Development of D-1 Field ONGC	2,163.64	2,163.64	12/2011	12/2011	06/2012	6
<u>Power</u>						
NORTHERN REGION SYSTEM STRENGTHENING- XI PGCIL	417.76	417.76	12/2010	09/2010	10/2010	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X PGCIL	408.36	408.36	12/2010	09/2010	10/2010	1
WESTERN REGION STRENGTHENING SCHEME- IX PGCIL	230.89	230.89	01/2011	01/2011	02/2011	1
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX PGCIL	525.14	525.14	07/2011	09/2010	10/2010	1
BARH STPP STAGE -II (NTPC) NTPC	7,341.04	7,341.04	08/2013	08/2013	10/2013	2
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) PGCIL	3,779.46	3,725.13	09/2009	12/2010	03/2011	3
EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	894.26	10/2009	12/2010	03/2011	3
KORBA STPP STAGE-III NTPC	2,448.50	2,448.49	02/2010	10/2010	01/2011	3
WESTERN REGION STRENGTHENING SCHEME-VI PGCIL	340.72	340.72	11/2010	11/2010	03/2011	4
BARH STPP(3X660MW) NTPC NTPC	8,692.97	8,693.00	11/2010	04/2014	09/2014	5
PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.56	2,304.52	10/2010	06/2011	12/2011	6
CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.26	621.28	02/2011	02/2011	08/2011	6
BONGAIGAON THERMAL POWER PROJECT (NTPC) NTPC	4,375.35	4,375.35	07/2011	03/2012	10/2012	7
CHAMERA,STAGE-III (NHPC) NHPC	1,405.63	1,405.63	08/2010	12/2010	08/2011	8
URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	1,724.79	11/2009	02/2011	10/2011	8
NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) NHPC	611.01	611.02	08/2010	12/2010	09/2011	9
LOWER SUBANSIRI H.E.P (NHPC) NHPC	6,285.33	6,285.33	09/2010	12/2012	12/2013	12
KOTESHWAR HEP(THDC) THDCL	1,301.56	2,398.39	04/2005	12/2010	03/2012	15
PARBATI HEP (NHPC) II NHPC	3,919.59	3,919.59	09/2009	03/2013	07/2014	16
RAMPUR HEP(412 MW) SJVNL	2,047.03	2,047.03	01/2012	03/2012	09/2013	18
Railways						
MUZAFFARPUR- SITAMARHI(NL),ECR ECR	100.00	322.29	N.A.	02/2011	03/2011	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) ER	180.73	358.00	12/2006	11/2010	02/2011	3
PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) WR	148.61	227.52	03/2008	03/2010	10/2010	7
TALCHER- BIMALAGARH(NL)(ECOR) ECR	726.96	810.78	N.A.	02/2011	03/2012	13
Road Transport & Highways						
HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	11/2011	06/2011	-5
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 NHAI	243.64	243.64	08/2009	12/2010	11/2010	-1
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 NHAI	243.38	243.38	09/2008	10/2010	11/2010	1
COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 NHAI	106.00	193.00	08/2006	10/2010	12/2010	2
AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 NHAI	193.00	193.00	10/2008	10/2010	12/2010	2
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 NHAI	217.00	217.00	10/2008	10/2010	12/2010	2
GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 NHAI	239.00	239.00	10/2008	10/2010	12/2010	2
GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 NHAI	205.00	205.00	10/2008	10/2010	12/2010	2
AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 NHAI	212.00	212.00	10/2008	10/2010	12/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 NHAI	208.46	208.46	08/2009	10/2010	12/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 NHAI	239.19	239.19	09/2009	09/2010	11/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 NHAI	205.92	205.92	08/2009	09/2010	11/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 NHAI	194.80	194.80	08/2009	09/2010	11/2010	2
BANGALORE- NEELAMANGALA NH-4 NHAI	445.00	445.00	07/2010	09/2010	11/2010	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 NHAI	565.00	565.00	07/2010	10/2010	12/2010	2
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 NHAI	227.00	227.00	10/2008	03/2011	06/2011	3
ORAI TO JHANSI (UP-5),NH- 25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	12/2010	03/2011	3
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 NHAI	359.00	359.00	03/2009	12/2010	03/2011	3
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	09/2010	12/2010	3
NAGAON BYPASS (NH- 37)(NHAI) NHAI	230.00	230.00	06/2008	09/2010	12/2010	3
FORBESGANJ TO SIMRAHI (NH-57)(NHAI) NHAI	332.94	332.94	09/2008	03/2011	06/2011	3
KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	09/2010	12/2010	3
RINGBUNDS TO JHAJHANPUR (BR-6) NHAI	340.00	340.00	06/2008	12/2010	03/2011	3
SITAPUR-LUCKNOW NHAI	322.00	322.00	06/2009	12/2010	03/2011	3
BARA TO ORAI, NH-2, 25 NHAI	465.00	465.00	04/2009	12/2010	03/2011	3
GORAKHPUR BYPASS, NH- 28, PHASE-II EAST-WEST CORRID NHAI	600.24	600.24	10/2009	03/2011	06/2011	3
GWALIOR BYPASS, NH-75,3 NHAI	300.93	300.93	10/2009	10/2010	01/2011	3
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	10/2010	01/2011	3
ORAI TO JHANSI (UP-4),NH- 25, KM.170.0 TO KM.104.0 NHAI	451.97	451.97	04/2008	10/2010	03/2011	5
KASIA TO GORAKHPUR (NH- 28)(NHAI) NHAI	242.00	242.00	12/2008	12/2010	05/2011	5
KURALI-KIRATPUR, NH-21 NHAI	309.00	309.00	06/2010	10/2010	03/2011	5
SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 NHAI	941.00	941.00	01/2011	01/2011	06/2011	5
ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) NHAI	295.00	295.00	08/2010	12/2010	05/2011	5
HALDIA PORT (PORT CONNECTIVITY) (NH-41) NHAI	273.00	522.00	03/2005	09/2010	03/2011	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) NHAI	227.00	227.00	12/2008	12/2010	06/2011	6

VIII. List of projects reporting additional delays



Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
JHANSI TO LALITPUR, NH-25,26 NHAI	355.06	355.06	09/2009	09/2010	03/2011	6
JHANSI TO LALITPUR, NH-26 NHAI	276.09	276.09	09/2009	09/2010	03/2011	6
TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	12/2010	06/2011	6
NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH NHAI	557.00	557.00	02/2010	10/2011	05/2012	7
MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 NHAI	200.00	200.00	04/2009	04/2011	12/2011	8
HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	280.00	280.00	02/2009	03/2011	12/2011	9
SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	03/2011	12/2011	9
NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	03/2011	12/2011	9
DARBHANGA- MUZAFFARPUR, NH-57 (NHAI) NHAI	305.00	305.00	06/2008	12/2010	11/2011	11
MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 NHAI	155.04	155.04	11/2008	12/2012	12/2013	12
HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 NHAI	212.00	212.00	09/2007	12/2012	12/2013	12
HARANGAJO TO MAIBANG, NH-54 NHAI	196.00	196.00	07/2009	12/2012	12/2013	12
PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A NHAI	284.00	359.00	05/2008	12/2010	08/2012	20
AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 NHAI	348.16	348.16	09/2007	02/2011	06/2013	28
MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 NHAI	199.81	199.81	04/2009	12/2010	12/2013	36
MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 NHAI	167.64	167.64	11/2008	12/2010	12/2013	36
Telecommunications						
GSM equipment of 975000 Lines (2G) 325000 lines 3G BSNL	625.53	625.53	02/2010	10/2010	11/2010	1
GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M BSNL	908.30	916.70	08/2009	09/2010	11/2010	2
GSM equipment of 900000 Lines (2G) Punjab Phase V.2 BSNL	241.49	241.49	09/2009	09/2010	11/2010	2



VIII. List of projects reporting additional delays



Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GSM equipment of 1900000Lines (2G) 335500lines 3(G BSNL	848.70	848.70	01/2010	09/2010	11/2010	2
GSM equipment of 1867000Lines (2G) 383000 lines 3(BSNL	868.00	868.00	08/2009	09/2010	12/2010	3
GSM equipment of 1700000Lines (2G) 234100 lines 3(BSNL	677.75	719.70	10/2009	09/2010	12/2010	3
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT DMRC	8,676.00	18,894.36	06/2010	09/2010	11/2010	2



Number of projects reporting additional delay = 115



Sector wise Trend and Graphical Analysis (July'10,Aug'10,Sep'10,Oct'10)

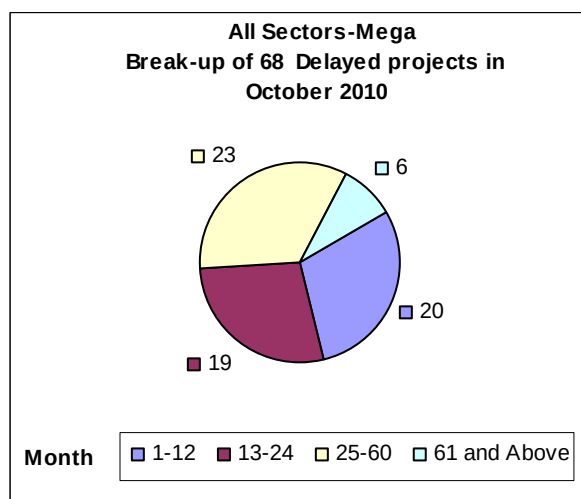
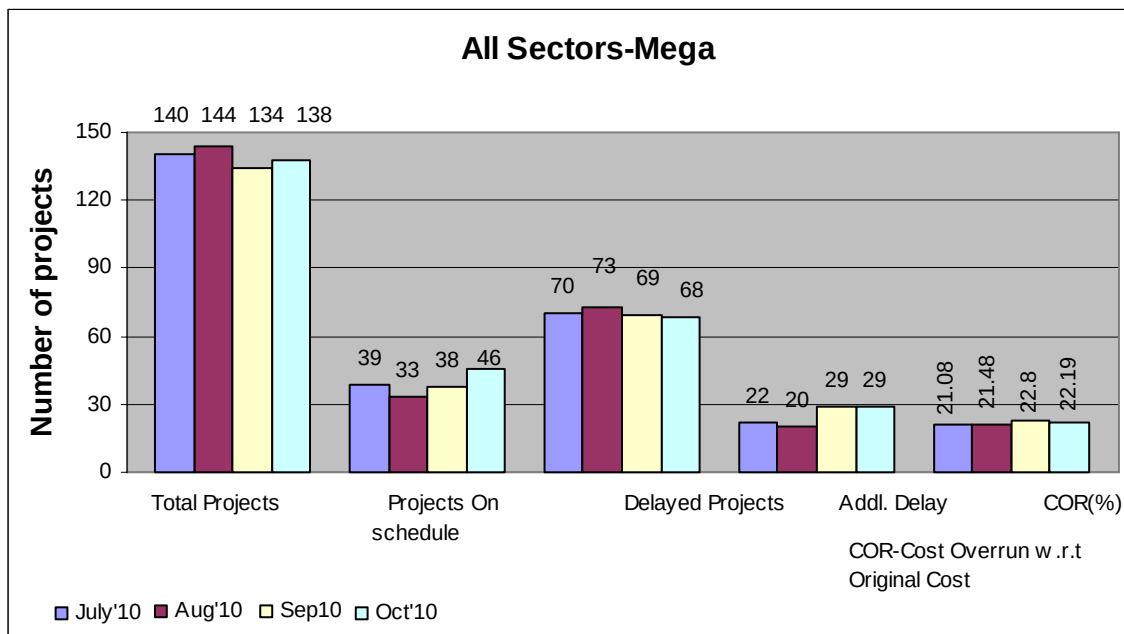


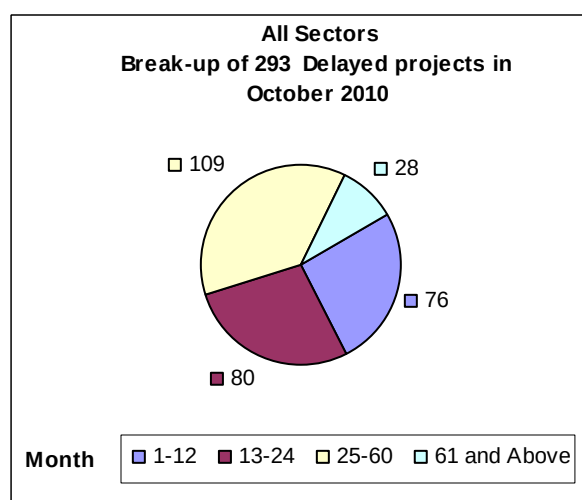
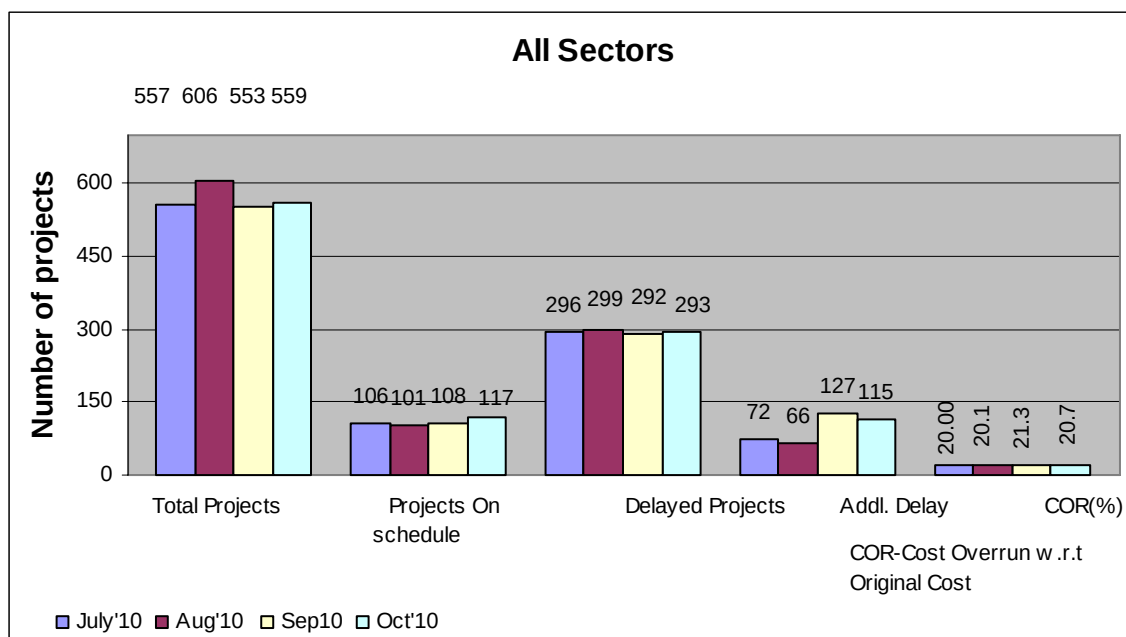


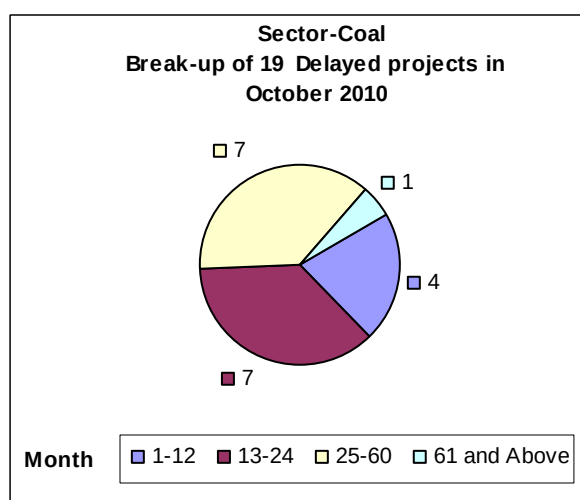
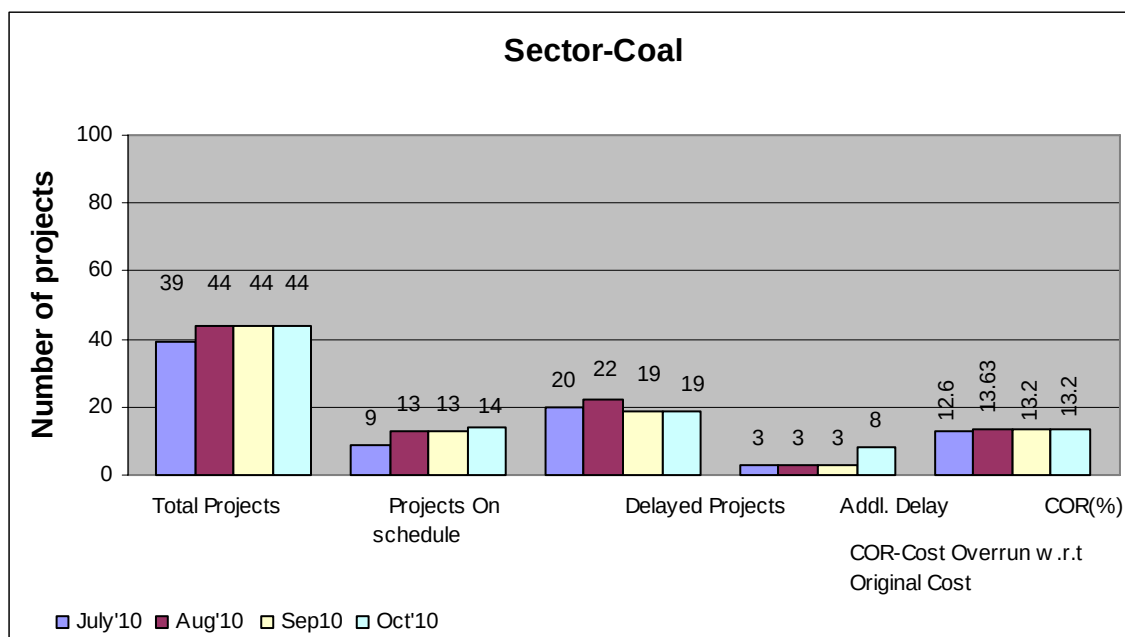


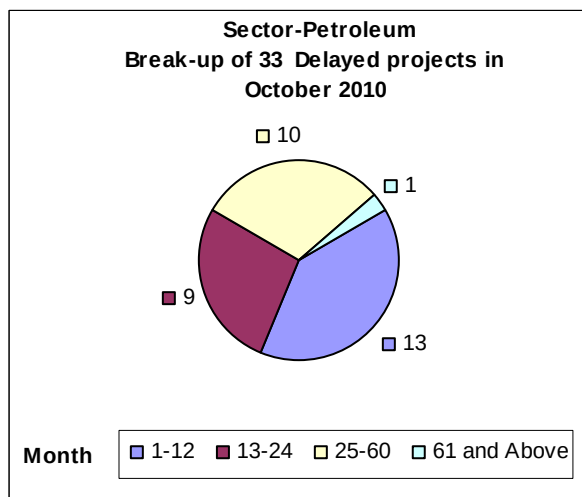
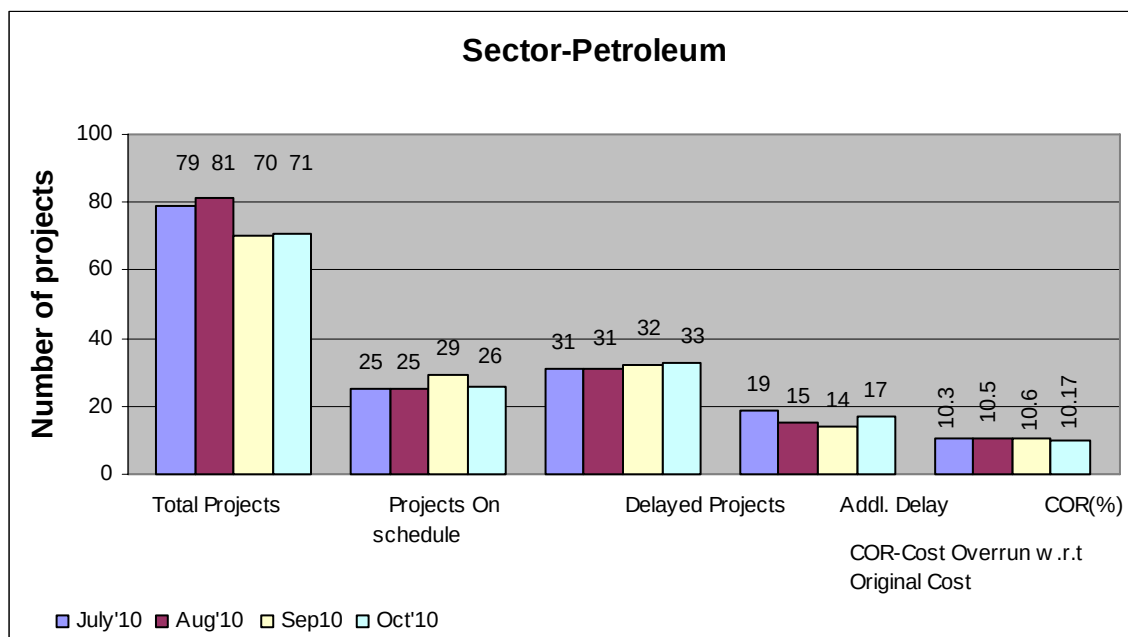


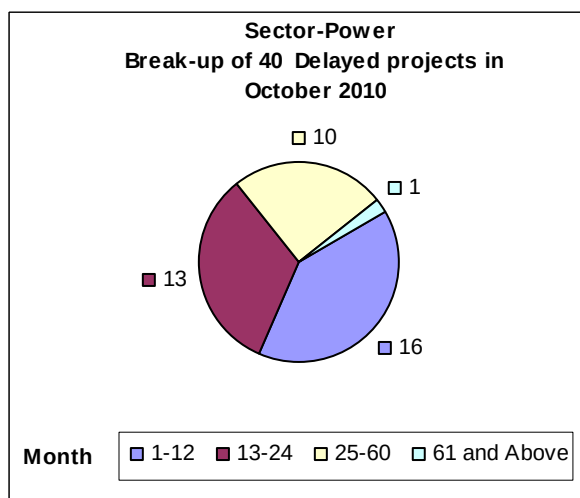
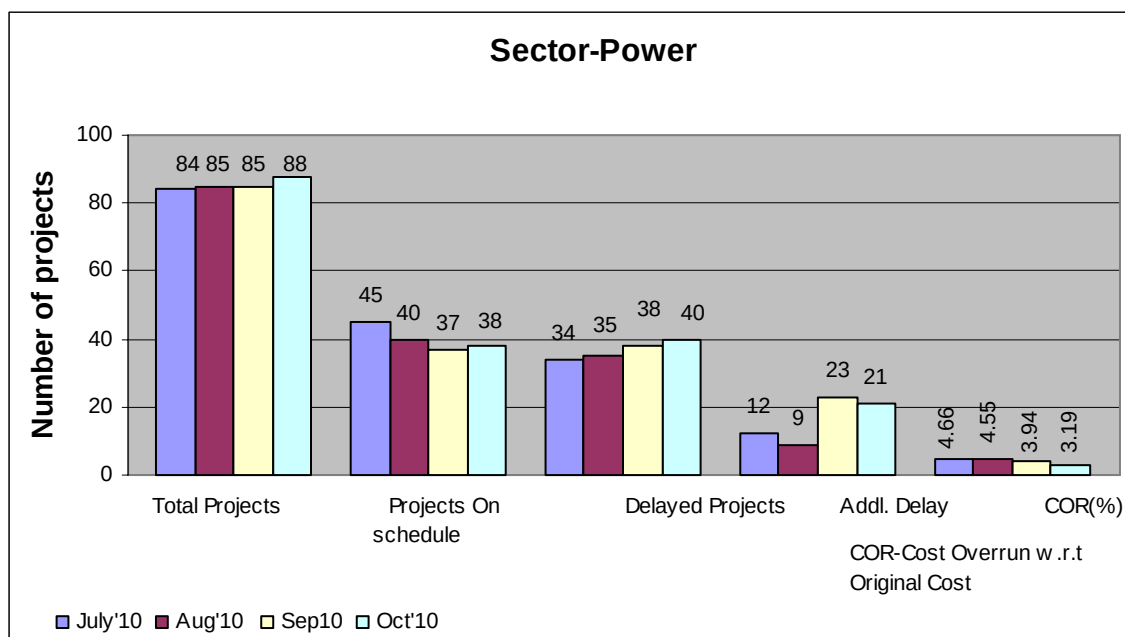


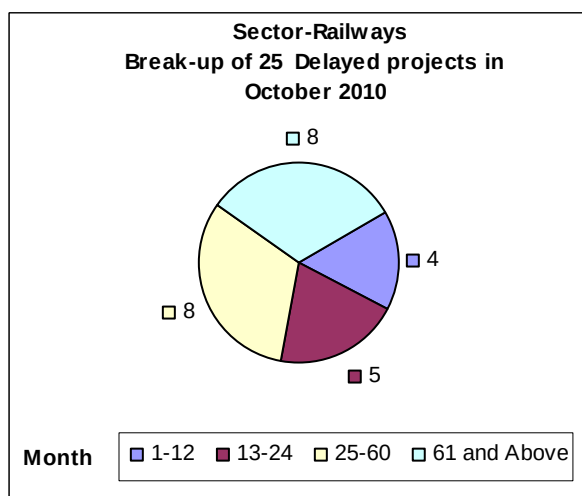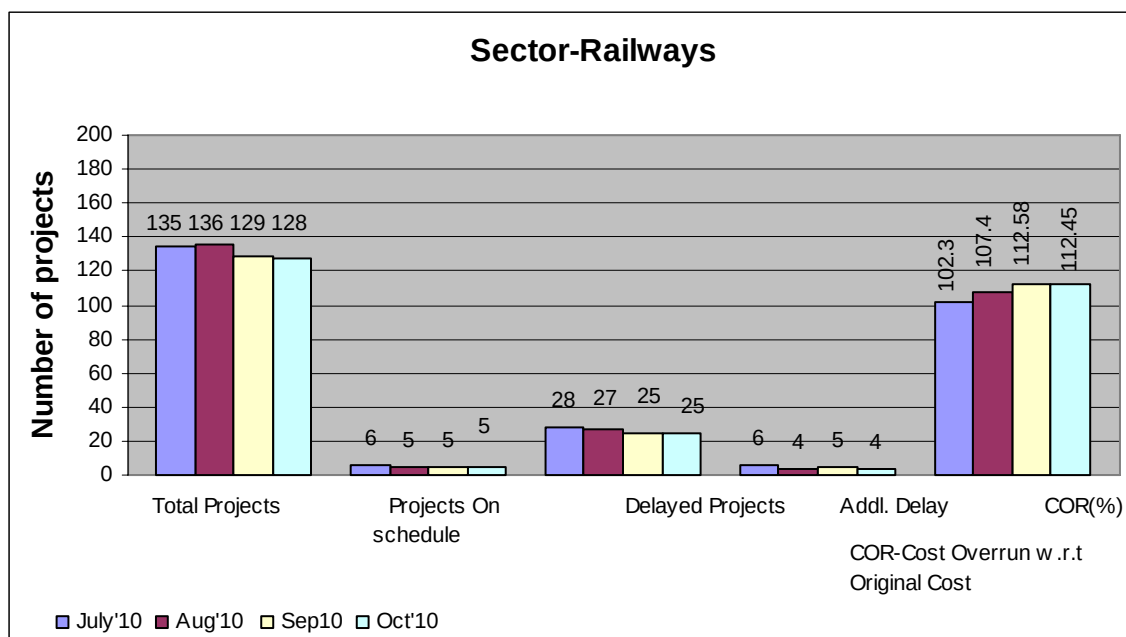

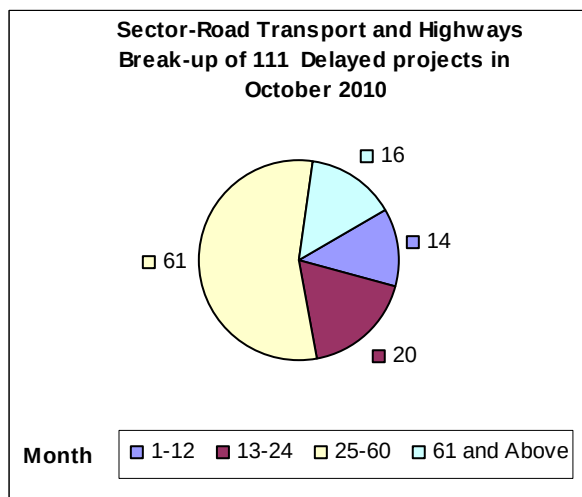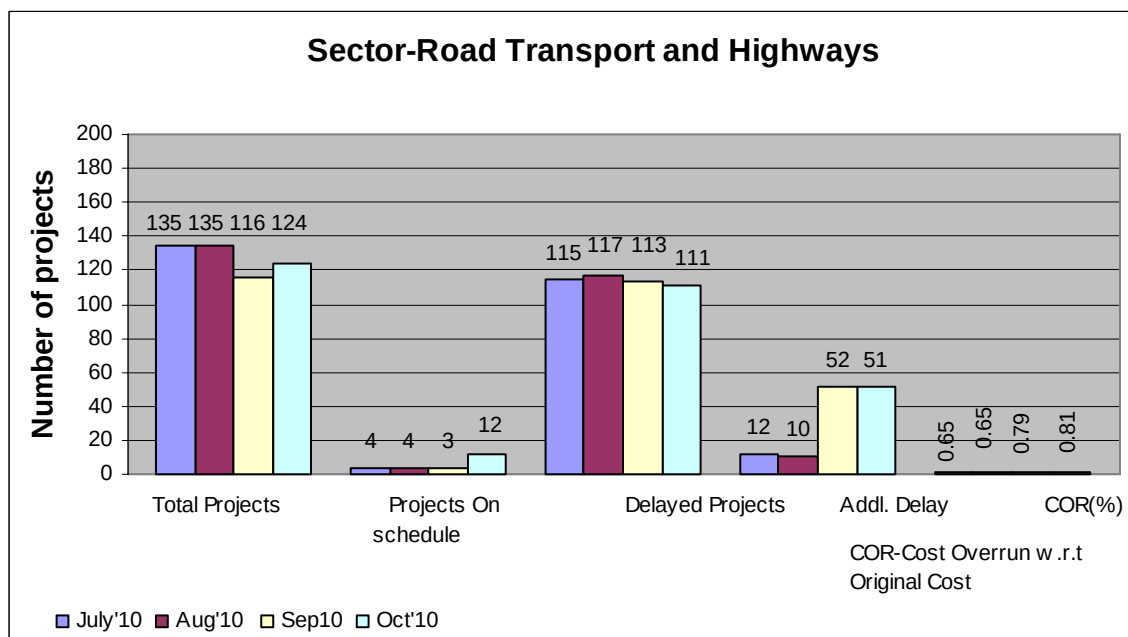

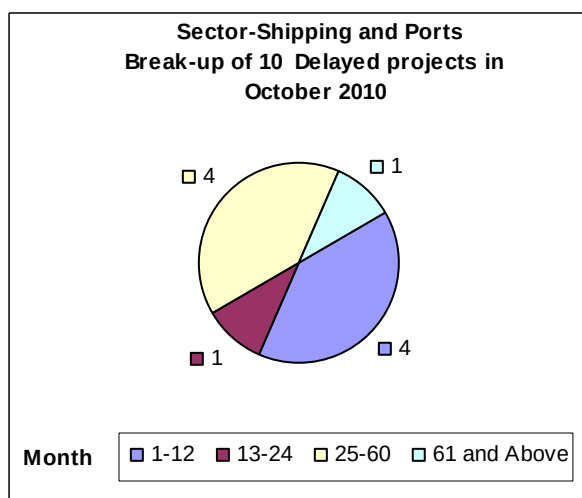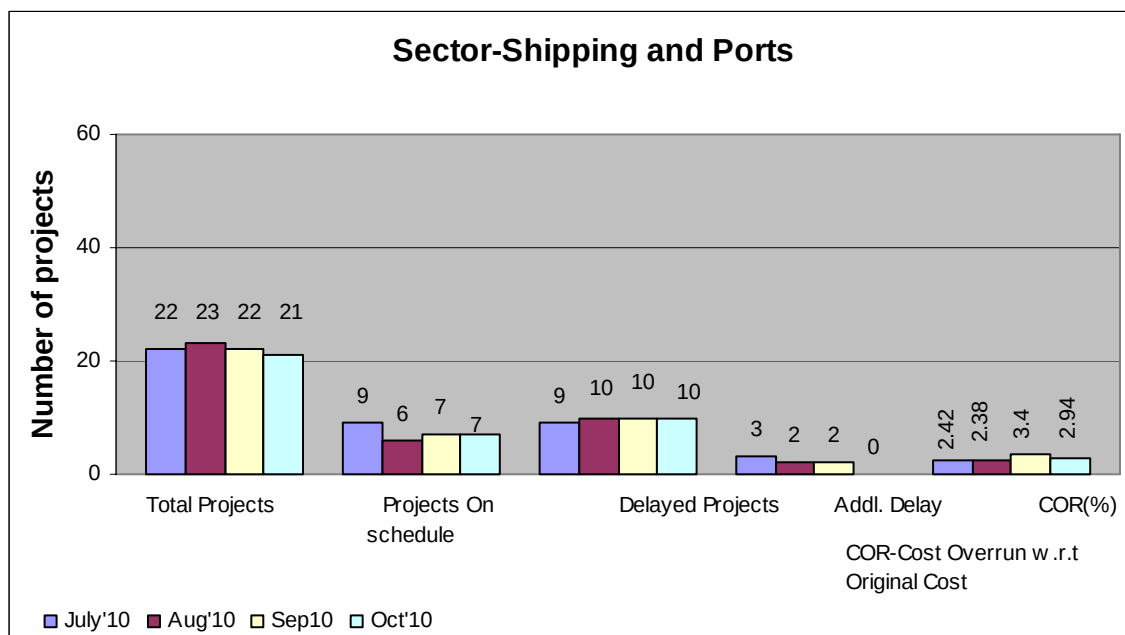

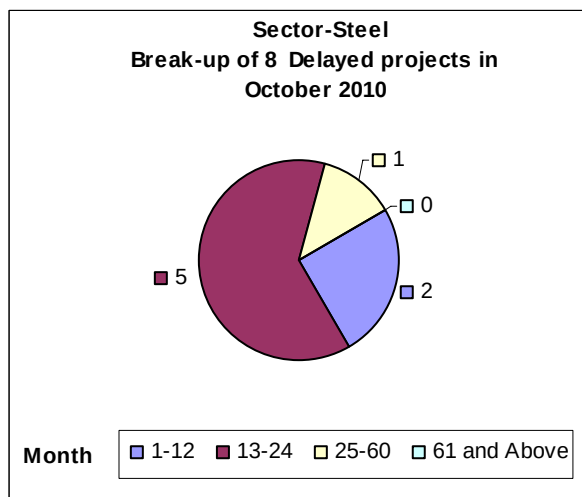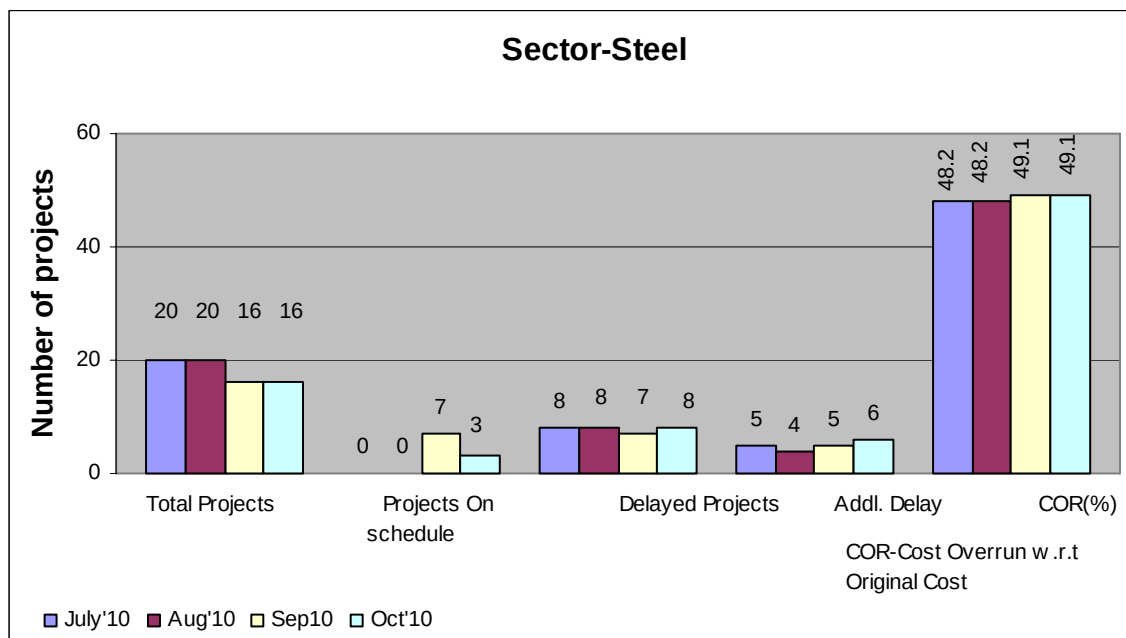

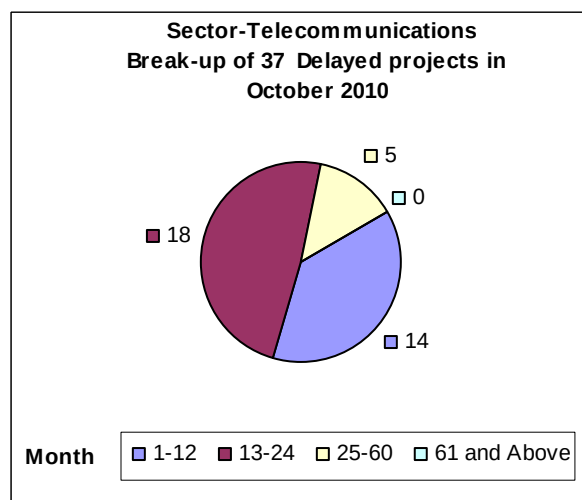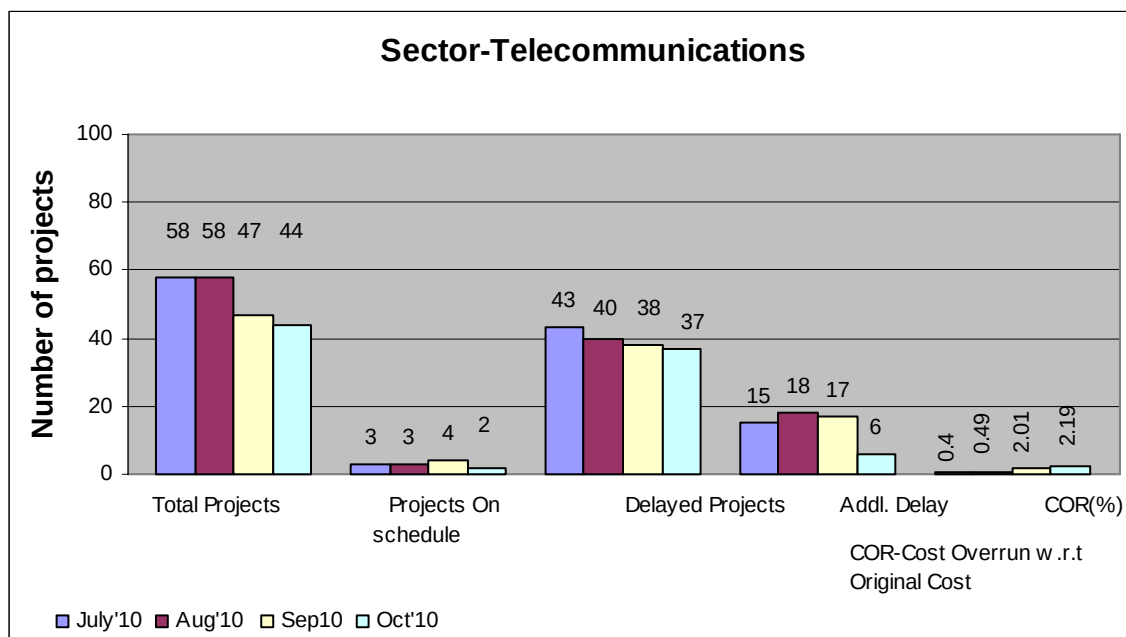

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	24,167.29
Civil Aviation	9	5,347.40	5,347.40	5,347.40
Coal	44	25,210.30	28,502.92	28,542.19
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	16	43,096.53	58,435.18	64,258.46
Petroleum	71	145,231.54	162,922.04	160,004.07
Power	88	182,037.84	182,956.89	187,852.55
Railways	128	48,823.84	59,832.18	103,728.73
Road Transport & Highways	124	44,552.67	44,552.67	44,917.67
Shipping & Ports	21	15,469.90	15,568.42	15,925.66
Telecommunications	44	21,442.79	21,488.40	21,913.49
Urban Development	2	15,071.00	15,000.36	30,503.36
Water Resources	1	542.90	542.90	1,187.00
Grand total	559	578,217.92	626,850.82	698,067.04

(Oct,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]NPCIL,Karnataka	05/2001	4,213.00	4,213.00	2,582.00	10/2009 09/2007	12/2010	39(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	778.60	- -	04/2011	-	0/1
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	2,592.29	09/2010 -	09/2011	12(O)	8/80
4	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	13,171.00	13,183.00	12/2008 -	12/2011	36(O)	61/119
Total			21,982.29	24,167.29	19,135.89				140/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35	213.35	153.05	09/2010 -	11/2010	2(O)	0/0
6	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]AAI,Tamil Nadu	01/2008	535.00	535.00	331.80	06/2010 06/2010	12/2010	6(R3)	0/0
7	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00	1,273.00	594.84	01/2011 -	01/2011	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29	264.29	264.29	01/2011 -	01/2011	0(O)	0/0
9	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00	230.00	188.12	01/2011 -	01/2011	0(O)	0/0
10	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	1,942.51	860.83	05/2011 -	08/2011	3(O)	0/0
11	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73	204.73	5.97	05/2012 -	05/2012	0(O)	0/0
12	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60	393.60	202.26	06/2013 -	06/2013	0(O)	0/0
13	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]AAI,Gujarat	02/2007	290.92	290.92	185.74	- -	-	-	1/24
Total			5,347.40	5,347.40	2,786.90				1/24
<u>Coal</u>									
14	BARSINGAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,499.96	06/2009 -	11/2010	17(O)	59/26
15	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08	172.08	500.71	03/2009 03/2010	03/2011	12(R3)	0/0
16	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	33.46	03/2011 -	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,037.50	06/2009 -	10/2011	28(O)	41/24
18	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	64.75	03/2010 03/2012	03/2012	0(R3)	0/4
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	100.68	03/2011 03/2012	03/2012	0(R3)	0/0
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	37.78	03/2012 -	03/2012	0(O)	8/42
21	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	0.93	03/2012 -	03/2012	0(O)	0/1
22	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	269.62	03/2012 -	03/2012	0(O)	0/0
23	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,	12/2009	418.57 418.97	418.97	66.56	- -	03/2012	-	7/7
24	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,	03/2010	181.91 -	181.19	0.07	- -	03/2012	-	2/8
25	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	68.36	03/2012 -	03/2012	0(O)	0/0
26	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	78.66	03/2012 -	03/2012	0(O)	0/0
27	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	130.51	03/2013 07/2012	07/2012	0(R3)	2/22
28	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,904.54	1,136.21	08/2012 -	08/2012	0(O)	0/0
29	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.56	741.56	136.37	03/2010 03/2013	03/2013	0(R3)	0/2
30	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 1,188.31	1,188.31	555.00	03/2011 03/2013	03/2013	0(R3)	0/4
31	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.23	07/2012 03/2013	03/2013	0(R3)	0/1
32	JALLARAM SHAFT PROJECT - [N06000025]SCCL,	03/2013	467.78 -	467.78	11.42	- -	03/2013	-	0/83
33	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	52.02	- -	03/2013	-	0/2
34	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 479.53	479.53	197.40	03/2013 -	03/2013	0(O)	0/0
35	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	20.05	03/2013 -	03/2013	0(O)	0/0
36	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 2,675.67	2,675.67	1,017.09	03/2010 03/2014	03/2014	0(R3)	3/7
37	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 1,943.66	1,943.66	895.54	03/2010 03/2014	03/2014	0(R3)	2/6
38	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	139.77	03/2014 03/2014	03/2014	0(R3)	1/1
39	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 462.35	462.35	252.55	06/2014 06/2014	03/2014	-3(R3)	0/0
40	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	02/2006	50.08 153.82	153.82	14.77	- 03/2014	03/2014	0(R3)	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77	339.77	-	03/2014	03/2014	0(O)	0/1
42	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
43	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.42 321.50	321.50	213.37	03/2013 03/2014	03/2014	0(R3)	0/0
44	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 437.34	437.34	137.16	03/2012 03/2015	03/2015	0(R3)	0/1
45	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	11/2009	03/2015	64(O)	0/0
46	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	24.33	03/2013 03/2015	03/2015	0(R3)	0/0
47	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2012 03/2015	03/2015	0(R3)	0/0
48	KAKATIYA LAONGWALL - [N06000048]SCCL,	12/2008	453.63	453.63	52.06	- 12/2012	03/2015	27(R3)	7/44
49	Batura OC - [N06000049]BCCL,Madhya pradesh	09/2008	203.82	203.82	-	03/2013 03/2015	03/2015	0(R3)	0/0
50	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
51	RKP OCP PHASE-I - [N06000079]SCCL,	03/2010	201.58 209.78	209.78	0.18	- -	03/2015	-	0/8
52	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	32.29	03/2014 03/2016	03/2016	0(R3)	1/2
53	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	6.04	03/2015 03/2016	03/2016	0(R3)	0/0
54	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	158.59	198.59	92.10	03/2016	03/2016	0(O)	0/0
55	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	290.99	03/2016	03/2016	0(O)	0/0
56	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.10	490.10	59.19	03/2014 03/2017	03/2017	0(R3)	0/0
57	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	-	- -	-	-	0/0
Total			25,210.30	28,542.19	10,241.68				133/297
Fertilisers									
58	CAPACITY ENHANCEMENT OF VIJAI PUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	15.57	07/2011	07/2011	0(O)	0/0
59	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	22.26	07/2011	07/2011	0(O)	0/0
60	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	29.49	- 11/2011	11/2011	0(R3)	2/22
61	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	43.41	12/2012	12/2012	0(O)	0/8
62	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	58.85	01/2013	01/2013	0(O)	0/5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	53.52	01/2013	01/2013	0(O)	0/5
	Total		5,317.41	5,317.41	223.10				2/40
	<u>Mines</u>								
64	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51	4,401.76	-	12/2008	03/2011	2(R3)	116/110
	Total		4,091.51	4,401.76	.00				116/110
	<u>Steel</u>								
65	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]SAIL,Jharkhandd	10/2007	892.32	892.32	616.57	08/2009	07/2010	11(O)	2/1
66	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,	07/2007	260.00	353.00	188.89	-	08/2010	-	0/1
67	EXPANSION OF SALEM STEEL PLANT - [N12000050]SAIL,Tamil Nadu	01/2008	1,902.00	1,902.00	1,754.78	06/2011	09/2010	-9(O)	2/6
68	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]SAIL,Orissa	07/2007	302.70	302.70	244.97	06/2009	10/2010	16(O)	0/0
69	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]SAIL,Orissa	01/2008	197.66	197.66	130.32	11/2009	10/2010	11(O)	0/0
70	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL,Jharkhandd	07/2008	172.78	172.78	113.40	01/2010	02/2011	13(O)	0/1
71	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	358.00	188.02	02/2010	03/2011	13(O)	0/0
72	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Madhya pradesh	07/2007	111.28	232.93	80.55	05/2011	05/2011	0(O)	0/1
73	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,228.00	7,323.00	10/2009	06/2011	20(O)	4/16
74	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC,Andhra Pradesh	01/2003	295.89	607.17	237.14	-	06/2011	-	2/21
75	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	222.49	04/2010	07/2011	15(O)	0/2
76	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	14,443.00	9,236.56	06/2011	12/2011	0(R3)	0/6
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00	6,325.00	1,368.32	12/2011	12/2011	0(R3)	0/7
78	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	8,128.00	2,506.34	02/2011	03/2013	25(O)	0/0
79	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	1,617.11	03/2013	03/2013	0(R3)	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
80	POWER PLANT-I - [N12000039]RINL,Andhra Pradesh	09/2007	462.00	350.00	84.40	12/2009	-	-	0/0
	Total		43,096.53	64,258.46	25,912.86				10/70
			-						
	<u>Petroleum</u>								
81	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	1.13	10/2010	10/2010	0(O)	0/0
			-			-			
82	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]IOCL,West Bengal	11/2005	1,876.00	3,155.00	2,747.34	04/2009	02/2010	2(R1)	41/36
			2,869.00			12/2009			
83	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]GAIL,Multi State	11/2007	5,595.31	4,262.00	3,297.77	11/2009	10/2010	6(R3)	0/0
			4,262.00			04/2010			
84	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA - [N16000017]IOCL,Haryana	06/2005	806.00	1,100.00	840.06	03/2008	11/2010	11(R1)	18/66
			1,007.83			12/2009			
85	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL,Gujarat	01/2007	5,693.00	6,898.00	5,767.55	-	11/2010	5(R3)	0/42
			6,898.00			06/2010			
86	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]IOCL,Assam	04/2008	372.00	276.00	223.98	-	11/2010	-	0/28
			-			-			
87	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]IOCL,Assam	04/2008	356.00	251.00	215.86	-	11/2010	-	0/27
			-			-			
88	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]IOCL,Bihar	04/2008	1,492.00	1,505.57	1,093.27	04/2010	11/2010	7(O)	0/0
			-			-			
89	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL,Multi State	11/2007	396.13	396.13	185.56	10/2009	11/2010	5(R3)	0/0
			-			06/2010			
90	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL,Maharashtra	03/2007	900.47	900.47	1,332.68	09/2009	11/2010	14(O)	0/0
			-			-			
91	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	1,676.00	1,453.07	09/2009	12/2010	15(O)	0/0
			1,646.39			-			
92	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL,Punjab	01/2009	605.40	605.40	298.01	12/2010	12/2010	0(O)	13/17
			-			-			
93	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80	3,941.41	3,139.40	12/2009	12/2010	12(O)	0/0
			3,941.41			-			
94	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	727.88	315.52	12/2010	12/2010	0(O)	0/0
			-			-			
95	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92	976.08	735.45	06/2006	01/2011	6(R3)	0/2
			1,493.49			07/2010			
96	CONSTRUCTION OF NEW TERMINAL AT ENnore CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	224.00	127.61	12/2010	02/2011	0(R3)	0/0
			-			02/2011			

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 -	600.00	542.47	03/2007 -	03/2011	48(O)	3/3
98	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 834.90	1,200.00	1,125.49	03/2007 03/2011	03/2011	0(R3)	6/6
99	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 -	219.22	-	03/2006 -	03/2011	60(O)	6/6
100	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.63	12/2008 12/2008	03/2011	27(R3)	0/0
101	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 -	2,305.30	2,061.15	06/2010 06/2010	03/2011	9(R3)	0/0
102	MSQ IMPROVMENT PROJECT - [N16000040]IOCL,Assam	04/2008	293.60 -	293.60	187.11	12/2009 -	03/2011	15(O)	0/0
103	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	160.73	12/2010 -	03/2011	3(O)	0/0
104	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	07/2011	1,816.07 1,816.07	1,400.00	395.68	- 04/2011	04/2011	0(R3)	0/1
105	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38 4,403.00	2,800.00	1,814.87	10/2011 04/2011	04/2011	0(R3)	0/2
106	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Multi State	11/2007	1,512.00 1,434.00	1,434.00	648.81	04/2011 04/2011	04/2011	0(R3)	0/2
107	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,061.93 1,167.00	1,167.00	26.86	04/2011 04/2011	04/2011	0(R3)	0/2
108	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	464.47	04/2010 -	04/2011	12(O)	0/0
109	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	86.34	04/2011 -	04/2011	0(O)	0/0
110	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,234.69	03/2005 05/2011	05/2011	0(R3)	0/0
111	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 -	330.40	2.45	05/2010 -	05/2011	12(O)	0/0
112	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	05/2011	26(O)	0/0
113	NORTH TAPTI GAS FIELD DEV. - [N16000085]ONGC,Gujarat	07/2008	589.70 -	589.70	71.11	03/2011 -	05/2011	2(O)	0/0
114	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	01/2010	589.70 755.76	755.76	71.11	03/2011 05/2011	05/2011	0(R3)	0/0
115	BNPL superlines(Uttranchal & Punjab) - [N16000091]GAIL,Multi State	12/2009	540.92 -	540.92	0.96	05/2011 -	06/2011	1(O)	0/0
116	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	463.32	0.13	06/2011 -	06/2011	0(O)	3/9
117	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	540.92	-	06/2011 -	06/2011	0(O)	7/9
118	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 -	3,597.00	146.54	09/2011 -	09/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
119	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	108.33	09/2011 -	09/2011	0(O)	0/0
120	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	478.17	12/2011 -	12/2011	0(O)	0/0
121	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	349.00 -	349.00	114.41	08/2011 -	12/2011	4(O)	0/0
122	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Multi State	06/2009	3,032.00 348.00	348.00	7.67	03/2012 -	12/2011	-3(O)	6/12
123	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL,Maharashtra	02/2008	825.00 -	825.00	80.65	- -	12/2011	-	0/203
124	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	154.37	12/2011 -	12/2011	0(O)	0/0
125	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	110.39	12/2011 -	12/2011	0(O)	0/0
126	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	411.41	03/2010 03/2012	03/2012	0(R1)	0/0
127	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	6,652.22	0.50	01/2013 -	03/2012	-10(O)	0/0
128	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	4,508.38	30.85	03/2012 -	03/2012	0(O)	11/10
129	Assam gas Cracker project - [N16000106]BCPL,Assam	04/2006	5,460.61 -	5,460.61	1,246.69	- -	04/2012	-	0/2
130	CONSTRUCTION OF NEW PROCESS COMPLEX MNH - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	1,513.12	05/2010 05/2012	05/2012	0(R3)	0/0
131	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	1,552.63 2,920.82	2,920.82	165.00	02/2009 03/2012	05/2012	2(R3)	0/0
132	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	-	07/2010 05/2012	05/2012	0(R3)	0/0
133	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	89.83	03/2010 03/2012	06/2012	3(R3)	0/0
134	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	55.84	06/2012 -	06/2012	0(O)	0/0
135	Additional Development of D-1 Field - [N16000097]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	110.39	12/2011 06/2012	06/2012	0(R3)	0/0
136	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	8.53	04/2011 -	07/2012	15(O)	0/0
137	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	-	08/2012 -	08/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
138	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	6,855.93	6,855.93	1,003.83	09/2012	09/2012	0(O)	0/0
139	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	18.73	09/2012	09/2012	0(O)	0/0
140	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78	234.78	-	09/2012	09/2012	0(O)	0/0
141	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	29,777.00	4,495.02	-	11/2012	-	0/103
142	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	1,797.35	9.78	12/2011	01/2013	13(O)	0/0
143	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	7.93	01/2013	01/2013	0(O)	0/0
144	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	-	02/2013	02/2013	0(O)	0/0
145	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	06/2007	1,252.75	8,813.41	5,364.58	06/2009 03/2013	03/2013	0(R3)	0/0
146	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	211.94	03/2013	03/2013	0(O)	0/0
147	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
148	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
149	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
150	Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	6.48	02/2014	02/2014	0(O)	0/0
151	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	-	-	12/2012	-	0/0
	Total		145,231.54	160,004.07	49,198.56				114/588
Power									
152	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]PGCIL,Haryana	02/2008	261.55	261.55	141.20	11/2010	09/2010	-2(O)	0/0
153	National Capital Thermal Power Project Stage-II - [N18000013]NTPC,Uttar Pradesh	10/2006	5,135.33	5,135.33	4,000.00	10/2010	10/2010	0(O)	12/40
154	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]PGCIL,Multi State	12/2007	417.76	417.76	266.42	12/2010	10/2010	-2(O)	0/0
155	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]PGCIL,Uttar Pradesh	12/2007	408.36	408.36	303.36	12/2010	10/2010	-2(O)	0/0
156	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]PGCIL,Multi State	07/2008	525.14	525.14	351.71	07/2011	10/2010	-9(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
157	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34	241.27	152.07	06/2008	12/2010	30(O)	8/20
158	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70	803.76	618.94	06/2009	12/2010	18(O)	1/20
159	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]NHPC,Multi State	12/2007	227.52	227.52	117.46	06/2010	12/2010	6(O)	0/0
160	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49	299.08	304.19	04/2010	12/2010	8(O)	0/0
161	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]NHPC,Himachal Pr.	09/2007	262.10	262.10	141.91	09/2010	12/2010	3(O)	0/0
162	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	215.12	07/2011	12/2010	-7(O)	0/0
163	KORBA STPP STAGE-III - [N18000011]NTPC,Madhya pradesh	08/2006	2,448.50	2,448.49	2,072.77	02/2010	01/2011	11(O)	5/24
164	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44	2,570.44	1,794.16	08/2010	02/2011	6(O)	13/26
165	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	50.52	01/2011	02/2011	1(O)	0/0
166	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,619.27	11/2008	03/2011	28(O)	25/38
167	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,414.68	09/2009	03/2011	18(O)	15/30
168	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Uttar Pradesh	10/2006	975.96	894.26	623.35	10/2009	03/2011	17(O)	2/20
169	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,621.67	07/2010	03/2011	8(O)	3/20
170	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	324.50	09/2010	03/2011	6(O)	0/0
171	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]PGCIL,Gujarat	02/2008	340.72	340.72	151.52	11/2010	03/2011	4(O)	0/0
172	Transmission system associated with Uri-II HEP - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	196.31	-	05/2011	-	0/0
173	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,103.39	3,346.00	05/2011	05/2011	0(O)	0/0
174	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	396.98	01/2010	06/2011	17(O)	0/22
175	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	82.30	06/2011	06/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
176	TRANSMISSION SYSTEM ASSOCIATED WITH CORBA III GENE - [N18000059]PGCIL, Madhya Pradesh	02/2009	276.61	276.61	154.76	06/2011	06/2011	0(O)	0/0
177	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL, Multi State	03/2009	196.10	196.10	25.26	07/2011	07/2011	0(O)	0/0
178	CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.	08/2005	1,405.63	1,405.63	1,328.69	08/2010	08/2011	12(O)	0/0
179	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC, J & K	08/2006	621.26	621.28	524.53	02/2011	08/2011	6(O)	0/1
180	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL, Rajasthan	02/2009	210.79	210.79	96.93	08/2011	08/2011	0(O)	0/0
181	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC, J & K	08/2006	611.01	611.02	534.41	08/2010	09/2011	13(O)	0/0
182	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL, Multi State	12/2008	328.97	328.97	157.13	09/2011	09/2011	0(O)	0/0
183	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC, J & K	08/2005	1,729.29	1,724.79	1,234.88	11/2009	10/2011	23(O)	0/0
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL, Multi State	02/2009	520.48	520.48	196.65	11/2011	11/2011	0(O)	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State	02/2009	509.66	509.66	127.10	11/2011	11/2011	0(O)	0/0
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL, Multi State	02/2009	317.69	317.69	14.92	11/2011	11/2011	0(O)	0/0
187	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19	184.19	66.23	11/2011	11/2011	0(O)	0/0
188	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.	10/2002	4,527.15	4,527.15	3,340.04	04/2009	12/2011	32(O)	19/41
189	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT - [180100222]NHPC, West Bengal	10/2003	768.92	768.92	1,203.38	03/2007	12/2011	57(O)	1/25
190	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC, Chhatisgarh	12/2003	8,323.39	8,323.39	7,021.69	12/2009	12/2011	24(O)	33/56
191	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC, Himachal Pr.	10/2005	2,304.56	2,304.52	1,163.62	10/2010	12/2011	14(O)	0/0
192	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01	623.44	58.15	01/2012	01/2012	0(O)	0/0
193	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL, Multi State	02/2009	664.96	664.96	69.61	02/2012	02/2012	0(O)	0/0
194	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL, Multi State	02/2009	409.50	409.50	12.11	02/2012	02/2012	0(O)	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, Multi State	02/2009	410.29	410.29	103.39	02/2012	02/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
196	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	145.27	07/2010	02/2012	19(O)	0/0
197	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	453.25	02/2012	02/2012	0(O)	0/0
198	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,066.19	04/2005	03/2012	83(O)	2/1
199	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	16.07	04/2012	04/2012	0(O)	0/0
200	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	91.66	05/2012	05/2012	0(O)	0/0
201	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	-	06/2012	06/2012	0(O)	0/0
202	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	24.90	06/2012	06/2012	0(O)	0/0
203	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	4.65	06/2012	06/2012	0(O)	0/0
204	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	817.89	09/2009	08/2012	35(O)	0/0
205	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	131.55	08/2012	08/2012	0(O)	4/13
206	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,316.77	08/2012	08/2012	0(O)	0/0
207	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	2,521.22	08/2012	08/2012	0(O)	0/0
208	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	103.21	08/2012	08/2012	0(O)	0/0
209	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	1,476.47	07/2011	10/2012	15(O)	0/0
210	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	1,501.21	02/2012 08/2012	10/2012	2(R3)	0/0
211	TRANSMISSION SYSTEM ASSOCIATED WITH MUNDRA ULTRA M - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	921.60	10/2012	10/2012	0(O)	0/0
212	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	9.84	10/2012	10/2012	0(O)	0/0
213	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF I - [N18000089]PGCIL,Multi State	10/2012	160.32	160.32	-	10/2012	10/2012	0(O)	0/0
214	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	11.89	11/2012	11/2012	0(O)	0/0
215	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2012	965.58	965.58	72.59	11/2012	11/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
216	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42	358.42	6.57	12/2008 09/2010	12/2012	27(R1)	0/15
217	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
218	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	1,335.69	12/2012	12/2012	0(O)	0/0
219	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00	5,915.00	1,145.94	11/2012	12/2012	1(O)	0/0
220	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	998.68	11/2012	12/2012	1(O)	0/0
221	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	83.08	12/2012	12/2012	0(O)	0/0
222	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	-	01/2013	01/2013	0(O)	0/0
223	Transmission System for phase-1 generation project - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	-	02/2013	02/2013	0(O)	0/0
224	Tapovan-Vishnugad HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	924.16	03/2013	03/2013	0(O)	5/31
225	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,280.08	05/2013 05/2013	05/2013	0(R3)	77/22
226	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	1,420.34	08/2013	08/2013	0(O)	0/0
227	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	973.67	01/2012	09/2013	20(O)	2/10
228	BARH STTP STAGE -II (NTPC) - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	1,143.48	08/2013	10/2013	2(O)	0/0
229	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	6,285.33	4,263.27	09/2010	12/2013	39(O)	2/11
230	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	2,953.44	09/2009	07/2014	58(O)	1/20
231	BARH STTP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	5,119.97	11/2010	09/2014	46(O)	15/51
232	Transm System for development of Pooling strn. in N - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
233	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00	3,124.76	249.53	07/2010	03/2015	56(O)	0/0
234	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	2,491.58	126.25	07/2014	03/2015	8(O)	0/8
235	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	487.22	07/2014	01/2016	18(O)	0/0
236	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,Manipur	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
237	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 877.06	913.63	217.13	07/2006 -	-	-	2/5
238	SEWA- II H.E.P (NHPC) - [180100220]NHPC,J & K	09/2003	665.46 -	1,016.74	961.39	09/2007 -	-	-	8/3
239	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	776.41	12/2007 -	-	-	14/18
Total			182,037.84 -	187,852.55	77,473.08				275/625
<u>Railways</u>									
240	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 -	281.20	310.09	- -	09/2010	-	0/0
241	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]RVNL,Kerala	07/2006	246.50 246.50	246.50	-	03/2009 03/2009	11/2009	8(R3)	0/0
242	MIRAJ-LATUR ROAD(GC),CR - [220100162]CR,Maharashtra	04/1993	225.00 323.00	816.40	824.67	03/2001 -	03/2010	108(O)	0/0
243	BHILDI-SAMDARI (GC) - [220100291]RVNL,Gujarat	04/1999	244.74 479.00	479.00	476.85	- 03/2009	03/2010	12(R1)	0/0
244	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 732.80	732.80	228.70	03/2008 06/2008	03/2010	21(R3)	0/0
245	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	241.77	03/2008 03/2009	10/2010	19(R1)	0/0
246	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	24.68	02/2015 -	11/2010	-51(O)	0/0
247	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	724.31	694.87	- -	12/2010	-	0/0
248	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	205.78	- 02/2009	12/2010	22(R1)	0/0
249	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	155.49	- 03/2009	12/2010	21(R1)	0/0
250	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	124.14	12/2007 03/2010	12/2010	9(R1)	0/0
251	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	267.19	03/2009 12/2008	12/2010	24(R1)	0/0
252	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 200.80	200.80	173.77	- -	12/2010	-	0/0
253	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 -	4,103.20	4,008.88	- -	12/2010	-	0/1
254	DEOGHAR-DUMKA NEW BG LINE (DOUBL.) (ER) - [220100264]ER,Jharkhand	02/1999	180.73 -	358.00	328.25	12/2006 12/2008	02/2011	26(R1)	0/0
255	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.16	413.63	02/2010 -	02/2011	12(O)	0/0
256	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056]GC,Karnataka	12/1992	46.00 -	218.00	227.16	- -	02/2011	-	0/0
257	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	356.97	06/1999 -	03/2011	141(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
258	MUZAFFARPUR-SITAMARHI(NL), ECR - [220100194] ECR, Bihar	03/1997	100.00	322.29	376.91	-	03/2011	-	0/0
259	RANCHI-LOHARDAGA(GC), SER - [220100214] SER, Jharkhand	04/1997	193.78	456.45	247.29	06/2004	03/2011	81(O)	0/0
260	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] NCR, Multi State	09/1998	925.00	925.00	474.60	05/2008	03/2011	34(O)	0/0
261	AGRA-ETAWAH VIA FATEBAD & BAD (NL), NCR - [220100243] NCR, Uttar Pradesh	04/1999	108.00	214.09	152.40	12/2009	03/2011	15(O)	0/0
262	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267] SCR, Andhra Pradesh	05/2002	304.50	306.00	341.81	-	03/2011	-	0/0
263	KHURDA ROAD-BOLANGIR(NL) ECR - [220100284] ECR, Orissa	04/1994	355.38	700.00	102.44	-	03/2011	-	0/0
264	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313] NWR, Rajasthan	04/1997	143.92	168.80	70.43	-	03/2011	-	0/0
265	HATHUA-BHATNI (N L) (NER) - [220100319] NER, Multi State	04/2005	200.73	230.03	129.96	-	03/2011	-	0/0
266	BILASPUR-URKURA (DL) - [220100321] RVNL, Chhattisgarh	04/1997	151.52	273.00	263.77	-	03/2011	24(R1)	0/0
267	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002] ECR, Bihar	04/1996	114.01	348.78	318.29	-	03/2011	-	0/0
268	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027] RVNL, Multi State	04/2005	240.00	329.70	268.75	03/2009	03/2011	15(R1)	0/0
269	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082] NEFR, Multi State	12/2006	170.00	272.11	212.76	-	03/2011	-	0/0
270	BARDHAMAN-KATWA, ER (GC) - [N22000091] GC, West Bengal	04/2007	245.15	245.15	69.84	12/2010	03/2011	3(O)	0/0
271	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094] RE, Uttar Pradesh	02/2008	171.10	171.10	43.83	03/2011	03/2011	0(O)	0/0
272	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095] RE, Uttar Pradesh	03/2006	258.35	258.35	9.38	03/2011	03/2011	0(O)	0/0
273	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096] GC, Gujarat	04/2006	196.97	196.97	123.20	03/2011	03/2011	0(O)	0/0
274	PANSPURA-KHARAGPUR 3D LINE - [N22000076] RVNL, West Bengal	09/2007	252.50	252.50	93.70	02/2010	11/2011	21(O)	0/0
275	HARIDASPUR-PARADEEP(NL) - [220100285] RVNL, Orissa	04/1996	301.64	735.10	175.76	-	12/2011	27(R1)	0/0
276	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240] ECR, Bihar	04/1997	233.00	727.52	483.17	-	03/2012	-	0/0
277	KOSI BRIDGE (NL), ECR - [220100304] ECR, Bihar	04/2002	323.41	341.41	185.63	-	03/2012	-	0/0
278	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328] ECR, Orissa	04/2005	726.96	810.78	75.92	-	03/2012	-	0/0
279	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028] MRT, Tamil Nadu	04/2006	415.59	495.74	89.61	-	03/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
280	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	324.90	116.94	03/2010	03/2012	24(O)	0/0
281	TAMLUK DIGHA - [N22000097]LD,West Bengal	03/1984	293.97	293.97	313.13	06/2005	04/2012	82(O)	0/0
282	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	288.01	- -	07/2012	-	0/0
283	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	480.90	03/1994	12/2012	225(O)	0/0
284	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	2,100.00	513.78	- -	12/2012	-	0/0
285	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1997	248.44 576.27	1,103.47	686.43	- -	12/2012	-	0/0
286	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	383.15	863.23	325.79	- -	12/2012	-	0/0
287	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	234.45	162.92	- -	12/2012	-	0/0
288	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00	1,389.00	381.86	03/2009	12/2012	45(O)	0/0
289	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47	1,389.00	704.37	10/2007	12/2012	62(O)	0/0
290	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	125.24	03/2010	12/2012	33(O)	0/0
291	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]LD,Uttar Pradesh	04/2006	325.00	369.90	88.23	03/2010	12/2012	33(O)	0/0
292	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84	410.08	101.53	- -	03/2013	-	0/0
293	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00	1,029.00	597.31	- -	03/2013	-	0/0
294	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	912.70 912.70	1,556.23	316.49	- -	03/2013	-	0/0
295	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	04/1996	1,000.00 1,500.00	3,230.02	1,933.45	04/2008 12/2011	03/2014	27(R1)	0/0
296	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	02/2000	733.00	1,655.80	520.84	12/2008	03/2014	63(O)	0/0
297	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00	160.48	98.53	- -	03/2014	-	0/0
298	AGARTALA SABROOM, NL, NEFR - [N22000099]NL,Tripura	04/2008	813.34	813.34	103.67	03/2014	03/2014	0(O)	0/0
299	BHAIRABI SAIRONG, NEFR - [N22000100]NL,Mizoram	04/2008	619.34	2,429.41	1.61	04/2014	03/2014	-1(O)	0/0
300	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66	324.66	136.27	- -	03/2015	-	0/0
301	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00	5,300.00	142.58	03/2014	03/2015	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
302	SEVOK RANGPO, NEFR - [N22000102]LD, Sikkim	04/2008	1,339.48	3,380.57	52.90	12/2015	12/2015	0(O)	0/0
303	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Multi State	04/2003	727.56 727.53	3,123.52	250.28	03/2011	03/2016	60(O)	0/0
304	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J & K	03/1995	2,500.00 8,000.00	11,270.00	6,613.74	03/2001	12/2017	201(O)	0/0
305	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 422.79	634.13	526.02	03/1995 03/2010	-	-	0/0
306	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43	617.63	378.63	-	-	-	0/0
307	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR, Gujarat	04/1992	112.53 320.66	464.50	497.71	03/1996 06/2009	-	-	0/0
308	HOTGI-GADAG(GC), SWR - [220100125]SWR, Multi State	04/1994	180.00	318.66	452.61	03/1999 03/2003	-	-	0/0
309	AMBALA-MORADABAD(RE) - [220100131]RE, Multi State	03/1993	152.21 157.76	265.00	265.33	03/1998	-	-	0/0
310	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	01/1986	36.80 274.41	285.93	232.14	-	-	-	0/0
311	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECR, Orissa	04/1993	100.00 142.98	170.00	135.03	03/2002 03/2011	-	-	0/0
312	DALLIRAJHARA-JAGDALPUR, NL, SECR - [220100149]SECR, Chhatisgarh	04/1995	369.00	968.60	0.43	-	-	-	0/0
313	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00	579.37	578.85	-	-	-	0/0
314	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, Jharkhand	04/1995	184.00	675.00	356.47	- 12/2011	-	-	0/0
315	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	1,010.00	67.32	-	-	-	0/0
316	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00	412.91	453.38	-	-	-	0/0
317	AJMER-UDAIPUR-CHITTAURGARH (GC), NWR - [220100185]NWR, Rajasthan	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
318	GONDIA-JABALPUR(GC), (SECR) - [220100186]SECR, Multi State	02/1997	356.00	511.86	413.02	03/1998	-	-	0/0
319	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL), (SWR) - [220100190]SWR, Karnataka	04/1996	157.00	465.00	102.28	- 03/2011	-	-	0/0
320	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55	712.00	399.69	-	-	-	0/0
321	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1997	155.74 164.36	429.49	352.10	02/2009	-	-	0/0
322	HUBLI-AKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00	997.58	54.19	-	-	-	0/0
323	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 598.98	1,548.95	1,101.82	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
324	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1996	377.32 236.41	497.47	72.33	- -	-	-	0/0
325	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	154.30	106.79	03/2007 03/2007	-	-	0/0
326	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
327	KODERMA-RANCHI VIA BARKAKHANA (NL), ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 -	1,099.20	829.64	07/2005 -	-	-	0/0
328	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR,Kerala	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0
329	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00 -	513.16	500.57	- -	-	-	0/0
330	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	64.99	- -	-	-	0/0
331	PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
332	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1999	242.42 369.70	369.70	159.67	- 05/2009	-	-	0/0
333	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	09/2001	320.10 -	522.56	282.57	- -	-	-	0/1
334	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	03/1997	78.23 -	162.87	79.22	- -	-	-	0/0
335	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 408.76	639.54	780.13	06/2007 -	-	-	0/0
336	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	265.87	04/2003 03/2010	-	-	0/0
337	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	418.89	- -	-	-	0/0
338	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
339	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 -	228.09	159.82	- -	-	-	0/0
340	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 240.59	607.09	250.08	- 12/2012	-	-	0/0
341	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
342	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	325.17	311.98	03/2005 12/2008	-	-	0/0
343	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	56.95	- -	-	-	0/0
344	RAJGIR-TILAIYA (NL), ECR - [220100312]ECR,Bihar	04/2001	180.82 180.82	180.82	270.13	03/2006 -	-	-	0/0
345	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	150.81	- -	-	-	0/0
346	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	104.10 -	218.19	72.12	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
347	KICHHA-KHATIMA (NL) - NER - [220100317]NER,Uttaranchal	04/2003	165.67	165.67	0.15	-	-	-	0/0
348	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79	585.93	102.78	-	-	-	0/0
349	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh	04/1992	458.45	573.12	555.49	-	-	-	0/0
350	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56	671.82	0.74	-	-	-	0/0
351	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1998	186.92	261.70	0.08	02/2006	-	-	0/0
352	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74	224.51	41.39	-	-	-	0/0
353	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09	881.19	86.35	-	-	-	0/0
354	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	72.83	-	-	-	0/0
355	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	251.23	-	-	-	0/0
356	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	15.35	-	-	-	0/0
357	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	38.60	-	-	-	0/0
358	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	529.88	26.09	-	-	-	0/0
359	KISHANGANJ JALALGARH, NEFR - [N22000101]NL,Bihar	04/2008	282.92	333.76	0.71	-	-	-	0/0
360	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]GC,Assam	04/1993	100.41	949.22	15.65	12/2009	-	-	0/0
361	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	129.54	-	03/2011	-24(R3)	0/0
362	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81	495.44	155.06	03/2004	12/2010	81(O)	0/0
363	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40	563.25	540.90	03/2004	-	-	0/0
364	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69	5,608.50	2,755.74	12/2006	09/2010	1(R3)	0/0
365	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96	762.33	310.11	-	12/2010	12(R1)	0/0
366	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36	452.35	287.65	-	03/2011	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
367	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR, Assam	09/2006	200.00	390.00	0.93	-	03/2014	-	0/0
	Total		48,823.84	103,728.73	46,164.32				0/2
<u>Road Transport & Highways</u>									
368	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	232.50	09/2009	09/2010	12(O)	0/0
369	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]NHAI, Tamil Nadu	12/2003	480.00	480.00	837.90	11/2007	11/2010	36(O)	0/0
370	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]NHAI, Andhra Pradesh	12/2003	239.19	239.19	224.50	09/2009	11/2010	14(O)	0/0
371	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]NHAI, Andhra Pradesh	12/2003	243.38	243.38	278.70	09/2008	11/2010	26(O)	0/0
372	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]NHAI, Andhra Pradesh	12/2003	205.92	205.92	204.50	08/2009	11/2010	15(O)	0/0
373	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]NHAI, Andhra Pradesh	12/2003	243.64	243.64	256.40	08/2009	11/2010	15(O)	0/0
374	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]NHAI, Andhra Pradesh	12/2003	194.80	194.80	174.30	08/2009	11/2010	15(O)	0/0
375	BANGALORE-NEELAMANGALALA NH-4 - [N24000104]NHAI, Karnataka	03/2005	445.00	445.00	802.00	07/2010	11/2010	4(O)	0/0
376	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]NHAI, Kerala	04/2000	106.00	193.00	141.70	08/2006	12/2010	52(O)	0/0
377	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	99.15	08/2004	12/2010	76(O)	0/0
378	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	110.72	08/2004	12/2010	76(O)	0/0
379	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI, Bihar	04/2000	205.73	205.73	244.60	07/2004	12/2010	77(O)	0/0
380	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY (NHAI) OTHERS - [240106203]NHAI, Tamil Nadu	12/2003	210.00	210.00	653.80	04/2007	12/2010	44(O)	0/0
381	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	275.00	284.10	09/2007	12/2010	39(O)	0/0
382	GAGODHAR-GARAMORE (PK-IV, NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78	479.54	424.60	11/2007	12/2010	37(O)	0/0
383	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI, Uttar Pradesh	12/2003	193.00	193.00	305.80	10/2008	12/2010	26(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
384	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00	217.00	332.40	10/2008	12/2010	26(O)	0/0
385	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	140.30	03/2008	12/2010	33(O)	0/0
386	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	105.30	03/2008	12/2010	33(O)	0/0
387	MADURAI - KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36	323.36	189.90	03/2008	12/2010	33(O)	0/0
388	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]NHAI,Uttar Pradesh	12/2003	239.00	239.00	389.90	10/2008	12/2010	26(O)	0/0
389	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI,Uttar Pradesh	12/2003	205.00	205.00	312.40	10/2008	12/2010	26(O)	0/0
390	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI,Uttar Pradesh	12/2003	212.00	212.00	363.60	10/2008	12/2010	26(O)	0/0
391	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	12/2010	23(O)	0/0
392	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	905.80	11/2010	12/2010	1(O)	0/0
393	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam	12/2003	230.00	230.00	291.80	06/2008	12/2010	30(O)	0/0
394	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]NHAI,Bihar	12/2003	291.80	291.80	431.30	06/2008	12/2010	30(O)	0/0
395	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	257.50	10/2008	12/2010	26(O)	0/0
396	SAGAR - RAJMARG CHORAH,KM 255-297, NH-26 (NHAI) - [240106302]NHAI,Madhya pradesh	12/2003	206.96	206.96	281.90	10/2008	12/2010	26(O)	0/0
397	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	172.10	07/2008	12/2010	29(O)	0/0
398	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	477.00	03/2009	12/2010	21(O)	0/0
399	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	202.70	06/2008	12/2010	30(O)	0/0
400	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	187.80	11/2008	12/2010	25(O)	0/0
401	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	305.40	12/2008	12/2010	24(O)	0/0
402	THANJAVUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	574.40	06/2009	12/2010	18(O)	0/0
403	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]NHAI,Andhra Pradesh	12/2003	208.46	208.46	194.40	08/2009	12/2010	16(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
404	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	182.20	06/2010	12/2010	6(O)	0/0
405	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI, Karnataka	03/2005	565.00	565.00	881.00	07/2010	12/2010	5(O)	0/0
406	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	88.78	02/2004	12/2010	82(O)	0/0
407	GONDE-VADAPE (THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI, Maharashtra	03/2005	579.00	579.00	678.70	04/2009	01/2011	21(O)	0/0
408	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	189.30	06/2008	01/2011	31(O)	0/0
409	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya pradesh	12/2003	300.93	300.93	232.10	10/2009	01/2011	15(O)	0/0
410	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	340.00	07/2010	01/2011	6(O)	0/0
411	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	285.00	241.40	07/2010	01/2011	6(O)	0/0
412	END OF DURGA BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	411.40	01/2011	01/2011	0(O)	0/0
413	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	140.00	09/2007	03/2011	42(O)	0/0
414	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	03/2011	72(O)	0/0
415	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	337.70	03/2005	03/2011	72(O)	0/0
416	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]NHAI, Uttar Pradesh	12/2003	158.06	158.06	158.30	08/2005	03/2011	67(O)	0/0
417	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI, Bihar	12/2003	239.00	239.00	273.50	07/2005	03/2011	68(O)	0/0
418	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]NHAI, Bihar	12/2003	275.00	275.00	299.70	07/2005	03/2011	68(O)	0/0
419	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	207.20	10/2008	03/2011	29(O)	0/0
420	ORAI TO JHANSI (UP-4), NH-25, KM.170.0 TO KM.104.0 - [240106249]NHAI, Uttar Pradesh	12/2003	451.97	451.97	510.30	04/2008	03/2011	35(O)	0/0
421	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	304.50	03/2008	03/2011	36(O)	0/0
422	MEERUT-MUZZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI, Uttar Pradesh	03/2005	359.00	359.00	632.80	03/2009	03/2011	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
423	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI,Assam	12/2003	225.00	225.00	204.40	06/2008	03/2011	33(O)	0/0
424	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	140.20	11/2008	03/2011	28(O)	0/0
425	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	208.50	10/2008	03/2011	29(O)	0/0
426	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	490.30	06/2008	03/2011	33(O)	0/0
427	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	275.40	06/2009	03/2011	21(O)	0/0
428	BARA TO ORAI, NH-2, 25 - [N24000069]NHAI,Uttar Pradesh	12/2003	465.00	465.00	36.22	04/2009	03/2011	23(O)	0/0
429	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00	309.00	538.30	06/2010	03/2011	9(O)	0/0
430	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	257.50	12/2009	03/2011	15(O)	0/0
431	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	243.60	09/2009	03/2011	18(O)	0/0
432	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	184.60	09/2009	03/2011	18(O)	0/0
433	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	632.80	07/2010	03/2011	8(O)	0/0
434	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	133.20	09/2010	03/2011	6(O)	0/0
435	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	227.93	02/2004	04/2011	86(O)	0/0
436	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	328.60	12/2008	05/2011	29(O)	0/0
437	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	589.20	08/2010	05/2011	9(O)	0/0
438	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI,Madhya pradesh	11/2008	549.00	549.00	657.40	05/2010	05/2011	12(O)	0/0
439	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	425.90	05/2010	05/2011	12(O)	0/0
440	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	175.10	09/2007	06/2011	45(O)	0/0
441	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	69.02	09/2008	06/2011	33(O)	0/0
442	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	282.80	10/2008	06/2011	32(O)	0/0
443	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	314.60	12/2008	06/2011	30(O)	0/0
444	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	220.00	09/2008	06/2011	33(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
445	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	205.60	10/2008 -	06/2011	32(O)	0/0
446	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	150.30	10/2008 -	06/2011	32(O)	0/0
447	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	524.50	10/2009 -	06/2011	20(O)	0/0
448	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04 -	418.04	253.30	03/2010 -	06/2011	15(O)	0/0
449	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	485.80	07/2010 -	06/2011	11(O)	0/0
450	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	598.50	01/2011 -	06/2011	5(O)	0/0
451	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	06/2011	0(O)	0/0
452	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	1,285.00	08/2011 -	08/2011	0(O)	0/0
453	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	145.54	04/2004 -	10/2011	90(O)	0/0
454	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	207.60	06/2008 -	10/2011	40(O)	0/0
455	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	70.51	10/2011 -	10/2011	0(O)	0/0
456	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	970.50	10/2011 -	10/2011	0(O)	0/0
457	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	8.92	10/2011 -	10/2011	0(O)	0/0
458	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI,Bihar	12/2003	305.00 -	305.00	468.80	06/2008 -	11/2011	41(O)	0/0
459	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	133.40	10/2008 -	11/2011	37(O)	0/0
460	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	1,108.00	1,344.00	11/2011 -	11/2011	0(O)	0/0
461	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	137.90	06/2005 -	12/2011	78(O)	0/0
462	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	170.90	02/2009 -	12/2011	34(O)	0/0
463	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	63.86	04/2009 -	12/2011	32(O)	0/0
464	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	125.80	06/2008 -	12/2011	42(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
465	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	122.90	06/2008 -	12/2011	42(O)	0/0
466	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	147.60	10/2008 -	12/2011	38(O)	0/0
467	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	351.50	09/2008 -	12/2011	39(O)	0/0
468	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	193.80	06/2008 -	12/2011	42(O)	0/0
469	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	253.90	03/2008 -	12/2011	45(O)	0/0
470	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	148.70	06/2008 -	12/2011	42(O)	0/0
471	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	168.60	04/2008 -	12/2011	44(O)	0/0
472	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	86.84	05/2008 -	12/2011	43(O)	0/0
473	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	152.50	06/2008 -	12/2011	42(O)	0/0
474	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	96.20	04/2008 -	03/2012	47(O)	0/0
475	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	141.70	04/2008 -	03/2012	47(O)	0/0
476	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	76.40	04/2010 -	03/2012	23(O)	0/0
477	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	177.40	02/2010 -	03/2012	25(O)	0/0
478	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	914.50	02/2010 -	05/2012	27(O)	0/0
479	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	199.08	05/2012 -	05/2012	0(O)	0/0
480	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	374.50	05/2012 -	05/2012	0(O)	0/0
481	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	835.00	67.60	06/2012 -	06/2012	0(O)	0/0
482	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	95.50	07/2012 -	07/2012	0(O)	0/0
483	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	52.44	05/2008 -	08/2012	51(O)	0/0
484	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00 -	229.00	52.44	05/2010 -	08/2012	27(O)	0/0
485	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	405.20	09/2012 -	09/2012	0(O)	0/0
486	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	348.16	108.90	09/2007 -	06/2013	69(O)	0/0
487	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	199.81	28.48	04/2009 -	12/2013	56(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
488	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	39.49	11/2008	12/2013	61(O)	0/0
489	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	155.04	28.35	11/2008	12/2013	61(O)	0/0
490	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	212.00	37.62	09/2007	12/2013	75(O)	0/0
491	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	196.00	25.33	07/2009	12/2013	53(O)	0/0
Total			44,552.67	44,917.67	36,718.91				0/0
<u>Shipping & Ports</u>									
492	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	819.21	10/2008	11/2010	25(O)	0/0
493	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	253.36	221.98	06/2007 07/2009	12/2010	17(R3)	0/0
494	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]PORT TRUST,Kerala	03/2007	245.67	298.17	297.86	04/2009	12/2010	20(O)	0/0
495	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
496	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
497	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00	165.00	107.58	12/2005	01/2011	61(O)	0/0
498	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,140.00	0.38	02/2011	02/2011	0(O)	0/0
499	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]SHIPP.,Maharashtra	08/2007	586.58	586.58	475.09	11/2010	03/2011	4(O)	0/0
500	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	1.02	03/2011	03/2011	0(O)	0/0
501	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	294.50	04/2011	04/2011	0(O)	0/0
502	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	290.85	290.85	72.59	03/2011	06/2011	3(O)	0/0
503	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra	08/2008	1,108.12	1,168.42	760.64	04/2011	12/2011	8(O)	0/0
504	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03	277.03	55.41	09/2011	12/2011	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
505	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
506	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	2,916.97	01/2012	01/2012	0(O)	0/0
507	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	252.00	-	03/2012	03/2012	0(O)	0/0
508	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
509	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
510	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00	272.50	-	01/2009	05/2013	52(O)	0/0
511	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.22	10/2008	-	-	0/0
512	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
	Total		15,469.90	15,925.66	6,496.03				0/0
	Telecommunications								
513	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	234.24	02/2008	09/2010	31(O)	0/0
514	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	109.31	12/2005	10/2010	58(O)	0/0
515	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	306.94	03/2009	10/2010	19(O)	0/0
516	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
517	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
518	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	378.85	02/2009	10/2010	20(O)	0/0
519	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	392.44	164.58	03/2009	10/2010	19(O)	0/0
520	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	215.65	09/2009	11/2010	14(O)	0/0
521	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]BSNL,Madhya pradesh	06/2008	908.30	916.70	211.83	08/2009 11/2010	11/2010	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
522	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81	336.81	105.16	01/2009	11/2010	22(O)	0/0
523	Procurement of DXC equipment - [N26000074]BSNL, Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
524	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL, Punjab	09/2008	241.49	241.49	90.14	09/2009	11/2010	14(O)	0/0
525	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84	336.84	31.06	10/2009	11/2010	13(O)	0/0
526	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL, Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	11/2010	9(O)	0/0
527	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) - [N26000090]BSNL, Madhya pradesh	11/2009	916.70	916.70	211.83	11/2010	11/2010	0(O)	0/0
528	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL, Kerala	01/2009	848.70	848.70	439.28	01/2010	11/2010	10(O)	0/0
529	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00	384.00	12.73	10/2010	11/2010	1(O)	0/0
530	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00	247.00	73.73	02/2007	12/2010	46(O)	0/0
531	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]BSNL, West Bengal	09/2006	208.50	208.50	146.00	09/2008	12/2010	27(O)	0/0
532	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL, Rajasthan	06/2007	601.49	601.49	475.27	12/2008	12/2010	24(O)	0/0
533	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL, Haryana	01/2008	192.48	192.48	110.88	03/2009	12/2010	21(O)	0/0
534	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94	373.94	176.33	12/2008	12/2010	24(O)	0/0
535	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL, Uttar Pradesh	05/2007	335.91	335.91	169.43	03/2009	12/2010	21(O)	0/0
536	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL, Uttaranchal	01/2009	149.15 158.72	158.72	88.17	06/2009	12/2010	18(O)	0/0
537	Procurement of 2.5G DWDM equipment - [N26000066]BSNL, Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
538	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL, Multi State	08/2006	590.10	590.10	-	03/2009	12/2010	21(O)	0/0
539	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL, Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
540	Procurement of STM-1 SDH equipment - [N26000069]BSNL, Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
541	Procurement of STM-16 MADM equipment - [N26000070]BSNL, Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
542	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
543	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	75.25	09/2010	12/2010	3(O)	0/0
544	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	127.42	06/2009	12/2010	18(O)	0/0
545	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	219.08	10/2008	12/2010	26(O)	0/0
546	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	274.30	08/2009	12/2010	16(O)	0/0
547	GSM equipment of 1900000Lines (2G) 401700 lines 3(-) [N26000091]BSNL,Tamil Nadu	01/2009	760.20	810.37	741.75	01/2010	12/2010	11(O)	0/0
548	GSM equipment of 1700000Lines (2G) 234100 lines 3(-) [N26000092]BSNL,Karnataka	10/2008	677.75 719.70	719.70	303.34	10/2009	12/2010	14(O)	0/0
549	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	266.06	01/2010	12/2010	11(O)	0/0
550	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	107.41	01/2010	12/2010	11(O)	0/0
551	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007	03/2011	49(O)	0/0
552	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	09/2011	389.86	389.86	2.13	09/2011	09/2011	0(O)	0/0
553	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
554	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
555	CENTRALISED TRANSMISSION NMS - [N26000064]BSNL,Multi State	08/2009	300.00	300.00	-	-	-	-	0/0
556	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	-	-	0/0
Total			21,442.79	21,913.49	7,112.04				0/0
<u>Urban Development</u>									
557	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00 8,605.36	18,894.36	16,066.27	06/2010	11/2010	5(O)	0/8
558	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,954.59	12/2011	03/2013	15(O)	6/6
Total			15,071.00	30,503.36	19,020.86				6/14
<u>Water Resources</u>									

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
559	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			578,217.92	698,067.04	300,519.72				797/2045


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

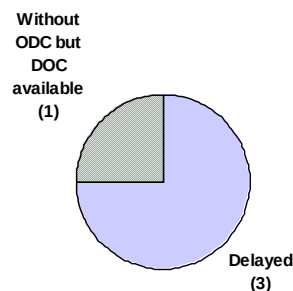

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs. 19135.89 Crores.

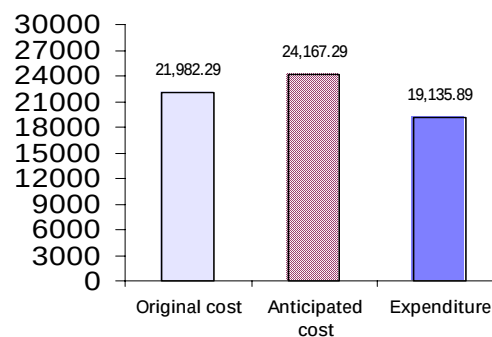


2. Sector: - Civil Aviation

Number of Projects	9
Number of Projects on schedule	5
Number of Projects Delayed	3
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 5 projects are on schedule, 3 projects are delayed and 1 projects are original date of commissioning.

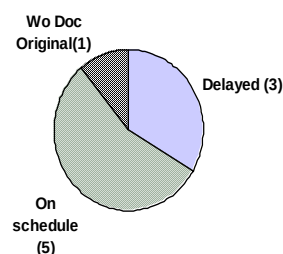

Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 5347.40 Crores but this was subsequently revised to Rs. 5347.40 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs 2786.90 Crores.

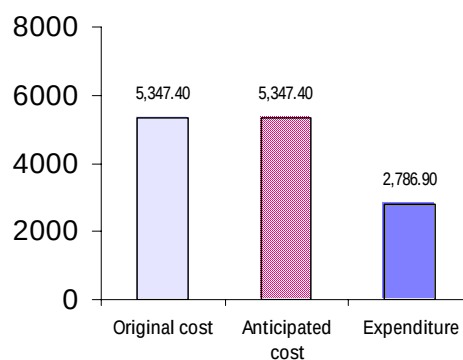


3. Sector: - Coal

Number of Projects	44
Number of Projects on schedule	14
Number of Projects Delayed	19
Number of Projects Ahead	3
Number of Projects Wo_ODC_Original	7
Number of Projects Wo_DOC_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 44 projects, 14 projects are on schedule, 19 projects are delayed and 3 projects are ahead and 7 Project W_Odc_Original and 1 Project W_Odc_Original .

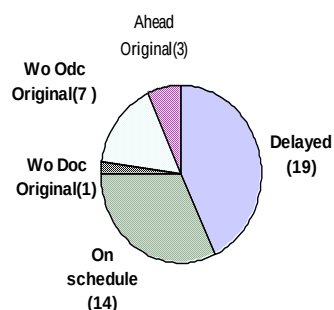

Investment Scenario

The total cost of implementation of 44 projects when sanctioned, was of the order of Rs. 25210.30 Crores but this was subsequently revised to Rs. 28542.29 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs 10241.68 Crores

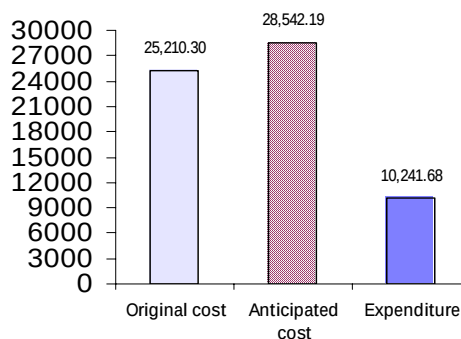


4. Sector: - Petroleum

Number of Projects	71
Number of Projects on schedule	26
Number of Projects Delayed	33
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	1
Number of Projects Without original date of commissioning	8


Brief Analysis

Project Status with respect to Original Schedule: Out of 71 projects, 26 projects are on schedule, 33 projects are delayed and 3 projects are ahead and 1 projects is without date of commissioning and 8 Project is Without original date of commissioning.

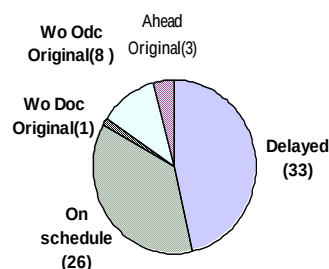

Investment Scenario

The total cost of implementation of 71 projects when sanctioned, was of the order of Rs. 145231.54 Crores but this was subsequently revised to Rs. 160004.07 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs. 49198.56 Crores.

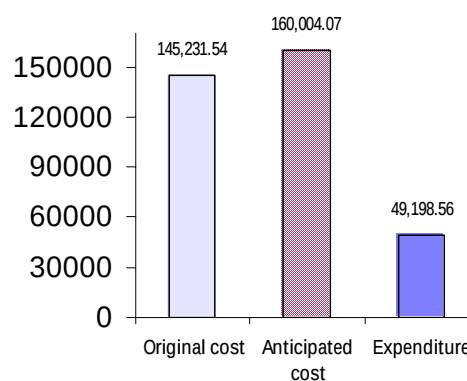


5. Sector: - Power


Number of Projects	88
Number of Projects on schedule	38
Number of Projects Delayed	40
Number of Projects Ahead	4
Number of Projects Wo_Doc_Original	5
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 88 projects, 38 projects are on schedule, 40 projects are delayed, and 4 Projects are Ahead, 5 projects are without date of commissioning and 1 project is without original date of commissioning

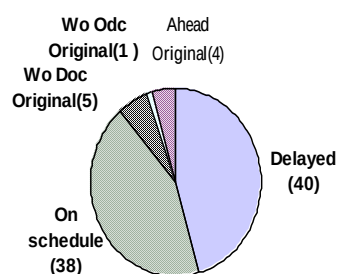

Investment Scenario

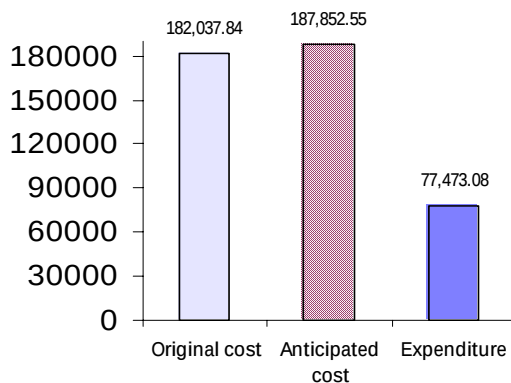


The total cost of implementation of 88 projects when sanctioned, was of the order of Rs. 182037.84 Crores but this was subsequently revised to Rs. 187852.55 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs. 77473.08 Crores.

6. Sector: - Railways

Number of Projects	128
Number of Projects on schedule	5
Number of Projects Delayed	25
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	60
Number of Projects Wo_Odc_Original	36


Brief Analysis

Project Status with out respect Original Schedule: Out of 128 projects, 5 projects are on schedule, 25 projects are delayed, 2 projects is ahead. 60 projects are Without date of commissioning and 36 projects are without original date of commissioning.

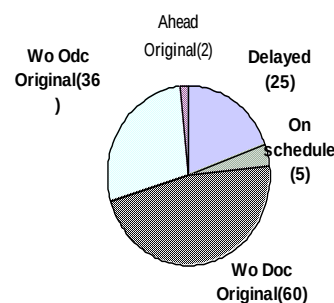

Investment Scenario

The total cost of implementation of 128 projects when sanctioned, was of the order of Rs. 48823.84 Crores but this was subsequently revised to Rs. 103726.73 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs. 46164.32 Crores.

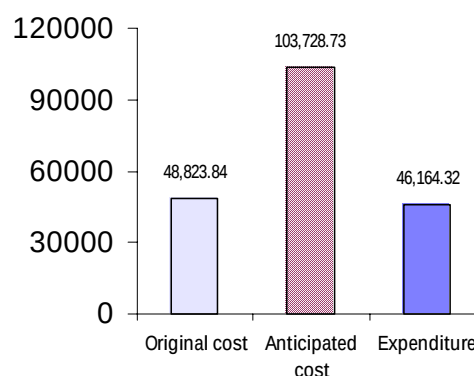


7. Sector: - Road Transport and Highways

Number of Projects	124
Number of Projects on schedule	12
Number of Projects Delayed	111
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 124 projects, 12 projects are on schedule, 111 projects are delayed 1 projects are Without date of commissioning



Investment Scenario

The total cost of implementation of 124 projects when sanctioned, was of the order of Rs 44662.67 Crores but this was subsequently revised to Rs. 44917.67 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs. 36718.91 Crores.

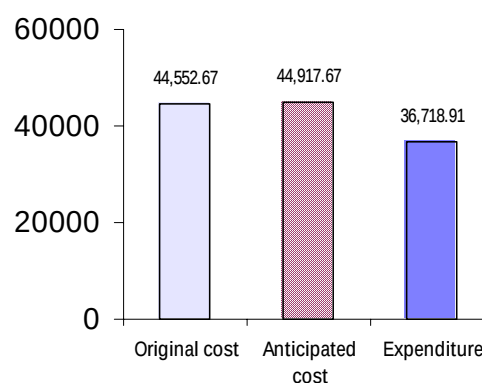


8. Sector: - Shipping and Ports

Number of Projects	21
Number of Projects on schedule	7
Number of Projects Delayed	10
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 21 projects, 7 projects are on schedule, 10 projects are delayed, 2 projects are ahead and 2 projects are without date of commissioning.

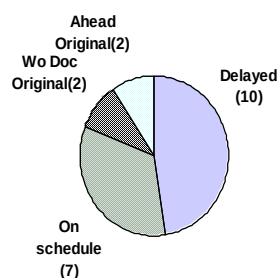

Investment Scenario

The total cost of implementation of 21 projects when sanctioned, was of the order of Rs.15469.90 Crores but this was subsequently revised to Rs. 15925.66 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs. 6496.03 Crores.

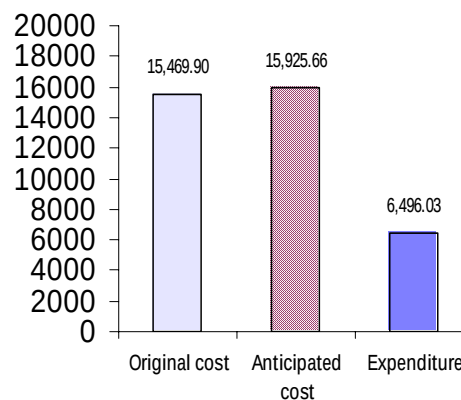


9. Sector: - Steel

Number of Projects	16
Number of Projects On schedule	3
Number of Projects Delayed	8
Number of Projects Wo_Doc_Original	4
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 16 projects, 8 projects are delayed and 3 projects are on Schedule and 4 projects are Wo_Doc_Original and 1 Project is Wo_Odc_Original.

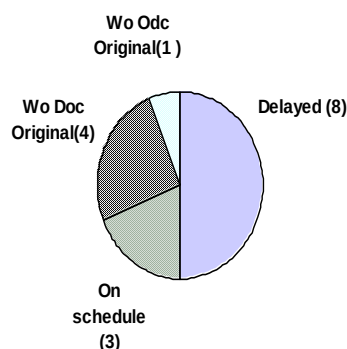

Investment Scenario

The total cost of implementation of 16 projects when sanctioned, was of the order of Rs.43096.53 Crores but this was subsequently revised to Rs. 64258.46 Crores. The expenditure incurred on these projects till Oct, 2010 is Rs. 25912.86Crores.

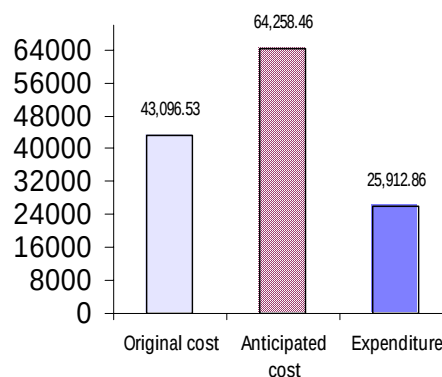


10. Sector: - Telecommunications

Number of Projects	44
Number of Projects Delayed	37
Number of Projects on Schedule	2
Number of Projects Wo_Doc_Original	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 44 projects, 37 projects are delayed and 5 projects are with out date of commissioning, and 2 projects are on schedule.



Investment Scenario

The total cost of implementation of 44 projects when sanctioned, was of the order of Rs 21442.79 Crores but this was subsequently revised to Rs. 21913.49 Crores. The expenditure incurred on these projects till Sep, 2010 is Rs 7112.04 Crores.

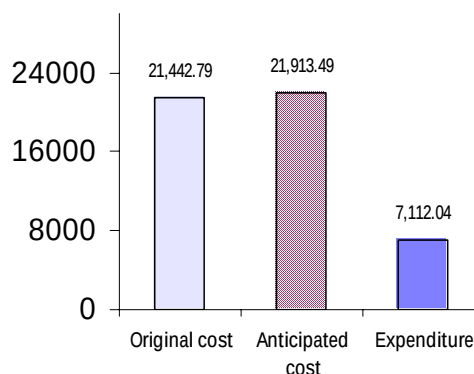

STATE WISE PROJECTS AS ON 01.11.2010

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	EXPENDITURE CUMM
1	Andhra Pradesh	34	28571.31	35076.77	16882.04
2	Arunachal Pr.	4	9512.22	9516.70	5773.43
3	Assam	40	23365.64	28402.60	11912.61
4	Bihar	31	29643.83	33099.19	17733.61
5	Chhatisgarh	16	20403.09	35378.16	12683.99
6	Delhi	2	8925.00	19123.77	16132.47
7	Goa	1	204.73	204.73	5.97
8	Gujarat	21	14926.08	17350.49	10301.59
9	Haryana	12	5888.87	6560.88	3832.25
10	Himachal Pr.	8	15381.72	15463.96	10304.92
11	J & K	9	8963.30	19472.30	10798.08
12	Jharkhandd	21	9761.89	14698.51	5214.89
13	Karnataka	18	15490.06	23417.38	10651.77
14	Kerala	11	9511.93	10939.72	8582.19
15	Madhya pradesh	26	19323.72	19588.25	7039.39
16	Maharashtra	49	63477.28	83086.69	27659.29
17	Manipur	1	578.62	578.62	28.33
18	Mizoram	2	988.06	3343.04	218.74
19	Multi State	100	118880.36	122886.56	32105.36
20	Orissa	26	49676.93	53643.23	10420.80
21	Punjab	9	5064.09	5994.12	1991.02
22	Rajasthan	10	9050.45	9778.51	6145.82
23	Sikkim	2	1603.77	3644.86	317.19
24	Tamil Nadu	33	40175.98	45866.09	32094.88
25	Tripura	3	1522.39	1724.82	161.82
26	Uttar Pradesh	39	24151.87	26070.62	15164.78
27	Uttaranchal	9	12100.46	14663.75	4159.03
28	West Bengal	22	31074.27	38492.72	22203.46
TOTAL		559	578217.92	698067.04	300519.72

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
