

**336th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
October 2013**



NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-70
Sector wise Graph	71-81
ANNEXURE	82-82
Central Sector Projects	83-83
List of Projects Having Expenditure More than cost	84-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-106
List of On schedule Projects Original Schedule	107-113
List of Delayed Projects w.r.t Original Schedule	114-127
List of Projects Having Time and cost overrun w.r.t original	128-132
List of Projects Having cost overrun w.r.t original	133-144
List of Projects without Milestones	145-166
List of On schedule Projects w.r.t. Latest Schedule	167-174
List of Projects Ahead of Schedule w.r.t Latest Schedule	175-175
List of Delayed Projects w.r.t Latest Schedule	176-189

कार्यकारी सारांश

अक्टूबर, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 739 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अक्टूबर, 2013 के दौरान 5 परियोजनाओं (विद्युत तथा रेलवे प्रत्येक की 2 परियोजनाएं तथा दूरसंचार क्षेत्र की 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 739 परियोजनाओं में से 289 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 33 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 33 परियोजनाओं में से, 17 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। परमाणु ऊर्जा, पोत परिवहन तथा पत्तन, कोयला, इस्पात, विद्युत, रेलवे तथा पेट्रोलियम क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 24 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	286	38	6	3
2.	सड़क परिवहन एवं राजमार्ग	151	100	0	0
3.	विद्युत	98	52	5	2
4.	पेट्रोलियम	85	44	8	4
5.	कोयला	55	30	5	3
6.	पोत परिवहन एवं पत्तन	19	1	1	1
7.	इस्पात	18	12	7	3
8.	दूरसंचार	9	4	0	0
9.	नागर विमानन	8	3	0	0
10.	परमाणु ऊर्जा	4	4	1	1
11.	शहरी विकास	4	1	0	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		739	289	33	17

3. 739 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ` 9,08,391.61 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ` 10,87,044.20 करोड़ रुपए होने की संभावना है जो ` 1,78,652.59 करोड़ (मूल लागत का 19.70%) की समग्र लागत वृद्धि को दर्शाता है। अक्टूबर, 2013 तक इन परियोजनाओं पर किया गया व्यय ` 5,11,194.29 करोड़ है जो परियोजनाओं की अनुमानित लागत का 47.00% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.10.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (` करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (31.10.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
3	सुबानश्री लोअर एचईपी (एनएचपीसी)	विद्युत	09/2003	6285.33	10667.00	4381.67
4	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00
5	बोगीबिल एंड लिंक लाईन पर ब्रह्मपुत्र पुल एनईएफआर	रेलवे	09/1997	1000.00	4996.65	3996.65

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 739 परियोजनाओं में से, 4 परियोजनाएं समय से पहले चल रही हैं, 157 समय पर तथा 289 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 301 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 27 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 262 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 289 विलंबित परियोजनाओं में से, 66 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 73 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 78 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 72 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.10.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
2	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	09/2013	138

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. समय एवं लागत वृद्धि के संबंध में गंभीर रूप से प्रभावित इन परियोजनाओं की समीक्षा में, रेल मंत्रालय ने सूचित किया है कि रेलवे परियोजनाओं को आगे बढ़ाने की दृष्टि से परित्यक्त बहुत ही कम है और वर्तमान मुद्रास्फीति को निष्क्रिय करने हेतु अपर्याप्त है । इसके कारण रेलवे, परियोजनाओं को पूरा करने से संबंधित लक्ष्यों को निश्चित करने की स्थिति में नहीं है । निधि की कमी ने रेलवे को वर्ष 2010-11 तथा 2011-12 में क्रमशः 2315 किमी तथा 2337 किमी की उपलब्धि के मुकाबले वर्ष 2013-14 हेतु लक्ष्य को कम करके 1525 किमी करने को विवश किया है ।

7. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, उपस्कर संस्थापना में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, कोनिकर भूखनन, कार्यान्वयन एजेंसी का बदलाव, कार्य-क्षेत्र में बदलाव, राज्य सरकार द्वारा जनोपयोगी सेवाओं को अन्यत्र ले जाने में विलंब, , स्थान की कमी, कार्यों को प्रदान करने में विलंब, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.10.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		संचयी व्यय (रु. करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

एन.आर.: सूचित नहीं।

9. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं। पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.10.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.10.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

एन.आर.: सूचित नहीं।

10. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- I. परमाणु ऊर्जा क्षेत्र में सभी 4 परियोजनाएं विलंबित हैं। 'कुंडकुलम परमाणु ऊर्जा संयंत्र, एनपीसीआईएल' के संबंध में मेसर्स एटमस्ट्रोय एक्सपोर्ट द्वारा वायदा पूरा न करने के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।
- II. पोत परिवहन तथा पत्तन क्षेत्र में 6 परियोजनाओं में से 1 परियोजना विलंबित है। भारतीय पोत परिवहन निगम के 'मुंबई पोर्ट ट्रस्ट द्वारा 2 ऑफशोर कंटेनर बर्थ तथा टर्मिनल का निर्माण एवं विकास' परियोजना के संबंध में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।
- III. कोयला क्षेत्र में 55 परियोजनाओं में से 30 परियोजनाएं विलंबित हैं। माह के दौरान 5 परियोजनाओं के संबंध में 2-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 3 मेगा परियोजनाएं हैं। 'टीपीएस-II विस्तार'⁷(1470 मेगावाट से 1970 मेगावाट), एनएलसी तथा

'नेवेली न्यू थर्मल पावर प्रोजेक्ट (2X500 मेगावाट), एनएलसी' परियोजनाओं के संबंध में उपस्करों के संस्थापन तथा ठेकेदार द्वारा अपर्याप्त श्रमिक लगाना तथा निविदा खोलने एवं मूल्यांकन में विलंब के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट, एनएलसी', 'आद्रियालाशेफ्ट प्रोजेक्ट , एससीसीएल' तथा 'काकतिया लौंगवाल, एससीसीएल' में क्रमशः 2, 4 तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

IV इस्पात क्षेत्र में 18 परियोजनाओं में से 12 विलंबित हैं । माह के दौरान 7 परियोजनाओं के संबंध में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । जिनमें से 3 मेगा परियोजनाएं हैं । 'बेलाडिला लौह अयस्क परियोजना डिपोजिट-11बी, एनएमडीसी' तथा '1.2 एमटीपीए पैलेट संयंत्र परियोजना, डोनीमलाई, एनएमडीसी' परियोजनाओं के संबंध में कानून तथा व्यवस्था समस्या के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; '67.5 मेगावाट टीजी-5 सहायक प्रणाली आकस्मिक विद्युत मांग विस्तार इकाई, आरआईएनएल' परियोजना के संबंध में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'दुर्गापुर इस्पात संयंत्र का विस्तार, सेल' तथा 'अन्य संबद्ध सुविधाओं के साथ 45 एमबीए साफ्ट का संस्थापन, सेल' परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा '3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार, आरआईएनएल' और 'भिलाई इस्पात संयंत्र का विस्तार, सेल' परियोजनाओं के संबंध में क्रमशः 5 और 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

V रेलवे क्षेत्र में 286 परियोजनाओं में से 38 परियोजनाएं विलंबित हैं । माह के दौरान, 6 परियोजनाओं के संबंध में 3-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । इनमें से 3 मेगा परियोजनाएं हैं । 'गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड नई लाइन, एनसीआर' तथा 'लुमडिंग-सिल्चर जिरीबाम, बदरपुर-बारेग्राम कुमारघाट (राष्ट्रीय परियोजना), एनईएफआर' के संबंध में क्रमशः भूमि अधिग्रहण तथा निधि की कमी के कारण प्रत्येक परियोजना के संबंध में 3 माह के अतिरिक्त विलंब की सूचना दी गई है; 'बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर' तथा 'तैतलिया से ब्यरनीहट तक नई बीजी लाइन परियोजना (राष्ट्रीय परियोजना), एनईएफआर' के परियोजना के संबंध में निधि की कमी के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'बाडानगर से बेरकपुर तथा मेट्रो रेलवे का निर्माण हेतु नए कार्य तथा दक्षिणेश्वर (एमटीपी), आरवीएनएल' परियोजना के संबंध में राज्य सरकार द्वारा जन सुविधाओं के हटाने में विलंब के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'आगरा-इटावा बरास्ता फतेहाबाद और बाह, नई लाइन, एनसीआर' परियोजना में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

V. विद्युत क्षेत्र में, 98 परियोजनाओं में से 52 परियोजनाएं विलंबित हैं। माह के दौरान, 5 परियोजनाओं के संबंध में 1-5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 2 मेगा परियोजनाएं हैं। 'तीस्ता लो डेम, एचईपी, स्टेज-IV एनएचपीसी' परियोजना के संबंध में कानून और व्यवस्था संबंधी समस्या के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'रामपुर एचईपी से सम्बद्ध पारेषण प्रणाली, पीजीसीआईएल' तथा 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XX पीजीसीआईएल' परियोजनाओं के संबंध में क्रमशः आरओडब्ल्यू समस्या तथा कार्यान्वयन एजेंसी में बदलाव के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'एमबी पावर लि.को जोड़ने के लिए पारेषण प्रणाली, पीजीसीआईएल' एवं आईपीपी जनरेशन परियोजनाओं के लिए डब्ल्यूआर के केन्द्रीय भाग के साथ छत्तीसगढ़ में पूर्लिंग स्टेशन का एकीकरण, पीजीसीआईएल' परियोजनाओं के संबंध में वन संबंधी अनुमति में विलंब के कारण क्रमशः 3 और 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

VI. पट्रोलियम क्षेत्र में 85 परियोजनाओं में से 44 परियोजनाएं विलंबित हैं। माह के दौरान, 8 परियोजनाओं के संबंध में 1-22 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 4 मेगा परियोजनाएं हैं। 'आरआईजी सागर सम्राट को मोबाइल ऑफशोर उत्पादन यूनिट (एमओपीएस) में बदलना, ओएनजीसी' तथा '6 ईटीपी का निर्माण, ओएनजीसी' परियोजनाओं के संबंध में कार्य की धीमी गति के कारण क्रमशः 1 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'पारादीप रिफाइनरी परियोजना, आईओसीएल' परियोजना के संबंध में वन संबंधी अनुमति तथा खराब मौसम की स्थिति के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'विजाग में स्ट्रेटेजिक क्रूड ऑयल स्टोरेज प्रोजेक्ट, आईएसपीआरएल' परियोजना के संबंध में विपरीत भू-खनन परिस्थिति के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'मंगलौर में स्ट्रेटेजिक क्रूड ऑयल स्टोरेज प्रोजेक्ट, आईएसपीआरएल' परियोजना के संबंध में कार्यों को प्रदान करने में विलंब के कारण 22 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है एवं 'पारादीप हल्दिया बरौनी पाइपलाइन का संवर्धन, आईओसीएल' 'एमआरपीएल फेस-III विस्तार, मंगलौर रिफाइनरी' तथा 'एसबी-14 फील्ड का विकास, ओएनजीसी' परियोजनाओं के संबंध में क्रमशः 1, 2 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

11. दिनांक 31.10.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

12. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for October 2013 contains information on the status of the 739 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During October 2013, 5 projects (2 projects each are in Power & Railways and 1 project is in Telecommunication Sector) have reported completion.

2. During the reference month, out of 739 projects, 289 projects are delayed with respect to latest schedule and 33 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 33 projects, 17 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 24 months in respect of projects relating to Atomic Energy, Shipping & Ports, Coal, Steel, Power, Railways and Petroleum Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Railways	286	38	6	3
2.	Road Transport And Highways	151	100	0	0
3.	Power	98	52	5	2
4.	Petroleum	85	44	8	4
5.	Coal	55	30	5	3
6.	Shipping And Ports	19	1	1	1
7.	Steel	18	12	7	3
8.	Telecommunications	9	4	0	0
9.	Civil Aviation	8	3	0	0
10.	Atomic Energy	4	4	1	1
11.	Urban Development	4	1	0	0
12.	Petrochemicals	1	0	0	0
13.	Water Resources	1	0	0	0
Total		739	289	33	17

3. Total original cost of implementation of the 739 projects was about ₹ 9,08,391.61 crore and their anticipated completion cost is likely to be ₹ 10,87,044.20 crore, which reflects overall cost overruns of ₹ 1,78,652.59 crore (19.70 % of original cost). The expenditure incurred on these projects till October 2013 is ₹ 5,11,194.29 crore, which is 47.00 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-10 -2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-10-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	11609.00	5214.00
3	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
4	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00
5	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	4996.65	3996.65

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 739 projects, 4 projects are ahead of schedule, 157 are on schedule and 289 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 301 if delay is calculated on the basis of original schedule of completion. Further, 27 projects have been sanctioned without any commissioning schedule/date and for 262 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 289 delayed projects, 66 projects have overall delay in the range of 1 to 12 months, 73 projects have a delay in the range of 13 to 24 months, 78 projects have a delay in the range of 25 to 60 months and 72 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-10-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2015	240
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	141
5	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	09/2013	138

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In a review of its severely affected projects in terms of time & cost overruns, Ministry of Railways has informed that outlay for Railway projects is very low of throw forward and is insufficient even to neutralize the prevailing inflation. Due to this, Railways is not in the position to fix the targets for completion of the projects. Paucity of funds has forced Railways to scale down the targets for 2013-14 to 1525 Km against the achievement of 2315 Km and 2337 Km in 2010-11 and 2011-12 respectively.

7. The brief reasons for time overruns as reported by various other project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipment, delay in equipment erection, fund constraints, geological surprises, change in scope of work, delay in shifting of utility by State Government, adverse geo-mining, change of implementing agency, space constraint, delay in award of works ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-10-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ crore)		EXPENDITURE CUMMULATIVE (₹ crore)	DATE OF COMMISSIONING		MILE STONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-10-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.10.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

10. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Atomic Energy Sector**, all 4 projects are delayed. The project 'Kudankulam Atomic Power Plant, NPCIL' has reported additional delay of 3 months due to slippage of commitment by M/s Atomstroy Export.

ii) In the **Shipping & Ports Sector**, out of 6 projects, 1 project is delayed. The project 'Construction & Development of 2 Offshore Container Berths & Terminal, Mumbai Port Trust of Shipping Corporation of India' has reported delay of 3 months (however, no specific reasons have been reported by the project authority for the delay in this project).

iii) In the **Coal Sector**, out of 55 projects, 30 projects are delayed. During the month 5 projects have reported additional delays in the range of 2-12 months, out of which 3 are Mega project. The projects 'TPS-II Expansion (1470MW TO 1970MW), NLC' and 'Neyveli New Thermal Power Project (2x500MW), NLC' have reported additional delay of 2 months each due to delay in equipment erection & inadequate mobilization by contractor and delay in opening & evaluation of bids; and the projects 'Tuticorin Thermal Power Project- 2X500 MW, NLC' , 'Adriyala Shaft Project, SCCL' and 'Kakatiya Longwall, SCCL' have reported additional delays of 2, 4 and 12 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).

iv) In the **Steel Sector**, out of 18 projects, 12 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-6 month, out of which 3 are Mega project. The projects 'Bailadila Iron Ore Project Deposit- 11B, NMDC' and '1.2 MTPA Pellet Plant Project, Donimalai, NMDC' have reported additional delay of 3 months each due to law and order problem; the project '67.5 MW TG-5 Auxiliary System Emergency Power Requirement Expansion Unit, RINL' has reported additional delay of 1 month; the projects 'Expansion of Durgapur Steel Plant, SAIL' and 'Installation of 45MVA Saft with other Associated Facilities, SAIL' have reported additional delays of 3 months each; and the projects 'Expansion of Liquid Steel Capacity from 3MT TO 6.3MT, RINL' and 'Expansion of Bhilai Steel Plant, SAIL' have reported additional delays of 5 and 6 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).

v) In the **Railways Sector**, out of 286 projects, 38 projects are delayed. During the month 6 projects have reported additional delays in the range of 3-24 months, out of which 3 are Mega projects. The projects 'Guna-Etawah VIA Shivpuri-Gwalior -Bhind New Line, NCR' and 'Lumding-Silchar Jiribam, Badarpur-Baraigram Kumarghat (National Project), NEFR' have reported additional delay of 3 months each due to delay in land acquisition and fund constraints respectively; the projects 'Brahmaputra Bridge at Bogibil and Link Lines, NEFR' and 'New B.G. Line from Tetelia to Byrnihat (National Project), NEFR' have reported additional delay of 12 months each due fund constraints; the project 'New Work for Construction of Metro Railway from Baranagar to Barrackpore and Dakshineswar (MTP), RVNL' has reported additional delay 24 months due to delay in shifting of utility by State Government; and the project 'Agra-Etawah VIA Fatehabad and Bah. New Line, NCR' has reported additional delay of 1 month (however, no specific reasons have been reported by the project authority for the delay in this project).

vi) In the **Power Sector**, out of 98 projects, 52 projects are delayed. During the month 5 projects have reported additional delays in the range of 1-5 months, out of which 2 are Mega projects. The project 'Teesta Low Dam HEP, STAGE-IV, NHPC' has reported additional delay of 1 month due to law & order problem; the projects 'Transmission System Associated with Rampur HEP, PGCIL' and 'Northern Region System Strengthening Scheme-XX, PGCIL' have reported additional delay of 2 months each due ROW problem and change of implanting agency respectively; and the projects 'Transmission System for Connectivity of MB Power Limited, PGCIL' and 'Integration of Pooling Station in Chattisgarh with Central Part of WR for IPP Generation Projects, PGCIL' have reported additional delays of 3 and 5 months respectively due to delay in environment clearance.

vii) In the **Petroleum Sector**, out of 85 projects, 44 projects are delayed. During the month 8 projects have reported additional delays in the range of 1-22 months., out of which 4 are Mega projects, The projects 'Conversion of RIG Sagar Samrat to Mobile Offshore Production Unit (MOPS), ONGC' and 'Construction of 6 ETPs, ONGC' have reported additional delays of 1 and 3 months respectively due to slow progress of work; the project 'Paradip Refinery Project, IOCL' has reported additional delay of 2 months due to environment clearance & bad weather condition; the project 'Strategic Crude Oil Storage Project at Vizag, ISPRL' has reported additional delay of 5 months due to adverse geo-mining condition; the project 'Strategic Crude Oil Storage Project at Mangalore, ISPRL' has reported additional delay of 22 months due to delay in award of works; and the projects 'Augmentation of Paradip Haldia Barauni Pipeline

IOCL’ , ‘MRPL Phase-III Expansion, Mangalore Refinery’ and ‘Development of SB-14 Field, ONGC’ have reported additional delays of 1, 2 and 4 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).


11. The status as on 31.10.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Railways	286	6
2	Road Transport And Highways	151	0
3	Power	98	5
4	Petroleum	85	8
5	Coal	55	5
6	Shipping And Ports	19	1
7	Steel	18	7
8	Telecommunications	9	0
9	Civil Aviation	8	0
10	Atomic Energy	4	1
11	Urban Development	4	0
12	Petrochemicals	1	0
13	Water Resources	1	0
	Total	739	33

Sectoral break up of on-going infrastructure projects.

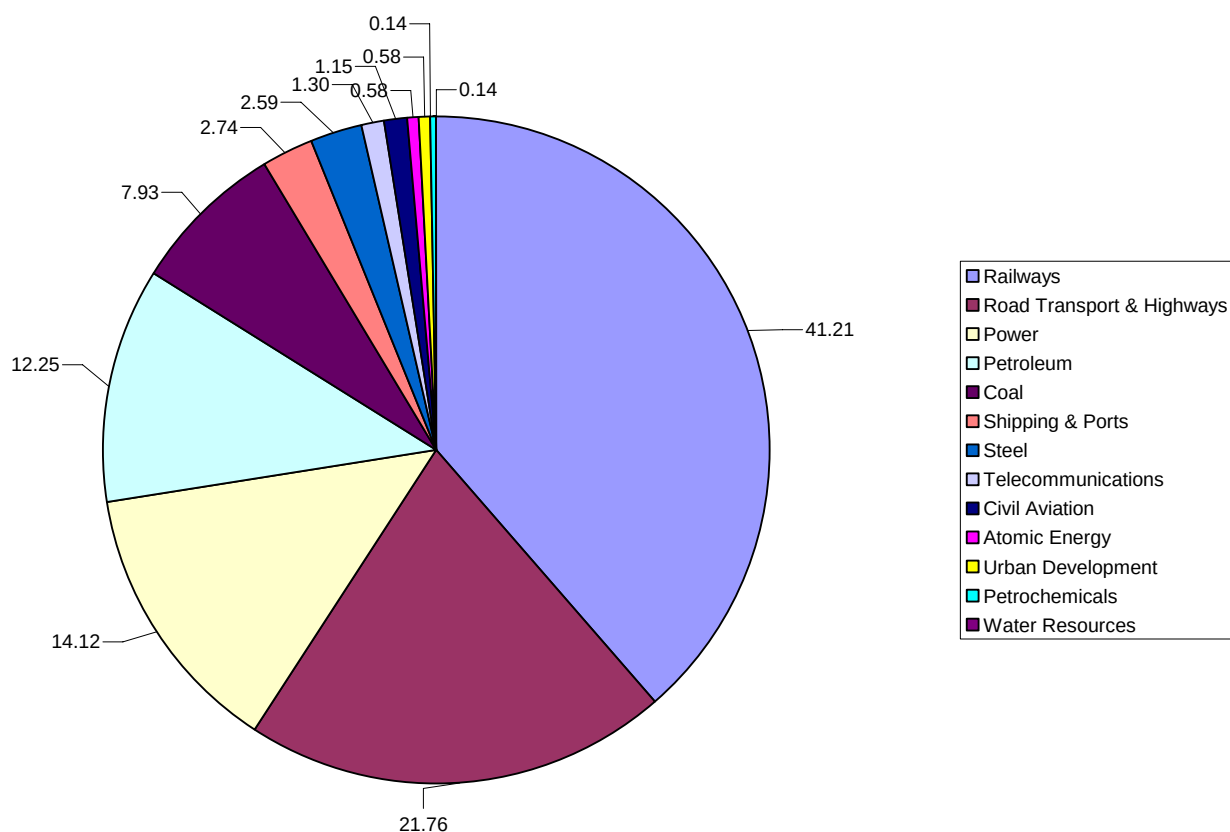

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>Power</u>			
1	Northern Region system strengthening scheme-XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>Railways</u>			
2	RENIGUNTA-GUNTAKAL(RE) (RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL) (RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>Fertilisers</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT (NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>Power</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV System for Central part of Northern Region Grid - Part-II (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>Road Transport And Highways</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56
	June,2013			
	<u>Railways</u>			
8	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000027]	240.00	03/2009	334.59
9	PANSPURA-KHARAGPUR 3D LINE (RAIL VIKAS NIGAM LTD.) - [N22000076]	252.50	02/2010	249.36
	July,2013			
	<u>Petroleum</u>			
10	North Tapti Gas Field Development (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000096]	589.70	03/2011	912.53

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>Power</u>			
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100222]	768.92	03/2007	1467.53
12	CHUTAK HYDRO-ELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000007]	621.26	02/2011	731.93
	August,2013			
13	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND BANGLADESH -INDIAN PORTION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000089]	160.32	10/2012	87.63
	<u>Railways</u>			
14	Madurai-Rameswaram-GC (SOUTHERN RAILWAY) - [N22000200]	240.00	-	367.21
15	Krishnanagar-Bethua Dahri doubling (EASTERN RAILWAYS) - [N22000226]	151.65	03/2015	90.21
16	Dharmavaram-Pakala GC (SAUTH COST RAILWAY) - [N22000284]	294.99	-	658.53
	September,2013			
	<u>Petroleum</u>			
17	Butadiene Extraction Unit(BDEU) at Panipat (INDIAN OIL CORPORATION LIMITED) - [N16000108]	341.50	02/2013	198.81
	<u>Power</u>			
18	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000046]	7,031.88	12/2012	4591.9
	<u>Road Transport And Highways</u>			
19	GWALIOR BYPASS, NH-75,3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000088]	300.93	10/2009	302.7
	October,2013			
	<u>Power</u>			
20	NIMOO BAZGO HYDROELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000006]	611.01	08/2010	883.85
21	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000018]	557.24	01/2010	648.43
	<u>Railways</u>			
22	CHANDIGARH-LUDHIANA(NEW BG LINE),NR (NORTHERN RAILWAY) - [220100241]	248.44	12/2012	972.91
23	RUPSA-BANGRIPOSI (GC)(SER) (SOUTH EASTERN RAILWAY) - [220100323]	57.94	03/1998	176.14

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>Telecommunications</u>			
24	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06 (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000029]	231.38	10/2007	86.11


Summary of projects in the Flash Report for the month of October, 2013

Project Implementation - Current Status:

Number of Projects in Previous Month	738
Number of Projects completed/dropped/frozen in Current Month	8
Number of Projects Added in Current Month	9
Number of Projects in Current Month	739


Brief Analysis

Project Status with respect to Original Schedule: Out of 739 projects, 4 projects are ahead of schedule, 145 projects are on schedule and 301 projects are delayed. Of the balance, 262 projects do not have fixed dates of commissioning while 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

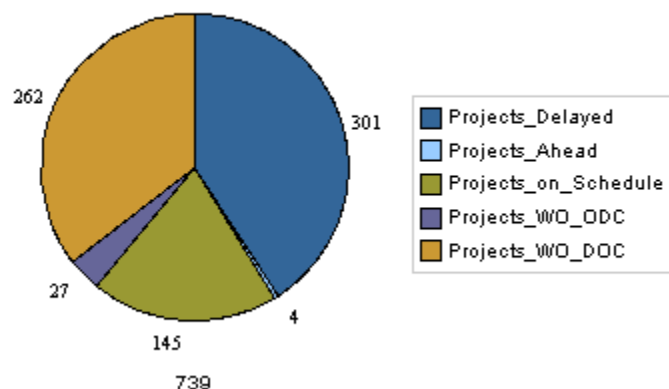

Investment Scenario

The Total Original cost of implementation of 739 projects when sanctioned, was of the order of Rs. 908391.61 crore but this was subsequently revised to Rs. 1087044.2 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till October, 2013 is Rs. 511194.29 crore, which is 47% of the revised cost of the projects.

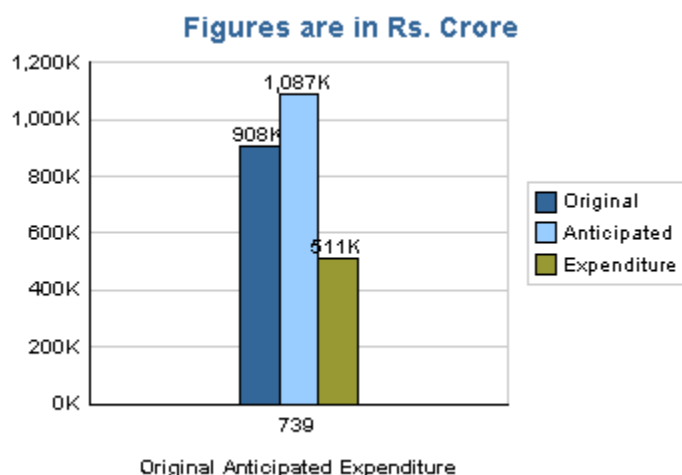

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	738
No of Projects Completed/Dropped/Frozen in Current Month	8
No of Projects added in Current Month	9
No of Projects in Current Month	739

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	301	4	145	27	262	739	40.73
Latest Approved (Date)	289	4	157	27	262	739	39.11

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	591	774,234.56	824,257.51	357,068.48	43.30	50,022.95	6.50
Latest Approved (RCE)	148	201,468.82	262,786.69	154,125.81	58.70	61,317.87	30.40
Total (RCE)	739	975,703.38	1,087,044.20	511,194.29	47.03	111340.82	11.41
Original Cost of All Projects							
Original Cost	739	908,391.61	1,087,044.20	511,194.29	47.00	178,652.59	19.70

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	301	483,075.60	592,256.64	374,821.59	63.30	109,181.04	22.60
Latest Approved (RCE)	289	500,746.43	567,395.56	363,847.12	64.10	66,649.13	13.30

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	33	112,437.34	136,260.76	98,013.74	71.90	23,823.42	21.20

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	8	6,035.5	6,625.0	9.8	2	3,750.5	4,340.0	15.7
3	Coal	55	38,127.1	41,212.5	8.1	7	8,579.5	12,262.6	42.9
4	Steel	18	65,597.2	71,782.4	9.4	6	24,000.9	30,216.1	25.9
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	Petroleum	85	184,960.0	200,046.8	8.2	25	59,168.9	80,361.0	35.8
7	Power	98	248,494.9	267,211.0	7.5	18	51,573.9	70,289.9	36.3
8	Railways	286	149,162.5	264,395.1	77.3	145	62,494.0	177,832.9	184.6
9	Road Transport And Highways	151	104,964.2	106,902.8	1.8	11	3,324.3	5,445.2	63.8
10	Shipping And Ports	19	15,617.1	17,871.5	14.4	9	8,629.0	11,187.6	29.7
11	Telecommunications	9	4,742.5	4,646.1	-2.0	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		739	908,391.6	1,087,044.2	19.7	232	252,090.5	438,252.9	73.8

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Andhra Pradesh	47	37,689.8	45,757.5	21.4	15	13,528.4	22,463.1	66.0
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	4	9,512.2	17,330.3	82.2
3	Assam	41	24,155.5	38,425.1	59.1	14	10,762.0	25,130.3	133.5
4	Bihar	46	32,579.0	41,000.0	25.8	17	13,347.2	21,784.5	63.2
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	33	38,022.7	39,925.4	5.0	8	3,415.2	5,629.7	64.8
7	Haryana	9	4,399.9	6,113.1	38.9	2	1,298.8	3,012.0	131.9
8	Himachal Pradesh	5	13,845.2	19,510.6	40.9	4	11,798.2	17,463.6	48.0
9	Jammu and Kashmir	8	13,694.7	32,976.6	140.8	4	6,634.2	25,916.1	290.6
10	Karnataka	38	54,153.6	64,689.4	19.5	14	10,895.4	21,924.3	101.2
11	Kerala	11	22,003.6	24,528.4	11.5	5	5,480.4	8,005.2	46.1
12	Madhya pradesh	21	31,448.2	32,674.6	3.9	5	3,317.9	4,963.7	49.6
13	Maharashtra	55	96,622.9	110,361.3	14.2	19	33,512.3	49,654.4	48.2
14	Manipur	1	727.6	7,392.7	916.1	1	727.6	7,392.7	916.1
15	Meghalaya	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,298.0	115.1	1	619.3	2,384.3	285.0
17	Nagaland	2	5,124.0	6,715.5	31.1	1	850.0	2,441.5	187.2
18	Odisha	31	56,463.3	63,174.1	11.9	12	32,763.5	39,474.3	20.5
19	Punjab	5	1,964.2	2,039.2	3.8	1	284.0	359.0	26.4
20	Rajasthan	25	25,257.1	25,682.6	1.7	6	2,489.1	3,400.6	36.6
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	42	53,703.7	70,043.6	30.4	21	31,221.2	47,561.1	52.3
23	Tripura	5	2,669.4	4,112.4	54.1	3	2,129.4	3,606.7	69.4
24	Uttar Pradesh	30	22,596.0	27,184.9	20.3	10	3,821.3	8,458.5	121.4
25	West Bengal	36	49,877.4	61,170.6	22.6	15	22,672.9	33,966.1	49.8
26	Chandigarh	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	Delhi	4	38,190.9	38,188.3	-0.0	0	0.0	0.0	0.0
28	Chhatisgarh	24	58,278.3	59,362.9	1.9	5	1,396.8	2,481.4	77.6
29	Jharkhand	26	15,873.2	20,138.4	26.9	8	2,534.9	6,971.9	175.0
30	Uttarakhand	6	7,844.0	10,199.3	30.0	4	5,839.0	8,194.3	40.3
31	Multi State	175	182,880.6	205,727.0	12.5	32	19,899.8	44,902.9	125.6
Total		739	908,391.6	1,087,044.2	19.7	232	252,090.5	438,252.9	73.8

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 69
2	Civil Aviation	8	6,035.5	6,625.0	9.8	3	989.4	989.4	3 - 50
3	Coal	55	38,127.1	41,212.5	8.1	30	26,241.1	29,697.9	12 - 120
4	Steel	18	65,597.2	71,782.4	9.4	14	64,410.3	70,505.9	8 - 63
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
6	Petroleum	85	184,960.0	200,046.8	8.2	48	124,334.0	141,671.0	2 - 94
7	Power	98	248,494.9	267,211.0	7.5	52	124,434.8	141,808.8	1 - 106
8	Railways	286	149,162.5	264,395.1	77.3	40	28,693.3	81,559.0	3 - 240
9	Road Transport And Highways	151	104,964.2	106,902.8	1.8	100	61,055.4	62,967.2	2 - 117
10	Shipping And Ports	19	15,617.1	17,871.5	14.4	4	2,502.6	3,073.8	5 - 93
11	Telecommunications	9	4,742.5	4,646.1	-2.0	4	2,018.2	1,843.9	31 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		739	908,391.6	1,087,044.2	19.7	301	483,075.6	592,256.6	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Andhra Pradesh	47	37,689.8	45,757.5	21.4	10	13,097.4	18,077.9	7 - 63
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	3	9,356.2	16,923.9	13 - 90
3	Assam	41	24,155.5	38,425.1	59.1	35	21,932.7	34,968.1	3 - 105
4	Bihar	46	32,579.0	41,000.0	25.8	12	20,814.3	25,475.5	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	18 - 18
6	Gujarat	33	38,022.7	39,925.4	5.0	10	24,752.4	24,691.1	4 - 24
7	Haryana	9	4,399.9	6,113.1	38.9	3	1,875.1	3,055.1	25 - 50
8	Himachal Pradesh	5	13,845.2	19,510.6	40.9	4	12,798.3	16,543.6	26 - 106
9	Jammu and Kashmir	8	13,694.7	32,976.6	140.8	6	12,427.7	31,682.8	10 - 181
10	Karnataka	38	54,153.6	64,689.4	19.5	12	19,346.4	19,349.1	10 - 179
11	Kerala	11	22,003.6	24,528.4	11.5	5	17,074.0	17,774.0	5 - 58
12	Madhya pradesh	21	31,448.2	32,674.6	3.9	9	4,002.9	4,115.7	5 - 69
13	Maharashtra	55	96,622.9	110,361.3	14.2	24	41,079.0	49,944.8	5 - 129
14	Manipur	1	727.6	7,392.7	916.1	1	727.6	7,392.7	72 - 72
15	Meghalaya	3	4,845.0	4,845.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,298.0	115.1	2	1,533.0	3,298.0	35 - 103
17	Nagaland	2	5,124.0	6,715.5	31.1	1	850.0	2,441.5	24 - 24
18	Odisha	31	56,463.3	63,174.1	11.9	19	51,780.8	55,150.2	4 - 139
19	Punjab	5	1,964.2	2,039.2	3.8	2	989.0	1,064.0	13 - 67
20	Rajasthan	25	25,257.1	25,682.6	1.7	8	16,423.9	15,977.6	3 - 65
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 50
22	Tamil Nadu	42	53,703.7	70,043.6	30.4	15	34,552.5	43,919.7	6 - 93
23	Tripura	5	2,669.4	4,112.4	54.1	4	2,417.4	3,860.4	10 - 96
24	Uttar Pradesh	30	22,596.0	27,184.9	20.3	16	15,569.9	18,324.5	9 - 84
25	West Bengal	36	49,877.4	61,170.6	22.6	13	28,749.0	34,196.1	3 - 141
26	Chandigarh	1	452.0	452.0	0.0	0	0.0	0.0	-
27	Delhi	4	38,190.9	38,188.3	-0.0	1	2,494.0	2,494.0	8 - 8
28	Chhatisgarh	24	58,278.3	59,362.9	1.9	12	27,784.7	28,096.0	5 - 120
29	Jharkhand	26	15,873.2	20,138.4	26.9	12	9,803.6	10,387.8	9 - 126
30	Uttarakhand	6	7,844.0	10,199.3	30.0	4	6,097.2	8,228.1	5 - 54
31	Multi State	175	182,880.6	205,727.0	12.5	55	82,762.1	90,799.1	1 - 240
	Total	739	908,391.6	1,087,044.2	19.7	301	483,075.6	592,256.6	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 69
2	Civil Aviation	8	6,035.5	6,625.0	9.8	3	989.4	989.4	3 - 50
3	Coal	55	38,127.1	41,212.5	8.1	30	26,241.1	29,697.9	12 - 120
4	Steel	18	65,597.2	71,782.4	9.4	12	63,403.8	69,390.6	8 - 53
5	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	Petroleum	85	184,960.0	200,046.8	8.2	44	117,375.9	130,217.4	2 - 94
7	Power	98	248,494.9	267,211.0	7.5	52	124,434.8	141,808.8	1 - 106
8	Railways	286	149,162.5	264,395.1	77.3	38	28,178.4	79,831.4	3 - 240
9	Road Transport And Highways	151	104,964.2	106,902.8	1.8	100	61,055.4	62,967.2	2 - 117
10	Shipping And Ports	19	15,617.1	17,871.5	14.4	1	1,228.0	1,429.1	51 - 51
11	Telecommunications	9	4,742.5	4,646.1	-2.0	4	2,018.2	1,843.9	31 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		739	908,391.6	1,087,044.2	19.7	289	467,860.8	567,395.6	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	44,541.0	46,726.0	4.9	1	3,492.0	5,677.0	62.6
2	Civil Aviation	8	6,242.5	6,625.0	6.1	1	1,942.5	2,325.0	19.7
3	Coal	55	40,988.6	41,212.5	0.5	5	2,211.1	2,694.1	21.8
4	Steel	18	69,847.4	71,782.4	2.8	1	14,443.0	16,408.0	13.6
5	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
6	Petroleum	85	199,859.8	200,046.8	0.1	10	33,232.0	37,568.1	13.0
7	Power	98	252,226.1	267,211.0	5.9	13	42,937.0	57,921.9	34.9
8	Railways	286	180,870.0	264,395.1	46.2	116	63,879.9	147,471.5	130.9
9	Road Transport And Highways	151	105,130.7	106,902.8	1.7	11	3,324.3	5,445.2	63.8
10	Shipping And Ports	19	17,488.0	17,871.5	2.2	5	3,157.6	3,783.5	19.8
11	Telecommunications	9	4,742.5	4,646.1	-2.0	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		739	975,703.4	1,087,044.2	11.4	168	176,951.3	293,571.9	65.9

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	8	6,035.46	6,624.95	9.77	1	1,808.00	2,015.00	13- 13
3	Coal	55	38,127.05	41,212.50	8.09	0	0.00	0.00	0- 0
4	Steel	18	65,597.22	71,782.40	9.43	5	9,557.89	13,808.07	27- 63
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	85	184,960.03	200,046.76	8.16	10	20,436.52	34,731.80	20- 94
7	Power	98	248,494.89	267,210.95	7.53	2	2,253.45	3,986.02	0- 79
8	Railways	286	149,162.48	264,395.10	77.25	13	5,296.61	20,447.40	0- 141
9	Road Transport And Highways	151	104,964.22	106,902.84	1.85	0	0.00	0.00	0- 0
10	Shipping And Ports	19	15,617.12	17,871.52	14.44	5	5,400.70	6,829.35	10- 93
11	Telecommunications	9	4,742.45	4,646.10	-2.03	0	0.00	0.00	0- 0
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		739	908391.61	1087044.2	19.67	37	50213.78	90737.64	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 69
2	Civil Aviation	8	6,035.46	6,624.95	9.77	0	0.00	0.00	0- 0
3	Coal	55	38,127.05	41,212.50	8.09	5	7,938.86	11,573.95	23- 57
4	Steel	18	65,597.22	71,782.40	9.43	5	23,740.89	29,866.43	24- 63
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	85	184,960.03	200,046.76	8.16	17	54,334.86	74,012.87	7- 94
7	Power	98	248,494.89	267,210.95	7.53	15	43,738.85	61,112.81	10- 106
8	Railways	286	149,162.48	264,395.10	77.25	34	22,778.05	75,653.23	9- 240
9	Road Transport And Highways	151	104,964.22	106,902.84	1.85	10	3,158.01	5,252.10	25- 115
10	Shipping And Ports	19	15,617.12	17,871.52	14.44	2	1,378.00	2,029.10	51- 93
11	Telecommunications	9	4,742.45	4,646.10	-2.03	1	149.15	158.72	54- 54
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		739	908391.61	1087044.2	19.67	92	179340.28	291526.21	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>Power</u>						
1	NIMOO BAZGO HYDROELECTRIC PROJECT	08/2006	611.01	08/2010	936.00	10/2013	883.85
2	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	07/2006	557.24	01/2010	775.25	10/2013	648.43
	<u>Railways</u>						
3	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	07/1998	248.44	12/2012	1,115.21	04/2013	972.91
4	RUPSA-BANGRIPOSI (GC)(SER)	02/1996	57.94	03/1998	173.49	08/2005	176.14
	<u>Telecommunications</u>						
5	CONVERGENT BILLING AND CRM-MTNL(DELHI)	12/2005	249.00	02/2007	229.41	02/2013	67.21
6	CONVERGENT BILLING AND CRM(MUMBAI)	01/2006	247.00	02/2007	247.00	N.A.	75.89
7	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06	06/2006	231.38	10/2007	176.00	12/2013	86.11
8	DELHI CONVERGENT BILLING AND CRM PE-5834	02/2006	229.41	03/2012	229.41	N.A.	67.21

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>Petroleum</u>					
1	Marketing Terminal at Paradeep	7/2009	199.75	6/2014	199.75	6/2014
2	Strategic Crude oil storage project at Padur	1/2006	993.00	1/2012	1,693.00	10/2015
	<u>Power</u>					
3	Inter-Regional System Strengthening Scheme in WR and NR (Part-A)	10/2013	1,315.90	11/2016	1,315.90	11/2016
4	Eastern Region Strengthening Scheme-V	10/2013	1,364.52	5/2016	1,364.52	5/2016
	<u>Railways</u>					
5	Quilon-Tirunelveli - Trichendur, Tenkasi	4/1999	460.94	1/1999	1,030.00	1/1999
6	Jaggayyapet - Mellacheruvu	4/2007	313.24	1/1999	313.24	1/1999
7	MM from Buramara-Chakulia	4/2008	466.48	1/1999	466.48	1/1999
8	Marikuppam - Kuppam	4/2012	285.57	1/1999	285.57	1/1999
9	MM from Panskura-Ghatal NL	4/2011	276.69	1/1999	276.69	1/1999

Milestones (Cumulative due & achieved)		
Total	3689	
Achieved up to month	1370	


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	06/2014	09/2014	3
	<u>Coal</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,027.59	06/2009	01/2014	03/2014	2
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,540.93	03/2012	03/2014	05/2014	2
4	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) NLC	5,907.11	5,907.11	12/2015	02/2018	04/2018	2
5	ADRIYALA SHAFT PROJECT SCCL	212.34	977.53	03/2013	10/2014	02/2015	4
6	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
	<u>Steel</u>						
7	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT EXP. UNIT RINL	202.00	343.58	01/2010	10/2013	11/2013	1
8	Bailadila Iron Ore Project Deposit- 11B (NMDC) NMDC	295.89	607.17	12/2011	12/2013	03/2014	3
9	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) NMDC	572.00	572.00	04/2013	12/2013	03/2014	3
10	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2013	03/2014	3
11	INSTALLATION OF 45MVA SAFETY WITH OTHER ASSOCIATED FACILITIES SAIL	187.33	187.33	10/2013	03/2014	06/2014	3
12	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) RINL	8,692.00	12,291.00	10/2009	10/2013	03/2014	5
13	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	03/2014	09/2014	6
	<u>Petroleum</u>						
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	761.68	05/2013	05/2014	06/2014	1

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
15	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	586.00	586.00	08/2015	07/2015	08/2015	1
16	PARADIP REFINERY PROJECT IOCL	29,777.00	32,710.00	11/2012	05/2014	07/2014	2
17	MRPL Phase-III Expansion Mangalore Refin	12,412.00	12,160.26	01/2012	10/2013	12/2013	2
18	Construction of 6 ETPs ONGC	302.26	240.95	09/2012	12/2013	03/2014	3
19	Development of SB-14 field ONGC	410.44	410.44	11/2012	10/2013	02/2014	4
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG ISPRL	672.00	1,038.00	10/2011	01/2014	06/2014	5
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE ISPRL	732.00	1,227.00	10/2011	12/2013	10/2015	22
	<u>Power</u>						
22	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	11/2014	12/2014	1
23	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP PGCIL	184.19	184.19	11/2011	10/2013	12/2013	2
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX PGCIL	182.68	182.68	01/2013	11/2013	01/2014	2
25	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED PGCIL	425.51	425.51	10/2013	12/2013	03/2014	3
26	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN PGCIL	1,391.97	1,391.97	12/2013	12/2013	05/2014	5
	<u>Railways</u>						
27	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) NCR	158.77	580.83	03/1994	10/2013	01/2014	3
28	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	108.00	432.72	12/2009	10/2013	01/2014	3
29	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project NEFR	1,676.31	5,000.00	03/2009	12/2014	03/2015	3
30	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	1,000.00	4,996.19	04/2008	12/2015	12/2016	12
31	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	200.00	385.20	N.A.	03/2015	03/2016	12

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
32	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24
	<u>Shipping And Ports</u>						
33	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL MUMBAI PORT TRU	1,228.00	1,429.10	12/2010	12/2014	03/2015	3
	33						

Graphical Presentation of All Projects w.r.t. Original Schedule

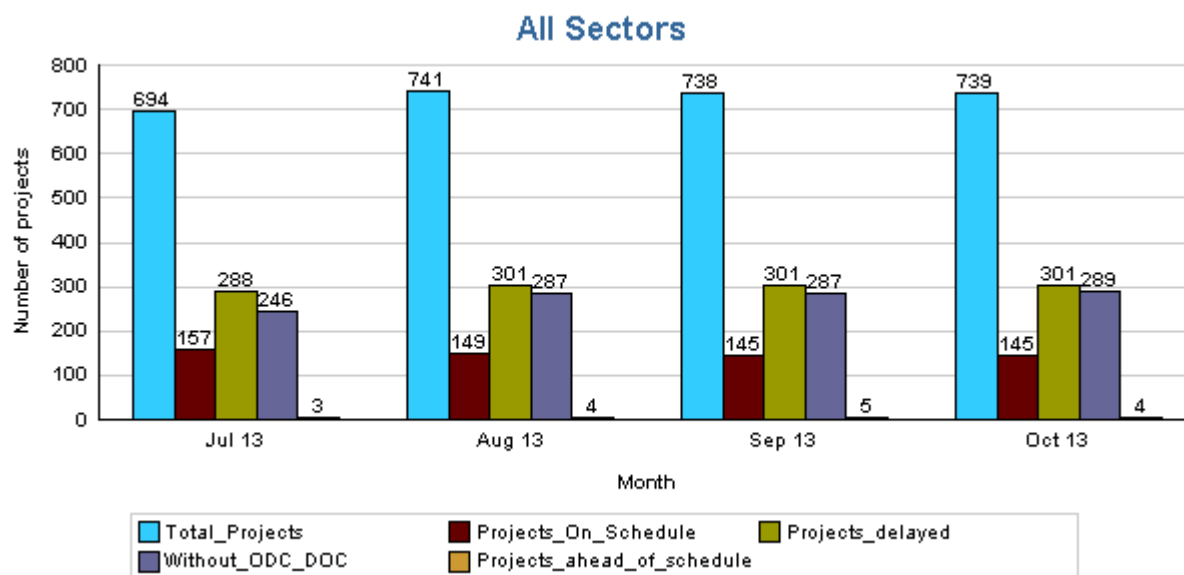


Break-up of 301 Delayed projects in October 2013

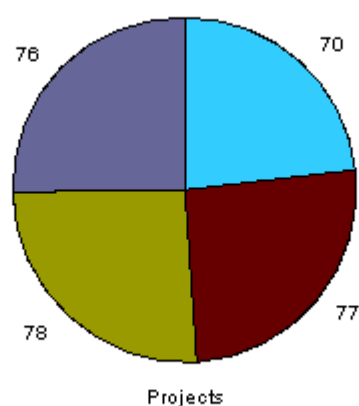


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
-----------------	------	-------	-------	--------------

Graphical Presentation of All Projects w.r.t. Revised Schedule

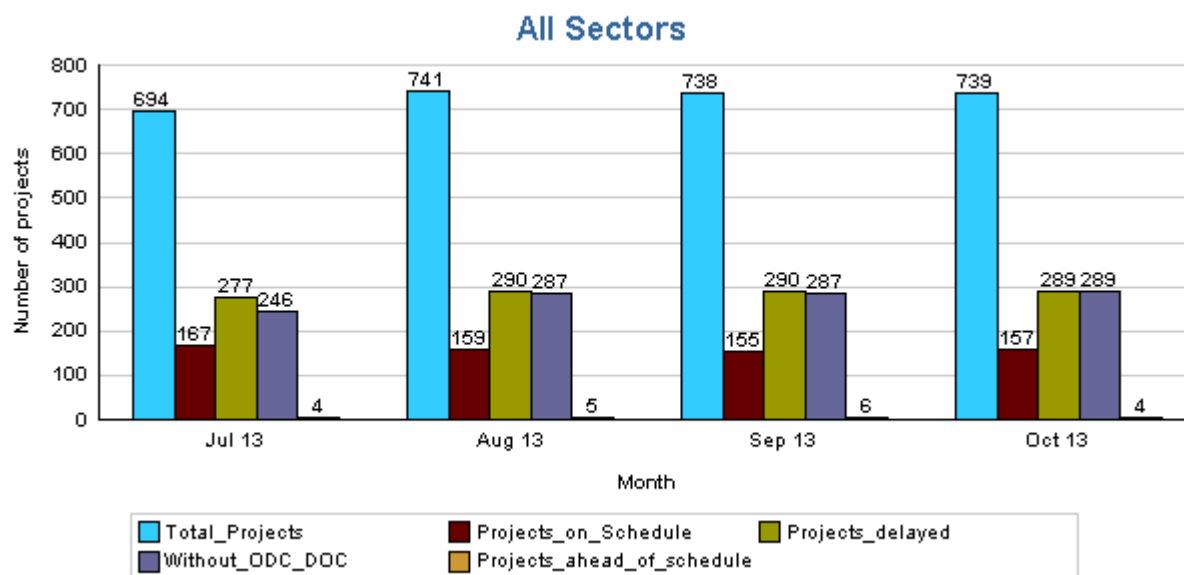


Break-up of 289 Delayed projects in October 2013

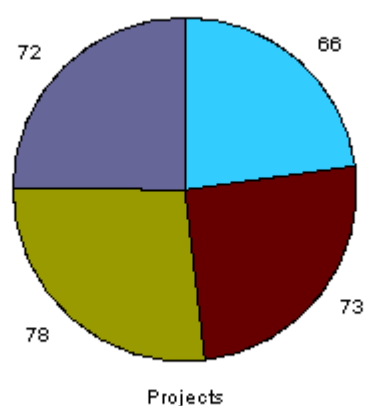


Delay in Months



Graphical Presentation of Urban Development Sector

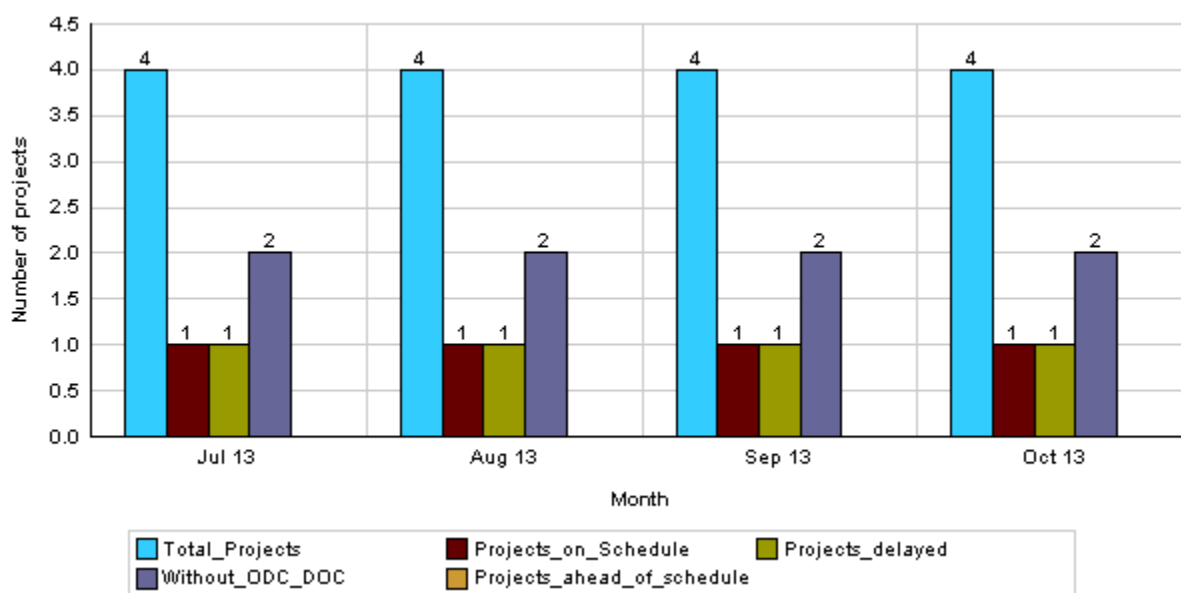


Break-up of 1 Delayed projects in October 2013




Delay in Months



Graphical Presentation of Telecommunications Sector

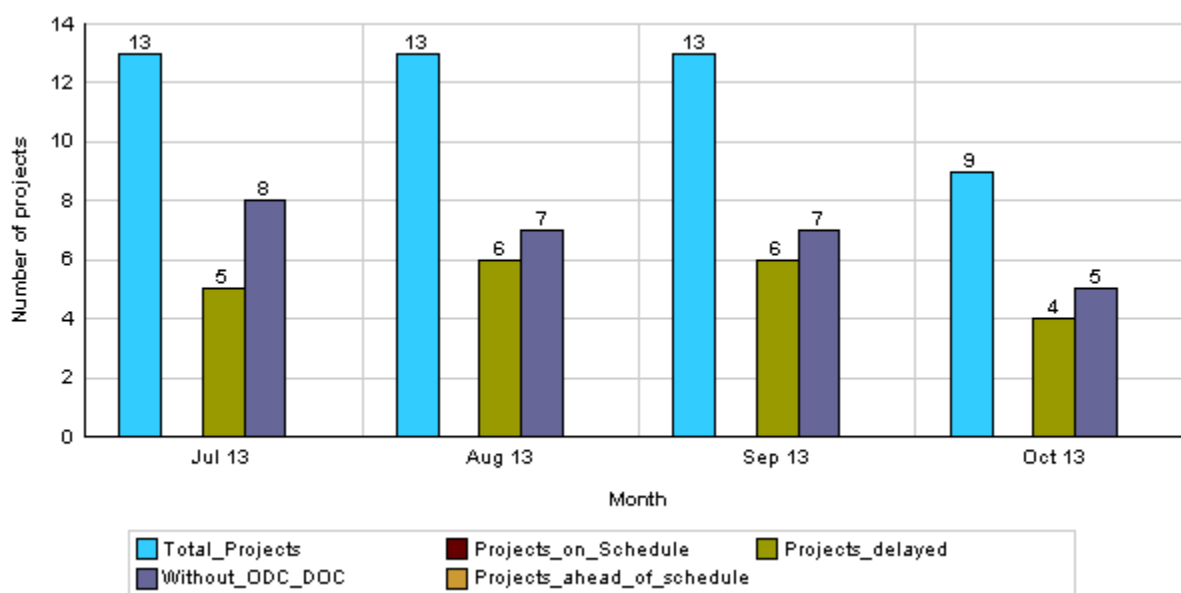


Break-up of 4 Delayed projects in October 2013




Delay in Months



Graphical Presentation of Shipping And Ports Sector

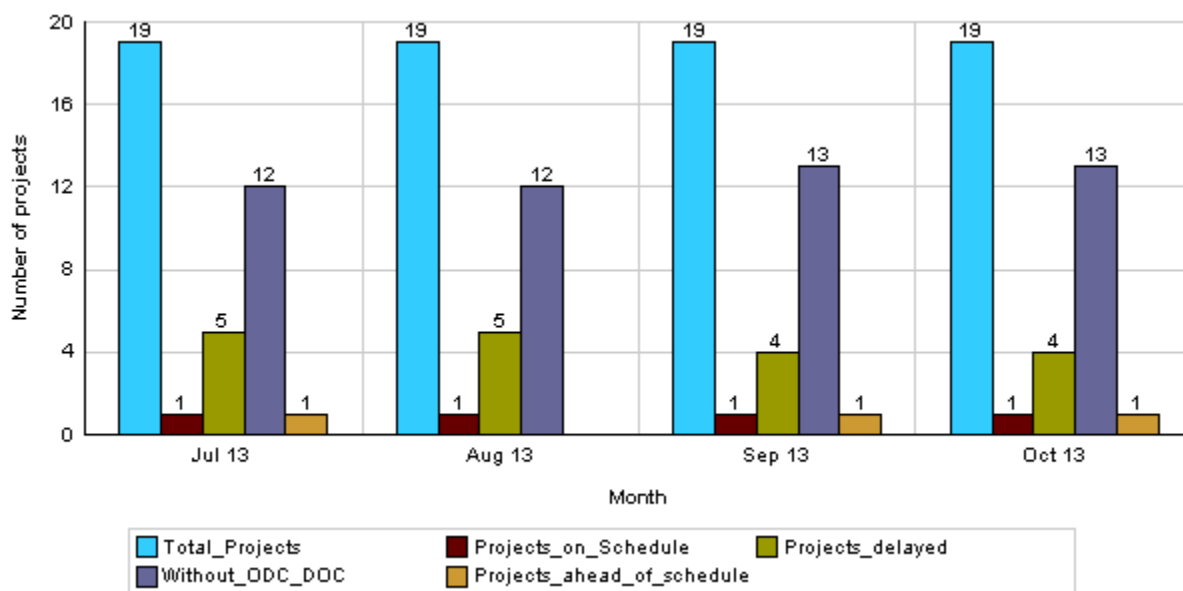


Break-up of 4 Delayed projects in October 2013

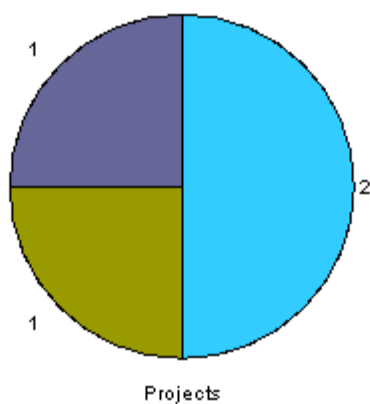


Delay in Months



Graphical Presentation of Road Transport And Highways Sector

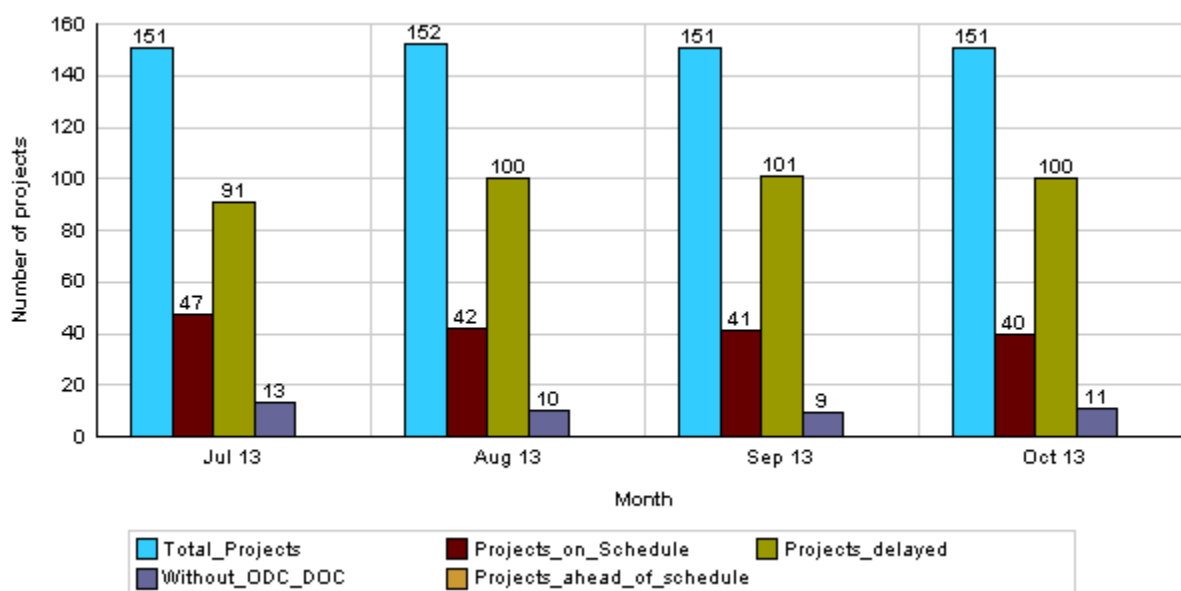


Break-up of 100 Delayed projects in October 2013

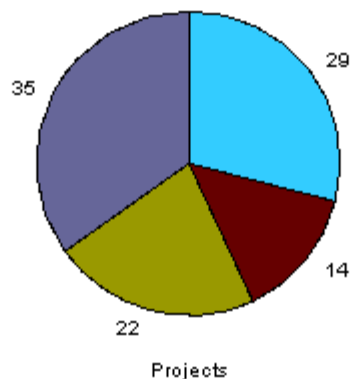


Delay in Months



Graphical Presentation of Railways Sector

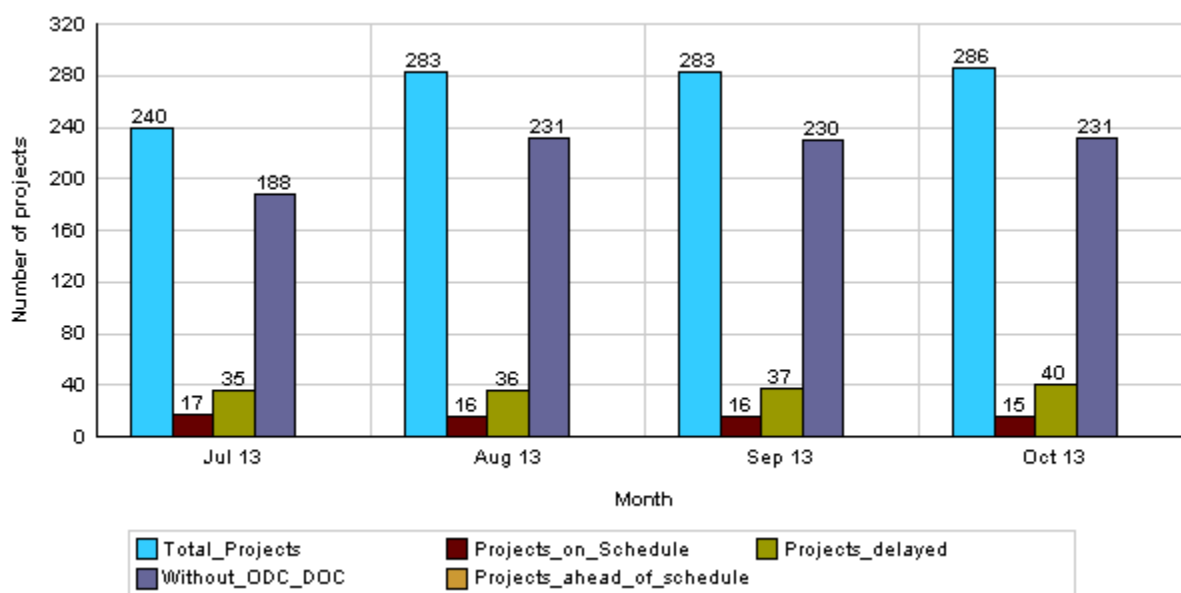


Break-up of 40 Delayed projects in October 2013

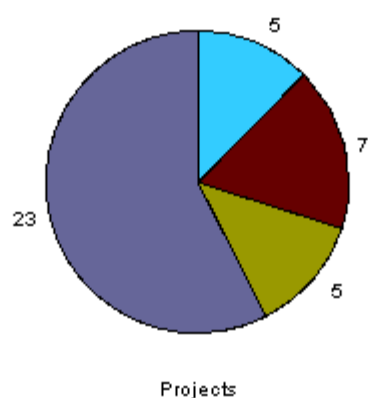


Delay in Months



Graphical Presentation of Power Sector

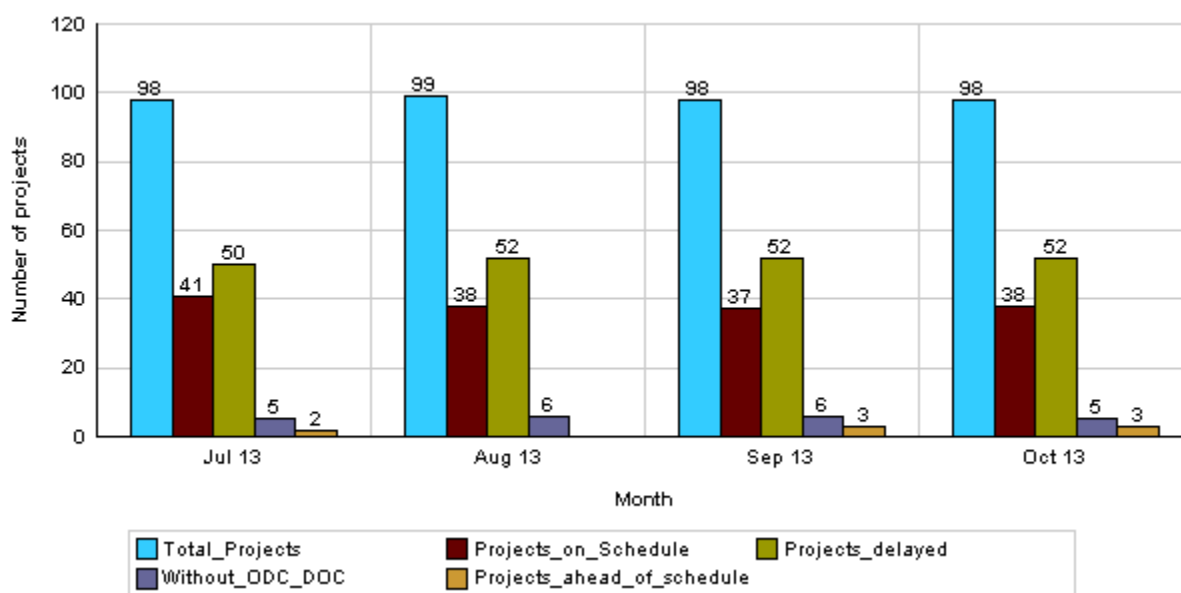


Break-up of 52 Delayed projects in October 2013

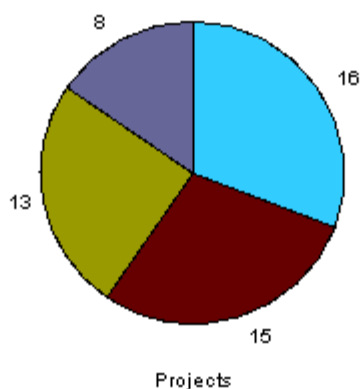


Delay in Months



Graphical Presentation of Petroleum Sector

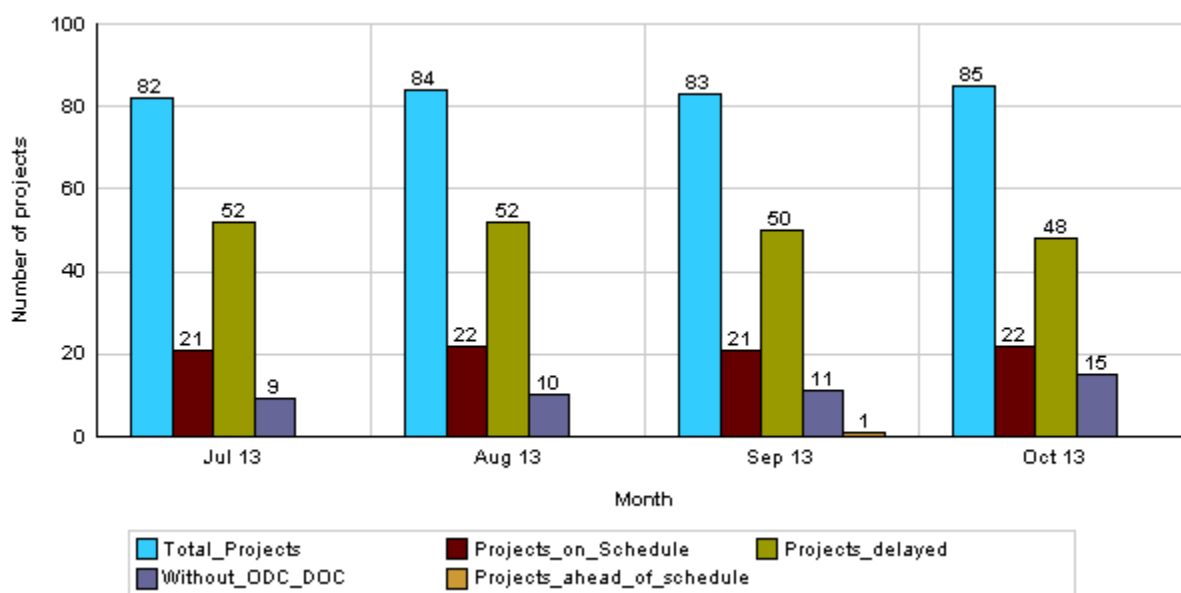


Break-up of 48 Delayed projects in October 2013

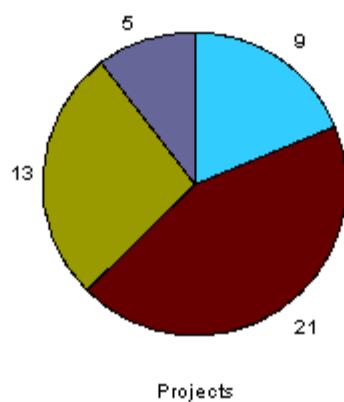

Delay in Months



Graphical Presentation of Steel Sector

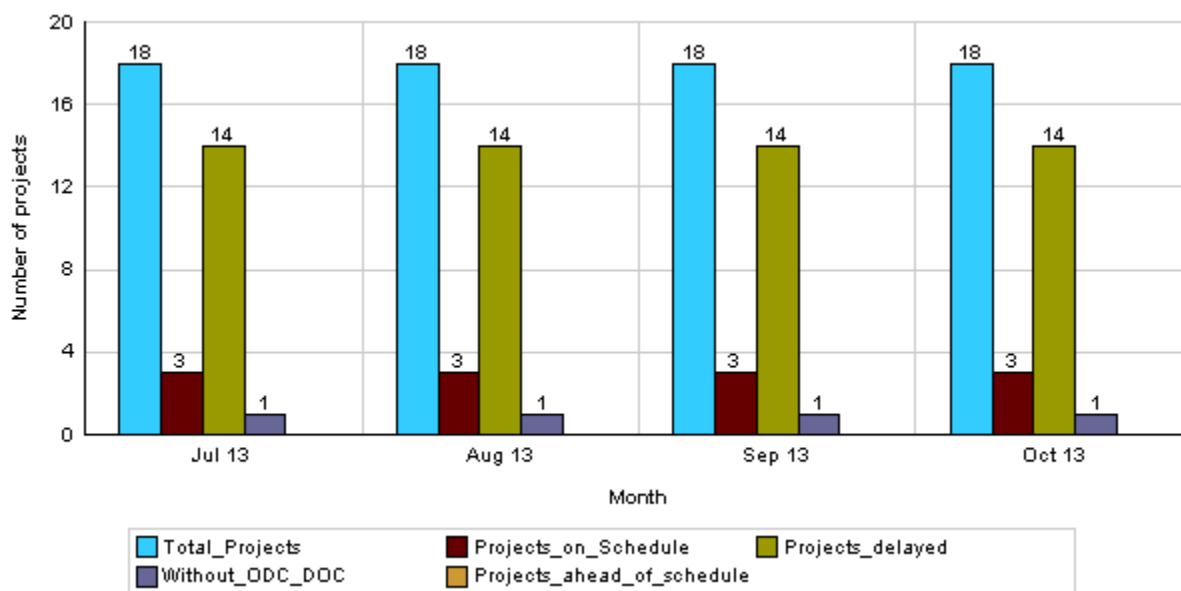


Break-up of 14 Delayed projects in October 2013




Delay in Months



Graphical Presentation of Coal Sector

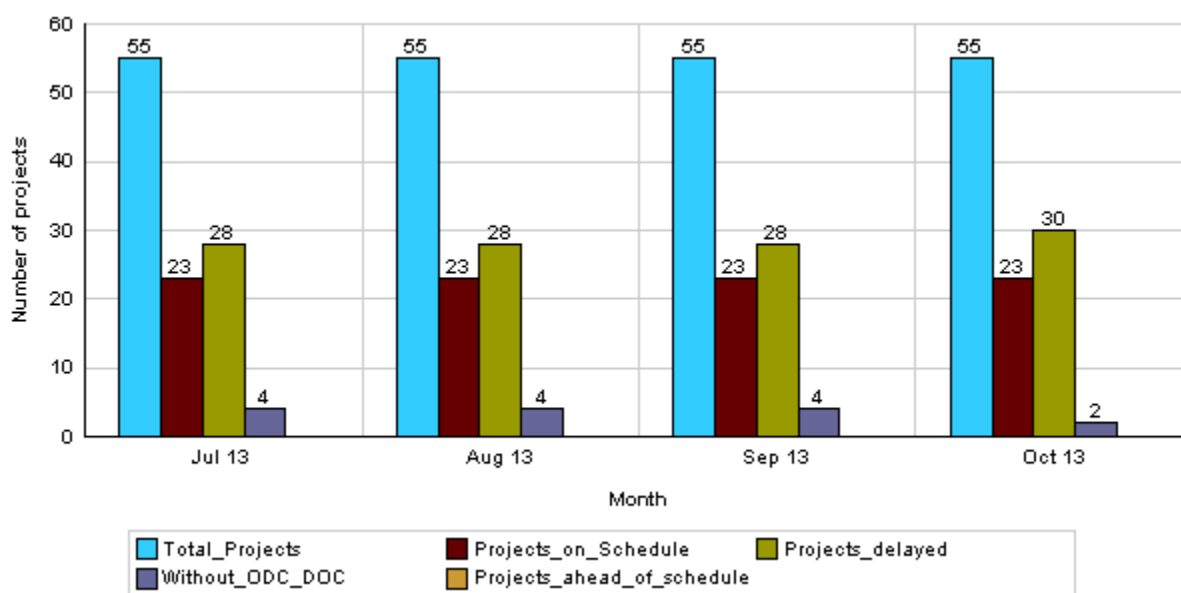


Break-up of 30 Delayed projects in October 2013

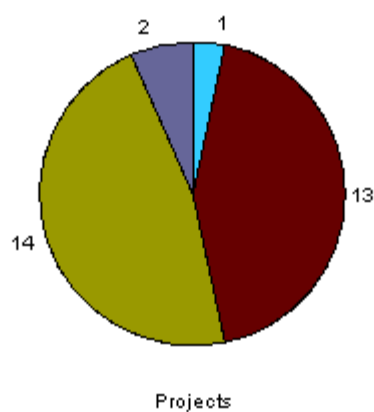

Delay in Months



Graphical Presentation of Civil Aviation Sector

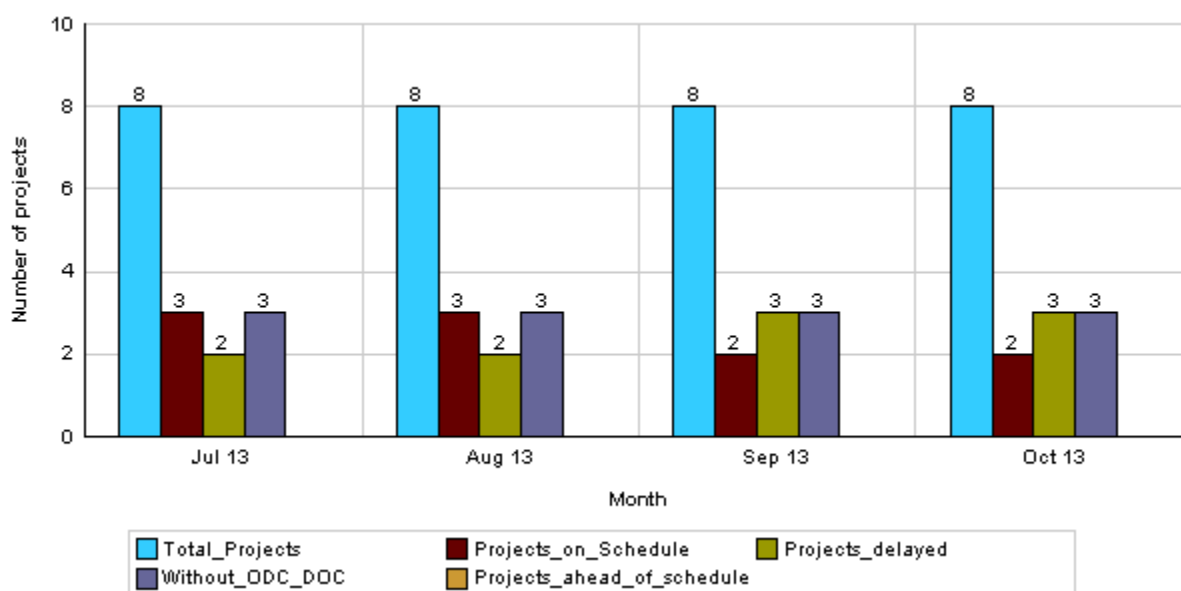


Break-up of 3 Delayed projects in October 2013




Delay in Months



Graphical Presentation of Atomic Energy Sector

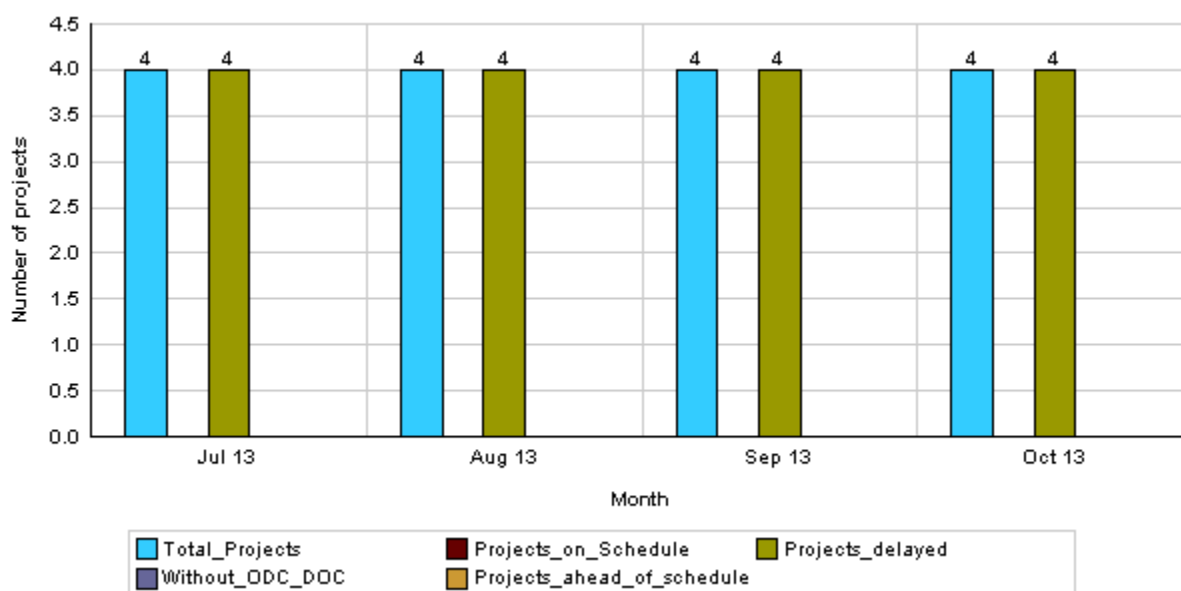

Break-up of 4 Delayed projects in October 2013

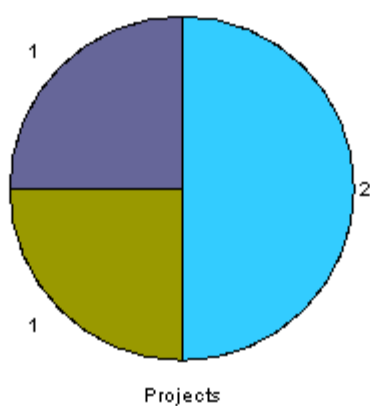

Delay in Months



Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
Atomic Energy	4	40,442.00	44,541.00	46,726.00	26,912.83
Civil Aviation	8	6,035.46	6,242.46	6,624.95	5,473.72
Coal	55	38,127.05	40,988.64	41,212.50	16,090.32
Steel	18	65,597.22	69,847.40	71,782.40	54,194.19
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	85	184,960.03	199,859.75	200,046.76	99,431.39
Power	98	248,494.89	252,226.06	267,210.95	128,626.60
Railways	286	149,162.48	180,869.97	264,395.10	73,591.95
Road Transport And Highways	151	104,964.22	105,130.72	106,902.84	83,933.30
Shipping And Ports	19	15,617.12	17,487.95	17,871.52	8,655.74
Telecommunications	9	4,742.45	4,742.45	4,646.10	1,736.42
Urban Development	4	44,245.18	44,304.08	49,518.08	8,001.83
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	739	908,391.61	975,703.38	1,087,044.20	511,194.29

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	3,478.00	12/2015 -	11/2016	11(O) -	1/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,746.00	12/2008 -	09/2014	69(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,309.83	09/2010 -	03/2015	54(O) -	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,379.00	12/2016 -	03/2017	3(O) -	0/69
	Total		40,442.00 -	46,726.00	26,912.83				48/327
	<u>Civil Aviation</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,474.41	05/2011 -	03/2013	-	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.71	01/2011 04/2013	03/2015	50(O) 23(R)	0/0
7	Construction of New International Terminal Building(Goa) - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	249.31	05/2012 -	11/2013	18(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,907.17	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,Chandigarh	02/2011	452.00 -	452.00	160.72	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,Multi State	02/2010	344.28 -	344.28	-	03/2014 -	06/2014	3(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	450.38	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,624.95	5,473.72				0/0
	<u>Coal</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	805.16	03/2013 09/2012	02/2015	23(O) 29(R)	18/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	90.05	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	582.00	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,Jharkhand	02/2012	858.11 -	858.11	49.40	03/2020 -	03/2020	0(O) -	0/3

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	117.75	03/2012 -	03/2014	24(O) -	5/6
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	118.26	03/2011 -	03/2014	36(O) -	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 Mty - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	129.20	03/2010 -	03/2015	60(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N060000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	53.45	03/2016 -	03/2016	0(O) -	0/6
21	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00 -	490.10	152.13	03/2017 -	03/2017	0(O) -	4/12
22	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	45.02	03/2014 -	03/2014	0(O) -	0/2
23	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 -	535.10	162.71	03/2015 -	03/2015	0(O) -	0/3
24	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	268.23	03/2014 -	03/2016	24(O) -	2/8
26	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,275.84	03/2014 -	03/2016	24(O) -	6/12
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,575.95	03/2014 -	03/2016	24(O) -	10/15
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87 -	395.87	74.32	03/2015 -	03/2015	0(O) -	1/13
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	118.03	03/2013 -	03/2015	24(O) -	3/8
31	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	14.03	03/2015 -	03/2015	0(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72(O) -	0/2
35	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	92.14	12/2012 -	03/2016	39(O) -	9/44
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,Andhra Pradesh	07/2012	417.33 -	417.33	0.11	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	113.59	03/2013 -	03/2015	24(O) -	5/10
38	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46 -	162.46	40.99	03/2014 -	03/2014	0(O) -	0/2
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
40	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018	0(O) -	0/4
41	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 -	741.62	377.80	03/2013 -	03/2014	12(O) -	0/2

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.47	03/2010 -	03/2014	48(O) -	9/10
43	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	739.17	03/2013 -	03/2023	120(O) -	0/9
44	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
45	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	27.60	07/2012 -	03/2016	44(O) -	0/3
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	210.11	03/2014 -	03/2016	24(O) -	1/6
47	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.65	03/2012 -	03/2015	36(O) -	4/6
48	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
49	Muraidih UG Turn-key Project - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
50	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	34.92	12/2015 -	04/2018	28(O) -	1/33
51	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.98	03/2012 -	03/2015	36(O) -	0/2
52	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	61.20	03/2012 -	03/2017	60(O) -	0/2
53	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
54	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.28	03/2014 -	03/2016	24(O) -	0/1
55	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.33	03/2013 -	03/2015	24(O) -	0/3
56	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	20.33	03/2014 -	03/2016	24(O) -	0/2
57	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	237.96	03/2012 -	03/2015	36(O) -	24/27
58	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	3.25	03/2015 -	03/2015	0(O) -	4/29
59	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	58.99	03/2016 -	03/2016	0(O) -	4/48
60	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,Andhra Pradesh	06/2012	365.01 -	365.01	1.81	06/2015 -	06/2015	0(O) -	2/51
61	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	52.12	03/2015 -	03/2015	0(O) -	8/31
62	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016	0(O) -	0/2
63	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	56.80	03/2012 -	-	-	16/42
64	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72 -	447.72	48.56	03/2016 -	03/2016	0(O) -	0/12
65	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,802.11	06/2009 -	03/2014	57(O) -	19/23
66	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,770.42	03/2012 -	05/2014	26(O) -	20/39
67	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	138.45	03/2012 -	03/2016	48(O) -	0/2

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		38,127.05 -	41,212.50	16,090.32				197/778
	<u>Steel</u>								
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	338.09	04/2013 12/2013	03/2014	11(O) 3(R)	17/18
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	08/2006	260.00 349.64	349.64	257.77	12/2009 08/2010	06/2013	-	1/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,Andhra Pradesh	07/2007	202.00 343.58	343.58	281.05	01/2010 02/2011	11/2013	46(O) 33(R)	3/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	229.26	05/2013 03/2014	03/2014	10(O) 0(R)	11/20
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	07/2007	480.00 -	450.00	288.01	09/2009 05/2012	12/2013	51(O) 19(R)	2/2
73	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	356.75	12/2011 03/2012	03/2014	27(O) 24(R)	15/20
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	06/2006	108.00 216.68	216.68	153.79	09/2008 12/2013	12/2013	63(O) 0(R)	3/4
75	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhatisgarh - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	332.65	68.92	08/2014 -	08/2014	0(O) -	0/2
76	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	83.02	11/2013 -	06/2015	19(O) -	1/3
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	10,590.79	03/2013 -	09/2014	18(O) -	23/32
78	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,779.97	12/2011 -	12/2013	24(O) -	18/21
79	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,841.57	12/2012 -	03/2014	15(O) -	10/16
80	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	15,038.24	12/2011 -	12/2013	24(O) -	20/23
81	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,603.02	10/2009 10/2012	03/2014	53(O) 17(R)	66/67
82	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	10,157.19	03/2013 -	12/2013	9(O) -	14/19
83	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	95.71	10/2013 -	06/2014	8(O) -	0/3
84	Rebuilding of Battery Block 5A and Re-construction of Battery Block 5B - [N12000080]SAIL,West Bengal	03/2012	339.35 -	339.35	21.03	06/2015 -	06/2015	0(O) -	0/0
85	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	254.90	10.01	12/2014 -	12/2014	0(O) -	0/1
	Total		65,597.22 -	71,782.40	54,194.19				204/255
	<u>Petrochemicals</u>								
86	Assam gas Cracker project - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20(O) 0(R)	19/29
	Total		5,460.61 -	8,920.00	4,510.51				19/29

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Petroleum</u>								
87	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	52.67	06/2012 -	03/2014	21(O) -	0/4
88	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23(O) -	0/0
89	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	794.14	12/2011 -	11/2013	23(O) -	0/5
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2014	12(O) 0(R)	0/5
91	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,Multi State	08/2011	586.00 -	586.00	81.00	08/2015 -	08/2015	0(O) -	0/0
92	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24(O) -	0/0
93	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24(O) -	0/0
94	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	540.92	332.02	07/2012 07/2012	-	-	6/7
95	BUTENE-1 PROJECT AT PANIPAT - [N16000139]OCL,Haryana	02/2012	190.00 -	190.00	90.20	03/2014 -	03/2014	0(O) -	0/24
96	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	133.48	06/2012 -	12/2013	18(O) -	0/0
97	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	445.86	09/2011 -	12/2014	39(O) -	0/0
98	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	59.74	06/2012 -	03/2014	21(O) -	0/0
99	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	312.61	- -	03/2013	-	18/19
100	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12(O) -	0/5
101	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	310.49	05/2013 06/2014	06/2014	13(O) 0(R)	0/5
102	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	152.89	123.93	06/2013 -	06/2013	-	0/0
103	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	104.65	08/2013 -	03/2014	7(O) -	0/5
104	Construction of 6 ETps - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	98.72	09/2012 -	03/2014	18(O) -	0/0
105	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]ONGC,Gujarat	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014	0(O) -	0/5
106	Construction of one Multipurpose Support Vessel (MSV) - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
107	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	-	0/5
108	Construction of three ETps, Mehsana - [N16000135]ONGC,Gujarat	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2014	0(O) -	0/5
109	Creation of Secondary Tank farm with dehydration facility and ETP at Madhuban - [N16000167]OIL,Multi State	08/2006	374.56 -	374.56	10.46	09/2012 -	10/2016	49(O) -	0/0
110	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	486.00	64.08	09/2013 -	09/2013	-	0/1

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
111	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Mult State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94(O) 20(R)	0/0
112	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,137.44	08/2010 03/2012	05/2014	45(O) 26(R)	0/10
113	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
114	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44(O) 22(R)	0/0
115	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63(O) 11(R)	0/0
116	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	-	6/76
117	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	-	56/59
118	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	507.63	- -	-	-	0/0
119	Development of BHE and BH-35 Area. - [N16000118]ONGC,Mult State	08/2010	372.11 -	372.11	234.31	03/2013 -	12/2013	9(O) -	0/5
120	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	45.76	05/2014 -	05/2014	0(O) -	0/9
121	Development of Cluster-7 Fields - [N16000104]ONGC,Mult State	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
122	Development of SB-14 field - [N16000116]ONGC,Mult State	01/2011	410.44 -	410.44	228.27	11/2012 -	02/2014	15(O) -	0/9
123	Development of WO-16 Cluster Fields - [N16000105]ONGC,Mult State	06/2010	2,523.00 -	2,523.00	983.55	01/2014 -	12/2015	23(O) -	0/9
124	Development of Western Periphery of MH South Field - [N16000136]ONGC,Mult State	04/2012	600.17 -	600.17	130.15	12/2014 -	12/2014	0(O) -	0/8
125	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu	05/2013	711.00 -	711.00	0.88	- -	-	-	0/0
126	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	716.68	01/2013 -	12/2013	11(O) -	18/18
127	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26(O) -	0/9
128	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,462.08	04/2013 -	11/2013	7(O) -	0/167
129	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	1,425.92	05/2015 -	05/2015	0(O) -	0/17
130	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,759.52	03/2007 03/2017	10/2013	79(O) -41(R)	6/6
131	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	750.00	743.72	03/2007 03/2014	09/2013	-	3/3
132	IOR of B-173A Field - [N16000140]ONGC,Mult State	01/2012	352.49 -	352.49	20.03	03/2014 -	05/2014	2(O) -	0/5
133	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93(O) 9(R)	6/6
134	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 2,665.65	2,665.65	362.59	03/2015 -	03/2015	0(O) -	0/12
135	Integrated Development of Bassein Field - [N16000160]ONGC,Maharashtra	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
136	Integrated Refinery Expansion Project - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	760.92	12/2015 -	05/2016	5(O) -	0/0
137	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35(O) -	0/0
138	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0
139	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,Multi State	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	-	0/1
140	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	1,246.09	12/2012 -	-	-	0/10
141	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015	0(O) -	0/0
142	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,813.90	01/2012 -	12/2013	23(O) -	0/108
143	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	03/2014	18(O) -	0/0
144	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46(O) 12(R)	0/0
145	Marketing Terminal at Paradeep - [N16000168]IOCL,Odisha	07/2009	199.75 -	199.75	89.65	06/2014 -	06/2014	0(O) -	0/0
146	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23(O) -	0/0
147	Mounded Bullet Project at CPCL - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	279.00	283.87	12/2014 -	12/2014	0(O) -	0/0
148	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	731.38	03/2010 03/2012	12/2013	45(O) 21(R)	0/0
149	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	913.00	44.38	07/2015 -	07/2015	0(O) -	0/0
150	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	23,613.00	11/2012 -	07/2014	20(O) -	60/100
151	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	898.87	09/2012 -	-	-	5/11
152	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	5,597.68	02/2014 -	02/2014	0(O) -	0/0
153	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	276.83	242.63	04/2012 -	12/2013	20(O) -	0/0
154	Pipeline Replacement Project, Ahmedabad - [N16000159]ONGC,Gujarat	09/2011	202.25 -	160.16	-	07/2016 -	07/2016	0(O) -	0/5
155	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	560.90	05/2014 -	05/2014	0(O) -	0/5
156	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	755.59	07/2012 -	12/2013	17(O) -	0/31
157	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165]OIL,Multi State	04/2010	270.00 -	270.00	-	12/2014 -	12/2014	0(O) -	0/0
158	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	- -	08/2013	-	52/53
159	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64 -	1,210.64	320.72	11/2015 -	11/2015	0(O) -	7/25
160	Reconstruction of BPA and BPB Platforms - [N16000161]ONGC,Maharashtra	03/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015	0(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
161	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	200.75	12/2014 -	12/2014	0(O) -	0/0
162	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20(O) -	0/0
163	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	729.75	10/2011 -	10/2015	48(O) -	0/0
164	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	912.81	10/2011 -	06/2014	32(O) -	0/0
165	Strategic Crude oil storage project at Padur - [N16000169]ISPRL,Kerala	01/2006	993.00 1,693.00	1,693.00	998.65	01/2012 -	10/2015	45(O) -	0/0
166	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	10,281.00	0.04	- -	04/2015	- -	0/0
167	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3(O) -	0/5
168	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.82	48.71	10/2014 -	10/2014	0(O) -	0/0
169	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	202.37	08/2012 -	03/2014	19(O) -	0/5
170	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	265.22	03/2012 -	12/2013	21(O) -	13/20
171	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	337.79	12/2013 -	12/2013	0(O) -	0/0
	Total		184,960.03 -	200,046.76	99,431.39				256/912
	<u>Power</u>								
172	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	6,023.11	08/2012 -	03/2014	19(O) -	0/11
173	765KV System for Central part of Northern Region Grid - Part-III - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	851.42	05/2012 -	12/2013	19(O) -	0/8
174	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	5.89	10/2014 -	10/2014	0(O) -	0/7
175	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,477.00	08/2013 -	09/2014	13(O) -	13/19
176	BARH STPP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,741.00	12/2009 -	03/2017	87(O) -	26/54
177	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	4,092.00	07/2011 -	06/2016	59(O) -	5/28
178	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	2,514.88	11.64	12/2015 -	12/2015	0(O) -	0/20
179	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	1,909.24	233.52	06/2015 -	06/2015	0(O) -	0/0
180	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	1,008.84	08/2014 -	08/2014	0(O) -	7/20

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
181	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	41.52	06/2014 -	06/2014	0(O) -	0/20
182	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,Multi State	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
183	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	182.80	3.60	10/2014 -	10/2014	0(O) -	2/2
184	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	1,066.41	09/2014 -	09/2014	0(O) -	7/20
185	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	885.97	10/2009 -	03/2014	53(O) -	5/15
186	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	737.73	11/2012 -	03/2015	28(O) -	2/13
187	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
188	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	1,176.91	05/2014 -	05/2014	0(O) -	1/11
189	Eastern Region Strengthening Scheme-V - [N18000155]PGCIL,Multi State	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016	0(O) -	0/0
190	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,351.27	08/2013 -	03/2014	7(O) -	1/12
191	Gadarwara Super Thermal Power Project Stage-I - [N18000151]NTPC,Madhya pradesh	02/2013	11,638.55 -	11,638.55	889.00	09/2017 -	09/2017	0(O) -	4/41
192	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	437.18	08/2014 -	08/2014	0(O) -	1/16
193	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	1,083.83	12/2013 -	05/2014	5(O) -	1/12
194	Inter-Regional System Strengthening Scheme in WR and NR (Part-A) - [N18000154]PGCIL,Maharashtra	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016	0(O) -	0/0
195	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	911.32	12/2007 12/2009	-	-	2/11
196	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,575.95	12/2009 05/2013	03/2017	87(O) 46(R)	11/22
197	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,817.16	01/2016 01/2016	11/2016	10(O) 10(R)	1/1
198	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,165.00	04/2009 -	09/2014	65(O) -	0/9
199	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	2,093.00	12/2016 -	12/2016	0(O) -	16/19
200	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,871.01	09/2008 -	03/2013	-	15/23
201	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00 -	11,846.00	1,139.00	05/2017 -	05/2017	0(O) -	7/43

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
202	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017	0(O) -	0/15
203	MOUDA STPP - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
204	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	1,242.00	09/2016 -	09/2016	0(O) -	14/14
205	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,969.63	08/2013 -	06/2015	22(O) -	0/17
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.83	02/2012 -	12/2013	22(O) -	1/13
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	364.17	11/2011 -	07/2014	32(O) -	0/11
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	385.35	11/2011 -	12/2013	25(O) -	1/14
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	136.78	01/2013 -	01/2014	12(O) -	1/6
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	233.38	11/2014 -	11/2014	0(O) -	2/12
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,Multi State	09/2013	680.69 -	680.69	-	03/2016 -	03/2016	0(O) -	0/0
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	122.75	03/2015 -	03/2015	0(O) -	3/15
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	51.97	04/2015 -	05/2015	1(O) -	0/16
214	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	613.65	11/2012 -	03/2014	16(O) -	0/11
215	Northern region system strengthening scheme XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	331.59	07/2013 -	03/2014	8(O) -	1/11
216	Northern region system strengthening scheme-XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	909.52	04/2013 -	03/2015	23(O) -	0/11
217	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,212.33	10/2010 01/2013	03/2014	41(O) 14(R)	0/6
218	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	4,121.24	09/2009 07/2014	07/2018	106(O) 48(R)	1/2
219	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	1,117.92	731.69	08/2013 -	09/2014	13(O) -	17/22
220	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,835.28	01/2012 -	03/2014	26(O) -	0/28
221	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,544.00	10/2012 -	10/2013	12(O) -	16/16
222	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	1,699.00	11/2016 -	11/2016	0(O) -	15/15
223	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,408.11	09/2010 08/2014	03/2018	90(O) 43(R)	11/11
224	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,Multi State	08/2008	2,360.95 2,580.90	2,580.90	2,076.70	08/2012 -	03/2014	19(O) -	0/5
225	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	119.62	06/2016 -	04/2015	-14(O) -	0/20
226	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	398.06	12/2014 -	11/2014	-1(O) -	2/2

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
227	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/7
228	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	207.18	08/2014 -	08/2014	0(O) -	2/19
229	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	495.42	02/2015 -	02/2015	0(O) -	0/14
230	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	357.54	11/2014 -	11/2014	0(O) -	0/16
231	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	490.30	01/2015 -	01/2015	0(O) -	3/19
232	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	158.93	08/2014 -	08/2014	0(O) -	7/20
233	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	220.72	06/2014 -	06/2014	0(O) -	7/20
234	Supplementary transmission associated with vellur TPS - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	101.95	04/2013 -	03/2014	11(O) -	4/15
235	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	160.94	06/2012 -	11/2013	17(O) -	0/3
236	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	912.05	08/2012 -	06/2014	22(O) -	0/11
237	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,400.74	09/2009 06/2013	12/2014	63(O) 18(R)	0/0
238	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	534.61	07/2010 02/2016	02/2017	79(O) 12(R)	1/10
239	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	112.33	01/2014 -	01/2014	0(O) -	3/18
240	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	573.52	08/2014 -	08/2014	0(O) -	2/19
241	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	1,032.40	10/2014 -	09/2014	-1(O) -	3/18
242	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,569.95	10/2012 -	06/2014	20(O) -	0/11
243	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	159.62	11/2011 -	12/2013	25(O) -	0/4
244	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	19.50	08/2014 -	08/2014	0(O) -	9/20
245	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	519.59	10/2014 -	10/2014	0(O) -	3/16
246	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	337.44	02/2014 -	02/2014	0(O) -	4/17
247	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	339.20	10/2013 -	03/2014	5(O) -	2/13

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
248	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	140.34	07/2013 -	12/2013	5(O) -	0/13
249	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	829.27	12/2013 -	03/2014	3(O) -	2/13
250	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	193.36	11/2013 -	09/2014	10(O) -	7/20
251	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,289.89	03/2013 -	05/2014	14(O) -	4/15
252	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	1,273.52	07/2014 -	07/2014	0(O) -	2/14
253	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	661.40	07/2013 -	05/2014	10(O) -	16/29
254	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	473.70	07/2006 -	02/2015	103(O) -	1/16
255	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	3,846.30	1,914.00	03/2013 -	03/2017	48(O) -	2/15
256	Trans. System associated with PALLATANA GBPP & BPTS. - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,452.60	12/2012 -	06/2014	18(O) -	0/11
257	Transm System for development of Pooling str. in NR part of West Bengal And Transfer of power from B - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	393.77	01/2015 -	12/2015	11(O) -	2/20
258	Transmission System associated with Mauda Stage-II - [N18000153]PGCIL,Multi State	09/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016	0(O) -	0/0
259	Transmission System of Vindhuchal -IV And Rihand -III Gen. Proj. - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,752.49	11/2012 -	03/2015	28(O) -	0/15
260	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,998.00	03/2014 -	05/2014	2(O) -	4/15
261	Transmission system for phase-I generation projects in orissa-part B - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,780.54	12/2013 -	05/2014	5(O) -	0/13
262	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.70	01/2013 -	03/2015	26(O) -	5/18
263	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	1,086.62	11/2013 -	03/2015	16(O) -	5/16
264	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 1,724.79	2,081.00	2,077.51	11/2009 02/2013	10/2013	47(O) 8(R)	0/3
265	VINDHYACHAL STTP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	573.00	08/2015 -	08/2015	0(O) -	11/12
266	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
267	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	368.16	07/2014 -	09/2017	38(O) -	1/1
268	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	457.27	09/2010 -	-	-	0/5

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
269	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	1,110.57	06/2015 -	06/2015	0(O) -	3/28
	Total		248,494.89 -	267,210.95	128,626.60				358/1363
	<u>Railways</u>								
270	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	184.06	2.00	- -	-	-	0/0
271	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	495.64	03/2014 -	12/2015	21(O) -	0/0
272	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	390.29	12/2009 03/2011	01/2014	49(O) 34(R)	0/0
273	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,820.00	134.16	- -	-	-	0/0
274	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	412.82	03/2011 03/2011	03/2011	-	0/0
275	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	725.00	559.04	06/1999 03/2011	03/2011	-	0/0
276	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	307.00	-	- -	-	-	0/0
277	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	1,566.00	122.20	- -	-	-	0/0
278	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	199.75	34.93	- -	-	-	0/0
279	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	252.00	-	- -	-	-	0/0
280	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	567.18	0.17	- -	-	-	0/0
281	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	1,215.30	37.48	03/2013 -	03/2013	-	0/0
282	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	218.39	16.64	- -	-	-	0/0
283	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	822.00	-	- -	-	-	0/0
284	Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh	04/2012	153.00 -	153.00	-	- -	-	-	0/0
285	Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State	04/2008	184.26 -	2,000.00	22.35	- -	-	-	0/0
286	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	242.09	-	- -	-	-	0/0
287	Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State	04/2010	338.54 -	338.54	77.27	- -	-	-	0/0
288	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12 -	312.12	30.77	- -	03/2015	-	0/0
289	Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi	04/2012	295.68 -	295.68	-	- -	-	-	0/0
290	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
291	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
292	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	528.00	2.88	- -	-	-	0/0
293	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.61	- -	-	-	0/0
294	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,039.29	1,423.98	484.15	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
295	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	225.47	12/2010 03/2011	03/2011	-	0/0
296	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	324.96	03/2004 12/2010	12/2014	129(O) 48(R)	0/0
297	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	99.62	04/2014 -	03/2017	35(O) -	0/0
298	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	195.64	72.35	- -	-	-	0/0
299	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya pradesh	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69(O) -	0/0
300	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.19	2,895.33	04/2008 03/2014	12/2016	104(O) 33(R)	0/0
301	Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka	04/2010	377.93 -	986.30	11.22	- -	-	-	0/0
302	Bandel-Boinchi 3rd line - [N22000221]ER,Multi State	04/2011	288.35 -	288.35	3.99	- -	-	-	0/0
303	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER) - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	179.63	12/2012 -	12/2013	12(O) -	0/0
304	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	246.08	0.11	- -	-	-	0/0
305	Bariarpur-Mananpurvia Kharagpuer, Lachimpur-Barahat - [N22000234]ER,Multi State	04/2007	450.55 -	450.55	9.35	- -	-	-	0/0
306	Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal	04/2012	255.64 -	255.64	-	- -	-	-	0/0
307	Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh	04/2010	337.49 -	337.49	0.12	- -	-	-	0/0
308	Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh	04/2012	923.23 -	923.23	-	- -	-	-	0/0
309	Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	289.64	0.07	- -	-	-	0/0
310	Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh	04/2008	1,046.88 -	2,966.99	37.92	- -	-	-	0/0
311	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	193.77	03/2011 -	-	-	0/0
312	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]WR,Gujarat	04/2008	318.24 -	485.65	1.89	03/2012 -	-	-	0/0
313	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	326.20	1.67	- -	-	-	0/0
314	Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State	04/2011	175.80 -	175.80	0.88	- -	-	-	0/0
315	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	267.37	33.82	- -	-	-	0/0
316	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
317	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	295.00	0.18	- -	-	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
318	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
319	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
320	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	243.78	26.85	- -	-	-	0/0
321	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	364.51	- -	12/2013	- -	0/0
322	Chhapra-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	177.38	42.98	03/2015 -	12/2015	9(O) -	0/0
323	Chandigarh-Baddi NL - [N22000296]NR,Multi State	04/2007	328.14 -	328.14	2.14	- -	-	-	0/0
324	Chandpara-Bangaon doubling with extension to Chandbazar and new MM for Bongaon-Poramaheshtala & Chand - [N22000242]ER,Multi State	04/2003	337.96 -	337.96	59.07	- -	-	-	0/0
325	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	951.24	525.75	- -	-	-	0/0
326	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	222.95	93.32	- -	-	-	0/0
327	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	520.00	458.96	- -	-	-	0/0
328	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	1,200.00	1.80	- -	-	-	0/0
329	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	378.56	104.60	- -	-	-	0/0
330	Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka	04/2013	327.25 -	327.25	-	- -	-	-	0/0
331	Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka	04/2013	558.00 -	558.00	-	- -	-	-	0/0
332	Chinai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-Sainthia via Kandi NL - [N22000225]ER,Multi State	04/2005	595.91 -	595.91	87.80	- -	-	-	0/0
333	Chottaudpur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	1,347.26	139.84	- -	-	-	0/0
334	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
335	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,242.25	944.72	03/2007 -	03/2015	96(O) -	0/0
336	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	556.64	266.48	- -	-	-	0/0
337	Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh	04/2013	829.00 -	829.00	-	- -	-	-	0/0
338	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
339	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	132.20	- -	-	-	0/0
340	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	233.72	- -	03/2014	- -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
341	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	501.62	12/2012 12/2012	02/2013	-	0/0
342	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	914.98	684.71	- -	12/2012	-	0/0
343	Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State	04/2007	1,640.04 -	1,640.04	153.94	- -	-	-	0/0
344	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	99.95	12/2011 02/2012	02/2012	-	0/0
345	Dangoaposi-Rajkharwan 3rd line Doubling - [N22000164]SER,Jharkhand	04/2010	309.44 -	388.67	47.81	12/2015 -	12/2015	0(O) -	0/0
346	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh 4th line with MM Baruipara Furfura NL - [N22000229]ER,Multi State	04/2010	296.44 -	296.44	3.21	- -	-	-	0/0
347	Darbhanga-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	366.73	4.20	- -	-	-	0/0
348	Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
349	Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State	04/2007	336.91 -	336.91	140.84	- -	-	-	0/0
350	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	376.59	0.17	- -	-	-	0/0
351	Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]NCR,Multi State	04/2010	622.41 2,030.50	2,030.50	1.22	02/2019 -	02/2019	0(O) -	0/0
352	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	651.17	7.08	- -	-	-	0/0
353	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
354	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
355	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
356	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	120.00 245.39	245.39	222.71	12/2008 -	09/2014	69(O) -	0/0
357	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	255.39	06/2013 06/2013	12/2014	18(O) 18(R)	0/0
358	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	189.24	1.79	- -	-	-	0/0
359	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	603.22	1.31	- -	-	-	0/0
360	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240(O) -	0/0
361	Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareilly - [N22000270]NR,Uttar Pradesh	04/2013	654.00 -	654.00	-	- -	-	-	0/0
362	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	281.61	02/2011 02/2011	03/2013	-	0/0
363	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	148.38	02/2006 -	06/2014	100(O) -	0/0
364	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	735.90	- -	03/2012	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
365	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
366	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	832.00	361.26	- 05/2009	05/2009	-	0/0
367	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	576.81	03/1994 -	01/2014	238(O) -	0/0
368	Gadag-Wadi NL - [N22000299]SWR,Karnataka	04/2013	1,117.00 -	1,117.00	-	- -	-	-	0/0
369	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	415.67	13.43	- -	-	-	0/0
370	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	445.25	0.94	- -	-	-	0/0
371	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	130.62	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
372	Grade Seperator at Dayabasti - [N22000269]NR,Delhi	04/1999	159.20 -	156.65	49.29	- -	-	-	0/0
373	Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0
374	Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	206.22	3.27	- -	-	-	0/0
375	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State	04/2011	1,176.09 3,845.60	3,845.60	1.71	02/2020 -	02/2020	0(O) -	0/0
376	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	192.85	- -	-	-	0/0
377	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	1,185.64	-	- 09/2009	-	-	0/0
378	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS and PU - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
379	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	412.91	730.05	- -	01/2013	-	0/0
380	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	147.94	- -	03/2014	- -	0/0
381	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	178.76	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
382	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	101.17	- -	-	-	0/0
383	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State	04/2000	157.17 -	157.17	75.86	- -	-	-	0/0
384	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	213.01	-	- -	-	-	0/0
385	Hansdiha-Godda NL - [N22000236]ER,Multi State	04/2011	267.09 -	267.09	0.10	- -	-	-	0/0
386	Hansnabad-Hingalgaon New BG line - [N22000218]ER,Multi State	04/2010	172.03 -	172.03	2.93	- -	-	-	0/0
387	Haridwar-Laksar - [N22000289]NR,Uttarakhand	04/2012	219.83 -	444.18	-	- -	-	-	0/0
388	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	38.33	03/2015 -	03/2015	0(O) -	0/0
389	Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana	04/2013	400.00 -	400.00	-	- -	-	-	0/0
390	Hospet-Hubli-Londa-Vascodagama DL - [N22000297]SWR,Karnataka	04/2010	2,127.00 -	2,127.00	47.34	- -	-	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
391	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State	04/2010	157.94 -	157.94	37.90	- -	-	-	0/0
392	Howrah-Development of station including segregation of arrival/departure and other amenities - [N22000249]ER,Multi State	04/2011	166.89 -	166.89	-	- -	-	-	0/0
393	Hyderabad/Secunderabad Multi Modal Transport System(MMTS) Phase-II - [N22000213]MRTP,Andhra Pradesh	04/2012	632.68 -	816.55	0.44	04/2012 -	-	-	0/0
394	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	836.10	06/2007 -	06/2007	-	0/0
395	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	718.40	03/2012 08/2012	-	-	0/0
396	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	724.00	485.23	03/2012 03/2012	12/2012	-	0/0
397	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	7,392.65	1,716.34	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
398	Jaggayyapet - Mellacheruvu - [N22000304]SCR,Andhra Pradesh	04/2007	313.24 -	313.24	-	01/1999 -	01/1999	-	0/0
399	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.47	237.99	03/2014 -	03/2014	0(O) -	0/0
400	Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State	04/2008	165.65 -	165.65	131.94	- -	-	-	0/0
401	Jaynagar-Bijalpur including extension Bijalpur-Bardibas(Nepal) GC - [N22000181]ECR,Bihar	04/2009	470.00 -	470.00	34.32	- -	-	-	0/0
402	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	322.56	03/2012 03/2012	03/2013	-	0/0
403	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,490.96	- -	03/2013	-	0/0
404	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	643.00	-	- -	-	-	0/0
405	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	744.71	510.40	- -	03/2014	-	1/1
406	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	800.00	759.11	- -	10/2012	-	0/0
407	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,022.64	741.46	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
408	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	124.50	- -	-	-	0/0
409	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
410	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	268.34	- -	03/2014	-	0/0
411	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
412	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	498.65	- 03/2010	03/2010	-	0/0
413	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,634.49	07/2005 -	-	-	0/0
414	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	175.15	- -	-	-	0/0
415	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	289.96	03/2012 03/2013	03/2013	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
416	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
417	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	358.07	- -	12/2012	-	0/0
418	Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State	04/2008	2,050.00 -	2,050.00	82.26	- -	-	-	0/0
419	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - Chapra new line and Naihati-Ranaghat 3 - [N22000224]ER,Multi State	04/2001	923.52 -	923.52	232.54	- -	-	-	0/0
420	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-Duttaphulia new line - [N22000227]ER,Multi State	04/2010	174.56 -	174.56	46.21	- -	-	-	0/0
421	Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra	04/2011	277.70 -	279.70	1.84	- -	-	-	0/0
422	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	218.36	126.65	12/2012 -	03/2015	27(O) -	0/0
423	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State	04/2010	423.66 -	423.66	136.58	03/2017 -	03/2017	0(O) -	0/0
424	Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State	04/2012	1,054.35 -	1,054.35	0.35	- -	-	-	0/0
425	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	287.99	425.91	01/1999 -	12/2013	179(O) -	0/0
426	Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh	04/2013	723.00 -	723.00	-	- -	-	-	0/0
427	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	252.96	1.57	- -	-	-	0/0
428	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
429	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	346.15	10.83	- -	-	-	0/0
430	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	397.91	05/2008 03/2011	-	-	0/0
431	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	231.61	03/2002 -	10/2013	139(O) -	0/0
432	Lakshmikantapur-Namkhana subsequently MM for Namkhana-Chandranagar, Kakdwip-Budakhali and Chandranag - [N22000216]ER,Multi State	04/1999	406.99 -	406.99	137.78	- -	-	-	0/0
433	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura Sharif NL - [N22000244]ER,Multi State	04/2009	257.42 -	257.42	33.39	03/2014 -	03/2014	0(O) -	0/0
434	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam	04/2012	246.07 -	246.07	0.11	- -	-	-	0/0
435	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,702.79	03/2009 -	03/2015	72(O) -	0/0
436	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.66	07/2008 -	07/2008	-	0/0
437	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	472.00	181.96	- -	02/2013	-	0/0
438	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	730.72	12/2011 12/2011	03/2013	-	0/0
439	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
440	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	444.28	03/2012 03/2013	03/2013	-	0/0
441	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	1,383.45	366.30	- -	-	-	0/0
442	MM from Buramara-Chakulia - [N22000305]SER,Multi State	04/2008	466.48 -	466.48	-	01/1999 -	01/1999	-	0/0
443	MM from Panskura-Ghatal NL - [N22000309]SER,West Bengal	04/2011	276.69 -	276.69	-	01/1999 -	01/1999	-	0/0
444	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,401.09	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
445	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	259.89	- -	03/2012	-	0/0
446	Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	450.00	11.07	- -	-	-	0/0
447	Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State	04/2011	601.43 -	800.00	0.15	- -	-	-	0/0
448	Magrahat-Diamond Harbour with MM Sangrampur-Krishnachandpur and Diamond Hatbour - Bahrahat-Kulpi NL - [N22000243]ER,Multi State	04/2009	493.96 -	493.96	115.49	- -	-	-	0/0
449	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20 -	258.20	0.29	- -	03/2016	-	0/0
450	Mansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur Mandi via Talwandi Saboo NL - [N22000268]NR,Punjab	04/2009	396.04 -	396.04	77.55	- -	-	-	0/0
451	Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
452	Marikuppam - Kuppam - [N22000308]SWR,Karnataka	04/2012	285.57 -	285.57	-	01/1999 -	01/1999	-	0/0
453	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittisgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	965.16	557.82	- -	-	-	0/0
454	Meerut-Muzaffarnagar Patch DL - [N22000267]NR,Uttar Pradesh	04/2012	289.79 -	289.79	-	- -	-	-	0/0
455	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	439.88	0.70	- -	-	-	0/0
456	Monigram- Nimitita - [N22000301]ER,Multi State	04/2012	250.93 -	250.93	-	- -	-	-	0/0
457	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
458	Mudkhed-Parbhani - [N22000283](SCR),Maharashtra	04/2011	390.60 -	390.60	1.23	- -	-	-	0/0
459	Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka	04/2007	179.65 -	645.00	168.74	- -	-	-	0/0
460	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	165.82	0.25	- -	-	-	0/0
461	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
462	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	228.05	0.65	- -	-	-	0/0
463	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	668.35	02/2009 -	03/2012	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
464	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	358.05	07/2012 -	-	-	0/0
465	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	42.43	- -	-	-	0/0
466	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	144.47	- -	03/2016	- -	0/0
467	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,483.63	12/2008 -	03/2015	75(O) -	0/0
468	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	169.82	32.10	- -	-	-	0/0
469	Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh	04/2011	1,313.48 -	1,313.48	0.52	- -	-	-	0/0
470	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	620.57	-	- -	-	-	0/0
471	New Alipur to Akra, MM for Budge Budge-Pujali NL, Pujali-Uluberia(Birshivpur) And Pujali-Bahrahat NL - [N22000240]ER,Multi State	04/2010	494.54 -	494.54	31.92	- -	-	-	0/0
472	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.35	- -	03/2015	- -	0/0
473	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	242.22	38.18	- -	-	-	0/0
474	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	4,083.02	2.79	- -	-	-	0/0
475	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	247.75	150.67	- -	03/2014	- -	0/0
476	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	238.83	98.33	- -	03/2015	- -	0/0
477	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	221.42	21.80	- -	-	-	0/0
478	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
479	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	209.77	22.93	- -	03/2015	- -	0/0
480	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	283.55	0.51	- -	03/2015	- -	0/0
481	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai - [N22000209]NEFR,Multi State	04/1999	523.17 -	1,393.44	1,033.00	- -	-	-	0/0
482	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24(O) -	0/0
483	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshinেশ্বর (MTP) - [N22000109]RVNL,West Bengal	04/2010	2,298.42 -	2,298.42	59.82	03/2014 -	03/2016	24(O) -	0/0
484	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,913.51	350.64	03/2016 -	03/2016	0(O) -	0/0
485	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	230.80	03/2016 -	03/2016	0(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
486	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbander (MTP) - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	57.27	03/2016 -	06/2016	3(O) -	0/0
487	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
488	PANVEL PEN DOUBLING - [N22000255]CR, Multi State	04/2006	191.00 -	191.00	199.52	- -	01/2014	- -	0/0
489	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47 2,921.00	2,921.00	1,903.68	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
490	PEDAPALI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	925.30	631.17	- -	02/2014	- -	0/0
491	PEN ROHA DOUBLING - [N22000254]CR, Multi State	04/2007	203.00 -	203.00	161.94	- -	03/2014	- -	0/0
492	Palanpur-Samakhayali (DL) - [N22000144]WR, Gujarat	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
493	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	293.74	139.31	12/2010 12/2010	12/2010	-	0/0
494	Pirpainti-Bhagalpur - [N22000222]ER, Multi State	04/2011	261.38 -	261.38	14.55	- -	-	-	0/0
495	Pirpainti-Jasidih - [N22000219]ER, Multi State	04/2013	915.98 -	915.98	-	- -	-	-	0/0
496	Plassey-Jiaganj Doubling - [N22000220]ER, Multi State	04/2011	248.07 -	248.07	9.83	03/2015 -	03/2015	0(O) -	0/0
497	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER, Multi State	04/2011	299.60 -	299.60	1.09	03/2017 -	03/2017	0(O) -	0/0
498	Pushkar-Merta - [N22000151]NWR, Rajasthan	04/2013	323.00 -	323.00	-	- -	-	-	0/0
499	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 842.35	1,029.92	821.56	- -	03/2013	-	0/6
500	Qadian-Beas - [N22000295]NR, Punjab	04/2011	205.22 -	205.22	1.22	- -	-	-	0/0
501	Quilon-Tirunelveli - Trichendur, Tenkasi - [N22000303]SR, Tamil Nadu	04/1999	460.94 -	1,030.00	-	01/1999 -	01/1999	-	0/0
502	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	289.93	-	12/2007 03/2010	-	-	0/0
503	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 2,363.00	2,363.00	1,177.39	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
504	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, Odisha	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
505	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.90	229.07	- -	-	-	0/0
506	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, Jharkhand	04/1997	194.07 194.07	596.90	350.33	06/2004 -	12/2014	126(O) -	0/0
507	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR, Multi State	01/2004	915.70 915.70	3,019.17	2,291.38	- -	03/2014	- -	0/0
508	Rajkot-Veraval, Wansjalja to Jataisar with new MM for Shapur-Saradiya And Somnath-Kodinar (GC) - [N22000143]WR, Gujarat	04/1994	320.66 -	913.48	461.38	- -	-	-	0/0
509	Ramanagaram-Mysore doubling with electrification of Kengesii- Mysore (SWR) - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	521.29	03/2013 -	03/2014	12(O) -	0/0
510	Rani-Marwar Jn. Patch doubling - [N22000156]NWR, Rajasthan	04/2012	288.97 -	288.97	0.07	- -	-	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
511	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC) - [N22000153]NWR,Rajasthan	04/2010	739.65 -	872.22	783.39	- -	-	-	0/0
512	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	2,082.75	11.81	- -	-	-	0/0
513	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	1,421.25	281.83	03/2012 -	-	-	0/0
514	Rayadurga-Tumkur NL - [N22000279]SWR,Multi State	04/2007	970.34 -	970.34	198.87	- -	-	-	0/0
515	Rohtak-Meham Hansi - [N22000272]NR,Haryana	04/2012	287.00 -	287.00	0.29	- -	-	-	0/0
516	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	714.10	6.83	- 12/2017	12/2017	- 0(R)	0/0
517	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
518	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	61.04	12/2015 -	03/2017	15(O) -	0/0
519	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	818.29	105.60	02/2015 -	02/2015	0(O) -	0/0
520	Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State	04/2011	193.44 -	193.44	12.34	- -	-	-	0/0
521	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	325.00	232.39	- -	-	-	0/0
522	Sakri-Nirmali and Jhanjharpur-Laukahabazar and Saharsa-Forbesganj (GC) - [N22000180]ECR,Bihar	04/2004	372.14 -	355.81	365.77	- -	-	-	0/0
523	Santoshpur-Remount Road via Garden Reach-Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	268.52	77.87	- -	-	-	0/0
524	Shimoga-Harihar NL - [N22000278]SWR,Karnataka	04/2011	562.74 -	562.74	0.06	- -	-	-	0/0
525	Sitamahi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	678.62	15.02	- -	-	-	0/0
526	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghatakpur NL - [N22000241]ER,Multi State	04/2000	297.47 -	297.47	51.70	- -	-	-	0/0
527	Sondalia-Champapukur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State	04/2010	277.28 -	277.28	35.91	- -	-	-	0/0
528	Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State	04/2013	296.00 -	296.00	-	- -	-	-	0/0
529	Sriperumbudur-Guduvanchery with spur to Irungattukkottai-Avadi-Sriperumbudur - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	839.00	-	- -	-	-	0/0
530	Sultanganj-Katuria via Asarganj, Tarapur And Belhar - [N22000217]ER,Multi State	04/2007	450.00 -	450.00	7.70	- -	-	-	0/0
531	Suratpura - Hanumangarh - Sriganganagar Gauge Conversion (NWR) - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	435.49	03/2014 -	03/2014	0(O) -	0/0
532	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	128.31	- -	-	-	0/0
533	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	1,074.47	449.48	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
534	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	640.12	- 12/2009	02/2012	-	0/0
535	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	820.00	179.17	- -	-	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
536	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	420.00	58.64	- -	-	-	0/0
537	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	900.00	551.56	- -	-	-	0/0
538	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268]MRTT,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,460.35	12/2006 08/2010	08/2010	-	0/0
539	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	171.02	104.84	06/2013 -	06/2014	12(O) -	0/0
540	Tarakeshwar-Magra New BG line - [N22000235]ER,Multi State	04/2010	365.17 -	365.17	1.43	- -	-	-	0/0
541	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.93 -	236.93	-	- -	-	-	0/0
542	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	49.10	03/2012 -	02/2013	-	0/0
543	Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka	04/2011	913.00 -	913.00	0.46	- -	-	-	0/0
544	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181(O) -	0/0
545	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	1,116.53	237.72	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
546	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	699.00	03/2014 -	03/2014	0(O) -	0/0
547	Unchahar-Amethi - [N22000294]NR,Uttar Pradesh	04/2012	380.00 -	380.00	0.36	- -	-	-	0/0
548	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	548.01	199.30	- 03/2010	-	-	0/0
549	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
550	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	685.17	29.05	- -	-	-	0/0
551	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	279.40	120.47	- -	04/2014	- -	0/0
552	Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra	04/2008	697.00 -	1,604.00	20.47	- -	-	-	0/0
553	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	297.85	2.15	- -	-	-	0/0
554	White Field-Kolar NL - [N22000280]SWR,Karnataka	04/2011	341.05 -	348.85	0.17	- -	-	-	0/0
555	Yamunanagar-Chandigarh via Sadhaura Narayanganh - [N22000293]NR,Multi State	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		149,162.48 -	264,395.10	73,591.95				1/7
	<u>Road Transport And Highways</u>								
556	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	250.50	230.10	10/2014 -	10/2014	0(O) -	0/0
557	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	373.47	40.66	07/2014 -	07/2014	0(O) -	0/0
558	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	395.20	05/2013 -	03/2014	10(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
559	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	642.20	11/2013 -	11/2013	0(O) -	0/0
560	2 Laning of Muzaffarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
561	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	318.00	08/2013 -	02/2015	18(O) -	0/0
562	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	624.00	314.70	04/2014 -	04/2014	0(O) -	0/0
563	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,Madhya pradesh	10/2011	1,565.00 -	1,565.00	691.40	10/2014 -	10/2014	0(O) -	0/0
564	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
565	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	98.48	01/2014 -	01/2014	0(O) -	0/0
566	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	189.10	02/2014 -	02/2014	0(O) -	0/0
567	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	564.60	02/2014 -	04/2014	2(O) -	0/0
568	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014	0(O) -	0/0
569	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	161.20	05/2014 -	05/2014	0(O) -	0/0
570	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,Gujarat	03/2012	828.00 -	828.00	490.60	09/2014 -	09/2014	0(O) -	0/0
571	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,734.00	08/2014 -	07/2015	11(O) -	0/0
572	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,352.00	06/2013 -	12/2013	6(O) -	0/0
573	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.39	09/2013 -	07/2014	10(O) -	0/0
574	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	843.90	08/2013 -	12/2013	4(O) -	0/0
575	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.40	07/2013 -	12/2013	5(O) -	0/0
576	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	398.00	441.10	02/2014 -	02/2014	0(O) -	0/0
577	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,266.00	08/2013 -	12/2014	16(O) -	0/0
578	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,328.00	08/2013 -	12/2014	16(O) -	0/0
579	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	299.60	08/2013 -	12/2015	28(O) -	0/0
580	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	1,396.18	1,048.00	09/2014 -	09/2014	0(O) -	0/0
581	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	240.70	09/2007 -	03/2014	78(O) -	0/0
582	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	2,125.24	34.28	12/2015 -	12/2015	0(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
583	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,144.00	11/2012 -	12/2013	13(O) -	0/0
584	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.60	01/2009 -	12/2013	59(O) -	0/0
585	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	-	0/0
586	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	11/2013	117(O) -	0/0
587	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	357.00	09/2013 -	12/2014	15(O) -	0/0
588	BARSAT-KRISHNANAGAR - [N24000229]NHAI,West Bengal	08/2012	867.00 -	867.00	-	02/2015 -	02/2015	0(O) -	0/0
589	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	2,388.00	1,388.00	06/2014 -	06/2014	0(O) -	0/0
590	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	567.90	- -	10/2013	-	2/2
591	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9(O) -	0/0
592	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	509.40	08/2013 -	12/2013	4(O) -	0/0
593	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	289.00	06/2008 -	03/2014	69(O) -	0/0
594	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	252.60	06/2008 -	03/2014	69(O) -	0/0
595	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	239.90	06/2005 -	03/2014	105(O) -	0/0
596	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	297.90	04/2010 -	12/2014	56(O) -	0/0
597	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65(O) -	0/0
598	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	839.20	03/2013 -	12/2013	9(O) -	0/0
599	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	667.90	- -	12/2013	-	0/1
600	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	12/2013	7(O) -	0/0
601	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	446.20	10/2011 -	03/2014	29(O) -	0/0
602	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.15) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	857.90	10/2011 -	06/2014	32(O) -	0/0
603	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.80	10/2008 -	06/2014	68(O) -	0/0
604	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015	0(O) -	0/0
605	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	660.30	05/2010 -	10/2013	41(O) -	0/0
606	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	582.90	07/2013 -	12/2013	5(O) -	0/0
607	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
608	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	718.70	- -	12/2013	- -	1/1
609	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	253.90	06/2008 -	03/2014	69(O) -	0/0
610	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	207.70	05/2008 -	12/2013	67(O) -	0/0
611	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	305.20	09/2010 -	08/2014	47(O) -	0/0
612	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	1,573.00	17.23	09/2015 -	09/2015	0(O) -	0/0
613	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	475.50	09/2008 -	12/2013	63(O) -	0/0
614	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015	0(O) -	0/0
615	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	160.00	10/2013 -	11/2015	25(O) -	0/0
616	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30(O) -	0/0
617	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	144.30	09/2008 -	03/2014	66(O) -	0/0
618	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.46	02/2004 -	09/2013	-	0/0
619	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,287.00	08/2013 -	06/2014	10(O) -	0/0
620	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	276.20	04/2008 -	03/2014	71(O) -	0/0
621	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	217.60	04/2008 -	03/2014	71(O) -	0/0
622	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60(O) -	0/0
623	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,123.00	09/2012 -	12/2013	15(O) -	0/0
624	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26(O) -	0/0
625	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74(O) -	0/0
626	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	324.60	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
627	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	158.70	07/2009 -	05/2014	58(O) -	0/0
628	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	70.00	09/2007 -	04/2014	79(O) -	0/0
629	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	281.10	10/2013 -	03/2014	5(O) -	0/0
630	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	196.57	08/2004 -	10/2013	110(O) -	0/0
631	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	204.82	08/2004 07/2010	10/2013	110(O) 39(R)	0/0
632	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	948.00	01/2013 -	10/2013	9(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
633	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,790.00	- -	10/2013	- -	3/3
634	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	532.70	05/2013 -	02/2014	9(O) -	0/0
635	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8(O) -	0/0
636	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	651.60	02/2013 -	12/2013	10(O) -	0/0
637	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11(O) -	0/0
638	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.40	09/2009 -	12/2013	51(O) -	0/0
639	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	536.00	518.00	01/2014 -	01/2014	0(O) -	0/0
640	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,975.00	12/2012 -	02/2014	14(O) -	0/0
641	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	280.40	10/2008 -	12/2013	62(O) -	0/0
642	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	295.00	10/2008 -	12/2013	62(O) -	0/0
643	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	702.16	498.90	07/2014 -	07/2014	0(O) -	0/0
644	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	938.40	- -	06/2014	- -	2/3
645	Kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	672.60	07/2013 -	06/2014	11(O) -	0/0
646	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	12/2013	19(O) -	0/0
647	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42(O) -	0/0
648	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	235.20	09/2009 -	09/2014	60(O) -	0/0
649	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	257.00	07/2012 -	07/2014	24(O) -	0/0
650	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	125.00	11/2008 -	06/2014	67(O) -	0/0
651	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	93.63	04/2009 -	12/2014	68(O) -	0/0
652	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	72.60	11/2008 -	12/2014	73(O) -	0/0
653	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	169.00	04/2009 -	12/2014	68(O) -	0/0
654	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,876.00	06/2013 -	03/2014	9(O) -	0/0
655	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	515.80	03/2013 -	03/2014	12(O) -	0/0
656	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	301.10	06/2008 -	03/2014	69(O) -	0/0
657	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
658	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19 -	484.19	282.80	10/2014 -	10/2014	0(O) -	0/0
659	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	308.70	04/2008 -	05/2014	73(O) -	0/0
660	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	266.10	06/2008 -	12/2013	66(O) -	0/0
661	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	288.30	06/2008 -	12/2013	66(O) -	0/0
662	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
663	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	288.40	06/2011 06/2011	10/2013	28(O) 28(R)	0/2
664	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	1,129.00	02/2010 -	12/2014	58(O) -	0/0
665	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11(O) -	0/0
666	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013	-	0/0
667	PANIKHOLI-RIMOLI - [N24000197]NHAI, Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13(O) -	0/0
668	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00 -	807.00	1,318.00	10/2014 -	10/2014	0(O) -	0/0
669	PANVEL-INDAPUR - [N24000216]NHAI, Multi State	12/2011	942.69 -	942.69	198.50	06/2014 -	06/2014	0(O) -	0/0
670	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	327.60	05/2008 -	12/2013	67(O) -	0/0
671	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00 -	574.00	655.30	03/2014 -	03/2014	0(O) -	0/0
672	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	671.30	625.90	02/2013 -	10/2013	8(O) -	0/0
673	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	1,325.00	07/2012 -	12/2013	17(O) -	0/0
674	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	1,724.55	1,201.00	03/2013 -	04/2014	13(O) -	0/0
675	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00 -	835.00	388.20	01/2014 -	01/2014	0(O) -	0/0
676	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	12/2013	25(O) -	0/0
677	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17(O) -	0/0
678	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	973.60	07/2015 -	06/2016	11(O) -	0/0
679	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	338.40	10/2008 -	03/2014	65(O) -	0/0
680	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, Multi State	12/2012	1,479.00 -	1,479.00	227.90	06/2015 -	06/2015	0(O) -	0/0
681	REENGUS SIKAR - [N24000227]NHAI, Rajasthan	03/2012	333.51 -	333.51	236.80	09/2014 -	09/2014	0(O) -	0/0
682	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00 -	650.00	1,119.00	11/2013 -	11/2013	0(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
683	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	12/2013	35(O) -	0/0
684	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	725.40	03/2013 -	12/2013	9(O) -	0/0
685	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	909.00	941.90	05/2014 -	05/2014	0(O) -	0/0
686	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	240.40	09/2007 -	03/2014	78(O) -	0/0
687	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	191.30	07/2008 -	03/2013	-	0/0
688	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0
689	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013	0(O) -	0/0
690	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	1,535.00	1,218.00	05/2014 -	05/2014	0(O) -	0/0
691	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31(O) -	0/0
692	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	03/2014	72(O) -	0/0
693	SRINAGAR TO BANIHAL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0
694	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	162.71	04/2004 -	11/2013	115(O) -	0/0
695	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,721.00	08/2011 -	12/2013	28(O) -	0/0
696	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	09/2014	63(O) -	0/0
697	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	860.70	07/2010 -	03/2014	44(O) -	0/0
698	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	1,166.00	11/2013 -	11/2013	0(O) -	0/0
699	Tirupati - Tiruthani - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	571.00	-	10/2013 -	10/2013	0(O) -	0/0
700	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	119.10	05/2013 -	12/2013	7(O) -	0/0
701	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	-	04/2013	-	2/2
702	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	921.30	03/2014 -	03/2014	0(O) -	0/0
703	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	193.10	198.60	03/2008 -	02/2008	-	0/0
704	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	54.59	11/2012 -	03/2014	16(O) -	0/0
705	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,Tamil Nadu	06/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	0(O) -	0/0
706	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	202.40	06/2014 -	06/2014	0(O) -	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		104,964.22 -	106,902.84	83,933.30				10/14
	<u>Shipping And Ports</u>								
707	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 11/2011	11/2011	-	0/0
708	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	-	0/0
709	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
710	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	448.43	12/2012 11/2013	11/2013	11(O) 0(R)	0/0
711	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
712	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014	0(O) -	0/0
713	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-1(O) 0(R)	0/0
714	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,429.10	978.39	12/2010 09/2012	03/2015	51(O) 30(R)	0/0
715	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
716	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
717	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	-	-	0/0
718	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
719	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 12/2013	12/2013	93(O) 0(R)	0/0
720	Mechanization of coal handling facilities to 200000 DWT Vessels on DBFOT basis - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
721	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
722	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
723	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	832.04	10/2008 11/2010	-	-	0/0
724	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUYPEEN COCHIN - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0

Sector Wise Details

(Oct,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
725	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT basis - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	17,871.52	8,655.74				0/1
	<u>Telecommunications</u>								
726	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59(O) -	0/0
727	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38(O) 21(R)	0/0
728	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	84.39	06/2009 -	12/2013	54(O) -	0/0
729	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 Punjab - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
730	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	-	0/0
731	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
732	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
733	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
734	Supply Installation testing and commissioning of Rural Wimax network Phase-II - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	237.44	05/2011 -	12/2013	31(O) -	0/0
	Total		4,742.45 -	4,646.10	1,736.42				0/0
	<u>Urban Development</u>								
735	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
736	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
737	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	5,302.74	03/2016 -	03/2016	0(O) -	0/0
738	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	431.52	09/2014 -	05/2015	8(O) -	0/0
	Total		44,245.18 -	49,518.08	8,001.83				3/3
	<u>Water Resources</u>								
739	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0

Sector Wise Details									
(Oct,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Grand Total		908,391.61	1,087,044.20	511,194.29				1096/3689

Sector wise current status of projects on the Flash Report

Urban Development


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

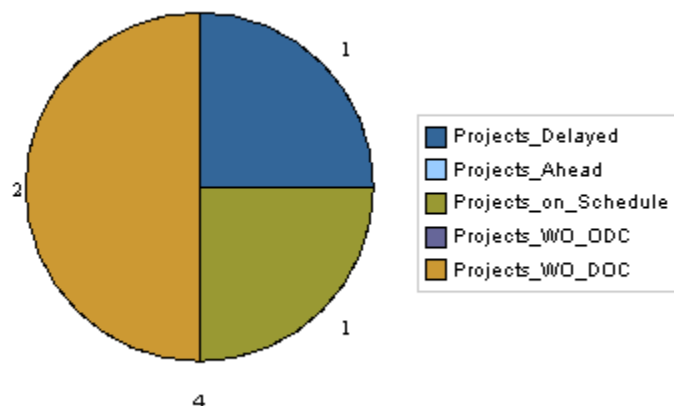

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till October, 2013 is Rs. 8001.83 crore, which is 16.2% of the revised cost of the projects.

Figures are in Rs. Crore

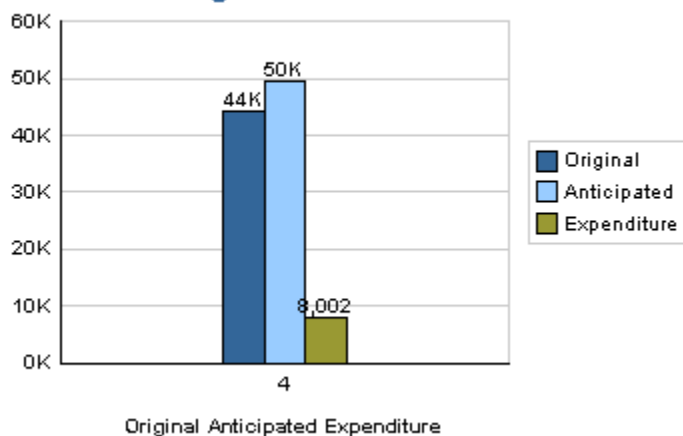

Sector wise current status of projects on the Flash Report

Telecommunications

Current Status:


Number of Projects 9

Number of Projects Delayed 4

Number of Projects Without Date Of Commissioning 5

Brief Analysis


Project Status with respect to Original Schedule: Out of 9 projects, 4 projects are delayed .5 projects do not have fixed dates of commissioning.

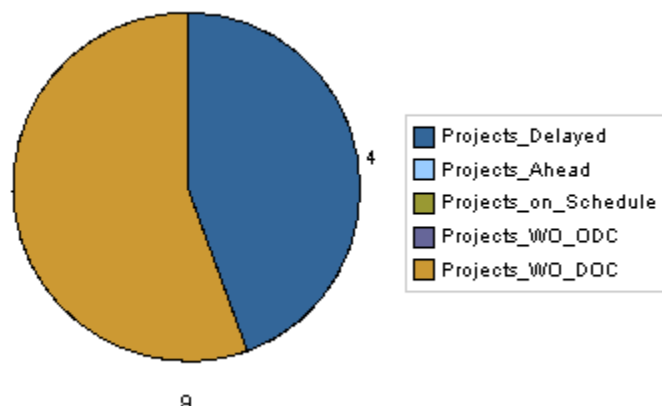

Investment Scenario

The Total Original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 4742.45 crore but this was subsequently revised to Rs. 4646.1 crore implying a cost overrun of -2%. The expenditure incurred on these projects till October, 2013 is Rs. 1736.42 crore, which is 37.4% of the revised cost of the projects.

Figures are in Rs. Crore

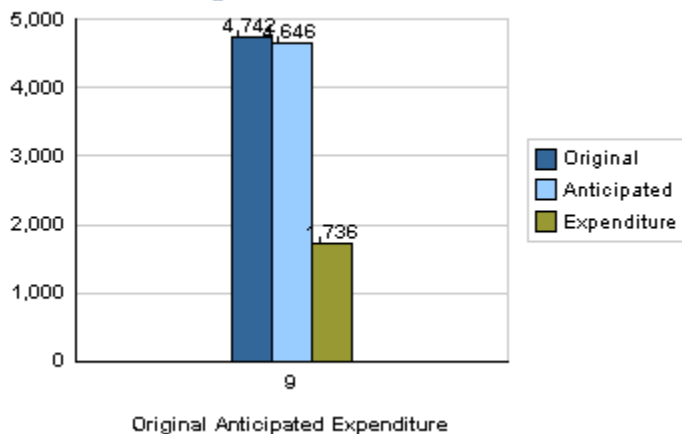

Sector wise current status of projects on the Flash Report


Shipping And Ports

Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	4
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	13

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 1 project are on schedule and 4 projects are delayed .13 projects do not have fixed dates of commissioning.

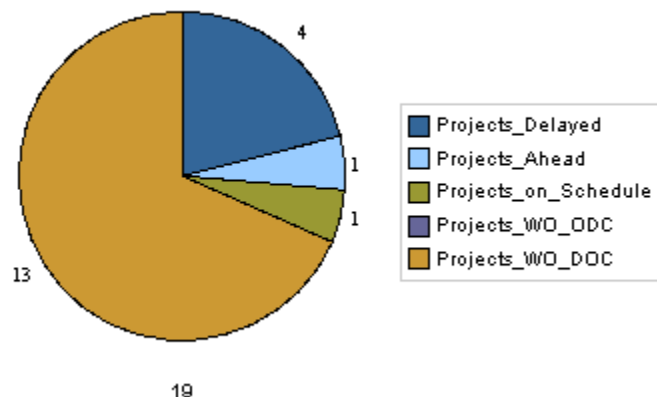

Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17871.52 crore implying a cost overrun of 14.4%. The expenditure incurred on these projects till October, 2013 is Rs. 8655.74 crore, which is 48.4% of the revised cost of the projects.

Figures are in Rs. Crore

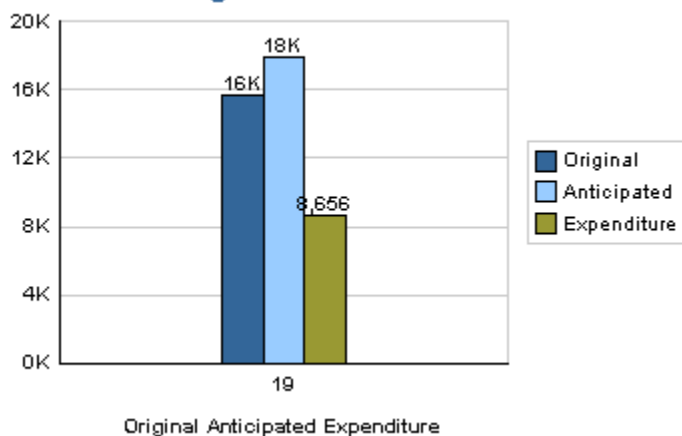

Sector wise current status of projects on the Flash Report

Road Transport And Highways


Current Status:

Number of Projects	151
Number of Projects On Schedule	40
Number of Projects Delayed	100

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	6

Brief Analysis


Project Status with respect to Original Schedule: Out of 151 projects, 40 projects are on schedule and 100 projects are delayed .6 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

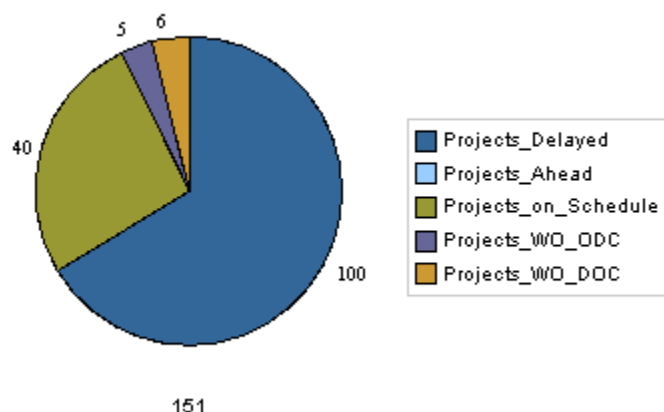

Investment Scenario

The Total Original cost of implementation of 151 projects when sanctioned, was of the order of Rs. 104964.22 crore but this was subsequently revised to Rs. 106902.84 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till October, 2013 is Rs. 83933.3 crore, which is 78.5% of the revised cost of the projects.

Figures are in Rs. Crore

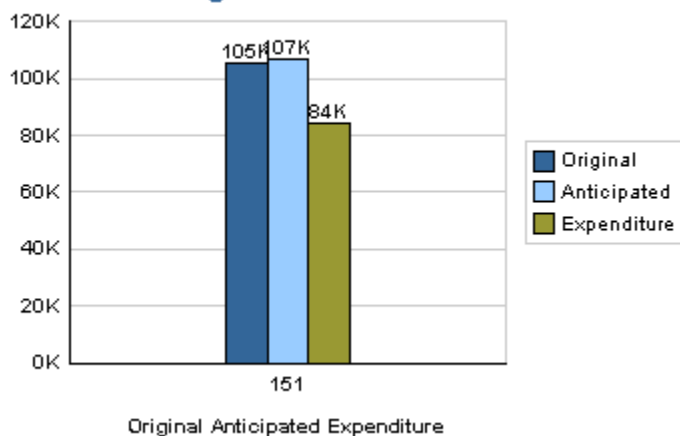

Sector wise current status of projects on the Flash Report

Railways


Current Status:

Number of Projects	286
Number of Projects On Schedule	15
Number of Projects Delayed	40

Number of Projects Without Original Date of Commissioning	21
Number of Projects Without Date Of Commissioning	210

Brief Analysis


Project Status with respect to Original Schedule: Out of 286 projects, 15 projects are on schedule and 40 projects are delayed .210 projects do not have fixed dates of commissioning.21 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

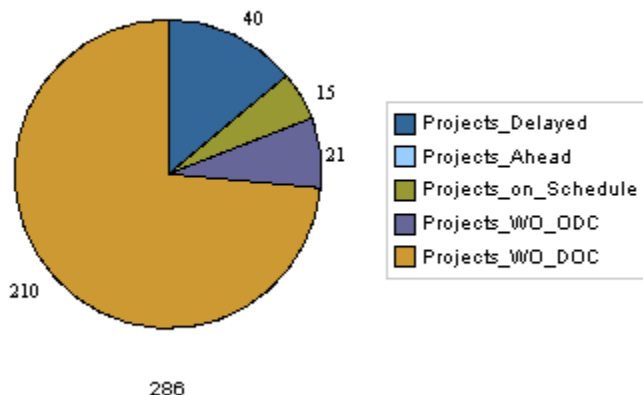

Investment Scenario

The Total Original cost of implementation of 286 projects when sanctioned, was of the order of Rs. 149162.48 crore but this was subsequently revised to Rs. 264395.1 crore implying a cost overrun of 77.3%. The expenditure incurred on these projects till October, 2013 is Rs. 73591.95 crore, which is 27.8% of the revised cost of the projects.

Figures are in Rs. Crore

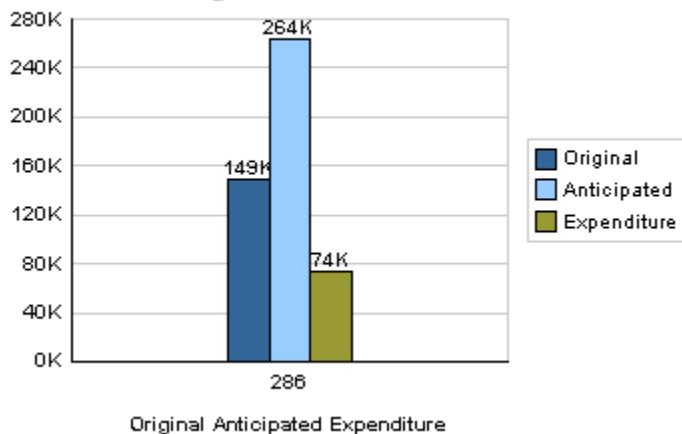

Sector wise current status of projects on the Flash Report

Power


Current Status:

Number of Projects	98
Number of Projects On Schedule	38
Number of Projects Delayed	52
Number of Projects Ahead	3

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 98 projects, 3 projects are ahead of schedule, 38 projects are on schedule and 52 projects are delayed .5 projects do not have fixed dates of commissioning.

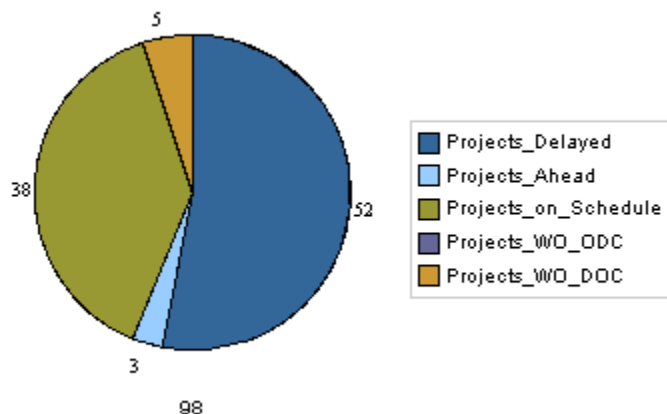

Investment Scenario

The Total Original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 248494.89 crore but this was subsequently revised to Rs. 267210.95 crore implying a cost overrun of 7.5%. The expenditure incurred on these projects till October, 2013 is Rs. 128626.6 crore, which is 48.1% of the revised cost of the projects.

Figures are in Rs. Crore

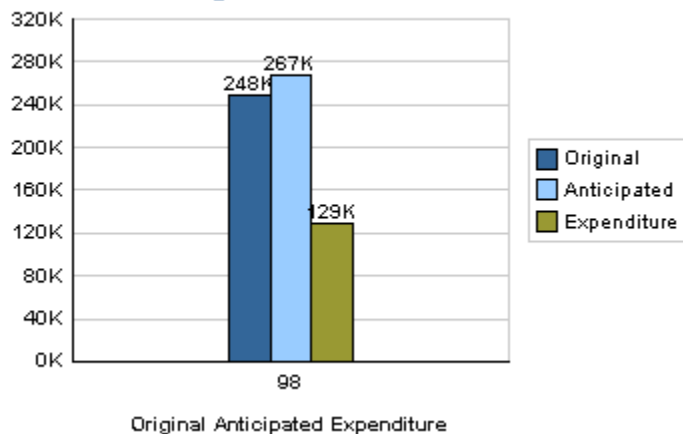

Sector wise current status of projects on the Flash Report

Petroleum


Current Status:

Number of Projects	85
Number of Projects On Schedule	22
Number of Projects Delayed	48

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	14

Brief Analysis


Project Status with respect to Original Schedule: Out of 85 projects, 22 projects are on schedule and 48 projects are delayed .14 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

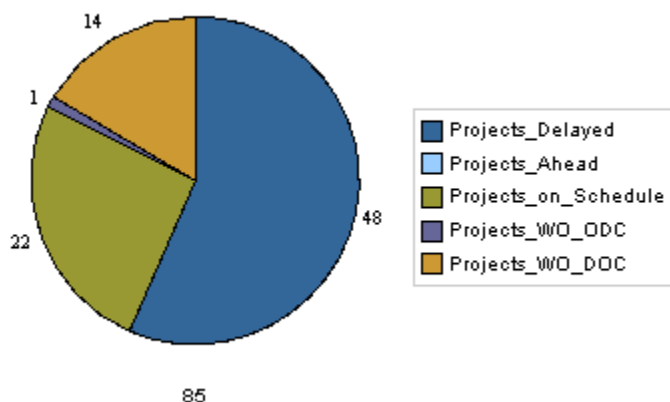

Investment Scenario

The Total Original cost of implementation of 85 projects when sanctioned, was of the order of Rs. 184960.03 crore but this was subsequently revised to Rs. 200046.76 crore implying a cost overrun of 8.2%. The expenditure incurred on these projects till October, 2013 is Rs. 99431.39 crore, which is 49.7% of the revised cost of the projects.

Figures are in Rs. Crore

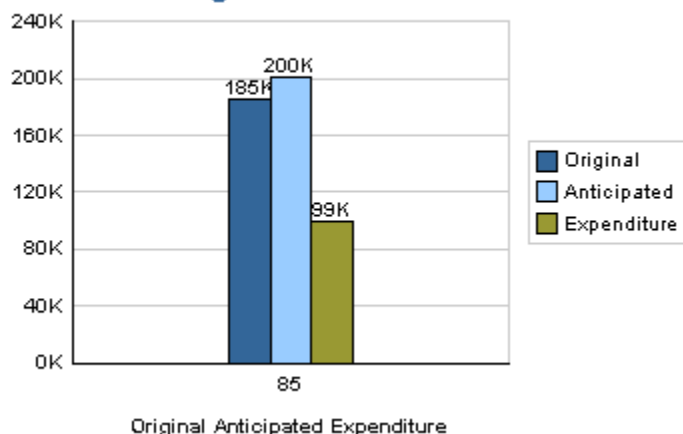

Sector wise current status of projects on the Flash Report

Steel


Current Status:

Number of Projects	18
Number of Projects On Schedule	3
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 18 projects, 3 projects are on schedule and 14 projects are delayed .1 project do not have fixed dates of commissioning.

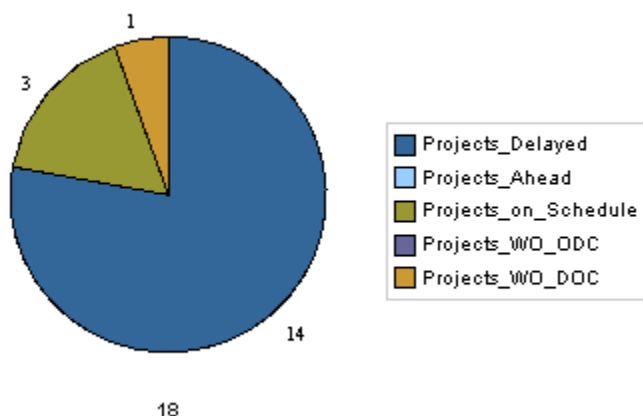

Investment Scenario

The Total Original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 65597.22 crore but this was subsequently revised to Rs. 71782.4 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till October, 2013 is Rs. 54194.19 crore, which is 75.5% of the revised cost of the projects.

Figures are in Rs. Crore

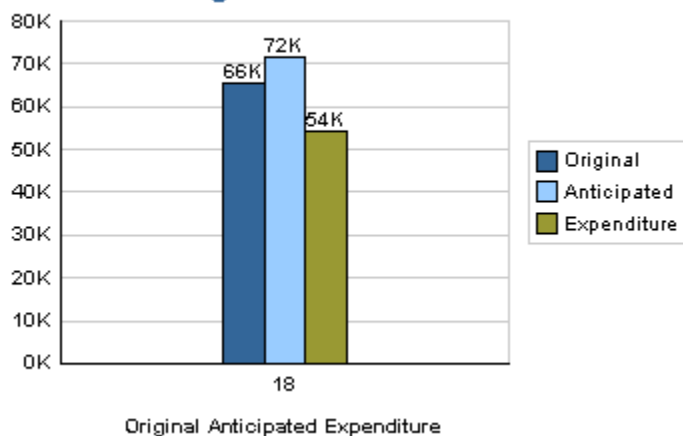

Sector wise current status of projects on the Flash Report

Coal


Current Status:

Number of Projects	55
Number of Projects On Schedule	23
Number of Projects Delayed	30

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 55 projects, 23 projects are on schedule and 30 projects are delayed .2 projects do not have fixed dates of commissioning.

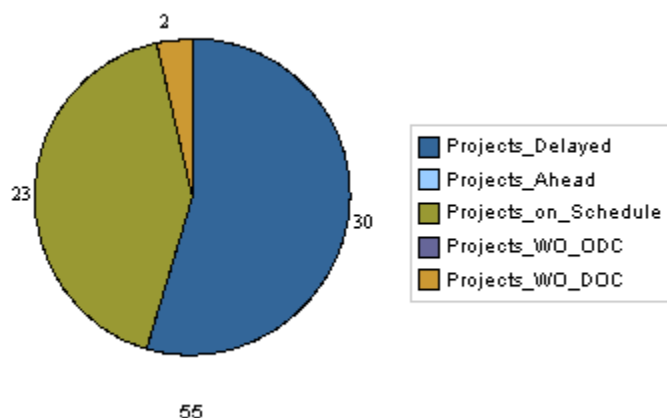

Investment Scenario

The Total Original cost of implementation of 55 projects when sanctioned, was of the order of Rs. 38127.05 crore but this was subsequently revised to Rs. 41212.5 crore implying a cost overrun of 8.1%. The expenditure incurred on these projects till October, 2013 is Rs. 16090.32 crore, which is 39% of the revised cost of the projects.

Figures are in Rs. Crore

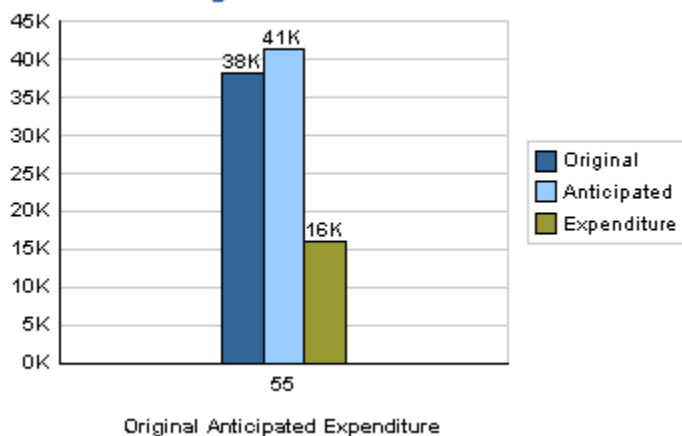

Sector wise current status of projects on the Flash Report

Civil Aviation


Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule and 3 projects are delayed .3 projects do not have fixed dates of commissioning.

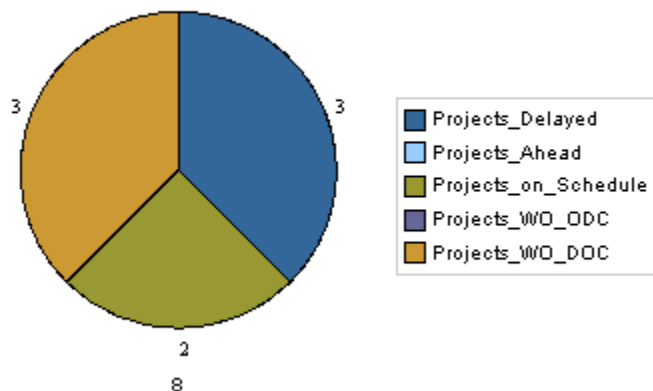

Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6624.95 crore implying a cost overrun of 9.8%. The expenditure incurred on these projects till October, 2013 is Rs. 5473.72 crore, which is 82.6% of the revised cost of the projects.

Figures are in Rs. Crore

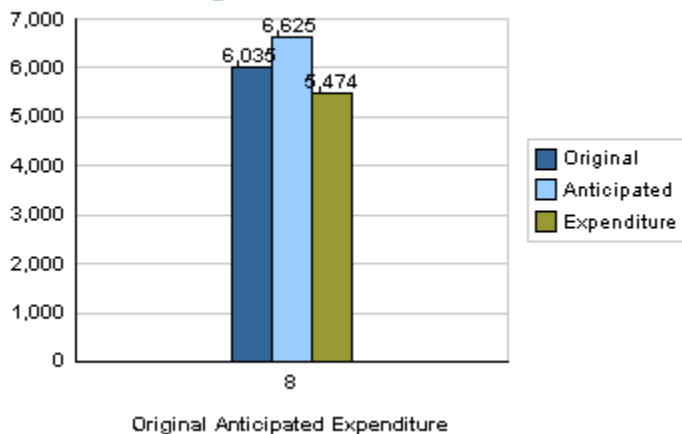

Sector wise current status of projects on the Flash Report


Atomic Energy

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

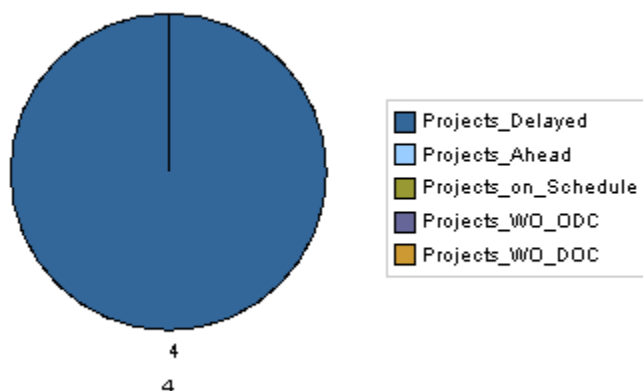

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till October, 2013 is Rs. 26912.83 crore, which is 57.6% of the revised cost of the projects.

Figures are in Rs. Crore

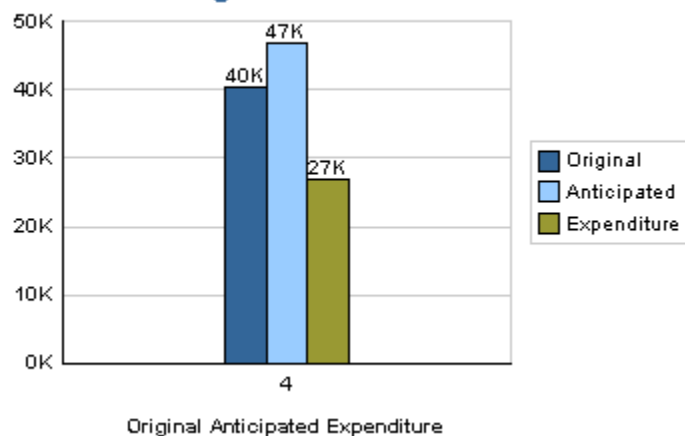

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COST 150 CRORS AND ABOVE

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	47	37689.79	45757.53	23129.48
2	Arunachal Pradesh	4	9512.22	17330.32	10080.26
3	Assam	41	24155.49	38425.08	25774.34
4	Bihar	46	32579.04	40999.96	28550.46
5	Chandigarh	1	452	452	160.72
6	Chhatisgarh	24	58278.32	59362.92	23326.44
7	Delhi	4	38190.88	38188.33	5783.55
8	Goa	1	335.61	335.61	249.31
9	Gujarat	33	38022.74	39925.38	14658.92
10	Haryana	9	4399.88	6113.07	7143.44
11	Himachal Pradesh	5	13845.21	19510.58	14371.77
12	Jammu and Kashmir	8	13694.69	32976.56	14889.37
13	Jharkhand	26	15873.15	20138.42	10008.17
14	Karnataka	38	54153.58	64689.41	27271.87
15	Kerala	11	22003.59	24528.37	7455.08
16	Madhya pradesh	21	31448.2	32674.58	9645.78
17	Maharashtra	55	96622.85	110361.29	51043.18
18	Manipur	1	727.56	7392.65	1716.34
19	Meghalaya	3	4845.02	4845.02	709.89
20	Mizoram	2	1532.97	3297.97	573.32
21	Multi State	175	182880.63	205727.01	84058.29
22	Nagaland	2	5124	6715.48	8.94
23	Odisha	31	56463.34	63174.09	41367.15
24	Punjab	5	1964.2	2039.2	2777.95
25	Rajasthan	25	25257.11	25682.57	11284.23
26	Sikkim	2	1648.94	3690.04	292.75
27	Tamil Nadu	42	53703.73	70043.62	44753.4
28	Tripura	5	2669.39	4112.35	2304.13
29	Uttar Pradesh	30	22596.01	27184.92	14844.85
30	Uttarakhand	6	7844.04	10199.28	2760.68
31	West Bengal	36	49877.43	61170.59	30200.23
TOTAL		739	908391.61	1087044.2	511194.29

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2003	3492	0	4309.83
2	IOR LAKWA - LAKHMANI (ONGCL)	Petroleum	09/2001	345.1	663.69	743.72
3	IOR GELEKI (ONGCL)	Petroleum	09/2001	390.09	1674.11	1759.52
4	PARBATI HEP (NHPC) II	Power	09/2002	3919.59	0	4121.24
5	KOLDAM HEP (NTPC)	Power	10/2002	4527.15	0	5165
6	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	0	6408.11
7	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	Power	12/2004	2496.9	0	2575.95
8	BARH STPP(3X660MW) NTPC	Power	12/2003	8692.97	0	8741
9	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	1061.38	0	1400.74
10	URI H.E.P STAGE -II (NHPC)	Power	08/2005	1729.29	1724.79	2077.51
11	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	631.17
12	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	Railways	03/1995	2500	2500	8822.5
13	LANJHIGARH- JUNAGARH NL(ECOR)	Railways	04/1993	100	142.98	231.61
14	CALICUT-MANGALORE (DL) (SR)	Railways	02/1996	240	0	599.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	Railways	02/1997	295	412.91	730.05
16	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL), (SWR)	Railways	04/1996	157	262.82	322.56
17	KARUR-SALEM(NL), SR	Railways	02/1997	155.55	155	759.11
18	NANDYAL-YERRAGUNTALA(NL), SCR	Railways	03/1996	155.74	429.49	668.35
19	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	Railways	09/1997	1000	1500	2895.33
20	KOTTUR-HARIHAR(NL), (SWR)	Railways	04/1995	65.94	302.23	358.07
21	RANCHI-LOHARDAGA(GC), SER	Railways	04/1997	194.07	194.07	350.33
22	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	Railways	04/1997	233	501.69	718.4
23	KATIHAR - JOGBANI (GC)(NEFR)	Railways	09/2001	100	492.98	741.46
24	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	04/1999	323.4	323.4	510.4
25	JALANDHAR-PATHANKOT-JAMMU-TAWI(LD), NR	Railways	03/2002	409	625.3	836.1
26	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	09/1995	100	100	551.56
27	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	Railways	04/2000	733	733	1483.63
28	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	03/2000	907.69	3156.32	3460.35

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	GADWAL - RAICHUR (NL), SCR	Railways	04/1998	92.63	228.09	281.61
30	JIND-SONEPAT (NL), NR	Railways	01/2004	190.81	238.56	485.23
31	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	727.53	1716.34
32	DANIAWAN-BIHARSARIF (NL), ECR	Railways	04/2001	104.79	0	132.2
33	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	01/2004	915.7	915.7	2291.38
34	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport And Highways	12/2003	157.47	0	240.4
35	HAPUR-GARHUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport And Highways	03/2005	220	0	284.2
36	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	Road Transport And Highways	12/2003	230	0	239.9
37	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	Road Transport And Highways	12/2003	166.27	0	198.6
38	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A	Road Transport And Highways	12/2003	284	0	327.6
39	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402	Road Transport And Highways	12/2003	240	0	295
40	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport And Highways	03/2005	190	0	264.6
41	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport And Highways	12/2003	280	0	324.6
42	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport And Highways	12/2003	195	0	252.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport And Highways	12/2003	237.8	0	289
44	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport And Highways	12/2003	332.94	0	475.5
45	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport And Highways	12/2003	275	0	280.4
46	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport And Highways	12/2003	251.03	0	338.4
47	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	08/2008	1942.51	0	2474.41
48	ADRIYALA SHAFT PROJECT	Coal	12/2009	212.34	779.26	805.16
49	EXPANSION OF IISCO STEEL PLANT	Steel	02/2008	14443	0	15038.24
50	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	01/2009	756	898	913.72
51	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	Petroleum	07/2009	238.68	0	293.12
52	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	04/2008	825	0	1462.08
53	Mounded Bullet Project at CPCL	Petroleum	12/2012	279	0	283.87
54	RAMPUR HEP(412 MW)	Power	01/2007	2047.03	0	2835.28
55	PARE HYDRO ELECTRIC PROJECT	Power	12/2008	573.99	0	731.69
56	TRIPURA GAS BASED POWER PROJECT	Power	07/2009	421.01	0	661.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	04/1996	114.01	332.92	444.28
58	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	09/2006	343.17	343.17	684.71
59	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	12/2006	170	170	412.82
60	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	09/1996	156	156	364.51
61	TAMLUK DIGHA, LINE DOUBLING (SER)	Railways	03/1984	293.97	0	449.48
62	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)	Railways	04/2007	482	482.7	521.29
63	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	1676.31	1676.31	3702.79
64	Rajkot-Veraval, Wansjalua to Jataisar with new MM for Shapur-Saradiya And Somnath-Kodinar (GC)	Railways	04/1994	320.66	0	461.38
65	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur	Railways	04/2013	456	0	557.82
66	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC)	Railways	04/2010	739.65	0	783.39
67	Sakri-Hasanpur Road (NL)	Railways	04/1999	175.69	0	232.39
68	Cuddalore-Salem via Vriddhachalam GC	Railways	04/1999	198.68	0	266.48
69	Chennai Beach-Tambaram-Chengalpattu Suburban GC	Railways	04/1999	271.24	0	458.96
70	Construction of NL from Kumarghat-Agartala	Railways	04/1999	895	0	944.72

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif	Railways	04/2007	247	0	525.75
72	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai	Railways	04/1999	523.17	0	1033
73	PANVEL PEN DOUBLING	Railways	04/2006	191	0	199.52
74	Kolar-Chickbalapur GC	Railways	04/2006	287.99	0	425.91
75	NALBARI TO BIJNI (AS-8)	Road Transport And Highways	12/2003	200	0	288.3
76	GUWHATI TO NALBARI (AS-4)	Road Transport And Highways	12/2003	175.96	0	217.6
77	NAGAON TO DHARAMTUL (AS-2)	Road Transport And Highways	12/2003	264.72	0	301.1
78	SONAPUR TO GUWAHTI (AS-3)	Road Transport And Highways	12/2003	245	0	491.2
79	GUWAHATI TO NALBARI (AS-5)	Road Transport And Highways	12/2003	198.16	0	276.2
80	NALBARI TO BIJNI (AS-6)	Road Transport And Highways	12/2003	225	0	266.1
81	NALBARI T BIJNI (AS-7)	Road Transport And Highways	12/2003	208	0	308.7
82	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	Road Transport And Highways	12/2003	160	0	207.7
83	DHARAMTUL TO SONAPUR (AS-19)	Road Transport And Highways	12/2003	200	0	253.9
84	NAGPUR-KONDHALI, NH-6(NHAI)	Road Transport And Highways	03/2005	168	0	457.3

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	THANJAUR-TRICHY, NH-67(NHAI)	Road Transport And Highways	03/2005	280	0	581.5
86	GANJAM-ICCHAPURUM, NH-5(NHAI)	Road Transport And Highways	04/2000	263.27	0	276.46
87	BRAHMPUTRA BRIDGE, NH NO-31	Road Transport And Highways	12/2003	217.61	0	297.9
88	JHANSI TO LALITPUR, NH-25,26	Road Transport And Highways	12/2003	355.06	0	507.4
89	TRICHY - KORUR NH-67	Road Transport And Highways	03/2005	516	0	860.7
90	SALEM - U / UNDRUPET(BOT - 1/TN-06) NH -68	Road Transport And Highways	03/2005	941	0	1901
91	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport And Highways	03/2005	557	0	1129
92	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport And Highways	12/2003	232.45	0	305.2
93	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport And Highways	04/2007	486	0	660.3
94	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport And Highways	03/2005	940	0	1325
95	Gujarat/Maharashtra Border Surat-Hazira Port Section	Road Transport And Highways	03/2010	1509.1	0	2123
96	Pune-sholapur, pkg1	Road Transport And Highways	11/2009	1110	0	1802
97	Kishangarh-Ajmer-Beawer	Road Transport And Highways	11/2009	795	0	1127
98	Chennai-Tada(Six lane)	Road Transport And Highways	04/2009	353.37	0	446.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport And Highways	04/2009	1673.7	0	2839
100	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport And Highways	02/2009	1693.75	0	2721
101	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport And Highways	05/2009	572.3	0	857.9
102	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport And Highways	05/2009	1108	0	3466
103	Jaipur-Tonk-Deoli	Road Transport And Highways	06/2010	792.06	0	1975
104	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport And Highways	09/2010	946	0	1790
105	Talegaon-amravati	Road Transport And Highways	11/2009	567	0	1166
106	Hazaribagh-Ranchi	Road Transport And Highways	08/2010	625.07	0	948
107	Armur to kadloor yellareddy	Road Transport And Highways	02/2010	390.56	0	772.4
108	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport And Highways	09/2010	671	0	938.4
109	AMRITSAR-PATHANKOT	Road Transport And Highways	05/2010	705	0	2144
110	PANIPAT-ROHTAK	Road Transport And Highways	04/2011	807	0	1318
111	DEVIHALLI-HASSAN	Road Transport And Highways	12/2010	453	0	718.7
112	MURADABAD-BAREILY	Road Transport And Highways	04/2010	1267	0	1876

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	BELGAUM-DHARWAD(NH-4)	Road Transport And Highways	12/2010	480	0	567.9
114	INDORE-DEWAS(NH-3)	Road Transport And Highways	11/2010	325	0	532.7
115	2 LANNING OF MOKAMA-MUNGER	Road Transport And Highways	05/2011	351.54	0	395.2
116	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport And Highways	12/2010	1008.5	0	1352
117	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	Road Transport And Highways	03/2011	785.5	0	843.9
118	ROHTAK-BAWAL	Road Transport And Highways	05/2011	650	0	1119
119	GHAZIABAD-ALIGARH NH-91	Road Transport And Highways	02/2011	1141	0	1287
120	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	Road Transport And Highways	09/2011	574	0	655.3
121	4-LANNING OF CHAPRA-HAJIPUR	Road Transport And Highways	01/2011	575	0	714.4
122	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport And Highways	05/2011	511.54	0	642.2
123	4-laning of Barhi-Hazaribagh	Road Transport And Highways	02/2012	398	0	441.1
124	BHUBANESWAR TO PURI	Road Transport And Highways	03/2011	500.29	0	509.4
125	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	Road Transport And Highways	11/2011	909	0	941.9
126	JAIPUR-REENGUS	Road Transport And Highways	08/2010	267.81	0	651.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	4-laning of Faraka-Raiganj	Road Transport And Highways	02/2011	1078.84	0	1328
128	4-laning of Brahampore-Faraka	Road Transport And Highways	02/2011	998.79	0	1266
129	Acquisition of Two nos. of 3060 DWT	Shipping And Ports	04/2009	277.03	280	294.87
130	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping And Ports	03/2007	245.67	298.17	371.18

List of Projects Ahead of Schedule w.r.t. Original Schedule

						(Oct,2013)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Power</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	119.62	06/2016 -	04/2015
2	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129	2/2012	3,201.44 -	3,201.44	1,032.40	10/2014 -	09/2014
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	398.06	12/2014 -	11/2014
	Total		6,645.53 -	6,645.53	1,550.08		
	<u>Shipping And Ports</u>						
4	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013
	Total		1,028.10 -	1,012.23	554.60		
	Grand Total		7,673.63	7,657.76	2,104.68		

List of projects without Original Date of Commissioning

(Oct,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Antici pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Petroleum</u>								
1	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	10,281.00	0.04	- -	04/2015	-	0/0
	Total		10,281.00 -	10,281.00	.04				0/0
	<u>Railways</u>								
2	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
3	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	364.51	- -	12/2013	-	0/0
4	PANVEL PEN DOUBLING - [N22000255]CR,Multi State	04/2006	191.00 -	191.00	199.52	- -	01/2014	-	0/0
5	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	631.17	- -	02/2014	-	0/0
6	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	233.72	- -	03/2014	-	0/0
7	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	744.71	510.40	- -	03/2014	-	0/1
8	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	268.34	- -	03/2014	-	0/0
9	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,Multi State	01/2004	915.70 915.70	3,019.17	2,291.38	- -	03/2014	-	0/0
10	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	147.94	- -	03/2014	-	0/0
11	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	247.75	150.67	- -	03/2014	-	0/0
12	PEN ROHA DOUBLING - [N22000254]CR,Multi State	04/2007	203.00 -	203.00	161.94	- -	03/2014	-	0/0
13	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	279.40	120.47	- -	04/2014	-	0/0
14	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.35	- -	03/2015	-	0/0
15	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
16	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	209.77	22.93	- -	03/2015	-	0/0
17	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	283.55	0.51	- -	03/2015	-	0/0
18	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	238.83	98.33	- -	03/2015	-	0/0
19	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12 -	312.12	30.77	- -	03/2015	-	0/0

(Oct,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
20	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, Assam	09/2006	200.00 200.00	385.20	144.47	- -	03/2016	-	0/0
21	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER, Jharkhand	04/2012	258.20 -	258.20	0.29	- -	03/2016	-	0/0
22	Running of 12 car trains on Harbour Line - [N22000214]MRTP, Maharashtra	04/2012	714.10 -	714.10	6.83	- 12/2017	12/2017	0(R3)	0/0
	Total		6,028.38 -	12,702.82	5,830.67				0/1
	<u>Road Transport And Highways</u>								
23	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00 -	946.00	1,790.00	- -	10/2013	-	3/3
24	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00 -	480.00	567.90	- -	10/2013	-	2/2
25	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00 -	453.00	718.70	- -	12/2013	-	1/1
26	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00 -	839.00	667.90	- -	12/2013	-	0/1
27	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00 -	671.00	938.40	- -	06/2014	-	2/3
	Total		3,389.00 -	3,389.00	4,682.90				8/10
	Grand Total		19,698.38	26,372.82	10,513.61				8/11

List of projects without Date of Commissioning

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Civil Aviation</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013
	Total		4,376.51 -		
	<u>Coal</u>				
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	-
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	03/2013 -	-
	Total		716.81 -		
	<u>Steel</u>				
6	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	08/2006	260.00 349.64	12/2009 08/2010	06/2013
	Total		260.00 -		
	<u>Petroleum</u>				
7	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	- -	03/2013
8	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013
9	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,Multi State	07/2009	238.68 -	01/2012 -	07/2013
10	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	- -	08/2013
11	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	08/2013
12	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	03/2007 03/2014	09/2013
13	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	09/2011 05/2012	09/2013
14	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	09/2012 -	09/2013
15	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	09/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	09/2012 -	-
17	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
18	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	07/2012 07/2012	-
19	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	12/2012 -	-
20	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu	05/2013	711.00 -	- -	-
	Total		16,862.37 -		
	<u>Power</u>				
21	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
22	MOUDA STTP - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	08/2012 -	03/2013
23	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	10/2012 -	03/2013
24	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	-
25	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		14,227.71 -		
	<u>Railways</u>				
26	Quilon-Tirunelveli - Trichendur, Tenkasi - [N22000303]SR,Tamil Nadu	04/1999	460.94 -	01/1999 -	01/1999
27	Jaggayyapet - Mellacheruvu - [N22000304]SCR,Andhra Pradesh	04/2007	313.24 -	01/1999 -	01/1999
28	MM from Buramara-Chakulia - [N22000305]SER,Multi State	04/2008	466.48 -	01/1999 -	01/1999
29	Marikuppam - Kuppam - [N22000308]SWR,Karnataka	04/2012	285.57 -	01/1999 -	01/1999
30	MM from Panskura-Ghatal NL - [N22000309]SER,West Bengal	04/2011	276.69 -	01/1999 -	01/1999
31	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
32	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
33	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
34	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
35	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
36	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
37	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011
38	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
39	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
40	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
41	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
42	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
43	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
44	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
45	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	03/2012
46	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS and PU - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
47	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
48	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
49	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
50	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
51	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013
53	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013
54	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013
55	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013
56	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013
57	KADUR-CHIKMAGALUR-SAKLLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013
58	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013
59	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
60	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013
61	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013
63	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013
64	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
65	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
66	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	- -	-
67	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-
68	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
69	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
70	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
71	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
72	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-
73	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-
74	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-
75	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-
76	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-
77	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-
78	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	- -	-
79	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	- -	-
80	Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State	04/2007	1,640.04 -	- -	-
81	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	- -	-
82	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	- -	-
83	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	- -	-
84	Rajkot-Veraval,Wansjalai to Jataisar with new MM for Shapur-Saradiya And Somnath-Kodinar (GC) - [N22000143]WR,Gujarat	04/1994	320.66 -	- -	-
85	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	- -	-
86	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	- -	-
88	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.93 -	- -	-
89	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	- -	-
90	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	- -	-
91	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittisgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	- -	-
92	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC) - [N22000153]NWR,Rajasthan	04/2010	739.65 -	- -	-
93	Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	- -	-
94	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	- -	-
95	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	- -	-
96	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	- -	-
97	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	- -	-
98	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	- -	-
99	Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	- -	-
100	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	- -	-
101	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	- -	-
102	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	- -	-
103	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	- -	-
104	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	- -	-
105	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	- -	-
106	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	- -	-
107	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	- -	-
108	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	- -	-
109	Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	- -	-
110	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	- -	-
111	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
112	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	- -	-
113	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	- -	-
114	Sakri-Nirmali and Jhanjharpur-Laukahabazar and Saharsa-Forbesganj (GC) - [N22000180]ECR,Bihar	04/2004	372.14 -	- -	-
115	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Nepal) GC - [N22000181]ECR,Bihar	04/2009	470.00 -	- -	-
116	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	- -	-
117	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	- -	-
118	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	- -	-
119	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	- -	-
120	Sriperumbudur-Guduvanchery with spur to Irungattukkottai-Avadi-Sriperumbudur - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	- -	-
121	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	- -	-
122	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	- -	-
123	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	- -	-
124	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	- -	-
125	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	- -	-
126	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	- -	-
127	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	- -	-
128	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	- -	-
129	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	- -	-
130	Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	- -	-
131	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	- -	-
132	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	- -	-
133	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	- -	-
134	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	- -	-
135	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	- -	-
136	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
137	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai - [N22000209]NEFR,Multi State	04/1999	523.17 -	- -	-
138	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam	04/2012	246.07 -	- -	-
139	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal	04/2009	573.78 -	- -	-
140	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Phase-II - [N22000213]MRTP,Andhra Pradesh	04/2012	632.68 -	04/2012 -	-
141	Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State	04/2011	601.43 -	- -	-
142	Lakshmikantapur-Namkhana subsequently MM for Namkhana-Chandranagar, Kakdwip-Budakhali and Chandranag - [N22000216]ER,Multi State	04/1999	406.99 -	- -	-
143	Sultanganj-Katuria via Asarganj, Tarapur And Belhar - [N22000217]ER,Multi State	04/2007	450.00 -	- -	-
144	Hansnabad-Hingalgaon New BG line - [N22000218]ER,Multi State	04/2010	172.03 -	- -	-
145	Pirpainti-Jasidih - [N22000219]ER,Multi State	04/2013	915.98 -	- -	-
146	Bandel-Boinchi 3rd line - [N22000221]ER,Multi State	04/2011	288.35 -	- -	-
147	Pirpainti-Bhagalpur - [N22000222]ER,Multi State	04/2011	261.38 -	- -	-
148	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State	04/2000	157.17 -	- -	-
149	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - Chapra new line and Naihati-Ranaghat 3 - [N22000224]ER,Multi State	04/2001	923.52 -	- -	-
150	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-Sainthia via Kandi NL - [N22000225]ER,Multi State	04/2005	595.91 -	- -	-
151	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-Duttaphulia new line - [N22000227]ER,Multi State	04/2010	174.56 -	- -	-
152	Sondalia-Champapukur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State	04/2010	277.28 -	- -	-
153	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh 4th line with MM Baruipara Furfura NL - [N22000229]ER,Multi State	04/2010	296.44 -	- -	-
154	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State	04/2010	157.94 -	- -	-
155	Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra	04/2008	697.00 -	- -	-
156	Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra	04/2011	277.70 -	- -	-
157	Bariarpur-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State	04/2007	450.55 -	- -	-
158	Tarakeshwar-Magra New BG line - [N22000235]ER,Multi State	04/2010	365.17 -	- -	-
159	Hansdiha-Godda NL - [N22000236]ER,Multi State	04/2011	267.09 -	- -	-
160	Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State	04/2011	193.44 -	- -	-
161	Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State	04/2011	175.80 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
162	New Alipur to Akra, MM for Budge Budge-Pujali NL, Pujali-Uluberia(Birshivpur) And Pujali-Bahrahat NL - [N22000240]ER,Multi State	04/2010	494.54 -	- -	-
163	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghatakpur NL - [N22000241]ER,Multi State	04/2000	297.47 -	- -	-
164	Chandpara-Bangaon doubling with extension to Chandbazar and new MM for Bongaon-Poramaheshtala & Chand - [N22000242]ER,Multi State	04/2003	337.96 -	- -	-
165	Magrahat-Diamond Harbour with MM Sangrampur-Krishnachandpur and Diamond Hatbour - Bahrahat-Kulpi NL - [N22000243]ER,Multi State	04/2009	493.96 -	- -	-
166	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	- -	-
167	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	- -	-
168	Santoshpur-Remount Road via Garden Reach- Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	- -	-
169	Howrah-Development of station including segregation of arrival/departure and other amenities - [N22000249]ER,Multi State	04/2011	166.89 -	- -	-
170	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	- -	-
171	Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka	04/2011	913.00 -	- -	-
172	Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka	04/2007	179.65 -	- -	-
173	Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka	04/2010	377.93 -	- -	-
174	Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh	04/2013	1,112.00 -	- -	-
175	Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh	04/2013	723.00 -	- -	-
176	Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State	04/2012	1,054.35 -	- -	-
177	Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State	04/2008	184.26 -	- -	-
178	Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh	04/2012	923.23 -	- -	-
179	Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh	04/2011	283.54 -	- -	-
180	Meerut-Muzafarnagar Patch DL - [N22000267]NR,Uttar Pradesh	04/2012	289.79 -	- -	-
181	Grade Separator at Dayabasti - [N22000269]NR,Delhi	04/1999	159.20 -	- -	-
182	Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareli - [N22000270]NR,Uttar Pradesh	04/2013	654.00 -	- -	-
183	Rohtak-Meham Hansi - [N22000272]NR,Haryana	04/2012	287.00 -	- -	-
184	Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh	04/2008	1,046.88 -	- -	-
185	Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State	04/2007	336.91 -	- -	-
186	Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka	04/2013	558.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
187	Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State	04/2013	296.00 -	- -	-
188	Shimoga-Harihar NL - [N22000278]SWR,Karnataka	04/2011	562.74 -	- -	-
189	Rayadurga-Tumkur NL - [N22000279]SWR,Multi State	04/2007	970.34 -	- -	-
190	White Field-Kolar NL - [N22000280]SWR,Karnataka	04/2011	341.05 -	- -	-
191	Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi	04/2012	295.68 -	- -	-
192	Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh	04/2013	829.00 -	- -	-
193	Mudkhed-Parbhani - [N22000283](SCR),Maharashtra	04/2011	390.60 -	- -	-
194	Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh	04/2012	153.00 -	- -	-
195	Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh	04/2011	1,313.48 -	- -	-
196	Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh	04/2010	337.49 -	- -	-
197	Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State	04/2008	2,050.00 -	- -	-
198	Haridwar-Laksar - [N22000289]NR,Uttarakhand	04/2012	219.83 -	- -	-
199	Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State	04/2008	165.65 -	- -	-
200	Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana	04/2013	400.00 -	- -	-
201	Yamunanagar-Chandigarh via Sadhaura Narayangarh - [N22000293]NR,Multi State	04/2013	876.00 -	- -	-
202	Unchahar-Amethi - [N22000294]NR,Uttar Pradesh	04/2012	380.00 -	- -	-
203	Qadian-Beas - [N22000295]NR,Punjab	04/2011	205.22 -	- -	-
204	Chandigarh-Baddi NL - [N22000296]NR,Multi State	04/2007	328.14 -	- -	-
205	Hospet-Hubli-Londa-Vascodagama DL - [N22000297]SWR,Karnataka	04/2010	2,127.00 -	- -	-
206	Gadag-Wadi NL - [N22000299]SWR,Karnataka	04/2013	1,117.00 -	- -	-
207	Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka	04/2013	327.25 -	- -	-
208	Monigram- Nimtita - [N22000301]ER,Multi State	04/2012	250.93 -	- -	-
209	Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal	04/2012	255.64 -	- -	-
210	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
211	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
213	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
214	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
215	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
216	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
217	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
218	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
219	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
220	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
221	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
222	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
223	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
224	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-
225	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
226	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
227	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
228	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
229	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
230	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-
231	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
232	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
233	Mansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur Mandi via Talwandi Saboo NL - [N22000268]NR,Punjab	04/2009	396.04 -	- -	-
234	Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State	04/2013	1,239.00 -	- -	-
235	Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State	04/2010	338.54 -	- -	-
	Total		96,086.48 -		

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Road Transport And Highways</u>				
236	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008
237	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013
238	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	- -	04/2013
239	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2013
240	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	09/2013
241	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013
	Total		3,380.10 -		
	<u>Shipping And Ports</u>				
242	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	- 01/2009	12/2010
243	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
244	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 11/2011	11/2011
245	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
246	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
247	Mechanization of coal handling facilities to 200000 DWT Vessels on DBFOT basis - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
248	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
249	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013
250	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013
251	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013
252	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUYPEEN COCHIN - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
253	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
254	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	-
	Total		11,119.97 -		
	<u>Telecommunications</u>				
255	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 Punjab - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
256	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013
257	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 12/2012	09/2013
258	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
259	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
	Total		2,724.30 -		
	<u>Urban Development</u>				
260	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	06/2011 -	03/2013
261	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>Water Resources</u>				
262	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		156,806.33		

List of on schedule Projects w.r.t. Original Schedule

(Oct,2013)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	160.72	03/2015 -	03/2015
2	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	160.74		
	<u>Coal</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	162.71	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	45.02	03/2014 -	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	74.32	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	52.12	03/2015 -	03/2015
8	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016
9	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	58.99	03/2016 -	03/2016
11	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.11	07/2016 -	07/2016
12	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	1.81	06/2015 -	06/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	53.45	03/2016 -	03/2016
14	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
15	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	14.03	03/2015 -	03/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	3.25	03/2015 -	03/2015
18	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.40	03/2020 -	03/2020
20	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	40.99	03/2014 -	03/2014

(Oct,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	90.05	03/2016 -	03/2016
22	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
23	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	48.56	03/2016 -	03/2016
24	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	152.13	03/2017 -	03/2017
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	582.00	03/2016 03/2016	03/2016
	Total		11,169.15 -	10,797.81	1,699.42		
	<u>Petroleum</u>						
26	Wax Project - [N16000101	6/2010	576.60 -	576.60	337.79	12/2013 -	12/2013
27	Marketing Terminal at Paradeep - [N16000168	7/2009	199.75 -	199.75	89.65	06/2014 -	06/2014
28	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165	4/2010	270.00 -	270.00	-	12/2014 -	12/2014
29	Reconstruction of BPA and BPB Platforms - [N16000161	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
30	Integrated Development of Bassein Field - [N16000160	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
31	Pipeline Replacement Project, Ahmedabad - [N16000159	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	48.71	10/2014 -	10/2014
33	Mounded Bullet Project at CPCL - [N16000154	12/2012	279.00 -	279.00	283.87	12/2014 -	12/2014
34	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149	8/2011	586.00 -	586.00	81.00	08/2015 -	08/2015
35	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	913.00	44.38	07/2015 -	07/2015
36	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
37	REWARI KANPUR PIPELINE PROJECT - [N16000145	2/2012	1,210.64 -	1,210.64	320.72	11/2015 -	11/2015
38	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	200.75	12/2014 -	12/2014
39	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	90.20	03/2014 -	03/2014
40	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	560.90	05/2014 -	05/2014
41	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	130.15	12/2014 -	12/2014
42	Construction of three ETPs, Mehsana - [N16000135	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
43	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014

(Oct,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	45.76	05/2014 -	05/2014
45	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	5,597.68	02/2014 -	02/2014
46	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,425.92	05/2015 -	05/2015
47	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,665.65	362.59	03/2015 -	03/2015
	Total		33,482.68 -	32,951.36	9,640.18		
	<u>Power</u>						
48	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	1,176.91	05/2014 -	05/2014
49	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	1,066.41	09/2014 -	09/2014
50	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,008.84	08/2014 -	08/2014
51	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	573.52	08/2014 -	08/2014
52	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	158.93	08/2014 -	08/2014
53	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	573.00	08/2015 -	08/2015
54	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,699.00	11/2016 -	11/2016
55	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,242.00	09/2016 -	09/2016
56	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	2,093.00	12/2016 -	12/2016
57	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	357.54	11/2014 -	11/2014
58	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	233.38	11/2014 -	11/2014
59	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	437.18	08/2014 -	08/2014
60	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	41.52	06/2014 -	06/2014
61	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	1,110.57	06/2015 -	06/2015
62	Gadarwara Super Thermal Power Project Stage-I - [N18000151]	2/2013	11,638.55 -	11,638.55	889.00	09/2017 -	09/2017
63	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	233.52	06/2015 -	06/2015
64	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	11.64	12/2015 -	12/2015

(Oct,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
65	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
66	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017
67	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,139.00	05/2017 -	05/2017
68	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
69	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	5.89	10/2014 -	10/2014
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	122.75	03/2015 -	03/2015
71	Eastern Region Strengthening Scheme-V - [N18000155]	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016
72	Inter-Regional System Strengthening Scheme in WR and NR (Part-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016
73	Transmission System associated with Mauda Stage-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
75	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
77	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	519.59	10/2014 -	10/2014
78	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	19.50	08/2014 -	08/2014
79	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	495.42	02/2015 -	02/2015
80	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	112.33	01/2014 -	01/2014
81	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	490.30	01/2015 -	01/2015
82	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	207.18	08/2014 -	08/2014
83	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	337.44	02/2014 -	02/2014
84	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	1,273.52	07/2014 -	07/2014
85	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	220.72	06/2014 -	06/2014
	Total		103,186.86 -	103,186.86	17,966.23		

(Oct,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Railways</u>						
86	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N20100325]	4/1998	183.23 -	818.29	105.60	02/2015 -	02/2015
87	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02 -	2,913.51	350.64	03/2016 -	03/2016
88	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113]	4/2008	653.19 -	653.47	237.99	03/2014 -	03/2014
89	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	699.00	03/2014 -	03/2014
90	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.71	02/2020 -	02/2020
91	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]	4/2010	423.66 -	423.66	136.58	03/2017 -	03/2017
92	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura Sharif NL - [N22000244]	4/2009	257.42 -	257.42	33.39	03/2014 -	03/2014
93	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]	4/2011	299.60 -	299.60	1.09	03/2017 -	03/2017
94	Plassey-Jiaganj Doubling - [N22000220]	4/2011	248.07 -	248.07	9.83	03/2015 -	03/2015
95	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]	4/2010	309.44 -	388.67	47.81	12/2015 -	12/2015
96	Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]	4/2010	622.41 -	2,030.50	1.22	02/2019 -	02/2019
97	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
98	Suratpura - Hanumangarh - Sriganaganagar Gauge Conversion (NWR) - [N22000114]	4/2008	516.23 -	516.23	435.49	03/2014 -	03/2014
99	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]	4/2008	829.74 -	829.74	38.33	03/2015 -	03/2015
100	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	230.80	03/2016 -	03/2016
	Total		18,354.28 -	23,440.94	2,329.48		
	<u>Road Transport And Highways</u>						
101	Talegaon-amravati - [N24000140]	11/2009	567.00 -	567.00	1,166.00	11/2013 -	11/2013
102	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,318.00	10/2014 -	10/2014
103	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
104	2 Laning of Muzaffarpur - Sonbarsa - [N24000174]	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
105	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	518.00	01/2014 -	01/2014
106	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	921.30	03/2014 -	03/2014
107	BARSAT-KRISHNANAGAR - [N24000229]	8/2012	867.00 -	867.00	-	02/2015 -	02/2015
108	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015

(Oct,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
109	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	236.80	09/2014 -	09/2014
110	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	691.40	10/2014 -	10/2014
111	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	490.60	09/2014 -	09/2014
112	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015
113	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	34.28	12/2015 -	12/2015
114	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	40.66	07/2014 -	07/2014
115	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	230.10	10/2014 -	10/2014
116	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	17.23	09/2015 -	09/2015
117	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
118	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	198.50	06/2014 -	06/2014
119	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	941.90	05/2014 -	05/2014
120	PUNE-SHOLAPUR,Pkg-II - [N24000193]	9/2011	835.00 -	835.00	388.20	01/2014 -	01/2014
121	4-laning of Barhi-Hazaribagh - [N24000191]	2/2012	398.00 -	398.00	441.10	02/2014 -	02/2014
122	2laning with PS Gopalganj-Chappra - [N24000190]	12/2011	325.00 -	325.00	161.20	05/2014 -	05/2014
123	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
124	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	642.20	11/2013 -	11/2013
125	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014
126	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	655.30	03/2014 -	03/2014
127	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,218.00	05/2014 -	05/2014
128	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	227.90	06/2015 -	06/2015
129	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	314.70	04/2014 -	04/2014
130	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
131	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	282.80	10/2014 -	10/2014
132	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	498.90	07/2014 -	07/2014
133	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	98.48	01/2014 -	01/2014

(Oct,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
134	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,048.00	09/2014 -	09/2014
135	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	202.40	06/2014 -	06/2014
136	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,388.00	06/2014 -	06/2014
137	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	189.10	02/2014 -	02/2014
138	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
139	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
140	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	1,119.00	11/2013 -	11/2013
	Total		37,139.74 -	37,139.74	16,491.58		
	<u>Shipping And Ports</u>						
141	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
	Total		966.46 -	994.82	363.20		
	<u>Steel</u>						
142	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	68.92	08/2014 -	08/2014
143	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	10.01	12/2014 -	12/2014
144	Rebuilding of Battery Block 5A and Re-construction of Battery Block 5B - [N12000080	3/2012	339.35 -	339.35	21.03	06/2015 -	06/2015
	Total		926.90 -	926.90	99.96		
	<u>Urban Development</u>						
145	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	5,302.74	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	5,302.74		
	Grand Total		241,137.67	245,350.03	54,053.53		

List of Delayed Projects w.r.t. Original and Revised Schedule

(Oct,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,746.00	12/2008 -	09/2014	69	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,309.83	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	3,478.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,379.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,912.83				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building(Goa) - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	249.31	05/2012 -	11/2013	18	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,Multi State	02/2010	344.28 -	344.28	-	03/2014 -	06/2014	3	-
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.71	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	989.35	481.02				
	<u>Coal</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,802.11	06/2009 -	03/2014	57	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.47	03/2010 -	03/2014	48	-
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	118.26	03/2011 -	03/2014	36	-
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 -	741.62	377.80	03/2013 -	03/2014	12	-
12	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	117.75	03/2012 -	03/2014	24	-
13	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,770.42	03/2012 -	05/2014	26	-
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	805.16	03/2013 09/2012	02/2015	23	29
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.98	03/2012 -	03/2015	36	-
16	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	113.59	03/2013 -	03/2015	24	-
17	BALRAM OCP EXTENSION,MCL 8.00 Mty - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	129.20	03/2010 -	03/2015	60	-
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	118.03	03/2013 -	03/2015	24	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	237.96	03/2012 -	03/2015	36	-
20	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.65	03/2012 -	03/2015	36	-
21	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.33	03/2013 -	03/2015	24	-
22	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,575.95	03/2014 -	03/2016	24	-
23	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,275.84	03/2014 -	03/2016	24	-
24	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	27.60	07/2012 -	03/2016	44	-
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	268.23	03/2014 -	03/2016	24	-
26	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	92.14	12/2012 -	03/2016	39	-
27	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	20.33	03/2014 -	03/2016	24	-
28	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.28	03/2014 -	03/2016	24	-
29	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
30	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	210.11	03/2014 -	03/2016	24	-
31	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
32	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	138.45	03/2012 -	03/2016	48	-
33	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72	-
34	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
35	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	61.20	03/2012 -	03/2017	60	-
36	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	34.92	12/2015 -	04/2018	28	-
37	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	739.17	03/2013 -	03/2023	120	-
	Total		26,241.09 -	29,697.88	14,321.79				
	<u>Steel</u>								
38	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,Andhra Pradesh	07/2007	202.00 343.58	343.58	281.05	01/2010 02/2011	11/2013	46	33
39	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	06/2006	108.00 216.68	216.68	153.79	09/2008 12/2013	12/2013	63	0
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	15,038.24	12/2011 -	12/2013	24	-
41	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	07/2007	480.00 -	450.00	288.01	09/2009 05/2012	12/2013	51	19

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,779.97	12/2011 -	12/2013	24	-
43	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	10,157.19	03/2013 -	12/2013	9	-
44	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,603.02	10/2009 10/2012	03/2014	53	17
45	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	356.75	12/2011 03/2012	03/2014	27	24
46	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	338.09	04/2013 12/2013	03/2014	11	3
47	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	229.26	05/2013 03/2014	03/2014	10	0
48	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,841.57	12/2012 -	03/2014	15	-
49	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	95.71	10/2013 -	06/2014	8	-
50	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	10,590.79	03/2013 -	09/2014	18	-
51	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	83.02	11/2013 -	06/2015	19	-
	Total		64,410.32 -	70,505.86	53,836.46				
	<u>Petrochemicals</u>								
52	Assam gas Cracker project - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	4,510.51				
	<u>Petroleum</u>								
53	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,759.52	03/2007 03/2017	10/2013	79	-41
54	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	794.14	12/2011 -	11/2013	23	-
55	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,462.08	04/2013 -	11/2013	7	-
56	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93	9
57	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	731.38	03/2010 03/2012	12/2013	45	21
58	VKPL UPGRADEATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	265.22	03/2012 -	12/2013	21	-
59	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	716.68	01/2013 -	12/2013	11	-
60	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	755.59	07/2012 -	12/2013	17	-
61	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,813.90	01/2012 -	12/2013	23	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	234.31	03/2013 -	12/2013	9	-
63	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	276.83	242.63	04/2012 -	12/2013	20	-
64	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20	-
65	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26	-
66	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	133.48	06/2012 -	12/2013	18	-
67	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
68	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	228.27	11/2012 -	02/2014	15	-
69	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
70	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
71	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
72	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	03/2014	18	-
73	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2014	12	0
74	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	202.37	08/2012 -	03/2014	19	-
75	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	98.72	09/2012 -	03/2014	18	-
76	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	52.67	06/2012 -	03/2014	21	-
77	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	104.65	08/2013 -	03/2014	7	-
78	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	59.74	06/2012 -	03/2014	21	-
79	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,137.44	08/2010 03/2012	05/2014	45	26
80	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
81	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	20.03	03/2014 -	05/2014	2	-
82	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	310.49	05/2013 06/2014	06/2014	13	0
83	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	912.81	10/2011 -	06/2014	32	-
84	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	23,613.00	11/2012 -	07/2014	20	-
85	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20	0
86	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	445.86	09/2011 -	12/2014	39	-
88	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
89	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3	-
90	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	729.75	10/2011 -	10/2015	48	-
91	Strategic Crude oil storage project at Padur - [N16000169]ISPRL,Kerala	01/2006	993.00 1,693.00	1,693.00	998.65	01/2012 -	10/2015	45	-
92	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
93	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35	-
94	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	983.55	01/2014 -	12/2015	23	-
95	Integrated Refinery Expansion Project - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	760.92	12/2015 -	05/2016	5	-
96	Construction of one Multipurpose Support Vessel (MSV) - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
97	Creation of Secondary Tank farm with dehydration facility and ETP at Madhuban - [N16000167]OIL,Multi State	08/2006	374.56 -	374.56	10.46	09/2012 -	10/2016	49	-
98	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24	-
99	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24	-
100	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23	-
	Total		124,333.98 -	141,670.95	81,101.11				
	Power								
101	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 1,724.79	2,081.00	2,077.51	11/2009 02/2013	10/2013	47	8
102	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,544.00	10/2012 -	10/2013	12	-
103	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	160.94	06/2012 -	11/2013	17	-
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	385.35	11/2011 -	12/2013	25	-
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.83	02/2012 -	12/2013	22	-
106	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	159.62	11/2011 -	12/2013	25	-
107	765KV System for Central part of Northern Region Grid - Part-III - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	851.42	05/2012 -	12/2013	19	-
108	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	140.34	07/2013 -	12/2013	5	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	136.78	01/2013 -	01/2014	12	-
110	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,212.33	10/2010 01/2013	03/2014	41	14
111	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	885.97	10/2009 -	03/2014	53	-
112	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,835.28	01/2012 -	03/2014	26	-
113	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,Multi State	08/2008	2,360.95 2,580.90	2,580.90	2,076.70	08/2012 -	03/2014	19	-
114	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	6,023.11	08/2012 -	03/2014	19	-
115	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	613.65	11/2012 -	03/2014	16	-
116	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,351.27	08/2013 -	03/2014	7	-
117	Northern region system strengthening scheme XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	331.59	07/2013 -	03/2014	8	-
118	Supplementary transmission associated with vellur TPS - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	101.95	04/2013 -	03/2014	11	-
119	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	829.27	12/2013 -	03/2014	3	-
120	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	339.20	10/2013 -	03/2014	5	-
121	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	661.40	07/2013 -	05/2014	10	-
122	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,289.89	03/2013 -	05/2014	14	-
123	Transmission system for phase-I generation projects in orissa-part B - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,780.54	12/2013 -	05/2014	5	-
124	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,998.00	03/2014 -	05/2014	2	-
125	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	1,083.83	12/2013 -	05/2014	5	-
126	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,569.95	10/2012 -	06/2014	20	-
127	Trans. System associated with PALLATANA GBPP & BPTS. - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,452.60	12/2012 -	06/2014	18	-
128	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	912.05	08/2012 -	06/2014	22	-
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	364.17	11/2011 -	07/2014	32	-
130	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,165.00	04/2009 -	09/2014	65	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
131	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	1,117.92	731.69	08/2013 -	09/2014	13	-
132	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,477.00	08/2013 -	09/2014	13	-
133	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	193.36	11/2013 -	09/2014	10	-
134	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,400.74	09/2009 06/2013	12/2014	63	18
135	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	473.70	07/2006 -	02/2015	103	-
136	Transmission System of Vinhuachal -IV And Rihand -III Gen. Proj. - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,752.49	11/2012 -	03/2015	28	-
137	Northern region system strengthening scheme-XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	909.52	04/2013 -	03/2015	23	-
138	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.70	01/2013 -	03/2015	26	-
139	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	1,086.62	11/2013 -	03/2015	16	-
140	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	737.73	11/2012 -	03/2015	28	-
141	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	51.97	04/2015 -	05/2015	1	-
142	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,969.63	08/2013 -	06/2015	22	-
143	Transm System for development of Pooling strn. in NR part of West Bengal And Transfer of power from B - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	393.77	01/2015 -	12/2015	11	-
144	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	4,092.00	07/2011 -	06/2016	59	-
145	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,817.16	01/2016 01/2016	11/2016	10	10
146	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	534.61	07/2010 02/2016	02/2017	79	12
147	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,575.95	12/2009 05/2013	03/2017	87	46
148	BARH STPP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,741.00	12/2009 -	03/2017	87	-
149	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	3,846.30	1,914.00	03/2013 -	03/2017	48	-
150	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	368.16	07/2014 -	09/2017	38	-
151	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,408.11	09/2010 08/2014	03/2018	90	43
152	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	4,121.24	09/2009 07/2014	07/2018	106	48
	Total		124,434.79 -	141,808.75	98,413.69				

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Railways</u>								
153	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	231.61	03/2002 -	10/2013	139	-
154	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	130.62	12/2011 11/2013	11/2013	23	0
155	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER) - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	179.63	12/2012 -	12/2013	12	-
156	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	287.99	425.91	01/1999 -	12/2013	179	-
157	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	576.81	03/1994 -	01/2014	238	-
158	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	390.29	12/2009 03/2011	01/2014	49	34
159	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
160	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	521.29	03/2013 -	03/2014	12	-
161	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	148.38	02/2006 -	06/2014	100	-
162	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	171.02	104.84	06/2013 -	06/2014	12	-
163	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66	66
164	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65	65
165	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	120.00 245.39	245.39	222.71	12/2008 -	09/2014	69	-
166	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	324.96	03/2004 12/2010	12/2014	129	48
167	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.90	350.33	06/2004 -	12/2014	126	-
168	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,177.39	03/2009 12/2012	12/2014	69	24
169	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	255.39	06/2013 06/2013	12/2014	18	18
170	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
171	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	178.76	03/2007 03/2007	03/2015	96	96
172	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,022.64	741.46	12/2010 12/2010	03/2015	51	51
173	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,483.63	12/2008 -	03/2015	75	-
174	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	218.36	126.65	12/2012 -	03/2015	27	-
175	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,702.79	03/2009 -	03/2015	72	-
176	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,242.25	944.72	03/2007 -	03/2015	96	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
177	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,903.68	10/2007 12/2012	12/2015	98	36
178	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69	-
179	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	495.64	03/2014 -	12/2015	21	-
180	Champurajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	177.38	42.98	03/2015 -	12/2015	9	-
181	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]RVNL,West Bengal	04/2010	2,298.42 -	2,298.42	59.82	03/2014 -	03/2016	24	-
182	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	1,074.47	449.48	06/2005 07/2011	06/2016	132	59
183	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbender (MTP) - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	57.27	03/2016 -	06/2016	3	-
184	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.19	2,895.33	04/2008 03/2014	12/2016	104	33
185	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,039.29	1,423.98	484.15	03/2005 12/2008	12/2016	141	96
186	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,401.09	03/2014 03/2016	12/2016	33	9
187	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	7,392.65	1,716.34	03/2011 03/2014	03/2017	72	36
188	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	1,116.53	237.72	03/2010 03/2017	03/2017	84	0
189	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	99.62	04/2014 -	03/2017	35	-
190	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	61.04	12/2015 -	03/2017	15	-
191	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24	-
192	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
	Total		28,693.34 -	81,558.98	31,697.50				
	<u>Road Transport And Highways</u>								
193	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	204.82	08/2004 07/2010	10/2013	110	39
194	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	196.57	08/2004 -	10/2013	110	-
195	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	288.40	06/2011 06/2011	10/2013	28	28
196	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	660.30	05/2010 -	10/2013	41	-
197	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17	-
198	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	948.00	01/2013 -	10/2013	9	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
199	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.90	02/2013 -	10/2013	8	-
200	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9	-
201	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	162.71	04/2004 -	11/2013	115	-
202	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74	-
203	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	11/2013	117	-
204	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	327.60	05/2008 -	12/2013	67	-
205	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	295.00	10/2008 -	12/2013	62	-
206	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.60	01/2009 -	12/2013	59	-
207	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	475.50	09/2008 -	12/2013	63	-
208	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	280.40	10/2008 -	12/2013	62	-
209	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	288.30	06/2008 -	12/2013	66	-
210	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	266.10	06/2008 -	12/2013	66	-
211	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	207.70	05/2008 -	12/2013	67	-
212	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42	-
213	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.40	09/2009 -	12/2013	51	-
214	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	12/2013	35	-
215	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,325.00	07/2012 -	12/2013	17	-
216	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
217	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,123.00	09/2012 -	12/2013	15	-
218	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	12/2013	19	-
219	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26	-
220	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,721.00	08/2011 -	12/2013	28	-
221	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	12/2013	25	-
222	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8	-
223	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	839.20	03/2013 -	12/2013	9	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
224	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	12/2013	7	-
225	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,144.00	11/2012 -	12/2013	13	-
226	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	582.90	07/2013 -	12/2013	5	-
227	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,352.00	06/2013 -	12/2013	6	-
228	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	843.90	08/2013 -	12/2013	4	-
229	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
230	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	119.10	05/2013 -	12/2013	7	-
231	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	725.40	03/2013 -	12/2013	9	-
232	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.40	07/2013 -	12/2013	5	-
233	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	509.40	08/2013 -	12/2013	4	-
234	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	651.60	02/2013 -	12/2013	10	-
235	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,975.00	12/2012 -	02/2014	14	-
236	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	532.70	05/2013 -	02/2014	9	-
237	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	240.40	09/2007 -	03/2014	78	-
238	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	144.30	09/2008 -	03/2014	66	-
239	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	239.90	06/2005 -	03/2014	105	-
240	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	252.60	06/2008 -	03/2014	69	-
241	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	289.00	06/2008 -	03/2014	69	-
242	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	338.40	10/2008 -	03/2014	65	-
243	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	217.60	04/2008 -	03/2014	71	-
244	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	301.10	06/2008 -	03/2014	69	-
245	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	03/2014	72	-
246	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	276.20	04/2008 -	03/2014	71	-
247	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	253.90	06/2008 -	03/2014	69	-
248	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
249	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	240.70	09/2007 -	03/2014	78	-
250	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	860.70	07/2010 -	03/2014	44	-
251	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	446.20	10/2011 -	03/2014	29	-
252	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	54.59	11/2012 -	03/2014	16	-
253	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,876.00	06/2013 -	03/2014	9	-
254	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	395.20	05/2013 -	03/2014	10	-
255	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	515.80	03/2013 -	03/2014	12	-
256	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	281.10	10/2013 -	03/2014	5	-
257	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	70.00	09/2007 -	04/2014	79	-
258	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,201.00	03/2013 -	04/2014	13	-
259	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	564.60	02/2014 -	04/2014	2	-
260	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	324.60	02/2009 03/2014	05/2014	63	2
261	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	308.70	04/2008 -	05/2014	73	-
262	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	158.70	07/2009 -	05/2014	58	-
263	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.80	10/2008 -	06/2014	68	-
264	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	125.00	11/2008 -	06/2014	67	-
265	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	857.90	10/2011 -	06/2014	32	-
266	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
267	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,287.00	08/2013 -	06/2014	10	-
268	Kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	672.60	07/2013 -	06/2014	11	-
269	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.39	09/2013 -	07/2014	10	-
270	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	257.00	07/2012 -	07/2014	24	-
271	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	305.20	09/2010 -	08/2014	47	-
272	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	09/2014	63	-
273	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	235.20	09/2009 -	09/2014	60	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
274	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	93.63	04/2009 -	12/2014	68	-
275	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	72.60	11/2008 -	12/2014	73	-
276	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	169.00	04/2009 -	12/2014	68	-
277	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	297.90	04/2010 -	12/2014	56	-
278	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60	-
279	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	1,129.00	02/2010 -	12/2014	58	-
280	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
281	BAREILY-SITAPUR - [N24000200]NHAI, Uttar Pradesh	03/2011	1,046.00 -	1,046.00	357.00	09/2013 -	12/2014	15	-
282	4-laning of Faraka-Raiganj - [N24000202]NHAI, Multi State	02/2011	1,078.84 -	1,078.84	1,328.00	08/2013 -	12/2014	16	-
283	4-laning of Brahmapore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79 -	998.79	1,266.00	08/2013 -	12/2014	16	-
284	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177]NHAI, Tamil Nadu	09/2011	485.00 -	485.00	318.00	08/2013 -	02/2015	18	-
285	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION (KM 240-270KM) - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31	-
286	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65	-
287	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76 -	2,498.76	1,734.00	08/2014 -	07/2015	11	-
288	PANIKHOLI-RIMOLI - [N24000197]NHAI, Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13	-
289	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, Kerala	04/2011	682.00 -	682.00	160.00	10/2013 -	11/2015	25	-
290	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43 -	580.43	299.60	08/2013 -	12/2015	28	-
291	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
292	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	973.60	07/2015 -	06/2016	11	-
	Total		61,055.38 -	62,967.17	60,926.36				
	<u>Shipping And Ports</u>								
293	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]SHIPP., Maharashtra	08/2010	612.72 532.83	532.83	448.43	12/2012 11/2013	11/2013	11	0
294	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 12/2013	12/2013	93	0

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
295	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
296	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,429.10	978.39	12/2010 09/2012	03/2015	51	30
	Total		2,502.59 -	3,073.80	1,673.34				
	<u>Telecommunications</u>								
297	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	84.39	06/2009 -	12/2013	54	-
298	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
299	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
300	Supply Installation testing and commissioning of Rural Wimax network Phase-II - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	237.44	05/2011 -	12/2013	31	-
	Total		2,018.15 -	1,843.90	515.46				
	<u>Urban Development</u>								
301	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	431.52	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	431.52				
	Grand Total		483,075.60	592,256.64	374,821.59				

List of ongoing projects having cost overrun w.r.t. to original schedule

(Oct,2013)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	09/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	05/2011 -	03/2013	19.69
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
	Total		3,750.51 -	27,287.00			
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	03/2014	49.09
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	03/2013 -	02/2015	360.36
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	03/2012 -	05/2014	33.36
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		8,579.45 -	39,549.64			
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	12/2013	63.35
	Total		5,460.61 -	48,469.64			
	<u>Petroleum</u>						

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	750.00	03/2007 -	09/2013	117.33
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	03/2007 -	10/2013	329.16
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	03/2006 -	12/2013	285.29
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	04/2006 -	02/2014	536.46
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40
20	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27
21	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057	01/2009	756.00 -	898.00	- -	08/2013	18.78
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	07/2014	9.85
23	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066	01/2008	224.00 -	394.00	- -	03/2013	75.89
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	04/2013 -	11/2013	121.45
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76
27	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29
28	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
29	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
30	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	12/2013	12.16
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	10/2014 -	10/2014	0.00
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	06/2014	54.46
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
35	Strategic Crude oil storage project at Padur - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
36	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	12/2013	41.85
37	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44
	Total		59,168.86 -	128,830.62			
	<u>Power</u>						
38	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
39	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69
40	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	03/2018	69.71
41	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	12/2009 06/2016	03/2017	105.82
42	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
43	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	12/2014	41.49
44	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
45	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85
46	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	10/2013	20.34
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
48	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
49	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
50	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69
51	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	09/2017	50.31
52	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	08/2013 -	09/2014	94.76
53	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
54	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32
55	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	07/2013 -	05/2014	48.08
	Total		51,573.87 -	199,120.55			

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Railways</u>						
56	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	03/1994 -	01/2014	265.83
57	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
58	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
59	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
60	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
61	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
62	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
63	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	10/2013	127.94
64	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
65	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
66	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58
67	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
68	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
69	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	412.91	- -	01/2013	39.97
70	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	- -	03/2014	170.07
71	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
72	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
73	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	03/2012 -	03/2013	112.42
74	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
75	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
76	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
77	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
78	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2016	399.62

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
79	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2012	195.55
80	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01
81	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	- -	12/2012	358.34
82	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57
83	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
84	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05
85	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
86	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
87	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	01/2014	300.67
88	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64
89	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
90	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
91	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) - [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47
92	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28
93	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	- -	-	108.19
94	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
95	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
96	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.92	- -	03/2013	267.83
97	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73
98	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,350.00	12/2008 -	03/2015	220.60
99	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
100	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
101	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
102	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92
103	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	- -	-	553.35
104	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
105	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	724.00	03/2012 -	12/2012	279.44
106	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	03/2014	461.44
107	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
108	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
109	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	7,392.65	03/2011 -	03/2017	916.09
110	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	- -	-	62.83
111	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
112	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04
113	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
114	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
115	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
116	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
117	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2014	229.71
118	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
119	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49
120	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
121	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
122	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
123	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53
124	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
125	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
126	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
127	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	186.92 -	261.70	02/2006 -	06/2014	40.01
128	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
129	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS and PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
130	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
131	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
132	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
133	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
134	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
135	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	435.87	03/2011 -	03/2011	156.39
136	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	406.40	- -	12/2013	160.51
137	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
138	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
139	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	385.20	- -	03/2016	92.60
140	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
141	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
142	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
143	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36
144	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
145	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50
146	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	12/2015	114.06
147	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,384.34	04/2014 -	03/2017	284.98
148	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
149	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	12/2015 -	03/2017	152.38
150	Ramanagram-Mysore doubling with electrification of Kengesii-Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15
151	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51	03/2016 -	03/2016	11.24
152	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
153	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
154	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
155	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74	12/2010 -	12/2010	30.16
156	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
157	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	1,215.30	03/2013 -	03/2013	208.34
158	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]	04/2008	318.24 -	485.65	03/2012 -	-	52.61
159	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	04/2006	850.00 -	2,441.48	03/2015 -	03/2017	187.23
160	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
161	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	5,000.00	03/2009 -	03/2015	198.27
162	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	- -	-	24.15
163	Rajkot-Veraval,Wansjalila to Jataisar with new MM for Shapur-Saradiya And Somnath-Kodinar (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
164	Virangam-Samakhiali (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
165	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
166	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66
167	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
168	Ajmer-Bangurgram - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
169	Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
170	Digha-Jaleswar including MM for Digha-Egra - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
171	Champajharan-Bimalgarh Doubling extension - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
172	Tamluk-Basulya-Sutahata Doubling - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	12/2015	25.60
174	Sakri-Hasanpur Road (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
175	Chhapra-Muzaffarpur (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
176	Attippattu-Puttur - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
177	Chennai-Cuddalore via Mamallapuram - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
178	Cuddalore-Salem via Vriddhachalam GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
179	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
180	Villupuram-Dindigul with Electrification - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
181	Kuruppanthara-Chingavanam - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
182	New BG line from Dudhnoi-Mendipatar - [N22000192]	04/1999	175.43 -	247.75	- -	03/2014	41.22
183	Construction of NL from Kumarghat-Agartala - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2015	38.80
184	Erode-Palani - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
185	Madurai-Bodinayakanur - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
186	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
187	Chengannur-Chingavanam - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
188	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai - [N22000209]	04/1999	523.17 -	1,393.44	- -	-	166.35
189	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Phase-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	-	29.06
190	Madurai-Tuticorin via Aruppukkottai - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
191	Wardha-Nanded Maharashtra - [N22000231]	04/2008	697.00 -	1,604.00	- -	-	130.13
192	Kalyan-Kasara 3rd line - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
193	3rd line between Bhusawal-Jalgaon - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
194	Munirabad (gingera) -Raichur NL - [N22000257]	04/2007	179.65 -	645.00	- -	-	259.03
195	Bagalkot-Kudachi NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
196	Akola-Khandwa GC Akola-Akot - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
197	Bhanupali-Bilaspur Beri NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
198	White Field-Kolar NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
199	Haridwar-Laksar - [N22000289]	04/2012	219.83 -	444.18	- -	-	102.06
200	Quilon-Tirunelveli - Trichendur, Tenkasi - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
	Total		62,493.95 -	376,953.48			
	<u>Road Transport And Highways</u>						
201	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	04/2004 -	11/2013	7.35
202	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2014	30.10
203	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	03/2008 -	02/2008	16.14
204	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00	05/2008 -	12/2013	26.41
205	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75
206	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68
207	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	04/2014	82.12
208	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	05/2014	85.58
209	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2015	2.29
210	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	03/2014	33.70
211	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2013	106.50
	Total		3,324.28 -	382,398.68			
	<u>Shipping And Ports</u>						
212	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003]	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
213	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
214	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	1,429.10	12/2010 -	03/2015	16.38

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
215	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2013	300.00
216	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
217	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
218	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
219	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	02/2014	2.93
220	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	393,586.28			
	<u>Steel</u>						
221	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2014	41.41
222	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	03/2014	105.20
223	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	12/2013	100.63
224	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	12/2011 -	12/2013	13.61
225	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09
226	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	08/2006	260.00 -	349.64	12/2009 -	06/2013	34.48
	Total		24,000.89 -	423,802.35			
	<u>Telecommunications</u>						
227	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	12/2013	6.42
228	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
229	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	425,283.80			
	<u>Urban Development</u>						
230	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53

(Oct,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
231	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	437,065.88			
	<u>Water Resources</u>						
232	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	438,252.88			
	Grand Total		252,090.45	3,343,547.80			

List of ongoing projects having time and cost overrun w.r.t original schedule

(Oct,2013)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>Atomic Energy</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	09/2014	31.12	69
	Total		16,663.00 -	22,947.00				
	<u>Coal</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	03/2013 -	02/2015	360.36	23
4	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	03/2014	49.09	57
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	03/2012 -	05/2014	33.36	26
	Total		7,938.86 -	34,520.95				
	<u>Petrochemicals</u>							
8	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	12/2013	63.35	20
	Total		5,460.61 -	43,440.95				
	<u>Petroleum</u>							
9	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	438.85	03/2006 -	12/2013	285.29	93
10	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44	21
11	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	12/2013	41.85	18
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	12/2013	12.16	20
13	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	03/2007 -	10/2013	329.16	79
14	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	04/2006 -	02/2014	536.46	94
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	06/2014	54.46	32

(Oct,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
17	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081]	04/2008	825.00 -	1,827.00	04/2013 -	11/2013	121.45	7
18	Strategic Crude oil storage project at Padur - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
19	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76	23
20	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63
21	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50	63
22	Development of Cluster-7 Fields - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
23	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40	45
24	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27	46
25	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	07/2014	9.85	20
	Total		54,334.86 -	117,453.82				
	<u>Power</u>							
26	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	07/2013 -	05/2014	48.08	10
27	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	08/2013 -	09/2014	94.76	13
28	TEESTA LOW DAM HEP, STAGE-IV (NHPC) [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	12/2014	41.49	63
29	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79
30	URI H.E.P STAGE -II (NHPC) [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	10/2013	20.34	47
31	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69	10
32	PARBATI H.E.P. STAGE -III (NHPC) [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85	41
33	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32	19
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	09/2017	50.31	38
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) [180100239]	12/2004	2,496.90 -	5,139.00	12/2009 06/2016	03/2017	105.82	87
36	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14	48

(Oct,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
37	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106
38	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69	65
39	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	03/2018	69.71	90
40	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87
	Total		43,738.85 -	178,566.63				
	<u>Railways</u>							
41	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01	96
42	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 119.29	227.94	03/2002 -	10/2013	127.94	139
43	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64	51
44	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	01/2014	300.67	49
45	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141
46	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49	69
47	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65
48	Tamluk-Basulya-Sutahata Doubling - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38	12
49	Champajharan-Bimalgarh Doubling extension - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33	9
50	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	580.83	03/1994 -	01/2014	265.83	238
51	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66
52	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03	24
53	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	186.92 -	261.70	02/2006 -	06/2014	40.01	100
54	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65	23
55	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57	126
56	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50	132
57	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58	129

(Oct,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
59	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15	12
60	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
61	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,384.34	04/2014 -	03/2017	284.98	35
62	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
63	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
64	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	7,392.65	03/2011 -	03/2017	916.09	72
65	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,350.00	12/2008 -	03/2015	220.60	75
66	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,741.00	03/2014 -	12/2015	114.06	21
67	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124	04/2006	850.00 -	2,441.48	03/2015 -	03/2017	187.23	24
68	Construction of NL from Kumarghat-Agartala - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2015	38.80	96
69	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2016	399.62	104
71	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	3,380.58	12/2015 -	03/2017	152.38	15
72	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	5,000.00	03/2009 -	03/2015	198.27	72
73	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
74	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36	33
	Total		22,778.05 -	254,219.86				
	<u>Road Transport And Highways</u>							
75	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	03/2014	30.10	66
76	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68	67
77	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	05/2014	85.58	58
78	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75	68
79	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2014	82.12	79

(Oct,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
80	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	04/2004 -	11/2013	7.35	115
81	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	07/2015	2.29	65
82	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	05/2008 -	12/2013	26.41	67
83	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	03/2014	33.70	78
84	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2013	106.50	25
	Total		3,158.01 -	259,471.96				
	<u>Shipping And Ports</u>							
85	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2013	300.00	93
86	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,429.10	12/2010 -	03/2015	16.38	51
	Total		1,378.00 -	261,501.06				
	<u>Steel</u>							
87	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	12/2013	100.63	63
88	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09	46
89	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	03/2014	105.20	27
90	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2014	41.41	53
91	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00	12/2011 -	12/2013	13.61	24
	Total		23,740.89 -	291,367.49				
	<u>Telecommunications</u>							
92	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	06/2009 -	12/2013	6.42	54
	Total		149.15 -	291,526.21				
	Grand Total		179,340.28	1,755,015.93				

List of Projects without Milestones w.r.t. Original Schedule

				(Oct,2013)		
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Civil Aviation</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013	0/0
4	Construction of New International Terminal Building(Goa) - [N04000069]AAI,Goa	05/2010	335.61	05/2012	11/2013	0/0
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,Multi State	02/2010	344.28	03/2014	06/2014	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011 04/2013	03/2015	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,Chandigarh	02/2011	452.00	03/2015	03/2015	0/0
8	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60	03/2015	03/2015	0/0
	Total		6,035.46			0/0
	<u>Coal</u>					
9	Muraidih UG Turn-key Project - [N06000096]BCCL,Jharkhand	02/2011	339.88	04/2014	04/2014	0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27	04/2015	04/2015	0/0
	Total		1,570.15			0/0
	<u>Steel</u>					
11	Rebuilding of Battery Block 5A and Re-construction of Battery Block 5B - [N12000080]SAIL,West Bengal	03/2012	339.35	06/2015	06/2015	0/0
	Total		339.35			0/0
	<u>Petroleum</u>					
12	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline - [N16000153]BPCL,Rajasthan	04/2011	152.89	06/2013	06/2013	0/0
13	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	03/2010 03/2012	12/2013	0/0
14	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	12/2013	12/2013	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	04/2012 -	12/2013	0/0
16	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	12/2013	0/0
17	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	06/2012 -	12/2013	0/0
18	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	02/2014	0/0
19	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
20	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	03/2014	0/0
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2014	0/0
22	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	03/2014	0/0
23	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	03/2014	0/0
24	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	03/2014	0/0
25	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	06/2012 -	03/2014	0/0
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	06/2012 -	05/2014	0/0
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	10/2011 -	06/2014	0/0
28	Marketing Terminal at Paradeep - [N16000168]IOCL,Odisha	07/2009	199.75 -	06/2014 -	06/2014	0/0
29	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	10/2014 -	10/2014	0/0
30	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
31	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2014	0/0
32	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
33	Mounded Bullet Project at CPCL - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	12/2014 -	12/2014	0/0
34	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165]OIL,Multi State	04/2010	270.00 -	12/2014 -	12/2014	0/0
35	Reconstruction of BPA and BPB Platforms - [N16000161]ONGC,Maharashtra	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
36	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	- -	04/2015	0/0
37	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
38	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	08/2015 -	08/2015	0/0
39	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	10/2011 -	10/2015	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	Strategic Crude oil storage project at Padur - [N16000169]ISPR, Kerala	01/2006	993.00 1,693.00	01/2012 -	10/2015	0/0
41	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
42	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
43	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
44	Integrated Development of Bassein Field - [N16000160]ONGC, Maharashtra	12/2012	3,513.07 -	02/2016 -	02/2016	0/0
45	Integrated Refinery Expansion Project - [N16000143]BPCL, Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
46	Construction of one Multipurpose Support Vessel (MSV) - [N16000103]ONGC, Multi State	01/2010	723.64 -	03/2013 -	06/2016	0/0
47	Creation of Secondary Tank farm with dehydration facility and ETP at Madhuban - [N16000167]OIL, Multi State	08/2006	374.56 -	09/2012 -	10/2016	0/0
48	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	12/2014 -	12/2016	0/0
49	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	12/2014 -	12/2016	0/0
50	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00 -	04/2015 -	03/2017	0/0
51	De-bottlenecking of SMPL - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	- -	-	0/0
52	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL, Tamil Nadu	05/2013	711.00 -	- -	-	0/0
	Total		89,999.96 -			0/0
	<u>Power</u>					
53	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
54	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38 -	09/2009 06/2013	12/2014	0/0
55	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL, Multi State	03/2013	514.20 -	06/2015 -	06/2015	0/0
56	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL, Andhra Pradesh	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
57	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, Multi State	09/2013	680.69 -	03/2016 -	03/2016	0/0
58	Transmission System associated with Mauda Stage-II - [N18000153]PGCIL, Multi State	09/2013	1,575.30 -	05/2016 -	05/2016	0/0
59	Eastern Region Strengthening Scheme-V - [N18000155]PGCIL, Multi State	10/2013	1,364.52 -	05/2016 -	05/2016	0/0
60	Inter-Regional System Strengthening Scheme in WR and NR (Part-A) - [N18000154]PGCIL, Maharashtra	10/2013	1,315.90 -	11/2016 -	11/2016	0/0
	Total		8,619.86 -			0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Railways</u>					
61	Quilon-Tirunelveli - Trichendur, Tenkasi - [N22000303]SR,Tamil Nadu	04/1999	460.94 -	01/1999 -	01/1999	0/0
62	Jaggayyapet - Mellacheruvu - [N22000304]SCR,Andhra Pradesh	04/2007	313.24 -	01/1999 -	01/1999	0/0
63	MM from Buramara-Chakulia - [N22000305]SER,Multi State	04/2008	466.48 -	01/1999 -	01/1999	0/0
64	Marikuppam - Kuppam - [N22000308]SWR,Karnataka	04/2012	285.57 -	01/1999 -	01/1999	0/0
65	MM from Panskura-Ghatal NL - [N22000309]SER,West Bengal	04/2011	276.69 -	01/1999 -	01/1999	0/0
66	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
67	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
68	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
69	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
70	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
71	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
72	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011	0/0
73	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
74	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
75	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
76	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
77	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
78	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
79	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
80	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	03/2012	0/0
81	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS and PU - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
82	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
83	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
84	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
85	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
86	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
87	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
88	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
89	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
90	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
91	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
92	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
93	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
94	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
95	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
96	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
97	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
98	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	10/2013	0/0
99	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
100	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
101	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	12/2013	0/0
102	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER) - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
103	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	01/1999 -	12/2013	0/0
104	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	01/2014	0/0
105	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	01/2014	0/0
106	PANVEL PEN DOUBLING - [N22000255]CR,Multi State	04/2006	191.00 -	- -	01/2014	0/0
107	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	02/2014	0/0
108	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2014	0/0
109	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
110	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
111	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
112	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
113	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
114	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
115	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
116	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
117	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	- -	03/2014	0/0
118	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura Sharif NL - [N22000244]ER,Multi State	04/2009	257.42 -	03/2014 -	03/2014	0/0
119	PEN ROHA DOUBLING - [N22000254]CR,Multi State	04/2007	203.00 -	- -	03/2014	0/0
120	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	- -	04/2014	0/0
121	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	06/2014	0/0
122	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	06/2013 -	06/2014	0/0
123	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
124	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
125	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	120.00 245.39	12/2008 -	09/2014	0/0
126	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
127	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2014	0/0
128	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
129	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	12/2014	0/0
130	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	02/2015	0/0
131	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
132	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
133	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
134	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
135	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2015	0/0
136	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
137	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
138	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0
139	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	03/2015	0/0
140	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	03/2007 -	03/2015	0/0
141	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	- -	03/2015	0/0
142	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	- -	03/2015	0/0
143	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	- -	03/2015	0/0
144	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12 -	- -	03/2015	0/0
145	Plassey-Jiaganj Doubling - [N22000220]ER,Multi State	04/2011	248.07 -	03/2015 -	03/2015	0/0
146	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
147	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2015	0/0
148	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
149	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	03/2015 -	12/2015	0/0
150	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]SER,Jharkhand	04/2010	309.44 -	12/2015 -	12/2015	0/0
151	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2016	0/0
152	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]RVNL,West Bengal	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
153	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
154	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
155	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
156	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20 -	- -	03/2016	0/0
157	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	06/2005 07/2011	06/2016	0/0
158	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbender (MTP) - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
159	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2016	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
160	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
162	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
163	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
164	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2017	0/0
165	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
166	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
167	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER,Multi State	04/2011	299.60 -	03/2017 -	03/2017	0/0
168	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State	04/2010	423.66 -	03/2017 -	03/2017	0/0
169	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
170	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	- 12/2017	12/2017	0/0
171	Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]NCR,Multi State	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
172	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
173	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
174	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
175	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	- -	-	0/0
176	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-	0/0
177	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
178	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
179	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
180	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
181	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-	0/0
182	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-	0/0
183	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-	0/0
184	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
185	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-	0/0
186	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-	0/0
187	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	- -	-	0/0
188	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	- -	-	0/0
189	Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State	04/2007	1,640.04 -	- -	-	0/0
190	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	- -	-	0/0
191	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	- -	-	0/0
192	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	- -	-	0/0
193	Rajkot-Veraval,Wansjalio to Jatalsar with new MM for Shapur-Saradiya And Somnath-Kodinar (GC) - [N22000143]WR,Gujarat	04/1994	320.66 -	- -	-	0/0
194	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	- -	-	0/0
195	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	- -	-	0/0
196	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	- -	-	0/0
197	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.93 -	- -	-	0/0
198	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	- -	-	0/0
199	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	- -	-	0/0
200	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	- -	-	0/0
201	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC) - [N22000153]NWR,Rajasthan	04/2010	739.65 -	- -	-	0/0
202	Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	- -	-	0/0
203	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	- -	-	0/0
204	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	- -	-	0/0
205	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	- -	-	0/0
206	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	- -	-	0/0
207	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	- -	-	0/0
208	Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	- -	-	0/0
209	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	- -	-	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
210	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	- -	-	0/0
211	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	- -	-	0/0
212	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	- -	-	0/0
213	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	- -	-	0/0
214	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	- -	-	0/0
215	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	- -	-	0/0
216	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	- -	-	0/0
217	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	- -	-	0/0
218	Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	- -	-	0/0
219	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	- -	-	0/0
220	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	- -	-	0/0
221	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	- -	-	0/0
222	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	- -	-	0/0
223	Sakri-Nirmali and Jhanjharpur-Laukahabazar and Saharsa-Forbesganj (GC) - [N22000180]ECR,Bihar	04/2004	372.14 -	- -	-	0/0
224	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Nepal) GC - [N22000181]ECR,Bihar	04/2009	470.00 -	- -	-	0/0
225	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	- -	-	0/0
226	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	- -	-	0/0
227	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	- -	-	0/0
228	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	- -	-	0/0
229	Sriperumbudur-Guduvanchery with spur to Irungattukottai-Avadi-Sriperumbudur - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	- -	-	0/0
230	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	- -	-	0/0
231	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	- -	-	0/0
232	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	- -	-	0/0
233	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	- -	-	0/0
234	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	- -	-	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
235	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR, West Bengal	04/2010	221.42 -	- -	-	0/0
236	Agartala-Akhaura NL - [N22000195]NEFR, Tripura	04/2012	252.00 -	- -	-	0/0
237	Dimapur-Tizit NL - [N22000196]NEFR, Nagaland	04/2013	4,274.00 -	- -	-	0/0
238	Erode-Palani - [N22000199]SR, Tamil Nadu	04/2008	288.57 -	- -	-	0/0
239	Madurai-Bodinayakanur - [N22000201]SR, Tamil Nadu	04/2008	164.41 -	- -	-	0/0
240	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif - [N22000202]SR, Tamil Nadu	04/2007	247.00 -	- -	-	0/0
241	Chengannur-Chingavanam - [N22000203]SR, Kerala	04/2006	191.72 -	- -	-	0/0
242	Ernakulam-Kumbalam - [N22000204]SR, Kerala	04/2010	189.24 -	- -	-	0/0
243	New BG line from Byrnihat to Shillong - [N22000205]NEFR, Meghalaya	04/2010	4,083.02 -	- -	-	0/0
244	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR, Multi State	04/2010	242.22 -	- -	-	0/0
245	Murkongselek-Pasighat NL - [N22000208]NEFR, Multi State	04/2011	165.82 -	- -	-	0/0
246	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai - [N22000209]NEFR, Multi State	04/1999	523.17 -	- -	-	0/0
247	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR, Assam	04/2012	246.07 -	- -	-	0/0
248	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP, West Bengal	04/2009	573.78 -	- -	-	0/0
249	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Phase-II - [N22000213]MRTP, Andhra Pradesh	04/2012	632.68 -	04/2012 -	-	0/0
250	Madurai-Tuticorin via Aruppukottai - [N22000215]SR, Multi State	04/2011	601.43 -	- -	-	0/0
251	Lakshmikanthapur-Namkhana subsequently MM for Namkhana-Chandranagar, Kakdwip-Budakhali and Chandranag - [N22000216]ER, Multi State	04/1999	406.99 -	- -	-	0/0
252	Sultanganj-Katuria via Asarganj, Tarapur And Belhar - [N22000217]ER, Multi State	04/2007	450.00 -	- -	-	0/0
253	Hansnabad-Hingalgaon New BG line - [N22000218]ER, Multi State	04/2010	172.03 -	- -	-	0/0
254	Pirpainti-Jasidih - [N22000219]ER, Multi State	04/2013	915.98 -	- -	-	0/0
255	Bandel-Boinchi 3rd line - [N22000221]ER, Multi State	04/2011	288.35 -	- -	-	0/0
256	Pirpainti-Bhagalpur - [N22000222]ER, Multi State	04/2011	261.38 -	- -	-	0/0
257	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER, Multi State	04/2000	157.17 -	- -	-	0/0
258	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - Chapra new line and Naihati-Ranaghat 3 - [N22000224]ER, Multi State	04/2001	923.52 -	- -	-	0/0
259	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-Sainthia via Kandi NL - [N22000225]ER, Multi State	04/2005	595.91 -	- -	-	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
260	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-Duttaphulia new line - [N22000227]ER,Multi State	04/2010	174.56 -	- -	-	0/0
261	Sondalia-Champapur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State	04/2010	277.28 -	- -	-	0/0
262	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh 4th line with MM Baruipara Furfura NL - [N22000229]ER,Multi State	04/2010	296.44 -	- -	-	0/0
263	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State	04/2010	157.94 -	- -	-	0/0
264	Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra	04/2008	697.00 -	- -	-	0/0
265	Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra	04/2011	277.70 -	- -	-	0/0
266	Bariarpur-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State	04/2007	450.55 -	- -	-	0/0
267	Tarakeswar-Magra New BG line - [N22000235]ER,Multi State	04/2010	365.17 -	- -	-	0/0
268	Hansdiha-Godda NL - [N22000236]ER,Multi State	04/2011	267.09 -	- -	-	0/0
269	Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State	04/2011	193.44 -	- -	-	0/0
270	Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State	04/2011	175.80 -	- -	-	0/0
271	New Alipur to Akra, MM for Budge Budge-Pujali NL, Pujali-Uluberia(Birshivpur) And Pujali-Bahrahat NL - [N22000240]ER,Multi State	04/2010	494.54 -	- -	-	0/0
272	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghatakpur NL - [N22000241]ER,Multi State	04/2000	297.47 -	- -	-	0/0
273	Chandpara-Bangaon doubling with extension to Chandbazar and new MM for Bongaon-Poramaheshtala & Chand - [N22000242]ER,Multi State	04/2003	337.96 -	- -	-	0/0
274	Magrahat-Diamond Harbour with MM Sangrampur-Krishnachandpur and Diamond Hatbour - Bahrahat-Kulpi NL - [N22000243]ER,Multi State	04/2009	493.96 -	- -	-	0/0
275	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	- -	-	0/0
276	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	- -	-	0/0
277	Santoshpur-Remount Road via Garden Reach- Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	- -	-	0/0
278	Howrah-Development of station including segregation of arrival/departure and other amenities - [N22000249]ER,Multi State	04/2011	166.89 -	- -	-	0/0
279	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	- -	-	0/0
280	Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka	04/2011	913.00 -	- -	-	0/0
281	Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka	04/2007	179.65 -	- -	-	0/0
282	Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka	04/2010	377.93 -	- -	-	0/0
283	Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh	04/2013	1,112.00 -	- -	-	0/0
284	Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh	04/2013	723.00 -	- -	-	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
285	Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State	04/2012	1,054.35 -	- -	-	0/0
286	Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State	04/2008	184.26 -	- -	-	0/0
287	Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh	04/2012	923.23 -	- -	-	0/0
288	Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh	04/2011	283.54 -	- -	-	0/0
289	Meerut-Muzafarnagar Patch DL - [N22000267]NR,Uttar Pradesh	04/2012	289.79 -	- -	-	0/0
290	Grade Seperator at Dayabasti - [N22000269]NR,Delhi	04/1999	159.20 -	- -	-	0/0
291	Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareli - [N22000270]NR,Uttar Pradesh	04/2013	654.00 -	- -	-	0/0
292	Rohtak-Meham Hansi - [N22000272]NR,Haryana	04/2012	287.00 -	- -	-	0/0
293	Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh	04/2008	1,046.88 -	- -	-	0/0
294	Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State	04/2007	336.91 -	- -	-	0/0
295	Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka	04/2013	558.00 -	- -	-	0/0
296	Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State	04/2013	296.00 -	- -	-	0/0
297	Shimoga-Harihar NL - [N22000278]SWR,Karnataka	04/2011	562.74 -	- -	-	0/0
298	Rayadurga-Tumkur NL - [N22000279]SWR,Multi State	04/2007	970.34 -	- -	-	0/0
299	White Field-Kolar NL - [N22000280]SWR,Karnataka	04/2011	341.05 -	- -	-	0/0
300	Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi	04/2012	295.68 -	- -	-	0/0
301	Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh	04/2013	829.00 -	- -	-	0/0
302	Mudkhed-Parbhani - [N22000283](SCR),Maharashtra	04/2011	390.60 -	- -	-	0/0
303	Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh	04/2012	153.00 -	- -	-	0/0
304	Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh	04/2011	1,313.48 -	- -	-	0/0
305	Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh	04/2010	337.49 -	- -	-	0/0
306	Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State	04/2008	2,050.00 -	- -	-	0/0
307	Haridwar-Laksar - [N22000289]NR,Uttarakhand	04/2012	219.83 -	- -	-	0/0
308	Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State	04/2008	165.65 -	- -	-	0/0
309	Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana	04/2013	400.00 -	- -	-	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
310	Yamunanagar-Chandigarh via Sadhaura Narayangarh - [N22000293]NR,Multi State	04/2013	876.00 -	- -	-	0/0
311	Unchahar-Amethi - [N22000294]NR,Uttar Pradesh	04/2012	380.00 -	- -	-	0/0
312	Qadian-Beas - [N22000295]NR,Punjab	04/2011	205.22 -	- -	-	0/0
313	Chandigarh-Baddi NL - [N22000296]NR,Multi State	04/2007	328.14 -	- -	-	0/0
314	Hospet-Hubli-Londa-Vascodagama DL - [N22000297]SWR,Karnataka	04/2010	2,127.00 -	- -	-	0/0
315	Gadag-Wadi NL - [N22000299]SWR,Karnataka	04/2013	1,117.00 -	- -	-	0/0
316	Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka	04/2013	327.25 -	- -	-	0/0
317	Monigram- Nimita - [N22000301]ER,Multi State	04/2012	250.93 -	- -	-	0/0
318	Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal	04/2012	255.64 -	- -	-	0/0
319	VIRAMGAM-BHILD(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
320	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-	0/0
321	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
322	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
323	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
324	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
325	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
326	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
327	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
328	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
329	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
330	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
331	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
332	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
333	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-	0/0
334	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
335	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
336	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
337	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
338	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
339	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
340	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
341	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
342	Mansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur Mandi via Talwandi Saboo NL - [N22000268]NR,Punjab	04/2009	396.04 -	- -	-	0/0
343	Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State	04/2013	1,239.00 -	- -	-	0/0
344	Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State	04/2010	338.54 -	- -	-	0/0
	Total		148,559.08 -			0/0
	<u>Road Transport And Highways</u>					
345	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008	0/0
346	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
347	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2013	0/0
348	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	09/2013	0/0
349	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
350	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	10/2013	0/0
351	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	10/2013	0/0
352	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	10/2013	0/0
353	Pune-sholapur,pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2013	0/0
354	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	10/2013	0/0
355	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	10/2013	0/0
356	Tirupati - Tiruthani - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
357	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	01/2013 -	10/2013	0/0
358	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Odisha	04/2000	225.00 -	04/2004 -	11/2013	0/0
359	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	09/2007 -	11/2013	0/0
360	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70 -	02/2004 -	11/2013	0/0
361	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
362	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
363	2 Laning of Muzaffarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
364	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
365	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	05/2008 -	12/2013	0/0
366	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	10/2008 -	12/2013	0/0
367	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2013	0/0
368	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	09/2008 -	12/2013	0/0
369	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	10/2008 -	12/2013	0/0
370	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	06/2008 -	12/2013	0/0
371	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	06/2008 -	12/2013	0/0
372	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	05/2008 -	12/2013	0/0
373	LAKHNAADON TO MP/MH BORDER, KM 596.75-653.22 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60 -	06/2010 -	12/2013	0/0
374	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2013	0/0
375	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	01/2011 -	12/2013	0/0
376	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	07/2012 -	12/2013	0/0
377	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	06/2011 -	12/2013	0/0
378	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	09/2012 -	12/2013	0/0
379	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	05/2012 -	12/2013	0/0
380	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	10/2011 -	12/2013	0/0
381	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	08/2011 -	12/2013	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
382	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	12/2013	0/0
383	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	12/2013	0/0
384	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	12/2013	0/0
385	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	12/2013	0/0
386	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	12/2013	0/0
387	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	07/2013 -	12/2013	0/0
388	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	12/2013	0/0
389	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	12/2013	0/0
390	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
391	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
392	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	12/2013	0/0
393	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	12/2013	0/0
394	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	12/2013	0/0
395	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	12/2013	0/0
396	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	08/2013 -	12/2013	0/0
397	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	12/2013	0/0
398	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
399	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
400	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
401	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	02/2014	0/0
402	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
403	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
404	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
405	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2014	0/0
406	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2014	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
407	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
408	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
409	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
410	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	03/2014	0/0
411	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
412	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	03/2014	0/0
413	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	03/2014	0/0
414	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
415	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	03/2014	0/0
416	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	03/2014	0/0
417	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
418	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2014	0/0
419	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
420	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
421	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	03/2014	0/0
422	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
423	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
424	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
425	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
426	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
427	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
428	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
429	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
430	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
431	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
432	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
433	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
434	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
435	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
436	2laning with PS Gopalganj-Chhapra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
437	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
438	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
439	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
440	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2014	0/0
441	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
442	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	06/2014	0/0
443	Kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
444	SRINAGAR TO BANIHAL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
445	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
446	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
447	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
448	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
449	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
450	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
451	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
452	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	07/2014 -	07/2014	0/0
453	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	08/2014	0/0
454	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	09/2014	0/0
455	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
456	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
457	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,Gujarat	03/2012	828.00 -	09/2014 -	09/2014	0/0
458	REENGUS SIKAR - [N24000227]NHAI,Rajasthan	03/2012	333.51 -	09/2014 -	09/2014	0/0
459	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
460	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
461	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	10/2014 -	10/2014	0/0
462	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI, Madhya pradesh	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
463	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
464	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
465	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
466	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2014	0/0
467	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2014	0/0
468	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
469	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	01/2014 -	12/2014	0/0
470	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	12/2014	0/0
471	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	12/2014	0/0
472	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	12/2014	0/0
473	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	02/2015	0/0
474	BARSAT-KRISHNANAGAR - [N24000229]NHAI,West Bengal	08/2012	867.00 -	02/2015 -	02/2015	0/0
475	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
476	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
477	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
478	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2015	0/0
479	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
480	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
481	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	09/2015 -	09/2015	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
482	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
483	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	11/2015	0/0
484	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,Tamil Nadu	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
485	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	12/2015	0/0
486	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	12/2015 -	12/2015	0/0
487	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
488	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		100,698.72 -			0/0
	<u>Shipping And Ports</u>					
489	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
490	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
491	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
492	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
493	Mechanization of coal handling facilities to 200000 DWT Vessels on DBFOT basis - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
494	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
495	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
496	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013	0/0
497	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
498	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
499	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0
500	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
501	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 12/2013	12/2013	0/0
502	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
503	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0

			(Oct,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
504	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	03/2015	0/0
505	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
506	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		15,462.28 -			0/0
	<u>Telecommunications</u>					
507	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 Punjab - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
508	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
509	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
510	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	12/2013	0/0
511	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	12/2013	0/0
512	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	12/2013	0/0
513	Supply Installation testing and commissioning of Rural Wimax network Phase-II - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	12/2013	0/0
514	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
515	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
	Total		4,742.45 -			0/0
	<u>Urban Development</u>					
516	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
517	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
518	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
	<u>Water Resources</u>					
519	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		414,420.39			0/0

List of Projects on schedule w.r.t. Latest Schedule

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	160.72	03/2015 -	03/2015
2	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	160.74		
	<u>Coal</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	162.71	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	45.02	03/2014 -	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	74.32	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	52.12	03/2015 -	03/2015
8	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016
9	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	58.99	03/2016 -	03/2016
11	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.11	07/2016 -	07/2016
12	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	1.81	06/2015 -	06/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	53.45	03/2016 -	03/2016
14	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
15	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	14.03	03/2015 -	03/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	3.25	03/2015 -	03/2015

(Oct,2013)

						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.40	03/2020 -	03/2020
20	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	40.99	03/2014 -	03/2014
21	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.05	03/2016 -	03/2016
22	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
23	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	48.56	03/2016 -	03/2016
24	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	152.13	03/2017 -	03/2017
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	582.00	03/2016 03/2016	03/2016
	Total		11,169.15 -	10,797.81	1,699.42		
	<u>Petrochemicals</u>						
26	Assam gas Cracker project - [N16000106]	4/2006	5,460.61 -	8,920.00	4,510.51	04/2012 12/2013	12/2013
	Total		5,460.61 -	8,920.00	4,510.51		
	<u>Petroleum</u>						
27	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2014
28	Marketing Terminal at Paradeep - [N16000168]	7/2009	199.75 -	199.75	89.65	06/2014 -	06/2014
29	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165]	4/2010	270.00 -	270.00	-	12/2014 -	12/2014
30	Reconstruction of BPA and BPB Platforms - [N16000161]	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
31	Integrated Development of Bassein Field - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
32	Pipeline Replacement Project, Ahmedabad - [N16000159]	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
33	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	48.71	10/2014 -	10/2014
34	Mounded Bullet Project at CPCL - [N16000154]	12/2012	279.00 -	279.00	283.87	12/2014 -	12/2014
35	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	81.00	08/2015 -	08/2015
36	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	44.38	07/2015 -	07/2015

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
37	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
38	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	320.72	11/2015 -	11/2015
39	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	200.75	12/2014 -	12/2014
40	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	90.20	03/2014 -	03/2014
41	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	560.90	05/2014 -	05/2014
42	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	130.15	12/2014 -	12/2014
43	Construction of three ETPs, Mehsana - [N16000135]	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
44	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014
45	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	45.76	05/2014 -	05/2014
46	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,425.92	05/2015 -	05/2015
47	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,665.65	362.59	03/2015 -	03/2015
48	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	761.68	310.49	05/2013 06/2014	06/2014
49	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	5,597.68	02/2014 -	02/2014
50	Development of Cluster-7 Fields - [N16000104]	3/2010	3,241.03 -	6,638.94	1,451.42	03/2013 11/2014	11/2014
51	Wax Project - [N16000101]	6/2010	576.60 -	576.60	337.79	12/2013 -	12/2013
	Total		40,050.65 -	42,730.84	12,898.28		
	<u>Power</u>						
52	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	1,176.91	05/2014 -	05/2014
53	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,008.84	08/2014 -	08/2014
54	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	1,273.52	07/2014 -	07/2014
55	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	220.72	06/2014 -	06/2014
56	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	1,066.41	09/2014 -	09/2014

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	573.52	08/2014 -	08/2014
58	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	158.93	08/2014 -	08/2014
59	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	573.00	08/2015 -	08/2015
60	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,699.00	11/2016 -	11/2016
61	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,242.00	09/2016 -	09/2016
62	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	2,093.00	12/2016 -	12/2016
63	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	357.54	11/2014 -	11/2014
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	233.38	11/2014 -	11/2014
65	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	437.18	08/2014 -	08/2014
66	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	41.52	06/2014 -	06/2014
67	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	1,110.57	06/2015 -	06/2015
68	Gadarwara Super Thermal Power Project Stage-I - [N18000151]	2/2013	11,638.55 -	11,638.55	889.00	09/2017 -	09/2017
69	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	233.52	06/2015 -	06/2015
70	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	11.64	12/2015 -	12/2015
71	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
72	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017
73	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,139.00	05/2017 -	05/2017
74	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
75	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	5.89	10/2014 -	10/2014
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	122.75	03/2015 -	03/2015

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	Eastern Region Strengthening Scheme-V - [N18000155]	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016
78	Inter-Regional System Strengthening Scheme in WR and NR (Part-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016
79	Transmission System associated with Mauda Stage-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
80	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
81	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
82	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
83	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	519.59	10/2014 -	10/2014
84	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	19.50	08/2014 -	08/2014
85	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	495.42	02/2015 -	02/2015
86	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD [N18000118]	1/2012	259.28 -	259.28	112.33	01/2014 -	01/2014
87	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	490.30	01/2015 -	01/2015
88	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	207.18	08/2014 -	08/2014
89	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED [N18000114]	12/2011	552.44 -	552.44	337.44	02/2014 -	02/2014
	Total		103,186.86 -	103,186.86	17,966.23		
	<u>Railways</u>						
90	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	105.60	02/2015 -	02/2015
91	New Work for Construction of Metro railway from Joka to Binooy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02 -	2,913.51	350.64	03/2016 -	03/2016
92	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	230.80	03/2016 -	03/2016
93	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,116.53	237.72	03/2010 03/2017	03/2017
94	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]	4/2008	829.74 -	829.74	38.33	03/2015 -	03/2015

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
95	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114	4/2008	516.23 -	516.23	435.49	03/2014 -	03/2014
96	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	699.00	03/2014 -	03/2014
97	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245	4/2010	423.66 -	423.66	136.58	03/2017 -	03/2017
98	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura Sharif NL - [N22000244	4/2009	257.42 -	257.42	33.39	03/2014 -	03/2014
99	Princepghat-Majerhat Doubling of Circular Railway - [N22000239	4/2011	299.60 -	299.60	1.09	03/2017 -	03/2017
100	Plassey-Jiaganj Doubling - [N22000220	4/2011	248.07 -	248.07	9.83	03/2015 -	03/2015
101	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164	4/2010	309.44 -	388.67	47.81	12/2015 -	12/2015
102	Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158	4/2010	622.41 -	2,030.50	1.22	02/2019 -	02/2019
103	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	1.71	02/2020 -	02/2020
104	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
105	Ghutiasharif-Canning (ER) - [N22000117	4/2009	189.97 -	611.03	130.62	12/2011 11/2013	11/2013
106	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113	4/2008	653.19 -	653.47	237.99	03/2014 -	03/2014
	Total		18,869.25 -	25,168.50	2,697.82		
	<u>Road Transport And Highways</u>						
107	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	1,166.00	11/2013 -	11/2013
108	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,318.00	10/2014 -	10/2014
109	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	1,119.00	11/2013 -	11/2013
110	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
111	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
112	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	518.00	01/2014 -	01/2014
113	BARSAT-KRISHNANAGAR - [N24000229	8/2012	867.00 -	867.00	-	02/2015 -	02/2015
114	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
115	REENGUS SIKAR - [N24000227	3/2012	333.51 -	333.51	236.80	09/2014 -	09/2014

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
116	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	691.40	10/2014 -	10/2014
117	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	490.60	09/2014 -	09/2014
118	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015
119	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	34.28	12/2015 -	12/2015
120	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	40.66	07/2014 -	07/2014
121	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	230.10	10/2014 -	10/2014
122	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	17.23	09/2015 -	09/2015
123	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
124	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	198.50	06/2014 -	06/2014
125	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	227.90	06/2015 -	06/2015
126	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	314.70	04/2014 -	04/2014
127	4-laning of Barhi-Hazaribagh - [N24000191]	2/2012	398.00 -	398.00	441.10	02/2014 -	02/2014
128	2laning with PS Gopalganj-Chappra - [N24000190]	12/2011	325.00 -	325.00	161.20	05/2014 -	05/2014
129	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
130	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	642.20	11/2013 -	11/2013
131	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014
132	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	655.30	03/2014 -	03/2014
133	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,218.00	05/2014 -	05/2014
134	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	921.30	03/2014 -	03/2014
135	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	189.10	02/2014 -	02/2014
136	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
137	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	282.80	10/2014 -	10/2014
138	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	498.90	07/2014 -	07/2014

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
139	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	98.48	01/2014 -	01/2014
140	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,048.00	09/2014 -	09/2014
141	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	202.40	06/2014 -	06/2014
142	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,388.00	06/2014 -	06/2014
143	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	941.90	05/2014 -	05/2014
144	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	388.20	01/2014 -	01/2014
145	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
146	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 [N24000172	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
	Total		37,139.74 -	37,139.74	16,491.58		
	<u>Shipping And Ports</u>						
147	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	139.80	03/2006 12/2013	12/2013
148	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051	8/2010	612.72 -	532.83	448.43	12/2012 11/2013	11/2013
149	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 -	1,012.23	554.60	12/2013 11/2013	11/2013
150	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
151	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		3,269.15 -	3,651.75	1,612.75		
	<u>Steel</u>						
152	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	6/2006	108.00 -	216.68	153.79	09/2008 12/2013	12/2013
153	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073	2/2011	898.55 -	898.55	229.26	05/2013 03/2014	03/2014
154	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	68.92	08/2014 -	08/2014
155	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	10.01	12/2014 -	12/2014
156	Rebuilding of Battery Block 5A and Re-construction of Battery Block 5B - [N12000080	3/2012	339.35 -	339.35	21.03	06/2015 -	06/2015
	Total		1,933.45 -	2,042.13	483.01		

(Oct,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Urban Development</u>						
157	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	5,302.74	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	5,302.74		
	Grand Total		256,990.46	269,549.23	63,823.08		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(Oct,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Petroleum</u>						
1	IOR GELEKI (ONGCL) - [160100216	9/2001	390.09 1,674.11	1,674.11	1,759.52	03/2007 03/2017	10/2013
	Total		390.09 -	1,674.11	1,759.52		
	<u>Power</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	119.62	06/2016 -	04/2015
3	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129	2/2012	3,201.44 -	3,201.44	1,032.40	10/2014 -	09/2014
4	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	398.06	12/2014 -	11/2014
	Total		6,645.53 -	6,645.53	1,550.08		
	Grand Total		7,035.62	8,319.64	3,309.60		

List of Delayed Projects w.r.t. Latest Schedule

(Oct,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,746.00	12/2008 -	09/2014	69	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,309.83	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	3,478.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,379.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,912.83				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building(Goa) - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	249.31	05/2012 -	11/2013	18	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,Multi State	02/2010	344.28 -	344.28	-	03/2014 -	06/2014	3	-
7	C/o New Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.71	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	989.35	481.02				
	<u>Coal</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,802.11	06/2009 -	03/2014	57	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.47	03/2010 -	03/2014	48	-
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	118.26	03/2011 -	03/2014	36	-
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 -	741.62	377.80	03/2013 -	03/2014	12	-
12	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	117.75	03/2012 -	03/2014	24	-
13	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,770.42	03/2012 -	05/2014	26	-
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	805.16	03/2013 09/2012	02/2015	23	29
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.98	03/2012 -	03/2015	36	-
16	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	113.59	03/2013 -	03/2015	24	-
17	BALRAM OCP EXTENSION,MCL 8.00 Mty - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	129.20	03/2010 -	03/2015	60	-
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	118.03	03/2013 -	03/2015	24	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	237.96	03/2012 -	03/2015	36	-
20	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.65	03/2012 -	03/2015	36	-
21	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.33	03/2013 -	03/2015	24	-
22	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,575.95	03/2014 -	03/2016	24	-
23	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,275.84	03/2014 -	03/2016	24	-
24	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	27.60	07/2012 -	03/2016	44	-
25	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	268.23	03/2014 -	03/2016	24	-
26	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	92.14	12/2012 -	03/2016	39	-
27	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	20.33	03/2014 -	03/2016	24	-
28	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.28	03/2014 -	03/2016	24	-
29	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
30	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	210.11	03/2014 -	03/2016	24	-
31	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
32	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	138.45	03/2012 -	03/2016	48	-
33	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72	-
34	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
35	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	61.20	03/2012 -	03/2017	60	-
36	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	34.92	12/2015 -	04/2018	28	-
37	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	739.17	03/2013 -	03/2023	120	-
	Total		26,241.09 -	29,697.88	14,321.79				
	<u>Steel</u>								
38	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,Andhra Pradesh	07/2007	202.00 343.58	343.58	281.05	01/2010 02/2011	11/2013	46	33
39	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	15,038.24	12/2011 -	12/2013	24	-
40	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	07/2007	480.00 -	450.00	288.01	09/2009 05/2012	12/2013	51	19
41	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,779.97	12/2011 -	12/2013	24	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Odisha	09/2008	11,812.00 -	11,812.00	10,157.19	03/2013 -	12/2013	9	-
43	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,603.02	10/2009 10/2012	03/2014	53	17
44	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	356.75	12/2011 03/2012	03/2014	27	24
45	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, Karnataka	04/2011	572.00 -	572.00	338.09	04/2013 12/2013	03/2014	11	3
46	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	1,841.57	12/2012 -	03/2014	15	-
47	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, Maharashtra	12/2011	187.33 -	187.33	95.71	10/2013 -	06/2014	8	-
48	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00 -	17,265.00	10,590.79	03/2013 -	09/2014	18	-
49	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, Odisha	11/2011	254.55 -	254.55	83.02	11/2013 -	06/2015	19	-
	Total		63,403.77 -	69,390.63	53,453.41				
	<u>Petroleum</u>								
50	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	794.14	12/2011 -	11/2013	23	-
51	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL, Maharashtra	04/2008	825.00 -	1,827.00	1,462.08	04/2013 -	11/2013	7	-
52	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93	9
53	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	731.38	03/2010 03/2012	12/2013	45	21
54	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	265.22	03/2012 -	12/2013	21	-
55	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery - [N16000107]IOCL, Uttar Pradesh	07/2010	1,000.00 -	1,000.00	716.68	01/2013 -	12/2013	11	-
56	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	1,803.78	755.59	07/2012 -	12/2013	17	-
57	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 -	12,160.26	10,813.90	01/2012 -	12/2013	23	-
58	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	372.11	234.31	03/2013 -	12/2013	9	-
59	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL, Maharashtra	08/2009	246.81 -	276.83	242.63	04/2012 -	12/2013	20	-
60	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin, Karnataka	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20	-
61	GAS TURBINE GENERATION SET - [N18000146]OIL, Assam	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, Assam	08/2008	144.02 -	204.29	133.48	06/2012 -	12/2013	18	-
63	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
64	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	410.44	228.27	11/2012 -	02/2014	15	-
65	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
66	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
67	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
68	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	03/2014	18	-
69	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	253.66	202.37	08/2012 -	03/2014	19	-
70	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	240.95	98.72	09/2012 -	03/2014	18	-
71	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	678.02	52.67	06/2012 -	03/2014	21	-
72	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	269.10	104.65	08/2013 -	03/2014	7	-
73	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL, Assam	08/2008	126.18 -	159.54	59.74	06/2012 -	03/2014	21	-
74	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,137.44	08/2010 03/2012	05/2014	45	26
75	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
76	IOR of B-173A Field - [N16000140]ONGC, Multi State	01/2012	352.49 -	352.49	20.03	03/2014 -	05/2014	2	-
77	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL, Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	912.81	10/2011 -	06/2014	32	-
78	PARADIP REFINERY PROJECT - [N16000058]IOCL, Odisha	02/2009	29,777.00 -	32,710.00	23,613.00	11/2012 -	07/2014	20	-
79	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
80	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	445.86	09/2011 -	12/2014	39	-
81	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC, Assam	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
82	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3	-
83	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, Karnataka	01/2006	732.00 1,227.00	1,227.00	729.75	10/2011 -	10/2015	48	-
84	Strategic Crude oil storage project at Padur - [N16000169]ISPRL, Kerala	01/2006	993.00 1,693.00	1,693.00	998.65	01/2012 -	10/2015	45	-
85	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
86	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	983.55	01/2014 -	12/2015	23	-
88	Integrated Refinery Expansion Project - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	760.92	12/2015 -	05/2016	5	-
89	Construction of one Multipurpose Support Vessel (MSV) - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
90	Creation of Secondary Tank farm with dehydration facility and ETP at Madhuban - [N16000167]OIL,Multi State	08/2006	374.56 -	374.56	10.46	09/2012 -	10/2016	49	-
91	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24	-
92	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24	-
93	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23	-
	Total		117,375.92 -	130,217.36	76,083.49				
	<u>Power</u>								
94	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 1,724.79	2,081.00	2,077.51	11/2009 02/2013	10/2013	47	8
95	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,544.00	10/2012 -	10/2013	12	-
96	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	160.94	06/2012 -	11/2013	17	-
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	385.35	11/2011 -	12/2013	25	-
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.83	02/2012 -	12/2013	22	-
99	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	159.62	11/2011 -	12/2013	25	-
100	765KV System for Central part of Northern Region Grid - Part-III - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	851.42	05/2012 -	12/2013	19	-
101	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	140.34	07/2013 -	12/2013	5	-
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	136.78	01/2013 -	01/2014	12	-
103	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,212.33	10/2010 01/2013	03/2014	41	14
104	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	885.97	10/2009 -	03/2014	53	-
105	RAMPUR HEP(412 MW) - [N18000024]SJVN,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,835.28	01/2012 -	03/2014	26	-
106	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,Multi State	08/2008	2,360.95 2,580.90	2,580.90	2,076.70	08/2012 -	03/2014	19	-
107	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	6,023.11	08/2012 -	03/2014	19	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
108	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	613.65	11/2012 -	03/2014	16	-
109	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,351.27	08/2013 -	03/2014	7	-
110	Northern region system strengthening scheme XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	331.59	07/2013 -	03/2014	8	-
111	Supplementary transmission associated with vellur TPS - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	101.95	04/2013 -	03/2014	11	-
112	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	829.27	12/2013 -	03/2014	3	-
113	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	339.20	10/2013 -	03/2014	5	-
114	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	661.40	07/2013 -	05/2014	10	-
115	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,289.89	03/2013 -	05/2014	14	-
116	Transmission system for phase-I generation projects in orissa-part B - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,780.54	12/2013 -	05/2014	5	-
117	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,998.00	03/2014 -	05/2014	2	-
118	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	1,083.83	12/2013 -	05/2014	5	-
119	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,569.95	10/2012 -	06/2014	20	-
120	Trans. System associated with PALLATANA GBPP & BPTS. - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,452.60	12/2012 -	06/2014	18	-
121	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	912.05	08/2012 -	06/2014	22	-
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	364.17	11/2011 -	07/2014	32	-
123	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,165.00	04/2009 -	09/2014	65	-
124	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	1,117.92	731.69	08/2013 -	09/2014	13	-
125	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,477.00	08/2013 -	09/2014	13	-
126	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	193.36	11/2013 -	09/2014	10	-
127	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,400.74	09/2009 06/2013	12/2014	63	18
128	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	473.70	07/2006 -	02/2015	103	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
129	Transmission System of Vindhuachal -IV And Rihand -III Gen. Proj. - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,752.49	11/2012 -	03/2015	28	-
130	Northern region system strengthening scheme-XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	909.52	04/2013 -	03/2015	23	-
131	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.70	01/2013 -	03/2015	26	-
132	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	1,086.62	11/2013 -	03/2015	16	-
133	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	737.73	11/2012 -	03/2015	28	-
134	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	51.97	04/2015 -	05/2015	1	-
135	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,969.63	08/2013 -	06/2015	22	-
136	Transm System for development of Pooling stn. in NR part of West Bengal And Transfer of power from B - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	393.77	01/2015 -	12/2015	11	-
137	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	4,092.00	07/2011 -	06/2016	59	-
138	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,817.16	01/2016 01/2016	11/2016	10	10
139	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	534.61	07/2010 02/2016	02/2017	79	12
140	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,575.95	12/2009 05/2013	03/2017	87	46
141	BARH STPP(3x660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,741.00	12/2009 -	03/2017	87	-
142	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	3,846.30	1,914.00	03/2013 -	03/2017	48	-
143	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	368.16	07/2014 -	09/2017	38	-
144	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,408.11	09/2010 08/2014	03/2018	90	43
145	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	4,121.24	09/2009 07/2014	07/2018	106	48
	Total		124,434.79 -	141,808.75	98,413.69				
	<u>Railways</u>								
146	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	231.61	03/2002 -	10/2013	139	-
147	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER) - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	179.63	12/2012 -	12/2013	12	-
148	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	287.99	425.91	01/1999 -	12/2013	179	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
149	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	576.81	03/1994 -	01/2014	238	-
150	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	390.29	12/2009 03/2011	01/2014	49	34
151	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
152	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	521.29	03/2013 -	03/2014	12	-
153	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	148.38	02/2006 -	06/2014	100	-
154	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	171.02	104.84	06/2013 -	06/2014	12	-
155	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66	66
156	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65	65
157	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	120.00 245.39	245.39	222.71	12/2008 -	09/2014	69	-
158	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	324.96	03/2004 12/2010	12/2014	129	48
159	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.90	350.33	06/2004 -	12/2014	126	-
160	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,177.39	03/2009 12/2012	12/2014	69	24
161	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	255.39	06/2013 06/2013	12/2014	18	18
162	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
163	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	178.76	03/2007 03/2007	03/2015	96	96
164	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,022.64	741.46	12/2010 12/2010	03/2015	51	51
165	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,483.63	12/2008 -	03/2015	75	-
166	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	218.36	126.65	12/2012 -	03/2015	27	-
167	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,702.79	03/2009 -	03/2015	72	-
168	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,242.25	944.72	03/2007 -	03/2015	96	-
169	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,903.68	10/2007 12/2012	12/2015	98	36
170	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69	-
171	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	495.64	03/2014 -	12/2015	21	-
172	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	177.38	42.98	03/2015 -	12/2015	9	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
173	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]RVNL, West Bengal	04/2010	2,298.42 -	2,298.42	59.82	03/2014 -	03/2016	24	-
174	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 -	1,074.47	449.48	06/2005 07/2011	06/2016	132	59
175	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbender (MTP) - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	57.27	03/2016 -	06/2016	3	-
176	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	4,996.19	2,895.33	04/2008 03/2014	12/2016	104	33
177	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,039.29	1,423.98	484.15	03/2005 12/2008	12/2016	141	96
178	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,401.09	03/2014 03/2016	12/2016	33	9
179	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	7,392.65	1,716.34	03/2011 03/2014	03/2017	72	36
180	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 -	2,384.34	99.62	04/2014 -	03/2017	35	-
181	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.58	61.04	12/2015 -	03/2017	15	-
182	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24	-
183	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
	Total		28,178.37 -	79,831.42	31,329.16				
	<u>Road Transport And Highways</u>								
184	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	204.82	08/2004 07/2010	10/2013	110	39
185	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	196.57	08/2004 -	10/2013	110	-
186	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	288.40	06/2011 06/2011	10/2013	28	28
187	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	660.30	05/2010 -	10/2013	41	-
188	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17	-
189	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	625.07	948.00	01/2013 -	10/2013	9	-
190	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	671.30	625.90	02/2013 -	10/2013	8	-
191	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9	-
192	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Odisha	04/2000	225.00 -	241.53	162.71	04/2004 -	11/2013	115	-
193	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74	-
194	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	11/2013	117	-
195	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	327.60	05/2008 -	12/2013	67	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
196	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	295.00	10/2008 -	12/2013	62	-
197	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.60	01/2009 -	12/2013	59	-
198	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	475.50	09/2008 -	12/2013	63	-
199	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	280.40	10/2008 -	12/2013	62	-
200	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	288.30	06/2008 -	12/2013	66	-
201	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	266.10	06/2008 -	12/2013	66	-
202	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	207.70	05/2008 -	12/2013	67	-
203	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42	-
204	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.40	09/2009 -	12/2013	51	-
205	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	12/2013	35	-
206	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,325.00	07/2012 -	12/2013	17	-
207	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
208	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,123.00	09/2012 -	12/2013	15	-
209	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	12/2013	19	-
210	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26	-
211	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,721.00	08/2011 -	12/2013	28	-
212	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	12/2013	25	-
213	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8	-
214	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	839.20	03/2013 -	12/2013	9	-
215	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	12/2013	7	-
216	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,144.00	11/2012 -	12/2013	13	-
217	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	582.90	07/2013 -	12/2013	5	-
218	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,352.00	06/2013 -	12/2013	6	-
219	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	843.90	08/2013 -	12/2013	4	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
220	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
221	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	119.10	05/2013 -	12/2013	7	-
222	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	725.40	03/2013 -	12/2013	9	-
223	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.40	07/2013 -	12/2013	5	-
224	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	509.40	08/2013 -	12/2013	4	-
225	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	651.60	02/2013 -	12/2013	10	-
226	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,975.00	12/2012 -	02/2014	14	-
227	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	532.70	05/2013 -	02/2014	9	-
228	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	240.40	09/2007 -	03/2014	78	-
229	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	144.30	09/2008 -	03/2014	66	-
230	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	239.90	06/2005 -	03/2014	105	-
231	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	252.60	06/2008 -	03/2014	69	-
232	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	289.00	06/2008 -	03/2014	69	-
233	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	338.40	10/2008 -	03/2014	65	-
234	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	217.60	04/2008 -	03/2014	71	-
235	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	301.10	06/2008 -	03/2014	69	-
236	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	03/2014	72	-
237	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	276.20	04/2008 -	03/2014	71	-
238	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	253.90	06/2008 -	03/2014	69	-
239	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63	-
240	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	240.70	09/2007 -	03/2014	78	-
241	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	860.70	07/2010 -	03/2014	44	-
242	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	446.20	10/2011 -	03/2014	29	-
243	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	54.59	11/2012 -	03/2014	16	-
244	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,876.00	06/2013 -	03/2014	9	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
245	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	395.20	05/2013 -	03/2014	10	-
246	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	515.80	03/2013 -	03/2014	12	-
247	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	281.10	10/2013 -	03/2014	5	-
248	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	70.00	09/2007 -	04/2014	79	-
249	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,201.00	03/2013 -	04/2014	13	-
250	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	564.60	02/2014 -	04/2014	2	-
251	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	324.60	02/2009 03/2014	05/2014	63	2
252	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	308.70	04/2008 -	05/2014	73	-
253	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	158.70	07/2009 -	05/2014	58	-
254	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)- NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.80	10/2008 -	06/2014	68	-
255	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	125.00	11/2008 -	06/2014	67	-
256	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	857.90	10/2011 -	06/2014	32	-
257	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
258	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,287.00	08/2013 -	06/2014	10	-
259	Kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	672.60	07/2013 -	06/2014	11	-
260	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.39	09/2013 -	07/2014	10	-
261	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	257.00	07/2012 -	07/2014	24	-
262	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	305.20	09/2010 -	08/2014	47	-
263	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	09/2014	63	-
264	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	235.20	09/2009 -	09/2014	60	-
265	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	93.63	04/2009 -	12/2014	68	-
266	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	72.60	11/2008 -	12/2014	73	-
267	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	169.00	04/2009 -	12/2014	68	-
268	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	297.90	04/2010 -	12/2014	56	-
269	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60	-

(Oct,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
270	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,129.00	02/2010 -	12/2014	58	-
271	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
272	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	357.00	09/2013 -	12/2014	15	-
273	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,328.00	08/2013 -	12/2014	16	-
274	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,266.00	08/2013 -	12/2014	16	-
275	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	318.00	08/2013 -	02/2015	18	-
276	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31	-
277	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65	-
278	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,734.00	08/2014 -	07/2015	11	-
279	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13	-
280	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	160.00	10/2013 -	11/2015	25	-
281	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	299.60	08/2013 -	12/2015	28	-
282	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
283	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	973.60	07/2015 -	06/2016	11	-
	Total		61,055.38 -	62,967.17	60,926.36				
	<u>Shipping And Ports</u>								
284	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,429.10	978.39	12/2010 09/2012	03/2015	51	30
	Total		1,228.00 -	1,429.10	978.39				
	<u>Telecommunications</u>								
285	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	84.39	06/2009 -	12/2013	54	-
286	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
287	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
288	Supply Installation testing and commissioning of Rural Wimax network Phase-II - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	237.44	05/2011 -	12/2013	31	-
	Total		2,018.15 -	1,843.90	515.46				

(Oct,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Urban Development</u>								
289	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	431.52	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	431.52				
	Grand Total		467,860.82	567,395.56	363,847.12				
