

**323rd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(` 150 Crores and above)
September, 2012**



Pradip Refinery Project



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary in Hindi	1 -4
Executive Summary in English	5-10
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	11-13
Summary of Projects	14-26
Trend and Graphical Analysis of Projects	27-39
Sector wise analysis of projects	40-40
List of All Ongoing Projects	41-70
Sector wise Graph	71-82
ANNEXURE	83-83
Central Sector Projects	84-84
List of Projects Having Expenditure More than cost	85-94
List of Projects Ahead of Schedule	95-95
List of Projects with out Original date of Commissioning	96-99
List of Projects with out date of Commissioning	100-103
List of On schedule Projects	104-113
List of Projects w.r.t Original and Revised	114-135
List of Delayed Projects without Milestones	136-151
Abbreviations	152-154

कार्यकारी सारांश

सितंबर, 2012 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 566 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। सितंबर, 2012 के दौरान 3 परियोजनाओं (दूरसंचार में 2 परियोजनाएं और पेट्रोलियम क्षेत्र में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 566 परियोजनाओं में से 258 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 43 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 43 परियोजनाओं में से, 13 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। सड़क परिवहन और राजमार्ग, कोयला, रेलवे, विद्युत, पेट्रोलियम, इस्पात तथा दूरसंचार क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 24 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित (बड़ी परियोजनाएं)
1.	रेलवे	127	37	3	2
2.	सड़क परिवहन एवं राजमार्ग	148	86	19	1
3.	विद्युत	98	46	7	7
4.	पेट्रोलियम	71	36	7	2
5.	कोयला	51	18	3	0
6.	दूरसंचार	13	8	1	0
7.	पोत परिवहन एवं पत्तन	19	6	0	0
8.	इस्पात	17	10	3	1
9.	उर्वरक	5	2	0	0
10.	नागर विमानन	6	2	0	0
11.	परमाणु ऊर्जा	5	5	0	0
12.	शहरी विकास	4	1	0	0
13.	जल संसाधन	1	1	0	0
14.	पेट्रोरसायन	1	0	0	0
कुल		566	258	43	13

3. 566 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,90,572.38 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,23,296.84 करोड़ रुपए होनेकी संभावना है जो 1,32,724.46 करोड़ रुपए (मूल लागत का 16.8%) की समग्र लागत वृद्धि को दर्शाता है । सितंबर, 2012 तक इन परियोजनाओं पर वहन किया गया व्यय 4,20,233.37 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 45.5% है ।

4. 566 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 226समय के अनुसार तथा 258 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि,विलंबित परियोजनाओं की संख्या 272 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है । इसके अलावा, 38 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 39 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना केअनुमानित रूप से पूरा होने का समय सूचित किया गया है । 258 विलंबित परियोजनाओं में से, 82 परियोजनाओंमें 1 से 12 माह तक का विलंब हुआ,51 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 94 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 31 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ ।

5. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचितसमयवृद्धि के संक्षिप्त कारणोंमें भूमि अधिग्रहण, नगरपालिका की अनुमति में विलंब,सामग्री की आपूर्ति में विलंब, कार्य सौंपने में विलंब,वन भूमि मिलने में विलंब, वन भूमि विमोचित करने में विलंब, बोली संबंधी मुद्दे, अपर्याप्त अनुषंगी, सिविल कार्य में विलंब, परिचालन संबंधी समस्याएं, माओवादी गतिविधियां, जनशक्ति की कमी, कार्य की धीमी प्रगति, मौसम की स्थिति,संविदा संबंधी मामले,आरओयू/आरओडब्ल्यू समस्याएं तथा ठेकेदारों द्वारा घटिया संघटन आदि शामिल हैं ।

6. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों कीनिगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी एजेंसियां उपलब्धियों की सूची प्रदाननहींकर रही हैं। यह भी पाया गया है कि परियोजना एजेंसियां बहुत सी परियोजनाओं के लिए लागत के संशोधित अनुमान तथा आरंभ संबंधी समय-सारणी की सूचना नहीं दे रही हैं, जिनसे यह संकेत मिलता है कि समय/लागतवृद्धि के आंकड़े कम करके बताए गए हैं ।

7. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

(i) दूरसंचार क्षेत्र में, 13 परियोजनाओं में से 8 परियोजनाएं विलंबित हैं । माह के दौरान '1625000 लाइन(2जी) 325000 लाइन (3जी) का जीएसएम उपस्कर, बीएसएनएल' नामक परियोजना के संबंध में नगरपालिका संबंधी अनुमति प्राप्त होने में विलंब होने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(ii) **कोयला क्षेत्र** में, 51 परियोजनाओं में से 21 परियोजनाएं विलंबित हैं। माह के दौरान, 3 परियोजनाओं के संबंध में प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'रामगुंडम ओसी-II एक्सटेंशन, एससीसीएल', 'मनुगुरु ओसी-II एक्सटेंशन फेज-II, एससीसीएल' तथा 'तापिन ओसीपी, सीसीएल' नामक परियोजनाओं के संबंध में वनभूमि की प्राप्ति/विमोचन में विलंब होने के कारण प्रत्येक में 12 महीने के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(iii) **पेट्रोलियम क्षेत्र** में, 71 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं। माह के दौरान, 7 परियोजनाओं के संबंध में 1-5 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें दो बड़ी परियोजनाएं हैं। 4 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'विशाख रिफाइनरी, एचपीसीएल में डीजल हाइड्रोट्रीटर परियोजना' नामक परियोजना के संबंध में संविदाओं की सुपुर्दगी में विलंब के कारण दो माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, '6 ईटीपी का निर्माण, ओएनजीसी' के संबंध में संविदा संबंधी समस्या के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'उरण, ओएनजीसी में फायर वॉटर' के संबंध में इंजीनियर प्रोक्योरमेंट में धीमी प्रगति के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(iv) **विद्युत क्षेत्र** में, 98 परियोजनाओं में से 45 परियोजनाएं विलंबित हैं। माह के दौरान 7 परियोजनाओं के संबंध में 1-12 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। ये सभी परियोजनाएं बड़ी परियोजनाएं हैं। 2 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'तीस्ता लो डैम एचईपी, स्टेज-IV, एनएचपीसी' और 'बाढ़ एसटीटीपी स्टेज-II, एनटीपीसी' के संबंध में बीएचईएल द्वारा आपूर्ति में विलंब के कारण क्रमशः 2 और 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'कुंडनकुलम एपीपी ट्रांस. सिस्टम, पीजीसीआईएल' और 'पल्लातना जीबीपीपी एवं बीपीटी से संबद्ध ट्रांस. सिस्टम, पीजीसीआईएल' नामक परियोजनाओं के संबंध में आरओडब्ल्यू समस्याओं के कारण क्रमशः 3 और 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'सासन और मुन्द्रा (यूएमपीपी), पीजीसीआईएल हेतु एनआर में सिस्टम सुदृढीकरण' के संबंध में संविदा संबंधी समस्या के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(v) **इस्पात क्षेत्र** में, 17 परियोजनाओं में से 9 परियोजनाएं विलंबित हैं। माह के दौरान 3 परियोजनाओं के संबंध में 1-3 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 1 परियोजना बड़ी परियोजना है। 'कोक ओवन बैटरी सं. 4 फेज-II, आरआईएनएल' नामक परियोजना के संबंध में बोली लगाने वालों द्वारा एनआईटी में रुचि न दिखाने के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'एक्सपेंशन ऑफ आरआईएनएल/वीएसपी फ्रॉम 3 एमटीपीवाई-6.3 एमटीपीवाई ऑफ लिक्विड स्टील' (बड़ी परियोजना) के संबंध में माओवादी समस्याओं के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है और 'बैलाडीला लौह अयस्क प्रोजेक्ट डिपॉजिट-11बी, एनएमडीसी' के संबंध में आंतरिक तकनीकी समस्याओं के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(vi) रेलवे क्षेत्र में, 127 परियोजनाओं में से 40 परियोजनाएं विलंबित हैं। माह के दौरान 3 परियोजनाओं के संबंध में 3-12 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 2 बड़ी परियोजनाएं हैं। 'हरमती-ईटानगर/नार तक नई लाइन का निर्माण, एनईएफआर' परियोजना के संबंध में कार्य की धीमी प्रगति के कारण 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। नई परियोजना 'बिमानबंदर होते हुए नोआपारा से बारासात तक मेट्रो रेलवे के निर्माण हेतु नया कार्य, आरवीएनएल' और 'चर्चगेट-विरार 1500 वोल्ट डीसी ट्रैक्शन का 25 किलोवॉट एसी में रूपांतरण, डब्ल्यूआर' के संबंध में क्रमशः 3 और 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों ने कोई विशिष्ट कारण नहीं बताए हैं।

(vii) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 148 परियोजनाओं में से 86 परियोजनाएं विलंबित हैं। माह के दौरान 19 परियोजनाओं के संबंध में 1-24 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 1 परियोजना बड़ी परियोजना है। 5 परियोजनाओं के संबंध में प्रत्येक में एक माह, 6 परियोजनाओं के संबंध में प्रत्येक में 3 माह तथा 1 परियोजना के संबंध में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'बिजनी से असम/प. बंगाल सीमा फेज-II, कि.मी.-30.00 से 0.00, एनएच-31 सी, एनएचएआई' और 'गुजरात/महाराष्ट्र सीमा सूरत-हजीरा पोर्ट सेक्शन, एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना दी गई है, 'ग्वालियर-झांसी, एनएच-75, एनएचएआई' के संबंध में 7 माह के अतिरिक्त विलंब की सूचना दी गई है, 'आगरा-बाईपास (एनएस-1/यूपी-1), कि.मी. 176.8-13.03 एनएच-2, 3, एनएचएआई' और 'मुजफ्फरनगर-हरिद्वार, एनएचएआई' के संबंध में क्रमशः 9 और 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'हरनगाजो से माईबंग, कि.मी. 164.08-190.587 एनएच-54, एनएचएआई' और 'लखनऊ-रायबरेली, एनएचएआई' परियोजनाओं के संबंध में क्रमशः 13 और 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना कार्यान्वयन एजेंसी ने इन परियोजनाओं में विलंब के लिए कोई विशिष्ट कारण नहीं बताए हैं। तथापि, इन परियोजनाओं में विलंब के सामान्य कारणों में भूमि अधिग्रहण में देरी, वन एवं पर्यावरण संबंधी अनापत्ति प्राप्त करने में विलंब, जन सुविधाओं के अंतरण संबंधी समस्या, ठेकेदार का खराब निष्पादन, आदि शामिल हैं।

8. रिपोर्ट में दिनांक 01.10.2012 की स्थिति के अनुसार विभिन्न क्षेत्रों में 150 करोड़ रुपए और उससे अधिक लागत वाली परियोजनाओं की स्थिति दर्शायी गई है।



(टी.सी.ए. अनंत)

सचिव,

सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय

EXECUTIVE SUMMARY

The Flash Report for September, 2012 contains information on the status of the 566 Central Sector Infrastructure Projects, costing ₹150Crores and above. During, September, 2012, 3 projects (2 projects in Telecommunication and 1 project in Petroleum Sector) have reported completion.

During the reference month, out of 566 projects 258 projects are delayed w.r.t latest schedule and 43 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. Out of these 43 projects, 13 are Mega Projects costing ₹ 1000 Crore and above. The additional delays are in the range of 1 to 24 months, in respect of projects relating to Road Transport and Highways, Coal, Railways, Power, Petroleum, Steel and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest Scheduled	Additionally delayed during the month under report	Additionally delayed (Mega Projects)
1.	RAILWAYS	127	37	3	2
2.	ROAD TRANSPORT & HIGHWAYS	148	86	19	1
3.	POWER	98	46	7	7
4.	PETROLEUM	71	36	7	2
5.	COAL	51	18	3	0
6.	TELECOMMUNICATION	13	8	1	0
7.	SHIPPING & PORTS	19	6	0	0
8.	STEEL	17	10	3	1
9.	FERTILISERS	5	2	0	0
10.	CIVIL AVIATION	6	2	0	0
11.	ATOMIC ENERGY	5	5	0	0
12.	URBAN DEVELOPMENT	4	1	0	0
13.	WATER RESOURCES	1	1	0	0
14.	PETROCHEMICALS	1	0	0	0
Total		566	258	43	13

3. The total original cost of implementation of the 566 projects was about ₹ 7,90,572.38Crores and their anticipated completion cost is likely to be ₹ 9,23,296.84Crores, which reflects an overall cost overrun of ₹1,32,724.46Crores (16.8 % of original cost). The expenditure incurred on these projects till September, 2012 is ₹ 4,20,233.37Crores, which is 45.5 % of the anticipated cost of the projects.

4. Out of the 566 projects, 5 projects are ahead of schedule, 226 are on schedule and 258 projects are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 272 if delay is calculated on the basis of original scheduled of completion. Further, 38 projects have been sanctioned without any commissioning schedule/date and for 39 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported. Out of 258 delayed projects, 82 projects had overall delay in the range of 1 to 12 months, 51 projects had a delay in the range of 13 to 24 months, 94 projects had a delay in the range of 25 to 60 months and 31 projects had a delay of 61 months and above.

5. The brief reasons for time overruns as reported by various projects implementing agencies are land acquisition, delay in municipal permission, delay in supply of material, delay in award of work, delay in diversion of forest land, delay in release of forest land, bid related issue, inadequate ancillary, delay in civil work, operational problems, Maoist activities, shortage of manpower, slow progress of work, weather condition, contractual issue, ROU/ROW problem and poor mobilization by the contractor, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedule for many projects, which suggest that time/cost overrun figures are underreported.

7. The Sector-wise details of delays/additional delays are as under:-

- i) In the **Telecommunications sector**, out of 13 projects, 08 projects are delayed. During the month projects namely 'GSM Equipment of 1625000 Lines (2G) 325000 Lines (3G), BSNL' has reported additional delays of 1 month due to delay in municipal permission.

- ii) In the **Coal sector**, out of 51 projects, 21 projects are delayed. During the month 3 projects have reported additional delays of 12 months each. The projects 'Ramagundam OC-II Extension, SCCL', 'Manuguru OC-II Extension Phase-II, SCCL' and 'Tapin OCP, CCL' have reported additional delay of 12 months each due to delay in diversion/release of forest land.

- iii) In the **Petroleum Sector**, out of 71 projects, 37 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-5 months, out of which two are Mega Projects. Four projects have reported additional delays of 1 month each. The project 'Diesel Hydrotreater Project at Visakh Refinery, HPCL' has reported additional delay of 2 months due to delay in award of contracts, 'Construction of 6 ETPs, ONGC' has reported additional delay of 3 months due to contractual problem and 'Fire water network at Uran, ONGC' has reported additional delay of 5 months due to slow progress in engineering procurement

- iv) In the **Power Sector**, out of 98 projects, 45 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-12 months. All of these projects are Mega Projects. Two projects have reported additional delays of one month each. The project 'Teesta Low Dam Hep, Stage-IV, NHPC' and Barh STPP Stage-II, NTPC have reported additional delay of 2 and 3 months respectively due to delay in supply by BHEL, 'Kunadankulam APP Trans. System, PGCIL' and 'Trans. System associated with Pallatana GBPP & BPT, PGCIL' have reported additional delay of 3 and 9 months respectively due to ROW problems, 'System Strengthening in NR for Sasan & Mundra (UMPP), PGCIL' has reported additional delays of 12 months due to contractual problem.

v)In **Steel sector**, out of 17 projects, 9 projects are delayed. During the month 3 projects have reported additional delays in the range of 1-3 months, out of which one is Mega Projects. The projects 'Coke Oven Battery NO. 4 Phase-II, RINL' has reported additional delay of 2 months due to non-response to the NIT by bidder, 'Bailadila Iron Ore Project Deposit- 11B, NMDC' has reported additional of 3 months due to Maoist problems and 'Expansion of RINL/VSP from 3 MTPY-6.3 MTPY of Liquid Steel, RINL' (a Mega project) has reported additional delay of 5 months due to delay in internal technological problems.

vi)In **Railways sector**, out of 127 projects, 40 projects are delayed. During the month 3 projects have reported additional delays in the range of 3-12 months, out of which two are Mega Projects. The projects 'Construction Of New Line From Harmati-Itanagar/Nar, NEFR' has reported additional delay of 9 months due to slow progress of work. The project 'New Work for Construction of Metro railway from Noapara to Barasat via Bimanbandar, RVNL' and 'Churchgate-Virar Conv. of 1500 V DC Traction To 25 KV AC, WR' have reported additional delay 3 and 12 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

vii) In the **Road Transport and Highways Sector**, out of 148 projects, 86 are delayed. During the month 19 projects have reported additional delays in the range of 1-24 months, out of which one is Mega Projects. Five projects have reported additional delays of one month each, 6 projects have reported additional delays of 3 months each and one project has reported additional delay of 5 months. The projects 'Bijni To Assam/Wb Border PH.II, KM.30.00 TO 0.00, NH-31 C, NHAI' and 'Gujarat/Maharashtra Border Surat-Hazira Port Section, NHAI' have reported additional delays of 6 months each, 'Gwalior-Jhansi, NH-75, NHAI' has reported additional delay of 7 months, 'Agra-Bypass(NS-1/UP-1), KM 176.8-13.03 NH-2,3, NHAI' and 'Muzaffarnagar-Haridwar, NHAI' have reported additional delays of 9 and 12 months respectively. The projects 'Harangajo To Maibang, KM164.08-190.587 NH-54, NHAI' and 'Lucknow-Raibareili, NHAI' have reported additional delays 13 and 24 months respectively. The project implementing agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

8. The status as on 01.10.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.



(T.C.A. Anant)
Secretary,
Ministry of Statistics and Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	148	19
2	Railways	127	3
3	Power	98	7
4	Petroleum	71	7
5	Coal	51	3
6	Shipping & Ports	19	0
7	Steel	17	3
8	Telecommunications	13	1
9	Civil Aviation	6	0
10	Atomic Energy	5	0
11	Fertilisers	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	566	43

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	N.A.
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
	<u>Railways</u>			
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
	<u>Road Transport & Highways</u>			
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
	<u>Shipping & Ports</u>			
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
	June,2012			
	<u>Steel</u>			
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
	<u>Power</u>			
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	N.A.
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
	<u>Railways</u>			
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
	<u>Road Transport & Highways</u>			
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9
	July,2012			
	<u>Power</u>			
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
	<u>Railways</u>			
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096]	196.97	03/2011	218.66
	August,2012			
	<u>Steel</u>			
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
	<u>Power</u>			
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
	<u>Road Transport & Highways</u>			
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235]	193.09	03/2008	189.15
	September,2012			
	<u>Petroleum</u>			
34	REVAMPING OF WIN PLATFORM AT MH ASSET(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000044]	333.40	05/2010	680.85
	<u>Telecommunications</u>			
35	PROJ.III OF NIB-II OF MESSAGING STORAGE(BHARAT SANCHAR NIGAM LIMITED) - [260100099]	250.00	12/2005	80.47
36	NIB Project Capacity Expansion(BHARAT SANCHAR NIGAM LIMITED) - [N26000098]	175.52	12/2008	60.84


Summary of projects in the Flash Report for the month of September, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	568
Number of Projects completed/dropped/frozen in Previous Month	6
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects Added in Current Month	7
Number of Projects in Current Month	566


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 566 projects, 5 projects are ahead of schedule, 175 projects are on schedule and 272 projects are delayed. Of the balance, 83 projects do not have fixed dates of commissioning while 31 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

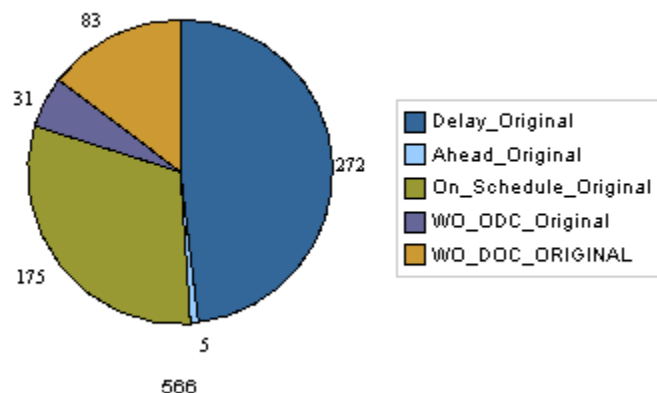

III. Investment Scenario

The Total Original cost of implementation of 566 projects when sanctioned, was of the order of Rs. 790572.38 crore but this was subsequently revised to Rs. 923296.84 crore implying a cost overrun of 16.8%. The expenditure incurred on these projects till September, 2012 is Rs. 420233.37 crore, which is 45.5% of the revised cost of the projects.

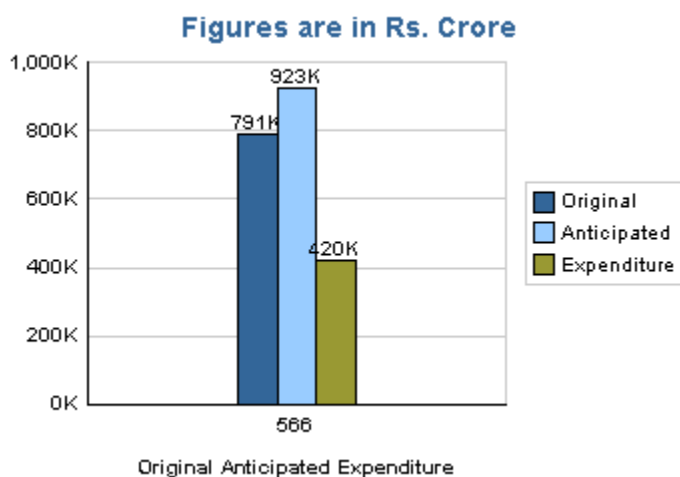

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	568
No of Projects Completed/Dropped/Frozen in Previous Month	6
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects added in Current Month	7
No of Projects in Current Month	566

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	272	5	175	31	83	566	48.06
Latest Approved (Date)	258	5	226	38	39	566	45.58

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	415	645,649.81	677,514.81	275,964.87	40.70	31,865.00	4.90
Latest Approved (RCE)	151	200,699.64	245,782.03	144,268.50	58.70	45,082.39	22.50
Total (RCE)	566	846,349.45	923,296.84	420,233.37	45.51	76947.39	9.09
Original Cost of All Projects							
Original Cost	566	790,572.38	923,296.84	420,233.37	45.50	132,724.46	16.80

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	272	438,951.26	527,497.18	304,331.22	57.70	88,545.92	20.20
Latest Approved (RCE)	258	398,625.86	454,400.97	262,995.95	57.90	55,775.11	14.00

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	43	46,959.69	52,506.31	36,251.99	69.00	5,546.62	11.80

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	36,056.5	37,312.3	3.5	7	8,579.5	10,433.0	21.6
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	71	174,773.8	183,290.2	4.9	15	51,023.0	67,509.5	32.3
8	Power	98	231,379.5	245,378.0	6.1	18	41,492.2	55,490.7	33.7
9	Railways	127	64,518.7	147,234.1	128.2	106	42,243.3	125,005.3	195.9
10	Road Transport & Highways	148	94,480.8	96,059.4	1.7	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	11	9,532.5	12,151.1	27.5
12	Telecommunications	13	5,735.5	5,676.3	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	790,572.4	923,296.8	16.8	184	214,215.6	356,516.6	66.4

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,031.6	38,457.2	23.9	14	12,420.0	20,712.6	66.8
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	36	22,463.9	34,047.4	51.6	12	10,491.8	22,169.3	111.3
4	Bihar	30	26,901.2	34,657.0	28.8	13	12,343.6	20,099.4	62.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	10	5,496.6	7,438.4	35.3	3	1,448.2	3,390.0	134.1
8	Himachal Pr.	5	13,355.6	15,414.9	15.4	3	6,781.4	8,840.8	30.4
9	J and K	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	24	44,634.8	54,126.8	21.3	9	8,598.8	18,497.3	115.1
11	Kerala	6	19,694.7	21,136.2	7.3	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	24	19,741.9	20,036.4	1.5	3	2,027.6	2,741.5	35.2
13	Maharashtra	55	97,571.2	112,834.4	15.6	18	32,285.0	50,022.8	54.9
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	30	57,409.1	60,949.0	6.2	12	32,671.6	36,211.5	10.8
19	Punjab	7	4,836.2	5,778.0	19.5	2	532.4	1,474.2	176.9
20	Rajasthan	14	26,544.1	26,138.3	-1.5	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	25	19,249.2	23,087.0	19.9	8	3,498.5	7,384.5	111.1
25	West Bengal	27	42,286.1	54,378.7	28.6	15	23,294.9	35,387.5	51.9
26	Delhi	5	38,572.6	38,553.0	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	24	46,715.2	47,998.3	2.7	6	1,548.3	2,831.4	82.9
28	Jharkhandd	22	14,293.6	18,275.2	27.9	6	1,897.3	6,050.7	218.9
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	35.6
30	Multi State	103	139,949.5	145,640.6	4.1	20	6,574.0	16,399.9	149.5
Total		566	790,572.4	923,296.8	16.8	184	214,215.6	356,516.6	66.4

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	7 - 27
3	Coal	51	36,056.5	37,312.3	3.5	18	17,226.7	18,902.0	19 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	71	174,773.8	183,290.2	4.9	43	114,450.9	122,888.7	1 - 120
8	Power	98	231,379.5	245,378.0	6.1	50	127,549.0	140,934.3	4 - 99
9	Railways	127	64,518.7	147,234.1	128.2	38	25,521.4	67,077.3	1 - 216
10	Road Transport & Highways	148	94,480.8	96,059.4	1.7	87	40,109.4	42,048.0	2 - 106
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	10	8,446.1	10,038.7	5 - 87
12	Telecommunications	13	5,735.5	5,676.3	-1.0	7	2,737.7	2,741.6	25 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	790,572.4	923,296.8	16.8	272	438,951.3	527,497.2	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,031.6	38,457.2	23.9	12	15,494.5	19,105.6	2 - 41
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	25 - 78
3	Assam	36	22,463.9	34,047.4	51.6	33	21,484.3	32,882.6	12 - 120
4	Bihar	30	26,901.2	34,657.0	28.8	14	20,578.4	26,451.2	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	7 - 7
6	Gujarat	22	31,111.6	31,313.5	0.6	6	15,224.5	15,394.7	6 - 24
7	Haryana	10	5,496.6	7,438.4	35.3	4	2,065.9	3,555.1	9 - 50
8	Himachal Pr.	5	13,355.6	15,414.9	15.4	5	13,355.6	15,414.9	20 - 99
9	J and K	10	14,927.0	34,825.6	133.3	9	13,826.3	33,724.9	10 - 201
10	Karnataka	24	44,634.8	54,126.8	21.3	9	22,364.3	27,354.5	7 - 98
11	Kerala	6	19,694.7	21,136.2	7.3	3	4,674.0	5,324.0	11 - 58
12	Madhya pradesh	24	19,741.9	20,036.4	1.5	13	10,571.4	10,585.3	5 - 60
13	Maharashtra	55	97,571.2	112,834.4	15.6	26	50,866.4	59,615.7	5 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 11
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	30	57,409.1	60,949.0	6.2	11	33,068.2	34,030.5	9 - 130
19	Punjab	7	4,836.2	5,778.0	19.5	4	1,611.4	2,553.2	1 - 58
20	Rajasthan	14	26,544.1	26,138.3	-1.5	6	19,992.2	19,687.9	3 - 52
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	11	30,528.8	36,459.4	9 - 87
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	7 - 7
24	Uttar Pradesh	25	19,249.2	23,087.0	19.9	13	12,061.4	14,042.7	5 - 91
25	West Bengal	27	42,286.1	54,378.7	28.6	15	27,126.9	33,755.9	3 - 135
26	Delhi	5	38,572.6	38,553.0	-0.1	1	249.0	229.4	72 - 72
27	Chhatisgarh	24	46,715.2	47,998.3	2.7	4	18,214.9	18,526.2	6 - 47
28	Jharkhandd	22	14,293.6	18,275.2	27.9	9	8,580.7	9,665.7	12 - 102
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	22 - 42
30	Multi State	103	139,949.5	145,640.6	4.1	53	81,821.7	83,134.6	1 - 216
Total		566	790,572.4	923,296.8	16.8	272	438,951.3	527,497.2	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	5	41,548.3	47,832.3	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	2,278.1	2,660.6	7 - 17
3	Coal	51	36,056.5	37,312.3	3.5	18	17,226.7	18,902.0	19 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	2	763.0	763.0	9 - 12
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	71	174,773.8	183,290.2	4.9	36	70,896.3	74,413.9	0 - 86
8	Power	98	231,379.5	245,378.0	6.1	46	120,132.5	131,579.3	4 - 99
9	Railways	127	64,518.7	147,234.1	128.2	37	16,860.2	55,233.1	0 - 216
10	Road Transport & Highways	148	94,480.8	96,059.4	1.7	86	39,829.4	41,768.0	2 - 106
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	6	7,001.8	8,242.8	11 - 34
12	Telecommunications	13	5,735.5	5,676.3	-1.0	8	3,074.6	3,078.4	17 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	790,572.4	923,296.8	16.8	258	377,522.7	454,401.0	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	37,022.5	37,312.3	0.8	5	6,336.3	6,626.1	4.6
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	71	188,226.3	183,290.2	-2.6	2	30,533.0	31,324.0	2.6
8	Power	98	235,186.6	245,378.0	4.3	12	34,502.4	44,693.8	29.5
9	Railways	127	94,031.1	147,234.1	56.6	81	47,783.8	101,197.4	111.8
10	Road Transport & Highways	148	94,647.3	96,059.4	1.5	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	18,109.6	18,554.1	2.5	8	4,615.6	5,370.0	16.3
12	Telecommunications	13	5,739.4	5,676.3	-1.1	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	846,349.5	923,296.8	9.1	128	161,928.7	245,925.9	51.9

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	51	36,056.46	37,312.25	3.48	0	0.00	0.00	0- 0
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	13- 13
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	71	174,773.81	183,290.21	4.87	11	20,638.48	35,088.71	24- 120
8	Power	98	231,379.54	245,378.02	6.05	2	2,253.45	3,986.02	0- 67
9	Railways	127	64,518.68	147,234.07	128.20	16	8,942.50	24,039.82	1- 141
10	Road Transport & Highways	148	94,480.80	96,059.42	1.67	0	0.00	0.00	0- 0
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	6	6,013.42	7,487.89	5- 87
12	Telecommunications	13	5,735.48	5,676.27	-1.03	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		566	790572.38	923296.84	16.79	38	45412.35	82144.61	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	17- 17
3	Coal	51	36,056.46	37,312.25	3.48	4	7,617.44	9,422.79	19- 45
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	2- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	71	174,773.81	183,290.21	4.87	12	49,217.95	64,390.50	10- 120
8	Power	98	231,379.54	245,378.02	6.05	16	40,474.74	53,860.08	7- 99
9	Railways	127	64,518.68	147,234.07	128.20	30	13,532.69	55,093.47	1- 216
10	Road Transport & Highways	148	94,480.80	96,059.42	1.67	11	3,324.28	5,445.20	21- 104
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	7	7,365.57	8,958.14	5- 87
12	Telecommunications	13	5,735.48	5,676.27	-1.03	2	1,065.85	1,089.32	25- 42
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	21- 21
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		566	790572.38	923296.84	16.79	93	174139.43	269786.93	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		Final
S.no	Project	DOA	Cost	DOC	Cost	DOC	Expenditure
<u>Petroleum</u>							
1	REVAMPING OF WIN PLATFORM AT MH ASSET	05/2008	333.40	05/2010	656.51	07/2012	680.85
<u>Telecommunications</u>							
2	PROJ.III OF NIB-II OF MESSAGING STORAGE	11/2003	250.00	12/2005	250.00	11/2012	80.47
3	NIB Project Capacity Expansion	06/2007	175.52	12/2008	175.52	11/2012	60.84

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	<u>Petroleum</u>					
1	Replacement of CDU/VDU at Mumbai Refinery	1/1999	1,419.00	12/2014	1,419.00	12/2014
2	IREP	1/1999	14,225.00	12/2015	14,225.00	12/2015
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	9/2012	1,508.74	6/2016	1,508.74	6/2016
	<u>Power</u>					
4	VINDHYACHAL STPP STAGE-V	12/2011	3,180.40	8/2015	3,180.40	8/2015
5	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	9/2012	524.40	4/2015	524.40	4/2015
6	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI	9/2012	803.34	3/2015	803.34	3/2015
7	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID	9/2012	1,935.35	12/2014	1,935.35	12/2015

VII. Milestones (Cumulative due & achieved)

Total	3365
Achieved up to month	1183


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
<u>Coal</u>							
1	RAMAGUNDAM OC-II EXTENSION SCCL	418.97	418.97	03/2012	03/2013	03/2014	12
2	MANUGURU OC-II EXTENSION PHASE-II SCCL	181.19	181.19	03/2012	03/2013	03/2014	12
3	Tapin OCP CCL	264.68	264.68	03/2012	03/2013	03/2014	12
<u>Steel</u>							
4	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	10/2012	10/2012	12/2012	2
5	Bailadila Iron Ore Project Deposit- 11B (NMDC)	295.89	607.17	12/2011	10/2012	01/2013	3
6	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,291.00	10/2009	10/2012	03/2013	5
<u>Petroleum</u>							
7	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) GAIL	1,167.00	798.00	04/2011	09/2012	10/2012	1
8	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-GAIL	238.68	312.00	01/2012	10/2012	11/2012	1
9	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	330.47	03/2012	09/2012	10/2012	1
10	EURO-IV DHDT CPCL	2,615.69	2,615.69	N.A.	09/2012	10/2012	1
11	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	09/2012	11/2012	2
12	Construction of 6 ETPs ONGC	302.26	240.95	09/2012	06/2013	09/2013	3
13	Fire water network at Uran ONGC	171.68	171.68	06/2013	06/2013	11/2013	5
<u>Power</u>							
14	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE NHPC	768.92	1,628.00	03/2007	01/2013	02/2013	1
15	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G PGCIL	1,736.36	1,736.36	06/2012	10/2012	11/2012	1
16	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	08/2013	10/2013	2
17	KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL	1,779.29	2,159.07	09/2008	12/2012	03/2013	3
18	BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	06/2014	09/2014	3
19	Trans. System associated with PALLATANA GBPP & BPT PGCIL	2,144.00	2,144.00	12/2012	03/2013	12/2013	9
20	System Strengthening in NR for SASAN & MUNDRA (UMPP) PGCIL	1,216.83	1,216.83	08/2012	12/2012	12/2013	12
<u>Railways</u>							


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
21	New Work for Construction of Metro railway from No RVNL	2,397.72	2,397.72	03/2016	03/2016	06/2016	3
22	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR NEFR	156.00	415.73	N.A.	03/2012	12/2012	9
23	CHURCHGATE-VIRAR: CONV.OF 1500V DC TRACTION TO 25 KV AC, WR RE	653.84	1,302.12	06/2013	06/2012	06/2013	12
<u>Road Transport & Highways</u>							
24	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 NHAI	275.00	275.00	09/2007	09/2012	10/2012	1
25	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	09/2012	10/2012	1
26	ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	09/2012	10/2012	1
27	Hyderabad-yadgiri N.H no-202 NHAI	388.00	388.00	05/2012	09/2012	10/2012	1
28	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	09/2012	10/2012	1
29	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	09/2012	12/2012	3
30	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	12/2012	03/2013	3
31	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	09/2012	12/2012	3
32	JHANSI TO LALITPUR, NH-25,26 NHAI	355.06	355.06	09/2009	12/2012	03/2013	3
33	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	09/2012	12/2012	3
34	Kishangarh-Ajmer-Beawer NHAI	795.00	795.00	05/2012	09/2012	12/2012	3
35	KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	09/2012	02/2013	5
36	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C NHAI	230.00	230.00	06/2005	09/2012	03/2013	6
37	Gujarat/Maharashtra Border Surat-Hazira Port Section NHAI	1,509.10	1,509.10	09/2012	09/2012	03/2013	6
38	GWALIOR-JHANSI, NH-75 NHAI	604.00	604.00	12/2009	12/2012	07/2013	7
39	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 NHAI	348.16	465.50	09/2007	06/2013	03/2014	9
40	MUZAFFARNAGAR-HARIDWAR NHAI	754.00	754.00	03/2013	03/2013	03/2014	12
41	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 NHAI	212.00	386.10	09/2007	03/2013	04/2014	13
42	LUCKNOW-RAIBAREILI NHAI	635.90	635.90	07/2012	07/2012	07/2014	24
<u>Telecommunications</u>							
43	GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	930.60	11/2010	11/2012	12/2012	1


Trend and Graphical Analysis of All Projects

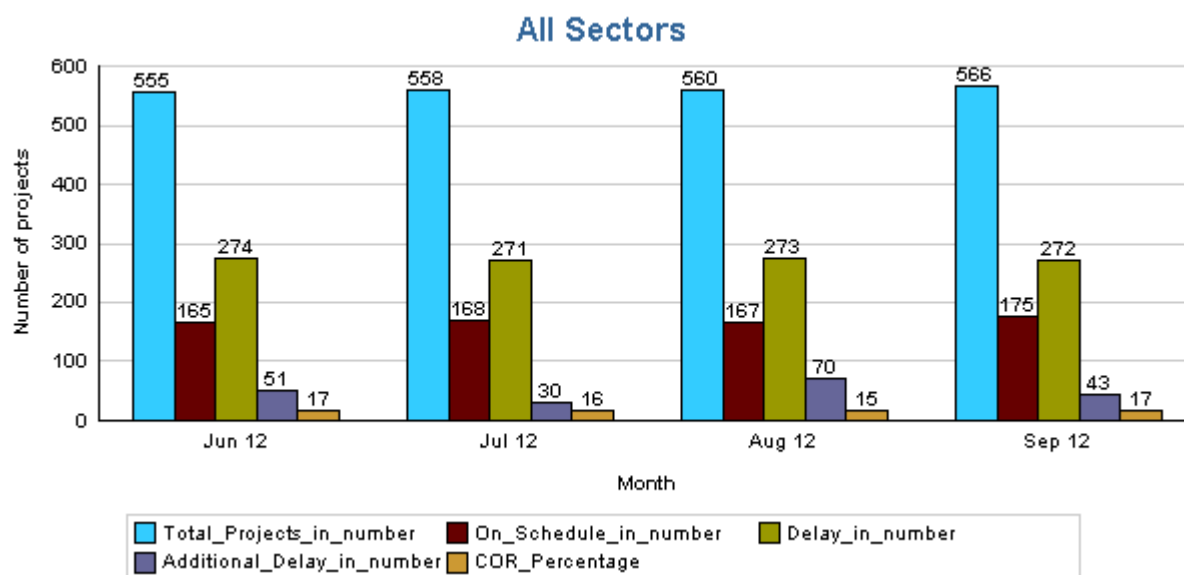


All Sectors Break-up of 272 Delayed projects in September 2012

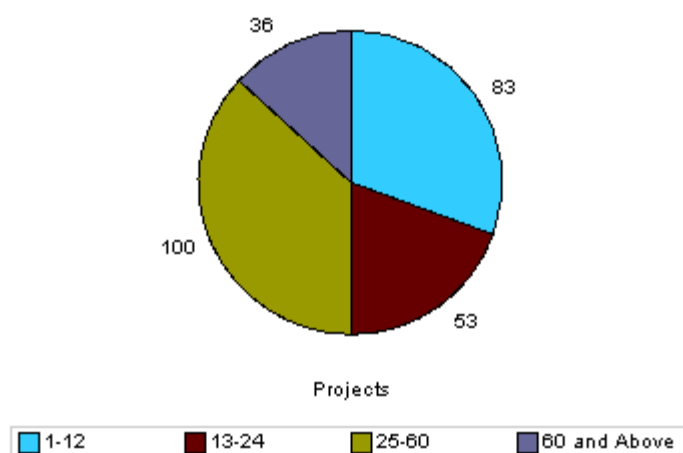


Trend and Graphical Analysis Telecommunications Sector

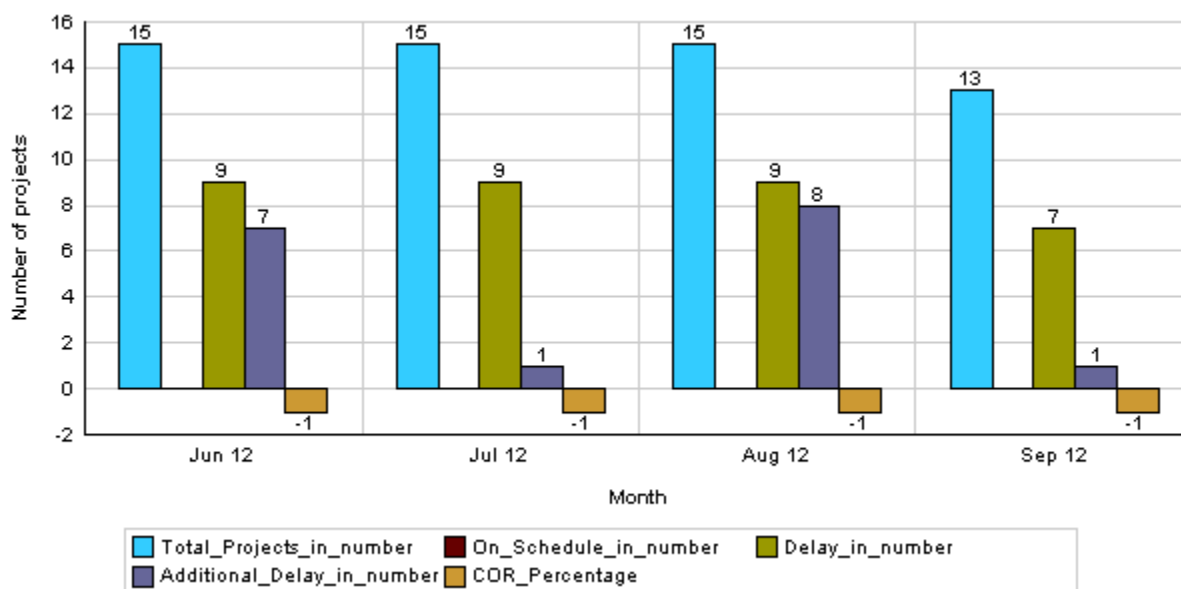


Telecommunications Sector Break-up of 7 Delayed projects in September 2012

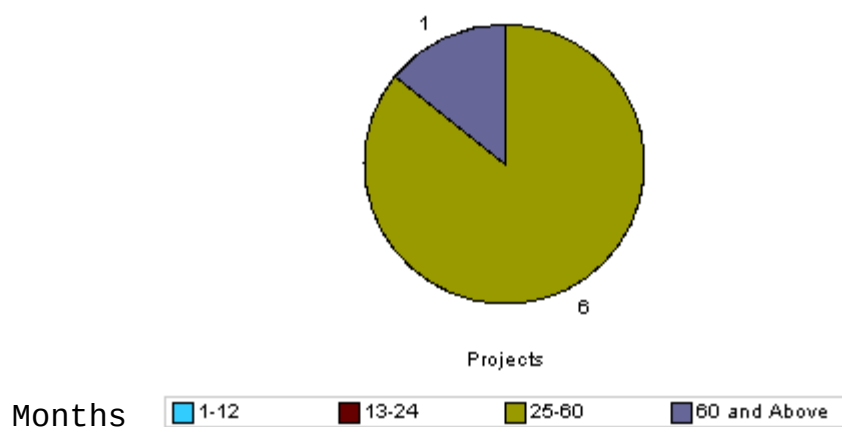


Trend and Graphical Analysis Shipping and Ports Sector

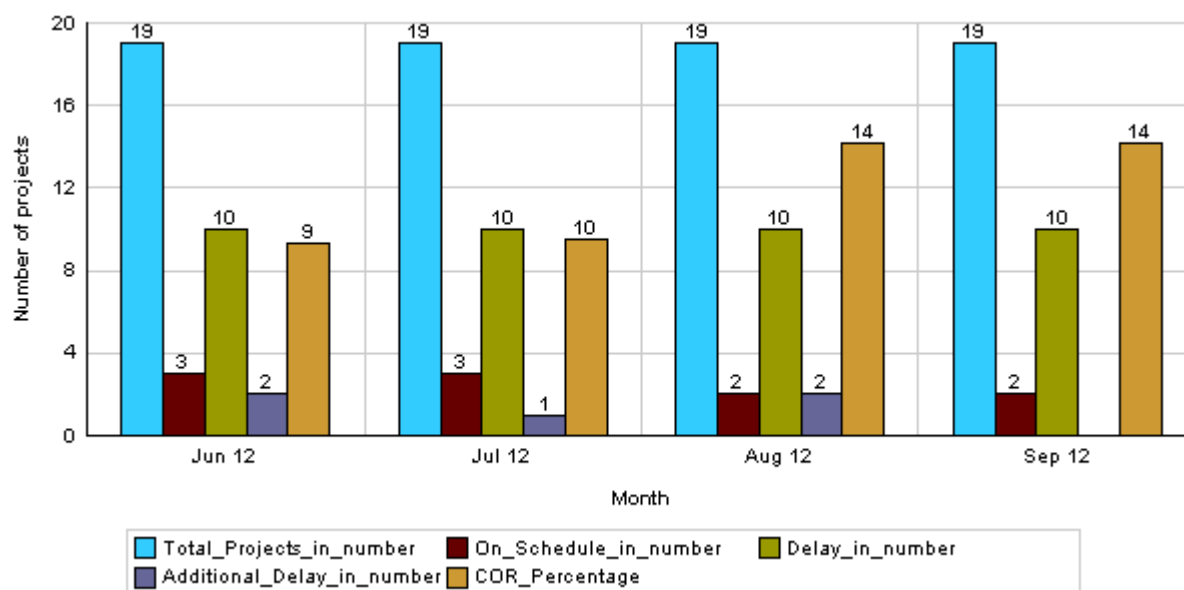


Sector Break-up of 10 Delayed projects in September 2012

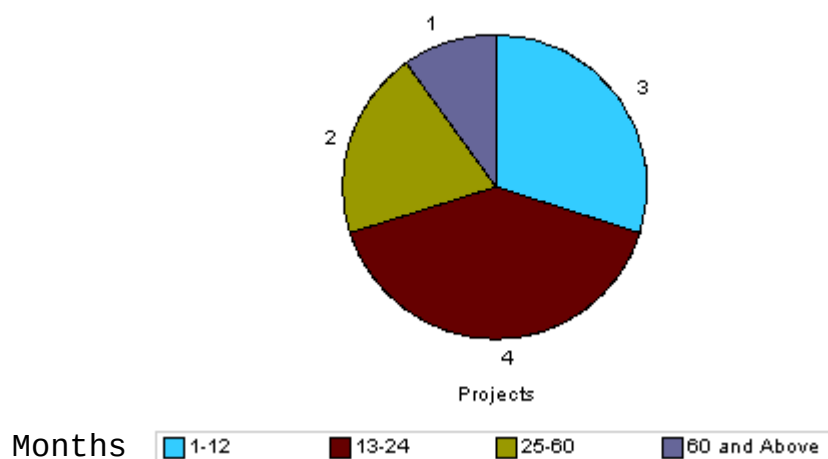

Trend and Graphical Analysis Road Transport and Highways Sector

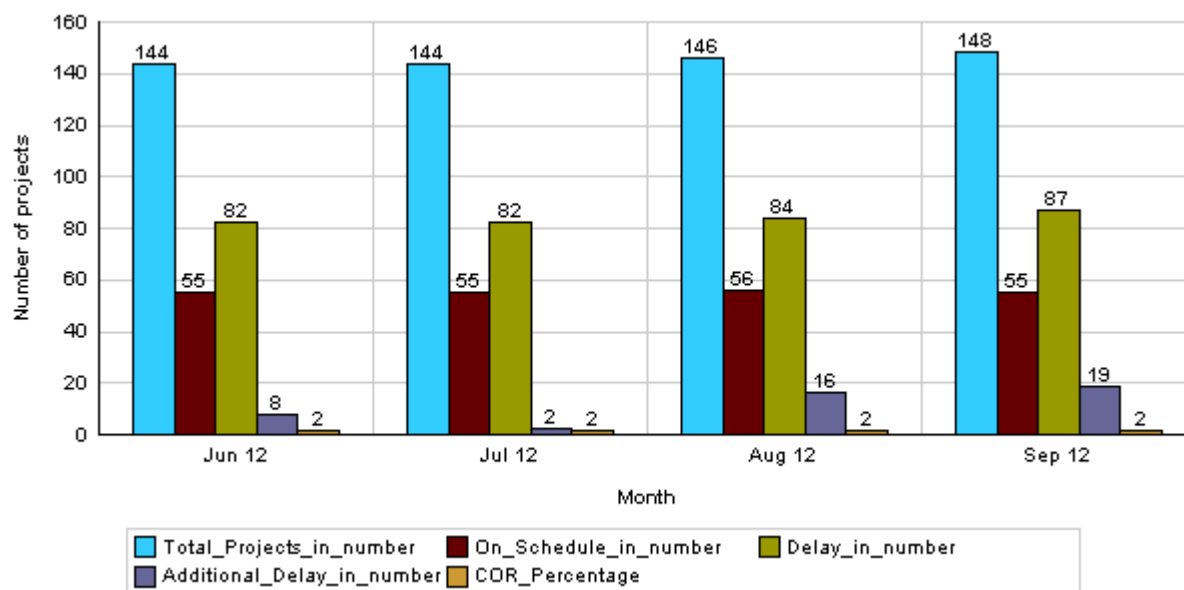


Sector Break-up of 87 Delayed projects in September 2012

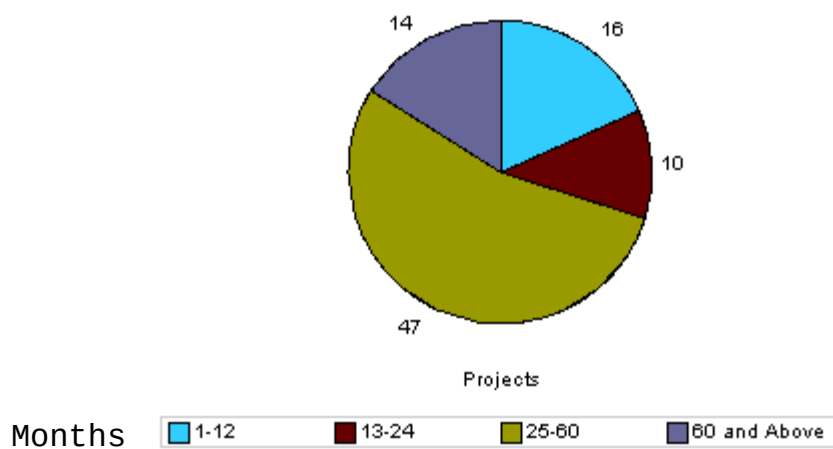


Trend and Graphical Analysis

Railways Sector

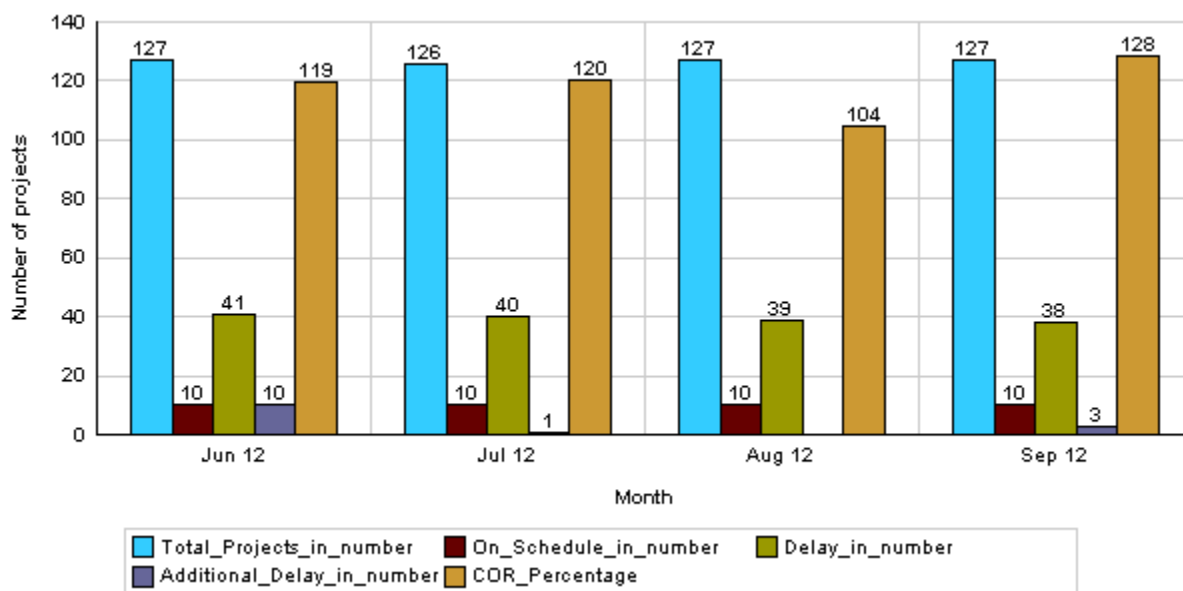


Railways Sector Sector Break-up of 38 Delayed projects in September 2012

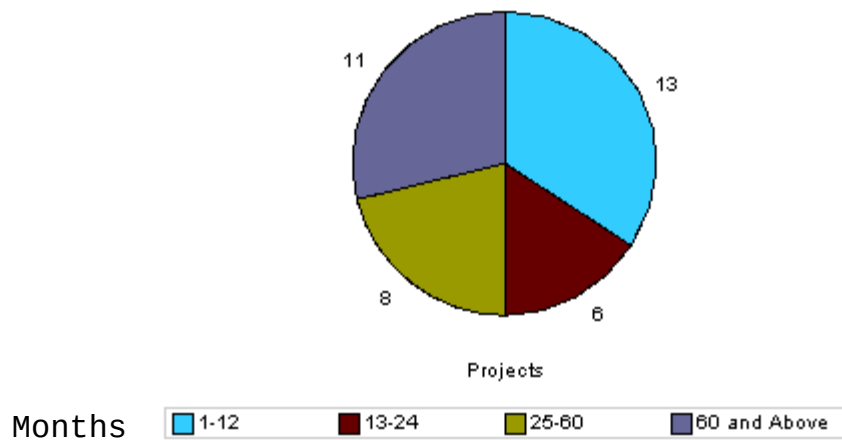


Trend and Graphical Analysis

Power Sector

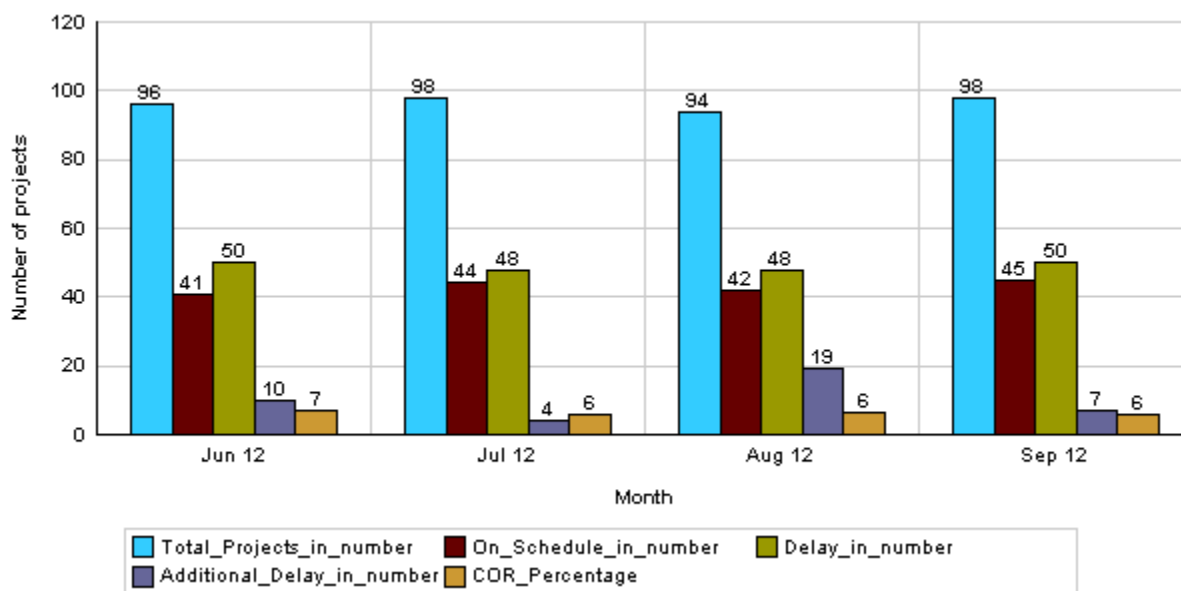


Power Sector Sector Break-up of 50 Delayed projects in September 2012

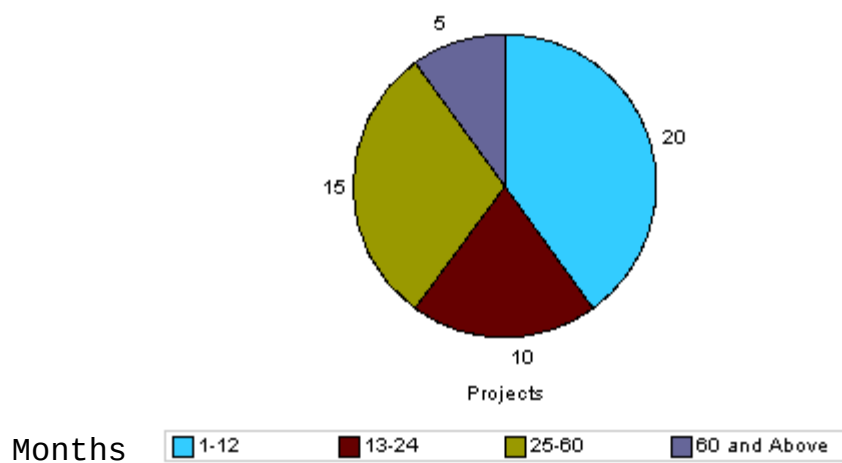


Trend and Graphical Analysis

Petroleum Sector

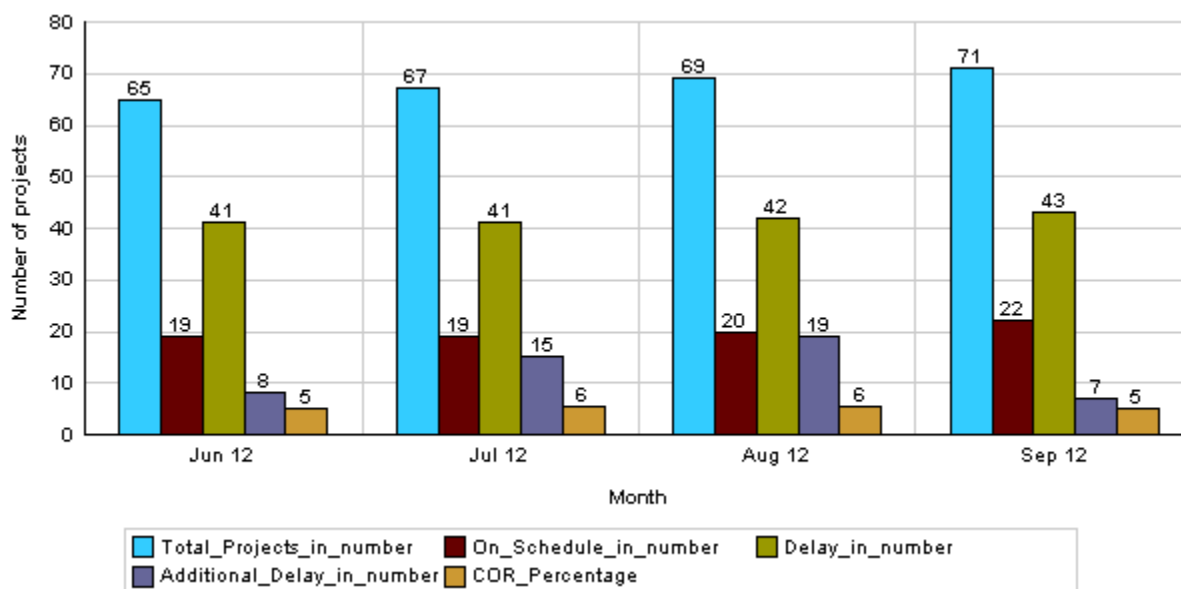


Petroleum Sector Sector Break-up of 43 Delayed projects in September 2012

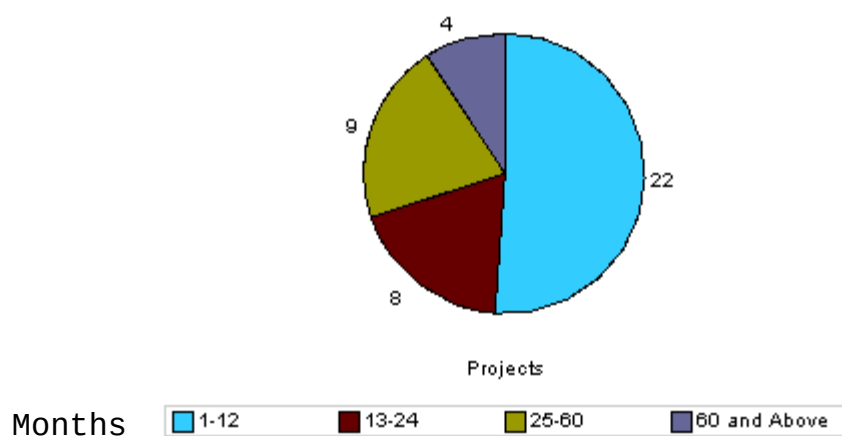


Trend and Graphical Analysis

Steel Sector

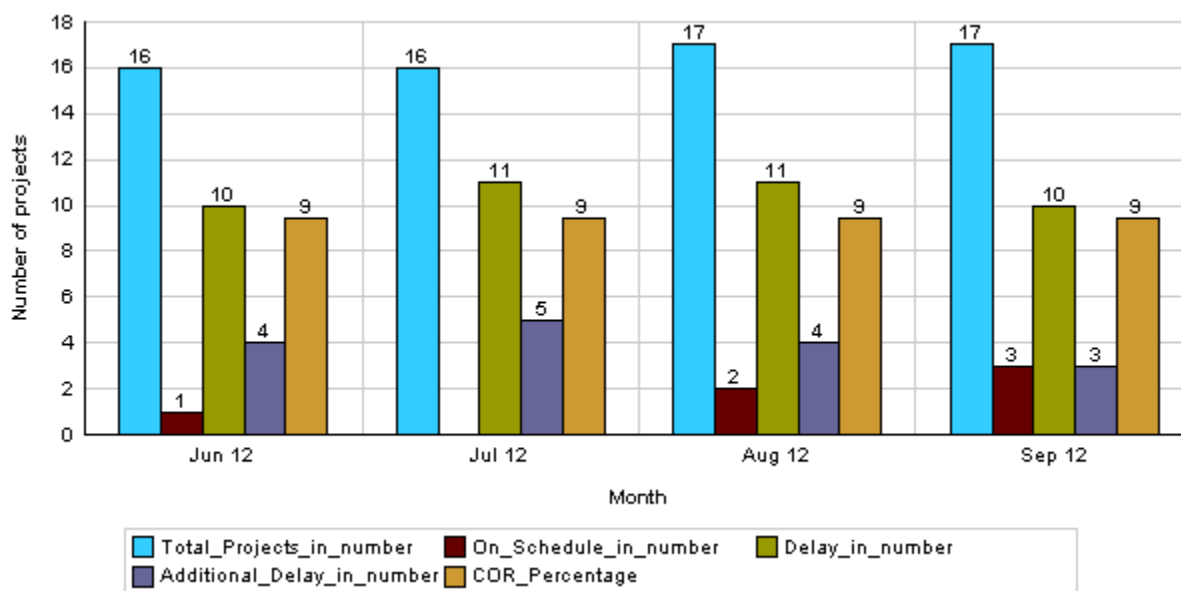


Steel Sector Sector Break-up of 10 Delayed projects in September 2012

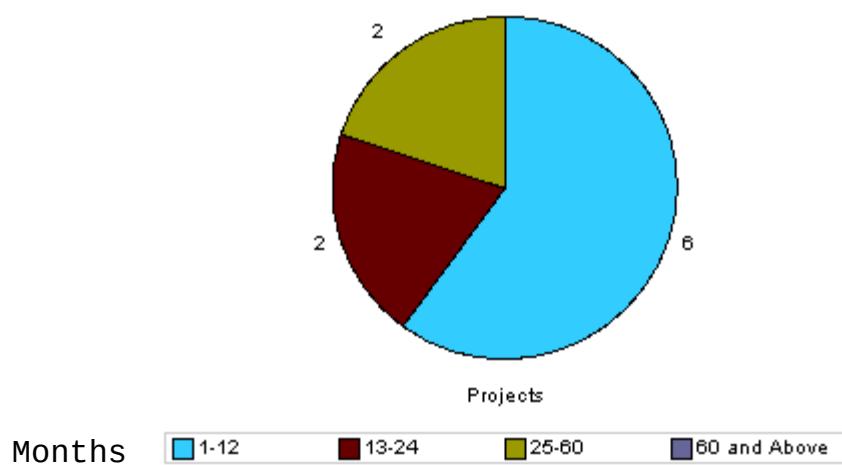


Trend and Graphical Analysis

Fertilisers Sector

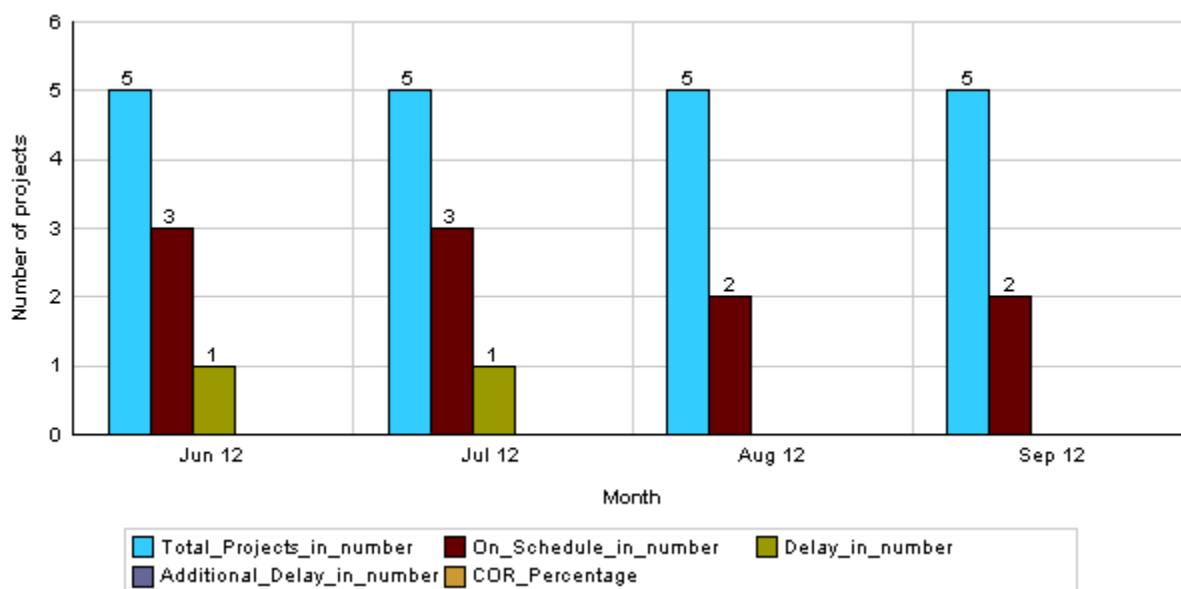


Fertilisers Sector Break-up of 0 Delayed projects in September 2012




Trend and Graphical Analysis

Coal Sector

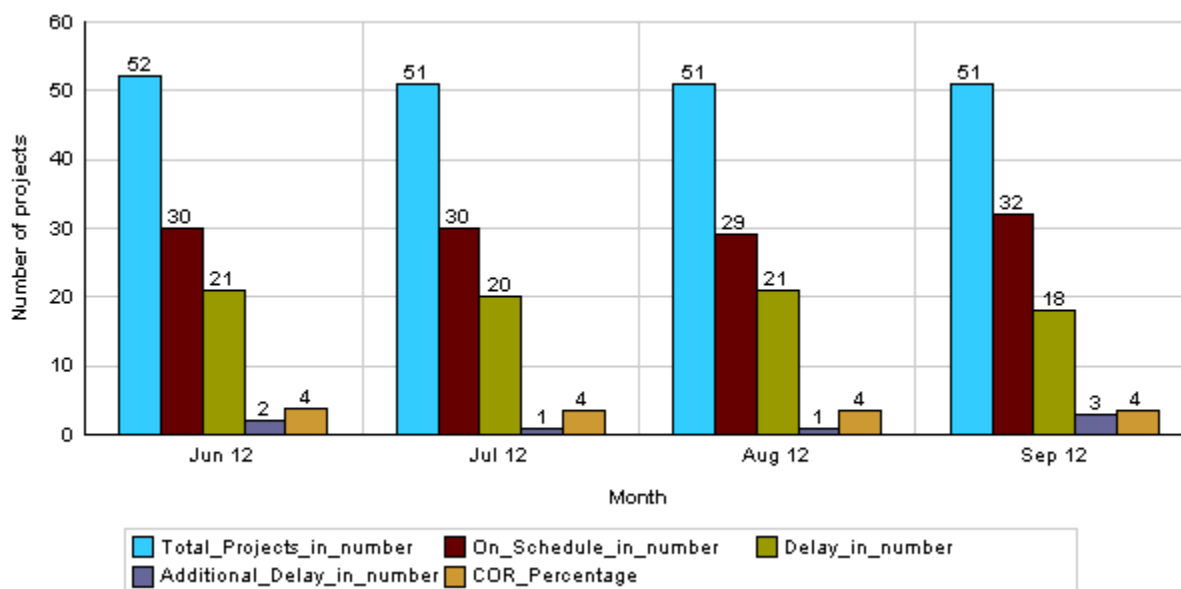


Coal Sector Sector Break-up of 18 Delayed projects in September 2012

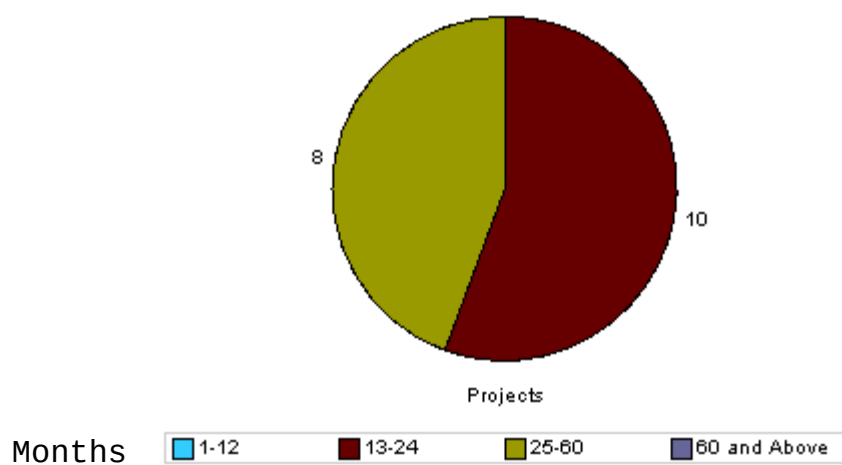


Trend and Graphical Analysis

Civil Aviation Sector

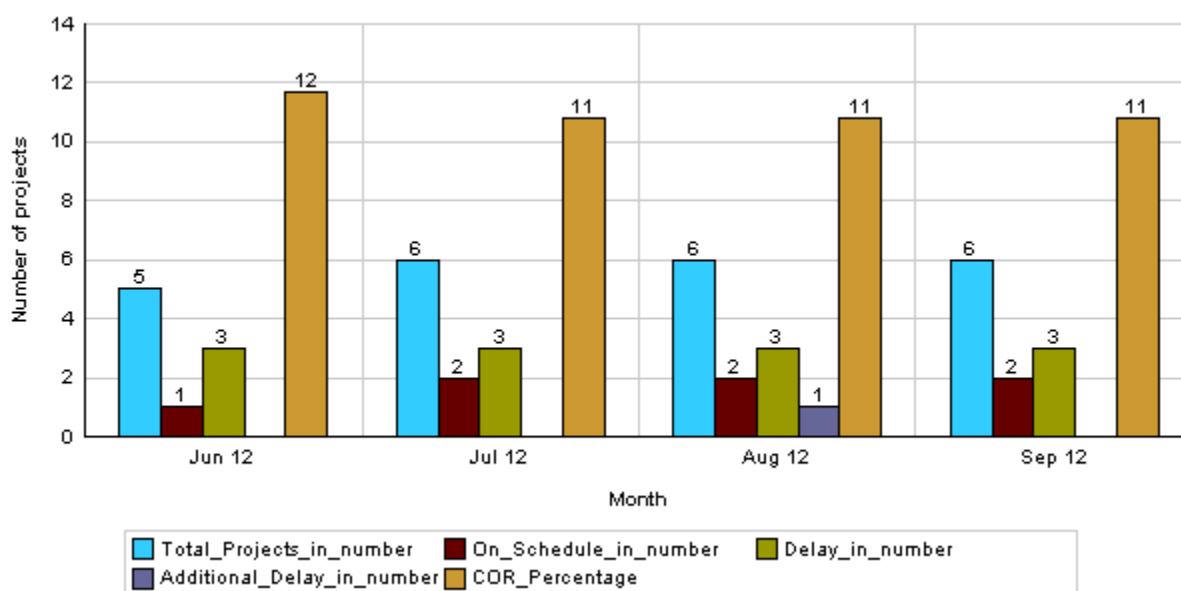


Civil Aviation Sector Break-up of 3 Delayed projects in September 2012

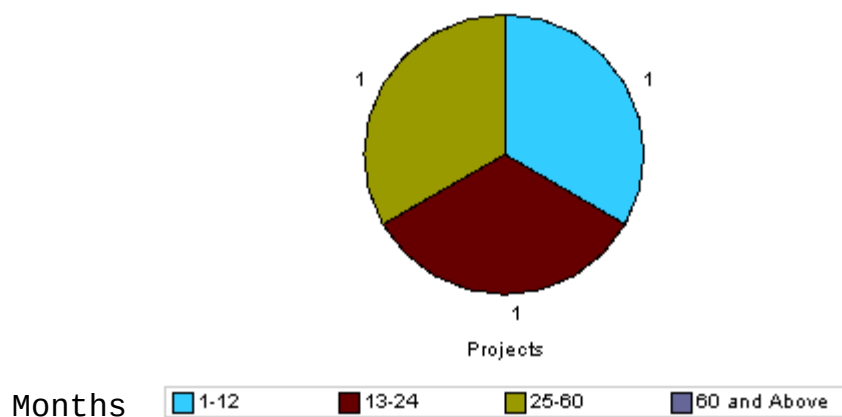


Trend and Graphical Analysis

Atomic Energy Sector

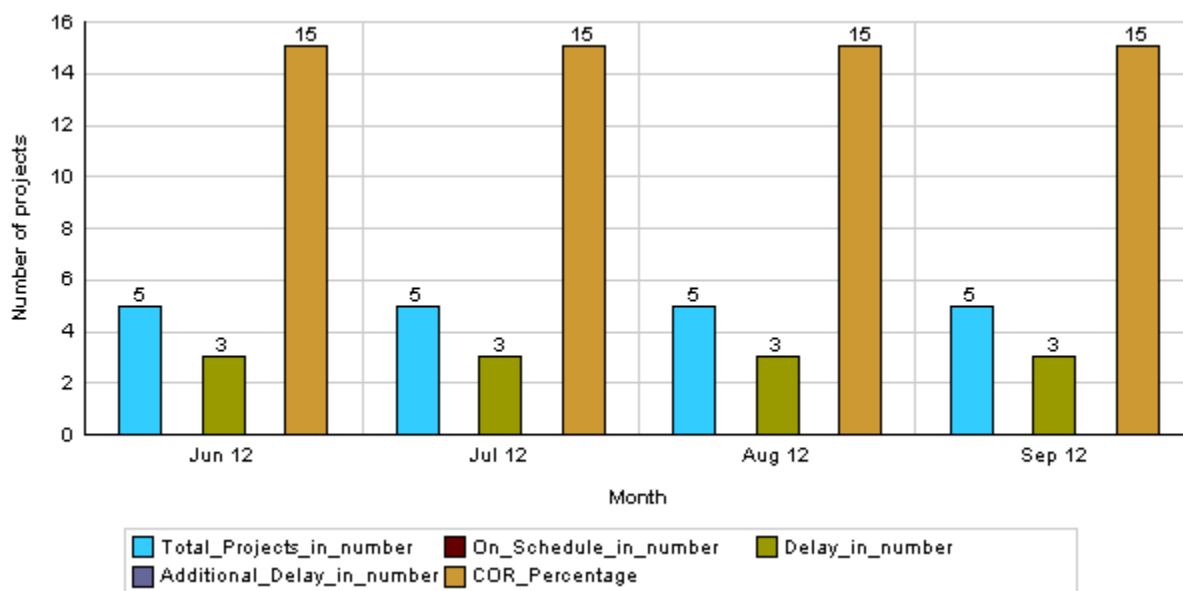


Atomic Energy Sector Sector Break-up of 3 Delayed projects in September 2012

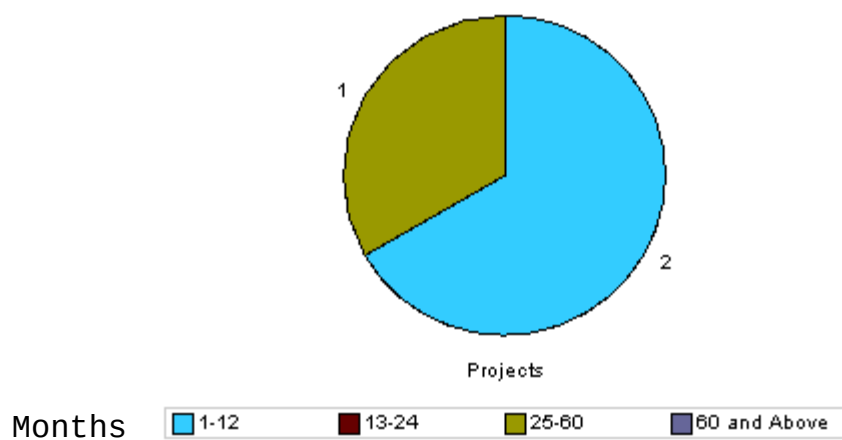


Trend and Graphical Analysis

Urban Development Sector

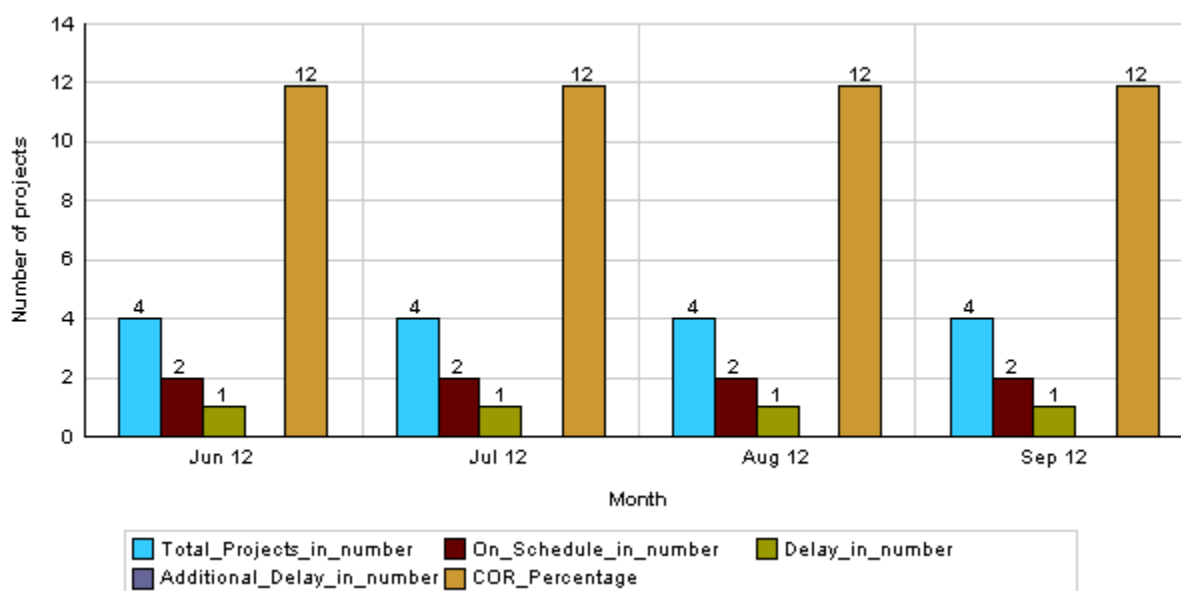

Urban Development Sector Break-up of 1 Delayed projects in September 2012

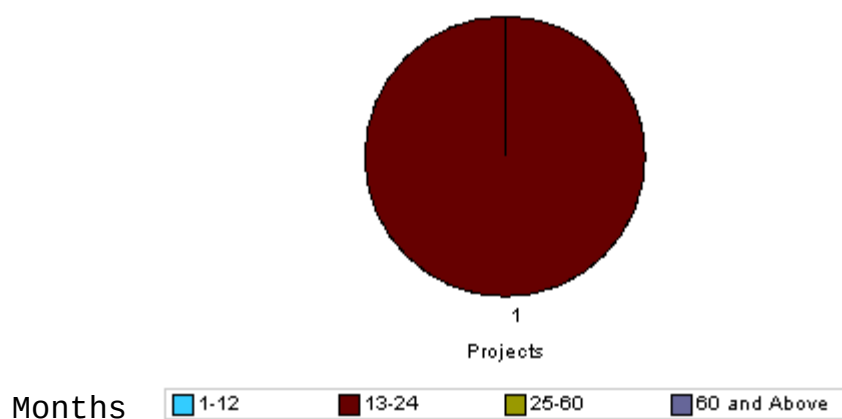

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	23,051.94
Civil Aviation	6	5,473.58	5,680.58	6,063.07	4,499.06
Coal	51	36,056.46	37,022.46	37,312.25	12,889.34
Fertilisers	5	4,828.66	4,828.66	4,828.66	2,875.03
Steel	17	65,285.87	67,562.15	71,443.41	43,661.77
Petrochemicals	1	5,460.61	8,920.00	8,920.00	5,573.34
Petroleum	71	174,773.81	188,226.32	183,290.21	80,925.17
Power	98	231,379.54	235,186.64	245,378.02	104,082.11
Railways	127	64,518.68	94,031.07	147,234.07	63,129.80
Road Transport & Highways	148	94,480.80	94,647.30	96,059.42	66,463.00
Shipping & Ports	19	16,242.52	18,109.64	18,554.09	8,143.40
Telecommunications	13	5,735.48	5,739.36	5,676.27	1,656.61
Urban Development	4	44,245.18	44,304.08	49,518.08	3,247.31
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	566	790,572.38	846,349.45	923,296.84	420,233.37

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,956.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	15,030.00	12/2008 -	03/2013	51(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,782.70	09/2010 -	01/2012	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,199.00	12/2016 -	03/2017	3(O) -	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,084.24	04/2011 04/2011	04/2012	-	0/0
Total			41,548.29 -	47,832.29	23,051.94				47/327
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,123.01	05/2011 03/2012	10/2012	17(O) 7(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	185.20	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	138.65	05/2012 -	12/2012	7(O) -	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,676.63	01/2011 02/2012	02/2012	-	0/0
10	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	452.00	3.36	02/2015 -	02/2015	0(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	372.21	06/2013 -	06/2013	0(O) -	0/0
Total			5,473.58 -	6,063.07	4,499.06				0/0
<u>Coal</u>									
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	779.26	320.46	03/2013 09/2012	10/2014	19(O) 25(R)	7/22
13	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	86.26	03/2016 -	03/2016	0(O) -	2/6

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	365.80	03/2016 03/2016	03/2016	0(O) 0(R)	2/2
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	100.35	03/2012 -	03/2014	24(O) -	5/7
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	12/2007	471.66 341.63	341.63	108.57	03/2011 -	03/2013	24(O) -	0/2
17	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	118.05	03/2010 -	03/2015	60(O) -	4/4
18	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	39.30	03/2016 -	03/2016	0(O) -	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	114.71	03/2017 -	03/2017	0(O) -	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.35	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	535.10	162.06	03/2015 03/2015	03/2015	0(O) 0(R)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	263.68	03/2014 -	03/2014	0(O) -	2/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	08/2007	163.51 -	163.51	34.52	03/2011 -	03/2014	36(O) -	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,226.21	03/2014 -	03/2014	0(O) -	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,386.87	03/2014 -	03/2014	0(O) -	10/15
27	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	70.82	03/2015 -	03/2015	0(O) -	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.63 -	479.63	110.33	03/2013 -	03/2013	0(O) -	5/7
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2015	0(O) -	1/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48(O) -	0/1
33	KAKATIYA LONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	72.12	12/2012 -	03/2015	27(O) -	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	111.49	03/2013 -	03/2013	0(O) -	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	30.89	03/2014 -	03/2014	0(O) -	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O) -	1/6

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	1.51	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	334.36	03/2013 -	03/2013	0(O) -	2/2
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	105.43	03/2010 -	03/2014	48(O) -	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	674.28	03/2013 -	03/2013	0(O) -	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44(O) -	1/2
43	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	204.58	03/2014 -	03/2014	0(O) -	1/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.22	03/2012 -	03/2014	24(O) -	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	23.29	12/2015 -	08/2017	20(O) -	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36(O) -	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	60.69	03/2012 -	03/2014	24(O) -	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.83	03/2014 -	03/2016	24(O) -	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	87.89	03/2013 -	03/2013	0(O) -	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	09/2009	153.82 -	153.82	24.39	03/2014 -	03/2014	0(O) -	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	95.86	03/2012 -	03/2014	24(O) -	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	27.24	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016	0(O) -	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	48.14	03/2012 -	-	-	11/42

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72 -	447.72	44.49	03/2016 -	03/2016	0(O) -	1/12
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,480.61	06/2009 -	03/2013	45(O) -	19/24
61	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	3,462.05	03/2012 -	03/2014	24(O) -	0/39
62	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	106.60	03/2012 -	03/2014	24(O) -	0/2
	Total		36,056.46 -	37,312.25	12,889.34				166/634
Fertilisers									
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	769.00	01/2013 -	01/2013	0(O) -	0/5
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya Pradesh	09/2008	438.00 -	438.00	239.93	07/2011 -	07/2012	-	0/0
65	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya Pradesh	09/2008	325.00 -	325.00	185.10	07/2011 -	04/2012	-	0/0
66	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	890.00	01/2013 12/2012	12/2012	-1(O) 0(R)	8/8
67	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	791.00	01/2013 -	01/2013	0(O) -	0/5
	Total		4,828.66 -	4,828.66	2,875.03				8/18
Steel									
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	170.48	- -	04/2013	- -	13/19
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	248.87	08/2010 -	11/2012	27(O) -	0/1
70	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	252.46	02/2011 -	12/2012	22(O) -	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	124.37	- -	05/2013	- -	11/21
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	220.32	05/2012 -	02/2013	9(O) -	1/2
73	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	340.39	12/2011 03/2012	01/2013	13(O) 10(R)	16/21

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	105.86	10/2012 -	12/2012	2(O) -	3/4
75	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh - [N12000078]SAIL, Delhi	07/2012	332.65 -	332.65	-	08/2014 -	08/2014	0(O) -	0/0
76	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL, Orissa	11/2011	254.55 -	254.55	11.51	11/2013 -	11/2013	0(O) -	1/1
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhattisgarh	09/2008	17,265.00 -	17,265.00	6,606.80	03/2013 -	09/2013	6(O) -	20/27
78	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00 -	6,325.00	3,007.61	12/2011 -	12/2012	12(O) -	10/16
79	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	1,127.86	12/2012 -	03/2013	3(O) -	7/12
80	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,785.94	12/2011 -	12/2012	12(O) -	16/19
81	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	9,787.70	10/2009 -	03/2013	41(O) -	62/64
82	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Orissa	09/2008	11,812.00 11,812.00	11,812.00	7,871.60	11/2013 -	03/2013	-8(O) -	8/14
83	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL, Maharashtra	12/2011	187.33 -	187.33	-	- -	12/2013	- -	0/1
84	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]SAIL, Delhi	01/2012	254.90 -	254.90	-	12/2014 -	12/2014	0(O) -	0/0
Total			65,285.87 -	71,443.41	43,661.77				170/225
Petrochemicals									
85	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	5,573.34	04/2012 12/2013	12/2013	20(O) 0(R)	13/29
Total			5,460.61 -	8,920.00	5,573.34				13/29
Petroleum									
86	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	10/2013	16(O) -	0/0
87	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	1,147.97	06/2012 -	06/2013	12(O) -	0/0
88	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	254.36	04/2011 -	10/2012	18(O) -	0/0
89	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	521.52	12/2011 -	01/2013	13(O) -	0/0
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	938.59	03/2013 -	03/2014	12(O) -	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
91	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	614.17	12/2014 -	12/2014	0(O) -	0/0
92	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014	0(O) -	0/0
93	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	252.30	07/2012 07/2012	06/2013	11(O) 11(R)	0/16
94	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]OCL,Haryana	11/2009	341.50 -	341.50	135.26	02/2013 -	02/2013	0(O) -	38/42
95	Butene-1 at Panipat - [N16000139]OCL,Haryana	02/2012	190.00 -	190.00	12.11	03/2014 -	03/2014	0(O) -	0/0
96	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	194.01	- -	09/2012	- -	36/36
97	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	739.84	04/2011 12/2011	10/2012	18(O) 10(R)	2/2
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.25	09/2011 -	08/2013	23(O) -	0/0
99	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,570.72	05/2010 05/2012	10/2012	29(O) 5(R)	0/0
100	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	368.23	- 08/2011	-	-	0/22
101	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	0.20	01/2014 -	01/2014	0(O) -	0/0
102	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	17.54	05/2013 -	05/2013	0(O) -	0/0
103	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5(O) -	0/0
104	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	43.73	09/2012 -	09/2013	12(O) -	0/0
105	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
106	Construction of tanks and blending facility at Vad - [N16000115]OCL,Gujarat	02/2009	267.00 -	267.00	211.53	09/2012 09/2012	09/2012	0(O) 0(R)	0/0
107	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,905.39	03/2012 08/2012	12/2012	9(O) 4(R)	0/17
108	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00 -	1,584.00	26.33	- -	-	-	0/0
109	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86(O) 12(R)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,777.01	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
111	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
112	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
113	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
114	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,203.81	09/2011 09/2012	09/2012	12(O) 0(R)	0/76
115	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,352.39	09/2011 03/2012	11/2012	14(O) 8(R)	0/0
116	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	75.58	03/2013 -	04/2013	1(O) -	0/0
117	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
118	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	427.67	03/2013 -	04/2014	13(O) -	0/0
119	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	43.99	11/2012 -	10/2013	11(O) -	0/0
120	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	187.77	01/2014 -	01/2014	0(O) -	0/0
121	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
122	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,951.99	- -	10/2012	- -	114/116
123	Fire water network at Uran - [N16000141]ONGC,Maharashtra	05/2010	171.68 -	171.68	2.40	06/2013 -	11/2013	5(O) -	0/0
124	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	199.82	01/2013 -	06/2013	5(O) -	18/18
125	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	611.55	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
126	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015	0(O) -	0/0
127	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,164.58	06/2012 03/2013	03/2013	9(O) 0(R)	8/8
128	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,535.20	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
129	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	629.66	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
130	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	03/2014	0(O) -	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	269.29	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
132	IREP - [N16000143]BPCL, Kerala	01/1999	14,225.00	14,225.00	30.11	12/2015	12/2015	0(O)	0/0
133	Integrated Development of B-127 fields - [N16000131]ONGC, Maharashtra	12/2011	2,059.63	2,059.63	-	03/2015	03/2015	0(O)	0/0
134	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18	7,596.18	2.54	01/2013	07/2015	30(O)	0/0
135	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07	281.07	3.48	10/2010	12/2014	50(O)	0/0
136	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL, Multi State	07/2009	238.68 312.00	312.00	250.81	01/2012 01/2012	11/2012	10(O) 10(R)	0/1
137	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL, Multi State	06/2009	2,915.00	2,915.00	1,059.76	12/2012 12/2012	12/2013	12(O) 12(R)	0/21
138	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL, Multi State	06/2009	348.00	261.00	198.79	03/2012 08/2012	09/2012	6(O) 1(R)	2/4
139	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 12,160.26	12,160.26	9,228.42	01/2012	11/2012	10(O)	0/95
140	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39	6,855.93	4,258.26	09/2012	09/2013	12(O)	0/0
141	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.38	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
142	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00	3,823.00	701.81	04/2015	04/2015	0(O)	0/0
143	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24(O) 22(R)	0/0
144	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02	740.02	514.86	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
145	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00	30,426.00	18,078.00	11/2012 09/2013	09/2013	10(O) 0(R)	60/100
146	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, Multi State	08/2009	1,793.00	1,793.00	691.16	09/2012	09/2012	0(O)	0/11
147	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00	8,140.00	1,813.56	02/2014	02/2014	0(O)	0/0
148	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL, Maharashtra	08/2009	246.81	246.81	184.00	04/2012	-	-	0/0
149	Pipeline Replacement Project-3 - [N16000137]ONGC, Multi State	04/2012	2,547.26	1,417.00	-	05/2014	05/2014	0(O)	0/0
150	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78	1,803.78	620.97	07/2012	04/2013	9(O)	0/31

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	898.00	905.36	- 03/2012	08/2012	-	0/53
152	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	5.96	12/2014 -	12/2014	0(O) -	0/0
153	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016	0(O) -	0/0
154	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012 -	03/2013	7(O) -	0/0
155	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	220.63	03/2012 -	10/2012	7(O) -	13/20
156	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	73.04	12/2013 12/2013	12/2013	0(O) 0(R)	0/0
Total			174,773.81 -	183,290.21	80,925.17				306/871
Power									
157	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,380.80	08/2012 -	03/2013	7(O) -	0/11
158	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,091.10	02/2012 -	11/2012	9(O) -	0/7
159	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	654.70	05/2012 -	12/2012	7(O) -	0/11
160	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,029.30	06/2012 -	11/2012	5(O) -	0/4
161	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,633.00	08/2013 -	09/2014	13(O) -	5/19
162	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,417.00	12/2009 12/2014	03/2016	75(O) 15(R)	26/47
163	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,325.00	07/2011 -	11/2014	40(O) -	4/28
164	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.00	754.57	02/2011 10/2012	10/2012	20(O) 0(R)	2/4
165	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	257.90	08/2014 -	08/2014	0(O) -	0/20
166	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	22.30	06/2014 -	06/2014	0(O) -	0/20

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	297.90	09/2014 -	09/2014	0(O) -	0/20
168	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	867.25	10/2009 -	03/2013	41(O) -	20/20
169	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	422.50	11/2012 -	03/2014	16(O) -	3/11
170	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
171	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	416.60	05/2014 -	05/2014	0(O) -	0/16
172	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	653.90	08/2013 -	08/2013	0(O) -	0/14
173	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	60.60	08/2014 -	08/2014	0(O) -	0/21
174	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	415.40	12/2013 -	12/2013	0(O) -	0/13
175	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	52.40	10/2012 -	03/2013	5(O) -	0/15
176	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	844.73	12/2007 12/2009	-	-	0/10
177	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,973.46	05/2013 06/2016	03/2017	46(O) 9(R)	4/22
178	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,689.17	01/2016 01/2016	11/2016	10(O) 10(R)	0/2
179	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,495.00	04/2009 03/2014	03/2014	59(O) 0(R)	0/9
180	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	987.00	12/2016 -	12/2016	0(O) -	0/0
181	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,840.51	09/2008 -	03/2013	54(O) -	17/37
182	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,456.00	08/2012 -	03/2013	7(O) -	10/16
183	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	564.00	09/2016 -	09/2016	0(O) -	0/0
184	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	794.58	08/2010 01/2013	01/2013	29(O) 0(R)	0/3
185	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,078.60	08/2013 -	09/2014	13(O) -	0/17

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	242.50	02/2012 -	12/2013	22(O) -	0/14
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	318.00	11/2011 -	12/2013	25(O) -	0/11
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	341.90	11/2011 -	12/2013	25(O) -	0/14
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	74.80	01/2013 -	01/2013	0(O) -	0/7
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	208.00	07/2013 -	07/2013	0(O) -	0/12
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	541.10	04/2013 -	10/2013	6(O) -	0/12
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	74.80	08/2013 -	08/2013	0(O) -	0/16
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	43.20	11/2014 -	11/2014	0(O) -	0/0
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	-	03/2015 -	03/2015	0(O) -	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	-	04/2015 -	04/2015	0(O) -	0/0
196	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	444.20	11/2012 -	03/2013	4(O) -	0/10
197	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,912.00	10/2010 01/2013	06/2013	32(O) 5(R)	0/0
198	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,554.41	09/2009 07/2014	12/2017	99(O) 41(R)	1/20
199	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	396.44	08/2012 08/2013	09/2014	25(O) 13(R)	14/21
200	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,948.02	01/2012 -	09/2013	20(O) -	0/0
201	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,567.00	10/2012 -	05/2013	7(O) -	10/16
202	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	760.00	11/2016 -	11/2016	0(O) -	0/0
203	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,761.64	09/2010 08/2014	03/2017	78(O) 31(R)	11/11
204	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	49.20	04/2013 -	04/2013	0(O) -	0/15

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
205	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,976.70	08/2012 -	03/2013	7(O) -	0/7
206	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2015	12(O) -	0/0
207	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/0
208	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	50.40	08/2014 -	08/2014	0(O) -	0/20
209	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	104.70	02/2015 -	02/2015	0(O) -	0/0
210	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	52.80	11/2014 -	11/2014	0(O) -	0/0
211	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	125.40	01/2015 -	01/2015	0(O) -	0/19
212	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	22.90	08/2014 -	08/2014	0(O) -	0/20
213	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	61.30	06/2014 -	06/2014	0(O) -	0/19
214	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	158.70	04/2012 -	10/2012	6(O) -	0/0
215	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	124.08	06/2012 -	10/2012	4(O) -	0/9
216	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	759.10	08/2012 -	12/2013	16(O) -	0/11
217	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,561.00	- -	09/2015	- -	2/14
218	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,194.26	09/2009 06/2013	10/2013	49(O) 4(R)	0/0
219	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,563.13	03/2007 09/2012	02/2013	71(O) 5(R)	25/25
220	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	376.32	07/2010 02/2016	02/2016	67(O) 0(R)	1/10
221	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	16.40	01/2014 -	01/2014	0(O) -	0/17

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	73.20	08/2014 -	08/2014	0(O) -	0/0
223	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	60.10	10/2014 -	10/2014	0(O) -	0/21
224	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	329.43	07/2011 -	11/2012	16(O) -	0/5
225	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,947.70	10/2012 -	09/2013	11(O) -	0/12
226	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	335.30	01/2015 -	01/2015	0(O) -	0/20
227	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	681.50	03/2014 -	03/2014	0(O) -	0/15
228	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	555.00	08/2013 -	08/2013	0(O) -	0/14
229	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	2.10	08/2014 -	08/2014	0(O) -	0/20
230	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	34.10	10/2014 -	10/2014	0(O) -	0/20
231	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	590.80	01/2010 -	02/2013	37(O) -	0/22
232	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	151.30	11/2011 -	03/2013	16(O) -	0/7
233	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	3,920.00	12/2012 -	12/2012	0(O) -	0/11
234	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	67.20	02/2014 -	02/2014	0(O) -	0/20
235	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	99.50	10/2013 -	10/2013	0(O) -	0/18
236	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	49.80	07/2013 -	07/2013	0(O) -	0/0
237	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	250.30	12/2013 -	12/2013	0(O) -	0/18

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	71.90	11/2013 -	11/2013	0(O) -	0/20
239	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	679.60	03/2013 -	03/2013	0(O) -	0/14
240	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	861.00	12/2013 -	12/2013	0(O) -	0/13
241	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,587.00	11/2012 -	06/2013	7(O) -	0/15
242	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	240.00	07/2014 -	07/2014	0(O) -	0/19
243	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	343.96	- 07/2013	07/2013	- 0(R)	6/29
244	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	349.99	07/2014 -	02/2015	7(O) -	0/16
245	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	917.70	12/2012 -	12/2013	12(O) -	0/11
246	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	404.30	11/2013 -	11/2013	0(O) -	0/15
247	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	58.40	01/2013 -	11/2013	10(O) -	0/16
248	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,081.00	1,787.44	11/2009 02/2013	03/2013	40(O) 1(R)	0/4
249	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	-	08/2015 -	08/2015	0(O) -	0/0
250	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,857.00	10/2012 -	03/2013	5(O) -	9/15
251	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	319.72	07/2014 -	05/2016	22(O) -	1/3
252	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,157.30	07/2010 -	12/2012	29(O) -	20/20
253	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	412.10	09/2010 -	03/2013	30(O) -	0/9
254	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	27.70	06/2015 -	06/2015	0(O) -	0/24

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		231,379.54	245,378.02	104,082.11				191/1233
			-						
	<u>Railways</u>								
255	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura	04/2008	813.34 813.34	1,141.75	426.35	03/2014 -	03/2014	0(O) -	0/0
256	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	03/2011	-	0/0
257	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 1,010.00	2,820.00	179.58	- -	03/2013	- -	0/0
258	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	453.04	392.85	03/2011 03/2011	03/2011	-	0/0
259	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	548.95	538.65	06/1999 03/2011	03/2011	-	0/0
260	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
261	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR, Gujarat	04/2008	394.14 385.60	404.39	3.77	03/2013 -	03/2013	0(O) -	0/0
262	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 901.62	901.62	0.29	- -	-	-	0/0
263	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	1,412.74	451.90	03/2005 12/2008	06/2016	135(O) 90(R)	0/0
264	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	1,106.62	207.07	12/2010 03/2011	03/2011	-	0/0
265	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, Maharashtra	03/1996	401.81 495.44	495.44	204.17	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
266	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 619.34	2,393.48	12.87	04/2014 -	03/2015	11(O) -	0/0
267	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya pradesh	09/2007	687.20 -	687.20	667.39	03/2010 -	12/2012	33(O) -	0/0
268	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	350.00	324.53	- 03/2009	03/2011	-	0/0
269	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	3,230.02	2,501.02	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
270	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52 207.52	207.52	145.89	12/2012 -	05/2013	5(O) -	0/0
271	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36 196.95	196.95	192.41	03/2011 -	-	-	0/0
272	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR, Gujarat	04/2008	318.24 -	468.62	1.00	03/2012 -	-	-	0/0
273	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
274	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR), Punjab	07/1998	248.44 576.27	1,115.21	897.49	12/2012 01/2013	01/2013	1(O) 0(R)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
276	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya Pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
277	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2013	06/2013	0(O) 0(R)	0/0
278	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	415.73	279.98	- -	12/2012	- -	0/0
279	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
280	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	78.91	- -	-	-	0/0
281	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	197.85	- -	03/2013	- -	0/0
282	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	420.44	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
283	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	559.19	- -	12/2012	- -	0/0
284	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	89.02	12/2011 02/2012	02/2012	-	0/0
285	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0
286	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
287	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	163.86	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
288	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
289	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.85	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
290	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	77.69	02/2006 -	-	-	0/0
291	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	587.54	- -	03/2012	-	0/0
292	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
293	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	345.31	- 05/2009	05/2009	-	0/0
294	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	108.12	12/2011 11/2013	11/2013	23(O) 0(R)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
295	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	181.87	- -	-	-	0/0
296	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	221.17	- 09/2009	-	-	0/0
297	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
298	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	530.46	- -	01/2013	- -	0/0
299	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	146.31	- -	03/2014	- -	0/0
300	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	169.68	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
301	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	69.70	- -	-	-	0/0
302	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	4.25	03/2015 -	03/2015	0(O) -	0/0
303	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.75	835.55	06/2007 -	06/2007	-	0/0
304	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	661.92	03/2012 08/2012	02/2013	11(O) 6(R)	0/0
305	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	425.36	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
306	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	937.59	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
307	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	211.26	03/2014 -	03/2014	0(O) -	0/0
308	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	339.00	221.13	03/2012 03/2012	10/2012	7(O) 7(R)	0/0
309	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,364.05	- -	03/2012	-	0/0
310	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	502.15	- -	03/2014	- -	1/1
311	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	732.14	- -	10/2012	- -	0/0
312	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	732.83	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
313	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	95.47	- -	03/2013	- -	0/0
314	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	213.62	03/2009 03/2009	04/2013	49(O) 49(R)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
315	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	235.89	- -	03/2013	- -	0/0
316	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
317	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	768.87	415.19	- 03/2010	03/2010	-	0/0
318	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	2,957.21	1,254.61	07/2005 -	-	-	0/0
319	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	120.30	- -	-	-	0/0
320	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	272.94	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
321	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
322	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	335.93	- -	03/2011	-	0/0
323	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	114.08	12/2012 -	03/2014	15(O) -	0/0
324	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	03/2011	-	0/0
325	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	-	0/0
326	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	204.65	03/2002 -	01/2013	130(O) -	0/0
327	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,195.95	03/2009 -	12/2013	57(O) -	0/0
328	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
329	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	263.79	- -	02/2013	-	0/0
330	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	565.12	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
331	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
332	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	395.87	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
333	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	900.00	260.55	- -	-	-	0/0
334	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,334.00	06/2011 03/2012	03/2012	-	0/0
335	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	851.16	03/2014 03/2016	03/2016	24(O) 0(R)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	135.22	- -	03/2012	-	0/0
337	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	632.79	02/2009 -	03/2012	-	0/0
338	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	352.01	07/2012 -	-	-	0/0
339	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	39.45	- -	-	-	0/0
340	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	114.85	- -	03/2014	- -	0/0
341	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,298.65	12/2008 -	03/2014	63(O) -	0/0
342	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.39	- -	03/2015	- -	0/0
343	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2015	0(O) -	0/0
344	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,913.51	159.50	03/2016 -	03/2016	0(O) -	0/0
345	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	36.41	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
346	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	26.54	03/2016 -	03/2016	0(O) -	0/0
347	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	24.50	03/2016 -	06/2016	3(O) -	0/0
348	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	443.39	03/2008 06/2008	-	-	0/0
349	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	355.00	405.53	03/2009 12/2009	03/2011	-	0/0
350	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	246.28	02/2010 -	-	-	0/0
351	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,514.74	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
352	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	589.35	- -	03/2012	-	0/0
353	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	137.07	12/2010 12/2010	12/2010	-	0/0
354	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	764.60	- -	03/2013	- -	0/6

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	233.88	12/2007 03/2010	12/2010	-	0/0
356	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	792.32	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
357	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
358	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13 727.13	1,225.00	232.01	- -	-	-	0/0
359	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	301.82	06/2004 -	12/2012	102(O) -	0/0
360	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,476.55	- -	03/2013	- -	0/0
361	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	356.60	04/2003 03/2010	-	-	0/0
362	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	602.00	494.36	02/2010 02/2011	02/2011	-	0/0
363	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	174.53	03/1998 08/2005	08/2005	-	0/0
364	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	401.19	03/2013 -	03/2014	12(O) -	0/0
365	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya Pradesh	04/2008	603.04 603.04	603.04	101.40	03/2012 -	03/2013	12(O) -	0/0
366	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	227.88	03/2010 -	03/2012	-	0/0
367	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015	0(O) -	0/0
368	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	818.29	74.17	02/2015 -	-	-	0/0
369	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	284.17	03/2014 -	03/2014	0(O) -	0/0
370	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	114.24	- -	03/2013	- -	0/0
371	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	427.98	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
372	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	530.19	- 12/2009	02/2012	-	0/0
373	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	135.54	- -	-	-	0/0
374	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	38.66	- -	-	-	0/0
375	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	548.96	510.29	- -	-	-	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
376	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	3,176.10	3,219.06	12/2006 08/2010	08/2010	-	0/0
377	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 167.73	167.73	48.02	03/2012 -	03/2012	-	0/0
378	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 2,500.00	20,000.00	8,069.06	03/2001 -	12/2017	201(O) -	0/0
379	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00 325.00	820.40	158.14	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
380	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62 -	1,389.62	366.00	03/2014 -	03/2013	-12(O) -	0/0
381	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	356.87	170.48	- 03/2010	-	-	0/0
Total			64,518.68 -	147,234.07	63,129.80				1/7
Road Transport & Highways									
382	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	352.38	05/2013 -	03/2014	10(O) -	0/0
383	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54 -	511.54	249.01	11/2013 -	11/2013	0(O) -	0/0
384	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, Uttar Pradesh	07/2012	291.36 -	291.36	10.01	01/2014 -	01/2014	0(O) -	0/0
385	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00 -	226.00	220.00	02/2014 -	02/2014	0(O) -	0/0
386	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	222.49	02/2014 -	04/2014	2(O) -	0/0
387	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014	0(O) -	0/0
388	2laning with PS Gopalganj-Chhapra - [N24000190]NHAI, Bihar	12/2011	325.00 -	325.00	131.01	05/2014 -	05/2014	0(O) -	0/0
389	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76 -	2,498.76	829.72	08/2014 -	08/2014	0(O) -	0/0
390	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013	0(O) -	0/0
391	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	34.16	09/2013 -	07/2014	10(O) -	0/0
392	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50 -	785.50	558.90	08/2013 -	08/2013	0(O) -	0/0
393	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00 -	575.00	441.01	07/2013 -	07/2013	0(O) -	0/0
394	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00 -	398.00	271.82	02/2014 -	02/2014	0(O) -	0/0
395	4-laning of Brahmapore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79 -	998.79	560.70	08/2013 -	08/2013	0(O) -	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
396	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	722.10	08/2013	08/2013	0(O)	0/0
397	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
398	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18	1,396.18	463.57	09/2014	09/2014	0(O)	0/0
399	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	181.87	09/2007	03/2014	78(O)	0/0
400	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	10/2012	91(O)	0/0
401	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,159.80	11/2012	06/2013	7(O)	0/0
402	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	285.12	11/2008	10/2012	47(O)	0/0
403	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	259.92	01/2009	12/2012	47(O)	0/0
404	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	10/2012	8(O)	0/0
405	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	189.38	02/2004	12/2012	106(O)	0/0
406	BAREILLY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	162.04	09/2013	09/2013	0(O)	0/0
407	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	470.08	06/2014	06/2014	0(O)	0/0
408	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	417.00	-	10/2013	-	2/2
409	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.82	01/2013	10/2013	9(O)	0/0
410	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	500.29	385.44	08/2013	08/2013	0(O)	0/0
411	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	249.10	06/2008	12/2012	54(O)	0/0
412	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	207.72	06/2008	03/2013	57(O)	0/0
413	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	226.46	06/2005	03/2013	93(O)	0/0
414	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	218.06	04/2010	12/2012	32(O)	0/0
415	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
416	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	731.65	03/2013	03/2013	0(O)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
417	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	330.95	-	12/2013	-	0/1
418	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	05/2013	0(O)	0/0
419	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	363.44	10/2011	03/2014	29(O)	0/0
420	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	703.31	10/2011	06/2013	20(O)	0/0
421	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	282.86	06/2008	12/2012	54(O)	0/0
422	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	175.01	10/2008	03/2014	65(O)	0/0
423	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	592.82	05/2010	12/2012	31(O)	0/0
424	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	390.90	07/2013	07/2013	0(O)	0/0
425	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
426	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	351.33	-	06/2013	-	1/1
427	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	231.15	06/2008	03/2013	57(O)	0/0
428	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	184.17	05/2008	03/2013	58(O)	0/0
429	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	274.33	09/2010	12/2012	27(O)	0/0
430	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	81.04	08/2013	08/2013	0(O)	0/0
431	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	535.42	01/2011	12/2012	23(O)	0/0
432	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	398.78	09/2008	12/2012	51(O)	0/0
433	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
434	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	129.40	09/2008	03/2013	54(O)	0/0
435	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	271.71	02/2004	12/2012	106(O)	0/0
436	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	306.65	09/2007	10/2012	61(O)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
437	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	689.41	08/2013	08/2013	0(O)	0/0
438	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	211.04	04/2008	12/2012	56(O)	0/0
439	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	152.01	04/2008	12/2012	56(O)	0/0
440	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38(O)	0/0
441	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	494.29	12/2009	07/2013	43(O)	0/0
442	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,427.90	09/2012	03/2013	6(O)	0/0
443	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,229.70	10/2011	12/2012	14(O)	0/0
444	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	279.16	09/2007	10/2012	61(O)	0/0
445	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	276.30	02/2009 05/2014	05/2013	51(O) -12(R)	0/0
446	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	51.63	07/2009	04/2014	57(O)	0/0
447	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	28.21	09/2007	04/2014	79(O)	0/0
448	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	187.45	08/2004	10/2012	98(O)	0/0
449	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	180.55	08/2004 07/2010	10/2012	98(O) 27(R)	0/0
450	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	625.07	862.54	01/2013	01/2013	0(O)	0/0
451	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
452	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,882.90	10/2012	10/2012	0(O)	0/0
453	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	515.85	05/2012	10/2012	5(O)	0/0
454	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	378.82	05/2013	02/2014	9(O)	0/0
455	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
456	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	267.81	528.89	02/2013	02/2013	0(O)	0/0
457	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
458	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	649.30	09/2008	12/2012	51(O)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
459	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	469.66	09/2009	03/2013	42(O)	0/0
460	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	536.00	387.88	01/2014	01/2014	0(O)	0/0
461	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	1,419.40	12/2012	12/2012	0(O)	0/0
462	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.36	10/2008	02/2013	52(O)	0/0
463	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	294.21	10/2008	03/2013	53(O)	0/0
464	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16	702.16	165.70	07/2014	07/2014	0(O)	0/0
465	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
466	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,025.70	05/2012	12/2012	7(O)	0/0
467	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	185.90	06/2010	10/2012	28(O)	0/0
468	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
469	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24(O)	0/0
470	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	93.99	11/2008	07/2013	56(O)	0/0
471	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	62.08	04/2009	07/2013	51(O)	0/0
472	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	21.35	11/2008	01/2014	62(O)	0/0
473	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	118.02	04/2009	03/2013	47(O)	0/0
474	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6(O)	0/0
475	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	1,264.30	06/2013	06/2013	0(O)	0/0
476	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00	754.00	414.01	03/2013	03/2014	12(O)	0/0
477	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	249.01	11/2013	11/2013	0(O)	0/0
478	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	287.76	06/2008	03/2013	57(O)	0/0
479	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48(O)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
480	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19	484.19	-	10/2014	10/2014	0(O)	0/0
481	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	266.78	04/2008	12/2012	56(O)	0/0
482	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	244.23	06/2008	03/2013	57(O)	0/0
483	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	274.59	06/2008	12/2012	54(O)	0/0
484	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
485	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	257.38	06/2011	12/2012	18(O)	0/2
486	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.92	02/2010	12/2014	58(O)	0/0
487	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00	586.00	237.55	01/2014	01/2014	0(O)	0/0
488	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	436.70	09/2013	09/2013	0(O)	0/0
489	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	386.80	03/2008	03/2013	60(O)	0/0
490	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00	1,410.00	148.10	09/2014	09/2014	0(O)	0/0
491	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	907.92	10/2014	10/2014	0(O)	0/0
492	PATHANKOT- BHOGPUR, KM.26- KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	223.07	05/2008	03/2013	58(O)	0/0
493	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00	574.00	420.39	03/2014	03/2014	0(O)	0/0
494	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	671.30	586.44	02/2013	02/2013	0(O)	0/0
495	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	11.43	07/2012	12/2012	5(O)	0/0
496	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	1,000.70	03/2013	03/2013	0(O)	0/0
497	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	835.00	104.67	01/2014	01/2014	0(O)	0/0
498	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,460.90	11/2011	08/2013	21(O)	0/0
499	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17(O)	0/0
500	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	1,987.00	-	07/2015	06/2016	11(O)	0/0
501	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHA) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	312.28	10/2008	12/2012	50(O)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
502	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI, Madhya Pradesh)	12/2003	229.91 -	229.91	266.58	10/2008 -	12/2012	50(O) -	0/0
503	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00 -	650.00	734.10	11/2013 -	11/2013	0(O) -	0/0
504	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHA) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	203.43	238.88	10/2008 -	12/2012	50(O) -	0/0
505	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHA) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30	190.61	10/2008 -	10/2012	48(O) -	0/0
506	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25(O) -	0/0
507	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	805.39	322.83	03/2013 -	03/2013	0(O) -	0/0
508	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Orissa	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014	0(O) -	0/0
509	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	203.42	09/2007 -	03/2013	66(O) -	0/0
510	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	184.45	07/2008 -	12/2012	53(O) -	0/0
511	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0
512	SIX LANNING OF KRISHNAGRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013	0(O) -	0/0
513	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014	0(O) -	0/0
514	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19(O) -	0/0
515	SNG toBANL - [N24000189]NHAI, J and K	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0
516	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60(O) -	0/0
517	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00 -	241.53	136.62	04/2004 -	12/2012	104(O) -	0/0
518	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,665.60	08/2011 -	10/2012	14(O) -	0/0
519	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	11/2012	41(O) -	0/0
520	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32(O) -	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
521	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	698.57	11/2013	11/2013	0(O)	0/0
522	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
523	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	77.34	05/2013	05/2013	0(O)	0/0
524	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	157.11	-	04/2013	-	2/2
525	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	682.60	03/2014	03/2014	0(O)	0/0
526	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	163.42	03/2008	10/2012	55(O)	0/0
527	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	32.79	11/2012	11/2012	0(O)	0/0
528	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	405.28	07/2013	07/2013	0(O)	0/0
529	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	148.11	06/2014	06/2014	0(O)	0/0
Total			94,480.80	96,059.42	66,463.00				10/14
Shipping & Ports									
530	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011 10/2012	10/2012	18(O) 0(R)	0/0
531	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	777.97	09/2012	09/2012	0(O)	0/0
532	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	214.65	12/2012 05/2013	05/2013	5(O) 0(R)	0/0
533	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	188.88	12/2011 09/2012	09/2012	9(O) 0(R)	0/0
534	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	305.00	194.14	06/2011 09/2012	09/2012	15(O) 0(R)	0/0
535	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	248.23	02/2014	02/2014	0(O)	0/0
536	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013	10/2013	-2(O)	0/0
537	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	863.93	12/2010 09/2012	10/2013	34(O) 13(R)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
538	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0
539	Construction of berthing and allied facilities off - [N25000037]PORT TRUST, Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0
540	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST, Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	10/2008	-	0/0
541	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1
542	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
543	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0
544	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
545	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0
546	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40 -	2,427.40	829.49	10/2008 11/2010	-	-	0/0
547	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,433.40	01/2012 09/2012	12/2012	11(O) 3(R)	0/0
548	Setting up of Single Point Mooring (SPM) and allied - [N25000060]PORT TRUST, Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
	Total		16,242.52 -	18,554.09	8,143.40				0/1
Telecommunications									
549	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	03/2013	50(O) -	0/0
550	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
551	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72(O) 11(R)	0/0
552	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2013	29(O) 12(R)	0/0

Sector Wise Details

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
554	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
555	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	80.04	06/2009 -	12/2012	42(O) -	0/0
556	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	12/2012	48(O) -	0/0
557	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	813.72	11/2010 -	12/2012	25(O) -	0/0
558	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	-	0/0
559	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	12/2012	45(O) -	0/0
560	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
561	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
	Total		5,735.48 -	5,676.27	1,656.61				0/0
Urban Development									
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21(O) -	6/6
563	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
564	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	923.05	03/2016 -	03/2016	0(O) -	0/0
565	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	56.69	09/2014 -	09/2014	0(O) -	0/0
	Total		44,245.18 -	49,518.08	3,247.31				6/6
Water Resources									
566	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O) -	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			790,572.38	923,296.84	420,233.37				918/3365

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **13**

Number of Projects Delayed **7**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 7 projects are delayed .6 projects do not have fixed dates of commissioning.

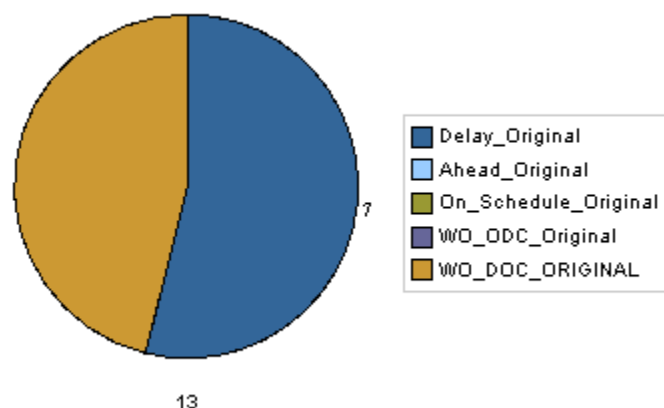

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5735.48 crore but this was subsequently revised to Rs. 5676.27 crore implying a cost overrun of -1%. The expenditure incurred on these projects till September, 2012 is Rs. 1656.61 crore, which is 29.2% of the revised cost of the projects.

Figures are in Rs. Crore

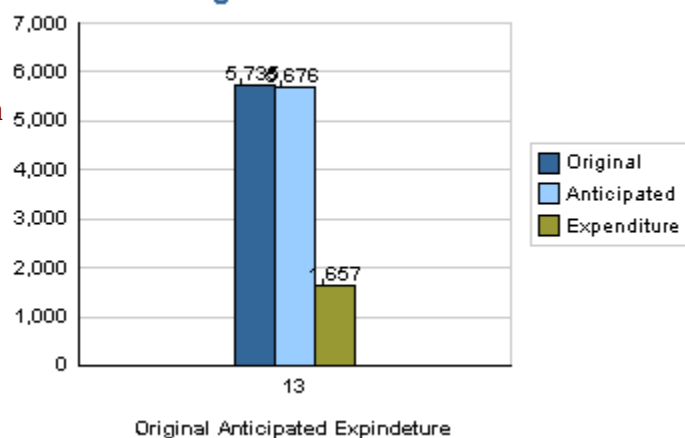

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	2
Number of Projects Delayed	10
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 2 projects are ahead of schedule, 2 projects are on schedule and 10 projects are delayed .5 projects do not have fixed dates of commissioning.

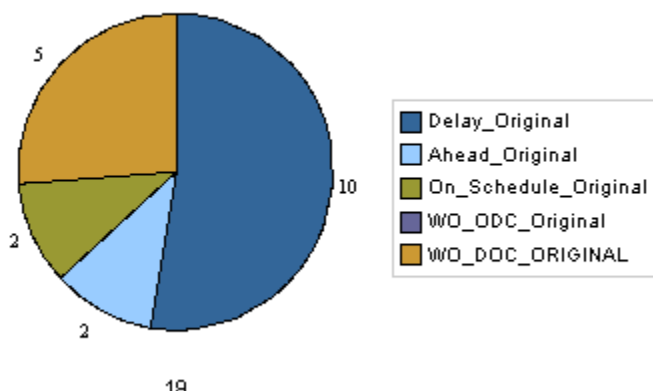

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 16242.52 crore but this was subsequently revised to Rs. 18554.09 crore implying a cost overrun of 14.2%. The expenditure incurred on these projects till September, 2012 is Rs. 8143.4 crore, which is 43.9% of the revised cost of the projects.

Figures are in Rs. Crore

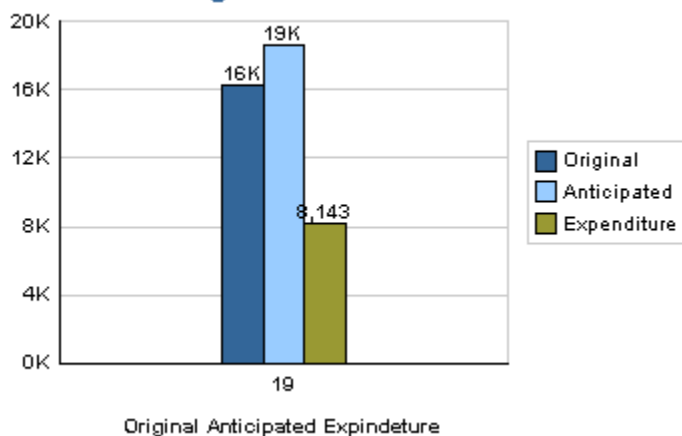

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	148
Number of Projects On Schedule	55
Number of Projects Delayed	87

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 148 projects, 55 projects are on schedule and 87 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

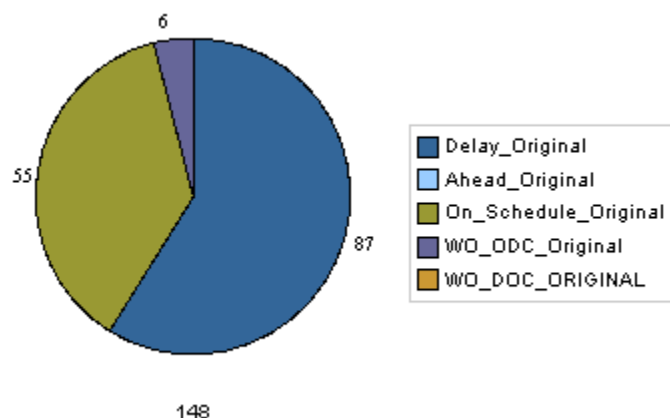

III. Investment Scenario

The Total Original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 94480.8 crore but this was subsequently revised to Rs. 96059.42 crore implying a cost overrun of 1.7%. The expenditure incurred on these projects till September, 2012 is Rs. 66463 crore, which is 69.2% of the revised cost of the projects.

Figures are in Rs. Crore

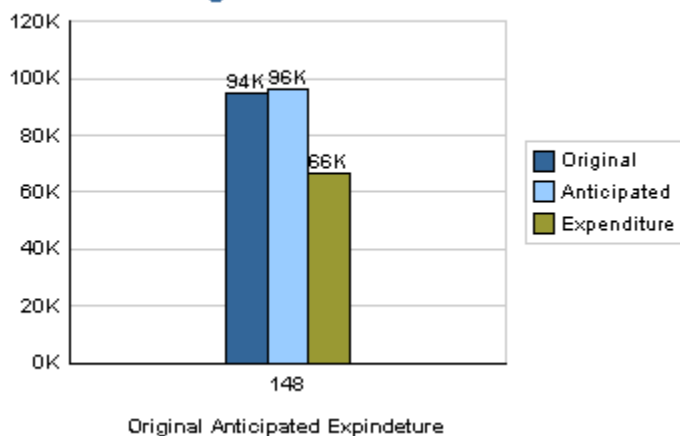

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	127
Number of Projects On Schedule	10
Number of Projects Delayed	38
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	18
Number of Projects Without Date Of Commissioning	60

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 127 projects, 1 project are ahead of schedule, 10 projects are on schedule and 38 projects are delayed .60 projects do not have fixed dates of commissioning.18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

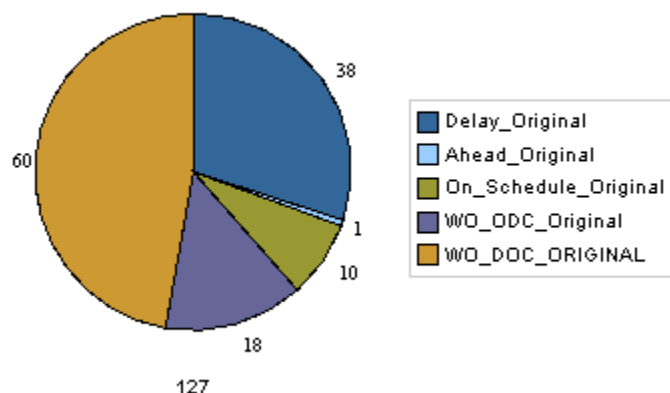

III. Investment Scenario

The Total Original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 64518.68 crore but this was subsequently revised to Rs. 147234.07 crore implying a cost overrun of 128.2%. The expenditure incurred on these projects till September, 2012 is Rs. 63129.8 crore, which is 42.9% of the revised cost of the projects.

Figures are in Rs. Crore

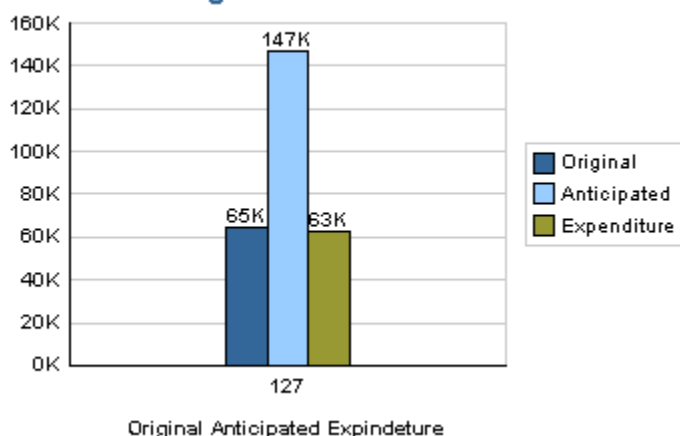

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	98
Number of Projects On Schedule	45
Number of Projects Delayed	50

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 98 projects, 45 projects are on schedule and 50 projects are delayed .1 project do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

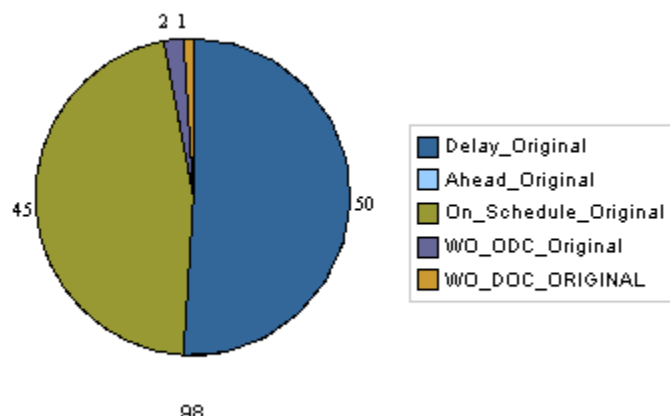

III. Investment Scenario

The Total Original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 231379.54 crore but this was subsequently revised to Rs. 245378.02 crore implying a cost overrun of 6.1%. The expenditure incurred on these projects till September, 2012 is Rs. 104082.11 crore, which is 42.4% of the revised cost of the projects.

Figures are in Rs. Crore

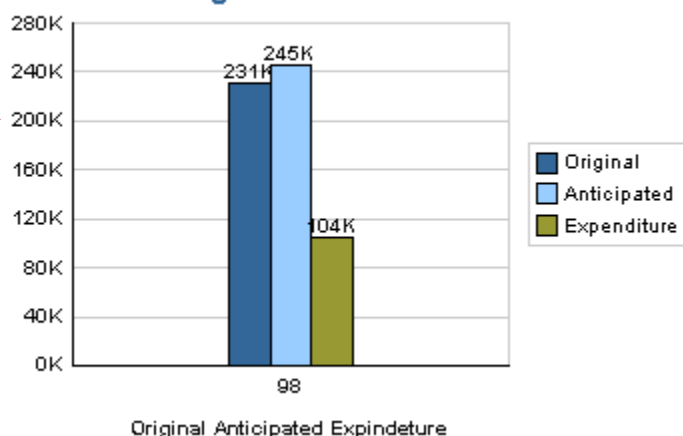

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	71
Number of Projects On Schedule	22
Number of Projects Delayed	43

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	4


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 71 projects, 22 projects are on schedule and 43 projects are delayed .4 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

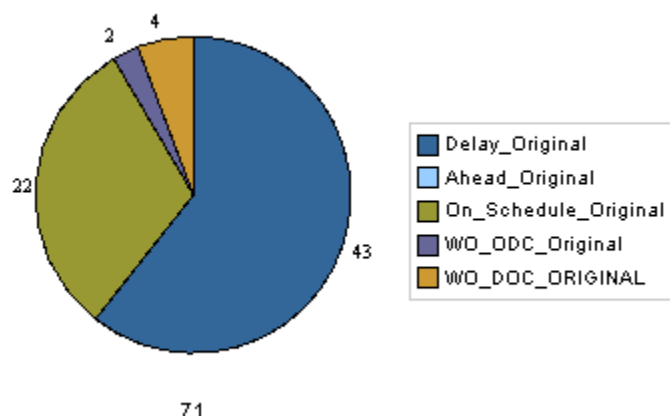

III. Investment Scenario

The Total Original cost of implementation of 71 projects when sanctioned, was of the order of Rs. 174773.81 crore but this was subsequently revised to Rs. 183290.21 crore implying a cost overrun of 4.9%. The expenditure incurred on these projects till September, 2012 is Rs. 80925.17 crore, which is 44.2% of the revised cost of the projects.

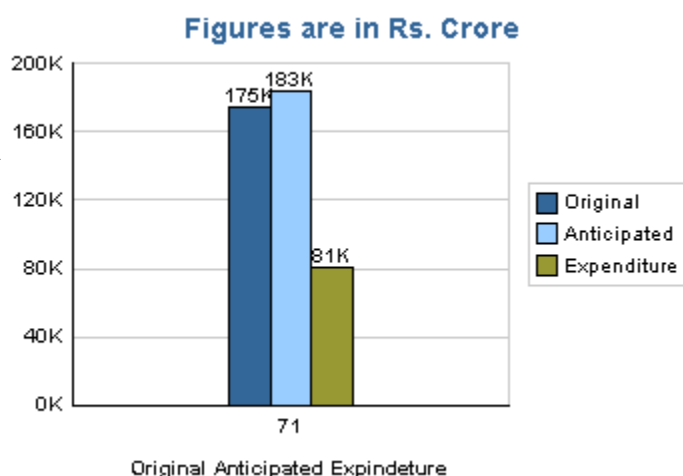

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 1 project are ahead of schedule, 3 projects are on schedule and 10 projects are delayed .3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

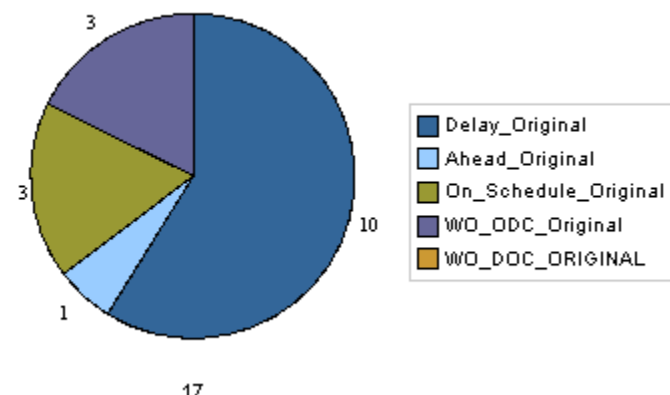

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till September, 2012 is Rs. 43661.77 crore, which is 61.1% of the revised cost of the projects.

Figures are in Rs. Crore

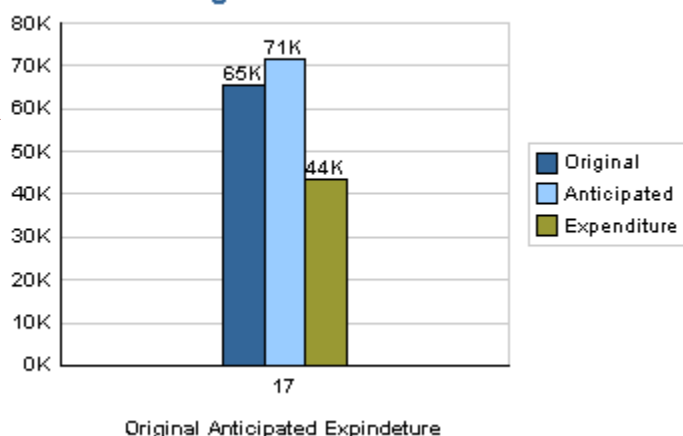

Sector wise current status of projects on theFlash Report


Fertilisers

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are ahead of schedule, 2 projects are on schedule and 2 projects do not have fixed dates of commissioning.

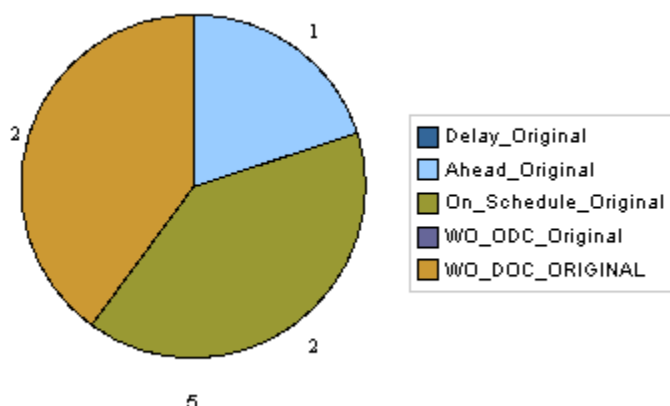

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4828.66 crore but this was subsequently revised to Rs. 4828.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till September, 2012 is Rs. 2875.03 crore, which is 59.5% of the revised cost of the projects.

Figures are in Rs. Crore

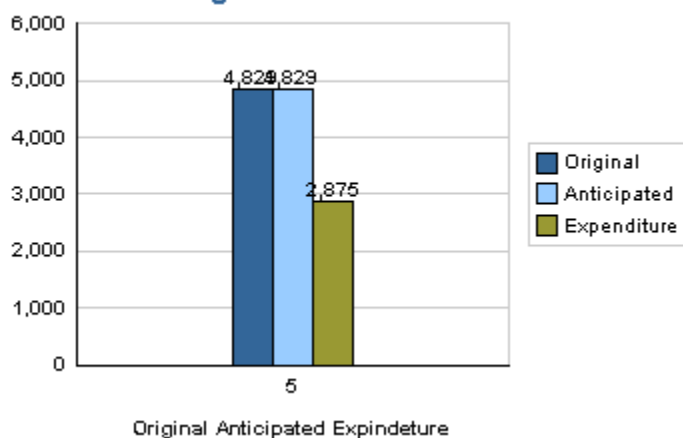

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	32
Number of Projects Delayed	18

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 32 projects are on schedule and 18 projects are delayed .1 project do not have fixed dates of commissioning.

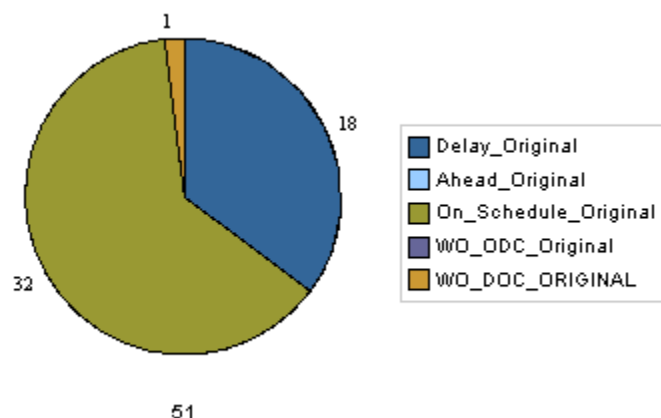

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37312.25 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till September, 2012 is Rs. 12889.34 crore, which is 34.5% of the revised cost of the projects.

Figures are in Rs. Crore

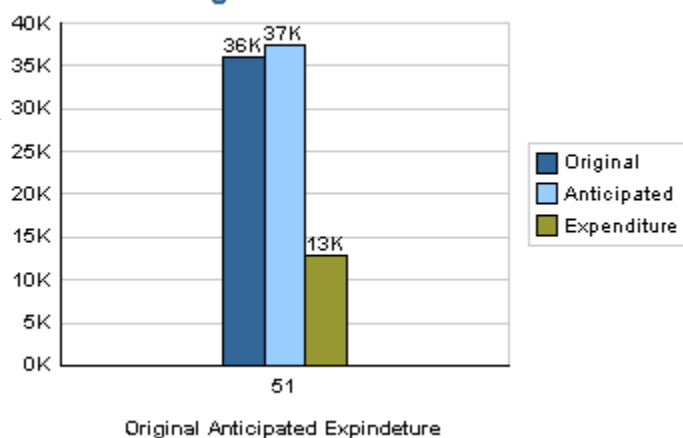

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

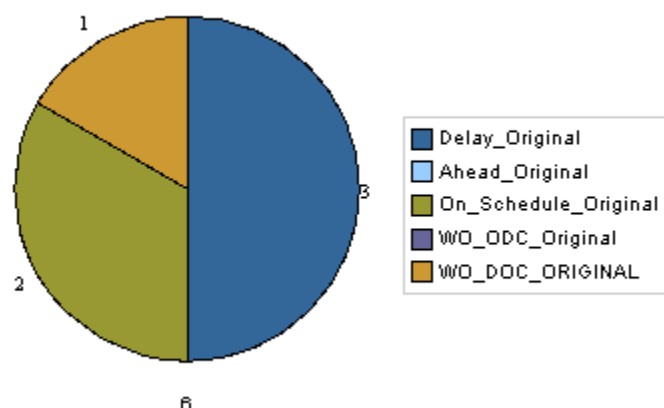

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till September, 2012 is Rs. 4499.06 crore, which is 74.2% of the revised cost of the projects.

Figures are in Rs. Crore

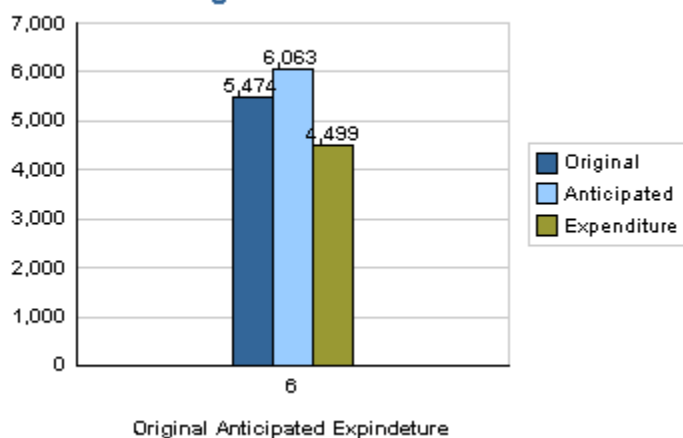

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

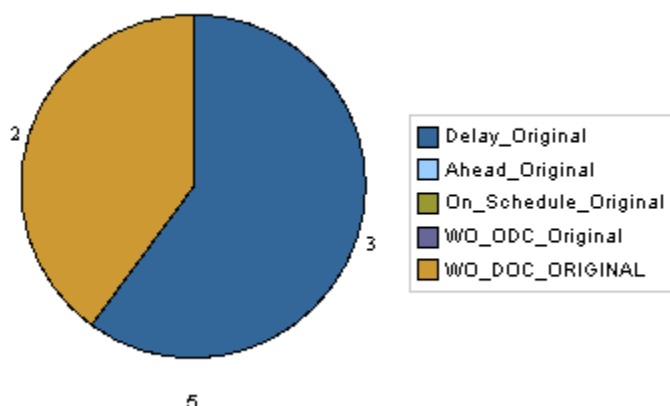

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till September, 2012 is Rs. 23051.94 crore, which is 48.2% of the revised cost of the projects.

Figures are in Rs. Crore

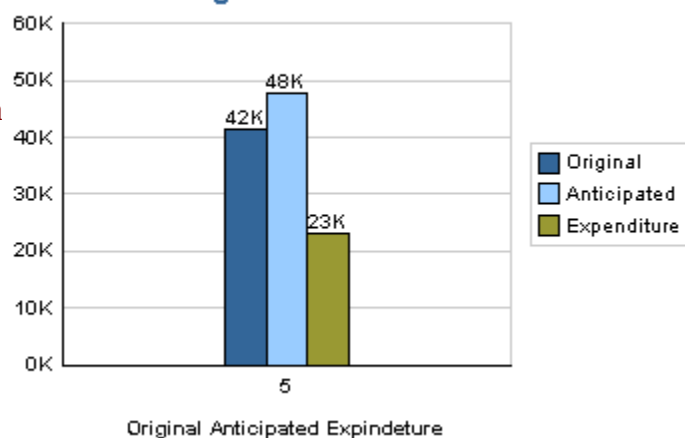

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

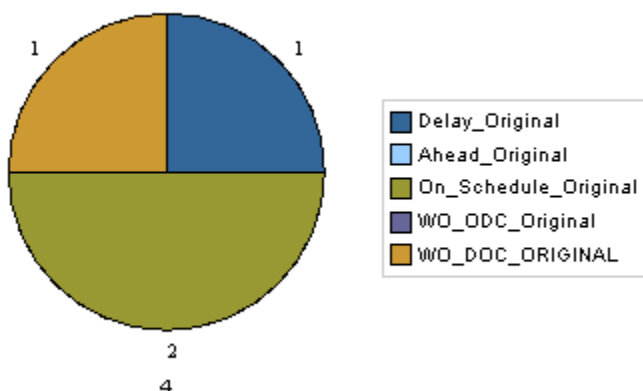

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till September, 2012 is Rs. 3247.31 crore, which is 6.6% of the revised cost of the projects.

Figures are in Rs. Crore

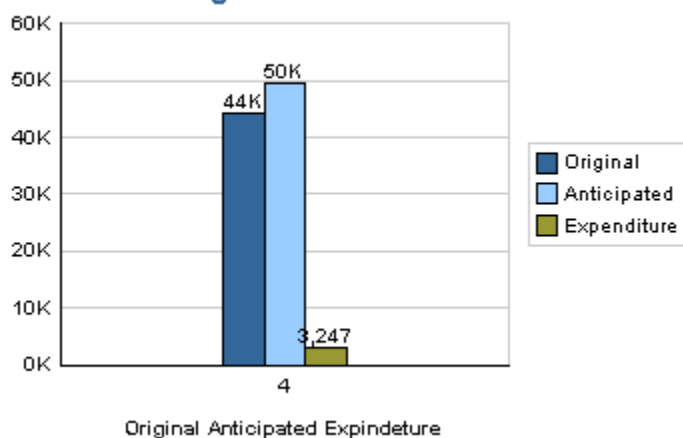

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	EXPENDITURE CUMM
1	Andhra Pradesh	36	31031.62	38457.22	22934.94
2	Arunachal Pr.	4	9512.22	14153.62	8411.52
3	Assam	36	22463.87	34047.37	22845.83
4	Bihar	30	26901.24	34657.04	22584.24
5	Chhatisgarh	24	46715.19	47998.27	14222.65
6	Delhi	5	38572.55	38552.96	1046.94
7	Goa	1	335.61	335.61	138.65
8	Gujarat	22	31111.55	31313.49	8461.23
9	Haryana	10	5496.60	7438.41	7557.31
10	Himachal Pr.	5	13355.57	15414.93	12500.23
11	J and K	10	14926.96	34825.56	13258.24
12	Jharkhandd	22	14293.58	18275.16	7857.02
13	Karnataka	24	44634.83	54126.75	20195.42
14	Kerala	6	19694.67	21136.22	4971.99
15	Madhya pradesh	24	19741.92	20036.39	8981.46
16	Maharashtra	55	97571.22	112834.43	50575.30
17	Manipur	1	727.56	4444.00	937.59
18	Meghalaya	2	762.00	762.00	607.88
19	Mizoram	2	1532.97	3307.11	362.86
20	Multi State	103	139949.49	145640.61	63643.33
21	Nagaland	1	850.00	850.00	8.45
22	Orissa	30	57409.06	60948.97	32894.31
23	Punjab	7	4836.20	5777.97	4174.72
24	Rajasthan	14	26544.10	26138.31	9347.39
25	Sikkim	2	1648.94	3690.04	237.83
26	Tamil Nadu	32	51275.95	62055.82	39468.70
27	Tripura	3	1522.39	2053.23	924.68
28	Uttar Pradesh	25	19249.20	23086.97	11767.93
29	Uttaranchal	3	5619.21	6559.64	1960.76
30	West Bengal	27	42286.11	54655.47	27429.58
TOTAL		566	790572.38	923573.57	420308.98

LIST OF PROJECTS MORE THAN COST

S.No.	PROJECT TITLE	AGENCY	SECTOR	STATE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	EXPENDITURE CUMMULATIVE
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	Atomic Energy	Tamil Nadu	09/2010	01/2012	3492.00	5677.00	3782.70
2	KUDANKULAM APP (NPCIL)	NPCIL	Atomic Energy	Tamil Nadu	12/2008	03/2013	13171.00	17270.00	15030.00
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	AAI	Civil Aviation	West Bengal	05/2011	10/2012	1942.51	2325.00	2123.01
4	RESITMENT OF MARKETING INSTALATION AT VISAKH	HPCL	Petroleum	Andhra Pradesh	N.A.	08/2012	756.00	898.00	905.36
5	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	NHPC	Power	West Bengal	03/2007	02/2013	768.92	1628.00	1563.13
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	NHPC	Power	West Bengal	09/2009	10/2013	1061.38	1501.75	1194.26
7	NIMOO BAZGO HYDROELECTRIC PROJECT	NHPC	Power	J and K	08/2010	01/2013	611.01	936.00	794.58
8	CHUTAK HYDRO-ELECTRIC PROJECT	NHPC	Power	J and K	02/2011	10/2012	621.26	913.00	754.57
9	URI H.E.P STAGE -II (NHPC)	NHPC	Power	J and K	11/2009	03/2013	1729.29	2081.00	1787.44
10	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	PGCIL	Power	Himachal Pr.	01/2010	02/2013	557.24	758.75	590.80
11	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	(NR)	Railways	Punjab	12/2012	01/2013	248.44	1115.21	897.49
12	JIND-SONEPAT (NL),NR	(NR)	Railways	Haryana	03/2012	12/2012	190.81	500.00	425.36
13	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	(NR)	Railways	J and K	03/2001	12/2017	2500.00	20000.00	8069.06
14	REWARI-ROHTAK (NL),NR	(NR)	Railways	Haryana	02/2010	02/2011	149.38	602.00	494.36
15	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	(NR)	Railways	Multi State	06/2007	06/2007	409.00	847.75	835.55
16	AMRAVATI-NARKHER NL(CR)	CR	Railways	Maharashtra	06/1999	03/2011	120.90	548.95	538.65
17	LANJHIGARH-JUNAGARH NL(ECOR)	ECOR	Railways	Orissa	03/2002	01/2013	100.00	227.94	204.65

18	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	Railways	Bihar	03/2012	03/2013	114.01	477.88	395.87
19	JAYANAGAR- DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	Railways	Bihar	03/2012	02/2013	233.00	1043.56	661.92
20	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara- NSCB Airport(MTP)	MRTTP	Railways	West Bengal	12/2006	08/2010	907.69	3176.10	3219.06
21	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	MRTTP	Railways	Maharas htra	06/2011	03/2012	3125.20	4501.80	4334.00
22	LALITPUR-SATNA-REWA- SINGRULI NL, (NCR)	NCR	Railways	Multi State	03/1994	12/2011	158.77	540.96	558.07
23	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	Railways	Uttar Pradesh	12/2009	03/2011	108.00	227.42	250.82
24	KATIHAR - JOGBANI (GC)(NEFR)	NEFR	Railways	Bihar	12/2010	03/2015	100.00	1041.79	732.83
25	RANGIA- MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NEFR	Railways	Multi State	N.A.	03/2013	915.70	1717.29	1476.55
26	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NEFR	Railways	Multi State	12/2008	03/2014	733.00	1655.81	1298.65
27	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NEFR	Railways	Multi State	03/2011	03/2011	170.00	453.04	392.85
28	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarghat national project	NEFR	Railways	Assam	03/2009	12/2013	1676.31	4255.37	3195.95
29	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAG UN, NEFR	NEFR	Railways	Arunach al Pr.	N.A.	12/2012	156.00	415.73	279.98
30	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NEFR	Railways	Manipur	03/2011	03/2016	727.56	4444.00	937.59
31	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	NEFR	Railways	Assam	04/2008	12/2015	1000.00	3230.02	2501.02
32	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	NER	Railways	Uttar Pradesh	N.A.	03/2012	381.17	863.23	587.54

33	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	Railways	Multi State	N.A.	03/2014	323.40	750.89	502.15
34	MAHARAJGANJ-MASRAKH (NL) - NER	NER	Railways	Bihar	N.A.	02/2013	218.19	218.19	263.79
35	KANPUR-KASGANJ-MATHURA(GC),NER	NER	Railways	Uttar Pradesh	N.A.	03/2012	395.00	1577.46	1364.05
36	ELECTRIFICATION OF MORADABAD-ROZA	RE	Railways	Uttar Pradesh	03/2011	03/2012	129.17	250.00	227.48
37	BILASPUR-URKURA (DL)	RVNL	Railways	Chhatisgarh	N.A.	03/2011	151.52	350.00	324.53
38	RENIGUNTA-GUNTAKAL(RE)	RVNL	Railways	Andhra Pradesh	04/2003	N.A.	168.34	370.00	356.60
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	Railways	Orissa	03/2009	04/2013	133.41	225.00	213.62
40	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	RVNL	Railways	Multi State	03/2009	03/2011	240.00	355.00	405.53
41	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	Railways	Andhra Pradesh	12/2007	12/2010	136.62	221.90	233.88
42	GADWAL - RAICHUR (NL), SCR	SCR	Railways	Multi State	02/2011	02/2013	92.63	270.00	260.85
43	NANDYAL-YERRAGUNTLA(NL),SCR	SCR	Railways	Andhra Pradesh	02/2009	03/2012	155.74	883.00	632.79
44	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	Railways	Andhra Pradesh	N.A.	03/2012	124.43	925.30	589.35
45	RANCHI-LOHARDAGA(GC),SER	SER	Railways	Jharkhand	06/2004	12/2012	194.07	456.45	301.82
46	CALICUT-MANGALORE (DL) (SR)	SR	Railways	Multi State	N.A.	02/2012	240.00	579.37	600.41
47	KARUR-SALEM(NL),SR	SR	Railways	Tamil Nadu	N.A.	10/2012	155.55	712.00	732.14
48	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	Railways	Tamil Nadu	N.A.	12/2012	343.17	900.00	559.19
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	Railways	Tamil Nadu	N.A.	N.A.	100.00	548.96	510.29
50	KOTTUR-HARIHAR(NL),(SWR)	SWR	Railways	Karnataka	N.A.	03/2011	65.94	302.23	335.93
51	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	Railways	Karnataka	N.A.	01/2013	295.00	944.55	530.46
52	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	NHAI	Road Transport & Highways	Bihar	10/2008	03/2013	240.00	240.00	294.21

53	Hyderabad-yadgiri N.H no-202	NHAI	Road Transport & Highways	Andhra Pradesh	05/2012	10/2012	388.00	388.00	515.85
54	Talegaon-amravati	NHAI	Road Transport & Highways	Maharashtra	11/2013	11/2013	567.00	567.00	698.57
55	NAGPUR-KONDHALI,NH-6(NHAI)	NHAI	Road Transport & Highways	Maharashtra	12/2008	12/2012	168.00	168.00	457.30
56	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	Road Transport & Highways	Multi State	09/2010	12/2012	232.45	232.45	274.33
57	GWALIOR BYPASS, NH-75,3	NHAI	Road Transport & Highways	Madhya pradesh	10/2009	12/2012	300.93	300.93	302.72
58	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	NHAI	Road Transport & Highways	Bihar	09/2008	12/2012	332.94	332.94	398.78
59	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	NHAI	Road Transport & Highways	Madhya pradesh	10/2008	12/2012	251.03	251.03	312.28
60	DAKOBA TO NAGAON (NH-36)(NHAI)	NHAI	Road Transport & Highways	Assam	06/2008	12/2012	225.00	225.00	282.86
61	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	NHAI	Road Transport & Highways	Assam	05/2008	03/2013	160.00	160.00	184.17
62	JHAJHARPUR TO DARBANGA (BR-7)	NHAI	Road Transport & Highways	Bihar	09/2008	12/2012	340.00	340.00	649.30

63	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	NHAI	Road Transport & Highways	West Bengal	11/2008	10/2012	221.82	221.82	285.12
64	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	NHAI	Road Transport & Highways	Assam	06/2008	03/2013	195.00	195.00	207.72
65	NALBARI TO BIJNI (AS-8)	NHAI	Road Transport & Highways	Assam	06/2008	12/2012	200.00	200.00	274.59
66	NALBARI TO BIJNI (AS-6)	NHAI	Road Transport & Highways	Assam	06/2008	03/2013	225.00	225.00	244.23
67	NALBARI T BIJNI (AS-7)	NHAI	Road Transport & Highways	Assam	04/2008	12/2012	208.00	208.00	266.78
68	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	Road Transport & Highways	Assam	04/2010	12/2012	217.61	217.61	218.06
69	SONAPUR TO GUWAHTI (AS-3)	NHAI	Road Transport & Highways	Assam	03/2008	03/2013	245.00	245.00	491.21
70	DHARAMTUL TO SONAPUR (AS-19)	NHAI	Road Transport & Highways	Assam	06/2008	03/2013	200.00	200.00	231.15
71	THANJAUR-TRICHY,NH-67(NHAI)	NHAI	Road Transport & Highways	Tamil Nadu	06/2009	11/2012	280.00	280.00	581.49
72	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	NHAI	Road Transport & Highways	Tamil Nadu	01/2011	02/2013	941.00	941.00	1901.00

73	Jaipur-Tonk-Deoli	NHAI	Road Transport & Highways	Rajasthan	12/2012	12/2012	792.06	792.06	1419.40
74	AMRITSAR-PATHANKOT	NHAI	Road Transport & Highways	Punjab	11/2012	06/2013	705.00	705.00	1159.80
75	Pune-sholapur, pkg1	NHAI	Road Transport & Highways	Maharashtra	05/2012	10/2013	1110.00	1110.00	1802.10
76	MP/Maharashtra Border-Dhula	NHAI	Road Transport & Highways	Maharashtra	06/2012	12/2012	835.00	835.00	1068.70
77	Hazaribagh-Ranchi	NHAI	Road Transport & Highways	Jharkhand	01/2013	01/2013	625.07	625.07	862.54
78	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	NHAI	Road Transport & Highways	Chhattisgarh	01/2009	12/2012	190.00	190.00	259.92
79	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	NHAI	Road Transport & Highways	Chhattisgarh	01/2011	12/2012	464.00	464.00	535.42
80	JAIPUR-REENGUS	NHAI	Road Transport & Highways	Rajasthan	02/2013	02/2013	267.81	267.81	528.89
81	KUNDUPUR-SURATHKAL & MANGLORE	NHAI	Road Transport & Highways	Karnataka	N.A.	03/2013	671.00	671.00	737.54
82	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	Road Transport & Highways	Assam	06/2008	12/2012	237.80	237.80	249.10

83	ROHTAK-BAWAL	NHAI	Road Transport & Highways	Haryana	11/2013	11/2013	650.00	650.00	734.10
84	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	Road Transport & Highways	Gujarat	06/2013	06/2013	1008.50	1008.50	1097.80
85	2 LANNING OF MOKAMA-MUNGER	NHAI	Road Transport & Highways	Bihar	05/2013	03/2014	351.54	351.54	352.38
86	Hungund-Surathkal and Mangalore-Knt/Kerala Border	NHAI	Road Transport & Highways	Karnataka	N.A.	03/2013	946.00	946.00	1394.40
87	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	NHAI	Road Transport & Highways	Kerala	02/2010	12/2014	557.00	557.00	930.92
88	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	NHAI	Road Transport & Highways	Andhra Pradesh	10/2011	06/2013	572.30	572.30	703.31
89	Surat- Dahisar(Six Lane) Km 263 to Km 502	NHAI	Road Transport & Highways	Multi State	08/2011	10/2012	1693.75	1693.75	2665.60
90	Gurgaon-Kotputli Km 42.70 to 54.4 Km	NHAI	Road Transport & Highways	Multi State	10/2011	12/2012	1673.70	1673.70	2229.70
91	Chennai-Tada(Six lane)	NHAI	Road Transport & Highways	Tamil Nadu	10/2011	03/2014	353.37	353.37	363.44
92	TRICHY - KORUR NH-67	NHAI	Road Transport & Highways	Tamil Nadu	07/2010	03/2013	516.00	516.00	760.07

93	GANJAM- ICCHAPURUM,NH- 5(NHAI)	NHAI	Road Transport & Highways	Orissa	02/2004	12/2012	263.27	263.27	271.71
94	Armur to kadloor yellareddy	NHAI	Road Transport & Highways	Andhra Pradesh	02/2012	10/2012	390.56	390.56	631.65
95	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	NHAI	Road Transport & Highways	Madhya pradesh	10/2008	12/2012	229.91	229.91	266.58
96	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI)	NHAI	Road Transport & Highways	Madhya pradesh	10/2008	12/2012	203.43	203.43	238.88
97	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	NHAI	Road Transport & Highways	Uttar Pradesh	10/2008	10/2012	151.30	151.30	190.61
98	JHANSI TO LALITPUR, NH-25,26	NHAI	Road Transport & Highways	Uttar Pradesh	09/2009	03/2013	355.06	355.06	469.66
99	KOTA BYPASS,RJ-4, NH- 76 (NHAI)	NHAI	Road Transport & Highways	Rajastha n	10/2008	02/2013	275.00	250.39	279.36
100	ORAI TO JHANSI (UP- 5),NH-25, KM.220.0 TO KM.170.0	NHAI	Road Transport & Highways	Uttar Pradesh	03/2008	03/2013	340.68	340.68	386.80
101	NAGAON TO DHARAMTUL (AS-2)	NHAI	Road Transport & Highways	Assam	06/2008	03/2013	264.72	264.72	287.76
102	INDORE-DEWAS(NH-3)	NHAI	Road Transport & Highways	Madhya pradesh	05/2013	02/2014	325.00	325.00	378.82

103	PANIPAT-ROHTAK	NHAI	Road Transport & Highways	Haryana	10/2014	10/2014	807.00	807.00	907.92
104	GUWAHATI TO NALBARI (AS-5)	NHAI	Road Transport & Highways	Assam	04/2008	12/2012	198.16	198.16	211.04
105	Hyderabad-Vijaywada Km. 40 to 221.50 Km	NHAI	Road Transport & Highways	Andhra Pradesh	10/2012	10/2012	1740.00	1740.00	1882.90
106	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	NHAI	Road Transport & Highways	Haryana	11/2011	08/2013	1108.00	2288.00	3460.90
107	Kishangarh-Ajmer-Beawer	NHAI	Road Transport & Highways	Rajasthan	05/2012	12/2012	795.00	795.00	1025.70
108	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	Road Transport & Highways	Haryana	05/2010	12/2012	486.00	486.00	592.82
109	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	NHAI	Road Transport & Highways	Uttar Pradesh	09/2007	10/2012	220.00	220.00	279.16
110	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	NHAI	Road Transport & Highways	Uttar Pradesh	09/2007	10/2012	275.00	275.00	306.65
111	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	NHAI	Road Transport & Highways	Uttar Pradesh	03/2005	10/2012	367.49	367.49	453.68
112	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	NHAI	Road Transport & Highways	Assam	09/2007	03/2013	157.47	154.57	203.42

113	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	Shipping & Ports	Kerala	04/2009	02/2011	245.67	373.22	326.08
114	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	Steel	Andhra Pradesh	10/2009	03/2013	8692.00	12291.00	9787.70
115	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT	RINL	Steel	Andhra Pradesh	02/2011	12/2012	230.00	343.58	252.46

List of Projects Ahead of Schedule

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Fertilisers</u>						
1	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT [N08000006]	1/2010	1,478.63 -	1,478.63	890.00	01/2013 12/2012	12/2012
	Total		1,478.63 -	1,478.63	890.00		
	<u>Steel</u>						
2	Expansion of Rourkela Steel Plant - [N12000056]	9/2008	11,812.00 11,812.00	11,812.00	7,871.60	11/2013 -	03/2013
	Total		11,812.00 -	11,812.00	7,871.60		
	<u>Railways</u>						
3	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	366.00	03/2014 -	03/2013
	Total		1,389.62 -	1,389.62	366.00		
	<u>Shipping & Ports</u>						
4	Acquistion of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052]	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	10/2013
5	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060]	2/2011	830.00 -	621.53	-	05/2013 -	03/2013
	Total		1,858.10 -	1,649.63	371.96		
	Grand Total		16,538.35	16,329.88	9,499.56		

Sectorwise Summary of Project Without Original Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Petroleum	2	2,949.68	.00	2,949.68	2,146.00
Power	2	3,399.49	623.44	3,601.92	1,904.96
Railways	18	5,486.04	7,218.02	14,255.57	6,631.57
Road Transport & Highways	6	4,069.00	.00	4,069.00	3,388.33
Steel	3	1,657.88	.00	1,657.88	294.85
Grand total	31	17,562.09	7,841.46	26,534.05	14,365.71

List of project Without Original Date of Commissioning

(Sep,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Steel</u>								
1	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	170.48	- -	04/2013	-	13/19
2	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	124.37	- -	05/2013	-	17/21
3	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	-	- -	12/2013	-	0/1
	Total		1,657.88 -	1,657.88	294.85				30/41
	<u>Petroleum</u>								
4	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	194.01	- -	09/2012	-	36/36
5	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,951.99	- -	10/2012	-	116/116
	Total		2,949.68 -	2,949.68	2,146.00				152/152
	<u>Power</u>								
6	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	343.96	- 07/2013	07/2013	0(R3)	6/29
7	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,561.00	- -	09/2015	-	7/14
	Total		3,399.49 -	3,601.92	1,904.96				13/43
	<u>Railways</u>								
8	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	732.14	- -	10/2012	-	0/0
9	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	559.19	- -	12/2012	-	0/0
10	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	415.73	279.98	- -	12/2012	-	0/0
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	530.46	- -	01/2013	-	0/0
12	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	263.79	- -	02/2013	-	0/0
13	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,820.00	179.58	- -	03/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	197.85	- -	03/2013	-	0/0
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	95.47	- -	03/2013	-	0/0
16	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	764.60	- -	03/2013	-	0/6
17	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	235.89	- -	03/2013	-	0/0
18	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,476.55	- -	03/2013	-	0/0
19	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	114.24	- -	03/2013	-	0/0
20	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
21	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	502.15	- -	03/2014	-	0/1
22	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	146.31	- -	03/2014	-	0/0
23	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	114.85	- -	03/2014	-	0/0
24	New BG line Rly line from Eklakhi-Balughat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.39	- -	03/2015	-	0/0
25	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
Total			5,486.04 -	14,255.57	6,631.57				0/7
Road Transport & Highways									
26	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
27	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3
28	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	157.11	- -	04/2013	-	2/2
29	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	351.33	- -	06/2013	-	1/1
30	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	417.00	- -	10/2013	-	2/2
31	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	330.95	- -	12/2013	-	0/1
Total			4,069.00 -	4,069.00	3,388.33				10/12
Grand Total			17,562.09	26,534.05	14,365.71				205/255

Sectorwise Summary Without Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	2	4,598.29	.00	6,783.29	4,866.94
Civil Aviation	1	1,808.00	2,015.00	2,015.00	1,676.63
Coal	1	249.03	.00	249.03	48.14
Fertilisers	2	763.00	.00	763.00	425.03
Petroleum	4	2,810.81	394.00	3,122.81	1,483.92
Power	1	596.45	1,007.16	1,007.16	844.73
Railways	60	19,500.65	31,150.24	48,567.82	25,868.96
Shipping & Ports	5	3,904.91	1,869.77	4,902.58	1,161.53
Telecommunications	6	2,997.75	.00	2,934.67	111.64
Urban Development	1	114.18	173.08	173.08	0.00
Grand total	83	37,343.07	36,609.25	70,518.44	36,487.52

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00	09/2010	01/2012
			-	-	
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	04/2012
			-	04/2011	
	Total		4,598.29		
			-		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
			2,015.00	02/2012	
	Total		1,808.00		
			-		
<u>Coal</u>					
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	-
			-	-	
	Total		249.03		
			-		
<u>Fertilisers</u>					
5	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	07/2011	04/2012
			-	-	
6	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	07/2011	07/2012
			-	-	
	Total		763.00		
			-		
<u>Petroleum</u>					
7	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	-	08/2012
			-	03/2012	
8	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
			-	-	
9	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	04/2012	-
			-	-	
10	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	-	-
			394.00	08/2011	
	Total		2,810.81		
			-		
<u>Power</u>					
11	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	12/2007	-
			1,007.16	12/2009	
	Total		596.45		
			-		
<u>Railways</u>					

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
12	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
13	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
14	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
15	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
16	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
17	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
18	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
19	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
20	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
21	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
22	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011
23	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
24	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
25	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
26	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
27	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
28	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
29	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
30	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
31	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
32	Dakshin-barasa-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
33	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
34	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
35	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012
36	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
37	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
38	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
39	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
40	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
41	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012
42	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
43	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
44	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	03/2012 -	03/2012
45	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	- -	-
46	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
47	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
48	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
49	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
50	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	-
51	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
52	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	- -	-
53	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	02/2006 -	-
54	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
55	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	02/2010 -	-
56	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
57	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 -	-
58	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
59	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	-
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
61	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
62	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
63	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
64	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
65	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
66	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDIL'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
67	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
68	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
69	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
70	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
71	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		19,500.65 -		
Shipping & Ports					
72	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
73	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	- 01/2009	01/2009
74	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
75	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
76	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		3,904.91 -		
Telecommunications					
77	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
78	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
79	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
80	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
81	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
82	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
	Total		2,997.75 -		
Urban Development					
83	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Grand Total			37,343.07		

Sectorwise Summary On Schedule

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Civil Aviation	2	1,078.00	.00	1,078.00	375.57
Coal	32	18,580.70	.00	18,161.18	5,691.30
Fertilisers	2	2,587.03	.00	2,587.03	1,560.00
Petroleum	22	54,562.42	.00	54,329.02	5,105.77
Power	45	99,834.65	.00	99,834.65	13,732.10
Railways	10	12,620.96	654.51	15,943.76	1,785.89
Road Transport & Highways	55	50,302.38	.00	49,942.38	25,281.28
Shipping & Ports	2	2,033.37	.00	1,963.17	1,026.20
Steel	3	842.10	.00	842.10	11.51
Urban Development	2	37,736.00	.00	37,736.00	979.74
Grand total	175	280,177.61	654.51	282,417.29	55,549.36

List of On schedule Projects

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	372.21	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070	2/2011	452.00 -	452.00	3.36	02/2015 -	02/2015
	Total		1,078.00 -	1,078.00	375.57		
	<u>Coal</u>						
3	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094	12/2009	1,943.66 -	1,943.66	1,226.21	03/2014 -	03/2014
4	KRISHNASHILA (NCL) (4MTY) - [N06000007	6/2011	789.88 -	741.62	334.36	03/2013 -	03/2013
5	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	162.06	03/2015 03/2015	03/2015
6	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	365.80	03/2016 03/2016	03/2016
7	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.35	03/2014 03/2014	03/2014
8	JALLARAM SHAFT PROJECT - [N06000025	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
9	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	114.71	03/2017 -	03/2017
10	KANIHA OCP, MCL, (10.0 Mty) - [N06000035	12/2007	457.77 -	457.77	111.49	03/2013 -	03/2013
11	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	70.82	03/2015 -	03/2015
12	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	44.49	03/2016 -	03/2016
13	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
14	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
15	RAJMAHAL OC EXP. - [N06000056	9/2009	153.82 -	153.82	24.39	03/2014 -	03/2014
16	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.63 -	479.63	110.33	03/2013 -	03/2013
17	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	27.24	03/2015 -	03/2015
18	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	204.58	03/2014 -	03/2014
19	Purnadih OCP - [N06000085	7/2008	210.98 -	210.98	87.89	03/2013 -	03/2013
20	JAGANNATHPOR OC - [N06000075	9/2008	152.43 -	152.43	-	03/2015 -	03/2015

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
21	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	1.51	03/2018 03/2018	03/2018
22	CHURCHA UG - [N06000046]	6/2008	462.35 -	462.35	263.68	03/2014 -	03/2014
23	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	6/2008	1,188.31 -	1,188.31	674.28	03/2013 -	03/2013
24	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	6/2010	2,675.67 -	2,675.67	1,386.87	03/2014 -	03/2014
25	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
26	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	39.30	03/2016 -	03/2016
27	KARTALI (EAST) OC - [N06000076]	7/2008	178.44 -	178.44	-	03/2014 -	03/2014
28	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	86.26	03/2016 -	03/2016
29	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
30	Rajrappa RCE OCP - [N06000087]	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016
31	KARMA OCP - [N06000088]	6/2009	162.46 -	162.46	30.89	03/2014 -	03/2014
32	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
33	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
34	JALAGAM VENGALA RAO OCP - [N06000094]	7/2011	447.06 -	447.06	-	03/2015 -	03/2015
	Total		18,580.70 -	18,161.18	5,691.30		
<u>Fertilisers</u>							
35	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJECT - [N08000005]	1/2010	1,294.19 -	1,294.19	769.00	01/2013 -	01/2013
36	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJECT - [N08000004]	1/2010	1,292.84 -	1,292.84	791.00	01/2013 -	01/2013
	Total		2,587.03 -	2,587.03	1,560.00		
<u>Petroleum</u>							
37	IOR of B-173A Field - [N16000140]	1/2012	352.49 -	352.49	-	03/2014 -	03/2014
38	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
39	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	-	05/2014 -	05/2014

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	6/2010	202.94 -	202.94	0.20	01/2014 -	01/2014
41	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014
42	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015
43	Wax Project - [N16000101	6/2010	576.60 -	576.60	73.04	12/2013 12/2013	12/2013
44	Construction of tanks and blending facility at Vadinar - [N16000115	2/2009	267.00 -	267.00	211.53	09/2012 09/2012	09/2012
45	Integrated Refinery Expansion Project - [N16000143	1/1999	14,225.00 -	14,225.00	30.11	12/2015 -	12/2015
46	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	12.11	03/2014 -	03/2014
47	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144	9/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016
48	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015
49	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
50	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	756.65	17.54	05/2013 -	05/2013
51	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108	11/2009	341.50 -	341.50	135.26	02/2013 -	02/2013
52	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	4/2008	825.00 -	1,827.00	611.55	04/2013 04/2013	04/2013
53	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA [N16000112	8/2010	8,140.00 -	8,140.00	1,813.56	02/2014 -	02/2014
54	Ahmedabad Redevelopment - [N16000120	11/2010	1,916.10 -	1,916.10	614.17	12/2014 -	12/2014
55	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	5.96	12/2014 -	12/2014
56	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088	8/2009	1,793.00 -	1,793.00	691.16	09/2012 -	09/2012
57	Development of WO-16 Cluster Fields - [N16000105	6/2010	2,523.00 -	2,523.00	187.77	01/2014 -	01/2014
58	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
	Total		54,562.42 -	54,329.02	5,105.77		
<u>Power</u>							
59	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121	2/2012	324.33 -	324.33	2.10	08/2014 -	08/2014

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
60	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126	3/2012	206.44 -	206.44	22.30	06/2014 -	06/2014
61	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	52.80	11/2014 -	11/2014
62	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	297.33	22.90	08/2014 -	08/2014
63	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	250.30	12/2013 -	12/2013
64	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118	1/2012	259.28 -	259.28	16.40	01/2014 -	01/2014
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	43.20	11/2014 -	11/2014
66	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111	8/2011	1,637.34 -	1,637.34	257.90	08/2014 -	08/2014
67	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	653.90	08/2013 -	08/2013
68	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	27.70	06/2015 -	06/2015
69	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
70	Supplementary transmission associated with vellur TPS - [N18000097	8/2010	170.36 -	170.36	49.20	04/2013 -	04/2013
71	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
72	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	416.60	05/2014 -	05/2014
73	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	1,746.65	50.40	08/2014 -	08/2014
74	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	67.20	02/2014 -	02/2014
75	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	901.77	60.60	08/2014 -	08/2014
76	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
77	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112	11/2011	2,127.51 -	2,127.51	240.00	07/2014 -	07/2014
78	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	-	08/2015 -	08/2015

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	Transmission system for phase-I generation projects in orissa-part B - [N18000093]	12/2010	2,743.19 -	2,743.19	861.00	12/2013 -	12/2013
80	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	99.50	10/2013 -	10/2013
81	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	104.70	02/2015 -	02/2015
82	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]	3/2011	2,569.25 -	2,569.25	681.50	03/2014 -	03/2014
83	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	335.30	01/2015 -	01/2015
84	Northern Region system strengthening scheme-XXII - [N18000091]	12/2010	209.78 -	209.78	74.80	08/2013 -	08/2013
85	Transmission system associated with krishnapatnam-Part-A - [N18000090]	12/2010	779.21 -	779.21	555.00	08/2013 -	08/2013
86	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	9/2010	2,074.86 -	2,074.86	679.60	03/2013 -	03/2013
87	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT - [N18000046]	12/2008	7,031.88 -	7,031.88	3,920.00	12/2012 -	12/2012
88	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX - [N18000088]	10/2010	182.68 -	182.68	74.80	01/2013 -	01/2013
89	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	415.40	12/2013 -	12/2013
90	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]	7/2011	181.93 -	181.93	49.80	07/2013 -	07/2013
91	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	34.10	10/2014 -	10/2014
92	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]	3/2011	1,585.12 -	1,585.12	404.30	11/2013 -	11/2013
93	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	60.10	10/2014 -	10/2014
94	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	297.90	09/2014 -	09/2014
95	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	125.40	01/2015 -	01/2015
96	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]	10/2011	558.26 -	558.26	71.90	11/2013 -	11/2013
97	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	61.30	06/2014 -	06/2014

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
98	Northern region system strengthening scheme XVI - [N18000094	7/2010	752.64 -	752.64	208.00	07/2013 -	07/2013
99	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL - PART-A2 - [N18000113	12/2011	2,422.66 -	2,422.66	73.20	08/2014 -	08/2014
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII [N18000135	9/2012	524.40 -	524.40	-	04/2015 -	04/2015
101	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	987.00	12/2016 -	12/2016
102	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	564.00	09/2016 -	09/2016
103	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	760.00	11/2016 -	11/2016
	Total		99,834.65 -	99,834.65	13,732.10		
<u>Railways</u>							
104	AGARTALA SABROOM, NL, NEFR - [N22000099	4/2008	813.34 -	1,141.75	426.35	03/2014 -	03/2014
105	SEVOK RANGPO, NEFR - [N22000102	4/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
106	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) [N22000110	4/2010	3,951.98 -	3,951.98	26.54	03/2016 -	03/2016
107	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. [N22000111	4/2010	2,619.02 -	2,913.51	159.50	03/2016 -	03/2016
108	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112	4/2008	829.74 -	829.74	4.25	03/2015 -	03/2015
109	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	7/1996	653.84 654.51	1,302.12	608.97	06/2013 06/2013	06/2013
110	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) [N22000113	4/2008	653.19 -	653.46	211.26	03/2014 -	03/2014
111	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) [N22000114	4/2008	516.23 -	516.23	284.17	03/2014 -	03/2014
112	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	4/2008	394.14 -	404.39	3.77	03/2013 -	03/2013
113	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124	4/2006	850.00 -	850.00	8.45	03/2015 -	03/2015
	Total		12,620.96 -	15,943.76	1,785.89		
<u>Road Transport & Highways</u>							
114	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	104.67	01/2014 -	01/2014
115	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150	2/2011	193.45 -	193.45	32.79	11/2012 -	11/2012

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
116	DEOLI-KOTA - [N24000148	1/2011	953.00 -	593.00	390.90	07/2013 -	07/2013
117	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
118	JAIPUR-REENGUS - [N24000198	8/2010	267.81 -	267.81	528.89	02/2013 -	02/2013
119	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
120	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	249.01	11/2013 -	11/2013
121	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	682.60	03/2014 -	03/2014
122	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	148.10	09/2014 -	09/2014
123	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	81.04	08/2013 -	08/2013
124	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.85	06/2013 -	06/2013
125	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
126	Indore-Jhabua-Gujrat/MP - [N24000136	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
127	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014
128	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013
129	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
130	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	10.01	01/2014 -	01/2014
131	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	-	10/2014 -	10/2014
132	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013
133	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	463.57	09/2014 -	09/2014
134	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	131.01	05/2014 -	05/2014
135	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	698.57	11/2013 -	11/2013
136	Kandla - Mundra port - [N24000175	1/2011	953.88 -	953.88	405.28	07/2013 -	07/2013
137	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	148.11	06/2014 -	06/2014
138	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	220.00	02/2014 -	02/2014
139	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	560.70	08/2013 -	08/2013

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
140	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	249.01	11/2013 -	11/2013
141	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	907.92	10/2014 -	10/2014
142	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	271.82	02/2014 -	02/2014
143	Hazaribagh-Ranchi - [N24000141	8/2010	625.07 -	625.07	862.54	01/2013 -	01/2013
144	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.55	01/2014 -	01/2014
145	Jaipur-Tonk-Deoli - [N24000135	6/2010	792.06 -	792.06	1,419.40	12/2012 -	12/2012
146	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	385.44	08/2013 -	08/2013
147	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	689.41	08/2013 -	08/2013
148	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	1,000.70	03/2013 -	03/2013
149	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134	4/2010	1,740.00 -	1,740.00	1,882.90	10/2012 -	10/2012
150	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
151	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	165.70	07/2014 -	07/2014
152	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	722.10	08/2013 -	08/2013
153	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4 - [N24000139	9/2010	1,655.00 -	1,655.00	436.70	09/2013 -	09/2013
154	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	420.39	03/2014 -	03/2014
155	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168	3/2011	785.50 -	785.50	558.90	08/2013 -	08/2013
156	SAMAIKHALI - GANDHIDHAM - [N24000179	9/2010	805.39 -	805.39	322.83	03/2013 -	03/2013
157	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	734.10	11/2013 -	11/2013
158	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM - [N24000145	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	05/2013
159	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
160	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	829.72	08/2014 -	08/2014
161	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	586.44	02/2013 -	02/2013
162	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	162.04	09/2013 -	09/2013

(Sep,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
163	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]	9/2010	852.00 -	852.00	731.65	03/2013 -	03/2013
164	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]	5/2010	374.00 -	374.00	77.34	05/2013 -	05/2013
165	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	470.08	06/2014 -	06/2014
166	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	441.01	07/2013 -	07/2013
167	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013
168	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	387.88	01/2014 -	01/2014
	Total		50,302.38 -	49,942.38	25,281.28		
<u>Shipping & Ports</u>							
169	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS - [N25000031]	8/2008	1,066.91 -	968.35	777.97	09/2012 -	09/2012
170	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
	Total		2,033.37 -	1,963.17	1,026.20		
<u>Steel</u>							
171	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]	1/2012	254.90 -	254.90	-	12/2014 -	12/2014
172	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]	11/2011	254.55 -	254.55	11.51	11/2013 -	11/2013
173	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078]	7/2012	332.65 -	332.65	-	08/2014 -	08/2014
	Total		842.10 -	842.10	11.51		
<u>Urban Development</u>							
174	FARIDABAD EXTENSION - [N28000057]	9/2011	2,494.00 -	2,494.00	56.69	09/2014 -	09/2014
175	DELHI MRTS PHASE-III - [N28000056]	9/2011	35,242.00 -	35,242.00	923.05	03/2016 -	03/2016
	Total		37,736.00 -	37,736.00	979.74		
	Grand Total		280,177.61	282,417.29	55,549.36		

List of Delay Project w.r.t Original and Revised

(Sep,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	15,030.00	12/2008 -	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,956.00	12/2015 -	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,199.00	12/2016 -	03/2017	3	-
Total			36,950.00 -	41,049.00	18,185.00				
<u>Civil Aviation</u>									
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,123.01	05/2011 03/2012	10/2012	17	7
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	138.65	05/2012 -	12/2012	7	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	185.20	01/2011 04/2013	04/2013	27	0
Total			2,587.58 -	2,970.07	2,446.86				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,480.61	06/2009 -	03/2013	45	-
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.57	03/2011 -	03/2013	24	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	105.43	03/2010 -	03/2014	48	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	3,462.05	03/2012 -	03/2014	24	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	100.35	03/2012 -	03/2014	24	-
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	95.86	03/2012 -	03/2014	24	-
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.22	03/2012 -	03/2014	24	-
14	Churi Benti UG - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	34.52	03/2011 -	03/2014	36	-
15	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	60.69	03/2012 -	03/2014	24	-
16	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	106.60	03/2012 -	03/2014	24	-
17	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	779.26	320.46	03/2013 09/2012	10/2014	19	25
18	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48	-
19	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36	-
20	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	118.05	03/2010 -	03/2015	60	-
21	KAKATIYA LONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	72.12	12/2012 -	03/2015	27	-
22	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44	-
23	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.83	03/2014 -	03/2016	24	-
24	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	23.29	12/2015 -	08/2017	20	-
Total			17,226.73 -	18,902.04	7,149.90				

Steel

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
25	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	248.87	08/2010 -	11/2012	27	-
26	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	105.86	10/2012 -	12/2012	2	-
27	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,785.94	12/2011 -	12/2012	12	-
28	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,007.61	12/2011 -	12/2012	12	-
29	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	252.46	02/2011 -	12/2012	22	-
30	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	340.39	12/2011 03/2012	01/2013	13	10
31	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	220.32	05/2012 -	02/2013	9	-
32	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 -	12,291.00	9,787.70	10/2009 -	03/2013	41	-
33	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,127.86	12/2012 -	03/2013	3	-
34	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	6,606.80	03/2013 -	09/2013	6	-
Total			50,973.89 -	57,131.43	35,483.81				
Petrochemicals									
35	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	5,573.34	04/2012 12/2013	12/2013	20	0
Total			5,460.61 -	8,920.00	5,573.34				
Petroleum									

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	0
36	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,203.81	09/2011 09/2012	09/2012	12	0
37	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,570.72	05/2010 05/2012	10/2012	29	5
38	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	739.84	04/2011 12/2011	10/2012	18	10
39	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	254.36	04/2011 -	10/2012	18	-
40	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	220.63	03/2012 -	10/2012	7	-
41	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,352.39	09/2011 03/2012	11/2012	14	8
42	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 312.00	312.00	250.81	01/2012 01/2012	11/2012	10	10
43	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	9,228.42	01/2012 -	11/2012	10	-
44	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,905.39	03/2012 08/2012	12/2012	9	4
45	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	521.52	12/2011 -	01/2013	13	-
46	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	269.29	03/2006 03/2013	03/2013	84	0
47	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.38	05/2010 03/2013	03/2013	34	0
48	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,164.58	06/2012 03/2013	03/2013	9	0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
49	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24	22
50	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012 -	03/2013	7	-
51	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
52	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
53	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	620.97	07/2012 -	04/2013	9	-
54	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	75.58	03/2013 -	04/2013	1	-
55	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	514.86	03/2010 03/2012	05/2013	38	14
56	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34	12
57	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86	12
58	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,147.97	06/2012 -	06/2013	12	-
59	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	252.30	07/2012 07/2012	06/2013	11	11
60	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	199.82	01/2013 -	06/2013	5	-
61	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.25	09/2011 -	08/2013	23	-

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
62	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	18,078.00	11/2012 09/2013	09/2013	10	0
63	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	4,258.26	09/2012 -	09/2013	12	-
64	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	43.73	09/2012 -	09/2013	12	-
65	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	43.99	11/2012 -	10/2013	11	-
66	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	10/2013	16	-
67	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
68	Fire water network at Uran - [N16000141]ONGC,Maharashtra	05/2010	171.68 -	171.68	2.40	06/2013 -	11/2013	5	-
69	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,777.01	08/2010 03/2012	12/2013	40	21
70	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	1,059.76	12/2012 12/2012	12/2013	12	12
71	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5	-
72	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	629.66	03/2007 03/2014	03/2014	84	0
73	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	938.59	03/2013 -	03/2014	12	-
74	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	427.67	03/2013 -	04/2014	13	-
75	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.48	10/2010 -	12/2014	50	-
76	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.54	01/2013 -	07/2015	30	-
77	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,535.20	03/2007 03/2017	03/2017	120	0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
78	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00	261.00	198.79	03/2012 08/2012	09/2012	6	1
	Total		114,450.90	122,888.70	72,189.48				
	<u>Power</u>								
79	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	754.57	02/2011 10/2012	10/2012	20	0
80	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	124.08	06/2012	10/2012	4	-
81	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	158.70	04/2012	10/2012	6	-
82	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	329.43	07/2011	11/2012	16	-
83	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,091.10	02/2012	11/2012	9	-
84	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	1,029.30	06/2012	11/2012	5	-
85	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	5,221.23	3,157.30	07/2010	12/2012	29	-
86	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	654.70	05/2012	12/2012	7	-
87	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	794.58	08/2010 01/2013	01/2013	29	0
88	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,563.13	03/2007 09/2012	02/2013	71	5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
89	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	590.80	01/2010 -	02/2013	37	-
90	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,081.00	1,787.44	11/2009 02/2013	03/2013	40	1
91	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,840.51	09/2008 -	03/2013	54	-
92	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	867.25	10/2009 -	03/2013	41	-
93	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	412.10	09/2010 -	03/2013	30	-
94	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,456.00	08/2012 -	03/2013	7	-
95	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	151.30	11/2011 -	03/2013	16	-
96	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,976.70	08/2012 -	03/2013	7	-
97	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,380.80	08/2012 -	03/2013	7	-
98	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00 -	5,915.00	3,857.00	10/2012 -	03/2013	5	-
99	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	444.20	11/2012 -	03/2013	4	-
100	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	52.40	10/2012 -	03/2013	5	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
101	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,567.00	10/2012 -	05/2013	7	-
102	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,912.00	10/2010 01/2013	06/2013	32	5
103	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,587.00	11/2012 -	06/2013	7	-
104	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,948.02	01/2012 -	09/2013	20	-
105	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,947.70	10/2012 -	09/2013	11	-
106	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,194.26	09/2009 06/2013	10/2013	49	4
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	541.10	04/2013 -	10/2013	6	-
108	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	58.40	01/2013 -	11/2013	10	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	318.00	11/2011 -	12/2013	25	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	341.90	11/2011 -	12/2013	25	-
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	242.50	02/2012 -	12/2013	22	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
112	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	917.70	12/2012 -	12/2013	12	-
113	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	759.10	08/2012 -	12/2013	16	-
114	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,495.00	04/2009 03/2014	03/2014	59	0
115	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	422.50	11/2012 -	03/2014	16	-
116	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	396.44	08/2012 08/2013	09/2014	25	13
117	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,633.00	08/2013 -	09/2014	13	-
118	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,078.60	08/2013 -	09/2014	13	-
119	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,325.00	07/2011 -	11/2014	40	-
120	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	349.99	07/2014 -	02/2015	7	-
121	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2015	12	-
122	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	376.32	07/2010 02/2016	02/2016	67	0
123	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,417.00	12/2009 12/2014	03/2016	75	15
124	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	319.72	07/2014 -	05/2016	22	-
125	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,689.17	01/2016 01/2016	11/2016	10	10

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
126	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,761.64	09/2010 08/2014	03/2017	78	31
127	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,973.46	05/2013 06/2016	03/2017	46	9
128	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,554.41	09/2009 07/2014	12/2017	99	41
Total			127,548.95	140,934.29	87,600.32				
<u>Railways</u>									
129	KADUR-CHIKMAGALUR-SAKLHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	339.00	221.13	03/2012 03/2012	10/2012	7	7
130	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	301.82	06/2004 -	12/2012	102	-
131	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	425.36	03/2012 03/2012	12/2012	9	9
132	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	792.32	03/2009 12/2012	12/2012	45	0
133	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,514.74	10/2007 12/2012	12/2012	62	0
134	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya Pradesh	09/2007	687.20 -	687.20	667.39	03/2010 -	12/2012	33	-
135	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	204.65	03/2002 -	01/2013	130	-
136	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	897.49	12/2012 01/2013	01/2013	1	0
137	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	661.92	03/2012 08/2012	02/2013	11	6
138	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.85	02/2011 02/2011	02/2013	24	24
139	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	420.44	12/2012 12/2012	02/2013	2	2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
140	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-
141	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	565.12	12/2011 12/2011	03/2013	15	15
142	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	272.94	03/2012 03/2013	03/2013	12	0
143	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	395.87	03/2012 03/2013	03/2013	12	0
144	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	101.40	03/2012 -	03/2013	12	-
145	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	02/2009 02/2009	04/2013	50	50
146	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	213.62	03/2009 03/2009	04/2013	49	49
147	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	145.89	12/2012 -	05/2013	5	-
148	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	108.12	12/2011 11/2013	11/2013	23	0
149	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,195.95	03/2009 -	12/2013	57	-
150	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	204.17	03/2004 12/2010	03/2014	120	39
151	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,298.65	12/2008 -	03/2014	63	-
152	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	163.86	06/2013 06/2013	03/2014	9	9
153	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	401.19	03/2013 -	03/2014	12	-
154	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	114.08	12/2012 -	03/2014	15	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	0
155	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 325.00	820.40	158.14	03/2010 06/2014	06/2014	51	0
156	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	169.68	03/2007 03/2007	03/2015	96	96
157	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	732.83	12/2010 12/2010	03/2015	51	51
158	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	12.87	04/2014 -	03/2015	11	-
159	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.02	2,501.02	04/2008 03/2014	12/2015	92	21
160	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	937.59	03/2011 03/2014	03/2016	60	24
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	851.16	03/2014 03/2016	03/2016	24	0
162	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	36.41	03/2014 03/2016	03/2016	24	0
163	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	451.90	03/2005 12/2008	06/2016	135	90
164	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	427.98	06/2005 07/2011	06/2016	132	59
165	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	24.50	03/2016 -	06/2016	3	-
166	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 2,500.00	20,000.00	8,069.06	03/2001 -	12/2017	201	-
	Total		25,521.41 -	67,077.30	28,477.38				
Road Transport & Highways									
167	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	180.55	08/2004 07/2010	10/2012	98	27

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
168	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	187.45	08/2004 -	10/2012	98	-
169	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	10/2012	91	-
170	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	275.00	306.65	09/2007 -	10/2012	61	-
171	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	279.16	09/2007 -	10/2012	61	-
172	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27 -	193.10	163.42	03/2008 -	10/2012	55	-
173	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30	190.61	10/2008 -	10/2012	48	-
174	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	285.12	11/2008 -	10/2012	47	-
175	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60 -	407.60	185.90	06/2010 -	10/2012	28	-
176	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16	-
177	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,665.60	08/2011 -	10/2012	14	-
178	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00 -	388.00	515.85	05/2012 -	10/2012	5	-
179	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	10/2012	8	-
180	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	11/2012	41	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
181	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	136.62	04/2004 -	12/2012	104	-
182	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	259.92	01/2009 -	12/2012	47	-
183	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	282.86	06/2008 -	12/2012	54	-
184	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	249.10	06/2008 -	12/2012	54	-
185	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	398.78	09/2008 -	12/2012	51	-
186	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhyapradesh	12/2003	203.43 -	203.43	238.88	10/2008 -	12/2012	50	-
187	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhyapradesh	12/2003	251.03 -	251.03	312.28	10/2008 -	12/2012	50	-
188	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhyapradesh	12/2003	229.91 -	229.91	266.58	10/2008 -	12/2012	50	-
189	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	184.45	07/2008 -	12/2012	53	-
190	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	649.30	09/2008 -	12/2012	51	-
191	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	274.59	06/2008 -	12/2012	54	-
192	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	152.01	04/2008 -	12/2012	56	-
193	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	257.38	06/2011 06/2011	12/2012	18	18
194	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	211.04	04/2008 -	12/2012	56	-
195	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	266.78	04/2008 -	12/2012	56	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
196	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48	-
197	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	271.71	02/2004	12/2012	106	-
198	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	218.06	04/2010	12/2012	32	-
199	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38	-
200	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	274.33	09/2010	12/2012	27	-
201	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	189.38	02/2004	12/2012	106	-
202	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	535.42	01/2011	12/2012	23	-
203	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	592.82	05/2010	12/2012	31	-
204	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	11.43	07/2012	12/2012	5	-
205	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6	-
206	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,025.70	05/2012	12/2012	7	-
207	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,229.70	10/2011	12/2012	14	-
208	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.36	10/2008	02/2013	52	-
209	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	02/2013	25	-

S.No Project		Date of Approval	Date of Commissioning		Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10	11	12
210	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	203.42	09/2007	03/2013	66	-		
211	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	129.40	09/2008	03/2013	54	-		
212	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	226.46	06/2005	03/2013	93	-		
213	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	223.07	05/2008	03/2013	58	-		
214	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	294.21	10/2008	03/2013	53	-		
215	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	386.80	03/2008	03/2013	60	-		
216	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	118.02	04/2009	03/2013	47	-		
217	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	207.72	06/2008	03/2013	57	-		
218	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	287.76	06/2008	03/2013	57	-		
219	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.21	03/2008	03/2013	60	-		
220	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	244.23	06/2008	03/2013	57	-		
221	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	184.17	05/2008	03/2013	58	-		
222	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	231.15	06/2008	03/2013	57	-		
223	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	469.66	09/2009	03/2013	42	-		

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
224	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32	-
225	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	1,509.10	1,427.90	09/2012 -	03/2013	6	-
226	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	276.30	02/2009 05/2014	05/2013	51	-12
227	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	703.31	10/2011 -	06/2013	20	-
228	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	1,159.80	11/2012 -	06/2013	7	-
229	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	62.08	04/2009 -	07/2013	51	-
230	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	93.99	11/2008 -	07/2013	56	-
231	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	494.29	12/2009 -	07/2013	43	-
232	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,460.90	11/2011 -	08/2013	21	-
233	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-
234	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	209.00	3.82	01/2013 -	10/2013	9	-
235	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-
236	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	21.35	11/2008 -	01/2014	62	-
237	INDORE-DEWAS (NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	378.82	05/2013 -	02/2014	9	-
238	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	175.01	10/2008 -	03/2014	65	-
239	AGRA-BYPASS (NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	181.87	09/2007 -	03/2014	78	-

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
240	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	363.44	10/2011 -	03/2014	29	-
241	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19	-
242	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	352.38	05/2013 -	03/2014	10	-
243	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	414.01	03/2013 -	03/2014	12	-
244	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014	79	-
245	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	51.63	07/2009 -	04/2014	57	-
246	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	222.49	02/2014 -	04/2014	2	-
247	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
248	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	34.16	09/2013 -	07/2014	10	-
249	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90 -	635.90	-	07/2012 -	07/2014	24	-
250	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
251	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
252	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
253	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
Total			40,109.42 -	42,048.04	37,793.39				

Shipping & Ports

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
254	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Mahara shtra	04/2009	290.85 -	305.00	194.14	06/2011 09/2012	09/2012	15	0
255	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Mahara shtra	04/2009	277.03 280.00	277.03	188.88	12/2011 09/2012	09/2012	9	0
256	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Mahara shtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18	0
257	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
258	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
259	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,433.40	01/2012 09/2012	12/2012	11	3
260	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
261	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Mahara shtra	08/2010	612.72 627.64	627.64	214.65	12/2012 05/2013	05/2013	5	0
262	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87	0
263	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	863.93	12/2010 09/2012	10/2013	34	13
Total			8,446.14 -	10,038.71	5,583.71				
<u>Telecommunications</u>									
264	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	12/2012	48	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
265	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	80.04	06/2009 -	12/2012	42	-
266	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	12/2012	45	-
267	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	813.72	11/2010 -	12/2012	25	-
268	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72	11
269	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	03/2013	50	-
270	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2013	29	12
Total			2,737.73 -	2,741.60	1,544.97				
Urban Development									
271	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21	-
Total			6,395.00 -	11,609.00	2,267.57				
Water Resources									
272	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-
Total			542.90 -	1,187.00	35.49				
Grand Total			438,951.26	527,497.18	304,331.22				

Sectorwise Summary of Project Without Milestone

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	1	1,106.29	.00	1,106.29	1,084.24
Civil Aviation	6	5,473.58	2,015.00	6,063.07	4,499.06
Coal	6	3,868.49	1,666.38	3,657.55	233.76
Fertilisers	2	763.00	.00	763.00	425.03
Petroleum	48	107,050.08	35,350.85	115,876.84	38,510.34
Power	18	50,930.65	.00	51,782.46	7,847.68
Railways	125	63,915.28	66,634.04	145,454.18	61,863.05
Road Transport & Highways	141	90,215.30	.00	91,793.92	62,817.29
Shipping & Ports	18	16,087.68	9,708.64	18,300.73	8,143.40
Steel	2	587.55	.00	587.55	0.00
Telecommunications	13	5,735.48	1,318.73	5,676.27	1,656.61
Urban Development	3	37,850.18	173.08	37,909.08	979.74
Water Resources	1	542.90	.00	1,187.00	35.49
Grand total	384	384,126.46	116,866.72	480,157.94	188,095.69

List of Projects Without Milestones

(Sep,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 04/2011	04/2012	0/0
	Total		1,106.29 -			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 03/2012	10/2012	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	12/2012	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	04/2013	0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	02/2015 -	02/2015	0/0
	Total		5,473.58 -			0/0
<u>Coal</u>						
8	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	03/2014 -	03/2014	0/0
9	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	04/2014 -	04/2014	0/0
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	03/2015 03/2015	03/2015	0/0
11	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	03/2016 -	03/2016	0/0
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 03/2018	03/2018	0/0
	Total		3,868.49 -			0/0
<u>Fertilisers</u>						
14	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012	0/0
15	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012	0/0
	Total		763.00 -			0/0
<u>Steel</u>						

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
16	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh - [N12000078]SAIL, Delhi	07/2012	332.65 -	08/2014 -	08/2014	0/0
17	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]SAIL, Delhi	01/2012	254.90 -	12/2014 -	12/2014	0/0
	Total		587.55 -			0/0
Petroleum						
18	Construction of tanks and blending facility at Vad - [N16000115]IOCL, Gujarat	02/2009	267.00 -	09/2012 09/2012	09/2012	0/0
19	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	10/2012	0/0
20	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	04/2011 -	10/2012	0/0
21	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	11/2012	0/0
22	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
23	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
24	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	03/2011 05/2011	03/2013	0/0
25	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	08/2012 -	03/2013	0/0
26	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
27	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
28	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
29	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
30	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
31	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
32	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
33	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
34	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	09/2011 -	08/2013	0/0
35	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
36	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
37	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
38	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	06/2012 -	10/2013	0/0
39	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	Fire water network at Uran - [N16000141]ONGC,Maharashtra	05/2010	171.68	06/2013	11/2013	0/0
			-	-		
41	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	08/2010	12/2013	0/0
			5,633.44	03/2012		
42	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	12/2013	12/2013	0/0
			-	12/2013		
43	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	01/2014	01/2014	0/0
			-	-		
44	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	08/2013	01/2014	0/0
			-	-		
45	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94	01/2014	01/2014	0/0
			-	-		
46	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	02/2014	02/2014	0/0
			-	-		
47	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	03/2013	03/2014	0/0
			-	-		
48	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00	03/2014	03/2014	0/0
			-	-		
49	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49	03/2014	03/2014	0/0
			-	-		
50	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	03/2013	04/2014	0/0
			-	-		
51	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17	05/2014	05/2014	0/0
			-	-		
52	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	05/2014	05/2014	0/0
			-	-		
53	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	10/2010	12/2014	0/0
			-	-		
54	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	12/2014	12/2014	0/0
			-	-		
55	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	12/2014	12/2014	0/0
			-	-		
56	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17	12/2014	12/2014	0/0
			-	-		
57	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00	12/2014	12/2014	0/0
			-	-		
58	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	03/2015	03/2015	0/0
			-	-		
59	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	04/2015	04/2015	0/0
			-	-		
60	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40	05/2015	05/2015	0/0
			-	-		
61	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	01/2013	07/2015	0/0
			-	-		
62	IROP - [N16000143]BPCL,Kerala	01/1999	14,225.00	12/2015	12/2015	0/0
			-	-		
63	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	06/2016	06/2016	0/0
			-	-		
64	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-	0/0
			-	-		
65	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	04/2012	-	0/0
			-	-		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		107,050.08			0/0
			-			
	<u>Power</u>					
66	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	10/2012	0/0
			-	-		
67	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	10/2010	06/2013	0/0
			-	01/2013		
68	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	07/2013	07/2013	0/0
			-	-		
69	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03	01/2012	09/2013	0/0
			-	-		
70	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	09/2009	10/2013	0/0
			-	06/2013		
71	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	03/2014	03/2014	0/0
			-	-		
72	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	08/2014	08/2014	0/0
			-	-		
73	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	09/2014	09/2014	0/0
			-	-		
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63	11/2014	11/2014	0/0
			-	-		
75	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	11/2014	11/2014	0/0
			-	-		
76	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	02/2015	02/2015	0/0
			-	-		
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34	03/2015	03/2015	0/0
			-	-		
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40	04/2015	04/2015	0/0
			-	-		
79	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40	08/2015	08/2015	0/0
			-	-		
80	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	12/2014	12/2015	0/0
			-	-		
81	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47	09/2016	09/2016	0/0
			-	-		
82	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18	11/2016	11/2016	0/0
			-	-		
83	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19	12/2016	12/2016	0/0
			-	-		
	Total		50,930.65			0/0
			-			
	<u>Railways</u>					
84	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	03/1998	08/2005	0/0
			604.04	08/2005		
85	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00	06/2007	06/2007	0/0
			625.30	-		
86	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00	07/2008	07/2008	0/0
			363.26	-		
87	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42	-	05/2009	0/0
			369.70	05/2009		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
88	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
89	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
90	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
91	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
92	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
93	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
94	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
95	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
96	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
97	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
98	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
99	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
100	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
101	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
102	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
103	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
104	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
105	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
106	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
107	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012	0/0
108	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
109	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
110	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
111	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
112	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
113	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
114	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
115	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
116	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	03/2012 -	03/2012	0/0
117	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	10/2012	0/0
118	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
119	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
120	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
121	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2012	0/0
122	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2012	0/0
123	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
124	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
125	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	- -	12/2012	0/0
126	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	01/2013	0/0
127	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
128	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0
129	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	02/2013	0/0
130	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
131	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
132	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
133	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
134	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
135	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	03/2013	0/0
136	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
137	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
138	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2013	0/0
139	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
140	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2013	0/0
141	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
142	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
143	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	03/2013	0/0
144	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
145	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
146	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
148	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	05/2013	0/0
149	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2013	06/2013	0/0
150	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
151	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
152	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2013	0/0
153	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
155	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
156	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
157	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2014	0/0
158	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	03/2014	0/0
159	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
160	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
161	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
162	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2014	0/0
163	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 325.00	03/2010 06/2014	06/2014	0/0
164	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
165	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
166	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
167	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	04/2014 -	03/2015	0/0
168	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
169	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
170	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2015	0/0
171	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
172	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
173	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2016	0/0
174	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
175	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
176	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
177	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
178	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
179	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
180	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
181	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
182	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
183	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
184	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
185	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
186	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
187	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	-	0/0
188	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-	0/0
189	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-	0/0
190	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	02/2006 -	-	0/0
191	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
192	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 -	02/2010 -	-	0/0
193	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
194	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
195	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
196	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	-	0/0
197	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
198	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
199	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
200	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
201	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
202	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
203	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
204	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
205	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
206	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
207	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
208	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		63,915.28 -			0/0
Road Transport & Highways						
209	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	10/2012	0/0
210	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	10/2012	0/0
211	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	10/2012	0/0
212	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	09/2007 -	10/2012	0/0
213	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	10/2012	0/0
214	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	10/2012	0/0
215	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	10/2008 -	10/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
216	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	10/2012	0/0
217	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012	0/0
218	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
219	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	10/2012	0/0
220	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
221	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	05/2012 -	10/2012	0/0
222	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	10/2012	0/0
223	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
224	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
225	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	12/2012	0/0
226	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2012	0/0
227	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	06/2008 -	12/2012	0/0
228	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
229	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
230	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
231	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
232	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	12/2012	0/0
233	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0
234	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	12/2012	0/0
235	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2012	0/0
236	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
237	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
238	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
239	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	12/2012	0/0
240	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	12/2012	0/0
241	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
242	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	10/2009	12/2012	0/0
			-	-		
243	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	09/2010	12/2012	0/0
			-	-		
244	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	02/2004	12/2012	0/0
			-	-		
245	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	01/2011	12/2012	0/0
			-	-		
246	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	05/2010	12/2012	0/0
			-	-		
247	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	07/2012	12/2012	0/0
			-	-		
248	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	06/2012	12/2012	0/0
			-	-		
249	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	05/2012	12/2012	0/0
			-	-		
250	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	10/2011	12/2012	0/0
			-	-		
251	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	12/2012	12/2012	0/0
			-	-		
252	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	01/2013	01/2013	0/0
			-	-		
253	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	10/2008	02/2013	0/0
			-	-		
254	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	01/2011	02/2013	0/0
			-	-		
255	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	02/2013	02/2013	0/0
			-	-		
256	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	02/2013	02/2013	0/0
			-	-		
257	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	09/2007	03/2013	0/0
			-	-		
258	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	09/2008	03/2013	0/0
			-	-		
259	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	06/2005	03/2013	0/0
			-	-		
260	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	05/2008	03/2013	0/0
			-	-		
261	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	10/2008	03/2013	0/0
			-	-		
262	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	03/2008	03/2013	0/0
			-	-		
263	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	04/2009	03/2013	0/0
			-	-		
264	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	06/2008	03/2013	0/0
			-	-		
265	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	06/2008	03/2013	0/0
			-	-		
266	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	03/2008	03/2013	0/0
			-	-		
267	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	06/2008	03/2013	0/0
			-	-		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
268	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	05/2008 -	03/2013	0/0
269	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	06/2008 -	03/2013	0/0
270	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	09/2009 -	03/2013	0/0
271	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
272	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	09/2012 -	03/2013	0/0
273	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
274	PUNE-SATARA (NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
275	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
276	Indore-Jhabua-Gujarat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
277	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	02/2009 05/2014	05/2013	0/0
278	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
279	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
280	Chilikaluripet-Vijaywada 6 lane (km 355 to km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
281	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
282	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
283	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
284	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
285	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
286	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
287	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	12/2009 -	07/2013	0/0
288	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0
289	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0
290	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
291	Panipat-Jalandhar 6 lane (km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
292	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
293	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
294	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	08/2013	08/2013	0/0
295	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	08/2013	08/2013	0/0
296	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
297	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	08/2013	08/2013	0/0
298	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	08/2013	08/2013	0/0
299	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
300	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
301	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	05/2012	10/2013	0/0
302	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
303	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	01/2013	10/2013	0/0
304	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
305	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
306	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
307	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
308	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	02/2010	12/2013	0/0
309	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
310	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
311	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	11/2008	01/2014	0/0
312	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	01/2014	01/2014	0/0
313	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	01/2014	01/2014	0/0
314	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00	01/2014	01/2014	0/0
315	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36	01/2014	01/2014	0/0
316	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	05/2013	02/2014	0/0
317	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00	02/2014	02/2014	0/0
318	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhandd	02/2012	398.00	02/2014	02/2014	0/0
319	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	10/2008	03/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
320	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
321	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
322	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2014	0/0
323	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
324	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
325	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
326	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
327	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
328	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
329	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
330	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
331	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
332	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
333	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
334	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
335	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
336	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
337	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
338	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
339	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
340	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
341	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
342	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
343	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
344	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
345	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
346	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19	10/2014	10/2014	0/0
			-	-		
347	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	02/2010	12/2014	0/0
			-	-		
348	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00	06/2015	05/2016	0/0
			-	-		
349	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	07/2015	06/2016	0/0
			-	-		
	Total		90,215.30			0/0
			-			
Shipping & Ports						
350	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	10/2008	10/2008	0/0
			1,571.60	-		
351	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	04/2009	02/2011	0/0
			298.17	11/2009		
352	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	03/2012	03/2012	0/0
			-	-		
353	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	09/2012	09/2012	0/0
			-	-		
354	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	06/2011	09/2012	0/0
			-	09/2012		
355	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03	12/2011	09/2012	0/0
			280.00	09/2012		
356	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	04/2011	10/2012	0/0
			-	10/2012		
357	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	06/2010	11/2012	0/0
			-	-		
358	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	02/2011	12/2012	0/0
			-	-		
359	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	01/2012	12/2012	0/0
			4,150.00	09/2012		
360	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	03/2011	03/2013	0/0
			-	-		
361	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00	05/2013	03/2013	0/0
			-	-		
362	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	12/2012	05/2013	0/0
			627.64	05/2013		
363	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00	03/2006	06/2013	0/0
			309.00	06/2013		
364	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	12/2010	10/2013	0/0
			1,460.00	09/2012		
365	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10	12/2013	10/2013	0/0
			1,012.23	-		
366	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	02/2014	02/2014	0/0
			-	-		
367	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	10/2008	-	0/0
			-	11/2010		
	Total		16,087.68			0/0
			-			

Telecommunications

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
368	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
369	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
370	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	12/2012	0/0
371	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	12/2012	0/0
372	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	12/2012	0/0
373	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2012	02/2013	0/0
374	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	03/2013	0/0
375	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	03/2013	0/0
376	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
377	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
378	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
379	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
380	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
	Total		5,735.48 -			0/0
Urban Development						
381	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
382	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
383	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
384	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			384,126.46			0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
