



287th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.100 Crore and above)
SEPTEMBER, 2009

Ministry of Statistics & Programme Implementation
Sardar Patel Bhawan, New Delhi
Website:- www.cspm.gov.in

Contents

Executive Summary	1 -3
Month wise list of completed projects Costing Rs. 100 Crore and Above During 2008-09	4-15
Summary of Projects	1-16
Graph	16-22
Sector wise analysis of projects	23-48

EXECUTIVE SUMMARY

The 287th Flash Report for September' 2009, that contains information on the status of 591 projects in the Central Sector, each costing Rs. 100 crore and above. During September' 2009, nine projects reported completion and have been dropped from the monitor of this Ministry. During the month under reference, 2 new projects have been added. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	154
2.	RAILWAYS	151
3.	POWER	83
4.	PETROLEUM	65
5.	COAL	40
6.	TELECOMMUNICATION	31
7.	STEEL	29
8.	SHIPPING & PORTS	18
9.	CIVIL AVIATION	9
10.	ATOMIC ENERGY	5
11.	URBAN DEVELOPMENT	3
12.	MINES	1
13.	HEALTH & FW	1
14.	WATER RESOURCES	1
Total		591

2. Forty seven (47) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1-26 months in respect of projects relating to Atomic Energy, Coal, Civil Aviation, Steel, Petroleum, Power, Railways and Road Transport and Highways sectors.

3. In the **Atomic Energy Sector**, 2 projects have reported additional delays as compared to the position in the previous month. Kaiga Atomic Power Project units 3&4, Kaiga and Rajasthan Atomic Power Project units 5&6, Rawatbhata have reported additional delay of one month each due to delay in supply of fuel.

4. In the **Civil Aviation Sector**, Construction of Expandable Modular Integrated terminal Building, Raja Bhoj Airport, Bhopal (MP) has reported additional delays of 3 months due to delay in issuance of drawings/details by consultant M/s D K Associates, New Delhi.
5. In the **Coal sector**, 3 projects have reported additional delays in the range of 2-3 months. Chitra East OCP has reported additional delays of 24 months due to delay in land acquisition and poor response of global tender. Rajmahal OC expansion has reported additional delays of 12 months due to diversion of forest land and delay in EMP clearance. Barsingasar Lignite Mine (Neyveli Lignite Corporation) has reported additional delay of 1 month due to delay in preparation of tender documents and inadequate mobilization of resources by the contractor. Barsingasar TPS of 250 MW has reported additional delay of 2 months due to delay in supply of indigenous equipments and delay in erection of equipment.
6. In the **Steel Sector**, 3 projects have reported additional delays in the range of 1-13 months. Rebuilding of Coke oven Battery No 4 has reported additional delay of two months due to delay in supply of equipment and erection by M/s Mecon. Installation of Turbo Blower-8 in Turbo Blower Station has reported additional delays of two months due to termination of contract for main package. Coal Dust Injection System for Blast Furnace-2 & 3 has reported additional delays of 5 months due to relocation of Coal handling and storage site under expansion plan.
7. In the **Petroleum Sector**, 5 projects have reported additional delays in the range of 2 to 13 months. Development of B – 193 Cluster fields have reported additional delay of 7 months due to termination of contract. Development of B – 22 Cluster fields have reported additional delays of 13 months due to court cases and subsequent termination of tender. Sultanpur Neemrana Pipeline Project, LPG processing & Compression, C2-C3 and LPG Recovery from LNG at Dahej have reported additional delays of 5 months, 2 months, and 3 months respectively, however, no reasons have been provided by the respective project authorities.
8. In the **Power Sector**, 9 projects have reported additional delays in the range of 1-26 months. Koldam HEP Transmission System 396 CKM, SIPAT II Supplementary transmission system (1167 CKM), Koteswar Transmission System (PGCIL), Kunadankulam

APP Transmission System (1838 CKM), Neyveli TS-II Transmission System (838 CKM) have reported additional delays of 2 months, 2 months, 3 months, 2 months, and 2 months respectively due to change in completion schedule of linked Generation Projects. Kameng Hydro Electric Project 4X150 MW has reported additional delay of 26 months due to change in design of works, adverse geological conditions and heavy seepage of water inside the tunnel. BARH STPP, 3x660 MW has reported additional delay of 4 months due to delay in supply of material. System Strengthening VII of Southern Region (396 CKM) has reported additional delay of 1 month due to revision of works. Northern region system strengthening Scheme VI (54 CKM) has reported additional delay of 2 months, however, no specific reason has been provided by the project authorities.

9. In the Road Transport and Highways Sector, 22 projects have reported additional delays in the range of 1-6 months. Ganga Bridge Ramdevi Crossing, KM 75 - KM 80.06 NH-25 (UP) has reported additional delay of 6 months due to delay in land acquisition and shifting of an archaeological monument near the project site. For other projects, the reason of delays include land acquisition problem, slow progress of work by the contractors, law and order problems and shifting of archeological monuments. However, the project authorities have not indicated any specific reasons for such delays.

10. In the Railways Sector, Manderhill -Dumka - Rampurhat has reported additional delay of 3 months due to delay in acquisition of land.

Status as on 01.11.2009 in respect of completion of projects costing Rs.100 crore and above in different sectors during 2009-10 is indicated in the following tables.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Delayed
1	Road Transport & Highways	154	22
2	Railways	151	4
3	Power	83	9
4	Petroleum	65	5
5	Coal	40	4
6	Telecommunications	31	0
7	Steel	29	3
8	Shipping & Ports	18	0
9	Civil Aviation	9	1
10	Atomic Energy	5	2
11	Urban Development	3	0
12	Mines	1	0
13	Health & Family Welfare	1	0
14	Water Resources	1	0
	Total	591	50

ANNEXURE-I

Month wise List of Completed Project Costing Rs.100 Crores and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crores)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crores)
April,2009				
<u>Steel</u>				
1	COKE OVEN BATTERY NO. 4(PHASE-1) (RINL)(RASTRIYA ISPAT NIGAM LIMITED) - [120100061]	286.63	12/2006	301.25
May,2009				
<u>Petroleum</u>				
2	AUGMENTATION OF MUNDRA-PANIPAT CRUDE OIL PIPELINE(INDIAN OIL CORPORATION LIMITED) - [160100291]	205.00	03/2008	140.55
<u>Road Transport & Highways</u>				
3	JHANSI-SHIVPURI ,NH-25,NH-25 KM-91-50(NHDP,P) - [240106251]	220.31	05/2008	149.02
4	BHARATPUR MAHAHA, NH-11, KM.63 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106259]	250.00	01/2010	341.10
5	AMBALA-ZIRAKPUR, NH-21AND22, KM.5/735 TO KM.39/961(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106261]	298.00	11/2010	364.62
6	KONDHALI-TELEGAON(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000041]	212.00	03/2010	331.87
<u>Telecommunications</u>				
7	GSM BASED NETWORK EXPANSION PH-IV (BSNL) (U.P. WEST)(BHARAT SANCHAR NIGAM LIMITED) - [260100081]	359.07	06/2009	36.19
8	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(PUNJAB)(BHARAT SANCHAR NIGAM LIMITED) - [260100089]	508.63	06/2010	365.16
9	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(RAJASTHAN)(BHARAT SANCHAR NIGAM LIMITED) - [260100090]	448.91	06/2009	154.52
10	GSM BASED NETWORK(PH-IV)(BSNL) ORISSA(BHARAT SANCHAR NIGAM LIMITED) - [260100093]	164.06	12/2009	89.29
11	GSM-NETWORK EXPANSION(PH-IV) (BSNL) W. BENGAL(BHARAT SANCHAR NIGAM LIMITED) - [260100094]	428.00	06/2009	200.00
June,2009				
<u>Petroleum</u>				
12	GREEN FUELS & EMISSION CONTROL (HPCL) MUMBAI REF.(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100236]	1,152.00	06/2009	1,551.79
<u>Railways</u>				
13	THANE-TURBHE-NERUL-VASHI(MTP)(METROPOLITAN TRANSPORT PROJECTS) - [220100159]	403.39	03/2000	400.60

Month wise List of Completed Project Costing Rs.100 Crores and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crores)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crores)
<u>Road Transport & Highways</u>				
14	PARADIP PORT, NH-5A (PORT CONNECTIVITY) KM 0 - KM 77(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100202]	428.00	02/2007	459.38
15	SWAROOPGANJ TO BAKARIA (RJ-1) PH.II, KM.29-KM.0 (NH-76)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106229]	220.00	04/2010	244.47
16	RAJASTHAN/MP BORDER TO KOTA(RJ-10), KM.509- 449.15, NH-76(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106254]	378.22	04/2008	365.05
17	RJ/MP BORDER TO KOTA(RJ-9) NH-76, KM.449.15 TO KM.406(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106255]	297.72	04/2008	289.88
18	AGRA-BHARATPUR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000027]	195.00	03/2009	192.10
19	PALANPUR TO SWAROOPGANJ, NH-14(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000067]	498.00	03/2009	82.09
July, 2009				
<u>Power</u>				
20	KAHAL GAON STPP STAGE - II (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100230]	5,868.31	05/2007	4,881.17
<u>Road Transport & Highways</u>				
21	GARAMORE TO BAMANBORE (PACK.-III) PH.-II, KM.254-KM.182.60(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106215]	360.70	11/2007	334.72
22	TINDIVANAM-UIUNDURPET, KM 121-192.25 NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000082]	480.00	03/2009	1,130.80
<u>Telecommunications</u>				
23	COMM. OF GSM EQU. OF 600K LINES(PH-4)(BHARAT SANCHAR NIGAM LIMITED) - [N26000032]	214.00	01/2007	120.48
24	PROJECT NIB-II BROADBAND MULTIPLY(BHARAT SANCHAR NIGAM LIMITED) - [N26000047]	1,008.00	03/2009	337.50
August, 2009				
<u>Power</u>				
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000025]	220.69	04/2009	131.26
<u>Railways</u>				
26	MADURAI-DINDIGUL, (LD)(SR)(SR) - [N22000047]	73.19	-	181.81
<u>Road Transport & Highways</u>				
27	TIRUNELVEI-PANAGUDI, KM 160-203(T.N)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106242]	423.54	03/2008	220.40

Month wise List of Completed Project Costing Rs.100 Crores and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crores)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crores)
28	SALEM TO KARUR (NS-21 OF TN-2), KM.207.050-KM.248.625, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106270]	253.50	01/2009	333.34
29	SALEM TO KARUR, KM.258-645 TO KM.292.6(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106271]	205.60	08/2008	323.94
30	SALEM TO KERALA BORDER SEC. (TN-7), KM.53 TO KM.100, NH-47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106274]	379.80	12/2008	453.20
September,2009				
31	MADURAI-KANNIAKUMARI, KM.42 TO KM.80, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106238]	474.21	03/2008	246.20
32	MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106239]	567.38	03/2008	382.50
33	MAHUA-JAIPUR, NH-11, KM.120 TO KM.228(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106258]	483.00	03/2009	578.30
34	KARUR TO MADURAI (TN-5), KM.373.275 TO KM.426.6, NH- 7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106275]	283.50	12/2008	448.30
35	INDORE-KALAGHAT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000034]	472.00	09/2009	663.90
36	Bharuch-Surat Package BOT-II(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000070]	492.00	07/2009	448.87
37	Vadodara-Bharuch Package BOT-I(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000071]	660.00	07/2009	789.84
38	UIUWDURPET-PADALUR,NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000084]	460.00	06/2009	799.19
<u>Shipping & Ports</u>				
39	ACQUISITION OF 2-300,000 DWT VERY LARGE CRUDE CARRIERS(SHIPPING) - [250100174]	1,136.08	09/2009	1,196.24

ANNEXURE-I

Month wise List of Deleted Project Costing Rs.100 Crores and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crores)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crores)
May,2009				
<u>Telecommunications</u>				
1	500K BROAD BAND ACCESS N/W PH-III(MAHANAGAR TELEPHONE NIGAM LIMITED) - [120100061]	134.25	10/2009	31.95


Summary of projects on the Flash Report for the month of September, 2009

I. Project Implementation – Current Status:

Number of Projects Previous Month	604
Number of Projects Completed/Dropped/Frozen in Previous Month	6
Number of Projects Completed/Dropped/Frozen in Current month	9
Number of Projects Added in Current month	2
Number of Projects in Current Month	591

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 591 projects, 14 projects are ahead of schedule, 139 projects are on schedule and 314 projects are delayed. Of the balance, 83 projects do not have fixed dates of commissioning while 41 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

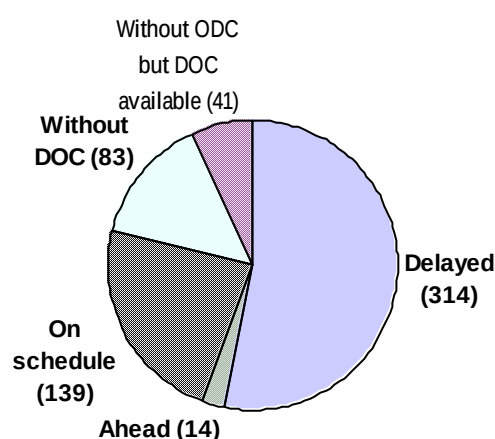

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 591 projects when sanctioned, was of the order of Rs. 541064.31 crore but this was subsequently revised to Rs. 596043.28 crore implying a cost overrun of 10.16%. The expenditure incurred on these projects till September, 2009 is Rs. 237717.02 crore, which is 39.88% of the revised cost of the projects.

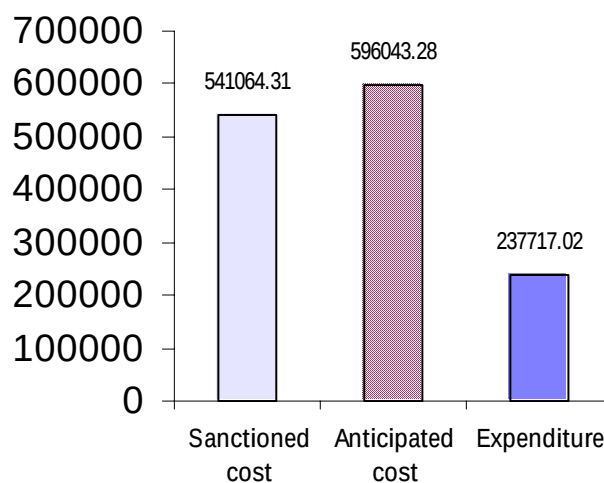

IV. List of projects completed/dropped current month

(Cost /Expenditure in Rs. Crores)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Road Transport & Highways</u>						
MAHUA-JAIPUR, NH-11, KM.120 TO KM.228	03/2005	483.00	03/2009	483.00	09/2009	578.30
MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7	12/2003	567.38	03/2008	567.38	09/2009	382.50

V. List of projects added

(Cost in Rs. Crores)

		Original		Anticipated	
Project	DOA	Cost	DOC	Cost	DOC
<u>Petroleum</u>					
Guru Govind Singh Refinery Product Evacuation	1/2009	605.40	12/2010	605.40	12/2010
Construction of Tanks and Blending Facility at Vad	2/2009	267.00	8/2011	349.00	8/2011

VI. Milestones (Cumulative due & achieved)

Total	1991
Achieved up to month	715

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crores)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	12/2009	01/2010	1
RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL)	3,072.00	3,072.00	02/2008	12/2009	01/2010	1
<u>Civil Aviation</u>						
C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA	135.04	135.04	09/2009	09/2009	12/2009	3
<u>Coal</u>						
BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)	254.07	254.60	06/2009	10/2009	11/2009	1
BARSINGSAR TPS (2X125MW) (NLC)	1,114.18	1,626.09	06/2009	01/2010	03/2010	2
RAJMAHAL OC EXP.	50.08	153.82	03/2010	03/2013	03/2014	12
CHITRA EAST OCP	112.69	112.69	11/2010	03/2011	03/2013	24
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO.-4	248.94	248.94	08/2009	10/2009	12/2009	2
INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S	105.33	116.35	08/2009	03/2011	05/2011	2
COAL DUST INJECTION IN BF-2 and 3	132.73	133.92	05/2008	10/2009	03/2010	5
<u>Petroleum</u>						
LPG PROCESSING & COMPRESSION	142.00	139.07	10/2009	10/2009	12/2009	2
C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)	900.92	1,493.49	06/2006	04/2010	07/2010	3
SULTANPUR NEEMRANA PIPE LINE PROJECT	396.13	396.13	10/2009	10/2009	03/2010	5
DEVELOPMENT OF B-193 CLUSTER FIELDS	3,248.78	2,710.10	03/2010	08/2011	03/2012	7
DEVELOPMENT OF B-22 CLUSTER FIELDS	1,552.63	1,849.50	02/2009	03/2011	04/2012	13
<u>Power</u>						
SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL)	279.30	340.14	07/2009	09/2009	10/2009	1

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crores)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL)	691.83	913.35	12/2007	12/2009	02/2010	2
SIPAT-II SUPP. TRANS. SYSTEM (PGCIL)	813.67	820.45	06/2008	09/2009	11/2009	2
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	1,779.29	1,896.65	11/2008	12/2009	02/2010	2
KOLDAM HEP TRANSMISSION LINE (PGCIL)	464.91	464.91	09/2008	09/2009	11/2009	2
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI	186.95	186.95	07/2009	12/2009	02/2010	2
KOTESWAR TRANSMISSION SYSTEM (PGCIL)	260.34	266.61	06/2008	12/2009	03/2010	3
BARH STPP(3X660MW) NTPC	8,692.97	8,692.97	11/2010	06/2013	10/2013	4
KAMENG HYDROELECTRIC PROJECT (NEEPCO)	2,496.90	3,253.22	12/2009	03/2011	05/2013	26
<u>Railways</u>						
MANDARHILL-DUMKA- RAMPURHAT (NL),ER	184.00	676.00	N.A.	03/2011	06/2011	3
HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	324.66	528.65	N.A.	03/2011	06/2011	3
RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	921.00	921.00	03/2009	10/2011	12/2012	14
SITAMARHI-RAXAUL- NARKATIAGANJ (GC)	501.69	501.69	03/2010	03/2010	06/2011	15
<u>Road Transport & Highways</u>						
ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2	440.93	440.93	12/2006	09/2009	10/2009	1
ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2	534.39	534.39	05/2007	09/2009	10/2009	1
GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH- 2)	399.75	399.75	03/2005	09/2009	10/2009	1
CHITTORGARH BYPASS(RJ- 6) NH-76 KM.159 TO KM.213	133.03	133.03	08/2005	09/2009	10/2009	1
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH- 7,KM.80 TO KM.120	323.36	323.36	03/2008	10/2009	11/2009	1
KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7	327.20	327.20	01/2009	10/2009	11/2009	1
SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47	469.80	469.80	12/2008	10/2009	11/2009	1

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crores)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
SAGAR - RAJMARG CHORAH, KM 255-297, NH- 26 (NHAI)	206.96	206.96	10/2008	11/2009	12/2009	1
AP/KARNATKA BORDER- NANDI HILL CROSSING AND DEVANHA	402.80	402.80	03/2009	10/2009	11/2009	1
BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7	110.00	110.00	06/2005	01/2010	03/2010	2
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	507.49	507.49	03/2008	09/2009	11/2009	2
BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5)	140.85	140.85	01/2004	09/2009	12/2009	3
KUNJWANI-VIJAYPUR(NS- 15) (NS & EW-PH-I) KM.80- KM.97.20,NH-1A	110.00	110.00	12/2004	12/2009	03/2010	3
MEHSI TO KOTWA (LMNHP- II), PH.II, KM.480 TO KM.440, NH-28	239.00	239.00	07/2005	12/2010	03/2011	3
MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28	275.00	275.00	07/2005	12/2010	03/2011	3
KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	240.00	240.00	10/2008	12/2010	03/2011	3
JHAJHARPUR TO DARBANGA (BR-7)	340.00	340.00	09/2008	12/2010	03/2011	3
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80	166.27	166.27	03/2008	12/2009	04/2010	4
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	193.09	193.09	03/2008	12/2009	05/2010	5
GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	155.00	201.66	09/2008	12/2010	06/2011	6
KELARPUR-PIMPALKATTI- KM 153 TO KM 175	117.40	117.40	11/2008	12/2010	06/2011	6
GANJAM-ICCHAPURUM,NH- 5(NHAI)	263.27	263.27	02/2004	12/2009	06/2010	6

Number of projects reporting additional delay = 50

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crores)		
		Original	Latest	Anticipated
Atomic Energy	5	25,054.29	25,054.29	24,123.29
Civil Aviation	9	4,832.24	4,820.66	4,832.24
Coal	40	25,688.03	25,794.62	27,063.70
Mines	1	4,091.51	4,091.51	4,091.51
Steel	29	45,596.58	45,596.58	49,524.19
Petroleum	65	137,003.68	137,003.68	146,644.65
Power	83	153,835.15	155,649.23	159,743.76
Health & Family Welfare	1	71.18	422.60	443.15
Railways	151	50,125.87	57,479.64	93,964.20
Road Transport & Highways	154	44,286.22	44,286.22	44,491.53
Shipping & Ports	18	12,475.83	12,554.69	12,747.59
Telecommunications	31	12,683.66	12,683.66	11,980.44
Urban Development	3	14,596.67	15,084.03	15,206.03
Water Resources	1	542.90	542.90	1,187.00
Grand total	591	530,883.81	541,064.31	596,043.28


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	5
Number of Projects on schedule	2
Number of Projects Delayed	3

Brief Analysis


Project Status w.r.t Original Schedule: Out of 5 projects, 2 projects are on schedule and 3 projects are delayed.



Investment Scenario

Figures are in Rs.

The total cost of implementation of 5 projects when sanctioned, was of the order of Rs. 25054.29 Crores but this was subsequently revised to Rs. 4123.29 Crores. The expenditure incurred on these projects till August, 2009 is Rs. 19166.61 Crores.

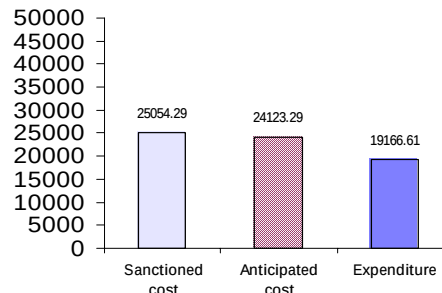


2. Sector: - Civil Aviation

Number of Projects	9
Number of Projects on schedule	3
Number of Projects Delayed	5
Number of Projects Ahead	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 9 projects, 3 projects are on schedule, 5 projects are delayed and 1 project is ahead.



Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 4832.24 Crores but this was subsequently revised to Rs. 4832.24 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 922.04 Crores.

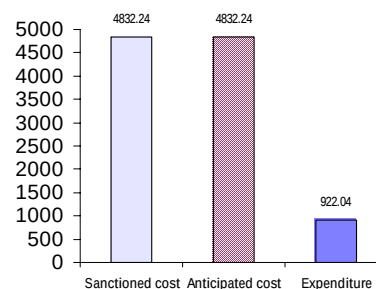


3. Sector : - Coal

Number of Projects	40
Number of Projects on schedule	18
Number of Projects Delayed	18
Number of Projects Ahead	4


Brief Analysis

Project Status w.r.t Original Schedule: Out of 40 projects, 18 projects are on schedule, 18 projects are delayed and 4 projects are ahead .



Investment Scenario

The total cost of implementation of 40 projects when sanctioned, was of the order of Rs. 25688.03 Crores but this was subsequently revised to Rs. 27036.70 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 10109.05 Crores

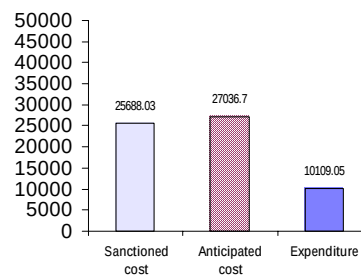


4. Sector : - Petroleum

Number of Projects	65
Number of Projects on schedule	28
Number of Projects Delayed	34
Number of Projects Ahead	3


Brief Analysis

Project Status w.r.t Original Schedule: Out of 65 projects, 28 projects are on schedule, 34 projects are delayed and 3 projects are ahead .



Investment Scenario

The total cost of implementation of 65 projects when sanctioned, was of the order of Rs. 137003.68 Crores but this was subsequently revised to Rs. 146644.65 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 41050.75 Crores.

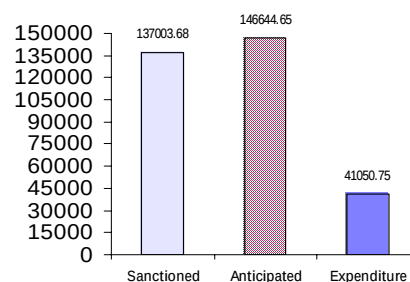


5. Sector : - Power

Number of Projects	83
Number of Projects on schedule	46
Number of Projects Delayed	35
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 83 projects, 46 projects are on schedule, 35 projects are delayed, 1 projects is Wo_Doc_Original and 1 projects is Wo_Odc_Original



Investment Scenario

The total cost of implementation of 83 projects when sanctioned, was of the order of Rs. 153835.15 Crores but this was subsequently revised to Rs. 159743.76 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 54428.51 Crores.




6. Sector : - Railways

Number of Projects	151
Number of Projects on schedule	8
Number of Projects Delayed	39
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	40
Number of Projects Wo_Odc_Original	63


Brief Analysis

Project Status w.r.t Original Schedule: Out of 151 projects, 8 projects are on schedule, 39 projects are delayed, 1 projects is ahead. 40 projects are Wo_Doc_Original and 63 projects are Wo_Odc_Original



Investment Scenario

The total cost of implementation of 151 projects when sanctioned, was of the order of Rs. 50125.87 Crores but this was subsequently revised to Rs. 93964.20 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 41686.22 Crores.

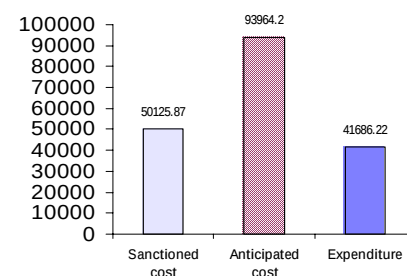


7. Sector : - Road Transport and Highways

Number of Projects	154
f Projects on schedule	15
Number of Projects Delayed	135
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 154 projects, 15 projects are on schedule, 135 projects are delayed, 3 projects are ahead and 1 projects is Wo_Doc_Original .



Investment Scenario

The total cost of implementation of 154 projects when sanctioned, was of the order of Rs. 44286.22 Crores but this was subsequently revised to Rs. 44491.53 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 33218.09 Crores.

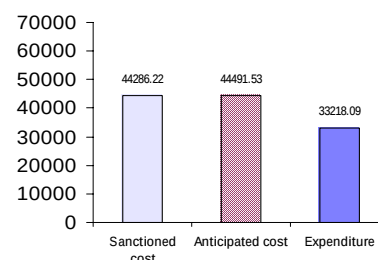


8. Sector : - Shipping and Ports

Number of Projects	18
Number of Projects on schedule	9
Number of Projects Delayed	4
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status w.r.t Original Schedule: Out of 18 projects, 9 projects are on schedule, 4 projects are delayed, 2 projects are ahead and 3 projects are Wo_Doc_Original.



Investment Scenario

The total cost of implementation of 18 projects when sanctioned, was of the order of Rs.12475.83 Crores but this was subsequently revised to Rs. 12747.59 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 2993.67 Crores.

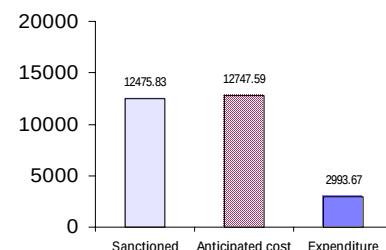


9. Sector : - Steel

Number of Projects	29
Number of Projects on schedule	4
Number of Projects Delayed	23
Number of Projects Wo_Doc_Original	2


Brief Analysis

Project Status w.r.t Original Schedule:
Out of 29 projects, 4 projects are on schedule, 23 projects are delayed and 2 projects are Wo_Doc_Original .



Investment Scenario

The total cost of implementation of 29 projects when sanctioned, was of the order of Rs. 45596.58 Crores but this was subsequently revised to Rs. 49524.19 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 14239.07 Crores.




10. Sector: - Telecommunications

Number of Projects	31
Number of Projects on schedule	4
Number of Projects Delayed	22
Number of Projects Wo_Doc_Original	5


Brief Analysis

Project Status w.r.t Original Schedule:
Out of 31 projects, 4 projects are on schedule, 22 projects are delayed and 5 projects are Wo_Doc_Original .



Investment Scenario

The total cost of implementation of 31 projects when sanctioned, was of the order of Rs. 12683.66 Crores but this was subsequently revised to Rs. 11980.44 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 18797.87 Crores.

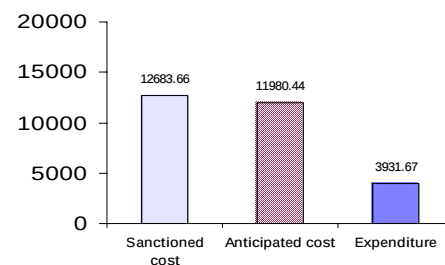

(Sep,2009)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,450.00	10/2009 09/2007	01/2010	28(R1)	71/75
2	RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL) - [020100042]	04/2002	3,072.00	3,072.00	2,049.00	02/2008	01/2010	23(O)	61/75
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	3,492.00	1,997.67	09/2010	09/2010	0(O)	8/80
4	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	12,313.00	12/2008	12/2010	24(O)	61/119
5	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	356.94	04/2011	04/2011	0(O)	0/0
Total			25,054.29	24,123.29	19,166.61				201/349
<u>Civil Aviation</u>									
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING - [N04000016]	10/2006	245.58 295.00	245.58	196.49	12/2008	10/2009	10(O)	1/28
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	146.12	02/2009	10/2009	8(O)	1/24
8	C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR - [N04000034]	03/2008	129.65	129.65	28.90	09/2009	12/2009	3(O)	0/0
9	C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA - [N04000035]	03/2008	135.04	135.04	37.06	09/2009	12/2009	3(O)	0/0
10	C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A - [N04000039]	08/2008	144.94	144.94	18.66	04/2010	01/2010	-3(O)	0/0
11	C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE - [N04000036]	02/2008	135.60	135.60	29.54	10/2009	02/2010	4(O)	0/0
12	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	101.82	06/2010	06/2010	0(O)	0/0
13	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE - [N04000038]	08/2008	1,273.00 1,212.00	1,273.00	178.68	01/2011	01/2011	0(O)	0/0
14	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	184.77	05/2011	05/2011	0(O)	0/0
Total			4,832.24	4,832.24	922.04				2/52
<u>Coal</u>									
15	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07	254.60	204.42	06/2009	11/2009	5(O)	11/21
16	EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC) - [060100088]	10/2004	2,161.28	2,295.93	1,658.39	06/2009	02/2010	8(O)	25/23

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	BARSINGAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,296.88	06/2009	03/2010	9(O)	22/26
18	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	825.70	03/2010	03/2010	0(O)	3/7
19	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53	1,268.53	744.90	03/2010	03/2010	0(O)	2/6
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88	789.88	134.33	03/2010	03/2010	0(O)	0/1
21	BHARATPUR OC EXPANSION PHASE-III PROJECT - [N06000030]	02/2007	131.39	131.39	358.14	03/2010	03/2010	0(O)	0/0
22	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	471.30	03/2009	03/2010	12(O)	0/0
23	JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II - [N06000057]	02/2009	122.35	122.35	-	03/2010	03/2010	0(O)	0/0
24	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,819.97	06/2009	11/2010	17(O)	18/24
25	AUGMENTATION OF PRODUCTION AT SAPRI UG MINE - [N06000058]	09/1987	147.86	147.86	25.50	03/2012	03/2011	-12(O)	0/0
26	LAKHANPUR OC EXP. PROJECT PH-II - [N06000069]	03/2004	98.74	116.54	245.46	03/2007	03/2011	48(O)	0/0
27	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	56.83	03/2010	03/2012	24(O)	0/4
28	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66	471.66	99.97	03/2011	03/2012	12(O)	0/0
29	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04	746.04	134.08	03/2012	03/2012	0(O)	0/1
30	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	249.03	28.42	03/2012	03/2012	0(O)	0/0
31	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18	287.17	-	11/2009	03/2012	28(O)	0/0
32	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	-	03/2012	03/2012	0(O)	0/0
33	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2012	0(O)	0/0
34	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	240.77	03/2012	03/2012	0(O)	0/0
35	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34	212.34	17.34	03/2013	09/2012	-6(O)	2/11
36	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	441.21	08/2012	09/2012	1(O)	0/0
37	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63	453.63	40.54	12/2012	12/2012	0(O)	0/0
38	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	580.07	03/2011 03/2013	03/2013	0(R3)	0/4
39	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 706.40	469.78	12.12	07/2012	03/2013	8(O)	0/0
40	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78	467.78	10.37	03/2013	03/2013	0(O)	0/7
41	KANIHA OCP - [N06000035]	12/2007	457.77	457.77	48.95	03/2012	03/2013	12(O)	0/0
42	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	NARAYANKURI UG - [N06000059]	02/2009	149.06	149.06	-	03/2013	03/2013	0(O)	0/0
44	CHITRA EAST OCP - [N06000060]	08/2007	112.69	112.69	-	11/2010	03/2013	28(O)	0/0
45	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93	479.53	167.77	03/2013	03/2013	0(O)	0/0
46	BINA EXTN. PROJ - [N06000019]	11/2006	168.97	168.97	75.42	03/2014	11/2013	-4(O)	1/1
47	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04	1,352.04	26.69	03/2014	03/2014	0(O)	1/1
48	CHURCHA UG - [N06000046]	06/2008	462.35	462.35	235.11	06/2014	03/2014	-3(O)	0/0
49	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	2.76	03/2010	03/2014	48(O)	0/0
50	PENGANGA OC - [N06000066]	10/2008	339.77	339.77	-	03/2014	03/2014	0(O)	0/0
51	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87	395.87	22.60	03/2013	03/2015	24(O)	0/0
52	BAROUD OC EXPANSION - [N06000065]	07/2008	135.58	135.58	23.26	03/2015	03/2015	0(O)	0/0
53	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	54.46	03/2014	03/2016	24(O)	0/0
54	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	5.32	03/2015	03/2016	12(O)	0/0
Total			25,688.03	27,063.70	10,109.05				85/137
<u>Mines</u>									
55	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	18/111
Total			4,091.51	4,091.51	3,316.00				18/111
<u>Steel</u>									
56	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89	607.17	188.36	10/2009	10/2009	0(O)	2/21
57	INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA - [N12000024]	07/2007	123.22	123.22	73.84	06/2009	10/2009	4(O)	0/0
58	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	72.36	10/2009	11/2009	1(O)	0/0
59	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	140.61	08/2009	12/2009	4(O)	0/0
60	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	186.33	06/2009	12/2009	6(O)	0/0
61	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	37.82	01/2010	01/2010	0(O)	0/0
62	ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE - [N12000049]	06/2008	124.88	119.88	30.80	12/2009	02/2010	2(O)	0/0
63	COAL DUST INJECTION IN BF-2 and 3 - [120100069]	04/2006	132.73	133.92	84.05	05/2008	03/2010	22(O)	0/2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
64	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	197.79	09/2009	03/2010	6(O)	0/0
65	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	434.93	08/2009	03/2010	7(O)	0/0
66	Pulverised coal injection system for bf-1&2 - [N12000037]	11/2007	125.00	187.00	30.66	09/2009	03/2010	6(O)	0/0
67	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	928.96	03/2010	06/2010	3(O)	0/0
68	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	163.31	28.15	06/2010	06/2010	0(O)	0/0
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	319.89	79.91	02/2010	08/2010	6(O)	0/0
70	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	99.18	04/2010	10/2010	6(O)	0/0
71	Air Separation Plant(ASU-5) - [N12000052]	06/2008	129.50	145.00	3.32	12/2010	12/2010	0(O)	0/0
72	POWER PLANT-I - [N12000039]	09/2007	462.00	465.00	40.51	12/2009	01/2011	13(O)	0/0
73	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	382.00	90.09	02/2010	01/2011	11(O)	0/0
74	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	244.30	232.96	41.79	07/2009	05/2011	22(O)	0/0
75	INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S - [N12000034]	10/2007	105.33	116.35	8.30	08/2009	05/2011	21(O)	0/0
76	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	4,620.00	10/2009	06/2011	20(O)	0/126
77	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	15.05	10/2009	06/2011	20(O)	0/0
78	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	4,244.35	07/2010	06/2011	11(O)	0/0
79	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,316.00	512.42	12/2010	10/2011	10(O)	0/0
80	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.18	-	09/2010	12/2011	15(O)	0/0
81	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	6,171.00	791.05	02/2011	03/2012	13(O)	0/0
82	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	4,792.00	1,050.50	05/2011	09/2012	16(O)	0/0
83	COKING COAL FACILITIES IN COAL HANDLING PLANT - [N12000010]	09/2006	133.91	134.32	103.45	03/2008	-	-	0/3
84	INSTALLATION OF MSDS-V AND TRANSMISSION NETWORK F - [N12000022]	05/2007	143.02	143.02	104.49	11/2008	-	-	0/0
Total			45,596.58	49,524.19	14,239.07				2/152
Petroleum									
85	DEVELOPMENT OF BASSEIN EAST (ONGCL) - [160100232]	04/2003	985.17	1,688.38	1,568.46	03/2006	09/2009	42(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
86	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	43(O)	29/45
87	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00	2,869.00	2,284.30	04/2009 12/2009	12/2009	0(R1)	31/36
88	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66	350.00	274.99	06/2008	12/2009	18(O)	0/0
89	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16	1,800.00	1,518.87	12/2008	12/2009	12(O)	0/0
90	CRUDE OIL RECEIPT FACILITIES,KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,481.92	09/2009	12/2009	3(O)	0/0
91	CHENNAI-BANGALORE PIPELINE - [N16000029]	07/2007	232.11	273.00	172.43	07/2009	12/2009	5(O)	0/0
92	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	144.43	12/2009	12/2009	0(O)	0/0
93	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	652.40	12/2009	12/2009	0(O)	0/0
94	LPG PROCESSING & COMPRESSION - [N16000041]	08/2007	142.00	139.07	19.44	10/2009	12/2009	2(O)	0/0
95	CHAINSA-JHAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77	571.64	292.14	09/2009	12/2009	3(O)	0/0
96	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00	5,882.00	3,959.60	01/2010	01/2010	0(O)	0/0
97	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	12,138.00	14,439.00	10,171.23	09/2009 11/2009	02/2010	3(R1)	61/101
98	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10	429.38	465.19	03/2007	03/2010	36(O)	3/3
99	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90	219.22	130.97	03/2006	03/2010	48(O)	6/6
100	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13	396.13	27.20	10/2009	03/2010	5(O)	0/0
101	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	2,722.96	11/2009	04/2010	5(O)	0/0
102	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70	706.70	42.91	04/2010	04/2010	0(O)	0/0
103	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90	1,030.00	437.06	04/2009	05/2010	13(O)	0/0
104	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	330.40	0.35	05/2010	05/2010	0(O)	0/0
105	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	58.19	03/2009	05/2010	14(O)	0/0
106	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2010	-2(O)	0/0
107	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	155.95	05/2010	05/2010	0(O)	0/0
108	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	396.73	09/2009	05/2010	8(O)	0/0
109	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	63.84	05/2010	05/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]	06/2006	1,431.91 -	1,646.39	1,133.88	09/2009 -	06/2010	9(O)	0/0
111	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30 -	1,339.25	1,131.39	06/2010 06/2010	06/2010	0(R1)	0/0
112	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00 -	372.00	77.80	02/2010 -	06/2010	4(O)	0/0
113	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00 -	356.00	72.12	02/2010 -	06/2010	4(O)	0/0
114	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00 -	1,492.00	314.63	04/2010 -	06/2010	2(O)	0/0
115	MSQ IMPROVEMENT PROJECT - [N16000040]	04/2008	293.60 -	293.60	61.98	12/2009 -	06/2010	6(O)	0/0
116	TWO PIPELINE REPLACEMENT PROJECT AT AHMEDABAD MEHS - [N16000042]	03/2008	188.18 -	143.84	66.65	06/2010 -	06/2010	0(O)	0/0
117	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92 -	1,493.49	592.91	06/2006 05/2008	07/2010	26(R1)	0/2
118	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA - [N16000017]	06/2005	806.00 -	1,007.83	490.82	03/2008 12/2009	08/2010	8(R1)	18/48
119	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07 -	1,816.07	5.23	10/2010 -	10/2010	0(O)	0/0
120	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38 -	3,000.00	12.20	10/2010 -	10/2010	0(O)	0/0
121	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00 -	1,512.00	4.56	10/2011 -	10/2010	-12(O)	0/0
122	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00 -	224.00	32.76	12/2010 -	12/2010	0(O)	0/0
123	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40 -	605.40	-	12/2010 -	12/2010	0(O)	0/0
124	CAPACITY AUGMENTATION OF AGRA& FERAZABAD REGION - [N16000074]	07/2009	199.57 -	125.02	-	01/2011 -	01/2011	0(O)	0/0
125	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	834.90	906.91	03/2007 -	03/2011	48(O)	6/6
126	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75 -	8,061.42	3,401.98	06/2009 -	04/2011	22(O)	0/0
127	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93 -	1,061.93	1.10	11/2011 -	04/2011	-7(O)	0/0
128	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08 -	305.08	18.52	04/2011 -	04/2011	0(O)	0/0
129	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	1,262.93	1,079.16	03/2005 -	05/2011	74(O)	0/0
130	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00 -	349.00	0.52	08/2011 -	08/2011	0(O)	0/0
131	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00 -	349.00	2.79	08/2011 -	08/2011	0(O)	0/0
132	Construction of Tanks and Blending Facility at Vad - [N16000077]	02/2009	267.00 -	349.00	-	08/2011 -	08/2011	0(O)	0/0
133	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00 -	3,597.00	60.31	09/2011 -	09/2011	0(O)	0/0
134	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00 -	3,284.00	37.01	09/2011 -	09/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
135	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	1.00	10/2010	12/2011	14(O)	0/0
136	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00	756.00	90.33	12/2011	12/2011	0(O)	0/0
137	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35	1,797.35	-	12/2011	12/2011	0(O)	0/0
138	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11	370.11	-	04/2011	12/2011	8(O)	0/0
139	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT. - [N16000070]	07/2009	238.68	238.68	-	01/2012	01/2012	0(O)	0/0
140	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	217.15	03/2010 03/2012	03/2012	0(R1)	0/0
141	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78	2,710.10	0.61	03/2010 08/2010	03/2012	19(R1)	0/0
142	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63	1,849.50	5.24	02/2009 09/2010	04/2012	19(R1)	0/0
143	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29	2,853.29	0.54	05/2010	05/2012	24(O)	0/0
144	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	0.54	09/2012	09/2012	0(O)	0/0
145	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	29,777.00	2,093.19	03/2012	11/2012	8(O)	0/0
146	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00	3,032.00	-	12/2012	12/2012	0(O)	0/0
147	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43	4,543.43	-	12/2012	12/2012	0(O)	0/0
148	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18	7,596.18	-	01/2013	01/2013	0(O)	0/0
149	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	-	03/2013	03/2013	0(O)	0/0
	Total		137,003.68	146,644.65	41,050.75				154/247
	Power								
150	SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL) - [180100253]	05/2005	279.30	340.14	276.43	07/2009	10/2009	3(O)	5/18
151	SIPAT-II SUPP. TRANS. SYSTEM (PGCIL) - [180100257]	06/2005	813.67	820.45	776.41	06/2008	11/2009	17(O)	9/22
152	KOLDAM HEP TRANSMISSION LINE (PGCIL) - [180100263]	09/2005	464.91	464.91	158.49	09/2008 09/2008	11/2009	14(R1)	9/22
153	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,018.98	857.06	09/2007	12/2009	27(O)	8/36
154	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-V - [N18000017]	06/2006	721.25	721.25	546.48	06/2009	12/2009	6(O)	4/19
155	SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN - [N18000020]	10/2006	150.26	153.54	106.83	10/2009	12/2009	2(O)	5/20

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST - [N18000026]	10/2006	103.80 -	103.80	63.65	06/2009 -	12/2009	6(O)	0/0
157	NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL) - [180100247]	01/2005	691.83 -	913.35	697.46	12/2007 -	02/2010	26(O)	13/20
158	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	1,896.65	1,417.96	11/2008 -	02/2010	15(O)	20/38
159	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50 -	2,448.49	1,652.71	02/2010 -	02/2010	0(O)	2/24
160	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI - [N18000021]	01/2007	186.95 -	186.95	119.22	07/2009 -	02/2010	7(O)	2/21
161	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72 -	836.14	318.09	07/2006 -	03/2010	44(O)	2/5
162	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 1,007.16	1,007.16	690.96	12/2007 -	03/2010	27(O)	7/18
163	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34 -	266.61	124.54	06/2008 -	03/2010	21(O)	6/20
164	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]	12/2005	3,779.46 -	3,779.46	3,009.36	09/2009 -	03/2010	6(O)	11/30
165	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]	06/2006	803.70 -	803.76	499.04	06/2009 -	03/2010	9(O)	0/20
166	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96 -	975.96	475.65	10/2009 -	03/2010	5(O)	2/20
167	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49 -	290.49	176.39	04/2010 -	04/2010	0(O)	0/0
168	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52 -	227.52	78.43	06/2010 -	06/2010	0(O)	0/0
169	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23 -	5,221.23	1,570.88	07/2010 -	07/2010	0(O)	2/20
170	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57 -	353.57	19.81	07/2010 -	07/2010	0(O)	0/0
171	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63 -	1,584.35	938.91	08/2010 -	08/2010	0(O)	0/0
172	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	796.00	348.23	08/2010 -	08/2010	0(O)	0/0
173	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44 -	2,570.44	1,311.44	08/2010 -	08/2010	0(O)	10/26
174	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	477.69	168.88	09/2010 -	09/2010	0(O)	0/0
175	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10 -	262.10	125.19	09/2010 -	09/2010	0(O)	0/0
176	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33 -	5,135.33	3,209.89	10/2010 -	10/2010	0(O)	8/40
177	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,217.00	805.58	10/2010 -	11/2010	1(O)	0/0
178	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24 -	557.24	216.71	01/2010 -	11/2010	10(O)	0/22
179	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72 -	340.72	70.34	11/2010 -	11/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
180	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55 -	261.55	51.44	11/2010 -	11/2010	0(O)	0/0
181	SYSTEM STRENGTHENING SCHEME-VIII OF SOUTHERN REGION - [N18000070]	02/2008	105.84 -	105.84	29.05	11/2010 -	11/2010	0(O)	0/0
182	KOTESHWAR HEP(THDC) - [180100184]	04/2000	1,301.56 -	1,301.56	1,438.41	04/2005 -	12/2010	68(O)	0/0
183	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76 -	417.76	186.20	12/2010 -	12/2010	0(O)	0/0
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36 -	408.36	203.22	12/2010 -	12/2010	0(O)	0/0
185	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89 -	230.89	4.88	01/2011 -	01/2011	0(O)	0/0
186	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92 -	1,279.40	993.11	03/2007 -	02/2011	47(O)	1/25
187	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	1,724.79	903.08	11/2009 -	02/2011	15(O)	0/0
188	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26 -	802.00	290.43	02/2011 -	02/2011	0(O)	0/0
189	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39 -	8,323.39	6,234.15	12/2009 -	03/2011	15(O)	33/56
190	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]	10/2006	238.25 -	238.25	152.90	-	05/2011	-	0/0
191	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39 -	5,038.53	1,865.66	05/2011 -	05/2011	0(O)	0/0
192	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07 -	204.07	15.14	06/2011 -	06/2011	0(O)	0/0
193	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61 -	276.61	24.07	06/2011 -	06/2011	0(O)	0/0
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14 -	525.14	235.13	07/2011 -	07/2011	0(O)	0/0
195	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37 -	297.37	98.10	07/2011 -	07/2011	0(O)	0/0
196	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10 -	196.10	3.58	07/2011 -	07/2011	0(O)	0/0
197	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,061.38	557.37	09/2009 -	08/2011	23(O)	0/0
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIV - [N18000057]	02/2009	132.19 -	132.19	9.62	08/2011 -	08/2011	0(O)	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79 -	210.79	-	08/2011 -	08/2011	0(O)	0/0
200	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97 -	328.97	23.60	09/2011 -	09/2011	0(O)	0/0
201	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	4,375.35	550.81	07/2011 -	11/2011	4(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
202	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48 -	520.48	86.18	11/2011 -	11/2011	0(O)	0/0
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66 -	509.66	5.33	11/2011 -	11/2011	0(O)	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69 -	317.69	0.37	11/2011 -	11/2011	0(O)	0/0
205	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19 -	184.19	11.24	11/2011 -	11/2011	0(O)	0/0
206	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	4,527.15	2,823.71	04/2009 -	12/2011	32(O)	19/41
207	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	421.01	59.72	01/2012 -	01/2012	0(O)	0/0
208	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96 -	664.96	17.07	02/2012 -	02/2012	0(O)	0/0
209	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50 -	409.50	-	02/2012 -	02/2012	0(O)	0/0
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29 -	410.29	5.50	02/2012 -	02/2012	0(O)	0/0
211	SYSTEM STRENGTHENING SCHEME-IX OF SOUTHERN REGIONA - [N18000060]	02/2009	120.62 -	120.62	3.25	02/2012 -	02/2012	0(O)	0/0
212	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32 -	1,347.32	72.01	02/2012 -	02/2012	0(O)	0/0
213	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03 -	2,047.03	625.24	01/2012 -	03/2012	2(O)	2/10
214	PARA HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	573.99	57.36	08/2012 -	08/2012	0(O)	0/0
215	MOUDA STPP - [N18000048]	11/2007	5,459.28 -	5,459.28	537.05	02/2012 -	08/2012	6(O)	0/0
216	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95 -	2,360.95	432.22	08/2012 -	08/2012	0(O)	0/0
217	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33 -	7,075.33	1,006.71	08/2012 -	08/2012	0(O)	0/0
218	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12 -	4,824.12	144.38	10/2012 -	10/2012	0(O)	0/0
219	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	7,452.99	3,394.80	09/2010 -	12/2012	27(O)	2/11
220	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42 -	358.42	6.09	12/2008 09/2010	12/2012	27(R1)	0/15
221	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10 -	2,895.10	507.06	11/2011 -	12/2012	13(O)	6/34
222	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88 -	7,031.88	177.94	12/2012 -	12/2012	0(O)	0/0
223	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	3,954.49	2,509.38	09/2009 -	03/2013	42(O)	1/20

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
224	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	604.66	03/2013	03/2013	0(O)	5/31
225	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	251.59	07/2010	04/2013	33(O)	0/0
226	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	972.90	12/2009	05/2013	41(O)	37/165
227	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	72.04	06/2013	06/2013	0(O)	0/0
228	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	557.96	08/2013	08/2013	0(O)	0/0
229	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	255.13	08/2013	08/2013	0(O)	0/0
230	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,318.07	11/2010	10/2013	35(O)	15/51
231	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67	3,642.04	184.25	07/2014	01/2016	18(O)	0/0
232	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
Total			153,835.15	159,743.76	54,428.51				246/920
Health & Family Welfare									
233	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18	443.15	381.31	03/1999	-	-	7/16
Total			71.18	443.15	381.31	03/2005			7/16
Railways									
234	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53	232.75	451.93	03/1996	08/2009	2(R1)	0/0
235	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82	180.82	230.44	03/2006	09/2009	42(O)	0/0
236	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50	246.50	283.10	03/2009	11/2009	8(R3)	0/0
237	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00	214.09	110.80	12/2009	12/2009	0(O)	0/0
238	KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR - [220100300]	04/1995	49.84	136.45	114.25	03/2002	12/2009	93(O)	0/0
239	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70	142.48	84.91	12/2008	12/2009	12(O)	0/0
240	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01	322.87	229.01	-	12/2009	-	0/0
241	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N220000052]	04/2003	98.74	224.51	41.39	-	12/2009	-	0/0
242	ABOHAR- FAZILKA - [N220000055]	09/2001	86.44	209.57	145.60	03/2009	02/2010	11(O)	0/0
243	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00	634.13	430.19	03/1995	03/2010	180(O)	0/0
244	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21	265.00	265.33	03/1998	03/2010	144(O)	0/0
245	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00	170.00	93.24	03/2002	03/2010	96(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
246	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	572.51	561.78	- -	03/2010	-	0/0
247	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	640.42	03/2001 -	03/2010	108(O)	0/0
248	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 -	281.20	246.86	- -	03/2010	-	0/0
249	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 -	960.48	970.90	03/2003 -	03/2010	84(O)	0/0
250	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	501.69	278.12	- -	03/2010	-	0/0
251	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 -	356.90	538.81	- 11/2008	03/2010	16(R1)	0/0
252	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 -	502.14	426.97	- -	03/2010	-	0/0
253	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	728.28	06/2007 -	03/2010	33(O)	0/0
254	DEOGHAR-DUMKA NEW BG LINE (DOUBL.) (ER) - [220100264]	02/1999	180.73 320.66	335.00	298.11	12/2006 12/2008	03/2010	15(R1)	0/0
255	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	934.99	12/2006 -	03/2010	39(O)	0/0
256	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 294.99	546.49	466.42	- 02/2009	03/2010	13(R1)	0/0
257	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 243.20	243.40	179.46	- 02/2009	03/2010	13(R1)	0/0
258	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	435.96	- 03/2009	03/2010	12(R1)	0/0
259	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	4.77	- -	03/2010	-	0/0
260	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 227.52	227.52	215.90	03/2008 03/2009	03/2010	12(R1)	0/0
261	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 137.56	137.57	131.08	03/1998 08/2005	03/2010	55(R1)	0/0
262	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 211.90	211.90	123.98	- 03/2009	03/2010	12(R1)	0/0
263	PODAPAHAR-BANSPANI,(LD)(SER) - [N22000046]	04/2006	129.74 129.74	129.74	123.13	03/2006 -	03/2010	48(O)	0/0
264	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 729.80	732.80	142.77	03/2008 06/2008	03/2010	21(R1)	0/0
265	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	158.95	204.55	- -	03/2010	-	0/0
266	NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I - [N22000078]	09/2007	99.84 99.84	110.94	57.98	03/2010 -	03/2010	0(O)	0/0
267	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 648.76	1,160.52	382.26	- -	06/2010	-	0/0
268	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 296.20	296.20	191.76	04/2003 03/2010	06/2010	3(R1)	0/0
269	BARAMATI - LONAND (NL), CR - [220100271]	03/1998	75.00 -	138.48	32.64	- -	06/2010	-	0/0
270	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	135.00	113.27	- -	06/2010	-	0/0
271	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	330.00	208.60	03/2009 12/2009	06/2010	6(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
272	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 221.90	221.90	74.60	12/2007 03/2010	07/2010	4(R1)	0/0
273	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
274	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	66.08	- -	09/2010	-	0/0
275	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 273.00	273.00	250.28	- 03/2009	11/2010	20(R1)	0/0
276	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	0.81	02/2015 -	11/2010	-51(O)	0/0
277	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	128.99	03/2004 -	12/2010	81(O)	0/0
278	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 492.98	672.38	630.60	- -	12/2010	-	0/0
279	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 -	567.00	157.19	- 12/2009	12/2010	12(R1)	0/0
280	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 718.30	718.60	598.72	03/2008 08/2008	12/2010	28(R1)	0/0
281	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	252.65	03/2009 12/2008	12/2010	24(R1)	0/0
282	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	245.15	7.53	12/2010 -	12/2010	0(O)	0/0
283	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,174.00	2,953.67	12/2010 -	12/2010	0(O)	0/0
284	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	305.66	02/2010 -	02/2011	12(O)	0/0
285	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38 -	1,000.00	79.07	- -	02/2011	-	0/0
286	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 810.78	810.78	32.36	- -	02/2011	-	0/0
287	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	356.87	177.18	- 03/2010	03/2011	12(R1)	0/0
288	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 175.30	284.27	245.80	06/1999 -	03/2011	141(O)	0/0
289	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	211.11	- -	03/2011	-	0/0
290	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	449.83	237.53	06/2004 -	03/2011	81(O)	0/0
291	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	329.92	- -	03/2011	-	0/0
292	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	371.36	234.34	- -	03/2011	-	0/0
293	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
294	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.30	03/2011 -	03/2011	0(O)	0/0
295	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97 -	196.97	12.84	03/2011 -	03/2011	0(O)	0/0
296	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 -	676.00	267.34	- 12/2010	06/2011	6(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
297	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	98.08	- -	06/2011	-	0/0
298	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69 -	501.69	278.12	03/2010 -	06/2011	15(O)	0/0
299	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 252.50	252.50	18.83	02/2010 -	11/2011	21(O)	0/0
300	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44 576.27	587.08	610.28	- -	12/2011	-	0/0
301	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 735.10	735.82	159.76	- 09/2009	12/2011	27(R1)	0/0
302	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	469.03	26.42	03/2010 -	12/2011	21(O)	0/0
303	LUMDING-SILCHAR(GC),NEFR - [220100170]	04/1996	648.00 1,676.31	4,010.70	1,835.46	03/2009 -	03/2012	36(O)	0/0
304	DLW GM 4000 / 3000 HP DIESEL LOCOS - [220100226]	04/1999	155.54 -	141.40	103.18	03/2003 -	03/2012	108(O)	0/0
305	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 238.56	234.45	52.77	- -	03/2012	-	0/0
306	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	322.95	95.63	- -	03/2012	-	0/0
307	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59 -	495.74	45.46	- -	03/2012	-	0/0
308	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	324.90	54.03	03/2010 -	03/2012	24(O)	0/0
309	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	11,270.00	5,735.26	03/2001 -	12/2012	141(O)	0/0
310	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	353.08 353.08	462.67	43.39	- -	12/2012	-	0/0
311	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	121.77	- 12/2012	12/2012	0(R1)	0/0
312	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	921.00	236.87	03/2009 -	12/2012	45(O)	0/0
313	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	1,480.71	445.84	10/2007 -	12/2012	62(O)	0/0
314	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	687.20	0.95	03/2010 -	12/2012	33(O)	0/0
315	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 -	900.00	504.36	- -	03/2013	-	0/0
316	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70 912.70	1,556.23	92.68	- -	03/2013	-	0/0
317	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00 1,500.00	3,087.44	1,560.89	04/2008 12/2011	03/2014	27(R1)	0/0
318	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00 735.00	1,502.29	385.47	12/2008 -	03/2014	63(O)	0/0
319	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00 -	160.48	40.56	- -	03/2014	-	0/0
320	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00 200.00	546.47	0.48	- -	03/2014	-	0/0
321	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	5,300.00	60.00	03/2014 -	03/2014	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
322	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 727.53	2,492.53	110.81	03/2011 -	03/2016	60(O)	0/0
323	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77 274.56	432.46	425.30	03/1994 -	-	-	0/0
324	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 408.43	517.63	306.82	- -	-	-	0/0
325	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
326	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	225.15	- -	-	-	0/0
327	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0
328	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	339.75	- -	-	-	0/0
329	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84 -	208.83	30.98	- -	-	-	0/0
330	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
331	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
332	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	518.76	03/2004 03/2005	-	-	0/0
333	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 -	730.00	908.04	- -	-	-	0/0
334	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	274.29	71.76	- -	-	-	0/0
335	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.11	271.78	- -	-	-	0/0
336	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.09	227.62	02/2009 -	-	-	0/0
337	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	997.58	49.28	- -	-	-	0/0
338	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 268.00	268.00	275.41	12/1999 03/2008	-	-	0/0
339	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0
340	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	52.36	- -	-	-	0/0
341	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	88.77	03/2007 03/2007	-	-	0/0
342	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	243.17	0.27	07/2008 -	-	-	0/0
343	2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR) - [220100221]	04/1997	93.10 109.45	122.00	126.11	- -	-	-	0/0
344	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	540.09	07/2005 -	-	-	0/0
345	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	309.11	05/2008 -	-	-	0/0
346	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
347	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	60.58	- -	-	-	0/0
348	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
349	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	117.78	- 05/2009	-	-	0/0
350	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15 -	381.17	80.02	- -	-	-	0/0
351	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
352	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	56.34	- -	-	-	0/0
353	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	353.63	- -	-	-	0/0
354	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 329.05	695.00	9.41	- -	-	-	0/0
355	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 108.51	207.80	106.09	- -	-	-	0/0
356	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	901.62	0.28	- -	-	-	0/0
357	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	111.90	274.56	03/2005 12/2008	-	-	0/0
358	HAPUR-KANKATHER (LD),NR - [220100278]	04/2003	106.64 117.31	106.64	138.75	03/2007 -	-	-	0/0
359	SURAT-KOSAMBA (LD),WR - [220100281]	04/2000	133.00 -	133.00	-	- -	-	-	0/0
360	TANUR (KUTTIPURAM) GURUVAYUR (NL) (SR) - [220100283]	04/1995	40.00 -	137.71	8.69	- -	-	-	0/0
361	REWARI-SADULPUR-HISSAR (GC),NWR - [220100290]	04/1997	198.96 -	364.19	77.05	- -	-	-	0/0
362	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	459.91	36.40	- -	-	-	0/0
363	BARBIGHA - SHEKHPURA + NEORA-DANIAWAN (NL), ECR - [220100309]	04/2002	120.23 -	120.23	220.17	- -	-	-	0/0
364	BIHARSHARIFF-BARBIGHA (NL), ECR - [220100310]	04/2001	103.86 -	103.86	28.93	- -	-	-	0/0
365	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	104.79	34.13	- -	-	-	0/0
366	RAMGANJMONDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	726.05	99.80	- -	-	-	0/0
367	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	104.10 -	113.75	40.35	- -	-	-	0/0
368	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
369	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73 -	230.03	45.76	- -	-	-	0/0
370	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	102.78	- -	-	-	0/0
371	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
372	BHATNI-JIRADEI PATCH DOUBLING (NER) - [N22000029]	04/2006	100.27 -	100.27	0.01	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
373	MUNDERWA-BABHNAN PATCH DOUBLING(NER) - [N22000030]	04/2006	102.10	102.10	22.75	-	-	-	0/0
374	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56	670.00	0.43	-	-	-	0/0
375	GAEKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92	283.10	1.86	02/2006	-	-	0/0
376	SETTING UP EAST COAST RLY.ZN. (SER) - [N22000054]	04/1997	41.67	129.78	90.84	-	-	-	0/0
377	PATTABIRAM-ARAKKONAM,SR - [N22000057]	04/2002	71.94	124.00	151.76	03/2004	-	-	0/0
378	AMROHA-KANKATHER,NR - [N22000058]	04/2000	57.00	103.57	104.98	03/2005	-	-	0/0
379	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]	09/2007	404.19	711.15	24.47	-	-	-	0/0
380	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17	639.00	128.61	-	-	-	0/0
381	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00	255.96	49.32	-	-	-	0/0
382	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00	227.40	9.64	-	-	-	0/0
383	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00	582.83	15.18	-	-	-	0/0
384	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00	529.88	18.30	-	-	-	0/0
	Total		50,125.87	93,964.20	41,686.22				0/0
Road Transport & Highways									
385	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93	440.93	588.51	12/2006	10/2009	34(O)	0/0
386	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39	534.39	631.48	05/2007	10/2009	29(O)	0/0
387	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	386.81	03/2005	10/2009	55(O)	0/0
388	CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213 - [240106232]	03/2005	133.03	133.03	244.80	08/2005	10/2009	50(O)	0/0
389	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	330.90	02/2009	10/2009	8(O)	0/0
390	HYDERABAD BANGALORE SECTION(NH-7)(NHAI) - [240106284]	12/2003	611.44	592.00	827.60	03/2009	10/2009	7(O)	0/0
391	JAWAHARLAL NEHRU PORT PHASE-II,SH-54 - [N24000039]	04/2000	143.00	143.00	120.30	05/2007	10/2009	29(O)	0/0
392	PANIPAT TO PANCHI GUJRAN, NH-1 - [N24000066]	12/2003	109.00	109.00	124.70	10/2008	10/2009	12(O)	0/0
393	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00	450.00	833.20	07/2008	10/2009	15(O)	0/0
394	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	402.30	11/2007	11/2009	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
395	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7, KM.80 TO KM.120 - [240106240]	12/2003	323.36 -	323.36	189.50	03/2008 -	11/2009	20(O)	0/0
396	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49 -	507.49	283.60	03/2008 -	11/2009	20(O)	0/0
397	KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7 - [240106272]	12/2003	327.20 -	327.20	457.60	01/2009 -	11/2009	10(O)	0/0
398	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80 -	469.80	665.80	12/2008 -	11/2009	11(O)	0/0
399	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00 -	261.00	269.60	08/2008 -	11/2009	15(O)	0/0
400	TOVARAMKURCHI-MADURAI, NH45B (NHAI) - [N24000054]	04/2000	263.00 -	263.00	296.57	08/2008 -	11/2009	15(O)	0/0
401	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80 -	402.80	447.30	03/2009 -	11/2009	8(O)	0/0
402	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00 -	320.00	575.40	05/2009 -	11/2009	6(O)	0/0
403	SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS - [N24000086]	03/2005	110.00 -	110.00	102.80	07/2008 -	11/2009	16(O)	0/0
404	KADAL TO ARMUR, NH-7 - [N24000092]	12/2003	271.73 -	271.73	279.70	11/2009 -	11/2009	0(O)	0/0
405	BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5) - [240101151]	04/2000	140.85 -	140.85	147.88	01/2004 -	12/2009	71(O)	0/0
406	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	225.00	145.54	04/2004 -	12/2009	68(O)	0/0
407	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49 -	367.49	415.56	03/2005 -	12/2009	57(O)	0/0
408	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40 -	372.40	380.72	07/2004 -	12/2009	65(O)	0/0
409	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93 -	467.93	446.73	03/2005 -	12/2009	57(O)	0/0
410	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00 -	480.00	716.49	11/2007 -	12/2009	25(O)	0/0
411	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00 -	210.00	561.04	04/2007 -	12/2009	32(O)	0/0
412	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00 -	275.00	247.86	09/2007 -	12/2009	27(O)	0/0
413	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00 -	220.00	112.47	09/2007 -	12/2009	27(O)	0/0
414	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06 -	158.06	130.50	08/2005 -	12/2009	52(O)	0/0
415	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00 -	276.00	309.30	04/2008 -	12/2009	20(O)	0/0
416	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00 -	310.00	321.00	04/2008 -	12/2009	20(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
417	GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73 - [240106231]	12/2003	266.00	288.06	360.10	08/2007	12/2009	28(O)	0/0
418	PATHANKOT- BHOGPUR, KM.26- KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	268.80	05/2008	12/2009	19(O)	0/0
419	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	448.30	03/2009	12/2009	9(O)	0/0
420	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	531.80	03/2009	12/2009	9(O)	0/0
421	SAGAR - RAJMARG CHORAH, KM.255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	12/2009	14(O)	0/0
422	SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4) - [N24000029]	12/2003	100.50	100.50	145.90	04/2008	12/2009	20(O)	0/0
423	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	12/2009	9(O)	0/0
424	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	132.44	06/2008	12/2009	18(O)	0/0
425	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]	03/2005	168.00	168.00	227.74	12/2008	12/2009	12(O)	0/0
426	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	23.82	04/2009	12/2009	8(O)	0/0
427	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	-	05/2010	12/2009	-5(O)	0/0
428	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	698.80	11/2010	01/2010	-10(O)	0/0
429	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	182.00	01/2009	02/2010	13(O)	0/0
430	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]	03/2005	557.00	557.00	717.37	02/2010	02/2010	0(O)	0/0
431	KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20, NH-1A - [240102193]	04/2000	110.00	110.00	135.13	12/2004	03/2010	63(O)	0/0
432	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	240.90	07/2004	03/2010	68(O)	0/0
433	DEVDHARI-KELAPUR - [240106207]	12/2003	144.00	144.00	95.12	07/2005	03/2010	56(O)	0/0
434	BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7 - [240106210]	12/2003	110.00	110.00	105.70	06/2005	03/2010	57(O)	0/0
435	ORAI TO JHANSI (UP-4), NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	366.30	04/2008	03/2010	23(O)	0/0
436	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	137.10	06/2008	03/2010	21(O)	0/0
437	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	524.60	06/2009	03/2010	9(O)	0/0
438	MAHARASHTRA/AP BORDER TO ISLAM NAGAR, (NS-2/BOT/AP-6), NH-7 - [N24000093]	12/2003	360.42	360.42	208.30	11/2009	03/2010	4(O)	0/0
439	BANGALORE-NEELAMANGALALA NH-4 - [N24000104]	03/2005	445.00	445.00	594.90	07/2010	03/2010	-4(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
440	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	75.88	08/2006	04/2010	44(O)	0/0
441	KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7 - [240102202]	01/2004	120.00	120.00	47.27	09/2006	04/2010	43(O)	0/0
442	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	63.26	03/2008	04/2010	25(O)	0/0
443	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	140.70	08/2009	04/2010	8(O)	0/0
444	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	144.40	08/2009	04/2010	8(O)	0/0
445	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	192.70	08/2009	04/2010	8(O)	0/0
446	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	124.60	08/2009	04/2010	8(O)	0/0
447	CHITRADURGA BY PASS (GQ) KM.207-KM.189 (NH-4) - [240101134]	04/2000	104.00	104.00	138.91	08/2004	05/2010	69(O)	0/0
448	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	81.77	03/2008	05/2010	26(O)	0/0
449	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	480.24	04/2009	05/2010	13(O)	0/0
450	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	123.50	10/2008	05/2010	19(O)	0/0
451	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	64.42	05/2010	05/2010	0(O)	0/0
452	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	111.00	09/2007	06/2010	33(O)	0/0
453	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	35.11	08/2004	06/2010	70(O)	0/0
454	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	242.00	10/2008	06/2010	20(O)	0/0
455	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	266.60	10/2008	06/2010	20(O)	0/0
456	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	275.20	10/2008	06/2010	20(O)	0/0
457	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	217.30	10/2008	06/2010	20(O)	0/0
458	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	262.40	10/2008	06/2010	20(O)	0/0
459	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68	340.68	189.90	03/2008	06/2010	27(O)	0/0
460	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00	242.00	255.70	12/2008	06/2010	18(O)	0/0
461	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00	227.00	222.90	12/2008	06/2010	18(O)	0/0
462	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	298.60	06/2008	06/2010	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
463	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	334.20	06/2008	06/2010	24(O)	0/0
464	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	142.10	10/2008	06/2010	20(O)	0/0
465	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	131.10	07/2008	06/2010	23(O)	0/0
466	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	350.10	06/2008	06/2010	24(O)	0/0
467	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	129.00	06/2008	06/2010	24(O)	0/0
468	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	171.20	06/2009	06/2010	12(O)	0/0
469	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	135.00	11/2008	06/2010	19(O)	0/0
470	NALBARI TO BIJNI (AS-9) - [N24000050]	12/2003	142.00	142.00	100.90	06/2008	06/2010	24(O)	0/0
471	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	182.81	02/2004	06/2010	76(O)	0/0
472	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	152.10	09/2009	06/2010	9(O)	0/0
473	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	152.20	09/2008	06/2010	21(O)	0/0
474	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	215.60	06/2010	06/2010	0(O)	0/0
475	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	216.00	03/2010	06/2010	3(O)	0/0
476	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]	12/2003	407.60	407.60	171.40	06/2010	06/2010	0(O)	0/0
477	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	238.40	09/2009	06/2010	9(O)	0/0
478	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	183.20	09/2009	06/2010	9(O)	0/0
479	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	92.93	06/2010	06/2010	0(O)	0/0
480	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	31.19	08/2004	07/2010	71(O)	0/0
481	TRICHY - DINDIGUAL NH-45 - [N24000099]	03/2005	576.00	576.00	163.00	07/2010	07/2010	0(O)	0/0
482	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	181.20	07/2010	07/2010	0(O)	0/0
483	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	07/2010	0(O)	0/0
484	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	320.80	07/2010	07/2010	0(O)	0/0
485	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	449.40	07/2010	07/2010	0(O)	0/0
486	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	316.00	03/2010	07/2010	4(O)	0/0
487	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	99.85	06/2008	08/2010	26(O)	0/0
488	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	182.10	08/2010	08/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
489	LUCKNOW-BYPASS (EW) (NS & EW-PH-I) NH-25 & NH-28 VIA NH-56 - [240103192]	04/2000	182.52	111.78	0.59	06/2004	09/2010	75(O)	0/0
490	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	191.60	03/2005	09/2010	66(O)	0/0
491	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]	12/2003	198.00	198.00	66.84	11/2008	09/2010	22(O)	0/0
492	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	198.00	09/2009	09/2010	12(O)	0/0
493	LUMDING TO DABOKA - [N24000110]	12/2003	130.00	130.00	27.22	08/2010	09/2010	1(O)	0/0
494	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	275.60	09/2010	09/2010	0(O)	0/0
495	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	155.60	10/2009	10/2010	12(O)	0/0
496	JAM-WADNER - [240106209]	12/2003	145.00	145.00	68.18	07/2005	12/2010	65(O)	0/0
497	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	87.70	06/2005	12/2010	66(O)	0/0
498	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00	227.00	172.70	10/2008	12/2010	26(O)	0/0
499	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	280.00	96.15	02/2009	12/2010	22(O)	0/0
500	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81	199.81	27.54	04/2009	12/2010	20(O)	0/0
501	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64	167.64	39.49	11/2008	12/2010	25(O)	0/0
502	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	155.04	27.96	11/2008	12/2010	25(O)	0/0
503	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00	200.00	36.15	04/2009	12/2010	20(O)	0/0
504	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00	225.00	86.47	06/2008	12/2010	30(O)	0/0
505	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]	12/2003	195.00	195.00	68.72	06/2008	12/2010	30(O)	0/0
506	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]	12/2003	237.80	237.80	66.24	06/2008	12/2010	30(O)	0/0
507	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94	332.94	124.40	09/2008	12/2010	27(O)	0/0
508	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30	151.30	83.78	10/2008	12/2010	26(O)	0/0
509	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43	203.43	63.28	10/2008	12/2010	26(O)	0/0
510	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]	12/2003	251.03	251.03	62.13	10/2008	12/2010	26(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
511	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]	12/2003	229.91	229.91	29.18	10/2008	12/2010	26(O)	0/0
512	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	47.21	04/2008	12/2010	32(O)	0/0
513	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	75.54	06/2008	12/2010	30(O)	0/0
514	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	179.10	03/2008	12/2010	33(O)	0/0
515	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	74.09	04/2008	12/2010	32(O)	0/0
516	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	105.80	06/2008	12/2010	30(O)	0/0
517	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	55.66	04/2008	12/2010	32(O)	0/0
518	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	49.83	05/2008	12/2010	31(O)	0/0
519	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	78.52	06/2008	12/2010	30(O)	0/0
520	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	33.75	09/2007	12/2010	39(O)	0/0
521	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.32	07/2009	12/2010	17(O)	0/0
522	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	57.53	04/2010	12/2010	8(O)	0/0
523	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	150.40	02/2010	12/2010	10(O)	0/0
524	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	361.20	10/2009	12/2010	14(O)	0/0
525	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	176.80	12/2009	12/2010	12(O)	0/0
526	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	192.36	02/2004	12/2010	82(O)	0/0
527	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	266.60	01/2011	01/2011	0(O)	0/0
528	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	169.30	01/2011	01/2011	0(O)	0/0
529	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	77.75	09/2007	02/2011	41(O)	0/0
530	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	161.30	07/2005	03/2011	68(O)	0/0
531	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	181.60	07/2005	03/2011	68(O)	0/0
532	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	119.70	10/2008	03/2011	29(O)	0/0
533	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	163.30	09/2008	03/2011	30(O)	0/0
534	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	78.27	09/2010	03/2011	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
535	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	313.90	05/2010	05/2011	12(O)	0/0
536	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	38.29	09/2008	06/2011	33(O)	0/0
537	KELARPUR-PIMPALKATTI-KM 153 TO KM 175 - [240106283]	12/2003	117.40	117.40	129.83	11/2008	06/2011	31(O)	0/0
538	DEVDHARI-WADNER - [240106208]	12/2003	145.00	145.00	24.71	07/2005	-	-	0/0
	Total		44,286.22	44,491.53	33,218.09				0/0
Shipping & Ports									
539	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	264.01	04/2009	11/2009	7(O)	0/0
540	CONSTRUCTION OF CAR /CLEAN CARGO TERMINAL - [N25000034]	01/2009	100.00	100.00	0.50	01/2010	01/2010	0(O)	0/0
541	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	36.18	12/2005	03/2010	51(O)	0/0
542	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	99.38	06/2007 01/2009	03/2010	14(R1)	0/0
543	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	277.87	03/2010	03/2010	0(O)	0/0
544	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	318.24	07/2010	07/2010	0(O)	0/0
545	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	173.68	11/2010	11/2010	0(O)	0/0
546	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00 444.86	366.00	1.43	12/2010	12/2010	0(O)	0/0
547	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
548	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	882.00	0.16	02/2011	02/2011	0(O)	0/0
549	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	702.00	0.73	03/2011	03/2011	0(O)	0/0
550	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	200.91	04/2011	04/2011	0(O)	0/0
551	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	341.48	04/2011	12/2011	8(O)	0/0
552	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
553	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
554	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	808.71	10/2008	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
555	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.24	10/2008	-	-	0/0
556	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
	Total		12,475.83	12,747.59	2,993.67				0/0
Telecommunications									
557	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	92.36	10/2007	08/2009	22(O)	0/0
558	500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB - [N26000038]	04/2007	134.25	133.75	34.05	06/2008	08/2009	14(O)	0/0
559	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	399.77	12/2008	08/2009	8(O)	0/0
560	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	45.97	03/2009	08/2009	5(O)	0/0
561	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	154.60	12/2008	08/2009	8(O)	0/0
562	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	10.96	03/2009	08/2009	5(O)	0/0
563	ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM - [N26000059]	03/2008	567.40	482.29	226.88	06/2009	08/2009	2(O)	0/0
564	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	118.44	02/2008	09/2009	19(O)	0/0
565	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	409.21	465.49	12/2008	09/2009	9(O)	0/0
566	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	26.37	09/2009	09/2009	0(O)	0/0
567	GSM EQUIPMENT OF 1015K LINES PH-4.5 - [N26000044]	10/2008	350.84	350.84	180.64	11/2008	09/2009	10(O)	0/0
568	GSM EQUIPMENT OF 1162K LINES PH-4.5 - [N26000045]	03/2008	325.00	325.00	220.75	12/2008	09/2009	9(O)	0/0
569	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	165.46	03/2009	09/2009	6(O)	0/0
570	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	09/2009	1(O)	0/0
571	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	366.00	-	09/2009	09/2009	0(O)	0/0
572	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	34(O)	0/0
573	GSM BASED NETWORK PH-4 - [N26000033]	11/2007	174.36	174.36	71.50	11/2007	10/2009	23(O)	0/0
574	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	10/2009	18(O)	0/0
575	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	10/2009	13(O)	0/0
576	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	278.16	278.16	152.53	12/2008	10/2009	10(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
577	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	174.36	71.50	01/2009	10/2009	9(O)	0/0
578	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007	11/2009	33(O)	0/0
579	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007	12/2009	34(O)	0/0
580	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	463.61	16.37	12/2009	12/2009	0(O)	0/0
581	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53	180.53	3.78	12/2009	12/2009	0(O)	0/0
582	NATIONAL RADIO SPECTRUM MANAGEMENT and MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.16	12/2004	02/2010	62(O)	0/0
583	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	341.41	03/2006	-	-	0/0
584	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	-	-	0/0
585	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	135.00	94.77	06/2006	-	-	0/0
586	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
587	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]	01/2009	149.15	149.15	40.87	06/2009	-	-	0/0
Total			12,683.66	11,980.44	3,931.67				0/0
<u>Urban Development</u>									
588	C/O GENERAL POOL OFFICE COMPLEX AT INA - [N28000016]	10/2004	83.67	135.03	-	02/2010	02/2010	0(O)	0/0
589	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00	8,676.00	10,933.06	06/2010	10/2010	4(O)	0/7
590	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	6,395.00	1,305.48	12/2011	12/2011	0(O)	0/0
Total			14,596.67	15,206.03	12,238.54				0/7
<u>Water Resources</u>									
591	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
Total			542.90	1,187.00	35.49				0/0
Grand Total			530,883.81	596,043.28	237,717.02				715/1991
