

**311th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
September, 2011**



GAIL India limited



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for September 2011 contains information on the status of the 566 projects in the Central Sector costing ₹ 150 Crores and above. During September 2011, four projects have reported completion (which has now been dropped from the monitor of this Ministry).

The online reporting of the implementation status of the ongoing projects from the project authorities has improved considerably with majority of project authorities reporting online during the current month, on account of continuous effort/persuasion by this Ministry. NHAI, however, has been a major defaulter on this count. During September 2011, thirty-four (34) projects have reported additional delays, vis-à-vis the date of completion reported the previous month. The additional delays are in the range of 1 to 16 months, in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	132	2
2.	ROAD TRANSPORT & HIGHWAYS	132	21
3.	POWER	83	3
4.	PETROLEUM	71	3
5.	COAL	48	2
6.	TELECOMMUNICATION	40	0
7.	SHIPPING & PORTS	26	0
8.	STEEL	12	2
9.	FERTILISERS	6	0
10.	CIVIL AVIATION	5	0
11.	ATOMIC ENERGY	4	1
12.	URBAN DEVELOPMENT	4	0
13.	MINES	1	0
14.	WATER RESOURCES	1	0
15.	PETROCHEMICALS	1	0
Total		566	34

3. The total original cost of implementation of the 566 projects was about ₹ 6,67,074.68 Crores and their anticipated completion cost is likely to be ₹ 7,87,393.95 Crores, which reflects an overall cost overrun of 18 %. The expenditure incurred on these projects till August, 2011 is ₹ 3, 27,255.18 Crores, which is 41.60 % of the revised cost of the projects .

4. Out of the 566 projects, 5 projects are ahead of schedule, 150 are on schedule, 234 projects are delayed and 124 projects have been sanctioned without any commissioning schedule/date Further, in case of 53 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month under reference the projects reporting delays have marginally decreased to 234 (from 243 in August'2011). Out of 234 delayed projects, 44 projects had overall delay in the range of 1 to 12 months, 58 projects had a delay in the range of 13 to 24 months, 98 projects had a delay in the range of 25 to 60 months and 34 projects had a delay of 61 months and above.

6. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. This has been objected to by various Ministries who have desired that since from time to time, RCEs regularize the time & cost overrun, hence we should monitor against RCEs not against OCE. If we do this, then the calculated time & cost overrun will reflect only the unregularized RCEs which will not serve the purpose of monitoring. If we measure against the RCEs, ultimately all time & cost overrun gets regularized which would reflect a zero time & cost overrun.

7. The brief reasons for time overruns have been reported as inadequate mobilization by the contractors, law and order problems, delays in engineering designs, change of scope delays in pre-project activity, Maoist problems and forest and environment clearances etc. Brief reasons for cost overruns are mainly due to inflation, fluctuation of exchange rate, higher tender value, change of scope etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

The Sector-wise details of additional delays are as under:-

i) In the **Coal sector**, 2 projects have reported additional delays in the range of 1 to 4 months. Barsingsar TPS, NLC has reported an additional delay of 1 month (overall delay of 27 months) due to delay in commissioning. Tuticorin Thermal Power Project NLC has reported an additional delay of 4 months due to delay in civil works and inadequate mobilization by the contractor.

ii) In the **Steel sector**, 2 projects have reported additional delays. 67.5MW TG-5 AUX. System Emergency Power Requirement RINL has reported an additional delay of 1 month due to delay in supply of equipments by BHEL. 330 TPH Boiler-6 and Auxiliary System RINL has an additional delay of 2 months due to delay in design of civil & structural works.

iii) In the **Petroleum Sector**, 3 projects have reported additional delays in the range of 1-12 months. Paradip Refinery Project, IOCL has reported an additional delay of 7 months due to law and order problems. Polypropylene Unit Mangalore Refinery has reported an additional delay of 1 month (overall delay of 1 month) due to delay in evacuation of the project displaced family. Construction of 12 Offshore Supply Vessels (OSV) ONGC has reported an additional delay of 12 months (overall delay of 3 months) due to delay in procurement of steel by PSL and less mobilization by the contractor at the site.

iv) In the **Power Sector**, 3 projects have reported additional delays in the range of 1-2 months. Chamera Stage-III, NHPC has reported an additional delay of 1 month (overall delay of 15 months) due to delay in heavy rainfall in August 2011. URI H.E.P Stage-II (NHPC) NHPC has reported an additional delay of 2 months (overall delay of

25 months) due to delay in flash flood in Gotta Nallah during September' 2011 thereby affecting the progress of works. Eastern Region Strengthening Scheme-II PGCIL has reported an additional delay of 2 months (overall delay of 15 months) due to pending court case.

v) In the **Road Transport and Highways Sector**, 21 projects have reported additional delays in the range of 1-16 months. 7 projects have reported additional delay of 1 month each due to slow progress of work by the contractor. Lalitpur to Sagar KM 132 to Km 187, NH-26, NHAH and Jhansi to Lalitpur, NH-25, 26 NHAH have reported an additional delay of 2 months each due to delay in tree cutting and utility shifting. Haveri-Harihar (GQ) KM 340-KM 284 (NH-4), NHAH and Harihar-Chitradurga (GQ) KM 284-KM 207 (NH-4), NHAH have reported an additional delay of 3 months each due to delay in poor performance by the contractor. Haldia Port (Port Connectivity) (NH-41), NHAH has reported an additional delay of 3 months (overall delay of 78 months) due to re-award of the project. Gagodhar-Garamore (PK-IV, NH-15) KM 245 to 281.3 and 308 to 254 NHAH has reported an additional delay of 3 months (overall delay of 46 months) due to reconstruction of existing pavements. Orai to Jhansi (UP-5), NH-25, KM 220 to KM 170, NHAH has reported an additional delay of 3 months (overall delay of 45 months) due to delay in utility shifting. Neelamangalar Junction on NH-48 to Devi, NHAH and Balsore Bhadrak (Revived) KM 136.5-199.14 NH-5, NHAH have reported an additional delay of 3 months each due to slow progress by the concessionaire. Assam(WB) Border to Gairkatta (WB-1), NHAH and Trichy-Korur NH-67, NHAH have reported an additional delay of 4 months each due to delay in land acquisition. Ganga Bridge to Ramdevi Crossing Ph-II NH-25, KM 75-80.06, NHAH has reported an additional delay of 6 months (overall delay of 39 months) due to land acquisition problem. Chambal Bridge, NH-76 (RJ-5), NHAH has reported an additional delay of 16 months (overall delay of 25 months) due to delay in forest clearness. Panipat-Jalandhar 6 lane project (KM 96 to 387.1KM), NHAH has reported an additional delay of 7 months; however no reason has been reported by the project authority.

vi) In the **Railway Sector**, 2 projects have reported additional delays in the range of 3-4 months. Lanjigarh-Junagarh NL, ECR has reported an additional delay of 3 months (overall delay of 114 months) due to delay in Stage-II clearance from M/o

Environment & forest, New Delhi. Khurda Road-Bolangir(NL), ECOR has reported an additional delay of 4 months (overall delay due to delay in land acquisition.

vii) In the **Atomic Energy Sector**, Kudankulam APP, NPCIL has reported an additional delay of 1 month (overall delay of 43 months) due to delay in slippage of commitments by M/s ASE and agitation by the local people.

The status as on 01.10.2011 in respect of completion of projects costing ₹150 Crores and above in different sectors during 2011-12 is indicated in the Report.



(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	132	2
2	Road Transport & Highways	132	21
3	Power	83	3
4	Petroleum	71	3
5	Coal	48	2
6	Telecommunications	40	0
7	Shipping & Ports	26	0
8	Steel	12	2
9	Fertilisers	6	0
10	Civil Aviation	5	0
11	Atomic Energy	4	1
12	Urban Development	4	0
13	Mines	1	0
14	Petrochemicals	1	0
15	Water Resources	1	0
	Total	566	34

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
<u>Road Transport & Highways</u>				
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
June,2011				
<u>Petroleum</u>				
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
<u>Power</u>				
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
<u>Railways</u>				
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
<u>Road Transport & Highways</u>				
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00
July,2011				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Steel</u>				
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
<u>Petroleum</u>				
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
30	KURALI-KIRATPUR, NH-21(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000087]	309.00	06/2010	553.56
<u>August,2011</u>				
<u>Power</u>				
31	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]	262.10	09/2010	164.00
<u>Railways</u>				
32	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]	262.00	-	548.54
<u>Road Transport & Highways</u>				
33	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]	193.00	10/2008	338.70
34	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256]	359.00	03/2009	870.60
<u>Telecommunications</u>				
35	NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]	312.86	02/2008	204.43
<u>Urban Development</u>				
36	DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]	8,676.00	06/2010	18,304.30

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
September, 2011				
<u>Petroleum</u>				
37	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF(INDIAN OIL CORPORATION LIMITED) - [N16000040]	293.60	12/2009	234.81
<u>Railways</u>				
38	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN(WESTERN RAILWAY) - [220100116]	112.53	03/1996	509.57
39	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves(NORTH WESTERN RAILWAY) - [N22000106]	643.36	03/2011	786.54
<u>Road Transport & Highways</u>				
40	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH- 28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106225]	217.00	10/2008	352.26

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2011				
<u>Civil Aviation</u>				
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97
August,2011				
<u>Steel</u>				
2	EXPENSION OF ROURKELA STEEL PLANT(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N16000049]	6,133.00	02/2011	1,253.17


Summary of projects in the Flash Report for the month of September, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	560
Number of Projects completed/dropped/frozen in Previous Month	7
Number of Projects completed/dropped/frozen in Current Month	4
Number of Projects Added in Current Month	17
Number of Projects in Current Month	566


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 566 projects, 5 projects are ahead of schedule, 150 projects are on schedule and 234 projects are delayed. Of the balance, 124 projects do not have fixed dates of commissioning while 53 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

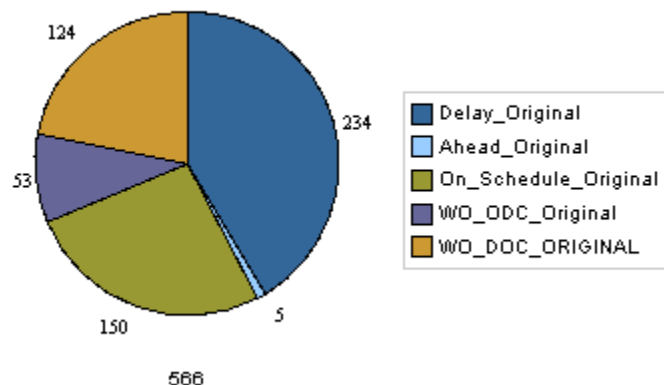

III. Investment Scenario

The Total Original cost of implementation of 566 projects when sanctioned, was of the order of Rs. 667074.68 crore but this was subsequently revised to Rs. 787393.95 crore implying a cost overrun of 18%. The expenditure incurred on these projects till September, 2011 is Rs. 327255.18 crore, which is 41.6% of the revised cost of the projects.

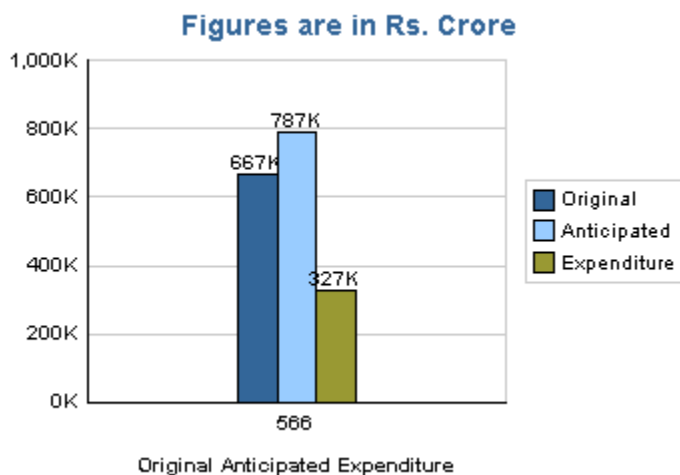

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	560
No of Projects Completed/Dropped/Frozen in Previous Month	7
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	17
No of Projects in Current Month	566

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	234	5	150	53	124	566	41.34
Latest Approved (Date)	253	10	184	35	87	566	44.70

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	461	543,758.95	579,524.33	220,615.57	38.10	35,765.38	6.60
Latest Approved (RCE)	105	180,306.41	207,869.62	106,639.61	51.30	27,563.21	15.30
Total (RCE)	566	724,065.36	787,393.95	327,255.18	41.56	63328.59	8.75
Original Cost of All Projects							
Original Cost	566	667,074.68	787,393.95	327,255.18	41.60	120,319.27	18.00

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	234	309,434.69	375,643.53	202,576.46	53.90	66,208.84	21.40
Latest Approved (RCE)	253	324,389.30	369,963.32	203,653.77	55.00	45,574.02	14.00

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	34	63,491.40	69,761.13	42,823.38	61.40	6,269.73	9.90

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Proj- ects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	4,123.2	5,435.0	31.8	3	3,609.1	4,966.0	37.6
3	Coal	48	27,241.5	30,628.5	12.4	12	13,742.8	17,727.6	29.0
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	7.6
6	Steel	12	34,591.7	55,969.9	61.8	9	32,641.2	54,039.4	65.6
7	Petrochemicals	1	5,460.6	5,460.6	0.0	0	0.0	0.0	0.0
8	Petroleum	71	156,539.5	163,927.1	4.7	16	51,517.3	68,076.3	32.1
9	Power	83	180,012.2	186,096.3	3.4	11	25,563.8	32,102.3	25.6
10	Railways	132	65,054.7	131,386.7	102.0	101	37,121.1	103,510.0	178.8
11	Road Transport & Highways	132	72,461.5	74,266.7	2.5	13	3,890.9	6,265.2	61.0
12	Shipping & Ports	26	18,451.4	19,434.9	5.3	11	6,524.5	7,709.1	18.2
13	Telecommunications	40	19,713.1	20,297.7	3.0	5	2,114.4	2,781.7	31.6
14	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	667,074.7	787,394.0	18.0	187	204,531.7	336,049.3	64.3

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	3	28,122.0	32,960.0	11 - 44
2	Civil Aviation	5	4,123.2	5,435.0	31.8	3	3,524.9	4,604.3	10 - 23
3	Coal	48	27,241.5	30,628.5	12.4	17	11,824.7	14,752.2	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	0	0.0	0.0	-
6	Steel	12	34,591.7	55,969.9	61.8	1	8,692.0	12,291.0	36 - 36
7	Petrochemicals	1	5,460.6	5,460.6	0.0	0	0.0	0.0	-
8	Petroleum	71	156,539.5	163,927.1	4.7	30	74,710.6	84,032.7	2 - 120
9	Power	83	180,012.2	186,096.3	3.4	45	109,856.8	115,653.9	2 - 90
10	Railways	132	65,054.7	131,386.7	102.0	26	22,320.7	51,942.3	2 - 213
11	Road Transport & Highways	132	72,461.5	74,266.7	2.5	90	31,999.9	34,165.2	4 - 106
12	Shipping & Ports	26	18,451.4	19,434.9	5.3	12	8,569.7	9,394.8	2 - 93
13	Telecommunications	40	19,713.1	20,297.7	3.0	2	634.0	809.5	17 - 72
14	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	667,074.7	787,394.0	18.0	234	309,434.7	375,643.5	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	4	29,228.3	34,066.3	0 - 44
2	Civil Aviation	5	4,123.2	5,435.0	31.8	3	3,524.9	4,604.3	10 - 23
3	Coal	48	27,241.5	30,628.5	12.4	16	11,353.0	14,410.6	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	30 - 30
6	Steel	12	34,591.7	55,969.9	61.8	4	15,228.9	17,708.8	0 - 0
7	Petrochemicals	1	5,460.6	5,460.6	0.0	0	0.0	0.0	-
8	Petroleum	71	156,539.5	163,927.1	4.7	17	49,470.3	54,638.4	2 - 73
9	Power	83	180,012.2	186,096.3	3.4	42	104,603.0	108,451.8	2 - 83
10	Railways	132	65,054.7	131,386.7	102.0	37	27,127.7	60,755.8	0 - 213
11	Road Transport & Highways	132	72,461.5	74,266.7	2.5	90	31,999.9	34,165.2	4 - 106
12	Shipping & Ports	26	18,451.4	19,434.9	5.3	11	8,281.2	9,187.2	2 - 93
13	Telecommunications	40	19,713.1	20,297.7	3.0	23	12,227.9	12,535.7	4 - 72
14	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		566	667,074.7	787,394.0	18.0	253	306,316.2	369,963.3	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	4,865.2	5,435.0	11.7	2	2,336.1	2,951.0	26.3
3	Coal	48	28,749.9	30,628.5	6.5	6	4,961.1	7,098.9	43.1
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,401.8	4,401.8	0.0	0	0.0	0.0	0.0
6	Steel	12	55,677.7	55,969.9	0.5	3	598.0	910.3	52.2
7	Petrochemicals	1	5,460.6	5,460.6	0.0	0	0.0	0.0	0.0
8	Petroleum	71	169,133.1	163,927.1	-3.1	4	32,736.9	35,849.3	9.5
9	Power	83	182,573.6	186,096.3	1.9	7	21,938.9	25,975.3	18.4
10	Railways	132	82,773.4	131,386.7	58.7	88	42,723.4	91,397.1	113.9
11	Road Transport & Highways	132	72,461.5	74,266.7	2.5	13	3,890.9	6,265.2	61.0
12	Shipping & Ports	26	18,830.7	19,434.9	3.2	9	6,498.8	7,204.5	10.9
13	Telecommunications	40	19,745.3	20,297.7	2.8	3	1,287.5	1,903.1	47.8
14	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	724,065.4	787,394.0	8.7	139	140,572.6	213,851.6	52.1

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	0	0.00	0.00	0- 0
2	Civil Aviation	5	4,123.24	5,435.02	31.81	0	0.00	0.00	0- 0
3	Coal	48	27,241.47	30,628.50	12.43	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	12	34,591.72	55,969.91	61.80	1	8,692.00	12,291.00	36- 36
7	Petrochemicals	1	5,460.61	5,460.61	0.00	0	0.00	0.00	0- 0
8	Petroleum	71	156,539.45	163,927.12	4.72	13	18,825.72	33,663.21	3- 120
9	Power	83	180,012.22	186,096.29	3.38	3	3,203.84	5,503.63	0- 90
10	Railways	132	65,054.74	131,386.73	101.96	5	2,285.97	7,657.76	0- 80
11	Road Transport & Highways	132	72,461.45	74,266.70	2.49	0	0.00	0.00	0- 0
12	Shipping & Ports	26	18,451.36	19,434.85	5.33	2	567.88	582.03	5- 7
13	Telecommunications	40	19,713.13	20,297.68	2.97	0	0.00	0.00	0- 0
14	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
15	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		566	667074.68	787393.95	18.04	26	38136.7	64805.79	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	2	16,663.00	21,501.00	16- 44
2	Civil Aviation	5	4,123.24	5,435.02	31.81	2	3,215.51	4,340.00	10- 11
3	Coal	48	27,241.47	30,628.50	12.43	7	6,813.24	10,338.47	9- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	12	34,591.72	55,969.91	61.80	1	8,692.00	12,291.00	36- 36
7	Petrochemicals	1	5,460.61	5,460.61	0.00	0	0.00	0.00	0- 0
8	Petroleum	71	156,539.45	163,927.12	4.72	16	51,517.26	68,076.31	3- 120
9	Power	83	180,012.22	186,096.29	3.38	10	24,967.32	31,154.36	3- 90
10	Railways	132	65,054.74	131,386.73	101.96	19	10,615.66	40,585.96	12- 213
11	Road Transport & Highways	132	72,461.45	74,266.70	2.49	13	3,890.90	6,265.24	7- 92
12	Shipping & Ports	26	18,451.36	19,434.85	5.33	7	3,728.52	4,751.17	6- 93
13	Telecommunications	40	19,713.13	20,297.68	2.97	4	1,354.24	1,681.67	17- 72
14	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	15- 15
15	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		566	667074.68	787393.95	18.04	84	142487.06	218182.94	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Railways</u>						
RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN	04/1992	112.53	03/1996	464.50	09/2011	509.57
<u>Road Transport & Highways</u>						
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	12/2003	217.00	10/2008	217.00	09/2011	352.26
<u>Railways</u>						
Sadulpur-Bikaner and Ratangarh- Degana Gauge Canves	04/2007	643.36	03/2011	803.39	03/2012	786.54
<u>Petroleum</u>						
MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF	04/2008	293.60	12/2009	261.75	09/2011	234.81

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Coal</u>					
RCE OF INDARAM OCP(1.20 MTPA)	7/2011	162.76	3/2015	162.76	3/2015
<u>Road Transport & Highways</u>					
JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	1,813.76	7/2013	1,813.76	7/2013
NASHRI CHANANI	6/2010	2,159.00	6/2015	2,159.00	6/2015
DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN	6/2011	600.00	6/2013	600.00	6/2013
SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO	6/2011	535.00	12/2013	535.00	12/2013
ROHTAK-BAWAL	5/2011	650.00	11/2013	650.00	11/2013
4 LANNING OF GODHARA TO GUJARAT/MP BORDER	3/2011	785.50	8/2013	785.50	8/2013
<u>Urban Development</u>					
FARIDABAD EXTENSION	9/2011	2,494.00	9/2014	2,494.00	9/2014
<u>Road Transport & Highways</u>					
QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	1,987.00	7/2015	1,987.00	7/2015
GHAZIABAD-ALIGARH NH-91	2/2011	1,141.00	8/2013	1,141.00	8/2013
<u>Petroleum</u>					
KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II	6/2009	2,915.00	10/2012	2,915.00	3/2013
<u>Urban Development</u>					
DELHI MRTS PHASE-III	9/2011	35,242.00	3/2016	35,242.00	3/2016
<u>Road Transport & Highways</u>					
2 LANNING OF MOKAMA-MUNGER	5/2011	351.54	5/2013	351.54	5/2013
4 LANNING OF AHMEDABAD TO GODHARA	12/2010	1,008.50	6/2013	1,008.50	6/2013
SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.	9/2011	1,250.00	12/2013	1,250.00	12/2013
PATNA-MUZZAFFARPUR	8/2010	671.30	2/2013	671.30	2/2013
<u>Coal</u>					
JALAGAM VENGALA RAO OCP	7/2011	447.06	3/2015	447.06	-

VII. Milestones (Cumulative due & achieved)

Total	2300
Achieved up to month	969

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	15,824.00	12/2008	07/2012	08/2012	1
<u>Coal</u>						
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	09/2011	10/2011	1
TUTICORIN THERMAL POWER PROJECT NLC	4,904.54	4,909.54	N.A.	10/2012	02/2013	4
<u>Steel</u>						
67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	N.A.	12/2011	01/2012	1
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	11/2011	01/2012	2
<u>Petroleum</u>						
Polypropylene unit Mangalore Refin	1,803.78	1,803.78	07/2012	06/2012	07/2012	1
PARADIP REFINERY PROJECT IOCL	29,777.00	30,426.00	11/2012	11/2012	06/2013	7
CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2011	12/2012	12
<u>Power</u>						
CHAMERA,STAGE-III (NHPC) NHPC	1,405.63	1,405.63	08/2010	11/2011	12/2011	1
URI H.E.P STAGE -II (NHPC) NHPC	1,724.79	1,724.79	11/2009	12/2011	02/2012	2
EASTERN REGION STRENGTHENING SCHEME- II PGCIL	227.52	227.52	06/2010	09/2011	11/2011	2
<u>Railways</u>						
LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	208.68	03/2002	09/2011	12/2011	3
KHURDA ROAD- BOLANGIR(NL)ECOR ECOR	355.38	1,100.00	N.A.	08/2011	12/2011	4
<u>Road Transport & Highways</u>						
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	09/2011	10/2011	1


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) NHAI	151.30	151.30	10/2008	11/2011	12/2011	1
RINGBUNDS TO JHAJHANPUR (BR-6) NHAI	340.00	340.00	06/2008	09/2011	10/2011	1
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	09/2011	10/2011	1
JHANSI TO LALITPUR, NH-26 NHAI	276.09	276.09	09/2009	10/2011	11/2011	1
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	09/2011	10/2011	1
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	09/2011	10/2011	1
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) NHAI	225.00	225.00	10/2008	09/2011	11/2011	2
JHANSI TO LALITPUR, NH-25,26 NHAI	355.06	355.06	09/2009	12/2011	02/2012	2
HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	09/2011	12/2011	3
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	09/2011	12/2011	3
HALDIA PORT (PORT CONNECTIVITY) (NH-41) NHAI	273.00	522.00	03/2005	09/2011	12/2011	3
GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 NHAI	412.78	479.54	11/2007	09/2011	12/2011	3
ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	12/2011	03/2012	3
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	07/2010	09/2011	12/2011	3
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	09/2011	12/2011	3
ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	09/2011	01/2012	4
TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	01/2012	05/2012	4
GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHAI	155.00	201.66	09/2008	12/2011	06/2012	6
Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) NHAI	1,108.00	2,288.00	11/2011	11/2011	06/2012	7
CHAMBAL BRIDGE, NH-76 (RJ-5) NHAI	275.00	281.31	02/2010	03/2012	07/2013	16


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
Number of projects reporting additional delay = 34						

Trend and Graphical Analysis of All Projects

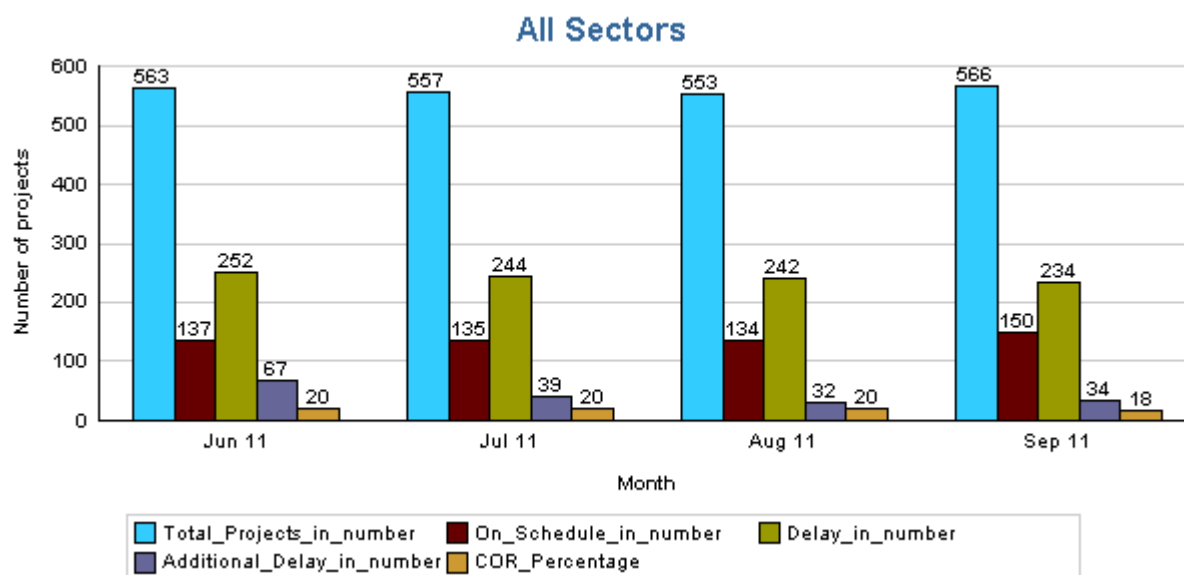


All Sectors Break-up of 234 Delayed projects in September 2011

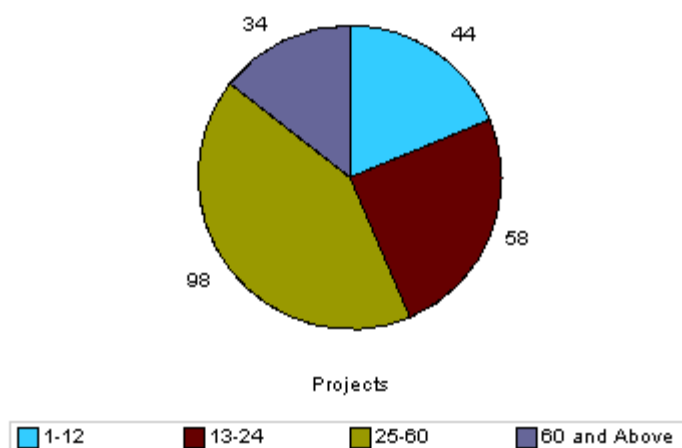


Trend and Graphical Analysis


Urban Development Sector

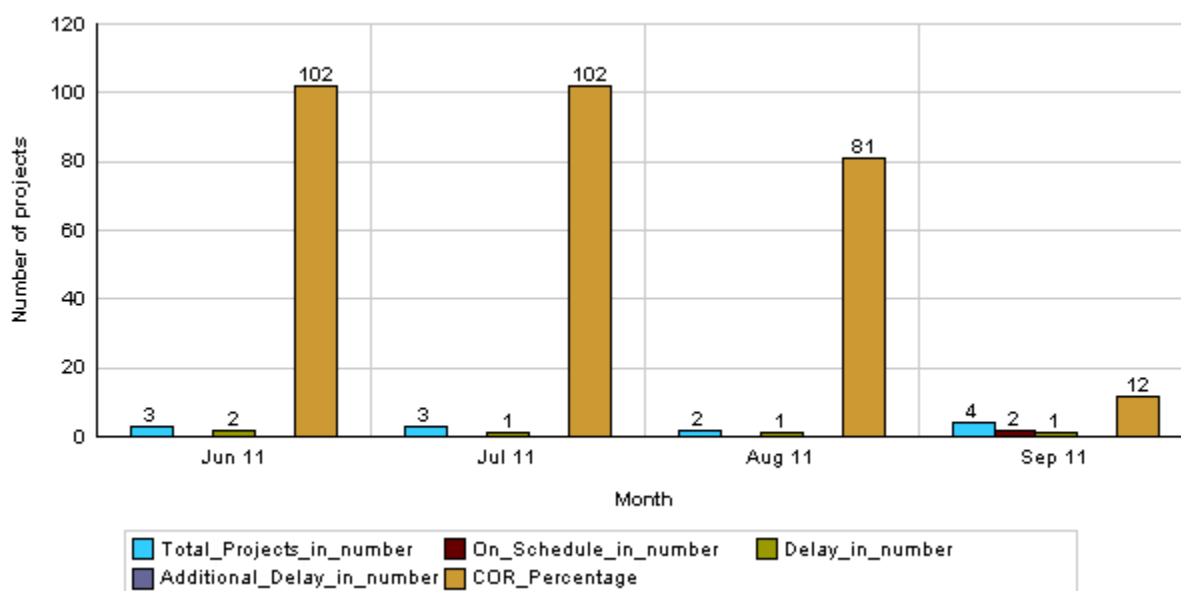


Urban Development Sector Break-up of 1 Delayed projects in September 2011

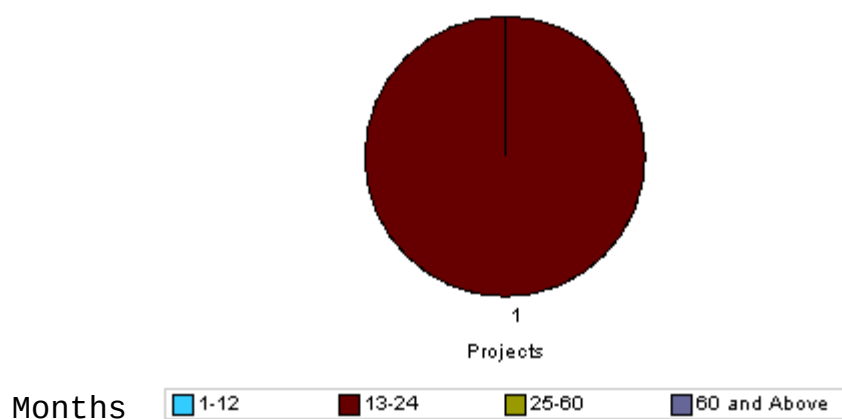

Trend and Graphical Analysis Telecommunications Sector

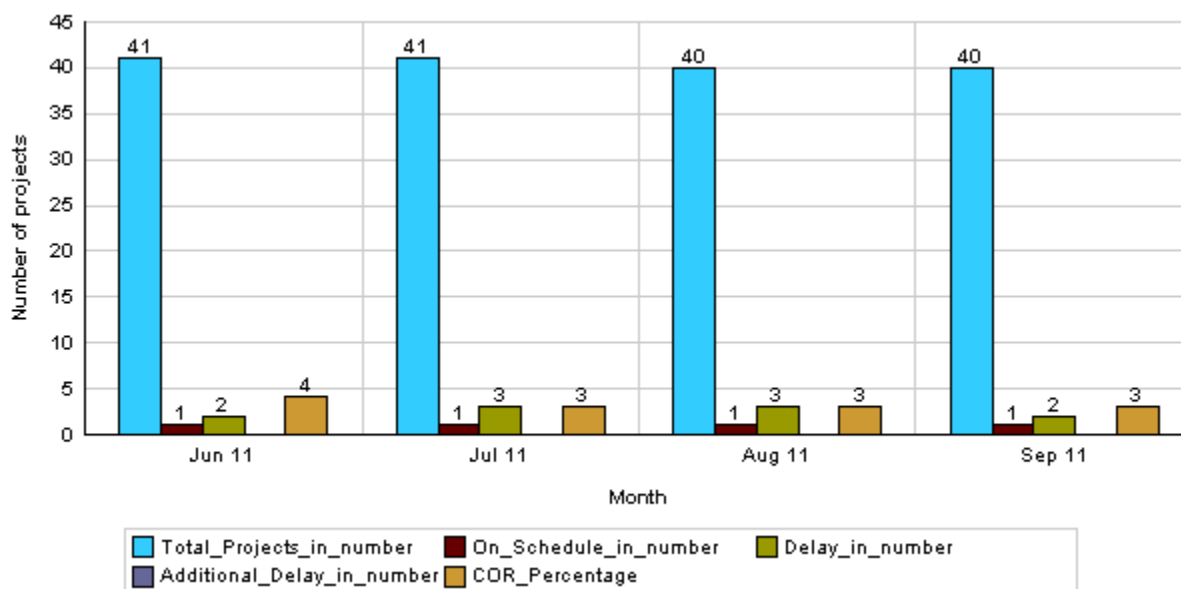


Telecommunications Sector Break-up of 2 Delayed projects in September 2011

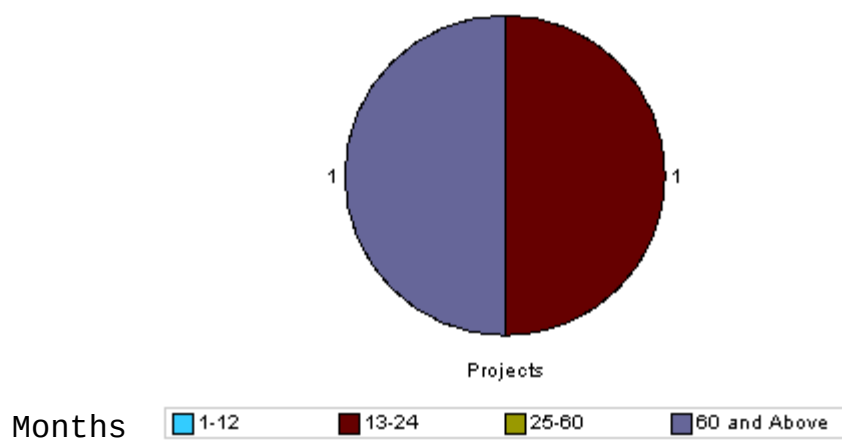


Trend and Graphical Analysis

Shipping and Ports Sector

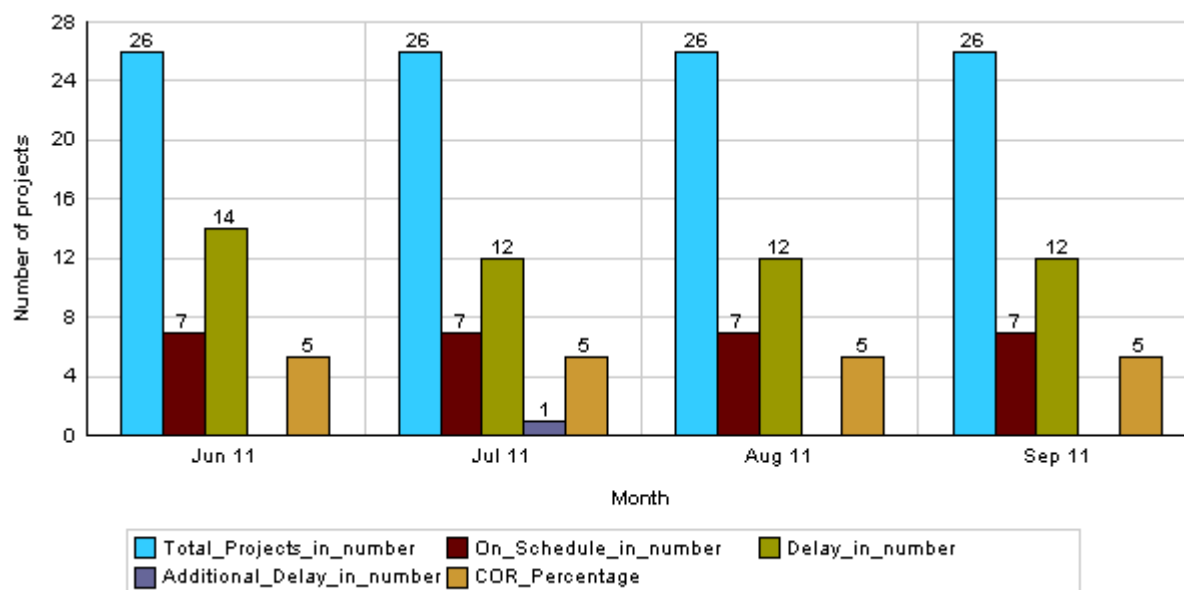


Sector Break-up of 12 Delayed projects in September 2011

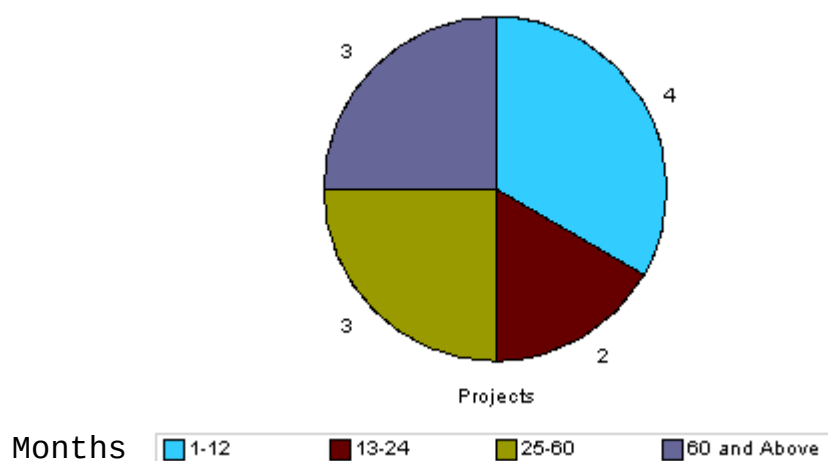


Trend and Graphical Analysis

Road Transport and Highways Sector

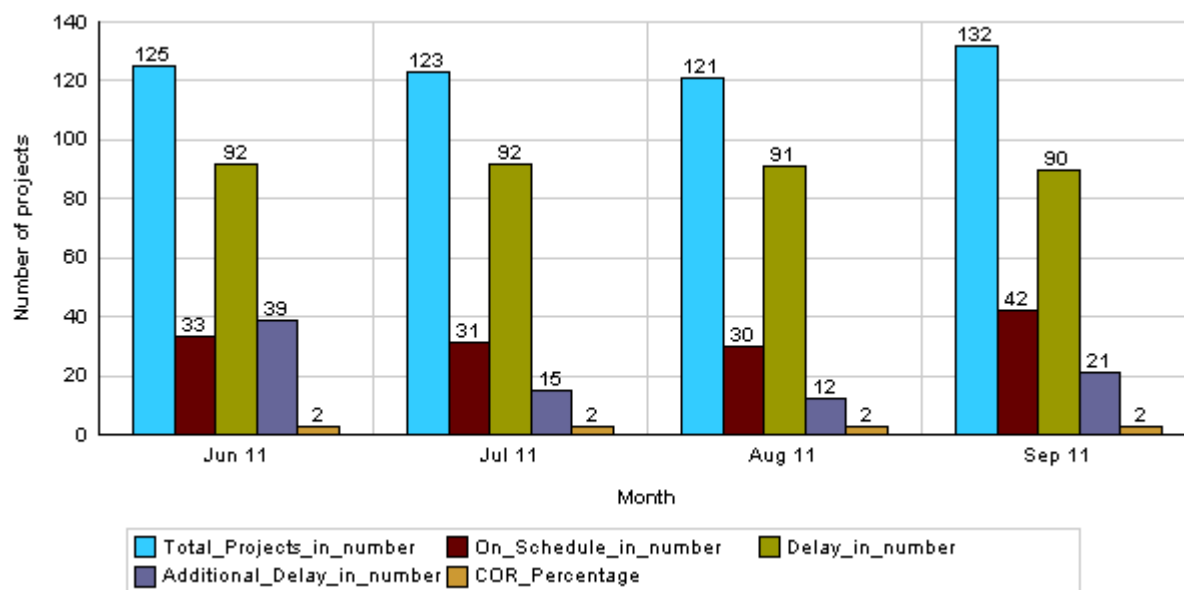


Sector Break-up of 90 Delayed projects in September 2011

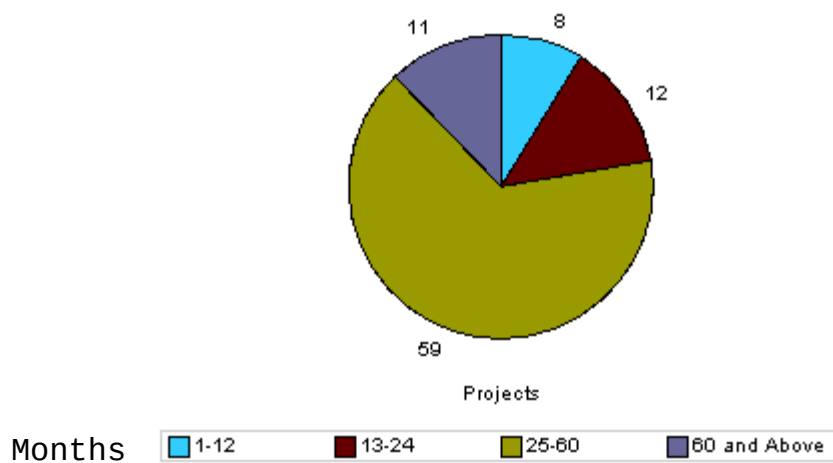


Trend and Graphical Analysis

Railways Sector

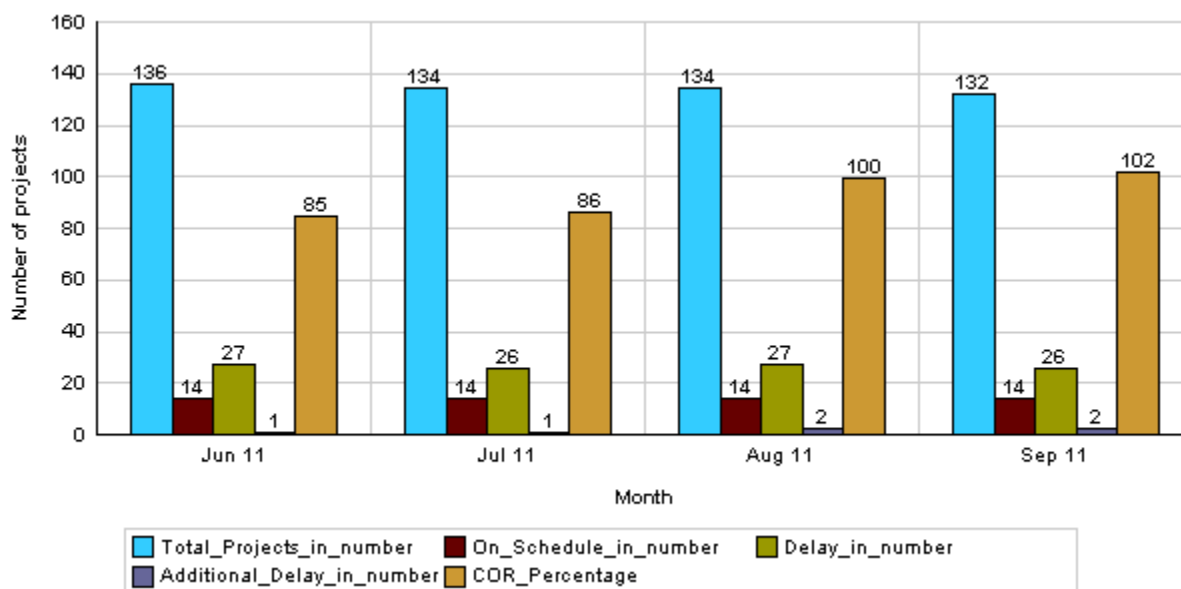


Railways Sector Sector Break-up of 26 Delayed projects in September 2011

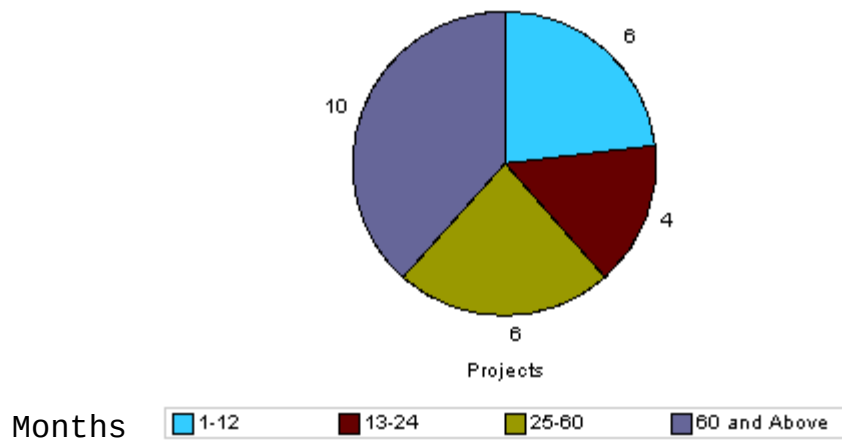


Trend and Graphical Analysis

Power Sector

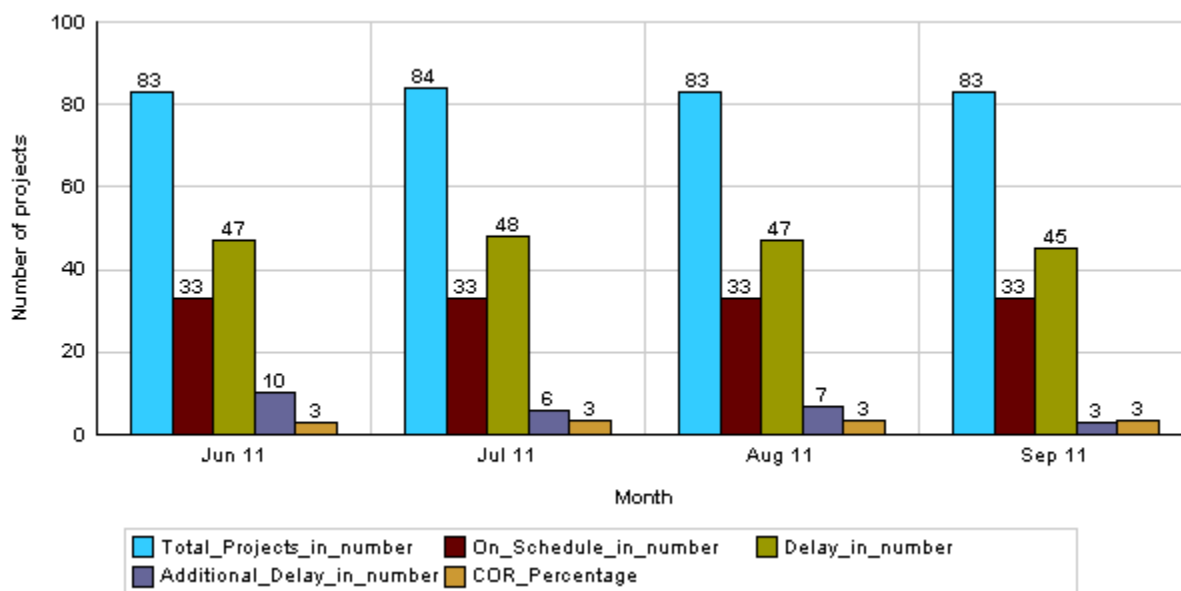


Power Sector Sector Break-up of 45 Delayed projects in September 2011

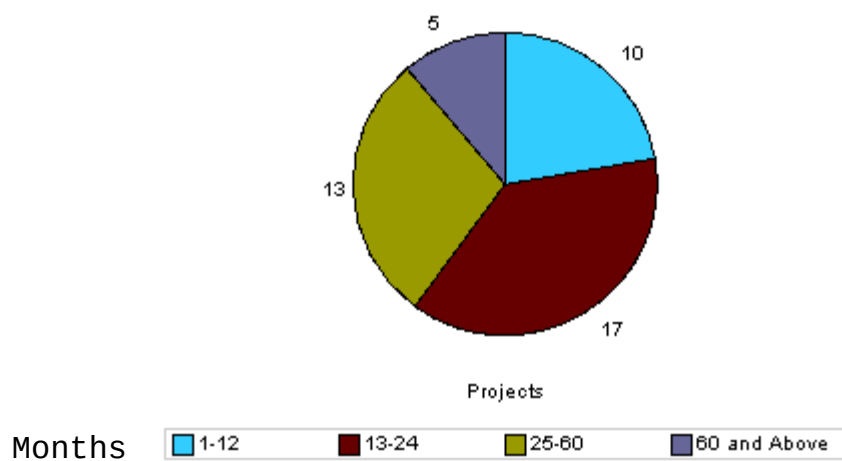


Trend and Graphical Analysis

Petroleum Sector

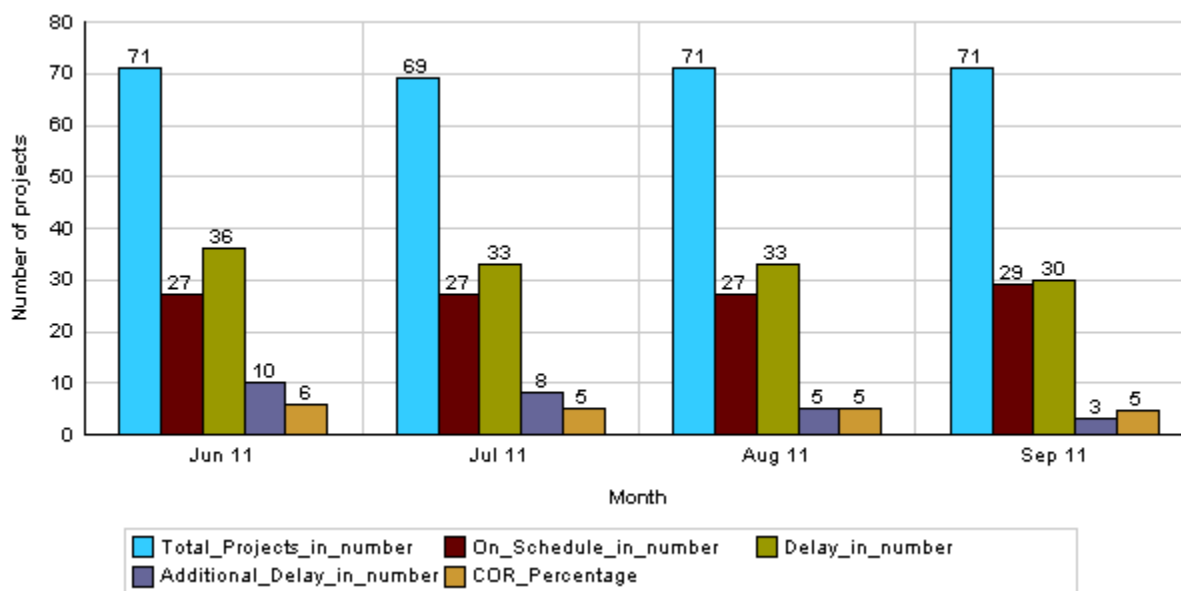


Petroleum Sector Sector Break-up of 30 Delayed projects in September 2011

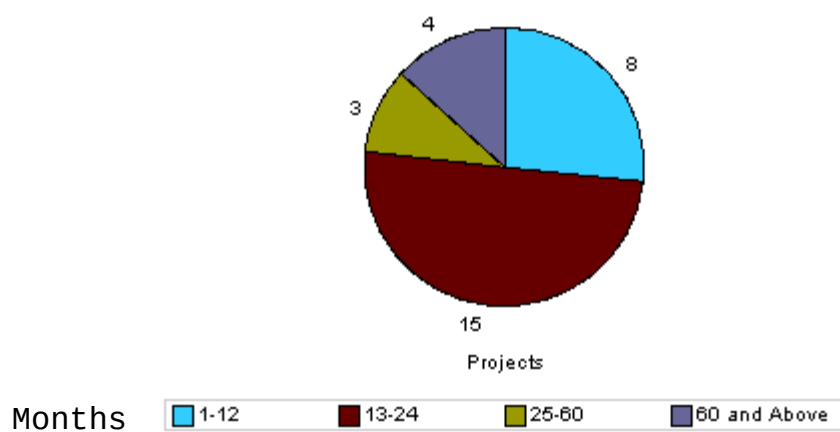


Trend and Graphical Analysis

Steel Sector

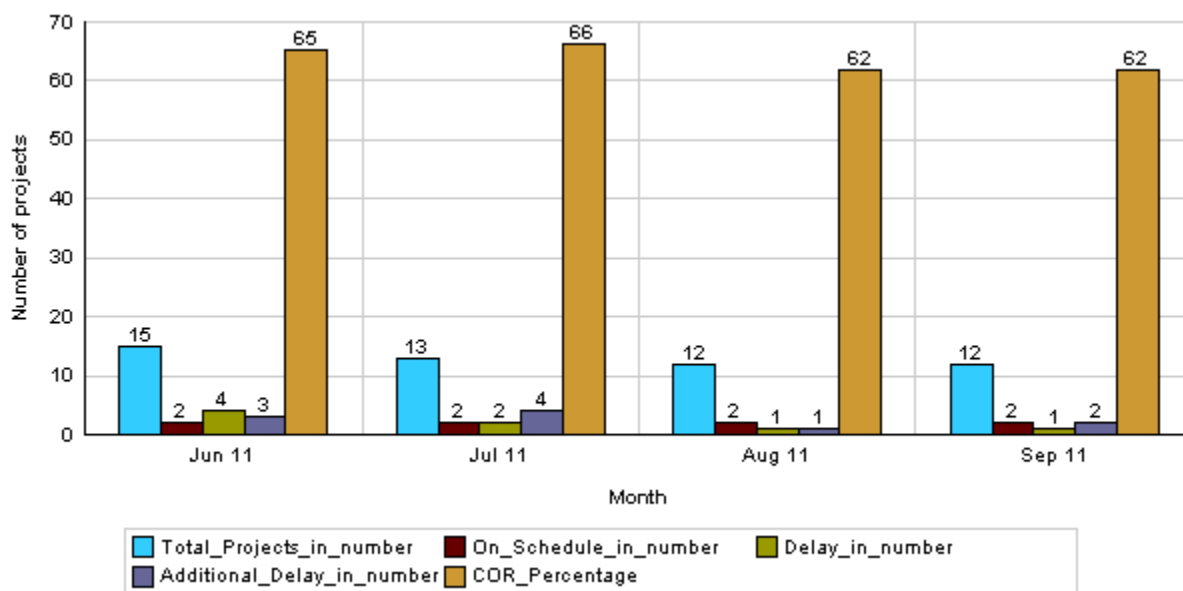


Steel Sector Sector Break-up of 1 Delayed projects in September 2011

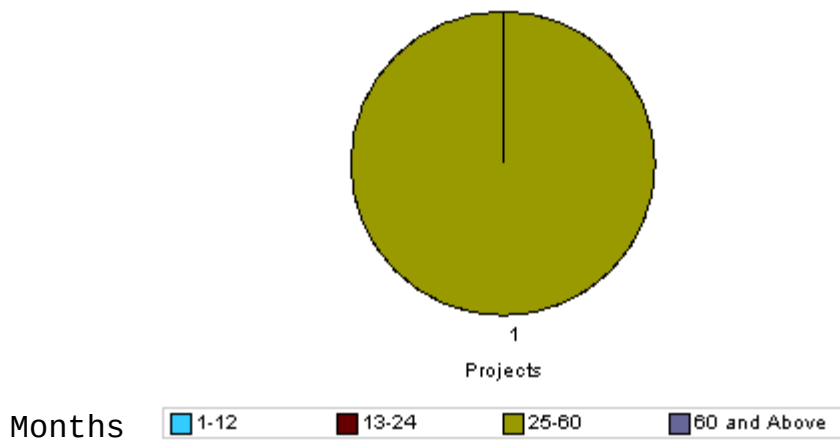


Trend and Graphical Analysis

Fertilisers Sector

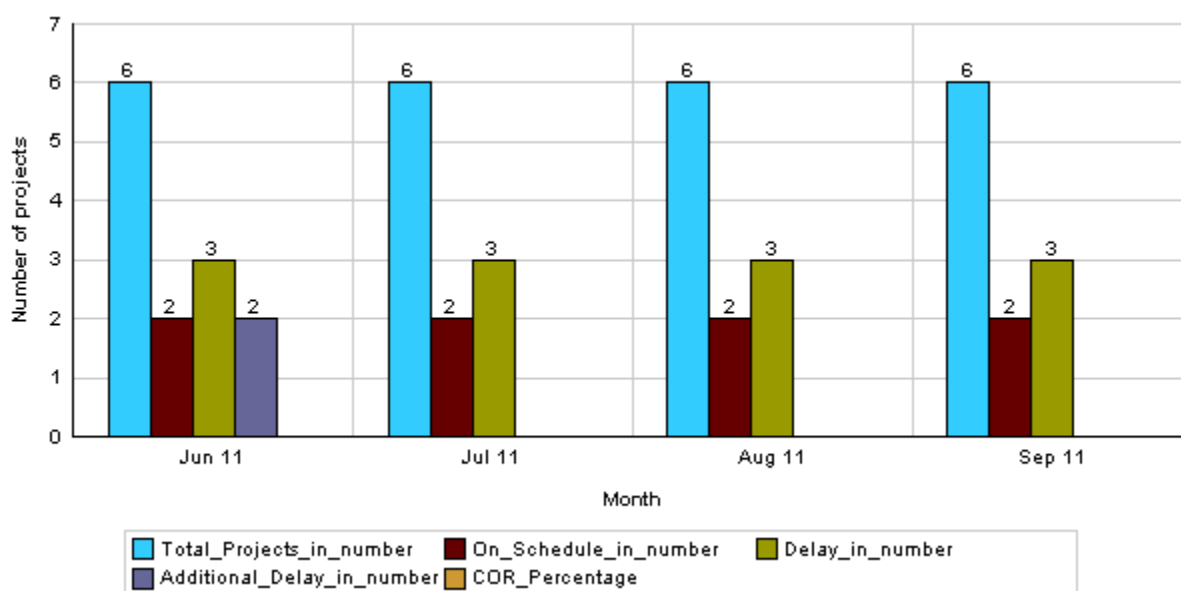


Fertilisers Sector Break-up of 3 Delayed projects in September 2011

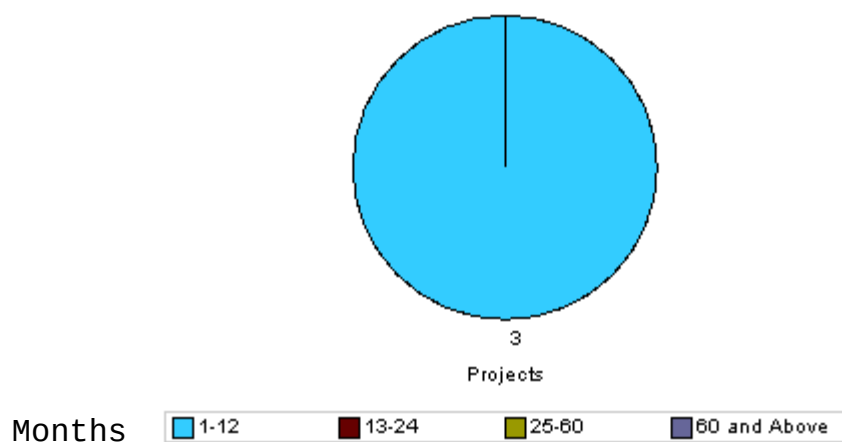


Trend and Graphical Analysis

Coal Sector

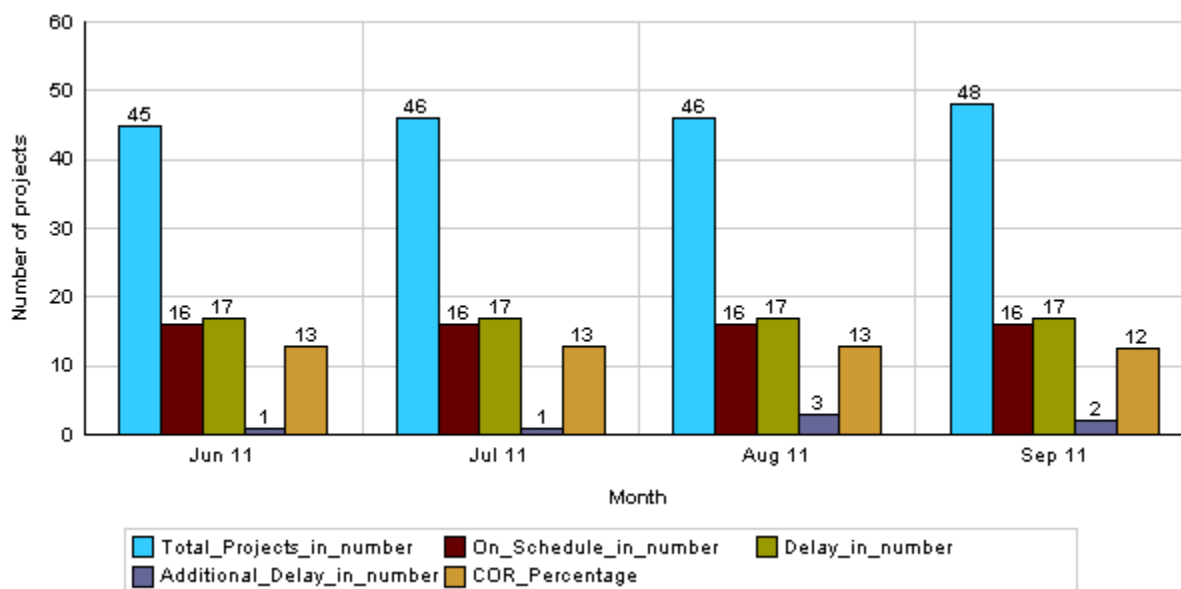


Coal Sector Sector Break-up of 17 Delayed projects in September 2011

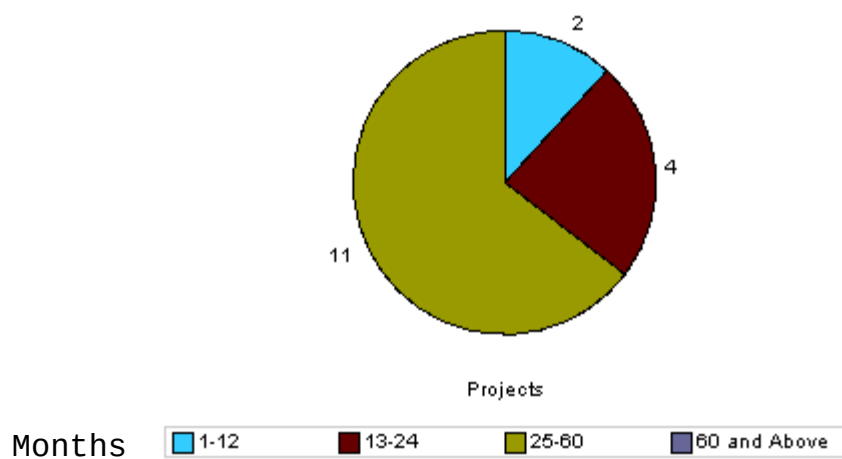


Trend and Graphical Analysis

Civil Aviation Sector

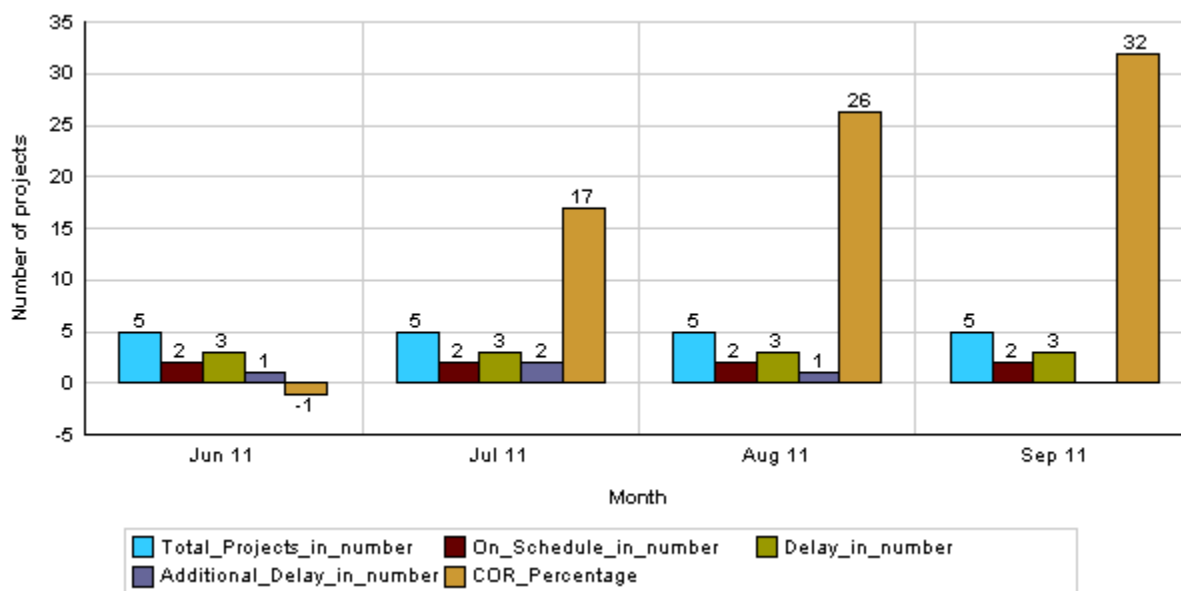


Civil Aviation Sector Break-up of 3 Delayed projects in September 2011

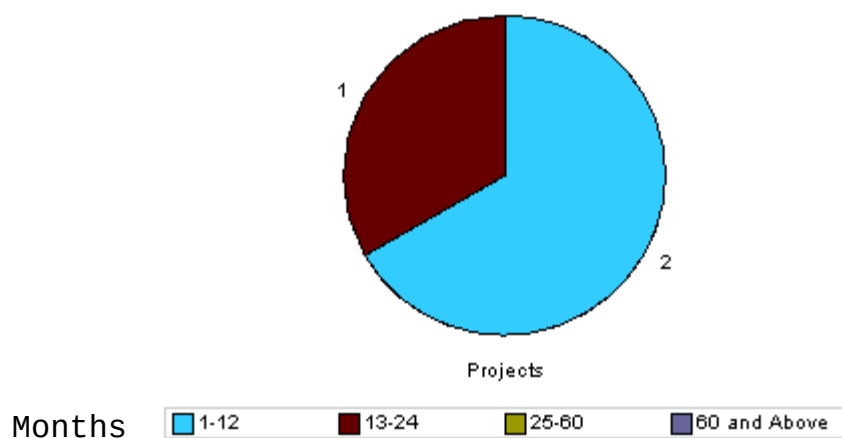


Trend and Graphical Analysis

Atomic Energy Sector

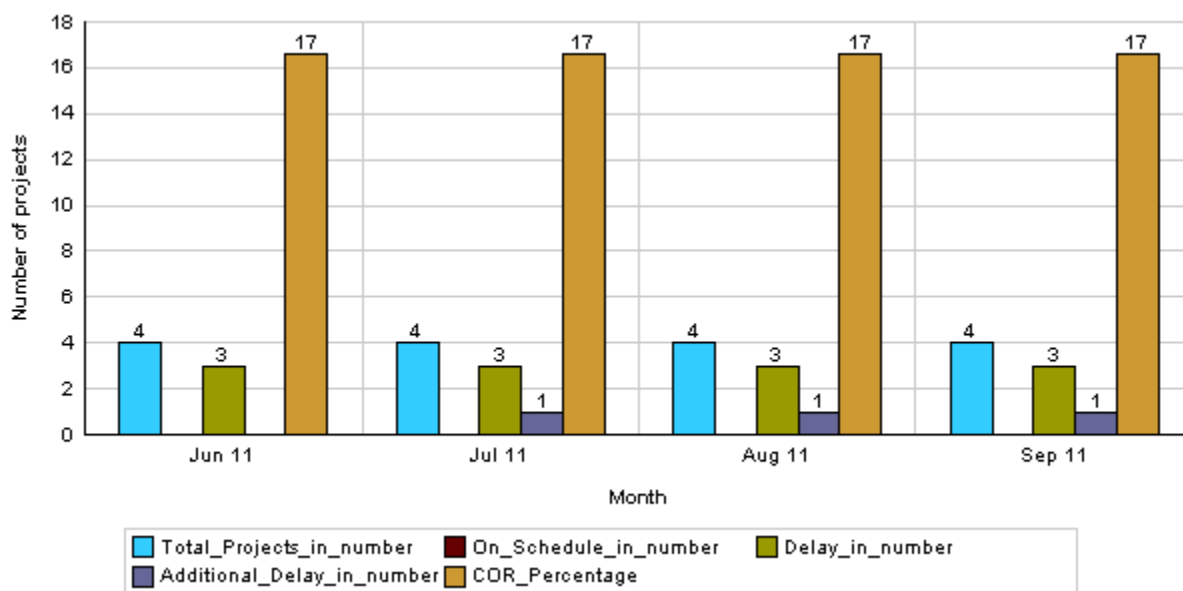

Atomic Energy Sector Sector Break-up of 3 Delayed projects in September 2011

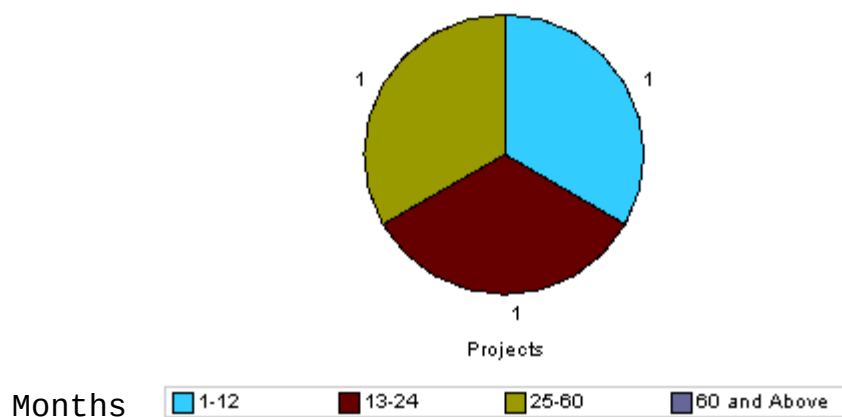

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	29,228.29	29,228.29	34,066.29
Civil Aviation	5	4,123.24	4,865.24	5,435.02
Coal	48	27,241.47	28,749.92	30,628.50
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	12	34,591.72	55,677.65	55,969.91
Petrochemicals	1	5,460.61	5,460.61	5,460.61
Petroleum	71	156,539.45	169,133.11	163,927.12
Power	83	180,012.22	182,573.64	186,096.29
Railways	132	65,054.74	82,773.37	131,386.73
Road Transport & Highways	132	72,461.45	72,461.45	74,266.70
Shipping & Ports	26	18,451.36	18,830.67	19,434.85
Telecommunications	40	19,713.13	19,745.26	20,297.68
Urban Development	4	44,245.18	44,304.08	49,518.08
Water Resources	1	542.90	542.90	1,187.00
Grand total	566	667,074.68	724,065.36	787,393.95

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,240.50	09/2010	01/2012	16(O)	8/80
2	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,054.00	12/2008	08/2012	44(O)	61/119
4	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,001.00	12/2015 05/2016	11/2016	6(R1)	0/70
Total			29,228.29	34,066.29	19,296.20				69/270
<u>Civil Aviation</u>									
5	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 2,015.00	2,015.00	940.61	01/2011	12/2011	11(O)	0/0
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,391.83	05/2011	03/2012	10(O)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73	204.73	48.41	05/2012	05/2012	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40	264.29	153.38	01/2011	12/2012	23(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60	626.00	324.99	06/2013	06/2013	0(O)	0/0
Total			4,123.24	5,435.02	2,859.22				0/0
<u>Coal</u>									
10	BARSINGAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,654.84	06/2009	10/2011	28(O)	59/26
11	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96	302.96	-	03/2010	03/2012	24(O)	9/11
12	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	101.43	03/2011 03/2012	03/2012	0(R3)	0/2
13	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	1.51	03/2012 03/2012	03/2012	0(R3)	0/1

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	-	-	03/2012	-	4/4
15	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Orissa	08/2008	207.28	207.28	67.90	-	03/2012	-	5/7
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	77.51	03/2012	03/2012	0(O)	28/27
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	21.20	03/2012	03/2012	0(O)	10/34
18	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,275.41	06/2009	05/2012	35(O)	60/24
19	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,079.84	-	02/2013	-	0/6
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88	741.62	143.22	03/2010	03/2013	36(O)	0/2
21	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	569.78	-	03/2013	-	0/8
22	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	-	-	03/2013	-	6/11
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	71.65	-	03/2013	-	5/7
24	Purnadih OCP - [N06000085]JCL,Jharkhandd	07/2008	210.98	210.98	24.25	03/2013	03/2013	0(O)	0/2
25	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	197.88	03/2013 09/2012	12/2013	15(R3)	2/22
26	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,267.89	03/2010	03/2014	48(O)	3/15
27	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	1,090.84	03/2010	03/2014	48(O)	2/13
28	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	37.71	03/2014	03/2014	0(O)	1/2
29	CHURCHA RO UG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	257.30	-	03/2014	-	0/4
30	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.49	03/2011	03/2014	36(O)	0/3
31	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/1
32	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	203.09	-	03/2014	-	0/5
33	Churi Benti UG - [N06000083]JCL,Jharkhandd	06/2007	163.51	163.51	33.57	03/2011 03/2012	03/2014	24(R3)	0/2
34	North Urimari OCP - [N06000084]JCL,Jharkhandd	12/2007	179.87	179.87	66.45	03/2012 03/2012	03/2014	24(R3)	0/2
35	Tapin OCP - [N06000086]JCL,Jharkhandd	08/2008	264.68	264.68	76.05	03/2012 03/2013	03/2014	12(R3)	0/2

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	26.36	03/2014	03/2014	0(O)	0/0
37	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77	339.77	0.65	-	10/2014	-	1/1
38	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	139.85	03/2012	03/2015	36(O)	0/2
39	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	1/5
40	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	-	-	03/2015	-	2/12
41	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
42	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	68.86	12/2012	03/2015	27(O)	11/44
43	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
44	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/1
45	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	18.17	03/2015	03/2015	0(O)	4/31
46	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
47	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.14	03/2015	03/2015	0(O)	0/0
48	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	211.50	03/2014	03/2016	24(O)	1/2
49	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.21	07/2012 03/2014	03/2016	24(R3)	0/2
50	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	-	-	03/2016	-	1/12
51	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	90.25	03/2016	03/2016	0(O)	0/1
52	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	290.44	03/2016	03/2016	0(O)	0/2
53	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	94.23	-	03/2017	-	6/12
54	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018	03/2018	0(O)	0/0
55	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015	-	-	0/0
56	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	40.04	03/2012 03/2012	-	-	13/42
57	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013 03/2013	-	-	0/83
Total			27,241.47	30,628.50	11,348.82				234/525

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Fertilisers									
58	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	178.07	- 11/2011	11/2011	0(R3)	4/22
59	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011	11/2011	4(O)	0/0
60	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011	03/2012	8(O)	0/0
61	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	175.88	01/2013	01/2013	0(O)	0/5
62	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	177.02	01/2013	01/2013	0(O)	0/5
63	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	223.57	12/2012	01/2013	1(O)	0/8
Total			5,317.41	5,317.41	944.64				4/40
Mines									
64	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51 4,401.76	4,401.76	4,144.00	12/2008 01/2011	06/2011	5(R3)	117/110
Total			4,091.51	4,401.76	4,144.00				117/110
Steel									
65	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	111.28 232.93	232.93	168.27	- -	10/2011	-	0/1
66	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00 6,325.00	6,325.00	2,109.69	- 12/2011	12/2011	0(R3)	0/11
67	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	234.15	- 02/2011	01/2012	11(R3)	2/3
68	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	221.73	- 08/2010	01/2012	17(R3)	1/2
69	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	291.61	- 12/2011	03/2012	3(R3)	18/21
70	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	460.00	130.64	- 05/2012	05/2012	0(R3)	1/2
71	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	11,272.00	- 12/2011	06/2012	6(R3)	6/14
72	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	8,855.52	10/2009 10/2012	10/2012	0(R3)	48/59

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
73	COKE OVEN BATTERY NO. 4 PHASE-II - [N1200038]RINL, Andhra Pradesh	08/2007	108.00	216.68	47.29	- 10/2012	10/2012	0(R3)	3/4
74	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	3,212.16	- 03/2013	03/2013	0(R3)	4/20
75	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka	04/2011	572.00	572.00	-	04/2013 -	04/2013	0(O)	0/0
76	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC, Karnataka	02/2011	898.55	898.55	-	05/2013 -	05/2013	0(O)	0/0
	Total		34,591.72	55,969.91	26,543.06				83/137
	Petrochemicals								
77	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61	5,460.61	3,020.26	- -	04/2012	-	0/30
	Total		5,460.61	5,460.61	3,020.26				0/30
	Petroleum								
78	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	527.43	03/2011 05/2011	06/2011	1(R3)	0/0
79	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar	06/2009	613.54	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
80	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]BRPL, Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
81	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 299.00	299.00	251.19	02/2011 08/2011	08/2011	0(R3)	0/0
82	DAHEJ-VIJAYPUR PIPE LINE PROJECT (PHASE-II) - [N16000052]GAIL, Multi State	11/2007	4,429.38	2,340.00	2,254.62	10/2010 09/2011	09/2011	0(R2)	0/0
83	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
84	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL, Maharashtra	06/2008	304.40	304.40	245.01	06/2010 07/2011	09/2011	2(R3)	0/0
85	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC, Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
86	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
87	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL, Multi State	11/2007	1,816.07	1,385.00	967.39	10/2010 12/2011	12/2011	0(R3)	0/1
88	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00	810.00	635.71	04/2011 12/2011	12/2011	0(R3)	0/2

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
89	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	202.12	03/2013 03/2013	12/2011	-15(R1)	0/0
90	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	644.81	04/2010 -	12/2011	20(O)	0/0
91	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	257.60	04/2011 -	12/2011	8(O)	0/0
92	EURO-IV DHD - [N16000109]CPCL,	09/2008	2,615.69 -	2,615.69	1,674.51	- -	12/2011	-	0/116
93	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	174.44	09/2012 -	12/2011	-9(O)	0/0
94	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- [N16000070]GAIL,Multi State	07/2009	238.68 -	204.00	134.55	01/2012 -	01/2012	0(O)	1/8
95	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	6,869.78	01/2012 -	01/2012	0(O)	0/0
96	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 02/2012	02/2012	0(R3)	0/0
97	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
98	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	0(R3)	0/0
99	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	163.18	03/2012 08/2012	03/2012	-5(R3)	7/12
100	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	6,652.22	-	01/2013 -	03/2012	-10(O)	0/0
101	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	155.13	06/2011 03/2012	03/2012	0(R3)	3/9
102	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
103	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
104	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,596.54	05/2010 05/2012	05/2012	0(R3)	0/0
105	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	38.35	05/2010 04/2012	05/2012	1(R3)	0/0
106	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	92.09	07/2010 05/2012	05/2012	0(R3)	0/0
107	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	56.16	05/2012 -	05/2012	0(O)	18/36

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,380.59	08/2010 03/2012	06/2012	3(R3)	0/0
109	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	535.59	06/2012 -	06/2012	0(O)	0/0
110	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	678.19	06/2012 -	06/2012	0(O)	6/9
111	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
112	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	70.85	04/2011 -	07/2012	15(O)	0/0
113	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	400.00	154.72	06/2011 07/2012	07/2012	0(R2)	7/9
114	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	413.47	07/2012 -	07/2012	0(O)	0/0
115	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,225.00	03/2012 08/2012	08/2012	0(R3)	11/10
116	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	105.00	08/2012 -	08/2012	0(O)	0/0
117	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,296.56	09/2012 -	09/2012	0(O)	0/0
118	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	444.44	09/2012 -	09/2012	0(O)	0/15
119	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	21.14	09/2012 -	09/2012	0(O)	0/0
120	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.53	09/2011 -	12/2012	15(O)	0/0
121	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	80.28	12/2011 -	01/2013	13(O)	0/0
122	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	29.35	01/2013 -	01/2013	0(O)	12/18
123	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2(O)	0/0
124	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	20.87	02/2013 -	02/2013	0(O)	15/42
125	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	231.94	03/2006 03/2013	03/2013	0(R3)	6/6
126	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,767.52	05/2010 03/2013	03/2013	0(R3)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
127	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	367.91	03/2013	03/2013	0(O)	0/0
128	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
129	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
130	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11	372.11	-	03/2013	03/2013	0(O)	0/0
131	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL, Multi State	06/2009	2,915.00	2,915.00	-	10/2012	03/2013	5(O)	0/0
132	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL, Maharashtra	04/2008	825.00 1,827.00	1,827.00	160.16	12/2011 04/2013	04/2013	0(R3)	0/203
133	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79	861.79	-	05/2013	05/2013	0(O)	0/0
134	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00	30,426.00	9,720.18	11/2012	06/2013	7(O)	107/100
135	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20	331.20	-	08/2013	08/2013	0(O)	0/0
136	Wax Project - [N16000101]NRL, Assam	06/2010	576.60	576.60	13.77	12/2013 12/2013	12/2013	0(R3)	0/0
137	Development of WO-16 Cluster Fields - [N16000105]ONGC, Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
138	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC, Assam	06/2010	202.94	202.94	-	01/2014	01/2014	0(O)	0/0
139	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00	8,140.00	-	02/2014	02/2014	0(O)	0/0
140	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC, Assam	09/2001	345.10 663.69	663.69	592.78	03/2007 03/2014	03/2014	0(R3)	3/3
141	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
142	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
143	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
144	IOR GELEKI (ONGCL) - [160100216]ONGC, Assam	09/2001	390.09 1,674.11	1,674.11	1,375.28	03/2007 03/2017	03/2017	0(R3)	6/6
145	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
146	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00	756.00	744.26	09/2011	-	-	0/0
147	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	-	-	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
148	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089])OCL,Maharashtra	12/2009	1,584.00	1,584.00	3.38	-	08/2013	-	0/0
	Total		156,539.45	163,927.12	57,373.16				202/605
	Power								
149	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	212.75	05/2011 05/2011	09/2011	4(R3)	0/0
150	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	132.86	06/2010	11/2011	17(O)	0/0
151	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,668.16	08/2010	12/2011	16(O)	0/0
152	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	467.55	01/2010	12/2011	23(O)	0/22
153	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,949.84	07/2010	12/2011	17(O)	3/20
154	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	295.81	07/2011	12/2011	5(O)	0/0
155	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,542.17	11/2009	02/2012	27(O)	0/0
156	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	693.43	02/2011	02/2012	12(O)	0/1
157	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	304.39	02/2012	02/2012	0(O)	0/0
158	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	60.03	02/2012	02/2012	0(O)	0/0
159	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	147.86	08/2011	02/2012	6(O)	0/0
160	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	209.58	07/2010 02/2012	02/2012	0(R3)	0/0
161	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	73.29	07/2011	02/2012	7(O)	0/0
162	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,283.69	2,492.85	04/2005	03/2012	83(O)	7/11
163	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,357.00	12/2009	03/2012	27(O)	33/60
164	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,562.46	10/2010	03/2012	17(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
165	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.G.R.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,483.30	09/2009	03/2012	30(O)	15/30
166	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	690.87	10/2009	03/2012	29(O)	2/20
167	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.83	4,076.00	-	03/2012	-	0/6
168	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	55.89	11/2011	03/2012	4(O)	0/0
169	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	76.44	04/2012	04/2012	0(O)	0/0
170	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,373.35	03/2007	05/2012	62(O)	1/25
171	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	287.91	05/2012	05/2012	0(O)	0/0
172	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	414.30	06/2012	06/2012	0(O)	0/0
173	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	118.40	06/2012	06/2012	0(O)	0/0
174	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	10.88	06/2012	06/2012	0(O)	0/0
175	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,687.14	08/2012	08/2012	0(O)	0/0
176	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	3,988.90	08/2012	08/2012	0(O)	0/0
177	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	396.22	08/2012	08/2012	0(O)	0/0
178	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,035.57	10/2012	10/2012	0(O)	0/0
179	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	174.37	10/2012	10/2012	0(O)	0/0
180	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	11.32	10/2012	10/2012	0(O)	0/0
181	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	670.42	08/2010	11/2012	27(O)	0/0
182	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	2,861.00	08/2012	11/2012	3(O)	3/16
183	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	323.94	11/2012	11/2012	0(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
184	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	253.39	11/2012 -	11/2012	0(O)	0/0
185	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	91.61	11/2012 -	11/2012	0(O)	0/0
186	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	1,020.22	09/2009 -	12/2012	39(O)	0/0
187	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,946.85	1,733.05	11/2008 -	12/2012	49(O)	25/38
188	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	685.00	11/2011 -	12/2012	13(O)	6/34
189	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	2,637.46	12/2012 -	12/2012	0(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	266.43	11/2011 -	12/2012	13(O)	0/0
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	260.37	11/2011 -	12/2012	13(O)	0/0
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	131.19	02/2012 -	12/2012	10(O)	0/0
193	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	2,225.00	10/2012 -	12/2012	2(O)	3/15
194	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,076.00	10/2012 -	12/2012	2(O)	3/16
195	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	350.24	12/2012 -	12/2012	0(O)	0/0
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	25.54	01/2013 -	01/2013	0(O)	0/0
197	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	19.25	01/2013 -	01/2013	0(O)	0/0
198	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	3,817.00	04/2009 -	03/2013	47(O)	19/9
199	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	343.31	09/2010 -	03/2013	30(O)	0/0
200	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	873.35	02/2012 -	03/2013	13(O)	0/0
201	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	167.23	03/2013 -	03/2013	0(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
202	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	76.42	04/2013 -	04/2013	0(O)	0/0
203	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	8.71	04/2013 -	04/2013	0(O)	0/0
204	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	70.41	01/2012 -	07/2013	18(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	50.10	07/2013 -	07/2013	0(O)	0/0
206	TRANSMISSION SYSTEM OF ESTABLISHMENT OF 400/220KV - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0
207	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	223.21	08/2013 08/2013	08/2013	0(R3)	10/17
208	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	74.08	08/2013 -	08/2013	0(O)	0/0
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	18.55	08/2013 -	08/2013	0(O)	0/0
210	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	125.67	08/2013 -	08/2013	0(O)	0/0
211	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,361.96	01/2012 -	09/2013	20(O)	2/10
212	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	131.66	11/2011 -	09/2013	22(O)	0/0
213	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,306.00	06/2011 -	10/2013	28(O)	0/29
214	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	2,889.00	- -	10/2013	-	2/18
215	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	57.33	11/2013 -	11/2013	0(O)	0/0
216	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	216.21	12/2013 -	12/2013	0(O)	0/0
217	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	265.42	07/2006 01/2014	01/2014	0(R3)	2/5
218	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	-	03/2014 -	03/2014	0(O)	0/0
219	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,159.00	03/2013 -	06/2014	15(O)	6/13
220	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	6,285.33	5,127.36	09/2010 -	08/2014	47(O)	2/11

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	6,104.00	12/2009	09/2014	57(O)	15/70
222	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	2,877.41	08/2013	09/2014	13(O)	0/0
223	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	3,293.30	09/2009	12/2014	63(O)	1/20
224	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
225	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	939.65	07/2014	01/2016	0(R3)	0/0
226	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,	07/2006	1,657.00	2,978.86	277.11	07/2010	02/2016	67(O)	1/10
227	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	3,422.44	172.38	07/2014	05/2016	22(O)	0/7
228	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,582.26	05/2013	06/2016	0(R3)	79/22
229	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	947.96	831.16	12/2007	-	-	14/18
230	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	113.23	06/2011	08/2011	2(O)	0/0
231	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	93.24	01/2011	-	-	0/1
Total			180,012.22	186,096.29	90,326.72				254/574
Railways									
232	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	233.90	-	12/2010	22(R1)	0/0
233	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41	211.90	188.11	02/2009	12/2010	21(R1)	0/0
234	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	221.90	157.88	12/2007	12/2010	9(R1)	0/0
235	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73	399.50	294.93	03/2009	12/2010	24(R1)	0/0
236	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80	200.80	-	-	12/2010	-	0/0
237	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	273.00	299.77	-	03/2011	24(R1)	0/0
238	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00	329.70	261.00	03/2009	03/2011	15(R1)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
239	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,270.81	- 12/2010	06/2011	6(R3)	0/1
240	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	194.44	02/2010 -	11/2011	21(O)	0/0
241	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O)	0/0
242	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	208.68	185.89	03/2002 -	12/2011	117(O)	0/0
243	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	822.57	491.60	02/2009 -	12/2011	34(O)	0/0
244	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	169.00	- -	12/2011	-	0/0
245	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	197.61	- 09/2009	12/2011	27(R1)	0/0
246	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	242.54	03/2013 -	12/2011	-15(O)	0/0
247	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,183.04	- -	02/2012	-	0/0
248	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	422.22	- 12/2009	02/2012	26(R1)	0/0
249	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	66.18	12/2011 -	02/2012	2(O)	0/0
250	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 637.46	634.13	542.82	03/1995 -	03/2012	204(O)	0/0
251	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	510.51	- -	03/2012	-	0/0
252	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	480.37	- 12/2011	03/2012	3(R3)	0/0
253	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	205.49	- 03/2012	03/2012	0(R3)	0/0
254	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	425.42	- -	03/2012	-	0/0
255	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	561.57	- -	03/2012	-	0/0
256	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	340.51	- 03/2011	03/2012	12(R3)	0/0
257	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012	-	0/0
258	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012	-	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
259	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	-	03/2010 -	03/2012	24(O)	0/0
260	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	191.49	- -	03/2012	-	0/0
261	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	137.47	03/2012 -	03/2012	0(O)	0/0
262	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	218.15	03/2011 -	03/2012	12(O)	0/0
263	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	381.93	06/2005 07/2011	03/2012	8(R3)	0/0
264	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	167.73	36.32	03/2012 -	03/2012	0(O)	0/0
265	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	145.14	03/2007 03/2007	06/2012	63(R1)	0/0
266	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	326.92	- 07/2012	07/2012	0(R3)	0/0
267	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	579.88	- -	12/2012	-	0/0
268	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	789.49	12/2012 -	12/2012	0(O)	0/0
269	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	390.16	03/2005 12/2008	12/2012	48(R1)	0/0
270	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	338.99	- 03/2012	12/2012	9(R3)	0/0
271	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	240.86	- -	12/2012	-	0/0
272	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	536.25	03/2009 -	12/2012	45(O)	0/0
273	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	998.45	10/2007 -	12/2012	62(O)	0/0
274	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33(O)	0/0
275	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	105.66	12/2012 -	12/2012	0(O)	0/0
276	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	150.36	- -	03/2013	-	0/0
277	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	691.73	- -	03/2013	-	0/0
278	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	45.88	03/2012 -	03/2013	12(O)	0/0
279	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.14	0.49	03/2013 -	03/2013	0(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
280	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,Tamil Nadu	04/2006	495.74 495.74	495.74	132.26	- 06/2013	06/2013	0(R3)	0/0
281	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	64.10	12/2011 -	11/2013	23(O)	0/0
282	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	176.03	- -	12/2013	-	0/0
283	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	83.52	12/2012 -	12/2013	12(O)	0/0
284	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,785.91	03/2009 -	12/2013	57(O)	0/0
285	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	820.57	12/2008 -	03/2014	63(O)	0/0
286	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	724.96	- -	03/2014	-	0/0
287	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.75	211.09	03/2014 -	03/2014	0(O)	0/0
288	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.49	3.61	04/2014 -	03/2014	-1(O)	0/0
289	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	7.30	03/2014 -	03/2014	0(O)	0/0
290	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	75.92	03/2014 -	03/2014	0(O)	0/0
291	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	192.09	03/2014 -	03/2014	0(O)	0/0
292	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	107.60	03/2010 06/2014	06/2014	0(R3)	0/0
293	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,226.12	04/2008 03/2014	12/2014	9(R3)	0/0
294	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	166.80	- -	03/2015	-	0/0
295	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTT,Maharashtra	04/2008	5,300.00 -	5,300.00	278.51	03/2014 -	03/2015	12(O)	0/0
296	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
297	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
298	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.63	12/2015 -	12/2015	0(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
299	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	467.89	03/2011 03/2014	03/2016	24(R3)	0/0
300	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	-	03/2014 -	03/2016	24(O)	0/0
301	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	-	03/2016 -	03/2016	0(O)	0/0
302	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	-	03/2016 -	03/2016	0(O)	0/0
303	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	0.02	03/2016 -	06/2016	3(O)	0/0
304	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	20,000.00	7,430.73	03/2001 -	12/2017	201(O)	0/0
305	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 -	356.87	149.63	- 03/2010	-	-	0/0
306	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.54	- -	-	-	0/0
307	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	87.09	12/2012 -	-	-	0/0
308	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	594.05	- -	-	-	0/0
309	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	97.90	- -	-	-	0/0
310	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	475.05	- -	-	-	0/0
311	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	553.42	03/1998 -	-	-	0/0
312	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	945.73	611.54	- -	-	-	0/0
313	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	63.92	- -	-	-	0/0
314	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	91.53	- -	-	-	0/0
315	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
316	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,083.81	07/2005 -	-	-	0/0
317	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	71.95	- -	-	-	0/0
318	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	554.55	255.68	- 05/2009	-	-	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
319	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23	162.87	87.25	-	-	-	0/0
320	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00	847.76	815.43	06/2007	-	-	0/0
321	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34	296.20	-	04/2003	-	-	0/0
322	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	548.96	473.44	-	-	-	0/0
323	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00	695.00	9.44	-	-	-	0/0
324	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00	607.09	338.40	-	-	-	0/0
325	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
326	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91	418.17	73.55	-	-	-	0/0
327	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13	1,225.00	210.51	-	-	-	0/0
328	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61	227.52	258.74	03/2008	-	-	0/0
329	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	173.49	176.56	03/1998	-	-	0/0
330	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	25.02	02/2015	-	-	0/0
331	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56	791.60	0.76	-	-	-	0/0
332	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92	261.70	21.60	02/2006	-	-	0/0
333	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	308.13	03/2008	-	-	0/0
334	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	190.84	-	-	-	0/0
335	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	418.72	-	-	-	0/0
336	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	21.98	-	-	-	0/0
337	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	87.07	-	-	-	0/0
338	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	529.88	36.59	-	-	-	0/0
339	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97	196.97	176.51	03/2011	-	-	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
340	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
341	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	170.78	03/2011 -	-	-	0/0
342	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	457.16	06/1999 03/2011	-	-	0/0
343	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	166.90	03/2004 -	-	-	0/0
344	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	327.81	- 03/2011	-	-	0/0
345	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	267.63	06/2004 04/2005	-	-	0/0
346	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
347	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
348	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	720.44	- 12/2010	-	-	0/0
349	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	428.04	- -	-	-	0/0
350	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	440.68	- -	-	-	0/1
351	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,076.13	12/2006 08/2010	-	-	0/0
352	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	234.86	- 02/2011	-	-	0/0
353	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	471.11	02/2010 02/2011	-	-	0/0
354	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	369.25	- -	-	-	0/0
355	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	235.66	- 03/2011	-	-	0/0
356	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	131.63	- -	-	-	0/0
357	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	134.27	- -	-	-	0/0
358	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	82.93	- -	12/2011	-	0/0
359	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	356.57	- 03/2011	-	-	0/0
360	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.80	- -	-	-	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
361	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15	245.15	162.33	12/2010 03/2011	-	-	0/0
362	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68	225.68	130.08	- 12/2010	-	-	0/0
363	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24	468.62	2.08	03/2012	-	-	0/0
	Total		65,054.74	131,386.73	53,234.96				0/2
	Road Transport & Highways								
364	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	10/2011	33(O)	0/0
365	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	910.00	11/2010	10/2011	11(O)	0/0
366	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	257.60	06/2008	10/2011	40(O)	0/0
367	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	566.40	06/2008	10/2011	40(O)	0/0
368	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	603.60	03/2009	10/2011	31(O)	0/0
369	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.30	12/2008	10/2011	34(O)	0/0
370	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	658.20	07/2010	10/2011	15(O)	0/0
371	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	359.20	07/2010	10/2011	15(O)	0/0
372	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	10/2011	9(O)	0/0
373	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	200.40	10/2011	10/2011	0(O)	0/0
374	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	277.10	10/2008	11/2011	37(O)	0/0
375	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	254.50	10/2008	11/2011	37(O)	0/0
376	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	295.30	09/2009	11/2011	26(O)	0/0
377	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	154.34	08/2004 07/2010	12/2011	17(R3)	0/0
378	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	163.13	08/2004	12/2011	88(O)	0/0
379	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	79.38	04/2004	12/2011	92(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
380	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
381	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	475.60	03/2005	12/2011	81(O)	0/0
382	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	298.70	09/2007	12/2011	51(O)	0/0
383	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	246.30	09/2007	12/2011	51(O)	0/0
384	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	436.70	11/2007	12/2011	49(O)	0/0
385	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	205.00	06/2005	12/2011	78(O)	0/0
386	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	181.80	03/2008	12/2011	45(O)	0/0
387	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	152.30	03/2008	12/2011	45(O)	0/0
388	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	399.40	10/2008	12/2011	38(O)	0/0
389	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	226.60	02/2009	12/2011	34(O)	0/0
390	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	80.65	04/2009	12/2011	32(O)	0/0
391	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	173.30	06/2008	12/2011	42(O)	0/0
392	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	393.20	12/2008	12/2011	36(O)	0/0
393	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	363.20	12/2008	12/2011	36(O)	0/0
394	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	202.40	06/2008	12/2011	42(O)	0/0
395	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	289.20	09/2008	12/2011	39(O)	0/0
396	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	187.10	11/2008	12/2011	37(O)	0/0
397	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	172.20	10/2008	12/2011	38(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
398	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	251.03	276.40	10/2008	12/2011	38(O)	0/0
399	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHAI) - [240106305]NHAI, Madhya Pradesh	12/2003	229.91	229.91	223.10	10/2008	12/2011	38(O)	0/0
400	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	436.30	09/2008	12/2011	39(O)	0/0
401	NALBARI TO BIJINI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	256.40	06/2008	12/2011	42(O)	0/0
402	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	12/2011	30(O)	0/0
403	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	233.60	06/2008	12/2011	42(O)	0/0
404	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	253.50	06/2008	12/2011	42(O)	0/0
405	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	476.20	03/2008	12/2011	45(O)	0/0
406	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	169.30	06/2008	12/2011	42(O)	0/0
407	NALBARI T BIJINI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	207.90	04/2008	12/2011	44(O)	0/0
408	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	123.30	05/2008	12/2011	43(O)	0/0
409	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	193.30	06/2008	12/2011	42(O)	0/0
410	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	580.70	06/2009	12/2011	30(O)	0/0
411	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	702.80	10/2009	12/2011	26(O)	0/0
412	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	326.40	03/2010	12/2011	21(O)	0/0
413	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11(O)	0/0
414	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	916.90	07/2010	12/2011	17(O)	0/0
415	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	341.80	05/2010	12/2011	19(O)	0/0
416	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	165.14	02/2004	12/2011	94(O)	0/0
417	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	624.30	08/2010	12/2011	16(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
418	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	551.50	05/2010	12/2011	19(O)	0/0
419	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,588.00	08/2011	12/2011	4(O)	0/0
420	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	245.20	11/2008	01/2012	38(O)	0/0
421	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	294.70	09/2009	02/2012	29(O)	0/0
422	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	389.40	02/2012	02/2012	0(O)	0/0
423	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	178.40	09/2007	03/2012	54(O)	0/0
424	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	269.40	10/2008	03/2012	41(O)	0/0
425	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	355.60	03/2008	03/2012	48(O)	0/0
426	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	207.90	10/2008	03/2012	41(O)	0/0
427	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	118.90	04/2008	03/2012	47(O)	0/0
428	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	178.80	04/2008	03/2012	47(O)	0/0
429	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	150.80	04/2010	03/2012	23(O)	0/0
430	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	05/2012	22(O)	0/0
431	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
432	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.00	05/2012	05/2012	0(O)	0/0
433	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	804.30	05/2012	05/2012	0(O)	0/0
434	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	355.60	05/2012	05/2012	0(O)	0/0
435	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	89.65	09/2008	06/2012	45(O)	0/0
436	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	167.60	10/2008	06/2012	44(O)	0/0
437	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.10	10/2009	06/2012	32(O)	0/0
438	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.60	12/2009	06/2012	30(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
439	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	162.90	09/2010	06/2012	21(O)	0/0
440	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	396.70	06/2012	06/2012	0(O)	0/0
441	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	1,527.00	10/2011	06/2012	8(O)	0/0
442	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	2,647.00	11/2011	06/2012	7(O)	0/0
443	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	323.60	07/2012	07/2012	0(O)	0/0
444	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	126.80	05/2008	08/2012	51(O)	0/0
445	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	572.30	510.50	10/2011	08/2012	10(O)	0/0
446	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	813.90	09/2012	09/2012	0(O)	0/0
447	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	407.60	184.40	06/2010	10/2012	28(O)	0/0
448	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	233.30	09/2009	10/2012	37(O)	0/0
449	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
450	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	1,060.00	10/2012	10/2012	0(O)	0/0
451	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
452	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
453	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	176.70	07/2008	12/2012	53(O)	0/0
454	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	252.69	02/2004	12/2012	106(O)	0/0
455	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	389.40	12/2012	12/2012	0(O)	0/0
456	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	666.00	01/2013	01/2013	0(O)	0/0
457	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	113.40	02/2013	02/2013	0(O)	0/0
458	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	1,086.00	09/2010	03/2013	30(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
459	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	-	03/2013 -	03/2013	0(O)	0/0
460	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	326.70	03/2013 -	03/2013	0(O)	0/0
461	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	173.20	03/2013 -	03/2013	0(O)	0/0
462	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	107.60	03/2013 -	03/2013	0(O)	0/0
463	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	04/2013	0(O)	0/0
464	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	198.70	05/2013 -	05/2013	0(O)	0/0
465	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	131.20	05/2013 -	05/2013	0(O)	0/0
466	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	138.70	05/2013 -	05/2013	0(O)	0/0
467	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	2.64	05/2013 -	05/2013	0(O)	0/0
468	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	348.16	117.69	09/2007 -	06/2013	69(O)	0/0
469	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	846.50	11/2012 -	06/2013	7(O)	0/0
470	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	-	06/2013 -	06/2013	0(O)	0/0
471	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	-	06/2013 -	06/2013	0(O)	0/0
472	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	568.40	06/2013 -	06/2013	0(O)	0/0
473	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	72.15	06/2013 -	06/2013	0(O)	0/0
474	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	30.98	04/2009 -	07/2013	51(O)	0/0
475	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	39.26	11/2008 -	07/2013	56(O)	0/0
476	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.00	02/2010 -	07/2013	41(O)	0/0
477	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00 -	593.00	67.24	07/2013 -	07/2013	0(O)	0/0
478	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J & K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	07/2013	0(O)	0/0
479	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	-	08/2013 -	08/2013	0(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
480	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	322.80	08/2013	08/2013	0(O)	0/0
481	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	182.50	08/2013	08/2013	0(O)	0/0
482	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	4.34	09/2013	09/2013	0(O)	0/0
483	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	0.99	09/2013	09/2013	0(O)	0/0
484	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
485	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0
486	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	-	11/2013	11/2013	0(O)	0/0
487	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
488	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	40.29	09/2007	12/2013	75(O)	0/0
489	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	27.94	07/2009	12/2013	53(O)	0/0
490	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
491	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
492	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
493	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	432.00	10/2014	10/2014	0(O)	0/0
494	NASHRI CHANANI - [N24000162]NHAI,J & K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
495	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J & K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
	Total		72,461.45	74,266.70	45,748.78				0/0
Shipping & Ports									
496	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	298.17	294.09	04/2009	02/2011	22(O)	0/0
497	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
498	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
499	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	241.50	48.10	09/2011 -	09/2011	0(O)	0/0
500	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	121.41	12/2005 01/2008	10/2011	45(R3)	0/0
501	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
502	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
503	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	360.80	03/2012 -	03/2012	0(O)	0/0
504	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
505	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
506	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	55.40	12/2011 05/2012	05/2012	0(R3)	0/0
507	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	590.00	12/2010 -	09/2012	21(O)	0/0
508	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
509	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
510	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	83.51	12/2012 -	12/2012	0(O)	0/0
511	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
512	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O)	0/0
513	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
514	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
515	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
516	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O)	0/0
517	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
518	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
519	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	-	-	0/0
520	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
521	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.48	10/2008 -	-	-	0/0
	Total		18,451.36 -	19,434.85	3,941.88				0/0
Telecommunications									
522	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	274.84	09/2009 -	02/2010	5(O)	0/0
523	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
524	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	192.48	119.45	03/2009 -	02/2011	23(O)	0/0
525	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	209.79	12/2008 -	02/2011	26(O)	0/0
526	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	377.54	308.13	03/2009 -	02/2011	23(O)	0/0
527	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	02/2011	20(O)	0/0
528	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	02/2011	25(O)	0/0
529	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	366.00	227.30	10/2008 -	02/2011	28(O)	0/0
530	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20 -	1,100.00	815.00	- 03/2011	02/2011	-1(R3)	0/1

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
531	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	02/2011	13(O)	0/0
532	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	712.86	01/2010	02/2011	13(O)	0/0
533	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	141.64	01/2010	02/2011	13(O)	0/0
534	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	496.20	12/2008	03/2011	27(O)	0/0
535	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
536	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	123.76	09/2009	03/2011	18(O)	0/0
537	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
538	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	403.71	02/2009	03/2011	25(O)	0/0
539	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	362.62	08/2009	03/2011	19(O)	0/0
540	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	280.72	11/2010	03/2011	4(O)	0/0
541	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	461.56	10/2009	03/2011	17(O)	0/0
542	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007	08/2011	54(O)	0/0
543	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
544	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
545	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	80.47	12/2005	12/2011	72(O)	0/0
546	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	20.90	10/2010	03/2012	17(O)	0/0
547	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
548	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
549	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
550	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	-	-	0/0
551	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
552	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	-	-	0/0
553	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	-	-	0/0
554	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	-	-	0/0
555	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	-	-	0/0
556	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
557	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	-	-	0/0
558	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	-	02/2010	-	-	0/0
559	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	-	-	0/0
560	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	-	06/2009	-	-	0/0
561	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13	328.12	164.58	03/2009	-	-	0/0
Total			19,713.13	20,297.68	6,146.04				0/1
Urban Development									
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013	15(O)	6/6
563	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	-	09/2014	09/2014	0(O)	0/0
564	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	24.38	03/2016	03/2016	0(O)	0/0
565	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
Total			44,245.18	49,518.08	2,291.95				6/6

Sector Wise Details

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Water Resources</u>									
566	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			667,074.68	787,393.95	327,255.18				969/2300

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

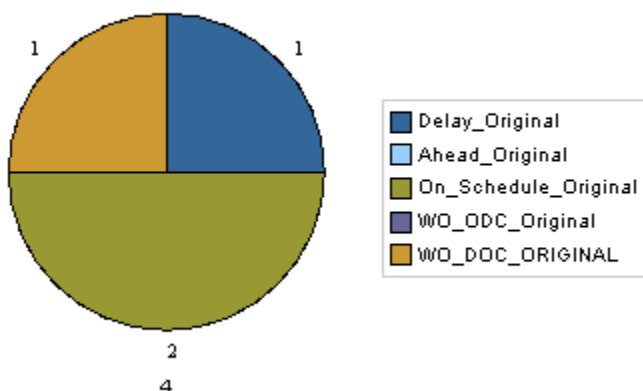

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till September, 2011 is Rs. 2291.95 crore, which is 4.6% of the revised cost of the projects.

Figures are in Rs. Crore

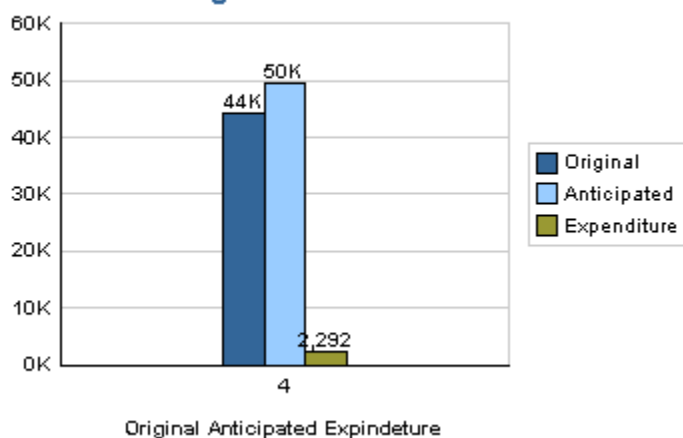

Sector wise current status of projects on theFlash Report

Telecommunications


I. Current Status:

Number of Projects	40
Number of Projects On Schedule	1
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning 37

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 40 projects, 1 project are on schedule and 2 projects are delayed .37 projects do not have fixed dates of commissioning.

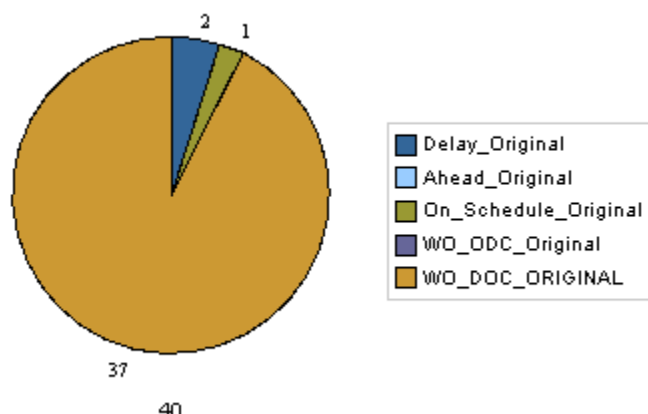

III. Investment Scenario

The Total Original cost of implementation of 40 projects when sanctioned, was of the order of Rs. 19713.13 crore but this was subsequently revised to Rs. 20297.68 crore implying a cost overrun of 3%. The expenditure incurred on these projects till September, 2011 is Rs. 6146.04 crore, which is 30.3% of the revised cost of the projects.

Figures are in Rs. Crore

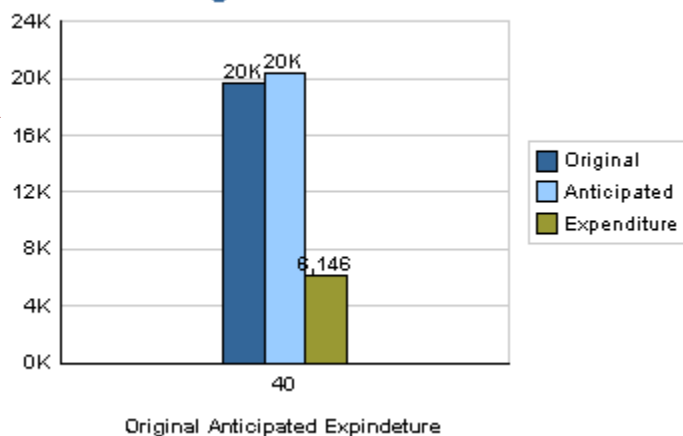

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	26
Number of Projects On Schedule	7
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning	7
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 26 projects, 7 projects are on schedule and 12 projects are delayed .7 projects do not have fixed dates of commissioning.

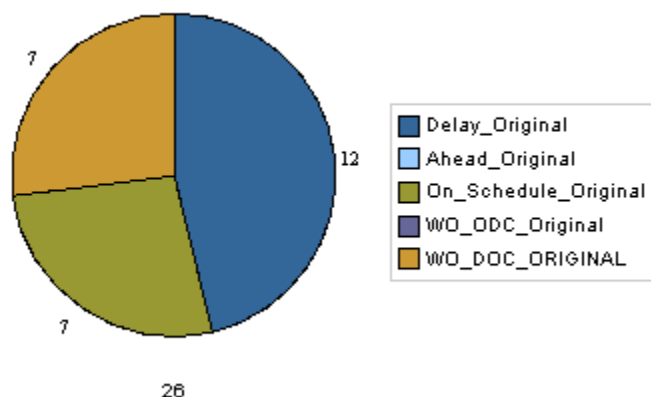

III. Investment Scenario

The Total Original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 18451.36 crore but this was subsequently revised to Rs. 19434.85 crore implying a cost overrun of 5.3%. The expenditure incurred on these projects till September, 2011 is Rs. 3941.88 crore, which is 20.3% of the revised cost of the projects.

Figures are in Rs. Crore

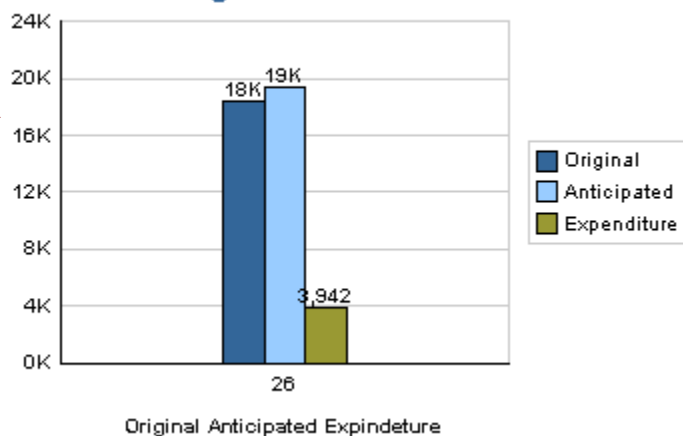

Sector wise current status of projects on theFlash Report


Road Transport & Highways

I. Current Status:

Number of Projects	132
Number of Projects On Schedule	42
Number of Projects Delayed	90

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 132 projects, 42 projects are on schedule and 90 projects are delayed .

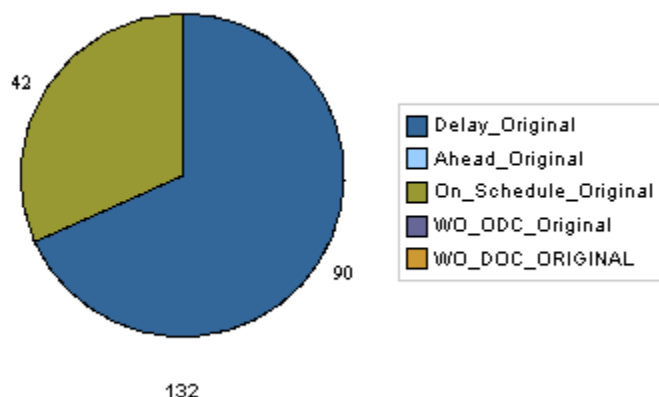

III. Investment Scenario

The Total Original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 72461.45 crore but this was subsequently revised to Rs. 74266.7 crore implying a cost overrun of 2.5%. The expenditure incurred on these projects till September, 2011 is Rs. 45748.78 crore, which is 61.6% of the revised cost of the projects.

Figures are in Rs. Crore

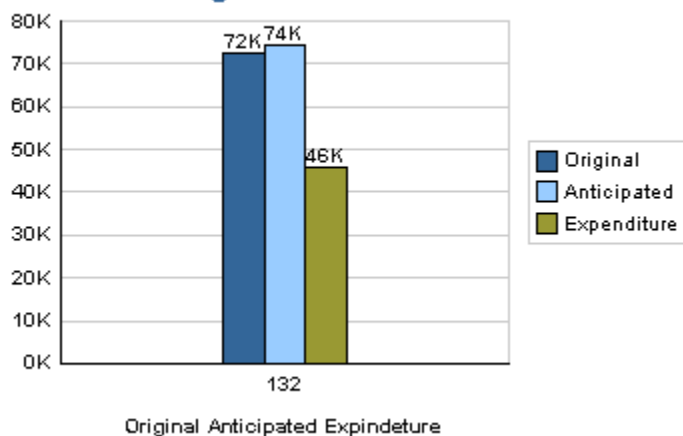

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	132
Number of Projects On Schedule	14
Number of Projects Delayed	26
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	25
Number of Projects Without Date Of Commissioning	65

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 132 projects, 2 projects are ahead of schedule, 14 projects are on schedule and 26 projects are delayed. 65 projects do not have fixed dates of commissioning. 25 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

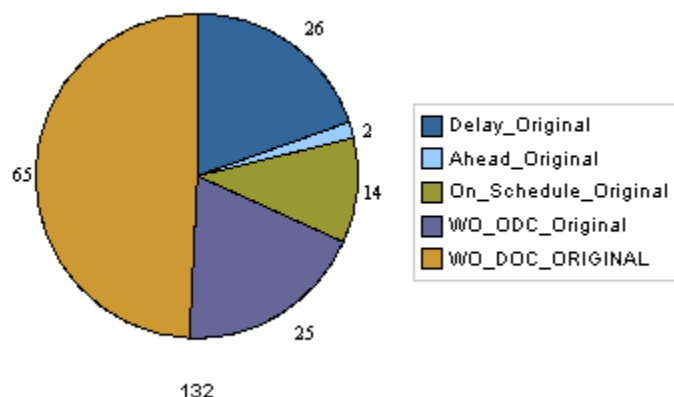

III. Investment Scenario

The Total Original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 65054.74 crore but this was subsequently revised to Rs. 131386.73 crore implying a cost overrun of 102%. The expenditure incurred on these projects till September, 2011 is Rs. 53234.96 crore, which is 40.5% of the revised cost of the projects.

Figures are in Rs. Crore

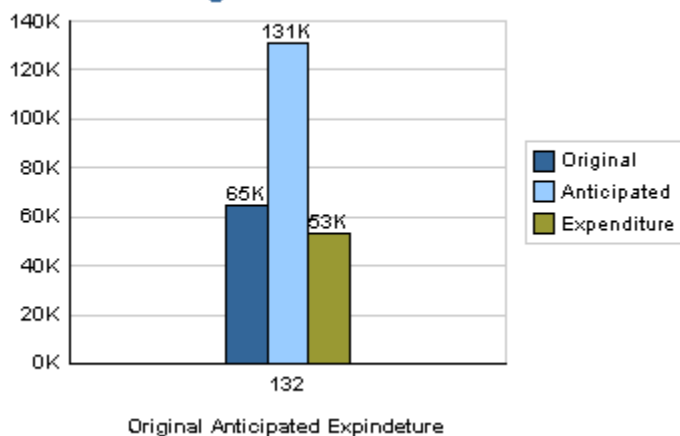

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	83
Number of Projects On Schedule	33
Number of Projects Delayed	45

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	3


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 83 projects, 33 projects are on schedule and 45 projects are delayed .3 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

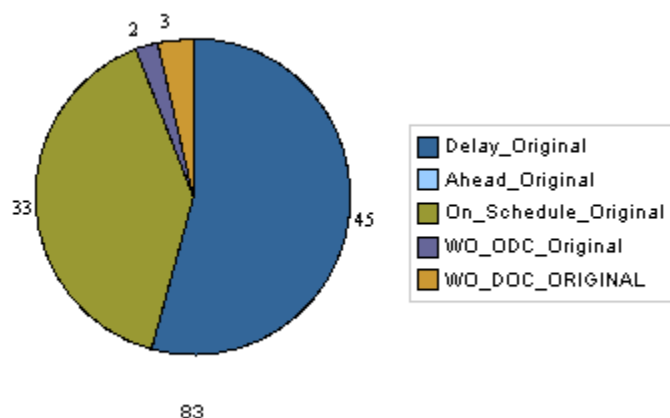

III. Investment Scenario

The Total Original cost of implementation of 83 projects when sanctioned, was of the order of Rs. 180012.22 crore but this was subsequently revised to Rs. 186096.29 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till September, 2011 is Rs. 90326.72 crore, which is 48.5% of the revised cost of the projects.

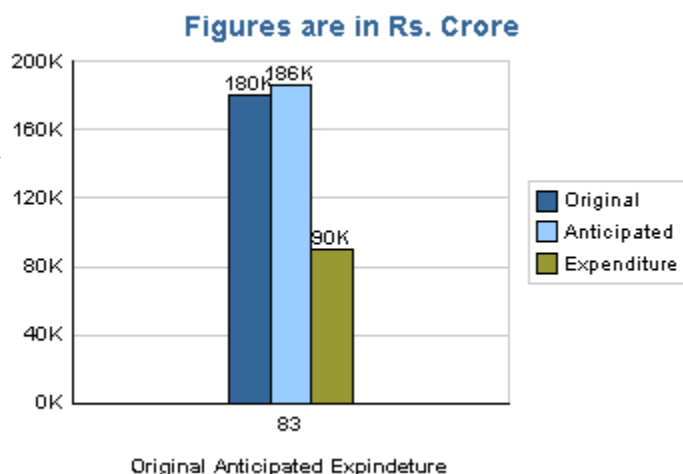

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	71
Number of Projects On Schedule	29
Number of Projects Delayed	30
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	7

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 71 projects, 3 projects are ahead of schedule, 29 projects are on schedule and 30 projects are delayed .7 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

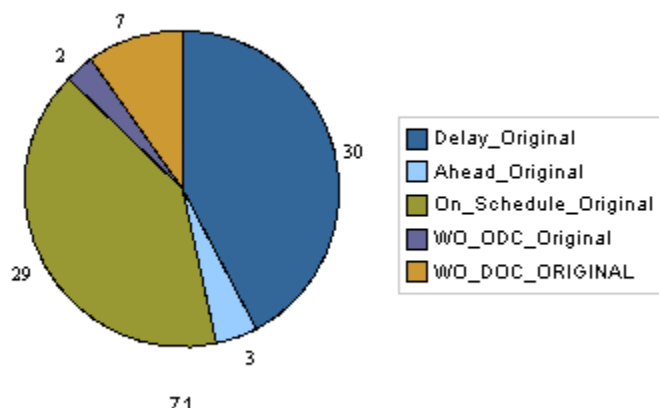

III. Investment Scenario

The Total Original cost of implementation of 71 projects when sanctioned, was of the order of Rs. 156539.45 crore but this was subsequently revised to Rs. 163927.12 crore implying a cost overrun of 4.7%. The expenditure incurred on these projects till September, 2011 is Rs. 57373.16 crore, which is 35% of the revised cost of the projects.

Figures are in Rs. Crore

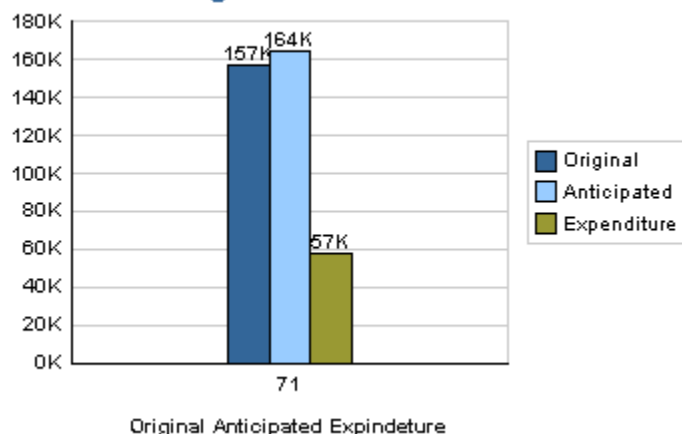

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	12
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Original Date of Commissioning	9
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 12 projects, 2 projects are on schedule and 1 project are delayed .9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

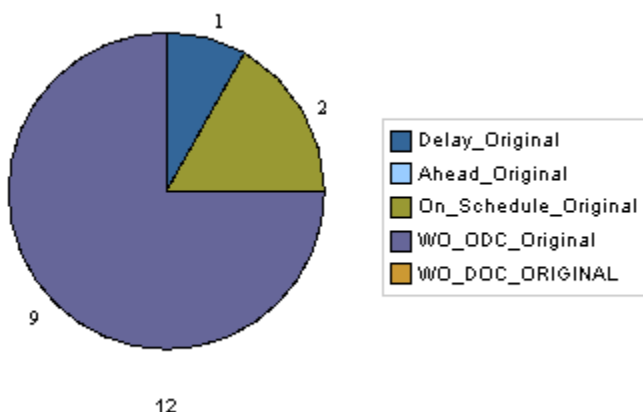

III. Investment Scenario

The Total Original cost of implementation of 12 projects when sanctioned, was of the order of Rs. 34591.72 crore but this was subsequently revised to Rs. 55969.91 crore implying a cost overrun of 61.8%. The expenditure incurred on these projects till September, 2011 is Rs. 26543.06 crore, which is 47.4% of the revised cost of the projects.

Figures are in Rs. Crore

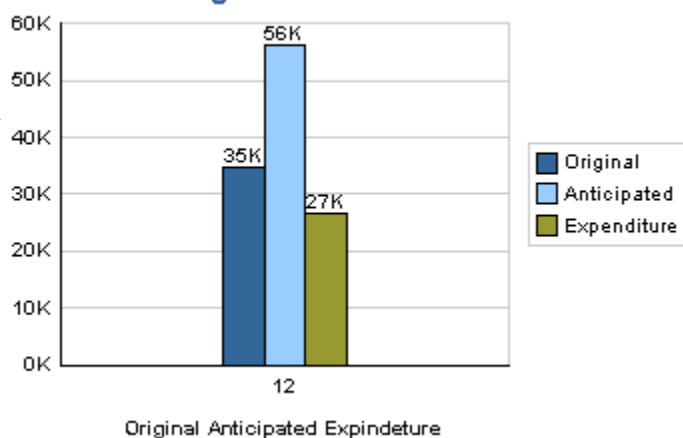

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Original Date of Commissioning	1
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

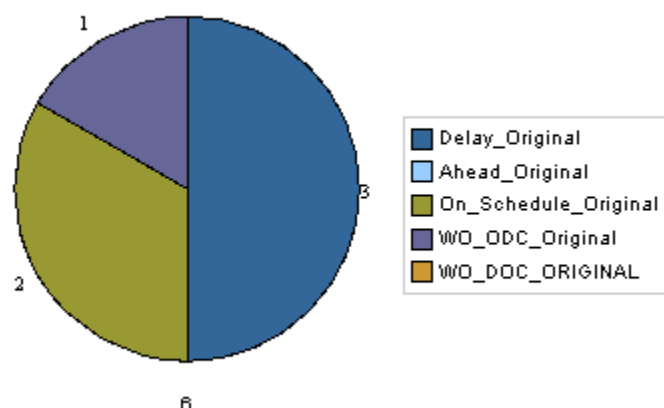

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till September, 2011 is Rs. 944.64 crore, which is 17.8% of the revised cost of the projects.

Figures are in Rs. Crore

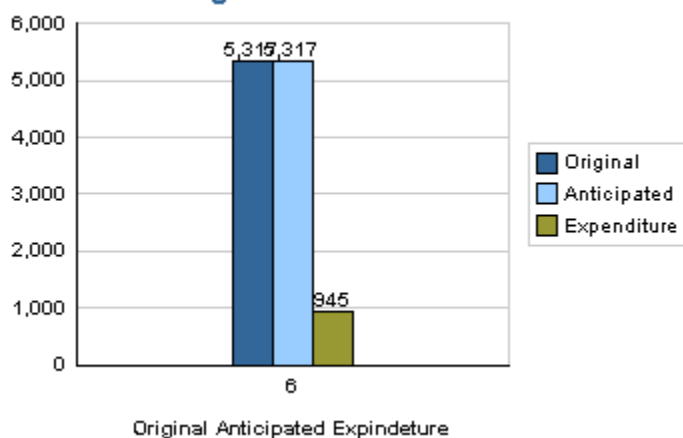

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	48
Number of Projects On Schedule	16
Number of Projects Delayed	17

Number of Projects Without Original Date of Commissioning	12
Number of Projects Without Date Of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 48 projects, 16 projects are on schedule and 17 projects are delayed .3 projects do not have fixed dates of commissioning.12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

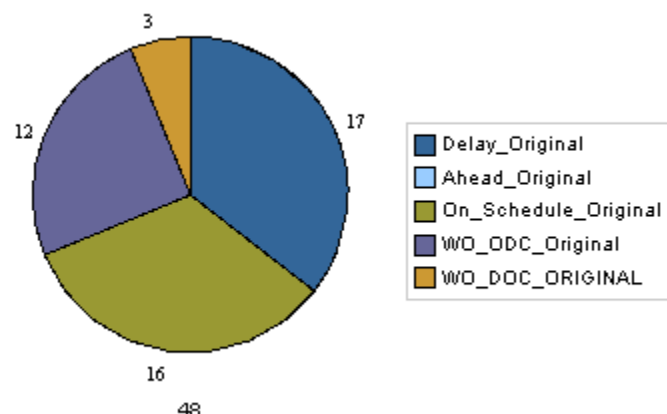

III. Investment Scenario

The Total Original cost of implementation of 48 projects when sanctioned, was of the order of Rs. 27241.47 crore but this was subsequently revised to Rs. 30628.5 crore implying a cost overrun of 12.4%. The expenditure incurred on these projects till September, 2011 is Rs. 11348.82 crore, which is 37.1% of the revised cost of the projects.

Figures are in Rs. Crore

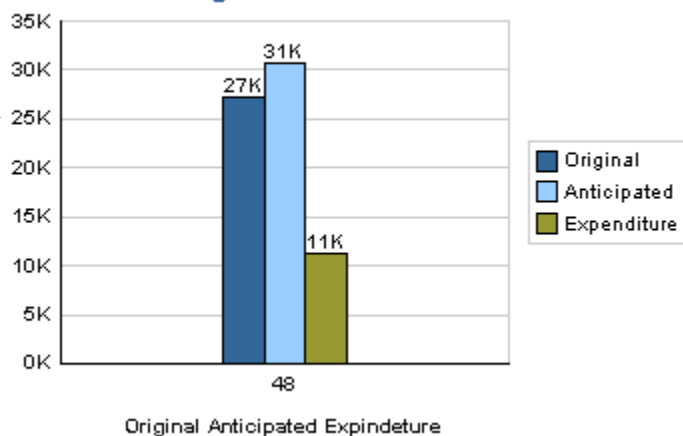

Sector wise current status of projects on theFlash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 3 projects are delayed .

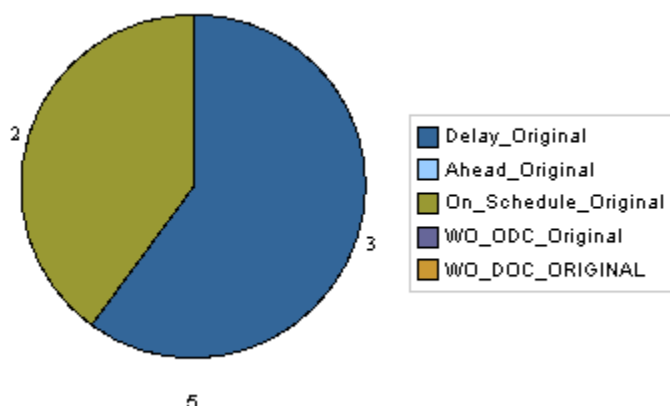

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4123.24 crore but this was subsequently revised to Rs. 5435.02 crore implying a cost overrun of 31.8%. The expenditure incurred on these projects till September, 2011 is Rs. 2859.22 crore, which is 52.6% of the revised cost of the projects.

Figures are in Rs. Crore

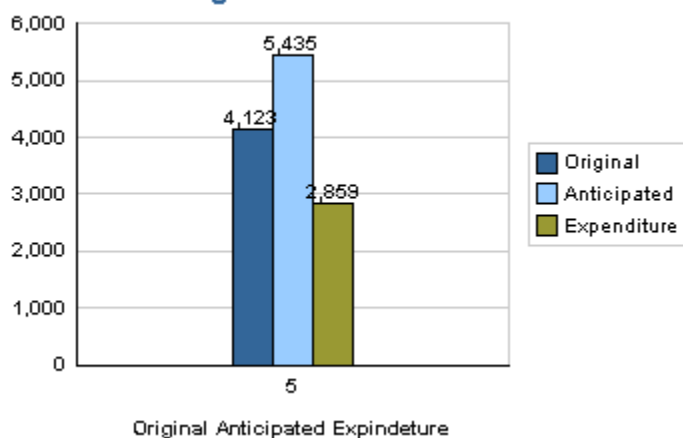

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

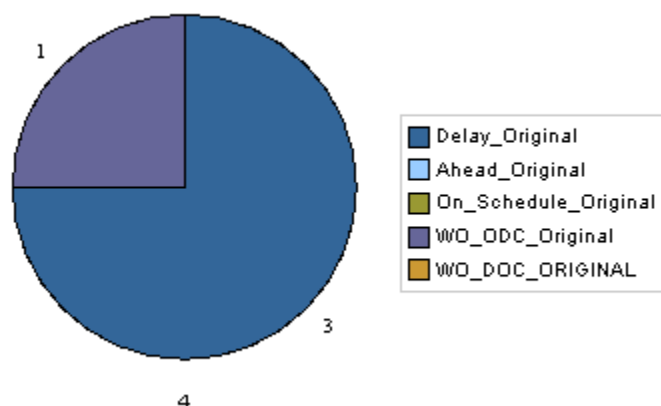

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 29228.29 crore but this was subsequently revised to Rs. 34066.29 crore implying a cost overrun of 16.6%. The expenditure incurred on these projects till September, 2011 is Rs. 19296.2 crore, which is 56.6% of the revised cost of the projects.

Figures are in Rs. Crore

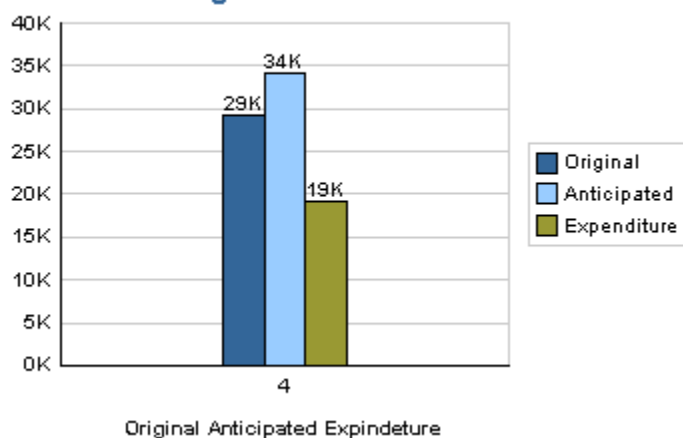

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	32	31217.87	37252.03	20640.32
2	Arunachal Pr.	4	9512.22	9610.51	7124.32
3	Assam	37	23895.78	32112.90	18499.82
4	Bihar	28	28191.41	32884.36	21040.24
5	Chhatisgarh	19	22504.78	37937.78	15667.62
6	Delhi	3	37985.00	37965.41	90.58
7	Goa	1	204.73	204.73	48.41
8	Gujarat	24	29952.71	30559.86	5115.27
9	Haryana	11	5987.83	7704.75	4938.16
10	Himachal Pr.	6	14761.16	14843.44	12170.43
11	J & K	11	14253.13	33145.32	11823.25
12	Jharkhandd	18	8758.17	13349.17	5907.56
13	Karnataka	27	31565.39	39116.07	15492.68
14	Kerala	9	7247.37	7861.37	2816.00
15	Madhya pradesh	23	16926.11	17158.42	5762.52
16	Maharashtra	52	72470.80	86887.47	36939.56
17	Manipur	1	727.56	3056.85	467.89
18	Mizoram	2	988.06	3307.12	269.03
19	Multi State	103	127210.06	129885.55	42174.27
20	Nagaland	1	850.00	850.00	8.44
21	Orissa	27	46642.14	49917.07	17224.60
22	Punjab	8	4854.69	5840.65	2838.73
23	Rajasthan	15	13638.67	13902.53	7435.02
24	Sikkim	2	1648.88	3644.86	206.01
25	Tamil Nadu	35	44994.48	54555.64	35693.13
26	Tripura	3	1522.39	2053.23	386.50
27	Uttar Pradesh	30	18540.31	20675.41	9862.22
28	Uttaranchal	7	11682.65	14927.07	4881.06
29	West Bengal	27	38340.33	46184.38	21731.54
TOTAL		566	667074.68	787393.95	327255.18

List of Projects in which Expenditure is more than cost

SN	PROJ TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	13171.00	0.00	14054.00
2	BARSINGSAR TPS (2X125MW) (NLC)	Coal	1114.18	1626.09	1654.84
3	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	613.54	0.00	671.52
4	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	Petroleum	2305.30	700.00	2416.96
5	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	Power	621.28	0.00	693.43
6	CHAMERA,STAGE-III (NHPC)	Power	1405.63	0.00	1668.16
7	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	768.92	0.00	1373.35
8	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	611.02	0.00	670.42
9	KOTESHWAR HEP (THDC)	Power	1301.56	0.00	2492.85
10	JIND-SONEPAT (NL),NR	Railways	190.81	238.56	338.99
11	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	248.44	576.27	789.49
12	REWARI-ROHTAK (NL),NR	Railways	149.38	330.23	471.11
13	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	409.00	625.30	815.43
14	AMRAVATI-NARKHER NL(CR)	Railways	120.90	284.27	457.16
15	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	100.00	142.90	185.89
16	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	114.01	283.95	340.51
17	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	Railways	78.23	0.00	87.25
18	MUZAFFARPUR-SITAMARHI(NL),ECR	Railways	100.00	322.29	425.42
19	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	233.00	335.77	561.57
20	PATNA GANGA BRIDGE (NL), ECR	Railways	624.47	0.00	998.45
21	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	184.00	254.07	480.37
22	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	907.69	1032.76	3076.13
23	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	108.00	214.09	250.82
24	GUNA-ETAWAH(NCR), NL	Railways	158.77	432.46	558.07
25	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	1676.31	0.00	2785.91
26	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	1000.00	1500.00	2226.12
27	KATIHAR - JOGBANI (GC)(NEFR)	Railways	100.00	492.98	720.44
28	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	733.00	0.00	820.57
29	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	156.00	0.00	191.49
30	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	170.00	170.00	356.57
31	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	323.40	0.00	440.68
32	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	395.00	1062.36	1183.04

SN	PROJ TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
33	ELECTRIFICATION OF MORADABAD-ROZA	Railways	129.17	0.00	218.15
34	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	240.00	0.00	261.00
35	RAJATGARH-BARANG(LD),ECOR	Railways	166.16	0.00	233.90
36	BILASPUR-URKURA (DL)	Railways	151.52	0.00	299.77
37	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	136.62	0.00	157.88
38	GADWAL - RAICHUR (NL), SCR	Railways	92.63	108.91	234.86
39	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	155.74	164.36	491.60
40	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	124.43	407.78	510.51
41	GONDIA-JABALPUR(GC),(SECR)	Railways	386.30	0.00	553.42
42	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	293.97	0.00	381.93
43	BANKURA - DAMODAR (GC) (SER)	Railways	111.90	0.00	390.16
44	RANCHI-LOHARDAGA(GC),SER	Railways	194.07	0.00	267.63
45	RUPSA-BANGRIPOSI (GC)(SER)	Railways	57.94	0.00	176.56
46	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	343.17	0.00	418.72
47	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	Railways	280.00	0.00	691.73
48	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	100.00	0.00	473.44
49	KARUR-SALEM(NL),SR	Railways	155.55	0.00	611.54
50	CALICUT-MANGALORE (DL) (SR)	Railways	240.00	0.00	594.05
51	KOTTUR-HARIHAR(NL),(SWR)	Railways	65.94	281.20	327.81
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	295.00	0.00	475.05
53	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	Railways	148.61	0.00	258.74
54	Hazaribagh-Ranchi	Road Transport & Highways	625.07	0.00	666.00
55	AMRITSAR-PATHANKOT	Road Transport & Highways	705.00	0.00	846.50
56	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	1108.00	0.00	2647.00
57	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	273.00	0.00	475.60
58	NEW MANGALORE PORT NH-17 AND 48	Road Transport & Highways	196.50	0.00	233.60
59	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	600.24	0.00	702.80
60	JHANSI TO LALITPUR, NH-26	Road Transport & Highways	276.09	0.00	295.30
61	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	Road Transport & Highways	629.00	0.00	910.00
62	SITAPUR-LUCKNOW	Road Transport & Highways	322.00	0.00	553.70
63	THRISSUR TO ANGAMALI (NH-47)	Road Transport & Highways	312.50	0.00	603.60
64	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	168.00	0.00	385.30

SN	PROJ_TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
65	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	280.00	0.00	580.70
66	TRICHY - DINDIGUAL NH-45	Road Transport & Highways	576.00	0.00	658.20
67	PONDICHERY - TINDIVANAU NH-66	Road Transport & Highways	285.00	0.00	359.20
68	TRICHY - KORUR NH-67	Road Transport & Highways	516.00	0.00	594.20
69	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	941.00	0.00	1901.00
70	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	441.00	0.00	916.90
71	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	295.00	0.00	624.30
72	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	486.00	0.00	551.50
73	RINGBUNDS TO JHAJHANPUR (BR-6)	Road Transport & Highways	340.00	0.00	566.40
74	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	340.00	0.00	436.30
75	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	200.00	0.00	256.40
76	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	245.00	0.00	476.20
77	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	221.82	0.00	245.20
78	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	557.00	0.00	930.90
79	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	229.00	0.00	341.80
80	Pune-sholapur, pkg1	Road Transport & Highways	1110.00	0.00	1802.00
81	Kishangarh-Ajmer-Beawer	Road Transport & Highways	795.00	0.00	804.30
82	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	367.49	0.00	453.68
83	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	275.00	0.00	298.70
84	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	220.00	0.00	246.30
85	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Road Transport & Highways	412.78	0.00	436.70
86	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	240.00	0.00	269.40
87	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	Road Transport & Highways	227.00	0.00	399.40
88	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	340.68	0.00	355.60

SN	PROJ_TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
89	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	190.00	0.00	227.00
90	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	225.00	0.00	257.60
91	KASIA TO GORAKHPUR (NH-28)(NHAI)	Road Transport & Highways	242.00	0.00	393.20
92	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	227.00	0.00	363.20
93	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	275.00	0.00	277.10
94	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	225.00	0.00	254.50
95	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	151.30	0.00	172.20
96	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	203.43	0.00	207.90
97	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	251.03	0.00	276.40
98	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	1693.75	0.00	2588.00
99	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	157.47	0.00	178.40
100	Bijapur-Hungund Section	Road Transport & Highways	748.00	0.00	1086.00
101	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	245.67	0.00	294.09
102	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	230.00	0.00	234.15
103	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	Telecommunication s	760.20	0.00	815.00
104	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	Telecommunication s	277.34	0.00	308.13

List of project Without Original Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/1
	Total		1,106.29	1,106.29	1,000.70				0/1
	<u>Coal</u>								
2	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	-	-	03/2012	-	4/4
3	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Orissa	08/2008	207.28	207.28	67.90	-	03/2012	-	5/7
4	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	2,079.84	-	02/2013	-	0/6
5	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	569.78	-	03/2013	-	0/8
6	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	-	-	03/2013	-	6/11
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	71.65	-	03/2013	-	5/7
8	CHURCHA RO UG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	257.30	-	03/2014	-	0/4
9	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	203.09	-	03/2014	-	0/5
10	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77	339.77	0.65	-	10/2014	-	1/1
11	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	-	-	03/2015	-	2/12
12	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	-	-	03/2016	-	1/12
13	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	94.23	-	03/2017	-	6/12
	Total		9,412.38	9,871.92	3,344.44				30/89
	<u>Fertilisers</u>								
14	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	178.07	- 11/2011	11/2011	0(R3)	4/22
	Total		488.75	488.75	178.07				4/22
	<u>Steel</u>								
15	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	111.28	232.93	168.27	-	10/2011	-	0/1

List of project Without Original Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	3,316.00 6,325.00	6,325.00	2,109.69	- 12/2011	12/2011	0(R3)	0/11
17	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	234.15	- 02/2011	01/2012	11(R3)	2/3
18	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	221.73	- 08/2010	01/2012	17(R3)	1/2
19	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	291.61	- 12/2011	03/2012	3(R3)	18/21
20	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	460.00	130.64	- 05/2012	05/2012	0(R3)	1/2
21	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	11,272.00	- 12/2011	06/2012	6(R3)	6/14
22	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	47.29	- 10/2012	10/2012	0(R3)	3/4
23	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	3,212.16	- 03/2013	03/2013	0(R3)	4/20
Total			24,429.17 -	42,208.36	17,687.54				35/78
<u>Petrochemicals</u>									
24	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 -	5,460.61	3,020.26	- -	04/2012	-	0/30
Total			5,460.61 -	5,460.61	3,020.26				0/30
<u>Petroleum</u>									
25	EURO-IV DHDH - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,674.51	- -	12/2011	-	0/116
26	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	3.38	- -	08/2013	-	0/0
Total			4,199.69 -	4,199.69	1,677.89				0/116
<u>Power</u>									
27	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,076.00	- -	03/2012	-	0/6
28	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	2,889.00	- -	10/2013	-	2/18
Total			12,444.43 -	12,379.87	6,965.00				2/24
<u>Railways</u>									
29	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	169.00	- -	12/2011	-	0/0
30	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	197.61	- 09/2009	12/2011	27(R1)	0/0

List of project Without Original Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
31	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,183.04	- -	02/2012	-	0/0
32	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	422.22	- 12/2009	02/2012	26(R1)	0/0
33	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	510.51	- -	03/2012	-	0/0
34	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	480.37	- 12/2011	03/2012	3(R3)	0/0
35	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	205.49	- 03/2012	03/2012	0(R3)	0/0
36	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	425.42	- -	03/2012	-	0/0
37	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	561.57	- -	03/2012	-	0/0
38	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	340.51	- 03/2011	03/2012	12(R3)	0/0
39	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012	-	0/0
40	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012	-	0/0
41	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	191.49	- -	03/2012	-	0/0
42	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	326.92	- 07/2012	07/2012	0(R3)	0/0
43	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	579.88	- -	12/2012	-	0/0
44	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	338.99	- 03/2012	12/2012	9(R3)	0/0
45	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	240.86	- -	12/2012	-	0/0
46	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	150.36	- -	03/2013	-	0/0
47	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	691.73	- -	03/2013	-	0/0
48	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	132.26	- 06/2013	06/2013	0(R3)	0/0
49	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	176.03	- -	12/2013	-	0/0
50	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	724.96	- -	03/2014	-	0/0

List of project Without Original Date of Commissioning

(Sep,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
51	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66	324.66	166.80	-	03/2015	-	0/0
52	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	338.40	- 12/2012	-	-	0/0
53	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	82.93	- -	12/2011	-	0/0
Total			7,089.51	18,346.77	9,766.25				0/0
Grand Total			64,630.83	94,062.26	43,640.15				71/360

List of project Without Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Coal</u>									
1	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015	-	-	0/0
2	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	40.04	03/2012	-	-	13/42
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013	-	-	0/83
Total			1,163.87	1,163.87	52.35				13/125
<u>Mines</u>									
4	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51	4,401.76	4,144.00	12/2008	06/2011	5(R3)	117/110
Total			4,091.51	4,401.76	4,144.00				117/110
<u>Petroleum</u>									
5	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70	755.76	527.43	03/2011	06/2011	1(R3)	0/0
6	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	727.88	671.52	12/2010	06/2011	6(O)	0/0
7	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	1,690.13	1,596.80	09/2009	08/2011	23(O)	0/0
8	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	299.00	251.19	02/2011	08/2011	0(R3)	0/0
9	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
10	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	756.00	744.26	09/2011	-	-	0/0
11	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	2,730.00	696.82	09/2011	-	-	0/0
Total			7,493.22	7,239.84	4,491.31				0/0
<u>Power</u>									
12	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	947.96	831.16	12/2007	-	-	14/18
13	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	113.23	06/2011	08/2011	2(O)	0/0
14	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	93.24	01/2011	-	-	0/1

List of project Without Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		1,031.41	1,382.92	1,037.63				14/19
			-						
	<u>Railways</u>								
15	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	233.90	- 02/2009	12/2010	22(R1)	0/0
16	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	188.11	- 03/2009	12/2010	21(R1)	0/0
17	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	221.90	157.88	12/2007 03/2010	12/2010	9(R1)	0/0
18	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	294.93	03/2009 12/2008	12/2010	24(R1)	0/0
19	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80	200.80	-	- -	12/2010	-	0/0
20	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	273.00	299.77	- 03/2009	03/2011	24(R1)	0/0
21	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00	329.70	261.00	03/2009 12/2009	03/2011	15(R1)	0/0
22	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,270.81	- 12/2010	06/2011	6(R3)	0/1
23	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	149.63	- 03/2010	-	-	0/0
24	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.54	- -	-	-	0/0
25	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00	968.60	87.09	12/2012 -	-	-	0/0
26	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	594.05	- -	-	-	0/0
27	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	97.90	- -	-	-	0/0
28	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00	412.91	475.05	- -	-	-	0/0
29	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30	1,038.00	553.42	03/1998 -	-	-	0/0
30	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55	945.73	611.54	- -	-	-	0/0
31	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00	997.58	63.92	- -	-	-	0/0
32	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	91.53	- -	-	-	0/0
33	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00	363.26	0.27	07/2008 -	-	-	0/0
34	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	1,099.20	1,083.81	07/2005 -	-	-	0/0

List of project Without Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
35	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	1,214.00	71.95	-	-	-	0/0
36	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	554.55	255.68	- 05/2009	-	-	0/0
37	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23	162.87	87.25	-	-	-	0/0
38	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	815.43	06/2007 -	-	-	0/0
39	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34	296.20	-	04/2003 03/2010	-	-	0/0
40	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	548.96	473.44	-	-	-	0/0
41	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00	695.00	9.44	-	-	-	0/0
42	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
43	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91	418.17	73.55	-	-	-	0/0
44	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	210.51	-	-	-	0/0
45	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61	227.52	258.74	03/2008 03/2009	-	-	0/0
46	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	173.49	176.56	03/1998 08/2005	-	-	0/0
47	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	25.02	02/2015	-	-	0/0
48	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	-	-	-	0/0
49	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92	261.70	21.60	02/2006	-	-	0/0
50	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	308.13	03/2008 06/2008	-	-	0/0
51	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	190.84	-	-	-	0/0
52	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	418.72	-	-	-	0/0
53	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	21.98	-	-	-	0/0
54	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	87.07	-	-	-	0/0
55	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	36.59	-	-	-	0/0
56	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97	196.97	176.51	03/2011	-	-	0/0

List of project Without Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
57	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	0.71	-	-	-	0/0
58	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	170.78	03/2011	-	-	0/0
59	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	457.16	06/1999 03/2011	-	-	0/0
60	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	166.90	03/2004	-	-	0/0
61	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	327.81	- 03/2011	-	-	0/0
62	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	267.63	06/2004 04/2005	-	-	0/0
63	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
64	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
65	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	720.44	- 12/2010	-	-	0/0
66	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	428.04	- -	-	-	0/0
67	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	440.68	- -	-	-	0/1
68	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,076.13	12/2006 08/2010	-	-	0/0
69	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	234.86	- 02/2011	-	-	0/0
70	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	471.11	02/2010 02/2011	-	-	0/0
71	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	369.25	- -	-	-	0/0
72	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	235.66	- 03/2011	-	-	0/0
73	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	131.63	- -	-	-	0/0
74	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	134.27	- -	-	-	0/0
75	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	356.57	- 03/2011	-	-	0/0
76	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.80	- -	-	-	0/0
77	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	162.33	12/2010 03/2011	-	-	0/0
78	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	130.08	- 12/2010	-	-	0/0

List of project Without Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
79	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24	468.62	2.08	03/2012	-	-	0/0
	Total		20,391.72	40,844.47	22,585.73				0/2
	Shipping & Ports								
80	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	298.17	294.09	04/2009	02/2011	22(O)	0/0
81	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
82	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.75	10/2008	-	-	0/0
83	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	253.36	-	12/2007 01/2009	-	-	0/0
84	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	399.13	-	08/2010	-	-	0/0
85	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010	-	-	0/0
86	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	821.48	10/2008	-	-	0/0
	Total		4,627.04	4,820.56	1,340.32				0/0
	Telecommunications								
87	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	274.84	09/2009	02/2010	5(O)	0/0
88	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
89	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	119.45	03/2009	02/2011	23(O)	0/0
90	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	209.79	12/2008	02/2011	26(O)	0/0
91	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	308.13	03/2009	02/2011	23(O)	0/0
92	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009	02/2011	20(O)	0/0
93	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	155.71	01/2009	02/2011	25(O)	0/0

List of project Without Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
94	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	366.00	227.30	10/2008	02/2011	28(O)	0/0
95	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,100.00	815.00	- 03/2011	02/2011	-1(R3)	0/1
96	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	02/2011	13(O)	0/0
97	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	712.86	01/2010	02/2011	13(O)	0/0
98	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	141.64	01/2010	02/2011	13(O)	0/0
99	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	496.20	12/2008	03/2011	27(O)	0/0
100	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
101	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	123.76	09/2009	03/2011	18(O)	0/0
102	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
103	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	403.71	02/2009	03/2011	25(O)	0/0
104	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	362.62	08/2009	03/2011	19(O)	0/0
105	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	280.72	11/2010	03/2011	4(O)	0/0
106	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75	719.90	461.56	10/2009	03/2011	17(O)	0/0
107	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007	08/2011	54(O)	0/0
108	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
109	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
110	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
111	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
112	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	-	-	0/0

List of project Without Date of Commissioning

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
113	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0
114	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	-	-	0/0
115	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	-	-	0/0
116	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	-	-	0/0
117	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	-	-	0/0
118	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
119	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	-	-	0/0
120	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53 -	625.53	-	02/2010 -	-	-	0/0
121	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75 -	624.75	-	09/2010 -	-	-	0/0
122	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	-	06/2009 -	-	-	0/0
123	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	-	-	0/0
Total			18,689.27 -	19,098.31	6,041.61				0/1
Urban Development									
124	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
Total			114.18 -	173.08	.00				0/0
Grand Total			57,602.22	79,124.81	39,692.95				144/257

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,240.50	09/2010	01/2012	16(O)	8/80
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,054.00	12/2008	08/2012	44(O)	61/119
3	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,001.00	12/2015 05/2016	11/2016	11(O)	0/70
Total			28,122.00	32,960.00	18,295.50				69/269
<u>Civil Aviation</u>									
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 2,015.00	2,015.00	940.61	01/2011	12/2011	11(O)	0/0
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,391.83	05/2011	03/2012	10(O)	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40	264.29	153.38	01/2011	12/2012	23(O)	0/0
Total			3,524.91	4,604.29	2,485.82				0/0
<u>Coal</u>									
7	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,654.84	06/2009	10/2011	28(O)	59/26
8	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96	302.96	-	03/2010	03/2012	24(O)	9/11
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	101.43	03/2011 03/2012	03/2012	12(O)	0/2
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,275.41	06/2009	05/2012	35(O)	60/24
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88	741.62	143.22	03/2010	03/2013	36(O)	0/2
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	197.88	03/2013 09/2012	12/2013	9(O)	2/22
13	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,267.89	03/2010	03/2014	48(O)	3/15
14	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	1,090.84	03/2010	03/2014	48(O)	2/13
15	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.49	03/2011	03/2014	36(O)	0/3
16	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	33.57	03/2011 03/2012	03/2014	36(O)	0/2

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	66.45	03/2012	03/2014	24(O)	0/2
18	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	76.05	03/2012	03/2014	24(O)	0/2
19	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	139.85	03/2012	03/2015	36(O)	0/2
20	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	1/5
21	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	68.86	12/2012	03/2015	27(O)	11/44
22	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	211.50	03/2014	03/2016	24(O)	1/2
23	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	16.21	07/2012	03/2016	44(O)	0/2
	Total		11,824.69	14,752.18	7,363.49				148/179
	Fertilisers								
24	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011	11/2011	4(O)	0/0
25	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011	03/2012	8(O)	0/0
26	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	223.57	12/2012	01/2013	1(O)	0/8
	Total		2,241.63	2,241.63	413.67				0/8
	Steel								
27	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	8,855.52	10/2009	10/2012	36(O)	48/59
	Total		8,692.00	12,291.00	8,855.52				48/59
	Petroleum								
28	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38	2,340.00	2,254.62	10/2010	09/2011	11(O)	0/0
29	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	304.40	245.01	06/2010	09/2011	15(O)	0/0
30	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30	3,005.30	2,416.96	06/2010	10/2011	16(O)	0/0
31	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	12/2008	11/2011	35(O)	0/0
32	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07	1,385.00	967.39	10/2010	12/2011	14(O)	0/1

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
33	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	810.00	635.71	04/2011 12/2011	12/2011	8(O)	0/2
34	HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70 -	706.70	644.81	04/2010 -	12/2011	20(O)	0/0
35	NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08 -	305.08	257.60	04/2011 -	12/2011	8(O)	0/0
36	MNW-NF BRIDGE PROJECT - [N16000045]ONGC, Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 02/2012	02/2012	35(O)	0/0
37	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	24(O)	0/0
38	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	18(O)	0/0
39	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	155.13	06/2011 03/2012	03/2012	9(O)	3/9
40	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	73(O)	0/0
41	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,596.54	05/2010 05/2012	05/2012	24(O)	0/0
42	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	38.35	05/2010 04/2012	05/2012	24(O)	0/0
43	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	92.09	07/2010 05/2012	05/2012	22(O)	0/0
44	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,380.59	08/2010 03/2012	06/2012	22(O)	0/0
45	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	70.85	04/2011 -	07/2012	15(O)	0/0
46	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	400.00	154.72	06/2011 07/2012	07/2012	13(O)	7/9
47	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,225.00	03/2012 08/2012	08/2012	5(O)	11/10
48	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.53	09/2011 -	12/2012	15(O)	0/0
49	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	80.28	12/2011 -	01/2013	13(O)	0/0
50	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2(O)	0/0
51	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	231.94	03/2006 03/2013	03/2013	84(O)	6/6

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
52	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,767.52	05/2010 03/2013	03/2013	34(O)	0/0
53	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	-	10/2012 -	03/2013	5(O)	0/0
54	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	160.16	12/2011 04/2013	04/2013	16(O)	0/203
55	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	9,720.18	11/2012 -	06/2013	7(O)	107/100
56	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	592.78	03/2007 03/2014	03/2014	84(O)	3/3
57	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,375.28	03/2007 03/2017	03/2017	120(O)	6/6
Total			74,710.56 -	84,032.74	38,677.44				143/349
<u>Power</u>									
58	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25 -	227.03	212.75	05/2011 05/2011	09/2011	4(O)	0/0
59	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	132.86	06/2010 -	11/2011	17(O)	0/0
60	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,668.16	08/2010 -	12/2011	16(O)	0/0
61	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	639.52	467.55	01/2010 -	12/2011	23(O)	0/22
62	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	4,978.56	2,949.84	07/2010 -	12/2011	17(O)	3/20
63	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.37	295.81	07/2011 -	12/2011	5(O)	0/0
64	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79 -	1,724.79	1,542.17	11/2009 -	02/2012	27(O)	0/0
65	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28 -	621.28	693.43	02/2011 -	02/2012	12(O)	0/1
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	147.86	08/2011 -	02/2012	6(O)	0/0
67	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	209.58	07/2010 02/2012	02/2012	19(O)	0/0
68	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	73.29	07/2011 -	02/2012	7(O)	0/0
69	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 -	2,283.69	2,492.85	04/2005 -	03/2012	83(O)	7/11

List of Delay Project w.r. t. Original

(Sep,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
70	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,357.00	12/2009	03/2012	27(O)	33/60
71	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,562.46	10/2010	03/2012	17(O)	0/0
72	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,483.30	09/2009	03/2012	30(O)	15/30
73	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	690.87	10/2009	03/2012	29(O)	2/20
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	55.89	11/2011	03/2012	4(O)	0/0
75	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,373.35	03/2007	05/2012	62(O)	1/25
76	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	670.42	08/2010	11/2012	27(O)	0/0
77	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	2,861.00	08/2012	11/2012	3(O)	3/16
78	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	1,020.22	09/2009	12/2012	39(O)	0/0
79	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,733.05	11/2008	12/2012	49(O)	25/38
80	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	685.00	11/2011	12/2012	13(O)	6/34
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	266.43	11/2011	12/2012	13(O)	0/0
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	260.37	11/2011	12/2012	13(O)	0/0
83	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	131.19	02/2012	12/2012	10(O)	0/0
84	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	2,225.00	10/2012	12/2012	2(O)	3/15
85	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	2,076.00	10/2012	12/2012	2(O)	3/16
86	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,817.00	04/2009	03/2013	47(O)	19/9
87	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	343.31	09/2010	03/2013	30(O)	0/0
88	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	873.35	02/2012	03/2013	13(O)	0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
89	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01 623.44	623.44	70.41	01/2012 -	07/2013	18(O)	0/0
90	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,361.96	01/2012 -	09/2013	20(O)	2/10
91	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19 -	184.19	131.66	11/2011 -	09/2013	22(O)	0/0
92	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, Assam	01/2008	4,375.35 -	4,375.35	2,306.00	06/2011 -	10/2013	28(O)	0/29
93	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72 913.63	913.63	265.42	07/2006 01/2014	01/2014	90(O)	2/5
94	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttaranchal	11/2006	2,978.48 -	2,978.48	1,159.00	03/2013 -	06/2014	15(O)	6/13
95	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33 -	6,285.33	5,127.36	09/2010 -	08/2014	47(O)	2/11
96	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97 -	8,693.00	6,104.00	12/2009 -	09/2014	57(O)	15/70
97	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19 -	11,130.19	2,877.41	08/2013 -	09/2014	13(O)	0/0
98	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59 -	3,919.59	3,293.30	09/2009 -	12/2014	63(O)	1/20
99	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67 3,642.04	3,642.04	939.65	07/2014 01/2016	01/2016	18(O)	0/0
100	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttaranchal	07/2006	1,657.00 -	2,978.86	277.11	07/2010 -	02/2016	67(O)	1/10
101	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	172.38	07/2014 -	05/2016	22(O)	0/7
102	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,582.26	05/2013 06/2016	06/2016	37(O)	79/22
Total			109,856.75 -	115,653.87	68,039.28				228/514
<u>Railways</u>									
103	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 -	252.50	194.44	02/2010 -	11/2011	21(O)	0/0
104	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O)	0/0
105	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, Orissa	04/1993	100.00 142.90	208.68	185.89	03/2002 -	12/2011	117(O)	0/0
106	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 164.36	822.57	491.60	02/2009 -	12/2011	34(O)	0/0
107	Dakshin-barasat-lakshmikanapur (ER) - [N22000116]ER, West Bengal	04/2009	259.51 -	259.51	66.18	12/2011 -	02/2012	2(O)	0/0
108	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 637.46	634.13	542.82	03/1995 -	03/2012	204(O)	0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
109	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	324.90	-	03/2010	03/2012	24(O)	0/0
110	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17	220.00	218.15	03/2011	03/2012	12(O)	0/0
111	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97	723.27	381.93	06/2005 07/2011	03/2012	81(O)	0/0
112	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	145.14	03/2007 03/2007	06/2012	63(O)	0/0
113	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	1,211.22	390.16	03/2005 12/2008	12/2012	93(O)	0/0
114	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00	981.00	536.25	03/2009	12/2012	45(O)	0/0
115	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47	1,389.98	998.45	10/2007	12/2012	62(O)	0/0
116	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	-	03/2010	12/2012	33(O)	0/0
117	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04	603.04	45.88	03/2012	03/2013	12(O)	0/0
118	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97	189.97	64.10	12/2011	11/2013	23(O)	0/0
119	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90	223.01	83.52	12/2012	12/2013	12(O)	0/0
120	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31	4,091.33	2,785.91	03/2009	12/2013	57(O)	0/0
121	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00	1,655.80	820.57	12/2008	03/2014	63(O)	0/0
122	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00	369.90	107.60	03/2010 06/2014	06/2014	51(O)	0/0
123	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,226.12	04/2008 03/2014	12/2014	80(O)	0/0
124	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00	5,300.00	278.51	03/2014	03/2015	12(O)	0/0
125	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	467.89	03/2011 03/2014	03/2016	60(O)	0/0
126	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60	2,069.60	-	03/2014	03/2016	24(O)	0/0
127	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	2,397.72	0.02	03/2016	06/2016	3(O)	0/0
128	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	20,000.00	7,430.73	03/2001	12/2017	201(O)	0/0
Total			22,320.65	51,942.31	19,019.93				0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Road Transport & Highways</u>									
129	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	10/2011	33(O)	0/0
130	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI, Tamil Nadu	03/2005	629.00	629.00	910.00	11/2010	10/2011	11(O)	0/0
131	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	257.60	06/2008	10/2011	40(O)	0/0
132	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI, Bihar	12/2003	340.00	340.00	566.40	06/2008	10/2011	40(O)	0/0
133	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI, Kerala	12/2003	312.50	312.50	603.60	03/2009	10/2011	31(O)	0/0
134	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	385.30	12/2008	10/2011	34(O)	0/0
135	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	658.20	07/2010	10/2011	15(O)	0/0
136	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	285.00	359.20	07/2010	10/2011	15(O)	0/0
137	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	10/2011	9(O)	0/0
138	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	277.10	10/2008	11/2011	37(O)	0/0
139	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya Pradesh	12/2003	225.00	225.00	254.50	10/2008	11/2011	37(O)	0/0
140	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09	276.09	295.30	09/2009	11/2011	26(O)	0/0
141	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	154.34	08/2004 07/2010	12/2011	88(O)	0/0
142	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	163.13	08/2004	12/2011	88(O)	0/0
143	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	79.38	04/2004	12/2011	92(O)	0/0
144	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
145	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	475.60	03/2005	12/2011	81(O)	0/0
146	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	275.00	298.70	09/2007	12/2011	51(O)	0/0
147	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	246.30	09/2007	12/2011	51(O)	0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
148	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	436.70	11/2007	12/2011	49(O)	0/0
149	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	205.00	06/2005	12/2011	78(O)	0/0
150	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	181.80	03/2008	12/2011	45(O)	0/0
151	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	152.30	03/2008	12/2011	45(O)	0/0
152	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	399.40	10/2008	12/2011	38(O)	0/0
153	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	226.60	02/2009	12/2011	34(O)	0/0
154	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	80.65	04/2009	12/2011	32(O)	0/0
155	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	173.30	06/2008	12/2011	42(O)	0/0
156	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	393.20	12/2008	12/2011	36(O)	0/0
157	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	363.20	12/2008	12/2011	36(O)	0/0
158	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	202.40	06/2008	12/2011	42(O)	0/0
159	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	289.20	09/2008	12/2011	39(O)	0/0
160	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	187.10	11/2008	12/2011	37(O)	0/0
161	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	172.20	10/2008	12/2011	38(O)	0/0
162	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	276.40	10/2008	12/2011	38(O)	0/0
163	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	223.10	10/2008	12/2011	38(O)	0/0
164	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	436.30	09/2008	12/2011	39(O)	0/0
165	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	256.40	06/2008	12/2011	42(O)	0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
166	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	12/2011	30(O)	0/0
167	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	233.60	06/2008	12/2011	42(O)	0/0
168	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	253.50	06/2008	12/2011	42(O)	0/0
169	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	476.20	03/2008	12/2011	45(O)	0/0
170	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	169.30	06/2008	12/2011	42(O)	0/0
171	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	207.90	04/2008	12/2011	44(O)	0/0
172	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	123.30	05/2008	12/2011	43(O)	0/0
173	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	193.30	06/2008	12/2011	42(O)	0/0
174	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	580.70	06/2009	12/2011	30(O)	0/0
175	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	702.80	10/2009	12/2011	26(O)	0/0
176	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	326.40	03/2010	12/2011	21(O)	0/0
177	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11(O)	0/0
178	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	916.90	07/2010	12/2011	17(O)	0/0
179	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	341.80	05/2010	12/2011	19(O)	0/0
180	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	165.14	02/2004	12/2011	94(O)	0/0
181	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	624.30	08/2010	12/2011	16(O)	0/0
182	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	551.50	05/2010	12/2011	19(O)	0/0
183	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,588.00	08/2011	12/2011	4(O)	0/0
184	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	245.20	11/2008	01/2012	38(O)	0/0
185	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	294.70	09/2009	02/2012	29(O)	0/0
186	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	178.40	09/2007	03/2012	54(O)	0/0
187	KOTWA TO DEWAPUR (10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	269.40	10/2008	03/2012	41(O)	0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
188	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	355.60	03/2008	03/2012	48(O)	0/0
189	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	207.90	10/2008	03/2012	41(O)	0/0
190	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	118.90	04/2008	03/2012	47(O)	0/0
191	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	178.80	04/2008	03/2012	47(O)	0/0
192	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	150.80	04/2010	03/2012	23(O)	0/0
193	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	05/2012	22(O)	0/0
194	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
195	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	89.65	09/2008	06/2012	45(O)	0/0
196	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	167.60	10/2008	06/2012	44(O)	0/0
197	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.10	10/2009	06/2012	32(O)	0/0
198	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.60	12/2009	06/2012	30(O)	0/0
199	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	162.90	09/2010	06/2012	21(O)	0/0
200	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,527.00	10/2011	06/2012	8(O)	0/0
201	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,647.00	11/2011	06/2012	7(O)	0/0
202	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	126.80	05/2008	08/2012	51(O)	0/0
203	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	510.50	10/2011	08/2012	10(O)	0/0
204	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	184.40	06/2010	10/2012	28(O)	0/0
205	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.30	09/2009	10/2012	37(O)	0/0
206	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
207	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	176.70	07/2008	12/2012	53(O)	0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
208	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	252.69	02/2004	12/2012	106(O)	0/0
209	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00	748.00	1,086.00	09/2010	03/2013	30(O)	0/0
210	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	117.69	09/2007	06/2013	69(O)	0/0
211	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7(O)	0/0
212	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	30.98	04/2009	07/2013	51(O)	0/0
213	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
214	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.00	02/2010	07/2013	41(O)	0/0
215	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
216	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
217	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	40.29	09/2007	12/2013	75(O)	0/0
218	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	27.94	07/2009	12/2013	53(O)	0/0
Total			31,999.93	34,165.18	35,527.14				0/0
Shipping & Ports									
219	MARINE LIQUID TERMINALS - [N25000054]JENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	63(O)	0/0
220	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	121.41	12/2005 01/2008	10/2011	70(O)	0/0
221	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	11/2011	7(O)	0/0
222	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	7(O)	0/0
223	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2(O)	0/0
224	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	55.40	12/2011 05/2012	05/2012	5(O)	0/0

List of Delay Project w.r. t. Original

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
225	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	1,460.00	590.00	12/2010	09/2012	21(O)	0/0
226	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
227	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.16	02/2011	03/2013	25(O)	0/0
228	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24(O)	0/0
229	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009	05/2013	52(O)	0/0
230	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006	12/2013	93(O)	0/0
	Total		8,569.67	9,394.82	1,494.24				0/0
	Telecommunications								
231	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	80.47	12/2005	12/2011	72(O)	0/0
232	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	20.90	10/2010	03/2012	17(O)	0/0
	Total		634.00	809.51	101.37				0/0
	Urban Development								
233	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013	15(O)	6/6
	Total		6,395.00	11,609.00	2,267.57				6/6
	Water Resources								
234	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			309,434.69	375,643.53	202,576.46				642/1384

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Civil Aviation</u>									
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 2,015.00	2,015.00	940.61	01/2011 -	12/2011	11(O)	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,391.83	05/2011 -	03/2012	10(O)	0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	48.41	05/2012 -	05/2012	0(O)	0/0
4	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40 -	264.29	153.38	01/2011 -	12/2012	23(O)	0/0
5	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	626.00	324.99	06/2013 -	06/2013	0(O)	0/0
	Total		4,123.24 -	5,435.02	2,859.22				0/0
<u>Coal</u>									
6	KARMA OCP - [N06000088]JCL,Jharkhandd	06/2009	162.46 -	162.46	26.36	03/2014 -	03/2014	0(O)	0/0
7	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	1.14	03/2015 -	03/2015	0(O)	0/0
8	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 -	03/2018	0(O)	0/0
9	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	-	-	0/0
	Total		1,903.56 -	1,903.56	27.50				0/0
<u>Fertilisers</u>									
10	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	84.31	07/2011 -	11/2011	4(O)	0/0
11	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	105.79	07/2011 -	03/2012	8(O)	0/0
	Total		763.00 -	763.00	190.10				0/0
<u>Steel</u>									
12	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
13	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
	Total		1,470.55 -	1,470.55	.00				0/0
<u>Petroleum</u>									

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	527.43	03/2011 05/2011	06/2011	1(R3)	0/0
15	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
16	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
17	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	251.19	02/2011 08/2011	08/2011	0(R3)	0/0
18	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38 -	2,340.00	2,254.62	10/2010 09/2011	09/2011	0(R2)	0/0
19	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
20	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	245.01	06/2010 07/2011	09/2011	2(R3)	0/0
21	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
22	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
23	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	202.12	03/2013 03/2013	12/2011	-15(R1)	0/0
24	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	644.81	04/2010 -	12/2011	20(O)	0/0
25	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	257.60	04/2011 -	12/2011	8(O)	0/0
26	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	174.44	09/2012 -	12/2011	-9(O)	0/0
27	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	6,869.78	01/2012 -	01/2012	0(O)	0/0
28	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 02/2012	02/2012	0(R3)	0/0
29	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
30	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	0(R3)	0/0
31	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	6,652.22	-	01/2013 -	03/2012	-10(O)	0/0
32	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
33	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
34	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,596.54	05/2010 05/2012	05/2012	0(R3)	0/0
35	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	38.35	05/2010 04/2012	05/2012	1(R3)	0/0
36	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	92.09	07/2010 05/2012	05/2012	0(R3)	0/0
37	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,380.59	08/2010 03/2012	06/2012	3(R3)	0/0
38	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	535.59	06/2012 -	06/2012	0(O)	0/0
39	Wind Power Project - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
40	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	70.85	04/2011 -	07/2012	15(O)	0/0
41	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	1,803.78	413.47	07/2012 -	07/2012	0(O)	0/0
42	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	288.04	105.00	08/2012 -	08/2012	0(O)	0/0
43	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	6,855.93	2,296.56	09/2012 -	09/2012	0(O)	0/0
44	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	302.26	21.14	09/2012 -	09/2012	0(O)	0/0
45	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.53	09/2011 -	12/2012	15(O)	0/0
46	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	80.28	12/2011 -	01/2013	13(O)	0/0
47	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2(O)	0/0
48	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,767.52	05/2010 03/2013	03/2013	0(R3)	0/0
49	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	367.91	03/2013 -	03/2013	0(O)	0/0
50	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
51	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
52	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
53	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	2,915.00	-	10/2012 -	03/2013	5(O)	0/0
54	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79 -	861.79	-	05/2013 -	05/2013	0(O)	0/0
55	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
56	Wax Project - [N16000101]NRL, Assam	06/2010	576.60 -	576.60	13.77	12/2013 12/2013	12/2013	0(R3)	0/0
57	Development of WO-16 Cluster Fields - [N16000105]ONGC, Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
58	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC, Assam	06/2010	202.94 -	202.94	-	01/2014 -	01/2014	0(O)	0/0
59	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00 -	8,140.00	-	02/2014 -	02/2014	0(O)	0/0
60	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	-	12/2014 -	12/2014	0(O)	0/0
61	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014	0(O)	0/0
62	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00 -	3,823.00	-	04/2015 -	04/2015	0(O)	0/0
63	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	281.07	3.29	10/2010 -	-	-	0/0
64	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 -	756.00	744.26	09/2011 -	-	-	0/0
65	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	-	-	0/0
66	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	1,584.00	3.38	- -	08/2013	-	0/0
	Total		108,394.43 -	115,630.49	38,953.62				0/0
Power									
67	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL, J & K	10/2006	238.25 -	227.03	212.75	05/2011 05/2011	09/2011	4(R3)	0/0
68	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL, Multi State	12/2007	227.52 -	227.52	132.86	06/2010 -	11/2011	17(O)	0/0
69	CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,668.16	08/2010 -	12/2011	16(O)	0/0
70	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL, Multi State	04/2008	297.37 -	297.37	295.81	07/2011 -	12/2011	5(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
71	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,542.17	11/2009	02/2012	27(O)	0/0
72	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	304.39	02/2012	02/2012	0(O)	0/0
73	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	60.03	02/2012	02/2012	0(O)	0/0
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	147.86	08/2011	02/2012	6(O)	0/0
75	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	209.58	07/2010 02/2012	02/2012	0(R3)	0/0
76	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	73.29	07/2011	02/2012	7(O)	0/0
77	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,562.46	10/2010	03/2012	17(O)	0/0
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	55.89	11/2011	03/2012	4(O)	0/0
79	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	76.44	04/2012	04/2012	0(O)	0/0
80	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	287.91	05/2012	05/2012	0(O)	0/0
81	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	414.30	06/2012	06/2012	0(O)	0/0
82	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	118.40	06/2012	06/2012	0(O)	0/0
83	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	10.88	06/2012	06/2012	0(O)	0/0
84	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,687.14	08/2012	08/2012	0(O)	0/0
85	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	3,988.90	08/2012	08/2012	0(O)	0/0
86	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	396.22	08/2012	08/2012	0(O)	0/0
87	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,035.57	10/2012	10/2012	0(O)	0/0
88	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	174.37	10/2012	10/2012	0(O)	0/0
89	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	11.32	10/2012	10/2012	0(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	670.42	08/2010	11/2012	27(O)	0/0
91	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	323.94	11/2012	11/2012	0(O)	0/0
92	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	253.39	11/2012	11/2012	0(O)	0/0
93	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	91.61	11/2012	11/2012	0(O)	0/0
94	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	1,020.22	09/2009	12/2012	39(O)	0/0
95	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	2,637.46	12/2012	12/2012	0(O)	0/0
96	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	266.43	11/2011	12/2012	13(O)	0/0
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	260.37	11/2011	12/2012	13(O)	0/0
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	131.19	02/2012	12/2012	10(O)	0/0
99	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	350.24	12/2012	12/2012	0(O)	0/0
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	25.54	01/2013	01/2013	0(O)	0/0
101	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	19.25	01/2013	01/2013	0(O)	0/0
102	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	343.31	09/2010	03/2013	30(O)	0/0
103	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	873.35	02/2012	03/2013	13(O)	0/0
104	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	167.23	03/2013	03/2013	0(O)	0/0
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	76.42	04/2013	04/2013	0(O)	0/0
106	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	8.71	04/2013	04/2013	0(O)	0/0
107	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	70.41	01/2012	07/2013	18(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	50.10	07/2013	07/2013	0(O)	0/0
109	TRANSMISSION SYSTEM OF ESTABLISHMENT OF 400/220KV - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	-	07/2013	07/2013	0(O)	0/0
110	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	74.08	08/2013	08/2013	0(O)	0/0
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	18.55	08/2013	08/2013	0(O)	0/0
112	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	125.67	08/2013	08/2013	0(O)	0/0
113	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	131.66	11/2011	09/2013	22(O)	0/0
114	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	57.33	11/2013	11/2013	0(O)	0/0
115	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	216.21	12/2013	12/2013	0(O)	0/0
116	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	-	03/2014	03/2014	0(O)	0/0
117	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	2,877.41	08/2013	09/2014	13(O)	0/0
118	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
119	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	939.65	07/2014 01/2016	01/2016	0(R3)	0/0
120	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	113.23	06/2011	08/2011	2(O)	0/0
Total			82,497.84	84,092.42	27,660.08				0/0
<u>Railways</u>									
121	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	233.90	- 02/2009	12/2010	22(R1)	0/0
122	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	188.11	- 03/2009	12/2010	21(R1)	0/0
123	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	221.90	157.88	12/2007 03/2010	12/2010	9(R1)	0/0
124	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	294.93	03/2009 12/2008	12/2010	24(R1)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
125	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	-	- -	12/2010	-	0/0
126	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	299.77	- 03/2009	03/2011	24(R1)	0/0
127	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	261.00	03/2009 12/2009	03/2011	15(R1)	0/0
128	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	194.44	02/2010 -	11/2011	21(O)	0/0
129	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O)	0/0
130	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	208.68	185.89	03/2002 -	12/2011	117(O)	0/0
131	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	822.57	491.60	02/2009 -	12/2011	34(O)	0/0
132	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	169.00	- -	12/2011	-	0/0
133	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	197.61	- 09/2009	12/2011	27(R1)	0/0
134	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	242.54	03/2013 -	12/2011	-15(O)	0/0
135	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,183.04	- -	02/2012	-	0/0
136	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	422.22	- 12/2009	02/2012	26(R1)	0/0
137	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	66.18	12/2011 -	02/2012	2(O)	0/0
138	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 637.46	634.13	542.82	03/1995 -	03/2012	204(O)	0/0
139	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	510.51	- -	03/2012	-	0/0
140	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	480.37	- 12/2011	03/2012	3(R3)	0/0
141	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	205.49	- 03/2012	03/2012	0(R3)	0/0
142	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	425.42	- -	03/2012	-	0/0
143	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	561.57	- -	03/2012	-	0/0
144	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	340.51	- 03/2011	03/2012	12(R3)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
145	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012	-	0/0
146	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012	-	0/0
147	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	-	03/2010 -	03/2012	24(O)	0/0
148	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	191.49	- -	03/2012	-	0/0
149	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	137.47	03/2012 -	03/2012	0(O)	0/0
150	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	218.15	03/2011 -	03/2012	12(O)	0/0
151	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	381.93	06/2005 07/2011	03/2012	8(R3)	0/0
152	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	167.73	36.32	03/2012 -	03/2012	0(O)	0/0
153	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	145.14	03/2007 03/2007	06/2012	63(R1)	0/0
154	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	326.92	- 07/2012	07/2012	0(R3)	0/0
155	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	579.88	- -	12/2012	-	0/0
156	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	789.49	12/2012 -	12/2012	0(O)	0/0
157	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	390.16	03/2005 12/2008	12/2012	48(R1)	0/0
158	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	338.99	- 03/2012	12/2012	9(R3)	0/0
159	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	240.86	- -	12/2012	-	0/0
160	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	536.25	03/2009 -	12/2012	45(O)	0/0
161	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	998.45	10/2007 -	12/2012	62(O)	0/0
162	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33(O)	0/0
163	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	105.66	12/2012 -	12/2012	0(O)	0/0
164	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	150.36	- -	03/2013	-	0/0
165	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	691.73	- -	03/2013	-	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
166	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh	04/2008	603.04	603.04	45.88	03/2012	03/2013	12(O)	0/0
167	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR, Gujarat	04/2008	394.13	394.14	0.49	03/2013	03/2013	0(O)	0/0
168	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, Tamil Nadu	04/2006	495.74	495.74	132.26	-	06/2013	0(R3)	0/0
169	Ghutiasharif-Canning (ER) - [N22000117]ER, West Bengal	04/2009	189.97	189.97	64.10	12/2011	11/2013	23(O)	0/0
170	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh	04/2005	383.79	585.93	176.03	-	12/2013	-	0/0
171	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90	223.01	83.52	12/2012	12/2013	12(O)	0/0
172	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam	04/1996	1,676.31	4,091.33	2,785.91	03/2009	12/2013	57(O)	0/0
173	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00	1,655.80	820.57	12/2008	03/2014	63(O)	0/0
174	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70	1,717.29	724.96	-	03/2014	-	0/0
175	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura	04/2008	813.34	1,141.75	211.09	03/2014	03/2014	0(O)	0/0
176	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34	2,393.49	3.61	04/2014	03/2014	-1(O)	0/0
177	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR, Rajasthan	04/2008	653.19	653.19	7.30	03/2014	03/2014	0(O)	0/0
178	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR, Rajasthan	04/2008	516.23	516.23	75.92	03/2014	03/2014	0(O)	0/0
179	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62	1,389.62	192.09	03/2014	03/2014	0(O)	0/0
180	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00	369.90	107.60	03/2010	06/2014	0(R3)	0/0
181	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR, Assam	09/1997	1,000.00	3,230.01	2,226.12	04/2008	12/2014	9(R3)	0/0
182	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66	324.66	166.80	-	03/2015	-	0/0
183	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP, Maharashtra	04/2008	5,300.00	5,300.00	278.51	03/2014	03/2015	12(O)	0/0
184	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR, Rajasthan	04/2008	829.74	829.74	-	03/2015	03/2015	0(O)	0/0
185	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00	850.00	8.44	03/2015	03/2015	0(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48	3,380.57	52.63	12/2015	12/2015	0(O)	0/0
187	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	467.89	03/2011 03/2014	03/2016	24(R3)	0/0
188	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60	2,069.60	-	03/2014	03/2016	24(O)	0/0
189	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98	3,951.98	-	03/2016	03/2016	0(O)	0/0
190	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02	2,619.02	-	03/2016	03/2016	0(O)	0/0
191	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	2,397.72	0.02	03/2016	06/2016	3(O)	0/0
192	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	20,000.00	7,430.73	03/2001	12/2017	201(O)	0/0
193	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	149.63	- 03/2010	-	-	0/0
194	New BG line Rly line from Eklakhi-Balughat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.54	- -	-	-	0/0
195	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00	968.60	87.09	12/2012	-	-	0/0
196	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	594.05	-	-	-	0/0
197	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	97.90	-	-	-	0/0
198	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00	412.91	475.05	-	-	-	0/0
199	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30	1,038.00	553.42	03/1998	-	-	0/0
200	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55	945.73	611.54	-	-	-	0/0
201	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00	997.58	63.92	-	-	-	0/0
202	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	91.53	-	-	-	0/0
203	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00	363.26	0.27	07/2008	-	-	0/0
204	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,083.81	07/2005	-	-	0/0
205	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	1,214.00	71.95	-	-	-	0/0
206	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	554.55	255.68	- 05/2009	-	-	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
207	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23	162.87	87.25	-	-	-	0/0
208	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	815.43	06/2007 -	-	-	0/0
209	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	-	04/2003 03/2010	-	-	0/0
210	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	473.44	- -	-	-	0/0
211	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
212	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	338.40	- 12/2012	-	-	0/0
213	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
214	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 -	418.17	73.55	- -	-	-	0/0
215	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	210.51	- -	-	-	0/0
216	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	258.74	03/2008 03/2009	-	-	0/0
217	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	173.49	176.56	03/1998 08/2005	-	-	0/0
218	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	25.02	02/2015 -	-	-	0/0
219	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
220	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	21.60	02/2006 -	-	-	0/0
221	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	308.13	03/2008 06/2008	-	-	0/0
222	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	190.84	- -	-	-	0/0
223	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	418.72	- -	-	-	0/0
224	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	21.98	- -	-	-	0/0
225	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	87.07	- -	-	-	0/0
226	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	36.59	- -	-	-	0/0
227	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	176.51	03/2011 -	-	-	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
228	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	0.71	-	-	-	0/0
229	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	170.78	03/2011	-	-	0/0
230	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	457.16	06/1999 03/2011	-	-	0/0
231	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	166.90	03/2004	-	-	0/0
232	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	327.81	- 03/2011	-	-	0/0
233	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	267.63	06/2004 04/2005	-	-	0/0
234	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
235	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
236	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	720.44	- 12/2010	-	-	0/0
237	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	428.04	- -	-	-	0/0
238	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,076.13	12/2006 08/2010	-	-	0/0
239	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	234.86	- 02/2011	-	-	0/0
240	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	471.11	02/2010 02/2011	-	-	0/0
241	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	369.25	- -	-	-	0/0
242	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	235.66	- 03/2011	-	-	0/0
243	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	131.63	- -	-	-	0/0
244	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	134.27	- -	-	-	0/0
245	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	82.93	- -	12/2011	-	0/0
246	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	356.57	- 03/2011	-	-	0/0
247	NEW B.G. LINE FROM TETELIA TO BYRNIAHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.80	- -	-	-	0/0
248	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	162.33	12/2010 03/2011	-	-	0/0
249	Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	130.08	- 12/2010	-	-	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
250	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24	468.62	2.08	03/2012	-	-	0/0
	Total		61,606.14	126,362.37	48,523.47				0/0
Road Transport & Highways									
251	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	10/2011	33(O)	0/0
252	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	910.00	11/2010	10/2011	11(O)	0/0
253	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	257.60	06/2008	10/2011	40(O)	0/0
254	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	566.40	06/2008	10/2011	40(O)	0/0
255	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	603.60	03/2009	10/2011	31(O)	0/0
256	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.30	12/2008	10/2011	34(O)	0/0
257	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	658.20	07/2010	10/2011	15(O)	0/0
258	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	359.20	07/2010	10/2011	15(O)	0/0
259	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	10/2011	9(O)	0/0
260	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	200.40	10/2011	10/2011	0(O)	0/0
261	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	277.10	10/2008	11/2011	37(O)	0/0
262	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	254.50	10/2008	11/2011	37(O)	0/0
263	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	295.30	09/2009	11/2011	26(O)	0/0
264	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	154.34	08/2004 07/2010	12/2011	17(R3)	0/0
265	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	163.13	08/2004	12/2011	88(O)	0/0
266	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	79.38	04/2004	12/2011	92(O)	0/0
267	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
268	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	475.60	03/2005	12/2011	81(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
269	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	298.70	09/2007	12/2011	51(O)	0/0
270	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	246.30	09/2007	12/2011	51(O)	0/0
271	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	436.70	11/2007	12/2011	49(O)	0/0
272	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	205.00	06/2005	12/2011	78(O)	0/0
273	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	181.80	03/2008	12/2011	45(O)	0/0
274	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	152.30	03/2008	12/2011	45(O)	0/0
275	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	399.40	10/2008	12/2011	38(O)	0/0
276	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	226.60	02/2009	12/2011	34(O)	0/0
277	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	80.65	04/2009	12/2011	32(O)	0/0
278	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	173.30	06/2008	12/2011	42(O)	0/0
279	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	393.20	12/2008	12/2011	36(O)	0/0
280	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	363.20	12/2008	12/2011	36(O)	0/0
281	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	202.40	06/2008	12/2011	42(O)	0/0
282	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	289.20	09/2008	12/2011	39(O)	0/0
283	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	187.10	11/2008	12/2011	37(O)	0/0
284	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	172.20	10/2008	12/2011	38(O)	0/0
285	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	276.40	10/2008	12/2011	38(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
286	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI, Madhya Pradesh)	12/2003	229.91	229.91	223.10	10/2008	12/2011	38(O)	0/0
287	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	436.30	09/2008	12/2011	39(O)	0/0
288	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	256.40	06/2008	12/2011	42(O)	0/0
289	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	12/2011	30(O)	0/0
290	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	233.60	06/2008	12/2011	42(O)	0/0
291	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	253.50	06/2008	12/2011	42(O)	0/0
292	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	476.20	03/2008	12/2011	45(O)	0/0
293	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	169.30	06/2008	12/2011	42(O)	0/0
294	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	207.90	04/2008	12/2011	44(O)	0/0
295	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	123.30	05/2008	12/2011	43(O)	0/0
296	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	193.30	06/2008	12/2011	42(O)	0/0
297	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	580.70	06/2009	12/2011	30(O)	0/0
298	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	702.80	10/2009	12/2011	26(O)	0/0
299	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	326.40	03/2010	12/2011	21(O)	0/0
300	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11(O)	0/0
301	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	916.90	07/2010	12/2011	17(O)	0/0
302	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	341.80	05/2010	12/2011	19(O)	0/0
303	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	165.14	02/2004	12/2011	94(O)	0/0
304	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	624.30	08/2010	12/2011	16(O)	0/0
305	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	551.50	05/2010	12/2011	19(O)	0/0
306	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,588.00	08/2011	12/2011	4(O)	0/0
307	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	245.20	11/2008	01/2012	38(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
308	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	294.70	09/2009	02/2012	29(O)	0/0
309	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	389.40	02/2012	02/2012	0(O)	0/0
310	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	178.40	09/2007	03/2012	54(O)	0/0
311	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	269.40	10/2008	03/2012	41(O)	0/0
312	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	355.60	03/2008	03/2012	48(O)	0/0
313	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	207.90	10/2008	03/2012	41(O)	0/0
314	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	118.90	04/2008	03/2012	47(O)	0/0
315	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	178.80	04/2008	03/2012	47(O)	0/0
316	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	150.80	04/2010	03/2012	23(O)	0/0
317	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	05/2012	22(O)	0/0
318	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
319	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.00	05/2012	05/2012	0(O)	0/0
320	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	804.30	05/2012	05/2012	0(O)	0/0
321	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	355.60	05/2012	05/2012	0(O)	0/0
322	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	89.65	09/2008	06/2012	45(O)	0/0
323	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	167.60	10/2008	06/2012	44(O)	0/0
324	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.10	10/2009	06/2012	32(O)	0/0
325	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.60	12/2009	06/2012	30(O)	0/0
326	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	162.90	09/2010	06/2012	21(O)	0/0
327	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	396.70	06/2012	06/2012	0(O)	0/0
328	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,527.00	10/2011	06/2012	8(O)	0/0
329	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,647.00	11/2011	06/2012	7(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
330	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	323.60	07/2012 -	07/2012	0(O)	0/0
331	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	126.80	05/2008 -	08/2012	51(O)	0/0
332	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	510.50	10/2011 -	08/2012	10(O)	0/0
333	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	813.90	09/2012 -	09/2012	0(O)	0/0
334	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	184.40	06/2010 -	10/2012	28(O)	0/0
335	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.30	09/2009 -	10/2012	37(O)	0/0
336	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16(O)	0/0
337	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,060.00	10/2012 -	10/2012	0(O)	0/0
338	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	29.04	11/2012 -	11/2012	0(O)	0/0
339	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	11/2012 -	11/2012	0(O)	0/0
340	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	176.70	07/2008 -	12/2012	53(O)	0/0
341	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	252.69	02/2004 -	12/2012	106(O)	0/0
342	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	389.40	12/2012 -	12/2012	0(O)	0/0
343	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	666.00	01/2013 -	01/2013	0(O)	0/0
344	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	113.40	02/2013 -	02/2013	0(O)	0/0
345	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00 -	748.00	1,086.00	09/2010 -	03/2013	30(O)	0/0
346	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	-	03/2013 -	03/2013	0(O)	0/0
347	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	326.70	03/2013 -	03/2013	0(O)	0/0
348	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	173.20	03/2013 -	03/2013	0(O)	0/0
349	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	107.60	03/2013 -	03/2013	0(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
350	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
351	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	198.70	05/2013	05/2013	0(O)	0/0
352	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	131.20	05/2013	05/2013	0(O)	0/0
353	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
354	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	351.54	2.64	05/2013	05/2013	0(O)	0/0
355	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	117.69	09/2007	06/2013	69(O)	0/0
356	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7(O)	0/0
357	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
358	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0
359	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50	1,008.50	568.40	06/2013	06/2013	0(O)	0/0
360	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI - [N24000173]NHAI, Tamil Nadu	06/2011	600.00	600.00	72.15	06/2013	06/2013	0(O)	0/0
361	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	30.98	04/2009	07/2013	51(O)	0/0
362	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
363	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	179.00	02/2010	07/2013	41(O)	0/0
364	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	593.00	67.24	07/2013	07/2013	0(O)	0/0
365	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J & K	07/2010	1,813.76	1,813.76	-	07/2013	07/2013	0(O)	0/0
366	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
367	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	785.50	322.80	08/2013	08/2013	0(O)	0/0
368	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00	1,141.00	182.50	08/2013	08/2013	0(O)	0/0
369	New 4 Lane elevated road from Chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	4.34	09/2013	09/2013	0(O)	0/0
370	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	0.99	09/2013	09/2013	0(O)	0/0
371	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
372	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0
373	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00	650.00	-	11/2013	11/2013	0(O)	0/0
374	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
375	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	40.29	09/2007	12/2013	75(O)	0/0
376	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	27.94	07/2009	12/2013	53(O)	0/0
377	SIX LANNING OF HOSUR-KRISHNAGIRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
378	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
379	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
380	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	432.00	10/2014	10/2014	0(O)	0/0
381	NASHRI CHANANI - [N24000162]NHAI, J & K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
382	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J & K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
Total			72,461.45	74,266.70	45,748.78				0/0
<u>Shipping & Ports</u>									
383	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67	298.17	294.09	04/2009	02/2011	22(O)	0/0
384	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST, Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
385	MARINE LIQUID TERMINALS - [N25000054]JENNORE TANK, Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
386	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP., Kerala	12/2010	241.50	241.50	48.10	09/2011	09/2011	0(O)	0/0
387	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00 165.00	165.00	121.41	12/2005 01/2008	10/2011	45(R3)	0/0
388	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
389	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP., Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
390	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	360.80	03/2012 -	03/2012	0(O)	0/0
391	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
392	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
393	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	55.40	12/2011 05/2012	05/2012	0(R3)	0/0
394	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	590.00	12/2010 -	09/2012	21(O)	0/0
395	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
396	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
397	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	83.51	12/2012 -	12/2012	0(O)	0/0
398	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
399	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O)	0/0
400	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
401	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0
402	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
403	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O)	0/0
404	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
405	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
406	DEVELOPMENT OF COAL TERMINAL - [N25000055]JENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	-	-	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
407	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
408	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.48	10/2008 -	-	-	0/0
	Total		18,451.36 -	19,434.85	3,941.88				0/0
<u>Telecommunications</u>									
409	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	274.84	09/2009 -	02/2010	5(O)	0/0
410	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
411	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	192.48	119.45	03/2009 -	02/2011	23(O)	0/0
412	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	209.79	12/2008 -	02/2011	26(O)	0/0
413	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	377.54	308.13	03/2009 -	02/2011	23(O)	0/0
414	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	02/2011	20(O)	0/0
415	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	02/2011	25(O)	0/0
416	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	366.00	227.30	10/2008 -	02/2011	28(O)	0/0
417	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	346.90	01/2010 -	02/2011	13(O)	0/0
418	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70 -	848.70	712.86	01/2010 -	02/2011	13(O)	0/0
419	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19 -	315.19	141.64	01/2010 -	02/2011	13(O)	0/0
420	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49 -	601.49	496.20	12/2008 -	03/2011	27(O)	0/0
421	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	335.91	182.45	03/2009 -	03/2011	24(O)	0/0
422	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49 -	241.49	123.76	09/2009 -	03/2011	18(O)	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
423	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	17(O)	0/0
424	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33 -	584.33	403.71	02/2009 -	03/2011	25(O)	0/0
425	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	362.62	08/2009 -	03/2011	19(O)	0/0
426	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	280.72	11/2010 -	03/2011	4(O)	0/0
427	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	461.56	10/2009 -	03/2011	17(O)	0/0
428	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 -	08/2011	54(O)	0/0
429	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0
430	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	389.86	3.06	09/2011 -	09/2011	0(O)	0/0
431	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	80.47	12/2005 -	12/2011	72(O)	0/0
432	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	20.90	10/2010 -	03/2012	17(O)	0/0
433	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
434	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	350.00	-	- -	-	-	0/0
435	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
436	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	-	-	0/0
437	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0
438	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	-	-	0/0
439	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	-	-	0/0
440	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	-	-	0/0
441	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	-	-	0/0

List of Projects Without Milestones

(Sep,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
442	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
443	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	-	-	0/0
444	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53 -	625.53	-	02/2010 -	-	-	0/0
445	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75 -	624.75	-	09/2010 -	-	-	0/0
446	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	-	06/2009 -	-	-	0/0
447	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	-	-	0/0
	Total		18,952.93 -	19,197.68	5,331.04				0/0
Urban Development									
448	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	-	09/2014 -	09/2014	0(O)	0/0
449	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	24.38	03/2016 -	03/2016	0(O)	0/0
450	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
	Total		37,850.18 -	37,909.08	24.38				0/0
Water Resources									
451	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			409,017.58	487,652.72	173,295.56				0/0
