

दलनह; {k= dh ifj;kt ukvk
CENTRAL SECTOR PROJECTS

₹150 djkM vkj vf/kd ykxr okyh
(₹ 150 Crore and above)

358oh ढYk'k fjikV@358th Flash Report
vxLr] 2015@August, 2015



Hkkjr ljdkj / **Government of India**

lkf[;dh vkj dk;Øe dk;kUo;u e=ky ;

Ministry of Statistics and Programme Implementation

vk/kkjh ljpuk vkj ifj;kt uk i=ck/ku iHkkx
Infrastructure and Project Monitoring Division

ljkj iV;y Hkou] lln ekx]

Sardar Patel Bhavan, Sansad Marg,

ub] fnYyh / **New Delhi-110001**

oc lkbV / **Website- www.cspm.gov.in**

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

	Pages
Executive Summary Hindi	1-21
Executive Summary English	22-37
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2014-2015	38-39
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2014-2015	40-40
Summary of projects	41-56
Graphical Presentation of All Projects	57-68
Sector wise Analysis of Projects	69-105
Sector wise Graph	106-117
Annexures	118-118
Status of central sector projects costing Rs.150 Crore and above	119-119
List of projects in which expenditure is more than approved cost	120-127
Details of Projects Ahead of Schedule w.r.t. Original Schedule	128-128
Details of On Schedule Projects w.r.t. Original Schedule	129-135
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	136-147
Details of Delayed Projects w.r.t. Original and Revised Schedule	148-172
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	173-177
Details of Projects Without Date of Commissioning	178-194
Details of projects without original Date of Commissioning	195-196
Details of projects without Milestones w.r.t. original schedule	197-220
List of Projects Ahead of Schedule w.r.t. Latest Schedule	221-221
List of Projects on schedule w.r.t. Latest Schedule	222-231
List of ongoing projects having cost overrun w.r.t. to revised schedule	232-241
List of Delayed Projects w.r.t. Latest Schedule	242-252
Details of Central Sector Projects Showing Time overruns of 6 Months and More	253-263
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	264-272
Details Of Central Sector Projects Showing Time Overruns Of 6 Months and More and cost overruns of Rs. 100 Crore	273-277

कार्यकारी सारांश

1. अगस्त, 2015 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 789 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अगस्त 2015 के दौरान, 11 परियोजनाओं (विद्युत तथा पेट्रोलियम क्षेत्र प्रत्येक में 4 परियोजनाएं, कोयला में 2 परियोजनाएं और नागर विमानन क्षेत्र में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 789 परियोजनाओं में से, 232 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 37 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 37 परियोजनाओं में से, 17 परियोजनाएं ₹1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	रेलवे	296	31	0	0
2.	सड़क परिवहन एवं राजमार्ग	158	17	3	0
3.	विद्युत	108	62	22	12
4.	पेट्रोलियम	69	41	4	3
5.	कोयला	80	44	5	1
6.	शहरी विकास	30	13	0	0
7.	इस्पात	26	11	0	0
8.	नागर विमानन	6	3	1	0
9.	पोत परिवहन एवं पत्तन	6	3	0	0
10.	परमाणु ऊर्जा	4	4	1	1
11.	दूरसंचार	2	1	1	0
12.	उर्वरक	1	0	0	0
13.	खदान	1	0	0	0
14.	पेट्रोसायन	1	1	0	0
15.	भारी उद्योग	1	1	0	0
कुल		789	232	37	17

3. 789 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹10,58,599.45 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹12,62,592.29 करोड़ होने की संभावना है, जो ₹2,03,992.84 करोड़ (मूल लागत का 19.27%) की समग्र लागत वृद्धि को दर्शाता है। अगस्त, 2015 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,18,326.58 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 41.05% है।

लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31.08.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	लागत वृद्धि(%)
परमाणु ऊर्जा					
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
2	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	31.12
नागर विमानन					
3	विभिन्न हवाई अड्डों पर सं.56 एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	12.18
4	चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	8.19
कोयला					
5	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
6	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	76.47
7	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	34.63
8	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
9	मनुगुरु ओसी परियोजनाओं के आरएफआर	11/2012	430.45	486.27	12.97
भारी उद्योग					
10	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
पेट्रोसायन					
11	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9833.52	80.08
पेट्रोलियम					
12	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
13	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
14	कोरबा में विपणन टीओपी	01/2011	141.86	232.00	63.54

15	उरान चकान/शिकरापुर एलपीजी पाइपलाइन	12/2009	309.81	462.79	49.38
16	रिंग सागर सम्राट से मोबाइल ऑफशोर प्रोडक्शन यूनिट (एमओपीएस) का रूपांतरण	03/2011	861.79	1256.72	45.83
विद्युत					
17	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
18	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी))	09/2003	6285.33	16885.00	168.64
19	कामेंग जल विद्युत परियोजना (नीपको	12/2004	2496.90	6476.34	159.38
20	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	159.15
21	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.68	139.35
रेलवे					
22	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
23	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
24	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
25	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
26	तिरुचिरापल्लई-नागोरे-करायकल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
सड़क परिवहन एवं राजमार्ग					
27	पानीपत-जालंधर छः लेन (96 किमी. से 387.1 किमी.)	05/2009	1108.00	2288.00	106.50
28	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
29	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
30	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	68.99
31	एनडब्ल्यूई एस के तहत एनएच-202 पर अप्रोच रोड सहित वेंकटपुरम के समीप गोदावरी नदी पुल का निर्माण	03/2011	218.31	339.82	55.66
पोत परिवहन एवं पत्तन					

32	एल्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	150.00	600.00	300.00
33	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
34	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	51.92
35	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	18.89
इस्पात					
36	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
37	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	41.41
शहरी विकास					
38	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार हैं:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.08.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	4099.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
नागर विमानन					
3	नई अंतर्राष्ट्रीय टर्मिनल बिल्डिंग (गोवा) का निर्माण	05/2010	335.61	388.53	52.92

4	चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डे का विकास (मोहाली) चरण-II	02/2011	452.00	489.00	37.00
कोयला					
5	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	1698.20
6	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	1552.99
7	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
8	मनुगुरु ओसी परियोजना का आरएफआर	11/2012	430.45	486.27	55.82
9	अमलाई ओसीपी विस्तार सेक्टर बी (1.50 एमटीवाई)	11/2009	150.59	198.59	48.00
भारी उद्योग					
10	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोरसायन					
11	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	4372.91
पेट्रोलियम					
12	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
13	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
14	बेसिन क्षेत्र का एकीकृत विकास	12/2012	3513.07	4619.94	1106.87
15	वशिष्ट तथा एस-1 क्षेत्रों का समेकित विकास	05/2013	4124.35	4941.49	817.14
16	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
विद्युत					
17	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	16885.00	10599.67
18	बाढ़ एसटीपीपी (3X660 मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
19	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	3979.44
20	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7818.68	3899.09
21	बोंगईगांव ताप विद्युत परियोजना	01/2008	4375.35	6749.18	2373.83
रेलवे					
22	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
23	जिरिबाम से इम्फाल	04/2003	727.56	6570.75	5843.19

	(तुपुई)(एनएल)(एनईएफआर)				
24	लुमडिंग-सिलचर जिरिबाम, बदरपुर-बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
25	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
26	सीवोक रंगपो, एनईएफआर	04/2008	1339.48	4190.00	2850.52
सड़क परिवहन एवं राजमार्ग					
27	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
28	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
29	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	135.23
30	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी. एनएच-54	12/2003	155.04	280.13	125.09
31	एनडब्ल्यूई एस के तहत एनएच-202 पर अप्रोच रोड सहित वैकटपुरम के समीप गोदावरी नदी पुल का निर्माण	03/2011	218.31	339.82	121.51
पोत परिवहन एवं पत्तन					
32	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	150.00	600.00	450.00
33	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
34	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	232.00
35	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	127.55
इस्पात					
36	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	3599.00
37	सिंटर मशीन -1 और 2का सुधार	12/2009	343.00	488.40	145.40
शहरी विकास					
38	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 789 परियोजनाओं में से, 7 परियोजनाएं समय से पहले चल रही हैं, 139 समय पर तथा 232 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या में 198 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है। इसके अलावा, 31 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 380 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतिम रूप से पूरा होने की अवधि सूचित की गई है। 232 विलंबित परियोजनाओं में से, 50 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 43 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 87 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 52 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.08.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	11/2015	83
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	09/2010	09/2016	72
3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	10/2017	22
4	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	05/2018	17
नागर विमानन					
5	पाकयांग (सिक्किम) हवाई अड्डा में नए हवाई अड्डे का निर्माण	01/2009	01/2011	09/2017	80
6	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) चरण-II	02/2011	03/2015	10/2015	7
7	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	03/2015	09/2015	6
कोयला					
8	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
9	कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड)	01/2005	03/2010	03/2016	72
10	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
11	झंझरा आर-VI सीम पीएसएलडब्ल्यू	11/2006	03/2011	03/2017	72
12	शांतिखानी लौंगवाल परियोजना-एससीसीएल	10/2006	03/2012	03/2018	72

	भारी उद्योग				
13	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
	पेट्रोरसायन				
14	असम गैस क्रैकर परियोजना	04/2006	04/2012	09/2015	41
	पेट्रोलियम				
15	फुलपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	12/2018	71
16	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	12/2009	06/2011	03/2016	57
17	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	03/2016	53
18	2000 एचपी ड्रिलिंग रिंग के 2 संख्या का खरीद	04/2010	06/2012	11/2016	53
19	12 ऑफशोर आपूर्ति उपकरणों की निर्माण (ओएसवी)	06/2007	09/2011	12/2015	51
	विद्युत				
20	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2016	123
21	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
22	कुडनकुलम एपीपी पारेषण प्रणाली (पीजीसीआईएल)	05/2005	11/2008	12/2016	97
23	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	10/2015	94
24	टेहरी पंड भंडारण संयंत्र (1000 मेगावाट)	07/2006	07/2010	05/2018	94
	रेलवे				
25	गोंडिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
26	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	11/2002	12/2018	193
27	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
28	तमलुक-दीघा लाइन दोहरीकरण, (एसईआर)	03/1984	06/2005	12/2019	174
29	बेलापुर-सीवुड-उरान विद्युतीकृत दोहरी लाइन (एमटीपी)	03/1996	03/2004	03/2016	144
	सड़क परिवहन एवं राजमार्ग				
30	नलबारी से बिजनी (एएस-7)	12/2003	04/2008	01/2017	105
31	सोनापुर से गुवाहाटी (एएस-3)	12/2003	03/2008	01/2016	94
32	गुवाहाटी से नलबारी (एएस-5)	12/2003	04/2008	12/2015	92
33	धरमतुल से सोनापुर, 205 किमी.-183 किमी.(एएस-20)	12/2003	05/2008	12/2015	91
34	नलबारी से बिजनी (एएस-6)	12/2003	06/2008	11/2015	89
	पोत परिवहन एवं पत्तन				

35	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	03/2006	12/2015	117
36	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	12/2010	09/2017	81
37	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	12/2010	01/2016	61
इस्पात					
38	बोकारो इस्पात संयंत्र का विस्तार	05/2010	12/2011	08/2015	44
39	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	03/2016	36
40	7.0 एमटीपीए कुमारस्वामी लौह अयस्क खनन परियोजना (एनएमडीसी)	02/2011	05/2013	08/2015	27
41	45 एमवीए साफ्ट से जुड़े दूसरी सुविधाओं की स्थापना	12/2011	10/2013	12/2015	26
42	एसएमएस -1 कन्वर्टर्स सुधार	05/2012	07/2015	03/2017	20
दूरसंचार					
43	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	10/2015	60
शहरी विकास					
44	प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	06/2017	34
45	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	10/2015	29
46	सार्वजनिक ट्रेनिंग (सीएपीटी) भोपाल के लिए सेंट्रल अकादमी का निर्माण	12/2012	12/2014	12/2016	24
47	प्लॉट नं. 4, सेक्टर- 10 द्वारिका नई दिल्ली पर पीएनबी के मुख्य कार्यालय भवन का निर्माण	05/2012	12/2014	04/2016	16
48	हरिघंटा कल्याणी नाडिया में आईआईएसईआर कोलकाता के स्थायी परिसर का निर्माण	02/2014	09/2015	12/2016	15

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल 2015 में, इस मंत्रालय की निगरानी पर चल रहे 758 परियोजनाओं में से, 231 परियोजनाओं के संबंध में लागतवृद्धि तथा 323 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि अगस्त 2015 के दौरान, 789 परियोजनाओं में से 228 परियोजनाओं के संबंध में लागतवृद्धि तथा 232 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है । अप्रैल 2015 की तुलना में,

लागतवृद्धि दर्शाने वाले परियोजनाओं की संख्या 30.47% से घटकर 28.90% हो गई, जबकि समयवृद्धि दर्शाने वाले परियोजनाओं के संबंध में 42.61% से घटकर 29.40% हो गई है।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना उपलब्धियों वाली पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.08.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण	05/2010	335.61	388.53	297.58	05/2012	03/2015

5	गगनपरियोजना	09/2008	626.00	626.00	514.70	06/2013	एनआर
कोयला							
6	मुराईदीह यूजी	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	उत्तरी तीसरा और दक्षिणी तीसरा विस्तार ओसीपी (6 एमटीवाई)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	अमेरा ओसी आरसीई	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	अमृतधारा ओसी परियोजना	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	बिजारी ओसीआरसीई (1.50 एमटीवाई)	05/2014	164.49	164.49	22.10	03/2020	03/2020
उर्वरक							
11	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	197.79	13.09	11/2016	11/2016
भारी उद्योग							
12	राष्ट्रीय ऑटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
खान							
13	मलंजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
पेट्रोलियम							
14	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	एक बहुदेशीय सहायता वेसेल्स का निर्माण	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	बी-173 ए क्षेत्र की विकसित तेल वसूली	01/2012	352.49	352.49	115.81	03/2014	05/2016

विद्युत							
19	बीआरबीसीएल- नबीनगर-जेवी	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	एनपीजीसीपीएल- नबीनगर-जेवी	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	यूआरटीडीएसएम चरण-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	दक्षिणी क्षेत्रकोसुदृढ बनानेकीयोजना-XXII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	किशनगंगा एचईपी के साथ जुडी पारेषण प्रणाली	01/2015	268.80	268.80	0.00	03/2018	03/2018
रेलवे							
24	जिंद-सोनीपत (एनएल), एनआर	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	लिंकड फिंगर के साथ-साथ रंगिया- मूरकौंगस्लेक	01/2004	915.70	3700.00	3198.30	एनआर	03/2015
26	कालीकट-मैंगलोर (डीएल) (एसआर)	02/1996	240.00	579.37	599.40	एनआर	02/2012
27	अहमदनगर-पर्ली वैजनाथ (एनएल),सीआर	02/1997	514.68	2820.00	329.67	एनआर	एनआर
28	दौसा-गंगापुर सीटी (एनएल), एनडब्ल्यूआर	02/1997	410.08	410.08	294.70	एनआर	एनआर
सड़क परिवहन एवं राजमार्ग							
29	छपरा-हाजीपुर की 4 लेनिंग	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	देवली-कोटा	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	जोरबट-बारापानी	01/2011	536.00	536.00	0.00	01/2014	एनआर
32	कांडला-मुंदरा पोर्ट	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	पीएस कानपुर कबराय की 2 लेनिंग	01/2013	373.47	373.47	0.00	07/2014	एनआर
पोत परिवहन एवं पत्तन							
34	सिंगल प्वाइंट मूरिंग (एसपीएम)	02/2011	830.00	621.53	0.00	05/2013	एनआर

	तथा एली की स्थापना करना						
35	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल संपर्क	03/2007	245.67	373.22	373.22	04/2009	एनआर
36	सेतु समुद्रम शिप चैनल परियोजना	06/2005	2427.40	2427.40	831.23	10/2008	एनआर
37	मौजूदा बर्थ एन का संशोधन तथा सुदृढीकरण करना	06/2010	277.00	277.00	0.21	03/2012	एनआर
38	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	एनआर
इस्पात							
39	गैस नेटवर्क बीएसएल	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	आरएसपी में नया एचएसएम	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	24.02	10/2016	10/2016
दूरसंचार							
42	एनएफएस	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	रक्षा क्षेत्र के टेलीकॉम नेटवर्क आवश्यकता का निष्पादन	05/2006	1077.00	1077.00	0.00	03/2009	एनआर
44	असम टेलीकॉम सर्किल, चरण-V.I, 2जीऔर3जी	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	384.00	384.00	55.22	10/2010	09/2015
शहरी विकास							
46	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी प.बं. में शैक्षिक सहित आवासीय परिसर	01/2009	225.81	225.81	0.00	06/2012	06/2015

47	एनआईटी कालीकट केरल के लिए मेगा होस्टल II कनिर्माण	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	आईआईटी हौज खास नई दिल्ली में लेक्चर थियेटर और लैब कॉम्प्लेक्स	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	प्लॉट संख्या सी-41-4 पर आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	बिहटा, पटना आईआईटी के कैम्पस के लिए आवासीय तथा अन्य परिसर	02/2012	171.10	171.10	0.00	09/2014	एनआर

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

9. यह भीपाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानों वाली शुरूआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-08-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	0.00	18271.00
नागरविमानन					
2	पाकयांग (सिक्किम) हवाई अड्डा में नया	01/2009	309.46	0.00	338.82

	हवाई अड्डा				
	कोयला				
3	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3027.59	3207.92
	पेट्रोलियम				
4	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	5925.40
	विद्युत				
5	बाढ़ एसटीपीपी फेज-II	02/2008	7341.04	0.00	8631.00
6	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7687.18
7	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	5040.21
8	किशनगंगा एचईपी (3x110 मेवा)	01/2009	3642.04	0.00	3934.97
9	छत्तीसगढ़ में आईपीपीएस जेनरेशन परियोजनाओं के लिए डब्ल्यूआर के पश्चिमी भाग में पारेषण प्रणाली का सुदृढीकरण	11/2011	2127.51	0.00	2172.33
10	तीस्ता लो डैम एचईपी चरण-IV (4X40 मेवा) (एनएचपीसी)	09/2005	1061.38	0.00	1742.55
	रेलवे				
11	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10658.34
12	लुमडिंग-सिलचर-जिरिबम बदरपुर-बराईग्राम-कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	0.00	4734.45
13	दमदम-नावपारा और नावपारा-एनएससीपी एयरपोर्ट तक विस्तार के साथ टॉलीगंज-गरिया (एमटीपी)	03/2000	1049.69	3385.14	3541.20
14	बोगीबिल तथा लिंक लाइनों पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	1000.00	3410.06
15	लिव्क फिंगर्स के साथ रंगिया-मुर्कोंगसलेक एनईएफआर	01/2004	915.70	915.70	3198.30
	सड़क परिवहन एवं राजमार्ग				
16	पानीपत-जालंधर 6 लेन(96 किमी. से 387.1 किमी.)	05/2009	1108.00	0.00	3466.00
17	नागपुर-बेतुल के 4 लेनिंग	02/2011	2498.76	0.00	2786.00
18	सूरत-दहिसर (छः लेन) 263 किमी. से 502 किमी.	02/2009	1693.75	0.00	2762.00
19	गाजियाबाद-अलीगढ़एनएच-91	02/2011	1141.00	0.00	2445.00
20	मुरादाबाद-बरेली	04/2010	1267.00	0.00	2425.00
	पोत परिवहन एवं पतन				
21	कोचीन पोर्ट्स के बल्लापड़म में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	0.00	373.22

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.08.2015 की स्थिति के अनुसार)

क्र. सं.	क्षेत्र/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	गगनपरियोजना	09/2008	06/2013	एनआर	06/2013
2	वीएसआई हवाई अड्डे, पोर्ट ब्लेयर में नए एकीकृत टर्मिनल भवन का निर्माण	10/2013	एनआर	एनआर	एनआर
कोयला					
1	शांतिखानी लौंगवॉल परियोजना-एससीसीएल	10/2006	03/2012	एनआर	एनआर
2	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एनआर	एनआर
3	रामागुंडम ओसी।। विस्तार	12/2009	03/2012	एनआर	एनआर
4	मुराड्डीह यूजी टर्नकी परियोजना	02/2011	04/2014	एनआर	04/2014
5	कृष्णाशिला (एनसीएल) (4एमटीवाई)	06/2011	03/2013	एनआर	03/2014
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	एनआर	एनआर
पेट्रोलियम					
1	एन्नोर में नई विपणन टर्मिनल	11/2006	एनआर	एनआर	एनआर
2	बीपीसीआर/एचपीसीआरसे उरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण के लिए पाइपलाइन	08/2009	08/2012	एनआर	एनआर
3	एन्नोर-त्रिची-मदुरै एलपीजी पाइपलाइन	05/2013	एनआर	एनआर	एनआर
विद्युत					

1	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2009	एनआर
2	कुंडनकुलम एपीपी ट्रांस प्रणाली (पीजीसीआईएल)	05/2005	09/2008	एनआर	03/2013
3	एसआरकी प्रणाली सुदृढीकरण-XII	02/2010	06/2012	एनआर	एनआर
4	आंध्र प्रदेश भाग-ए1 के वैमागिरी क्षेत्र में आईएसजीएस परियोजनाओं से जुड़ी सामान्य प्रणाली	03/2012	06/2014	एनआर	एनआर
रेलवे					
1	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एनआर	एनआर
2	गजोली-ईटाहर (एनएल), एनईएफआर सहित एकलाखी-बालुरघाट से नई बीजी रेलवे लाइन	04/1983	एनआर	एनआर	एनआर
3	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	06/2005	07/2011	एनआर
4	नामखाना चंद्रनगर काकद्वीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एमएम	04/1987	एनआर	एनआर	एनआर
5	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	एनआर	03/2010	एनआर
सड़क परिवहन एवं राजमार्ग					
1	लखनऊ-रायबरेली	07/1999	07/2012	एनआर	09/2014
2	दीवापुरसे यूपी/बिहारसीमा (एलएमएनएचपी-9) एनएच-28, किमी.402-360.915	12/2003	10/2008	एनआर	एनआर
3	सिलिगुडी से इस्लामपुर (पश्चिमबंगाल-7)	12/2003	07/2008	एनआर	एनआर
4	नलबाड़ी सेबिजनी (एएस-8)	12/2003	06/2008	एनआर	एनआर
5	पिंपलगांव-नासिक-गोंडी, एनएच-3 (एनएचडीपीचरणIII)	03/2005	07/2012	एनआर	07/2012
पोत परिवहन एवं पत्तन					
1	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	02/2011	एनआर	12/2012
2	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	11/2010	एनआर
3	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत करना	10/2005	10/2008	एनआर	एनआर
4	पारादीप बंदरगाह पर चैनल का सुदृढीकरण	12/2005	एनआर	01/2009	12/2010
5	कांडला में 13 और 14 कार्गो बर्थ का निर्माण	12/2005	03/2011	एनआर	03/2013
शहरी विकास					
1	सैन्य रक्षा मंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय का निर्माण	08/2005	08/2007	एनआर	एनआर
2	बंगलोर मेट्रो रेल परियोजना	05/2006	06/2011	एनआर	03/2013
3	बांद्रा कुर्ली कॉम्प्लेक्स, मुंबई में आईडीबी आई के लिए कार्यालय भवन का निर्माण	11/2006	04/2009	एनआर	एनआर

4	एनआईटी कालीकट केरल के लिए मेगा हॉस्टल II का निर्माण	01/2010	10/2012	एनआर	एनआर
5	आईआईटी हॉजखास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	एनआर	07/2012

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार कार्यशुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

- i) विद्युत क्षेत्र में, 108 परियोजनाओं में से, 62 परियोजनाएं विलंबित हैं। माह के दौरान, 22 परियोजनाओं के संबंध में 1-9 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 22 परियोजनाओं में से, 12 परियोजनाएं मेगा परियोजनाएं हैं। 3 परियोजनाएं 'कुडनकुलम एपीपी पारेषण प्रणाली, पीजीसीआईएल', 'मुंद्रा अल्ट्रा मेगा विद्युत परियोजना से जुड़े पारेषण प्रणाली, पीजीसीआईएल' और 'पश्चिम बंगाल के उत्तरी भाग में पूर्लिंग स्टेशन के विकास के लिए पारेषण प्रणाली तथा विद्युत का हस्तांतरण, पीजीसीआईएल' के संबंध में क्रमशः गंभीर आरओडब्ल्यू समस्याएं, वन संबंधी अनुमति (चरण-I प्रतीक्षित) और पुनतसांगचू-अलीपुरदुवार लाइन के लिए प्रतीक्षित वन्य जीव अभ्यारण्य संबंधी अनुमति में प्रत्येक में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 1 परियोजना 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना XVI, पीजीसीआईएल' के संबंध में वन संबंधी अनुमति में विलंब तथा वर्ष से ढके हुए क्षेत्र होने के कारण सीमित कार्य अवधि के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 2 परियोजनाएं 'छत्तीसगढ़ में आईपीपी परियोजना के लिए पश्चिम क्षेत्र के उत्तर/पश्चिम भाग में प्रणाली सुदृढीकरण, पीजीसीआईएल' तथा 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना XVII, पीजीसीआईएल के संबंध में क्रमशः वन संबंधी अनुमति में विलंब तथा गंभीर आरओडब्ल्यू समस्या, दुलहस्ती-किशनपुर के पूरा किए जाने में बादल फटने के प्रभाव के कारण प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 9 परियोजनाएं 'पश्चिमी क्षेत्र सुदृढीकरण योजना V पीजीसीआईएल', 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना XVIII, पीजीसीआईएल', 'पल्लटाना जीबीपीपी और बीपीटीएस से जुड़े पारेषण प्रणाली, पीजीसीआईएल', 'छत्तीसगढ़ में आईपीपीएस जनरेशन परियोजनाओं के लिए पश्चिमी क्षेत्र के पश्चिमी भाग में पारेषण प्रणाली सुदृढीकरण, पीजीसीआईएल' 'झारखंड और पश्चिम बंगाल भाग ए-2 में चरण-I जनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल', 'एस्सार पावर गुजरात लि. के कनेक्टिविटी के लिए पारेषण प्रणाली, पीजीसीआईएल', छत्तीसगढ़ में आईपीपी परियोजनाओं के

लिए राइलपुर-वर्धा में प्रणाली सुदृढीकरण, पीजीसीआईएल', झारखंड व पश्चिम बंगाल भाग ख में जनरेशन परियोजनाएं चरण-I के लिए पारेषण प्रणाली, पीजीसीआईएल', उत्तरी क्षेत्रीय प्रणाली सुदृढीकरण योजना XXV, पीजीसीआईएलके संबंध में गंभीर आरओडब्ल्यू समस्या, स्थानीय अशांति, एनईआर में भू-वैज्ञानिक गतिविधियां, वन संबंधी अनुमति तथा भूमि अधिग्रहण में विलंब आदि के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; एक परियोजना 'सिक्किम से एनआर/डब्ल्यूआर भाग-क में जनरेशन परियोजना से विद्युत का हस्तांतरण के लिए पारेषण प्रणाली, पीजीसीआईएल' के संबंध में किशनगंज सब-स्टेशन के भूमि अधिग्रहण में विलंब होने के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 2 परियोजनाएं 'त्रिपुरा गैस आधारित विद्युत परियोजना, नीपको और 'कृष्णपट्टनम यूएमपीपी से जुड़े पारेषण प्रणाली- भाग-ख, पीजीसीआईएल'के संबंध में ओएनजीसी द्वारा गैस की अपेक्षित मात्रा की आपूर्ति नहीं होने और गंभीर आरओडब्ल्यू समस्या के कारण प्रत्येक में क्रमशः 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 4 परियोजनाएं 'पूर्वी क्षेत्रीय सुदृढीकरण योजना IX पीजीसीआईएल', उत्तरी क्षेत्रीय प्रणाली सुदृढीकरण योजना-XVIII, पीजीसीआईएल', 'दक्षिणी क्षेत्रीय ग्रिड में प्रणाली सुदृढीकरण-XVII, पीजीसीआईएल' और डब्ल्यूआर तथा एनआर (लाइनबेज और रिएक्टर प्रोविजन) के लिए सामान्य सुदृढीकरण प्रणाली, पीजीसीआईएल'के संबंध में प्रत्येक में 4 माह, 3 माह, 1 माह और 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

- ii) कोयला क्षेत्र में, 80 परियोजनाओं में से 44 परियोजनाएं विलंबित हैं।** माह के दौरान, 5 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 5 परियोजनाओं में से, 1 परियोजना 'तूतीकोरिन ताप विद्युत परियोजना-2X500 मेवा., एनएलसी', मेगा परियोजना है। परियोजनाएं 'मानिकपुर ओसी विस्तार (3.5 एमटीवाई), एसईसीएल' के संबंध में प्रत्येक में 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पूर्णाडीह ओसीपी (3.0 एमटीवाई), सीसीएल' के संबंध में प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है); परियोजनाएं 'तूतीकोरिन ताप विद्युत परियोजना-2X500 मेवा., एनएलसी' और 'विंड पावर प्रोजेक्ट कझुनीरकुलम, तमिलनाडु, एनएलएस' के संबंध में क्रमशः ठेकेदार द्वारा अपर्याप्त संसाधन जुटाने तथा उपस्करों की आपूर्ति में विलंब के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

iii) पेट्रोलियम क्षेत्र में, 69 परियोजनाओं में से, 41 परियोजनाएं विलंबित हैं। माह के दौरान, 4 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 4 परियोजनाओं में से, 3 परियोजनाएं मेगा परियोजनाएं हैं; परियोजना '2000 एचपी ड्रिलिंग रिग के संख्या 2 के खरीद, ऑयल' के संबंध में ड्रिलिंग रिग्स संबंधी आदेश जारी करने में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'मंगलौर में सामरिक कच्चा तेल भंडारण उत्पाद, आईएसपीआरएल' और पादुर में सामरिक कच्चा तेल भंडारण उत्पाद, आईएसपीआरएल' में कैवर्न स्वीकृति जांच के दौरान सामना किए गए समस्याएं, जो प्रगति में हैं और अवधि के दौरान भारी वर्षा के कारण धीमी प्रगति में हैं, के संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'मुंबई रिफाइनरी में सीडीयू/वीडीयू के प्रतिस्थापन, बीपीसीएल' के संबंध में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

iv) सड़क परिवहन तथा राजमार्ग क्षेत्र में, 158 परियोजनाओं में से, 17 परियोजनाएं विलंबित हैं। माह के दौरान, 3 परियोजनाओं के संबंध में 2-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजनाएं 'नलबाड़ी से बिजनी (एस-7), एनएचएआई'; परियोजना 'नलबाड़ी से बिजनी (एस-6), एनएचएआई' और धरमतुल से सोनारपुर 205-183 किमी (एस-20), एनएचएआई' के संबंध में क्रमशः 12 माह, 3 माह और 2 माह के अतिरिक्त विलंब की सूचना प्राप्त होती है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

v) नागर विमानन क्षेत्र में, 6 परियोजनाओं में से, 3 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना 'चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डा (मोहाली) का विकास चरण-II, एएआई' के संबंध में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

vi) दूरसंचार क्षेत्र में, 2 परियोजनाओं में से, 1 परियोजना विलंबित है। माह के दौरान, 1 परियोजना 'टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन, बीएसएनएल' के संबंध में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

- vi) परमाणु ऊर्जा क्षेत्र में,** 4 परियोजनाओं में से, सभी 4 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना के संबंध में अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'कुडनकुलम एपीपी (एनपीसीआईएल), एनपीसीआईएल' के संबंध में मेसर्स एटमस्ट्रोयएक्सोर्ट, रसियन फेडरेशन द्वारा प्रतिबद्धताओं को न निभाने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।
12. रेलवे मंत्रालय ने इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी चल रही परियोजनाओं संबंधी मासिक स्थिति रिपोर्टों को प्रस्तुत करना बंद कर दिया है। अतः, उपलब्ध सूचना/आंकड़े (जनवरी 2015 की स्थिति के अनुसार) का उपयोग रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में किया गया है।
 13. भारतीय राष्ट्रीय राजमार्ग प्राधिकरणद्वारा 158 सड़क क्षेत्र परियोजनाओं संबंधी सूचना/आंकड़े को ऑनलाइन अद्यतन नहीं किया गया है।
 14. दिनांक 31.08.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।
 15. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for August 2015 contains information on the status of the 789 Central Sector Infrastructure Projects costing ₹150 crore and above. During August 2015, 11 projects (4 projects each in Power and Petroleum sector, 2 projects in Coal and 1 project in Civil Aviation sector) have reported completion.

2. During the reference month, out of 789 projects, 232 projects are delayed with respect to original schedule and 37 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 37 projects, 17 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	RAILWAYS	296	31	0	0
2	ROAD TRANSPORT AND HIGHWAYS	158	17	3	0
3	POWER	108	62	22	12
4	PETROLEUM	69	41	4	3
5	COAL	80	44	5	1
6	URBAN DEVELOPMENT	30	13	0	0
7	STEEL	26	11	0	0
8	CIVIL AVIATION	6	3	1	0
9	SHIPPING AND PORTS	6	3	0	0
10	ATOMIC ENERGY	4	4	1	1
11	TELECOMMUNICATIONS	2	1	1	0
12	FERTILISERS	1	0	0	0
13	MINES	1	0	0	0
14	PETROCHEMICALS	1	1	0	0
15	HEAVY INDUSTRIES	1	1	0	0
Total		789	232	37	17

3. Total original cost of implementation of the 789 projects was ₹10,58,599.45 crore and their anticipated completion cost is likely to be ₹12,62,592.29 crore, which reflects overall cost overruns of ₹2,03,992.84 crore (19.27% of original cost). The expenditure incurred on these projects till August 2015 is ₹5,18,326.58 crore, which is 41.05% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost

Overruns (as on 31-8-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
2	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	31.12
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	15.77
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	8.19
COAL					
5	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	76.47
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	34.63
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
9	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
HEAVY INDUSTRY					
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
11	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	80.08
PETROLEUM					
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
14	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
15	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	12/2009	309.81	462.79	49.38
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	45.83
POWER					
17	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
18	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	16885.00	168.64
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	159.38
20	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	159.15
21	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.68	139.35
RAILWAYS					
22	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
23	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62

24	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
25	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
26	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
ROAD TRANSPORT AND HIGHWAYS					
27	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
29	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
30	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	68.99
31	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	55.66
SHIPPING AND PORTS					
32	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
33	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
34	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	51.92
35	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	18.89
STEEL					
36	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
37	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	41.41
URBAN DEVELOPMENT					
38	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 31-8-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	4099.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					

3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	52.92
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	37.00
COAL					
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	1698.20
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	1552.99
7	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
8	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	48.00
HEAVY INDUSTRY					
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
11	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	4372.91
PETROLEUM					
12	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
13	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
14	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	12/2012	3513.07	4619.94	1106.87
15	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	05/2013	4124.35	4941.49	817.14
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
POWER					
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	16885.00	10599.67
18	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	3979.44
20	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7818.68	3899.09
21	BONGAIGAN THERMAL POWER PROJECT	01/2008	4375.35	6749.18	2373.83
RAILWAYS					
22	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
23	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
24	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
25	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
26	SEVOK RANGPO, NEFR	04/2008	1339.48	4190.00	2850.52
ROAD TRANSPORT AND HIGHWAYS					
27	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
30	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
31	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	121.51

SHIPPING AND PORTS					
32	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
33	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
34	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	232.00
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	127.55
STEEL					
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	3599.00
37	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
URBAN DEVELOPMENT					
38	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 789 projects, 7 projects are ahead of schedule, 139 are on schedule and 232 are delayed with respect to their original schedule. However, the number of delayed projects decreases to 198 if delay is calculated on the basis of latest schedule of completion. Further, 31 projects have been sanctioned without original commissioning schedule date and for 380 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 232 delayed projects, 50 projects have overall delay in the range of 1 to 12 months, 43 projects have delay in the range of 13 to 24 months, 87 projects have delay in the range of 25 to 60 months and 52 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)

(as on 31-8-2015)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	11/2015	83
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	05/2018	17
CIVIL AVIATION					
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	03/2015	10/2015	7

7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	09/2015	6
COAL					
8	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
9	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2016	72
10	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
11	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2017	72
12	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2018	72
HEAVY INDUSTRY					
13	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	12/2017	75
PETROCHEMICALS					
14	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	09/2015	41
PETROLEUM					
15	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
16	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	03/2016	53
18	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	04/2010	06/2012	11/2016	53
19	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	12/2015	51
POWER					
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
21	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
22	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2016	97
23	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	10/2015	94
24	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	07/2010	05/2018	94
RAILWAYS					
25	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
26	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
27	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
28	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
29	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2016	144
ROAD TRANSPORT AND HIGHWAYS					
30	NALBARI T BIJNI (AS-7)	12/2003	04/2008	01/2017	105
31	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	01/2016	94
32	GUWAHATI TO NALBARI (AS-5)	12/2003	04/2008	12/2015	92
33	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	12/2015	91
34	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	11/2015	89
SHIPPING AND PORTS					
35	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	12/2015	117

36	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	12/2010	09/2017	81
37	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	01/2016	61
STEEL					
38	EXPANSION OF BOKARO STEEL PLANT	05/2010	12/2011	08/2015	44
39	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	03/2016	36
40	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	08/2015	27
41	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	12/2015	26
42	SMS-1 CONVERTERS REVAMPING	05/2012	07/2015	03/2017	20
TELECOMMUNICATIONS					
43	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	10/2010	10/2015	60
URBAN DEVELOPMENT					
44	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	06/2017	34
45	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	10/2015	29
46	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	12/2014	12/2016	24
47	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	05/2012	12/2014	04/2016	16
48	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	02/2014	09/2015	12/2016	15

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during August 2015, out of 789 projects, 228 projects reported cost overruns and 232 projects reported time overruns. In comparison to April 2015, number of **projects** reporting **cost overruns** has gone **down** from **30.47%** to **28.90%** whereas **projects** reporting **time overruns** have **decreased** from **42.61%** to **29.40%**.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones is as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-8-2015)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	GAGAN PROJECT	09/2008	626.00	626.00	514.70	06/2013	N.R.
COAL							
6	MURAI DIH UG	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	AMERA OC RCE	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	AMRITDHARA OC PROJECT	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	BIJARI OC RCE (1.50 MTY)	05/2014	164.49	164.49	22.10	03/2020	03/2020
FERTILISERS							
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	197.79	13.09	11/2016	11/2016
HEAVY INDUSTRY							
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
13	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
PETROLEUM							
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	944.84	10/2011	10/2015

15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	IMPROVED OIL RECOVERY OF B-173A FIELD	01/2012	352.49	352.49	115.81	03/2014	05/2016
POWER							
19	BRBCL-NABINAGAR - JV	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	NPGCPL-NABINAGAR - JV	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	URTDSP PHASE-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	01/2015	268.80	268.80	0.00	03/2018	03/2018
RAILWAYS							
24	JIND-SONEPAT (NL),NR	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER	01/2004	915.70	3700.00	3198.30	N.R.	03/2015
26	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	579.37	599.40	N.R.	02/2012
27	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	514.68	2820.00	329.67	N.R.	N.R.
28	DAUSA-GANGAPUR CITY(NL),NWR	02/1997	410.08	410.08	294.70	N.R.	N.R.
ROAD TRANSPORT AND HIGHWAYS							
29	4-LANNING OF CHAPRA-HAJIPUR	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	DEOLI-KOTA	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	JORBAT - BARAPANI	01/2011	536.00	536.00	0.00	01/2014	N.R.
32	KANDLA - MUNDRA PORT	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	2 LANING WITH PS KANPUR KABRAI	01/2013	373.47	373.47	0.00	07/2014	N.R.
SHIPPING AND PORTS							
34	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIE	02/2011	830.00	621.53	0.00	05/2013	N.R.
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	373.22	373.22	04/2009	N.R.
36	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	N.R.
37	MODIFICATION AND STRENGTHENING OF EXISTING BERTH N	06/2010	277.00	277.00	0.21	03/2012	N.R.
38	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE	10/2002	150.00	600.00	139.80	03/2006	N.R.
STEEL							
39	GAS NETWORK BSL	03/2015	255.19	255.19	0.00	03/2018	03/2018

40	NEW HSM AT RSP	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	24.02	10/2016	10/2016
TELECOMMUNICATIONS							
42	NFS	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE	05/2006	1077.00	1077.00	0.00	03/2009	N.R.
44	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	55.22	10/2010	09/2015
URBAN DEVELOPMENT							
46	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-4	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	171.10	0.00	09/2014	N.R.

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-8-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	0.00	18271.00
CIVIL AVIATION					
2	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	338.82
COAL					
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3027.59	3207.92
PETROLEUM					
4	DEVELOPMENT OF B-193 CLUSTER	06/2007	3248.78	5633.44	5925.40

	FIELDS				
	POWER				
5	BARH STPP STAGE -II	02/2008	7341.04	0.00	8631.00
6	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7687.18
7	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5040.21
8	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	3934.97
9	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	11/2011	2127.51	0.00	2172.33
10	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1742.55
	RAILWAYS				
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
12	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	0.00	4734.45
13	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1049.69	3385.14	3541.20
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	1000.00	3410.06
15	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	01/2004	915.70	915.70	3198.30
	ROAD TRANSPORT AND HIGHWAYS				
16	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	0.00	3466.00
17	4 LANING OF NAGPUR-BETUL	02/2011	2498.76	0.00	2786.00
18	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2762.00
19	GHAZIABAD-ALIGARH NH-91	02/2011	1141.00	0.00	2445.00
20	MURADABAD-BAREILY	04/2010	1267.00	0.00	2425.00
	SHIPPING AND PORTS				
21	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	0.00	373.22

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31-8-2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
	COAL				
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.

3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURAIIDH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013
3	SYSTEM STRENGTHENING -XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.
3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.
4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010
5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013

URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Power Sector**, out of 108 projects, 62 projects are delayed. During the month, 22 projects have reported additional delay in the range of 1-9 months. Out of 22 projects, 12 are mega projects. 3 projects 'Kunadankulam APP Transmission System, PGCIL', 'Transmission System Associated with Mundra Ultra Mega Power Project, PGCIL' and 'Transmission System for Development of Pooling Station in NR Part of West Bengal and Transfer of Power, PGCIL' have reported additional delay of 9 months each due to severe ROW problem, forest clearance (Stage-I awaited) and Wildlife Sanctuary Clearance awaited for Punatsangchu- Alipurduar line respectively.; 1 project 'Northern Region System Strengthening Scheme XVI, PGCIL' has reported additional delay of 7 months due to delay in forest clearance and limited working period due to snowbound area.; 2 projects 'System Strengthening in North/ West Part of WR for IPP Projects in Chattisgarh, PGCIL' and 'Northern Region System Strengthening Scheme XXIV, PGCIL' have reported additional delay of 6 months each due to delay in forest clearance and severe ROW problem, effects of cloud bursts on the completion of Dulhasti-Kishanpur respectively; 9 projects 'Western Region Strengthening Scheme V, PGCIL', 'Northern Region System Strengthening Scheme XVIII, PGCIL', 'Transmission System Associated with Pallatana GBPP and BPTS, PGCIL', 'Transmission System Strengthening in Western Part of WR for IPPS Generation Projects in Chattisgarh, PGCIL', 'Transmission System for Phase-I Generation Projects in Jharkhand and West Bengal Part A-2, PGCIL', 'Transmission System For Connectivity of Essar Power Gujarat Ltd, PGCIL', 'System Strengthening in Railpur Wardha Corridor For IPP Projects in Chattisgarh, PGCIL', 'Transmission System for Phase-I Generation Projects in Jharkhand and West Bengal Part B, PGCIL', 'Northern Region System Strengthening Scheme XXV, PGCIL' have reported additional delay of 3 months each due to severe

ROW problem, local disturbance, geographical constraints in NER, delay in forest clearance and land acquisition; 1 project 'Transmission System For Transfer of Power From Generation Project in Sikkim to NR/WR Part – A, PGCIL' has reported additional delay of 2 months due to delay in land acquisition of Kishanganj Sub-station; 2 projects 'Tripura Gas Based Power Project, NEEPCO' and 'Transmission System Associated With Krishnapatnam UMPP – Part –B, PGCIL' have reported additional delay of 1 month each due to non-supply of requisite quantum of gas by ONGC and severe ROW problem respectively; 4 projects 'Eastern Region Strengthening Scheme IX, PGCIL', 'Northern Region System Strengthening Scheme XXVIII, PGCIL', 'System Strengthening-XVII in Southern Regional Grid, PGCIL' and 'System Strengthening Common For WR And NR (Line Bays And Reactor Provision), PGCIL' have reported additional delay of 4 months, 3 months, 1 month and 1 month (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).

- ii) In the **Coal Sector**, out of 80 projects, 44 projects are delayed. During the month, 5 projects have reported additional delay in the range of 1-24 months. Out of 5 projects, 1 project 'Tuticorin Thermal Power Project- 2X500 MW, NLC' is mega project. The projects 'Manikpur OC Expansion (3.5 MTY), SECL' and 'Baroud OC Expansion (RCE) -3.5 MTY, SECL' have reported additional delay of 24 months each; the project 'Purnadih OCP (3.0 MTY), CCL' has reported additional delay of 12 months. (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects); The projects 'Tuticorin Thermal Power Project- 2X500 MW, NLC' and 'Wind Power Project, Kazhuneerkulam, Tamilnadu, NLS' have reported additional delay of 1 month each due to inadequate mobilization by the contractor and delay in supply of equipments respectively.
- iii) In the **Petroleum Sector**, out of 69 projects, 41 projects are delayed. During the month, 4 projects have reported additional delays in the range of 1-12 months. Out of 4 projects, 3 projects are mega project; the project 'Purchase of 2 Nos. of 2000 HP Drilling RIG, OIL' has reported additional delay of 12 months due to delay in placement of order for drilling rigs. The project 'Strategic Crude Oil Storage Product at Mangalore, ISPRL' and 'Strategic Crude Oil Storage Product at Padur, ISPRL' have reported additional delay of 2 months each due to difficulties faced during Cavern acceptance test, which is in progress and slow progress due to heavy rains during the period. The project 'Replacement of CDU/VDU at Mumbai Refinery, BPCL' has reported additional delay of 1 month. (however, no specific reason has been reported by the project implementing agency for the delay in project).

- iv) In the **Road Transport & Highways Sector**, out of 158 projects, 17 projects are delayed. During the month, 3 project has reported additional delay in the range of 2-12 months. The Projects 'Nalbari to Bijni (AS-7), NHAI'; the project 'Nalbari to Bijni (AS-6), NHAI' and Dharamtul to Sonarpur, KM 205-183 (AS-20), NHAI' have reported additional delay of 12 months, 3 months and 2 months respectively. (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).
- v) In the **Civil Aviation Sector**, out of 6 projects, 3 projects are delayed. During the month, 1 project 'Development of Chandigarh International airport (Mohali) Ph-II, AAI' has reported additional delay of 3 months. (however, no specific reason has been reported by the project implementing agency for the delay in project).
- vi) In the **Telecommunications Sector**, out of 2 projects, 1 project is delayed. During the month, 1 project 'ERP Implementation in BSNL on Turnkey Basis, BSNL' has reported additional delay of 1 month. (however, no specific reason has been reported by the project implementing agency for the delay in project).
- vii) In the **Atomic Energy Sector**, out of 4 projects, all the 4 projects are delayed . During the month, 1 project has reported additional delay. The Project 'Kudankulam App (NPCIL), NPCIL' has reported additional delay of 1 month due to slippage of commitments by M/s Atomstroyexport, Russian Federation.

12. Ministry of Railway has **discontinued** the practice of furnishing monthly status reports on all on-going projects being implemented by Railways to this Ministry. Therefore, the available information/data (**as on January 2015**) has been used in respect of all projects of Railways sector.

13. The information/data of 158 Road Sector Projects have not been updated online by the NHAI.


14. The status as on 31.08.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

15. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	296	0
2	ROAD TRANSPORT AND HIGHWAYS	158	3
3	POWER	108	22
4	COAL	80	5
5	PETROLEUM	69	4
6	URBAN DEVELOPMENT	30	0
7	STEEL	26	0
8	CIVIL AVIATION	6	1
9	SHIPPING AND PORTS	6	0
10	ATOMIC ENERGY	4	1
11	TELECOMMUNICATIONS	2	1
12	FERTILISERS	1	0
13	MINES	1	0
14	PETROCHEMICALS	1	0
15	HEAVY INDUSTRY	1	0
	Total	789	37

Sectoral break up of on-going infrastructure projects

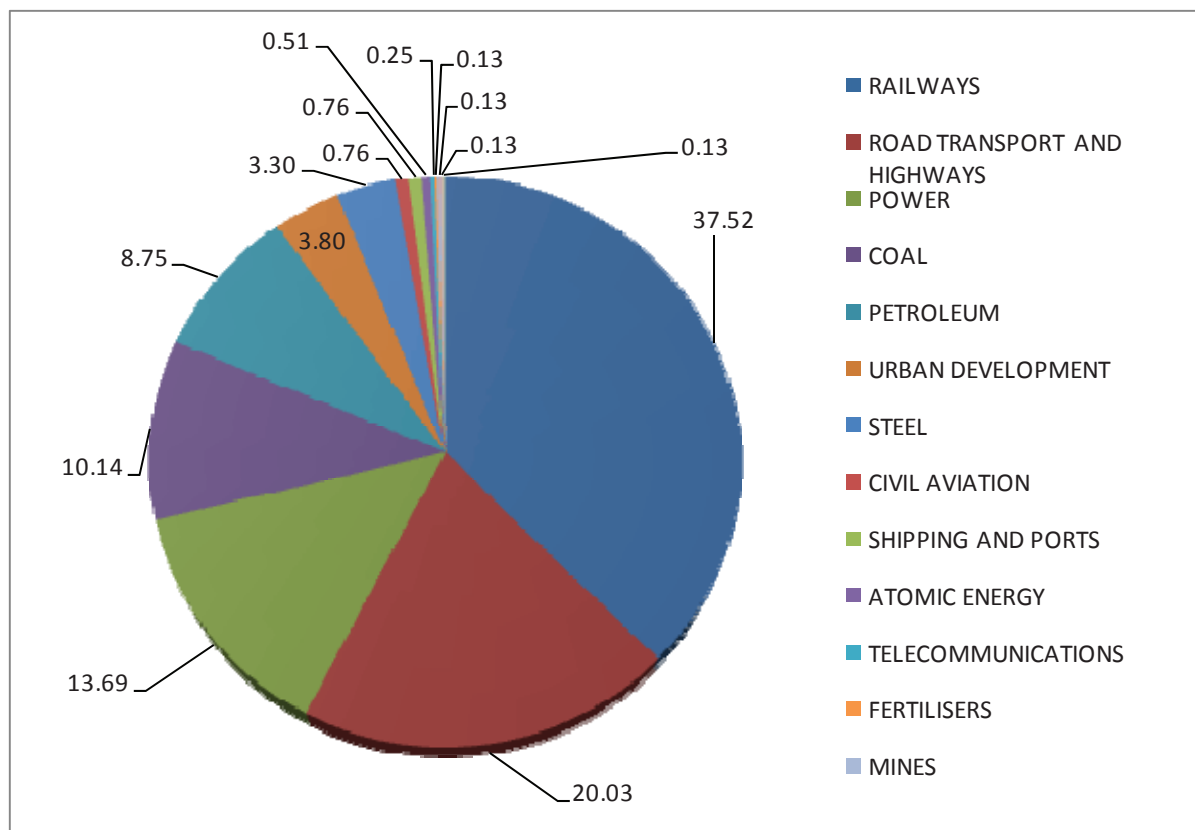

Month wise List of Completed Projects Costing Rs. 150 crore and above during 2015-16

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April, 2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170] <u>ROAD TRANSPORT AND HIGHWAYS</u>	276.26	12/2015	241.63
2	PUNE-SHOLAPUR, PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May, 2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
	June, 2015			
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during 2015-16

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	July,2015			
	<u>STEEL</u>			
15	AUGMENTATION OF IRON ORE STORAGE IN RMHP (RASTRIYA ISPAT NIGAM LIMITED) - [N12000053]	480.00	09/2009	388.52
	<u>PETROLEUM</u>			
16	SURAT PARADIP PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000163]	10,281.00	04/2015	1.49
	<u>POWER</u>			
17	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000130]	1,263.26	11/2014	1,131.58
	August,2015			
	<u>CIVIL AVIATION</u>			
18	GAGAN PROJECT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000065]	626.00	06/2013	483.53
	<u>COAL</u>			
19	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) (NEYVELI LIGNITE CORPORATION) - [060100087]	2,030.78	06/2009	3,215.91
20	TUTICORIN THERMAL POWER PROJECT- 2X500 MW (NEYVELI LIGNITE CORPORATION) - [N06000047]	4,904.54	03/2012	6,426.43
	<u>PETROLEUM</u>			
21	DEVELOPMENT OF G1 AND GS-15 (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100231]	429.82	04/2006	3,439.38
22	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000098]	288.04	08/2012	229.16
23	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000123]	331.20	08/2013	190.04
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000156]	672.00	10/2011	1,082.12
	<u>POWER</u>			
25	BARH STPP STAGE -II (NATIONAL THERMAL POWER CORPORATION) - [N18000047]	7,341.04	10/2013	8,962.00
26	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000076]	4,672.99	11/2012	3,769.57
27	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000096]	2,569.25	03/2014	2,876.57
28	VINDHYACHAL STPP STAGE-V (NATIONAL THERMAL POWER CORPORATION) - [N18000134]	3,180.40	08/2015	2,042.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2015-16

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2015			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000170]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N24000127]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000127]	2,913.10	05/2016	13.86
	June,2015			
7	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000136]	2,913.10	05/2016	13.86
8	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N26000062]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
9	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N12000074]	1,077.00	03/2009	.00
	August,2015			
	<u>SHIPPING AND PORTS</u>			
10	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N12000075]	277.00	03/2012	.21
11	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [180100211]	830.00	05/2013	.00


Summary of projects in the Flash Report for the month of August, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	769
Number of Projects completed/dropped/frozen in Current Month	13
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	32
Number of Projects in Current Month	789


Brief Analysis

Project Status with respect to Original Schedule: Out of 789 projects, 7 projects are ahead of schedule, 139 projects are on schedule 232 projects are delayed. 380 projects do not have fixed dates of commissioning. 31 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

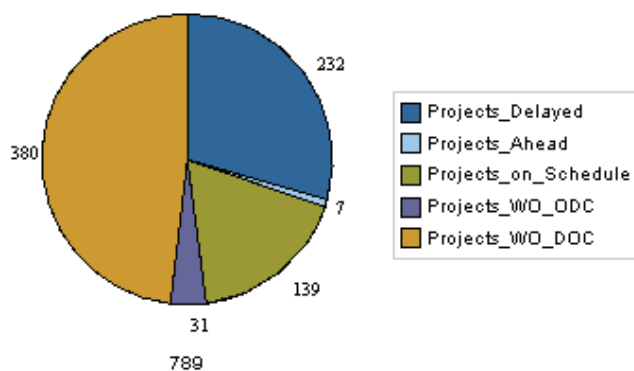

Investment Scenario

Total original cost of implementation of 789 projects when sanctioned, was of the order of Rs. 1058599.45 crore but this was subsequently revised to Rs. 1262592.29 crore implying a cost overrun of 19.3%. The expenditure incurred on these projects till August, 2015 is Rs. 518326.58 crore, which is 41.1% of the revised cost of the projects.

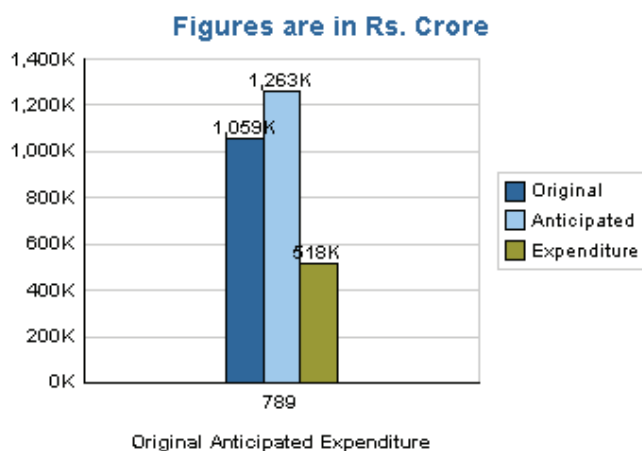

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	769
No of Projects Completed/Dropped/Frozen in Current Month	13
No of Project elevated to Major project	1
No of Projects added in Current Month	32
No of Projects in Current Month	789

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	232	7	139	31	380	789	29.40
Latest Approved (Date)	198	7	173	31	380	789	25.10

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	672	8,60,977.13	9,49,487.40	3,32,747.69	35.00	88,510.27	10.30
Project with Revision in Cost	117	2,58,845.99	3,13,104.89	1,85,578.89	59.30	54,258.90	21.00
Total	789	11,19,823.12	12,62,592.29	5,18,326.58	41.05	142769.17	12.75
Original Cost of All Projects							
Original Cost	789	10,58,599.45	12,62,592.29	5,18,326.58	41.05	2,03,992.84	19.27

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	232	485,417.23	596,575.83	342,115.00	57.30	111,158.60	22.90
Latest Approved (RCE)	198	448,364.86	509,158.34	308,818.47	60.70	60,793.48	13.60
Total	430	933,782.09	1,105,734.17	650,933.47	58.87	171952.08	18.41

Additional Delayed Project cost						
(All Cost/ Expenditure in Rs. crore)						
					Cost overrun	
No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
37	56,885.87	65,489.74	59,404.04	90.70	8,603.87	15.10
37	56,885.87	65,489.74	59,404.04	90.71	8603.87	15.12

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Cost overrun ^ (%)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	37.71
2	CIVIL AVIATION	6	1,973.56	2,063.48	4.56	2	787.61	877.53	11.42
3	COAL	80	61,374.97	65,278.13	6.36	6	8,208.23	12,579.39	53.25
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	26	66,135.16	69,879.56	5.66	2	9,035.00	12,779.40	41.44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	80.08
8	PETROLEUM	69	148,572.08	159,409.56	7.29	16	65,744.28	78,145.54	18.86
9	POWER	108	295,956.73	335,667.00	13.42	21	48,538.28	88,312.16	81.94
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	160	81,685.74	208,168.14	154.84
12	ROAD TRANSPORT AND HIGHWAYS**	158	105,220.04	107,360.97	2.03	12	3,623.15	5,791.59	59.85
13	SHIPPING AND PORTS	6	5,412.28	5,932.32	9.61	4	1,990.06	3,102.68	55.91
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		789	1,058,599.45	1,262,592.29	19.27	228	249,848.96	457,973.25	83.30

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - The information/data of Road Sector Projects have not been updated online by the NHAI.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of cost overrun in projects with respect to original schedule(State Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	28	24,696.13	30,412.21	23.15	6	10,400.36	16,116.44	54.96
2	ARUNACHAL PRADESH	3	9,356.22	24,848.83	165.59	3	9,356.22	24,848.83	165.59
3	ASSAM	34	22,255.53	37,810.44	69.89	14	15,918.17	31,590.74	98.46
4	BIHAR	47	50,385.63	64,163.83	27.35	15	13,737.73	28,243.47	105.59
5	GOA	5	1,395.15	1,448.07	3.79	1	335.61	388.53	15.77
6	GUJARAT	28	36,601.56	37,389.20	2.15	4	1,202.26	2,117.22	76.10
7	HARYANA	9	4,659.81	6,630.43	42.29	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,966.47	10,785.67	117.17
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	34	66,563.29	81,944.97	23.11	18	14,289.04	29,676.75	107.69
11	KERALA	15	24,980.58	29,311.93	17.34	7	16,728.30	21,059.65	25.89
12	MADHYA PRADESH	19	21,773.92	23,757.84	9.11	4	2,144.95	4,548.31	112.05
13	MAHARASHTRA	57	111,215.89	121,508.82	9.25	13	21,963.17	33,300.60	51.62
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	325.27
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	42	72,186.50	81,274.54	12.59	15	35,919.03	45,028.41	25.36
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	0.00
20	RAJASTHAN	31	28,164.75	28,220.22	0.20	6	2,574.16	3,142.63	22.08
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	42	68,208.56	85,860.44	25.88	20	30,028.23	47,680.11	58.78
23	TRIPURA	5	2,678.22	6,376.31	138.08	5	2,678.22	6,376.31	138.08
24	UTTAR PRADESH	29	35,842.78	38,623.19	7.76	7	1,739.99	4,568.66	162.57
25	WEST BENGAL	38	39,963.90	49,354.81	23.50	12	4,495.64	14,409.88	220.53
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	8.19
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
28	DELHI	12	50,903.45	50,903.45	0.00	0	0.00	0.00	0.00
29	CHHATISGARH	28	80,681.93	82,344.09	2.06	6	3,494.57	5,157.03	47.57
30	JHARKHAND	39	46,039.33	48,522.08	5.39	6	3,485.18	6,009.67	72.44
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,346.89	10,900.21	48.37
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
33	TELANGANA	31	11,908.91	14,872.86	24.89	8	2,417.24	5,381.19	122.62
34	MULTI STATE	180	189,338.04	214,441.59	13.26	39	24,137.81	49,755.31	106.13
Total		789	1,058,599.45	1,262,592.29	19.27	228	249,848.96	457,973.25	83.30

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	4	40,442.00	46,726.00	17 - 83
2	CIVIL AVIATION	6	1,973.56	2,063.48	4.56	3	979.06	1,016.06	6 - 80
3	COAL	80	61,374.97	65,278.13	6.36	44	29,386.88	31,842.03	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	26	66,135.16	69,879.56	5.66	11	42,526.04	42,526.04	6 - 44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41 - 41
8	PETROLEUM	69	148,572.08	159,409.56	7.29	41	95,122.89	103,221.35	3 - 71
9	POWER	108	295,956.73	335,667.00	13.42	62	141,079.35	170,123.09	1 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	31	31,140.62	88,821.64	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS**	158	105,220.04	107,360.97	2.03	17	13,725.67	13,817.62	6 - 105
13	SHIPPING AND PORTS	6	5,412.28	5,932.32	9.61	3	1,744.39	2,729.46	61 - 117
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	60 - 60
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	13	81,707.72	81,707.72	2 - 34
Total		789	1,058,599.45	1,262,592.29	19.27	232	485,417.23	596,575.83	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.** -

** - The information/data of Road Sector Projects have not been updated online by the NHAI.

\$ - Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	28	24,696.13	30,412.21	23.15	2	1,281.89	1,281.89	8 - 20
2	ARUNACHAL PRADESH	3	9,356.22	24,848.83	165.59	2	3,070.89	7,963.83	31 - 78
3	ASSAM	34	22,255.53	37,810.44	69.89	14	18,006.40	32,510.86	15 - 110
4	BIHAR	47	50,385.63	64,163.83	27.35	7	20,548.45	31,923.97	5 - 98
5	GOA	5	1,395.15	1,448.07	3.79	0	0.00	0.00	-
6	GUJARAT	28	36,601.56	37,389.20	2.15	6	20,257.81	20,181.12	22 - 48
7	HARYANA	9	4,659.81	6,630.43	42.29	0	0.00	0.00	-
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,190.42	8,089.51	11 - 111
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	10 - 193
10	KARNATAKA	34	66,563.29	81,944.97	23.11	5	3,366.80	4,845.36	12 - 94
11	KERALA	15	24,980.58	29,311.93	17.34	1	993.00	1,693.00	50 - 50
12	MADHYA PRADESH	19	21,773.92	23,757.84	9.11	6	2,304.29	2,206.15	12 - 69
13	MAHARASHTRA	57	111,215.89	121,508.82	9.25	19	60,875.88	67,283.55	2 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	0	0.00	0.00	-
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	47 - 123
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	42	72,186.50	81,274.54	12.59	17	40,039.91	45,211.60	6 - 84
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	-
20	RAJASTHAN	31	28,164.75	28,220.22	0.20	3	15,814.00	15,386.02	17 - 39
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 80
22	TAMIL NADU	42	68,208.56	85,860.44	25.88	11	49,698.18	58,510.16	8 - 117
23	TRIPURA	5	2,678.22	6,376.31	138.08	3	2,129.35	5,125.93	26 - 108
24	UTTAR PRADESH	29	35,842.78	38,623.19	7.76	6	11,352.29	12,772.94	9 - 84
25	WEST BENGAL	38	39,963.90	49,354.81	23.50	11	17,184.44	21,446.19	3 - 177
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	7 - 7
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
28	DELHI	12	50,903.45	50,903.45	0.00	5	42,630.16	42,630.16	9 - 34
29	CHHATISGARH	28	80,681.93	82,344.09	2.06	15	55,943.90	56,425.95	12 - 72
30	JHARKHAND	39	46,039.33	48,522.08	5.39	20	14,774.36	17,113.52	2 - 138
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	3	7,127.06	10,570.24	69 - 94
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
33	TELANGANA	31	11,908.91	14,872.86	24.89	11	3,359.39	4,375.44	8 - 72
34	MULTI STATE	180	189,338.04	214,441.59	13.26	53	73,573.68	79,145.05	1 - 261
Total		789	1,058,599.45	1,262,592.29	19.27	232	485,417.23	596,575.83	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	17 - 83
2	CIVIL AVIATION	6	1,973.56	2,063.48	4.56	3	979.06	1,016.06	6 - 80
3	COAL	80	61,374.97	65,278.13	6.36	42	22,249.50	24,704.65	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	26	66,135.16	69,879.56	5.66	10	27,001.04	27,001.04	6 - 44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41 - 41
8	PETROLEUM	69	148,572.08	159,409.56	7.29	24	62,609.33	67,534.46	3 - 71
9	POWER	108	295,956.73	335,667.00	13.42	59	137,639.74	160,777.55	1 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	28	24,665.62	76,297.64	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS**	158	105,220.04	107,360.97	2.03	10	12,295.94	12,295.94	6 - 61
13	SHIPPING AND PORTS	6	5,412.28	5,932.32	9.61	3	1,744.39	2,729.46	61 - 117
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	60 - 60
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	13	81,707.72	81,707.72	2 - 34
Total		789	1,058,599.45	1,262,592.29	19.27	198	415,404.95	509,158.34	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - The information/data of Road Sector Projects have not been updated online by the NHAI.

\$ - Time Overrun = Anticipated Date of Commissioning minus Latest Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of cost overrun in projects with respect to latest schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	46,726.00	0.00	0	0.00	0.00	0.00
2	CIVIL AVIATION	6	2,010.56	2,063.48	2.63	1	335.61	388.53	15.77
3	COAL	80	65,438.83	65,278.13	-0.25	2	630.12	678.22	7.63
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	26	69,734.16	69,879.56	0.21	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,833.52	10.24	1	8,920.00	9,833.52	10.24
8	PETROLEUM	69	156,755.50	159,409.56	1.69	6	16,329.58	19,278.40	18.06
9	POWER	108	316,673.71	335,667.00	6.00	7	22,127.17	41,120.46	85.84
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS*	296	185,296.44	296,947.84	60.26	154	87,045.00	200,328.20	130.14
12	ROAD TRANSPORT AND HIGHWAYS**	158	105,510.96	107,360.97	1.75	12	3,783.63	5,683.15	50.20
13	SHIPPING AND PORTS	6	6,586.35	5,932.32	-9.93	2	395.67	973.22	145.97
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		789	1,119,823.12	1,262,592.29	12.75	188	148,022.78	294,208.40	98.76

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - The information/data of Road Sector Projects have not been updated online by the NHAI.

[^] - Cost Overrun = Anticipated Cost minus Latest Approved Cost..

Extent of time & cost overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	1	3,492.00	5,677.00	72- 72
2	CIVIL AVIATION	6	1,973.56	2,063.48	4.56	0	0.00	0.00	0- 0
3	COAL	80	61,374.97	65,278.13	6.36	2	6,935.32	10,186.51	41- 73
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	26	66,135.16	69,879.56	5.66	1	8,692.00	12,291.00	66- 66
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41- 41
8	PETROLEUM	69	148,572.08	159,409.56	7.29	6	41,001.84	48,876.88	12- 35
9	POWER	108	295,956.73	335,667.00	13.42	10	20,165.40	35,224.81	16- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	RAILWAYS	296	171,881.41	296,947.84	72.76	4	5,873.07	10,121.84	48- 174
12	ROAD TRANSPORT AND HIGHWAYS	158	105,220.04	107,360.97	2.03	2	425.61	517.56	69- 105
13	SHIPPING AND PORTS	6	5,412.28	5,932.32	9.61	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		789	1058599.45	1262592.29	19.27	27	92045.85	132729.12	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - The information/data of Road Sector Projects have not been updated online by the NHAI.

<u>Extent of time & cost overrun in projects with respect to original schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	72- 83
2	CIVIL AVIATION	6	1,973.56	2,063.48	4.56	1	452.00	489.00	7- 7
3	COAL	80	61,374.97	65,278.13	6.36	3	5,596.41	8,310.76	36- 48
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	26	66,135.16	69,879.56	5.66	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41- 41
8	PETROLEUM	69	148,572.08	159,409.56	7.29	11	44,107.75	53,699.40	12- 53
9	POWER	108	295,956.73	335,667.00	13.42	19	41,956.08	71,063.43	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	27	22,946.70	80,627.72	3- 261
12	ROAD TRANSPORT AND HIGHWAYS**	158	105,220.04	107,360.97	2.03	1	217.61	309.56	69- 69
13	SHIPPING AND PORTS	6	5,412.28	5,932.32	9.61	3	1,744.39	2,729.46	61- 117
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		789	1058599.45	1262592.29	19.27	69	140862.55	253837.15	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - The information/data of Road Sector Projects have not been updated online by the NHAI.

\$ - Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>CIVIL AVIATION</u>						
1	GAGAN PROJECT	09/2008	626.00	06/2013	644.70	N.A.	483.53
	<u>COAL</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2,030.78	06/2009	3,583.77	04/2015	3,215.91
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4,904.54	03/2012	6,602.74	08/2015	6,426.43
	<u>PETROLEUM</u>						
4	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	04/2003	429.82	04/2006	3,955.21	06/2015	3,439.38
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	10/2011	1,178.35	06/2015	1,082.12
6	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA	07/2008	288.04	08/2012	253.66	06/2015	229.16
7	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV)	11/2010	331.20	08/2013	269.10	06/2015	190.04
	<u>POWER</u>						
8	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	03/2011	2,569.25	03/2014	3,105.51	08/2015	2,876.57
9	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ.	03/2010	4,672.99	11/2012	4,672.99	08/2015	3,769.57
10	BARH STPP STAGE -II	02/2008	7,341.04	10/2013	10,852.46	03/2015	8,962.00
11	VINDHYACHAL STPP STAGE-V	05/2012	3,180.40	08/2015	3,180.40	08/2015	2,042.00
	<u>SHIPPING AND PORTS</u>						
12	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6	06/2010	277.00	03/2012	277.00	N.A.	.21
13	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS	02/2011	830.00	05/2013	621.53	N.A.	.00

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	AMALGAMATED PAUNI-II & III OC MINE	6/2015	483.69	3/2021	483.69	3/2021
2	AMALGAMATED YEKONA-I & YEKONA-II	8/2015	727.28	3/2025	727.28	3/2025
3	ADASA UG TO OC	8/2015	288.90	3/2023	288.90	3/2023
	<u>PETROLEUM</u>					
4	GAMJI REDEVELOPMENT PROJECT	5/2015	1,671.22	11/2019	1,671.22	11/2019
5	PIPELINE REPLACEMENT PROJECT -4	2/2015	2,899.93	5/2017	2,899.93	5/2017
6	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	2,818.88	3/2019	2,818.88	3/2019
	<u>POWER</u>					
7	BOKARO THERMAL POWER STATION-A	8/2006	2,313.00	12/2011	4,237.67	3/2016
8	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7&8 - PART B	7/2015	307.18	11/2017	307.18	11/2017
9	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C	7/2015	2,247.37	7/2018	2,247.37	7/2018
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
10	REHABILITATION AND UPGRADATION OF NH - 365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S	12/2013	177.18	3/2016	177.18	3/2016
11	REHABILITATION AND UPGRADATION OF NH - 365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO	12/2013	158.65	3/2016	158.65	3/2016
12	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW	12/2013	244.08	3/2016	244.08	3/2016
13	REHABILITATION AND UPGRADATION OF NH - 765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	1/2014	340.00	3/2016	340.00	3/2016
14	REHABILITATION AND UPGRADATION OF NH - 565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	270.00	3/2016	270.00	3/2016
15	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	10/2014	244.30	12/2016	244.30	12/2016
16	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	295.47	2/2017	313.27	2/2017
17	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	153.21	1/2017	153.21	1/2017
18	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	3/2011	218.31	12/2015	339.82	12/2015
19	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337	6/2014	260.39	11/2016	260.39	11/2016

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
20	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	297.00	/	297.00	10/2017
21	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	168.30	/	168.30	10/2017
22	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO 45	8/2014	187.79	7/2016	187.79	7/2016
23	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	446.77	/	446.77	6/2017
24	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A	12/2014	201.12	2/2015	201.12	2/2015
25	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	1/2014	267.16	11/2017	352.05	11/2017
26	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	255.75	9/2017	348.43	9/2017
27	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00	12/2013	220.72	11/2016	220.72	11/2016
28	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 101.00 TO 161.570 UP TO AANE GHAT	11/2014	292.98	9/2016	292.28	9/2016
29	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	298.33	/	298.33	-
30	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO	3/2015	184.05	/	184.05	-
31	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	280.16	/	280.16	-
	<u>STEEL</u>					
32	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	2/2014	4,749.00	9/2017	4,749.00	9/2017

Milestones (Cumulative due & achieved)


Total	3818
Achieved up to month	1878

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	10/2015	11/2015	1
	<u>CIVIL AVIATION</u>						
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II AAI	452.00	489.00	03/2015	07/2015	10/2015	3
	<u>COAL</u>						
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,602.74	03/2012	07/2015	08/2015	1
4	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	08/2015	09/2015	1
5	PURNADIH OCP (3.0 MTY) CCL	210.98	210.98	03/2013	03/2016	03/2017	12
6	MANIKPUR OC EXPANSION (3.5 MTY) SECL	321.50	321.50	03/2014	03/2016	03/2018	24
7	BAROUD OC EXPANSION (RCE)- 3MTY SECL	258.56	258.56	03/2016	03/2016	03/2018	24
	<u>PETROLEUM</u>						
8	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY BPCL	1,419.00	1,419.00	12/2014	08/2015	09/2015	1
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE ISPRL	732.00	1,227.00	10/2011	01/2016	03/2016	2
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR ISPRL	993.00	1,693.00	01/2012	01/2016	03/2016	2
11	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG OIL	270.00	215.66	06/2012	11/2015	11/2016	12
	<u>POWER</u>						
12	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID PGCIL	1,508.74	1,508.74	03/2015	09/2015	10/2015	1
13	TRIPURA GAS BASED POWER PROJECT NEEPCO	421.01	1,007.68	07/2013	08/2015	09/2015	1


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B PGCIL	1,927.16	1,927.16	10/2014	09/2015	10/2015	1
15	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	08/2015	09/2015	1
16	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	250.03	250.03	01/2013	09/2015	11/2015	2
17	WESTERN REGION STRENGTHENING SCHEME-V PGCIL	477.69	721.81	09/2010	03/2016	06/2016	3
18	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII PGCIL	509.66	509.66	11/2011	03/2016	06/2016	3
19	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. PGCIL	2,144.00	2,144.00	12/2012	03/2016	06/2016	3
20	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH PGCIL	2,127.51	2,127.51	07/2014	03/2016	06/2016	3
21	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 PGCIL	2,422.66	2,422.66	08/2014	09/2015	12/2015	3
22	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED PGCIL	552.44	552.44	02/2014	09/2015	12/2015	3
23	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,422.85	1,422.85	01/2015	03/2016	06/2016	3
24	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B PGCIL	3,201.44	3,201.44	10/2014	03/2016	06/2016	3
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	05/2015	09/2015	12/2015	3
26	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV PGCIL	680.69	680.69	03/2016	03/2016	06/2016	3
27	EASTERN REGION STRENGTHENING SCHEME-IX PGCIL	196.58	196.58	02/2016	02/2016	06/2016	4
28	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH PGCIL	1,746.65	2,228.70	08/2014	03/2016	09/2016	6
29	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	723.63	723.63	11/2014	12/2015	06/2016	6

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
30	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI PGCIL	752.64	689.03	07/2013	11/2015	06/2016	7
31	KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL	1,779.29	2,159.07	11/2008	03/2016	12/2016	9
32	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	03/2016	12/2016	9
33	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER PGCIL	4,404.57	4,404.57	01/2015	03/2016	12/2016	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
34	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	10/2015	12/2015	2
35	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	08/2015	11/2015	3
36	NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	01/2016	01/2017	12
	<u>TELECOMMUNICATIONS</u>						
37	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS BSNL	384.00	384.00	10/2010	09/2015	10/2015	1


Graphical Presentation of All Projects w.r.t. Original Schedule

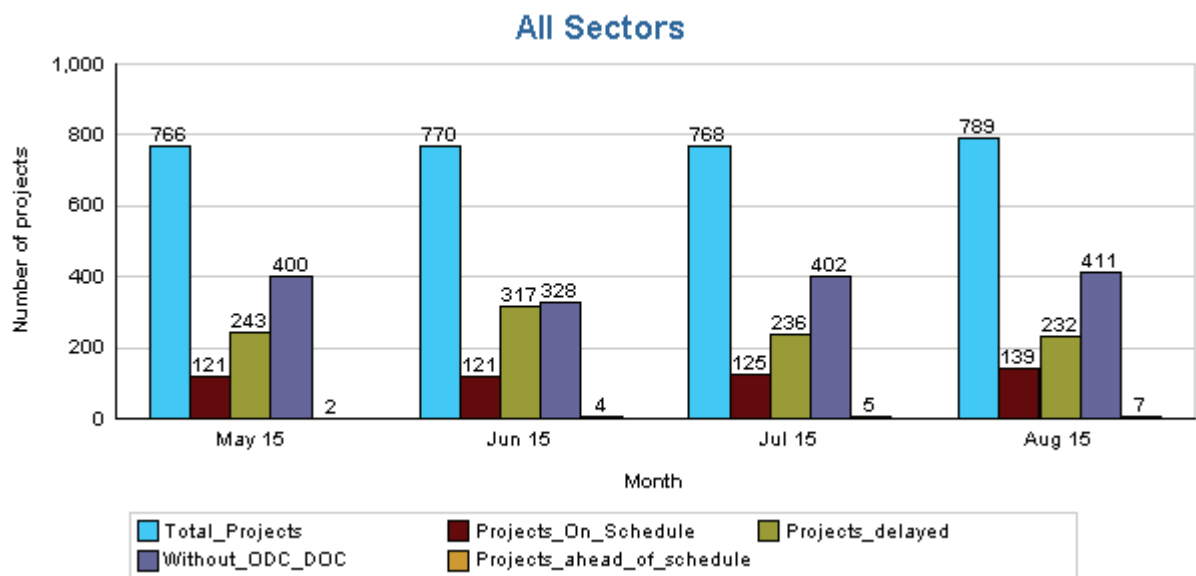


Break-up of 232 Delayed projects in August 2015

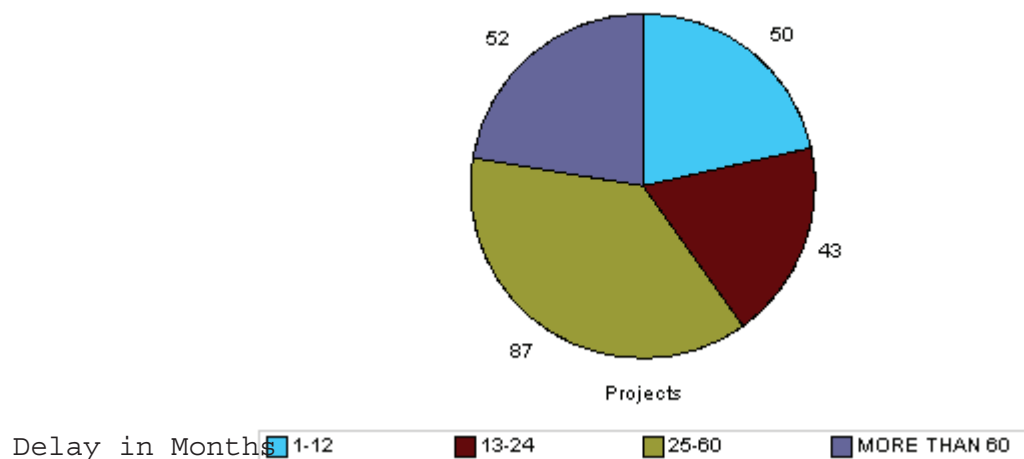


Graphical Presentation of ATOMIC ENERGY Sector

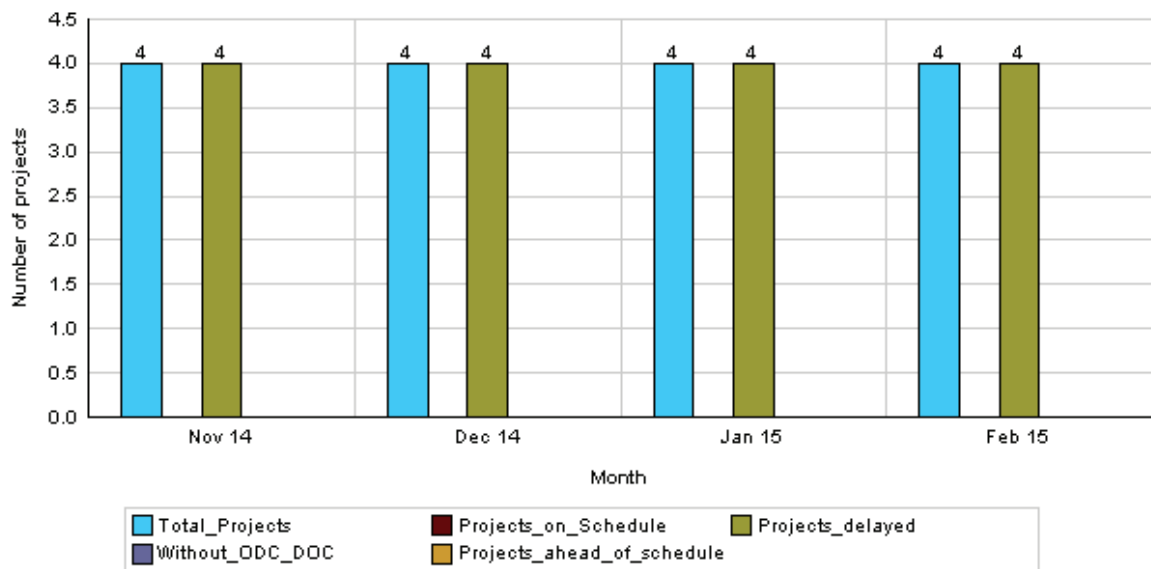


Break-up of 4 Delayed projects in February 2015

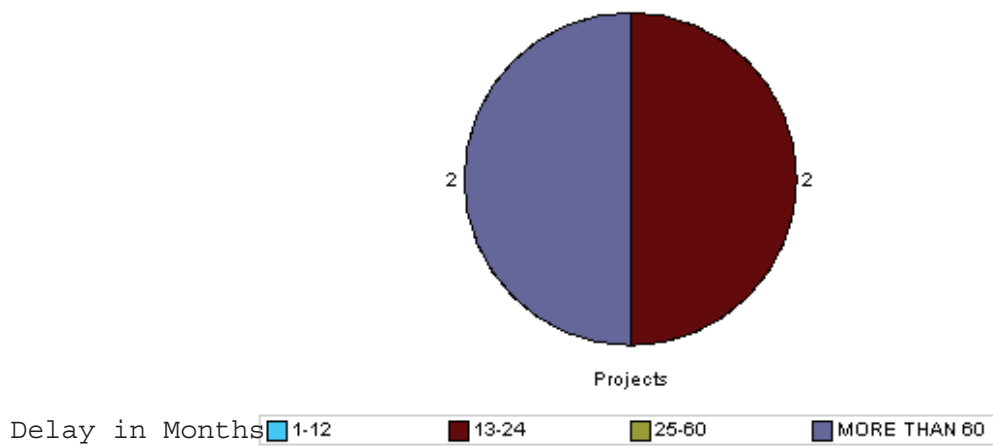


Graphical Presentation of CIVIL AVIATION Sector

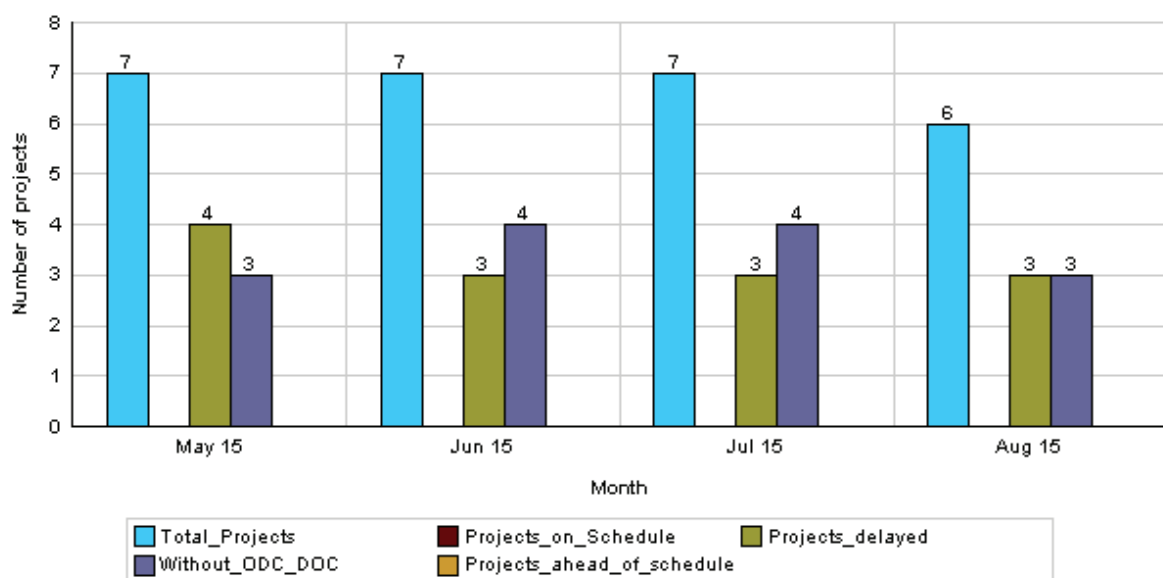


Break-up of 3 Delayed projects in August 2015

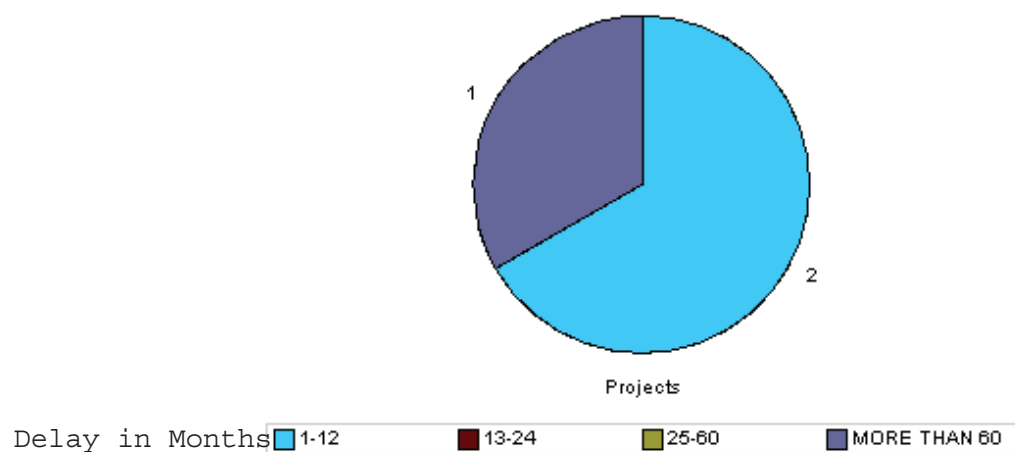


Graphical Presentation of COAL Sector

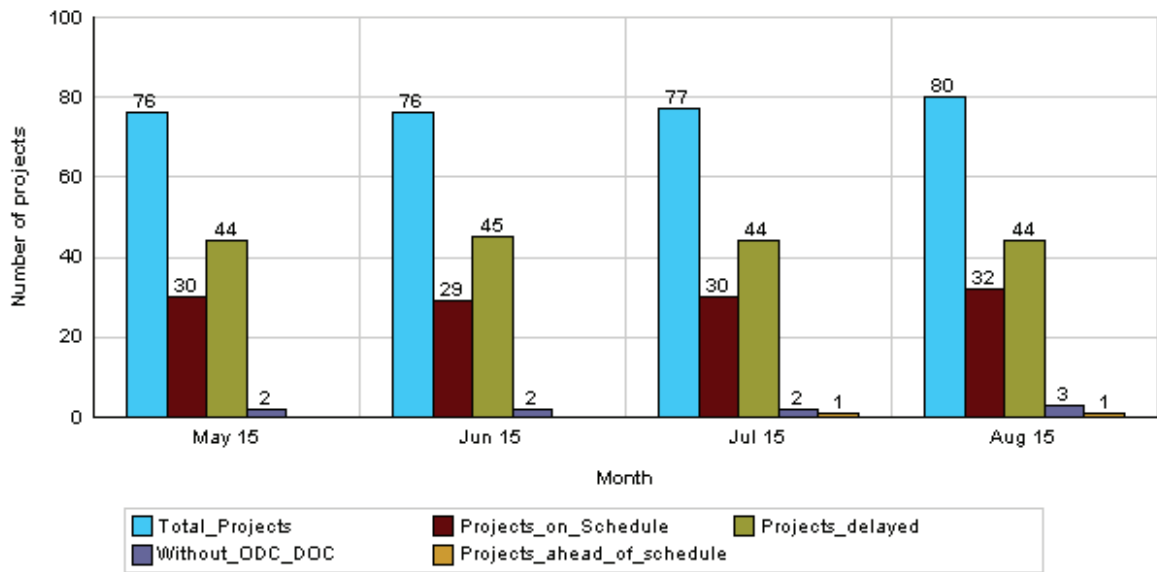


Break-up of 44 Delayed projects in August 2015

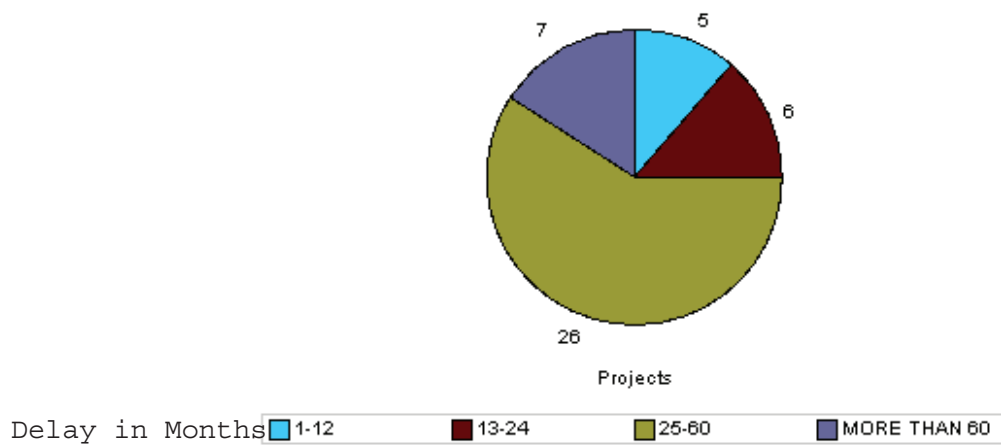


Graphical Presentation of STEEL Sector

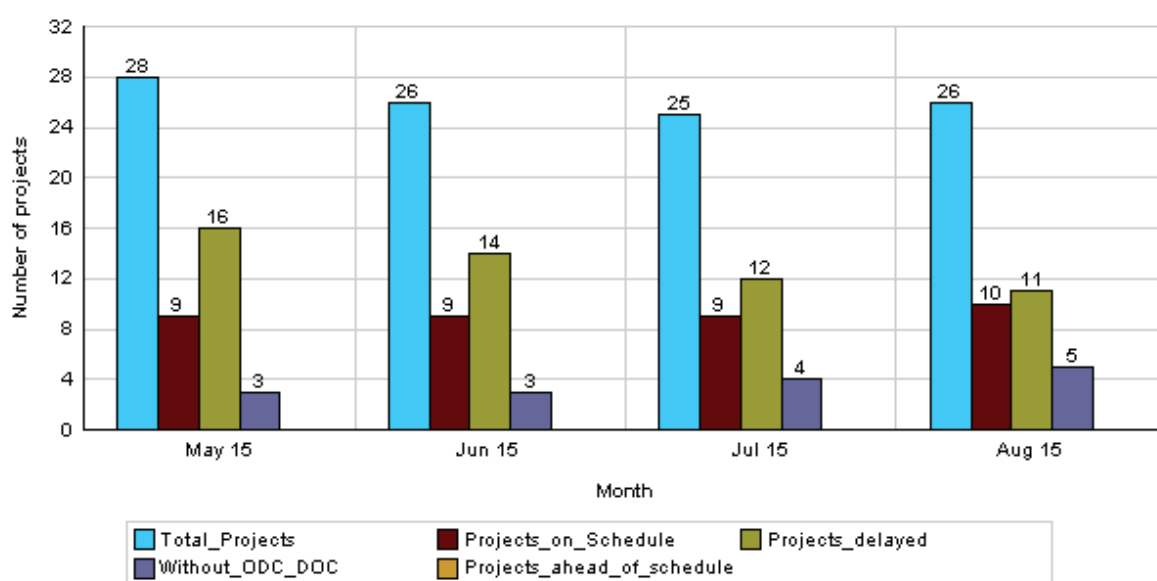


Break-up of 11 Delayed projects in August 2015

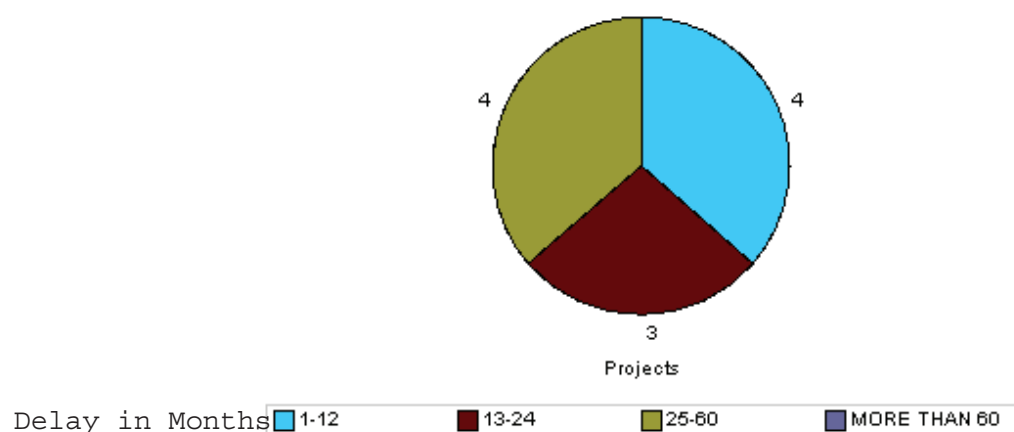

Graphical Presentation of PETROLEUM Sector

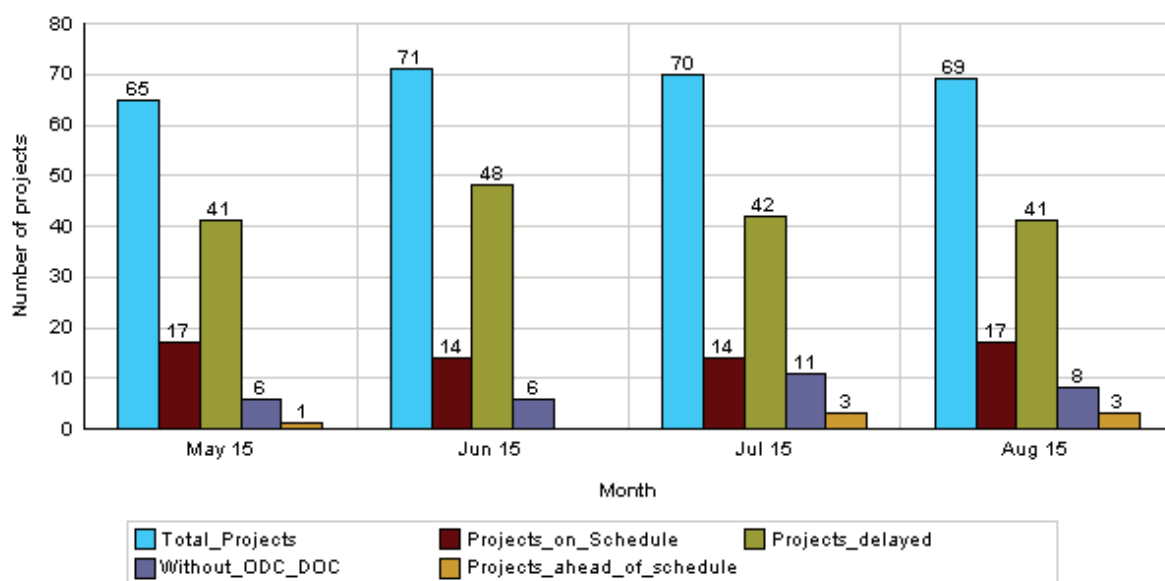


Break-up of 41 Delayed projects in August 2015

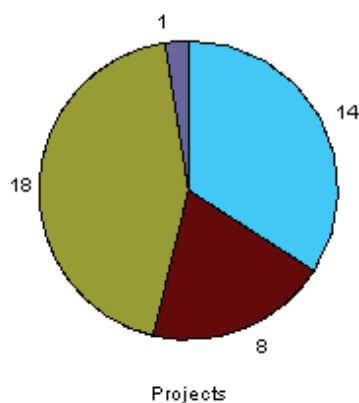


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

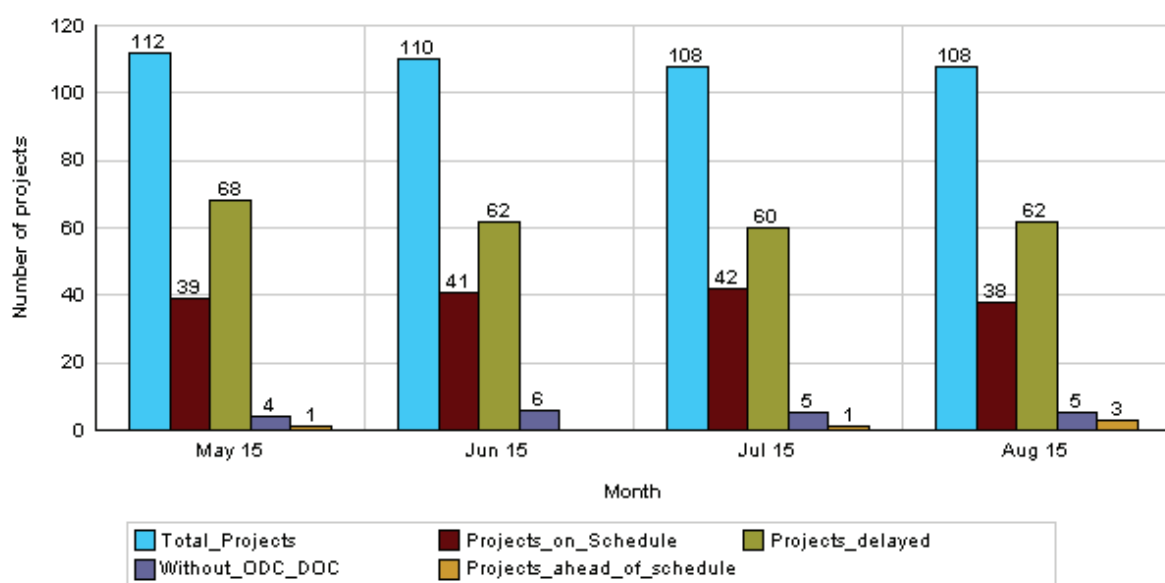


Break-up of 62 Delayed projects in August 2015

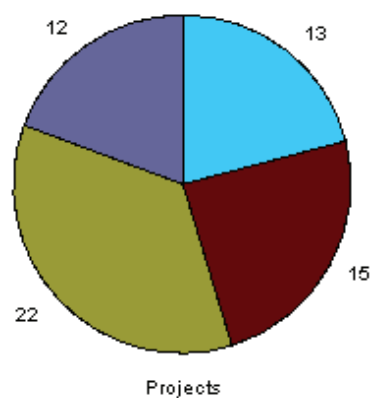


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of RAILWAYS Sector

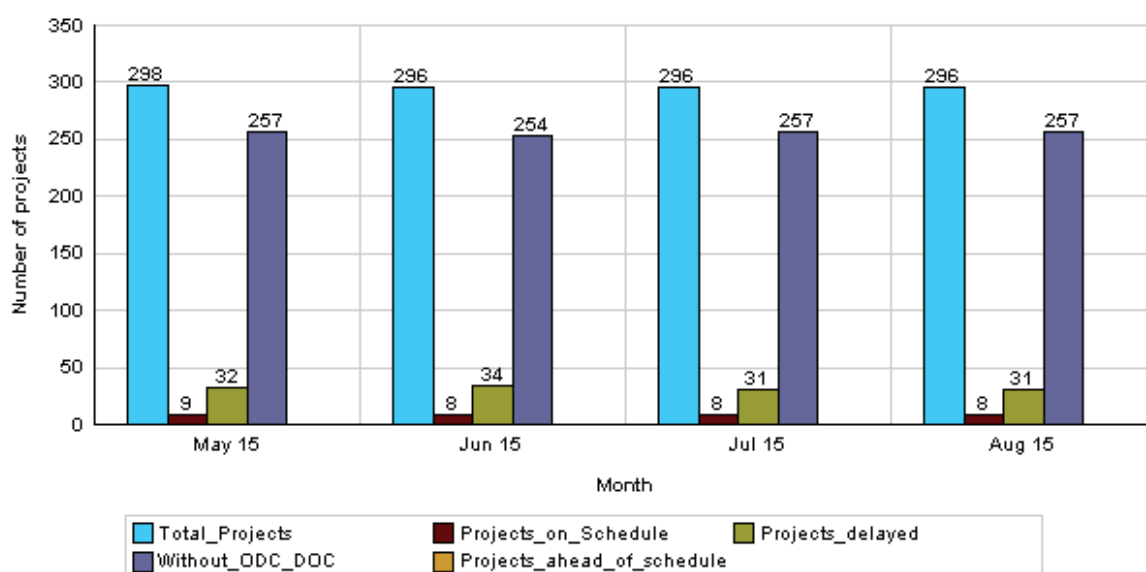


Break-up of 31 Delayed projects in August 2015

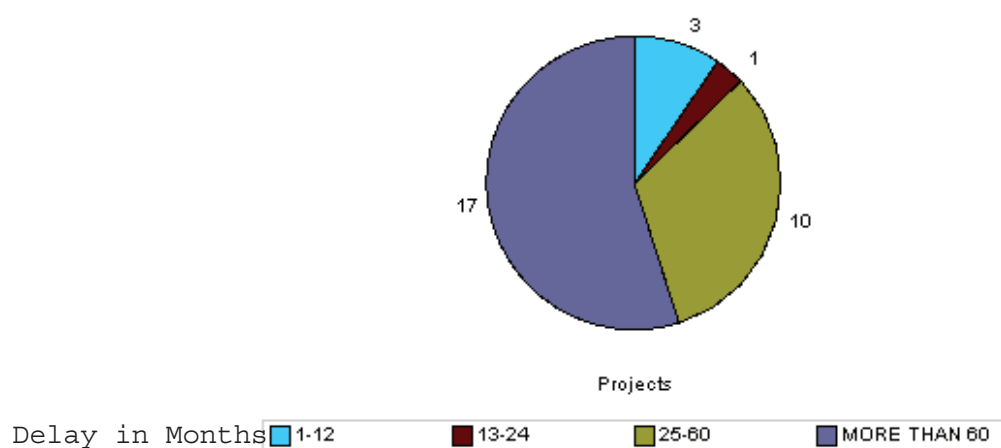

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

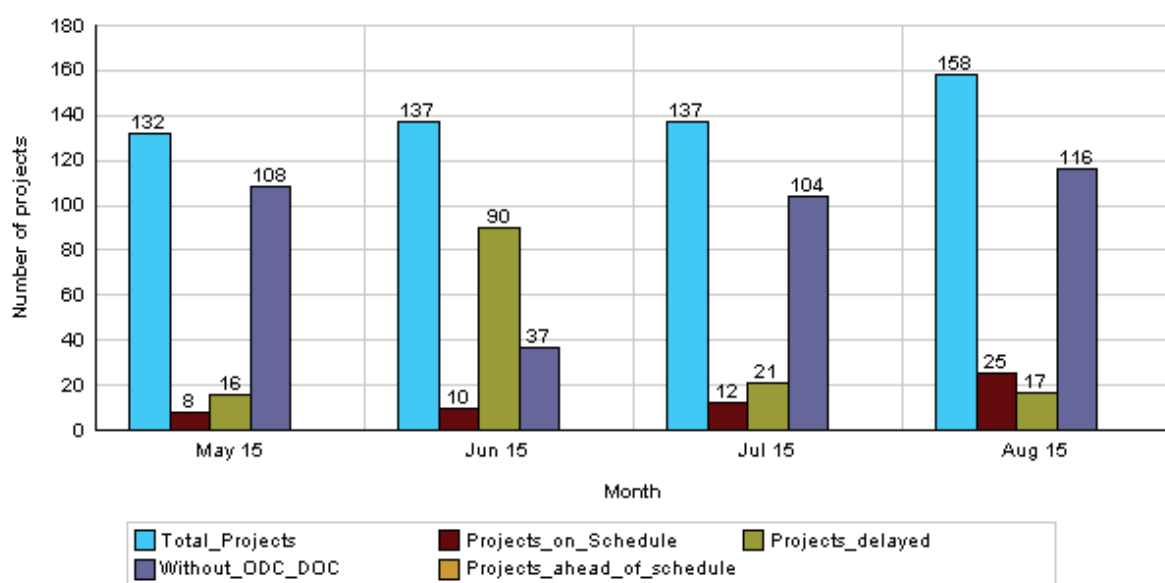


Break-up of 17 Delayed projects in August 2015

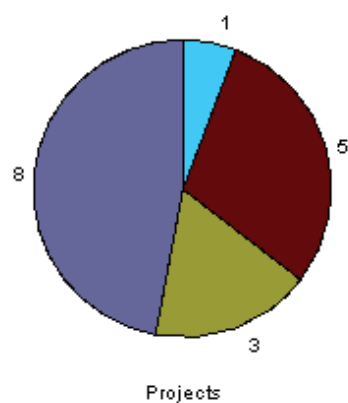


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of SHIPPING AND PORTS Sector

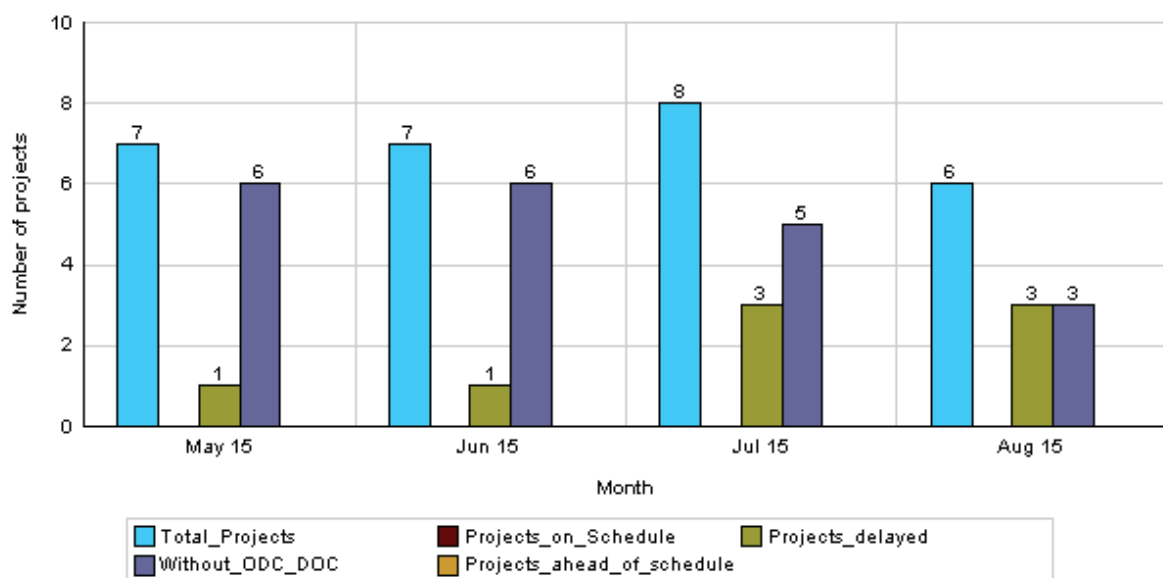

Break-up of 3 Delayed projects in August 2015

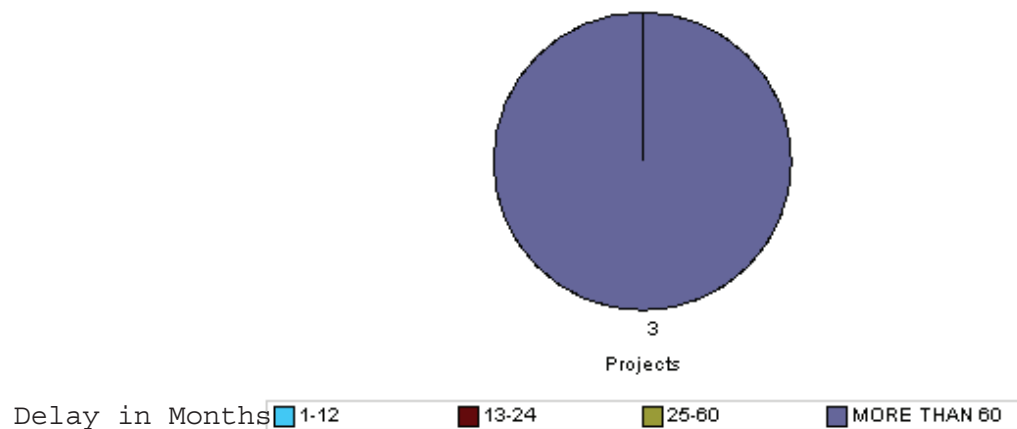

Graphical Presentation of TELECOMMUNICATIONS Sector

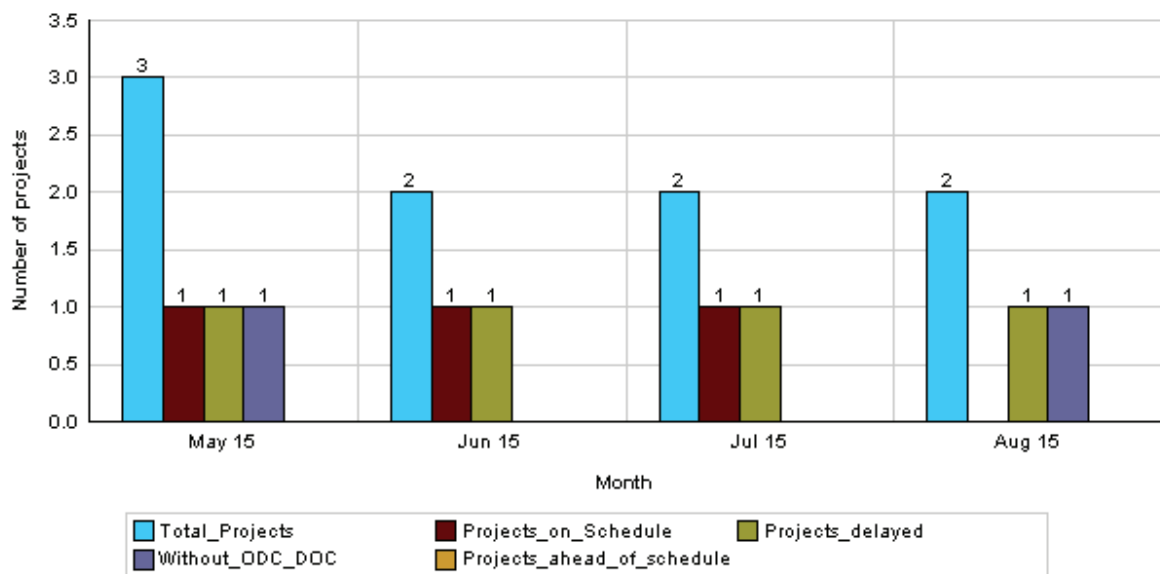


Break-up of 1 Delayed projects in August 2015




Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

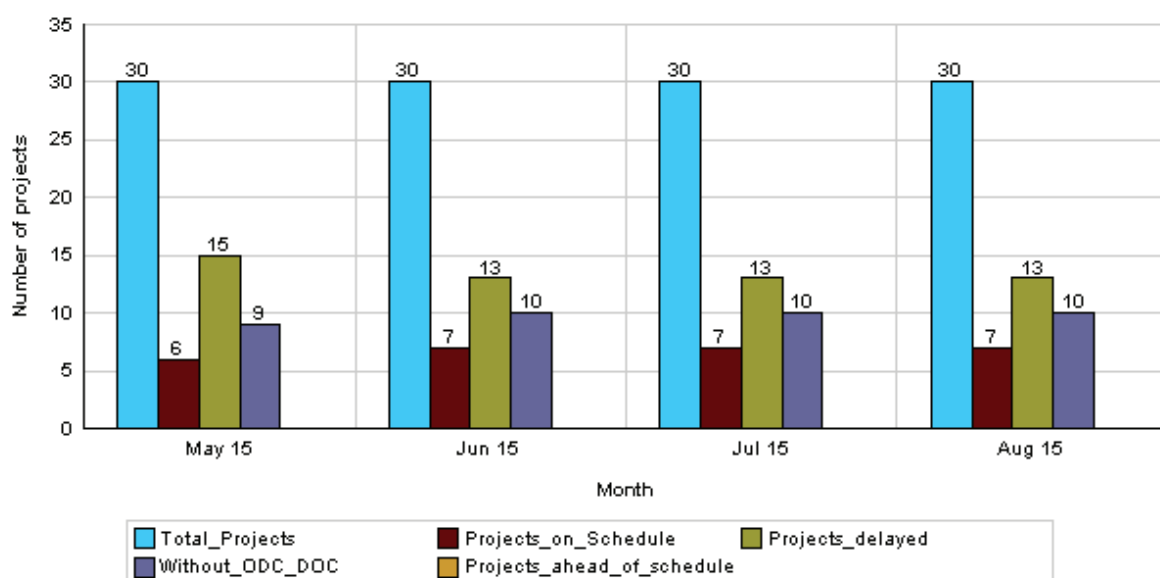

Break-up of 13 Delayed projects in August 2015

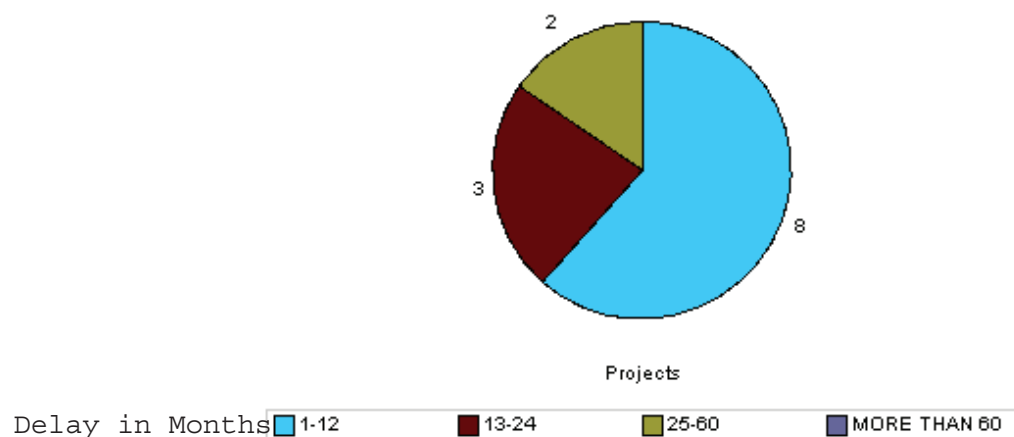

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	46,726.00	46,726.00	37,827.45
CIVIL AVIATION	6	1,973.56	2,010.56	2,063.48	1,193.81
COAL	80	61,374.97	65,438.83	65,278.13	22,901.46
FERTILISERS	1	197.79	197.79	197.79	30.36
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	26	66,135.16	69,734.16	69,879.56	42,983.16
PETROCHEMICALS	1	5,460.61	8,920.00	9,833.52	0.00
PETROLEUM	69	148,572.08	156,755.50	159,409.56	70,200.48
POWER	108	295,956.73	316,673.71	335,667.00	161,731.90
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
RAILWAYS	296	171,881.41	185,296.44	296,947.84	90,385.01
ROAD TRANSPORT AND HIGHWAYS	158	105,220.04	105,510.96	107,360.97	55,483.94
SHIPPING AND PORTS	6	5,412.28	6,586.35	5,932.32	3,201.74
TELECOMMUNICATIONS	2	13,718.00	13,718.00	13,718.00	72.17
URBAN DEVELOPMENT	30	138,680.82	138,680.82	143,894.82	32,315.10
Grand total	789	1,058,599.45	1,119,823.12	1,262,592.29	518,326.58

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(August 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00	11,459.00	7,095.00	12/2015	10/2017	22(O)	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00	17,270.00	20,775.00	12/2008	11/2015	83(O)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,TAMIL NADU	09/2003	3,492.00	5,677.00	5,053.45	09/2010	09/2016	72(O)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00	12,320.00	4,904.00	12/2016	05/2018	17(O)	4/69
	Total		40,442.00	46,726.00	37,827.45				60/329
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46	309.46	357.62	01/2011	09/2017	80(O)	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	18.02	-	-	-	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61	388.53	302.35	05/2012	-	-	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00	489.00	439.81	03/2015	10/2015	7(O)	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28	344.28	75.97	03/2014	-	-	0/0
10	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60	217.60	0.04	03/2015	09/2015	6(O)	0/0
	Total		1,973.56	2,063.48	1,193.81				0/0
	<u>COAL</u>								
11	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90	288.90	-	03/2023	03/2023	0(O)	0/15
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34	1,228.39	860.52	03/2013	03/2016	36(O)	21/22
13	AMALGAMATED PAUNI-II & III OC MINE - [N06000131]WCL,MAHARASHTRA	06/2015	483.69	483.69	1.57	03/2021	03/2021	0(O)	0/14
14	AMALGAMATED YEKONA-I & YEKONA-II - [N06000132]WCL,MAHARASHTRA	08/2015	727.28	727.28	-	03/2025	03/2025	0(O)	0/20
15	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97	335.97	29.83	03/2018	03/2018	0(O)	0/4
16	AMLAJ OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59	198.59	111.96	03/2016	03/2016	0(O)	3/7
17	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04	1,143.54	804.65	03/2016	03/2016	0(O)	0/4
18	AMRAPALI OC(12MTY) - [N06000103]JCL,JHARKHAND	02/2012	858.11	858.11	107.63	03/2020	03/2020	0(O)	3/4

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60	481.60	-	03/2023	03/2023	0(O)	0/7
20	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	192.31	03/2012	03/2017	60(O)	4/5
21	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63	341.63	126.14	03/2011	03/2017	72(O)	2/5
22	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	148.86	03/2010	03/2017	84(O)	2/4
23	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56	258.56	87.64	03/2016	03/2018	24(O)	3/6
24	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15	479.15	0.30	03/2019	03/2019	0(O)	1/9
25	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82	203.82	-	03/2015	03/2015	-	1/6
26	BHANEAGAN OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94	187.94	42.23	03/2023	03/2023	0(O)	5/21
27	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10	490.10	204.45	03/2017	03/2017	0(O)	11/11
28	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49	164.49	76.43	03/2020	03/2020	0(O)	1/6
29	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04	535.10	409.02	03/2015	03/2016	12(O)	0/3
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63	610.33	-	03/2022	03/2022	0(O)	1/7
31	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35	462.35	298.77	03/2014	03/2016	24(O)	7/9
32	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	35.92	03/2011	03/2016	60(O)	0/3
33	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16	611.16	6.11	03/2020	03/2020	0(O)	3/15
34	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66	1,943.66	1,695.40	03/2014	03/2016	24(O)	10/13
35	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38	1,375.38	11.97	03/2021	03/2021	0(O)	1/9
36	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67	2,675.67	1,862.99	03/2014	03/2016	24(O)	11/16
37	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67	267.67	161.05	03/2018	03/2018	0(O)	2/18
38	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72(O)	2/13
39	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.63	173.69	03/2013	03/2017	48(O)	4/8
40	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66	337.66	0.24	03/2019	03/2019	0(O)	2/6
41	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60(O)	1/7
42	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36(O)	4/13
43	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78	467.78	2.85	03/2013	-	-	6/83
44	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18	287.18	225.39	03/2011	03/2017	72(O)	7/15

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
45	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51(O) -	11/44
46	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL, TELANGANA	05/2015	397.09 -	397.09	-	03/2019 -	03/2019	0(O) -	0/18
47	KALYANIKHANI OPENCAS PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	13.85	07/2016 -	03/2017	8(O) -	6/28
48	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	28.23	03/2021 -	03/2021	0(O) -	0/6
49	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	181.15	03/2013 -	03/2017	48(O) -	8/9
50	KAPURIA UG(PSLV) - [N06000108]BCCL, JHARKHAND	08/2011	988.35 -	988.35	45.15	04/2017 -	04/2017	0(O) -	0/2
51	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	67.28	03/2014 -	03/2017	36(O) -	3/4
52	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
53	KHADIA EXPANSION OPENCAS PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH	06/2011	1,131.28 1,131.28	1,131.28	97.98	03/2018 -	03/2018	0(O) -	0/4
54	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36(O) -	0/5
55	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	481.99	03/2013 -	03/2016	36(O) -	0/2
56	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
57	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL, ODISHA	01/2005	302.96 -	302.96	147.58	03/2010 -	03/2016	72(O) -	8/10
58	KUSMUNDA EXPN. OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH	08/2013	7,612.33 7,612.33	7,612.33	778.77	03/2023 03/2023	03/2023	0(O) 0(R)	1/17
59	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	-	05/2014 -	10/2016	29(O) -	0/8
60	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	77.19	07/2012 -	03/2016	44(O) -	1/3
61	MAKARDHOKRA I OC - [N06000119]WCL, MAHARASHTRA	09/2014	266.23 -	266.23	82.58	03/2021 -	03/2021	0(O) -	3/22
62	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	207.52	03/2014 -	03/2018	48(O) -	4/7
63	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	47.90	03/2012 -	03/2016	48(O) -	4/6
64	MOONIDH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	43.62	04/2015 04/2019	04/2019	48(O) 0(R)	2/12
65	MURADH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	11.26	04/2014 -	03/2016	23(O) -	3/6
66	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	295.56	69.93	03/2019 -	03/2019	0(O) -	4/20
67	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,056.99	12/2015 04/2018	04/2018	28(O) 0(R)	11/35
68	NIGAIH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	259.40	25.80	03/2012 -	03/2017	60(O) -	0/2
69	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL, JHARKHAND	02/2014	555.52 -	555.52	3.52	03/2021 -	03/2017	-48(O) -	0/2

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
70	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87	179.87	85.40	03/2012	03/2017	60(O)	2/3
71	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	48.35	04/2014	11/2016	31(O)	0/10
72	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH	11/2014	1,624.59	1,624.59	5.43	03/2023	03/2023	0(O)	1/10
73	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA	09/2014	441.82	441.82	119.03	03/2020	03/2020	0(O)	5/27
74	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98	210.98	150.78	03/2013	03/2017	48(O)	4/4
75	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82	153.82	60.62	03/2014	03/2016	24(O)	3/9
76	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80	357.80	108.44	03/2021	03/2021	0(O)	0/7
77	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	223.38	03/2016	03/2016	0(O)	2/4
78	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97	418.97	365.83	03/2012	03/2016	48(O)	0/2
79	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76	162.76	1.31	03/2015	03/2019	48(O)	4/29
80	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45	486.27	93.51	03/2016	03/2016	0(O)	7/39
81	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2016	9(O)	18/51
82	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78	209.78	72.86	03/2015	03/2016	12(O)	8/31
83	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03	249.03	75.60	03/2012	03/2018	72(O)	27/42
84	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36	3,756.36	0.56	03/2026	03/2026	0(O)	3/15
85	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05	1,055.05	167.35	03/2018	03/2018	0(O)	1/10
86	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48(O)	2/11
87	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	145.20	03/2012	03/2016	48(O)	2/4
88	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78	3,583.77	3,213.77	06/2009	07/2015	-	23/23
89	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54	6,602.74	6,355.68	03/2012	08/2015	41(O)	39/39
90	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75	364.75	170.77	10/2014	09/2015	11(O)	8/10
	Total		61,374.97	65,278.13	22,901.46				348/1072
	FERTILISERS								
91	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79	197.79	30.36	11/2016	11/2016	0(O)	0/0
	Total		197.79	197.79	30.36				0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>MINES</u>								
92	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N1000007]HCL,MADHYA PRADESH	09/2011	1,856.00	1,856.00	-	09/2017	09/2017	0(O)	0/0
	Total		1,856.00	1,856.00	.00				0/0
	<u>STEEL</u>								
93	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00	572.00	472.79	04/2013 09/2014	06/2015	-	18/19
94	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67	245.67	54.37	05/2016	05/2016	0(O)	1/3
95	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76	974.76	147.85	07/2016	07/2016	0(O)	1/2
96	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55	898.55	398.16	05/2013 01/2015	08/2015	27(O) 7(R)	19/20
97	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19	255.19	-	03/2018	03/2018	0(O)	0/0
98	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17	607.17	394.84	12/2011 01/2015	03/2015	-	20/20
99	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73	877.73	284.58	07/2015	03/2016	8(O)	2/2
100	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00	677.00	533.30	09/2013	07/2015	-	0/1
101	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65	332.65	211.55	08/2014	11/2015	15(O)	4/5
102	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93	188.93	32.98	04/2015	04/2015	-	1/4
103	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00	17,265.00	14,854.52	03/2013	03/2016	36(O)	31/35
104	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00	6,325.00	5,232.17	12/2011	08/2015	44(O)	24/25
105	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00	4,749.00	1.29	09/2017	09/2017	0(O)	0/0
106	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,423.76	10/2009 10/2012	04/2015	-	70/70
107	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33	187.33	163.67	10/2013	12/2015	26(O)	2/6
108	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48	160.48	136.08	09/2014	09/2015	12(O)	2/3
109	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30	3,127.30	22.53	04/2018	04/2018	0(O)	0/0

Sector Wise Details									
(August 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
110	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	0.53	12/2017 -	12/2017	0(O) -	0/0
111	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017	0(O) -	0/0
112	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	7,729.64	05/2015 12/2016	12/2016	19(O) 0(R)	17/81
113	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	267.06	06/2015 -	12/2015	6(O) -	3/4
114	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	204.11	12/2014 -	11/2015	11(O) -	2/3
115	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]JINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	25.49	10/2016 -	10/2016	0(O) -	0/0
116	SMS-1 CONVERTERS REVAMPING - [N12000090]JINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	178.99	07/2015 -	03/2017	20(O) -	0/1
117	TURBO BLOWER - 5 - [N12000092]JINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016	0(O) -	0/1
118	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	199.13	04/2016 -	04/2016	0(O) -	2/2
	Total		66,135.16 -	69,879.56	42,983.16				219/307
	<u>PETROCHEMICALS</u>								
119	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	9,833.52	-	04/2012 12/2013	09/2015	41(O) 21(R)	21/26
	Total		5,460.61 -	9,833.52	.00				21/26
	<u>PETROLEUM</u>								
120	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	437.69	06/2012 03/2015	09/2015	39(O) 6(R)	1/1
121	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	2,476.82	223.28	12/2018 -	12/2018	0(O) -	3/9
122	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36(O) -	0/0
123	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48(O) -	0/0
124	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,783.31	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
125	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	355.47	08/2015 -	12/2015	4(O) -	0/12
126	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	1,823.00	0.48	- -	-	-	0/0
127	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	419.04	-	01/2017 -	06/2016	-7(O) -	0/0
128	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	490.55	09/2011 12/2015	12/2015	51(O) 0(R)	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
129	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	117.49	09/2012 12/2015	12/2015	39(O) 0(R)	0/5
130	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 -	-	-	0/2
131	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39(O) 0(R)	0/0
132	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	910.72	05/2013 12/2015	12/2015	31(O) 0(R)	1/5
133	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016	0(O) -	0/0
134	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	118.17	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
135	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,282.08	08/2015 -	12/2015	4(O) -	0/12
136	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	578.28	05/2014 05/2016	05/2016	24(O) 0(R)	0/21
137	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
138	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
139	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,561.33	01/2014 12/2015	12/2015	23(O) 0(R)	0/13
140	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	367.98	10/2014 10/2015	10/2015	12(O) 0(R)	0/0
141	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	98.96	09/2017 -	12/2017	3(O) -	0/0
142	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	7.02	- -	-	-	0/0
143	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 -	1,671.22	-	11/2019 -	11/2019	0(O) -	0/0
144	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	4,457.47	05/2015 05/2015	08/2015	3(O) 3(R)	0/17
145	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	26.70	07/2016 -	07/2016	0(O) -	4/6
146	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,222.16	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
147	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	450.37	02/2016 12/2017	12/2017	22(O) 0(R)	0/0
148	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,941.49	4,941.49	75.24	04/2016 12/2017	12/2017	20(O) 0(R)	0/6
149	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00 -	16,504.00	8,205.43	05/2016 -	05/2016	0(O) -	0/30
150	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	128.87	03/2014 05/2016	05/2016	26(O) 0(R)	0/3
151	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	890.00	0.24	- -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
152	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,360.48	12/2012 -	06/2015	-	0/14
153	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 714.25	607.06	57.96	01/2016 -	-	-	11/48
154	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	507.74	11/2015 11/2016	11/2016	12(O) 0(R)	25/29
155	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 239.73	239.73	198.69	07/2013 -	10/2015	27(O) -	0/1
156	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 -	232.00	148.69	09/2016 -	12/2015	-9(O) -	0/12
157	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017	32(O) 0(R)	0/0
158	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	1,743.40	05/2017 05/2017	05/2017	0(O) 0(R)	6/16
159	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	166.96	12/2014 -	09/2015	9(O) -	57/58
160	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	6,068.80	403.22	04/2019 -	03/2019	-1(O) -	0/0
161	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
162	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	31.94	11/2016 -	11/2016	0(O) -	5/22
163	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
164	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	428.36	08/2015 -	06/2016	10(O) -	0/0
165	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	2,321.00	1.50	- -	-	-	0/0
166	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	07/2018	0(O) -	0/31
167	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,824.71	11/2012 11/2013	10/2015	35(O) 23(R)	89/100
168	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,188.73	09/2012 -	03/2016	42(O) -	6/7
169	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	238.50	1.07	03/2017 -	03/2017	0(O) -	0/0
170	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	6.98	01/2013 -	12/2018	71(O) -	0/0
171	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,899.93	68.90	05/2017 -	05/2017	0(O) -	0/0
172	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	60.63	07/2016 -	07/2016	0(O) -	5/12
173	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	108.32	09/2017 -	09/2017	0(O) -	0/0
174	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2016	53(O) 12(R)	0/0
175	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	501.91	04/2015 04/2015	12/2015	8(O) 8(R)	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
176	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,228.45	12/2014 -	09/2015	9(O) -	0/20
177	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	57.02	02/2016 -	07/2016	5(O) -	2/6
178	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	857.20	11/2015 07/2016	07/2016	8(O) 0(R)	39/52
179	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	93.65	05/2015 -	12/2015	7(O) -	0/12
180	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	5.10	02/2016 02/2016	02/2016	0(O) 0(R)	0/0
181	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	1,149.45	11/2015 -	11/2015	0(O) -	20/24
182	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
183	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,002.51	10/2011 -	03/2016	53(O) -	0/0
184	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,430.61	01/2012 -	03/2016	50(O) -	0/0
185	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	214.19	132.32	12/2016 -	12/2016	0(O) -	0/0
186	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	320.88	03/2015 11/2015	06/2016	15(O) 7(R)	0/5
187	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 -	462.79	240.74	10/2014 10/2016	10/2016	24(O) 0(R)	28/40
188	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	287.63	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
	Total		148,572.08 -	159,409.56	70,200.48				320/716
	POWER								
189	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	318.66	12/2014 -	05/2015	-	15/17
190	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	1.00	03/2016 -	05/2016	2(O) -	4/6
191	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,802.00	01/2011 10/2014	03/2018	86(O) 41(R)	25/48
192	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51(O) -	0/0
193	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,422.00	09/2011 -	03/2017	66(O) -	15/37
194	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,924.79	05/2014 -	06/2017	37(O) -	0/0
195	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	903.85	12/2015 -	06/2016	6(O) -	17/18

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
196	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,837.46	09/2014 -	06/2016	21(O) -	12/13
197	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	810.03	06/2015 -	08/2016	14(O) -	5/5
198	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	-	06/2014 -	-	-	12/20
199	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	247.00	06/2015 -	08/2016	14(O) -	7/10
200	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017	0(O) -	4/9
201	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	780.33	-	07/2017 -	07/2017	0(O) -	0/0
202	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	1,841.00	08/2018 -	08/2018	0(O) -	13/14
203	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	31.54	02/2014 -	09/2017	43(O) -	1/1
204	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	1.00	02/2016 -	06/2016	4(O) -	9/17
205	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,138.53	11/2012 -	12/2016	49(O) -	12/13
206	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	319.24	04/2016 -	04/2016	0(O) -	12/12
207	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	33.30	11/2016 -	11/2016	0(O) -	4/12
208	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	83.82	09/2014 -	06/2016	21(O) -	0/0
209	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	-	04/2018 -	04/2018	0(O) -	0/0
210	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,736.75	05/2014 -	06/2016	25(O) -	8/12
211	FGUTPP, UNCHAHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	749.00	12/2016 -	12/2016	0(O) -	13/16
212	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	3,895.00	09/2017 -	09/2017	0(O) -	16/40
213	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	42.40	04/2017 -	04/2017	0(O) -	3/8
214	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	57.40	04/2018 -	04/2018	0(O) -	3/9

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
215	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	2.00	07/2018 -	07/2018	0(O) -	0/0
216	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	2.30	07/2016 -	07/2016	0(O) -	2/9
217	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	-	09/2017 -	09/2017	0(O) -	0/0
218	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	578.67	10/2016 -	10/2015	-12(O) -	10/10
219	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	166.90	04/2018 -	04/2018	0(O) -	3/12
220	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	588.25 -	1,007.16	1,017.21	12/2007 12/2009	10/2015	94(O) 70(R)	7/7
221	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	4,015.23	12/2009 06/2016	06/2016	78(O) 0(R)	16/28
222	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,989.30	01/2013 -	03/2016	38(O) -	0/1
223	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,107.18	01/2016 -	11/2016	10(O) -	5/9
224	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	8,877.00	01/2017 -	01/2017	0(O) -	24/31
225	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,895.55	11/2008 03/2012	12/2016	97(O) 57(R)	22/22
226	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	4,698.00	06/2017 -	06/2017	0(O) -	20/40
227	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	141.00	08/2017 -	-	-	0/9
228	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,397.00	09/2016 -	09/2016	0(O) -	24/29
229	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9(O) -	0/28
230	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	2,154.00	02/2019 -	02/2019	0(O) -	6/7
231	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,025.10	08/2013 -	12/2016	40(O) -	13/26
232	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	70.00	06/2016 -	06/2016	0(O) -	11/18
233	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	498.72	07/2013 11/2015	06/2016	35(O) 7(R)	9/9
234	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	335.37	02/2012 -	03/2016	49(O) -	10/10
235	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	474.66	11/2011 -	06/2016	55(O) -	11/11
236	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	63.40	06/2016 -	06/2016	0(O) -	10/11
237	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,368.02	04/2013 -	12/2015	32(O) -	11/11
238	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	540.92	11/2014 -	06/2016	19(O) -	9/10

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
239	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	331.99	03/2016 -	06/2016	3(O) -	10/12
240	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	201.22	05/2015 -	12/2015	7(O) -	10/12
241	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	744.54	11/2012 -	12/2015	37(O) -	10/10
242	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	4,085.09	01/2018 -	01/2018	0(O) -	0/0
243	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0
244	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,185.15	09/2009 -	12/2018	111(O) -	8/14
245	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,025.86	08/2013 03/2016	03/2016	31(O) 0(R)	28/38
246	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,381.84	120.00	09/2019 -	09/2019	0(O) -	3/3
247	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,263.00	11/2016 -	08/2017	9(O) -	23/25
248	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	2.00	08/2016 -	08/2016	0(O) -	3/4
249	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	71.50	12/2015 -	12/2015	0(O) -	7/8
250	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/3
251	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	16,885.00	7,779.10	09/2010 -	-	-	0/0
252	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH	03/2015	550.06 -	550.06	1.60	03/2018 -	03/2018	0(O) -	0/3
253	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	06/2012	1,508.74 -	1,508.74	1,028.18	03/2015 -	10/2015	7(O) -	19/21
254	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	24.10	02/2017 -	02/2017	0(O) -	0/12
255	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	203.04	03/2014 -	09/2015	18(O) -	5/7
256	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,305.13	08/2014 12/2015	09/2016	25(O) 9(R)	11/11
257	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,057.39	08/2012 -	03/2016	43(O) -	5/5
258	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	162.50	08/2016 -	03/2016	-5(O) -	10/10
259	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	203.28	0.20	07/2017 -	07/2017	0(O) -	4/5
260	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	198.19	06/2012 -	-	-	4/4

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
261	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,267.32	01/2015 -	06/2016	17(O) -	11/11
262	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE	12/2011	297.33 346.79	346.79	286.77	08/2014 06/2015	12/2015	16(O) 6(R)	10/10
263	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	487.49	386.02	06/2014 -	11/2015	17(O) -	12/12
264	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	748.00	03/2019 -	03/2019	0(O) -	8/12
265	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,534.00	03/2013 -	12/2018	69(O) -	2/15
266	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,853.00	09/2009 -	06/2016	81(O) -	2/6
267	TEHRI PUMPED STORAGE PLANT (1000MW) - [N18000010]THDCIL, UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,382.65	07/2010 02/2016	05/2018	94(O) 27(R)	6/21
268	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL, MULTI STATE	12/2011	2,422.66 -	2,422.66	2,151.06	08/2014 -	12/2015	16(O) -	11/14
269	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44 -	3,201.44	2,543.51	10/2014 -	06/2016	20(O) -	10/17
270	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 -	4,824.12	4,137.48	10/2012 -	12/2016	50(O) -	11/11
271	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL, GUJARAT	02/2014	378.71 -	378.71	85.90	10/2016 -	10/2016	0(O) -	10/11
272	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL, MULTI STATE	01/2015	268.80 -	268.80	0.80	03/2018 -	03/2018	0(O) -	0/3
273	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 -	1,927.16	1,539.87	10/2014 -	10/2015	12(O) -	11/15
274	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL, MULTI STATE	06/2014	400.47 -	400.47	12.10	04/2017 -	04/2017	0(O) -	0/3
275	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL, MULTI STATE	09/2013	1,575.30 -	1,575.30	409.80	05/2016 -	05/2016	0(O) -	12/13
276	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL, MULTI STATE	02/2010	2,144.00 -	2,144.00	2,187.60	12/2012 -	06/2016	42(O) -	12/23
277	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7&8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	307.18	0.80	11/2017 -	11/2017	0(O) -	0/0
278	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62 -	871.62	1.90	10/2017 -	11/2017	1(O) -	5/5
279	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL, ANDHRA PRADESH	08/2014	188.75 -	188.75	1.00	02/2017 -	03/2016	-11(O) -	0/2
280	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	539.80	02/2014 -	12/2015	22(O) -	10/10

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
281	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,084.75	01/2015 -	12/2016	23(O) -	11/16
282	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND	10/2011	558.26 -	558.26	468.01	11/2013 -	12/2015	25(O) -	12/12
283	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL, ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,886.04	03/2013 06/2015	10/2015	31(O) 4(R)	11/11
284	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL, ODISHA	12/2010	2,743.19 -	2,743.19	2,801.90	12/2013 -	09/2015	21(O) -	11/11
285	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	151.20	01/2013 -	11/2015	34(O) -	13/15
286	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	1,585.12	1,507.86	11/2013 -	12/2015	25(O) -	12/12
287	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL, ANDHRA PRADESH	05/2015	312.94 -	312.94	-	05/2016 -	05/2016	0(O) -	0/0
288	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL, CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,224.73	07/2014 -	06/2016	23(O) -	8/8
289	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE	06/2014	5,151.37 -	5,151.37	498.00	03/2018 -	03/2018	0(O) -	12/12
290	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEPCO, TRIPURA	07/2009	421.01 1,007.68	1,007.68	907.18	07/2013 -	09/2015	26(O) -	25/26
291	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NNEPCO, MIZORAM	07/1998	368.72 1,381.71	1,381.71	872.46	07/2006 10/2016	10/2016	123(O) 0(R)	5/13
292	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	11/2016	7(O) -	0/0
293	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58 -	3,745.08	724.79	06/2013 -	12/2019	78(O) -	2/8
294	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL, MULTI STATE	01/2015	3,662.02 -	3,662.02	137.90	05/2018 -	05/2018	0(O) -	3/5
295	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, MAHARASHTRA	12/2007	477.69 721.81	721.81	521.59	09/2010 06/2013	06/2016	69(O) 36(R)	7/8
296	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,854.89	06/2015 -	06/2016	12(O) -	23/30
	Total		295,956.73 -	335,667.00	161,731.90				891/1293
	HEAVY INDUSTRY								
297	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE, MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		1,718.00 -	3,827.30	.00				0/0
	<u>RAILWAYS</u>								
298	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MTRP, TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	03/2016	0(O) -	0/0
299	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
300	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
301	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
302	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	-	0/0
303	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
304	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
305	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
306	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	873.71	-	- -	-	-	0/0
307	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	218.39	23.63	- -	-	-	0/0
308	AJMER-KOTA (NASIRABAD- JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
309	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR, MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
310	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
311	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	242.09	0.39	- -	-	-	0/0
312	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR, MULTI STATE	04/2010	338.54 -	338.54	129.14	- -	-	-	0/0
313	AMBARA FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
314	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
315	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	295.68	0.86	- -	-	-	0/0
316	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
317	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
318	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
319	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
320	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	960.00	-	-	-	-	0/0
321	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	-	-	-	0/0
322	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	76.08	-	-	-	0/0
323	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	100.76	-	-	-	0/0
324	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	9.60	-	-	-	0/0
325	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012	09/2015	33(O)	0/0
326	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	1,382.78	2.81	-	-	-	0/0
327	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	4.20	-	-	-	0/0
328	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
329	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,106.62	244.99	12/2010	-	-	0/0
330	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	13.53	-	-	-	0/0
331	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	255.64	-	-	-	-	0/0
332	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
333	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	337.50	0.21	-	-	-	0/0
334	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	923.23	1.01	-	-	-	0/0
335	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	837.33	1.15	-	-	-	0/0
336	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	760.00	0.09	-	-	-	0/0
337	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
338	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	-	-	-	0/0
339	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011	-	-	0/0
340	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	94.11	-	-	-	0/0
341	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010	12/2015	69(O)	0/0
342	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	2.91	03/2012	-	-	0/0
343	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.68	-	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
344	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.46	-	-	-	0/0
345	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	434.00	35.90	-	-	-	0/0
346	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
347	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	-	02/2012	-	0/0
348	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
349	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.30	-	-	-	0/0
350	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	61.36	-	-	-	0/0
351	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	619.87	-	03/2015	-	0/0
352	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	112.40	-	-	-	0/0
353	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	520.00	462.69	-	-	-	0/0
354	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.07	-	-	-	0/0
355	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	4.22	-	-	-	0/0
356	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	111.87	-	-	-	0/0
357	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	-	03/2017	-	0/0
358	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	30.05	-	-	-	0/0
359	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	-	-	-	0/0
360	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	-	-	-	0/0
361	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	-	-	-	0/0
362	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	164.55	-	-	-	0/0
363	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	573.78	166.89	-	-	-	0/0
364	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108(O) -	0/0
365	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.56	-	-	-	0/0
366	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	-	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
367	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
368	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	1,640.04	187.84	-	-	-	0/0
369	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
370	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
371	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
372	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	339.00	204.83	-	-	-	0/0
373	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	296.44 -	296.44	4.55	-	-	-	0/0
374	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
375	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	410.08	297.58	-	-	-	0/0
376	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	234.71	137.01	03/2015 -	03/2015	-	0/0
377	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR, MULTI STATE	04/2013	1,239.00 -	1,239.00	-	-	-	-	0/0
378	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91 -	336.91	144.25	-	-	-	0/0
379	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
380	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	376.59	4.58	-	-	-	0/0
381	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
382	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	-	12/2019	-	0/0
383	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,487.70	-	-	03/2020	-	0/0
384	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	914.98	846.18	-	03/2016	-	0/0
385	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27(O) -	0/0
386	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
387	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	189.24	1.52	-	-	-	0/0
388	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 -	603.22	1.64	-	-	-	0/0
389	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82(O) -	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
390	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
391	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	-	-	-	0/0
392	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	1.89	-	-	-	0/0
393	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
394	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	14.00	-	-	-	0/0
395	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	-	-	-	0/0
396	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	197.73	-	-	-	-	0/0
397	GHUTIAHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
398	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	141.82	02/2006 -	-	-	0/0
399	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
400	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.00	-	-	-	0/0
401	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	-	-	-	0/0
402	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0
403	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
404	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	179.32	75.76	-	-	-	0/0
405	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
406	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	-	-	-	0/0
407	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	720.00	-	-	-	-	0/0
408	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	367.17	17.19	-	-	-	0/0
409	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	324.66	227.03	-	-	-	0/0
410	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	-	-	-	0/0
411	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	-	-	-	0/0
412	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	-	-	0/0
413	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	2.38	-	-	-	0/0
414	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	1,092.98	-	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	172.58	-	-	-	0/0
416	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	96.76	03/2015 -	03/2015	-	0/0
417	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	-	-	-	0/0
418	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	153.29	-	09/2015	-	0/0
419	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	325.00	-	-	-	0/0
420	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	1,618.00	-	-	-	-	0/0
421	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	-	-	-	0/0
422	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	-	0/0
423	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	-	-	-	0/0
424	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	1,900.00	-	-	-	-	0/0
425	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	117.24	-	-	-	0/0
426	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
427	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.55	258.78	03/2014 -	-	-	0/0
428	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	143.62	-	-	-	0/0
429	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
430	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	1,043.56	819.19	03/2012 -	-	-	0/0
431	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	40.00	-	-	-	0/0
432	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	230.00	218.67	-	-	-	0/0
433	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
434	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
435	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.45	-	-	-	0/0
436	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	-	-	-	0/0
437	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	-	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
438	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.73	-	-	-	0/0
439	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	-	03/2018	-	0/0
440	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	-	-	-	0/0
441	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	-	03/2016	-	1/1
442	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	800.70	-	-	-	0/0
443	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012	03/2016	39(O)	0/0
444	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010	03/2018	87(O)	0/0
445	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	163.59	03/2017	03/2017	0(O)	0/0
446	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	8.06	-	-	-	0/0
447	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	541.00	158.58	-	-	-	0/0
448	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	277.33	03/2009 03/2009	08/2014	-	0/0
449	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	-	-	-	0/0
450	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	-	03/2018	-	0/0
451	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	03/2014	03/2018	48(R)	0/0
452	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	682.31	-	03/2010	-	0/0
453	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005	-	-	0/0
454	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	260.67	-	-	-	0/0
455	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	-	-	-	0/0
456	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	325.36	03/2012	-	-	0/0
457	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	-	-	-	0/0
458	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.48	-	-	-	0/0
459	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	-	-	-	0/0
460	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.61	-	-	-	0/0
461	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	-	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
462	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0
463	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
464	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
465	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0
466	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
467	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
468	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.69	- -	-	-	0/0
469	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRATH-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
470	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0
471	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
472	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
473	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
474	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	188.93	- -	-	-	0/0
475	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	498.37	03/2012 -	-	-	0/0
476	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
477	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	279.54	1.38	01/1999 -	-	-	0/0
478	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.82	- -	-	-	0/0
479	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	457.88	- -	-	-	0/0
480	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	7.50	- -	-	-	0/0
481	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	1,830.00	-	- -	-	-	0/0
482	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
483	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
484	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
485	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	- -	-	-	0/0
486	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
487	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.69	- -	-	-	0/0
488	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
489	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	- -	03/2015	-	0/0
490	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	380.62	- -	-	-	0/0
491	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	- -	0/0
492	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
493	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
494	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	- -	-	-	0/0
495	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
496	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
497	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
498	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
499	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	- -	0/0
500	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	- -	0/0
501	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	- -	0/0
502	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
503	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	- -	0/0
504	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	- -	0/0
505	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	- -	0/0
506	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	- -	0/0
507	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
508	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
509	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	- -	0/0
510	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
511	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
512	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.37	03/2014 -	-	-	0/0
513	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.02	536.36	03/2016 -	03/2016	0(O) -	0/0
514	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(O) -	0/0
515	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,951.98	626.11	03/2016 -	03/2016	0(O) -	0/0
516	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	424.42	03/2008 06/2008	-	-	0/0
517	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
518	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
519	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	240.21	- -	01/2015	-	0/0
520	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
521	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	712.02	- -	02/2014	-	0/0
522	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	- -	03/2015	-	0/0
523	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	600.00	-	- -	-	-	0/0
524	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
525	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
526	PLASSEY-JAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	-	0/0
527	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
528	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
529	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
530	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	1,030.00	800.90	01/1999 -	-	-	0/0
531	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	1,122.00	889.95	-	-	-	0/6
532	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	289.93	277.09	12/2007 03/2010	-	-	0/0
533	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	79(O) 34(R)	0/0
534	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	305.47	02/2009 02/2009	08/2014	-	0/0
535	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
536	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]JWR,GUJARAT	04/1994	320.66 913.48	913.48	457.67	-	-	-	0/0
537	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	30(O) -	0/0
538	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	-	03/2017	-	0/0
539	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138(O) -	0/0
540	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	1.09	-	-	-	0/0
541	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	794.11	-	-	-	0/0
542	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	3,500.00	54.23	-	-	-	0/0
543	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]JWR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
544	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	359.06	-	-	-	0/0
545	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	400.00	-	-	-	-	0/0
546	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	576.18	3.40	-	-	-	0/0
547	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11(O) -	0/0
548	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	53.01	-	-	-	0/0
549	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	258.31	-	-	-	0/0
550	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	294.07	-	-	-	0/0
551	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	230.21	03/2010 -	-	-	0/0
552	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	380.00	-	-	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	- -	0/0
554	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	- -	-	-	0/0
555	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
556	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
557	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.94	- -	-	-	0/0
558	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0
559	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
560	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
561	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	-	-	0/0
562	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
563	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	113.50	02/2015 -	-	-	0/0
564	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	- -	-	-	0/0
565	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	516.23	597.72	03/2014 -	-	-	0/0
566	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	160.80	- -	-	-	0/0
567	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
568	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
569	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
570	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
571	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	- -	-	-	0/0
572	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	0.41	- -	-	-	0/0
573	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	- -	-	-	0/0
574	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	- -	-	-	0/0
575	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
576	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	-	-	-	0/0
577	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
578	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.32	-	-	-	0/0
579	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.47	-	-	-	0/0
580	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O) -	0/0
581	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
582	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	-	-	-	0/0
583	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
584	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	-	-	-	0/0
585	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	-	-	-	0/0
586	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
587	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	-	-	-	0/0
588	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	-	-	-	0/0
589	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	-	-	-	0/0
590	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	-	-	-	0/0
591	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	-	-	-	0/0
592	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	-	-	-	0/0
593	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	-	-	-	-	0/0
	Total		171,881.41 -	296,947.84	90,385.01				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
594	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	340.00	-	03/2016 -	03/2016	0(O) -	0/0
595	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	303.40	08/2013 -	-	-	0/0
596	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	65.26	10/2014 -	-	-	0/0
597	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	28.51	07/2014 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
598	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	-	-	0/0
599	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	579.50	11/2013 -	-	-	0/0
600	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	-	-	0/0
601	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	-	07/2014 -	-	-	0/0
602	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	240.10	-	03/2016 -	03/2016	0(O)	0/0
603	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	-	12/2015 -	12/2015	0(O)	0/0
604	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	177.32	-	01/2016 -	01/2016	0(O)	0/0
605	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	52.86	01/2014 -	-	-	0/0
606	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
607	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
608	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	124.40	04/2014 -	-	-	0/0
609	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	-	05/2014 -	-	-	0/0
610	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	677.79	-	04/2016 -	04/2016	0(O)	0/0
611	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	52.01	09/2014 -	-	-	0/3
612	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	-	-	0/0
613	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,151.00	06/2013 -	-	-	0/3
614	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	38.30	09/2013 -	-	-	0/0
615	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	745.80	08/2013 -	-	-	0/3
616	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O)	0/0
617	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19(O)	0/0
618	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	805.50	08/2013 -	-	-	0/0
619	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	967.10	08/2013 -	-	-	0/0
620	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	218.50	08/2013 -	-	-	0/0
621	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	-	10/2015 -	10/2015	0(O)	0/0
622	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	712.70	07/2013 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
623	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	-	-	0/0
624	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	348.16	269.40	09/2007 -	-	-	0/0
625	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015	0(O) -	0/3
626	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
627	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	291.00	09/2013 -	-	-	0/0
628	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	429.10	02/2015 -	-	-	0/0
629	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17(O) -	0/0
630	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	438.00	-	-	-	2/2
631	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35(O) -	0/0
632	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	450.90	08/2013 -	-	-	0/0
633	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	237.80	-	06/2008 -	-	-	0/0
634	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00 -	195.00	-	06/2008 -	-	-	0/0
635	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	-	-	0/0
636	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
637	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
638	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	790.90	03/2013 -	-	-	0/0
639	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	353.37	395.10	10/2011 -	-	-	0/0
640	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	572.30	761.40	10/2011 -	-	-	0/0
641	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH, GOA	03/2015	280.16 -	280.16	-	-	-	-	0/0
642	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH, GOA	03/2015	184.05 -	184.05	-	-	-	-	0/0
643	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA	01/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017	0(O) -	0/0
644	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA	01/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017	0(O) -	0/0
645	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD, TELANGANA	03/2011	218.31 -	339.82	-	12/2015 -	12/2015	0(O) -	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
646	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP, MAHARASHTRA	03/2015	168.30 -	168.30 -	-	- -	10/2017	- -	0/0
647	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO 45 - [N24000253]NHDP, MAHARASHTRA	08/2014	187.79 -	187.79 -	-	07/2016 -	07/2016	0(O) -	0/0
648	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH, GOA	03/2015	298.33 -	298.33 -	-	- -	-	-	0/0
649	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00 -	957.80	05/2013 -	-	-	0/0
650	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00 -	300.00 -	-	10/2008 -	-	-	0/0
651	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22 -	255.30	04/2015 -	04/2015	-	0/0
652	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00 -	638.00	05/2010 -	-	-	0/0
653	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00 -	485.70	07/2013 -	-	-	0/0
654	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00 -	-	06/2013 -	-	-	0/0
655	DEVIHALLI-HASSAN - [N24000152]NHAI, KARNATAKA	12/2010	453.00 -	453.00 -	487.90	- -	-	-	1/1
656	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00 -	289.50	06/2008 -	05/2015	-	0/0
657	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00 -	197.60	05/2008 12/2015	12/2015	91(O) 0(R)	0/0
658	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45 -	-	09/2010 -	-	-	0/0
659	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	153.21 -	-	01/2017 -	01/2017	0(O) -	0/0
660	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	1,573.00 -	13.39	09/2015 -	09/2015	0(O) -	0/0
661	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94 -	-	09/2008 -	-	-	0/0
662	FOUR LANNING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79 -	-	11/2016 -	11/2016	0(O) -	0/0
663	FOUR LANNING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	1,232.00 -	590.90	08/2015 -	02/2016	6(O) -	0/0
664	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP, GOA	03/2015	297.00 -	297.00 -	-	- -	10/2017	- -	0/0
665	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	682.00 -	34.81	10/2013 -	-	-	0/0
666	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66 -	-	09/2008 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
667	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,200.00	08/2013 -	-	-	0/0
668	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	-	-	2/3
669	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 12/2015	12/2015	92(O) 0(R)	0/0
670	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 08/2015	08/2015	88(O) 0(R)	0/0
671	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	-	-	0/0
672	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	-	-	0/0
673	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	-	-	0/0
674	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	-	-	0/0
675	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	245.20	10/2013 -	-	-	0/0
676	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	-	0/0
677	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	-	-	-	3/3
678	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	447.50	05/2013 -	-	-	0/0
679	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	-	-	0/0
680	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	564.50	02/2013 -	-	-	0/0
681	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,649.00	12/2012 -	-	-	0/0
682	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	-	-	0/0
683	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	450.50	01/2014 -	-	-	0/0
684	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	560.10	07/2013 -	-	-	0/0
685	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,056.00	05/2012 -	-	-	0/0
686	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	-	10/2008 -	-	-	0/0
687	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	398.20	07/2014 -	-	-	0/0
688	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	-	12/2015	-	2/3
689	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	-	07/2012 -	-	-	0/0
690	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	-	-	0/0
691	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
692	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	-	-	0/0
693	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	-	-	0/0
694	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	1,313.00	06/2013 -	-	-	0/0
695	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	511.00	03/2013 -	-	-	0/0
696	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	-	-	0/0
697	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17(O)	0/0
698	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2017	01/2017	105(O) 0(R)	0/0
699	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 11/2015	11/2015	89(O) 0(R)	0/0
700	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
701	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	-	06/2015 -	-	-	0/0
702	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	494.70	09/2013 -	-	-	0/0
703	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	932.30	02/2010 -	-	-	0/0
704	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O)	0/0
705	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21(O)	0/0
706	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	-	-	0/0
707	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	-	0/0
708	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	128.50	06/2014 -	-	-	0/0
709	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	536.00	03/2014 -	-	-	0/0
710	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	-	-	0/0
711	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,293.00	07/2012 -	-	-	0/0
712	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,127.00	03/2013 -	-	-	0/0
713	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	122.70	01/2014 -	-	-	0/0
714	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	764.60	07/2015 -	-	-	0/0
715	RAJMARG CHORAHA TO LAKHNANDON KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	326.30	10/2008 -	01/2015	-	0/0
716	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	162.70	06/2015 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
717	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	152.50	09/2014 -	-	-	0/0
718	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	220.72	-	11/2016 -	11/2016	0(0) -	0/0
719	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	260.39	-	11/2016 -	11/2016	0(0) -	0/0
720	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	446.77	-	-	06/2017	-	0/0
721	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	201.12	14.71	02/2015 -	02/2015	-	0/0
722	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	158.65	-	03/2016 -	03/2016	0(0) -	0/3
723	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	177.18	-	03/2016 -	03/2016	0(0) -	0/3
724	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	270.00	-	03/2016 -	03/2016	0(0) -	0/0
725	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA- JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	0(0) -	0/0
726	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA- JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	244.30	-	12/2016 -	12/2016	0(0) -	0/0
727	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	928.70	11/2013 -	-	-	0/0
728	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	543.70	03/2013 -	-	-	0/0
729	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	07/2015	-	0/0
730	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	228.30	09/2007 03/2014	03/2015	-	0/0
731	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
732	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21(0) -	0/0
733	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	-	12/2013 -	-	-	0/0
734	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	14.58	12/2013 -	-	-	0/0
735	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	823.00	05/2014 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
736	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	154.50	08/2012 -	-	-	0/0
737	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2016	01/2016	94(O) 0(R)	0/0
738	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	-	-	0/0
739	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	09/2016	61(O) -	2/2
740	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	891.10	11/2013 -	-	-	0/0
741	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	-	-	0/0
742	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	101.30	05/2013 -	-	-	0/0
743	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	188.40	-	07/2014	-	2/2
744	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37(O) -	0/0
745	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	-	-	-	0/0
746	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	-	11/2012 -	-	-	0/0
747	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	0(O) -	0/0
748	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	-	01/2016 -	01/2016	0(O) -	0/0
749	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	02/2014 -	-	-	0/0
750	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
751	YAN TO NIRMAL SEREHAIBLITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	244.08	-	03/2016 -	03/2016	0(O) -	0/0
	Total		105,220.04 -	107,360.97	55,483.94				14/34
	SHIPPING AND PORTS								
752	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN - [N25000064]SHIPP.,MAHARASHTRA	10/2010	994.82 -	402.24	427.54	11/2013 -	11/2013	-	0/0
753	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 2,099.00	1,460.00	1,038.00	12/2010 -	09/2017	81(O) -	0/0
754	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	407.32	12/2010 -	01/2016	61(O) -	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
755	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2015	117(O) -	0/0
756	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	373.22	351.18	04/2009 -	-	-	0/0
757	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	837.90	10/2008 -	-	-	0/0
	Total		5,412.28 -	5,932.32	3,201.74				0/0
	<u>TELECOMMUNICATIONS</u>								
758	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	72.17	10/2010 08/2015	10/2015	60(O) 2(R)	0/0
759	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015	-	0/0
	Total		13,718.00 -	13,718.00	72.17				0/0
	<u>URBAN DEVELOPMENT</u>								
760	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
761	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	05/2015	-	0/0
762	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	-	-	3/3
763	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
764	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,032.96	12/2015 -	08/2016	8(O) -	1/24
765	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34(O) -	0/0
766	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24(O) -	0/0
767	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	142.00	05/2013 -	10/2015	29(O) -	0/0
768	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
769	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0
770	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	-	08/2007 -	03/2015	-	0/0
771	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0

Sector Wise Details									
(August 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
772	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2(O) -	0/0
773	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15(O) -	0/0
774	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	-	03/2017 -	03/2017	0(O) -	0/0
775	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	16,971.38	03/2016 -	12/2016	9(O) -	0/0
776	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	-	03/2010 -	10/2014	-	0/0
777	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11(O) -	0/0
778	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
779	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	1,280.91	09/2014 -	08/2015	11(O) -	0/0
780	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017	0(O) -	0/0
781	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	-	07/2012 -	06/2014	-	0/0
782	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(O) -	0/0
783	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018	0(O) -	0/0
784	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	1.75	11/2014 -	12/2014	-	0/0
785	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	4,264.00	609.63	11/2019 -	11/2019	0(O) -	0/7
786	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	246.90	-	-	-	-	0/0
787	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	-	09/2014 -	-	-	0/0
788	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	09/2016	0(O) -	0/0
789	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	-	03/2012 -	04/2015	-	0/0
	Total		138,680.82 -	143,894.82	32,315.10				4/34
	Grand Total		1,058,599.45	1,262,592.29	518,326.58				1878/3818


Summary of projects in the Flash Report for the month of August, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	769
Number of Projects completed/dropped/frozen in Current Month	13
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	32
Number of Projects in Current Month	789


Brief Analysis

Project Status with respect to Original Schedule: Out of 789 projects, 7 projects are ahead of schedule, 139 projects are on schedule 232 projects are delayed. 380 projects do not have fixed dates of commissioning. 31 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

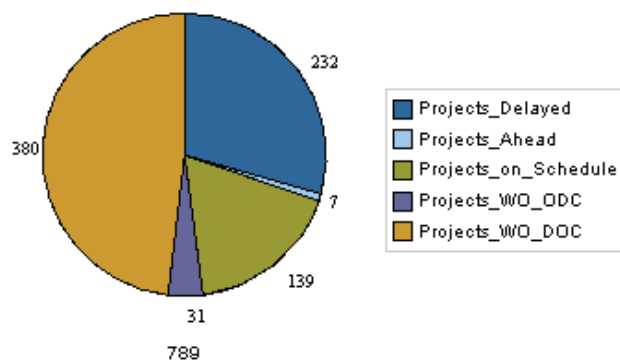

Investment Scenario

Total original cost of implementation of 789 projects when sanctioned, was of the order of Rs. 1058599.45 crore but this was subsequently revised to Rs. 1262592.29 crore implying a cost overrun of 19.3%. The expenditure incurred on these projects till August, 2015 is Rs. 518326.58 crore, which is 41.1% of the revised cost of the projects.

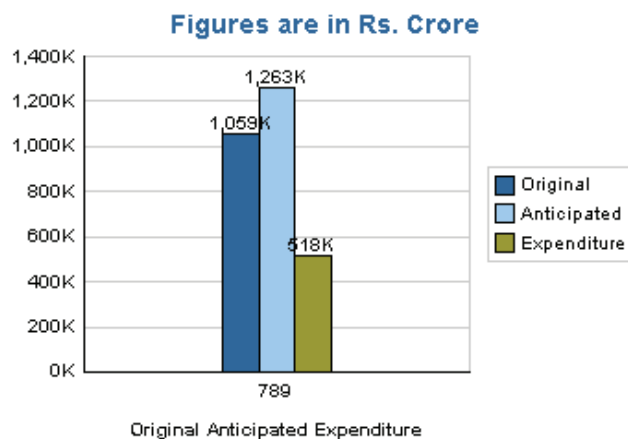

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

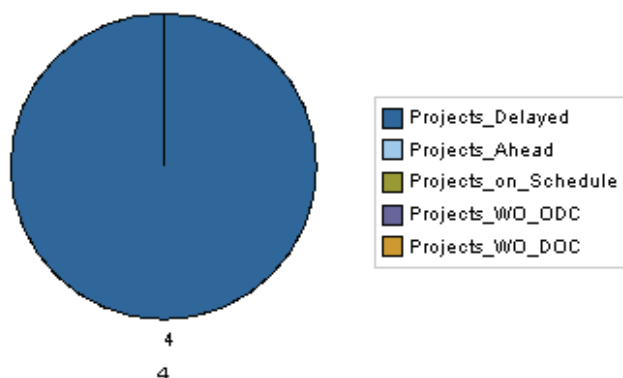

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till August, 2015 is Rs. 37827.45 crore, which is 81% of the revised cost of the projects.

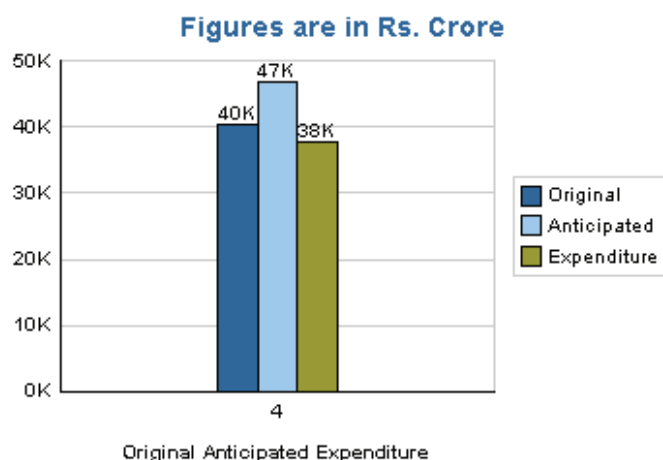

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	6
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 3 projects are delayed. 3 projects do not have fixed dates of commissioning.

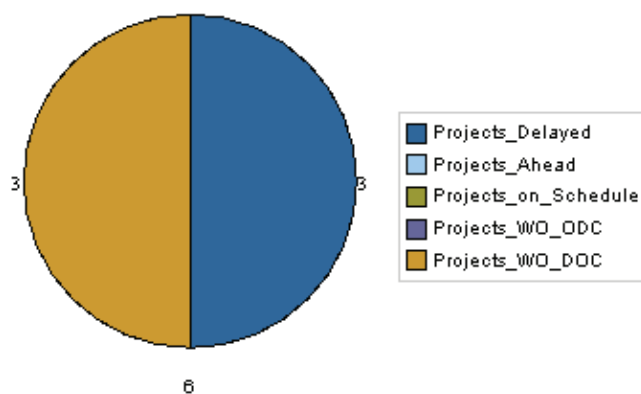

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 1973.56 crore but this was subsequently anticipated to Rs. 2063.48 crore implying a cost overrun of 4.6%. The expenditure incurred on these projects till August, 2015 is Rs. 1193.81 crore, which is 57.9% of the revised cost of the projects.

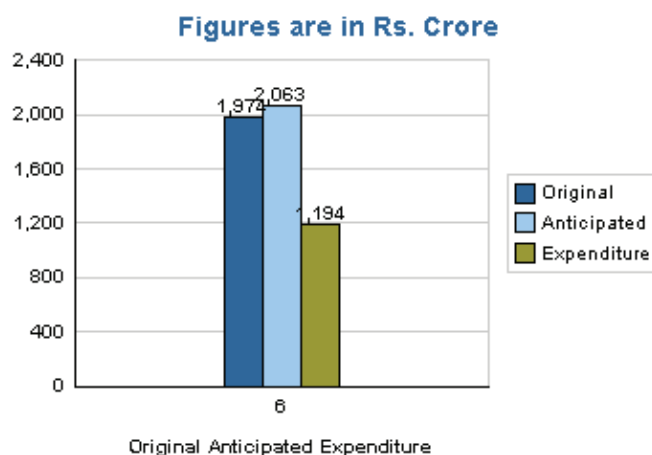

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	80
Number of Projects On Schedule	32
Number of Projects Delayed	44
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 80 projects, 1 project is ahead of schedule, 32 projects are on schedule 44 projects are delayed. 3 projects do not have fixed dates of commissioning.

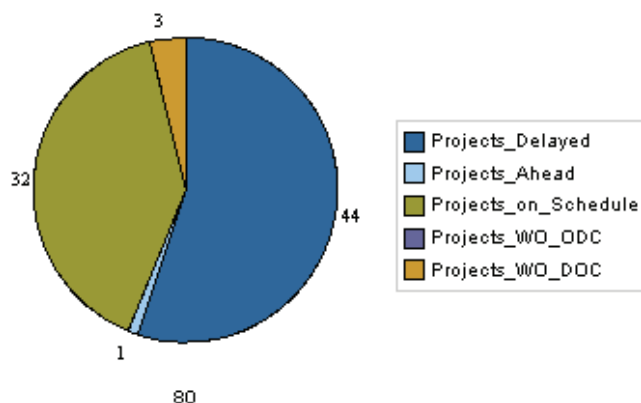

Investment Scenario

Total original cost of implementation of 80 projects when sanctioned, was of the order of Rs. 61374.97 crore but this was subsequently anticipated to Rs. 65278.13 crore implying a cost overrun of 6.4%. The expenditure incurred on these projects till August, 2015 is Rs. 22901.46 crore, which is 35.1% of the revised cost of the projects.

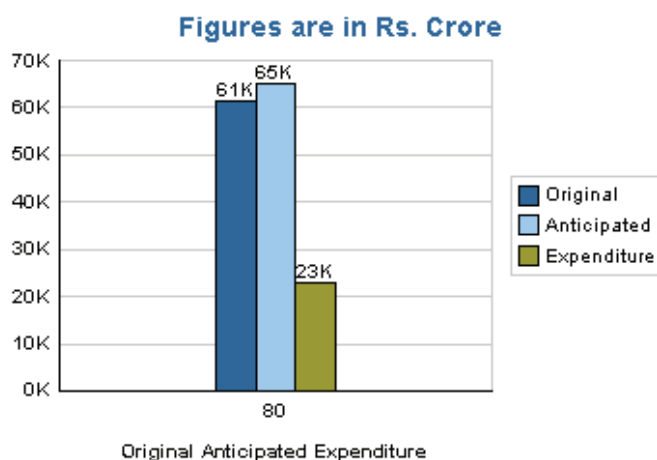

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	26
Number of Projects On Schedule	10
Number of Projects Delayed	11

Number of Projects Without Date Of Commissioning	5
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 26 projects, 10 projects are on schedule 11 projects are delayed. 5 projects do not have fixed dates of commissioning.

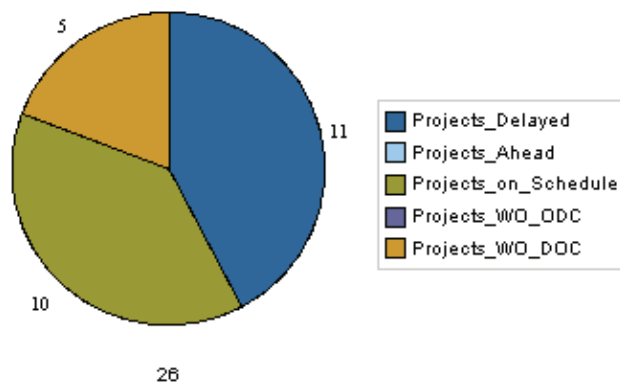

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 66135.16 crore but this was subsequently anticipated to Rs. 69879.56 crore implying a cost overrun of 5.7%. The expenditure incurred on these projects till August, 2015 is Rs. 42983.16 crore, which is 61.5% of the revised cost of the projects.

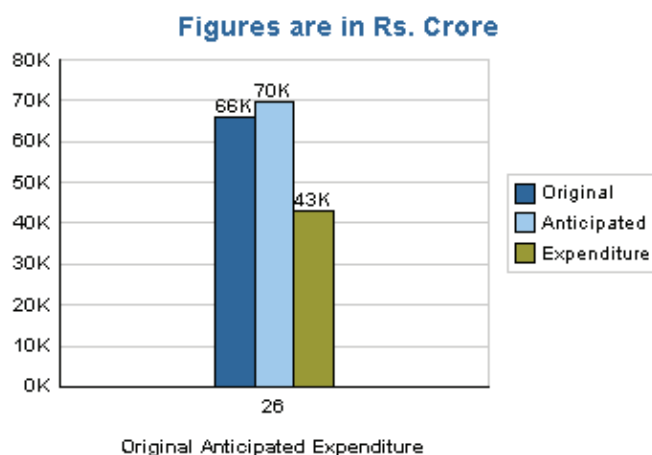

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	69
Number of Projects On Schedule	17
Number of Projects Delayed	41
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	8

Brief Analysis


Project Status with respect to Original Schedule: Out of 69 projects, 3 projects are ahead of schedule, 17 projects are on schedule 41 projects are delayed. 8 projects do not have fixed dates of commissioning.

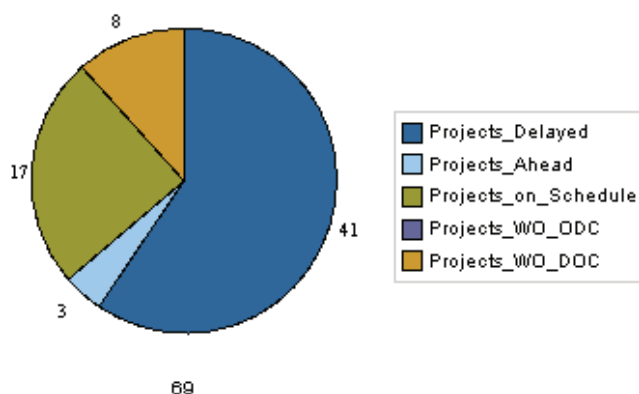

Investment Scenario

Total original cost of implementation of 69 projects when sanctioned, was of the order of Rs. 148572.08 crore but this was subsequently anticipated to Rs. 159409.56 crore implying a cost overrun of 7.3%. The expenditure incurred on these projects till August, 2015 is Rs. 70200.48 crore, which is 44% of the revised cost of the projects.

Figures are in Rs. Crore

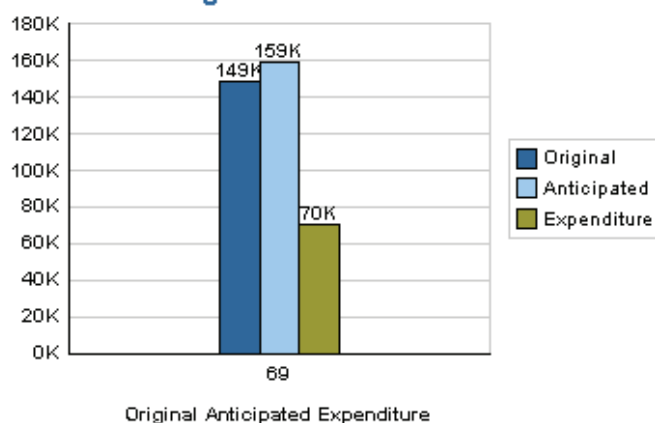

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	108
Number of Projects On Schedule	38
Number of Projects Delayed	62
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 108 projects, 3 projects are ahead of schedule, 38 projects are on schedule 62 projects are delayed. 5 projects do not have fixed dates of commissioning.

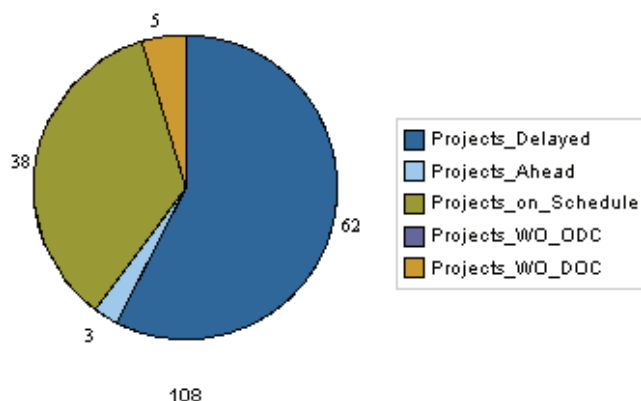

Investment Scenario

Total original cost of implementation of 108 projects when sanctioned, was of the order of Rs. 295956.73 crore but this was subsequently anticipated to Rs. 335667 crore implying a cost overrun of 13.4%. The expenditure incurred on these projects till August, 2015 is Rs. 161731.9 crore, which is 48.2% of the revised cost of the projects.

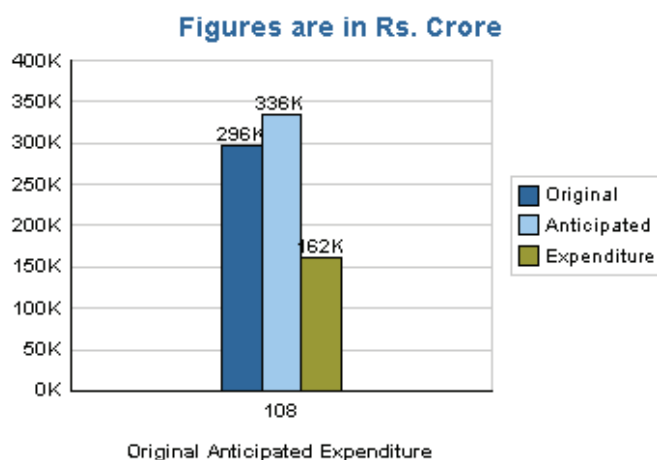

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	296
Number of Projects On Schedule	8
Number of Projects Delayed	31
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	230


Brief Analysis

Project Status with respect to Original Schedule: Out of 296 projects, 8 projects are on schedule 31 projects are delayed. 230 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

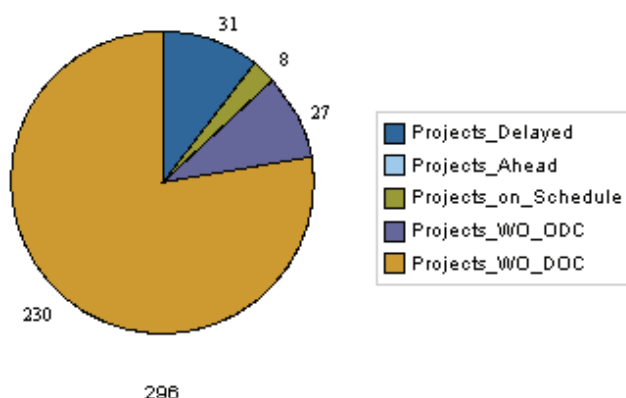

Investment Scenario

Total original cost of implementation of 296 projects when sanctioned, was of the order of Rs. 171881.41 crore but this was subsequently anticipated to Rs. 296947.84 crore implying a cost overrun of 72.8%. The expenditure incurred on these projects till August, 2015 is Rs. 90385.01 crore, which is 30.4% of the revised cost of the projects.

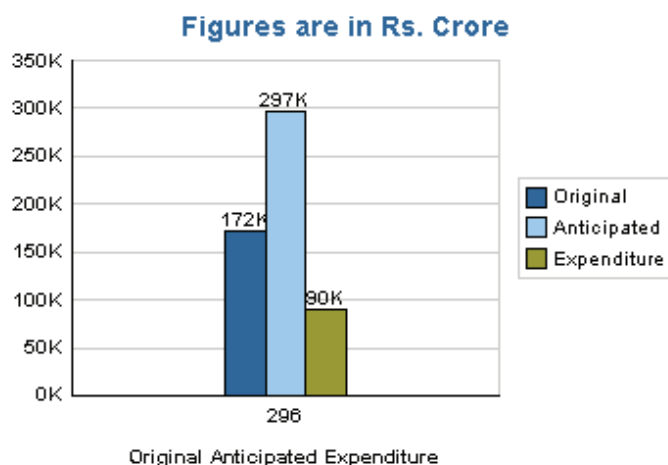

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHW

Current Status:

Number of Projects	158
Number of Projects On Schedule	25
Number of Projects Delayed	17
Number of Projects Without Original Date of Commissioning	4
Number of Projects Without Date Of Commissioning	112


Brief Analysis

Project Status with respect to Original Schedule: Out of 158 projects, 25 projects are on schedule 17 projects are delayed. 112 projects do not have fixed dates of commissioning. 4 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

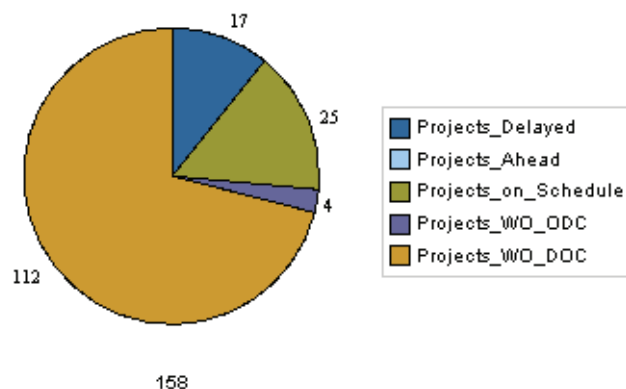

Investment Scenario

Total original cost of implementation of 158 projects when sanctioned, was of the order of Rs. 105220.04 crore but this was subsequently anticipated to Rs. 107360.97 crore implying a cost overrun of 2%. The expenditure incurred on these projects till August, 2015 is Rs. 55483.94 crore, which is 51.7% of the revised cost of the projects.

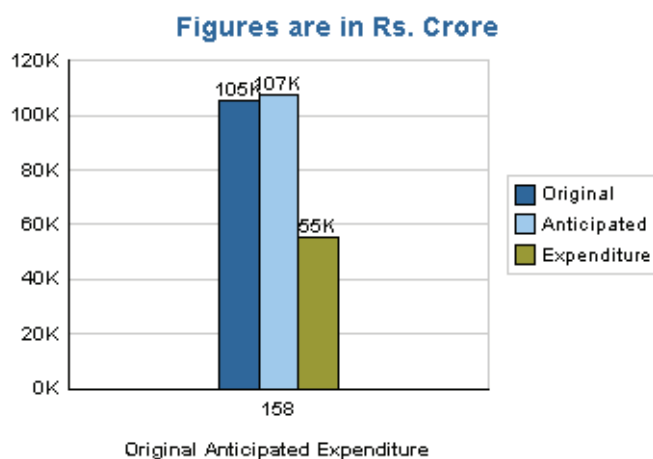

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	6
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 3 projects are delayed. 3 projects do not have fixed dates of commissioning.

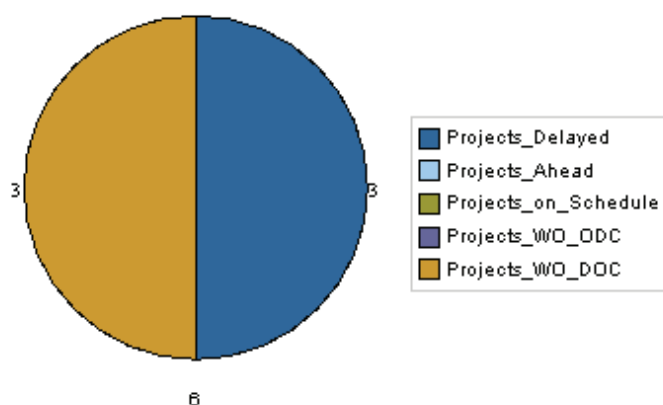

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5412.28 crore but this was subsequently anticipated to Rs. 5932.32 crore implying a cost overrun of 9.6%. The expenditure incurred on these projects till August, 2015 is Rs. 3201.74 crore, which is 54% of the revised cost of the projects.

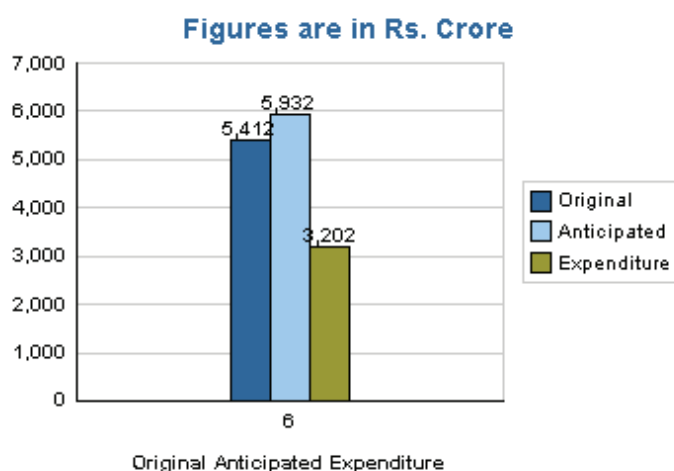

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

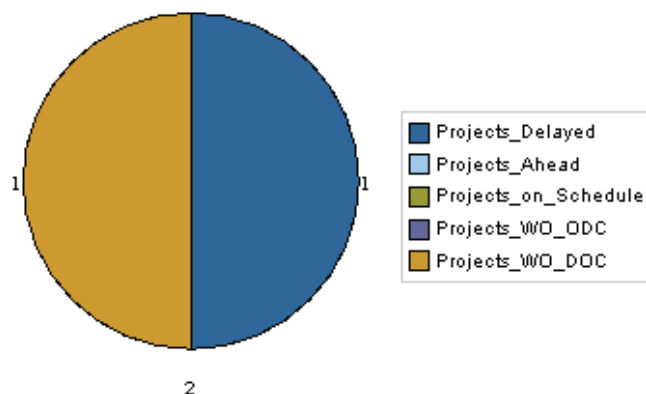

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 13718 crore but this was subsequently anticipated to Rs. 13718 crore. The expenditure incurred on these projects till August, 2015 is Rs. 72.17 crore, which is .5% of the revised cost of the projects.

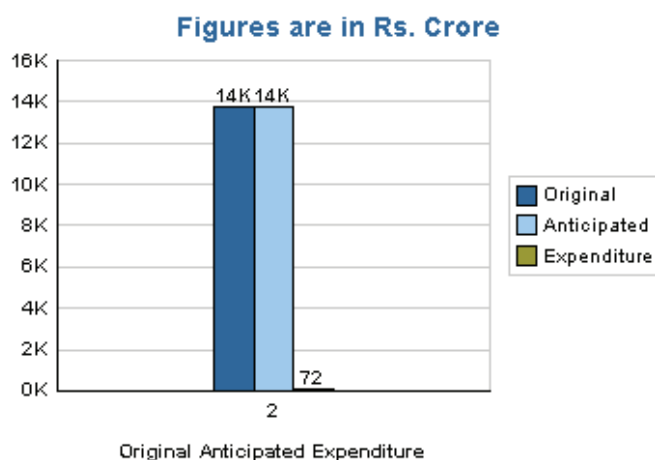

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	30
Number of Projects On Schedule	7
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	10
--	----


Brief Analysis

Project Status with respect to Original Schedule: Out of 30 projects, 7 projects are on schedule 13 projects are delayed. 10 projects do not have fixed dates of commissioning.

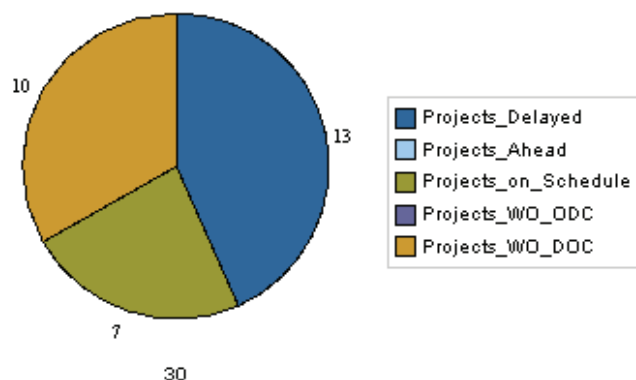

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 138680.82 crore but this was subsequently anticipated to Rs. 143894.82 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till August, 2015 is Rs. 32315.1 crore, which is 22.5% of the revised cost of the projects.

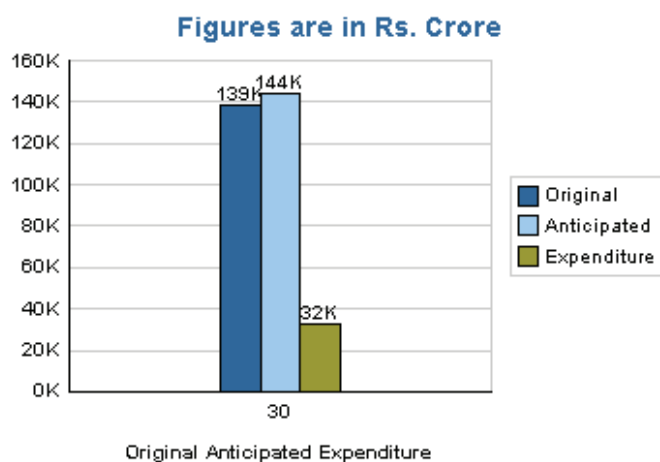

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE					
S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	(All Cost /Expenditure in Rs. crore)	
				COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	18.02
2	ANDHRA PRADESH	28	24696.13	30412.21	16630.99
3	ARUNACHAL PRADESH	3	9356.22	24848.83	12820.19
4	ASSAM	34	22255.53	37810.44	19083.25
	BIHAR	47	50385.63	64163.83	33027.34
6	CHANDIGARH	1	452.00	489.00	439.81
7	CHHATISGARH	28	80681.93	82344.09	45058.13
8	D & N HAVELI	1	6086.08	6086.08	118.17
9	DELHI	12	50903.45	50903.45	19057.78
	GOA	5	1395.15	1448.07	302.35
11	GUJARAT	28	36601.56	37389.20	18360.29
12	HARYANA	9	4659.81	6630.43	6885.30
13	HIMACHAL PRADESH	4	7154.09	12973.29	5225.95
14	JAMMU AND KASHMIR	7	21314.62	40235.30	15530.12
	JHARKHAND	39	46039.33	48522.08	18073.92
16	KARNATAKA	34	66563.29	81944.97	21485.60
17	KERALA	15	24980.58	29311.93	11436.17
18	MADHYA PRADESH	19	21773.92	23757.84	8070.29
19	MAHARASHTRA	57	111215.89	121508.82	33862.75
	MANIPUR	1	727.56	6570.75	2787.99
21	MEGHALAYA	3	4845.02	6069.90	740.59
22	MIZORAM	2	988.06	4201.96	1071.77
23	MULTI STATE	180	189338.04	214441.59	69592.99
24	NAGALAND	2	5124.00	7461.12	10.44
	ODISHA	42	72186.50	81274.54	42924.34
26	PUNJAB	3	792.50	765.46	190.47
27	RAJASTHAN	31	28164.75	28220.22	14259.44
28	SIKKIM	2	1648.94	4499.46	446.18
29	TAMIL NADU	42	68208.56	85860.44	61018.48
	TELANGANA	31	11908.91	14872.86	3024.13
31	TRIPURA	5	2678.22	6376.31	3055.48
32	UTTAR PRADESH	29	35842.78	38623.19	11920.98
33	UTTARAKHAND	6	9351.89	12905.21	5030.02
34	WEST BENGAL	38	39963.90	49354.81	16766.86
Total		789	1058599.45	1262592.29	518326.58

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	20,775
2	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,185.15
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,779.1
4	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,853
5	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	POWER	03/2005	588.25	-	1,017.21
6	VIRAMGAM-BHILDI (WR) ,GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	RAILWAYS	03/1995	2,500	3000	10,658.34
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	RAILWAYS	02/1997	295	-	1,092.98
12	KARUR-SALEM (NL) , SR	RAILWAYS	02/1997	155.55	-	800.7
13	NANDYAL-YERRAGUNTALA (NL) , SCR	RAILWAYS	03/1996	155.74	164.36	755.5
14	KANPUR-KASGANJ-MATHURA (GC) , NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06
16	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
17	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
18	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	819.19
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
21	KATI HAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
22	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
23	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
24	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
26	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
27	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53
28	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	301.84

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	639.77
30	RAJATGARH-BARANG (LD), ECR	RAILWAYS	04/1999	166.16	-	305.47
31	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
32	KOSI BRIDGE (NL), ECR	RAILWAYS	04/2002	322.95	-	325.36
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	RAILWAYS	04/2002	921	-	1,691.12
34	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,521.72
35	ETAWAH-MAINPURI (NL), NCR	RAILWAYS	04/1997	120	245.39	249.33
36	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	277.33
38	RAICHUR-GUNTAKAL (DL) (SCR)	RAILWAYS	04/2003	136.62	-	277.09
39	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	228.3
40	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	326.3
41	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	357.62
42	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	-	148.69

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	4,107.18
44	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	POWER	02/2010	2,144	-	2,187.6
45	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	POWER	12/2010	2,743.19	-	2,801.9
46	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,224.73
47	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
48	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	793.71
49	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
50	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
51	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
52	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
53	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
54	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
55	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
56	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
58	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45
59	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
60	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.11
61	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	258.31
62	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
63	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
64	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
65	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
66	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
67	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
68	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
69	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
70	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	800.9
72	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
73	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
74	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	182.5
75	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
76	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
77	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	258.4
78	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	290.6
79	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.6
80	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	289.5
81	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
82	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	638
83	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,293
84	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	1,675

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,056
86	CHENNAI-TADA (SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	395.1
87	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
88	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	761.4
89	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
90	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,649
91	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	891.1
92	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
93	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
94	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273
95	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
96	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	487.9
97	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	1,313
98	INDORE-DEWAS (NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	447.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,151
100	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	928.7
101	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	1,200
102	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
103	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	712.7
104	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	579.5
105	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	982.9
106	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	564.5
107	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	-	351.18

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(August 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154	10/2013	1,315.90 -	1,315.90	578.67	10/2016 -	10/2015
2	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160	2/2014	243.53 -	243.53	162.50	08/2016 -	03/2016
	Total		1,559.43 -	1,559.43	741.17		
	<u>COAL</u>						
3	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
4	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170	8/2014	188.75 -	188.75	1.00	02/2017 -	03/2016
	Total		188.75 -	188.75	1.00		
	<u>PETROLEUM</u>						
5	MARKETING TOP AT KORBA - [N16000186	1/2011	141.86 -	232.00	148.69	09/2016 -	12/2015
6	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190	7/2014	419.04 -	419.04	-	01/2017 -	06/2016
7	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	6,068.80	403.22	04/2019 -	03/2019
	Total		6,629.70 -	6,719.84	551.91		
	Grand Total		8,933.40	9,023.54	1,297.60		

Details of On Schedule Projects w.r.t. Original Schedule

							(August 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
2	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
3	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	0.30	03/2019 -	03/2019
4	GOKUL - [N06000120]	11/2014	267.67 -	267.67	161.05	03/2018 -	03/2018
5	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	29.83	03/2018 -	03/2018
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	204.45	03/2017 -	03/2017
7	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.38	03/2016 -	03/2016
8	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
9	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	107.63	03/2020 -	03/2020
10	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	804.65	03/2016 -	03/2016
11	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	69.93	03/2019 -	03/2019
12	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	119.03	03/2020 -	03/2020
13	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	93.51	03/2016 -	03/2016
14	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	778.77	03/2023 03/2023	03/2023
15	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
16	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.24	03/2019 -	03/2019
17	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	28.23	03/2021 -	03/2021
18	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
19	AMALGAMATED PAUNI-II & III OC MINE - [N06000131]	6/2015	483.69 -	483.69	1.57	03/2021 -	03/2021
20	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.11	03/2020 -	03/2020
21	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.15	04/2017 -	04/2017
22	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	82.58	03/2021 -	03/2021

						(August 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	167.35	03/2018 -	03/2018
24	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.96	03/2016 -	03/2016
25	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
26	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
27	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	97.98	03/2018 -	03/2018
28	AMALGAMATED YEKONA-I & YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	-	03/2025 -	03/2025
29	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
30	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	42.23	03/2023 -	03/2023
31	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
32	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	11.97	03/2021 -	03/2021
	Total		28,730.19 -	28,625.21	3,378.76		
	<u>FERTILISERS</u>						
33	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	30.36	11/2016 -	11/2016
	Total		197.79 -	197.79	30.36		
	<u>MINES</u>						
34	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
35	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,149.45	11/2015 -	11/2015
36	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
37	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	132.32	12/2016 -	12/2016
38	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	223.28	12/2018 -	12/2018
39	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	1,743.40	05/2017 05/2017	05/2017
40	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018

						(August 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
42	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
43	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	108.32	09/2017 -	09/2017
44	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	5.10	02/2016 02/2016	02/2016
45	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	26.70	07/2016 -	07/2016
46	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	31.94	11/2016 -	11/2016
47	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	60.63	07/2016 -	07/2016
48	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,671.22	-	11/2019 -	11/2019
49	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,899.93	68.90	05/2017 -	05/2017
50	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	8,205.43	05/2016 -	05/2016
51	CRU TO ISOMERIZATION (ISOM) - [N16000200]	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016
	Total		37,177.66 -	39,840.59	11,791.05		
	<u>POWER</u>						
52	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,841.00	08/2018 -	08/2018
53	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	749.00	12/2016 -	12/2016
54	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017
55	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	4,085.09	01/2018 -	01/2018
56	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
57	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	498.00	03/2018 -	03/2018
58	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	71.50	12/2015 -	12/2015
59	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,877.00	01/2017 -	01/2017
60	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	24.10	02/2017 -	02/2017
61	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,154.00	02/2019 -	02/2019

						(August 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	2.00	08/2016 -	08/2016
63	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,397.00	09/2016 -	09/2016
64	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	166.90	04/2018 -	04/2018
65	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME - PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	57.40	04/2018 -	04/2018
66	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	-	05/2016 -	05/2016
67	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	42.40	04/2017 -	04/2017
68	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
69	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	09/2017 -	09/2017
70	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	33.30	11/2016 -	11/2016
71	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	409.80	05/2016 -	05/2016
72	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	137.90	05/2018 -	05/2018
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	70.00	06/2016 -	06/2016
74	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
75	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	748.00	03/2019 -	03/2019
76	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	85.90	10/2016 -	10/2016
77	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
78	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,895.00	09/2017 -	09/2017
79	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	120.00	09/2019 -	09/2019
80	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	63.40	06/2016 -	06/2016
82	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	12.10	04/2017 -	04/2017
83	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	319.24	04/2016 -	04/2016
84	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	2.00	07/2018 -	07/2018
85	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	4,698.00	06/2017 -	06/2017

						(August 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
87	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
88	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7&8 - PART B - [N18000201]	7/2015	307.18 -	307.18	0.80	11/2017 -	11/2017
89	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
	Total		144,581.22 -	144,581.22	33,565.73		
	<u>RAILWAYS</u>						
90	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANTPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
91	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
92	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	536.36	03/2016 -	03/2016
93	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	626.11	03/2016 -	03/2016
94	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	-	03/2016 -	03/2016
95	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
96	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
97	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
	Total		10,168.70 -	14,195.91	1,335.74		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
98	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	-	01/2016 -	01/2016
99	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	-	01/2016 -	01/2016
100	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	13.39	09/2015 -	09/2015
101	YAN TO NIRMAL SEREHAABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]	12/2013	244.08 -	244.08	-	03/2016 -	03/2016
102	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
103	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015

						(August 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
104	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79	1,916.79	-	11/2016	11/2016
105	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24	2,125.24	163.30	12/2015	12/2015
106	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]	1/2014	270.00	270.00	-	03/2016	03/2016
107	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]	10/2014	244.30	244.30	-	12/2016	12/2016
108	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO 45 - [N24000253]	8/2014	187.79	187.79	-	07/2016	07/2016
109	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79	677.79	-	04/2016	04/2016
110	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]	12/2013	220.72	220.72	-	11/2016	11/2016
111	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]	12/2013	177.18	177.18	-	03/2016	03/2016
112	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	13.79	09/2017	09/2017
113	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]	1/2014	158.04	158.04	-	12/2015	12/2015
114	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]	3/2015	153.21	153.21	-	01/2017	01/2017
115	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]	12/2013	158.65	158.65	-	03/2016	03/2016
116	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	2.79	11/2017	11/2017
117	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	3/2011	218.31	339.82	-	12/2015	12/2015
118	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47	313.27	-	02/2017	02/2017
119	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60	1,266.60	-	09/2016	09/2016
120	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95	1,287.95	-	11/2015	11/2015
121	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]	1/2014	340.00	340.00	-	03/2016	03/2016
122	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10	240.10	-	03/2016	03/2016
	Total		13,367.24	13,684.12	193.27		

						(August 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
123	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	54.37	05/2016 -	05/2016
124	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	1.29	09/2017 -	09/2017
125	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	0.53	12/2017 -	12/2017
126	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	199.13	04/2016 -	04/2016
127	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	25.49	10/2016 -	10/2016
128	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
129	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	147.85	07/2016 -	07/2016
130	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
131	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	22.53	04/2018 -	04/2018
132	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016
	Total		12,872.02 -	13,017.42	464.96		
	<u>URBAN DEVELOPMENT</u>						
133	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
134	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
135	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
136	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
137	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
138	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	609.63	11/2019 -	11/2019
139	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	-	09/2016 -	09/2016
	Total		46,240.70 -	46,240.70	609.63		
	Grand Total		295,191.52	302,238.96	51,369.50		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	11/2015	31.12
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	-	15.77
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II [N04000070]	02/2011	452.00 -	489.00	03/2015 -	10/2015	8.19
	Total		787.61 -	877.53			
	<u>COAL</u>						
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	07/2015	76.47
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
8	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2015	34.63
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2016	12.97
	Total		8,208.23 -	12,579.39			
	<u>HEAVY INDUSTRY</u>						
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
12	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		5,460.61	9,833.52			
	<u>PETROLEUM</u>						
13	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07	4,619.94	02/2016	12/2017	31.51
14	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56	450.55	03/2017	03/2017	27.79
15	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75	239.73	07/2013	10/2015	20.02
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00	1,693.00	01/2012	03/2016	70.49
17	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35	4,941.49	04/2016	12/2017	19.81
18	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86	232.00	09/2016	12/2015	63.54
19	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47	5,813.25	05/2017	05/2017	1.87
20	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79	1,256.72	05/2013	12/2015	45.83
21	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	34,555.00	11/2012	10/2015	16.05
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63	2,665.65	03/2015	05/2016	29.42
23	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00	16,504.00	05/2016	05/2016	16.02
24	REWARI KANPUR PIPELINE PROJECT - [N16000145]	02/2012	1,210.64	1,446.34	11/2015	11/2015	19.47
25	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00	838.08	11/2015	11/2016	25.84
26	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81	462.79	10/2014	10/2016	49.38
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00	1,227.00	10/2011	03/2016	67.62
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35	1,200.00	03/2015	06/2016	37.72
	Total		65,744.28	78,145.54			
	<u>POWER</u>						
29	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59	7,818.68	09/2009	12/2018	99.48
30	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33	16,885.00	09/2010	-	168.64
31	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38	1,929.15	09/2009	06/2016	81.76

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
32	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	06/2016	51.10
33	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	10/2015	13.18
34	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52
35	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
36	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
37	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21
38	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31
39	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	06/2016	159.38
40	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
41	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15
42	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63
43	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.70	08/2014 -	09/2016	27.60
44	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
45	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	11/2008 -	12/2016	21.34
46	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2018	73.65
47	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	588.25 -	1,007.16	12/2007 -	10/2015	71.21
48	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
49	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	09/2015	139.35
	Total		48,538.28 -	88,312.16			
	<u>RAILWAYS</u>						
50	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
51	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
52	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
53	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
54	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
55	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
56	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
57	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
58	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
59	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
60	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
61	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
62	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
63	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
64	RAMGANJUMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
65	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
66	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
67	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
68	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	-	346.59
69	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
71	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
72	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
73	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	-	6.99
74	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
75	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079	09/2007	404.19 -	1,383.45	- -	-	242.28

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
76	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
77	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
78	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
79	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
80	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
81	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
82	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
83	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
84	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
85	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
86	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
87	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
88	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
89	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
90	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
91	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
92	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
93	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
94	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
95	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
96	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
97	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
98	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
99	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
100	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
101	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
102	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
103	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
104	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
105	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
106	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
107	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
108	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
109	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
110	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
111	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
112	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
113	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
114	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
115	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
116	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
117	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
118	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
119	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
120	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
121	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
122	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
123	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
124	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
125	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
126	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
127	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
129	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
130	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
131	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
132	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
133	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
134	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
135	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
136	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
138	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
139	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
140	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
141	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
142	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
143	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
144	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
145	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
146	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
147	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
148	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
149	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
150	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
151	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
152	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
153	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
154	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
155	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
156	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
157	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
158	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
159	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
160	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
161	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
162	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
163	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
164	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	- -	-	184.87
165	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63
166	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	3,500.00	- -	-	68.05
167	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
168	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	262.00	- -	-	10.58
169	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR [N22000152	04/2013	456.00 -	855.16	- -	-	87.54

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
170	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65	872.22	-	-	17.92
171	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39	218.39	-	-	2.34
172	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41	2,030.50	02/2019	02/2019	226.23
173	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37	434.00	-	-	62.32
174	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63	1,009.00	-	12/2019	82.25
175	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64	760.00	-	-	162.39
176	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90	230.00	03/2015	12/2016	53.44
177	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44	583.00	12/2015	03/2016	88.40
178	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20	365.00	-	12/2017	41.36
179	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69	325.00	-	-	84.98
180	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07	378.56	-	-	32.80
181	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00	926.09	-	-	338.91
182	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01	367.17	-	-	72.37
183	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00	1,887.90	-	03/2019	5.00
184	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87	528.00	-	-	18.16
185	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52	1,200.00	-	-	129.22
186	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00	1,500.00	-	-	78.78
187	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68	556.64	-	-	180.17
188	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24	520.00	-	-	91.71
189	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39	1,280.83	-	-	55.74
190	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14	346.15	-	-	28.14
191	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42	563.13	-	03/2019	154.33
192	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00	1,242.25	03/2007	03/2016	38.80

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
193	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65 -	- -	03/2018	251.85
194	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70 -	- -	03/2020	5.00
195	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45 -	- -	03/2018	110.44
196	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81 -	- -	03/2018	1.86
197	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22 -	- -	-	109.04
198	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00 -	- -	-	173.71
199	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24 -	- -	03/2015	285.12
200	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95 -	- -	-	16.29
201	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90 -	- -	03/2020	30.00
202	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57 -	- -	03/2018	180.56
203	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28 -	- -	03/2017	63.25
204	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58 -	- -	03/2018	162.68
205	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55 -	- -	03/2018	216.06
206	AMBARAI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10 -	- -	03/2018	45.17
207	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06 -	- -	03/2019	47.95
208	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55 -	03/2016 -	03/2016	29.06
209	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00 -	- -	-	33.02
	Total		81,685.74 -	208,168.14 -			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00 -	02/2009 -	-	28.93
211	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13 -	04/2009 -	-	92.75
212	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13 -	11/2008 -	-	80.68
213	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23 -	07/2009 -	-	68.99
214	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00 -	11/2011 -	-	106.50

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
215	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
216	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	-	30.10
217	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
218	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
219	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	12/2015	55.66
220	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
221	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
	Total		3,623.15 -	5,791.59			
	<u>SHIPPING AND PORTS</u>						
222	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	09/2017	18.89
223	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2015	300.00
224	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
225	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,990.06 -	3,102.68			
	<u>STEEL</u>						
226	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
227	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	04/2015	41.41
	Total		9,035.00 -	12,779.40			
	<u>URBAN DEVELOPMENT</u>						
228	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			

(August 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Grand Total		249,848.96	457,973.25			

Details of Delayed Projects w.r.t. Original and Revised Schedule

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	20,775.00	12/2008 -	11/2015	83	31.12	Slippage of commitments by M/s Atomstroyexport, Russian Federation.
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	5,053.45	09/2010 09/2016	09/2016	72	62.57	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	7,095.00	12/2015 -	10/2017	22	0	Late receipt of financial sanction. Delay in supply/equipment from various vendors in general
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,904.00	12/2016 -	05/2018	17	0	Delay in supply of equipments from various vendors.
	Total		40,442.00 -	46,726.00	37,827.45					
	<u>CIVIL AVIATION</u>									
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	0	
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	489.00	439.81	03/2015 -	10/2015	7	8.19	
7	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	357.62	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		979.06 -	1,016.06	797.47					
	<u>COAL</u>									

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,355.68	03/2012 05/2014	08/2015	41	34.63	Delay in finalization of sub-contractors and mobilization of resources. Delay in release of work front by M/s BHEL to other contractors like ABB and L&T has delayed the start-up power supply. Inadequate manpower deployment by BHEL. Delay in initial commencement of civil works for boiler. Delay in Engineering. Enormous dewatering and excavation involved for the open type of foundation adopted by BHEL, instead of pile foundation suggested in the contract.
9	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	170.77	10/2014 -	09/2015	11	0	Delay in acquisition of private land Delay in supply of equipment Delay in civil works
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	147.58	03/2010 -	03/2016	72	0	
11	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,862.99	03/2014 -	03/2016	24	0	
12	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,695.40	03/2014 -	03/2016	24	0	
13	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	481.99	03/2013 -	03/2016	36	-6.11	
14	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH	06/2011	746.04 535.10	535.10	409.02	03/2015 -	03/2016	12	-28.27	
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	77.19	07/2012 -	03/2016	44	0	
16	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	860.52	03/2013 09/2012	03/2016	36	478.5	
17	CHURCHA ROUG (1.35MTY) - [N06000046]SECL, CHHATISGARH	06/2008	462.35 -	462.35	298.77	03/2014 -	03/2016	24	0	
18	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	60.62	03/2014 -	03/2016	24	0	(1) Delay in finalization of Global tender. (2) Delay in rehabilitation and Resettlement activity due to resistance by villagers.

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
19	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	418.97	365.83	03/2012 -	03/2016	48	0	
20	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	72.86	03/2015 -	03/2016	12	0	All the important activities of the project have been completed and coal production has been commenced from March, 2014. Project is delayed due to acquisition of forest land.
21	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	47.90	03/2012 -	03/2016	48	0	
22	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL, JHARKHAND	08/2007	163.51 -	163.51	35.92	03/2011 -	03/2016	60	0	
23	TAPIN OCP (2.5 MTY) - [N06000086]JCL, JHARKHAND	08/2008	264.68 -	264.68	145.20	03/2012 -	03/2016	48	0	
24	MURAI DIH UG TURN-KEY PROJECT - [N06000096]JCL, JHARKHAND	02/2011	339.88 -	339.88	11.26	04/2014 -	03/2016	23	0	
25	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	0	
26	MADHUBAND NLW WASHERY - [N06000126]JCL, JHARKHAND	08/2010	289.45 -	289.45	-	05/2014 -	10/2016	29	0	
27	PATHERDIH NLW WASHERY - [N06000127]JCL, JHARKHAND	10/2012	269.82 -	269.82	48.35	04/2014 -	11/2016	31	0	
28	ASHOK EXPN OCP CCL (10 MTY) - [N060100096]JCL, JHARKHAND	12/2007	341.63 341.63	341.63	126.14	03/2011 -	03/2017	72	0	i) Law & Order ii) Coal evacuation problems

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.18	225.39	03/2011 -	03/2017	72	0	Lol for procurement of transporting equipment was issued on 14-01-2015 subject to the pending approval of CIL Board. It was placed before CIL Board on 22-02-2015. CIL Board advised to prepare a comprehensive report of Jhanjra. Further ECL has appealed to CIL for approval of advance actions for procurement of transporting equipment on 09-05-2015 citing the comprehensive report is under process of approval by ECL Board. Finally CIL Board approved the advance action proposal on 12-05-2015. Work Order for transporting equipment issued on 29-05-2015. Equipments are yet to be received by the project. Completion of Coal Project having a rated production capacity of 1.70 MTY.
30	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]JNCL, MADHYA PRADESH	10/2007	259.40 -	259.40	25.80	03/2012 -	03/2017	60	0	
31	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	181.15	03/2013 -	03/2017	48	0	
32	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	148.86	03/2010 -	03/2017	84	0	
33	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51	0	
34	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	192.31	03/2012 -	03/2017	60	0	
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	173.69	03/2013 -	03/2017	48	.02	
36	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL, JHARKHAND	12/2007	179.87 -	179.87	85.40	03/2012 -	03/2017	60	0	
37	PURNADIH OCP (3.0 MTY) - [N06000085]JCL, JHARKHAND	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48	0	
38	KARMA OCP (1.0 MTY) - [N06000088]JCL, JHARKHAND	06/2009	162.46 -	162.46	67.28	03/2014 -	03/2017	36	0	

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
39	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	13.85	07/2016 -	03/2017	8	0	
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	75.60	03/2012 -	03/2018	72	0	
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	207.52	03/2014 -	03/2018	48	0	
42	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	
44	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	87.64	03/2016 -	03/2018	24	0	
45	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,056.99	12/2015 04/2018	04/2018	28	0	Re-tendering of Steam Generator & Auxiliaries package has resulted in time delay.
46	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2019	48	0	
47	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	43.62	04/2015 04/2019	04/2019	48	0	
48	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	
49	JAGANNATHPOR OCP (3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	
50	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	
51	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	
	Total		29,386.88 -	31,842.03	16,302.56					
	STEEL									
52	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,232.17	12/2011 -	08/2015	44	0	
53	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	398.16	05/2013 01/2015	08/2015	27	0	
54	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	136.08	09/2014 -	09/2015	12	0	

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
55	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	211.55	08/2014 -	11/2015	15	0	
56	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	204.11	12/2014 -	11/2015	11	0	
57	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	163.67	10/2013 -	12/2015	26	0	
58	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	267.06	06/2015 -	12/2015	6	0	
59	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,854.52	03/2013 -	03/2016	36	0	
60	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	284.58	07/2015 -	03/2016	8	0	
61	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	7,729.64	05/2015 12/2016	12/2016	19	0	
62	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	178.99	07/2015 -	03/2017	20	0	
	Total		42,526.04 -	42,526.04	29,660.53					
	<u>PETROCHEMICALS</u>									
63	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	-	04/2012 12/2013	09/2015	41	80.08	Time & Cost Overrun
	Total		5,460.61 -	9,833.52	.00					
	<u>PETROLEUM</u>									
64	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC, MAHARASHTRA	03/2012	5,608.40 -	5,608.40	4,457.47	05/2015 05/2015	08/2015	3	0	nil

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
65	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 678.02	678.02	437.69	06/2012 03/2015	09/2015	39	-38.7	Delay in NOC from the MOD (air force) -ROW problem at site due to intervention of local villagers. Work commenced under police protection.
66	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,228.45	12/2014 -	09/2015	9	0	
67	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	166.96	12/2014 -	09/2015	9	0	The originally conceived independent piping corridor for Mounded bullet has been combined with Ongoing Resid project due to space constraints.
68	PARADIP REFINERY PROJECT - [N16000058]OCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,824.71	11/2012 11/2013	10/2015	35	16.05	
69	MARKETING TERMINAL AT PARADEEP - [N16000168]OCL, ODISHA	07/2009	199.75 239.73	239.73	198.69	07/2013 -	10/2015	27	20.02	
70	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 429.00	429.06	367.98	10/2014 10/2015	10/2015	12	0	
71	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	490.55	09/2011 12/2015	12/2015	51	0	-Delay in preparation of drawing and additional model testing of Hull form in Austria. - Shortage of skilled manpower at contractor end. - Inadequate ancillary/sub-contractors at the location -Lack of planning to match resources to work targets. - Change in delivery location. -Delay in procurement of steel by PSL.
72	DE-BOTTLENECKING OF SMPL - [N16000089]OCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,282.08	08/2015 -	12/2015	4	0	
73	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,561.33	01/2014 12/2015	12/2015	23	0	-Slow progress by contractor. - Slow progress by the contractor in laying of pipelines.

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
74	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	117.49	09/2012 12/2015	12/2015	39	-24.14	-Slow progress in civil work and fabrication work due to less resource mobilization. -Unresolved commercial issues between M/s UEM and NSF Vendor. -Delay in finalization of Process package leading to delay in engg and procurement services. -Delay in delivery of Nut Shell filters and internal of IGF units.
75	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	910.72	05/2013 12/2015	12/2015	31	45.83	-Increase in scope of work -Delay in procurement of steel and fabrication of legs by the contractor.
76	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	355.47	08/2015 -	12/2015	4	0	
77	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	501.91	04/2015 04/2015	12/2015	8	-39.69	
78	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	93.65	05/2015 -	12/2015	7	0	
79	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,188.73	09/2012 -	03/2016	42	0	
80	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	287.63	06/2011 03/2012	03/2016	57	0	
81	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,002.51	10/2011 -	03/2016	53	67.62	Some difficulties being faced during Cavern Acceptance Test, which is in progress.
82	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,430.61	01/2012 -	03/2016	50	70.49	Progress is slow due to heavy rains during the period.
83	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,222.16	03/2015 05/2016	05/2016	14	29.42	Pipeline package: Non-performance by the contractor Delay in conversion of Rig Sagar Laxmi to MOPU due to financial issues and non-performance of the contractor.

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
84	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	578.28	05/2014 05/2016	05/2016	24	0	Delayed due to retendering. -Package-1 delayed due to representation by M/s Essar in IEM. -Slow progress by contractor.
85	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	Non-performance by the contractor of Pipeline package: Contractor was served notice of termination of the contract on 11.01.2014 and on 07.03.2014 in view of contractor's inability to execute the work on time. The contractor served notice of arbitration on 01.10.2014 and again on 03.04.2015. Contractor proposed certain pre-conditions to start the work and since then holding up the work.
86	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	128.87	03/2014 05/2016	05/2016	26	0	-Design platform integrity issue was raised by the contractor which required review of integrity analysis and this took time in resolution. - Clubbing of project facilities alongwith C-26 Cluster development project. - slow progress by the contractor.
87	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC, MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39	0	
88	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 -	913.00	428.36	08/2015 -	06/2016	10	0	
89	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	320.88	03/2015 11/2015	06/2016	15	37.72	Heavy rain in Assam. Refloating of tender will have impact on timeline
90	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL, BIHAR	04/2013	480.00 -	480.00	57.02	02/2016 -	07/2016	5	0	

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
91	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36	3,110.36	857.20	11/2015 07/2016	07/2016	8	0	Restricted working environment due to nearby operating plants, availability of limited space for storage & fabrication, Restricted timings for radiography activities etc.. were affecting the progress of the work.Process fuel oil system in DCU, Liquid Sulphur Loading in SRU and other latest improvement in the process packages reviewed and implemented for performance
92	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81	462.79	240.74	10/2014 10/2016	10/2016	24	49.38	
93	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	507.74	11/2015 11/2016	11/2016	12	25.84	
94	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00	215.66	-	06/2012 11/2015	11/2016	53	-20.13	Delay in placement of order for 2 nos drilling rigs. One of the bidder went to court in anticipation of disqualification of their bid
95	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,783.31	03/2013 03/2016	03/2017	48	-3.5	-Substantial time taken for mobilization by survey and other agency. -ROU acquisition and issue related to payment -Delay in forest clearance. -Inadequate manpower at working sites affected the construction progress. -Local problem and court cases by tea gardener. -Slow progress in engineering and procurement.
96	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82	284.82	-	04/2015 05/2017	05/2017	25	0	
97	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10	1,916.10	1,161.74	12/2014	12/2017	36	0	
98	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00	3,823.00	1,076.57	04/2015 12/2017	12/2017	32	0	

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
99	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC, MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	450.37	02/2016 12/2017	12/2017	22	31.51	NIL
100	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 4,941.49	4,941.49	75.24	04/2016 12/2017	12/2017	20	19.81	Delayed due to re-tendering of various package and due to prolonged legal battle on eligibility and representations from different bidders.
101	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	98.96	09/2017 -	12/2017	3	0	
102	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	6.98	01/2013 -	12/2018	71	-10.01	
103	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	0	
104	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	6,086.08	118.17	05/2019 03/2020	03/2020	10	0	no delay
	Total		95,122.89 -	103,221.35	56,427.84					
	<u>POWER</u>									
105	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,007.68	1,007.68	907.18	07/2013 -	09/2015	26	139.35	- Trial operation of gas Turbine for 72 hr is planned w.e.f. 4th to 6th Sept 2015 subject to availability of gas & evacuation System.
106	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL, ODISHA	12/2010	2,743.19 -	2,743.19	2,801.90	12/2013 -	09/2015	21	0	
107	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL, MADHYA PRADESH	03/2012	213.78 -	213.78	203.04	03/2014 -	09/2015	18	0	
108	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, KARNATAKA	03/2005	588.25 -	1,007.16	1,017.21	12/2007 12/2009	10/2015	94	71.21	
109	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL, MULTI STATE	06/2012	1,508.74 -	1,508.74	1,028.18	03/2015 -	10/2015	7	0	
110	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL, ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,886.04	03/2013 06/2015	10/2015	31	13.18	

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
111	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,539.87	10/2014 -	10/2015	12	0	
112	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	151.20	01/2013 -	11/2015	34	0	
113	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	386.02	06/2014 -	11/2015	17	0	
114	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	744.54	11/2012 -	12/2015	37	0	
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,368.02	04/2013 -	12/2015	32	0	
116	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,507.86	11/2013 -	12/2015	25	0	
117	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	468.01	11/2013 -	12/2015	25	0	
118	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,151.06	08/2014 -	12/2015	16	0	
119	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	539.80	02/2014 -	12/2015	22	0	
120	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	286.77	08/2014 06/2015	12/2015	16	16.63	
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	201.22	05/2015 -	12/2015	7	0	

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
122	PARE HYDRO ELECTRIC PROJECT - [N18000045]NNEPCO, ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,025.86	08/2013 03/2016	03/2016	31	159.15	- All activities of the Dam was suspended w.e.f. 7th June 2015 due to overtopping of U/s & D/s Cofferdam - Access to dam site is still restricted due to erosion of approach road.
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	335.37	02/2012 -	03/2016	49	0	
124	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL, MULTI STATE	12/2009	1,216.83 -	1,216.83	1,057.39	08/2012 -	03/2016	43	0	
125	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR	03/2010	3,984.03 -	3,984.03	2,989.30	01/2013 -	03/2016	38	0	- Non performance of civil, Swyd, CHP, AHP agencies
126	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	83.21	
127	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE	03/2014	155.57 -	155.57	1.00	03/2016 -	05/2016	2	0	
128	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NNEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	4,015.23	12/2009 06/2016	06/2016	78	159.38	REASONS FOR DELAY: (1) Redesign of Dam parameter. (2) Geological surprise. (3) Realignment of HPT. (4) Slope Stabilization of power house area. (5) Flash flood/rain. (6) Deviation in work. (7) Contractual issue. (8) Major deviation in encountered geology than that envisaged. (9) Permission for quarry operation yet to be received from Govt. Arunachal Pradesh.

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
129	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,853.00	09/2009 -	06/2016	81	81.76	1. Initial delay in handing over of forest land & start of work 2. Bandh/ closure by locals, political outfits like GJMM and its effect 3. Due to inordinate delay and extended stay, BOQ rates become unworkable and resulted in cash deficit of Civil Contractor. 4. Delay in award of E&M contract due to clarification regarding participation of Chinese firm
130	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, MAHARASHTRA	12/2007	477.69 721.81	721.81	521.59	09/2010 06/2013	06/2016	69	51.1	
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, MULTI STATE	02/2009	509.66 -	509.66	474.66	11/2011 -	06/2016	55	0	
132	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL, MULTI STATE	02/2010	2,144.00 -	2,144.00	2,187.60	12/2012 -	06/2016	42	0	
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, MULTI STATE	07/2010	752.64 689.03	689.03	498.72	07/2013 11/2015	06/2016	35	-8.45	
134	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,736.75	05/2014 -	06/2016	25	0	
135	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,837.46	09/2014 -	06/2016	21	0	

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
136	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL, CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,224.73	07/2014 -	06/2016	23	0	
137	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,267.32	01/2015 -	06/2016	17	0	
138	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	83.82	09/2014 -	06/2016	21	0	
139	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,854.89	06/2015 -	06/2016	12	0	
140	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE	11/2011	723.63 -	723.63	540.92	11/2014 -	06/2016	19	0	
141	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44 -	3,201.44	2,543.51	10/2014 -	06/2016	20	0	
142	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL, MULTI STATE	03/2013	2,514.88 -	2,514.88	903.85	12/2015 -	06/2016	6	0	
143	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE	09/2013	680.69 -	680.69	331.99	03/2016 -	06/2016	3	0	
144	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL, MULTI STATE	02/2014	196.58 -	196.58	1.00	02/2016 -	06/2016	4	0	
145	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL, MULTI STATE	03/2013	514.20 -	514.20	247.00	06/2015 -	08/2016	14	0	

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
146	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24	1,909.24	810.03	06/2015	08/2016	14	0	
147	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,305.13	08/2014 12/2015	09/2016	25	27.6	
148	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	872.46	07/2006 10/2016	10/2016	123	274.73	- Po or approach road condition from Bhagabazar to Natachera affecting seriously transportation of man, material, equipment and POL to the project site. - Progress work is affected due to rain and slippery road condition.
149	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04	5,497.72	4,107.18	01/2016	11/2016	10	50.95	1. La w & order problem in the project area and Kashmir Valley. 2. De lay in settlement of R&R plan of the project which is pending with J&K State Govt. for approval and strike by PFA's 3. Du e to delay decision of International Court of Arbitration
150	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63	374.63	-	04/2016	11/2016	7	0	
151	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,895.55	11/2008 03/2012	12/2016	97	21.34	
152	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12	4,824.12	4,137.48	10/2012	12/2016	50	0	
153	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19	11,130.19	11,025.10	08/2013	12/2016	40	0	

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
154	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57	4,404.57	2,084.75	01/2015	12/2016	23	0	
155	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80	1,272.80	1,138.53	11/2012	12/2016	49	0	
156	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,422.00	09/2011	03/2017	66	54.25	-Inadequate deployment of manpower & resources by M/s BHEL and its sub-agencies have affected the erection/commissioning progress of U#1 -Frequent Bandh calls by local outfits (Total Bandh- 270 days) leading to stoppage of work at site for more than 500 days. - Poor performance of BOP/Civil contractors due to geo-political situation in the region. - Heavy rainfall leads to stoppage of work.
157	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00	5,353.00	4,924.79	05/2014	06/2017	37	0	- Delay in balance land acquisition. - Law & order problem.
158	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18	9,395.18	5,263.00	11/2016	08/2017	9	0	- Delay of 12 months in Engineering & supplies by BGR which has led to a consequent delay of 12 months in erection.
159	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42	195.42	31.54	02/2014	09/2017	43	0	Law and order: Resistance by locals and pressure groups demanding works at rates of their choice.
160	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89	9,750.89	3,530.14	12/2016	09/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
161	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62	871.62	1.90	10/2017	11/2017	1	0	

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
162	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,802.00	01/2011 10/2014	03/2018	86	73.65	- Non performance of Russian agency M/s TPE & M/s PM. - M/s TPE stopped work from Oct-2013 and the contract of M/s TPE was terminated on 14.01.15. - Award of balance works on "as is where is basis in expected by Sep-15. Schedule for U#1 commissioning is 16 months i.e. Jan-17 and subsequent units at 6 months interval.
163	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL, UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,382.65	07/2010 02/2016	05/2018	94	79.77	1. No availability of Asena Quarry 2. 4.668 Ha. Land diversion case for dumping area at Village Chopra.
164	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,185.15	09/2009 -	12/2018	111	99.48	1. Initial delay in start of Dam works due to delay in Revised Forest clearance 2. Bu rial of TBM during Nov, 06. Heavy ingress of water with silt from TBM face. Treatment of shear zone, 3. Ba ck hill slope failure of Power House three times, 4. Ba n on use of aggregates by Hon'ble High Court, Shimla
165	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,534.00	03/2013 -	12/2018	69	29.14	- Unprecedented flood in Uttarakhand during Aug-12 and Jun-13 damaging cofferdam and approach roads. TBM stuck up thrice & L&T Alpine JV did not perform leading to termination of contract. - Head Race Tunnel (HRT) Package is under retender. NIT done in May-15 & award anticipated by Sep-15.
166	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58 -	3,745.08	724.79	06/2013 -	12/2019	78	50.31	Court case

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		141,079.35	170,123.09	118,987.05					
			-							
	<u>HEAVY INDUSTRY</u>									
167	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE, MULTI STATE	04/2011	1,718.00	3,827.30	-	09/2011	12/2017	75	122.78	
	Total		1,718.00	3,827.30	.00					
			-							
	<u>RAILWAYS</u>									
168	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00	874.57	730.11	03/2013	09/2015	30	81.45	Commissioning target is subject to handing over of land by GoK.
169	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52	207.52	223.44	12/2012	09/2015	33	0	
170	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00	2,363.00	1,691.12	03/2009 12/2012	10/2015	79	156.57	Railway bridge targeted for commissioning in October, 2015 (resettlement of 3 families is involved.) Road bridge would take time as there are issues in land acquisition.
171	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008	10/2015	82	104.49	
172	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07	335.00	230.67	06/2004	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
173	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	367.76	Railway bridge targeted for commissioning in October, 2015. However Road bridge would take time as there are issues in land acquisition.
174	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20	800.00	793.71	03/2010	12/2015	69	16.41	

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
175	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 12/2010	03/2016	144	259.68	Total length of railway line is 27 km. Land has not been acquired in 2.7 km length between Kharkopar and Ranjanpada (25 hectare private land and also forest land). Construction is in progress in part of the line and only part commissioning can be done.
176	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defrozen and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut-Saharanpur).
177	KATAKHAL TO BHAI RABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	
178	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	Line commissioned and freight train operations commenced. Passenger operations to commence in August 2015.
179	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	Work delayed due to foundation problem.
180	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.
181	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
182	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
183	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	
184	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	
185	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	
186	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
187	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
188	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
189	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	
190	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	Phase- I of the project is to be completed by June, 2018 subject to availability of land and funds. Target for phase-II cannot be fixed since the works are held up due to State Govt's proposal for change of alignment of the underground portion.
191	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	
192	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
193	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
194	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Progress is going as per the allotment of budget grant.
195	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
196	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.
197	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
198	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
	Total		31,140.62 -	88,821.64	40,201.58					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
199	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 08/2015	08/2015	88	0	
200	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	0	Project abandoned by contractor
201	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 11/2015	11/2015	89	0	
202	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0	
203	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 12/2015	12/2015	92	0	
204	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 12/2015	12/2015	91	0	
205	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	0	Land acquisition Forest clearance Poor progress by the contractor
206	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2016	01/2016	94	0	
207	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69	42.25	
208	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6	0	
209	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21	0	
210	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	0	
211	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	0	

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
212	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	09/2016	61	0	
213	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	
214	NALBARI T BIJINI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2017	01/2017	105	0	
215	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	0	
	Total		13,725.67 -	13,817.62	10,817.08					
	<u>SHIPPING AND PORTS</u>									
216	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2015	117	300	
217	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	407.32	12/2010 -	01/2016	61	82.72	
218	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 2,099.00	1,460.00	1,038.00	12/2010 -	09/2017	81	18.89	
	Total		1,744.39 -	2,729.46	1,585.12					
	<u>TELECOMMUNICATIONS</u>									
219	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	72.17	10/2010 08/2015	10/2015	60	0	
	Total		384.00 -	384.00	72.17					
	<u>URBAN DEVELOPMENT</u>									
220	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	1,280.91	09/2014 -	08/2015	11	0	CMRS inspection is to be done shortly for giving statutory clearances for starting the commercial operation of line. Mandatory clearances are being perused.

(August 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
221	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	Finalization of flooring work in 1st year lab building and approval of sample flat for Grade- A qtr from client awaited.
222	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2	0	
223	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	0	
224	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	142.00	05/2013 -	10/2015	29	0	
225	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	
226	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	Extra time involved in finalization of tender for addressing certain issues of client department.
227	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
228	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,032.96	12/2015 -	08/2016	8	0	
229	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	16,971.38	03/2016 -	12/2016	9	0	
230	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	0	
231	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0	

(August 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
232	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	0	The work was terminated on 24-07-2014 because of the non performance of the contractor for the first package. However, the tender for balance items of the package I along with package III has been awarded and work started at site.
	Total		81,707.72 -	81,707.72	29,436.15					
	Grand Total		485,417.23	596,575.83	342,115.00					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	11/2015	31.12	83
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	10/2015	8.19	7
	Total		452.00 -	489.00				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50	36
5	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2015	34.63	41
	Total		5,596.41 -	8,310.76				
	<u>HEAVY INDUSTRY</u>							
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIPI) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROCHEMICALS</u>							
8	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08	41
	Total		5,460.61 -	9,833.52				
	<u>PETROLEUM</u>							
9	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	10/2015	20.02	27
10	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38	24

(August 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
11	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62	53
13	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2015	45.83	31
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72	15
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	03/2016	70.49	50
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
17	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	12/2017	31.51	22
18	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	4,941.49	04/2016 -	12/2017	19.81	20
19	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05	35
	Total		44,107.75 -	53,699.40				
	POWER							
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63	16
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
22	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	09/2015	139.35	26
23	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	06/2016	51.10	69
24	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15	31
25	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	588.25 -	1,007.16	12/2007 -	10/2015	71.21	94
26	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76	81
27	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
28	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.70	08/2014 -	09/2016	27.60	25
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	11/2008 -	12/2016	21.34	97
30	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	10/2015	13.18	31

(August 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
31	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21	51
32	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31	78
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	06/2016	159.38	78
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69
35	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
36	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48	111
37	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
38	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2018	73.65	86
	Total		41,956.08 -	71,063.43				
	<u>RAILWAYS</u>							
39	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
40	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49	82
41	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
42	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
43	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
44	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
45	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
46	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
47	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
48	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
49	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45	30
50	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
51	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144

(August 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
52	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
53	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
54	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
56	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
57	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
58	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
59	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
60	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57	79
61	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
62	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
63	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
64	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
65	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		22,946.70 -	80,627.72				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
66	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
	Total		217.61 -	309.56				
	<u>SHIPPING AND PORTS</u>							
67	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2015	300.00	117
68	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72	61

(August 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
69	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	09/2017	18.89	81
	Total		1,744.39 -	2,729.46				
	Grand Total		140,862.55	253,837.15				

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	-
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- -	-
	Total		994.50 -		
	<u>COAL</u>				
4	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	03/2015 -	03/2015
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,583.77	06/2009 03/2013	07/2015
6	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		2,702.38 -		
	<u>STEEL</u>				
7	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	12/2011 01/2015	03/2015
8	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	10/2009 10/2012	04/2015
9	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	04/2015
10	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	04/2013 09/2014	06/2015
11	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	09/2013 -	07/2015
	Total		10,737.10 -		
	<u>PETROLEUM</u>				
12	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	06/2015
13	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
14	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 714.25	01/2016 -	-
15	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
17	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
18	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
19	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	01/2014 -	-
	Total		9,641.83 -		
	<u>POWER</u>				
20	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	12/2014 -	05/2015
21	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
22	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
24	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
	Total		8,547.98 -		
	<u>RAILWAYS</u>				
25	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
26	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
27	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
28	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
29	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
30	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
31	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
32	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
33	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
34	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
36	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	- 10/2014	10/2014
37	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
38	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	- -	01/2015
39	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
40	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
41	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2015
42	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
43	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
44	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
45	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015
46	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
47	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	- -	03/2015
48	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	03/2015
49	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015
50	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-
51	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-
52	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	- 03/2010	-
53	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
54	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	514.68 -	- -	-
55	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	- -	-
56	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	- -	-
57	NANGALDAM-TALWARA(NL), NR - [220100188]NR, MULTI STATE	03/1981	450.00 -	07/2012 -	-
58	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 -	- -	-
59	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	227.00 997.58	- -	-
60	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
61	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
62	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
63	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
64	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
65	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
66	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
67	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
68	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
69	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
70	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
71	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
72	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
73	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
74	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
75	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
76	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
77	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
78	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
79	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
80	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
81	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
82	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
83	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
84	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
85	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR,TELANGANA	04/2006	378.56 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
87	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
88	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
89	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
90	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
91	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
92	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
93	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
94	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
95	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
96	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
97	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
98	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
99	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
100	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
101	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
102	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
103	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
104	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
105	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
106	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
107	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
108	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
109	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
110	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
111	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
112	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
113	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
114	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
115	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
116	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
117	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
118	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
119	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
120	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
121	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
122	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
123	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
124	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
125	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
126	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
127	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
128	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
129	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
130	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
131	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
132	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
133	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
134	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
135	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
136	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
137	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
138	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
139	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
140	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
141	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
142	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
143	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
144	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
145	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
146	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
147	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
148	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
149	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
150	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
151	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
152	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
153	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
154	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
155	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
156	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
157	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
158	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
159	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
160	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
161	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
162	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
163	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
164	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
165	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
166	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
167	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
168	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
169	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
170	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
171	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
172	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
173	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
174	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
175	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
176	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
177	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
178	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
179	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
180	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
181	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
182	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
183	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
185	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
186	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
187	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
188	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
189	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
190	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
191	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
192	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
193	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
194	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
195	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
196	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
197	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
198	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
199	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
200	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
201	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
202	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
203	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
204	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
205	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
206	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
207	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
208	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
209	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
210	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
211	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
212	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
213	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
214	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
215	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
216	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
217	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
218	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
219	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
220	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
221	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
222	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
223	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
224	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
225	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
226	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
227	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
228	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
229	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
230	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
231	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
232	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
233	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
234	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
235	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
236	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
237	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
238	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
239	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
240	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
241	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
242	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
243	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
244	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
245	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
246	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
247	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
248	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
249	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
250	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
251	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
252	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
253	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
254	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-
	Total		112,281.52 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
255	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
256	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
257	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014
259	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015
260	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	02/2015
261	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	03/2015
262	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015
263	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	05/2015
264	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	05/2015
265	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	07/2015
266	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-
267	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-
268	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
269	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
270	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
271	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
272	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
273	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-
274	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-
275	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-
276	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-
277	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-
278	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
279	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
280	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-
281	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	-
282	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
283	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	02/2010 -	-
284	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	-
285	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	09/2007 -	-
286	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00 -	02/2010 -	-
287	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	09/2010 -	-
288	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	-
289	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	07/2012 -	-
290	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
291	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	05/2012 -	-
292	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	10/2011 -	-
293	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
294	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	11/2011 -	-
295	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	-
296	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
297	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	- -	-
298	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
299	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
300	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	03/2013 -	-
301	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
302	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	07/2013 -	-
303	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	-
304	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	11/2012 -	-
305	DEVIHALLI-HASSAN - [N24000152]NHAI, KARNATAKA	12/2010	453.00 -	- -	-
306	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	09/2013 -	-
307	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-
308	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
309	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-
310	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
311	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
312	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	-
313	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
314	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
315	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
316	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
317	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	-
318	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
319	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-
320	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
321	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	-
322	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
323	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
324	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
325	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
326	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
327	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
328	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-
329	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	-
330	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
331	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
332	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
333	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
334	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
335	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-
336	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
337	2 LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	05/2014 -	-
338	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	01/2014 -	-
339	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	08/2013 -	-
340	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	-
341	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
342	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	-
343	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	08/2013 -	-
344	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	08/2013 -	-
345	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	08/2013 -	-
346	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
347	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
348	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
349	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-
350	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	-
351	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	10/2013 -	-
352	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	04/2014 -	-
353	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	10/2013 -	-
354	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	06/2015 -	-
355	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	06/2014 -	-
356	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
357	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-
358	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	09/2014 -	-
359	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	09/2014 -	-
360	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
361	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
362	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	- -	-
363	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17 -	- -	-
364	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH, GOA	03/2015	298.33 -	- -	-
365	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH, GOA	03/2015	184.05 -	- -	-
366	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH, GOA	03/2015	280.16 -	- -	-
	Total		76,544.06 -		
	<u>SHIPPING AND PORTS</u>				
367	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD., CHIN - [N25000064]SHIPP., MAHARASHTRA	10/2010	994.82 -	11/2013 -	11/2013
368	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	04/2009 -	-
369	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		3,667.89 -		
	<u>TELECOMMUNICATIONS</u>				
370	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 -	07/2015
	Total		13,334.00 -		
	<u>URBAN DEVELOPMENT</u>				
371	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD, DELHI	01/2010	162.90 -	07/2012 -	06/2014
372	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD, BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
373	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
374	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD, PUNJAB	08/2005	191.24 -	08/2007 -	03/2015
375	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 -	03/2012 -	04/2015
376	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	06/2012 -	05/2015
377	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 -	06/2011 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
378	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-
379	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
380	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		10,732.40 -		
	Grand Total		249,183.66		

Details of Projects Without Original Date of Commissioning

(August 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
1	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	153.29	- -	09/2015	-	0/0
2	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	0/1
3	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2016	-	0/0
4	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
5	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
6	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
7	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
8	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
9	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
10	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
12	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
13	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
14	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
15	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
16	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
17	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
18	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
19	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0

(August 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
21	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
22	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
23	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
24	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
25	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
26	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
27	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
	Total		18,290.57 -	29,584.45	5,970.54				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
28	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	12/2015	-	2/3
29	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP, MAHARASHTRA	01/2014	446.77 -	446.77	-	- -	06/2017	-	0/0
30	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL. FOUR LANE KHINDEAPAR BRIDGE - [N24000251]NHDP, GOA	03/2015	297.00 -	297.00	-	- -	10/2017	-	0/0
31	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP, MAHARASHTRA	03/2015	168.30 -	168.30	-	- -	10/2017	-	0/0
	Total		1,583.07 -	1,583.07	1,273.00				2/3
	Grand Total		19,873.64	31,167.52	7,243.54				2/4

Details of Projects Without Milestones w.r.t. Original Schedule

			(August 2015)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	03/2015 -	10/2015	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	09/2017	0/0
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-	0/0
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	-	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- -	-	0/0
	Total		1,973.56 -			0/0
	<u>FERTILISERS</u>					
7	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 197.79	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
8	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	09/2017	0/0
	Total		1,856.00 -			0/0
	<u>STEEL</u>					
9	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	10/2016	0/0
10	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
11	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
12	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
13	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
14	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		10,662.68			0/0
	<u>PETROLEUM</u>					
15	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	10/2014 10/2015	10/2015	0/0
16	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 12/2015	12/2015	0/0
17	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 04/2015	12/2015	0/0
18	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	02/2016	0/0
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	03/2016	0/0
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	03/2016	0/0
21	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 06/2016	06/2016	0/0
22	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	06/2016	0/0
23	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	01/2017 -	06/2016	0/0
24	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 11/2015	11/2016	0/0
25	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	11/2016 -	11/2016	0/0
26	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
27	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
28	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	03/2017 -	03/2017	0/0
29	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	05/2017 -	05/2017	0/0
30	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
31	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2017	0/0
32	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 12/2017	12/2017	0/0
33	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	02/2016 12/2017	12/2017	0/0
34	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	09/2017 -	12/2017	0/0
35	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	01/2013 -	12/2018	0/0
36	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2018	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
37	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
38	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA	08/2015	2,818.88 -	03/2019 -	03/2019	0/0
39	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT	05/2015	1,671.22 -	11/2019 -	11/2019	0/0
40	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	05/2019 03/2020	03/2020	0/0
41	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	- -	-	0/0
42	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU	11/2006	171.83 -	- -	-	0/0
43	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
44	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL, MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
45	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE	02/2015	890.00 -	- -	-	0/0
	Total		55,146.13 -			0/0
	<u>POWER</u>					
46	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,139.00	12/2011 -	03/2016	0/0
47	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL, ANDHRA PRADESH	05/2015	312.94 -	05/2016 -	05/2016	0/0
48	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
49	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 -	11/2016	0/0
50	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	05/2014 -	06/2017	0/0
51	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
52	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2017	0/0
53	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7&8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
54	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 -	01/2018 -	01/2018	0/0
55	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	04/2018 -	04/2018	0/0
56	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL, MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
57	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC, JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
58	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		40,517.77 -			0/0
	<u>HEAVY INDUSTRY</u>					
59	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]HIPE, MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>RAILWAYS</u>					
60	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
61	KODERMA GIRIDH (NL), ECR - [220100306]ECR, JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
62	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
63	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
64	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
65	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
66	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
67	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
68	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
69	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
71	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
72	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
73	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
74	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015	0/0
75	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
76	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
77	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
78	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
79	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
80	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
81	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
82	PEN ROHA DOUBLING - [N22000254]JR, MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
83	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
84	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
85	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0
86	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
87	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
88	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	03/2009 12/2012	10/2015	0/0
89	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
90	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
91	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
92	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
93	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	03/2004 12/2010	03/2016	0/0
94	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
95	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
96	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
98	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
99	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
100	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
101	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	03/2007 -	03/2016	0/0
102	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	03/2016 -	03/2016	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
103	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
104	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
105	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	12/2016	0/0
106	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
107	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
108	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
109	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
110	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
111	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
112	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
113	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
114	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
115	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	04/2008 03/2014	06/2017	0/0
116	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
117	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
118	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
119	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
120	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
121	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
122	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
123	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	- -	03/2018	0/0
124	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
125	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
126	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
127	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
128	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
129	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
130	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
131	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
132	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0
133	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
134	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
135	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
136	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
137	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
138	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
139	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
140	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
141	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	03/1998 -	12/2019	0/0
142	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
143	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
144	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
145	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
146	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
147	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
148	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
149	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
150	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
151	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
152	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
153	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
154	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
155	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
156	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
157	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
158	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
159	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
160	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
161	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-	0/0
162	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
163	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
164	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
165	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
166	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
167	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
168	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
169	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
170	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
171	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
172	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
173	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
174	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
175	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
176	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
177	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
178	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
179	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
180	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
181	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
182	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
183	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
184	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
185	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
186	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
187	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
188	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
189	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
190	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
191	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
192	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
193	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
194	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
195	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
196	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
197	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
198	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
199	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
200	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
201	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
202	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
203	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
204	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
205	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
206	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
207	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
208	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
209	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
210	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
211	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
212	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
213	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
214	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
215	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
216	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
217	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
218	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
219	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
220	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
221	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
222	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
223	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-	0/0
224	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 -	- -	-	0/0
225	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR, RAJASTHAN	04/2010	739.65 -	- -	-	0/0
226	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-	0/0
227	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	- -	-	0/0
228	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-	0/0
229	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	-	0/0
230	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
231	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
232	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-	0/0
233	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0
234	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-	0/0
235	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-	0/0
236	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-	0/0
237	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-	0/0
238	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-	0/0
239	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-	0/0
240	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
241	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-	0/0
242	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0
243	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-	0/0
244	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-	0/0
245	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-	0/0
246	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
247	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
248	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
249	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
250	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
251	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
252	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
253	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
254	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
255	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
256	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
257	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
258	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
259	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
260	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
261	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
262	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
263	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
264	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
265	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
266	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
267	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
268	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
269	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
270	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
271	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
272	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
273	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
274	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
275	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
276	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
277	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
278	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
279	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
280	HANSIDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
281	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
282	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
283	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
284	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
285	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
286	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
287	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
288	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
289	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
290	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
291	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
292	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
293	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
294	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
295	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
296	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
297	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
298	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
299	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
300	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
301	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
302	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
303	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
304	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
305	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
306	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
307	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
308	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
309	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
310	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
311	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
312	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
313	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
314	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
315	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
316	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
317	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
318	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0

			(August 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
319	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
320	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR, MULTI STATE	04/2010	338.54 -	- -	-	0/0
321	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR, MULTI STATE	04/2008	162.96 -	- -	-	0/0
322	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR, HARYANA	04/2013	400.00 -	- -	-	0/0
323	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR, MULTI STATE	04/2013	876.00 -	- -	-	0/0
324	UNCHAHAR-AMETHI - [N22000294]NR, UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
325	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	- -	-	0/0
326	CHANDIGARH-BADDI NL - [N22000296]NR, MULTI STATE	04/2007	328.14 -	- -	-	0/0
327	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]SWR, KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
328	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	- -	-	0/0
329	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
330	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 -	- -	-	0/0
331	MONIGRAM- NIMTITA - [N22000301]ER, MULTI STATE	04/2012	250.93 -	- -	-	0/0
332	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-	0/0
333	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
334	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
335	MM FROM BURAMARA-CHAKULIA - [N22000305]SER, MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
336	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
337	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
338	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
339	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	- -	-	0/0
340	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	-	0/0
341	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA	03/2006	201.00 -	- -	-	0/0
342	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
343	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
344	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0
345	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
346	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-	0/0
347	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-	0/0
348	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
349	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
350	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
351	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-	0/0
352	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-	0/0
353	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-	0/0
	Total		170,856.70 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
354	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
355	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
356	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
357	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015	0/0
358	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	02/2015	0/0
359	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	03/2015	0/0
360	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
361	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	05/2015	0/0
362	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	05/2015	0/0
363	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	07/2015	0/0
364	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 08/2015	08/2015	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
365	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	09/2015	0/0
366	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
367	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
368	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 11/2015	11/2015	0/0
369	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	11/2015	0/0
370	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
371	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 12/2015	12/2015	0/0
372	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 12/2015	12/2015	0/0
373	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	12/2015	0/0
374	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	12/2015	0/0
375	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	12/2015	0/0
376	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2016	01/2016	0/0
377	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	01/2016	0/0
378	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	01/2016	0/0
379	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	01/2016	0/0
380	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	02/2016	0/0
381	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	03/2016	0/0
382	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	03/2016	0/0
383	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	03/2016	0/0
384	YAN TO NIRMAL SEREHAABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	03/2016	0/0
385	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	03/2016	0/0
386	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	03/2016	0/0
387	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	04/2016 -	04/2016	0/0
388	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	06/2016	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
389	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO 45 - [N24000253]NHDP,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016	0/0
390	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
391	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
392	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016	0/0
393	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016	0/0
394	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
395	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016	0/0
396	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	01/2017	0/0
397	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
398	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017	0/0
399	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2017	0/0
400	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	06/2017	0/0
401	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
402	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	- -	10/2017	0/0
403	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	10/2017	0/0
404	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
405	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-	0/0
406	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-	0/0
407	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
408	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
409	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
410	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
411	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
412	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-	0/0

			(August 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
413	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-	0/0
414	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-	0/0
415	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-	0/0
416	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-	0/0
417	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
418	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
419	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-	0/0
420	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	-	0/0
421	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
422	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
423	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
424	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	-	0/0
425	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
426	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-	0/0
427	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
428	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-	0/0
429	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-	0/0
430	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-	0/0
431	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
432	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
433	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-	0/0
434	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
435	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
436	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
437	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-	0/0
438	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
439	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-	0/0
440	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
441	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-	0/0
442	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	-	0/0
443	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-	0/0
444	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
445	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
446	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
447	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	-	0/0
448	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
449	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
450	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
451	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
452	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-	0/0
453	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
454	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	-	0/0
455	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
456	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
457	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
458	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
459	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
460	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
461	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	03/2013 -	-	0/0
462	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	01/2014 -	-	0/0
463	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
464	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	02/2014 -	-	0/0
465	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
466	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
467	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
468	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
469	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
470	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	05/2014 -	-	0/0
471	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	01/2014 -	-	0/0
472	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	08/2013 -	-	0/0
473	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	-	0/0
474	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
475	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
476	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	08/2013 -	-	0/0
477	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	08/2013 -	-	0/0
478	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	08/2013 -	-	0/0
479	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
480	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0
481	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
482	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-	0/0
483	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	-	0/0
484	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	10/2013 -	-	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
485	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	-	0/0
486	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-	0/0
487	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	-	0/0
488	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	-	0/0
489	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-	0/0
490	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-	0/0
491	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	-	0/0
492	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	-	0/0
493	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-	0/0
494	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
495	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
496	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-	0/0
497	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-	0/0
498	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-	0/0
	Total		93,704.12 -			0/0
	<u>SHIPPING AND PORTS</u>					
499	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHINA - [N25000064]SHIPP.,MAHARASHTRA	10/2010	994.82 -	11/2013 -	11/2013	0/0
500	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	12/2015	0/0
501	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	12/2010 -	01/2016	0/0
502	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 2,099.00	12/2010 -	09/2017	0/0
503	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-	0/0
504	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		5,412.28 -			0/0

			(August 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>TELECOMMUNICATIONS</u>					
505	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	07/2015	0/0
506	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 08/2015	10/2015	0/0
	Total		13,718.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
507	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014	0/0
508	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014	0/0
509	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014	0/0
510	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	03/2015	0/0
511	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	04/2015	0/0
512	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	06/2012 -	05/2015	0/0
513	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	09/2014 -	08/2015	0/0
514	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	08/2015	0/0
515	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	08/2015	0/0
516	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	10/2015	0/0
517	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 -	10/2015	0/0
518	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
519	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
520	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	05/2016	0/0
521	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	09/2016	0/0
522	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
523	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2014 -	12/2016	0/0
524	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	09/2015 -	12/2016	0/0
525	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
526	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	06/2017	0/0

			(August 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
527	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
528	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	07/2017	0/0
529	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
530	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
531	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-	0/0
532	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
533	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		113,421.82 -			0/0
	Grand Total		509,184.85			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	578.67	10/2016 -	10/2015
2	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	162.50	08/2016 -	03/2016
	Total		1,559.43 -	1,559.43	741.17		
	<u>COAL</u>						
3	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
4	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	1.00	02/2017 -	03/2016
	Total		188.75 -	188.75	1.00		
	<u>PETROLEUM</u>						
5	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	148.69	09/2016 -	12/2015
6	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	-	01/2017 -	06/2016
7	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	403.22	04/2019 -	03/2019
	Total		6,629.70 -	6,719.84	551.91		
	Grand Total		8,933.40	9,023.54	1,297.60		

List of Projects on schedule w.r.t. Latest Schedule

						(August 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	5,677.00	5,053.45	09/2010 09/2016	09/2016
	Total		3,492.00 -	5,677.00	5,053.45		
	<u>COAL</u>						
2	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
3	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
4	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	0.30	03/2019 -	03/2019
5	GOKUL - [N06000120]	11/2014	267.67 -	267.67	161.05	03/2018 -	03/2018
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	204.45	03/2017 -	03/2017
7	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	107.63	03/2020 -	03/2020
8	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
9	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	93.51	03/2016 -	03/2016
11	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	778.77	03/2023 03/2023	03/2023
12	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
13	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.24	03/2019 -	03/2019
14	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	28.23	03/2021 -	03/2021
15	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
16	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
17	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	97.98	03/2018 -	03/2018
18	AMALGAMATED YEKONA-I & YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	-	03/2025 -	03/2025

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	AMALGAMATED PAUNI-II & III OC MINE - [N06000131]	6/2015	483.69 -	483.69	1.57	03/2021 -	03/2021
20	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.11	03/2020 -	03/2020
21	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.15	04/2017 -	04/2017
22	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	82.58	03/2021 -	03/2021
23	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	43.62	04/2015 04/2019	04/2019
24	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	167.35	03/2018 -	03/2018
25	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	1,056.99	12/2015 04/2018	04/2018
26	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.96	03/2016 -	03/2016
27	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
28	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	804.65	03/2016 -	03/2016
29	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	69.93	03/2019 -	03/2019
30	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	119.03	03/2020 -	03/2020
31	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	42.23	03/2023 -	03/2023
32	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	11.97	03/2021 -	03/2021
33	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	29.83	03/2018 -	03/2018
34	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.38	03/2016 -	03/2016
35	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
	Total		35,867.57 -	35,762.59	4,479.37		
	<u>FERTILISERS</u>						
36	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	30.36	11/2016 -	11/2016
	Total		197.79 -	197.79	30.36		
	<u>MINES</u>						
37	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,856.00	1,856.00	.00		
			-				
	<u>PETROLEUM</u>						
38	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63	2,665.65	1,222.16	03/2015 05/2016	05/2016
39	REWARI KANPUR PIPELINE PROJECT - [N16000145	2/2012	1,210.64	1,446.34	1,149.45	11/2015 -	11/2015
40	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	3/2012	14,225.00	16,504.00	8,205.43	05/2016 -	05/2016
41	IOR OF B-173A FIELD - [N16000140	1/2012	352.49	352.49	128.87	03/2014 05/2016	05/2016
42	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183	3/2014	2,476.82	2,476.82	223.28	12/2018 -	12/2018
43	MH NORTH REDEVELOPMENT PHASE III - [N16000188	6/2014	5,706.47	5,813.25	1,743.40	05/2017 05/2017	05/2017
44	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105	6/2010	2,523.00	2,523.00	1,561.33	01/2014 12/2015	12/2015
45	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133	3/2012	2,592.17	2,592.17	578.28	05/2014 05/2016	05/2016
46	PARADIP LPG IMPORT FACILITY - [N16000196	1/2015	690.00	690.00	-	07/2018 -	07/2018
47	RESID UPGRADATION PROJECT - [N16000184	2/2011	3,110.36	3,110.36	857.20	11/2015 07/2016	07/2016
48	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	7/2011	352.56	450.55	10.60	03/2017 -	03/2017
49	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	2/2012	666.00	838.08	507.74	11/2015 11/2016	11/2016
50	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY [N16000204	8/2015	2,818.88	2,818.88	-	03/2019 -	03/2019
51	TWENTY NOS. FEEDER GAS LINES - [N16000192	3/2009	228.64	214.19	132.32	12/2016 -	12/2016
52	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084	6/2007	736.65	736.65	490.55	09/2011 12/2015	12/2015
53	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191	12/2011	160.00	160.00	5.10	02/2016 02/2016	02/2016
54	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79	1,256.72	910.72	05/2013 12/2015	12/2015
55	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY [N16000180	2/2014	163.88	163.88	26.70	07/2016 -	07/2016
56	CONSTRUCTION OF 6 ETPS - [N16000117	3/2009	317.64	240.95	117.49	09/2012 12/2015	12/2015
57	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY [N16000199	5/2015	257.87	257.87	31.94	11/2016 -	11/2016

						(August 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	60.63	07/2016 -	07/2016
59	MEHESANA REDEVELOPMENT PROJECT - [N16000121]	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017
60	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
61	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	108.32	09/2017 -	09/2017
62	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,671.22	-	11/2019 -	11/2019
63	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	450.37	02/2016 12/2017	12/2017
64	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	240.74	10/2014 10/2016	10/2016
65	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,941.49	75.24	04/2016 12/2017	12/2017
66	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]	1/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016
67	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,899.93	68.90	05/2017 -	05/2017
68	CRU TO ISOMERIZATION (ISOM) - [N16000200]	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016
69	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
70	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	118.17	05/2019 03/2020	03/2020
71	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	367.98	10/2014 10/2015	10/2015
	Total		69,691.22 -	75,527.48	20,494.46		
	<u>POWER</u>						
72	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,841.00	08/2018 -	08/2018
73	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	749.00	12/2016 -	12/2016
74	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017
75	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	4,085.09	01/2018 -	01/2018
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
77	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
78	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,877.00	01/2017 -	01/2017
79	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	8/2014	288.49 -	288.49	24.10	02/2017 -	02/2017
80	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	1,025.86	08/2013 03/2016	03/2016
81	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,154.00	02/2019 -	02/2019
82	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	2.00	08/2016 -	08/2016
83	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,397.00	09/2016 -	09/2016
84	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	166.90	04/2018 -	04/2018
85	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	57.40	04/2018 -	04/2018
86	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	-	05/2016 -	05/2016
87	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	42.40	04/2017 -	04/2017
88	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
89	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	09/2017 -	09/2017
90	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	33.30	11/2016 -	11/2016
91	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	409.80	05/2016 -	05/2016
92	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	4,015.23	12/2009 06/2016	06/2016
93	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	137.90	05/2018 -	05/2018
94	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII [N18000159]	2/2014	908.08 -	908.08	70.00	06/2016 -	06/2016
95	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
96	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	748.00	03/2019 -	03/2019
97	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	85.90	10/2016 -	10/2016

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
98	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
99	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,895.00	09/2017 -	09/2017
100	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	120.00	09/2019 -	09/2019
101	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	63.40	06/2016 -	06/2016
103	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,381.71	872.46	07/2006 10/2016	10/2016
104	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	12.10	04/2017 -	04/2017
105	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	319.24	04/2016 -	04/2016
106	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	2.00	07/2018 -	07/2018
107	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	4,698.00	06/2017 -	06/2017
108	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
109	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
110	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	71.50	12/2015 -	12/2015
111	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7&8 - PART B - [N18000201]	7/2015	307.18 -	307.18	0.80	11/2017 -	11/2017
112	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	498.00	03/2018 -	03/2018
	Total		148,020.83 -	153,926.76	39,479.28		
	<u>RAILWAYS</u>						
113	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
114	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
115	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	-	03/2016 -	03/2016
116	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
117	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
118	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
119	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	536.36	03/2016 -	03/2016
120	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017
121	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	626.11	03/2016 -	03/2016
122	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
123	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
	Total		16,643.70 -	26,719.91	4,210.51		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
124	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	-	01/2016 -	01/2016
125	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]	1/2014	270.00 -	270.00	-	03/2016 -	03/2016
126	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	290.60	04/2008 01/2017	01/2017
127	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
128	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015
129	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	258.40	06/2008 11/2015	11/2015
130	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	242.40	04/2008 12/2015	12/2015
131	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
132	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
133	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	-	01/2016 -	01/2016
134	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	258.40	04/2010 01/2016	01/2016
135	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]	10/2014	244.30 -	244.30	-	12/2016 -	12/2016

						(August 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
136	GUWHATI TO NALBARI (AS-4) - [N24000038	12/2003	175.96 -	175.96	182.50	04/2008 08/2015	08/2015
137	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	13.39	09/2015 -	09/2015
138	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	-	04/2016 -	04/2016
139	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
140	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241	12/2013	177.18 -	177.18	-	03/2016 -	03/2016
141	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017
142	SONAPUR TO GUWAHTI (AS-3) - [N24000044	12/2003	245.00 -	245.00	491.20	03/2008 01/2016	01/2016
143	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238	1/2014	158.04 -	158.04	-	12/2015 -	12/2015
144	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
145	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLLY SECTIO - [N24000242	12/2013	158.65 -	158.65	-	03/2016 -	03/2016
146	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	160.00	197.60	05/2008 12/2015	12/2015
147	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
148	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LWE S - [N24000249	3/2011	218.31 -	339.82	-	12/2015 -	12/2015
149	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA- JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
150	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
151	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
152	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
153	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243	12/2013	244.08 -	244.08	-	03/2016 -	03/2016
154	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO 45 - [N24000253	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
155	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240	3/2014	240.10 -	240.10	-	03/2016 -	03/2016

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		14,796.97 -	15,205.80	2,114.37		
	<u>STEEL</u>						
156	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	54.37	05/2016 -	05/2016
157	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	1.29	09/2017 -	09/2017
158	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
159	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	0.53	12/2017 -	12/2017
160	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	199.13	04/2016 -	04/2016
161	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	25.49	10/2016 -	10/2016
162	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
163	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	22.53	04/2018 -	04/2018
164	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	147.85	07/2016 -	07/2016
165	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	7,729.64	05/2015 12/2016	12/2016
166	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016
	Total		28,397.02 -	28,542.42	8,194.60		
	<u>URBAN DEVELOPMENT</u>						
167	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
168	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
169	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
170	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	-	09/2016 -	09/2016
171	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
172	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	609.63	11/2019 -	11/2019
173	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017

(August 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		46,240.70	46,240.70	609.63		
	Grand Total		365,203.80	389,656.45	84,666.03		

List of ongoing projects having cost overrun w.r.t. to revised schedule

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	-	15.77
	Total		335.61 -	388.53			
	<u>COAL</u>						
2	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
3	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
	Total		630.12 -	678.22			
	<u>HEAVY INDUSTRY</u>						
4	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
5	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						
6	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
7	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	10/2014 -	10/2015	0.00
8	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
9	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
10	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72
	Total		16,329.64 -	19,278.40			
	<u>POWER</u>						
12	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	16,885.00	09/2010 -	-	168.64
14	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
15	BOKARO THERMAL POWER STATION-A - [N18000199	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21
16	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31
17	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
18	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	588.25 -	1,007.16	12/2007 -	10/2015	71.21
	Total		20,301.17 -	41,120.46			
	<u>RAILWAYS</u>						
19	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
20	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
21	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
22	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
23	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
24	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
25	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
26	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
27	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
28	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
29	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
30	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
31	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
32	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
33	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
34	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
35	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	-	346.59
36	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
38	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
39	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
40	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	-	6.99
41	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
42	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	1,383.45	- -	-	242.28
43	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	914.98	- -	03/2016	166.63
44	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	490.00	- -	-	292.00
45	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	1,080.00	- -	-	136.84
46	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
47	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
48	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
49	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
50	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11
51	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
52	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
53	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
54	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
55	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
56	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
57	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
58	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
59	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
60	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
61	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
62	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
63	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
64	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
65	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
66	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
67	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
68	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
69	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
70	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
71	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
72	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
73	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
74	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
75	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
77	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
78	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
79	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
80	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
81	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
82	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
83	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
84	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
85	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
86	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
87	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
88	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
89	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
90	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
91	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
92	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
93	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
94	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
95	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
96	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
97	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
99	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
100	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
101	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
102	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
103	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
104	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
105	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
106	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
107	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
108	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
109	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
110	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
111	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
112	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
113	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
114	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
115	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
116	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
117	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
118	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
119	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
120	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
121	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
122	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
123	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
124	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
125	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
126	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
127	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
128	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
129	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
130	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
131	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
132	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
133	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
134	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
135	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
136	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
137	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
138	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
139	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
140	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
141	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
142	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
143	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
144	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09 -	- -	- -	338.91
145	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17 -	- -	- -	72.37
146	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90 -	- -	03/2019 -	5.00
147	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00 -	- -	- -	18.16
148	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00 -	- -	- -	129.22
149	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00 -	- -	- -	78.78
150	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64 -	- -	- -	180.17
151	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00 -	- -	- -	91.71
152	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83 -	- -	- -	55.74
153	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15 -	- -	- -	28.14
154	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13 -	- -	03/2019 -	154.33
155	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25 -	03/2007 -	03/2016 -	38.80
156	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65 -	- -	03/2018 -	251.85
157	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70 -	- -	03/2020 -	5.00
158	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45 -	- -	03/2018 -	110.44
159	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81 -	- -	03/2018 -	1.86
160	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22 -	- -	- -	109.04
161	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00 -	- -	- -	173.71
162	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24 -	- -	03/2015 -	285.12
163	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95 -	- -	- -	16.29
164	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90 -	- -	03/2020 -	30.00
165	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57 -	- -	03/2018 -	180.56
166	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28 -	- -	03/2017 -	63.25

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
167	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
168	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
169	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
170	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
171	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
172	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
	Total		79,170.45 -	200,328.20			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
173	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
174	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
175	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
176	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
177	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
178	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	-	30.10
179	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
180	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
181	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	12/2015	55.66
182	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
183	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
184	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	02/2015	0.00
	Total		3,606.66 -	5,683.15			

(August 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
185	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2015	300.00
186	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		395.67 -	973.22			
	<u>STEEL</u>						
187	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
188	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		134,685.93	294,208.40			

List of Delayed Projects w.r.t. Latest Schedule

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	20,775.00	12/2008 -	11/2015	83	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	7,095.00	12/2015 -	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,904.00	12/2016 -	05/2018	17	-
	Total		36,950.00 -	41,049.00	32,774.00				
	CIVIL AVIATION								
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	-
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	489.00	439.81	03/2015 -	10/2015	7	-
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	357.62	01/2011 06/2016	09/2017	80	15
	Total		979.06 -	1,016.06	797.47				
	COAL								
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,355.68	03/2012 05/2014	08/2015	41	15
8	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	170.77	10/2014 -	09/2015	11	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	147.58	03/2010 -	03/2016	72	-
10	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,862.99	03/2014 -	03/2016	24	-
11	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,695.40	03/2014 -	03/2016	24	-
12	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 741.62	741.62	481.99	03/2013 -	03/2016	36	-
13	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 535.10	535.10	409.02	03/2015 -	03/2016	12	-
14	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	77.19	07/2012 -	03/2016	44	-
15	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	860.52	03/2013 09/2012	03/2016	36	42
16	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.77	03/2014 -	03/2016	24	-
17	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	60.62	03/2014 -	03/2016	24	-
18	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	365.83	03/2012 -	03/2016	48	-

(August 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	72.86	03/2015 -	03/2016	12	-
20	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	47.90	03/2012 -	03/2016	48	-
21	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	35.92	03/2011 -	03/2016	60	-
22	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	145.20	03/2012 -	03/2016	48	-
23	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	11.26	04/2014 -	03/2016	23	-
24	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	-
25	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	-	05/2014 -	10/2016	29	-
26	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	48.35	04/2014 -	11/2016	31	-
27	ASHOK EXPN OCP CCL (10 MTY) - [N06000096]CCL, JHARKHAND	12/2007	341.63 -	341.63	126.14	03/2011 -	03/2017	72	-
28	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.18	225.39	03/2011 -	03/2017	72	-
29	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	259.40	25.80	03/2012 -	03/2017	60	-
30	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	181.15	03/2013 -	03/2017	48	-
31	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	148.86	03/2010 -	03/2017	84	-
32	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51	-
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	192.31	03/2012 -	03/2017	60	-
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	173.69	03/2013 -	03/2017	48	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	85.40	03/2012 -	03/2017	60	-
36	PUKNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48	-
37	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	67.28	03/2014 -	03/2017	36	-
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	13.85	07/2016 -	03/2017	8	-
39	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	75.60	03/2012 -	03/2018	72	-
40	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	207.52	03/2014 -	03/2018	48	-
41	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	-
42	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	-
43	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	87.64	03/2016 -	03/2018	24	-
44	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2019	48	-

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
45	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	-
46	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60	-
47	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72	-
48	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72	-
	Total		22,249.50	24,704.65	15,201.95				
	<u>STEEL</u>								
49	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00	6,325.00	5,232.17	12/2011	08/2015	44	-
50	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55	898.55	398.16	05/2013 01/2015	08/2015	27	7
51	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48	160.48	136.08	09/2014	09/2015	12	-
52	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65	332.65	211.55	08/2014	11/2015	15	-
53	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09	237.09	204.11	12/2014	11/2015	11	-
54	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33	187.33	163.67	10/2013	12/2015	26	-
55	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05	313.05	267.06	06/2015	12/2015	6	-
56	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00	17,265.00	14,854.52	03/2013	03/2016	36	-
57	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]JINL,ANDHRA PRADESH	07/2011	877.73	877.73	284.58	07/2015	03/2016	8	-
58	SMS-1 CONVERTERS REVAMPING - [N12000090]JINL,ANDHRA PRADESH	05/2012	404.16	404.16	178.99	07/2015	03/2017	20	-
	Total		27,001.04	27,001.04	21,930.89				
	<u>PETROCHEMICALS</u>								
59	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61	9,833.52	-	04/2012 12/2013	09/2015	41	21
	Total		5,460.61	9,833.52	.00				
	<u>PETROLEUM</u>								
60	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40	5,608.40	4,457.47	05/2015 05/2015	08/2015	3	3
61	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00	678.02	437.69	06/2012 03/2015	09/2015	39	6

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,228.45	12/2014 -	09/2015	9	-
63	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	166.96	12/2014 -	09/2015	9	-
64	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,824.71	11/2012 11/2013	10/2015	35	23
65	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL, ODISHA	07/2009	199.75 239.73	239.73	198.69	07/2013 -	10/2015	27	-
66	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,282.08	08/2015 -	12/2015	4	-
67	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	355.47	08/2015 -	12/2015	4	-
68	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	501.91	04/2015 04/2015	12/2015	8	8
69	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	93.65	05/2015 -	12/2015	7	-
70	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,188.73	09/2012 -	03/2016	42	-
71	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	287.63	06/2011 03/2012	03/2016	57	48
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,002.51	10/2011 -	03/2016	53	-
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,430.61	01/2012 -	03/2016	50	-
74	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	12
75	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 -	913.00	428.36	08/2015 -	06/2016	10	-
76	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	320.88	03/2015 11/2015	06/2016	15	7
77	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL, BIHAR	04/2013	480.00 -	480.00	57.02	02/2016 -	07/2016	5	-
78	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2016	53	12
79	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,783.31	03/2013 03/2016	03/2017	48	12
80	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	-
81	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	98.96	09/2017 -	12/2017	3	-
82	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	6.98	01/2013 -	12/2018	71	-
83	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	-
	Total		62,609.33 -	67,534.46	47,724.43				

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
84	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,007.68	1,007.68	907.18	07/2013 -	09/2015	26	-
85	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL, ODISHA	12/2010	2,743.19 -	2,743.19	2,801.90	12/2013 -	09/2015	21	-
86	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL, MADHYA PRADESH	03/2012	213.78 -	213.78	203.04	03/2014 -	09/2015	18	-
87	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, KARNATAKA	03/2005	588.25 -	1,007.16	1,017.21	12/2007 12/2009	10/2015	94	70
88	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL, MULTI STATE	06/2012	1,508.74 -	1,508.74	1,028.18	03/2015 -	10/2015	7	-
89	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL, ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,886.04	03/2013 06/2015	10/2015	31	4
90	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 -	1,927.16	1,539.87	10/2014 -	10/2015	12	-
91	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	151.20	01/2013 -	11/2015	34	-
92	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	487.49	386.02	06/2014 -	11/2015	17	-
93	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	965.58	744.54	11/2012 -	12/2015	37	-
94	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL, MULTI STATE	08/2010	1,677.57 -	1,677.57	1,368.02	04/2013 -	12/2015	32	-
95	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	1,585.12	1,507.86	11/2013 -	12/2015	25	-
96	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND	10/2011	558.26 -	558.26	468.01	11/2013 -	12/2015	25	-
97	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL, MULTI STATE	12/2011	2,422.66 -	2,422.66	2,151.06	08/2014 -	12/2015	16	-
98	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	539.80	02/2014 -	12/2015	22	-
99	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE	12/2011	297.33 346.79	346.79	286.77	08/2014 06/2015	12/2015	16	6
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL, MULTI STATE	09/2012	524.40 -	524.40	201.22	05/2015 -	12/2015	7	-
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	335.37	02/2012 -	03/2016	49	-

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
102	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,057.39	08/2012 -	03/2016	43	-
103	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,989.30	01/2013 -	03/2016	38	-
104	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	-
105	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	1.00	03/2016 -	05/2016	2	-
106	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,853.00	09/2009 -	06/2016	81	-
107	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	521.59	09/2010 06/2013	06/2016	69	36
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	474.66	11/2011 -	06/2016	55	-
109	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,187.60	12/2012 -	06/2016	42	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	498.72	07/2013 11/2015	06/2016	35	7
111	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,736.75	05/2014 -	06/2016	25	-
112	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,837.46	09/2014 -	06/2016	21	-
113	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,224.73	07/2014 -	06/2016	23	-
114	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,267.32	01/2015 -	06/2016	17	-
115	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	83.82	09/2014 -	06/2016	21	-
116	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,854.89	06/2015 -	06/2016	12	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	540.92	11/2014 -	06/2016	19	-
118	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,543.51	10/2014 -	06/2016	20	-
119	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	903.85	12/2015 -	06/2016	6	-

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
120	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	331.99	03/2016 -	06/2016	3	-
121	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	1.00	02/2016 -	06/2016	4	-
122	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	247.00	06/2015 -	08/2016	14	-
123	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	810.03	06/2015 -	08/2016	14	-
124	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,305.13	08/2014 12/2015	09/2016	25	9
125	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,107.18	01/2016 -	11/2016	10	-
126	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	11/2016	7	-
127	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,895.55	11/2008 03/2012	12/2016	97	57
128	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,137.48	10/2012 -	12/2016	50	-
129	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,025.10	08/2013 -	12/2016	40	-
130	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,084.75	01/2015 -	12/2016	23	-
131	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,138.53	11/2012 -	12/2016	49	-
132	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,422.00	09/2011 -	03/2017	66	-
133	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,924.79	05/2014 -	06/2017	37	-
134	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,263.00	11/2016 -	08/2017	9	-
135	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	31.54	02/2014 -	09/2017	43	-
136	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9	-
137	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	1.90	10/2017 -	11/2017	1	-
138	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,802.00	01/2011 10/2014	03/2018	86	41
139	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,382.65	07/2010 02/2016	05/2018	94	27

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
140	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59	7,818.68	5,185.15	09/2009	12/2018	111	-
141	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48	3,846.30	2,534.00	03/2013	12/2018	69	-
142	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58	3,745.08	724.79	06/2013	12/2019	78	-
	Total		137,639.74	160,777.55	113,073.50				
	HEAVY INDUSTRY								
143	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE, MULTI STATE	04/2011	1,718.00	3,827.30	-	09/2011	12/2017	75	-
	Total		1,718.00	3,827.30	.00				
	RAILWAYS								
144	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00	874.57	730.11	03/2013	09/2015	30	-
145	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]JER, WEST BENGAL	04/1999	207.52	207.52	223.44	12/2012	09/2015	33	-
146	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]JECR, BIHAR	04/2002	921.00	2,363.00	1,691.12	03/2009	10/2015	79	34
147	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00	245.39	249.33	12/2008	10/2015	82	-
148	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07	335.00	230.67	06/2004	12/2015	138	-
149	PATNA GANGA BRIDGE (NL), ECR - [220100308]JECR, BIHAR	04/2001	624.47	2,921.00	2,521.72	10/2007	12/2015	98	36
150	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20	800.00	793.71	03/2010	12/2015	69	-
151	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44	1,781.98	440.08	03/2004	03/2016	144	63
152	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]JRE, UTTAR PRADESH	02/2008	171.10	275.08	141.55	03/2012	03/2016	48	27
153	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90	331.40	182.22	12/2012	03/2016	39	-
154	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31	5,500.00	4,734.45	03/2009	03/2016	84	-
155	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44	583.00	144.66	12/2015	03/2016	3	-
156	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00	1,242.25	1,005.81	03/2007	03/2016	108	-
157	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72	2,397.72	204.56	03/2016	06/2016	3	-

(August 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
158	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90	230.00	68.67	03/2015	12/2016	21	-
159	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10	714.10	65.93	04/2016	03/2017	11	-
160	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00	4,996.19	3,410.06	04/2008	06/2017	110	39
161	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98	1,727.27	743.74	12/2010	03/2018	87	-
162	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00	2,531.34	1,732.43	12/2008	03/2018	111	-
163	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34	2,876.00	823.83	03/2014	03/2018	48	-
164	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34	2,820.25	199.31	04/2014	03/2018	47	36
165	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58	4,874.58	1,911.65	03/2016	06/2018	27	-
166	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00	19,565.00	10,658.34	11/2002	12/2018	193	-
167	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56	6,570.75	2,787.99	03/2011	03/2019	96	60
168	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30	1,544.40	590.26	03/1998	12/2019	261	-
169	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90	2,371.85	486.25	03/2005	12/2019	177	132
170	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97	1,428.00	466.36	06/2005	12/2019	174	101
171	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48	4,190.00	88.56	12/2015	03/2020	51	-
	Total		24,665.62	76,297.64	37,326.81				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
172	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00	398.00	344.40	02/2014	09/2015	19	-
173	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00	2,388.00	2,301.00	06/2014	11/2015	17	-
174	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00	209.00	11.28	01/2013	12/2015	35	-
175	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00	1,232.00	590.90	08/2015	02/2016	6	-
176	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00	1,047.00	295.70	06/2014	03/2016	21	-
177	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	484.19	285.50	10/2014	03/2016	17	-
178	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	1,410.00	929.60	09/2014	06/2016	21	-
179	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75	1,693.75	2,762.00	08/2011	09/2016	61	-
180	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00	586.00	237.60	01/2014	12/2016	35	-

(August 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
181	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00	2,848.00	1,138.00	03/2014	04/2017	37	-
	Total		12,295.94	12,295.94	8,895.98				
	<u>SHIPPING AND PORTS</u>								
182	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00	600.00	139.80	03/2006	12/2015	117	-
183	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39	669.46	407.32	12/2010	01/2016	61	-
184	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00	1,460.00	1,038.00	12/2010	09/2017	81	-
	Total		1,744.39	2,729.46	1,585.12				
	<u>TELECOMMUNICATIONS</u>								
185	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00	384.00	72.17	10/2010	10/2015	60	2
	Total		384.00	384.00	72.17				
	<u>URBAN DEVELOPMENT</u>								
186	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00	2,494.00	1,280.91	09/2014	08/2015	11	-
187	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43	238.43	-	02/2015	08/2015	6	-
188	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00	315.00	3.11	06/2015	08/2015	2	-
189	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83	270.83	-	11/2014	10/2015	11	-
190	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85	261.85	142.00	05/2013	10/2015	29	-
191	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00	23,136.00	-	01/2015	12/2015	11	-
192	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01	405.01	-	12/2014	04/2016	16	-
193	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86	171.86	-	03/2016	05/2016	2	-
194	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00	14,600.00	11,032.96	12/2015	08/2016	8	-

(August 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
195	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	16,971.38	03/2016 -	12/2016	9	-
196	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	-
197	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	-
198	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	-
	Total		81,707.72 -	81,707.72	29,436.15				
	Grand Total		415,404.95	509,158.34	308,818.47				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	05/2018	12320	17
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	11/2015	13171	83
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	AAI	10/2012	03/2015	09/2015	217.6	6
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT (MOHALI) PH - II	AAI	02/2011	03/2015	10/2015	452	7
7	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
8	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
9	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2016	365.01	9
10	BAROUD OC EXPANSION (RCE) - 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
11	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	08/2015	4904.54	41
13	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
14	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
15	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
16	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2016	209.78	12
17	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
18	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
19	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24
20	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
22	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	36
23	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
24	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
25	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2016	302.96	72
26	CHURCHA ROUG (1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	24
27	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
28	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
29	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
30	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
31	JAGANNATHPOR OCP (3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
32	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	706.4	44
33	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
34	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
35	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
36	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2016	418.97	48
37	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
38	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
39	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
40	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
41	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
42	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
43	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
45	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
46	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
47	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
48	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
49	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	09/2015	364.75	11
50	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
51	RCE OF INDARAM OCP (1.20 MTPA)	SCCL	07/2011	03/2015	03/2019	162.76	48

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	HIPE	04/2011	09/2011	12/2017	1718	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	09/2015	5460.61	41

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
54	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	06/2016	871.35	15
55	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732	53
56	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
57	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2016	2592.17	24
58	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
59	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV)	ONGC	01/2010	03/2013	06/2016	723.64	39
60	MEHESANA REDEVELOPMENT PROJECT	ONGC	11/2010	04/2015	12/2017	3823	32

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
61	102 MW WIND POWER PROJECT	ONGC	07/2010	06/2012	09/2015	1106	39
62	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	11/2016	270	53
63	MARKETING TERMINAL AT PARADEEP	IOCL	07/2009	07/2013	10/2015	199.75	27
64	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	03/2016	993	50
65	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
66	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
67	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	ONGC	10/2013	10/2014	10/2015	429.06	12
68	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
69	AHMEDABAD REDEVELOPMENT PROJECT	ONGC	11/2010	12/2014	12/2017	1916.1	36
70	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	22
71	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	12/2015	1138.5	8
72	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	12/2015	736.65	51
73	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523	23
74	ANKLESWAR REDEVELOPMENT	ONGC	11/2010	12/2014	12/2018	2189.63	48
75	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
76	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	12/2015	317.64	39
77	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
78	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2015	861.79	31
79	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
80	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	29777	35
81	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
82	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
83	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	07/2016	3110.36	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
84	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	600.17	17
85	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	352.49	26
86	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY	BPCL	03/2012	12/2014	1419	9
87	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	913	10
88	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	24
89	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	279	9

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
90	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
91	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2016	2514.88	6
92	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	25
93	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
94	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
95	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	06/2016	752.64	35
96	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	11/2015	250.03	34
97	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2016	1272.8	49
98	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313	51
99	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
100	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	12/2015	2422.66	16
101	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2016	2496.9	78
102	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	12/2015	558.26	25
103	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER (MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
104	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	05/2018	1657	94
105	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	11/2015	487.49	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
106	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	06/2016	2127.51	23
107	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	31
108	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	10/2015	588.25	94
109	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
110	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
111	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2016	477.69	69
112	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX	PGCIL	02/2009	02/2012	03/2016	410.29	49
113	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2016	4824.12	50
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	12/2015	1677.57	32
115	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	12/2015	965.58	37
116	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	12/2015	1585.12	25
117	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XVIII	PGCIL	02/2009	11/2011	06/2016	509.66	55
118	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	12/2016	4404.57	23
119	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	10/2015	2074.86	31
120	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2016	11130.19	40
121	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
122	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2016	2144	42
123	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	PGCIL	12/2010	12/2013	09/2015	2743.19	21
124	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	11/2016	374.63	7
125	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	09/2017	195.42	43
126	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	06/2017	5353	37
127	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
128	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
129	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
130	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	09/2015	421.01	26
131	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMP-PART B	PGCIL	02/2012	10/2014	10/2015	1927.16	12
132	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
133	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION)	PGCIL	03/2012	03/2014	09/2015	213.78	18
134	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2016	9569.76	12
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2016	723.63	19
136	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2016	3201.44	20
137	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	12/2015	552.44	22
138	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2015	297.33	16
139	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	12/2011	08/2014	09/2016	1746.65	25
140	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
141	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	97
142	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2018	8692.97	86
143	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	06/2016	1422.85	17
144	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
145	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	PGCIL	06/2012	03/2015	10/2015	1508.74	7
146	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	12/2015	524.4	7
147	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
148	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
149	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
150	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
151	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
152	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	MRTP	03/1996	03/2004	03/2016	495.44	144
153	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2018	733	111
155	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
156	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	98
157	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
158	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTP	04/2008	03/2014	03/2019	5300	60
159	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	09/2015	207.52	33
160	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
161	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
162	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
163	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	10/2015	921	79
164	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	10/2015	120	82
165	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.2	69
166	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
167	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
168	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
169	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
170	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2018	2500	193
171	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
172	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
173	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
174	RANCHI-LOHARDAGA (GC) ,SER	SER	04/1997	06/2004	12/2015	194.07	138
175	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482	30
176	KATAKHAL TO BHAI RABI	NFR	04/1998	12/2012	03/2016	227.9	39

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
177	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	02/2016	1232	6
178	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
179	BEAWAR-PALI-PINDWARA	NHAI	12/2011	06/2014	11/2015	2388	17
180	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
181	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2016	1410	21
182	BHOPAL-SANCHI	NHAI	10/2011	01/2013	12/2015	209	35
183	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
184	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	09/2015	398	19
185	DHARAMTUL TO SONAPUR, KM 205-183 (AS- 20)	NHAI	12/2003	05/2008	12/2015	160	91
186	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	08/2015	175.96	88
187	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	12/2015	198.16	92
188	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	01/2016	245	94
189	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	01/2016	217.61	69
190	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	01/2017	208	105
191	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	11/2015	225	89
192	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	09/2016	1693.75	61
193	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
194	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	01/2016	366.39	61
195	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT TR	11/2007	12/2010	09/2017	1228	81

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
196	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	SAIL	11/2012	06/2015	12/2015	313.05	6
197	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	12/2015	187.33	26
198	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	11/2015	237.09	11
199	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	03/2016	877.73	8
200	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
201	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	09/2015	160.48	12
202	EXPANSION OF BOKARO STEEL PLANT	SAIL	05/2010	12/2011	08/2015	6325	44
203	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	03/2016	17265	36
204	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	NMDC	02/2011	05/2013	08/2015	898.55	27
205	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	03/2017	404.16	20
206	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	11/2015	332.65	15

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
207	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	10/2015	384	60

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
208	FARIDABAD EXTENSION	DMRCL	09/2011	09/2014	08/2015	2494	11
209	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	06/2017	884.3	34
210	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	10/2015	261.85	29
211	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2015	270.83	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
212	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
213	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	12/2016	156.57	15
214	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	CPWD	11/2012	02/2015	08/2015	238.43	6
215	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
216	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8
217	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	12/2015	23136	11
218	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185	
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	17270	4099	
COAL								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	2030.78	3583.77	1552.99	
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05	
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	4904.54	6602.74	1698.2	
HEAVY INDUSTRY								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	1718	3827.3	2109.3	
PETROCHEMICALS								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9833.52	4372.91	
PETROLEUM								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
8	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	3513.07	4619.94	1106.87	
9	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	4941.49	817.14	
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65	
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495	
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98	
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08	
14	REWARI KANPUR PIPELINE PROJECT	HPCL	02/2012	11/2015	1210.64	1446.34	235.7	
15	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279	
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02	
17	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778	

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
21	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7818.68	3899.09
22	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	16885	10599.67
23	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
24	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77
25	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
26	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.68	586.67
27	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
28	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	588.25	1007.16	418.91
29	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2159.07	379.78
31	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68
32	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.7	482.05
33	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1487.49	913.5
34	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	1657	2978.86	1321.86
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6476.34	3979.44
36	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3745.08	1253.5
37	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
38	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
40	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
41	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
42	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
43	KARUR-SALEM (NL) , SR	SR	02/1997	N.A.	155.55	800	644.45
44	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
45	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
46	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
47	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
48	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
49	GADWAL - RAICHUR (NL) , SCR	SCR	04/1998	02/2011	92.63	270	177.37
50	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
51	JIND-SONEPAT (NL) , NR	NR	01/2004	03/2012	238.56	740	501.44
52	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
53	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	921	2363	1442
54	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
55	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
56	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
57	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
58	KATAKHAL TO BHAI RABI	NFR	04/1998	12/2012	227.9	331.4	103.5
59	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
60	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	03/2008	743	1117.11	374.11

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
62	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
63	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
64	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
65	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
66	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
67	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
68	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
69	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
70	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
71	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
72	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
73	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
74	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
75	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
76	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
77	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
78	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
79	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
80	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
81	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
82	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87
83	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
85	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
86	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
87	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
88	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
89	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
90	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
91	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
92	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
93	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
94	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
95	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
96	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
97	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
98	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
99	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
100	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
101	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
102	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
103	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
104	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
105	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
106	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
108	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
109	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
110	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
111	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
112	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
113	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
114	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
115	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
116	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
117	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
118	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
119	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
120	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	SWR	02/1997	N.A.	295	1289.92	994.92
121	HUBLI-ANKOLA (NL) , SWR	SWR	04/1997	N.A.	227	2135	1908
122	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
123	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
124	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
125	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
126	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
127	MUNEERABAD-MAHABOONNAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	645	426.76
128	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
129	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
131	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
132	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
133	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
134	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
135	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	288	121.84
136	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	968.6	664.6
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
138	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	847.75	222.45
139	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	19565	17065
140	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
141	KANPUR-KASGANJ-MATHURA (GC) , NER	NER	03/1997	N.A.	677.97	1651.54	973.57
142	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
143	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
144	KHURDA ROAD-BOLANGIR (NL) ECOR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
145	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
146	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
147	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
148	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
149	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	1630.97	1383.31
150	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
151	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
152	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
154	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
155	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
156	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
157	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
158	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
159	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
160	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
161	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
162	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	800	112.8
163	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	289.93	153.31
164	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	276	142.59
165	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	818.29	635.06
166	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
167	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
168	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
169	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
170	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
171	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
172	RAMGANJMUNDI-BHOPAL (NL) ,WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
173	MAIBANG TO LUMDING (AS-25) , KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
174	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
175	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
176	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
177	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
178	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT	11/2007	12/2010	1228	1460	232
179	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
180	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
181	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	373.22	127.55
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
182	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
183	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	8692	12291	3599
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
184	BANGALORE METRO RAIL PROJECT	MRTP	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	11/2015	1,3171.00	1,7270.00	4099	83
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	08/2015	4904.54	6602.74	1698.2	41
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	1228.39	1016.05	36

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	HIPE	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	09/2015	5460.61	9833.52	4372.91	41

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	06/2016	871.35	1200.00	328.65	15
8	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	4941.49	817.14	20
9	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	4619.94	1106.87	22
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	03/2016	993.00	1693.00	700	50
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732.00	1227.00	495	53
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2015	861.79	1256.72	394.93	31

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	462.79	152.98	24
14	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	2,9777.00	3,4555.00	4778	35
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
16	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
17	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	09/2015	421.01	1007.68	586.67	26
18	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
19	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
20	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313.00	4237.67	1924.67	51
21	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	3745.08	1253.5	78
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2016	2496.90	6476.34	3979.44	78
23	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	07/2010	05/2018	1657.00	2978.86	1321.86	94
24	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	1487.49	913.5	31
25	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	09/2016	1746.65	2228.70	482.05	25
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7818.68	3899.09	111
27	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81
28	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2016	477.69	721.81	244.12	69

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
29	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	10/2015	2074.86	2348.37	273.51	31
30	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
31	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	10/2015	588.25	1007.16	418.91	94
32	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	2159.07	379.78	97
33	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10
34	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2018	8692.97	1,5095.67	6402.7	86

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
35	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
37	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
38	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
39	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
40	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	10/2015	921.00	2363.00	1442	79
41	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	10/2015	120.00	245.39	125.39	82
42	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	112.8	69
43	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
44	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
45	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
46	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	MRTD	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
47	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
49	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
50	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
51	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
52	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTD	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
53	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
54	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
55	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
56	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482.00	874.57	392.57	30
57	RANCHI-LOHARDAGA (GC) ,SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138
58	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
59	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
60	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	01/2016	366.39	669.46	303.07	61

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
61	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT TRU	11/2007	12/2010	09/2017	1228.00	1460.00	232	81

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun
