

केन्द्रीय क्षेत्र की परियोजनाओं
CENTRAL SECTOR PROJECTS
₹150 करोड़ और अधिक लागत वाली
(₹ 150 Crore and above)
370वीं फ्लैश रिपोर्ट / 370th Flash Report
अगस्त, 2016 / August, 2016



भारत सरकार / Government of India
सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय
Ministry of Statistics and Programme Implementation
आधारी संरचना और परियोजना प्रबोधन प्रभाग
Infrastructure and Project Monitoring Division
सरदार पटेल भवन, संसद मार्ग
Sardar Patel Bhavan, Sansad Marg,
नई दिल्ली / New Delhi-110001
वेबसाइट / Website- www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents	
	Pages
Executive Summary Hindi	1-24
Executive Summary English	25-43
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2016-2017	44-47
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2016-2017	48-48
Summary of projects	49-65
Graphical Presentation of All Projects	66-82
Sector wise Analysis of Projects	83-141
Sector wise Graph	142-158
Annexures	159-159
Status of central sector projects costing Rs.150 Crore and above	160-160
List of projects in which expenditure is more than approved cost	161-167
Details of Projects Ahead of Schedule w.r.t. Original Schedule	168-168
Details of On Schedule Projects w.r.t. Original Schedule	169-182
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	183-196
Details of Delayed Projects w.r.t. Original Schedule	197-224
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	225-229
Details of Projects Without Date of Commissioning	230-251
Details of projects without original Date of Commissioning	252-256
Details of projects without Milestones w.r.t. original schedule	257-292
List of Projects Ahead of Schedule w.r.t. Latest Schedule	293-294
List of Projects on schedule w.r.t. Latest Schedule	295-312
List of ongoing projects having cost overrun w.r.t. to Latest schedule	313-322
List of Delayed Projects w.r.t. Latest Schedule	223-337
Details of Central Sector Projects Showing Time overruns of 6 Months and More	338-352
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	353-363
Details Of Central Sector Projects Showing Time Overruns of 6 Months and More and cost overruns of Rs. 100 Crore and above	364-368
Details of Ongoing Projects Under Public-Private Partnership Mode	369-373

कार्यकारी सारांश

1. अगस्त, 2016 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 1167 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अगस्त, 2016 के दौरान, 4 परियोजनाएं (सड़क तथा परिवहन में 2 और विद्युत तथा रेलवे क्षेत्र में प्रत्येक में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 1167 परियोजनाओं में से, 337 परियोजनाएं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 32 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 32 परियोजनाओं में से, 7 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	सड़क परिवहन एवं राजमार्ग	425	111	11	1
2.	रेलवे	360	41	2	0
3.	विद्युत	117	61	7	4
4.	कोयला	88	40	4	0
5.	पेट्रोलियम	80	38	1	1
6.	इस्पात	34	14	4	0
7.	शहरी विकास	29	17	2	1
8.	स्वास्थ्य और परिवार कल्याण	9	4	0	0
9.	पोत परिवहन एवं पत्तन	8	3	1	0
10.	परमाणु ऊर्जा	4	3	0	0
11.	नागर विमानन	4	1	0	0
12.	खान	3	1	0	0
13.	उर्वरक	2	1	0	0
14.	दूरसंचार	2	1	0	0
15.	पेट्रोरसायन	1	0	0	0
16.	भारी उद्योग	1	1	0	0
कुल		1167	337	32	7

3. 1167 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹14,33,476.53 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹16,10,504.54 करोड़ होने की संभावना है, जो ₹1,77,028.01 करोड़ (मूल लागत का 12.35%) की समग्र लागत वृद्धि को दर्शाता है। अगस्त, 2016 तक इन परियोजनाओं पर किया गया व्यय ₹6,30,581.41 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 39.15% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31-08-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	लागत वृद्धि (%)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं 56. फायर निविदाओं की एयरफील्ड आपूर्ति	10/2012	217.60	244.10	12.18
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
2	जगन्नाथपुर ओसीपी (3.00 मेवा.)	09/2008	152.43	459.59	201.51
3	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	87.58
4	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	16.86
5	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	12.97
उर्वरक					
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ ट्रॉम्बे	10/2014	197.79	209.44	5.89
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78

	पेट्रोरसायन				
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	9965.00	82.49
	पेट्रोलियम				
1	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
2	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
3	इम्फाल में पॉल डीपोट के निर्माण मणिपुर	08/2010	103.02	171.04	66.03
4	कोरबा में मार्केटिंग टॉप	01/2011	141.86	232.00	63.54
5	उरान चाकन/शिकरापुर एलपीजी पाइपलाइन	12/2009	309.81	462.79	49.38
	विद्युत				
1	तुरीअल हाइड्रो इलेक्ट्रिक परियोजना (60 मेवा.)	07/1998	368.72	1441.52	290.95
2	सुबनसिरी लोअर एचईपी(8X250मेगावाट) एनएचपीसी	09/2003	6285.33	17435.15	177.39
3	पारे जल विद्युत परियोजना	12/2008	573.99	1581.04	175.45
4	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	147.51
5	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.57	139.32
	रेलवे				
1	गजोल-इटाहार सहित इकलाखी-बेलूरघाट से नई बीजी लाइन (एनएल) एनईएफआर	04/1983	36.80	1336.57	3531.98
2	ललितपुर-सतना-रीवा-सिंगरौली एनएल, (एनसीआर)	09/1998	247.66	5050.00	1939.09
3	जिरिबम से इम्फाल (तुपुई) एनएल, (एनईएफआर)	04/2003	727.56	9658.00	1227.45
4	अकोला-खंडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
5	बंगलूर सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
	सड़क परिवहन एवं राजमार्ग				
1	पानीपत-जालंधर 6 लेन (96 किमी . से 387.1 किमी)	05/2009	1108.00	2288.00	106.50
2	अरुणाचल प्रदेश पैकेज के तहत अरुणाचल प्रदेश में यूपिया-एचओजे सेक्शन की दो लेनिंग	12/2009	104.00	201.00	93.27

	(20.40किमी.)				
3	मैबंग से लुमडिंग (एस-25) 83.400 किमी से 111.000 किमी	12/2003	199.81	385.13	92.75
4	मैबंग से लुमडिंग (एस-24) 111.000 किमी से 126.450 किमी.	12/2003	155.04	280.13	80.68
5	अरुणाचल प्रदेश के तहत अरुणाचल प्रदेश में खोंसा-टीस्सा-लुमडिंग (एनएच-52बी) (42.50 किमी.)	12/2011	156.63	276.00	76.21
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
3	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	66.82
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-3 का निर्माण	10/2013	198.94	235.15	18.20
5	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 का निर्माण	02/2015	244.50	258.33	5.66
इस्पात					
1	सिंटर मशीन की रिक्विजिटिंग - 1 और 2	12/2009	343.00	488.40	42.39
2	गुलबर्गा में मेडिकल कॉलेज और आस्पताल का निर्माण	05/2005	768.88	1070.97	39.29
3	प्रधानमंत्री ग्राम सड़क योजना चरण- VIII के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	206.71	17.79
4	प्रधानमंत्री ग्राम सड़क योजना चरण- V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	175.94	17.50
5	प्रधानमंत्री ग्राम सड़क योजना चरण- VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	12.04
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	14405.01	125.25
2	प्लॉट सं. सी-41-43 जी ब्लॉक बांद्रा में आयकर विभाग के लिए कार्यालय	02/2011	241.33	349.33	44.75

	भवन				
3	पूर्व किदवई नगर का पुनर्विकास	06/2012	4264.00	5298.00	24.25

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार हैं:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31-08-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	लागत वृद्धि (रु. करोड़)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं 56. फायर निविदाओं की एयरफील्ड आपूर्ति	10/2012	217.60	244.10	26.50
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
2	जगन्नाथपुर ओसीपी (3.00 एमटीवाई)	09/2008	152.43	459.59	307.16
3	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	227.17
4	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	70.65
5	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	55.82
उर्वरक					
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ थ्रोम्बे	10/2014	197.79	209.44	11.65
भारी उद्योग					

1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोरसायन					
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9965.00	4504.39
पेट्रोलियम					
1	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
2	बी-127 क्षेत्रों का एकीकृत विकास	12/2011	2059.63	2665.65	606.02
3	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	495.00
4	रिग सागर सम्राट से मोबाइल ऑफशोर यूनिट का परिवर्तन (एमओपीएस)	03/2011	861.79	1256.72	394.93
5	नहरकटिया-बरौनी कच्चा तेल ट्रंक पाइपलाइन के कच्चा तेल पंप स्टेशनों का उन्नयन	09/2012	871.35	1200.00	328.65
विद्युत					
1	सुबानसिरी लोअर एच.ई.पी (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	17435.15	11149.82
2	बाढ़ एसटीपीपी (3X660मेवा.), एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	रघुनाथपुर थर्मल पावर स्टेशन चरण-	04/2007	4122.00	9606.82	5484.82
4	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) द्वितीय	09/2002	3919.59	8398.75	4479.16
5	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	3683.06
रेलवे					
1	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	2500.00	19565.00	17065.00
2	जिरीबाम से इंफाल (तुपुई) (एनएल) (एनईएफआर)	04/2003	727.56	9658.00	8930.44
3	लुमडिंग-सिलचर जिरीबाम, बदरपुर-बरायग्रामकुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	7000.00	5323.69
4	ललितपुर-सतना-रीवा-सिंगरौलीएनएल, (एनसीआर)	09/1998	247.66	5050.00	4802.34
5	भैरबी सैरांग, एनएल, एनईएफआर	04/2008	619.34	4600.00	3980.66

सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर 6 लेन 96 किमी . 387.1 किमी	05/2009	1108.00	2288.00	1180.00
2	गोलियार शिवपुरी के चार लेनिंग	05/2013	1055.00	1601.77	546.77
3	मैबंग से लुमडिंग (एएस-25) 83.400 किमी से 111.000 किमी	12/2003	199.81	385.13	185.32
4	हरंगाजों से मैबंग, एनएच-54	12/2003	196.00	331.23	135.23
5	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी से 126.450 किमी एनएच -54	12/2003	155.04	280.13	125.09
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
3	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	164.16
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-3 के निर्माण	10/2013	198.94	235.15	36.21
5	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	13.83
इस्पात					
1	गुलबर्गा में पैरामेडिकल और संबद्ध स्वास्थ्य संस्थान का निर्माण	05/2005	768.88	1070.97	302.09
2	सिंटर मशीन की रिवैम्पिंग - 1 और 2	12/2009	343.00	488.40	145.40
3	पीएमजीएसवाई चरण-VIII के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	206.71	31.22
4	पीएमजीएसवाई चरण-V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	175.94	26.21
5	पीएमजीएसवाई चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	24.39
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	14405.01	8010.01
2	पूर्व किदवई नगर का पुनर्विकास	06/2012	4264.00	5298.00	1034.00

3	बांद्रा प्लाट सं. सी 41-43 ब्लॉक के आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	349.33	108.00
---	--	---------	--------	--------	--------

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 1167 परियोजनाओं में से, 282 समय पर, 337 विलंबित तथा 273 परियोजनाएं लागत वृद्धि दर्शाती हैं तथा 85 परियोजनाएं समय तथा लागत वृद्धि दोनों दर्शाती हैं । तथापि, विलंबित परियोजनाओं की संख्या में 283 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 81 परियोजनाएं किसी आरंभ संबंधी तारीख के बिना स्वीकृत की गई हैं तथा 460 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 337 विलंबित परियोजनाओं में से, 68 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 54 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 138 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 77 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31-08-2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत की तारीख	अनुमानित लागत की तारीख	समय वृद्धि (माह में)
परमाणु ऊर्जा					
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी 500 मेगावाट)	09/2003	09/2010	10/2017	85
2	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	12/2019	36
3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	11/2018	35
नागर विमानन					
1	पाक्यांग सिक्किम हवाई अड्डे में नए हवाई अड्डे का निर्माण	01/2009	01/2011	09/2017	80
कोयला					
1	रामागुंडम ओसी-II विस्तार	12/2009	03/2012	03/2023	132
2	बलराम ओसीपी विस्तार, एमसीएल 8.00	12/2007	03/2010	03/2019	108

	एमटीवाई				
3	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	07/2012	03/2021	104
4	कुल्दा ओसीपी (महानदी कोयला फील्ड लिमिटेड)	01/2005	03/2010	03/2017	84
5	चूरी बेंटी यूजी (0.81 एमटीवाई)	08/2007	03/2011	03/2018	84
उर्वरक					
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ ट्रोम्बे	10/2014	11/2016	09/2017	10
स्वास्थ्य एवं परिवार कल्याण					
1	एम्स-रायबरेली-हाउसिंग	10/2013	11/2013	10/2016	35
2	आईआईटी खड़गपुर अस्पताल ब्लॉक का निर्माण	12/2014	05/2017	07/2017	2
3	एम्स- मातृ एवं शिशु ब्लॉक	12/2013	05/2017	06/2017	1
4	एम्स ओपीडी (नए)	08/2014	05/2017	06/2017	1
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
खान					
1	सीएपीएसी के वर्तमान ओपन कास्ट खान के तहत मलंजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	09/2017	04/2020	31
पेट्रोलियम					
1	फुप्लुर-हल्दिया पाइपलाइन परियोजना चरण -I	07/2009	01/2013	12/2018	71
2	12 ऑफशोर सप्लाय वेसेल्स (ओएसवी) का निर्माण	06/2007	09/2011	03/2017	66
3	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	12/2009	06/2011	10/2016	64
4	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	01/2012	09/2016	56
5	2000 एचपी ड्रिलिंग रिग का 2 एनओएस की खरीद	04/2010	06/2012	08/2016	50
विद्युत					
1	तुरीअल जल विद्युत परियोजना (60 मेवा.)	07/1998	07/2006	09/2017	134
2	पार्वती एचईपी (4X200 मेगावाट)	09/2002	09/2009	12/2018	111

	(एनएचपीसी) II				
3	कुडनकुलम एपीपी पारेषण प्रणाली (पीजीसीआईएल)	05/2005	11/2008	12/2017	109
4	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	12/2009	10/2017	94
5	बाढ़ एसटीपीपी (3X660मेवा.), एनटीपीसी	02/2005	01/2011	05/2018	88
रेलवे					
1	गोंदिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
2	जग्गाएपेट -मेललेचेरिक	04/2007	01/1999	06/2017	221
3	एनएल के लिए 6 एमएमएस के साथ 96 किमी. जीसी बांकुड़ा - दामोदर घाटी रेलवे लाइन (जीसी) (एसईआर)	04/1998	03/2003	03/2021	216
4	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	11/2002	12/2018	193
5	ललितपुर-सतना-रेवा सिंगराली एनएल, एनसीआर	09/1998	05/2008	03/2023	178
सड़क परिवहन एवं राजमार्ग					
1	बिजनी से असम/पश्चिम बंगाल सीमा चरण.II, 30.00 किमी. से 0.00 किमी., एनएच-31 सी	12/2003	06/2005	12/2016	138
2	हरंगाजो से मैबंग, 164.08 किमी.- 190.587 किमी. एनएच-54	12/2003	09/2007	03/2017	114
3	आगरा-बाईपास (एन एस -1 / यूपी-1), एनएच 2,3	12/2003	09/2007	09/2016	108
4	नलबारी से बिजनी (एएस-7)	12/2003	04/2008	12/2016	104
5	सोनापुर से गुवाहाटी (एएस -3)	12/2003	03/2008	10/2016	103
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे एफ/ओ स्पेशल पर्पस ब्लीकल (एसपीवी)	10/2002	03/2006	12/2016	129
2	मुंबई बीओटी आधार पर ऑफशोर कंटेनर बर्थ्स का निर्माण तथा कंटेनर टर्मिनल का विकास	01/2007	12/2010	12/2018	96
3	कोचीन पोर्ट ट्रस्ट में बल्लापाडम में आईसीटीटी से रेल कनेक्टिविटी	03/2007	04/2009	08/2016	88
इस्पात					
1	भिलाई इस्पात प्लांट का विस्तार	08/2010	03/2013	12/2016	45
2	45 एमवीए साफ के साथ अन्य एसोसिएटेड सुविधाओं का संग्रहण	12/2011	10/2013	09/2016	35
3	एनएमडीसी समेकित इस्पात संयंत्र	01/2010	05/2015	12/2017	31

4	एसएमएस-1 कन्वर्टर्स रिवैम्पिंग	05/2012	07/2015	09/2017	26
5	बागमती का सिंचाई कार्य	10/2005	03/2015	03/2017	24
दूरसंचार					
1	इंटेलिजेंट फाइबर ऑप्टिक सी के पैकेज एफ तथा जी भाग ख स्पेक्ट्रम (एनएफएस) ओएफसी लेयिंग प्रोजेक्ट के लिए नेटवर्क	09/2014	09/2014	03/2017	30
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	06/2011	01/2017	67
2	नागपुर महाराष्ट्र में राष्ट्रीय फायर कॉलेज का उन्नयन	06/2010	03/2012	03/2017	60
3	कालीकट केरल एनआईटी के लिए मेगा होस्टल	01/2010	10/2012	04/2017	54
4	संसदीय सौध संसद भवन परिसर में भवन के विस्तार हेतु निर्माण कार्य, नई दिल्ली	05/2009	05/2013	10/2016	41
5	इंफाल मणिपुर में एनआईटी अकादमी भवन	02/2014	03/2015	10/2017	31

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीयसलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल 2016 में, इस मंत्रालय की निगरानी पर चल रहे 1061 परियोजनाओं में से, 241 परियोजनाओं के संबंध में लागतवृद्धि तथा 326 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि अगस्त 2016 के दौरान, 1167 परियोजनाओं में से 273 परियोजनाओं के संबंध में लागतवृद्धि तथा 337 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है । अप्रैल, 2016 की तुलना में, लागतवृद्धि दर्शाने वाली परियोजनाओं की संख्या 22.71% से बढ़कर 23.39% हो गई, जबकि समयवृद्धि दर्शाने वाली परियोजनाओं के संबंध में 30.73% से घटकर 28.88% हो गई है ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय संबंधी मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित

रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-08-2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	अनुमानित लागत (रु. करोड़)	संचयी व्यय (रु. करोड़)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	309.46	435.10	01/2011	09/2017
2	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	318.00	305.59	05/2012	03/2015
3	विभिन्न हवाई अड्डों पर सं. 56 एयर फ़िल्ड फायर टैंडर की आपूर्ति	10/2012	217.60	244.10	30.74	03/2015	09/2015
4	वीएसआई एयरपोर्ट पर नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण, पोर्ट ब्लेयर	10/2013	314.61	314.61	26.30	09/2018	09/2018
कोयला							
1	बिथनोक लिग्नाइट खान परियोजना (2.25एमटीपीए)	03/2015	513.63	513.63	74.76	12/2019	12/2019
2	हल्दा लिग्नाइट खान परियोजना (1.90 एमटीपीए)	03/2015	522.45	522.45	2.57	09/2019	09/2019
उर्वरक							
1	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसी एफ ट्राम्बे	10/2014	197.79	209.44	75.85	11/2016	09/2017
स्वास्थ्य एवं परिवार कल्याण							
1	एलजीबीआरआईएमएच-तेजपुर, असम	07/2012	175.57	175.57	113.50	12/2014	03/2016
2	एलएचएमसी नई दिल्ली पुनर्विकास	02/2013	414.11	414.11	210.92	11/2013	11/2014
3	सफदरजंग हॉस्पिटल का पुनर्विकास और अन्य-सुपर स्पेशलिटी ब्लॉक	09/2013	444.70	444.70	400.00	12/2015	06/2016
4	एम्स-रायबरेली हाउसिंग	10/2013	159.50	159.50	127.80	11/2013	10/2016
5	सफदरजंग हॉस्पिटल, नई दिल्ली पुनः विकास और अन्य इमरजेंसी ब्लॉक	11/2013	196.70	196.70	197.38	01/2016	04/2016
भारी उद्योग							
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	2289.00	09/2011	12/2017

	खान						
1	मलंजखंड खान का विस्तार -भूमिगत खान के अंतर्गत सीएपीएसी के मौजूद ओपन कास्ट खान का विकास	09/2011	1856.00	1176.00	15.48	09/2017	04/2020
2	देवीकोट में 50 मेगावाट पवन विद्युत परियोजना का कार्यान्वयन	12/2015	344.50	344.50	201.17	11/2016	11/2016
पेट्रोलियम							
1	हल्दिया में एलपीजी आयात टर्मिनल, पश्चिम बंगाल	01/1991	694.00	694.00	57.19	10/2018	10/2018
2	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	1158.24	10/2011	04/2016
3	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1493.81	01/2012	09/2016
4	एन्नोर में नई विपणन टर्मिनल	11/2006	171.83	171.83	0.00	एन.ए.	एन.ए.
5	12 ऑफशोर सप्लाई वेजेल्स (ओएसवी) का निर्माण	06/2007	736.65	736.65	517.01	09/2011	03/2017
विद्युत							
1	पूर्वी क्षेत्र सुदृढीकरण स्कीम-XV	01/1991	454.11	454.11	0.00	04/2018	04/2018
2	सुबनसिरी लोअर एच.ई.पी (8x250 मेवा) (एनएचपीसी)	09/2003	6285.33	17435.15	8637.42	09/2010	एन.ए.
3	उत्तर में फाइबर ऑप्टिक संचार की स्थापना	03/2012	198.63	198.63	112.53	09/2014	10/2016
4	श्रीनगर एलईएच पारेषण परियोजना	01/2014	1788.41	1788.41	0.00	09/2017	09/2017
5	एकीकृत वास्तविक समय गतिशील राज्य माप चरण-I	01/2014	374.63	374.63	29.70	04/2016	03/2017
रेलवे							
1	हावड़ा अमटा चम्पादंगा एनएल, एसईआर	04/1974	393.46	1026.00	181.89	03/2007	एन.ए.
2	नांगलडम-तलवाड़ा (एनएल), एन.आर.	03/1981	450.00	2100.00	502.85	07/2012	एन.ए.
3	एकलाखी-बलूरघाट सहित जी से नई बीजी रेलवे लाइन	04/1983	36.80	1336.57	259.58	एन.ए.	03/2019
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	749.69	0.00	06/2005	12/2019
5	गुना-इटावा वाया शिवपुरी-ग्वालियर -भिंड एनएल, (एनसीआर)	04/1986	158.77	634.48	631.43	03/1994	02/2016
सड़क परिवहन एवं राजमार्ग							
1	जामगुरी से विश्वनाथ छरियाली तक चार लेनिंग, एनएच-52 के 182 किमी. से 208 किमी. तक	01/1991	520.01	520.01	0.00	एन.ए.	एन.ए.

2	एनएच-31 के बख्तियार-मोकामा सेक्शन के चार लेनिंग	01/1991	1167.45	1167.45	0.00	एन.ए.	एन.ए.
3	भोजपुर से बक्सर तक चार लेनिंग	01/1991	642.41	642.41	0.00	एन.ए.	एन.ए.
4	होस्पेट चित्रदुर्गा के चार लेनिंग	01/1991	1388.00	1388.00	175.79	एन.ए.	08/2018
5	पेल्ड शोल्डर के विन्यास के साथ दो लेनों-दो लेन के लिए पुनर्वास तथा उन्नयन	01/1991	478.35	478.35	0.00	एन.ए.	एन.ए.
पोत परिवहन एवं पत्तन							
1	एन्नौर मनाली एक्सप्रेस वे, एफ/ओस्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	525.49	03/2006	12/2016
2	सेतुसमुंद्रम शिप चैनल प्रोजेक्ट	06/2005	2427.40	2427.40	831.21	10/2008	एन.ए.
3	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	415.01	12/2010	12/2018
4	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटी के लिए रेल कनक्टिविटी	03/2007	245.67	409.83	350.68	04/2009	08/2016
5	कामराजर पोर्ट लिमिटेड पर रोरा सह जीसीबी-II विकास	09/2015	210.00	210.00	0.00	01/2018	01/2018
इस्पात							
1	गुलबर्गा में मेडिकल कॉलेज एवं अस्पताल	05/2005	768.88	1070.97	1070.97	02/2014	03/2016
2	बागमती का सिंचाई कार्य	10/2005	956.00	956.00	650.45	03/2015	03/2017
3	पीएमजीएसवाई चरण V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	175.94	178.91	12/2015	03/2017
4	पीएमजीएसवाई चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	200.20	12/2016	12/2016
5	गिरीडीह, कोडरमा, हजारीबाग, रामगढ़ तथा छतरा जिला में रोड एवं पुल का निर्माण	12/2007	200.00	200.00	136.65	03/2018	03/2018
दूरसंचार							
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	13334.00	13334.00	0.00	07/2015	एन.ए.
शहरी विकास							
1	मूसी जोन के दक्षिण पर पुरानी शहरी क्षेत्र में सेवरेज प्रणाली के पुनर्वास तथा सुदृढीकरण	08/2007	246.90	246.90	0.00	एन.ए.	एन.ए.
2	संसद भवन सौध परिसर में भवन के विस्तार हेतु निर्माण कार्य, नई दिल्ली	05/2009	261.85	261.85	208.53	05/2013	10/2016
3	एनआईटी कालीकट केरल के लिए मेगा होस्टल II का निर्माण	01/2010	165.23	165.23	36.54	10/2012	04/2017
4	नागपुर, महाराष्ट्र में राष्ट्रीय फायर सर्विसेज कॉलेज का उन्नयन	06/2010	205.00	191.97	133.13	03/2012	03/2017
5	प्लॉट सं. सी-41-43 पर आयकर विभाग के लिए कार्यालय भवन, बांद्रा	02/2011	241.33	349.33	123.13	11/2014	एन.ए.

एन.ए.:उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यतथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीयसलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं । बिना संशोधित लागत अनुमानों वाली शुरुआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-08-2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़)	संशोधित लागत (रु. करोड़)	संचयी व्यय (रु. करोड़)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	10/2013	05/2016
नागर विमानन					
1	नई राष्ट्रीय टर्मिनल बिल्डिंग (गोवा) का निर्माण	05/2010	05/2012	एन.ए.	03/2015
2	विभिन्न हवाई अड्डों पर सं. 56 एयर फील्ड फायर टैंडर की आपूर्ति	10/2012	03/2015	एन.ए.	09/2015
कोयला					
1	जल्लाराम शाफ्ट परियोजना	09/2007	03/2013	एन.ए.	एन.ए.
2	अद्वियाला शाफ्ट परियोजना	12/2009	03/2013	एन.ए.	03/2016
स्वास्थ्य एवं परिवार कल्याण					
1	एलजीबीआरआईएमएच-तेजपुर, असम	07/2012	12/2014	एन.ए.	03/2016
2	एलएचएमसी नई दिल्ली पुनर्विकास	02/2013	11/2013	एन.ए.	11/2014
3	सफदरजंग हॉस्पिटल का पुनर्विकास और अन्य-सुपर स्पेशलिटी ब्लॉक	09/2013	12/2015	एन.ए.	06/2016
4	सफदरजंग अस्पताल, नई दिल्ली पुनर्विकास तथा अन्य आपातकालीन ब्लॉक	11/2013	01/2016	एन.ए.	04/2016
पेट्रोलसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2015	एन.ए.
पेट्रोलियम					
1	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	एन.ए.	04/2016
2	एन्नोर में नई विपणन टर्मिनल	11/2006	एन.ए.	एन.ए.	एन.ए.

3	एक ईटीपी और तीन ईटीपी सह जल इंजेक्शन प्लांट (डब्ल्यूआईपी)	06/2010	01/2014	एन.ए.	एन.ए.
4	गुजरात रिफाइनरी में ईटीपी के रिवर्स ऑस्मोसिस प्लांट	12/2011	02/2016	07/2016	07/2016
5	एलपीजी मार्केटिंग टर्मिनल, पारादीप	09/2012	03/2015	एन.ए.	एन.ए.
विद्युत					
1	सुबनसिरी लोअर एचईपी (8X250 मेवा) (एनएचपीसी)	09/2003	09/2010	एन.ए.	एन.ए.
2	पार्वती एचईपी से जुड़े पारेषण प्रणाली (एनएचपीसी)	12/2005	12/2008	09/2010	एन.ए.
3	रघुनाथपुर थर्मल विद्युत स्टेशन चरण-I	04/2007	02/2011	एन.ए.	03/2016
4	किशनगंगा एचईपी (3X110 मेवा.)	01/2009	01/2016	एन.ए.	एन.ए.
5	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	07/2013	एन.ए.	एन.ए.
रेलवे					
1	हावड़ा-अमटा-चंपादंगा एनएल (एसईआर)	04/1974	03/2007	03/2007	एन.ए.
2	नंगलडम-तलवारा (एनएल) एनआर	03/1981	07/2012	एन.ए.	एन.ए.
3	गुना-इटावा वाया शिवपुरी ग्वालियर ग्रिड, एनएल (एनसीआर)	04/1986	03/1994	02/2016	02/2016
4	नमखाना-चन्द्रनगर, काकद्वीप-बुदखली तथा चन्द्रनाग के बाद लक्ष्मीकांतपुर-नमखाना एमएम के साथ	04/1987	एन.ए.	एन.ए.	एन.ए.
5	मुजफ्फरनगर सीतामढ़ी नई लाइन	01/1991	07/2014	एन.ए.	एन.ए.
सड़क परिवहन एवं राजमार्ग					
1	लालसोत-करोली के पेव्ड सोल्डर विन्यास के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन	01/1991	05/2016	एन.ए.	05/2016
2	जमुगिरी से विश्वनाथ चरौली के चार लेनिंग, एनएच-52 के 182 किमी. से 208 किमी	01/1991	एन.ए.	एन.ए.	एन.ए.
3	एनएच-104 के पेव्ड सोल्डर (40 किमी. से 219.945 किमी.) के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन	01/1991	एन.ए.	एन.ए.	एन.ए.
4	सीतामढ़ी के पेव्ड सोल्डर विन्यास के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन 40 किमी.	01/1991	एन.ए.	एन.ए.	एन.ए.
5	पेव्ड सोल्डर विन्यास के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन	01/1991	एन.ए.	एन.ए.	एन.ए.
पोत एवं पत्तन					
1	सेतसमुन्द्रम शिप चैनल परियोजना	06/2005	10/2008	एन.ए.	एन.ए.
इस्पात					
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल का निर्माण	05/2005	02/2014	एन.ए.	03/2016

2	पीएमजीएसवाई झारखंड के अंतर्गत पांच वर्षीय रख-रखाव के साथ ग्रामीण सड़कों के निर्माण	12/2007	06/2016	एन.ए.	06/2016
3	गुलबर्गा में पारा मेडिकल और एलिड स्वास्थ्य इंस्टीट्यूट का निर्माण	07/2011	12/2015	एन.ए.	04/2016
4	डिफर में 24 सं. नई औद्योगिक प्रशिक्षण संस्थानों (आईटीआई) के लिए कार्यशालाओं और भवनों का निर्माण	08/2012	03/2016	एन.ए.	03/2016
5	इनडोर खेल हॉल के लिए तेलंगाना में 123 ब्लॉकों तथा आंध्र प्रदेश में 167 ब्लॉकों का निर्माण, पंजाब	07/2014	01/1999	एन.ए.	एन.ए.
दूरसंचार					
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	एन.ए.	एन.ए.
शहरी विकास					
1	मूसी जोन 2 के दक्षिण पर पुरानी शहरी क्षेत्र में सेवरेज प्रणाली के पुनर्वास तथा सुदृढीकरण	08/2007	एन.ए.	एन.ए.	एन.ए.
2	प्लॉट सं. सी-41-43 पर आयकर विभाग के लिए कार्यालय भवन, बांद्रा	02/2011	11/2014	07/2016	एन.ए.
3	संसद भवन सौध परिसर में भवन के विस्तार हेतु निर्माण कार्य, नई दिल्ली	07/2012	08/2014	एन.ए.	एन.ए.
4	मुम्बई मेट्रो लाइन 3 (कोलाबा-बांद्रा-सीपज)	07/2013	01/2015	एन.ए.	12/2015
5	रोपर में आईआईटी रोपर के लिए चरण-I के अंतर्गत विभिन्न बिल्डिंग का निर्माण	02/2014	01/2015	एन.ए.	एन.ए.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीयसलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-08-2016 की स्थिति के अनुसार)

क्र.सं.	सेक्टर/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	10/2013	05/2016
नागर विमानन					

1	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	एन.ए.	03/2015
2	विभिन्न हवाई अड्डों पर 56 एनओएस एयरफील्ड फायर टैंडर की सप्लाई	10/2012	03/2015	एन.ए.	09/2015
कोयला					
1	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.ए.	एन.ए.
2	अदरियाला शॉफ्ट परियोजना	12/2009	03/2013	एन.ए.	03/2016
स्वास्थ्य एवं परिवार कल्याण					
1	एलजीबीआरआईएमएच-तेजपुर, असम	07/2012	12/2014	एन.ए.	03/2016
2	एलएचएमसी नई दिल्ली पुनः-विकास	02/2013	11/2013	एन.ए.	11/2014
3	सफदरजंग हॉस्पिटल का पुनर्विकास और अन्य-सुपर स्पेशलिटी ब्लॉक	09/2013	12/2015	एन.ए.	06/2016
4	सफदरजंग अस्पताल, नई दिल्ली-पुनर्विकास अन्य -इमरजेंसी ब्लॉक	11/2013	01/2016	एन.ए.	04/2016
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2015	एन.ए.
पेट्रोलियम					
1	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	एन.ए.	04/2016
2	एन्नोर में नई मार्केटिंग टर्मिनल	11/2006	एन.ए.	एन.ए.	एन.ए.
3	एक ईटीपी और तीन ईटीपी सह वाटर इंजेक्शन संयंत्रों का निर्माण (डब्ल्यूआईपी)	06/2010	01/2014	एन.ए.	एन.ए.
4	गुजरात रिफाइनरी में ईटीपी के लिए रिवर्स ऑस्मोसिस प्लांट	12/2011	02/2016	07/2016	07/2016
5	एलपीजी मार्केटिंग टर्मिनल पारादीप	09/2012	03/2015	एन.ए.	एन.ए.
विद्युत					
1	सुबनसिरी लोअर एचईपी (8X250 मेवा) (एनएचपीसी)	09/2003	09/2010	एन.ए.	एन.ए.
2	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी)	12/2005	12/2008	09/2010	एन.ए.
3	रघुनाथपुर थर्मल विद्युत स्टेशन चरण-I	04/2007	02/2011	एन.ए.	03/2016
4	किशनगंगा एचईपी (3X110 मेवा.)	01/2009	01/2016	एन.ए.	एन.ए.
5	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	07/2013	एन.ए.	एन.ए.
रेलवे					
1	हावड़ा अमटा चंपादंगा एनएल	04/1974	03/2007	03/2007	एन.ए.
2	नांगलडैम-तालवारा (एनएल) एनआर	03/1981	07/2012	एन.ए.	एन.ए.

3	गुना-इटावा वाया शिवपुरी-ग्वालियर-भिंड एनएल, एनसीआर	04/1986	03/1994	02/2016	02/2016
4	नामखाना-चंद्रनगर, काकद्वीप-बुदाखलीऔर चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना के बाद एमएम	04/1987	एन.ए.	एन.ए.	एन.ए.
5	मुजफ्फरपुर-सीतामढ़ी नई लाइन	01/1991	07/2014	एन.ए.	एन.ए.
सड़क परिवहन एवं राजमार्ग					
1	लालसोत-करौली के पेव्ड सोल्डर विन्यास के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन	01/1991	05/2016	एन.ए.	05/2016
2	जमुगिरी से विश्वनाथ चरैली के चार लेनिंग, एनएच-52 के 182 किमी. से 208 किमी	01/1991	एन.ए.	एन.ए.	एन.ए.
3	एनएच-104 के पेव्ड सोल्डर (40 किमी. से 219.945 किमी.) के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन	01/1991	एन.ए.	एन.ए.	एन.ए.
4	सीतामढ़ी के पेव्ड सोल्डर विन्यास के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन 40 किमी.	01/1991	एन.ए.	एन.ए.	एन.ए.
5	पेव्ड सोल्डर विन्यास के साथ दो लेनों-दो लेन के पुनर्वास तथा उन्नयन	01/1991	एन.ए.	एन.ए.	एन.ए.
पोत परिवहन एवं पत्तन					
1	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	एन.ए.	एन.ए.
इस्पात					
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल का निर्माण	05/2005	02/2014	एन.ए.	03/2016
2	पीएमजीएसवाई झारखंड के अंतर्गत पांच वर्षीय रख-रखाव के साथ ग्रामीण सड़कों के निर्माण	12/2007	06/2016	एन.ए.	06/2016
3	गुलबर्गा में पारा मेडिकल और एलिड स्वास्थ्य इंस्टीट्यूट का निर्माण	07/2011	12/2015	एन.ए.	04/2016
4	डिफर में 24 सं. नई औद्योगिक प्रशिक्षण संस्थानों (आईटीआई) के लिए कार्यशालाओं और भवनों का निर्माण	08/2012	03/2016	एन.ए.	03/2016
5	राजीव गांधी के अंतर्गत इनडोर खेल हॉल के लिए तेलंगाना में 123 ब्लोको तथा आंध्र प्रदेश में 167 ब्लोको का निर्माण	07/2014	01/1999	एन.ए.	एन.ए.
दूरसंचार					
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	एन.ए.	एन.ए.

शहरी विकास					
1	जोन 2 में मूसी के दक्षिण हेतु पुराने शहर क्षेत्र में सीवरेज प्रणाली का पुनर्वास तथा सुदृढीकरण	08/2007	एन.ए.	एन.ए.	एन.ए.
2	प्लॉट सं. सी-41-43 पर आयकर विभाग के लिए कार्यालय भवन, बांद्रा	02/2011	11/2014	07/2016	एन.ए.
3	प्रगति मैदान से सटी हुई भूमि पर सर्वोच्च न्यायालय के अतिरिक्त ओडी का निर्माण	07/2012	08/2014	एन.ए.	एन.ए.
4	मुंबई मेट्रो लाइन 3 (कोलाबा-बांद्रा सीपज)	07/2013	01/2015	एन.ए.	12/2015
5	रोपर में आईआईटी लिए चरण-I के अंतर्गत विभिन्न भवनों का निर्माण, पंजाब	02/2014	01/2015	एन.ए.	एन.ए.

एनए: उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीयसलाहकार कार्य शुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

- i) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 425 परियोजनाओं में से, 111 परियोजनाएं विलंबित हैं । माह के दौरान 11 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	फोरबसगंज से सिमाही (एनएच 57) (एनएचएआई) एनएचएआई	1	एनआर
2	बड़ोदरा-सूरत सेक्शन एनएचएआई	1	एनआर
3	गोरखपुर-गोपालगंज के फोर लेनिंग के शेष कार्य एनएचएआई	1	एनआर
4	सिमाई ख्याली गांधीधाम एनएचएआई पीपीपी (बीओटी)	2	एनआर
5	मोकामा-मुंगेर के दो लेनिंग एनएचएआई, पीपीपी (एन्यूटी)	3	एनआर
6	निंबी जोधा-डेगाना-मेड़ता सिटी सेक्शन के पी एस साथ 2 लेन का सुदृढीकरण तथा	3	एनआर

	चौड़ीकरण एनएचएआई		
7	चेंगापल्ली से कोयम्बटूर बाइपास 102.035 किमी.-144.740 किमी. एनएचएआई, पीपीपी (बीओटी)	4	एनआर
8	पटना-बख्तियारपुर 181.3 किमी. से 231.95 किमी. एनएचएआई पीपीपी (बीओटी)	7	एनआर
9	राजसमंद-गंगापुर-भीलवाड़ा के 4लेनिंग एनएचएआई, पीपीपी (बीओटी)	7	एनआर
10	कुडप्पा-मईदुकर-कुर्नूल 167.750 किमी.-356.502 किमी. एनएचएआई पीपीपी (बीओटी)	10	एनआर
11	चंडीगढ़- खरार की चार लेनिंग, एनएचएआई	12	एनआर

एनआर: परियोजना क्रियान्वयनकर्ता एजेंसी द्वारा परियोजना में विलंब के मामले में कोई विशेष कारण सूचित नहीं किया गया है ।

- ii) **विद्युत क्षेत्र में**, 117 परियोजनाओं में से, 61 परियोजनाएं विलंबित है । माह के दौरान 7 परियोजनाओं के संबंध में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	एनआर / डब्ल्यू आर भाग-क के लिए सिक्किम में जेनरेशन परियोजना के लिए विद्युत का हस्तांतरण के लिए पारेषण प्रणाली पीजीसीआईएल	1	भूमि अधिग्रहण
2	उत्तर क्षेत्रीय सुदृढीकरण योजना -XXIV	1	उत्तराखंड में आरओडब्ल्यू समस्या, जम्मू व कश्मीर में अशांति
3	पारे जल विद्युत परियोजना, नीपको	2	अप्रोच रोड के कटाव के कारण बांध स्थल प्रतिबंधित
4	पूर्वी क्षेत्र प्रणाली सुदृढीकरण - XIV पीजीसीआईएल	3	भूमि अधिग्रहण

5	दक्षिणी क्षेत्र में स्टैटिक वीएआर कॉम्पैसेटर्स (एसवीसीएस) पीजीसीआईएल	3	एन.आर.
6	कामेंग जल विद्युत परियोजना (नीपको)नीपको	4	संविदात्मक मुद्दे
7	तुरीअल जल विद्युत परियोजना (60 मेवा) नीपको	6	भाग बजार से नाताचेरा तक अप्रोच सड़क की स्थिति खराब है, वर्षा तथा फिसलनी सड़क हालत

एनआर: परियोजना क्रियान्वयनकर्ता एजेंसी द्वारा परियोजना में विलंब के मामले में कोई विशेष कारण सूचित नहीं किया गया है।

- iii) **कोयला क्षेत्र में**, 88 परियोजनाओं में से, 40 परियोजना विलंबित है। माह के दौरान, 4 परियोजना के संदर्भ में 2-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	विंड पावर परियोजना, काजहुनीरकुलम, तमिलनाडु एनएलसी	2	भूमि अधिग्रहण तथा सिविल कार्य
2	पूर्णडीह ओसीपी (3.0 एमटीवाई) सीसीएल	12	भूमि अधिग्रहण
3	चूरी बेंटी यूजी (0.81 एमटीवाई) सीसीएल	24	वन भूमि में परिवर्तन
4	रजरप्पा आरसीई ओसीपी (3.0 एमटीवाई) सीसीएल	24	भूमि अधिग्रहण और वन संबंधी अनुमति

- iv) **इस्पात क्षेत्र में**, 34 परियोजनाओं में से, 14 परियोजना विलंबित है। माह के दौरान, 4 परियोजनाओं में 1-3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	अन्य संबद्ध सुविधाओं के साथ 45 एसएएफ टी की स्थापना, सेल	2	पर्यावरण संबंधी अनुमति तथा ठेकेदार द्वारा कम संसाधन की तैनाती

2	आरएसपी सेल में ब्लास्ट फर्नेस-1 का उन्नयन	1	ठेकेदार द्वारा उपस्करों की आपूर्ति में विलंब
3	बीएसएल सेल में सीओबी-7 का पुनर्निर्माण	3	ठेकेदार द्वारा धीमी प्रगति
4	सिंटर मशीन 1 और 2 की रिवैम्पिंग, आरआईएनएल	3	ठेकेदार द्वारा खरीद तथा निर्माण में धीमी प्रगति

- v) **शहरी विकास क्षेत्र में**, 29 परियोजनाओं में से 17 परियोजनाएं विलंबित हैं। माह के दौरान 2 परियोजनाओं के संबंध में 1-2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	संसद सौध संसद भवन में भवन के विस्तार हेतु निर्माण कार्य, नई दिल्ली	1	निधियों की अनुपलब्धता
2	बेंगलुरु मेट्रो रेल परियोजना एमआरटीपी	2	घनी आबादी क्षेत्र इस वजह से संरचना को नुकसान से बचाने के लिए धीमी प्रगति

- vi) **पोत परिवहन एवं पत्तन क्षेत्र में**, 8 परियोजनाओं में से, 3 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजनाओं के संबंध में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी) पोर्ट ट्रस्ट पब्लिक प्राइवेट (एसपीवी)	5	अतिक्रमण

- vii) **पेट्रोलियम क्षेत्र में**, 80 परियोजनाओं में से, 38 परियोजनाएं विलंबित हैं। माह के दौरान 1 परियोजनाओं के संबंध में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

क्र.सं.	परियोजना का नाम	अतिरिक्त विलंब	अतिरिक्त विलंब के कारण
1	रेसिड उन्नयन परियोजना सीपीसीएल	3	रेडियोग्राफी गतिविधियों के लिए प्रतिबंधित समय

12. रेल मंत्रालय ने मंत्रालय के ओसीएमएस पर 500 करोड़ रु. और उससे अधिक लागत वाली चालू परियोजनाओं के संबंध में अद्यतन सूचना प्रदान की है। शेष परियोजनाओं के मामले में आंकड़ा 01.01.2015 से संबंधित है।

13. दिनांक 31.08.2016 की स्थिति के अनुसार, विभिन्न क्षेत्रों में रु. 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

14. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for August 2016 contains information on the status of the 1167 Central Sector Infrastructure Projects costing ₹150 crore and above. During August 2016, 4 projects (2 in Road & Transport and 1 project each is in Power and Railways Sector) have reported completion.

2. During the reference month, out of 1167 projects, 337 projects are delayed with respect to their original schedules and 32 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 32 projects, 7 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	425	111	11	1
2	RAILWAYS	360	41	2	0
3	POWER	117	61	7	4
4	COAL	88	40	4	0
5	PETROLEUM	80	38	1	1
6	STEEL	34	14	4	0
7	URBAN DEVELOPMENT	29	17	2	1
8	HEALTH AND FAMILY WELFARE	9	4	0	0
9	SHIPPING AND PORTS	8	3	1	0
10	ATOMIC ENERGY	4	3	0	0
11	CIVIL AVIATION	4	1	0	0
12	MINES	3	1	0	0
13	FERTILISERS	2	1	0	0
14	TELECOMMUNICATIONS	2	1	0	0
15	PETROCHEMICALS	1	0	0	0
16	HEAVY INDUSTRY	1	1	0	0
Total		1167	337	32	7

3. Total original cost of implementation of the 1167 projects was ₹14,33,476.53 crore and their anticipated completion cost is likely to be ₹16,10,504.54 crore, which reflects overall cost overruns of ₹1,77,028.01 crore (12.35% of original cost). The expenditure incurred on these projects till August 2016 is ₹6,30,581.41 crore, which is 39.15% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-08-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
2	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.59	201.51
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
4	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	16.86
5	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	82.49
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
3	BULK PETROLEUM OIL AND LUBRICANT (POL) DEPOT AT IMPHAL, MANIPUR	08/2010	103.02	171.04	66.03
4	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
5	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	462.79	49.38
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1441.52	290.95
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	177.39
3	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1581.04	175.45
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
5	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.57	139.32

RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
2	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	5050.00	1939.09
3	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	9658.00	1227.45
4	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
5	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
2	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
5	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	156.63	276.00	76.21
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	66.82
4	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	235.15	18.20
5	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	5.66
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	39.29
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	17.79
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	17.50
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	14405.01	125.25

2	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	44.75
3	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	5298.00	24.25

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 31-08-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
2	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.59	307.16
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
4	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	70.65
5	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	4504.39
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
2	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	495.00
4	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	394.93
5	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	871.35	1200.00	328.65
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	11149.82
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	5484.82
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.75	4479.16

5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	3683.06
RAILWAYS					
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	9658.00	8930.44
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	7000.00	5323.69
4	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	5050.00	4802.34
5	BHAIRABI SAIRONG, NL, NEFR	04/2008	619.34	4600.00	3980.66
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
2	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
4	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	164.16
4	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED	10/2013	198.94	235.15	36.21
5	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	13.83
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	302.09
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	31.22
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	26.21
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	14405.01	8010.01
2	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	5298.00	1034.00
3	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	108.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1167 projects, 282 are on schedule, 337 are delayed, 273 projects reported cost overrun and 85 projects reported both time and cost overrun with respect to their original project

implementation schedules. However, the number of delayed projects decreases to 283 if delay is calculated on the basis of latest schedule of completion. Further, 81 projects have been sanctioned without original commissioning date and for 460 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 337 delayed projects, 68 projects have overall delay in the range of 1 to 12 months, 54 projects have delay in the range of 13 to 24 months, 138 projects have delay in the range of 25 to 60 months and 77 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 31-08-2016)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2017	85
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2019	36
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11/2018	35
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
COAL					
1	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2019	108
3	MAGADH OC 20 MTY (CCL)	08/2008	07/2012	03/2021	104
4	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
5	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2018	84
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	09/2017	10
HEALTH AND FAMILY WELFARE					
1	AIIMS-RAEBARELI-HOUSING	10/2013	11/2013	10/2016	35
2	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	07/2017	2
3	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	06/2017	1
4	AIIMS - OPD(NEW)	08/2014	05/2017	06/2017	1
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	09/2011	12/2017	75
MINES					
1	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	09/2011	09/2017	04/2020	31
PETROLEUM					
1	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	03/2017	66
3	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	10/2016	64

4	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	09/2016	56
5	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	04/2010	06/2012	08/2016	50
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	09/2017	134
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2017	109
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	10/2017	94
5	BARH STPP(3X660 MW) NTPC	02/2005	01/2011	05/2018	88
RAILWAYS					
1	GONDIA-JABALPUR(GC), (SECR)	02/1997	03/1998	12/2019	261
2	JAGGAYYAPET - MELLACHERUVU	04/2007	01/1999	06/2017	221
3	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2021	216
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	03/1995	11/2002	12/2018	193
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	05/2008	03/2023	178
ROAD TRANSPORT AND HIGHWAYS					
1	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2016	138
2	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	12/2003	09/2007	03/2017	114
3	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	09/2016	108
4	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2016	104
5	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	10/2016	103
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	12/2016	129
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	12/2018	96
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	08/2016	88
STEEL					
1	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	12/2016	45
2	INSTALLATION OF 45 MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	09/2016	35
3	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	12/2017	31
4	SMS-1 CONVERTERS REVAMPING	05/2012	07/2015	09/2017	26
5	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2017	24
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	09/2014	09/2014	03/2017	30
URBAN DEVELOPMENT					
	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	01/2017	67
1	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARAstra	06/2010	03/2012	03/2017	60
2	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	04/2017	54
3	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	10/2016	41

4	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2017	31
---	---	---------	---------	---------	----

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2016, out of 1061 projects on the monitor of this Ministry, 241 projects reported cost overruns and 326 projects reported time overruns; while during August 2016, out of 1167 projects, 273 projects reported cost overruns and 337 projects reported time overruns. In comparison to April 2016, number of projects reporting cost overrun has increased from 22.71% to 23.39% whereas projects reporting time overruns have decreased from 30.73% to 28.88%.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-08-2016)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	309.46	435.10	01/2011	09/2017
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	318.00	305.59	05/2012	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	30.74	03/2015	09/2015
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	314.61	26.30	09/2018	09/2018
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	74.76	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	2.57	09/2019	09/2019

	FERTILISERS						
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	75.85	11/2016	09/2017
	HEALTH AND FAMILY WELFARE						
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	03/2016
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	414.11	210.92	11/2013	11/2014
3	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	444.70	444.70	400.00	12/2015	06/2016
4	AIIMS-RAEBARELI-HOUSING	10/2013	159.50	159.50	127.80	11/2013	10/2016
5	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	196.70	197.38	01/2016	04/2016
	HEAVY INDUSTRY						
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2289.00	09/2011	12/2017
	MINES						
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	09/2011	1856.00	1176.00	15.48	09/2017	04/2020
2	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT	12/2015	344.50	344.50	201.17	11/2016	11/2016
	PETROLEUM						
1	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL	01/1991	694.00	694.00	57.19	10/2018	10/2018
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	1158.24	10/2011	04/2016
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1493.81	01/2012	09/2016
4	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	171.83	0.00	N.A.	N.A.
5	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	517.01	09/2011	03/2017
	POWER						
1	EASTERN REGION STRENGTHENING SCHEME-XV	01/1991	454.11	454.11	0.00	04/2018	04/2018
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	17435.15	8637.42	09/2010	N.A.
3	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	03/2012	198.63	198.63	112.53	09/2014	10/2016
4	SRINAGAR-LEH TRANSMISSION PROJECT	01/2014	1788.41	1788.41	0.00	09/2017	09/2017

5	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	29.70	04/2016	03/2017
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	181.89	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	502.85	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	259.58	N.A.	03/2019
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	749.69	0.00	06/2005	12/2019
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	634.48	631.43	03/1994	02/2016
ROAD TRANSPORT AND HIGHWAYS							
1	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	520.01	520.01	0.00	N.A.	N.A.
2	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	01/1991	1167.45	1167.45	0.00	N.A.	N.A.
3	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	0.00	N.A.	N.A.
4	FOUR LANING OF HOSPET - CHITRADURGA	01/1991	1388.00	1388.00	175.79	N.A.	08/2018
5	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	525.49	03/2006	12/2016
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	415.01	12/2010	12/2018
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	350.68	04/2009	08/2016
5	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED	09/2015	210.00	210.00	0.00	01/2018	01/2018
STEEL							
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1070.97	02/2014	03/2016

2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	650.45	03/2015	03/2017
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.91	12/2015	03/2017
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	200.20	12/2016	12/2016
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	200.00	200.00	136.65	03/2018	03/2018
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	13334.00	0.00	07/2015	N.A.
URBAN DEVELOPMENT							
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE	08/2007	246.90	246.90	0.00	N.A.	N.A.
2	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	261.85	261.85	208.53	05/2013	10/2016
3	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	165.23	165.23	36.54	10/2012	04/2017
4	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	205.00	191.97	133.13	03/2012	03/2017
5	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	123.13	11/2014	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-08-2016)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	10/2013	05/2016
CIVIL AVIATION					

1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	N.A.	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015
COAL					
1	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
2	ADRIYALA SHAFT PROJECT	12/2009	03/2013	N.A.	03/2016
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2016
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
3	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	12/2015	N.A.	06/2016
4	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT AND OTHERS-EMERGENCY BLOCK	11/2013	01/2016	N.A.	04/2016
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2015	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	N.A.	04/2016
2	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY	12/2011	02/2016	07/2016	07/2016
5	LPG MARKETING TERMINAL, PARADIP	09/2012	03/2015	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP	12/2005	12/2008	09/2010	N.A.
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	02/2011	N.A.	03/2016
4	KISHANGANGA HEP (3X110 MW)	01/2009	01/2016	N.A.	N.A.
5	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	02/2016	02/2016
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI	01/1991	05/2016	N.A.	05/2016
2	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	N.A.	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	N.A.	N.A.	N.A.

4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40	01/1991	N.A.	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	N.A.	N.A.	N.A.
SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	03/2016
2	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	06/2016
3	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	07/2011	12/2015	N.A.	04/2016
4	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER	08/2012	03/2016	N.A.	03/2016
5	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA	07/2014	01/1999	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	N.A.	N.A.
URBAN DEVELOPMENT					
1	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
2	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	11/2014	07/2016	N.A.
3	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	N.A.	N.A.
4	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	N.A.	12/2015
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	01/2015	N.A.	N.A.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31-08-2016)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	10/2013	05/2016
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	N.A.	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015

	COAL				
1	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
2	ADRIYALA SHAFT PROJECT	12/2009	03/2013	N.A.	03/2016
	HEALTH AND FAMILY WELFARE				
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2016
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
3	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	12/2015	N.A.	06/2016
4	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT AND OTHERS-EMERGENCY BLOCK	11/2013	01/2016	N.A.	04/2016
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2015	N.A.
	PETROLEUM				
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	N.A.	04/2016
2	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY	12/2011	02/2016	07/2016	07/2016
5	LPG MARKETING TERMINAL, PARADIP	09/2012	03/2015	N.A.	N.A.
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP	12/2005	12/2008	09/2010	N.A.
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	02/2011	N.A.	03/2016
4	KISHANGANGA HEP (3X110 MW)	01/2009	01/2016	N.A.	N.A.
5	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
	RAILWAYS				
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	02/2016	02/2016
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
	ROAD TRANSPORT AND HIGHWAYS				
1	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	01/1991	05/2016	N.A.	05/2016
2	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	N.A.	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	N.A.	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	01/1991	N.A.	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	N.A.	N.A.	N.A.

SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	03/2016
2	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	06/2016
3	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	07/2011	12/2015	N.A.	04/2016
4	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER	08/2012	03/2016	N.A.	03/2016
5	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA	07/2014	01/1999	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	07/2015	N.A.	N.A.
URBAN DEVELOPMENT					
1	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
2	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	11/2014	07/2016	N.A.
3	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	N.A.	N.A.
4	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	N.A.	12/2015
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	01/2015	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

i) Road Transport & Highways Sector,

Out of 425 projects, 111 projects are delayed. During the month, the following 11 projects have reported additional delay in the range of 1-12 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	1	NR
2	VADODARA-SURAT SECTION	1	NR
3	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	1	NR

4	SAMAIKHALI-GANDHIDHAM NHAI PPP (BOT)	2	NR
5	2 LANNING OF MOKAMA-MUNGER NHAI PPP (ANNUITY)	3	NR
6	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION NHAI	3	NR
7	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035- 144.740 KM NHAI PPP (BOT)	4	NR
8	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 NHAI PPP (BOT)	7	NR
9	4-LANING OF RAJSAMAND-GANGAPUR-BHILWARA NHAI PPP (BOT)	7	NR
10	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM NHAI PPP (BOT)	10	NR
11	FOUR LANING OF CHADIGARH - KHARAR NHAI	12	NR

NR: No specific reason has been reported by the project implementing agency for the delay.

ii) Power Sector

Out of 117 projects, 61 projects are delayed. During the month, 7 projects have reported additional delay in the range of 1- 6 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	1	Land acquisition
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	1	RoW problem in Uttarakhand, disturbance in J& K
3	PARE HYDRO ELECTRIC PROJECT NEEPCO	2	Access to dam site is restricted due to erosion of approach road.
4	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	3	Land acquisition
5	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION PGCIL	3	NR
6	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	4	Contractual issue
7	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) NEEPCO	6	Poor approach road condition from Bhagabazar to Natachera, Rain and slippery road condition.

NR: No specific reason has been reported by the project implementing agency for the delay.

- (iii) In the **Coal Sector**, out of 88 projects, 40 projects are delayed. During the month, 4 projects have reported additional delays in the range of 2-24 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	WIND POWE PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	2	Land acquisition and civil works
2	PURNADIH OCP (3.0 MTY) CCL	12	Land acquisition
3	CHURI BENTI UG (0.81 MTY) CCL	24	Diversion of forest land
4	RAJRAPPA RCE OCP (3.0 MTY) CCL	24	Land acquisition and forest clearance

- (iv) In the **Steel Sector**, out of 34 projects, 14 projects are delayed. During the month, 4 projects have reported additional delays in the range of 1-3 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	INSTALLATION OF 45 MVA SAF T WITH OTHER ASSOCIATED FACILITIES SAIL	1	Environment clearance and less resource deployment by contractor
2	UPGRADATION OF BLAST FURNACE-1 AT RSP SAIL	1	Delay in supply equipment from contractor
3	REBUILDING OF COB-7 AT BSL SAIL	3	Slow progress by contractor
4	REVAMPING OF SINTER MACHINES - 1 AND 2 RINL	3	Slow progress of procurement and construction from contractor

- (v) In the **Urban Development Sector**, out of 29 projects, 17 projects are delayed. During the month 2 projects have reported additional delays in the range of 1-2 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI CPWD	1	Non-availability of funds

2	BANGALORE METRO RAIL PROJECT MRTP	2	Densely populated area hence progress is slow to avoid damages to structures.
---	--------------------------------------	---	---

(vi) In the **Shipping and Ports**, out of 8 projects, 3 projects are delayed. During the month, 1 project has reported additional delay of 5 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) PORT TRUST	5	. Encroachment

(vii) In the **Petroleum**, out of 80 projects, 38 projects are delayed. During the month, 1 project has reported additional delay of 3 months.

Sr No.	Project Name	Additional Delay (in months)	Reasons for Additional Delay
1	RESID UPGRADATION PROJECT CPCL	3	Restricted timings for radiography activities


12. Ministry of Railways have provided the latest information of all its ongoing projects costing Rs.500 crore and above on the OCMS of this Ministry. For remaining projects data pertain to 01.01.2015.

13. The status as on 31.08.2016 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

14. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	425	11
2	RAILWAYS	360	2
3	POWER	117	7
4	COAL	88	4
5	PETROLEUM	80	1
6	STEEL	34	4
7	URBAN DEVELOPMENT	29	2
8	HEALTH AND FAMILY WELFARE	9	0
9	SHIPPING AND PORTS	8	1
10	ATOMIC ENERGY	4	0
11	CIVIL AVIATION	4	0
12	MINES	3	0
13	FERTILISERS	2	0
14	TELECOMMUNICATIONS	2	0
15	PETROCHEMICALS	1	0
16	HEAVY INDUSTRY	1	0
	Total	1167	32

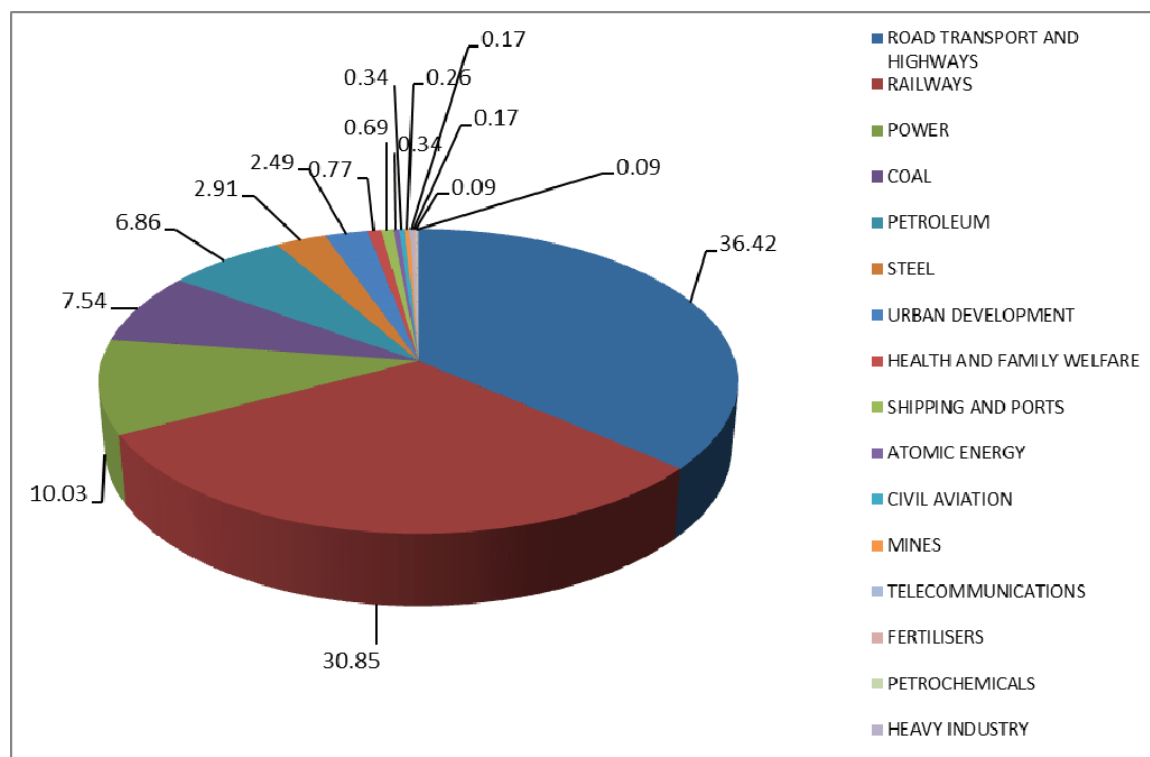

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April, 2016			
	<u>COAL</u>			
1	KRISHNASHILA (NCL) (4MTY) (NORTHERN COAL FIELDS LIMITED) - [N06000007]	789.88	03/2013	511.19
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) (NORTHERN COAL FIELDS LIMITED) - [N06000010]	1,352.04	03/2016	848.99
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
3	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100207]	157.47	09/2007	238.50
4	KOTA BYPASS,RJ-4, NH-76 (NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106297]	275.00	10/2008	184.63
5	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106304]	251.03	10/2008	326.30
6	SILIGURI TO ISLAMPUR (WB-7) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000028]	225.00	07/2008	191.00
7	NALBARI TO BIJNI (AS-8) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000035]	200.00	06/2008	281.60
8	GUWAHATI TO NALBARI (AS-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000046]	198.16	04/2008	242.40
9	DHARAMTUL TO SONAPUR (AS-19) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000051]	200.00	06/2008	289.50
10	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000107]	557.00	02/2010	932.30
11	KISHANGARH-AJMER-BEAWER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000128]	795.00	05/2012	1,512.11
12	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000132]	572.30	10/2011	761.40
13	JAIPUR-TONK-DEOLI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000135]	792.06	12/2012	1,983.00
14	HAZARIBAGH-RANCHI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000141]	625.07	01/2013	995.90
15	ARMUR TO KADLOOR YELLAREDDY (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000143]	390.56	02/2012	631.60
16	PANIPAT-ROHTAK (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000151]	807.00	10/2014	1,209.43
17	DEVIHALLI-HASSAN (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000152]	453.00	-	487.90
18	BELGAUM-DHARWAD(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000158]	480.00	-	438.00
19	UGRADATION OF HYDERABAD-BANGALORE SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000160]	680.00	-	188.40
20	2-LANNING OF SHILONG BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000181]	226.00	02/2014	282.30
21	BHOPAL-SANCHI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000192]	209.00	01/2013	11.28

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
22	PUNE-SHOLAPUR,PKG-II PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000193]	835.00	01/2014	1,684.00
23	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000196]	909.00	05/2014	844.10
24	LUCKNOW-RAIBAREILI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000207]	635.90	07/2012	616.50
25	NAGPUR-WAINGANGA BRIDGE PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000210]	484.19	10/2014	458.86
26	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000214]	682.00	10/2013	34.81
27	2 LANING WITH PS AGRA ALIGARH (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000220]	250.50	10/2014	65.30
28	2 LANING WITH PS KANPUR KABRAI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000221]	373.47	07/2014	358.30
29	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000237]	177.32	01/2016	86.50
30	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000304]	186.96	-	132.80
31	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000428]	569.38	06/2016	737.59
32	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000466]	285.00	01/2008	285.00
	May,2016			
	<u>STEEL</u>			
33	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000072]	572.00	04/2013	451.58
34	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000073]	898.55	05/2013	379.57
	<u>PETROLEUM</u>			
35	MOUNDED BULLET PROJECT AT CPCL (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000154]	279.00	12/2014	190.86
	<u>URBAN DEVELOPMENT</u>			
36	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000061]	225.81	06/2012	143.72
37	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000063]	171.10	09/2014	192.24
	June,2016			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
38	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000108]	232.45	09/2010	343.71
	July,2016			
	<u>PETROLEUM</u>			
39	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000183]	2,476.82	12/2018	982.92
	<u>POWER</u>			
40	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000056]	410.29	02/2012	390.87
41	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000083]	965.58	11/2012	791.84
42	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000095]	1,677.57	04/2013	1,487.22
43	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000104]	558.26	11/2013	629.41
44	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000113]	2,422.66	08/2014	2,497.86
45	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000122]	1,927.16	10/2014	1,642.57
46	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000198]	312.94	05/2016	109.00
	<u>RAILWAYS</u>			
47	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR (EAST CENTRAL RAILWAYS) - [N220100307]	921.00	03/2009	1,649.05
48	PATNA GANGA BRIDGE (NL), ECR (EAST CENTRAL RAILWAYS) - [N220100308]	624.47	10/2007	3,104.92
49	CONSTRUCTION OF STEEL SUPERSTRUCTURE AND OTHER ANCILLARY WORKS OF RAIL CUM ROAD BRIDGE. FABRICATION (EAST CENTRAL RAILWAYS) - [N22000342]	1,191.31	06/2012	1,296.95
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
50	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N240106221]	155.00	09/2008	248.73
51	4 LANNING OF GODHARA TO GUJARAT/MP BORDER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000168]	785.50	08/2013	923.28
52	JAIPUR-REENGUS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000198]	267.81	02/2013	699.60
53	BEAWAR PALI PINDWARA PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000199]	2,388.51	06/2014	2,490.61
54	REENGUS SIKAR PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000227]	333.51	09/2014	226.96

Month wise List of Completed Projects Costing Rs. 150 crore and above during 2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
55	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000238]	158.04	12/2015	129.37
56	4 LANING OF GOMTI CHAURAHA - UDAIPUR EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000455]	914.50	10/2015	1,128.25
57	4-LANING OF ROHTAK - HISSAR SECTION PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000456]	959.25	06/2016	1,229.40
	August,2016			
	<u>POWER</u>			
58	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100243]	1,061.38	09/2009	2,048.42
	<u>RAILWAYS</u>			
59	CUTTACK - BARANG (LD) (RAIL VIKAS NIGAM LTD.) - [220100326]	127.13	-	237.96
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
60	GUWHATI TO NALBARI (AS-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000038]	175.96	04/2008	309.01
61	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000171]	535.00	12/2013	924.70

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2016			
	<u>URBAN DEVELOPMENT</u>			
1	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000066]	238.43	02/2015	.00
	July,2016			
	<u>PETROLEUM</u>			
2	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000129]	2,915.00	12/2012	1,381.86
	August,2016			
	<u>COAL</u>			
3	GOPAL PRASAD OCP (15MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000042]	395.87	03/2015	76.74
4	TALABIRA OCP (MAHANADI COAL FIELDS LIMITED) - [N06000043]	447.72	03/2016	52.36


Summary of projects in the Flash Report for the month of August, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1144
Number of Projects completed/dropped/frozen in Current Month	6
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	28
Number of Projects in Current Month	1167


Brief Analysis

Project Status with respect to Original Schedule: Out of 1167 projects, 7 projects are ahead of schedule, 282 projects are on schedule 337 projects are delayed. 460 projects do not have fixed dates of commissioning. 81 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

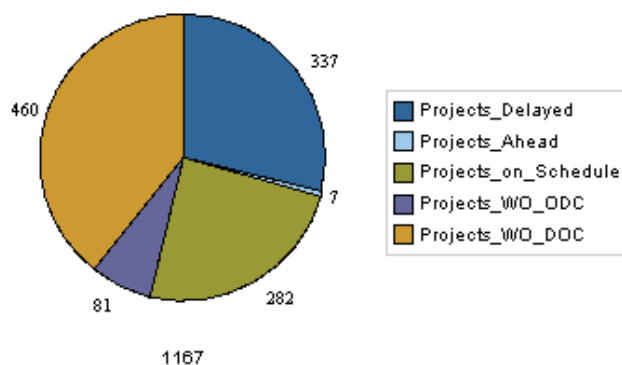

Investment Scenario

Total original cost of implementation of 1167 projects when sanctioned, was of the order of Rs. 1433476.53 crore but this was subsequently revised to Rs. 1610504.54 crore implying a cost overrun of 12.3%. The expenditure incurred on these projects till August, 2016 is Rs. 630581.41 crore, which is 39.2% of the revised cost of the projects.

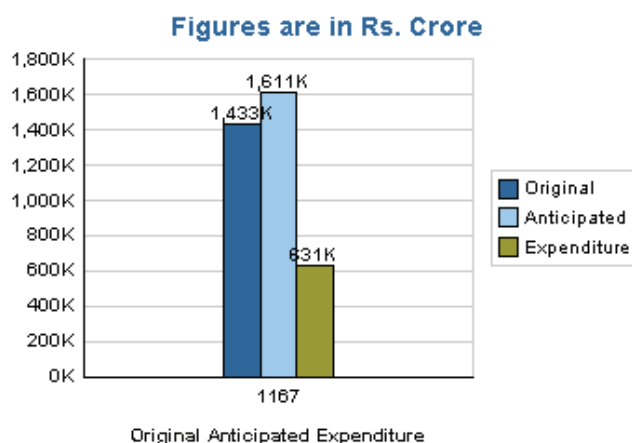

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	1144
No of Projects Completed/Dropped/Frozen in Current Month	6
No. of Projects elevated to the status of Major Projects during the Current Month	1
No of Projects added in Current Month	28
No of Projects in Current Month	1167

Project status

Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	337	7	282	81	460	1167	28.88
Latest Approved (Date)	283	9	341	74	460	1167	24.25

Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	983	12,23,713.82	12,85,683.14	4,25,292.90	33.10	61,969.32	5.10
Project with Revision in Cost	184	2,98,195.88	3,24,821.40	2,05,288.51	63.20	26,625.52	8.90
Total	1,167	15,21,909.70	16,10,504.54	6,30,581.41	39.15	88594.84	5.82
Original Cost of All Projects							
Original Cost	1167	14,33,476.53	16,10,504.54	6,30,581.41	39.15	1,77,028.01	12.35

Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	337	564,129.10	677,729.16	419,810.90	61.90	113,600.06	20.10
Latest Approved (RCE)	281	432,179.64	497,703.43	309,824.77	62.30	65,523.79	15.20

Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	32	26,704.90	42,077.88	35,314.44	83.90	15,372.98	57.60

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	88	68,729.81	70,406.76	2.44	6	1,953.12	3,630.07	85.86
4	FERTILISERS	2	680.64	692.29	1.71	1	197.79	209.44	5.89
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	34	57,600.51	57,771.82	0.30	5	1,639.71	2,169.02	32.28
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	80	136,063.71	137,688.98	1.19	14	15,385.77	18,964.03	23.26
9	POWER	117	331,536.75	380,903.08	14.89	27	68,713.35	118,143.29	71.94
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	360	358,611.57	452,613.73	26.21	188	97,908.57	250,572.15	155.92
13	ROAD TRANSPORT AND HIGHWAYS	425	272,789.46	275,538.97	1.01	19	7,246.67	10,240.42	41.31
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	5	1,205.50	2,172.77	80.24
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	29	133,984.49	143,123.47	6.82	3	10,900.33	20,052.34	83.96
Total		1167	1,433,476.53	1,610,504.54	12.35	273	229,210.02	468,328.93	104.32

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	52	58,490.76	62,196.35	6.34	8	2,504.74	7,091.26	183.11
2	ARUNACHAL PRADESH	15	12,006.22	28,062.52	133.73	5	9,616.85	25,673.15	166.96
3	ASSAM	52	36,951.00	54,911.99	48.61	15	20,218.17	38,284.91	89.36
4	BIHAR	73	64,649.96	77,718.17	20.21	15	13,203.03	26,617.48	101.60
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	0.00
6	GUJARAT	42	37,127.23	39,183.68	5.54	10	5,088.97	7,272.74	42.91
7	HARYANA	18	12,060.70	14,031.32	16.34	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	9	10,659.35	17,058.62	60.03	2	4,966.47	11,365.74	128.85
9	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	2	6,142.04	25,348.17	312.70
10	KARNATAKA	42	74,476.15	92,794.43	24.60	19	15,462.67	34,927.98	125.89
11	KERALA	19	33,504.08	35,120.13	4.82	6	2,117.36	3,733.41	76.32
12	MADHYA PRADESH	52	56,376.91	60,820.87	7.88	7	4,634.35	9,766.85	110.75
13	MAHARASHTRA	96	156,010.09	164,632.84	5.53	16	18,773.13	29,705.84	58.24
14	MANIPUR	3	1,047.27	10,045.73	859.23	2	830.58	9,829.04	1083.39
15	MEGHALAYA	5	6,744.03	8,661.01	28.42	1	4,083.02	6,000.00	46.95
16	MIZORAM	5	2,001.20	7,054.66	252.52	2	988.06	6,041.52	511.45
17	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
18	ODISHA	55	59,391.88	65,327.97	9.99	13	4,420.53	10,377.96	134.77
19	PUNJAB	25	14,354.28	14,358.28	0.03	1	573.96	605.00	5.41
20	RAJASTHAN	59	39,324.78	40,491.87	2.97	9	3,810.47	5,037.97	32.21
21	SIKKIM	5	2,149.08	4,894.01	127.73	1	1,339.48	4,084.69	204.95
22	TAMIL NADU	61	71,269.10	92,215.95	29.39	24	24,329.86	45,276.71	86.10
23	TRIPURA	10	4,140.67	9,124.56	120.36	7	2,909.18	7,893.07	171.32
24	UTTAR PRADESH	76	77,839.61	81,239.51	4.37	9	3,695.80	7,095.70	91.99
25	WEST BENGAL	50	52,822.74	63,408.95	20.04	14	9,567.47	21,881.33	128.71
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	17	50,768.66	51,802.66	2.04	1	4,264.00	5,298.00	24.25
28	CHHATISGARH	41	96,809.69	99,835.63	3.13	9	9,008.64	12,034.58	33.59
29	JHARKHAND	46	45,227.61	48,236.81	6.65	9	8,111.31	11,120.51	37.10
30	UTTARAKHAND	9	15,810.70	18,110.01	14.54	3	4,855.31	7,155.13	47.37
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
32	TELANGANA	37	26,031.22	29,431.19	13.06	9	2,836.21	6,324.39	122.99
33	MULTI STATE	170	271,276.73	254,241.47	-6.28	50	38,374.80	75,881.62	97.74
Total		1167	1,433,476.53	1,610,504.54	12.35	273	229,210.02	468,328.93	104.32

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of time overrun in projects with respect to original schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	3	27,271.00	29,456.00	35 - 85
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	88	68,729.81	70,406.76	2.44	40	20,664.84	21,325.74	6 - 132
4	FERTILISERS	2	680.64	692.29	1.71	1	197.79	209.44	10 - 10
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	34	57,600.51	57,771.82	0.30	14	38,281.71	38,484.54	6 - 45
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	80	136,063.71	137,688.98	1.19	38	59,483.71	61,030.75	1 - 71
9	POWER	117	331,536.75	380,903.08	14.89	61	194,770.21	224,717.21	3 - 134
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	4	826.49	826.49	1 - 35
12	RAILWAYS	360	358,611.57	452,613.73	26.21	41	44,580.32	111,000.19	11 - 261
13	ROAD TRANSPORT AND HIGHWAYS	425	272,789.46	275,538.97	1.01	111	82,117.55	84,499.81	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	3	762.06	1,679.29	88 - 129
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	2,111.17	2,011.17	30 - 30
16	URBAN DEVELOPMENT	29	133,984.49	143,123.47	6.82	17	89,178.79	97,175.77	4 - 67
Total		1167	1,433,476.53	1,610,504.54	12.35	337	564,129.10	677,729.16	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	52	58,490.76	62,196.35	6.34	17	8,815.31	9,771.95	6 - 106
2	ARUNACHAL PRADESH	15	12,006.22	28,062.52	133.73	2	3,070.89	7,761.00	45 - 94
3	ASSAM	52	36,951.00	54,911.99	48.61	20	13,968.98	26,027.48	21 - 138
4	BIHAR	73	64,649.96	77,718.17	20.21	16	33,799.30	40,971.02	1 - 96
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	-
6	GUJARAT	42	37,127.23	39,183.68	5.54	13	21,814.16	21,690.22	1 - 84
7	HARYANA	18	12,060.70	14,031.32	16.34	5	3,130.20	4,310.20	24 - 79
8	HIMACHAL PRADESH	9	10,659.35	17,058.62	60.03	2	4,190.42	8,669.58	30 - 111
9	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	5	15,513.58	32,578.58	23 - 193
10	KARNATAKA	42	74,476.15	92,794.43	24.60	10	52,131.53	61,013.62	6 - 67
11	KERALA	19	33,504.08	35,120.13	4.82	8	23,065.25	23,336.60	3 - 88
12	MADHYA PRADESH	52	56,376.91	60,820.87	7.88	10	7,341.14	8,547.19	11 - 120
13	MAHARASHTRA	96	156,010.09	164,632.84	5.53	21	39,753.54	43,551.09	1 - 96
14	MANIPUR	3	1,047.27	10,045.73	859.23	3	1,047.27	10,045.73	1 - 96
15	MEGHALAYA	5	6,744.03	8,661.01	28.42	1	536.00	536.00	41 - 41
16	MIZORAM	5	2,001.20	7,054.66	252.52	2	988.06	6,041.52	71 - 134
17	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	72 - 72
18	ODISHA	55	59,391.88	65,327.97	9.99	17	10,390.97	10,881.60	5 - 108
19	PUNJAB	25	14,354.28	14,358.28	0.03	2	971.14	971.14	12 - 14
20	RAJASTHAN	59	39,324.78	40,491.87	2.97	10	16,616.99	16,688.18	6 - 87
21	SIKKIM	5	2,149.08	4,894.01	127.73	2	1,648.94	4,394.15	51 - 80
22	TAMIL NADU	61	71,269.10	92,215.95	29.39	19	39,052.61	42,142.11	4 - 129
23	TRIPURA	10	4,140.67	9,124.56	120.36	3	1,138.56	3,833.65	7 - 72
24	UTTAR PRADESH	76	77,839.61	81,239.51	4.37	16	20,976.56	22,233.09	3 - 108
25	WEST BENGAL	50	52,822.74	63,408.95	20.04	17	27,716.95	27,151.74	2 - 216
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	-
27	DELHI	17	50,768.66	51,802.66	2.04	5	39,749.95	39,749.95	1 - 41
28	CHHATISGARH	41	96,809.69	99,835.63	3.13	16	64,319.99	66,593.75	3 - 93
29	JHARKHAND	46	45,227.61	48,236.81	6.65	21	27,448.95	29,663.20	10 - 155
30	UTTARAKHAND	9	15,810.70	18,110.01	14.54	4	7,605.57	9,794.74	35 - 78
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	37	26,031.22	29,431.19	13.06	12	4,210.18	4,520.52	21 - 132
33	MULTI STATE	170	271,276.73	254,241.47	-6.28	57	72,266.11	91,259.56	1 - 261
Total		1167	1,433,476.53	1,610,504.54	12.35	337	564,129.10	677,729.16	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	3	27,271.00	29,456.00	35 - 85
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	88	68,729.81	70,406.76	2.44	37	13,040.16	13,473.89	6 - 132
4	FERTILISERS	2	680.64	692.29	1.71	0	.00	.00	-
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	34	57,600.51	57,771.82	0.30	13	22,756.71	22,959.54	6 - 45
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	.00	.00	-
8	PETROLEUM	80	1,36,063.71	1,37,688.98	1.19	19	35,604.28	36,246.11	1 - 66
9	POWER	117	3,31,536.75	3,80,903.08	14.89	47	1,00,438.07	1,11,023.34	4 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	4	826.49	826.49	1 - 35
12	RAILWAYS	360	3,58,611.57	4,52,613.73	26.21	35	37,076.74	97,864.10	0 - 261
13	ROAD TRANSPORT AND HIGHWAYS	425	2,72,789.46	2,75,538.97	1.01	107	81,286.94	83,577.25	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	395.67	1,009.83	88 - 129
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	2,111.17	2,011.17	30 - 30
16	URBAN DEVELOPMENT	29	1,33,984.49	1,43,123.47	6.82	12	87,843.30	95,840.28	8 - 67
Total		1167	14,33,476.53	16,10,504.54	12.35	283	4,12,533.99	4,99,600.76	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	44,541.00	51,918.00	16.56	2	20,762.00	28,139.00	35.53
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	88	68,956.98	70,406.76	2.10	5	1,693.72	3,143.50	85.60
4	FERTILISERS	2	692.29	692.29	0.00	0	0.00	0.00	0.00
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	34	57,981.48	57,771.82	-0.36	2	516.00	664.34	28.75
7	PETROCHEMICALS	1	9,965.00	9,965.00	0.00	0	0.00	0.00	0.00
8	PETROLEUM	80	135,996.03	137,688.98	1.24	6	4,761.99	6,672.25	40.11
9	POWER	117	362,207.70	380,903.08	5.16	6	27,068.67	45,764.05	69.07
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	360	396,917.50	452,613.73	14.03	148	97,158.06	209,429.64	115.56
13	ROAD TRANSPORT AND HIGHWAYS	425	274,664.54	275,538.97	0.32	15	6,163.32	8,697.76	41.12
14	SHIPPING AND PORTS	8	5,048.08	5,085.02	0.73	2	631.22	668.16	5.85
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	29	141,479.87	143,123.47	1.16	3	18,251.38	19,894.98	9.01
Total		1167	1,521,909.70	1,610,504.54	5.82	191	178,941.96	327,145.08	82.82

[^] - Cost Overrun = Anticipated Cost minus Latest Approved Cost.

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	1	3,492.00	5,677.00	85- 85
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	88	68,729.81	70,406.76	2.44	4	1,481.38	1,915.11	24- 132
4	FERTILISERS	2	680.64	692.29	1.71	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	34	57,600.51	57,771.82	0.30	2	492.73	664.34	11- 15
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	80	136,063.71	137,688.98	1.19	2	1,864.35	2,893.00	21- 56
9	POWER	117	331,536.75	380,903.08	14.89	2	6,232.59	12,636.42	58- 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	360	358,611.57	452,613.73	26.21	24	16,736.60	78,805.25	21- 261
13	ROAD TRANSPORT AND HIGHWAYS	425	272,789.46	275,538.97	1.01	8	4,443.85	6,734.67	13- 97
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	1	245.67	409.83	88- 88
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	29	133,984.49	143,123.47	6.82	2	6,600.00	14,596.98	60- 67
Total		1167	1433476.53	1610504.54	12.35	47	43307.17	128159.9	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest approved Cost

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	1	3,492.00	5,677.00	85- 85
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	88	68,729.81	70,406.76	2.44	5	1,740.78	2,401.68	24- 132
4	FERTILISERS	2	680.64	692.29	1.71	1	197.79	209.44	10- 10
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	34	57,600.51	57,771.82	0.30	3	668.22	871.05	7- 15
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	80	136,063.71	137,688.98	1.19	10	7,134.22	9,810.56	1- 56
9	POWER	117	331,536.75	380,903.08	14.89	22	53,690.53	83,701.14	23- 134
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	360	358,611.57	452,613.73	26.21	29	26,856.49	92,845.61	21- 261
13	ROAD TRANSPORT AND HIGHWAYS	425	272,789.46	275,538.97	1.01	9	4,661.46	7,044.23	13- 97
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	3	762.06	1,679.29	88- 129
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	29	133,984.49	143,123.47	6.82	1	6,395.00	14,405.01	67- 67
Total		1167	1433476.53	1610504.54	12.35	85	107316.55	222472.31	

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning
^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>List of projects completed/dropped/Frozen during current month</u>							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	GOPAL PRASAD OCP (15MTY)	02/2008	395.87	03/2015	395.87	03/2021	76.74
2	TALABIRA OCP	03/2008	447.72	03/2016	447.72	03/2020	52.36
	<u>POWER</u>						
3	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1,061.38	09/2009	2,193.08	09/2016	2,048.42
	<u>RAILWAYS</u>						
4	CUTTACK - BARANG (LD)	04/1995	127.13	N.A.	225.00	N.A.	237.96
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
5	GUWHATI TO NALBARI (AS-4)	12/2003	175.96	04/2008	175.96	09/2016	309.01
6	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 PPP (BOT)	06/2011	535.00	12/2013	535.00	06/2016	924.70

List of projects added					(All Cost in Rs. Crore) (August 2016)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	327.78	4/2018	327.78	4/2018
2	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	2/2017	678.00	2/2017
3	VISAKH REFINERY MODERNISATION PROJECT	7/2016	20,928.00	7/2020	20,928.00	7/2020
	<u>POWER</u>					
4	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	808.63	1/2018	808.63	1/2018
5	EASTERN REGION STRENGTHENING SCHEME-XV	1/1991	454.11	4/2018	454.11	4/2018
6	SRINAGAR-LEH TRANSMISSION PROJECT	1/2014	1,788.41	9/2017	1,788.41	9/2017
7	NORTH EASTERN REGION STRENGTHENING SCHEME IV	5/2016	364.60	5/2018	364.60	5/2018
8	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	3,519.59	5/2019	3,519.59	5/2019
9	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I	4/2016	810.48	/	810.48	-
10	EASTERN REGION STRENGTHENING SCHEME XIV	5/2016	167.01	11/2018	167.01	11/2019
11	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	844.64	4/2019	844.64	4/2019
12	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS	4/2016	790.13	6/2018	790.13	6/2018
13	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	4/2016	287.99	6/2018	287.99	6/2018
14	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	14,733.37	11/2019	14,733.37	11/2019
15	EASTERN REGION STRENGTHENING SCHEME XI	5/2016	766.21	11/2018	766.21	11/2018
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
16	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	1,388.34	/	1,388.34	-

List of projects added					(August 2016)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
17	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	1,169.61	/	1,169.61	-
18	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	1,664.20	/	1,664.20	-
19	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	323.72	/	323.72	-
20	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	1,583.18	/	1,583.18	-
21	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	227.49	/	227.49	-
22	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	1,167.42	/	1,167.42	-
23	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	2,016.00	/	2,016.00	-
24	4-LANING OF HOSKOTE-DOBBASPET	5/2014	720.69	/	720.69	-
25	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1)	5/2015	600.85	/	600.85	-
26	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	248.97	/	248.97	-
27	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	320.30	/	320.30	-
28	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	771.18	/	771.18	-

Milestones (Cumulative due & achieved)


Total	3938
Achieved up to month	1777

List of projects reporting additional delays (August 2016)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	08/2016	10/2016	2
2	PURNADIH OCP (3.0 MTY) CCL	210.98	210.98	03/2013	03/2016	03/2017	12
3	CHURI BENTI UG (0.81 MTY) CCL	163.51	163.51	03/2011	03/2016	03/2018	24
4	RAJRAPPA RCE OCP (3.0 MTY) CCL	510.85	510.85	03/2016	03/2016	03/2018	24
	<u>STEEL</u>						
5	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES SAIL	187.33	187.33	10/2013	08/2016	09/2016	1
6	UPGRADATION OF BLAST FURNACE-1 AT RSP SAIL	708.91	708.91	04/2016	09/2016	10/2016	1
7	REBUILDING OF COB-7 AT BSL SAIL	245.67	245.67	05/2016	12/2016	03/2017	3
8	REVAMPING OF SINTER MACHINES - 1 AND 2 RINL	343.00	488.40	10/2016	06/2017	09/2017	3
	<u>PETROLEUM</u>						
9	RESID UPGRADATION PROJECT CPCL	3,110.36	3,110.36	11/2015	11/2016	02/2017	3
	<u>POWER</u>						
10	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	250.03	390.51	01/2013	08/2016	09/2016	1
11	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	723.63	723.63	11/2014	11/2016	12/2016	1
12	PARE HYDRO ELECTRIC PROJECT NEEPCO	573.99	1,581.04	08/2013	03/2017	05/2017	2
13	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,364.52	04/2016	12/2016	03/2017	3
14	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION PGCIL	829.98	829.98	08/2016	09/2016	12/2016	3
15	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	6,179.96	12/2009	06/2017	10/2017	4


List of projects reporting additional delays (August 2016)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) NEEPCO	368.72	1,441.52	07/2006	03/2017	09/2017	6
	<u>RAILWAYS</u>						
17	MURKONGSELEK-PASIGHAT NL NFR	165.82	450.00	N.A.	03/2018	03/2019	12
18	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR NFR	200.00	780.00	N.A.	03/2017	03/2019	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
19	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) NHAI	332.94	332.94	09/2008	08/2016	09/2016	1
20	VADODARA-SURAT SECTION NHAI	503.16	503.16	08/2016	08/2016	09/2016	1
21	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ NHAI	581.84	581.84	05/2017	05/2017	06/2017	1
22	SAMAIKHIALI - GANDHIDHAM NHAI PPP (BOT)	805.39	805.39	03/2013	07/2016	09/2016	2
23	2 LANNING OF MOKAMA-MUNGER NHAI PPP (ANNUITY)	351.54	351.54	05/2013	08/2016	11/2016	3
24	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION NHAI	368.15	368.15	01/2016	08/2016	11/2016	3
25	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM NHAI PPP (BOT)	852.00	852.00	03/2013	08/2016	12/2016	4
26	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 NHAI PPP (BOT)	574.00	574.00	03/2014	08/2016	03/2017	7
27	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA NHAI PPP (BOT)	677.79	677.79	04/2016	08/2016	03/2017	7
28	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM NHAI PPP (BOT)	1,585.00	1,585.00	05/2013	08/2016	06/2017	10
29	FOUR LANING OF CHADIGARH - KHARAR NHAI	447.29	447.29	12/2017	12/2017	12/2018	12
	<u>SHIPPING AND PORTS</u>						
30	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) PORT TRUST Public Private (SPV)	150.00	600.00	03/2006	07/2016	12/2016	5

List of projects reporting additional delays							(August 2016)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>URBAN DEVELOPMENT</u>						
31	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI CPWD	261.85	261.85	05/2013	09/2016	10/2016	1
32	BANGALORE METRO RAIL PROJECT MRTD	6,395.00	14,405.01	06/2011	11/2016	01/2017	2

Graphical Presentation of All Projects w.r.t. Original Schedule

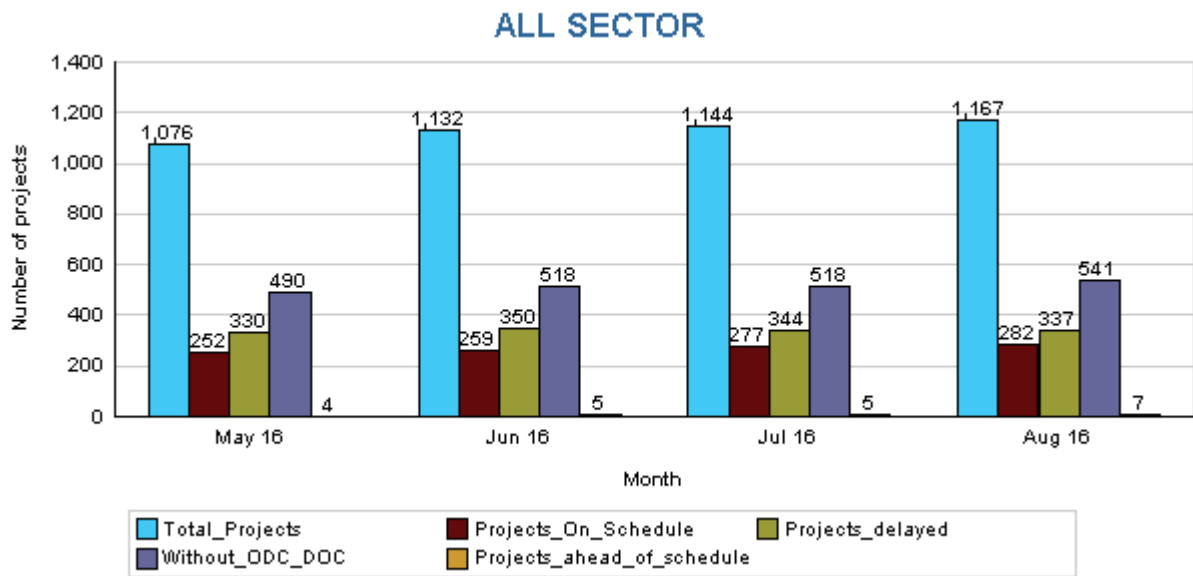


Break-up of 337 Delayed projects in August 2016

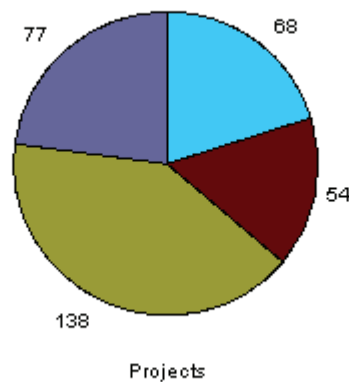


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

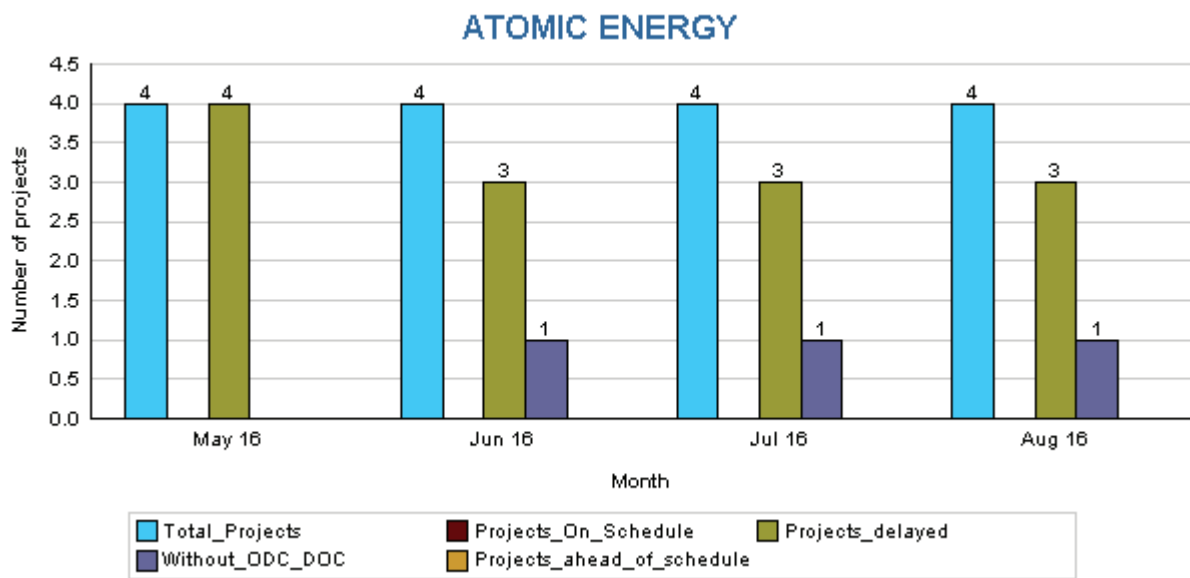


Break-up of 3 Delayed projects in August 2016

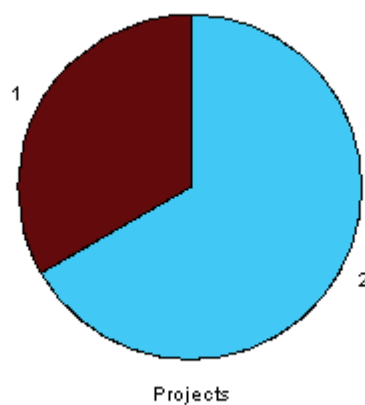


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

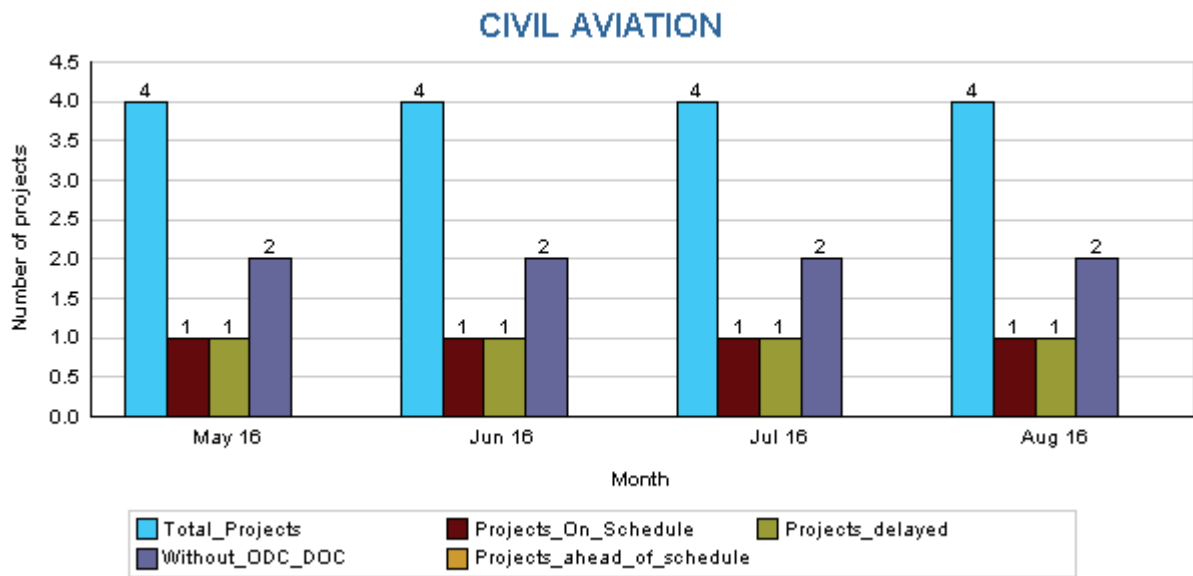


Break-up of 1 Delayed projects in August 2016




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

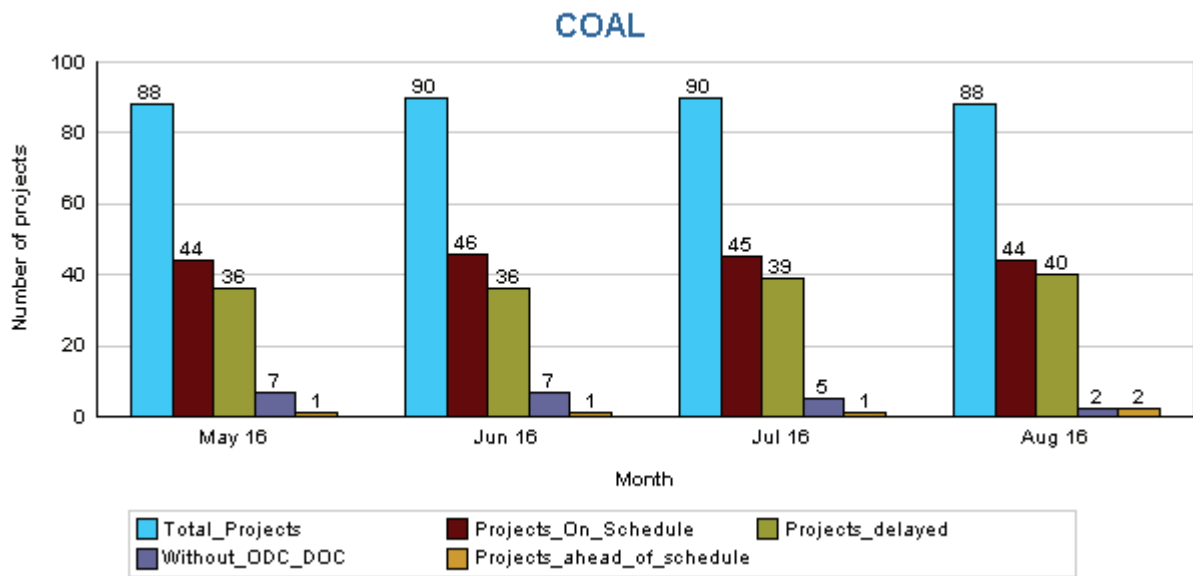


Break-up of 40 Delayed projects in August 2016

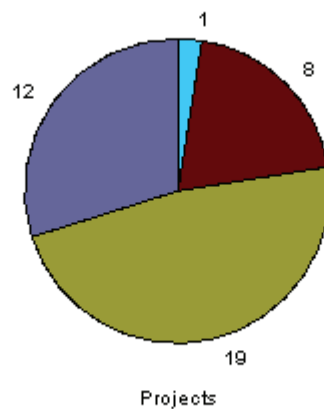


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

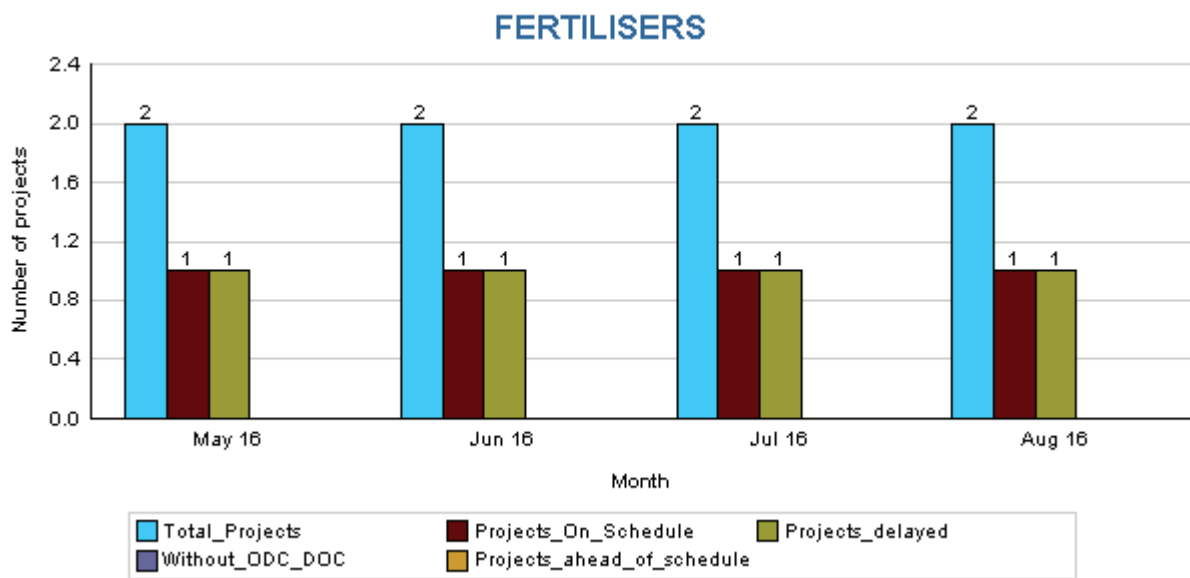


Break-up of 1 Delayed projects in August 2016

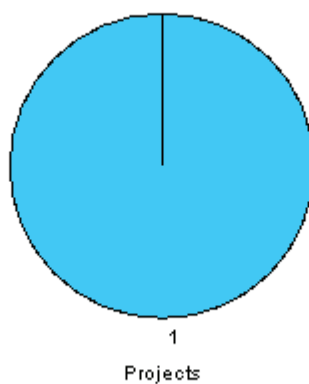


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

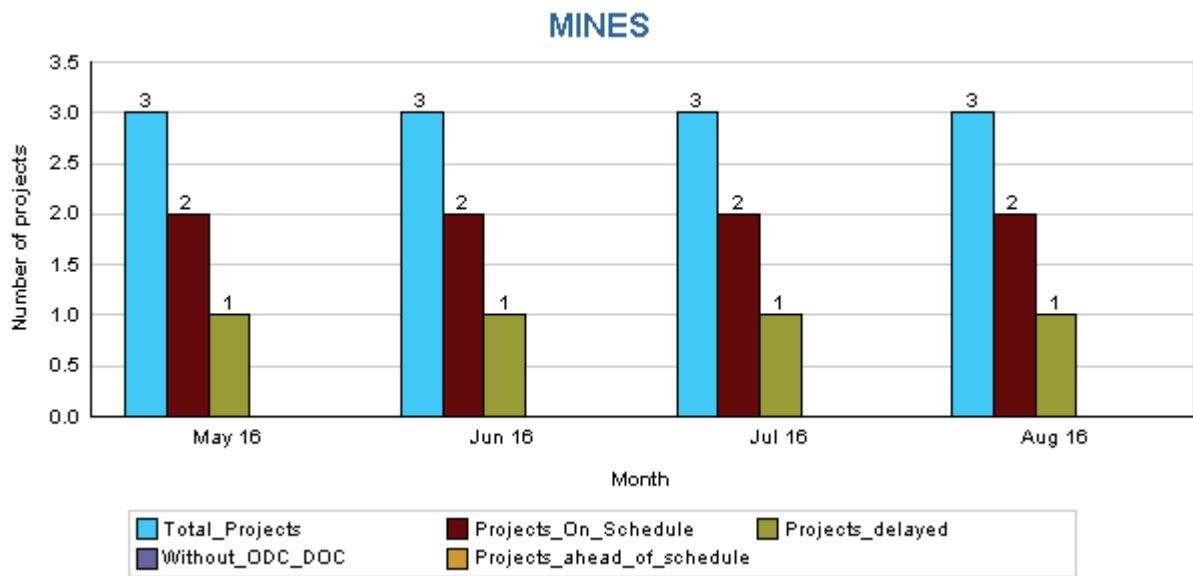


Break-up of 1 Delayed projects in August 2016

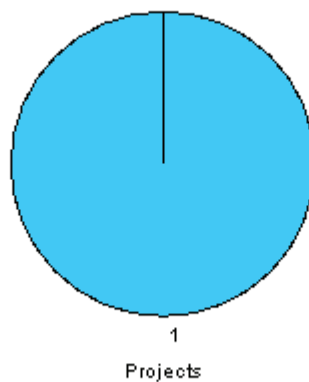


Delay in Months

25-60

Graphical Presentation of All Projects w.r.t. Original Schedule

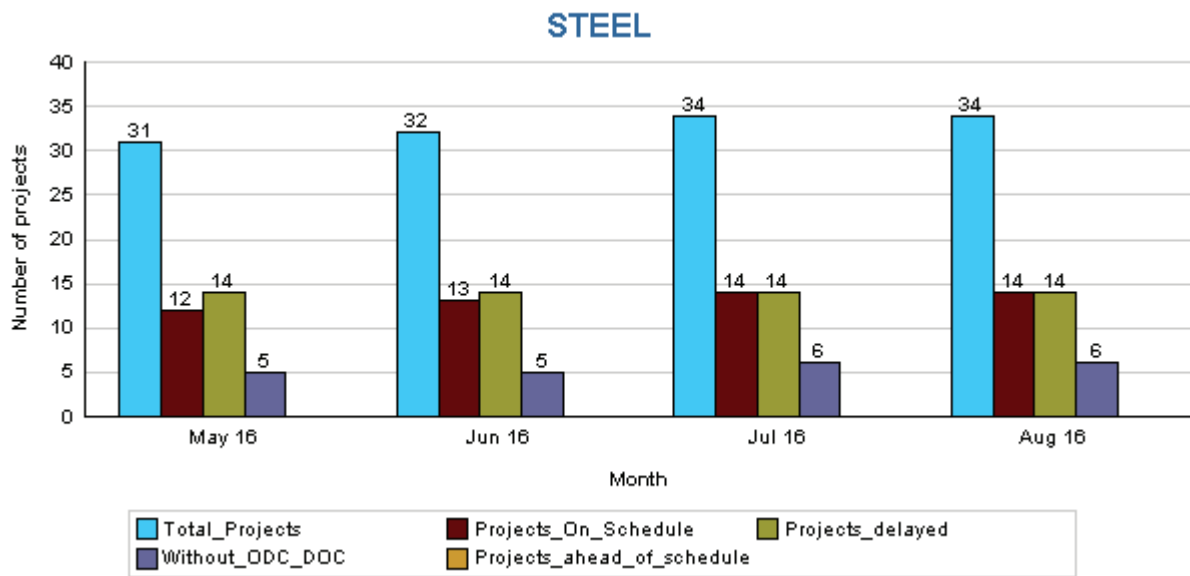


Break-up of 14 Delayed projects in August 2016

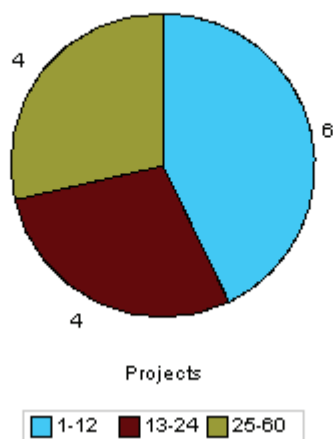


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

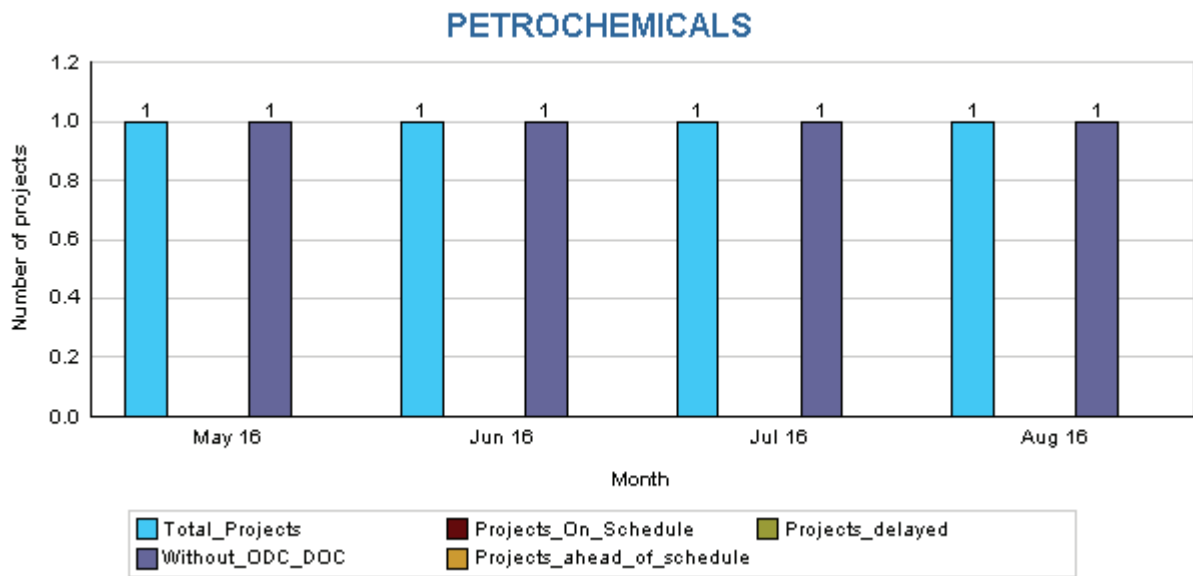


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

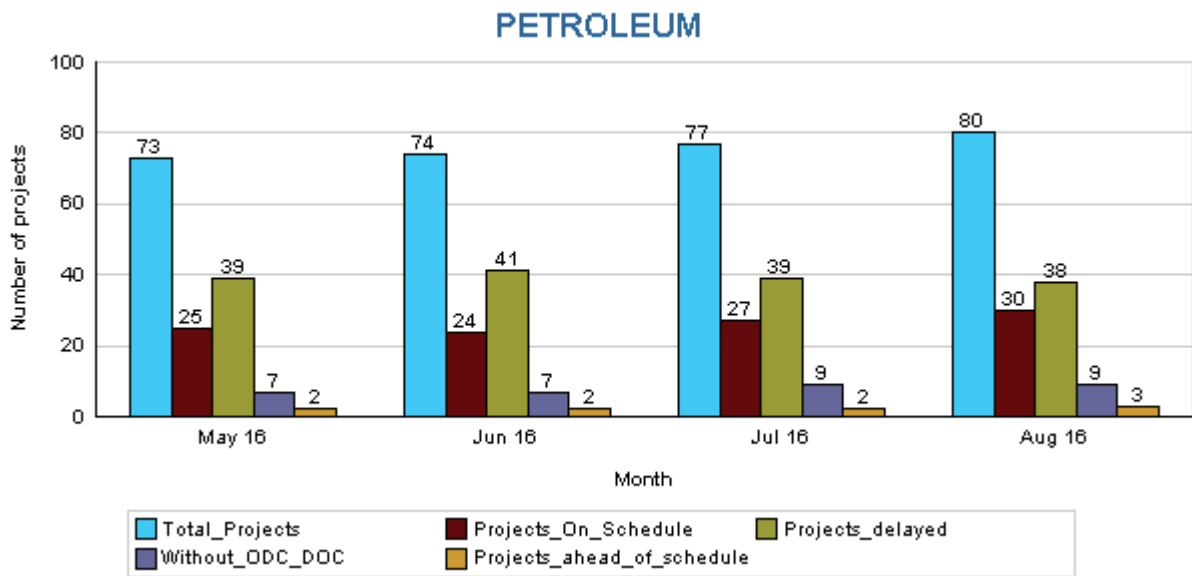


Break-up of 38 Delayed projects in August 2016

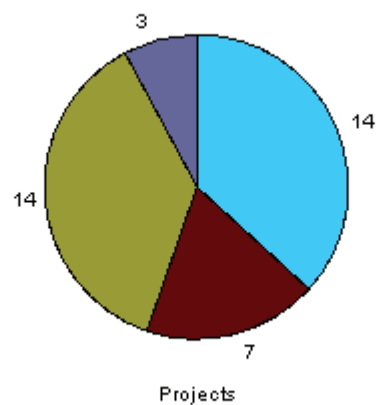


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

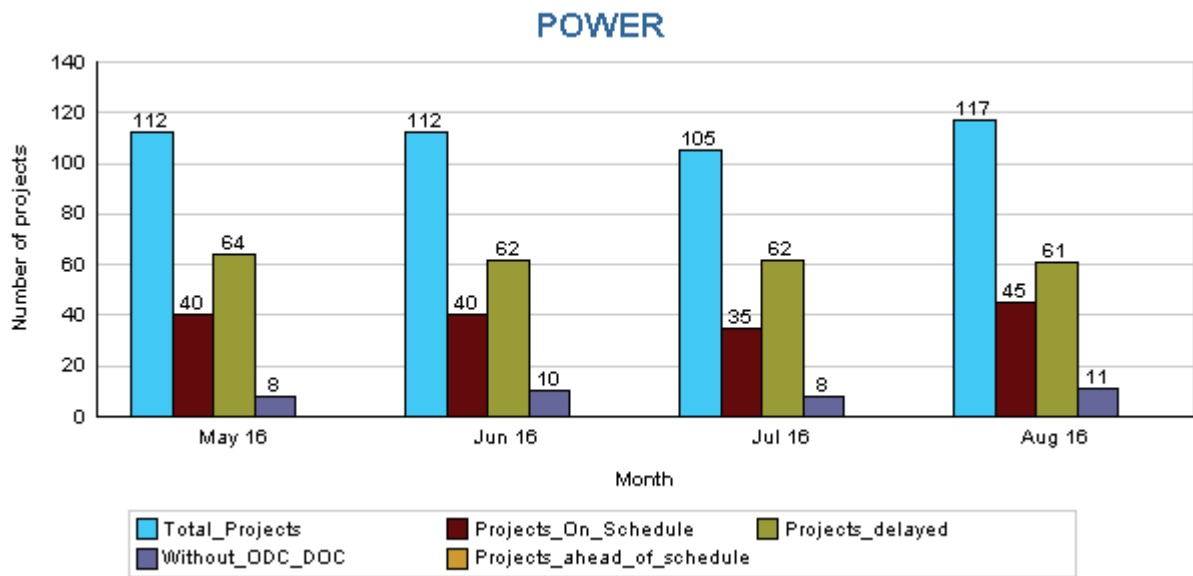


Break-up of 61 Delayed projects in August 2016

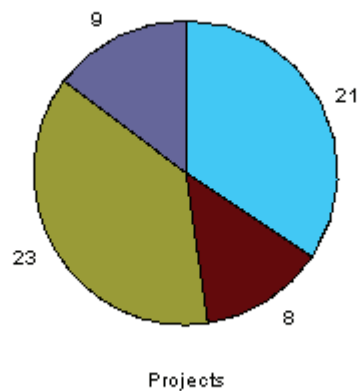


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

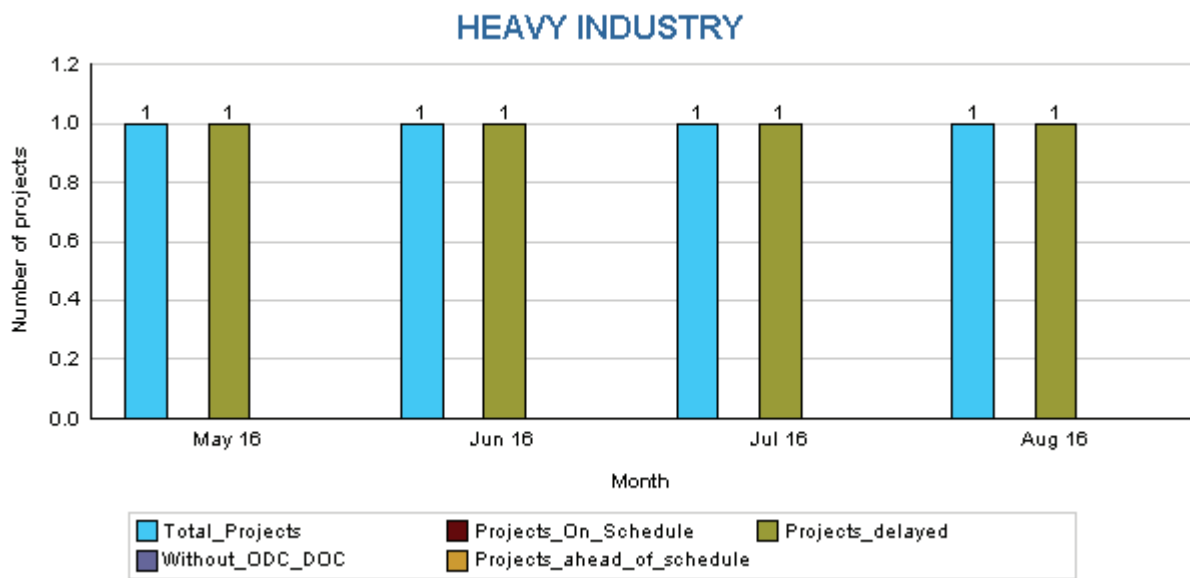


Break-up of 1 Delayed projects in August 2016




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

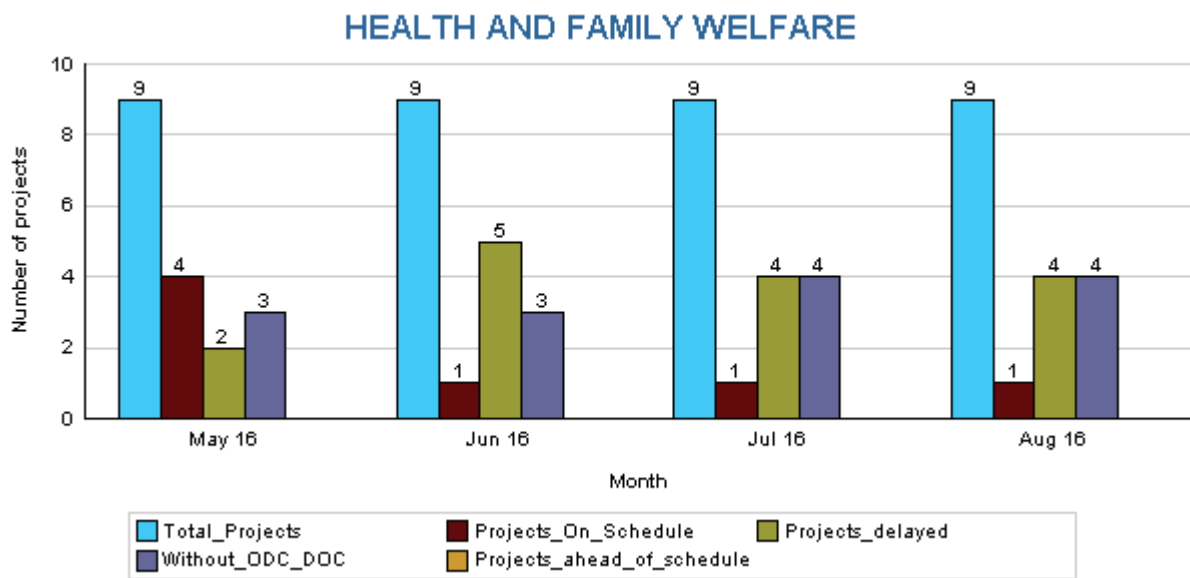


Break-up of 4 Delayed projects in August 2016

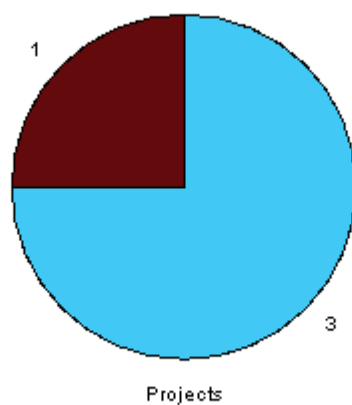


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

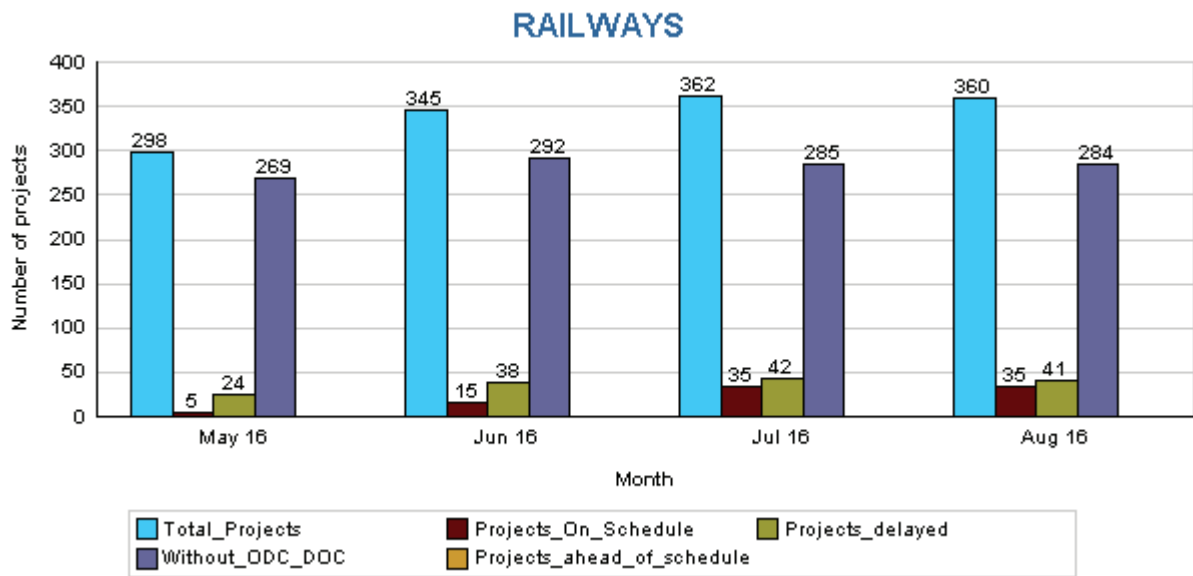


Break-up of 41 Delayed projects in August 2016

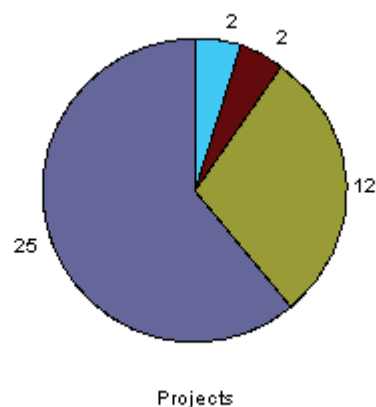


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

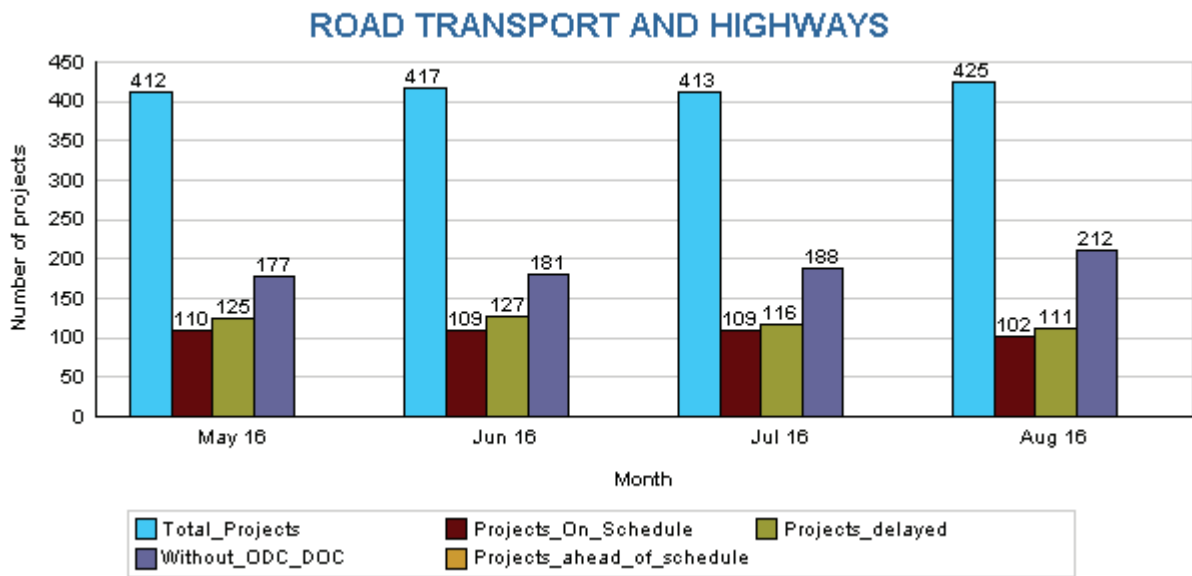


Break-up of 111 Delayed projects in August 2016

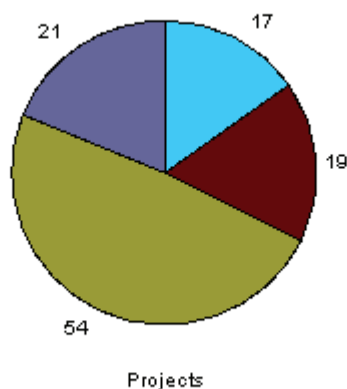


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

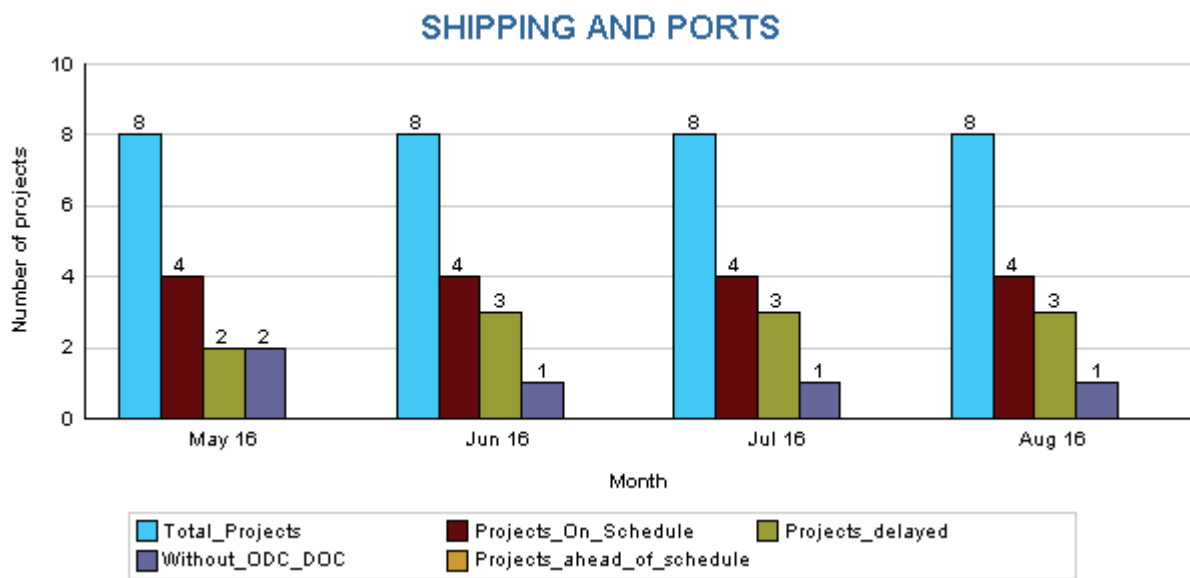


Break-up of 3 Delayed projects in August 2016




Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

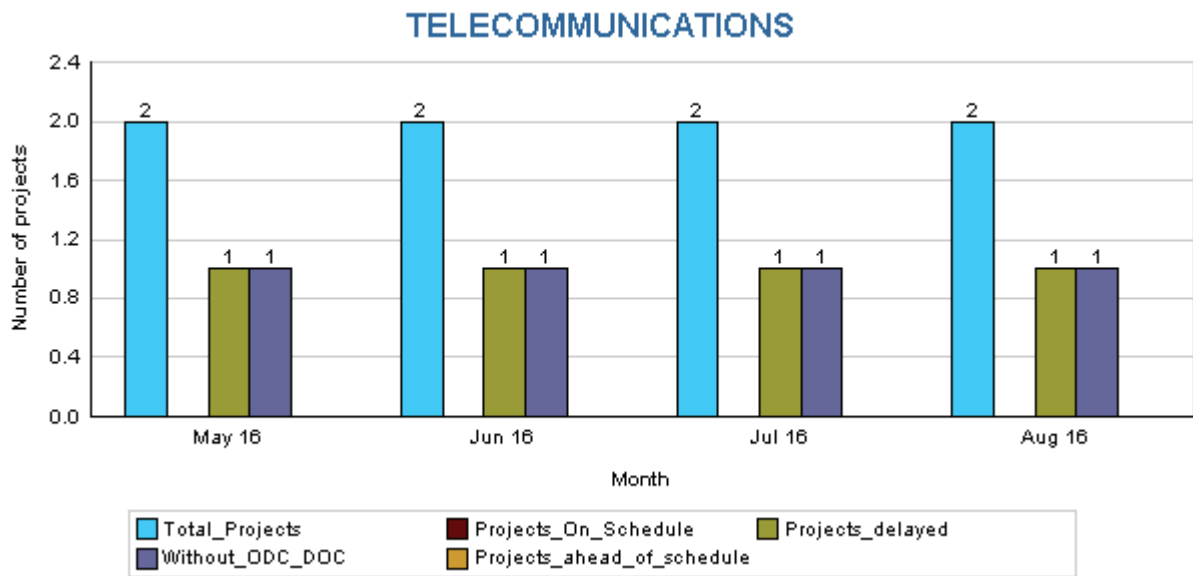


Break-up of 1 Delayed projects in August 2016




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

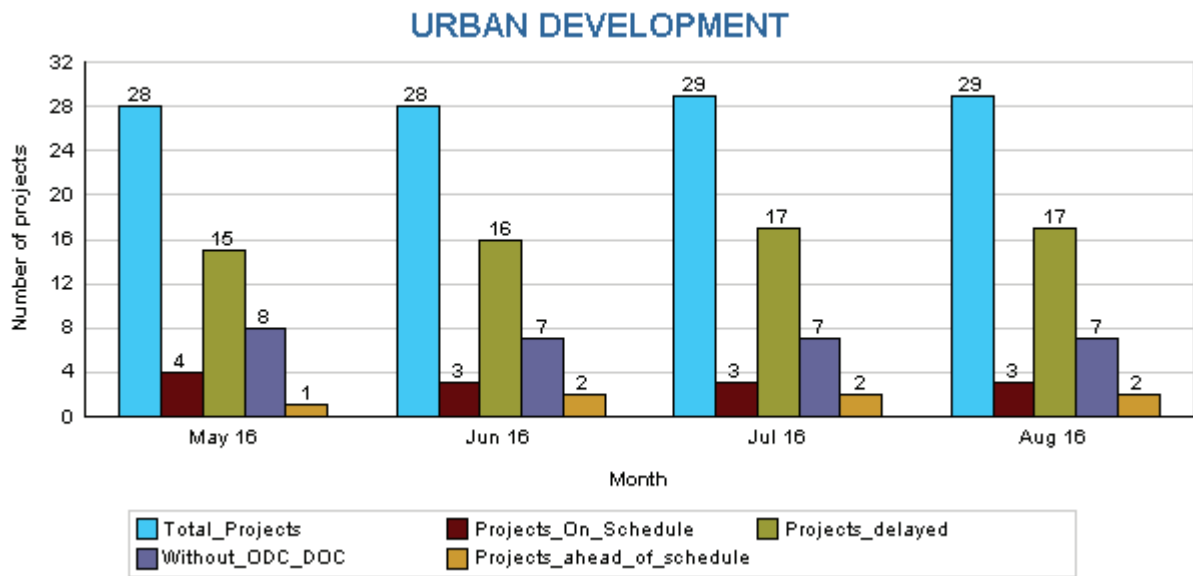

Break-up of 17 Delayed projects in August 2016

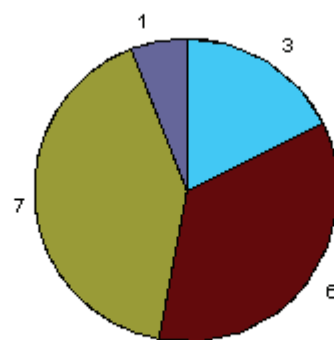

Projects

Delay in Months



Sector wise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	44,541.00	51,918.00	42,385.12
CIVIL AVIATION	4	1,177.28	1,177.28	1,186.17	797.73
COAL	88	68,729.81	68,956.98	70,406.76	14,791.30
FERTILISERS	2	680.64	692.29	692.29	113.81
MINES	3	2,555.63	2,555.63	1,875.63	459.84
STEEL	34	57,600.51	57,981.48	57,771.82	33,361.78
PETROCHEMICALS	1	5,460.61	9,965.00	9,965.00	9,895.57
PETROLEUM	80	136,063.71	135,996.03	137,688.98	45,924.48
POWER	117	331,536.75	362,207.70	380,903.08	200,112.78
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	2,563.15	1,296.39
RAILWAYS	360	358,611.57	396,917.50	452,613.73	105,447.51
ROAD TRANSPORT AND HIGHWAYS	425	272,789.46	274,664.54	275,538.97	114,247.72
SHIPPING AND PORTS	8	4,117.75	5,048.08	5,085.02	2,531.03
TELECOMMUNICATIONS	2	15,445.17	15,445.17	15,345.17	301.57
URBAN DEVELOPMENT	29	133,984.49	141,479.87	143,123.47	56,625.78
Grand total	1167	1,433,476.53	1,521,909.70	1,610,504.54	630,581.41

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU ,	12/2001	13,171.00 17,270.00	22,462.00	21,749.00	12/2008 10/2013	05/2016	-	63/102
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	5,677.00	5,264.12	09/2010 09/2016	10/2017	85(O) 13(R)	12/88
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	11,459.00	8,782.00	12/2015 11/2016	11/2018	35(O) 24(R)	43/70
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	6,590.00	12/2016 03/2017	12/2019	36(O) 33(R)	30/69
	Total		40,442.00 -	51,918.00	42,385.12				148/329
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA ,	05/2010	335.61 -	318.00	305.59	05/2012 -	03/2015	-	0/0
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE ,	10/2012	217.60 -	244.10	30.74	03/2015 -	09/2015	-	0/0
7	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	309.46	435.10	01/2011 -	09/2017	80(O) -	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS ,	10/2013	314.61 -	314.61	26.30	09/2018 -	09/2018	0(O) -	0/0
	Total		1,177.28 -	1,186.17	797.73				0/0
	COAL								
9	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA ,	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	319.40	03/2010 -	03/2017	84(O) -	8/10
11	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,093.73	03/2023 -	03/2023	0(O) -	11/16
12	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND ,	12/2007	341.63 -	341.63	121.94	03/2011 -	03/2017	72(O) -	2/5
13	KUMMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 7,612.33	7,612.33	840.32	03/2023 03/2023	03/2023	0(O) 0(R)	2/18
14	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	79.50	07/2012 03/2017	03/2021	104(O) 48(R)	1/3
15	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA ,	12/2009	212.34 -	1,228.39	888.70	03/2013 -	03/2016	-	21/22
16	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	249.03	121.47	03/2012 -	03/2018	72(O) -	32/42
17	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	193.77	03/2022 -	03/2022	0(O) -	4/8

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 486.57	486.57	204.72	03/2012 03/2018	03/2017	60(O) -12(R)	1/1
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	182.37	03/2010 -	03/2019	108(O) -	2/4
20	PELMA OCP(15.00MTY) - [N06000045]SECL,MADHYA PRADESH ,	11/2014	1,624.59 1,624.59	1,624.59	5.53	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
21	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	122.11	12/2012 -	03/2017	51(O) -	11/44
22	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	1,186.64	13.00	03/2023 -	03/2023	0(O) -	2/10
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	84.21	03/2014 -	03/2017	36(O) -	4/6
24	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	154.15	03/2020 -	03/2020	0(O) -	5/13
25	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	208.48	03/2012 -	03/2019	84(O) -	4/5
26	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.63	188.94	03/2013 -	03/2019	72(O) -	4/8
27	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 -	459.59	35.44	03/2015 -	03/2020	60(O) -	1/7
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	4.40	03/2014 -	03/2020	72(O) -	1/7
29	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132(O) -	0/2
30	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	87.72	03/2015 -	03/2017	24(O) -	8/31
31	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	167.29	03/2012 -	03/2017	60(O) -	5/6
32	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	197.83	03/2014 -	03/2018	48(O) -	1/3
33	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	138.67	03/2016 -	03/2018	24(O) -	4/7
34	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2018	84(O) -	1/3
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,	12/2007	179.87 -	179.87	96.01	03/2012 -	03/2017	60(O) -	1/3
36	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND ,	07/2008	210.98 -	210.98	152.14	03/2013 -	03/2017	48(O) -	1/3
37	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	147.95	03/2012 -	03/2018	72(O) -	1/3
38	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2018	24(O) -	1/4
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	72.47	03/2014 -	03/2017	36(O) -	1/2
40	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	242.29	0.09	03/2015 -	03/2018	36(O) -	0/5
41	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 1,131.28	1,131.28	330.34	03/2018 -	03/2018	0(O) -	6/9
42	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36(O) -	4/29

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	447.06	85.36	03/2015 -	03/2018	36(O) -	4/13
44	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	03/2017	35(O) -	4/7
45	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	123.92	03/2016 -	03/2018	24(O) -	3/6
46	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	39.49	06/2015 -	03/2017	21(O) -	15/36
47	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	417.33	32.46	07/2016 -	03/2019	32(O) -	6/28
48	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	486.27	92.33	03/2016 -	03/2018	24(O) -	22/39
49	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	110.96	03/2020 -	03/2020	0(O) -	2/4
50	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	-	03/2022 -	03/2022	0(O) -	1/7
51	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.36	03/2021 -	03/2017	-48(O) -	0/2
52	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	90.59	03/2020 -	03/2020	0(O) -	3/6
53	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	14.84	03/2019 -	03/2019	0(O) -	1/9
54	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	621.84	03/2026 -	03/2026	0(O) -	3/15
55	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	1.27	03/2019 -	03/2019	0(O) -	2/6
56	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
57	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	338.55	03/2021 -	03/2021	0(O) -	1/9
58	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	249.04	03/2020 -	03/2020	0(O) -	3/9
59	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	112.08	03/2021 -	03/2021	0(O) -	4/12
60	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	178.29	03/2018 -	03/2018	0(O) -	3/8
61	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	187.94	59.62	03/2023 -	03/2023	0(O) -	6/10
62	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
63	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	34.55	03/2018 -	03/2018	0(O) -	1/5
64	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	111.94	03/2021 -	03/2021	0(O) -	0/7
65	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	27.56	03/2021 -	03/2021	0(O) -	1/6
66	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	85.12	03/2019 -	03/2019	0(O) -	7/13
67	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	397.09	0.30	03/2019 -	03/2019	0(O) -	5/18
68	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	57.02	03/2020 -	03/2020	0(O) -	3/10

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
69	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	57.98	03/2021 -	03/2021	0(O) -	3/8
70	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	81.73	03/2025 -	03/2025	0(O) -	3/13
71	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
72	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	0/6
73	AMGAON OPENCASST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	17.60	03/2020 -	03/2020	0(O) -	0/5
74	DURGAPUR OPENCASST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	-	03/2023 -	03/2023	0(O) -	1/9
75	MALACHUA OPENCASST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	-	03/2023 -	03/2023	0(O) -	0/8
76	MADANNAGAR OPENCASST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/4
77	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	277.65	-	03/2021 -	03/2021	0(O) -	2/8
78	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	0.27	03/2020 -	03/2020	0(O) -	1/6
79	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022	0(O) -	0/21
80	KOYAGUDEM OPENCASST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2018	0(O) -	0/11
81	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	0/17
82	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	108.64	03/2021 -	03/2021	0(O) -	0/1
83	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	1.95	03/2019 -	03/2019	0(O) -	1/9
84	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	103.25	03/2019 -	03/2018	-12(O) -	1/8
85	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	2,503.92	12/2015 04/2018	04/2018	28(O) 0(R)	13/35
86	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	54.30	04/2015 -	04/2019	48(O) -	1/6
87	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	04/2017	0(O) -	0/3
88	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	207.09	03/2017 -	05/2018	14(O) -	11/11
89	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 -	1,458.17	82.49	06/2015 08/2019	08/2019	50(O) 0(R)	1/7
90	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	244.64	03/2018 -	09/2018	6(O) -	5/15
91	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	2.57	09/2019 -	09/2019	0(O) -	0/0
92	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU ,	04/2012	364.75 -	364.75	229.14	10/2014 -	10/2016	24(O) -	8/10
93	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	122.07	05/2014 -	10/2016	29(O) -	0/8

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
94	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA ,	12/2007	457.77 -	457.77	278.09	03/2013 -	11/2018	68(O) -	8/9
95	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND ,	10/2012	269.82 -	269.82	86.46	04/2014 -	11/2016	31(O) -	0/10
96	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	74.76	12/2019 -	12/2019	0(O) -	0/0
	Total		68,729.81 -	70,406.76	14,791.30				319/987
	<u>FERTILISERS</u>								
97	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA ,	10/2014	197.79 209.44	209.44	75.85	11/2016 09/2017	09/2017	10(O) 0(R)	0/0
98	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF, MAHARASHTRA ,	02/2016	482.85 482.85	482.85	37.96	12/2017 -	12/2017	0(O) -	0/1
	Total		680.64 -	692.29	113.81				0/1
	<u>MINES</u>								
99	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL, MADHYA PRADESH ,	09/2011	1,856.00 -	1,176.00	15.48	09/2017 -	04/2020	31(O) -	0/0
100	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT JATH SANGLI MA ARASHTRA - [N10000008]NALCO, MAHARASHTRA , Private	12/2015	355.13 355.13	355.13	243.19	11/2016 11/2016	11/2016	0(O) 0(R)	0/5
101	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO, RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 344.50	344.50	201.17	11/2016 11/2016	11/2016	0(O) 0(R)	0/0
	Total		2,555.63 -	1,875.63	459.84				0/5
	<u>STEEL</u>								
102	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL, ANDHRA PRADESH ,	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
103	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND ,	10/2013	245.67 -	245.67	160.88	05/2016 -	03/2017	10(O) -	1/3
104	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH ,	07/2011	974.76 -	974.76	412.53	07/2016 -	03/2017	8(O) -	1/1
105	TURBO BLOWER - 5 - [N12000092]RINL, ANDHRA PRADESH ,	12/2009	280.00 -	280.00	72.17	09/2016 -	03/2017	6(O) -	1/1
106	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL, JHARKHAND ,	03/2015	255.19 -	255.19	53.47	03/2018 -	03/2018	0(O) -	0/1
107	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA ,	03/2007	149.73 173.00	175.94	178.91	12/2015 -	03/2017	15(O) -	0/0
108	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL, KARNATAKA ,	05/2005	768.88 1,070.97	1,070.97	1,070.97	02/2014 -	03/2016	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
109	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN ,	05/2015	189.00 -	189.00	-	03/2017 -	03/2017	0(O) -	0/0
110	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR ,	10/2005	956.00 -	956.00	650.45	03/2015 -	03/2017	24(O) -	0/0
111	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL, JHARKHAND ,	12/2007	200.00 -	200.00	136.65	03/2018 -	03/2018	0(O) -	0/0
112	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL, WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	03/2016	-	0/0
113	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA ,	04/2015	3,127.30 -	3,127.30	380.84	04/2018 -	04/2018	0(O) -	0/2
114	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL, KARNATAKA ,	07/2011	324.87 - 324.87	324.87	263.57	12/2015 -	04/2016	-	0/0
115	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL, JHARKHAND ,	04/2013	170.00 -	170.00	91.91	04/2018 -	04/2018	0(O) -	0/0
116	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL, JHARKHAND ,	12/2007	253.92 - 253.92	253.92	194.97	06/2016 -	06/2016	-	0/0
117	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC, CHHATISGARH ,	11/2015	818.00 -	818.00	2.44	06/2020 -	06/2020	0(O) -	1/11
118	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA ,	10/2011	175.49 - 206.71	206.71	141.17	12/2016 -	07/2017	7(O) -	0/0
119	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA ,	12/2011	187.33 -	187.33	180.35	10/2013 -	09/2016	35(O) -	2/5
120	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH ,	05/2012	404.16 -	404.16	344.45	07/2015 -	09/2017	26(O) -	0/1
121	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH ,	12/2009	343.00 -	488.40	104.50	10/2016 -	09/2017	11(O) -	0/0
122	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL, JHARKHAND ,	02/2014	4,749.00 -	4,749.00	17.32	09/2017 -	09/2017	0(O) -	0/0
123	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL, MEGHALAYA ,	04/2014	151.33 -	151.33	15.04	09/2017 -	09/2017	0(O) -	0/0
124	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	27.47	09/2018 -	09/2018	0(O) -	0/0
125	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA ,	06/2014	708.91 -	708.91	490.16	04/2016 -	10/2016	6(O) -	1/3
126	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND ,	03/2015	1,034.01 -	1,034.01	66.80	10/2017 -	10/2017	0(O) -	0/2
127	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH ,	07/2011	877.73 -	877.73	589.13	07/2015 -	11/2016	16(O) -	2/2
128	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH ,	08/2010	17,265.00 -	17,265.00	16,513.62	03/2013 -	12/2016	45(O) -	33/37

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
129	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH ,	01/2010	15,525.00	15,525.00	10,082.02	05/2015 12/2017	12/2017	31(O) 0(R)	38/81
130	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND ,	05/2015	1,154.18	1,154.18	116.30	12/2017 -	12/2017	0(O) -	0/2
131	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA ,	12/2007	202.61 227.00	227.00	200.20	12/2016 -	12/2016	0(O) -	0/0
132	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL, GUJARAT ,	01/2013	175.00	175.00	-	- -	12/2017	- -	0/0
133	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND ,	02/2014	787.29	787.29	328.23	12/2016 -	12/2016	0(O) -	0/0
134	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH ,	12/2011	2,858.00	2,500.00	209.43	12/2017 -	12/2017	0(O) -	0/0
135	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH ,	04/2014	188.93	188.93	87.53	04/2015 -	12/2016	20(O) -	2/4
	Total		57,600.51	57,771.82	33,361.78				82/156
	<u>PETROCHEMICALS</u>								
136	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM ,	04/2006	5,460.61 9,965.00	9,965.00	9,895.57	04/2012 12/2015	-	-	25/26
	Total		5,460.61	9,965.00	9,895.57				25/26
	<u>PETROLEUM</u>								
137	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]JSPL, KARNATAKA ,	01/2006	732.00	1,227.00	1,158.24	10/2011 -	04/2016	-	0/0
138	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU ,	05/2013	711.00	711.00	10.29	- -	-	-	0/0
139	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU ,	11/2006	171.83	171.83	-	- -	-	-	0/0
140	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE ,	01/2015	1,823.00	1,823.00	5.82	- -	-	-	0/0
141	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL, MULTI STATE ,	01/2015	2,321.00	2,321.00	11.70	- -	-	-	0/0
142	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE ,	02/2015	890.00	890.00	7.86	- -	-	-	0/0
143	DIESEL HYDROTREATOR - [N16000207]NRL, ASSAM , Central Sector Projects	07/2015	1,031.37	1,031.37	80.29	01/2018 -	01/2018	0(O) -	33/61
144	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN ,	11/2011	310.00 370.00	370.00	-	03/2013 01/2017	01/2017	46(O) 0(R)	0/27
145	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH , Central Sector Projects	03/2009	181.02	173.28	104.89	01/2017 -	01/2017	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
146	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL, ASSAM ,	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30(O) -	0/12
147	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA ,	10/2015	607.06 714.25	714.25	108.81	10/2017 -	02/2018	4(O) -	21/52
148	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	1,970.53	11/2015 11/2016	02/2017	15(O) 3(R)	48/52
149	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	231.02	02/2020 -	02/2020	0(O) -	0/0
150	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU ,	11/2012	678.00 -	678.00	-	02/2017 -	02/2017	0(O) -	0/0
151	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM ,	03/2009	2,465.15 2,378.89	2,378.89	1,879.11	03/2013 03/2017	03/2017	48(O) 0(R)	5/15
152	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE ,	06/2007	736.65 -	736.65	517.01	09/2011 10/2016	03/2017	66(O) 5(R)	0/0
153	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA ,	12/2009	1,584.00 -	1,584.00	1,465.03	03/2017 03/2017	03/2017	0(O) 0(R)	3/12
154	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,350.72	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
155	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA ,	03/2012	2,592.17 2,592.17	2,592.17	1,426.00	05/2014 03/2017	03/2017	34(O) 0(R)	0/21
156	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE ,	04/2012	600.17 600.17	600.17	375.14	12/2014 03/2018	03/2018	39(O) 0(R)	0/8
157	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE ,	02/2011	913.00 -	913.00	-	08/2015 -	03/2018	31(O) -	0/0
158	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE ,	12/2009	309.81 462.79	462.79	303.92	10/2014 03/2017	03/2017	29(O) 0(R)	28/40
159	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL ,	03/2014	3,076.00 -	3,076.00	507.53	09/2017 03/2018	03/2018	6(O) 0(R)	1/7
160	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL, ODISHA ,	03/2014	3,150.00 -	3,150.00	378.78	09/2017 -	03/2018	6(O) -	2/6
161	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA ,	11/2014	6,068.80 -	6,068.80	1,899.13	04/2019 -	03/2019	-1(O) -	0/0
162	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU ,	05/2015	257.87 -	257.87	69.50	11/2016 -	03/2017	4(O) -	16/22
163	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
164	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL, GUJARAT , Central Sector Projects	11/2015	500.00 -	500.00	-	03/2017 -	03/2017	0(O) -	0/0
165	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL, GUJARAT ,	07/2014	199.95 -	199.95	62.19	03/2018 -	03/2018	0(O) -	13/22
166	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC, GUJARAT ,	09/2011	202.25 -	160.16	89.64	07/2016 -	04/2017	9(O) -	5/12
167	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,190.69	83.38	04/2018 -	04/2018	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
168	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects	02/2016	367.11 -	367.11	19.42	04/2017 -	04/2017	0(O) -	15/22
169	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219]BPCL,MAHARASHTRA ,	08/2014	393.00 -	393.00	-	04/2018 -	04/2018	0(O) -	0/0
170	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU ,	08/2014	393.00 -	393.00	93.83	04/2018 -	04/2018	0(O) -	0/0
171	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	327.78	-	04/2018 -	04/2018	0(O) -	0/0
172	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE ,	04/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
173	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA ,	06/2014	5,706.47 5,813.25	5,813.25	4,309.00	05/2017 05/2017	05/2017	0(O) 0(R)	7/16
174	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 -	6,086.08	1,221.41	05/2019 05/2019	05/2019	0(O) 0(R)	0/0
175	PIPELINE REPLACEMENT PROJECT - 4 - [N16000203]ONGC,MAHARASHTRA ,	02/2015	2,899.93 2,098.43	2,098.43	1,263.13	05/2017 -	05/2017	0(O) -	0/0
176	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	6.92	05/2019 -	05/2019	0(O) -	0/13
177	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]IOIL,MULTI STATE ,	07/2011	352.56 -	439.03	1.57	03/2017 06/2018	06/2018	15(O) 0(R)	0/0
178	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT ,	12/2011	160.00 -	160.00	119.42	02/2016 07/2016	07/2016	-	4/4
179	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020	0(O) -	0/0
180	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]IOIL,MULTI STATE ,	04/2010	270.00 -	251.66	172.53	06/2012 08/2016	08/2016	50(O) 0(R)	0/0
181	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA ,	03/2014	238.50 -	238.50	38.87	03/2017 -	08/2017	5(O) -	3/6
182	BULK PETROLEUM OIL AND LUBRICANT (POL) DEPOT AT IMPHAL, MANIPUR - [N16000215]IOCL,MANIPUR , Central Sector Projects	08/2010	103.02 171.04	171.04	122.29	07/2016 08/2016	08/2016	1(O) 0(R)	10/10
183	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT ,	03/2009	317.64 -	240.95	150.26	09/2012 09/2016	09/2016	48(O) 0(R)	2/5
184	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA ,	03/2012	16,504.00 -	16,504.00	11,986.69	05/2016 -	09/2016	4(O) -	0/16
185	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,493.81	01/2012 -	09/2016	56(O) -	0/0
186	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH ,	01/2011	141.86 -	232.00	183.99	09/2016 -	09/2016	0(O) -	0/12
187	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH ,	07/2014	419.04 -	419.04	366.03	01/2017 -	09/2016	-4(O) -	13/16
188	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	195.63	81.86	09/2018 -	09/2018	0(O) -	0/0
189	NEW 250 TMTPA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL ,	08/2014	190.45 -	190.45	58.20	09/2017 -	09/2017	0(O) -	0/0
190	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE ,	12/2009	463.32 -	463.32	357.01	06/2011 10/2016	10/2016	64(O) 0(R)	13/20

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
191	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR ,	04/2013	480.00 -	422.00	288.40	02/2016 10/2016	10/2016	8(O) 0(R)	5/6
192	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221]BPCL,MAHARASHTRA ,	01/1991	694.00 -	694.00	57.19	10/2018 -	10/2018	0(O) -	0/0
193	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 -	694.00	62.87	10/2018 -	10/2018	0(O) -	0/0
194	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA ,	02/2012	666.00 838.08	838.08	648.51	11/2015 11/2016	11/2016	12(O) 0(R)	27/29
195	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
196	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	07/2009	3,957.00 3,561.00	3,561.00	243.81	01/2013 12/2018	12/2018	71(O) 0(R)	15/38
197	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,532.49	12/2016 -	12/2016	0(O) -	6/7
198	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,256.72	1,256.72	1,056.23	05/2013 12/2016	12/2016	43(O) 0(R)	1/5
199	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE ,	01/2012	352.49 -	352.49	187.62	03/2014 05/2016	12/2016	33(O) 7(R)	0/3
200	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE ,	08/2011	586.00 -	586.00	502.33	08/2015 12/2016	12/2016	16(O) 0(R)	3/12
201	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA ,	03/2013	1,138.50 686.58	686.58	654.96	04/2015 05/2016	12/2016	20(O) 7(R)	0/0
202	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE ,	05/2013	4,124.35 4,124.35	4,124.35	1,022.55	04/2016 12/2017	12/2017	20(O) 0(R)	0/3
203	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	123.11	05/2015 -	12/2016	19(O) -	0/12
204	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM ,	03/2009	228.64 -	214.19	141.59	12/2016 -	12/2016	0(O) -	0/0
205	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5(O) -	1/38
206	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE ,	10/2011	725.00 -	725.00	327.87	11/2016 -	12/2016	1(O) -	0/12
207	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA ,	05/2015	2,443.00 -	2,443.00	290.83	12/2017 -	12/2017	0(O) -	0/0
208	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	1,382.08	12/2017 -	12/2017	0(O) -	0/0
209	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	4.91	02/2019 -	12/2018	-2(O) -	1/10
210	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220]BPCL,MAHARASHTRA ,	02/2015	184.00 -	184.00	12.43	12/2017 -	12/2017	0(O) -	0/0
211	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA ,	02/2015	184.00 -	184.00	28.56	06/2017 -	12/2017	6(O) -	0/0
212	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	1,427.94	0.86	12/2018 -	12/2018	0(O) -	5/21

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
213	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM ,	09/2012	871.35 -	1,200.00	696.37	03/2015 -	12/2016	21(O) -	0/5
214	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC, ASSAM ,	06/2010	202.94 -	202.94	2.95	01/2014 -	-	-	0/2
215	LPG MARKETING TERMINAL, PARADIP - [N16000174]IOCL, ODISHA ,	09/2012	158.91 -	158.91	-	03/2015 -	-	-	1/1
216	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA ,	11/2014	4,588.29 -	4,588.29	365.19	05/2018 -	08/2018	3(O) -	0/0
	Total		136,063.71 -	137,688.98	45,924.48				307/735
	POWER								
217	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI - II HEP - [180100261]PGCIL, HIMACHAL PRADESH ,	12/2005	358.42 -	358.42	-	12/2008 09/2010	-	-	0/15
218	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA ,	07/2009	421.01 1,007.57	1,007.57	972.11	07/2013 -	-	-	25/26
219	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL, ANDHRA PRADESH ,	03/2012	206.44 -	206.44	-	06/2014 -	-	-	11/20
220	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL, MULTI STATE ,	04/2016	810.48 -	810.48	-	- -	-	-	0/0
221	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,761.00	09/2016 01/2017	01/2017	4(O) 0(R)	35/40
222	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE ,	03/2016	808.63 -	808.63	0.10	01/2018 -	01/2018	0(O) -	0/0
223	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH ,	03/2012	9,569.76 -	9,569.76	6,460.99	06/2015 -	02/2017	20(O) -	21/30
224	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL, MULTI STATE ,	08/2014	288.49 -	288.49	127.90	02/2017 -	02/2017	0(O) -	1/12
225	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL, ANDHRA PRADESH ,	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	2/2
226	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND ,	02/2014	14,366.58 -	14,366.58	3,267.00	02/2019 02/2020	02/2020	12(O) 0(R)	14/18
227	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH ,	05/2011	195.42 -	195.42	77.96	02/2014 -	02/2018	48(O) -	1/3
228	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, MAHARASHTRA ,	12/2007	477.69 738.48	738.48	605.39	09/2010 01/2016	03/2017	78(O) 14(R)	4/8
229	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE ,	10/2008	4,824.12 -	4,824.12	4,334.48	10/2012 -	03/2017	53(O) -	7/11

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
230	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N1800077]PGCIL, WEST BENGAL ,	04/2010	4,404.57 -	4,404.57	2,945.15	01/2015 -	03/2017	26(O) -	8/16
231	SYSTEM STRENGTHENING XII OF SR - [N1800085]PGCIL, MULTI STATE ,	02/2010	232.34 -	232.34	220.89	06/2012 -	03/2017	57(O) -	1/4
232	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N1800099]PGCIL, MULTI STATE ,	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	03/2016	-	11/12
233	SYSTEM STRENGTHENING XIII OF SR GRID - [N1800109]PGCIL, MULTI STATE ,	10/2011	487.49 639.46	639.46	452.92	06/2014 03/2016	03/2017	33(O) 12(R)	10/12
234	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N1800114]PGCIL, GUJARAT ,	12/2011	552.44 609.44	609.44	501.60	02/2014 03/2016	03/2016	-	10/10
235	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N1800116]PGCIL, CHHATTISGARH ,	12/2011	1,746.65 2,228.71	2,228.71	1,672.23	08/2014 12/2015	03/2017	31(O) 15(R)	7/11
236	EASTERN REGION STRENGTHENING SCHEME-V - [N1800155]PGCIL, MULTI STATE ,	10/2013	1,364.52 -	1,364.52	904.84	04/2016 -	03/2017	11(O) -	8/12
237	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N1800157]PGCIL, MULTI STATE ,	01/2014	374.63 -	374.63	29.70	04/2016 -	03/2017	11(O) -	0/0
238	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N1800158]PGCIL, MULTI STATE ,	02/2014	539.82 -	539.82	219.30	06/2016 -	03/2017	9(O) -	8/11
239	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N1800159]PGCIL, MULTI STATE ,	02/2014	908.08 -	908.08	465.80	06/2016 -	03/2017	9(O) -	10/18
240	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N1800168]PGCIL, MULTI STATE ,	06/2014	5,151.37 -	5,151.37	881.40	03/2018 -	03/2018	0(O) -	8/12
241	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N1800172]CVPPPL, JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	360.55	04/2020 -	03/2022	23(O) -	0/0
242	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N1800174]NTPC, UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	1,589.00	12/2016 03/2017	03/2017	3(O) 0(R)	20/22
243	TANDA TPP STAGE-II (2X660 MW) - [N1800175]NTPC, UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	1,718.00	03/2019 -	03/2019	0(O) -	16/17
244	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N1800180]PGCIL, MULTI STATE ,	01/2015	268.80 -	268.80	60.30	03/2018 -	03/2018	0(O) -	0/3
245	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N1800184]PGCIL, MULTI STATE ,	03/2015	197.40 -	197.40	5.70	03/2018 -	03/2018	0(O) -	0/0
246	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N1800186]PGCIL, ANDHRA PRADESH ,	03/2015	550.06 -	550.06	62.60	03/2018 -	03/2018	0(O) -	0/3
247	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N1800191]NTPC, BIHAR ,	03/2010	3,984.03 -	3,984.03	3,413.45	01/2013 -	03/2016	-	1/1
248	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N1800202]DVC, WEST BENGAL ,	04/2007	4,122.00 8,781.30	9,606.82	8,483.49	02/2011 -	03/2016	-	26/26
249	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N1800206]PGCIL, MADHYA PRADESH ,	01/2016	305.04 -	305.04	17.90	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
250	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE ,	06/2014	400.47 -	400.47 -	180.40	04/2017 -	04/2017	0(O) -	1/3
251	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE ,	12/2014	6,517.36 -	6,517.36 -	935.60	04/2018 -	04/2018	0(O) -	3/12
252	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61 -	702.80	04/2018 -	04/2018	0(O) -	4/9
253	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE ,	04/2015	1,479.30 -	1,479.30 -	322.50	04/2017 -	04/2017	0(O) -	2/8
254	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL ,	01/1991	454.11 -	454.11 -	-	04/2018 -	04/2018	0(O) -	0/0
255	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA ,	04/2016	844.64 -	844.64 -	-	04/2019 -	04/2019	0(O) -	0/0
256	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	12,000.00	01/2011 05/2018	05/2018	88(O) 0(R)	27/48
257	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH ,	12/2008	573.99 1,581.04	1,581.04	1,275.79	08/2013 05/2017	05/2017	45(O) 0(R)	31/38
258	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE ,	01/2015	3,662.02 -	3,662.02 -	1,006.50	05/2018 -	05/2018	0(O) -	0/5
259	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52 -	1.70	05/2017 -	05/2017	0(O) -	0/9
260	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU ,	01/2016	162.11 -	162.11 -	3.50	05/2018 -	05/2018	0(O) -	0/0
261	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA ,	05/2016	364.60 -	364.60 -	-	05/2018 -	05/2018	0(O) -	0/0
262	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59 -	-	05/2019 -	05/2019	0(O) -	0/0
263	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 3,846.30	3,846.30	2,944.00	03/2013 06/2019	06/2019	75(O) 0(R)	3/15
264	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 6,749.18	6,749.18	6,187.00	09/2011 06/2017	06/2017	69(O) 0(R)	22/37
265	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,368.30	12/2012 12/2016	06/2017	54(O) 6(R)	11/23
266	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,308.43	11/2012 03/2016	06/2017	55(O) 15(R)	10/13
267	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 -	2,514.88 -	1,415.35	12/2015 -	06/2017	18(O) -	15/18
268	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR ,	01/2013	12,964.60 -	12,964.60 -	7,093.73	01/2018 -	06/2018	5(O) -	23/31
269	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL, ODISHA ,	01/2016	187.04 -	187.04 -	5.90	06/2018 -	06/2018	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
270	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	-	06/2018 -	06/2018	0(O) -	0/0
271	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 -	790.13	-	06/2018 -	06/2018	0(O) -	0/0
272	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	15,166.19	11,603.00	01/2017 07/2017	07/2017	6(O) 0(R)	32/46
273	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	203.28	42.80	07/2017 -	07/2017	0(O) -	0/5
274	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	0.70	09/2017 -	07/2018	10(O) -	0/0
275	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	0.90	07/2017 -	07/2017	0(O) -	0/0
276	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	89.30	07/2018 -	07/2018	0(O) -	0/0
277	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT ,	01/2016	244.19 -	244.19	-	07/2018 -	07/2018	0(O) -	0/0
278	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	32.40	07/2018 -	07/2018	0(O) -	0/0
279	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH ,	01/2016	207.88 -	207.88	4.00	07/2018 -	07/2018	0(O) -	0/0
280	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	175.00	07/2020 -	07/2020	0(O) -	4/4
281	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	6,764.00	11/2016 08/2017	08/2017	9(O) 0(R)	29/35
282	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE ,	09/2012	524.40 -	524.40	367.82	05/2015 -	08/2016	15(O) -	11/12
283	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017	0(O) -	0/9
284	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	12,532.44	3,925.00	08/2018 -	08/2018	0(O) -	19/22
285	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	2,978.86	1,845.71	02/2016 09/2019	09/2019	43(O) 0(R)	13/23
286	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE ,	05/2010	250.03 390.51	390.51	266.70	01/2013 03/2016	09/2016	44(O) 6(R)	13/15
287	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM ,	07/1998	368.72 1,441.52	1,441.52	1,066.32	07/2006 09/2017	09/2017	134(O) 0(R)	5/13
288	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE ,	02/2012	3,201.44 -	3,201.44	3,426.91	10/2014 -	09/2016	23(O) -	13/17
289	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	11,846.00	6,807.00	06/2017 09/2017	09/2017	3(O) 0(R)	25/40
290	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	11,638.55	6,210.00	09/2017 -	09/2017	0(O) -	21/41

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
291	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA ,	02/2014	167.40 -	167.40	113.00	12/2015 -	09/2016	9(O) -	6/8
292	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	210.00	09/2019 -	09/2019	0(O) -	4/6
293	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	5,353.00	5,760.32	05/2014 03/2017	09/2017	40(O) 6(R)	1/4
294	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH ,	04/2012	9,750.89 -	9,750.89	5,529.80	12/2016 -	09/2017	9(O) -	26/32
295	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	9,870.51	1,794.00	09/2019 -	09/2019	0(O) -	14/14
296	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	1,788.41	-	09/2017 -	09/2017	0(O) -	0/0
297	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	4,715.05	12/2009 10/2017	10/2017	94(O) 0(R)	16/30
298	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE ,	07/2010	752.64 689.03	689.03	576.22	07/2013 11/2015	10/2016	39(O) 11(R)	7/9
299	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH ,	05/2011	1,961.87 2,310.58	2,310.58	1,840.05	05/2014 06/2016	10/2016	29(O) 4(R)	8/12
300	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE ,	03/2012	198.63 -	198.63	112.53	09/2014 -	10/2016	25(O) -	0/0
301	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE ,	09/2013	680.69 -	680.69	524.59	03/2016 -	10/2016	7(O) -	10/12
302	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 -	155.57	34.50	03/2016 -	10/2016	7(O) -	2/6
303	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT ,	02/2014	378.71 -	378.71	170.30	10/2016 -	10/2016	0(O) -	8/11
304	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	65.40	10/2017 -	10/2017	0(O) -	0/5
305	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND ,	08/2006	2,313.00 4,138.41	4,237.67	3,645.88	12/2011 03/2016	10/2016	58(O) 7(R)	13/14
306	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL,GUJARAT ,	10/2015	315.00 -	315.00	256.02	10/2016 -	10/2016	0(O) -	2/2
307	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE ,	02/2009	509.66 -	509.66	593.76	11/2011 -	11/2016	60(O) -	8/11
308	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE ,	12/2009	1,216.83 1,428.87	1,428.87	1,082.49	08/2012 09/2016	11/2016	51(O) 2(R)	3/5
309	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 -	522.29	235.70	11/2016 -	11/2016	0(O) -	2/12
310	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE ,	11/2014	972.42 -	972.42	236.50	11/2017 -	11/2017	0(O) -	0/3
311	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	35.90	11/2017 -	11/2017	0(O) -	0/0
312	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	-	11/2018 -	11/2018	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
313	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37 -	-	11/2019 -	11/2019	0(O) -	0/0
314	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01 -	-	11/2018 -	11/2019	12(O) -	0/0
315	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75 -	5,871.70	09/2009 -	12/2018	111(O) -	2/3
316	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	1,908.55	11/2008 01/2016	12/2017	109(O) 23(R)	20/22
317	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	2,491.58 -	866.49	06/2013 -	12/2019	78(O) -	6/11
318	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,037.00	08/2013 12/2017	12/2017	52(O) 0(R)	19/26
319	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 -	1,940.13 -	2,149.36	09/2014 -	12/2016	27(O) -	8/13
320	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH ,	11/2011	2,127.51 2,619.56	2,619.56	2,442.83	07/2014 06/2016	12/2016	29(O) 6(R)	6/8
321	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 346.79	346.79	319.67	08/2014 06/2015	12/2016	28(O) 18(R)	8/10
322	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH ,	01/2012	1,422.85 1,875.13	1,875.13	1,613.12	01/2015 06/2016	12/2016	23(O) 6(R)	9/11
323	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE ,	11/2011	723.63	723.63	639.72	11/2014 -	12/2016	25(O) -	7/10
324	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE ,	03/2013	514.20 -	514.20 -	399.80	06/2015 -	12/2016	18(O) -	7/10
325	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE ,	06/2012	1,909.24 -	1,909.24 -	1,182.53	06/2015 -	12/2016	18(O) -	3/5
326	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE ,	09/2013	1,575.30 -	1,575.30 -	1,088.60	05/2016 -	12/2016	7(O) -	8/13
327	STATIC VAR COMPENSATORS (SVCs) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE ,	05/2014	829.98 -	829.98 -	276.70	08/2016 -	12/2016	4(O) -	1/4
328	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE ,	05/2014	303.07 -	303.07 -	95.80	07/2016 -	12/2016	5(O) -	3/9
329	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 -	196.58 -	49.40	02/2016 -	12/2016	10(O) -	7/17
330	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN, BIHAR ,	05/2015	436.68 -	436.68 -	447.48	12/2016 -	12/2016	0(O) -	1/6
331	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	17,435.15 -	8,637.42	09/2010 -	-	-	0/0
332	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR ,	01/2009	3,642.04 -	5,783.17 -	4,676.44	01/2016 -	-	-	5/6

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
333	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN ,	02/2015	302.49 302.00	302.49	289.89	02/2016 -	06/2016	-	0/1
	Total		331,536.75 -	380,903.08	200,112.78				852/1307
	<u>HEAVY INDUSTRY</u>								
334	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
335	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	-	0/0
336	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	505.58	70.00	03/2018 -	03/2018	0(O) -	0/0
337	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI ,	11/2013	196.70 -	196.70	197.38	01/2016 -	04/2016	-	0/0
338	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI ,	09/2013	444.70 -	444.70	400.00	12/2015 -	06/2016	-	0/0
339	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	59.29	05/2017 -	06/2017	1(O) -	0/0
340	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	101.00	05/2017 -	06/2017	1(O) -	0/0
341	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	168.90	16.50	05/2017 -	07/2017	2(O) -	0/0
342	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH ,	10/2013	159.50 -	159.50	127.80	11/2013 -	10/2016	35(O) -	0/0
343	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	210.92	11/2013 -	11/2014	-	0/0
	Total		2,563.15 -	2,563.15	1,296.39				0/0
	<u>RAILWAYS</u>								
344	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [Z20100106]SCR,TELANGANA ,	12/1994	124.43 926.23	1,010.00	944.02	- -	-	-	0/0
345	AMRAVATI-NARKHER NL(CR) - [Z20100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	668.34	621.36	06/1999 -	-	-	0/0
346	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [Z20100149]RVNL,CHHATISGARH ,	04/1995	304.00 -	631.78	322.36	12/2012 -	-	-	0/0
347	CALICUT-MANGALORE (DL) (SR) - [Z20100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	532.98	- -	-	-	0/0
348	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [Z20100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	253.55	03/2004 -	-	-	0/0
349	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [Z20100181]CR,MAHARASHTRA ,	02/1997	514.68 2,271.50	2,271.50	841.22	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
350	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	780.98	313.50	-	-	-	0/0
351	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	502.85	07/2012 -	-	-	0/0
352	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 774.90	870.00	845.57	-	-	-	0/0
353	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA ,	04/1997	227.00 -	2,135.00	127.04	-	-	-	0/0
354	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	181.89	03/2007 03/2007	-	-	0/0
355	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND ,	04/1997	194.07 -	335.00	226.39	06/2004 -	-	-	0/0
356	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	125.00 458.26	480.00	3.49	07/2008 -	-	-	0/0
357	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR ,	04/1997	501.69 335.77	1,043.56	891.01	03/2012 -	-	-	0/0
358	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	-	12/2009 -	-	-	0/0
359	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA ,	02/1998	242.42 369.70	1,542.41	959.72	-	-	-	0/1
360	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	541.00	198.17	-	-	-	0/0
361	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 781.02	876.10	842.61	06/2007 -	-	-	0/0
362	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	100.00 712.82	980.00	615.68	-	-	-	0/0
363	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	330.00 1,045.20	2,125.18	39.61	-	-	-	0/0
364	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE ,	04/1998	92.63 -	270.00	318.58	02/2011 -	-	-	0/0
365	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,500.00	614.98	12/2012 12/2012	-	-	0/0
366	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	138.00 1,382.78	1,382.78	4.41	-	-	-	0/0
367	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	301.64 -	1,185.64	-	-	-	-	0/0
368	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	324.66	376.05	-	-	-	0/0
369	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	230.92	-	-	-	0/0
370	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	183.23 -	1,202.70	254.22	02/2015 -	-	-	0/0
371	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 -	811.36	277.84	-	-	-	0/0
372	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH ,	04/2003	136.62 -	376.00	-	12/2007 03/2010	-	-	0/0
373	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTTP,TAMIL NADU ,	04/2006	495.74 722.21	495.74	349.52	06/2013 -	-	-	1/4
374	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	378.56 1,160.47	1,160.47	1.74	-	-	-	0/1
375	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	318.00	288.07	02/2006 -	-	-	0/1

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
376	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	743.00 -	1,825.00	-	03/2008 06/2008	-	-	0/0
377	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	404.19 1,449.72	2,072.50	609.63	- -	-	-	0/0
378	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	969.97	- -	-	-	0/0
379	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	125.00 227.40	490.00	54.91	- -	-	-	0/0
380	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	456.00 582.83	1,080.00	202.02	- -	-	-	0/0
381	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	1,106.62 -	1,106.62	407.13	12/2010 -	-	-	3/7
382	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA ,	04/2007	482.00 874.57	874.57	896.20	03/2013 -	-	-	0/0
383	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	1,655.68	38.99	03/2014 -	-	-	0/0
384	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN ,	04/2008	516.23 732.06	735.00	730.05	03/2014 -	-	-	0/0
385	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL ,	04/2009	533.38 -	533.38	128.07	12/2011 -	-	-	0/0
386	GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL ,	04/2009	611.03 -	611.03	147.31	12/2011 -	-	-	0/0
387	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH ,	03/2013	643.00 -	643.00	-	- -	-	-	0/0
388	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE ,	04/2007	1,347.26 -	1,347.26	313.79	- -	-	-	0/0
389	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT ,	04/2012	376.59 -	644.38	0.11	- -	-	-	0/0
390	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT ,	04/2011	439.88 -	845.68	1.56	- -	-	-	0/0
391	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE ,	04/2011	2,082.75 -	3,500.00	148.63	- -	-	-	0/1
392	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN ,	04/2013	822.00 -	822.00	-	- -	-	-	0/1
393	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE ,	04/2010	553.63 -	1,009.00	7.08	- -	-	-	0/0
394	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL ,	04/2011	289.64 -	760.00	0.13	- -	-	-	0/0
395	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND ,	04/2010	309.44 388.67	583.00	302.39	12/2015 -	03/2016	-	0/0
396	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR ,	04/2008	490.80 633.87	490.80	0.39	- -	-	-	0/0
397	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR ,	04/2008	620.57 -	620.57	-	- -	-	-	0/0
398	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR ,	04/2008	445.25 -	445.25	-	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
399	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 549.75	549.75	14.65	- -	-	-	0/0
400	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
401	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
402	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
403	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
404	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	446.87 528.00	528.00	3.04	- -	-	-	0/0
405	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 1,200.00	1,200.00	2.26	- -	-	-	0/0
406	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 1,500.00	1,500.00	0.26	- -	-	-	0/0
407	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 377.71	556.64	303.72	- -	-	-	0/0
408	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 520.00	520.00	464.00	- -	-	-	0/0
409	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	346.15	155.87	- -	-	-	0/0
410	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	5.39	- -	-	-	0/0
411	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 603.22	603.22	1.64	- -	-	-	0/0
412	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 302.90	450.00	27.30	- -	-	-	0/0
413	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	247.00 931.98	951.24	709.44	- -	-	-	0/0
414	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	342.85	280.75	- -	-	-	0/0
415	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	4.21	- -	-	-	0/0
416	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	601.43 800.00	800.00	28.35	- -	-	-	0/0
417	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,103.00	0.60	- -	-	-	0/0
418	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	288.35	-	- -	-	-	0/0
419	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	923.52	231.38	- -	-	-	0/0
420	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.91 595.91	595.91	103.65	- -	-	-	0/0
421	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	499.30 2,491.43	2,491.43	166.23	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
422	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	277.70 792.89	792.89	66.69	- -	-	-	0/0
423	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	199.12	77.12	- -	-	-	0/0
424	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	297.85 540.02	540.02	22.26	- -	-	-	0/0
425	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE ,	04/2007	98.74 203.00	365.00	332.05	- -	-	-	0/0
426	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE ,	04/2006	96.16 260.16	280.00	270.71	- -	-	-	0/0
427	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	913.00 1,801.00	1,801.01	2.09	- 06/2016	-	-	0/0
428	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	558.85	- -	-	-	0/1
429	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	377.93 986.30	986.30	229.39	- -	-	-	0/1
430	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	1,112.00	0.36	- -	-	-	0/1
431	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,054.35 -	2,200.00	112.29	- -	-	-	0/0
432	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	923.23	1.24	- -	-	-	0/1
433	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	283.54 -	759.41	0.51	- -	-	-	0/0
434	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	156.65	50.64	- -	-	-	0/0
435	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	576.18	4.70	- -	-	-	0/0
436	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	2,966.99	5.76	- -	-	-	0/0
437	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	142.78	- -	-	-	0/0
438	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	-	- -	-	-	0/0
439	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 466.65	466.65	-	- -	-	-	0/0
440	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	562.74 832.47	832.47	0.94	- -	-	-	0/0
441	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 1,714.49	1,714.49	504.97	- 06/2014	-	-	0/2
442	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 348.85	348.85	0.35	- -	-	-	0/0
443	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	0.68	- -	-	-	0/0
444	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	0.48	- -	-	-	0/1
445	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	1,313.48 -	1,313.48	11.64	- -	-	-	0/1
446	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	337.49 -	792.01	1.13	- -	-	-	0/1
447	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,050.00 -	2,050.00	206.35	- -	-	-	0/1

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
448	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	-	-	-	-	0/0
449	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	-	-	-	-	0/0
450	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	328.14	47.25	-	-	-	0/0
451	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	1,117.00 1,922.00	1,922.00	2.62	-	-	-	0/0
452	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	-	-	-	-	0/0
453	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU ,	04/1999	460.94 893.69	1,170.00	1,030.52	01/1999 -	-	-	0/0
454	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	285.57 279.54	279.54	1.51	01/1999 -	-	-	0/0
455	KAKINADA-PITHAPURAM - [N22000314]SCR,ANDHRA PRADESH ,	03/1999	215.06 -	220.29	0.01	-	-	-	0/0
456	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA ,	04/2010	203.40 -	203.40	258.44	-	-	-	0/0
457	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,900.00 1,141.00	1,141.00	133.73	- 03/2016	-	-	0/1
458	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	-	-	-	-	0/0
459	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	873.71	-	-	-	-	0/0
460	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,618.00 1,614.59	1,614.59	102.50	-	-	-	0/0
461	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH ,	04/1997	836.26 1,072.52	1,072.52	1,045.82	-	-	-	0/0
462	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	-	-	-	0/0
463	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	-	-	-	-	0/0
464	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	2,425.00	-	-	-	-	0/0
465	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	2,750.00	-	-	-	-	0/0
466	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	630.00 1,272.19	1,272.19	-	-	-	-	0/0
467	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,326.00 -	2,326.00	-	-	-	-	0/0
468	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	4,670.00 3,627.00	3,627.00	0.02	-	-	-	0/0
469	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	1,876.00	-	-	-	-	0/0
470	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	854.00 -	854.00	-	-	-	-	0/0
471	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	912.00 -	912.00	-	-	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
472	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	616.08 -	616.08	0.36	-	-	-	0/1
473	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	-	-	-	-	0/0
474	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	0.29	-	-	-	0/0
475	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	4,000.00 3,631.00	3,631.00	-	-	-	-	0/0
476	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,246.26	-	-	-	-	0/0
477	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	-	-	-	-	0/0
478	SECUNDERABAD-MOHABOBNAGAR - [N22000371]RVNL,TELANGANA ,	04/2015	728.10 -	728.10	-	-	-	-	0/0
479	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.54	07/2014 -	-	-	0/0
480	INDORE-DEWAS-UJJAIN(80 KM) DL - [N22000375]WR,MADHYA PRADESH ,	04/2016	600.00 -	600.00	-	-	-	-	0/0
481	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM ,	04/2093	971.22 -	966.27	834.11	-	-	-	0/0
482	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	556.31 -	556.31	-	-	-	-	0/0
483	INDORE DEWAS UJJAIN (80 KM) - [N22000393]WR,GUJARAT ,	04/2016	600.00 -	600.00	-	-	-	-	0/0
484	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	900.00 -	900.00	-	-	-	-	0/0
485	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,000.00	-	-	-	-	0/0
486	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.67	-	-	-	-	0/0
487	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA ,	01/2004	238.56 717.15	740.00	732.57	03/2012 01/2016	01/2016	-	0/0
488	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.30	03/2011 -	01/2011	-	0/0
489	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 608.02	634.48	631.43	03/1994 02/2016	02/2016	-	0/0
490	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE ,	04/1990	155.66 551.50	548.01	265.18	- 03/2019	03/2019	- 0(R)	0/0
491	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND ,	04/1995	900.05 1,125.89	1,125.89	982.31	12/2011 03/2020	03/2020	99(O) 0(R)	0/0
492	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE ,	04/1997	218.24 372.09	525.00	549.50	-	03/2019	-	0/0
493	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	5,050.00	-	05/2008 -	03/2023	178(O) -	0/0
494	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE ,	04/2000	733.00 -	3,010.00	2,323.49	12/2008 -	03/2019	123(O) -	0/0
495	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 1,319.33	1,319.33	771.67	- 12/2009	03/2019	- 111(R)	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
496	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	727.56 4,454.18	9,658.00	5,472.86	03/2011 -	03/2019	96(O) -	0/0
497	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	03/2017	- -	0/0
498	NEW B.G. LINE FROM TETELIA TO BYRNHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM ,	09/2006	200.00 -	780.00	320.50	- -	03/2019	- -	0/0
499	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR ,	09/2006	300.00 -	2,145.00	362.59	- -	03/2020	- -	0/0
500	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	325.00 -	1,581.53	665.09	03/2010 -	03/2017	84(O) -	0/0
501	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
502	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	-	0/0
503	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA ,	04/2008	813.34 -	3,451.00	1,780.37	03/2014 -	03/2020	72(O) -	0/0
504	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM ,	04/2008	619.34 2,393.48	4,600.00	786.14	04/2014 -	03/2020	71(O) -	0/0
505	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	389.32	12/2015 -	03/2020	51(O) -	0/0
506	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	829.74	222.82	03/2015 -	03/2019	48(O) -	0/0
507	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 658.07	658.07	467.45	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
508	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	603.04 1,030.29	1,421.25	693.76	03/2012 -	03/2022	120(O) -	0/0
509	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	394.14 -	385.60	35.50	03/2013 -	03/2020	84(O) -	0/0
510	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	44.65	03/2012 03/2019	03/2019	84(O) 0(R)	0/0
511	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	850.00 -	3,000.00	150.74	03/2015 -	03/2021	72(O) -	0/0
512	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM ,	04/1998	227.90 -	509.00	327.26	12/2012 -	03/2016	-	0/0
513	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM ,	04/1996	1,676.31 -	7,000.00	6,402.53	03/2009 -	03/2017	96(O) -	0/0
514	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	349.24	- 03/2022	03/2022	- 0(R)	0/0
515	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	567.18 -	975.62	90.27	- -	03/2020	- -	0/0
516	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 -	399.63	20.01	- -	03/2019	- -	0/0
517	VIRAMGAM-SAMAKHALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	446.00 -	1,037.15	657.18	- -	03/2019	- -	0/0
518	RATANGARH-SARDARSARAH (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN ,	04/2010	739.65 -	872.22	805.97	- -	03/2017	- -	0/1

Sector Wise Details									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
519	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00	1,798.00	-	-	03/2019	-	0/0
520	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE ,	04/2008	822.39	1,480.83	1,461.01	-	03/2018	-	0/1
521	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00	1,857.00	1,287.74	03/2007	03/2016	-	0/0
522	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	252.00 967.85	967.85	97.63	-	03/2019	-	1/1
523	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00	4,274.00	-	-	03/2020	-	0/0
524	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL ,	04/2011	209.77	445.00	391.51	-	03/2018	-	0/0
525	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL ,	04/2012	283.55	330.00	98.32	-	03/2018	-	0/0
526	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	4,083.02	6,000.00	21.10	-	03/2020	-	0/0
527	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 210.00	394.28	148.33	-	03/2017	-	0/0
528	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	165.82	450.00	0.79	-	03/2019	-	0/0
529	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE ,	04/1999	523.17	1,653.55	1,071.96	-	03/2018	-	0/0
530	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	312.12	508.00	326.08	-	03/2018	-	0/0
531	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07	386.68	0.57	-	03/2019	-	0/0
532	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10	714.10	65.20	04/2016	03/2017	11(O)	0/0
533	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07	248.07	12.88	03/2015	03/2015	-	0/0
534	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60	299.60	-	03/2017	03/2017	0(O)	0/0
535	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42	257.42	67.47	03/2014	03/2014	-	0/0
536	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE ,	04/2010	423.66	423.66	163.59	03/2017	03/2017	0(O)	0/0
537	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00	2,127.00	632.11	-	03/2019	-	0/1
538	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71	1,503.71	-	-	03/2020	-	0/0
539	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	679.27	1,111.99	254.82	-	03/2021	-	0/0
540	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	858.67	837.33	-	-	03/2021	-	0/0
541	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	826.57 1,160.83	1,160.83	224.90	- 03/2020	03/2020	- 0(R)	0/1

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
542	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	112.11	-	03/2020	-	0/0
543	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU ,	04/2011	190.10 -	355.96	192.71	-	03/2019	-	0/0
544	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 860.43	860.43	57.15	-	03/2020	-	0/0
545	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	960.00 578.00	578.00	93.09	-	03/2020	-	0/2
546	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,750.00 -	1,750.00	-	03/2022	03/2022	0(O)	0/0
547	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	524.00 668.00	668.00	-	03/2020	03/2020	0(O)	0/6
548	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 187.26	233.73	35.10	04/2014 -	03/2018	47(O)	0/0
549	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 -	1,547.38	-	03/2021	03/2021	0(O)	0/0
550	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	0.40	03/2021	03/2021	0(O)	0/0
551	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 -	2,361.74	0.93	03/2021	03/2021	0(O)	0/0
552	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	701.61	-	03/2021	03/2021	0(O)	0/0
553	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	-	03/2021	03/2021	0(O)	0/0
554	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,232.32	1.30	-	03/2021	-	0/0
555	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	870.96	-	-	03/2021	-	0/0
556	VIRAMGAM BHILDI - [N22000391]WR,GUJARAT ,	04/1990	237.13 -	237.13	25.05	03/2018	03/2018	0(O)	0/0
557	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	0.86	-	03/2021	-	0/0
558	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	-	03/2021	03/2021	0(O)	0/3
559	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	969.83	26.23	03/2020	03/2020	0(O)	0/0
560	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	108.75	03/2021	03/2021	0(O)	0/0
561	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 -	1,027.40	483.36	03/2003	03/2021	216(O)	0/0
562	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	927.01	516.85	03/2019	03/2019	0(O)	0/0
563	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,514.45	-	03/2020	03/2020	0(O)	0/0
564	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	960.18 -	960.18	495.97	03/2020	03/2020	0(O)	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
565	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH ,	03/2007	758.09 -	758.09	482.81	03/2020 -	03/2020	0(O) -	0/0
566	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA ,	03/2009	942.95 -	942.95	682.92	03/2019 -	03/2019	0(O) -	0/0
567	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR, MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022	0(O) -	0/0
568	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR, MADHYA PRADESH ,	08/2016	582.13 -	582.13	-	03/2020 -	03/2020	0(O) -	0/0
569	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	-	03/2020 -	03/2020	0(O) -	0/0
570	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR, ODISHA ,	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0
571	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH ,	08/2015	528.57 -	528.57	-	03/2018 -	03/2019	12(O) -	0/0
572	HARMUTI-NAHARLAGUN - [N22000382]NFR, MULTI STATE ,	04/2096	614.54 -	613.00	518.52	-	04/2014	-	0/0
573	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR, ASSAM ,	04/2003	4,300.00 -	4,520.00	4,209.80	-	05/2015	-	0/0
574	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR, ASSAM ,	04/2007	180.09 -	180.00	154.42	-	05/2011	-	0/0
575	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM ,	09/1997	1,500.00 -	5,000.00	4,245.16	04/2008 12/2011	06/2017	110(O) 66(R)	0/0
576	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND ,	03/1999	2,957.21 3,020.95	3,020.95	2,393.07	07/2005 03/2018	06/2018	155(O) 3(R)	0/0
577	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA ,	04/1994	470.21 -	3,004.90	629.60	- 06/2021	06/2021	- 0(R)	0/0
578	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH ,	09/2007	687.20 -	950.00	947.78	03/2010 -	06/2017	87(O) -	0/0
579	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	06/2016	-	0/0
580	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
581	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE ,	04/2007	313.24 -	554.70	407.65	01/1999 06/2017	06/2017	221(O) 0(R)	0/0
582	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA ,	03/2011	165.16 -	234.71	227.37	03/2015 -	07/2015	-	0/0
583	DUDHNOI-MENDHIPATHAR - [N22000378]NFR, MULTI STATE ,	04/1992	315.64 -	315.00	310.80	-	08/2014	-	0/0
584	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL ,	04/1999	207.52 -	207.52	191.41	12/2012 -	09/2015	-	0/0
585	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT ,	04/2010	279.40 -	355.00	325.07	-	09/2015	-	0/0
586	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE ,	05/2015	600.00 -	620.00	-	-	09/2019	-	0/0
587	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE ,	04/1999	744.71 744.71	1,126.79	808.84	-	10/2016	-	1/1

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
588	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 245.39	245.39	210.67	12/2008 -	10/2015	-	0/0
589	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	10/2016	91(O) 91(R)	1/1
590	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE ,	12/2006	170.00 -	436.00	435.57	03/2011 -	10/2011	-	0/0
591	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA ,	03/2006	201.00 -	230.00	245.21	- -	10/2015	-	0/0
592	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	19,565.00	-	11/2002 -	12/2018	193(O) -	0/0
593	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA ,	02/1997	295.00 1,289.92	1,289.92	1,310.08	- -	12/2016	-	0/1
594	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE ,	02/1997	386.30 1,160.54	1,776.81	1,078.77	03/1998 -	12/2019	261(O) -	0/0
595	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	155.74 843.45	966.98	901.74	02/2009 12/2017	12/2017	106(O) 0(R)	0/0
596	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH ,	03/1997	677.97 1,595.40	1,679.13	1,721.58	- -	12/2016	-	0/0
597	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA ,	04/1999	166.16 -	370.00	358.96	02/2009 02/2009	12/2016	94(O) 94(R)	0/1
598	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND ,	04/1996	768.87 926.00	926.00	718.19	- -	12/2018	-	0/0
599	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	324.90 -	516.40	419.63	03/2010 -	12/2017	93(O) -	0/3
600	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	3,161.58	1,056.84	03/2016 -	12/2020	57(O) -	0/0
601	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	2,619.00	649.28	03/2016 -	12/2018	33(O) -	0/0
602	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 2,173.50	1,389.62	1,614.79	03/2014 12/2017	12/2017	45(O) 0(R)	0/0
603	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,266.89 -	1,266.89	87.25	- -	12/2020	-	0/0
604	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
605	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	456.00 855.16	860.00	557.38	- -	12/2018	-	0/0
606	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022	46(O) 0(R)	0/0
607	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	12/2016	21(O) -	0/0
608	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL ,	04/2010	171.02 -	235.00	228.37	06/2013 -	12/2016	42(O) -	0/0
609	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 315.13	365.00	1.19	- -	12/2017	-	0/0
610	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	-	03/2016 -	12/2017	21(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
611	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	209.00	0.36	12/2016 -	12/2016	0(O) -	0/0
612	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	720.00 678.54	678.54	0.75	- 12/2018	12/2018	- 0(R)	0/38
613	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	0.23	12/2020 -	12/2020	0(O) -	0/1
614	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	0.12	12/2020 -	12/2020	0(O) -	1/1
615	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(O) -	1/1
616	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL ,	01/1991	763.18 1,013.45	1,428.00	480.38	12/2021 -	12/2021	0(O) -	0/0
617	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	183.93	12/2021 -	12/2021	0(O) -	0/0
618	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	750.55 -	943.60	-	12/2024 -	12/2024	0(O) -	0/0
619	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	728.10 -	728.10	0.46	12/2024 -	12/2024	0(O) -	0/0
620	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025	0(O) -	0/0
621	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	4,295.30 -	4,295.30	87.74	12/2026 -	12/2026	0(O) -	0/0
622	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	0.13	12/2025 -	12/2025	0(O) -	0/0
623	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	458.72	12/2020 -	12/2020	0(O) -	0/0
624	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.65 -	1,485.65	403.93	12/2020 -	12/2020	0(O) -	0/0
625	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	36.80 274.41	1,336.57	259.58	- -	03/2019	- -	0/0
626	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	492.98 -	1,320.00	753.67	12/2010 -	03/2018	87(O) -	0/0
627	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
628	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.61	- -	-	-	0/6
629	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 3,385.14	3,404.92	3,544.30	12/2006 -	-	-	0/0
630	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR ,	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
631	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
632	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	470.92 727.13	3,000.00	317.00	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
633	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	343.00	191.82	-	-	-	0/0
634	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	151.26	-	-	-	0/0
635	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	332.92 332.92	477.88	495.40	03/2012 -	-	-	0/0
636	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL ,	03/1984	293.97 -	749.69	-	06/2005 -	12/2019	174(O) -	0/0
637	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR ,	04/2008	282.92 -	360.00	3.13	-	-	-	0/0
638	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 -	167.73	84.90	03/2012 -	-	-	0/0
639	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL ,	04/2004	293.74 -	293.74	139.08	12/2010 -	-	-	0/0
640	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	307.00	-	-	-	-	0/0
641	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	243.78	27.13	-	-	-	0/0
642	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	195.64	79.93	-	-	-	0/0
643	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	199.75	45.47	-	-	-	0/0
644	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	494.92	0.32	-	-	-	0/0
645	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	246.08	4.13	-	-	-	0/0
646	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	262.00	0.41	-	-	-	0/0
647	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	323.00	-	-	-	-	0/0
648	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN ,	04/2011	239.73 -	179.32	30.33	-	-	-	0/0
649	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	218.39	21.65	-	-	-	0/0
650	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 -	288.97	0.62	-	-	-	0/0
651	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	242.09	-	-	-	-	0/0
652	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	434.00	34.01	-	-	-	0/0
653	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	175.69 -	325.00	253.10	-	-	-	0/0
654	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	285.07 -	378.56	111.71	-	-	-	0/0
655	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
656	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	304.41 -	304.41	0.19	-	-	-	0/0
657	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	0.38	-	-	-	0/0
658	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	0.58	-	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
659	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	355.81	283.44	- -	-	-	0/0
660	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
661	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
662	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	25.99	- -	-	-	0/0
663	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	43.40	- -	-	-	0/0
664	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	573.78	166.89	- -	-	-	0/0
665	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	406.99	140.17	- -	-	-	0/0
666	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	450.00	7.41	- -	-	-	0/0
667	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	172.03	5.05	- -	-	-	0/0
668	PIRAPINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	261.38	14.71	- -	-	-	0/0
669	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE ,	04/2000	157.17 -	157.17	76.53	- -	-	-	0/0
670	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	53.02	- -	-	-	0/0
671	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	277.28	55.74	- -	-	-	0/0
672	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	296.44 -	296.44	3.86	- -	-	-	0/0
673	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	41.67	- -	-	-	0/0
674	BARIAPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	450.55	10.91	- -	-	-	0/0
675	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	365.17	1.29	- -	-	-	0/0
676	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
677	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE ,	04/2011	193.44 -	193.44	15.86	- -	-	-	0/0
678	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	175.80	1.22	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
679	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
680	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	297.47	51.81	- -	-	-	0/0
681	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	337.96	60.00	- -	-	-	0/0
682	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	493.96 -	493.96	118.87	- -	-	-	0/0
683	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
684	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
685	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE ,	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
686	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	0.36	- -	-	-	0/0
687	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	88.77	- -	-	-	0/0
688	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	-	- -	-	-	0/0
689	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
690	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA ,	04/2011	390.60 -	390.60	2.11	- -	-	-	0/0
691	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	329.97	0.34	- -	-	-	0/0
692	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	104.75	- -	-	-	0/0
693	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	141.13	- -	-	-	0/0
694	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	1.02	- -	-	-	0/0
695	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
696	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	0.32	- -	-	-	0/0
697	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	250.93	-	- -	-	-	0/0
698	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	255.64	-	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
699	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
700	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL ,	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
701	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	-	-	-	-	0/0
702	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	-	-	-	-	0/0
703	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA ,	05/2015	400.00 -	400.00	-	-	-	-	0/0
	Total		358,611.57 -	452,613.73	105,447.51				9/98
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
704	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
705	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU , PPP (BOT)	04/2009	353.37 -	353.37	365.08	10/2011 -	-	-	0/0
706	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU , PPP (BOT)	09/2010	1,655.00 -	1,655.00	641.78	09/2013 -	-	-	0/0
707	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
708	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	312.80	06/2013 -	08/2016	38(O) -	0/0
709	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	-	03/2016 -	-	-	3/4
710	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	104.19	03/2016 -	-	-	3/4
711	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
712	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
713	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAHAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
714	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
715	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , EPC	03/2015	298.33 -	298.33	32.92	-	-	-	0/4

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
716	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	32.86	- -	-	-	0/4
717	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	55.73	- -	-	-	0/4
718	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
719	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 200.69	207.40	192.97	07/2014 -	-	-	0/1
720	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	- -	-	-	0/1
721	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	- -	-	-	0/4
722	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	- -	-	-	0/0
723	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	0.05	- -	-	-	0/0
724	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	69.34	- 03/2013	-	-	0/0
725	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	214.86	- 11/2014	-	-	0/0
726	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	-	-	0/0
727	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	-	-	0/0
728	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	-	-	0/0
729	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
730	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
731	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH , EPC	11/2015	485.44 -	485.44 -	-	12/2015 -	-	-	0/0
732	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH, CHHATISGARH , EPC	03/2015	422.34 -	422.34 -	49.93	-	-	-	0/0
733	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90 -	50.74	-	-	-	0/0
734	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68 -	77.55	-	-	-	0/0
735	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	-	-	-	0/0
736	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	217.74	-	-	-	0/0
737	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21 -	-	-	-	-	0/0
738	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	59.97	01/2015 -	-	-	0/0
739	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	53.14	01/2015 -	-	-	0/0
740	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
741	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
742	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
743	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
744	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
745	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
746	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49 -	-	03/2011 -	-	-	0/0
747	TWO LANING OF GOBOK- SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03 -	-	05/2012 -	-	-	0/0
748	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59 -	-	08/2013 -	-	-	0/0
749	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27 -	-	08/2013 -	-	-	0/0
750	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00 -	24.36	02/2013 -	-	-	0/0
751	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00 -	-	02/2011 -	-	-	0/0
752	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
753	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	161.70	-	07/2015 -	-	-	0/0
754	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14 -	-	08/2015 -	-	-	0/0
755	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74 -	-	- -	-	-	0/0
756	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41 -	-	03/2016 -	-	-	0/0
757	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81 -	6.53	- -	-	-	0/0
758	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC, IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38 -	101.48	- -	-	-	0/0
759	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36 -	96.10	- -	-	-	0/0
760	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74 -	189.42	- -	-	-	0/0

Sector Wise Details									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
761	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
762	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	205.09	05/2015 -	-	-	0/0
763	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	69.06	02/2016 -	-	-	0/0
764	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
765	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	27.40	- -	-	-	0/0
766	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.69	- -	-	-	0/0
767	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	267.63	- -	-	-	0/0
768	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
769	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
770	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	-	-	0/0
771	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
772	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	18.13	- -	-	-	0/0
773	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	-	-	0/0
774	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
775	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	135.20	- -	-	-	0/0
776	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
777	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86 -	252.03	04/2015 -	-	-	0/0
778	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04 -	130.82	10/2010 -	-	-	0/0
779	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00 -	-	09/2010 -	-	-	0/0
780	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00 -	-	09/2010 -	-	-	0/0
781	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18 -	-	- -	-	-	0/0
782	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94 -	-	- -	-	-	0/0
783	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01 -	-	- -	-	-	0/0
784	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74 -	-	- -	-	-	0/0
785	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50 -	29.92	- -	-	-	0/0
786	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40 -	56.97	- -	-	-	0/0
787	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82 -	590.00	02/2015 -	-	-	0/0
788	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72 -	-	- -	-	-	0/0
789	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00 -	-	10/2013 -	-	-	0/0
790	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00 -	-	10/2013 -	-	-	0/0
791	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00 -	279.92	06/2006 -	-	-	0/0
792	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07 -	-	- -	-	-	0/0
793	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10 -	-	- -	-	-	0/0
794	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04 -	-	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
795	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	-	-	-	-	0/0
796	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	-	-	-	-	0/0
797	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	-	03/2016 -	-	-	0/0
798	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	-	-	-	-	0/0
799	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	-	-	-	0/0
800	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	-	-	-	-	0/0
801	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	-	-	-	-	0/0
802	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	-	-	0/0
803	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
804	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	41.76	-	-	-	0/0
805	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	22.00	-	-	-	0/0
806	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	-	-	-	-	0/0
807	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	-	-	-	-	0/0
808	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	45.25	-	-	-	0/0
809	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	42.99	-	-	-	0/0
810	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.26	07/2008 -	-	-	0/0
811	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
812	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	-	-	-	0/0
813	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	-	-	-	0/0

Sector Wise Details									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
814	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	22.18	08/2014 -	-	-	0/0
815	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	136.47	11/2014 -	-	-	0/0
816	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	0.45	- -	-	-	0/0
817	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	-	- -	-	-	0/0
818	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	-	- -	-	-	0/0
819	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	-	- -	-	-	0/0
820	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	-	- -	-	-	0/0
821	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	-	- -	-	-	0/0
822	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	-	- -	-	-	0/0
823	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	-	- -	-	-	0/0
824	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	-	- -	-	-	0/0
825	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	-	- -	-	-	0/0
826	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	-	- -	-	-	0/0
827	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	-	- -	-	-	0/0
828	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	-	- -	-	-	0/0
829	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	-	- -	-	-	0/0
830	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	-	- -	-	-	0/0
831	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	-	- -	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
832	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00 -	-	-	-	-	0/0
833	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00 -	-	-	-	-	0/0
834	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00 -	-	-	-	-	0/0
835	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00 -	-	-	-	-	0/0
836	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18 -	-	-	-	-	0/0
837	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64 -	-	-	-	-	0/0
838	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE- IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64 -	-	-	-	-	0/0
839	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08 -	-	-	-	-	0/0
840	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60 -	-	-	-	-	0/0
841	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	364.56 -	-	-	-	-	0/0
842	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17 -	-	01/2016 -	-	-	0/0
843	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00 -	-	01/2016 -	-	-	0/0
844	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62 -	-	-	-	-	0/0
845	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58 -	-	-	-	-	0/0
846	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70 -	-	-	-	-	0/0
847	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97 -	-	-	-	-	0/0
848	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46 -	-	-	-	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
849	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	-	-	-	-	0/0
850	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA ,	05/2015	600.85 -	600.85	-	-	-	-	0/0
851	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	-	-	-	-	0/0
852	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	-	-	-	-	0/0
853	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	-	-	-	-	0/0
854	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	-	-	-	-	0/0
855	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	-	-	-	-	0/0
856	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	-	-	-	-	0/0
857	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	-	-	-	-	0/0
858	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	-	-	-	-	0/0
859	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	-	-	-	-	0/0
860	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	-	-	-	-	0/0
861	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	-	-	-	-	0/0
862	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I), NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	771.18	-	-	-	-	0/0
863	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	1,850.96	04/2015 -	01/2017	21(O) -	0/0
864	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	0(O) -	0/0
865	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	-	01/2019 -	01/2019	0(O) -	0/4
866	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	-	01/2019 -	01/2019	0(O) -	0/0
867	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	246.10	01/2017 -	01/2017	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
868	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40 -	-	01/2018 -	01/2018	0(O) -	0/0
869	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05 -	-	01/2017 -	01/2017	0(O) -	0/0
870	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL ,	10/2015	361.15 -	361.15 -	-	- -	01/2018	- -	0/0
871	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20 -	-	- -	01/2019	- -	0/0
872	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50 -	1,135.69	07/2017 -	01/2018	6(O) -	0/0
873	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,WEST BENGAL , PPP (BOT)	07/2015	1,393.00 -	1,393.00 -	1,386.53	- -	01/2018	- -	0/0
874	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34 -	1,620.11	01/2018 -	01/2018	0(O) -	0/0
875	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16 -	391.77	07/2014 -	02/2017	31(O) -	0/0
876	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00 -	1,890.00	09/2015 -	02/2017	17(O) -	0/0
877	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27 -	-	02/2017 -	02/2017	0(O) -	0/1
878	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61 -	46.68	02/2017 -	02/2017	0(O) -	0/1
879	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00 -	-	02/2017 -	02/2017	0(O) -	0/0
880	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55 -	38.13	02/2015 -	02/2017	24(O) -	0/1
881	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN ,	08/2015	538.08 -	538.08 -	70.35	02/2018 -	02/2018	0(O) -	0/0
882	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 -	723.54 -	292.34	02/2018 -	02/2018	0(O) -	0/0
883	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN ,	08/2015	482.27 -	482.27 -	111.99	02/2018 -	02/2018	0(O) -	0/0
884	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22 -	-	02/2018 -	02/2018	0(O) -	0/0
885	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31 -	-	02/2018 -	02/2018	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
886	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN ,	08/2015	275.90 -	275.90 -	28.00 -	-	02/2018	-	0/0
887	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM ,	12/2003	199.81 -	385.13 -	217.29 -	04/2009	03/2017	95(O) -	0/0
888	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM ,	12/2003	212.00 -	212.00 -	122.77 -	09/2007	03/2017	114(O) -	0/0
889	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM ,	12/2003	196.00 -	331.23 -	373.08 -	07/2009	03/2017	92(O) -	0/0
890	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA ,	09/2010	946.00 -	946.00 -	818.53 -	-	03/2017	-	3/3
891	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA , PPP (BOT)	02/2010	617.00 -	617.00 -	584.38 -	08/2012	03/2017	55(O) -	0/0
892	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR , PPP (BOT)	09/2011	574.00 -	574.00 -	899.81 -	03/2014	03/2017	36(O) -	0/0
893	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR ,	10/2011	375.09 -	375.09 -	510.91 -	04/2014	03/2017	35(O) -	0/0
894	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00 -	1,652.28 -	06/2014	03/2017	33(O) -	0/0
895	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN , PPP (BOT)	10/2013	677.79 -	677.79 -	883.59 -	04/2016	03/2017	11(O) -	0/0
896	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00 -	-	03/2018	03/2018	0(O) -	0/4
897	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB ,	01/2014	523.85 -	523.85 -	119.97 -	01/2016	03/2017	14(O) -	0/0
898	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN ,	09/2015	567.51 -	567.51 -	42.79 -	03/2018	03/2018	0(O) -	0/0
899	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH , EPC	10/2013	445.89 -	445.89 -	20.11 -	03/2017	03/2017	0(O) -	0/0
900	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD, UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49 -	-	03/2017	03/2017	0(O) -	0/0
901	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH , EPC	06/2015	774.57 -	774.57 -	6.33 -	03/2018	03/2018	0(O) -	0/0
902	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL , EPC	01/1991	322.00 -	322.00 -	66.59 -	03/2018	03/2018	0(O) -	0/0
903	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP, UTTAR PRADESH , EPC	10/2013	317.76 -	317.76 -	15.70 -	03/2017	03/2017	0(O) -	0/0
904	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH , EPC	10/2013	493.94 -	493.94 -	20.76 -	03/2017	03/2017	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
905	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH ,	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(O) -	0/0
906	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH ,	09/2015	664.53 -	664.53	-	03/2018 -	03/2018	0(O) -	0/0
907	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH ,	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(O) -	0/0
908	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
909	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	-	03/2018 -	03/2018	0(O) -	0/0
910	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0
911	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	57.93	03/2018 -	03/2018	0(O) -	0/0
912	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69(O) -	0/0
913	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
914	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	731.90	03/2014 -	04/2017	37(O) -	0/0
915	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	84.84	-	04/2018	-	0/1
916	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	-	04/2017 -	04/2017	0(O) -	0/3
917	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN ,	10/2014	206.12 -	206.12	121.88	04/2017 -	04/2017	0(O) -	0/0
918	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN ,	10/2014	264.72 -	264.72	136.71	04/2017 -	04/2017	0(O) -	0/0
919	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA ,	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
920	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	133.00	04/2018 -	04/2018	0(O) -	0/0
921	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	-	-	04/2018	-	0/0
922	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	81.69	-	04/2018	-	0/0
923	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN ,	12/2003	275.00 -	281.31	195.99	02/2010 -	05/2017	87(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
924	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA , PPP (BOT)	03/2005	940.00	940.00	1,415.36	07/2012	05/2017	58(O)	3/3
925	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL , PPP (BOT)	02/2011	580.43	580.43	272.37	08/2013	05/2017	45(O)	0/0
926	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00	1,479.00	590.00	06/2015	05/2017	23(O)	0/0
927	REHABILITATION AND UPGRADE OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83	224.83	-	05/2015	05/2017	24(O)	2/4
928	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89	454.89	-	05/2018	05/2018	0(O)	0/1
929	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11	194.11	46.11	05/2018	05/2018	0(O)	0/4
930	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14	279.14	122.20	05/2017	05/2017	0(O)	0/0
931	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09	261.09	41.87	05/2017	05/2017	0(O)	0/0
932	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05	497.05	0.54	05/2017	05/2017	0(O)	0/0
933	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08	268.08	-	05/2017	05/2017	0(O)	0/0
934	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49	532.49	166.22	05/2017	05/2017	0(O)	0/0
935	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	219.99	05/2016	05/2016	-	0/0
936	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41	229.41	10.32	05/2018	05/2018	0(O)	0/0
937	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83	224.83	-	04/2015	05/2016	-	0/0
938	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08	235.08	-	05/2018	05/2018	0(O)	0/4
939	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51	414.00	-	-	05/2018	-	0/0
940	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13	531.13	-	-	05/2018	-	0/0
941	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26	593.26	-	-	05/2018	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
942	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00 -	-	- -	05/2018	- -	0/0
943	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32 -	162.33	05/2017 -	05/2017	0(O) -	0/0
944	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66 -	228.50	- -	05/2018	- -	0/0
945	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20 -	6.99	- -	05/2018	- -	0/0
946	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69 -	-	- -	05/2018	- -	0/0
947	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85 -	-	05/2016 -	05/2016	-	0/0
948	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30 -	-	05/2016 -	05/2016	-	0/0
949	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00 -	2,035.69	05/2013 -	06/2017	49(O) -	0/0
950	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00 -	696.22	01/2014 -	06/2017	41(O) -	0/0
951	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00 -	1,863.25	09/2014 -	06/2017	33(O) -	0/0
952	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77 -	107.87	- -	06/2017	- -	0/4
953	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61 -	-	06/2014 -	06/2016	-	0/2
954	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39 -	-	06/2018 -	06/2018	0(O) -	0/4
955	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49 -	-	06/2018 -	06/2018	0(O) -	0/4
956	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00 -	-	06/2018 -	06/2018	0(O) -	0/0
957	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43 -	-	06/2018 -	06/2018	0(O) -	0/0
958	2 LANING WITH PAVED SHOULDER OF KARAUKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI,TAMIL NADU ,	12/2014	451.58 -	451.58 -	28.00	06/2017 -	06/2017	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
959	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
960	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
961	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24(O) -	0/0
962	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018	0(O) -	0/0
963	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	-	- -	06/2017	- -	0/0
964	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	-	- -	06/2017	- -	0/0
965	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
966	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018	0(O) -	0/0
967	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	431.50	- -	06/2018	- -	0/0
968	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	-	06/2018 -	06/2018	0(O) -	0/0
969	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	5.92	06/2018 -	06/2018	0(O) -	0/0
970	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	6.02	06/2018 -	06/2018	0(O) -	0/0
971	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	-	- -	06/2017	- -	0/0
972	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	-	- -	06/2018	- -	0/0
973	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019 -	06/2019	0(O) -	0/0
974	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019 -	06/2019	0(O) -	0/0
975	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI,RAJASTHAN , PPP (BOT)	06/2016	725.95 -	725.95	-	06/2019 -	06/2019	0(O) -	0/0
976	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	-	06/2019 -	06/2019	0(O) -	0/0
977	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	-	05/2017 -	06/2017	1(O) -	0/0
978	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM ,	12/2003	237.80 -	237.80	418.17	06/2008 -	07/2016	-	0/0
979	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	314.79	06/2008 06/2016	07/2016	-	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
980	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00 -	1,682.27	07/2015 -	07/2017	24(O) -	0/0
981	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00 -	4,266.60	06/2015 -	07/2016	-	0/0
982	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00 -	1,948.72	08/2013 -	07/2016	-	0/0
983	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54 -	551.33	11/2013 -	07/2016	-	0/0
984	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79 -	68.07	07/2016 -	07/2016	-	0/12
985	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99 -	16.54	07/2014 -	07/2016	-	0/1
986	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83 -	63.38	07/2017 -	07/2017	0(O) -	0/0
987	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN ,	07/2015	455.60 -	455.60 -	65.88	07/2017 -	07/2017	0(O) -	0/0
988	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28 -	-	07/2018 -	07/2018	0(O) -	0/0
989	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70 -	2,946.14	10/2011 -	07/2016	-	0/0
990	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00 -	-	07/2018 -	07/2018	0(O) -	0/0
991	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36 -	-	07/2018 -	07/2018	0(O) -	0/0
992	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17 -	27.95	-	07/2018	-	0/0
993	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83 -	-	07/2016 -	07/2016	-	0/0
994	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50 -	-	07/2016 -	07/2016	-	0/0
995	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80 -	-	07/2016 -	07/2016	-	0/0
996	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT , PPP (BOT)	12/2010	1,008.50 -	1,008.50 -	1,282.25	06/2013 -	08/2016	38(O) -	0/3
997	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00 -	654.59	02/2014 -	08/2016	30(O) -	0/0
998	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20 -	1,630.57	02/2014 -	08/2017	42(O) -	2/2

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
999	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23(O) -	0/4
1000	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	75.32	08/2016 -	08/2016	0(O) -	0/0
1001	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	393.88	09/2015 -	08/2016	11(O) -	0/0
1002	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	-	08/2016 -	08/2016	0(O) -	0/0
1003	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH , PPP (BOT)	02/2012	912.00 -	912.00	-	08/2016 -	08/2016	0(O) -	0/0
1004	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	978.00	08/2016 -	08/2017	12(O) -	0/0
1005	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	01/1991	1,388.00 -	1,388.00	175.79	-	08/2018	-	0/0
1006	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	0(O) -	0/0
1007	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	-	-	08/2018	-	0/0
1008	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	102.34	08/2014 -	08/2014	-	0/0
1009	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	434.58	02/2009 -	09/2016	91(O) -	0/0
1010	BIJINI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM ,	12/2003	195.00 -	195.00	294.65	06/2008 -	09/2016	99(O) -	0/0
1011	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR ,	12/2003	332.94 -	332.94	518.85	09/2008 -	09/2016	96(O) -	0/0
1012	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM ,	12/2003	264.72 -	264.72	322.50	06/2008 -	09/2016	99(O) -	0/0
1013	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 309.56	309.56	409.32	04/2010 09/2016	09/2016	77(O) 0(R)	0/0
1014	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH ,	12/2003	348.16 -	348.16	418.19	09/2007 -	09/2016	108(O) -	0/0
1015	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	-	05/2013 -	09/2016	40(O) -	0/0
1016	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT , PPP (BOT)	09/2010	805.39 -	805.39	1,407.71	03/2013 -	09/2016	42(O) -	0/0
1017	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	368.94	01/2014 -	09/2016	32(O) -	0/0
1018	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	284.73	10/2013 -	09/2016	35(O) -	0/0
1019	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	957.30	09/2016 -	09/2016	0(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1020	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN ,	03/2014	240.10 -	240.10	165.44	03/2016 -	09/2016	6(O) -	0/0
1021	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017	0(O) -	0/0
1022	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	20.56	09/2017 -	09/2017	0(O) -	0/0
1023	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND ,	09/2015	341.61 -	341.61	140.65	09/2017 -	09/2017	0(O) -	0/0
1024	TWO LANING WITH PAVED SHOULDER OF KARAUHI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	274.20	09/2016 -	09/2016	0(O) -	0/0
1025	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	268.27	08/2016 -	09/2016	1(O) -	0/0
1026	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	112.62	09/2016 -	09/2017	12(O) -	0/0
1027	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	192.55	08/2015 -	09/2016	13(O) -	0/0
1028	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,410.79	-	09/2016	-	0/0
1029	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	-	03/2014 -	09/2016	30(O) -	0/0
1030	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	10/2016	103(O) 0(R)	0/0
1031	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,771.99	08/2013 -	10/2017	50(O) -	0/0
1032	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	871.15	09/2014 -	10/2017	37(O) -	0/3
1033	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU , PPP (BOT)	06/2013	1,287.95 -	1,287.95	757.57	11/2015 -	10/2017	23(O) -	0/0
1034	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	24.63	-	10/2017	-	0/4
1035	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
1036	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	-	10/2018 -	10/2018	0(O) -	0/4
1037	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	0(O) -	0/0
1038	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	215.70	01/2016 -	10/2016	9(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1039	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	346.60	01/2016 -	10/2016	9(O) -	0/0
1040	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	218.10	10/2016 -	10/2016	0(O) -	0/0
1041	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	17.71	10/2016 -	10/2016	0(O) -	0/0
1042	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	41.21	10/2017 -	10/2017	0(O) -	0/0
1043	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	200.21	10/2016 -	10/2016	0(O) -	0/0
1044	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	21.03	10/2016 -	10/2016	0(O) -	0/0
1045	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	0(O) -	0/0
1046	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	81.34	10/2017 -	10/2017	0(O) -	0/0
1047	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	-	10/2016 -	10/2016	0(O) -	0/0
1048	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	11/2016	42(O) -	0/0
1049	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,544.63	11/2016 -	11/2016	0(O) -	0/0
1050	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN ,	01/2014	368.15 -	368.15	216.38	01/2016 -	11/2016	10(O) -	0/0
1051	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	119.70	11/2016 -	11/2016	0(O) -	0/2
1052	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	113.36	11/2016 -	11/2016	0(O) -	0/4
1053	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017	0(O) -	0/0
1054	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24(O) -	0/4
1055	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	24(O) -	0/4

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1056	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39 -	-	11/2018 -	11/2018 -	0(O) -	0/4
1057	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95 -	-	11/2018 -	11/2018 -	0(O) -	0/4
1058	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67 -	-	11/2015 -	11/2017 -	24(O) -	0/0
1059	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12 -	-	11/2015 -	11/2017 -	24(O) -	0/0
1060	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11 -	234.99	11/2017 -	11/2017 -	0(O) -	0/0
1061	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92 -	146.29	11/2016 -	11/2016 -	0(O) -	0/0
1062	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24 -	148.92	-	11/2017 -	-	0/0
1063	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06 -	-	-	11/2017 -	-	0/0
1064	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH ,	02/2013	1,232.00 -	1,232.00 -	-	08/2015 -	11/2016 -	15(O) -	0/0
1065	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39 -	-	11/2017 -	11/2017 -	0(O) -	0/0
1066	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL ,	03/2016	229.37 -	229.37 -	-	-	11/2018 -	-	0/0
1067	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00 -	-	-	11/2018 -	-	0/0
1068	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66 -	-	-	11/2018 -	-	0/0
1069	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24 -	16.23	11/2015 -	11/2015 -	-	0/0
1070	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM ,	12/2003	230.00 -	230.00 -	203.60	06/2005 -	12/2016 -	138(O) -	0/0
1071	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64 -	282.52	11/2008 -	12/2016 -	97(O) -	0/0
1072	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13 -	199.25	11/2008 -	12/2016 -	97(O) -	0/0
1073	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00 -	251.26	04/2009 -	12/2016 -	92(O) -	0/0
1074	NALBARI T BIJUNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 230.00	208.00	309.52	04/2008 01/2017	12/2016	104(O) -1(R)	0/0
1075	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00 -	202.41	05/2008 12/2016	12/2016	103(O) 0(R)	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1076	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	469.41	05/2010 -	12/2016	79(O) -	0/0
1077	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 2,782.54	1,509.10	3,272.71	09/2012 -	12/2016	51(O) -	2/3
1078	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.34	08/2011 -	12/2016	64(O) -	2/2
1079	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,846.48	11/2011 -	12/2016	61(O) -	0/0
1080	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	-	04/2013 -	12/2016	44(O) -	0/0
1081	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	902.60	03/2013 -	12/2016	45(O) -	0/0
1082	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,038.84	07/2013 -	12/2016	41(O) -	0/0
1083	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	39(O) -	0/0
1084	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	12/2016	42(O) -	0/0
1085	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2016	28(O) -	0/0
1086	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	1,893.03	03/2013 -	12/2016	45(O) -	0/0
1087	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,415.99	07/2013 -	12/2016	41(O) -	0/0
1088	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	880.96	02/2013 -	12/2016	46(O) -	0/0
1089	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	12/2016	37(O) -	0/0
1090	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48(O) -	0/0
1091	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.34	07/2013 -	12/2016	41(O) -	0/0
1092	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55(O) -	0/0
1093	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	311.51	08/2013 -	12/2017	52(O) -	0/0
1094	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	623.47	10/2013 -	12/2017	50(O) -	0/0
1095	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,851.90	05/2014 -	12/2016	31(O) -	0/0
1096	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	604.85	07/2013 -	12/2016	41(O) -	0/0
1097	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,363.70	06/2014 -	12/2016	30(O) -	0/0
1098	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA , PPP (BOT)	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1099	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	875.56	08/2013 -	12/2016	40(O) -	0/0
1100	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	621.48	09/2013 -	12/2016	39(O) -	0/0
1101	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	-	03/2013 -	12/2016	45(O) -	0/0
1102	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,202.40	08/2013 -	12/2016	40(O) -	0/0
1103	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,475.09	09/2014 -	12/2016	27(O) -	0/0
1104	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR , PPP (BOT)	07/2012	356.40 -	356.40	352.00	07/2014 -	12/2017	41(O) -	0/0
1105	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2016	32(O) -	0/0
1106	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	354.08	06/2014 -	12/2016	30(O) -	0/0
1107	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	12/2016	12(O) -	0/3
1108	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1109	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA , PPP (BOT)	10/2013	283.25 -	283.25	181.61	10/2015 -	12/2017	26(O) -	0/0
1110	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	0(O) -	0/4
1111	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 - 333.21	333.21	-	12/2015 -	12/2016	12(O) -	0/2
1112	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12(O) -	0/0
1113	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	21.06	12/2017 -	12/2017	0(O) -	0/0
1114	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	67.32	01/2016 -	12/2016	11(O) -	0/0
1115	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA ,	06/2015	996.37 -	996.37	2.18	12/2017 -	12/2017	0(O) -	0/0
1116	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	0(O) -	0/0
1117	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	225.02	-	12/2018 -	12/2018	0(O) -	0/0
1118	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
1119	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	350.23	11/2016 -	12/2016	1(O) -	0/0

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1120	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	360.06	- -	12/2016	-	0/0
1121	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB ,	12/2015	239.23 -	239.23	40.30	12/2017 -	12/2017	0(O)	0/0
1122	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O)	0/0
1123	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
1124	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	-	11/2015 -	12/2016	13(O)	0/0
1125	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	-	12/2017 -	12/2018	12(O)	0/0
1126	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	110.62	- -	12/2017	-	0/0
1127	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
1128	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	01/1991	1,167.45 -	1,167.45	-	- -	-	-	0/0
	Total		272,789.46 -	275,538.97	114,247.72				22/160
	<u>SHIPPING AND PORTS</u>								
1129	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1130	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU ,	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O)	0/0
1131	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU ,	12/2014	274.85 -	274.85	189.52	04/2017 -	04/2017	0(O)	0/1
1132	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 235.15	235.15	176.55	06/2017 -	06/2017	0(O)	0/1
1133	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA ,	03/2007	245.67 373.22	409.83	350.68	04/2009 03/2010	08/2016	88(O) 77(R)	0/0
1134	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 600.00	600.00	525.49	03/2006 03/2016	12/2016	129(O) 9(R)	0/0
1135	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 669.46	669.46	415.01	12/2010 12/2018	12/2018	96(O) 0(R)	0/0
1136	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	42.57	12/2017 -	12/2017	0(O)	0/1
	Total		4,117.75 -	5,085.02	2,531.03				0/3
	<u>TELECOMMUNICATIONS</u>								

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1137	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00	13,334.00	-	07/2015	-	-	0/0
1138	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17	2,011.17	301.57	09/2014	03/2017	30(O)	0/70
	Total		15,445.17	15,345.17	301.57				0/70
	URBAN DEVELOPMENT								
1139	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33	349.33	123.13	11/2014	-	-	0/0
1140	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30	884.30	304.26	08/2014	-	-	0/0
1141	CONSTRUCTION OF 100 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI , Central Sector Projects	06/2015	197.33	197.33	0.14	-	-	-	0/0
1142	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00	388.00	136.68	01/2015	-	-	5/12
1143	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00	209.00	-	-	-	-	0/0
1144	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA ,	05/2006	6,395.00	14,405.01	14,081.31	06/2011	01/2017	67(O)	3/3
1145	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72	332.72	133.58	09/2016	01/2017	4(O)	0/0
1146	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14	26,405.14	901.75	02/2019	03/2020	13(O)	0/0
1147	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH ,	12/2012	188.87	188.87	124.48	12/2014	03/2017	27(O)	0/0
1148	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00	191.97	133.13	03/2012	03/2017	60(O)	0/0
1149	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84	157.84	49.18	03/2017	03/2017	0(O)	0/0
1150	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI ,	05/2012	405.01	405.01	249.90	12/2014	03/2017	27(O)	1/3
1151	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00	8,680.00	221.25	03/2018	03/2018	0(O)	0/0
1152	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN , Central Sector Projects	08/2014	350.02	350.02	161.29	03/2015	03/2017	24(O)	0/0
1153	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57	156.57	60.59	09/2015	04/2017	19(O)	1/7

Sector Wise Details									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1154	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	36.54	10/2012 04/2017	04/2017	54(O) 0(R)	0/0
1155	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 270.83	270.83	-	11/2014 05/2017	05/2017	30(O) 0(R)	0/0
1156	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017	-1(O) -	0/0
1157	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 14,600.00	14,600.00	13,069.22	12/2015 -	08/2016	8(O) -	3/24
1158	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	24.52	03/2016 -	09/2017	18(O) -	0/5
1159	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI ,	05/2009	261.85 -	261.85	208.53	05/2013 10/2015	10/2016	41(O) 12(R)	0/0
1160	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	22.45	03/2015 10/2017	10/2017	31(O) 0(R)	0/0
1161	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA ,	12/2012	315.00 315.00	315.00	214.40	06/2015 08/2016	11/2016	17(O) 3(R)	0/0
1162	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	5,298.00	1,680.80	11/2019 -	11/2019	0(O) -	0/7
1163	CONSTRUCTION OF CIVIL STRUCTURES AN OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD,KERALA ,	07/2015	154.00 -	154.00	19.54	11/2015 -	11/2017	24(O) -	0/0
1164	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI ,	09/2011	38,585.00 -	38,585.00	24,669.11	03/2016 -	12/2016	9(O) -	0/0
1165	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,219.21	-	10/2019 -	12/2018	-10(O) -	0/0
1166	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	-	0/0
1167	REHABILITATION AND STRENGTHENING OF SEWERWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	-	-	-	-	0/0
	Total		133,984.49 -	143,123.47	56,625.78				13/61
	Grand Total		1,433,476.53	1,610,504.54	630,581.41				1777/3938


Summary of projects in the Flash Report for the month of August, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1144
Number of Projects completed/dropped/frozen in Current Month	6
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	28
Number of Projects in Current Month	1167


Brief Analysis

Project Status with respect to Original Schedule: Out of 1167 projects, 7 projects are ahead of schedule, 282 projects are on schedule 337 projects are delayed. 460 projects do not have fixed dates of commissioning. 81 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

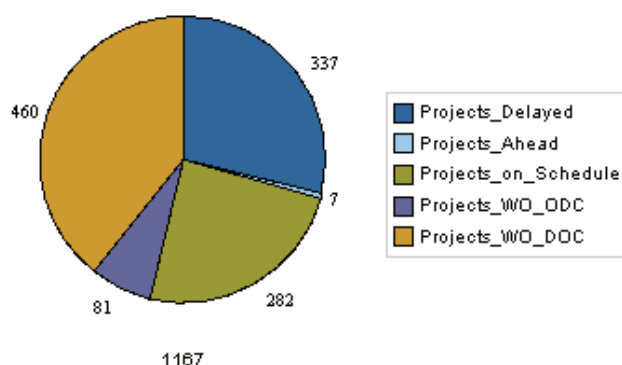

Investment Scenario

Total original cost of implementation of 1167 projects when sanctioned, was of the order of Rs. 1433476.53 crore but this was subsequently revised to Rs. 1610504.54 crore implying a cost overrun of 12.3%. The expenditure incurred on these projects till August, 2016 is Rs. 630581.41 crore, which is 39.2% of the revised cost of the projects.

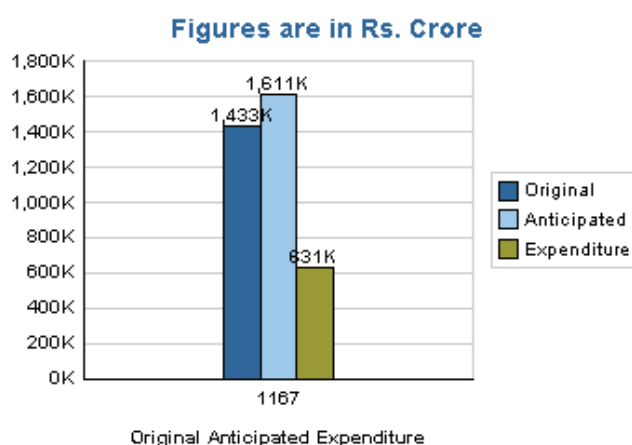

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed. 1 project does not have fixed dates of commissioning.

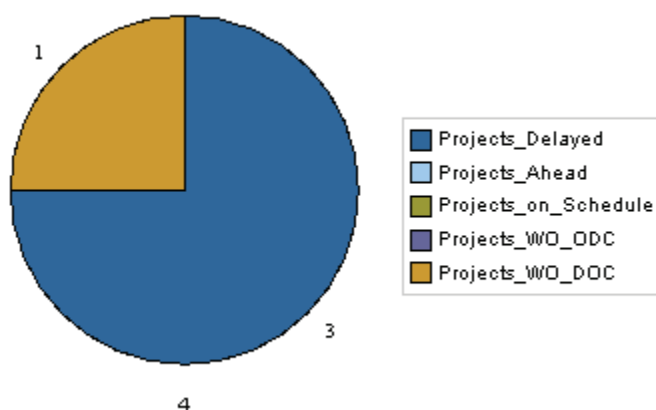

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till August, 2016 is Rs. 42385.12 crore, which is 81.6% of the revised cost of the projects.

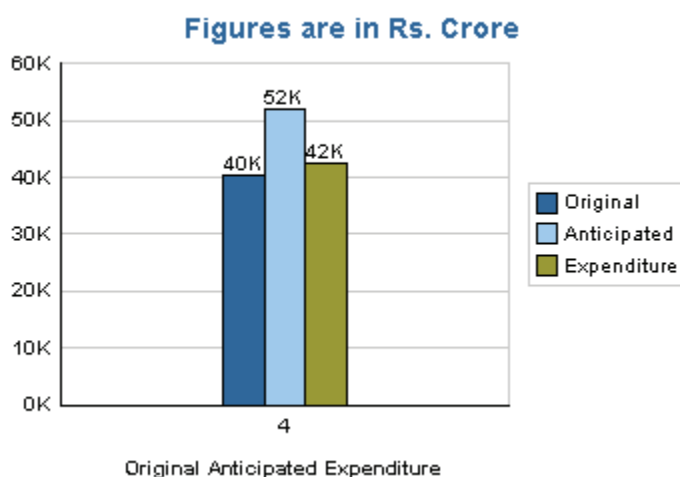

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 1 project is delayed. 2 projects do not have fixed dates of commissioning.

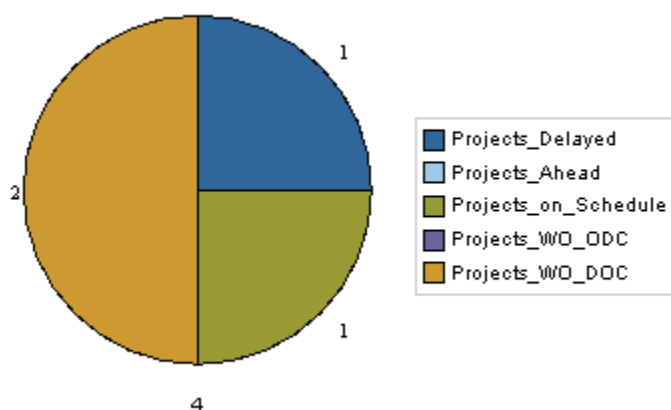

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1177.28 crore but this was subsequently anticipated to Rs. 1186.17 crore implying a cost overrun of .8%. The expenditure incurred on these projects till August, 2016 is Rs. 797.73 crore, which is 67.3% of the revised cost of the projects.

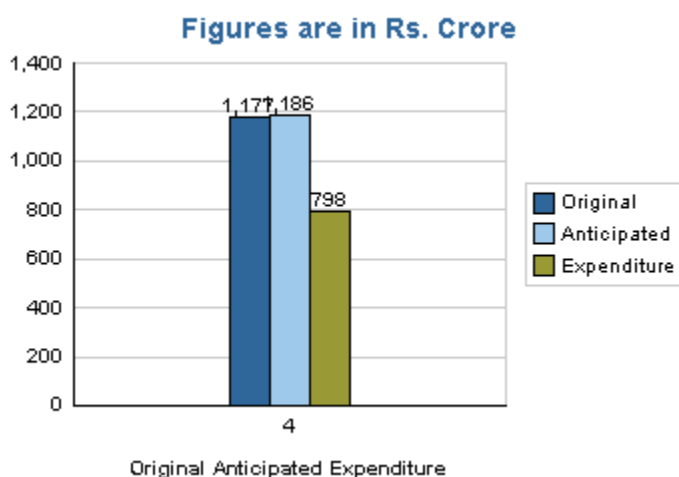

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	88
Number of Projects On Schedule	44
Number of Projects Delayed	40
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 88 projects, 2 projects are ahead of schedule, 44 projects are on schedule 40 projects are delayed. 2 projects do not have fixed dates of commissioning.

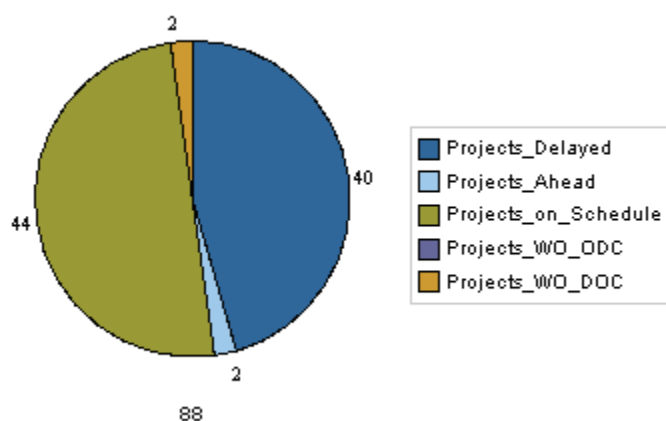

Investment Scenario

Total original cost of implementation of 88 projects when sanctioned, was of the order of Rs. 68729.81 crore but this was subsequently anticipated to Rs. 70406.76 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till August, 2016 is Rs. 14791.3 crore, which is 21% of the revised cost of the projects.

Figures are in Rs. Crore

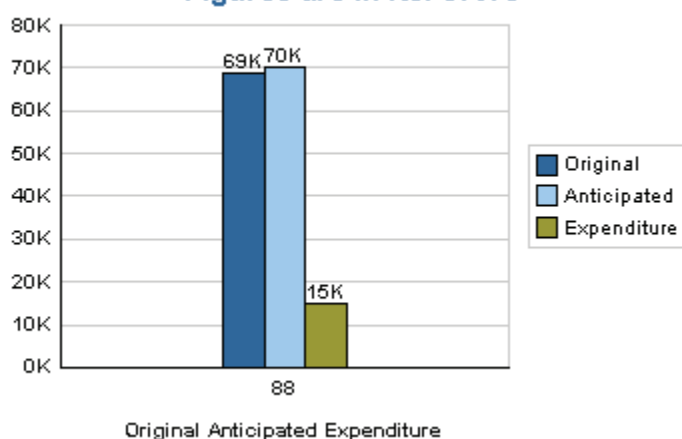

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

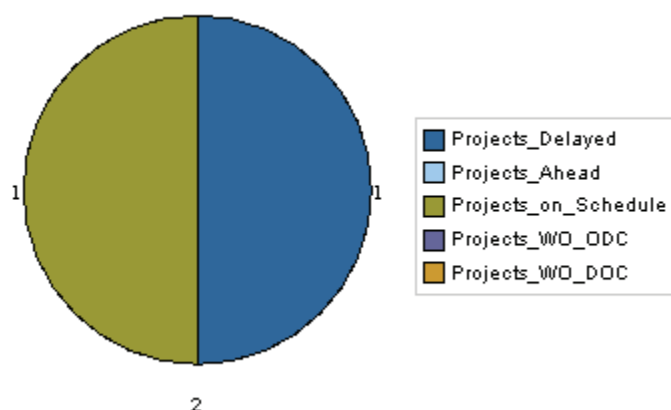

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 692.29 crore implying a cost overrun of 1.7%. The expenditure incurred on these projects till August, 2016 is Rs. 113.81 crore, which is 16.4% of the revised cost of the projects.

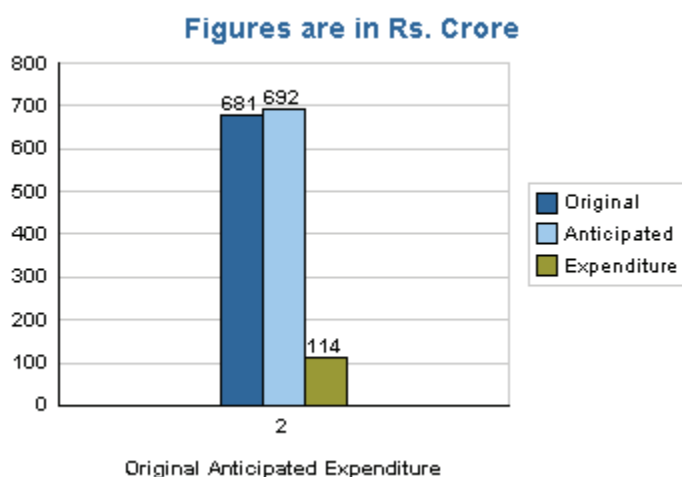

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	3
Number of Projects On Schedule	2
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are on schedule 1 project is delayed.

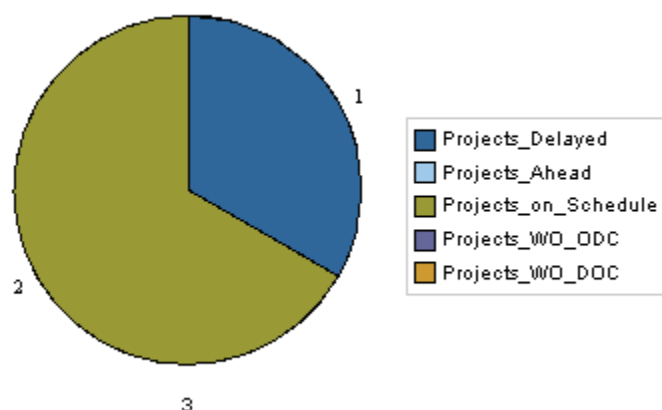

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 2555.63 crore but this was subsequently anticipated to Rs. 1875.63 cr The expenditure incurred on these projects till August, 2016 is Rs. 459.84 crore, which is 24.5% of the revised cost of the projects.

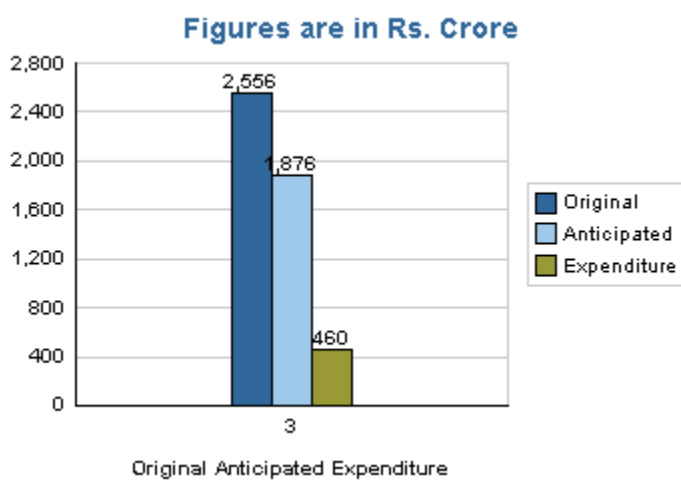

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	34
Number of Projects On Schedule	14
Number of Projects Delayed	14
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 34 projects, 14 projects are on schedule 14 projects are delayed. 5 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

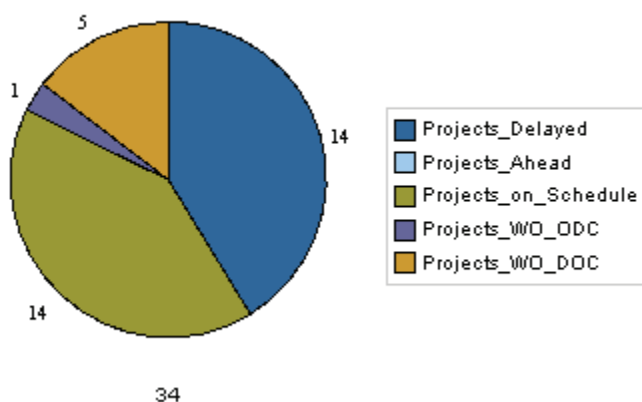

Investment Scenario

Total original cost of implementation of 34 projects when sanctioned, was of the order of Rs. 57600.51 crore but this was subsequently anticipated to Rs. 57771.82 crore implying a cost overrun of .3%. The expenditure incurred on these projects till August, 2016 is Rs. 33361.78 crore, which is 57.7% of the revised cost of the projects.

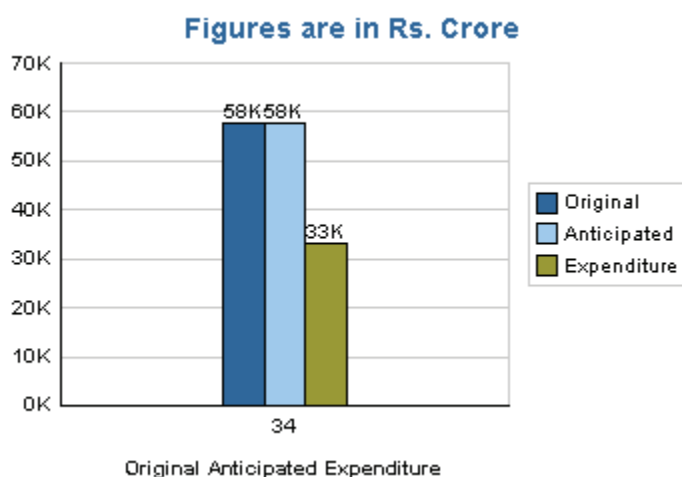

Sector wise current status of projects on the Flash Report

PETROCHEMICALS


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1


Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

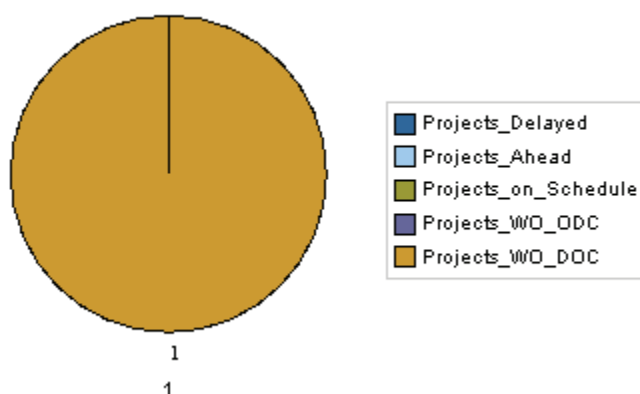

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 5460.61 crore but this was subsequently anticipated to Rs. 9965 crore implying a cost overrun of 82.5%. The expenditure incurred on these projects till August, 2016 is Rs. 9895.57 crore, which is 99.3% of the revised cost of the projects.

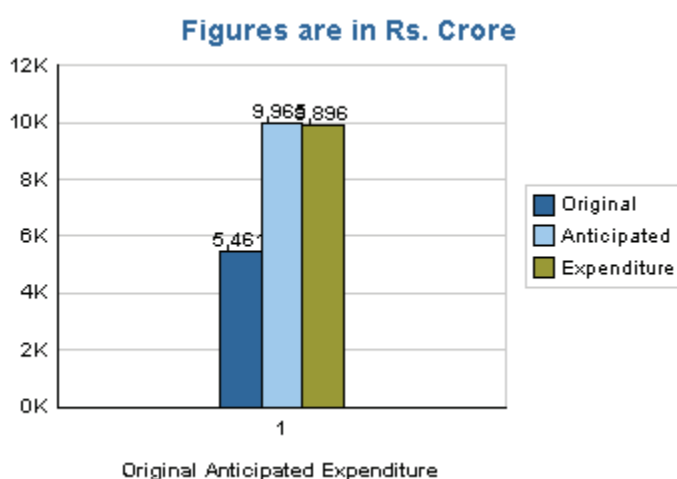

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	80
Number of Projects On Schedule	30
Number of Projects Delayed	38
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 80 projects, 3 projects are ahead of schedule, 30 projects are on schedule 38 projects are delayed. 9 projects do not have fixed dates of commissioning.

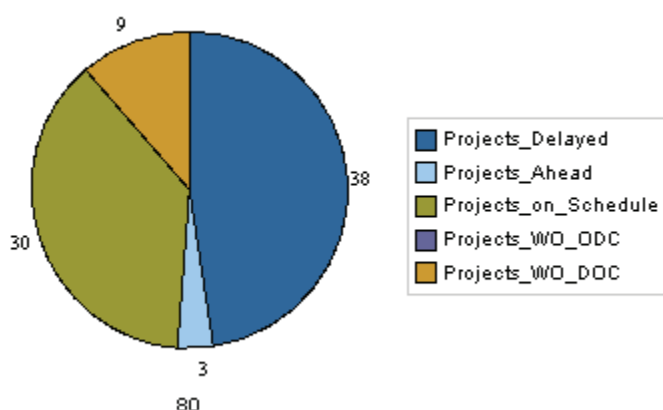

Investment Scenario

Total original cost of implementation of 80 projects when sanctioned, was of the order of Rs. 136063.71 crore but this was subsequently anticipated to Rs. 137688.98 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till August, 2016 is Rs. 45924.48 crore, which is 33.4% of the revised cost of the projects.

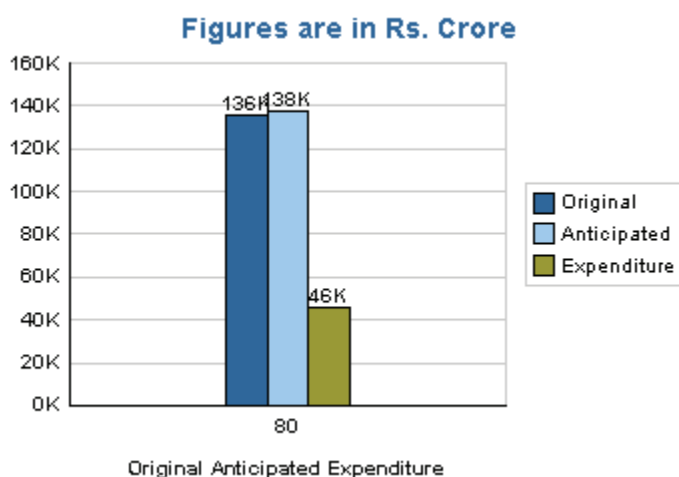

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	117
Number of Projects On Schedule	45
Number of Projects Delayed	61

Number of Projects Without Date Of Commissioning	11
--	----


Brief Analysis

Project Status with respect to Original Schedule: Out of 117 projects, 45 projects are on schedule 61 projects are delayed. 11 projects do not have fixed dates of commissioning.

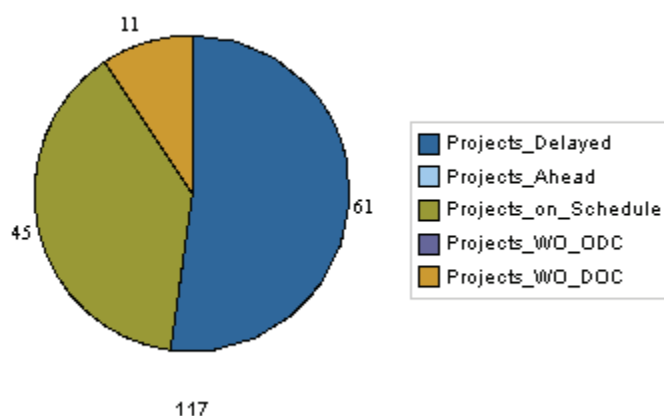

Investment Scenario

Total original cost of implementation of 117 projects when sanctioned, was of the order of Rs. 331536.75 crore but this was subsequently anticipated to Rs. 380903.08 crore implying a cost overrun of 14.9%. The expenditure incurred on these projects till August, 2016 is Rs. 200112.78 crore, which is 52.5% of the revised cost of the projects.

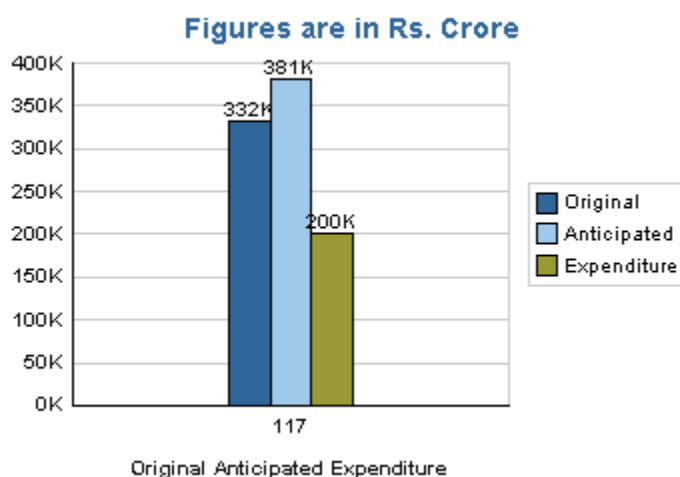

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.



Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till August, 2016 is Rs. 2289 crore, which is 59.8% of the revised cost of the projects.

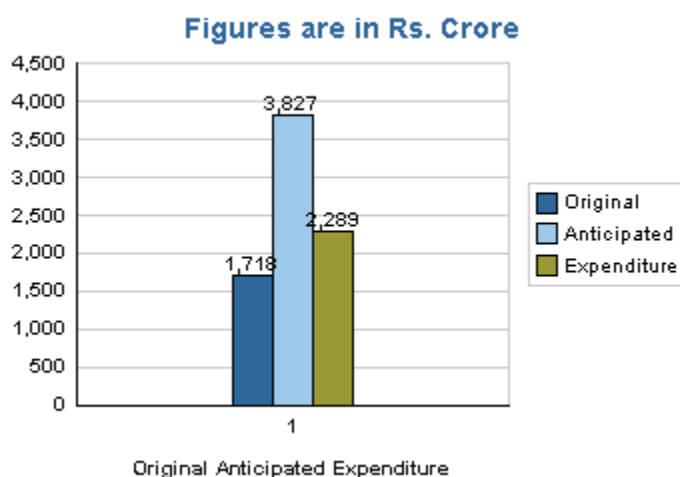

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	4
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 4 projects are delayed. 4 projects do not have fixed dates of commissioning.

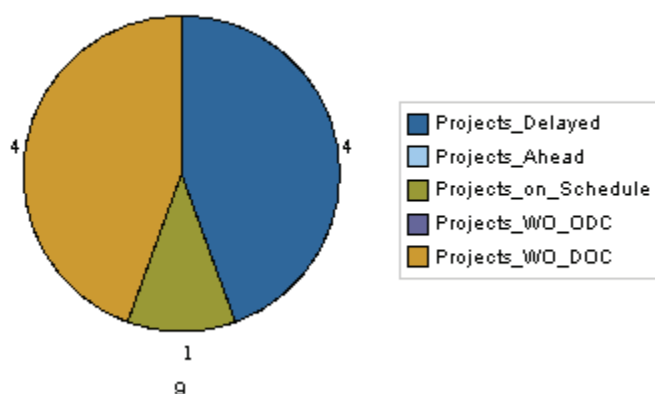

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 2563.15 crore but this was subsequently anticipated to Rs. 2563.15 crore. The expenditure incurred on these projects till August, 2016 is Rs. 1296.39 crore, which is 50.6% of the revised cost of the projects.

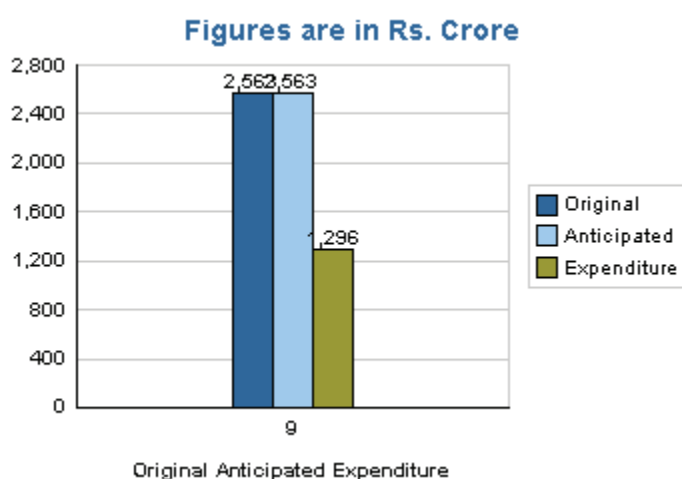

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	360
Number of Projects On Schedule	35
Number of Projects Delayed	41
Number of Projects Without Original Date of Commissioning	46
Number of Projects Without Date Of Commissioning	238


Brief Analysis

Project Status with respect to Original Schedule: Out of 360 projects, 35 projects are on schedule 41 projects are delayed. 238 projects do not have fixed dates of commissioning. 46 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

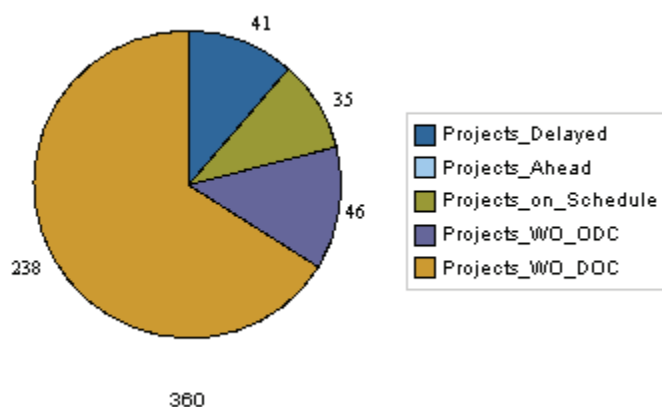

Investment Scenario

Total original cost of implementation of 360 projects when sanctioned, was of the order of Rs. 358611.57 crore but this was subsequently anticipated to Rs. 452613.73 crore implying a cost overrun of 26.2%. The expenditure incurred on these projects till August, 2016 is Rs. 105447.51 crore, which is 23.3% of the revised cost of the projects.

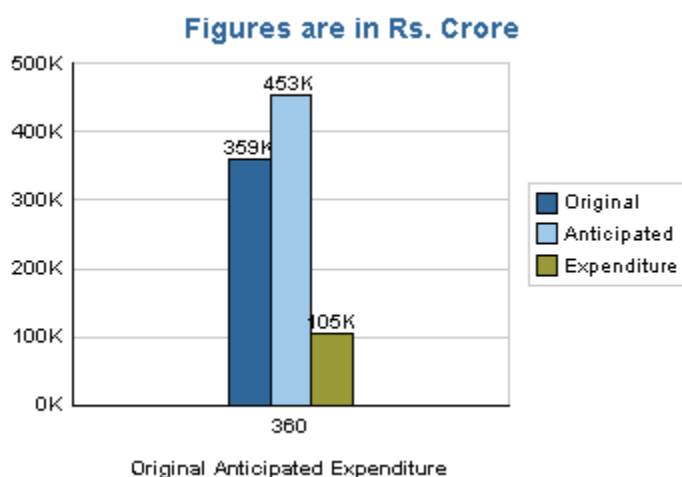

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	425
Number of Projects On Schedule	102
Number of Projects Delayed	111
Number of Projects Without Original Date of Commissioning	34
Number of Projects Without Date Of Commissioning	178


Brief Analysis

Project Status with respect to Original Schedule: Out of 425 projects, 102 projects are on schedule 111 projects are delayed. 178 projects do not have fixed dates of commissioning. 34 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

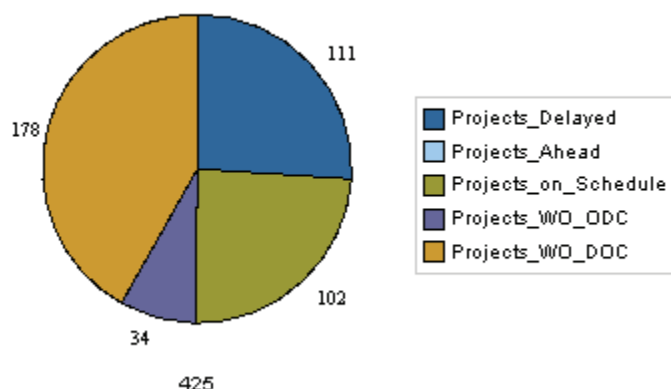

Investment Scenario

Total original cost of implementation of 425 projects when sanctioned, was of the order of Rs. 272789.46 crore but this was subsequently anticipated to Rs. 275538.97 crore implying a cost overrun of 1%. The expenditure incurred on these projects till August, 2016 is Rs. 114247.72 crore, which is 41.5% of the revised cost of the projects.

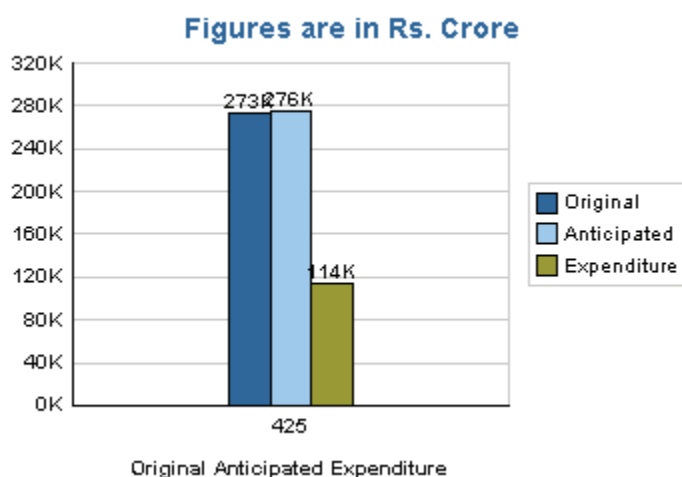

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule 3 projects are delayed. 1 project does not have fixed dates of commissioning.

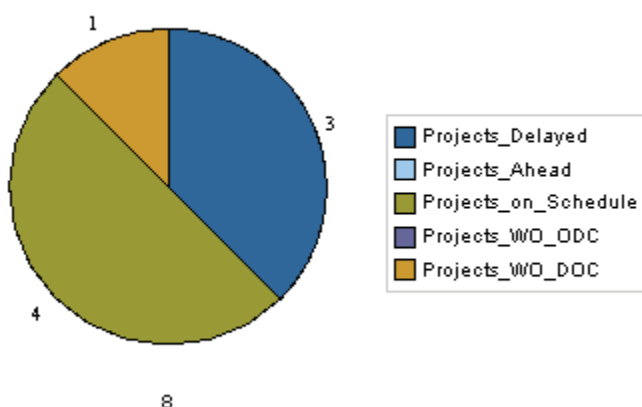

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5085.02 crore implying a cost overrun of 23.5%. The expenditure incurred on these projects till August, 2016 is Rs. 2531.03 crore, which is 49.8% of the revised cost of the projects.

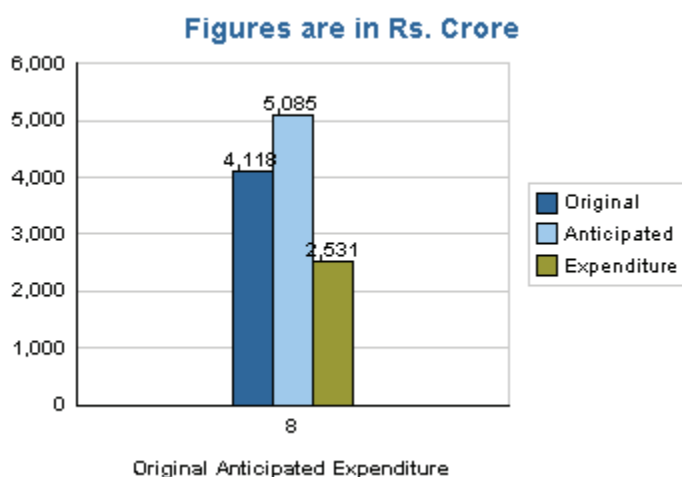

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.



Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 15445.17 crore but this was subsequently anticipated to Rs. 15345.17 cr The expenditure incurred on these projects till August, 2016 is Rs. 301.57 crore, which is 2% of the revised cost of the projects.

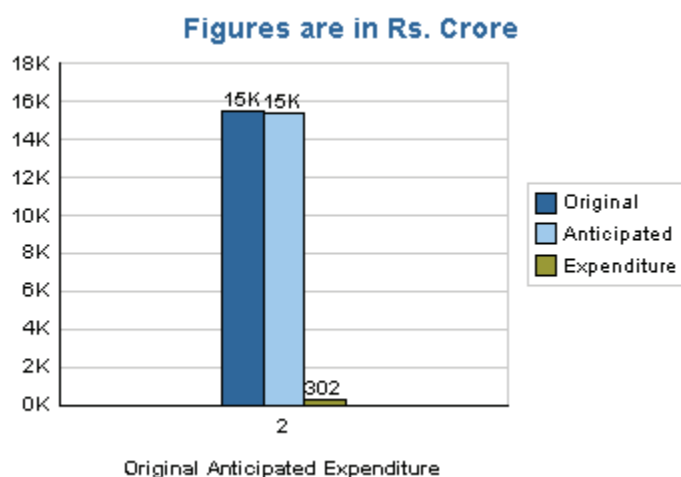

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	29
Number of Projects On Schedule	3
Number of Projects Delayed	17
Number of Projects Ahead	2

Number of Projects Without Date Of Commissioning	7
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 2 projects are ahead of schedule, 3 projects are on schedule 17 projects are delayed. 7 projects do not have fixed dates of commissioning.

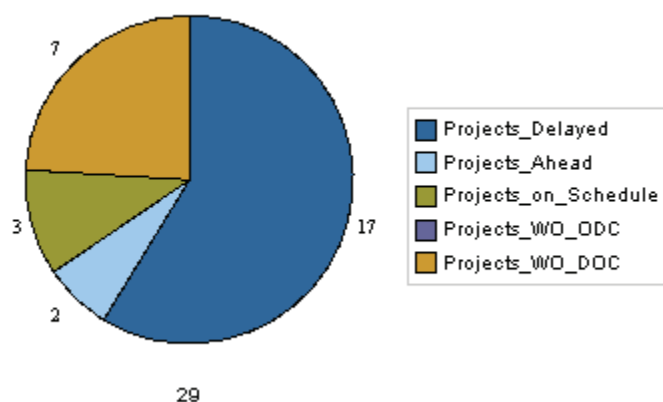

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 133984.49 crore but this was subsequently anticipated to Rs. 143123.47 crore implying a cost overrun of 6.8%. The expenditure incurred on these projects till August, 2016 is Rs. 56625.78 crore, which is 39.6% of the revised cost of the projects.

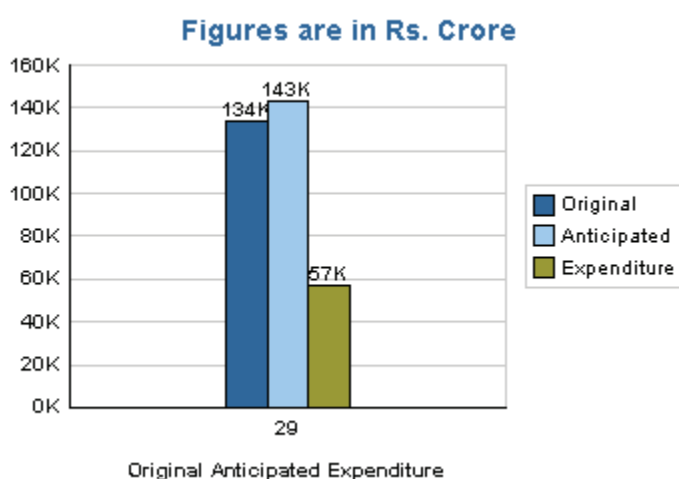

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (AS On 31-AUG-16)
 (All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	26.3
2	ANDHRA PRADESH	52	58,490.76	62,196.35	9,041.38
3	ARUNACHAL PRADESH	15	12,006.22	28,062.52	14,811.49
4	ASSAM	52	36,951	54,911.99	40,528.72
5	BIHAR	73	64,649.96	77,718.17	40,650.85
6	CHHATISGARH	41	96,809.69	99,835.63	52,788.03
7	D & N HAVELI	1	6,086.08	6,086.08	1,221.41
8	DELHI	17	50,768.66	51,802.66	28,135.25
9	GOA	8	3,925.48	3,907.87	632.67
10	GUJARAT	42	37,127.23	39,183.68	26,097.01
11	HARYANA	18	12,060.7	14,031.32	8,044.53
12	HIMACHAL PRADESH	9	10,659.35	17,058.62	7,486.94
13	JAMMU AND KASHMIR	10	27,408.66	46,614.79	14,765.55
14	JHARKHAND	46	45,227.61	48,236.81	15,751.3
15	KARNATAKA	42	74,476.15	92,794.43	38,771.69
16	KERALA	19	33,504.08	35,120.13	14,057.1
17	MADHYA PRADESH	52	56,376.91	60,820.87	13,627.12
18	MAHARASHTRA	96	1,56,010.09	1,64,632.84	48,371.47
19	MANIPUR	3	1,047.27	10,045.73	5,617.6
20	MEGHALAYA	5	6,744.03	8,661.01	739.35
21	MIZORAM	5	2,001.2	7,054.66	1,983.28
22	MULTI STATE	170	2,71,276.73	2,54,241.47	73,072.42
23	NAGALAND	3	6,420	8,570	150.74
24	ODISHA	55	59,391.88	65,327.97	15,990.83
25	PUNJAB	25	14,354.28	14,358.28	3,064.45
26	RAJASTHAN	59	39,324.78	40,491.87	17,920.49
27	SIKKIM	5	2,149.08	4,894.01	848.78
28	TAMIL NADU	61	71,269.1	92,215.95	64,110.88
29	TELANGANA	37	26,031.22	29,431.19	5,007.65
30	TRIPURA	10	4,140.67	9,124.56	4,658.13
31	UTTAR PRADESH	76	77,839.61	81,239.51	23,100.42
32	UTTARAKHAND	9	15,810.7	18,110.01	6,174.01
33	WEST BENGAL	50	52,822.74	63,408.95	33,333.57
TOTAL		1,167	14,33,476.53	16,10,504.54	6,30,581.41

Annexure- II

List of Projects in which Expenditure is More than Approved Cost

(Aug, 2016)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	5,677.00	5,264.12	09/2010 09/2016	10/2017
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	21,749.00	12/2008 10/2013	05/2016
	Total		16,663.00 -	28,139.00	27,013.12		
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	1/2009	309.46 -	309.46	435.10	01/2011 -	09/2017
	Total		309.46 -	309.46	435.10		
	<u>COAL</u>						
4	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023
5	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	208.48	03/2012 -	03/2019
6	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	182.37	03/2010 -	03/2019
7	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]	1/2005	302.96 -	302.96	319.40	03/2010 -	03/2017
8	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	888.70	03/2013 -	03/2016
	Total		1,313.63 -	2,400.33	2,080.26		
	<u>HEALTH AND FAMILY WELFARE</u>						
9	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70 -	196.70	197.38	01/2016 -	04/2016
	Total		196.70 -	196.70	197.38		
	<u>HEAVY INDUSTRY</u>						
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	4/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017
	Total		1,718.00 -	3,827.30	2,289.00		
	<u>PETROLEUM</u>						
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,493.81	01/2012 -	09/2016

(Aug, 2016)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
12	MARKETING TOP AT KORBA - [N16000186	1/2011	141.86 -	232.00	183.99	09/2016 -	09/2016
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	1/2006	732.00 -	1,227.00	1,158.24	10/2011 -	04/2016
	Total		1,866.86 -	3,152.00	2,836.04		
	<u>POWER</u>						
14	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	9/2002	3,919.59 -	8,398.75	5,871.70	09/2009 -	12/2018
15	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053	2/2009	509.66 -	509.66	593.76	11/2011 -	11/2016
16	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	1/2007	5,353.00 -	5,353.00	5,760.32	05/2014 03/2017	09/2017
17	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129	2/2012	3,201.44 -	3,201.44	3,426.91	10/2014 -	09/2016
18	KISHANGANGA HEP (3X110 MW) - [N18000031	1/2009	3,642.04 -	5,783.17	4,676.44	01/2016 -	-
19	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103	9/2011	1,940.13 -	1,940.13	2,149.36	09/2014 -	12/2016
20	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194	5/2015	436.68 -	436.68	447.48	12/2016 -	12/2016
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	9/2003	6,285.33 -	17,435.15	8,637.42	09/2010 -	-
	Total		25,287.87 -	43,057.98	31,563.39		
	<u>RAILWAYS</u>						
22	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	4/1986	158.77 274.56	634.48	631.43	03/1994 02/2016	02/2016
23	CALICUT-MANGALORE (DL) (SR) - [220100151	2/1996	240.00 -	579.37	532.98	- -	-
24	KARUR-SALEM(NL),SR - [220100191	2/1997	155.55 -	870.00	845.57	- -	-
25	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	9/2001	492.98 -	1,320.00	753.67	12/2010 -	03/2018
26	GULBARGA-BIDAR,SCR(NL) - [220100254	2/1998	242.42 369.70	1,542.41	959.72	- 05/2009	-
27	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	3/1998	280.00 -	1,122.00	834.61	- -	-
28	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	3/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-
29	PANVEL PEN DOUBLING - [N22000255	4/2006	96.16 -	280.00	270.71	- -	-
30	PEN ROHA DOUBLING - [N22000254	4/2007	98.74 -	365.00	332.05	- -	-
31	KATAKHAL TO BHAIRABI - [N22000126	4/1998	227.90 -	509.00	327.26	12/2012 -	03/2016
32	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	203.00	202.30	03/2011 -	01/2011

						(Aug, 2016)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
33	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	4/1996	332.92 283.95	477.88	495.40	03/2012 -	-
34	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	9/2006	343.17 -	1,065.00	969.97	- -	-
35	BHOPAL BINA 3D LINE DOUBLING - [N22000077	9/2007	687.20 -	950.00	947.78	03/2010 -	06/2017
36	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	3/1997	261.70 -	318.00	288.07	02/2006 -	-
37	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	1,202.70	254.22	02/2015 -	-
38	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	436.00	435.57	03/2011 -	10/2011
39	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	4/2003	727.56 -	9,658.00	5,472.86	03/2011 -	03/2019
40	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	4/1994	470.21 -	3,004.90	629.60	- 06/2021	06/2021
41	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	4/2000	733.00 -	3,010.00	2,323.49	12/2008 -	03/2019
42	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	4/1997	162.87 -	541.00	198.17	- -	-
43	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	4/1997	501.69 335.77	1,043.56	891.01	03/2012 -	-
44	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	9/1997	1,500.00 -	5,000.00	4,245.16	04/2008 12/2011	06/2017
45	JAGGAYYAPET - MELLACHERUVU - [N22000304	4/2007	313.24 -	554.70	407.65	01/1999 06/2017	06/2017
46	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303	4/1999	460.94 -	1,170.00	1,030.52	01/1999 -	-
47	NEW COOCHBEHAR TO SAMUKTALA - [N22000197	4/2011	209.77 -	445.00	391.51	- -	03/2018
48	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	4/1999	895.00 -	1,857.00	1,287.74	03/2007 -	03/2016
49	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	4/2008	822.39 -	1,480.83	1,461.01	- -	03/2018
50	SAKRI-HASANPUR ROAD (NL) - [N22000171	4/1999	175.69 -	325.00	253.10	- -	-
51	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163	4/2010	171.02 -	235.00	228.37	06/2013 -	12/2016
52	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153	4/2010	739.65 -	872.22	805.97	- -	03/2017
53	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146	4/2010	279.40 -	355.00	325.07	- -	09/2015
54	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	4/2011	446.00 -	1,037.15	657.18	- -	03/2019
55	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	4/2007	482.00 -	874.57	896.20	03/2013 -	-
56	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183	2/1997	295.00 -	1,289.92	1,310.08	- -	12/2016
57	RANCHI-LOHARDAGA(GC),SER - [220100214	4/1997	194.07 -	335.00	226.39	06/2004 -	-

(Aug, 2016)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
58	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [N220100205]	4/1997	218.24 236.41	525.00	549.50	- -	03/2019
59	NANDYAL-YERRAGUNTALA(NL),SCR - [N220100192]	3/1996	155.74 164.36	966.98	901.74	02/2009 12/2017	12/2017
60	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	9/2006	324.90 -	516.40	419.63	03/2010 -	12/2017
61	RAJATGARH-BARANG(LD),ECOR - [N220100286]	4/1999	166.16 -	370.00	358.96	02/2009 02/2009	12/2016
62	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [N220100149]	4/1995	304.00 -	631.78	322.36	12/2012 -	-
63	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,581.53	665.09	03/2010 -	03/2017
64	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [N220100106]	12/1994	124.43 -	1,010.00	944.02	- -	-
65	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]	4/2010	203.40 -	203.40	258.44	- -	-
66	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE- PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	4/2011	190.10 -	355.96	192.71	- -	03/2019
67	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	227.37	03/2015 -	07/2015
68	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	3/2006	201.00 -	230.00	245.21	- -	10/2015
69	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [N220100258]	3/2002	625.30 408.76	876.10	842.61	06/2007 -	-
70	NANGALDAM-TALWARA(NL),NR - [N220100188]	3/1981	450.00 -	2,100.00	502.85	07/2012 -	-
71	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [N220100256]	4/1999	744.71 -	1,126.79	808.84	- -	10/2016
72	KANPUR KASGANJ MATHURA(GC) NER - [N220100197]	3/1997	677.97 1,062.36	1,679.13	1,721.58	- -	12/2016
73	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	813.34 -	3,451.00	1,780.37	03/2014 -	03/2020
74	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	4/1996	1,676.31 -	7,000.00	6,402.53	03/2009 -	03/2017
75	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	9/2006	300.00 -	2,145.00	362.59	- -	03/2020
76	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	200.00 -	780.00	320.50	- -	03/2019
77	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	559.91	538.54	07/2014 -	-
78	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	312.12 -	508.00	326.08	- -	03/2018
79	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]	4/1999	523.17 -	1,653.55	1,071.96	- -	03/2018
80	CHENGANNUR-CHINGAVANAM - [N22000203]	4/2006	191.72 -	342.85	280.75	- -	-
81	GADWAL - RAICHUR (NL), SCR - [N220100270]	4/1998	92.63 -	270.00	318.58	02/2011 -	-
82	DEOGHAR - SULTANGANJ (INL), ER - [N220100273]	4/2000	607.09 -	1,500.00	614.98	12/2012 12/2012	-

(Aug, 2016)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
83	JIND-SONEPAT (NL),NR - [220100280	1/2004	238.56 -	740.00	732.57	03/2012 01/2016	01/2016
	Total		24,880.49 -	79,726.70	57,377.05		
	ROAD TRANSPORT AND HIGHWAYS						
84	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	434.58	02/2009 -	09/2016
85	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	217.29	04/2009 -	03/2017
86	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	167.64	282.52	11/2008 -	12/2016
87	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	199.25	11/2008 -	12/2016
88	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281	12/2003	200.00 -	200.00	251.26	04/2009 -	12/2016
89	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	12/2016
90	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	883.59	04/2016 -	03/2017
91	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131	2/2009	1,693.75 -	1,693.75	2,675.34	08/2011 -	12/2016
92	CHENNAI-TADA(SIX LANE) - [N24000129	4/2009	353.37 -	353.37	365.08	10/2011 -	-
93	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123	3/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017
94	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	3/2010	1,509.10 -	1,509.10	3,272.71	09/2012 -	12/2016
95	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145	11/2010	1,585.00 -	1,585.00	2,035.69	05/2013 -	06/2017
96	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144	9/2010	852.00 -	852.00	902.60	03/2013 -	12/2016
97	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290	12/2003	195.00 -	195.00	294.65	06/2008 -	09/2016
98	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	314.79	06/2008 06/2016	07/2016
99	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	623.47	10/2013 -	12/2017
100	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	976.34	07/2013 -	12/2016
101	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017
102	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	07/2016
103	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	832.39	11/2013 -	12/2016
104	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,282.25	06/2013 -	08/2016
105	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	880.96	02/2013 -	12/2016

(Aug, 2016)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,415.99	07/2013 -	12/2016
107	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,159.00	4,266.60	06/2015 -	07/2016
108	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	1,890.00	09/2015 -	02/2017
109	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	368.94	01/2014 -	09/2016
110	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,475.09	09/2014 -	12/2016
111	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,652.28	06/2014 -	03/2017
112	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,771.99	08/2013 -	10/2017
113	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,202.40	08/2013 -	12/2016
114	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,863.25	09/2014 -	06/2017
115	BHUBANESWAR TO PURI - [N24000195]	3/2011	500.29 -	500.29	875.56	08/2013 -	12/2016
116	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	1,363.70	06/2014 -	12/2016
117	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	761.26	07/2008 -	-
118	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANON AND NAGPUR BYPASS - [N24000509]	4/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018
119	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	2,946.14	10/2011 -	07/2016
120	NAGPUR - KONDHALI - [N24000472]	9/2005	168.00 -	168.00	279.92	06/2006 -	-
121	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,135.69	07/2017 -	01/2018
122	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	551.33	11/2013 -	07/2016
123	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	604.85	07/2013 -	12/2016
124	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	510.91	04/2014 -	03/2017
125	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	899.81	03/2014 -	03/2017
126	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	2,851.90	05/2014 -	12/2016
127	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	696.22	01/2014 -	06/2017
128	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]	12/2003	237.80 -	237.80	418.17	06/2008 -	07/2016
129	SAMAIKHALI - GANDHIDHAM - [N24000179]	9/2010	805.39 -	805.39	1,407.71	03/2013 -	09/2016
130	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	309.52	04/2008 01/2017	12/2016

(Aug, 2016)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
131	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	409.32	04/2010 09/2016	09/2016
132	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72 -	264.72	322.50	06/2008 -	09/2016
133	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	1,893.03	03/2013 -	12/2016
134	MURADABAD-BAREILY - [N24000154]	4/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	12/2016
135	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]	5/2013	1,348.20 -	1,348.20	1,630.57	02/2014 -	08/2017
136	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	871.15	09/2014 -	10/2017
137	DEOLI-KOTA - [N24000148]	1/2011	593.00 -	593.00	1,038.84	07/2013 -	12/2016
138	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,288.00	3,846.48	11/2011 -	12/2016
139	TALEGAON-AMRAVATI - [N24000140]	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-
140	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	373.08	07/2009 -	03/2017
141	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94 -	332.94	518.85	09/2008 -	09/2016
142	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	202.41	05/2008 12/2016	12/2016
143	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	348.16	418.19	09/2007 -	09/2016
	Total		49,587.06 -	51,385.65	77,925.63		
	<u>STEEL</u>						
144	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	175.94	178.91	12/2015 -	03/2017
	Total		149.73 -	175.94	178.91		
	<u>URBAN DEVELOPMENT</u>						
145	BANGALORE METRO RAIL PROJECT - [N28000008]	5/2006	6,395.00 -	14,405.01	14,081.31	06/2011 12/2013	01/2017
	Total		6,395.00 -	14,405.01	14,081.31		
	Grand Total		128,367.80	226,776.07	215,977.19		

Annexure - III

Details of Projects Ahead of Schedule w.r.t. Original Schedule

							(August 2016)	
							Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	
1	2	3	4	5	6	7	8	
	<u>COAL</u>							
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52	555.52	4.36	03/2021 -	03/2017	
2	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	103.25	03/2019 -	03/2018	
	Total		860.04 -	860.04	107.61			
	<u>PETROLEUM</u>							
3	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	366.03	01/2017 -	09/2016	
4	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	1,899.13	04/2019 -	03/2019	
5	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	4.91	02/2019 -	12/2018	
	Total		6,735.36 -	6,735.36	2,270.07			
	<u>URBAN DEVELOPMENT</u>							
6	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	10/2019 -	12/2018	
7	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017	
	Total		6,401.00 -	6,401.00	.00			
	Grand Total		13,996.40	13,996.40	2,377.68			

Annexure - IV

Details of On Schedule Projects w.r.t. Original Schedule

(August 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	314.61	26.30	09/2018 -	09/2018
	Total		314.61 -	314.61	26.30		
	<u>COAL</u>						
2	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	108.64	03/2021 -	03/2021
3	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
4	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
5	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	111.94	03/2021 -	03/2021
6	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	338.55	03/2021 -	03/2021
7	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.55	03/2018 -	03/2018
8	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	81.73	03/2025 -	03/2025
9	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	330.34	03/2018 -	03/2018
10	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	17.60	03/2020 -	03/2020
11	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
12	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	112.08	03/2021 -	03/2021
13	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
14	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
15	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	0.27	03/2020 -	03/2020
16	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	57.02	03/2020 -	03/2020
17	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	193.77	03/2022 -	03/2022
18	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	154.15	03/2020 -	03/2020
19	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	85.12	03/2019 -	03/2019
20	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	1.95	03/2019 -	03/2019

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,093.73	03/2023 -	03/2023
22	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
23	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.53	03/2023 03/2023	03/2023
24	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	1.27	03/2019 -	03/2019
25	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	90.59	03/2020 -	03/2020
26	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
27	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	59.62	03/2023 -	03/2023
28	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	74.76	12/2019 -	12/2019
29	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
30	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.57	09/2019 -	09/2019
31	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	249.04	03/2020 -	03/2020
32	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
33	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
34	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
35	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
36	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	110.96	03/2020 -	03/2020
37	GOKUL - [N06000120]	11/2014	267.67 -	267.67	178.29	03/2018 -	03/2018
38	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	13.00	03/2023 -	03/2023
39	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	14.84	03/2019 -	03/2019
40	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.30	03/2019 -	03/2019
41	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
42	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	57.98	03/2021 -	03/2021
43	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	840.32	03/2023 03/2023	03/2023
44	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	27.56	03/2021 -	03/2021
45	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	621.84	03/2026 -	03/2026

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		46,524.81 -	46,524.81	6,121.66		
	<u>FERTILISERS</u>						
46	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	37.96	12/2017 -	12/2017
	Total		482.85 -	482.85	37.96		
	<u>HEALTH AND FAMILY WELFARE</u>						
47	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	70.00	03/2018 -	03/2018
	Total		505.58 -	505.58	70.00		
	<u>MINES</u>						
48	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT JATH SANGLI MA ARASHTRA - [N10000008]	12/2015	355.13 -	355.13	243.19	11/2016 11/2016	11/2016
49	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	201.17	11/2016 11/2016	11/2016
	Total		699.63 -	699.63	444.36		
	<u>PETROLEUM</u>						
50	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	327.78	-	04/2018 -	04/2018
51	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	0.86	12/2018 -	12/2018
52	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219]	8/2014	393.00 -	393.00	-	04/2018 -	04/2018
53	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]	2/2016	367.11 -	367.11	19.42	04/2017 -	04/2017
54	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	80.29	01/2018 -	01/2018
55	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,190.69	83.38	04/2018 -	04/2018
56	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]	1/2015	4,619.94 -	4,619.94	1,382.08	12/2017 -	12/2017
57	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
58	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	195.63	81.86	09/2018 -	09/2018
59	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	173.28	104.89	01/2017 -	01/2017
60	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	231.02	02/2020 -	02/2020
61	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]	8/2009	1,793.00 -	1,793.00	1,532.49	12/2016 -	12/2016
63	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220]	2/2015	184.00 -	184.00	12.43	12/2017 -	12/2017
64	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	183.99	09/2016 -	09/2016
65	DE-BOTTLENECKING OF SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	1,465.03	03/2017 03/2017	03/2017
66	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	141.59	12/2016 -	12/2016
67	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	6.92	05/2019 -	05/2019
68	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	4,309.00	05/2017 05/2017	05/2017
69	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	62.19	03/2018 -	03/2018
70	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	62.87	10/2018 -	10/2018
71	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	678.00	-	02/2017 -	02/2017
72	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
73	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	290.83	12/2017 -	12/2017
74	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221]	1/1991	694.00 -	694.00	57.19	10/2018 -	10/2018
75	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	93.83	04/2018 -	04/2018
76	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	58.20	09/2017 -	09/2017
77	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
78	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,263.13	05/2017 -	05/2017
79	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	1,221.41	05/2019 05/2019	05/2019
	Total		62,673.96 -	62,257.19	12,744.90		
	POWER						
80	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017
81	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	42.80	07/2017 -	07/2017
82	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	35.90	11/2017 -	11/2017
83	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	32.40	07/2018 -	07/2018
84	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	702.80	04/2018 -	04/2018

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	256.02	10/2016 -	10/2016
86	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	-	05/2019 -	05/2019
87	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	62.60	03/2018 -	03/2018
88	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	170.30	10/2016 -	10/2016
89	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	3.50	05/2018 -	05/2018
90	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
91	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	89.30	07/2018 -	07/2018
92	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	447.48	12/2016 -	12/2016
93	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	-	04/2019 -	04/2019
94	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.13	-	06/2018 -	06/2018
95	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
96	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	-	11/2018 -	11/2018
97	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
98	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	5.70	03/2018 -	03/2018
99	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	3,925.00	08/2018 -	08/2018
100	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
101	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	235.70	11/2016 -	11/2016
102	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	1,006.50	05/2018 -	05/2018
103	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	322.50	04/2017 -	04/2017
104	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	364.60 -	364.60	-	05/2018 -	05/2018
105	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	17.90	03/2017 -	03/2017
106	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	1,718.00	03/2019 -	03/2019
107	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	4.00	07/2018 -	07/2018
108	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]	1/2014	1,788.41 -	1,788.41	-	09/2017 -	09/2017

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
109	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	60.30	03/2018 -	03/2018
110	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	6,210.00	09/2017 -	09/2017
111	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	210.00	09/2019 -	09/2019
112	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04 -	187.04	5.90	06/2018 -	06/2018
113	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	65.40	10/2017 -	10/2017
114	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	180.40	04/2017 -	04/2017
115	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	175.00	07/2020 -	07/2020
116	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	236.50	11/2017 -	11/2017
117	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	127.90	02/2017 -	02/2017
118	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	1/1991	454.11 -	454.11	-	04/2018 -	04/2018
119	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	-	06/2018 -	06/2018
120	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	1,794.00	09/2019 -	09/2019
121	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	0.10	01/2018 -	01/2018
122	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	935.60	04/2018 -	04/2018
123	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	-	11/2019 -	11/2019
124	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	881.40	03/2018 -	03/2018
	Total		114,496.74 -	114,496.74	20,108.50		
	RAILWAYS						
125	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
126	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	-	03/2021 -	03/2021
127	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
128	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
129	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	4,295.30	87.74	12/2026 -	12/2026

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
130	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
131	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021
132	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
133	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	0.36	12/2016 -	12/2016
134	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020
135	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	682.92	03/2019 -	03/2019
136	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	0.40	03/2021 -	03/2021
137	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,750.00	-	03/2022 -	03/2022
138	VIRAMGAM BHILDI - [N22000391]	4/1990	237.13 -	237.13	25.05	03/2018 -	03/2018
139	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	-	03/2021 -	03/2021
140	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	927.01	516.85	03/2019 -	03/2019
141	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	0.46	12/2024 -	12/2024
142	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.65	403.93	12/2020 -	12/2020
143	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
144	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	480.38	12/2021 -	12/2021
145	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	0.12	12/2020 -	12/2020
146	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.25	458.72	12/2020 -	12/2020
147	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	0.23	12/2020 -	12/2020
148	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	482.81	03/2020 -	03/2020
149	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
150	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	0.93	03/2021 -	03/2021
151	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	108.75	03/2021 -	03/2021
152	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	-	03/2020 -	03/2020
153	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	495.97	03/2020 -	03/2020

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
154	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	26.23	03/2020 -	03/2020
155	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.13	12/2025 -	12/2025
156	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	-	03/2021 -	03/2021
157	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.93	12/2021 -	12/2021
158	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
159	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
	Total		47,470.93 -	48,947.60	4,119.50		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
160	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	6.02	06/2018 -	06/2018
161	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]	7/2014	401.11 -	401.11	246.10	01/2017 -	01/2017
162	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	46.11	05/2018 -	05/2018
163	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
164	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	6.33	03/2018 -	03/2018
165	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,620.11	01/2018 -	01/2018
166	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
167	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	957.30	09/2016 -	09/2016
168	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
169	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
170	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
171	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018
172	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
173	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
174	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017
175	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
176	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017
177	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	63.38	07/2017 -	07/2017
178	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017
179	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	0.54	05/2017 -	05/2017
180	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	282.41	75.32	08/2016 -	08/2016
181	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]	11/2010	305.49 -	305.49	-	03/2017 -	03/2017
182	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	1/1991	358.22 -	358.22	200.21	10/2016 -	10/2016
183	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
184	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
185	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
186	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
187	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	-	01/2019 -	01/2019
188	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]	5/2014	497.89 -	497.89	-	04/2017 -	04/2017
189	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
190	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	66.59	03/2018 -	03/2018
191	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	-	10/2018 -	10/2018
192	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	-	03/2018 -	03/2018

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
193	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]	12/2013	220.72 -	220.72	113.36	11/2016 -	11/2016
194	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
195	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017
196	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
197	4 LANING FROM KALIABHOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
198	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
199	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
200	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
201	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377]	1/2014	397.04 -	397.04	17.71	10/2016 -	10/2016
202	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]	6/2015	532.49 -	532.49	166.22	05/2017 -	05/2017
203	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017
204	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	-	06/2018 -	06/2018
205	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
206	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]	10/2013	283.45 -	283.45	21.03	10/2016 -	10/2016
207	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]	10/2014	244.30 -	156.09	-	12/2016 -	12/2016
208	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
209	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
210	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	-	05/2018 -	05/2018
211	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	-	06/2018 -	06/2018

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	41.21	10/2017 -	10/2017
213	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
214	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]	10/2014	227.74 -	227.74	-	10/2016 -	10/2016
215	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	-	05/2018 -	05/2018
216	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
217	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	225.02	-	12/2018 -	12/2018
218	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
219	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	-	08/2016 -	08/2016
220	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,544.63	11/2016 -	11/2016
221	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	133.00	04/2018 -	04/2018
222	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
223	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
224	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]	6/2015	563.92 -	563.92	21.06	12/2017 -	12/2017
225	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
226	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	292.34	02/2018 -	02/2018
227	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
228	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	234.99	11/2017 -	11/2017
229	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342]	5/2015	709.00 -	709.00	20.56	09/2017 -	09/2017
230	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	2.18	12/2017 -	12/2017
231	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	111.99	02/2018 -	02/2018
232	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018

						(August 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
233	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589	6/2016	649.00	649.00	-	06/2019	06/2019
234	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56	768.56	-	03/2018	03/2018
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26	269.26	218.10	10/2016	10/2016
236	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32	327.32	162.33	05/2017	05/2017
237	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51	788.51	-	03/2018	03/2018
238	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08	538.08	70.35	02/2018	02/2018
239	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00	597.00	81.34	10/2017	10/2017
240	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340	12/2014	451.58	451.58	28.00	06/2017	06/2017
241	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39	260.39	119.70	11/2016	11/2016
242	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00	667.00	-	07/2018	07/2018
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41	229.41	10.32	05/2018	05/2018
244	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66	2,168.66	-	06/2019	06/2019
245	FOUR LANING OF VARANASI BYPASS - [N24000356	5/2015	261.09	261.09	41.87	05/2017	05/2017
246	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368	11/2014	563.92	563.92	146.29	11/2016	11/2016
247	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579	1/2014	1,408.85	1,408.85	-	10/2016	10/2016
248	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23	239.23	40.30	12/2017	12/2017
249	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53	1,027.53	5.92	06/2018	06/2018
250	PADI - DAHOD - [N24000353	11/2014	279.14	279.14	122.20	05/2017	05/2017
251	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28	574.28	-	07/2018	07/2018
252	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343	9/2015	341.61	341.61	140.65	09/2017	09/2017
253	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00	1,083.00	-	06/2018	06/2018
254	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46	934.46	57.93	03/2018	03/2018
255	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28	815.28	-	06/2018	06/2018

(August 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
256	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19 -	425.19	274.20	09/2016 -	09/2016
257	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	46.68	02/2017 -	02/2017
258	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	121.88	04/2017 -	04/2017
259	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]	10/2014	264.72 -	264.72	136.71	04/2017 -	04/2017
260	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	65.88	07/2017 -	07/2017
261	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
	Total		56,899.48 -	57,038.86	8,179.01		
	<u>SHIPPING AND PORTS</u>						
262	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]	12/2014	274.85 -	274.85	189.52	04/2017 -	04/2017
263	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	235.15	176.55	06/2017 -	06/2017
264	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	42.57	12/2017 -	12/2017
265	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
	Total		928.29 -	978.33	408.64		
	<u>STEEL</u>						
266	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	17.32	09/2017 -	09/2017
267	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	136.65	03/2018 -	03/2018
268	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	200.20	12/2016 -	12/2016
269	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
270	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]	4/2014	151.33 -	151.33	15.04	09/2017 -	09/2017
271	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]	2/2014	787.29 -	787.29	328.23	12/2016 -	12/2016
272	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	53.47	03/2018 -	03/2018
273	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	116.30	12/2017 -	12/2017

							(August 2016)	
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8	
274	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	27.47	09/2018 -	09/2018	
275	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	66.80	10/2017 -	10/2017	
276	COKE OVEN BATTERY-5 - [N12000117	12/2011	2,858.00 -	2,500.00	209.43	12/2017 -	12/2017	
277	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	2.44	06/2020 -	06/2020	
278	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	91.91	04/2018 -	04/2018	
279	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094	4/2015	3,127.30 -	3,127.30	380.84	04/2018 -	04/2018	
	Total		17,378.76 -	17,045.15	1,646.10			
	<u>URBAN DEVELOPMENT</u>							
280	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	221.25	03/2018 -	03/2018	
281	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	157.84	49.18	03/2017 -	03/2017	
282	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	5,298.00	1,680.80	11/2019 -	11/2019	
	Total		13,101.84 -	14,135.84	1,951.23			
	Grand Total		361,477.48	363,427.19	55,858.16			

Annexure - V

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	10/2017	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071]	10/2012	217.60 -	244.10	03/2015 -	-	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.59	03/2015 -	03/2020	201.51
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
8	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2019	0.02
9	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,953.12 -	3,630.07			
	<u>FERTILISERS</u>						
10	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2017	5.89
	Total		197.79 -	209.44			
	<u>HEAVY INDUSTRY</u>						
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>PETROCHEMICALS</u>						
12	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	-	82.49
	Total		5,460.61 -	9,965.00			
	<u>PETROLEUM</u>						
13	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	06/2018	24.53
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	09/2016	70.49
15	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	02/2018	17.66
16	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	09/2016	63.54
17	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
18	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2016	45.83
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
22	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	-	67.62
24	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	12/2016	37.72
25	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	01/2017	19.35
26	BULK PETROLEUM OIL AND LUBRICANT (POL) DEPOT AT IMPHAL, MANIPUR - [N16000215]	08/2010	103.02 -	171.04	07/2016 -	08/2016	66.03
	Total		15,385.77 -	18,964.03			
	<u>POWER</u>						
27	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
28	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
29	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	03/2017	54.59

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
30	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
31	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]	12/2009	1,216.83 -	1,428.87	08/2012 -	11/2016	17.43
32	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2017	36.79
33	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	05/2011	1,961.87 -	2,310.58	05/2014 -	10/2016	17.77
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14
35	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	06/2017	54.25
36	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]	05/2010	250.03 -	390.51	01/2013 -	09/2016	56.19
37	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	06/2017	36.01
38	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	10/2016	83.21
39	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06
40	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	10/2017	147.51
41	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
42	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	03/2017	31.17
43	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	12/2016	23.13
44	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,581.04	08/2013 -	05/2017	175.45
45	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
46	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2016	16.63
47	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	03/2017	27.60
48	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	-	58.79
49	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2017	22.93
50	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
51	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	01/2012	1,422.85 -	1,875.13	01/2015 -	12/2016	31.79

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
52	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,441.52	07/2006 02/2015	09/2017	290.95
53	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	-	139.32
	Total		68,713.35 -	118,143.29			
	<u>RAILWAYS</u>						
54	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	02/2016	299.62
55	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	-	3,531.98
56	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
57	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	870.00	- -	-	459.31
58	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]	03/1999	2,957.21 -	3,020.95	07/2005 -	06/2018	2.16
59	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
60	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	536.26
61	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
62	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	-	543.99
63	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
64	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
65	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
66	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,500.00	12/2012 12/2012	-	147.08
67	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	01/2016	210.19
68	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
69	RAMGANJ-MUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	3,000.00	- -	-	537.05
70	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
71	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
72	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
73	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N220100325]	04/1998	183.23	1,202.70	02/2015	-	556.39
74	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	10/2016	154.85
75	TALCHER-BIMALAGARH(NL)(ECOR) - [N220100328]	04/2005	810.78	811.36	-	-	0.07
76	RAICHUR-GUNTAKAL(DL)(SCR) - [N220100329]	04/2003	136.62	376.00	12/2007 03/2010	-	175.22
77	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045]	03/1997	261.70	318.00	02/2006	-	21.51
78	BHOPAL BINA 3D LINE DOUBLING - [N220000077]	09/2007	687.20	950.00	03/2010	06/2017	38.24
79	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N220000079]	09/2007	404.19	2,072.50	-	-	412.75
80	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080]	09/2006	343.17	1,065.00	-	-	210.34
81	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]	09/2006	125.00	490.00	-	-	292.00
82	TIDIVANAM-NAGARI (NL) - [N220000085]	09/2006	456.00	1,080.00	-	-	136.84
83	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N220000094]	02/2008	171.10	275.08	03/2012	03/2016	60.77
84	BHAIRABI SAIRONG, NL, NEFR - [N220000100]	04/2008	619.34	4,600.00	04/2014	03/2020	642.73
85	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N220000002]	04/1996	332.92 283.95	477.88	03/2012	-	43.54
86	VIRAMGAM-BHILDI(WR),GC - [N220100062]	04/1990	155.66	548.01	- 03/2010	03/2019	252.06
87	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]	04/2006	378.56	1,160.47	-	-	206.55
88	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]	07/2006	743.00	1,825.00	03/2008 06/2008	-	145.63
89	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N220000113]	04/2008	653.19	658.07	03/2014	03/2019	0.75
90	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N220000120]	04/2008	603.04	1,421.25	03/2012	03/2022	135.68
91	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N220000125]	04/2006	117.36 196.95	203.00	03/2011	01/2011	72.97
92	KATAKHAL TO BHAIRABI - [N220000126]	04/1998	227.90	509.00	12/2012	03/2016	123.34
93	WARDHA-NANDED MAHARASHTRA - [N220000231]	04/2008	499.30	2,491.43	-	-	398.98
94	KALYAN-KASARA 3RD LINE - [N220000233]	04/2011	277.70	792.89	-	-	185.52
95	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N220000247]	04/2011	184.06	199.12	-	-	8.18
96	WARDHA-SEWAGRAM NGP 3RD LINE - [N220000250]	04/2012	297.85	540.02	-	-	81.31

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
97	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	365.00	- -	-	269.66
98	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
99	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
100	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
101	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
102	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
103	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
104	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
105	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
106	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
107	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
108	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
109	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
110	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
111	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
112	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
113	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
114	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
115	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
116	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
117	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,170.00	01/1999 -	-	153.83
118	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017	77.08
119	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
120	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
121	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,271.50	- -	-	341.34
122	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	768.87 -	926.00	- -	12/2018	20.44
123	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	-	259.68
124	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
125	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2017	233.33
126	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	5,050.00	05/2008 -	03/2023	1,939.09
127	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
128	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
129	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
130	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64
131	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
132	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,658.00	03/2011 -	03/2019	1,227.45
133	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
134	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47
135	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	780.00	- -	03/2019	290.00
136	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	2,145.00	- -	03/2020	615.00
137	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	3,000.00	03/2015 -	03/2021	252.94
138	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
139	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58
140	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
141	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	360.00	- -	-	27.24
142	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
143	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,679.13	- -	12/2016	147.67

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
144	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79 -	- -	10/2016	51.31
145	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	780.98 -	- -	-	90.45
146	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]	04/2008	516.23 -	735.00 -	03/2014 -	-	42.38
147	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00 -	07/2012 -	-	366.67
148	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00 -	11/2002 -	12/2018	682.60
149	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10 -	06/2007 -	-	40.11
150	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53 -	03/2010 -	03/2017	386.62
151	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	631.78 -	12/2012 -	-	107.82
152	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	370.00 -	02/2009 02/2009	12/2016	122.68
153	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	516.40 -	03/2010 -	12/2017	58.94
154	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98 -	02/2009 -	12/2017	520.89
155	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	525.00 -	- -	03/2019	140.56
156	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00 -	07/2008 -	-	284.00
157	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81 -	03/1998 -	12/2019	359.96
158	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00 -	03/2007 03/2007	-	160.76
159	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69 -	06/2005 -	-	155.02
160	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00 -	06/2004 -	-	72.62
161	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00 -	- -	-	840.53
162	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]	04/1997	836.26 -	1,072.52 -	- -	-	28.25
163	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	1,289.92 -	- -	12/2016	337.26
164	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78 -	- -	-	902.01
165	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57 -	03/2013 -	-	81.45
166	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00 -	- -	-	880.00

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
167	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
168	KAKINADA-PITHAPURAM - [N22000314]	03/1999	215.06 -	220.29	- -	-	2.43
169	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	03/2021	63.70
170	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	10/2015	14.43
171	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	- -	03/2020	40.44
172	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	- -	03/2020	52.77
173	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
174	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
175	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	355.96	- -	03/2019	87.25
176	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
177	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	620.00	- -	09/2019	3.33
178	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
179	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	668.34	06/1999 -	-	0.80
180	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
181	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
182	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
183	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	-	71.11
184	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
185	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
186	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
187	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	09/2015	27.06
188	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
189	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
190	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
191	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	860.00	-	12/2018	88.60
192	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	-	03/2017	17.92
193	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	-	-	2.34
194	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019	12/2022	226.23
195	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	-	-	62.32
196	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	-	-	82.25
197	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	-	-	162.39
198	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015	12/2016	53.44
199	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013	12/2016	37.41
200	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015	-	88.40
201	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	-	12/2017	41.36
202	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	-	-	32.26
203	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	-	-	84.98
204	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	-	-	32.80
205	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	-	-	338.91
206	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	-	252.66
207	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	-	-	72.37
208	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	-	-	18.16
209	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	-	-	129.22
210	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	-	-	78.78
211	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	-	-	180.17
212	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	-	-	91.71

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
213	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39	1,480.83	-	03/2018	80.06
214	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14	346.15	-	-	28.14
215	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42	380.00	-	-	71.62
216	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00	1,857.00	03/2007	03/2016	107.49
217	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00	967.85	-	03/2019	284.07
218	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77	445.00	-	03/2018	112.14
219	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55	330.00	-	03/2018	16.38
220	ERODE-PALANI - [N22000199]	04/2008	288.57	603.22	-	-	109.04
221	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41	450.00	-	-	173.71
222	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00	951.24	-	-	285.12
223	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72	342.85	-	-	78.83
224	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02	6,000.00	-	03/2020	46.95
225	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22	471.00	-	-	94.45
226	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52	394.28	-	03/2017	63.25
227	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82	450.00	-	03/2019	171.38
228	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17	1,653.55	-	03/2018	216.06
229	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12	508.00	-	03/2018	62.76
230	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07	386.68	-	03/2019	57.14
231	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68	816.55	03/2016	12/2017	29.06
232	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43	800.00	-	-	33.02
233	PIRPAINI-JASIDIH - [N22000219]	04/2013	915.98	2,103.00	-	-	129.59
234	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00	1,272.19	-	-	101.93
235	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00	668.00	03/2020	03/2020	27.48

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
236	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	233.73	04/2014 -	03/2018	24.82
237	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
238	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	05/2015	5.12
239	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
240	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
241	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	943.60	12/2024 -	12/2024	25.72
	Total		97,908.57 -	250,572.15			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
242	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	09/2016	28.93
243	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2017	92.75
244	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	12/2016	80.68
245	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2017	68.99
246	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50
247	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]	11/2014	573.96 605.00	605.00	- -	-	5.41
248	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
249	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
250	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	161.70	07/2015 -	-	2.88
251	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25
252	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
253	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	12/2016	2.65
254	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
255	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
256	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
257	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
258	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
259	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
260	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2016	51.83
	Total		7,246.67 -	10,240.42			
	<u>SHIPPING AND PORTS</u>						
261	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2016	300.00
262	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20
263	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
264	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
265	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
266	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	12/2016	12.04
267	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79
268	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29
269	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	09/2017	42.39
270	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50

(August 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		1,639.71 -	2,169.02			
	<u>URBAN DEVELOPMENT</u>						
271	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	14,405.01	06/2011 -	01/2017	125.25
272	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA [N28000068	02/2011	241.33 -	349.33	11/2014 -	-	44.75
273	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	5,298.00	11/2019 -	11/2019	24.25
	Total		10,900.33 -	20,052.34			
	Grand Total		229,210.02	468,328.93			

Annexure - VI

Details of Delayed Projects w.r.t. Original Schedule

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,264.12	09/2010 09/2016	10/2017	85	62.57	Local Protests - Law & Order issues
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	8,782.00	12/2015 11/2016	11/2018	35	0	NR
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	6,590.00	12/2016 03/2017	12/2019	36	0	Delay in supply/equipment, lack of skilled manpower, cash flow problems
	Total		27,271.00 -	29,456.00	20,636.12					
	<u>CIVIL AVIATION</u>									
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	435.10	01/2011 -	09/2017	80	0	i) Long spell of Rainy Season and chilled winter, ii) Non availability of land for AAI residential complex
	Total		309.46 -	309.46	435.10					
	<u>COAL</u>									
5	WIND POWER PROJECT, KAZHUNEERKULAM, TAMIL NADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	229.14	10/2014 -	10/2016	24	0	i) Land acquisition, ii) delay in civil works, iii) delay in supply of equipment
6	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	122.07	05/2014 -	10/2016	29	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator
7	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	86.46	04/2014 -	11/2016	31	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	319.40	03/2010 -	03/2017	84	0	i) Coal evacuation problem, ii) delay in completion of railway line
9	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL, JHARKHAND	12/2007	341.63 -	341.63	121.94	03/2011 -	03/2017	72	0	i) Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator.

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 486.57	486.57	204.72	03/2012 03/2018	03/2017	60	87.58	i) Land acquisition ii) Rehabilitation and Resettlement problem
11	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	122.11	12/2012 -	03/2017	51	0	i)Contractual Issues ii)Adverse Geomining Conditions
12	RAJMAHAL OC EXP. - [N06000056]JEL,JHARKHAND	09/2009	153.82 -	153.82	84.21	03/2014 -	03/2017	36	0	Delay/ non issuance of Patta for land/plots allotted to PAFs in area acquired under CBA Act & delay in finalization of pending title cases of land in CBA tribunals.
13	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	87.72	03/2015 -	03/2017	24	0	N.R.
14	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	167.29	03/2012 -	03/2017	60	0	Delay in forest land diversion
15	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	96.01	03/2012 -	03/2017	60	0	Delay in land authentication ii) Delay in release of forest land.
16	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	152.14	03/2013 -	03/2017	48	0	i) Delay in acquisition of land
17	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	72.47	03/2014 -	03/2017	36	0	i) Delay in land authentication ii) Delay in release of forest land.
18	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	03/2017	35	0	Delay in Environmental Clearance
19	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	39.49	06/2015 -	03/2017	21	0	i) Delay in land acquisition ii) Resettlement and Rehabilitation issues.
20	SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	121.47	03/2012 -	03/2018	72	0	Adverse Geo-mining condition.
21	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	197.83	03/2014 -	03/2018	48	0	Delay in getting possession of forest land and environment clearance.
22	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	138.67	03/2016 -	03/2018	24	0	i) Delay in getting CTO(consent to operate) ii) Delay in getting forest clearance.
23	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2018	84	0	i) Delay in diversion of forest land.
24	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	147.95	03/2012 -	03/2018	72	0	i) Delay in receiving forestry clearance and handing over the site.
25	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2018	24	0	i) Delay in acquisition of land and forestry clearance.

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (AS Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
26	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.09	03/2015 -	03/2018	36	0	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues. iii) delay in diversion of forest land.
27	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	0	i) Land acquisition ii) Rehabilitation and Resettlement problem
28	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	85.36	03/2015 -	03/2018	36	0	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues. iii) delay in diversion of forest land.
29	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	123.92	03/2016 -	03/2018	24	0	Delay in land acquisition and forestry clearance.
30	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	486.27	92.33	03/2016 -	03/2018	24	12.97	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues
31	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	2,503.92	12/2015 04/2018	04/2018	28	0	i) Delay in supply of equipments ii) Delay in civil works.
32	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	207.09	03/2017 -	05/2018	14	0	i) Rehabilitation and Resettlement problem
33	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	244.64	03/2018 -	09/2018	6	0	i) Delay in forest clearance ii) Delay in tendering of CHP.
34	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	278.09	03/2013 -	11/2018	68	0	i) Delay in forest land diversion and construction of MGR by NTPC.
35	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	182.37	03/2010 -	03/2019	108	0	i) Land acquisition ii) Rehabilitation and Resettlement problem
36	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	208.48	03/2012 -	03/2019	84	0	Delay in forest land diversion and EMP clearance.
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	188.94	03/2013 -	03/2019	72	.02	Delay in forest land diversion and EMP clearance.
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	32.46	07/2016 -	03/2019	32	0	Delay in Acquisition of non forest land and R&R issues.
39	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	54.30	04/2015 -	04/2019	48	0	i) Land Acquisition ii) Contractual issues.
40	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	1,458.17	82.49	06/2015 08/2019	08/2019	50	0	i) Delay in completion of linked project.

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
41	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.59	35.44	03/2015 -	03/2020	60	201.51	i) Delay in forest and environment clearance ii) Delay in land acquisition.
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	4.40	03/2014 -	03/2020	72	0	i) Delay in forest and environment clearance ii) Delay in land acquisition.
43	MAGADH OC 20 MTY (CCL) - [N06000015]JCL,JHARKHAND	08/2008	706.40 -	706.40	79.50	07/2012 03/2017	03/2021	104	0	i) Coal Evacuation problem ii) Delay in land authentication iii) Delay in forestry clearance and handing over site.
44	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132	16.86	i) Delay in acquisition of non-forest land ii) Resettlement and Rehabilitation issues.
	Total		20,664.84 -	21,325.74	7,670.48					
	<u>FERTILISERS</u>									
45	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	75.85	11/2016 09/2017	09/2017	10	5.89	i) Delay in implementation by the Contractor ii) Financial constraints of the contractor iii) Technical challenge.
	Total		197.79 -	209.44	75.85					
	<u>MINES</u>									
46	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	1,176.00	15.48	09/2017 -	04/2020	31	-36.64	N.R.
	Total		1,856.00 -	1,176.00	15.48					
	<u>STEEL</u>									
47	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	180.35	10/2013 -	09/2016	35	0	i)Contractual issues ii) Delay in environment clearance.
48	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	490.16	04/2016 -	10/2016	6	0	Delay in supply & erection of structures & equipment by M/s Danieli & Essar Projects.

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
49	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	589.13	07/2015 -	11/2016	16	0	N.R.
50	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	16,513.62	03/2013 -	12/2016	45	0	i) Site infringement due to Brown Field Area.ii) Poor performance by the contractor iii) Inadequate resource deployment by Contractor
51	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND	10/2013	245.67 -	245.67	160.88	05/2016 -	03/2017	10	0	i) Delay in supply and erection by the contractors.
52	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH	07/2011	974.76 -	974.76	412.53	07/2016 -	03/2017	8	0	N.R.
53	TURBO BLOWER - 5 - [N12000092]RINL, ANDHRA PRADESH	12/2009	280.00 -	280.00	72.17	09/2016 -	03/2017	6	0	N.R.
54	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	175.94	178.91	12/2015 -	03/2017	15	17.5	N.R.
55	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	650.45	03/2015 -	03/2017	24	0	N.R.
56	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 206.71	206.71	141.17	12/2016 -	07/2017	7	17.79	N.R.
57	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	344.45	07/2015 -	09/2017	26	0	N.R.
58	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	104.50	10/2016 -	09/2017	11	42.39	N.R.
59	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	10,082.02	05/2015 12/2017	12/2017	31	0	i) Delay in obtaining forest clearance ii) Delay in approval from eascoast Railways iii) Inadequate man power and resource mobilization by the contractors.
60	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93 -	188.93	87.53	04/2015 -	12/2016	20	0	Delay in deployment of Security Forces and handing over of clear site by Government.
	Total		38,281.71 -	38,484.54	30,007.87					
	PETROLEUM									

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
61	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	251.66	172.53	06/2012 08/2016	08/2016	50	-6.79	Court Cases
62	BULK PETROLEUM OIL AND LUBRICANT (POL) DEPOT AT IMPHAL, MANIPUR - [N16000215]IOCL, MANIPUR	08/2010	103.02 171.04	171.04	122.29	07/2016 08/2016	08/2016	1	66.03	
63	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	150.26	09/2012 09/2016	09/2016	48	-24.14	Slow progress in civil work and fabrication work Delay in delivery of Nut Shell filters and internal of IGF units.
64	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	16,504.00 -	16,504.00	11,986.69	05/2016 -	09/2016	4	0	Increase in Capacity
65	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL, KARNATAKA	01/2006	993.00 -	1,693.00	1,493.81	01/2012 -	09/2016	56	70.49	Progress is slow due to heavy rains during the period, RoU issue, court case.
66	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	357.01	06/2011 10/2016	10/2016	64	0	Forest clearance, termination of contract
67	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL, BIHAR	04/2013	480.00 -	422.00	288.40	02/2016 10/2016	10/2016	8	-12.08	Delay by vendor
68	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, KARNATAKA	02/2012	666.00 838.08	838.08	648.51	11/2015 11/2016	11/2016	12	25.84	interference by land owners and there is law and order problem, Delay in getting forest clearance and weather problem
69	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,056.23	05/2013 12/2016	12/2016	43	45.83	Increase in scope of work
70	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	187.62	03/2014 05/2016	12/2016	33	0	Slow progress by contractor
71	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	502.33	08/2015 12/2016	12/2016	16	0	Delay in acquisition of land at Balasore by Govt of Odisha
72	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	654.96	04/2015 05/2016	12/2016	20	-39.69	Shut down issues for the hook up, financial problem of contractor, slow progress of contractor
73	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	123.11	05/2015 -	12/2016	19	0	delay in acquisition of additional land
74	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL, MULTI STATE	10/2011	725.00 -	725.00	327.87	11/2016 -	12/2016	1	0	Forest clearance

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (AS Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
75	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	696.37	03/2015 -	12/2016	21	37.72	Heavy rain in Assam, Refloating of tender. Delay in delivery of critical items due to financial instability. Poor participation of vendors bundhs, environmental issues in North East
76	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN	11/2011	310.00 370.00	370.00	-	03/2013 01/2017	01/2017	46	19.35	
77	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL, ASSAM	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30	0	
78	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU	03/2013	3,110.36 -	3,110.36	1,970.53	11/2015 11/2016	02/2017	15	0	Restricted timings for radiography activities
79	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,879.11	03/2013 03/2017	03/2017	48	-3.5	ROU acquisition Delay in forest clearance. Inadequate manpower at -Local problem and court cases by tea gardener. Slow progress in engineering and procurement
80	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	517.01	09/2011 10/2016	03/2017	66	0	Delay in preparation of drawings, shortage of skilled manpower, change in delivery location
81	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	1,426.00	05/2014 03/2017	03/2017	34	0	Retendering
82	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	12/2009	309.81 462.79	462.79	303.92	10/2014 03/2017	03/2017	29	49.38	delay in getting pipeline permission
83	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU	05/2015	257.87 -	257.87	69.50	11/2016 -	03/2017	4	0	Delay due to poor response to purchase & works tender
84	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC, GUJARAT	09/2011	202.25 -	160.16	89.64	07/2016 -	04/2017	9	-20.81	Intermittent problems/ protests. Acquisition of Land Slow manufacturing
85	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC, MULTI STATE	04/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017	25	0	Re-visit of the techno-economics of the project in view of new development.
86	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA	03/2014	238.50 -	238.50	38.87	03/2017 -	08/2017	5	0	Delay in getting approval

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
87	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,124.35	4,124.35	1,022.55	04/2016 12/2017	12/2017	20	0	Non-performance of contractor
88	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00 -	184.00	28.56	06/2017 -	12/2017	6	0	
89	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	108.81	10/2017 -	02/2018	4	17.66	
90	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,350.72	03/2015 03/2018	03/2018	36	29.42	
91	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 03/2018	03/2018	39	0	Non-performance of contractor
92	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	-	08/2015 -	03/2018	31	0	Land acquisition
93	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	507.53	09/2017 03/2018	03/2018	6	0	Change in execution methodology
94	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL, ODISHA	03/2014	3,150.00 -	3,150.00	378.78	09/2017 -	03/2018	6	0	
95	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	439.03	1.57	03/2017 06/2018	06/2018	15	24.53	land litigation
96	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	243.81	01/2013 12/2018	12/2018	71	-10.01	
97	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	0	
98	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	4,588.29	365.19	05/2018 -	08/2018	3	0	
	Total		59,483.71 -	61,030.75	29,593.23					
	POWER									
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	367.82	05/2015 -	08/2016	15	0	Project completed - Completion delayed due to non-availability of shut

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (AS Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
100	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 390.51	390.51	266.70	01/2013 03/2016	09/2016	44	56.19	due to flood/water logging in the area.
101	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	3,426.91	10/2014 -	09/2016	23	0	due to delay in land acquisition of Kanpur S/stn. (completion delayed due to non-availability of shut-down due to system constraints.
102	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	113.00	12/2015 -	09/2016	9	0	Completion matching with TBCB lines.
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	576.22	07/2013 11/2015	10/2016	39	-8.45	Progress affected due to delay in forest/ NBWL clearance & State Govt. clearance. Forest clearance received in Oct'15 Limited working period due to snow-bound area affecting implementation. Work stand still due to disturbance in Kashmir since 07.08.16.
104	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 2,310.58	2,310.58	1,840.05	05/2014 06/2016	10/2016	29	17.77	Land acquisition for Champa S/S was delayed.
105	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	112.53	09/2014 -	10/2016	25	0	i) During the installation of OPGW, RoW problems are being encountered across the TL, which hampered the progress. Work is also delayed due to heavy fog in NR and snowfall in hilly area.
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	524.59	03/2016 -	10/2016	7	0	Completion delayed due to severe ROW problem at Bhiwani end. ROW being resolved with support from State/ Distt. Admn. Bay at Jaipur (RRVPNL).

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
107	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	34.50	03/2016 -	10/2016	7	0	Completion delay due to delay in equipment supply(Off-shore).
108	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,645.88	12/2011 03/2016	10/2016	58	83.21	NIL
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	593.76	11/2011 -	11/2016	60	0	Severe ROW problem in Western U.P.
110	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 1,428.87	1,428.87	1,082.49	08/2012 09/2016	11/2016	51	17.43	Financial constraints encountered and being addressed with support by POWERGRID. ROW problem also being faced.
111	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	2,149.36	09/2014 -	12/2016	27	0	Severe ROW problem being faced in Karnataka.
112	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 2,619.56	2,619.56	2,442.83	07/2014 06/2016	12/2016	29	23.13	severe ROW in routing of line through grape garden. Critical
113	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	319.67	08/2014 06/2015	12/2016	28	16.63	Completion delayed due to severe ROW problem in Bengaluru area
114	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 1,875.13	1,875.13	1,613.12	01/2015 06/2016	12/2016	23	31.79	Completion delayed due to delay in forest clearance. (Huge forest)
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	639.72	11/2014 -	12/2016	25	0	Severe ROW problem in Uttarakhand in Dehradun-Abdullapur line. disturbance in J&K. ROW problem in Doda & Ramban distt.
116	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	399.80	06/2015 -	12/2016	18	0	Commissioning linked to Angul - Srikakulam line & readiness of Srikakulam - Vemagiri line being executed under TBCB route & system at Vemagiri end. Progress being expedited.

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
117	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,182.53	06/2015 -	12/2016	18	0	Stage – I forest clearance & working permission received. 01 pkg. & system at Vemagiri end for export of power from ER to SR. 01 loc.
118	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	1,088.60	05/2016 -	12/2016	7	0	Completion delay due to severe ROW problem in Mauda-II – Betul line. Betul – Khandwa - Indore line erection completed. Commissioning matching with Mauda-II - Betul line.
119	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	276.70	08/2016 -	12/2016	4	0	Progress affected due to heavy rains & work stopped due to disturbance in Kashmir.
120	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	95.80	07/2016 -	12/2016	5	0	Progress affected due to heavy rains. Completion matching with GETCO line.
121	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	49.40	02/2016 -	12/2016	10	0	Completion delayed due to delay in manufacturing of Reactors by M/s. BHEL. Reactors now under manufacturing & supply started.
122	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	5,761.00	09/2016 01/2017	01/2017	4	0	
123	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	6,460.99	06/2015 -	02/2017	20	0	Implementation affected due to delay in land acquisition of Champa
124	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	605.39	09/2010 01/2016	03/2017	78	54.59	Severe ROW problem in balance
125	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,334.48	10/2012 -	03/2017	53	0	Navsari-Boisar line affected due to severe ROW problem & forest clearance..
126	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,945.15	01/2015 -	03/2017	26	0	Work slowed down to the extent feasible to match Gen. Severe ROW problem & delay in forest clearance also affecting implementation.

(August 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
127	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	220.89	06/2012 -	03/2017	57	0	Severe ROW/Court case problem..
128	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	452.92	06/2014 03/2016	03/2017	33	31.17	Prolonged severe ROW problem being faced in Karnataka. Matter taken up at State level but no break through yet. Down stream system being executed by State not available.
129	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,672.23	08/2014 12/2015	03/2017	31	27.6	due to delay in forest clearance and NOC for wildlife (awaited for Aurangabad – Padghe) & anticipated delay in completion.
130	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	904.84	04/2016 -	03/2017	11	0	Completion delayed due to delay in sub station land acquisition (land acquired in Feb'14). Severe ROW problem faced in Jharkhand area & near Rajarhat . Progress being expedited.
131	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	29.70	04/2016 -	03/2017	11	0	
132	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	219.30	06/2016 -	03/2017	9	0	Progress affected due to severe ROW problem & heavy rains.
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	465.80	06/2016 -	03/2017	9	0	Progress affected due to severe ROW problem & forest clearance awaited.
134	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	1,589.00	12/2016 03/2017	03/2017	3	0	
135	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,581.04	1,581.04	1,275.79	08/2013 05/2017	05/2017	45	175.45	
136	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,187.00	09/2011 06/2017	06/2017	69	54.25	

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
137	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,368.30	12/2012 12/2016	06/2017	54	36.79	Implementing of balance lines affected due to stiff resistance/ local disturbances & geographical constraints in NER.
138	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,308.43	11/2012 03/2016	06/2017	55	36.01	Completion affected due to delay in land acquisition of Daltonganj .
139	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,415.35	12/2015 -	06/2017	18	0	Implementation affected due to severe ROW problems in Odisha & Huger
140	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	11,603.00	01/2017 07/2017	07/2017	6	0	
141	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	6,764.00	11/2016 08/2017	08/2017	9	0	
142	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,441.52	1,441.52	1,066.32	07/2006 09/2017	09/2017	134	290.95	
143	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	6,807.00	06/2017 09/2017	09/2017	3	0	
144	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,760.32	05/2014 03/2017	09/2017	40	0	
145	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,529.80	12/2016 -	09/2017	9	0	
146	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	4,715.05	12/2009 10/2017	10/2017	94	147.51	
147	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,908.55	11/2008 01/2016	12/2017	109	22.93	delayed due to prolonged severe ROW problem in Kerala.
148	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,037.00	08/2013 12/2017	12/2017	52	23.65	due to agitation against Big Dam proj. affecting the construction works in Assam and adverse law & order situation in NER...
149	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	77.96	02/2014 -	02/2018	48	0	
150	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	12,000.00	01/2011 05/2018	05/2018	88	73.65	

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60	12,964.60	7,093.73	01/2018	06/2018	5	0	
152	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE	03/2015	1,071.24	1,071.24	0.70	09/2017	07/2018	10	0	
153	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59	8,398.75	5,871.70	09/2009	12/2018	111	114.28	
154	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48	3,846.30	2,944.00	03/2013	06/2019	75	29.14	
155	TEHRI PUMPED STORAGE PLANT (1000MW) - [N18000010]THDCIL, UTTARAKHAND	07/2006	1,657.00	2,978.86	1,845.71	02/2016	09/2019	43	79.77	law and order problem.
156	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01	167.01	-	11/2018	11/2019	12	0	
157	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58	2,491.58	866.49	06/2013	12/2019	78	0	frequent hindrances by local villagers since mobilization of works since Jan 2014. Now the works at various fronts are in progress with intermittent hindrances by villagers. Regular support of Distt. Administration is required.
158	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND	02/2014	14,366.58	14,366.58	3,267.00	02/2019	02/2020	12	0	
159	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12	8,112.12	360.55	04/2020	03/2022	23	0	
	Total		194,770.21	224,717.21	151,577.42					
	HEAVY INDUSTRY									
160	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS, MULTI STATE	04/2011	1,718.00	3,827.30	2,289.00	09/2011	12/2017	75	122.78	train manpower was not available in the country
	Total		1,718.00	3,827.30	2,289.00					
	HEALTH AND FAMILY WELFARE									

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
161	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	127.80	11/2013 -	10/2016	35	0	i) Delay in Civil Works ii) Stoppage of Work for demanding local employment iii) Delay in deployment of MOHFW representative.
162	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	59.29	05/2017 -	06/2017	1	0	i) Delay in release of funds ii) Work suspended due to safety aspect.
163	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	101.00	05/2017 -	06/2017	1	0	i) Delay in release of funds ii) Work suspended due to safety aspect.
164	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	168.90	16.50	05/2017 -	07/2017	2	0	i) Non availability of funds in time ii) Local protest for demanding local employment.
	Total		826.49 -	826.49	304.59					
	<u>RAILWAYS</u>									
165	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	10/2016	91	154.85	N.R
166	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	370.00	358.96	02/2009 02/2009	12/2016	94	122.68	i) Delay in awarding contract and cancellation of contract.
167	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	54.96	03/2015 -	12/2016	21	53.44	N.R
168	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL	04/2010	171.02 -	235.00	228.37	06/2013 -	12/2016	42	37.41	i) Delay in release of funds ii) Work suspended due to safety aspect.
169	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,581.53	665.09	03/2010 -	03/2017	84	386.62	N.R
170	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	7,000.00	6,402.53	03/2009 -	03/2017	96	317.58	N.R
171	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11	0	N.R
172	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,000.00	4,245.16	04/2008 12/2011	06/2017	110	233.33	N.R
173	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	947.78	03/2010 -	06/2017	87	38.24	N.R

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
174	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	554.70	407.65	01/1999 06/2017	06/2017	221	77.08	N.R
175	NANDYAL- YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 843.45	966.98	901.74	02/2009 12/2017	12/2017	106	520.89	N.R
176	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	516.40	419.63	03/2010 -	12/2017	93	58.94	N.R
177	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,173.50	1,389.62	1,614.79	03/2014 12/2017	12/2017	45	0	N.R
178	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	12/2017	21	29.06	N.R
179	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 187.26	233.73	35.10	04/2014 -	03/2018	47	24.82	N.R
180	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 3,020.95	3,020.95	2,393.07	07/2005 03/2018	06/2018	155	2.16	N.R
181	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	N.R
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]JNR,JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	-	11/2002 -	12/2018	193	682.6	N.R
183	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.00	649.28	03/2016 -	12/2018	33	-10.11	N.R
184	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,010.00	2,323.49	12/2008 -	03/2019	123	310.64	25.26 Ha estimate for land acquisition not submitted by DC/Jalpaiguri. Hence, Y Connection at NMX-NQH could not be completed.
185	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 4,454.18	9,658.00	5,472.86	03/2011 -	03/2019	96	1227.45	In Tupul- Imphal section, estimate for land acquisition was to be submitted by state gov. on 31.7.16 but not received, hence work stopped.
186	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (AS Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
187	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	222.82	03/2015 -	03/2019	48	0	N.R
188	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 658.07	658.07	467.45	03/2014 03/2019	03/2019	60	.75	N.R
189	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	44.65	03/2012 03/2019	03/2019	84	1.06	N.R
190	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	-	03/2018 -	03/2019	12	0	N.R
191	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,160.54	1,776.81	1,078.77	03/1998 -	12/2019	261	359.96	N.R
192	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 1,125.89	1,125.89	982.31	12/2011 03/2020	03/2020	99	25.09	Total land acquisition required for 32 Mouzas, out of which, proposal for 26 Moluzas are with Government of West Bengal, also the remaining will be submitted by the end of September - 2016.
193	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	1,780.37	03/2014 -	03/2020	72	324.3	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
194	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 2,393.48	4,600.00	786.14	04/2014 -	03/2020	71	642.73	N.R
195	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	389.32	12/2015 -	03/2020	51	204.95	Forest Clearance awaited for Kurseong Division and Kalimpong Division in West Bengal.
196	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	35.50	03/2013 -	03/2020	84	-2.17	N.R
197	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	1,056.84	03/2016 -	12/2020	57	-20	N.R
198	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	150.74	03/2015 -	03/2021	72	252.94	Finalization of alignment. Take off point shifted to Dhansiri from Dimapur
199	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 -	1,027.40	483.36	03/2003 -	03/2021	216	0	N.R

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
200	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	1,421.25	693.76	03/2012 -	03/2022	120	135.68	N.R
201	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	N.R
202	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022	46	226.23	i) Delay in clearances from Govt. of Rajasthan.
203	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	5,050.00	-	05/2008 -	03/2023	178	1939.09	N.R
204	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,320.00	753.67	12/2010 -	03/2018	87	167.76	N.R
205	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	749.69	-	06/2005 -	12/2019	174	155.02	N.R
	Total		44,580.32 -	111,000.19	40,430.71					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
206	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	08/2016	38	0	N.R
207	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,282.25	06/2013 -	08/2016	38	0	N.R
208	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	08/2016	30	0	N.R
209	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	871.15	393.88	09/2015 -	08/2016	11	0	N.R
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	434.58	02/2009 -	09/2016	91	28.93	N.R
211	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	294.65	06/2008 -	09/2016	99	0	N.R
212	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	518.85	09/2008 -	09/2016	96	0	N.R
213	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	322.50	06/2008 -	09/2016	99	0	N.R

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
214	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	409.32	04/2010 09/2016	09/2016	77	42.25	N.R
215	AGRA-BYPASS(NS-1/UP-1), NH-2.3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	348.16	418.19	09/2007 -	09/2016	108	0	N.R
216	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	-	05/2013 -	09/2016	40	0	N.R
217	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	1,407.71	03/2013 -	09/2016	42	0	N.R
218	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	368.94	01/2014 -	09/2016	32	0	N.R
219	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	284.73	10/2013 -	09/2016	35	-11	N.R
220	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	240.10	165.44	03/2016 -	09/2016	6	0	N.R
221	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	503.16	268.27	08/2016 -	09/2016	1	0	N.R
222	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD, MADHYA PRADESH	01/2012	320.48 -	320.48	192.55	08/2015 -	09/2016	13	0	N.R
223	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH, BIHAR	10/2014	377.64 -	377.64	-	03/2014 -	09/2016	30	0	N.R
224	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	10/2016	103	0	N.R
225	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	351.34	215.70	01/2016 -	10/2016	9	0	N.R
226	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	495.78	346.60	01/2016 -	10/2016	9	0	N.R
227	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	11/2016	42	0	N.R
228	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI, RAJASTHAN	01/2014	368.15 -	368.15	216.38	01/2016 -	11/2016	10	0	N.R

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
229	REHABILITATION AND UPGRADE OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	0	N.R
230	REHABILITATION AND UPGRADE OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	24	0	N.R
231	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	11/2016	15	0	N.R
232	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	203.60	06/2005 -	12/2016	138	0	N.R
233	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	282.52	11/2008 -	12/2016	97	0	N.R
234	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	199.25	11/2008 -	12/2016	97	80.68	N.R
235	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	251.26	04/2009 -	12/2016	92	0	N.R
236	NALBARI T BIJUNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	309.52	04/2008 01/2017	12/2016	104	0	N.R
237	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	202.41	05/2008 12/2016	12/2016	103	0	N.R
238	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	469.41	05/2010 -	12/2016	79	0	Delay is on account of lack of work planning, machinery labor and frequent changes in the project management personnel by the concessionaire.
239	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 2,782.54	1,509.10	3,272.71	09/2012 -	12/2016	51	0	N.R
240	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,675.34	08/2011 -	12/2016	64	0	Delay is on account of land acquisition and Forest Issues.
241	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,846.48	11/2011 -	12/2016	61	106.5	Delay is on account of Poor performance by contractor.
242	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	-	04/2013 -	12/2016	44	2.65	N.R

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
243	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	902.60	03/2013 -	12/2016	45	0	N.R
244	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,038.84	07/2013 -	12/2016	41	0	N.R
245	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	39	0	Land acsition and Wildlife clearance
246	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	12/2016	42	0	N.R
247	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2016	28	0	N.R
248	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,893.03	03/2013 -	12/2016	45	0	N.R
249	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,415.99	07/2013 -	12/2016	41	0	N.R
250	PATNA-MUZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	880.96	02/2013 -	12/2016	46	0	N.R
251	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	12/2016	37	0	N.R
252	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	976.34	07/2013 -	12/2016	41	0	N.R
253	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,851.90	05/2014 -	12/2016	31	0	N.R
254	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.85	07/2013 -	12/2016	41	0	N.R
255	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,363.70	06/2014 -	12/2016	30	0	N.R
256	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35	0	N.R
257	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	875.56	08/2013 -	12/2016	40	0	N.R
258	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	621.48	09/2013 -	12/2016	39	0	N.R
259	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	-	03/2013 -	12/2016	45	0	Delay is on account of Poor performance of Contractor and delay in land acquisition.
260	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,202.40	08/2013 -	12/2016	40	0	N.R

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
261	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,475.09	09/2014 -	12/2016	27	0	N.R
262	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2016	32	0	N.R
263	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	354.08	06/2014 -	12/2016	30	0	Inadequate mobilization of resources by contractor. Forest clearance. Land related issues.
264	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	12/2016	12	0	N.R
265	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD, ANDHRA PRADESH	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	12	0	N.R
266	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	0	N.R
267	2-LANING WITH PS SITARGANJ BAREILLY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	301.04	67.32	01/2016 -	12/2016	11	0	N.R
268	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	923.04	350.23	11/2016 -	12/2016	1	0	N.R
269	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	-	11/2015 -	12/2016	13	51.83	N.R
270	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	1,850.96	04/2015 -	01/2017	21	0	N.R
271	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	0	N.R
272	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,890.00	09/2015 -	02/2017	17	0	N.R
273	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	0	N.R

(August 2016)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
274	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [N240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	217.29	04/2009 -	03/2017	95	92.75	N.R
275	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 -	212.00	122.77	09/2007 -	03/2017	114	0	N.R
276	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	331.23	373.08	07/2009 -	03/2017	92	68.99	N.R
277	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	584.38	08/2012 -	03/2017	55	0	N.R
278	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	899.81	03/2014 -	03/2017	36	0	N.R
279	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	510.91	04/2014 -	03/2017	35	0	N.R
280	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,652.28	06/2014 -	03/2017	33	0	N.R
281	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN	10/2013	677.79 -	677.79	883.59	04/2016 -	03/2017	11	0	N.R
282	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	119.97	01/2016 -	03/2017	14	0	N.R
283	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	731.90	03/2014 -	04/2017	37	0	N.R
284	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	195.99	02/2010 -	05/2017	87	2.29	Delay is on account of rehabilitation and corrective action necessitated after construction accident on 24.12.2009.
285	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	0	Delay is on account of i) Court order on cutting of trees ii) Public agitation and stopping of works.
286	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43 -	580.43	272.37	08/2013 -	05/2017	45	0	N.R
287	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	590.00	06/2015 -	05/2017	23	0	N.R
288	REHABILITATION AND UPGRADE OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	0	N.R

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
289	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,035.69	05/2013 -	06/2017	49	0	N.R
290	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	696.22	01/2014 -	06/2017	41	0	N.R
291	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	1,863.25	09/2014 -	06/2017	33	0	N.R
292	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	-	05/2017 -	06/2017	1	0	N.R
293	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,682.27	07/2015 -	07/2017	24	0	N.R
294	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,630.57	02/2014 -	08/2017	42	0	N.R
295	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	0	N.R
296	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	978.00	08/2016 -	08/2017	12	0	N.R
297	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	112.62	09/2016 -	09/2017	12	0	N.R
298	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,771.99	08/2013 -	10/2017	50	0	N.R
299	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	871.15	09/2014 -	10/2017	37	0	N.R
300	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	757.57	11/2015 -	10/2017	23	0	N.R
301	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	N.R

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
302	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	0	N.R
303	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	0	N.R
304	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48	0	N.R
305	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55	0	N.R
306	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	311.51	08/2013 -	12/2017	52	0	N.R
307	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	623.47	10/2013 -	12/2017	50	0	N.R
308	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	352.00	07/2014 -	12/2017	41	0	N.R
309	BARSAAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	N.R
310	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	181.61	10/2015 -	12/2017	26	0	N.R
311	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,135.69	07/2017 -	01/2018	6	0	N.R
312	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69	0	N.R
313	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	N.R
314	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	N.R

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
315	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65	611.65	-	06/2016	06/2018	24	0	N.R
316	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29	447.29	-	12/2017	12/2018	12	0	N.R
	Total		82,117.55	84,499.81	81,071.96					
	<u>SHIPPING AND PORTS</u>									
317	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	409.83	350.68	04/2009 03/2010	08/2016	88	66.82	
318	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 600.00	600.00	525.49	03/2006 03/2016	12/2016	129	300	Relocating of fishing stalls for a length about 300m in fishing harbour.
319	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	415.01	12/2010 12/2018	12/2018	96	82.72	NIL
	Total		762.06	1,679.29	1,291.18					
	<u>TELECOMMUNICATIONS</u>									
320	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE	09/2014	2,111.17	2,011.17	301.57	09/2014	03/2017	30	-4.74	
	Total		2,111.17	2,011.17	301.57					
	<u>URBAN DEVELOPMENT</u>									
321	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	13,069.22	12/2015	08/2016	8	0	Contractual problem
322	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85	261.85	208.53	05/2013 10/2015	10/2016	41	0	Non-availability of funds

(August 2016)

(August 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
323	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	315.00	214.40	06/2015 08/2016	11/2016	17	0	
324	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	24,669.11	03/2016 -	12/2016	9	0	Rehabilitation and Resettlement, Land Acquisition problem
325	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 13,845.01	14,405.01	14,081.31	06/2011 12/2013	01/2017	67	125.25	difficult geological conditions, densely populated area
326	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	133.58	09/2016 01/2017	01/2017	4	0	
327	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	124.48	12/2014 12/2016	03/2017	27	0	
328	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	191.97	133.13	03/2012 08/2016	03/2017	60	-6.36	
329	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 405.01	405.01	249.90	12/2014 -	03/2017	27	0	
330	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 -	350.02	161.29	03/2015 03/2017	03/2017	24	0	Delay by consultant
331	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	60.59	09/2015 07/2016	04/2017	19	0	Slow work
332	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	36.54	10/2012 04/2017	04/2017	54	0	
333	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 270.83	270.83	-	11/2014 05/2017	05/2017	30	0	
334	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	24.52	03/2016 -	09/2017	18	0	

(August 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
335	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	22.45	03/2015 10/2017	10/2017	31	0	stopped due to water-logging of the site and non-depositing of fund by NIT Authority
336	CONSTRUCTION OF CIVIL STRUCTURES AN OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	19.54	11/2015 -	11/2017	24	0	
337	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	901.75	02/2019 -	03/2020	13	0	land acquisition
	Total		89,178.79 -	97,175.77	54,110.34					
	Grand Total		564,129.10	677,729.16	419,810.90					

Annexure - VII

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00 -	09/2010 -	10/2017	62.57	85
	Total		3,492.00 -	5,677.00 -				
	<u>COAL</u>							
2	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.59 -	03/2015 -	03/2020	201.51	60
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57 -	03/2012 -	03/2017	87.58	60
4	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62 -	03/2012 -	03/2023	16.86	132
5	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27 -	03/2016 -	03/2018	12.97	24
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63 -	03/2013 -	03/2019	0.02	72
	Total		1,740.78 -	2,401.68 -				
	<u>FERTILISERS</u>							
7	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44 -	11/2016 -	09/2017	5.89	10
	Total		197.79 -	209.44 -				
	<u>HEAVY INDUSTRY</u>							
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30 -	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30 -				
	<u>PETROLEUM</u>							
9	BULK PETROLEUM OIL AND LUBRICANT (POL) DEPOT AT IMPHAL, MANIPUR - [N16000215]	08/2010	103.02 -	171.04 -	07/2016 -	08/2016	66.03	1
10	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79 -	10/2014 -	03/2017	49.38	29
11	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00 -	03/2013 -	01/2017	19.35	46
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03 -	03/2017 -	06/2018	24.53	15
13	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25 -	10/2017 -	02/2018	17.66	4

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
14	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00	838.08	11/2015	11/2016	25.84	12
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79	1,256.72	05/2013	12/2016	45.83	43
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35	1,200.00	03/2015	12/2016	37.72	21
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00	1,693.00	01/2012	09/2016	70.49	56
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63	2,665.65	03/2015	03/2018	29.42	36
	Total		7,134.22	9,810.56				
	<u>POWER</u>							
19	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]	05/2010	250.03	390.51	01/2013	09/2016	56.19	44
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33	346.79	08/2014	12/2016	16.63	28
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72	1,441.52	07/2006	09/2017	290.95	134
22	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69	738.48	09/2010	03/2017	54.59	78
23	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49	639.46	06/2014	03/2017	31.17	33
24	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99	1,581.04	08/2013	05/2017	175.45	45
25	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]	12/2009	1,216.83	1,428.87	08/2012	11/2016	17.43	51
26	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80	1,731.10	11/2012	06/2017	36.01	55
27	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	01/2012	1,422.85	1,875.13	01/2015	12/2016	31.79	23
28	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	2,978.86	02/2016	09/2019	79.77	43
29	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65	2,228.71	08/2014	03/2017	27.60	31
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	2,187.32	11/2008	12/2017	22.93	109
31	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	05/2011	1,961.87	2,310.58	05/2014	10/2016	17.77	29

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
32	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	12/2016	23.13	29
33	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2017	36.79	54
34	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	10/2016	83.21	58
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	10/2017	147.51	94
36	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14	75
37	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28	111
38	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	06/2017	54.25	69
39	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
40	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		53,690.53 -	83,701.14				
	<u>RAILWAYS</u>							
41	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	10/2016	154.85	91
42	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
43	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89	106
44	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	370.00	02/2009 02/2009	12/2016	122.68	94
45	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41	42
46	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	233.73	04/2014 -	03/2018	24.82	47
47	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	5,050.00	05/2008 -	03/2023	1,939.09	178
48	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
49	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94	93
50	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	03/2017	386.62	84
51	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
52	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	03/2022	135.68	120
53	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
54	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
55	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06	21
56	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) [N22000113]	04/2008	653.19 -	658.07	03/2014 -	03/2019	0.75	60
57	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24	87
58	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2019	1,227.45	96
59	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64	123
60	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72
61	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2021	252.94	72
62	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
63	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
64	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
65	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2017	233.33	110
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58	96
67	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
68	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]	03/1999	2,957.21 -	3,020.95	07/2005 -	06/2018	2.16	155
69	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		26,856.49 -	92,845.61				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
70	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	12/2016	80.68	97
71	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2017	68.99	92

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
72	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2017	92.75	95
73	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25	77
74	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29	87
75	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	09/2016	28.93	91
76	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2016	51.83	13
77	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50	61
78	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	12/2016	2.65	44
	Total		4,661.46 -	7,044.23				
	<u>SHIPPING AND PORTS</u>							
79	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2016	300.00	129
80	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82	88
81	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		762.06 -	1,679.29				
	<u>STEEL</u>							
82	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50	15
83	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79	7
84	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	09/2017	42.39	11
	Total		668.22 -	871.05				
	<u>URBAN DEVELOPMENT</u>							
85	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	14,405.01	06/2011 -	01/2017	125.25	67
	Total		6,395.00 -	14,405.01				
	Grand Total		107,316.55	222,472.31				

Annexure - VIII

Details of Projects Without Date of Commissioning

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>ATOMIC ENERGY</u>				
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	12/2008 10/2013	05/2016
	Total		13,171.00 -		
	<u>CIVIL AVIATION</u>				
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61 -	05/2012 -	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015
	Total		553.21 -		
	<u>COAL</u>				
4	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 -	03/2013 -	03/2016
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL, TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		680.12 -		
	<u>STEEL</u>				
6	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL, KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	03/2016
7	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016
8	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL, KARNATAKA	07/2011	324.87 324.87	12/2015 -	04/2016
9	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL, JHARKHAND	12/2007	253.92 253.92	06/2016 -	06/2016
10	CONSTRUCTION OF 123 BLOCKS IN TELANGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL, ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
	Total		1,765.04 -		
	<u>PETROCHEMICALS</u>				
11	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 9,965.00	04/2012 12/2015	-
	Total		5,460.61 -		

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	PETROLEUM				
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 -	10/2011 -	04/2016
13	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 07/2016	07/2016
14	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
15	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
16	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
17	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
18	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
19	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	01/2014 -	-
20	LPG MARKETING TERMINAL, PARADIP - [N16000174]IOCL,ODISHA	09/2012	158.91 -	03/2015 -	-
	Total		7,170.68 -		
	POWER				
21	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	11/2013 -	03/2016
22	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 609.44	02/2014 03/2016	03/2016
23	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	01/2013 -	03/2016
24	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016
25	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,HIMACHAL PRADESH	12/2005	358.42 -	12/2008 09/2010	-
26	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.57	07/2013 -	-
27	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
28	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE	04/2016	810.48 -	- -	-
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
30	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	01/2016 -	-
31	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	02/2016 -	06/2016
	Total		22,269.80 -		

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>HEALTH AND FAMILY WELFARE</u>				
32	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014
33	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016
34	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	04/2016
35	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	06/2016
	Total		1,231.08 -		
	<u>RAILWAYS</u>				
36	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016
37	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	01/2011
38	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011
39	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011
40	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
41	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2096	614.54 -	- -	04/2014
42	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	08/2014
43	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
44	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	05/2015
45	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	07/2015
46	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015
47	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	09/2015
48	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
49	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	10/2015
50	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 717.15	03/2012 01/2016	01/2016
51	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016
52	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016
53	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	03/2016

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
54	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016
55	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016
56	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- -	-
57	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
58	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
59	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
60	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	-
61	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- -	-
62	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
63	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
64	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 774.90	- -	-
65	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
66	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
67	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-
68	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 458.26	07/2008 -	-
69	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
70	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
71	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	-
72	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
73	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 781.02	06/2007 -	-
74	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 712.82	- -	-
75	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,045.20	- -	-
76	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-
77	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
78	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
79	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
80	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
81	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
82	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
83	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
84	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
85	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 722.21	06/2013 -	-
86	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 1,160.47	- -	-
87	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	02/2006 -	-
88	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
89	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 1,449.72	- -	-
90	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
91	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 227.40	- -	-
92	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- -	-
93	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
94	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	-
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
96	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
97	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
98	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 -	-
99	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
100	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
101	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	- -	-
102	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
103	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
104	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
105	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
106	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
107	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 633.87	- -	-
108	NAWADA-LAXMIPUR (NL) - [N22000167]JECR,BIHAR	04/2008	620.57 -	- -	-
109	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]JECOR,BIHAR	04/2008	445.25 -	- -	-
110	GAYA-CHATRA (NL) - [N22000169]JECOR,MULTI STATE	04/2008	415.67 549.75	- -	-
111	BIHTA-AURANGABAD (NL) - [N22000170]JECOR,BIHAR	04/2008	326.20 -	- -	-
112	MOTIHARI-SITAMARHI (NL) - [N22000174]JECR,BIHAR	04/2006	211.00 -	- -	-
113	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]JECR,BIHAR	04/2008	678.62 -	- -	-
114	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]JECR,BIHAR	04/2008	228.05 -	- -	-
115	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 528.00	- -	-
116	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 1,200.00	- -	-
117	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 1,500.00	- -	-
118	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 377.71	- -	-
119	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 520.00	- -	-
120	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
121	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
122	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 603.22	- -	-
123	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 302.90	- -	-
124	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 931.98	- -	-
125	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
126	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
127	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 800.00	- -	-
128	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
129	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
130	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
131	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 595.91	- -	-
132	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	- -	-
133	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- -	-
134	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- -	-
135	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	-
136	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	- -	-
137	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-
138	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 1,801.00	- 06/2016	-
139	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	- -	-
140	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
141	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
142	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
143	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
144	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
145	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
146	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
147	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
148	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
149	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
150	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	- -	-
151	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 832.47	- -	-
152	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 1,714.49	- 06/2014	-
153	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 348.85	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
154	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
155	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
156	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
157	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
158	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
159	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
160	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
161	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
162	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
163	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
164	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 893.69	01/1999 -	-
165	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
166	KAKINADA-PITHAPURAM - [N22000314]SCR,ANDHRA PRADESH	03/1999	215.06 -	- -	-
167	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-
168	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 1,141.00	- 03/2016	-
169	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
170	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
171	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
172	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 1,072.52	- -	-
173	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
174	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-
175	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-
176	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-
177	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- -	-
178	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 -	- -	-
179	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
180	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- -	-
181	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- -	-
182	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	- -	-
183	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
184	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
185	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	- -	-
186	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 3,631.00	- -	-
187	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
188	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
189	SECUNDERABAD-MOHABOBNAGAR - [N22000371]RVNL,TELANGANA	04/2015	728.10 -	- -	-
190	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
191	INDORE-DEWAS-UJJAIN(80 KM) DL - [N22000375]WR,MADHYA PRADESH	04/2016	600.00 -	- -	-
192	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2093	971.22 -	- -	-
193	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-
194	INDORE DEWAS UJJAIN (80 KM) - [N22000393]WR,GUJARAT	04/2016	600.00 -	- -	-
195	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
196	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
197	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	-
198	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
199	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
200	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
201	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
202	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
203	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-
204	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
205	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
206	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
207	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-
208	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
209	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
210	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
211	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
212	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
213	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
214	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
215	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
216	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
217	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
218	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
219	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
220	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
221	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
222	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
223	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
224	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
225	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
226	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
227	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
228	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
229	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
230	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
232	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
233	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	- -	-
234	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
235	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	- -	-
236	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	450.00 -	- -	-
237	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	- -	-
238	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	- -	-
239	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER, MULTI STATE	04/2000	157.17 -	- -	-
240	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER, MULTI STATE	04/2010	174.56 -	- -	-
241	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 -	- -	-
242	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	296.44 -	- -	-
243	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	- -	-
244	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55 -	- -	-
245	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17 -	- -	-
246	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	267.09 -	- -	-
247	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER, MULTI STATE	04/2011	193.44 -	- -	-
248	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	- -	-
249	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	494.54 -	- -	-
250	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER, MULTI STATE	04/2000	297.47 -	- -	-
251	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER, MULTI STATE	04/2003	337.96 -	- -	-
252	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER, MULTI STATE	04/2009	493.96 -	- -	-
253	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER, MULTI STATE	04/2010	268.52 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
254	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]JER,MULTI STATE	04/2011	166.89 -	- -	-
255	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
256	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
257	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
258	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
259	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
260	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
261	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
262	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
263	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
264	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
265	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
266	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
267	MONIGRAM- NIMITTA - [N22000301]JER,MULTI STATE	04/2012	250.93 -	- -	-
268	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]JER,WEST BENGAL	04/2012	255.64 -	- -	-
269	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
270	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
271	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
272	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
273	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
	Total		228,626.88 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
274	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	08/2014
275	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	11/2015

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
276	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
277	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
278	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	05/2016
279	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	05/2016
280	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
281	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	07/2016
282	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 06/2016	07/2016
283	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	07/2016
284	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	07/2016
285	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	07/2016
286	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
287	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
288	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	07/2016
289	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	07/2016
290	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	07/2016
291	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	07/2016
292	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
293	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-
294	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
295	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
296	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
297	REHABILITATION AND UPGADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
298	YAN TO NIRMAL SEREHABILITATION AND UPGADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
299	REHABILITATION AND UPGADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
300	REHABILITATION AND UPGADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
301	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
302	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
303	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
304	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
305	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
306	REHABILITATION AND UPGADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
307	REHABILITATION AND UPGADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
308	REHABILITATION AND UPGADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
309	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
310	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
311	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
312	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	-
313	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
314	REHABILITATION AND UPGADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
315	REHABILITATION AND UPGRADE OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
316	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
317	REHABILITATION AND UPGRADE OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
318	REHABILITATION AND UPGRADE OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
319	REHABILITATION AND UPGRADE OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
320	REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
321	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
322	4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
323	4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
324	REHABILITATION AND UPGRADE OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
325	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
326	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
327	REHABILITATION AND UPGRADE TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
328	REHABILITATION AND UPGRADE TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
329	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
330	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
331	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
332	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
333	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
334	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
335	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
336	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
337	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
338	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
339	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
340	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
341	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
342	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
343	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
344	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
345	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
346	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
347	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
348	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
349	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
350	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
351	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
352	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
353	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
354	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
355	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
356	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
357	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-
358	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
359	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
360	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
361	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
362	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
363	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
364	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-
365	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-
366	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
367	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
368	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-
369	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
370	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
371	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-
372	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-
373	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
374	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
375	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-
376	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
377	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
378	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
379	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
380	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-
381	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
382	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
383	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-
384	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
385	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-
386	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-
387	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
388	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-
389	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
390	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
391	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
392	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
393	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-
394	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
395	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
396	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
397	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
398	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
399	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
400	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
401	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
402	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-
403	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
404	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	-
405	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	-
406	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	-
407	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	-
408	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	-
409	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
410	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	-
411	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
412	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
413	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	-
414	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-
415	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-
416	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	-
417	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
418	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA	03/2016	244.00 -	- -	-
419	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
420	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-
421	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	- -	-
422	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 -	- -	-
423	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-
424	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-
425	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-
426	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-
427	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-
428	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	-
429	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	01/2016 -	-
430	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	01/2016 -	-
431	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD, MAHARASHTRA	03/2016	1,142.62 -	- -	-
432	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD, MAHARASHTRA	03/2016	1,101.58 -	- -	-
433	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	-
434	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-
435	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	- -	-
436	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
437	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	- -	-
438	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
439	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	-
440	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	-
441	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
442	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	-
443	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	-
444	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-
445	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	- -	-
446	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
447	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	-
448	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	-
449	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
450	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
451	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-
	Total		110,021.28 -		
	<u>SHIPPING AND PORTS</u>				
452	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		2,427.40 -		
	<u>TELECOMMUNICATIONS</u>				
453	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	-
	Total		13,334.00 -		
	<u>URBAN DEVELOPMENT</u>				
454	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015

(August 2016)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
455	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	11/2014 07/2016	-
456	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-
457	CONSTRUCTION OF 100 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	- -	-
458	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	01/2015 -	-
459	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
460	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		25,302.86 -		
	Grand Total		432,013.96		

Annexure - IX

Details of Projects Without Original Date of Commissioning

(August 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	175.00	-	- -	12/2017	-	0/0
	Total		175.00 -	175.00	.00				0/0
	<u>RAILWAYS</u>								
2	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	1,126.79	808.84	- -	10/2016	-	0/1
3	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 1,289.92	1,289.92	1,310.08	- -	12/2016	-	0/1
4	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,595.40	1,679.13	1,721.58	- -	12/2016	-	0/0
5	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	1,101.16	194.91	- -	03/2017	-	0/0
6	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	805.97	- -	03/2017	-	0/1
7	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	148.33	- -	03/2017	-	0/0
8	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	1.19	- -	12/2017	-	0/0
9	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE	04/2008	822.39 -	1,480.83	1,461.01	- -	03/2018	-	0/1
10	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	445.00	391.51	- -	03/2018	-	0/0
11	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	330.00	98.32	- -	03/2018	-	0/0
12	NEW JALPAIGURI SILIGURI-NEW BONGAIGAN INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	1,653.55	1,071.96	- -	03/2018	-	0/0
13	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	508.00	326.08	- -	03/2018	-	0/0
14	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 926.00	926.00	718.19	- -	12/2018	-	0/0

(August 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 855.16	860.00	557.38	- -	12/2018	-	0/0
16	HAJIPUR - BACHAWARA - [N22000334]JECR,MULTI STATE	05/2015	720.00 678.54	678.54	0.75	- 12/2018	12/2018	0(R3)	0/38
17	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 551.50	548.01	265.18	- 03/2019	03/2019	0(R3)	0/0
18	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 372.09	525.00	549.50	- -	03/2019	-	0/0
19	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,319.33	1,319.33	771.67	- 12/2009	03/2019	111(R1)	0/0
20	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	780.00	320.50	- -	03/2019	-	0/0
21	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	399.63	20.01	- -	03/2019	-	0/0
22	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	1,037.15	657.18	- -	03/2019	-	0/0
23	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
24	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 967.85	967.85	97.63	- -	03/2019	-	1/1
25	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	450.00	0.79	- -	03/2019	-	0/0
26	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	386.68	0.57	- -	03/2019	-	0/0
27	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,127.00	632.11	- -	03/2019	-	0/1
28	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	355.96	192.71	- -	03/2019	-	0/0
29	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	620.00	-	- -	09/2019	-	0/0
30	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	2,145.00	362.59	- -	03/2020	-	0/0
31	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	567.18 -	975.62	90.27	- -	03/2020	-	0/0
32	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0
33	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	6,000.00	21.10	- -	03/2020	-	0/0
34	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	- -	03/2020	-	0/0
35	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]JECOR,CHHATISGARH	12/2012	826.57 1,160.83	1,160.83	224.90	- 03/2020	03/2020	0(R3)	1/1

(August 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	238.03	112.11	- -	03/2020	-	0/0
37	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 860.43	860.43	57.15	- -	03/2020	-	0/0
38	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 578.00	578.00	93.09	- 11/2015	03/2020	52(R3)	0/2
39	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,266.89 -	1,266.89	87.25	- -	12/2020	-	0/0
40	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	1,111.99	254.82	- -	03/2021	-	0/0
41	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	837.33	-	- -	03/2021	-	0/0
42	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	2,232.32	1.30	- -	03/2021	-	0/0
43	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	870.96	-	- -	03/2021	-	0/0
44	SURENDRA NAGAR RAJKOT - [N22000392]WR, GUJARAT	04/2015	1,002.39 -	1,002.39	0.86	- -	03/2021	-	0/0
45	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	470.21 -	3,004.90	629.60	- 06/2021	06/2021	0(R3)	0/0
46	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	1,640.04	349.24	- 03/2022	03/2022	0(R3)	0/0
47	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	1,336.57	259.58	- -	03/2019	-	0/0
	Total		37,933.44 -	56,064.04	15,667.81				2/47
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
48	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	1,665.00	1,410.79	- -	09/2016	-	0/0
49	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	479.00	360.06	- -	12/2016	-	0/0
50	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	818.53	- -	03/2017	-	3/3
51	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP, MAHARASHTRA	01/2014	446.77 -	446.77	107.87	- -	06/2017	-	0/4
52	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	795.76	-	- -	06/2017	-	0/0
53	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	794.30	-	- -	06/2017	-	0/0

(August 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
54	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	-	- -	06/2017	-	0/0
55	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	24.63	- -	10/2017	-	0/4
56	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	148.92	- -	11/2017	-	0/0
57	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	-	- -	11/2017	-	0/0
58	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
59	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	854.80	110.62	- -	12/2017	-	0/0
60	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	-	- -	01/2018	-	0/0
61	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	1,393.00	1,386.53	- -	01/2018	-	0/0
62	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	28.00	- -	02/2018	-	0/0
63	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHINDEAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	84.84	- -	04/2018	-	0/1
64	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
65	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	81.69	- -	04/2018	-	0/0
66	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	-	- -	05/2018	-	0/0
67	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	-	- -	05/2018	-	0/0
68	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	-	- -	05/2018	-	0/0
69	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	-	- -	05/2018	-	0/0
70	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	228.50	- -	05/2018	-	0/0

(August 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
71	TWO LANE WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	6.99	- -	05/2018	-	0/0
72	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	197.69	-	- -	05/2018	-	0/0
73	FOUR LANE OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	431.50	- -	06/2018	-	0/0
74	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0
75	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	27.95	- -	07/2018	-	0/0
76	FOUR LANE OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	1,388.00	175.79	- -	08/2018	-	0/0
77	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	-	- -	08/2018	-	0/0
78	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	-	- -	11/2018	-	0/0
79	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	-	- -	11/2018	-	0/0
80	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	-	- -	11/2018	-	0/0
81	6 LANE OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	1,657.20	-	- -	01/2019	-	0/0
	Total		23,751.15 -	23,750.64	5,433.21				3/12
	Grand Total		61,859.59	79,989.68	21,101.02				5/59

Annexure - X

Details of Projects Without Milestones w.r.t. Original Schedule

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 -	09/2017	0/0
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	09/2018	0/0
	Total		1,177.28 -			0/0
	<u>COAL</u>					
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
	Total		1,036.08 -			0/0
	<u>FERTILISERS</u>					
7	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 09/2017	09/2017	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
8	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 344.50	11/2016 11/2016	11/2016	0/0
9	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	04/2020	0/0
	Total		2,200.50 -			0/0
	<u>STEEL</u>					
10	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	03/2016	0/0
11	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016	0/0
12	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	04/2016	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
13	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	06/2016	0/0
14	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2016	0/0
15	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2016	0/0
16	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	03/2017	0/0
17	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	03/2017	0/0
18	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2017	0/0
19	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	07/2017	0/0
20	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	09/2017	0/0
21	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
22	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	09/2017	0/0
23	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
24	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 -	12/2017	0/0
25	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
26	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
27	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	09/2018 -	09/2018	0/0
28	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
	Total		14,554.34 -			0/0
	<u>PETROLEUM</u>					
29	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 -	10/2011 -	04/2016	0/0
30	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 08/2016	08/2016	0/0
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	09/2016	0/0
32	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 05/2016	12/2016	0/0
33	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
34	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	01/2017 -	01/2017	0/0

			(August 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	02/2017	0/0
36	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 10/2016	03/2017	0/0
37	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT	11/2015	500.00 -	03/2017 -	03/2017	0/0
38	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 2,098.43	05/2017 -	05/2017	0/0
39	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL	08/2014	190.45 -	09/2017 -	09/2017	0/0
40	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA	05/2015	2,443.00 -	12/2017 -	12/2017	0/0
41	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	12/2017 -	12/2017	0/0
42	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220]BPCL,MAHARASHTRA	02/2015	184.00 -	12/2017 -	12/2017	0/0
43	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00 -	06/2017 -	12/2017	0/0
44	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	03/2018	0/0
45	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 -	04/2018	0/0
46	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219]BPCL,MAHARASHTRA	08/2014	393.00 -	04/2018 -	04/2018	0/0
47	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU	08/2014	393.00 -	04/2018 -	04/2018	0/0
48	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	04/2018 -	04/2018	0/0
49	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 06/2018	06/2018	0/0
50	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 -	09/2018	0/0
51	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221]BPCL,MAHARASHTRA	01/1991	694.00 -	10/2018 -	10/2018	0/0
52	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0
53	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
54	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 -	03/2019	0/0
55	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 05/2019	05/2019	0/0
56	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 -	11/2019 -	11/2019	0/0
57	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
58	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 -	07/2020 -	07/2020	0/0

			(August 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
59	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
60	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
61	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
62	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
63	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-	0/0
64	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	05/2018 -	08/2018	0/0
	Total		71,959.89 -			0/0
	<u>POWER</u>					
65	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	10/2016	0/0
66	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	03/2017	0/0
67	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 -	03/2017	0/0
68	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
69	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2017	0/0
70	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
71	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 -	01/2018	0/0
72	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
73	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	01/1991	454.11 -	04/2018 -	04/2018	0/0
74	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	05/2018	0/0
75	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA	05/2016	364.60 -	05/2018 -	05/2018	0/0
76	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA	01/2016	187.04 -	06/2018 -	06/2018	0/0
77	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
78	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2018 -	06/2018	0/0
79	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	07/2018	0/0
80	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0

			(August 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
81	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT	01/2016	244.19 -	07/2018 -	07/2018	0/0
82	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
83	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
84	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
85	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
86	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
87	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
88	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE	05/2016	167.01 -	11/2018 -	11/2019	0/0
89	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	03/2022	0/0
90	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE	04/2016	810.48 -	- -	-	0/0
91	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		47,471.13 -			0/0
	<u>HEAVY INDUSTRY</u>					
92	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
93	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014	0/0
94	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016	0/0
95	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	04/2016	0/0
96	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	06/2016	0/0
97	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 -	10/2016	0/0
98	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	06/2017	0/0
99	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	06/2017	0/0
100	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2017	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
101	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	03/2018	0/0
	Total		2,563.15 -			0/0
	<u>RAILWAYS</u>					
102	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
103	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	01/2011	0/0
104	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011	0/0
105	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011	0/0
106	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
107	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	04/2014	0/0
108	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	08/2014	0/0
109	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
110	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	05/2015	0/0
111	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	07/2015	0/0
112	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
113	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	09/2015	0/0
114	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
115	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	10/2015	0/0
116	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 717.15	03/2012 01/2016	01/2016	0/0
117	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016	0/0
118	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
119	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	03/2016	0/0
120	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016	0/0
121	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
122	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,595.40	- -	12/2016	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
123	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
124	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016	0/0
125	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
126	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	03/2017	0/0
127	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 -	03/2017	0/0
128	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	03/2009 -	03/2017	0/0
129	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
130	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
131	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
132	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
133	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2017	0/0
134	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
135	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	01/1999 06/2017	06/2017	0/0
136	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 843.45	02/2009 12/2017	12/2017	0/0
137	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 2,173.50	03/2014 12/2017	12/2017	0/0
138	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
139	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
140	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
141	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 -	- -	03/2018	0/0
142	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJBHATKHOWA-JAI - [N22000209]NFR, MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
143	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 -	- -	03/2018	0/0
144	OMALUR-METTURDAM- DOUBLING WITH ELCTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU	10/2013	187.26 187.26	04/2014 -	03/2018	0/0
145	VIRAMGAM BHILDI - [N22000391]WR, GUJARAT	04/1990	237.13 -	03/2018 -	03/2018	0/0
146	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 3,020.95	07/2005 03/2018	06/2018	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
147	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
148	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2018	0/0
149	KODERMA GIRIDH (NL), ECR - [220100306]ECR, JHARKHAND	04/1996	768.87 926.00	- -	12/2018	0/0
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
151	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 855.16	- -	12/2018	0/0
152	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 551.50	- 03/2019	03/2019	0/0
153	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 372.09	- -	03/2019	0/0
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
155	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,319.33	- 12/2009	03/2019	0/0
156	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 4,454.18	03/2011 -	03/2019	0/0
157	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 -	- -	03/2019	0/0
158	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
159	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2019	0/0
160	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000123]NWR, RAJASTHAN	04/2008	653.19 658.07	03/2014 03/2019	03/2019	0/0
161	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 321.62	03/2012 03/2019	03/2019	0/0
162	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	- -	03/2019	0/0
163	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	03/2019	0/0
164	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
165	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 -	- -	03/2019	0/0
166	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	- -	03/2019	0/0
167	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU	04/2011	190.10 -	- -	03/2019	0/0
168	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
169	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
170	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
171	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	09/2019	0/0
172	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,160.54	03/1998 -	12/2019	0/0
173	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 1,125.89	12/2011 03/2020	03/2020	0/0
174	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	- -	03/2020	0/0
175	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
176	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 2,393.48	04/2014 -	03/2020	0/0
177	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
178	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2020	0/0
179	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
180	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
181	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- -	03/2020	0/0
182	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
183	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	03/2020	0/0
184	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	- -	03/2020	0/0
185	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
186	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
187	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0
188	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
189	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	03/2020 -	03/2020	0/0
190	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0
191	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
192	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
193	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
194	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
195	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
196	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 -	03/2021	0/0
197	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	03/2021	0/0
198	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	03/2021	0/0
199	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2021 -	03/2021	0/0
200	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2021 -	03/2021	0/0
201	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2021 -	03/2021	0/0
202	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
203	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2021	0/0
204	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	03/2021	0/0
205	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	03/2021	0/0
206	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0
207	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
208	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	03/2021	0/0
209	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- 06/2021	06/2021	0/0
210	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	763.18 1,013.45	12/2021 -	12/2021	0/0
211	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2021	0/0
212	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	03/2012 -	03/2022	0/0
213	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- 03/2022	03/2022	0/0
214	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
215	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	03/2022 -	03/2022	0/0
216	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
217	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 12/2022	12/2022	0/0
218	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	03/2023	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
219	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
220	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
221	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
222	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
223	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
224	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- -	-	0/0
225	AMRAVATI-NARKHER NL (CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
226	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
227	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
228	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTD,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	-	0/0
229	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- -	-	0/0
230	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
231	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
232	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 774.90	- -	-	0/0
233	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
234	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
235	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-	0/0
236	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 458.26	07/2008 -	-	0/0
237	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
238	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
239	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
240	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 781.02	06/2007 -	-	0/0
241	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 712.82	- -	-	0/0
242	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,045.20	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
243	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-	0/0
244	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
245	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
246	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
247	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
248	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
249	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
250	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
251	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
252	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
253	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 1,449.72	- -	-	0/0
254	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
255	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 227.40	- -	-	0/0
256	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- -	-	0/0
257	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	-	0/0
258	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
259	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
260	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
261	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
262	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
263	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
264	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	- -	-	0/0
265	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
266	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
267	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
268	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 633.87	- -	-	0/0
269	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0
270	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-	0/0
271	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 549.75	- -	-	0/0
272	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-	0/0
273	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
274	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-	0/0
275	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0
276	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 528.00	- -	-	0/0
277	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 1,200.00	- -	-	0/0
278	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 1,500.00	- -	-	0/0
279	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU	04/1999	198.68 377.71	- -	-	0/0
280	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU	04/1998	271.24 520.00	- -	-	0/0
281	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR, MULTI STATE	04/2007	270.14 -	- -	-	0/0
282	KUMBALAM-TURAVUR - [N22000191]SR, KERALA	04/2011	252.96 -	- -	-	0/0
283	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 603.22	- -	-	0/0
284	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41 302.90	- -	-	0/0
285	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 931.98	- -	-	0/0
286	CHENGANNUR-CHINGAVANAM - [N22000203]SR, KERALA	04/2006	191.72 -	- -	-	0/0
287	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	- -	-	0/0
288	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR, MULTI STATE	04/2011	601.43 800.00	- -	-	0/0
289	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	- -	-	0/0
290	BANDEL-BOINCHI 3RD LINE - [N22000221]ER, MULTI STATE	04/2011	288.35 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
291	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
292	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 595.91	- -	-	0/0
293	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	- -	-	0/0
294	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- -	-	0/0
295	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- -	-	0/0
296	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	-	0/0
297	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	- -	-	0/0
298	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-	0/0
299	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 1,801.00	- 06/2016	-	0/0
300	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
301	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
302	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
303	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
304	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
305	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
306	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
307	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	- -	-	0/0
308	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 832.47	- -	-	0/0
309	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 348.85	- -	-	0/0
310	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
311	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
312	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
313	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
314	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
316	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 893.69	01/1999 -	-	0/0
317	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
318	KAKINADA-PITHAPURAM - [N22000314]SCR,ANDHRA PRADESH	03/1999	215.06 -	- -	-	0/0
319	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-	0/0
320	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
321	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
322	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
323	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 1,072.52	- -	-	0/0
324	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
325	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-	0/0
326	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-	0/0
327	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-	0/0
328	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- -	-	0/0
329	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 -	- -	-	0/0
330	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-	0/0
331	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- -	-	0/0
332	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- -	-	0/0
333	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	- -	-	0/0
334	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
335	KAZIPET-BALHARSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	- -	-	0/0
336	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 3,631.00	- -	-	0/0
337	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
338	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
339	SECUNDERABAD-MOHABOONNAGAR - [N22000371]RVNL, TELANGANA	04/2015	728.10	-	-	0/0
340	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR, BIHAR	01/1991	332.15	07/2014	-	0/0
341	INDORE-DEWAS-UJJAIN(80 KM) DL - [N22000375]WR, MADHYA PRADESH	04/2016	600.00	-	-	0/0
342	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR, ASSAM	04/2093	971.22	-	-	0/0
343	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31	-	-	0/0
344	INDORE DEWAS UJJAIN (80 KM) - [N22000393]WR, GUJARAT	04/2016	600.00	-	-	0/0
345	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR, KERALA	02/2015	900.00	-	-	0/0
346	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR, KERALA	02/2015	1,000.00	-	-	0/0
347	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67	-	-	0/0
348	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	-	03/2019	0/0
349	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98	12/2010	03/2018	0/0
350	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 517.70	-	-	0/0
351	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006	-	0/0
352	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	322.95	03/2012	-	0/0
353	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92	-	-	0/0
354	RAMGANJ-MUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	-	-	0/0
355	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19	-	-	0/0
356	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03	-	-	0/0
357	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	332.92 332.92	03/2012	-	0/0
358	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97	06/2005	12/2019	0/0
359	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92	-	-	0/0
360	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73	03/2012	-	0/0
361	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74	12/2010	-	0/0
362	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00	-	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
363	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
364	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
365	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
366	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
367	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
368	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
369	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
370	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
371	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
372	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
373	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
374	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
375	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
376	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
377	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
378	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
379	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
380	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
381	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
382	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
383	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
384	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
385	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
386	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
387	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
388	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
389	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
390	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
391	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
392	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
393	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
394	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
395	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
396	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
397	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
398	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
399	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
400	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
401	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
402	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
403	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
404	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
405	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
406	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
407	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
408	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
409	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
410	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
411	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
412	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
413	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
414	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
415	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
416	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
417	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
418	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
419	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
420	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
421	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
422	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
423	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
424	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
425	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
	Total		328,605.80 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
426	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	08/2016	0/0
427	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	08/2014	0/0
428	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	11/2015	0/0
429	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0
430	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
431	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	05/2016	0/0
432	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	05/2016	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
433	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	07/2016	0/0
434	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 06/2016	07/2016	0/0
435	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	07/2016	0/0
436	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	07/2016	0/0
437	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	07/2016	0/0
438	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	07/2016	0/0
439	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	07/2016	0/0
440	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	07/2016	0/0
441	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	07/2016	0/0
442	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	08/2016	0/0
443	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
444	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWV,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
445	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	08/2016	0/0
446	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH	02/2012	912.00 -	08/2016 -	08/2016	0/0
447	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	09/2016	0/0
448	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	09/2016	0/0
449	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	09/2016	0/0
450	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	09/2016	0/0
451	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2016	09/2016	0/0
452	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	09/2016	0/0
453	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	09/2016	0/0
454	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	09/2016	0/0
455	2-LANNING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2016	0/0
456	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	09/2016	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
457	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
458	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	09/2016	0/0
459	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2016	0/0
460	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	09/2016	0/0
461	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
462	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	09/2016	0/0
463	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	09/2016	0/0
464	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 10/2016	10/2016	0/0
465	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
466	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	10/2016	0/0
467	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	10/2016	0/0
468	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
469	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
470	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
471	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
472	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
473	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	10/2016	0/0
474	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	11/2016	0/0
475	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
476	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	11/2016	0/0
477	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	11/2016	0/0
478	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATTISGARH	02/2013	1,232.00 -	08/2015 -	11/2016	0/0
479	BIJINI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	12/2016	0/0
480	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	12/2016	0/0

			(August 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
481	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	12/2016	0/0
482	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	12/2016	0/0
483	NALBARI T BIJINI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	12/2016	0/0
484	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 12/2016	12/2016	0/0
485	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	12/2016	0/0
486	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	12/2016	0/0
487	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	12/2016	0/0
488	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	12/2016	0/0
489	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	12/2016	0/0
490	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
491	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	12/2016	0/0
492	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2016	0/0
493	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2016	0/0
494	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	12/2016	0/0
495	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2016	0/0
496	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	12/2016	0/0
497	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2016	0/0
498	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	12/2016	0/0
499	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2016	0/0
500	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2016	0/0
501	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
502	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	12/2016	0/0
503	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2016	0/0
504	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2016	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
505	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2016	0/0
506	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2016	0/0
507	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	12/2016	0/0
508	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	06/2014 -	12/2016	0/0
509	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
510	2-LANING WITH PS SITARGANJ BAREILLY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016	0/0
511	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	12/2016	0/0
512	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	- -	12/2016	0/0
513	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2016	0/0
514	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	01/2017	0/0
515	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
516	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	01/2017	0/0
517	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD, ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
518	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	02/2017	0/0
519	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	02/2017	0/0
520	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
521	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	04/2009 -	03/2017	0/0
522	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 -	09/2007 -	03/2017	0/0
523	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	03/2017	0/0
524	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	03/2017	0/0
525	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	03/2017	0/0
526	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	03/2017	0/0
527	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	03/2017	0/0
528	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN	10/2013	677.79 -	04/2016 -	03/2017	0/0

			(August 2016)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
529	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85	01/2016	03/2017	0/0
530	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89	03/2017	03/2017	0/0
531	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49	03/2017	03/2017	0/0
532	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76	03/2017	03/2017	0/0
533	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94	03/2017	03/2017	0/0
534	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00	03/2014	04/2017	0/0
535	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN	10/2014	206.12	04/2017	04/2017	0/0
536	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72	04/2017	04/2017	0/0
537	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00	02/2010	05/2017	0/0
538	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43	08/2013	05/2017	0/0
539	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00	06/2015	05/2017	0/0
540	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14	05/2017	05/2017	0/0
541	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09	05/2017	05/2017	0/0
542	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05	05/2017	05/2017	0/0
543	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08	05/2017	05/2017	0/0
544	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49	05/2017	05/2017	0/0
545	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32	05/2017	05/2017	0/0
546	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00	05/2013	06/2017	0/0
547	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00	01/2014	06/2017	0/0
548	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	09/2014	06/2017	0/0
549	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI,TAMIL NADU	12/2014	451.58	06/2017	06/2017	0/0
550	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76	-	06/2017	0/0
551	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30	-	06/2017	0/0
552	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22	-	06/2017	0/0

			(August 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
553	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	06/2017	0/0
554	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	07/2017	0/0
555	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP, MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
556	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
557	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2017	0/0
558	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD, MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
559	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
560	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
561	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI, JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
562	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
563	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	10/2017	0/0
564	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	11/2015 -	10/2017	0/0
565	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
566	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAP - [N24000379]MORTH, ODISHA	01/1991	218.63 -	10/2017 -	10/2017	0/0
567	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2017	0/0
568	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
569	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
570	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
571	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
572	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- -	11/2017	0/0
573	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, PUNJAB	09/2015	273.06 -	- -	11/2017	0/0
574	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
575	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2017	0/0
576	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
577	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2017	0/0
578	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
579	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	12/2017	0/0
580	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
581	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	12/2017	0/0
582	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2017	0/0
583	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
584	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
585	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
586	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0
587	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	12/2017	0/0
588	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
589	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0
590	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
591	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
592	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
593	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
594	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
595	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
596	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
597	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
598	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	02/2018	0/0
599	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
600	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
601	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
602	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI, UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
603	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI, UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
604	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI, UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
605	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
606	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
607	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
608	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
609	FOUR LANING FROM MP MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
610	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
611	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA - BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI, HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
612	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
613	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	- -	04/2018	0/0
614	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	- -	04/2018	0/0
615	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH, ODISHA	01/1991	229.41 -	05/2018 -	05/2018	0/0
616	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	- -	05/2018	0/0
617	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	- -	05/2018	0/0
618	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH - 54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	- -	05/2018	0/0
619	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	- -	05/2018	0/0
620	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	- -	05/2018	0/0
621	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	- -	05/2018	0/0
622	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	- -	05/2018	0/0
623	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	06/2018	0/0
624	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
625	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
626	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
627	4-LANING OF GHAGHRA BRIDGE TO VARANASI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
628	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
629	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
630	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	- -	06/2018	0/0
631	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
632	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
633	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
634	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	- -	06/2018	0/0
635	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
636	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	07/2018	0/0
637	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI, MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
638	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0
639	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	01/1991	1,388.00 -	- -	08/2018	0/0
640	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0
641	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
642	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	- -	11/2018	0/0
643	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	- -	11/2018	0/0
644	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL, ASSAM	12/2015	225.02 -	12/2018 -	12/2018	0/0
645	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
646	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
647	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	12/2018	0/0
648	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL, ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	01/2019	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
649	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
650	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
651	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0
652	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
653	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI,RAJASTHAN	06/2016	725.95 -	06/2019 -	06/2019	0/0
654	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
655	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
656	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-	0/0
657	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
658	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
659	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
660	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
661	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
662	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	-	0/0
663	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
664	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
665	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
666	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
667	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
668	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
669	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
670	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
671	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
672	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
673	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
674	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
675	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
676	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
677	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
678	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
679	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
680	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
681	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
682	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
683	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
684	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
685	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
686	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
687	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
688	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
689	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
690	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
691	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
692	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
693	CONSTRUCTION OF RING ROAD FOR RAE BARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
694	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
695	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC.IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
696	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0

			(August 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
697	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
698	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
699	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
700	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
701	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
702	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
703	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOU LA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
704	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
705	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
706	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
707	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
708	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
709	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
710	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
711	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
712	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
713	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
714	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-	0/0
715	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0
716	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
717	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
718	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-	0/0
719	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
720	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0

			(August 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
721	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-	0/0
722	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-	0/0
723	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
724	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
725	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-	0/0
726	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
727	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
728	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
729	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
730	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-	0/0
731	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-	0/0
732	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
733	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-	0/0
734	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
735	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-	0/0
736	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-	0/0
737	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
738	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-	0/0
739	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
740	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
741	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
742	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
743	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-	0/0
744	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
745	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
746	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
747	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
748	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
749	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
750	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
751	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
752	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-	0/0
753	MEERUT-BULANDSHAHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
754	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	-	0/0
755	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	-	0/0
756	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	-	0/0
757	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	-	0/0
758	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	-	0/0
759	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
760	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	-	0/0
761	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
762	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
763	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	-	0/0
764	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-	0/0
765	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-	0/0
766	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	-	0/0
767	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
768	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
769	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
770	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
771	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
772	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
773	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0
774	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
775	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
776	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0
777	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
778	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
779	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	-	0/0
780	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-	0/0
781	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
782	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
783	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
784	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
785	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	- -	-	0/0
786	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
787	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	- -	-	0/0
788	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
789	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	-	0/0
790	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	-	0/0
791	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
792	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	-	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
793	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	-	0/0
794	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-	0/0
795	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	- -	-	0/0
796	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
797	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	-	0/0
798	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	-	0/0
799	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-	0/0
800	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
801	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-	0/0
	Total		250,257.90 -			0/0
	<u>SHIPPING AND PORTS</u>					
802	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	04/2009 03/2010	08/2016	0/0
803	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 600.00	03/2006 03/2016	12/2016	0/0
804	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
805	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	12/2010 12/2018	12/2018	0/0
806	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		3,399.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
807	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	-	0/0
	Total		13,334.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
808	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
809	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 10/2015	10/2016	0/0

			(August 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
810	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	06/2015 08/2016	11/2016	0/0
811	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
812	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 01/2017	01/2017	0/0
813	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2014 12/2016	03/2017	0/0
814	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	03/2012 08/2016	03/2017	0/0
815	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
816	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 -	03/2015 03/2017	03/2017	0/0
817	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 04/2017	04/2017	0/0
818	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 270.83	11/2014 05/2017	05/2017	0/0
819	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	06/2017	0/0
820	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	03/2015 10/2017	10/2017	0/0
821	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD,KERALA	07/2015	154.00 -	11/2015 -	11/2017	0/0
822	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
823	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	10/2019 -	12/2018	0/0
824	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
825	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	11/2014 07/2016	-	0/0
826	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-	0/0
827	CONSTRUCTION OF 100 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	- -	-	0/0
828	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-	0/0
829	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		107,604.05 -			0/0
	Grand Total		846,079.37			0/0

Annexure - XI

List of Projects Ahead of Schedule w.r.t. Latest Schedule

						(August 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	204.72	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	204.72		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
2	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 230.00	208.00	309.52	04/2008 01/2017	12/2016
	Total		208.00 -	208.00	309.52		
	<u>COAL</u>						
3	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52	555.52	4.36	03/2021 -	03/2017
	Total		555.52 -	555.52	4.36		
	<u>PETROLEUM</u>						
4	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	366.03	01/2017 -	09/2016
	Total		419.04 -	419.04	366.03		
	<u>URBAN DEVELOPMENT</u>						
5	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	10/2019 -	12/2018
6	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017
	Total		6,401.00 -	6,401.00	.00		
	<u>PETROLEUM</u>						
7	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	1,899.13	04/2019 -	03/2019
8	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	4.91	02/2019 -	12/2018
	Total		6,316.32 -	6,316.32	1,904.04		

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	COAL						
9	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	103.25	03/2019 -	03/2018
	Total		304.52 -	304.52	103.25		
	Grand Total		14,463.80	14,690.97	2,891.92		

Annexure - XII

List of Projects on schedule w.r.t. Latest Schedule

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	CIVIL AVIATION						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073	10/2013	314.61 -	314.61	26.30	09/2018 -	09/2018
	Total		314.61 -	314.61	26.30		
	COAL						
2	JHANJRA COMBINED PR(3.50 MTY) - [N06000020	11/2015	602.86 -	602.86	193.77	03/2022 -	03/2022
3	RAMPUR BATURA OCP (4.0 MTY) - [N06000049	8/2015	1,186.64 -	1,186.64	13.00	03/2023 -	03/2023
4	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
5	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138	4/2013	1,458.17 -	1,458.17	82.49	06/2015 08/2019	08/2019
6	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
7	MADANNAGAR OPENCAST PROJECT - [N06000140	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
8	MALACHUA OPENCAST PROJECT - [N06000139	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
9	PELMA OCP(15.00MTY) - [N06000045	11/2014	1,624.59 -	1,624.59	5.53	03/2023 03/2023	03/2023
10	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142	11/2015	498.42 -	498.42	0.27	03/2020 -	03/2020
11	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
12	BHANEGAON OC - [N06000121	2/2015	187.94 -	187.94	59.62	03/2023 -	03/2023
13	GOKUL - [N06000120	11/2014	267.67 -	267.67	178.29	03/2018 -	03/2018
14	MAKARDHOKRA I OC - [N06000119	9/2014	266.23 -	266.23	112.08	03/2021 -	03/2021
15	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	249.04	03/2020 -	03/2020
16	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	338.55	03/2021 -	03/2021
17	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
18	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	1.27	03/2019 -	03/2019

(August 2016)								
						Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated	
1	2	3	4	5	6	7	8	
19	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	621.84	03/2026 -	03/2026	
20	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095	6/2011	5,907.11 -	5,907.11	2,503.92	12/2015 04/2018	04/2018	
21	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093	6/2010	11,816.40 -	11,816.40	2,093.73	03/2023 -	03/2023	
22	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	154.15	03/2020 -	03/2020	
23	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091	6/2011	1,131.28 -	1,131.28	330.34	03/2018 -	03/2018	
24	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	840.32	03/2023 03/2023	03/2023	
25	DURGAPUR OPENCAST PROJECT - [N06000136	2/2015	916.24 -	916.24	-	03/2023 -	03/2023	
26	AMGAON OPENCAST PROJECT RCE - [N06000135	7/2015	316.10 -	316.10	17.60	03/2020 -	03/2020	
27	BATURA HIGHWALL PROJECT - [N06000134	7/2015	231.92 -	231.92	-	03/2022 -	03/2022	
28	ADASA UG TO OC - [N06000133	8/2015	288.90 -	288.90	-	03/2023 -	03/2023	
29	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149	2/2016	198.68 -	198.68	1.95	03/2019 -	03/2019	
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148	3/2016	869.44 -	869.44	108.64	03/2021 -	03/2021	
31	KALYANIKHANI 6 INCLINE PROJECT - [N06000147	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	
32	KOYAGUDEM OPENCAST PROJECT - [N06000146	10/2015	426.79 -	426.79	-	03/2018 -	03/2018	
33	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145	3/2015	513.63 -	513.63	74.76	12/2019 -	12/2019	
34	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144	3/2015	522.45 -	522.45	2.57	09/2019 -	09/2019	
35	AMALGAMATED YEKONA-I YEKONA-II - [N06000132	8/2015	727.28 -	727.28	81.73	03/2025 -	03/2025	
36	AMALGAMATED PAUNI-II III OC MINE - [N06000131	6/2015	483.69 -	483.69	57.98	03/2021 -	03/2021	
37	SINGHORI OC MINE - [N06000130	6/2015	205.49 -	205.49	57.02	03/2020 -	03/2020	
38	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129	5/2015	397.09 -	397.09	0.30	03/2019 -	03/2019	
39	NEW MAJRI UG TO OC - [N06000128	5/2015	295.56 -	295.56	85.12	03/2019 -	03/2019	
40	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	27.56	03/2021 -	03/2021	
41	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	111.94	03/2021 -	03/2021	
42	AMERA OC RCE - [N06000123	2/2015	335.97 -	335.97	34.55	03/2018 -	03/2018	

						(August 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
43	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	110.96	03/2020 -	03/2020
44	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	14.84	03/2019 -	03/2019
45	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	90.59	03/2020 -	03/2020
46	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
47	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
	Total		53,890.09 -	53,890.09	8,708.07		
	<u>FERTILISERS</u>						
48	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	75.85	11/2016 09/2017	09/2017
49	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	37.96	12/2017 -	12/2017
	Total		680.64 -	692.29	113.81		
	<u>HEALTH AND FAMILY WELFARE</u>						
50	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	70.00	03/2018 -	03/2018
	Total		505.58 -	505.58	70.00		
	<u>MINES</u>						
51	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT JATH SANGLI MA ARASHTRA - [N10000008]	12/2015	355.13 -	355.13	243.19	11/2016 11/2016	11/2016
52	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	201.17	11/2016 11/2016	11/2016
	Total		699.63 -	699.63	444.36		
	<u>PETROLEUM</u>						
53	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	1,879.11	03/2013 03/2017	03/2017
54	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	507.53	09/2017 03/2018	03/2018
55	REPLACEMENT OF COKE CHAMBERS - [N16000177]	4/2013	480.00 -	422.00	288.40	02/2016 10/2016	10/2016
56	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	6.92	05/2019 -	05/2019

						(August 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	ENNORE TERMINAL - [N16000224	8/2014	393.00 -	393.00	93.83	04/2018 -	04/2018
58	HALDIA LPG IMPORT FACILITY - [N16000223	3/2015	694.00 -	694.00	62.87	10/2018 -	10/2018
59	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222	8/2014	190.45 -	190.45	58.20	09/2017 -	09/2017
60	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL - [N16000221	1/1991	694.00 -	694.00	57.19	10/2018 -	10/2018
61	LPG STORAGE TERMINAL AT PALAKKAD, KERALA - [N16000220	2/2015	184.00 -	184.00	12.43	12/2017 -	12/2017
62	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE - [N16000219	8/2014	393.00 -	393.00	-	04/2018 -	04/2018
63	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218	2/2016	367.11 -	367.11	19.42	04/2017 -	04/2017
64	BULK PETROLEUM OIL AND LUBRICANT (POL) DEPOT AT IMPHAL, MANIPUR - [N16000215	8/2010	103.02 -	171.04	122.29	07/2016 08/2016	08/2016
65	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
66	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	678.00	-	02/2017 -	02/2017
67	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233	4/2016	327.78 -	327.78	-	04/2018 -	04/2018
68	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232	7/2014	199.95 -	199.95	62.19	03/2018 -	03/2018
69	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231	7/2015	1,427.94 -	1,427.94	0.86	12/2018 -	12/2018
70	SIX PIPELINE REPLACEMENT PROJECT - [N16000214	3/2009	181.02 -	173.28	104.89	01/2017 -	01/2017
71	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,190.69	83.38	04/2018 -	04/2018
72	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212	1/2015	4,619.94 -	4,619.94	1,382.08	12/2017 -	12/2017
73	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211	11/2014	195.63 -	195.63	81.86	09/2018 -	09/2018
74	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	2/2015	749.00 -	749.00	231.02	02/2020 -	02/2020
75	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	-	03/2013 01/2017	01/2017
76	DE-BOTTLENECKING OF SMPL - [N16000089	12/2009	1,584.00 -	1,584.00	1,465.03	03/2017 03/2017	03/2017
77	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088	8/2009	1,793.00 -	1,793.00	1,532.49	12/2016 -	12/2016
78	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	1,256.72	1,056.23	05/2013 12/2016	12/2016
79	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072	7/2009	3,957.00 -	3,561.00	243.81	01/2013 12/2018	12/2018

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
80	CONSTRUCTION OF 6 ETPS - [N16000117]	3/2009	317.64 -	240.95	150.26	09/2012 09/2016	09/2016
81	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
82	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,263.13	05/2017 -	05/2017
83	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
84	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	1,221.41	05/2019 05/2019	05/2019
85	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	141.59	12/2016 -	12/2016
86	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
87	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	80.29	01/2018 -	01/2018
88	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	303.92	10/2014 03/2017	03/2017
89	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	502.33	08/2015 12/2016	12/2016
90	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	648.51	11/2015 11/2016	11/2016
91	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	375.14	12/2014 03/2018	03/2018
92	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	1,426.00	05/2014 03/2017	03/2017
93	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,350.72	03/2015 03/2018	03/2018
94	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]	12/2009	463.32 -	463.32	357.01	06/2011 10/2016	10/2016
95	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	183.99	09/2016 -	09/2016
96	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	4,309.00	05/2017 05/2017	05/2017
97	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	290.83	12/2017 -	12/2017
98	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017
99	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	439.03	1.57	03/2017 06/2018	06/2018
100	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	1,022.55	04/2016 12/2017	12/2017
101	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	251.66	172.53	06/2012 08/2016	08/2016

(August 2016)								
						Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated	
1	2	3	4	5	6	7	8	
	Total		86,553.39 -	87,041.83	23,160.79			
	<u>POWER</u>							
102	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	6,210.00	09/2017 -	09/2017	
103	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	60.30	03/2018 -	03/2018	
104	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	935.60	04/2018 -	04/2018	
105	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	210.00	09/2019 -	09/2019	
106	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	3,267.00	02/2019 02/2020	02/2020	
107	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	3,925.00	08/2018 -	08/2018	
108	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	1,718.00	03/2019 -	03/2019	
109	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,589.00	12/2016 03/2017	03/2017	
110	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	236.50	11/2017 -	11/2017	
111	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017	
112	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	-	04/2019 -	04/2019	
113	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.13	-	06/2018 -	06/2018	
114	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	-	06/2018 -	06/2018	
115	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	-	11/2019 -	11/2019	
116	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	-	05/2019 -	05/2019	
117	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	-	11/2018 -	11/2018	
118	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	364.60 -	364.60	-	05/2018 -	05/2018	
119	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]	1/2014	1,788.41 -	1,788.41	-	09/2017 -	09/2017	

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
120	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	1/1991	454.11 -	454.11	-	04/2018 -	04/2018
121	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	0.10	01/2018 -	01/2018
122	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	175.00	07/2020 -	07/2020
123	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS [N18000211]	1/2016	187.04 -	187.04	5.90	06/2018 -	06/2018
124	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	4.00	07/2018 -	07/2018
125	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	3.50	05/2018 -	05/2018
126	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	32.40	07/2018 -	07/2018
127	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
128	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	17.90	03/2017 -	03/2017
129	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	1,794.00	09/2019 -	09/2019
130	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	145.00	08/2017 -	08/2017
131	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	6,807.00	06/2017 09/2017	09/2017
132	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	6,764.00	11/2016 08/2017	08/2017
133	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	5,761.00	09/2016 01/2017	01/2017
134	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	11,603.00	01/2017 07/2017	07/2017
135	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,441.52	1,066.32	07/2006 09/2017	09/2017
136	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	8/2014	288.49 -	288.49	127.90	02/2017 -	02/2017
137	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	881.40	03/2018 -	03/2018
138	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC [N18000167]	6/2014	400.47 -	400.47	180.40	04/2017 -	04/2017
139	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	1/2008	4,375.35 -	6,749.18	6,187.00	09/2011 06/2017	06/2017
140	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	2,944.00	03/2013 06/2019	06/2019

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166	2/2014	378.71 -	378.71	170.30	10/2016 -	10/2016
142	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 -	522.29	235.70	11/2016 -	11/2016
143	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204	10/2015	315.00 -	315.00	256.02	10/2016 -	10/2016
144	BARH STPP(3X660MW) NTPC - [180100242	2/2005	8,692.97 -	15,095.67	12,000.00	01/2011 05/2018	05/2018
145	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,581.04	1,275.79	08/2013 05/2017	05/2017
146	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	7/2006	1,657.00 -	2,978.86	1,845.71	02/2016 09/2019	09/2019
147	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,179.96	4,715.05	12/2009 10/2017	10/2017
148	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201	7/2015	307.18 -	307.18	35.90	11/2017 -	11/2017
149	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200	7/2015	2,247.37 -	2,247.37	89.30	07/2018 -	07/2018
150	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197	4/2015	1,479.30 -	1,479.30	322.50	04/2017 -	04/2017
151	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196	4/2015	3,705.61 -	3,705.61	702.80	04/2018 -	04/2018
152	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
153	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194	5/2015	436.68 -	436.68	447.48	12/2016 -	12/2016
154	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
155	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186	3/2015	550.06 -	550.06	62.60	03/2018 -	03/2018
156	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184	3/2015	197.40 -	197.40	5.70	03/2018 -	03/2018
157	WARDHA-HYDERABAD 765 KV LINK - [N18000183	1/2015	3,662.02 -	3,662.02	1,006.50	05/2018 -	05/2018
158	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	1/2015	203.28 -	203.28	42.80	07/2017 -	07/2017
159	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181	1/2015	871.62 -	871.62	65.40	10/2017 -	10/2017
160	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	2/2009	11,130.19 -	13,762.80	12,037.00	08/2013 12/2017	12/2017

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		208,828.88	228,190.61	97,970.37		
			-				
	<u>RAILWAYS</u>						
161	VIRAMGAM-BHILDI(WR),GC - [N220100062	4/1990	155.66	548.01	265.18	- 03/2019	03/2019
162	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113	4/2008	653.19	658.07	467.45	03/2014 03/2019	03/2019
163	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60	299.60	-	03/2017 -	03/2017
164	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [N220100168	4/1995	900.05	1,125.89	982.31	12/2011 03/2020	03/2020
165	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	4/2008	5,300.00	7,986.04	2,423.55	03/2014 03/2019	03/2019
166	NANDYAL-YERRAGUNTLA(NL),SCR - [N220100192	3/1996	155.74 164.36	966.98	901.74	02/2009 12/2017	12/2017
167	KHURDA ROAD-BOLANGIR(NL)ECOR - [N220100284	4/1994	470.21	3,004.90	629.60	- 06/2021	06/2021
168	KIUL - GAYA DOUBLING PROJECT - [N22000349	12/2015	1,200.20	1,200.20	0.23	12/2020 -	12/2020
169	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,750.00	1,750.00	-	03/2022 -	03/2022
170	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41	2,030.50	12.23	02/2019 12/2022	12/2022
171	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	4/2007	1,640.04	1,640.04	349.24	- 03/2022	03/2022
172	HAJIPUR - BACHAWARA - [N22000334	5/2015	720.00	678.54	0.75	- 12/2018	12/2018
173	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77	209.00	0.36	12/2016 -	12/2016
174	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57	1,160.83	224.90	- 03/2020	03/2020
175	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	4/2008	318.24	321.62	44.65	03/2012 03/2019	03/2019
176	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122	4/2008	1,389.62	1,389.62	1,614.79	03/2014 12/2017	12/2017
177	VIRAMGAM BHILDI - [N22000391	4/1990	237.13	237.13	25.05	03/2018 -	03/2018
178	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92	1,172.92	-	03/2021 -	03/2021
179	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	4/2015	701.61	701.61	-	03/2021 -	03/2021
180	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379	4/2015	2,361.74	2,361.74	0.93	03/2021 -	03/2021
181	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71	2,499.71	0.40	03/2021 -	03/2021

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
182	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021
183	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
184	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
185	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	0.12	12/2020 -	12/2020
186	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.65	403.93	12/2020 -	12/2020
187	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.25	458.72	12/2020 -	12/2020
188	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	682.92	03/2019 -	03/2019
189	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	482.81	03/2020 -	03/2020
190	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	495.97	03/2020 -	03/2020
191	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020
192	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.13	12/2025 -	12/2025
193	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	4,295.30	87.74	12/2026 -	12/2026
194	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
195	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
196	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	-	03/2020 -	03/2020
197	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
198	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
199	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	927.01	516.85	03/2019 -	03/2019
200	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	0.46	12/2024 -	12/2024
201	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
202	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.93	12/2021 -	12/2021
203	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	480.38	12/2021 -	12/2021

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
204	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	108.75	03/2021 -	03/2021
205	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	26.23	03/2020 -	03/2020
206	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	-	03/2021 -	03/2021
207	JAGGAYYAPET - MELLACHERUVU - [N22000304]	4/2007	313.24 -	554.70	407.65	01/1999 06/2017	06/2017
208	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
	Total		60,935.90 -	71,013.34	12,443.54		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
209	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	202.41	05/2008 12/2016	12/2016
210	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	-	06/2018 -	06/2018
211	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
212	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	46.11	05/2018 -	05/2018
213	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	-	10/2018 -	10/2018
214	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	-	03/2018 -	03/2018
215	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	292.34	02/2018 -	02/2018
216	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19 -	425.19	274.20	09/2016 -	09/2016
217	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	140.65	09/2017 -	09/2017
218	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00 -	709.00	20.56	09/2017 -	09/2017
219	2 LANING WITH PAVED SHOULDER OF KARAUKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH - [N24000340]	12/2014	451.58 -	451.58	28.00	06/2017 -	06/2017
220	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	121.88	04/2017 -	04/2017

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
221	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	70.35	02/2018 -	02/2018
222	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	-	10/2016 -	10/2016
223	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
224	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377	1/2014	397.04 -	397.04	17.71	10/2016 -	10/2016
225	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
226	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373	11/2010	305.49 -	305.49	-	03/2017 -	03/2017
227	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017
228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26 -	269.26	218.10	10/2016 -	10/2016
229	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368	11/2014	563.92 -	563.92	146.29	11/2016 -	11/2016
230	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366	6/2015	996.37 -	996.37	2.18	12/2017 -	12/2017
231	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	246.10	01/2017 -	01/2017
232	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
233	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017
234	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	10.32	05/2018 -	05/2018
236	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
237	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
238	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
239	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
240	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]	10/2013	283.45 -	283.45	21.03	10/2016 -	10/2016
241	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	1/1991	358.22 -	358.22	200.21	10/2016 -	10/2016
242	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]	2/2015	327.32 -	327.32	162.33	05/2017 -	05/2017
243	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
244	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
245	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
246	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
247	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
248	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
249	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	133.00	04/2018 -	04/2018
250	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
251	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
252	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
253	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
254	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
255	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]	1/2014	1,408.85 -	1,408.85	-	10/2016 -	10/2016
256	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	-	11/2017 -	11/2017

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
257	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
258	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,620.11	01/2018 -	01/2018
259	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
260	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	6.02	06/2018 -	06/2018
261	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
262	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53 -	1,027.53	5.92	06/2018 -	06/2018
263	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
264	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
265	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23 -	239.23	40.30	12/2017 -	12/2017
266	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	57.93	03/2018 -	03/2018
267	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018
268	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
269	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
270	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
271	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
272	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
273	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	225.02	-	12/2018 -	12/2018
274	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	-	08/2016 -	08/2016
275	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]	10/2015	597.00 -	597.00	81.34	10/2017 -	10/2017
276	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	-	05/2018 -	05/2018

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
277	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017
278	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	282.41	75.32	08/2016 -	08/2016
279	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	66.59	03/2018 -	03/2018
280	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	6.33	03/2018 -	03/2018
281	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]	6/2015	532.49 -	532.49	166.22	05/2017 -	05/2017
282	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
283	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	0.54	05/2017 -	05/2017
284	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATTA - [N24000379]	1/1991	218.63 -	218.63	41.21	10/2017 -	10/2017
285	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
286	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	41.87	05/2017 -	05/2017
287	PADI - DAHOD - [N24000353]	11/2014	279.14 -	279.14	122.20	05/2017 -	05/2017
288	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]	10/2014	264.72 -	264.72	136.71	04/2017 -	04/2017
289	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	65.88	07/2017 -	07/2017
290	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]	6/2015	563.92 -	563.92	21.06	12/2017 -	12/2017
291	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	111.99	02/2018 -	02/2018
292	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	234.99	11/2017 -	11/2017
293	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
294	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]	10/2014	244.30 -	156.09	-	12/2016 -	12/2016

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
295	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	957.30	09/2016 -	09/2016
296	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,544.63	11/2016 -	11/2016
297	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	409.32	04/2010 09/2016	09/2016
298	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	10/2016
299	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
300	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]	5/2014	497.89 -	497.89	-	04/2017 -	04/2017
301	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017
302	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	46.68	02/2017 -	02/2017
303	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
304	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017
305	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]	12/2013	220.72 -	220.72	113.36	11/2016 -	11/2016
306	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]	6/2014	260.39 -	260.39	119.70	11/2016 -	11/2016
307	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
308	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
309	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
310	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	-	01/2019 -	01/2019
311	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	-	06/2018 -	06/2018
312	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	63.38	07/2017 -	07/2017

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
313	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	-	05/2018 -	05/2018
	Total		57,522.09 -	57,753.42	9,005.62		
	<u>SHIPPING AND PORTS</u>						
314	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	176.55	06/2017 -	06/2017
315	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	1/2007	366.39 -	669.46	415.01	12/2010 12/2018	12/2018
316	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	42.57	12/2017 -	12/2017
317	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
318	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	274.85	189.52	04/2017 -	04/2017
	Total		1,294.68 -	1,647.79	823.65		
	<u>STEEL</u>						
319	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	200.20	12/2016 -	12/2016
320	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103	4/2014	151.33 -	151.33	15.04	09/2017 -	09/2017
321	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
322	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	136.65	03/2018 -	03/2018
323	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111	2/2014	787.29 -	787.29	328.23	12/2016 -	12/2016
324	COKE OVEN BATTERY-5 - [N12000117	12/2011	2,858.00 -	2,500.00	209.43	12/2017 -	12/2017
325	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	27.47	09/2018 -	09/2018
326	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	2.44	06/2020 -	06/2020
327	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097	2/2014	4,749.00 -	4,749.00	17.32	09/2017 -	09/2017
328	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096	5/2015	1,154.18 -	1,154.18	116.30	12/2017 -	12/2017

(August 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
329	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	66.80	10/2017 -	10/2017
330	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	380.84	04/2018 -	04/2018
331	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	53.47	03/2018 -	03/2018
332	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	10,082.02	05/2015 12/2017	12/2017
333	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	91.91	04/2018 -	04/2018
	Total		32,903.76 -	32,570.15	11,728.12		
	<u>URBAN DEVELOPMENT</u>						
334	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	133.58	09/2016 01/2017	01/2017
335	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	5,298.00	1,680.80	11/2019 -	11/2019
336	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	221.25	03/2018 -	03/2018
337	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	49.18	03/2017 -	03/2017
338	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]	2/2014	216.69 -	216.69	22.45	03/2015 10/2017	10/2017
339	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]	8/2014	350.02 -	350.02	161.29	03/2015 03/2017	03/2017
340	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]	1/2010	165.23 -	165.23	36.54	10/2012 04/2017	04/2017
341	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]	11/2012	270.83 -	270.83	-	11/2014 05/2017	05/2017
	Total		14,437.33 -	15,471.33	2,305.09		
	Grand Total		518,566.58	549,790.67	166,799.72		

Annexure - XIII

List of ongoing projects having cost overrun w.r.t. to latest schedule

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	10/2017	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071]	10/2012	217.60 -	244.10	03/2015 -	-	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.59	03/2015 -	03/2020	201.51
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2019	0.02
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,693.72 -	3,143.50			
	<u>HEAVY INDUSTRY</u>						
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
10	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	06/2018	24.53
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	09/2016	70.49

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	09/2016	63.54
13	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	-	67.62
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	12/2016	37.72
	Total		4,761.99 -	6,672.25			
	<u>POWER</u>						
16	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
18	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49	02/2016 -	-	0.16
19	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	10/2016	2.38
20	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	9.40
21	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	-	58.79
	Total		20,584.45 -	45,764.05			
	<u>RAILWAYS</u>						
22	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	02/2016	131.09
23	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	-	387.07
24	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
25	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	870.00	- -	-	459.31
26	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
27	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	317.21
28	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
29	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	-	543.99

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
30	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
31	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
32	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,500.00	12/2012 12/2012	-	147.08
33	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	01/2016	210.19
34	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	09/2009 -	-	293.06
35	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	3,000.00	- -	-	312.58
36	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
37	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
38	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	340.00	03/2009 03/2009	10/2016	64.25
40	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	811.36	- -	-	0.07
41	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
42	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	318.00	02/2006 -	-	21.51
43	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
44	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	2,072.50	- -	-	412.75
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	1,065.00	- -	-	210.34
46	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	490.00	- -	-	292.00
47	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	1,080.00	- -	-	136.84
48	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
49	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
50	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
51	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,825.00	03/2008 06/2008	-	145.63
52	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,421.25	03/2012 -	03/2022	135.68

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	01/2011 -	3.07
54	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	03/2016 -	123.34
55	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	365.00	- -	- -	269.66
56	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	- -	191.18
57	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	- -	97.26
58	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	- -	108.66
59	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	- -	985.42
60	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	- -	167.83
61	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	- -	100.76
62	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	- -	183.41
63	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	- -	134.68
64	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	- -	50.10
65	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	- -	14.14
66	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,170.00	01/1999 -	- -	153.83
67	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017 -	77.08
68	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	- -	71.50
69	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	- -	53.96
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2017 -	233.33
71	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	5,050.00	05/2008 -	03/2023 -	1,939.09
72	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	- -	210.80
73	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	- -	300.67
74	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	- -	232.17
75	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019 -	310.64

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
77	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,658.00	03/2011 -	03/2019	1,227.45
78	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
79	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47
80	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	780.00	- -	03/2019	290.00
81	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	2,145.00	- -	03/2020	615.00
82	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	3,000.00	03/2015 -	03/2021	252.94
83	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
84	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58
85	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
86	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	360.00	- -	-	27.24
87	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
88	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,679.13	- -	12/2016	58.06
89	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	744.71 -	1,126.79	- -	10/2016	51.31
90	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	780.98	- -	-	90.45
91	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114	04/2008	516.23 -	735.00	03/2014 -	-	42.38
92	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
93	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
94	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
95	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	03/2017	386.62
96	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
97	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	12/2016	122.68

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
99	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	488.33
100	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
101	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
102	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
103	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
104	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
105	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	-	72.62
106	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
107	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
108	KAKINADA-PITHAPURAM - [N22000314	03/1999	215.06 -	220.29	- -	-	2.43
109	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	03/2021	63.70
110	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	10/2015	14.43
111	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	- -	03/2020	52.77
112	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
113	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
114	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322	04/2011	190.10 -	355.96	- -	03/2019	87.25
115	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
116	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	620.00	- -	09/2019	3.33
117	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	1,010.00	- -	-	711.70
118	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
119	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
120	AHMEDABAD-BOTAD (GC) - [N22000140	04/2012	567.18 -	975.62	- -	03/2020	72.01

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
121	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	-	71.11
122	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
123	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
124	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
125	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	09/2015	27.06
126	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
127	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
128	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
129	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	860.00	- -	12/2018	88.60
130	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	03/2017	17.92
131	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
132	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
133	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
134	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
135	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
136	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
137	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41
138	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
139	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
141	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
142	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
143	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62	2,393.23	-	-	252.66
144	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01	367.17	-	-	72.37
145	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68	556.64	-	-	180.17
146	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39	1,480.83	-	03/2018	80.06
147	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14	346.15	-	-	28.14
148	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42	380.00	-	-	71.62
149	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00	1,857.00	03/2007	03/2016	107.49
150	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77	445.00	-	03/2018	112.14
151	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55	330.00	-	03/2018	16.38
152	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41	450.00	-	-	173.71
153	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00	951.24	-	-	285.12
154	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72	342.85	-	-	78.83
155	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02	6,000.00	-	03/2020	46.95
156	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22	471.00	-	-	94.45
157	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52	394.28	-	03/2017	63.25
158	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82	450.00	-	03/2019	171.38
159	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17	1,653.55	-	03/2018	216.06
160	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12	508.00	-	03/2018	62.76
161	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07	386.68	-	03/2019	57.14
162	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68	816.55	03/2016	12/2017	29.06
163	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98	2,103.00	-	-	129.59
164	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26	233.73	04/2014	03/2018	24.82
165	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15	559.91	07/2014	-	68.57

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
166	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00 -	- -	05/2015	5.12
167	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00 -	12/2021 -	12/2021	87.11
168	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00 -	12/2021 -	12/2021	79.05
169	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	943.60 -	12/2024 -	12/2024	25.72
	Total		75,435.75 -	209,429.64 -			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
170	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00 -	02/2009 -	09/2016	28.93
171	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13 -	04/2009 -	03/2017	92.75
172	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13 -	11/2008 -	12/2016	80.68
173	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23 -	07/2009 -	03/2017	68.99
174	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00 -	11/2011 -	12/2016	106.50
175	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]	01/2014	361.30 -	207.40 -	07/2014 -	-	-42.60
176	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31 -	02/2010 -	05/2017	2.29
177	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10 -	04/2013 -	12/2016	2.65
178	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27 -	02/2017 -	02/2017	6.02
179	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82 -	12/2015 -	-	55.66
180	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43 -	09/2017 -	09/2017	0.12
181	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05 -	11/2017 -	11/2017	0.01
182	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12 -	02/2015 -	-	0.06
183	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]	12/2009	104.00 -	201.00 -	09/2010 -	-	93.27

(August 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
184	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77 -	11/2015 -	12/2016	51.83
	Total		6,146.96 -	8,697.76 -			
	<u>SHIPPING AND PORTS</u>						
185	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33 -	12/2017 -	12/2017	0.13
186	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83 -	04/2009 -	08/2016	66.82
	Total		490.17 -	668.16 -			
	<u>STEEL</u>						
187	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40 -	10/2016 -	09/2017	42.39
188	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94 -	12/2015 -	03/2017	1.70
	Total		492.73 -	664.34 -			
	<u>URBAN DEVELOPMENT</u>						
189	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	14,405.01 -	06/2011 -	01/2017	125.25
190	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073	06/2010	205.00 -	191.97 -	03/2012 -	03/2017	-6.36
191	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	5,298.00 -	11/2019 -	11/2019	24.25
	Total		10,864.00 -	19,894.98 -			
	Grand Total		139,068.37	327,145.08			

Annexure- XIV

List of Delayed Projects w.r.t. Latest Schedule

(August 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,264.12	09/2010 09/2016	10/2017	85	13
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	8,782.00	12/2015 11/2016	11/2018	35	24
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	6,590.00	12/2016 03/2017	12/2019	36	33
	Total		27,271.00 -	29,456.00	20,636.12				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	435.10	01/2011 -	09/2017	80	-
	Total		309.46 -	309.46	435.10				
	<u>COAL</u>								
5	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	229.14	10/2014 -	10/2016	24	-
6	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	122.07	05/2014 -	10/2016	29	-
7	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	86.46	04/2014 -	11/2016	31	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	319.40	03/2010 -	03/2017	84	-
9	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	121.94	03/2011 -	03/2017	72	-
10	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	122.11	12/2012 -	03/2017	51	-
11	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	84.21	03/2014 -	03/2017	36	-
12	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	87.72	03/2015 -	03/2017	24	-
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	167.29	03/2012 -	03/2017	60	-
14	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	96.01	03/2012 -	03/2017	60	-
15	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	152.14	03/2013 -	03/2017	48	-
16	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	72.47	03/2014 -	03/2017	36	-
17	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	03/2017	35	-

(August 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	39.49	06/2015 -	03/2017	21	-
19	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	121.47	03/2012 -	03/2018	72	-
20	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	197.83	03/2014 -	03/2018	48	-
21	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	138.67	03/2016 -	03/2018	24	-
22	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2018	84	-
23	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	147.95	03/2012 -	03/2018	72	-
24	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2018	24	-
25	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.09	03/2015 -	03/2018	36	-
26	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	-
27	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	85.36	03/2015 -	03/2018	36	-
28	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	123.92	03/2016 -	03/2018	24	-
29	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	486.27	92.33	03/2016 -	03/2018	24	-
30	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	207.09	03/2017 -	05/2018	14	-
31	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	244.64	03/2018 -	09/2018	6	-
32	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	278.09	03/2013 -	11/2018	68	-
33	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	182.37	03/2010 -	03/2019	108	-
34	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	208.48	03/2012 -	03/2019	84	-
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	188.94	03/2013 -	03/2019	72	-
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	32.46	07/2016 -	03/2019	32	-
37	MOONDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	54.30	04/2015 -	04/2019	48	-
38	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	459.59	35.44	03/2015 -	03/2020	60	-
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	4.40	03/2014 -	03/2020	72	-
40	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	79.50	07/2012 03/2017	03/2021	104	48
41	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132	-
	Total		13,040.16 -	13,473.89	4,879.35				
	<u>MINES</u>								

(August 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N1000007]HCL, MADHYA PRADESH	09/2011	1,856.00 -	1,176.00	15.48	09/2017 -	04/2020	31	-
	Total		1,856.00 -	1,176.00	15.48				
	<u>STEEL</u>								
43	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	180.35	10/2013 -	09/2016	35	-
44	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	490.16	04/2016 -	10/2016	6	-
45	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	589.13	07/2015 -	11/2016	16	-
46	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	16,513.62	03/2013 -	12/2016	45	-
47	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND	10/2013	245.67 -	245.67	160.88	05/2016 -	03/2017	10	-
48	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH	07/2011	974.76 -	974.76	412.53	07/2016 -	03/2017	8	-
49	TURBO BLOWER - 5 - [N12000092]RINL, ANDHRA PRADESH	12/2009	280.00 -	280.00	72.17	09/2016 -	03/2017	6	-
50	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HCL, TRIPURA	03/2007	149.73 173.00	175.94	178.91	12/2015 -	03/2017	15	-
51	IRRIGATION WORK OF BAGMATI - [N12000108]HCL, BIHAR	10/2005	956.00 -	956.00	650.45	03/2015 -	03/2017	24	-
52	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HCL, TRIPURA	10/2011	175.49 206.71	206.71	141.17	12/2016 -	07/2017	7	-
53	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	344.45	07/2015 -	09/2017	26	-
54	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	104.50	10/2016 -	09/2017	11	-
55	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93 -	188.93	87.53	04/2015 -	12/2016	20	-
	Total		22,756.71 -	22,959.54	19,925.85				
	<u>PETROLEUM</u>								
56	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	16,504.00 -	16,504.00	11,986.69	05/2016 -	09/2016	4	-
57	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL, KARNATAKA	01/2006	993.00 -	1,693.00	1,493.81	01/2012 -	09/2016	56	-
58	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	187.62	03/2014 05/2016	12/2016	33	7
59	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	654.96	04/2015 05/2016	12/2016	20	7

(August 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
60	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]JOCL,JHARKHAND	04/2011	191.96 -	191.96	123.11	05/2015 -	12/2016	19	-
61	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	327.87	11/2016 -	12/2016	1	-
62	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	696.37	03/2015 -	12/2016	21	-
63	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]JOCL,ASSAM	06/2012	150.00 -	150.00	140.02	07/2014 -	01/2017	30	-
64	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	1,970.53	11/2015 11/2016	02/2017	15	3
65	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	517.01	09/2011 10/2016	03/2017	66	5
66	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	69.50	11/2016 -	03/2017	4	-
67	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	89.64	07/2016 -	04/2017	9	-
68	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]JOCL,ODISHA	03/2014	238.50 -	238.50	38.87	03/2017 -	08/2017	5	-
69	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00 -	184.00	28.56	06/2017 -	12/2017	6	-
70	LPG TERMINAL AT KOCHI - [N16000171]JOCL,KERALA	10/2015	607.06 714.25	714.25	108.81	10/2017 -	02/2018	4	-
71	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]JOCL,MULTI STATE	02/2011	913.00 -	913.00	-	08/2015 -	03/2018	31	-
72	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]JOCL,ODISHA	03/2014	3,150.00 -	3,150.00	378.78	09/2017 -	03/2018	6	-
73	PARADIP LPG IMPORT FACILITY - [N16000196]JOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	-
74	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	4,588.29	365.19	05/2018 -	08/2018	3	-
	Total		35,604.28 -	36,246.11	19,177.34				
	POWER								
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	367.82	05/2015 -	08/2016	15	-
76	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 390.51	390.51	266.70	01/2013 03/2016	09/2016	44	6
77	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	3,426.91	10/2014 -	09/2016	23	-
78	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	113.00	12/2015 -	09/2016	9	-

(August 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	576.22	07/2013 11/2015	10/2016	39	11
80	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 2,310.58	2,310.58	1,840.05	05/2014 06/2016	10/2016	29	4
81	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	112.53	09/2014 -	10/2016	25	-
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	524.59	03/2016 -	10/2016	7	-
83	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	34.50	03/2016 -	10/2016	7	-
84	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,645.88	12/2011 03/2016	10/2016	58	7
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	593.76	11/2011 -	11/2016	60	-
86	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 1,428.87	1,428.87	1,082.49	08/2012 09/2016	11/2016	51	2
87	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	2,149.36	09/2014 -	12/2016	27	-
88	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 2,619.56	2,619.56	2,442.83	07/2014 06/2016	12/2016	29	6
89	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	319.67	08/2014 06/2015	12/2016	28	18
90	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 1,875.13	1,875.13	1,613.12	01/2015 06/2016	12/2016	23	6
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	639.72	11/2014 -	12/2016	25	-
92	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	399.80	06/2015 -	12/2016	18	-
93	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,182.53	06/2015 -	12/2016	18	-
94	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	1,088.60	05/2016 -	12/2016	7	-
95	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	276.70	08/2016 -	12/2016	4	-

(August 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
96	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	95.80	07/2016 -	12/2016	5	-
97	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	49.40	02/2016 -	12/2016	10	-
98	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	6,460.99	06/2015 -	02/2017	20	-
99	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	605.39	09/2010 01/2016	03/2017	78	14
100	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,334.48	10/2012 -	03/2017	53	-
101	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,945.15	01/2015 -	03/2017	26	-
102	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	220.89	06/2012 -	03/2017	57	-
103	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	452.92	06/2014 03/2016	03/2017	33	12
104	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,672.23	08/2014 12/2015	03/2017	31	15
105	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	904.84	04/2016 -	03/2017	11	-
106	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	29.70	04/2016 -	03/2017	11	-
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	219.30	06/2016 -	03/2017	9	-
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	465.80	06/2016 -	03/2017	9	-
109	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,368.30	12/2012 12/2016	06/2017	54	6
110	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,308.43	11/2012 03/2016	06/2017	55	15
111	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,415.35	12/2015 -	06/2017	18	-
112	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,760.32	05/2014 03/2017	09/2017	40	6
113	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,529.80	12/2016 -	09/2017	9	-
114	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,908.55	11/2008 01/2016	12/2017	109	23
115	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	77.96	02/2014 -	02/2018	48	-

(August 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60	12,964.60	7,093.73	01/2018	06/2018	5	-
117	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24	1,071.24	0.70	09/2017	07/2018	10	-
118	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59	8,398.75	5,871.70	09/2009	12/2018	111	-
119	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE	05/2016	167.01	167.01	-	11/2018	11/2019	12	-
120	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	2,491.58	866.49	06/2013	12/2019	78	-
121	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]JCVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12	8,112.12	360.55	04/2020	03/2022	23	-
	Total		100,438.07	111,023.34	73,715.55				
	HEAVY INDUSTRY								
122	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00	3,827.30	2,289.00	09/2011	12/2017	75	-
	Total		1,718.00	3,827.30	2,289.00				
	HEALTH AND FAMILY WELFARE								
123	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50	159.50	127.80	11/2013	10/2016	35	-
124	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44	204.44	59.29	05/2017	06/2017	1	-
125	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65	293.65	101.00	05/2017	06/2017	1	-
126	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90	168.90	16.50	05/2017	07/2017	2	-
	Total		826.49	826.49	304.59				
	RAILWAYS								
127	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41	340.00	-	03/2009	10/2016	91	91
128	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16	370.00	358.96	02/2009	12/2016	94	94
129	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90	230.00	54.96	03/2015	12/2016	21	-
130	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL	04/2010	171.02	235.00	228.37	06/2013	12/2016	42	-
131	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]JNR,UTTAR PRADESH	04/2006	325.00	1,581.53	665.09	03/2010	03/2017	84	-
132	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31	7,000.00	6,402.53	03/2009	03/2017	96	-
133	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]JMRT,MAHARASHTRA	04/2012	714.10	714.10	65.20	04/2016	03/2017	11	-

(August 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
134	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	5,000.00	4,245.16	04/2008 12/2011	06/2017	110	66
135	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	950.00	947.78	03/2010 -	06/2017	87	-
136	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	516.40	419.63	03/2010 -	12/2017	93	-
137	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	12/2017	21	-
138	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU	10/2013	187.26 187.26	233.73	35.10	04/2014 -	03/2018	47	-
139	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 3,020.95	3,020.95	2,393.07	07/2005 03/2018	06/2018	155	3
140	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
141	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	-	11/2002 -	12/2018	193	-
142	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.00	649.28	03/2016 -	12/2018	33	-
143	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,010.00	2,323.49	12/2008 -	03/2019	123	-
144	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,319.33	1,319.33	771.67	- 12/2009	03/2019	-	111
145	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 4,454.18	9,658.00	5,472.86	03/2011 -	03/2019	96	-
146	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	829.74	222.82	03/2015 -	03/2019	48	-
147	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	-	03/2018 -	03/2019	12	-
148	GONDIA-JABALPUR(GC), (SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,160.54	1,776.81	1,078.77	03/1998 -	12/2019	261	-
149	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	3,451.00	1,780.37	03/2014 -	03/2020	72	-
150	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 2,393.48	4,600.00	786.14	04/2014 -	03/2020	71	-
151	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	389.32	12/2015 -	03/2020	51	-
152	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	385.60	35.50	03/2013 -	03/2020	84	-
153	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 578.00	578.00	93.09	- 11/2015	03/2020	-	52
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	1,056.84	03/2016 -	12/2020	57	-
155	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	3,000.00	150.74	03/2015 -	03/2021	72	-

(August 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40	1,027.40	483.36	03/2003	03/2021	216	-
157	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04	1,421.25	693.76	03/2012	03/2022	120	-
158	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09	3,845.60	1.92	02/2020	12/2022	34	-
159	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66	5,050.00	-	05/2008	03/2023	178	-
160	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98	1,320.00	753.67	12/2010	03/2018	87	-
161	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97	749.69	-	06/2005	12/2019	174	-
	Total		37,076.74	97,864.10	34,441.10				
	ROAD TRANSPORT AND HIGHWAYS								
162	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00	600.00	312.80	06/2013	08/2016	38	-
163	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50	1,008.50	1,282.25	06/2013	08/2016	38	-
164	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00	664.00	654.59	02/2014	08/2016	30	-
165	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD, MADHYA PRADESH	11/2011	871.15	871.15	393.88	09/2015	08/2016	11	-
166	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00	361.00	434.58	02/2009	09/2016	91	-
167	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00	195.00	294.65	06/2008	09/2016	99	-
168	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94	332.94	518.85	09/2008	09/2016	96	-
169	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72	264.72	322.50	06/2008	09/2016	99	-
170	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16	348.16	418.19	09/2007	09/2016	108	-
171	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00	325.00	-	05/2013	09/2016	40	-
172	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39	805.39	1,407.71	03/2013	09/2016	42	-
173	2-LANNING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36	291.36	368.94	01/2014	09/2016	32	-
174	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51	478.00	284.73	10/2013	09/2016	35	-
175	2-LANNING WITH PS BHLWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10	240.10	165.44	03/2016	09/2016	6	-
176	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16	503.16	268.27	08/2016	09/2016	1	-
177	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD, MADHYA PRADESH	01/2012	320.48	320.48	192.55	08/2015	09/2016	13	-

(August 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
178	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH, BIHAR	10/2014	377.64 -	377.64	-	03/2014 -	09/2016	30	-
179	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	351.34	215.70	01/2016 -	10/2016	9	-
180	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	495.78	346.60	01/2016 -	10/2016	9	-
181	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	11/2016	42	-
182	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI, RAJASTHAN	01/2014	368.15 -	368.15	216.38	01/2016 -	11/2016	10	-
183	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD, ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	-
184	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD, ANDHRA PRADESH	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	24	-
185	FOUR LANING OF ORISSA/CHHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	11/2016	15	-
186	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00 -	230.00	203.60	06/2005 -	12/2016	138	-
187	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	282.52	11/2008 -	12/2016	97	-
188	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	199.25	11/2008 -	12/2016	97	-
189	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	251.26	04/2009 -	12/2016	92	-
190	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	469.41	05/2010 -	12/2016	79	-
191	GUJARAT/MAHARASHTRA BORDERSURAT- HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 2,782.54	1,509.10	3,272.71	09/2012 -	12/2016	51	-
192	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,675.34	08/2011 -	12/2016	64	-
193	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,846.48	11/2011 -	12/2016	61	-
194	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	-	04/2013 -	12/2016	44	-
195	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	902.60	03/2013 -	12/2016	45	-
196	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	1,038.84	07/2013 -	12/2016	41	-
197	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	39	-

(August 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
198	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	12/2016	42	-
199	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2016	28	-
200	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,893.03	03/2013 -	12/2016	45	-
201	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,415.99	07/2013 -	12/2016	41	-
202	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	880.96	02/2013 -	12/2016	46	-
203	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	12/2016	37	-
204	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	976.34	07/2013 -	12/2016	41	-
205	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,851.90	05/2014 -	12/2016	31	-
206	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.85	07/2013 -	12/2016	41	-
207	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,363.70	06/2014 -	12/2016	30	-
208	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	35	-
209	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	875.56	08/2013 -	12/2016	40	-
210	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	621.48	09/2013 -	12/2016	39	-
211	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	-	03/2013 -	12/2016	45	-
212	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,202.40	08/2013 -	12/2016	40	-
213	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,475.09	09/2014 -	12/2016	27	-
214	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2016	32	-
215	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	354.08	06/2014 -	12/2016	30	-
216	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	12/2016	12	-
217	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	12	-
218	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	-
219	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	301.04	67.32	01/2016 -	12/2016	11	-
220	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	350.23	11/2016 -	12/2016	1	-
221	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	-	11/2015 -	12/2016	13	-

(August 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	1,850.96	04/2015 -	01/2017	21	-
223	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	-
224	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,890.00	09/2015 -	02/2017	17	-
225	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	-
226	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	217.29	04/2009 -	03/2017	95	-
227	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 -	212.00	122.77	09/2007 -	03/2017	114	-
228	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	331.23	373.08	07/2009 -	03/2017	92	-
229	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	584.38	08/2012 -	03/2017	55	-
230	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	899.81	03/2014 -	03/2017	36	-
231	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	510.91	04/2014 -	03/2017	35	-
232	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,652.28	06/2014 -	03/2017	33	-
233	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN	10/2013	677.79 -	677.79	883.59	04/2016 -	03/2017	11	-
234	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	119.97	01/2016 -	03/2017	14	-
235	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	731.90	03/2014 -	04/2017	37	-
236	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	195.99	02/2010 -	05/2017	87	-
237	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	-
238	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43 -	580.43	272.37	08/2013 -	05/2017	45	-
239	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	590.00	06/2015 -	05/2017	23	-
240	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
241	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,035.69	05/2013 -	06/2017	49	-
242	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	696.22	01/2014 -	06/2017	41	-
243	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	1,863.25	09/2014 -	06/2017	33	-
244	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	581.84	-	05/2017 -	06/2017	1	-
245	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,682.27	07/2015 -	07/2017	24	-

(August 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
246	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,630.57	02/2014 -	08/2017	42	-
247	REHABILITATION AND UPGRADE OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	-
248	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	1,655.01	978.00	08/2016 -	08/2017	12	-
249	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	368.73	112.62	09/2016 -	09/2017	12	-
250	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,771.99	08/2013 -	10/2017	50	-
251	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	871.15	09/2014 -	10/2017	37	-
252	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	1,287.95	757.57	11/2015 -	10/2017	23	-
253	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
254	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	-
255	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	-
256	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48	-
257	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55	-
258	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	311.51	08/2013 -	12/2017	52	-
259	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	623.47	10/2013 -	12/2017	50	-
260	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	352.00	07/2014 -	12/2017	41	-
261	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
262	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	283.25	181.61	10/2015 -	12/2017	26	-
263	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,135.69	07/2017 -	01/2018	6	-
264	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69	-

(August 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
265	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
266	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
267	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	-
268	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	12/2018	12	-
	Total		81,286.94 -	83,577.25	79,935.83				
	<u>SHIPPING AND PORTS</u>								
269	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	409.83	350.68	04/2009 03/2010	08/2016	88	77
270	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 600.00	600.00	525.49	03/2006 03/2016	12/2016	129	9
	Total		395.67 -	1,009.83	876.17				
	<u>TELECOMMUNICATIONS</u>								
271	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	301.57	09/2014 -	03/2017	30	-
	Total		2,111.17 -	2,011.17	301.57				
	<u>URBAN DEVELOPMENT</u>								
272	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	13,069.22	12/2015 -	08/2016	8	-
273	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	208.53	05/2013 10/2015	10/2016	41	12
274	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 315.00	315.00	214.40	06/2015 08/2016	11/2016	17	3
275	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	24,669.11	03/2016 -	12/2016	9	-
276	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 13,845.01	14,405.01	14,081.31	06/2011 12/2013	01/2017	67	37
277	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	124.48	12/2014 12/2016	03/2017	27	3
278	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 142.37	191.97	133.13	03/2012 08/2016	03/2017	60	7

(August 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
279	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 405.01	405.01	249.90	12/2014 -	03/2017	27	-
280	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	60.59	09/2015 07/2016	04/2017	19	9
281	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	24.52	03/2016 -	09/2017	18	-
282	CONSTRUCTION OF CIVIL STRUCTURES AN OTHER INFRASTRUCURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	19.54	11/2015 -	11/2017	24	-
283	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	901.75	02/2019 -	03/2020	13	-
	Total		87,843.30 -	95,840.28	53,756.48				
	Grand Total		412,533.99	499,600.76	310,689.53				

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2019	12320	36
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2018	11459	35
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492	85

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
6	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2019	417.33	32
7	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
8	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
9	RCE OF INDARAM OCP (1.20 MTPA)	SCCL	07/2011	03/2015	03/2018	162.76	36
10	BAROUD OC EXPANSION (RCE) - 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
11	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2017	339.88	35
12	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
13	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2018	510.85	24
14	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	11/2018	457.77	68
15	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
16	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	05/2018	490.1	14
17	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2019	207.28	84
18	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72
19	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2017	209.78	24
20	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2018	264.68	72
22	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
23	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
24	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2017	153.82	36
25	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
26	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
27	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
28	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2018	198.59	24
29	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2017	181.19	60
30	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
31	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
32	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
33	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
34	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
35	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2018	163.51	84
36	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
37	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
38	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	08/2019	1458.17	50
39	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	09/2018	1055.05	6
40	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	10/2016	364.75	24
41	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
42	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
44	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
45	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	09/2017	197.79	10

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	AIIMS-RAEBARELI-HOUSING	HSCC	10/2013	11/2013	10/2016	159.5	35

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718	75

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	HCL	09/2011	09/2017	04/2020	1856	31

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
49	PALAKKAD LPG PLANT	BPCL	02/2015	06/2017	12/2017	184	6
50	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	01/2017	150	30
51	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	12/2016	871.35	21
52	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	HPCL	11/2011	03/2013	01/2017	310	46
53	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	29
54	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	03/2018	913	31
55	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	03/2018	3150	6
56	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	02/2017	3110.36	15
57	RESITEMENT OF TATA NAGAR AND RACHI	IOCL	04/2011	05/2015	12/2016	191.96	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DEPOTS TO KHUNTI (JHARKHAND)						
58	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	09/2016	317.64	48
59	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
60	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2016	861.79	43
61	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	10/2016	463.32	64
62	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
63	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	03/2017	2592.17	34
64	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
65	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	04/2017	202.25	9
66	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	12/2016	1138.5	20
67	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	03/2017	736.65	66
68	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	08/2016	270	50
69	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	06/2018	352.56	15
70	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	09/2016	993	56
71	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
72	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
73	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	03/2018	3076	6
74	REPLACEMENT OF COKE CHAMBERS	IOCL	04/2013	02/2016	10/2016	480	8
75	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	03/2018	600.17	39
76	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	12/2016	352.49	33
77	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
78	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	IOCL	08/2011	08/2015	12/2016	586	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	EASTERN REGION STRENGTHENING SCHEME XIV	PGCIL	05/2016	11/2018	11/2019	167.01	12
80	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	12/2016	1909.24	18
81	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2016	723.63	25
83	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	05/2017	573.99	45
84	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2016	297.33	28
85	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2017	1746.65	31
86	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2017	1779.29	109
87	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
88	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	12/2016	1422.85	23
89	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	09/2017	368.72	134
90	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	10/2016	198.63	25
91	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	02/2017	9569.76	20
92	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
93	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
94	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	10/2016	2313	58
95	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
96	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2017	2496.9	94
97	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND- BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	12/2016	1940.13	27
98	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43
99	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2017	487.49	33
100	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPFS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	12/2016	2127.51	29
101	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	12/2016	196.58	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	03/2022	8112.12	23
103	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	02/2020	14366.58	12
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	10/2016	752.64	39
105	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	09/2016	250.03	44
106	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	06/2017	1272.8	55
107	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	07/2018	1071.24	10
108	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	03/2017	232.34	57
109	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48
110	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
111	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2017	477.69	78
112	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2017	4824.12	53
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	11/2016	509.66	60
114	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2017	4404.57	26
115	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
116	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	11/2016	1216.83	51
117	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2017	2144	54
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV	PGCIL	09/2013	03/2016	10/2016	680.69	7
119	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II	PGCIL	09/2013	05/2016	12/2016	1575.3	7
120	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	03/2017	1364.52	11
121	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	03/2017	374.63	11
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	03/2017	539.82	9
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	03/2017	908.08	9
124	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS	PGCIL	02/2014	12/2015	09/2016	167.4	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
125	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	10/2016	155.57	7
126	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	10/2016	1961.87	29
127	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	75
128	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2017	4375.35	69
129	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	09/2016	3201.44	23
130	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	07/2017	15166.19	6
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	08/2016	524.4	15
132	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2017	2514.88	18
133	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2016	514.2	18

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
134	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
135	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	21
136	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
137	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	07/2005	06/2018	2957.21	155
138	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
139	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	91
140	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87
141	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
142	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
143	NANDYAL-YERRAGUNTALA (NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	106
144	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
145	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
146	UDHNA-JALGAON WITH	WR	04/2008	03/2014	12/2017	1389.62	45

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	ELECTRIFICATION (DOUBLING) (WR)						
147	BHUJ-NALIYA (GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
148	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
149	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2019	829.74	48
150	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
151	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
152	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
153	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	03/2022	603.04	120
154	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2021	850	72
155	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
156	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2017	1676.31	96
157	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
158	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
159	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
160	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
161	RAJATGARH-BARANG (LD), ECOR	RVNL	04/1999	02/2009	12/2016	166.16	94
162	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
163	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	221
164	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	99
165	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
166	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
167	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733	123
168	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
169	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
170	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
171	TAMLUK-BASULYA-SUTAHATA DOUBLING	RVNL	04/2010	06/2013	12/2016	171.02	42
172	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
173	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2021	1027.4	216
174	OMALUR-METTURDAM- DOUBLING WITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2018	187.26	47

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
175	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	MORTH	10/2014	03/2014	09/2016	377.64	30
176	2-LANING WITH PS SITARGANJ BAREILLY SECTION	NHAI	06/2014	01/2016	12/2016	301.04	11
177	ETAWAH CHAKERI	NHAI	03/2013	09/2015	02/2017	1573	17
178	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	12/2016	2125.24	12
179	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	01/2017	1928.22	21
180	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	01/2018	972.5	6
181	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	08/2017	1655.01	12
182	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	12/2016	1055	13
183	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2016	230	138
184	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	09/2016	280	91
185	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2017	199.81	95
186	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50
187	SAMAIKHIALI - GANDHIDHAM	NHAI	09/2010	03/2013	09/2016	805.39	42
188	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
189	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	12/2016	1535	31

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
190	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	03/2017	574	36
191	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
192	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	12/2016	500.29	40
193	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2017	1410	33
194	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
195	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24
196	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	PWD	01/2014	11/2014	11/2016	195.45	24
197	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	PWD	02/2014	11/2014	11/2016	170.21	24
198	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
199	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	PWD	03/2015	09/2015	08/2017	309.01	23
200	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
201	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
202	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
203	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
204	SATANA-BELA SECTION OF NH-75(4L) IN MP	PWD	01/2012	08/2015	09/2016	320.48	13
205	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	08/2016	871.15	11
206	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
207	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	12/2016	2498.76	28
208	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	07/2017	1987	24
209	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	12/2016	1813.76	41
210	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2016	671.3	46
211	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	11/2016	351.54	42
212	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
213	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2017	485	52
214	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2017	536	41
215	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	08/2016	664	30
216	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2016	575	41
217	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2016	1100.7	30
218	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
219	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	12/2016	624	32
220	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	05/2017	1479	23
221	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	12/2016	486	79
222	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	12/2016	1108	61
223	DEOLI-KOTA	NHAI	01/2011	07/2013	12/2016	593	41
224	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	10/2017	828	37
225	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	10/2017	1287.95	23
226	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2017	1348.2	42
227	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2017	617	55
228	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
229	MURADABAD-BAREILY	NHAI	04/2010	06/2013	12/2016	1267	42
230	PUNE-SATARA (NH-4)	NHAI	10/2010	03/2013	12/2016	1724.55	45
231	INDORE-DEWAS (NH-3)	NHAI	11/2010	05/2013	09/2016	325	40
232	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM	NHAI	09/2010	03/2013	12/2016	852	45
233	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM	NHAI	11/2010	05/2013	06/2017	1585	49
234	4-LANING OF ROHATAK JIND (LENGTH 45 KM)	NHAI	10/2013	10/2015	12/2017	283.25	26
235	GUJARAT/MAHARASHTRA BORDERSURAT- HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2016	1509.1	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
236	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	12/2016	1175	44
237	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	07/2012	05/2017	940	58
238	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	12/2016	1693.75	64
239	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA	NHAI	10/2013	04/2016	03/2017	677.79	11
240	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	08/2016	1008.5	38
241	ROHTAK-BAWAL	NHAI	05/2011	11/2013	12/2016	650	37
242	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2017	1250	48
243	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	12/2016	953.88	41
244	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2016	754	45
245	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2016	1078.84	40
246	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	10/2017	998.79	50
247	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
248	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2017	1047	33
249	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2016	1396.18	27
250	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2016	291.36	32
251	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	12/2017	356.4	41
252	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	12/2016	167.64	97
253	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	12/2016	155.04	97
254	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	12/2016	200	92
255	AGRA-BYPASS(NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	09/2016	348.16	108
256	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	NHAI	12/2003	05/2008	12/2016	160	103
257	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	09/2008	09/2016	332.94	96
258	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	03/2017	212	114

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
259	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2017	196	92
260	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	08/2016	600	38
261	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2017	375.09	35
262	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	09/2016	478.51	35
263	PANVEL-INDAPUR	NHAI	12/2011	06/2014	12/2016	942.69	30
264	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	03/2017	523.85	14
265	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	10/2016	351.34	9
266	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH- 125	NHAI	09/2015	09/2016	09/2017	368.73	12
267	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	10/2016	495.78	9
268	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	PWD	07/2015	12/2015	12/2016	333.21	12
269	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	12/2016	333.21	12
270	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	09/2016	264.72	99
271	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	10/2016	245	103
272	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	09/2016	217.61	77
273	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2016	208	104
274	BIJNI TO ASSAM WB BORDER (NH- 31.C) (1) (NHAI)	NHAI	12/2003	06/2008	09/2016	195	99
275	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
276	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION	NHAI	01/2014	01/2016	11/2016	368.15	10
277	2-LANING WITH PS BHILWARA-LODPURA SECTION	NHAI	03/2014	03/2016	09/2016	240.1	6
278	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
279	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	11/2016	1232	15
280	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
281	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
282	FOUR LANING OF CHADIGARH - KHARAR	NHAI	10/2015	12/2017	12/2018	447.29	12

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
283	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	88
284	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2016	150	129
285	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
286	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	09/2016	187.33	35
287	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	03/2017	245.67	10
288	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	07/2017	175.49	7
289	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2017	956	24
290	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	12/2016	17265	45
291	UPGRADATION OF BLAST FURNACE-1 AT RSP	SAIL	06/2014	04/2016	10/2016	708.91	6
292	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	SAIL	04/2014	04/2015	12/2016	188.93	20
293	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2017	15525	31
294	TURBO BLOWER - 5	RINL	12/2009	09/2016	03/2017	280	6
295	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	09/2017	343	11
296	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	09/2017	404.16	26
297	3RD CONVERTER AND 4TH CASTER	RINL	07/2011	07/2016	03/2017	974.76	8
298	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	11/2016	877.73	16
299	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	03/2017	149.73	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AS On 31-AUG-16)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
300	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	ITI	09/2014	09/2014	03/2017	2111.17	30

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
301	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AT IISER CAMUS	CPWD	07/2015	11/2015	11/2017	154	24
302	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
303	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	03/2017	350.02	24
304	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2017	216.69	31
305	BANGALORE METRO RAIL PROJECT	MRTD	05/2006	06/2011	01/2017	6395	67
306	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
307	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	03/2017	188.87	27
308	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	04/2017	156.57	19
309	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	05/2017	270.83	30
310	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2017	171.86	18
311	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	10/2016	261.85	41
312	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	03/2017	205	60
313	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	CPWD	12/2012	06/2015	11/2016	315	17
314	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	04/2017	165.23	54
315	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	03/2017	405.01	27
316	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.59	307.16
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
9	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
12	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
16	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210
17	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
19	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
20	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	1216.83	1428.87	212.04
21	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
22	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	17435.15	11149.82
23	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
25	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9606.82	5484.82
26	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
27	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
28	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	250.03	390.51	140.48
29	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
30	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
31	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	1961.87	2310.58	348.71
32	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.57	586.56
33	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1441.52	1072.8
34	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	1422.85	1875.13	452.28
35	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
37	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5783.17	2141.13
38	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1581.04	1007.05
40	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	2127.51	2619.56	492.05
41	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
42	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
43	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
44	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
45	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
46	KARUR-SALEM (NL) ,SR	SR	02/1997	N.A.	155.55	870	714.45
47	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02
48	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	1542.41	1299.99
49	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
50	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
51	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
52	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	376	239.38
53	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	340	206.59
54	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
55	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
56	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
57	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
58	RAMGANJMUNDI-BHOPAL (NL) ,WCR	WCR	04/2001	N.A.	470.92	3000	2529.08
59	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	03/2008	743	1825	1082
60	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
63	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
64	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
65	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
66	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
67	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
68	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
69	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
70	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	2966.99	1920.11
71	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
72	GUDUR-DURGARAJPATNAM	SCR	04/2011	N.A.	283.54	759.41	475.87
73	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
74	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
75	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
76	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
77	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
79	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	5050	4802.34
80	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5000	3500
81	MANDARHILL-DUMKA-RAMPURHAT (NL) , ER	ER	04/1995	12/2011	900.05	1125.89	225.84
82	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	KODERMA GIRIDH (NL), ECR	ECR	04/1996	N.A.	768.87	926	157.13
84	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
85	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
86	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	12/2024	750.55	943.6	193.05
87	RUPSA BANGRIPOSTI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
88	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
89	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	N.A.	4300	4520	220
90	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
91	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
92	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
93	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	2103	1187.02
94	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
95	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
96	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	386.68	140.61
97	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	508	195.88
98	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
99	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
100	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
101	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
102	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
103	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
104	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
105	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
107	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	445	235.23
108	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	967.85	715.85
109	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1857	962
110	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
111	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1480.83	658.44
112	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
113	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
114	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
115	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
116	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
117	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
118	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
119	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
120	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
121	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
122	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
123	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
124	DIGHA-JALESWAR INCLUDING MM FOR DIGHA- EGRA	SER	04/2010	N.A.	553.63	1009	455.37
125	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
126	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
127	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
128	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR	NWR	04/2013	N.A.	456	860	404

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
130	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
131	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	1037.15	591.15
132	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	845.68	405.8
133	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79
134	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
135	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
136	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
137	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	516.23	735	218.77
138	DAUSA-GANGAPUR CITY (NL) ,NWR	NWR	02/1997	N.A.	410.08	780.98	370.9
139	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
140	KANPUR KASGANJ MATHURA (GC) NER	NER	03/1997	N.A.	677.97	1679.13	1001.16
141	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
142	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
143	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	7000	5323.69
144	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
145	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
146	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
147	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	355.96	165.86
148	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
149	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
150	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
151	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA (NL) , SWR	SWR	02/1997	N.A.	295	1289.92	994.92

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	N.A.	836.26	1072.52	236.26
153	HUBLI-ANKOLA (NL) , SWR	SWR	04/1997	N.A.	227	2135	1908
154	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
155	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
156	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
157	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
158	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
159	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
160	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
161	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	525	306.76
162	NANDYAL-YERRAGUNTLA (NL) , SCR	SCR	03/1996	02/2009	155.74	966.98	811.24
163	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	516.4	191.5
164	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	370	203.84
165	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
166	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
167	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	876.1	250.8
168	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	19565	17065
169	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
170	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) , NEFR	NFR	09/2006	N.A.	300	2145	1845
171	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) , NEFR	NFR	09/2006	N.A.	200	780	580
172	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	436	266
173	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44
174	KHURDA ROAD-BOLANGIR (NL) ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	3010	2277
176	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
177	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
178	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	554.7	241.46
179	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1170	709.06
180	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
181	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
182	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52
183	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
184	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
185	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
186	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	280	183.84
187	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	365	266.26
188	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
189	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
190	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2491.43	1992.13
191	KATAKHAL TO BHAIKABI	NFR	04/1998	12/2012	227.9	509	281.1
192	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
193	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18
194	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
195	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	270	177.37
196	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42
197	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	1500	892.91

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	JIND-SONEPAT (NL), NR	NR	01/2004	03/2012	238.56	740	501.44
199	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
200	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
201	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
202	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
203	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
204	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
205	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
206	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
207	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
208	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
209	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
210	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1070.97	302.09
211	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
212	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	14405.01	8010.01
213	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	11/2014	241.33	349.33	108
214	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	5298	1034

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AS ON 31-AUG-16

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(AS On 31-AUG-16)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492.00	5677.00	2185	85

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60
3	JAGANNATHPOR OCP (3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.59	307.16	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	12/2016	871.35	1200.00	328.65	21
6	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	462.79	152.98	29
7	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36
8	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2016	861.79	1256.72	394.93	43
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	09/2016	993.00	1693.00	700	56
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
11	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	09/2017	368.72	1441.52	1072.8	134
12	BARH STPP (3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2017	1746.65	2228.71	482.06	31
14	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	12/2016	2127.51	2619.56	492.05	29
15	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
16	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	10/2016	1961.87	2310.58	348.71	29
17	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	3846.30	867.82	75
18	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2017	4375.35	6749.18	2373.83	69
19	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	09/2016	250.03	390.51	140.48	44
20	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	06/2017	1272.80	1731.10	458.3	55
21	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	10/2016	2313.00	4237.67	1924.67	58
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2017	2496.90	6179.96	3683.06	94
23	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2017	487.49	639.46	151.97	33
24	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	05/2017	573.99	1581.04	1007.05	45
25	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	4479.16	111
26	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2017	477.69	738.48	260.79	78
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
28	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	11/2016	1216.83	1428.87	212.04	51
29	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2017	2144.00	2932.88	788.88	54
30	KUNADANKULAM APP TRANS SYSTEM	PGCIL	05/2005	11/2008	12/2017	1779.29	2187.32	408.03	109

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	(PGCIL)								
31	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	12/2016	1422.85	1875.13	452.28	23

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
32	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
33	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
34	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
35	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.90	516.40	191.5	93
36	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1581.53	1256.53	84
37	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
38	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1320.00	827.02	87
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	340.00	206.59	91
40	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
41	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
42	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	03/2022	603.04	1421.25	818.21	120
43	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	554.70	241.46	221
44	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
45	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	5000.00	3500	110
46	LALITPUR-SATNA-REWA-SINGRULI	WCR	09/1998	05/2008	03/2023	247.66	5050.00	4802.34	178

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	NL, (NCR)								
47	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	03/2019	733.00	3010.00	2277	123
48	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	9658.00	8930.44	96
49	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2021	850.00	3000.00	2150	72
50	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
51	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2017	1676.31	7000.00	5323.69	96
52	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
53	UDHAMPUR-SRINAGAR-BARAMULLA (NL) ,NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
54	RAJATGARH-BARANG (LD) ,ECOR	RVNL	04/1999	02/2009	12/2016	166.16	370.00	203.84	94
55	NANDYAL-YERRAGUNTALA (NL) ,SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	811.24	106
56	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	749.69	455.72	174
57	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
58	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2017	196.00	331.23	135.23	92
59	FOUR LANING OF GWALIOR- SHIVPURI	NHAI	05/2013	11/2015	12/2016	1055.00	1601.77	546.77	13
60	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	12/2016	1108.00	2288.00	1180	61
61	MAIBANG TO LUMDING (AS-24) , KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	12/2016	155.04	280.13	125.09	97
62	MAIBANG TO LUMDING (AS-25) ,	NHAI	12/2003	04/2009	03/2017	199.81	385.13	185.32	95

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(AS On 31-AUG-16)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	KM.83.400 TO KM.111.000								

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
63	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	409.83	164.16	88
64	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2016	150.00	600.00	450	129
65	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMBAI	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
66	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	09/2017	343.00	488.40	145.4	11

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
67	BANGALORE METRO RAIL PROJECT	MRTD	05/2006	06/2011	01/2017	6395.00	1,4405.01	8010.01	67

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure- XVIII

Details of Ongoing Projects Under -Public Private Partnership Mode

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
1	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT PPP (ANNUITY) - [N10000009]	12/2015	344.50 -	344.50	11/2016 -	11/2016	0.00	0
	Total		344.50 -	344.50				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
2	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - PPP (BOT) - [N24000231]	10/2013	283.25 -	283.25	10/2015 -	12/2017	0.00	26
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	09/2016	0.00	32
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	09/2016	0.00	40
5	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	11/2016	0.00	42
6	CHENNAI-TADA(SIX LANE) - PPP (BOT) - [N24000129]	04/2009	353.37 -	353.37	10/2011 -	-	0.00	0
7	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - PPP (BOT) - [N24000211]	07/2012	356.40 -	356.40	07/2014 -	12/2017	0.00	41
8	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - PPP (BOT) - [N24000153]	03/2011	359.00 -	359.00	09/2013 -	12/2016	0.00	39
9	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2017	0.00	55
10	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2017	0.00	52
11	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	12/2016	0.00	79
12	BHUBANESWAR TO PURI - PPP (BOT) - [N24000195]	03/2011	500.29 -	500.29	08/2013 -	12/2016	0.00	40
13	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	07/2016	0.00	32
14	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	0.00	0
15	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	08/2016	0.00	0

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
16	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00	536.00	01/2014	06/2017	0.00	41
17	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00	567.00	11/2013	-	0.00	0
18	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00	571.00	10/2013	12/2017	0.00	50
19	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00	574.00	03/2014	03/2017	0.00	36
20	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00	575.00	07/2013	12/2016	0.00	41
21	4-LANING OF RAIGANJ-DALKOLA - PPP (BOT) - [N24000204]	02/2011	580.43	580.43	08/2013	05/2017	0.00	45
22	NIROLI-ROXY-RAJAMUNDA - PPP (BOT) - [N24000194]	07/2011	586.00	586.00	01/2014	12/2016	0.00	35
23	DEOLI-KOTA - PPP (BOT) - [N24000148]	01/2011	593.00	593.00	07/2013	12/2016	0.00	41
24	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00	604.00	12/2009	-	0.00	0
25	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00	617.00	08/2012	03/2017	0.00	55
26	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	12/2016	0.00	32
27	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18	637.18	06/2019	06/2019	0.00	0
28	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00	650.00	11/2013	12/2016	0.00	37
29	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00	664.00	02/2014	08/2016	0.00	30
30	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	12/2016	0.00	46
31	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - PPP (BOT) - [N24000236]	10/2013	677.79	677.79	04/2016	03/2017	0.00	11
32	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16	702.16	07/2014	02/2017	0.00	31
33	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - PPP (BOT) - [N24000588]	06/2016	725.95	725.95	06/2019	06/2019	0.00	0
34	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	12/2016	0.00	45
35	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	06/2019	0.00	0
36	SAMAIKHALI - GANDHIDHAM - PPP (BOT) - [N24000179]	09/2010	805.39	805.39	03/2013	09/2016	0.00	42
37	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	04/2018	0.00	0

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - PPP (BOT) - [N24000225]	03/2012	828.00 -	828.00	09/2014 -	10/2017	0.00	37
39	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36 -	830.36	07/2018 -	07/2018	0.00	0
40	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - PPP (BOT) - [N24000144]	09/2010	852.00 -	852.00	03/2013 -	12/2016	0.00	45
41	BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229]	08/2012	867.00 -	867.00	02/2015 -	12/2017	0.00	34
42	4 LANING OF OBEDULLAGANJ-BETUL SECTION - PPP (BOT) - [N24000457]	02/2012	912.00 -	912.00	08/2016 -	08/2016	0.00	0
43	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	12/2016	0.00	1
44	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - PPP (BOT) - [N24000123]	03/2005	940.00 -	940.00	07/2012 -	05/2017	0.00	58
45	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	12/2016	0.00	41
46	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	01/2018	0.00	6
47	4-LANING OF BRAHAMPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	10/2017	0.00	50
48	4 LANNING OF AHMEDABAD TO GODHARA - PPP (BOT) - [N24000167]	12/2010	1,008.50 -	1,008.50	06/2013 -	08/2016	0.00	38
49	BAREILY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	12/2016	0.00	39
50	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2017	0.00	33
51	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2016	51.83	13
52	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	12/2016	0.00	40
53	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	12/2016	0.00	30
54	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2016	106.50	61
55	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	07/2016	0.00	35
56	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	12/2016	2.65	44
57	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2017	0.00	48
58	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,266.60	09/2016 -	09/2016	0.00	0

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	MURADABAD-BAREILY - PPP (BOT) - [N24000154]	04/2010	1,267.00	1,267.00	06/2013	12/2016	0.00	42
60	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - PPP (BOT) - [N24000228]	06/2013	1,287.95	1,287.95	11/2015	10/2017	0.00	23
61	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	08/2017	0.00	42
62	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	01/1991	1,388.00	1,388.00	-	08/2018	0.00	0
63	FOUR LANING OF KATHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00	1,393.00	-	01/2018	0.00	0
64	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	12/2016	0.00	27
65	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	06/2017	0.00	33
66	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	05/2017	0.00	23
67	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	12/2016	0.00	51
68	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	12/2016	0.00	31
69	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	02/2017	0.00	17
70	FOUR LANING OF BIAORA-DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	-	-	0.00	0
71	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00	1,585.00	05/2013	06/2017	0.00	49
72	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - PPP (BOT) - [N24000139]	09/2010	1,655.00	1,655.00	09/2013	-	0.00	0
73	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	08/2017	0.00	12
74	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	-	01/2019	0.00	0
75	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	09/2016	0.00	0
76	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	07/2016	0.00	57
77	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	12/2016	0.00	64
78	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	12/2016	0.00	45
79	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	12/2016	0.00	41
80	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	01/2018	0.00	0

(August 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
81	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	11/2016	0.00	0
82	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	01/2017	0.00	21
83	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	07/2017	0.00	24
84	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	12/2016	0.00	12
85	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	-	-	0.00	0
86	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,159.00	06/2015	07/2016	0.00	13
87	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	-	-	0.00	0
88	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	12/2016	0.00	28
89	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00	2,848.00	03/2014	04/2017	0.00	37
	Total		95,422.80	97,180.67				
	SHIPPING AND PORTS							
90	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94	235.15	06/2017	06/2017	18.20	0
91	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50	258.33	12/2017	12/2017	5.66	0
92	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39	669.46	12/2010	12/2018	82.72	96
	Total		809.83	1,162.94				
	Grand Total		96,577.13	98,688.11				
