

382nd
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
August 2017



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for August 2017 contains information on the status of the 1272 Central Sector Infrastructure Projects costing ₹ 150 crore and above.

2. The implementation status of **Central Sector Projects (costing Rs 150 crore and above)** may be summarized as below:-

(i). During the reference month, 47 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 47 projects, 18 are **Mega** Projects costing ₹ 1000 crore and above.

(ii). Total original cost of implementation of the 1272 projects was Rs. 15,89,750.53 crore and their anticipated completion cost is likely to be Rs. 17,71,039.29 crore, which reflects overall cost overruns of Rs. 1,81,288.76 crore (11.40% of original cost). The expenditure incurred on these projects till August 2017 is Rs. 6,89,034.34 crore, which is 38.91% of the anticipated cost of the projects.

(iii). Out of a total of 1272 projects, 1 project has reported completion and 12 new projects have been initiated on the monitor of this ministry during the current month. Of these, 12 projects are ahead of schedule, 308 are on schedule, 296 are delayed, 341 projects are showing cost overrun and 96 projects are showing both time and cost overrun with respect to original implementation schedules. However, the number of delayed projects decreases to 239 if delay is calculated with reference to latest revised schedules of completion. For 656 projects, where original/anticipated commissioning date has not been reported, all concerned have been requested to provide the original/anticipated commissioning date so that these projects can be monitored for completion vis-a-vis the targeted dates.

(iv). Out of 296 delayed projects, 51 projects have overall delay in the range of 1 to 12 months, 61 projects have delay in the range of 13 to 24 months, 113 projects have delay in the range of 25 to 60 months and 71 projects have delay of 61 months and above.

(v). Further, out of the 296 delayed projects, 96 projects have cost overruns. Out of these, the cost for 46 projects has been revised and for 50 projects the cost has not yet been revised. Of the 46 projects where cost has been revised, the anticipated cost of 5 projects has again exceeded the revised cost. Out of 295 delayed projects, 153 projects have not provided any milestones and in 90 cases the dates of completion of the milestones have already lapsed.

(vi). In addition to above there are 245 projects which though on schedule but are having cost overruns. Of these, the cost for 56 projects has since been revised. Of the 56 projects where cost has been revised, the anticipated cost of 23 projects has exceeded even the revised costs. Out of these 245 projects, 175 projects have not provided any milestones and for 6 projects the completion date of milestone(s) has already lapsed.

(vii). In the current month, there are 286 projects showing time overrun of more than 6 months; 244 projects showing cost overruns of more than Rs.100 crore and 78 projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore. Further, expenditure has exceeded the approved cost in 143 projects and in 919 projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimates.

3. The implementation status of **Central Sector Mega Projects** (costing Rs.1000 crore and above) may be summaries as below:-

(i) During the reference month out of 1272 projects 379 are mega projects. Total original cost of implementation of these 379 projects was Rs. 12,27,815.53 crore and their anticipated completion cost is likely to be Rs. 13,79,421.88 crore, which reflects overall cost overruns of Rs. 1,51,606.35 crore (12.35% of original cost). The expenditure incurred on these projects till August 2017 is Rs. 5,85,008.37 crore, which is 42.41% of the anticipated cost of the projects. Out of the 379 mega projects, 134 projects have cost overruns with respect to original cost and the number of such projects decreases to 107 when cost overrun is calculated on the basis of revised cost.

(ii) Further, out of the 124 delayed mega projects, 52 projects have cost overruns. Out of these, the cost for 21 projects has been revised and for 31 projects the cost has not yet been revised. Of the 21 projects where cost has been revised, the anticipated cost of 2 projects has again exceeded the revised cost. Out of 124 delayed projects, 65 projects have not provided any milestones and in 39 cases the dates of completion of the milestones have already lapsed.

(iii) In addition to above there are 82 mega projects which though are on schedule but are having cost overruns. Of these, the cost for 18 projects has since been revised. Of the 18 projects where cost has been revised, the anticipated cost of 9 projects has exceeded even the revised costs. Out of these 82 projects, 54 projects have not provided any milestones and for 2 projects the completion date of milestone(s) has already lapsed.

(iv). In the current month, there are 121 mega projects showing time overruns of more than 6 months; 127 mega projects showing cost overruns of more than Rs.100 crore and 51 mega projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore.

Further, expenditure has exceeded the approved cost in 71 mega projects and in 261 mega projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimate.

4. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

5. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones.

6. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported.

7. Ministry of Railways have provided the latest information of all its ongoing projects costing ₹500 crore and above on the OCMS of this Ministry. The recent and latest updated information in respect of projects costing below ₹500 crore is reported as and when received.

8. The status as on 31.08.2017 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report available at [www.cspm.gov.in /publication](http://www.cspm.gov.in/publication).

9. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	482	14
2	RAILWAYS	353	1
3	POWER	127	14
4	PETROLEUM	108	3
5	COAL	92	3
6	URBAN DEVELOPMENT	36	7
7	STEEL	34	3
8	HEALTH AND FAMILY WELFARE	13	2
9	SHIPPING AND PORTS	8	0
10	ATOMIC ENERGY	4	0
11	MINES	4	0
12	CIVIL AVIATION	3	0
13	TELECOMMUNICATIONS	3	0
14	FERTILISERS	2	0
15	DEFENCE PRODUCTION	2	0
16	HEAVY INDUSTRY	1	0
	Total	1272	47

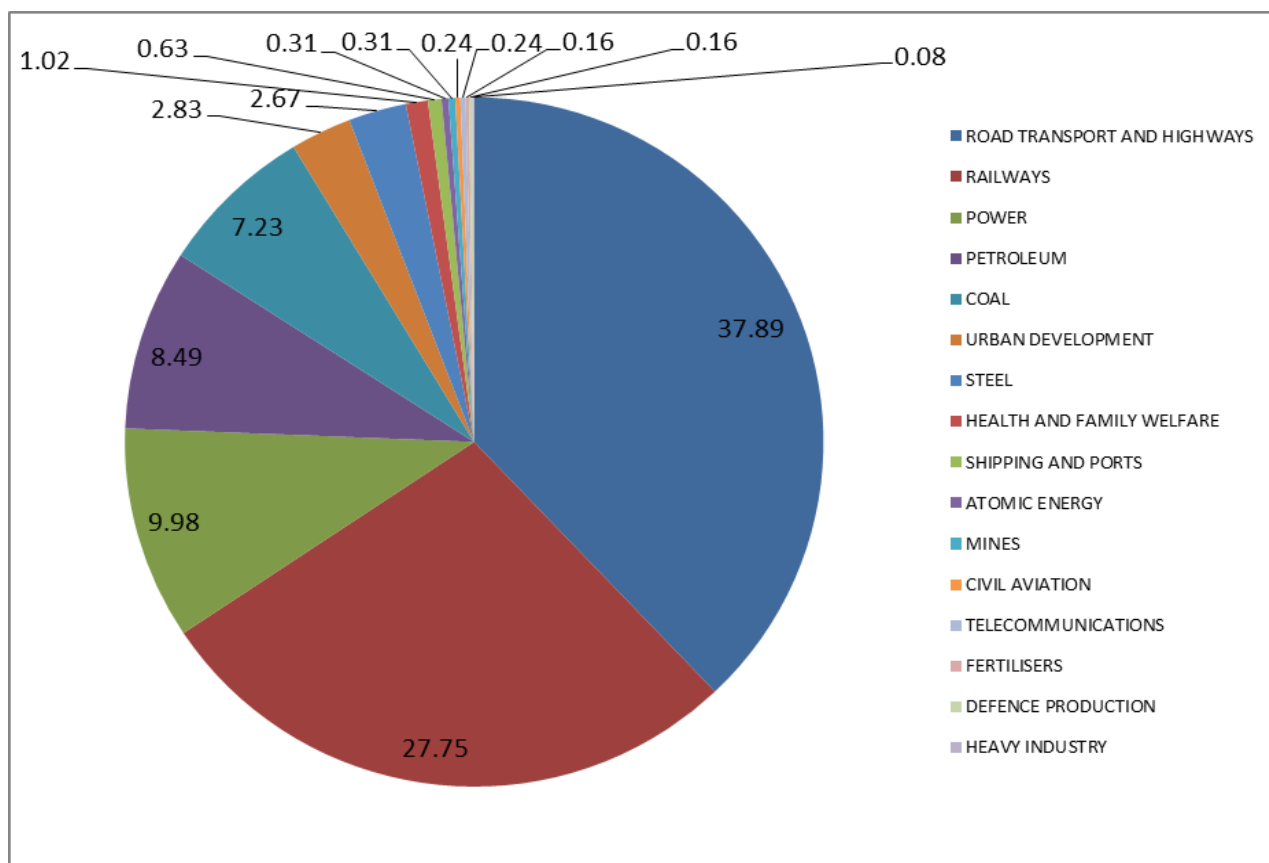


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2017			
	<u>PETROCHEMICALS</u>			
1	ASSAM GAS CRACKER PROJECT G(BRAHMAPUTRA CRECKER & POLYMER LTD.) - [N16000106]	5,460.61	04/2012	9,895.05
	<u>POWER</u>			
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000053]	509.66	11/2011	566.26
3	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000081]	1,216.83	08/2012	1,074.89
4	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000101]	1,961.87	05/2014	1,817.05
5	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000117]	1,422.85	01/2015	1,490.42
6	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000145]	1,909.24	06/2015	1,093.03
7	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000163]	303.07	07/2016	48.50
8	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000173]	972.42	11/2017	92.20
	May,2017			
	<u>CIVIL AVIATION</u>			
9	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS G(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000071]	217.60	03/2015	196.94
	June,2017			
	<u>STEEL</u>			
10	SMS-1 CONVERTERS REVAMPING G(RASTRIYA ISPAT NIGAM LIMITED) - [N12000090]	404.16	07/2015	394.74
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000166]	378.71	10/2016	257.90
12	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000167]	400.47	04/2017	265.20
13	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000211]	187.04	06/2018	54.60
	July,2017			
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000094]	752.64	07/2013	633.62
15	WARDHA-HYDERABAD 765 KV LINK G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000183]	3,662.02	05/2018	2,302.40
	August,2017			
16	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000153]	1,575.30	05/2016	1,328.51

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2017			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000123]	940.00	07/2012	1,415.36
2	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000153]	359.00	09/2013	2.74
3	BHUBANESWAR TO PURI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000195]	500.29	08/2013	869.91
4	4-LANING OF RAIGANJ-DALKOLA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000204]	580.43	08/2013	226.67
5	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000225]	828.00	09/2014	870.15
6	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH- 200 FROM KM 301.89 TO KM 427.85 INCLUDING KM(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000366]	996.37	12/2017	0.00
7	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000588]	725.95	06/2019	0.00


Summary of projects in the Flash Report for the month of August, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1257
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects elevated to the status of Major project during the current month	4
Number of Projects Added in Current Month	12
Number of Projects in Current Month	1272

Brief Analysis

Project Status with respect to Original Schedule: Out of 1272 projects, 12 projects are ahead of schedule, 308 projects are on schedule 296 projects are delayed. 533 projects do not have fixed dates of commissioning. 123 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

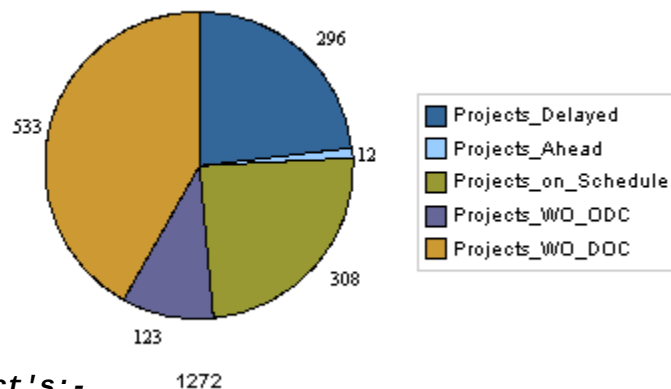

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1272 projects when sanctioned, was of the order of Rs. 1589750.53 crore but this was subsequently revised to Rs. 1771039.29 crore implying a cost overrun of 11.4%. The expenditure incurred on these projects till August, 2017 is Rs. 689034.34 crore, which is 38.9% of the anticipated cost of the projects.

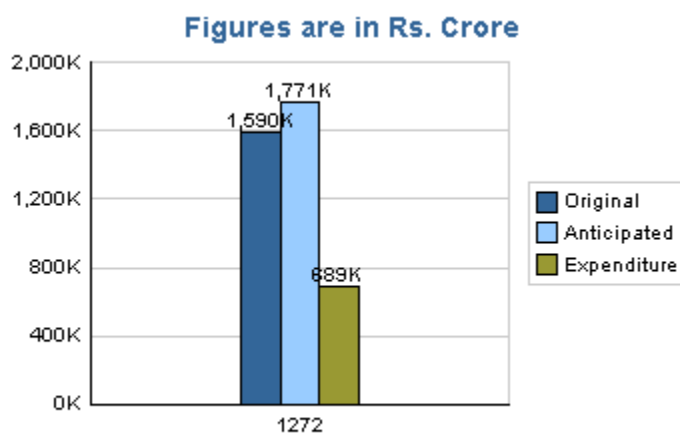


TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1257
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	12
No of Projects elevated to the status of Major Projects	8
No of Projects in Current Month	1272

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	296 (23.27%)	12 (.94%)	308 (24.21%)	123 (9.67%)	533 (41.90%)	1272
Latest Approved (Date)	239 (18.79%)	10 (.79%)	370 (29.09%)	119 (9.36%)	534 (41.98%)	1272

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1131	14,07,886.52	15,29,046.76	5,21,415.19	34.10	1,21,160.24	8.60
Project with Revision in Cost	141	2,37,303.27	2,41,992.53	1,67,619.15	69.30	4,689.26	2.00
Total	1,272	16,45,189.79	17,71,039.29	6,89,034.34	38.91	1,25,849.50	7.65
Original Cost of All Projects							
Original Cost	1,272	15,89,750.53	17,71,039.29	6,89,034.34	38.91	1,81,288.76	11.40

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	296	5,37,975.84	6,54,892.71	4,02,226.95	61.40	1,16,916.87	21.70
Latest Approved (RCE)	239	4,31,574.63	5,13,856.29	2,99,971.46	58.40	82,281.66	19.10
Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	47	91,693.86	98,769.51	73,108.26	74.00	7,075.65	7.70

TABLE-5

Extent of cost overrun in projects with respect to original schedule (Sector Wise) Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	59.41
3	COAL	92	88,124.99	88,310.36	0.21	7	18,876.68	19,914.04	5.50
4	FERTILISERS	2	680.64	703.44	3.35	2	680.64	703.44	3.35
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	34	57,349.49	57,563.17	0.37	5	1,639.71	2,211.39	34.86
7	PETROLEUM	108	2,08,215.16	2,09,608.54	0.67	19	25,330.13	31,941.76	26.10
8	POWER	127	3,44,032.76	3,97,114.95	15.43	43	88,811.97	1,42,172.89	60.08
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	1	196.70	209.00	6.25
11	RAILWAYS	353	3,54,063.17	4,46,938.49	26.23	205	1,06,335.90	2,60,041.87	144.55
12	ROAD TRANSPORT AND HIGHWAYS	482	3,17,373.88	3,23,746.08	2.01	43	25,598.69	32,656.93	27.57
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	5	1,205.50	2,172.77	80.24
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	36	1,45,945.23	1,57,932.60	8.21	4	21,350.59	33,518.34	56.99
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	2	453.64	469.04	3.39
Total		1272	15,89,750.53	17,71,039.29	11.40	341	3,09,485.22	5,59,295.63	80.72

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule (State Wise) Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun^ (%)
1	ANDHRA PRADESH	60	97,457.47	1,01,158.09	3.80	8	3,331.30	8,058.07	141.89
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	6	9,755.78	25,584.87	162.25
3	ASSAM	50	33,769.60	47,399.82	40.36	16	15,110.50	28,922.44	91.41
4	BIHAR	78	68,807.61	82,224.21	19.50	18	15,102.73	28,815.28	90.80
5	GOA	10	4,379.12	4,376.91	-0.05	2	453.64	469.04	3.39
6	GUJARAT	43	39,902.03	42,376.41	6.20	10	4,926.85	8,629.39	75.15
7	HARYANA	21	14,081.22	15,967.45	13.40	3	1,633.56	3,653.00	123.62
8	HIMACHAL PRADESH	13	15,017.74	21,417.01	42.61	2	4,966.47	11,365.74	128.85
9	JAMMU AND KASHMIR	10	27,408.66	47,277.79	72.49	3	7,930.45	27,799.58	250.54
10	KARNATAKA	47	79,393.90	97,719.96	23.08	23	17,879.22	37,369.06	109.01
11	KERALA	21	37,154.14	38,770.19	4.35	6	2,117.36	3,733.41	76.32
12	MADHYA PRADESH	53	55,860.99	60,307.08	7.96	7	4,634.35	9,088.98	96.12
13	MAHARASHTRA	113	1,70,980.76	1,80,382.47	5.50	27	33,696.88	47,110.55	39.81
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	1227.45
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	500.11
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	252.94
18	ODISHA	66	72,116.99	79,775.64	10.62	19	6,641.38	14,316.32	115.56
19	PUNJAB	28	15,555.77	15,561.50	0.04	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	62	44,007.10	46,166.34	4.91	14	5,657.08	7,816.32	38.17
21	SIKKIM	6	2,537.08	5,585.45	120.15	3	2,036.94	5,085.59	149.67
22	TAMIL NADU	57	76,796.39	99,583.49	29.67	20	39,195.11	62,731.32	60.05
23	TRIPURA	11	4,400.64	9,067.42	106.05	7	2,909.18	7,575.96	160.42
24	UTTAR PRADESH	83	1,09,253.66	1,13,086.92	3.51	16	25,523.56	29,811.40	16.80
25	WEST BENGAL	53	56,102.34	68,521.71	22.14	20	19,094.91	33,611.60	76.02
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	0.00
27	DELHI	17	50,925.07	50,831.89	-0.18	2	353.35	406.17	14.95
28	CHHATISGARH	41	94,608.92	96,545.85	2.05	7	5,623.92	7,839.58	39.40
29	JHARKHAND	48	46,724.53	50,366.69	7.80	10	9,447.31	13,093.25	38.59
30	UTTARAKHAND	13	16,833.35	20,347.26	20.87	5	5,112.02	8,626.44	68.75
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	40.28
32	TELANGANA	35	24,832.84	27,489.74	10.70	10	3,002.30	5,850.29	94.86
33	MULTI STATE	180	2,89,659.25	2,74,260.37	-5.32	69	55,057.32	95,541.95	73.53
Total		1272	15,89,750.53	17,71,039.29	11.40	341	3,09,485.22	5,59,295.63	80.72

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule RS.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	3	27,271.00	29,779.00	47 - 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	21 - 80
3	COAL	92	88,124.99	88,310.36	0.21	39	20,618.90	20,758.14	2 - 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	29 - 29
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	34	57,349.49	57,563.17	0.37	17	46,224.80	46,036.59	5 - 72
7	PETROLEUM	108	2,08,215.16	2,09,608.54	0.67	33	58,967.97	60,599.99	1 - 93
8	POWER	127	3,44,032.76	3,97,114.95	15.43	60	2,01,036.97	2,34,794.53	5 - 136
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	5	1,183.93	1,183.93	6 - 15
11	RAILWAYS	353	3,54,063.17	4,46,938.49	26.23	34	39,358.15	1,06,823.44	12 - 261
12	ROAD TRANSPORT AND HIGHWAYS	482	3,17,373.88	3,23,746.08	2.01	77	66,519.05	70,193.85	5 - 116
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	516.39	1,269.46	96 - 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	1	13,334.00	13,334.00	26 - 26
15	URBAN DEVELOPMENT	36	1,45,945.23	1,57,932.60	8.21	21	60,404.82	65,088.18	2 - 72
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	-
Total		1272	15,89,750.53	17,71,039.29	11.40	296	5,37,975.84	6,54,892.71	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule (State Wise) Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	60	97,457.47	1,01,158.09	3.80	11	8,968.69	10,649.33	6 - 144
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	3	3,209.82	7,672.72	36 - 99
3	ASSAM	50	33,769.60	47,399.82	40.36	11	11,529.00	23,031.10	15 - 122
4	BIHAR	78	68,807.61	82,224.21	19.50	10	31,086.63	37,655.09	7 - 98
5	GOA	10	4,379.12	4,376.91	-0.05	0	0.00	0.00	-
6	GUJARAT	43	39,902.03	42,376.41	6.20	7	16,203.35	17,884.87	7 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	4	2,846.95	4,026.95	24 - 87
8	HIMACHAL PRADESH	13	15,017.74	21,417.01	42.61	3	6,107.21	10,586.37	15 - 111
9	JAMMU AND KASHMIR	10	27,408.66	47,277.79	72.49	7	20,944.03	40,813.16	12 - 193
10	KARNATAKA	47	79,393.90	97,719.96	23.08	5	43,551.13	43,551.13	10 - 24
11	KERALA	21	37,154.14	38,770.19	4.35	5	10,696.37	10,803.56	9 - 65
12	MADHYA PRADESH	53	55,860.99	60,307.08	7.96	10	16,666.98	17,727.08	2 - 96
13	MAHARASHTRA	113	1,70,980.76	1,80,382.47	5.50	23	54,314.13	58,583.67	6 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	2	944.25	9,874.69	44 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	3	1,051.32	1,051.32	15 - 50
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	71 - 136
17	NAGALAND	7	8,126.79	10,276.79	26.46	4	2,049.11	4,199.11	36 - 60
18	ODISHA	66	72,116.99	79,775.64	10.62	14	9,632.59	10,858.30	5 - 108
19	PUNJAB	28	15,555.77	15,561.50	0.04	4	1,512.09	1,512.09	3 - 23
20	RAJASTHAN	62	44,007.10	46,166.34	4.91	10	17,938.02	18,557.77	6 - 74
21	SIKKIM	6	2,537.08	5,585.45	120.15	2	1,648.94	4,638.22	51 - 80
22	TAMIL NADU	57	76,796.39	99,583.49	29.67	19	38,205.14	46,042.58	1 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	3	1,231.33	3,893.38	4 - 72
24	UTTAR PRADESH	83	1,09,253.66	1,13,086.92	3.51	13	17,881.83	17,981.01	12 - 58
25	WEST BENGAL	53	56,102.34	68,521.71	22.14	14	25,834.58	26,594.11	6 - 57
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	1	6,086.08	5,479.75	5 - 5
27	DELHI	17	50,925.07	50,831.89	-0.18	5	3,996.12	3,996.12	5 - 27
28	CHHATISGARH	41	94,608.92	96,545.85	2.05	13	60,746.34	61,940.28	10 - 93
29	JHARKHAND	48	46,724.53	50,366.69	7.80	22	25,136.25	25,418.39	5 - 166
30	UTTARAKHAND	13	16,833.35	20,347.26	20.87	5	7,719.83	11,020.99	50 - 89
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	35	24,832.84	27,489.74	10.70	13	5,449.94	5,987.93	12 - 132
33	MULTI STATE	180	2,89,659.25	2,74,260.37	-5.32	47	83,485.12	1,06,490.88	5 - 261
Total		1272	15,89,750.53	17,71,039.29	11.40	296	5,37,975.84	6,54,892.71	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	3	27,271.00	29,779.00	47 - 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	1	314.61	441.33	21 - 21
3	COAL	92	88,248.46	88,310.36	0.07	35	13,134.81	13,195.91	2 - 132
4	FERTILISERS	2	692.29	703.44	1.61	0	0.00	0.00	-
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	34	57,730.46	57,563.17	-0.29	16	30,724.19	30,511.59	5 - 72
7	PETROLEUM	108	2,11,120.11	2,09,608.54	-0.72	11	10,649.76	10,266.71	1 - 71
8	POWER	127	3,78,154.11	3,97,114.95	5.01	36	1,60,559.89	1,66,833.45	5 - 111
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	4	819.94	819.94	6 - 7
11	RAILWAYS	353	3,58,101.75	4,46,938.49	24.81	37	41,508.91	1,09,906.41	0 - 261
12	ROAD TRANSPORT AND HIGHWAYS	482	3,17,947.90	3,23,746.08	1.82	77	66,534.77	70,193.85	5 - 116
13	SHIPPING AND PORTS	8	4,131.25	5,085.02	23.09	2	516.39	1,269.46	96 - 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	1	13,334.00	13,334.00	26 - 26
15	URBAN DEVELOPMENT	36	1,59,215.64	1,57,932.60	-0.81	15	64,488.36	63,477.34	5 - 70
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	-
Total		1272	16,45,189.79	17,71,039.29	7.65	239	4,31,574.63	5,13,856.29	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	59.41
3	COAL	92	88,248.46	88,310.36	0.07	2	17,655.97	17,727.42	0.40
4	FERTILISERS	2	692.29	703.44	1.61	1	482.85	494.00	2.31
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	34	57,730.46	57,563.17	-0.29	3	1,586.97	1,777.68	12.02
7	PETROLEUM	108	2,11,120.11	2,09,608.54	-0.72	9	12,393.82	15,719.05	26.83
8	POWER	127	3,78,154.11	3,97,114.95	5.01	15	37,863.85	59,469.72	57.06
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	1	196.70	209.00	6.25
11	RAILWAYS	353	3,58,101.75	4,46,938.49	24.81	196	1,04,132.82	2,52,794.64	142.76
12	ROAD TRANSPORT AND HIGHWAYS	482	3,17,947.90	3,23,746.08	1.82	33	23,181.71	29,854.53	28.78
13	SHIPPING AND PORTS	8	4,131.25	5,085.02	23.09	5	1,219.00	2,172.77	78.24
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	36	1,59,215.64	1,57,932.60	-0.81	2	662.97	666.80	0.58
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	2	454.00	469.04	3.31
Total		1272	16,45,189.79	17,71,039.29	7.65	274	2,18,835.73	4,14,638.81	89.47

^ - Cost Overrun = Anticipated Cost minus latest Cost.

TABLE-11

<u>Extent of time & cost overrun in projects with respect to latest schedule</u> Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	1	3,492.00	6,000.00	85- 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	1	314.61	441.33	21- 21
3	COAL	92	88,248.46	88,310.36	0.07	1	418.97	489.62	132- 132
4	FERTILISERS	2	692.29	703.44	1.61	0	0.00	0.00	0- 0
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	34	57,730.46	57,563.17	-0.29	1	343.00	488.40	17- 17
7	PETROLEUM	108	2,11,120.11	2,09,608.54	-0.72	2	502.56	698.96	20- 38
8	POWER	127	3,78,154.11	3,97,114.95	5.01	8	14,241.41	23,159.97	12- 111
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	0	0.00	0.00	0- 0
11	RAILWAYS	353	3,58,101.75	4,46,938.49	24.81	27	24,892.22	93,368.75	33- 261
12	ROAD TRANSPORT AND HIGHWAYS	482	3,17,947.90	3,23,746.08	1.82	6	5,344.71	9,004.30	22- 106
13	SHIPPING AND PORTS	8	4,131.25	5,085.02	23.09	2	516.39	1,269.46	96- 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	36	1,59,215.64	1,57,932.60	-0.81	0	0.00	0.00	0- 0
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	0- 0
Total		1272	16,45,189.79	17,71,039.29	7.65	50	51,783.87	1,38,748.09	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus latest Cost.

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	1	3,492.00	6,000.00	85- 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	21- 80
3	COAL	92	88,124.99	88,310.36	0.21	5	1,242.59	2,233.82	60- 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	29- 29
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	34	57,349.49	57,563.17	0.37	2	545.61	715.40	12- 17
7	PETROLEUM	108	2,08,215.16	2,09,608.54	0.67	10	17,450.61	22,029.58	9- 70
8	POWER	127	3,44,032.76	3,97,114.95	15.43	35	69,821.30	1,03,857.59	5- 136
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	0	0.00	0.00	0- 0
11	RAILWAYS	353	3,54,063.17	4,46,938.49	26.23	27	24,810.01	93,368.75	33- 261
12	ROAD TRANSPORT AND HIGHWAYS	482	3,17,373.88	3,23,746.08	2.01	7	5,483.64	9,159.30	22- 106
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	516.39	1,269.46	96- 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	36	1,45,945.23	1,57,932.60	8.21	3	14,955.59	19,673.33	21- 70
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	0- 0
Total		1272	15,89,750.53	17,71,039.29	11.40	96	1,40,857.60	2,63,338.83	

\$- Time overrun = Anticipated Date of Commissioning minus original schedule Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus original Cost.

TABLE-13

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	60	97,457.47	1,01,158.09	3.80	3	1,241.74	3,280.38	17 - 144
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	3	3,209.82	7,672.72	36 - 99
3	ASSAM	50	33,769.60	47,399.82	40.36	7	8,402.21	20,010.02	38 - 122
4	BIHAR	78	68,807.61	82,224.21	19.50	2	9,129.65	15,698.11	12 - 98
5	GOA	10	4,379.12	4,376.91	-0.05	0	0.00	0.00	-
6	GUJARAT	43	39,902.03	42,376.41	6.20	2	1,827.34	3,559.49	63 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	1	1,108.00	2,288.00	76 - 76
8	HIMACHAL PRADESH	13	15,017.74	21,417.01	42.61	1	3,919.59	8,398.75	111 - 111
9	JAMMU AND KASHMIR	10	27,408.66	47,277.79	72.49	3	7,930.45	27,799.58	12 - 193
10	KARNATAKA	47	79,393.90	97,719.96	23.08	0	0.00	0.00	-
11	KERALA	21	37,154.14	38,770.19	4.35	1	607.06	714.25	17 - 17
12	MADHYA PRADESH	53	55,860.99	60,307.08	7.96	4	3,176.60	4,244.44	22 - 96
13	MAHARASHTRA	113	1,70,980.76	1,80,382.47	5.50	9	15,706.53	21,470.35	12 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	71 - 136
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	60 - 60
18	ODISHA	66	72,116.99	79,775.64	10.62	2	316.64	1,542.70	58 - 105
19	PUNJAB	28	15,555.77	15,561.50	0.04	0	0.00	0.00	-
20	RAJASTHAN	62	44,007.10	46,166.34	4.91	2	1,482.93	2,102.68	48 - 60
21	SIKKIM	6	2,537.08	5,585.45	120.15	2	1,648.94	4,638.22	51 - 80
22	TAMIL NADU	57	76,796.39	99,583.49	29.67	5	21,961.42	30,547.97	24 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	2	1,015.95	3,678.00	12 - 72
24	UTTAR PRADESH	83	1,09,253.66	1,13,086.92	3.51	1	195.42	294.60	58 - 58
25	WEST BENGAL	53	56,102.34	68,521.71	22.14	2	7,480.57	9,325.01	9 - 38
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	-
27	DELHI	17	50,925.07	50,831.89	-0.18	0	0.00	0.00	-
28	CHHATISGARH	41	94,608.92	96,545.85	2.05	4	4,351.49	5,824.16	38 - 93
29	JHARKHAND	48	46,724.53	50,366.69	7.80	2	1,161.75	1,443.89	99 - 166
30	UTTARAKHAND	13	16,833.35	20,347.26	20.87	3	4,749.74	8,051.41	58 - 75
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	35	24,832.84	27,489.74	10.70	4	1,463.44	2,104.31	33 - 132
33	MULTI STATE	180	2,89,659.25	2,74,260.37	-5.32	26	35,890.09	59,621.03	5 - 261
Total		1272	15,89,750.53	17,71,039.29	11.40	96	1,40,857.60	2,63,338.83	

\$- Time overrun = Anticipated Date of Commissioning minus original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus original Cost.

TABLE-14

EXECUTIVE SUMMARY COSTING Rs.1000 crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	128	0
2	ROAD TRANSPORT AND HIGHWAYS	102	7
3	POWER	64	9
4	PETROLEUM	44	2
5	COAL	12	0
6	URBAN DEVELOPMENT	11	0
7	STEEL	9	0
8	ATOMIC ENERGY	4	0
9	TELECOMMUNICATIONS	2	0
10	MINES	1	0
11	HEAVY INDUSTRY	1	0
12	SHIPPING AND PORTS	1	0
	Total	379	18

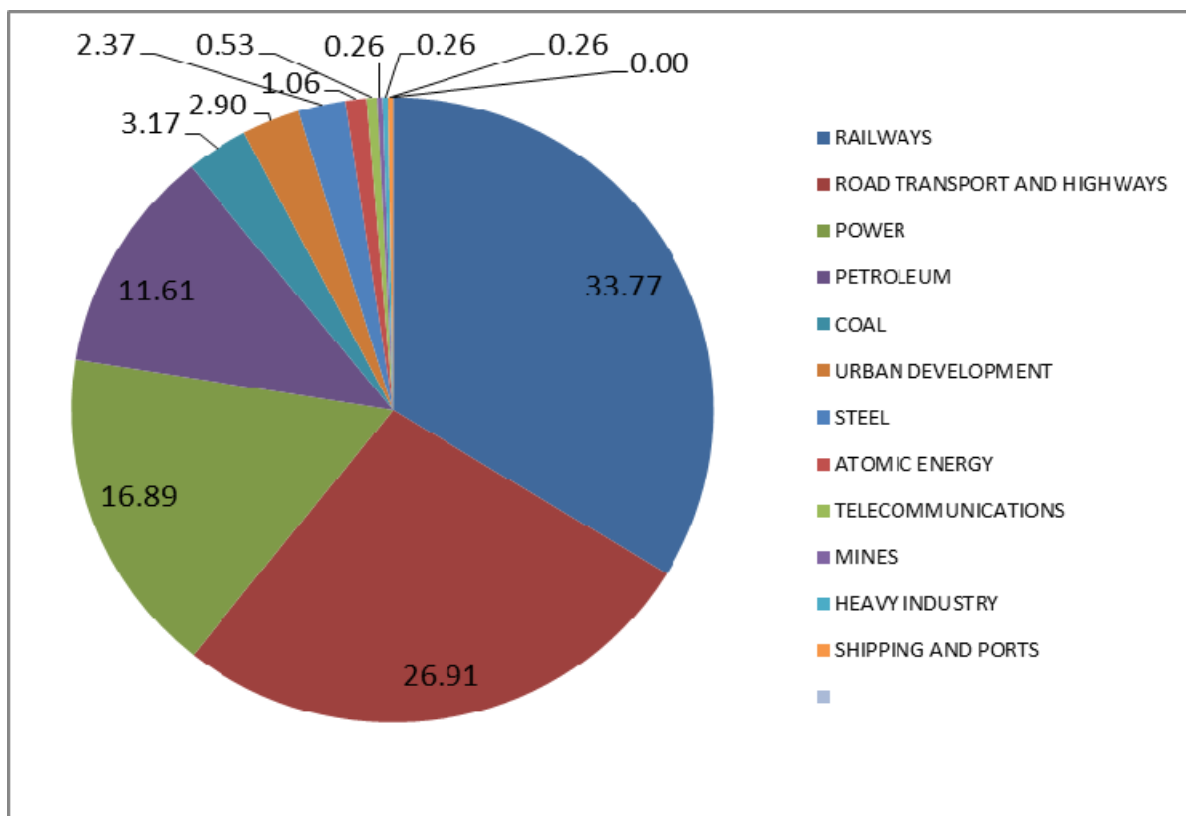


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	372
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	5
No of Projects elevated to the status of Mega Projects	3
No of Projects in Current Month	379

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	124 (32.72%)	2 (.53%)	93 (24.54%)	44 (11.61%)	116 (30.61%)	379
Latest Approved (Date)	96 (25.33%)	1 (.26%)	124 (32.72%)	41 (10.82%)	117 (30.87%)	379

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	329	10,77,052.15	11,74,320.29	4,33,895.53	36.90	97,268.14	9.00
Project with Revision in Cost	50	2,01,480.16	2,05,101.59	1,51,112.84	73.70	3,621.43	1.80
Total	379	12,78,532.31	13,79,421.88	5,85,008.37	42.41	1,00,889.57	7.89
Original Cost of All Projects							
Original Cost	379	12,27,815.53	13,79,421.88	5,85,008.37	42.41	1,51,606.35	12.35

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	124	4,69,149.69	5,80,122.98	3,63,601.29	62.70	1,10,973.29	23.70
Latest Approved (RCE)	96	3,73,022.95	4,51,690.13	2,69,022.77	59.60	78,667.18	21.10
Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	18	78,230.33	84,847.81	64,062.62	75.50	6,617.48	8.50

TABLE-16

Extent of cost overrun in projects with respect to original schedule (Sector Wise) RS._1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	COAL	12	55,807.73	55,808.53	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,164.22	48,150.68	-0.03	1	768.88	1,113.34	44.80
5	PETROLEUM	44	1,82,124.15	1,83,579.32	0.80	9	21,796.28	27,032.81	24.02
6	POWER	64	3,18,954.02	3,70,426.56	16.14	26	81,561.53	1,33,312.80	63.45
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	128	2,69,422.64	3,37,107.65	25.12	77	68,576.52	1,94,534.78	183.68
9	ROAD TRANSPORT AND HIGHWAYS	102	1,48,606.06	1,54,042.12	3.66	15	17,413.21	22,849.27	31.22
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
12	URBAN DEVELOPMENT	11	1,39,164.14	1,50,926.15	8.45	2	20,995.00	32,903.01	56.72
Total		379	12,27,815.53	13,79,421.88	12.35	134	2,46,729.42	4,61,273.11	86.96

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

<u>Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	16	82,287.82	84,583.48	2.79	3	2,114.62	5,137.28	142.94
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	3	9,356.22	24,952.87	166.70
3	ASSAM	9	21,033.85	32,693.76	55.43	5	12,723.01	24,469.18	92.32
4	BIHAR	14	41,018.97	52,350.17	27.62	5	10,666.26	21,997.46	106.23
5	GUJARAT	10	23,570.79	25,890.71	9.84	2	1,955.10	4,275.02	118.66
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	12,226.08	18,625.35	52.34	2	4,966.47	11,365.74	128.85
8	JAMMU AND KASHMIR	10	27,408.66	47,277.79	72.49	3	7,930.45	27,799.58	250.54
9	KARNATAKA	22	67,362.06	84,410.34	25.31	13	14,079.10	31,886.38	126.48
10	KERALA	6	31,137.08	32,153.08	3.26	1	550.00	1,566.00	184.73
11	MADHYA PRADESH	14	36,811.17	40,775.83	10.77	5	3,687.75	7,652.41	107.51
12	MAHARASHTRA	45	1,43,334.61	1,51,277.32	5.54	17	29,763.57	41,277.58	38.68
13	MANIPUR	1	727.56	9,658.00	1227.45	1	727.56	9,658.00	1227.45
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	500.11
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	24	56,413.98	63,001.36	11.68	6	3,733.20	10,320.58	176.45
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	1	829.74	1,161.64	40.00
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	15	58,917.76	79,396.45	34.76	8	36,568.78	57,047.47	56.00
22	TRIPURA	3	2,129.35	6,386.31	199.92	3	2,129.35	6,386.31	199.92
23	UTTAR PRADESH	33	86,307.66	88,855.13	2.95	6	22,325.93	25,327.98	13.45
24	WEST BENGAL	22	44,076.95	54,342.93	23.29	8	16,025.21	28,018.84	74.84
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	0.00
26	DELHI	4	45,462.73	45,316.73	-0.32	0	0.00	0.00	0.00
27	CHHATISGARH	12	83,067.13	84,096.77	1.24	3	4,700.73	6,009.10	27.83
28	JHARKHAND	10	33,188.25	35,781.77	7.81	3	7,451.01	10,044.53	34.81
29	UTTARAKHAND	6	14,392.36	17,542.29	21.89	2	4,635.48	7,785.41	67.95
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	502.99	2,170.47	331.51
31	MULTI STATE	65	2,43,198.62	2,21,340.96	-8.99	26	40,938.33	73,661.16	79.93
Total		379	12,27,815.53	13,79,421.88	12.35	134	2,46,729.42	4,61,273.11	86.96

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	3	27,271.00	29,779.00	47 - 85
2	COAL	12	55,807.73	55,808.53	0.00	3	8,192.43	8,192.43	6 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	6	40,963.49	40,605.49	5 - 55
5	PETROLEUM	44	1,82,124.15	1,83,579.32	0.80	15	52,116.04	53,137.93	5 - 71
6	POWER	64	3,18,954.02	3,70,426.56	16.14	38	1,91,162.37	2,23,439.53	6 - 136
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
8	RAILWAYS	128	2,69,422.64	3,37,107.65	25.12	23	34,772.64	1,00,242.94	27 - 261
9	ROAD TRANSPORT AND HIGHWAYS	102	1,48,606.06	1,54,042.12	3.66	29	43,533.58	47,020.22	15 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	13,334.00	13,334.00	26 - 26
12	URBAN DEVELOPMENT	11	1,39,164.14	1,50,926.15	8.45	5	56,086.14	60,544.14	5 - 29
Total		379	12,27,815.53	13,79,421.88	12.35	124	4,69,149.69	5,80,122.98	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	16	82,287.82	84,583.48	2.79	3	5,186.00	5,910.00	6 - 144
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	2	3,070.89	7,517.72	55 - 99
3	ASSAM	9	21,033.85	32,693.76	55.43	4	10,016.81	21,128.07	66 - 122
4	BIHAR	14	41,018.97	52,350.17	27.62	3	27,010.57	33,413.27	7 - 98
5	GUJARAT	10	23,570.79	25,890.71	9.84	3	14,357.72	16,086.49	45 - 63
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	18,625.35	52.34	2	5,836.38	10,315.54	15 - 111
8	JAMMU AND KASHMIR	10	27,408.66	47,277.79	72.49	7	20,944.03	40,813.16	12 - 193
9	KARNATAKA	22	67,362.06	84,410.34	25.31	3	43,226.34	43,226.34	10 - 19
10	KERALA	6	31,137.08	32,153.08	3.26	2	9,770.08	9,770.08	9 - 29
11	MADHYA PRADESH	14	36,811.17	40,775.83	10.77	4	14,881.45	15,459.32	6 - 53
12	MAHARASHTRA	45	1,43,334.61	1,51,277.32	5.54	14	49,672.70	53,293.11	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	71 - 136
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	24	56,413.98	63,001.36	11.68	3	6,460.53	7,480.00	10 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	3	14,823.44	15,155.34	48 - 74
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	15	58,917.76	79,396.45	34.76	7	32,078.89	40,215.44	23 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	33	86,307.66	88,855.13	2.95	5	14,777.89	14,777.89	15 - 51
24	WEST BENGAL	22	44,076.95	54,342.93	23.29	8	22,750.71	23,510.24	6 - 57
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	1	6,086.08	5,479.75	5 - 5
26	DELHI	4	45,462.73	45,316.73	-0.32	2	2,613.73	2,613.73	5 - 25
27	CHHATISGARH	12	83,067.13	84,096.77	1.24	7	59,311.92	60,007.30	10 - 55
28	JHARKHAND	10	33,188.25	35,781.77	7.81	6	20,164.09	20,389.93	5 - 99
29	UTTARAKHAND	6	14,392.36	17,542.29	21.89	3	7,127.06	10,276.99	58 - 89
30	TELANGANA	6	14,904.53	16,572.01	11.19	1	1,266.60	1,266.60	18 - 18
31	MULTI STATE	65	2,43,198.62	2,21,340.96	-8.99	24	71,889.34	93,605.55	7 - 261
Total		379	12,27,815.53	13,79,421.88	12.35	124	4,69,149.69	5,80,122.98	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

\$ - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	3	27,271.00	29,779.00	47 - 85
2	COAL	12	55,807.73	55,808.53	0.00	2	2,285.32	2,285.32	6 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,466.31	48,150.68	-0.65	5	25,438.49	25,080.49	5 - 55
5	PETROLEUM	44	1,84,949.77	1,83,579.32	-0.74	2	7,067.36	6,507.36	23 - 71
6	POWER	64	3,51,811.90	3,70,426.56	5.29	23	1,54,556.85	1,60,564.39	7 - 111
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
8	RAILWAYS	128	2,71,234.80	3,37,107.65	24.29	25	36,263.19	1,02,747.91	0 - 261
9	ROAD TRANSPORT AND HIGHWAYS	102	1,48,606.06	1,54,042.12	3.66	29	43,533.58	47,020.22	15 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	13,334.00	13,334.00	26 - 26
12	URBAN DEVELOPMENT	11	1,52,083.17	1,50,926.15	-0.76	5	61,555.16	60,544.14	5 - 29
Total		379	12,78,532.31	13,79,421.88	7.89	96	3,73,022.95	4,51,690.13	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

TABLE-21

<u>Extent of cost overrun in projects with respect to latest schedule</u> RS.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	COAL	12	55,807.73	55,808.53	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,466.31	48,150.68	-0.65	1	1,070.97	1,113.34	3.96
5	PETROLEUM	44	1,84,949.77	1,83,579.32	-0.74	5	11,374.26	14,442.84	26.98
6	POWER	64	3,51,811.90	3,70,426.56	5.29	9	35,467.42	56,727.11	59.94
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	128	2,71,234.80	3,37,107.65	24.29	73	68,827.34	1,90,529.42	176.82
9	ROAD TRANSPORT AND HIGHWAYS	102	1,48,606.06	1,54,042.12	3.66	15	17,413.21	22,849.27	31.22
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
12	URBAN DEVELOPMENT	11	1,52,083.17	1,50,926.15	-0.76	0	0.00	0.00	0.00
Total		379	12,78,532.31	13,79,421.88	7.89	107	1,69,771.20	3,35,189.08	97.44

^ - Cost Overrun = Anticipated Cost minus latest Cost.

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	1	3,492.00	6,000.00	85- 85
2	COAL	12	55,807.73	55,808.53	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,466.31	48,150.68	-0.65	0	0.00	0.00	0- 0
5	PETROLEUM	44	1,84,949.77	1,83,579.32	-0.74	0	0.00	0.00	0- 0
6	POWER	64	3,51,811.90	3,70,426.56	5.29	5	13,283.90	21,936.44	12- 111
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
8	RAILWAYS	128	2,71,234.80	3,37,107.65	24.29	19	21,642.95	88,198.16	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	102	1,48,606.06	1,54,042.12	3.66	4	4,847.10	8,333.74	22- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	11	1,52,083.17	1,50,926.15	-0.76	0	0.00	0.00	0- 0
Total		379	12,78,532.31	13,79,421.88	7.89	30	44,983.95	1,28,295.64	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

TABLE-23

<u>Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	1	3,492.00	6,000.00	85- 85
2	COAL	12	55,807.73	55,808.53	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROLEUM	44	1,82,124.15	1,83,579.32	0.80	5	15,828.24	19,562.62	9- 55
6	POWER	64	3,18,954.02	3,70,426.56	16.14	21	64,182.23	96,738.12	12- 136
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
8	RAILWAYS	128	2,69,422.64	3,37,107.65	25.12	19	21,642.95	88,198.16	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	102	1,48,606.06	1,54,042.12	3.66	4	4,847.10	8,333.74	22- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	11	1,39,164.14	1,50,926.15	8.45	1	14,600.00	19,058.00	24- 24
Total		379	12,27,815.53	13,79,421.88	12.35	52	1,26,310.52	2,41,717.94	

\$- Time overrun = Anticipated Date of Commissioning minus original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus original Cost.

TABLE-24

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	16	82,287.82	84,583.48	2.79	1	743.00	1,825.00	144 - 144
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	2	3,070.89	7,517.72	55 - 99
3	ASSAM	9	21,033.85	32,693.76	55.43	3	7,551.66	18,749.18	75 - 122
4	BIHAR	14	41,018.97	52,350.17	27.62	1	8,692.97	15,095.67	98 - 98
5	GUJARAT	10	23,570.79	25,890.71	9.84	1	1,509.10	3,237.87	63 - 63
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	18,625.35	52.34	1	3,919.59	8,398.75	111 - 111
8	JAMMU AND KASHMIR	10	27,408.66	47,277.79	72.49	3	7,930.45	27,799.58	12 - 193
9	KARNATAKA	22	67,362.06	84,410.34	25.31	0	0.00	0.00	-
10	KERALA	6	31,137.08	32,153.08	3.26	0	0.00	0.00	-
11	MADHYA PRADESH	14	36,811.17	40,775.83	10.77	2	2,230.00	2,807.87	22 - 53
12	MAHARASHTRA	45	1,43,334.61	1,51,277.32	5.54	5	14,423.33	19,503.64	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	71 - 136
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	24	56,413.98	63,001.36	11.68	1	183.23	1,202.70	58 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	1	829.74	1,161.64	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	15	58,917.76	79,396.45	34.76	4	21,811.42	29,947.97	24 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	33	86,307.66	88,855.13	2.95	0	0.00	0.00	-
24	WEST BENGAL	22	44,076.95	54,342.93	23.29	2	7,480.57	9,325.01	9 - 38
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	-
26	DELHI	4	45,462.73	45,316.73	-0.32	0	0.00	0.00	-
27	CHHATISGARH	12	83,067.13	84,096.77	1.24	2	3,874.16	4,848.27	38 - 40
28	JHARKHAND	10	33,188.25	35,781.77	7.81	1	900.05	1,125.89	99 - 99
29	UTTARAKHAND	6	14,392.36	17,542.29	21.89	2	4,635.48	7,785.41	58 - 75
30	TELANGANA	6	14,904.53	16,572.01	11.19	0	0.00	0.00	-
31	MULTI STATE	65	2,43,198.62	2,21,340.96	-8.99	13	30,698.44	52,974.65	20 - 261
Total		379	12,27,815.53	13,79,421.88	12.35	52	1,26,310.52	2,41,717.94	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

TABLE-25

<u>List of projects completed/dropped/Frozen during current month</u> Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>POWER</u>						
1	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II G	09/2013	1,575.30	05/2016	1,656.15	08/2017	1,328.51

TABLE-26

List of projects added Rs.150 Crore and above					(August 2017)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY G	5/2016	429.00	1/2019	429.00	1/2019
2	PIPELINE NETWORK PROJECT GELEKI, ASSAM G	7/2016	249.85	5/2020	244.70	5/2020
3	REDEVELOPMENT OF SANTHAL FIELD G	2/2017	1,162.56	3/2026	1,162.56	3/2026
4	SITARGANJ LPG PROJECT Central Sector Projects	2/2017	160.10	2/2020	160.10	2/2020
5	MUMBAI REFINERY EXPANSION PROJECT Central Sector Projects	9/2015	4,199.00	3/2020	4,199.00	3/2020
6	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG G	4/2017	420.76	9/2018	420.76	9/2018
7	LPG BP PROJECT KHORDHA Central Sector Projects	12/2016	161.59	12/2019	161.59	12/2019
	<u>POWER</u>					
8	AMELIA COAL MINE Central Sector Projects	1/2017	2,104.21	9/2020	2,104.21	9/2020
9	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A Central Sector Projects	3/2015	955.00	12/2015	1,364.00	3/2018
10	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) Central Sector Projects	4/2015	2,525.00	11/2017	2,525.00	11/2017
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
11	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH Central Sector Projects	3/2016	641.17	7/2016	641.17	7/2016
12	RHENOK-RORATHANG-PAKYONG ON NH 717A Central Sector Projects	4/2017	388.00	10/2017	447.37	10/2017

TABLE-27

Milestones (Cumulative due & achieved) Rs. 150 Crore and above

Total 3985

Achieved up to month 2190

TABLE-28


List of projects reporting additional delayed Rs. 150 Crore and above							(August 2017)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>COAL</u>						
1	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC G	364.75	364.75	10/2014	06/2017	07/2017	1
2	NEYVELI SOLAR POWER PROJECT 130 MW NLC G	687.28	687.28	06/2017	06/2017	08/2017	2
3	BATURA HIGHWALL PROJECT SECL G	231.92	231.92	03/2022	03/2020	03/2022	24
	<u>STEEL</u>						
4	3RD CONVERTER AND 4TH CASTER RINL G	974.76	974.76	07/2016	09/2017	10/2017	1
5	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS RINL G	877.73	877.73	07/2015	08/2017	09/2017	1
6	TURBO BLOWER - 5 RINL G	280.00	280.00	09/2016	08/2017	09/2017	1
	<u>PETROLEUM</u>						
7	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC G	861.79	1,256.72	05/2013	10/2017	12/2017	2
8	ASSAM RENEWAL PROJECT FOR GROUP A ONGC G	2,465.15	2,378.89	03/2013	03/2018	09/2018	6
9	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC G	736.65	571.47	09/2011	05/2018	06/2019	13
	<u>POWER</u>						
10	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL G	9,569.76	9,291.03	06/2015	08/2017	09/2017	1

List of projects reporting additional delayed Rs. 150 Crore and above							(August 2017)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
11	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION PGCIL G	550.06	550.06	03/2018	08/2017	09/2017	1
12	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO G	2,496.90	6,179.96	12/2009	01/2018	03/2018	2
13	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) NEEPCO G	368.72	1,329.43	07/2006	09/2017	11/2017	2
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL G	723.63	882.13	11/2014	10/2017	12/2017	2
15	KUDGI STPP STAGE 1 NTPC G	15,166.19	15,166.19	01/2017	09/2017	11/2017	2
16	EASTERN REGION STRENGTHENING SCHEME -IX PGCIL G	196.58	225.28	02/2016	09/2017	11/2017	2
17	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	12,964.60	01/2018	06/2018	08/2018	2
18	PARE HYDRO ELECTRIC PROJECT NEEPCO G	573.99	1,337.76	08/2013	12/2017	03/2018	3
19	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL G	487.49	639.46	06/2014	03/2018	06/2018	3
20	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B PGCIL G	2,514.88	2,514.88	12/2015	12/2017	03/2018	3
21	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) CVPPPL G	8,112.12	8,112.12	04/2020	01/2023	05/2023	4
22	NORTH KARANPURA STPP (3X660 MW) NTPC G	14,366.58	14,366.58	02/2019	02/2020	02/2021	12
23	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTRIC PGCIL G	808.63	808.63	01/2018	01/2018	03/2019	14
	<u>HEALTH AND FAMILY WELFARE</u>						
24	NEIGRIHMS SHILLONG MEGHALYA HSCC G	363.99	363.99	05/2018	05/2019	08/2019	3
25	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB HSCC G	152.95	152.95	02/2018	02/2018	08/2018	6
	<u>RAILWAYS</u>						
26	MURKONGSELEK-PASIGHAT NL NFR G	165.82	450.00	N.A.	03/2019	03/2020	12


List of projects reporting additional delayed Rs. 150 Crore and above							(August 2017)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
27	MURADABAD-BAREILY NHAI PPP (BOT)	1,267.00	1,267.00	06/2013	06/2017	09/2017	3
28	BAREILY-SITAPUR (NH-24) NHAI PPP (BOT)	1,046.00	1,046.00	09/2013	05/2017	10/2017	5
29	HUNGUND-SURATHKAL AND MANGALORE- KNT/KERALA BORDER NHAI G	946.00	946.00	N.A.	06/2017	12/2017	6
30	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	06/2017	12/2017	6
31	2-LANING WITH PS RAIBAREILI TO ALLAHABAD NHAI PPP (BOT)	291.36	291.36	01/2014	06/2017	12/2017	6
32	KRISHNANAGAR-BERHAMPUR NHAI PPP (ANNUITY)	702.16	702.16	07/2014	09/2017	03/2018	6
33	PANVEL-INDAPUR NHAI G	942.69	942.69	06/2014	09/2017	03/2018	6
34	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 NHAI PPP (BOT)	1,348.20	1,348.20	02/2014	09/2017	03/2018	6
35	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION NHAI G	479.00	479.00	N.A.	06/2017	12/2017	6
36	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) NHAI PPP (BOT)	1,108.00	2,288.00	11/2011	08/2017	03/2018	7
37	4-LANING OF GOA/KARNATAKA BORDER- KUNDAPUR SECTION NHAI PPP (BOT)	1,655.01	1,655.01	08/2016	08/2017	03/2018	7
38	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 NHAI PPP (BOT)	1,266.60	1,266.60	09/2016	07/2017	03/2018	8
39	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 NHAI G	605.84	605.84	N.A.	07/2017	07/2018	12
40	FOUR LANING OF VARANASI BYPASS NHAI G	261.09	261.09	05/2017	05/2017	06/2018	13
	<u>URBAN DEVELOPMENT</u>						
41	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD G	332.72	332.72	09/2016	10/2017	11/2017	1
42	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI CPWD G	405.01	405.01	12/2014	06/2017	07/2017	1
43	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR CPWD Central Sector Projects	216.69	216.69	03/2015	10/2018	11/2018	1
44	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CPWD G	154.00	154.00	11/2015	11/2017	12/2017	1

<u>List of projects reporting additional delayed Rs. 150 Crore and above</u>							(August 2017)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
45	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY CPWD EPC	164.00	164.00	01/2018	01/2018	03/2018	2
46	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL CPWD G	188.87	188.87	12/2015	09/2017	12/2017	3
47	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD CPWD G	171.86	171.86	03/2016	02/2018	12/2018	10

Graphical Presentation of All Projects w.r.t. Original Schedule

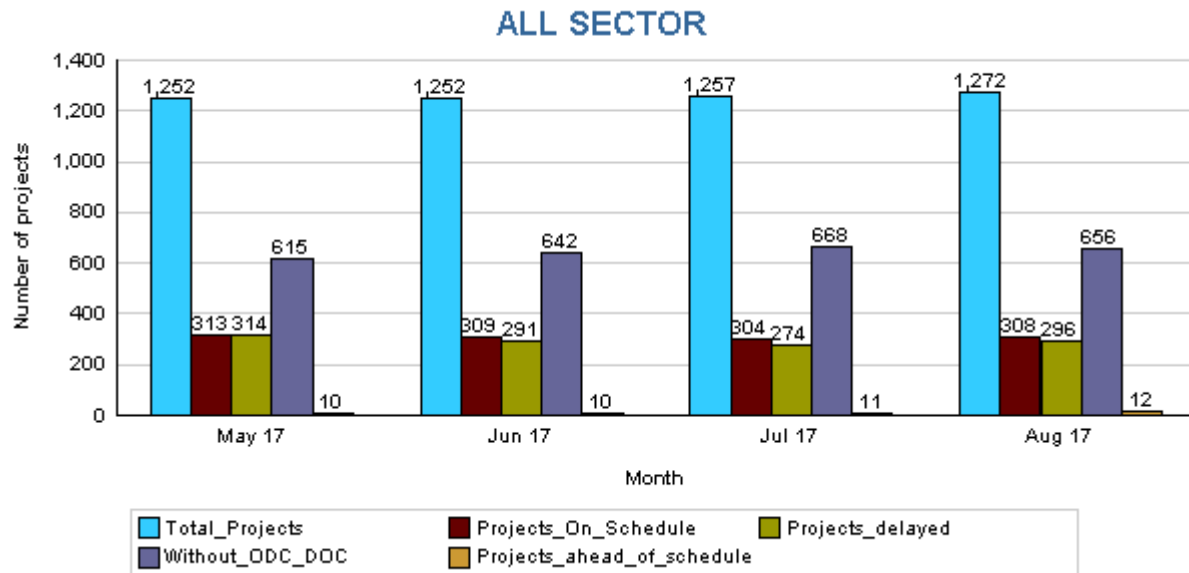


Break-up of 296 Delayed projects in August 2017

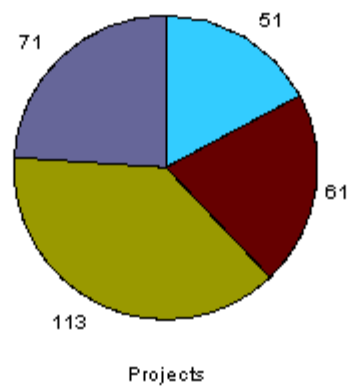


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

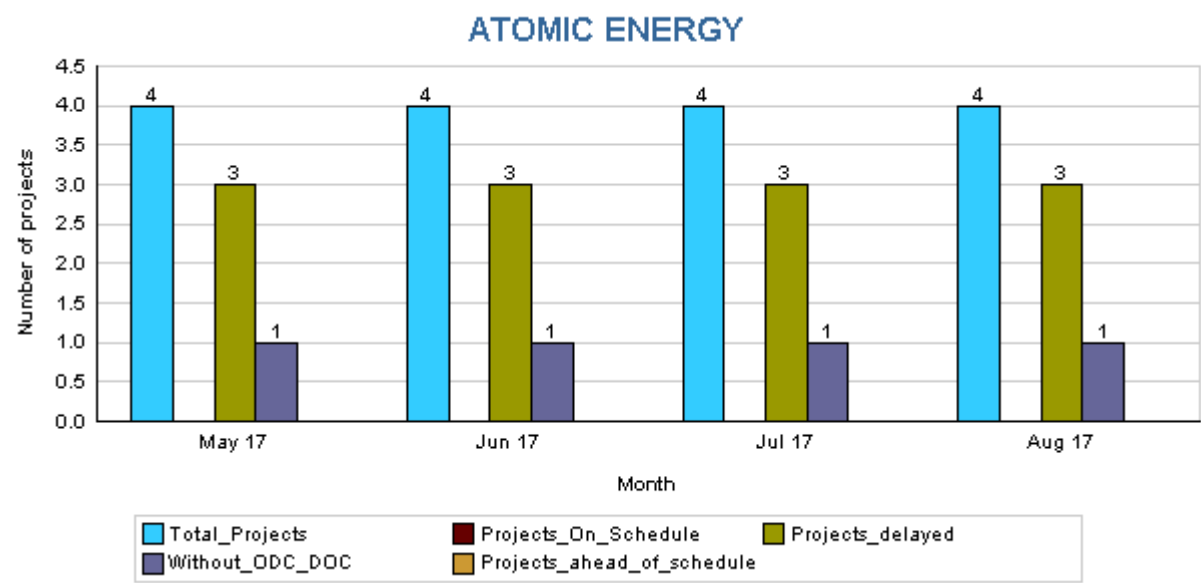


Break-up of 3 Delayed projects in August 2017

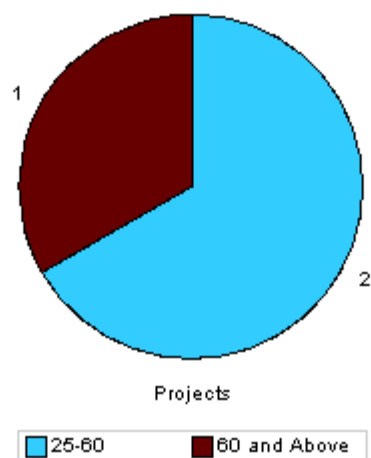


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

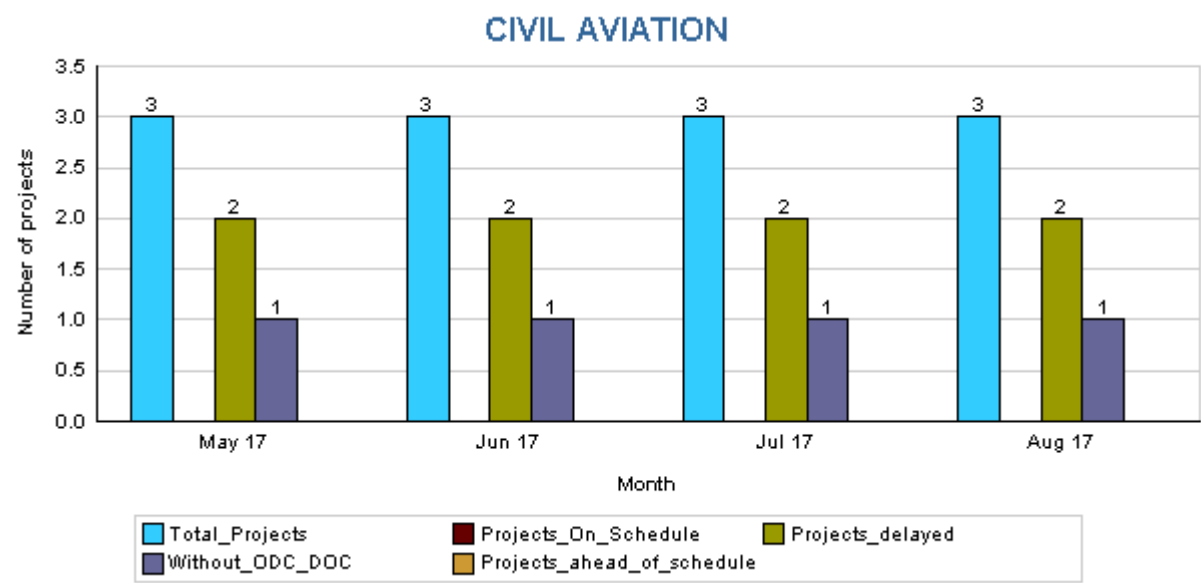


Break-up of 2 Delayed projects in August 2017

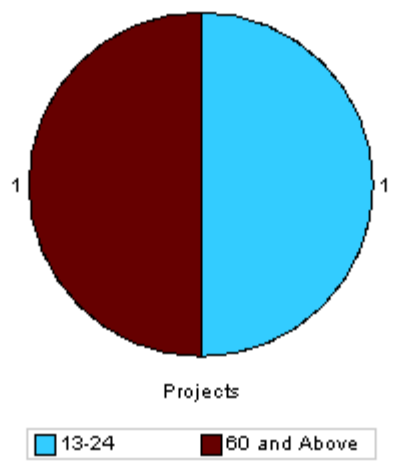


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

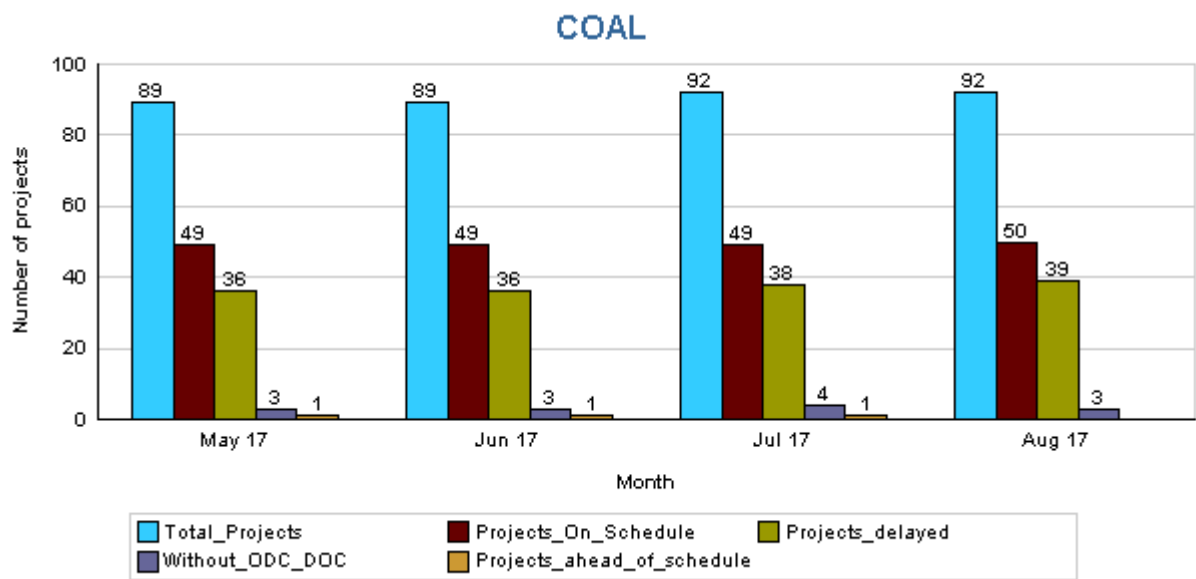


Break-up of 39 Delayed projects in August 2017

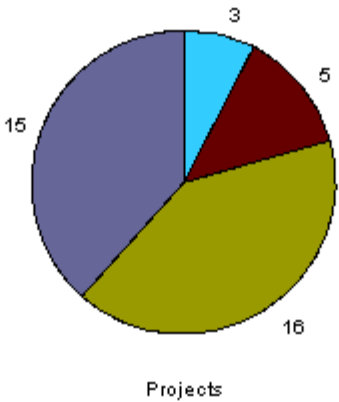


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

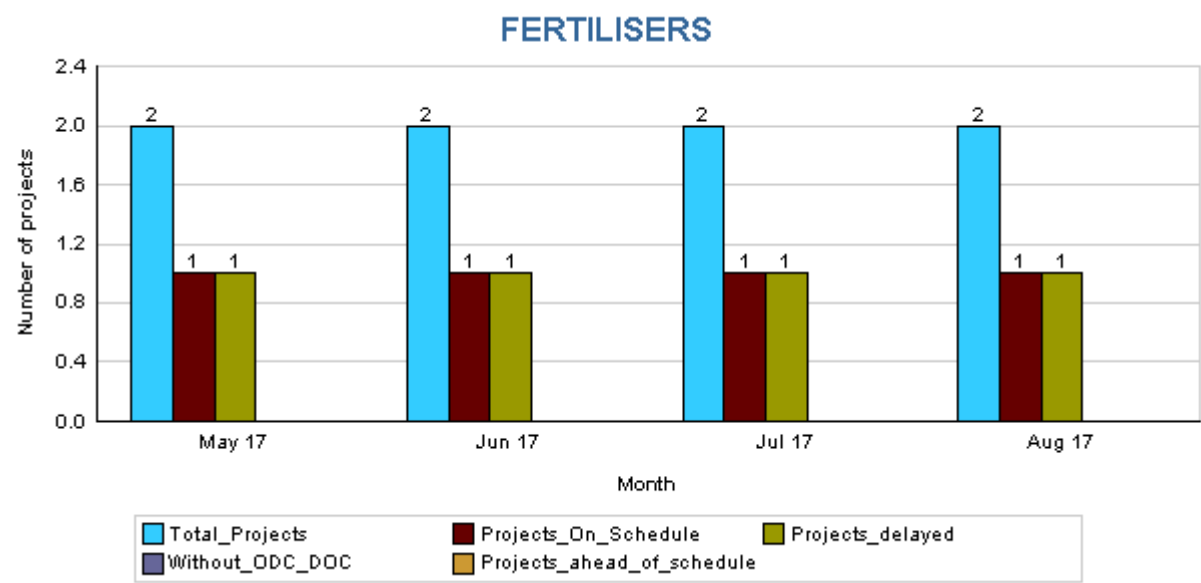


Break-up of 1 Delayed projects in August 2017

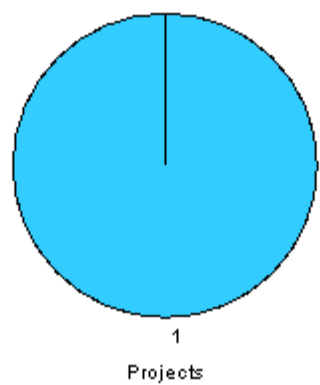

Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

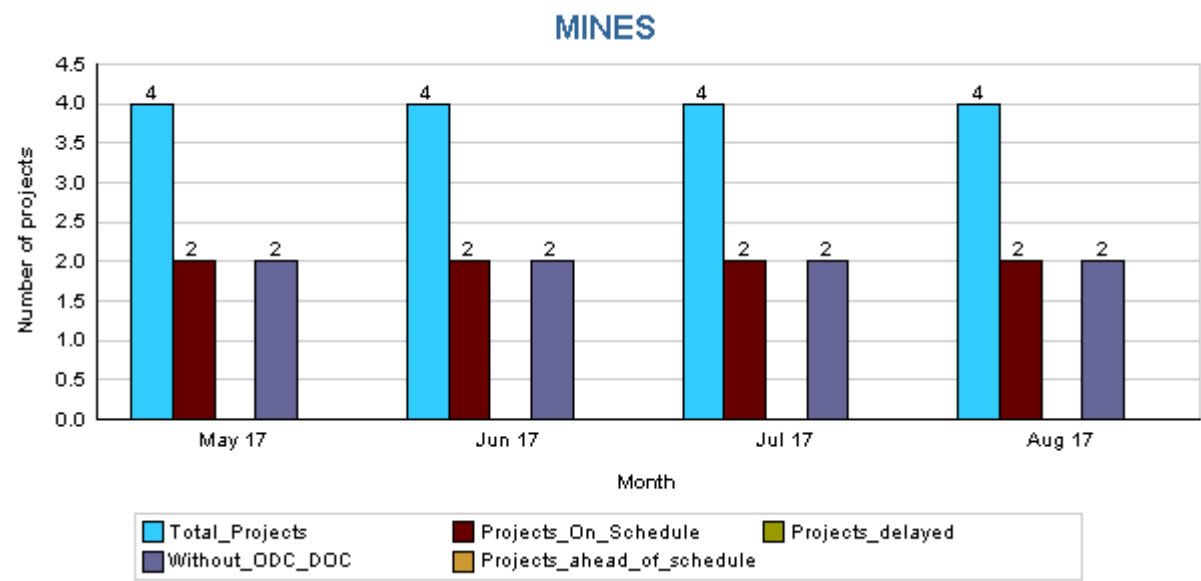


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

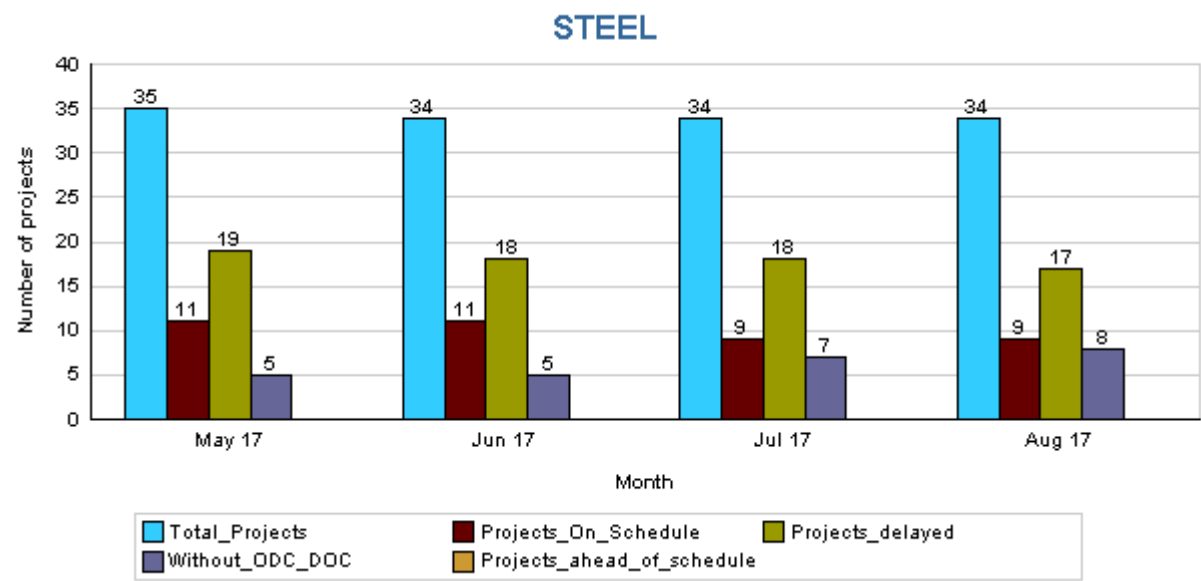


Break-up of 17 Delayed projects in August 2017

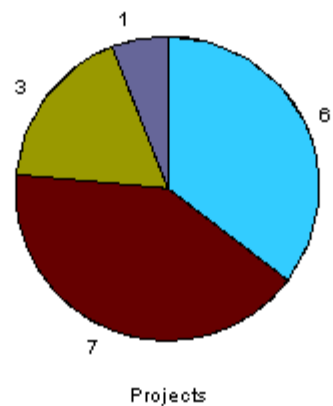


Delay in Months

Delay in Months	Count
1-12	6
13-24	7
25-60	3
60 and Above	1

Graphical Presentation of All Projects w.r.t. Original Schedule

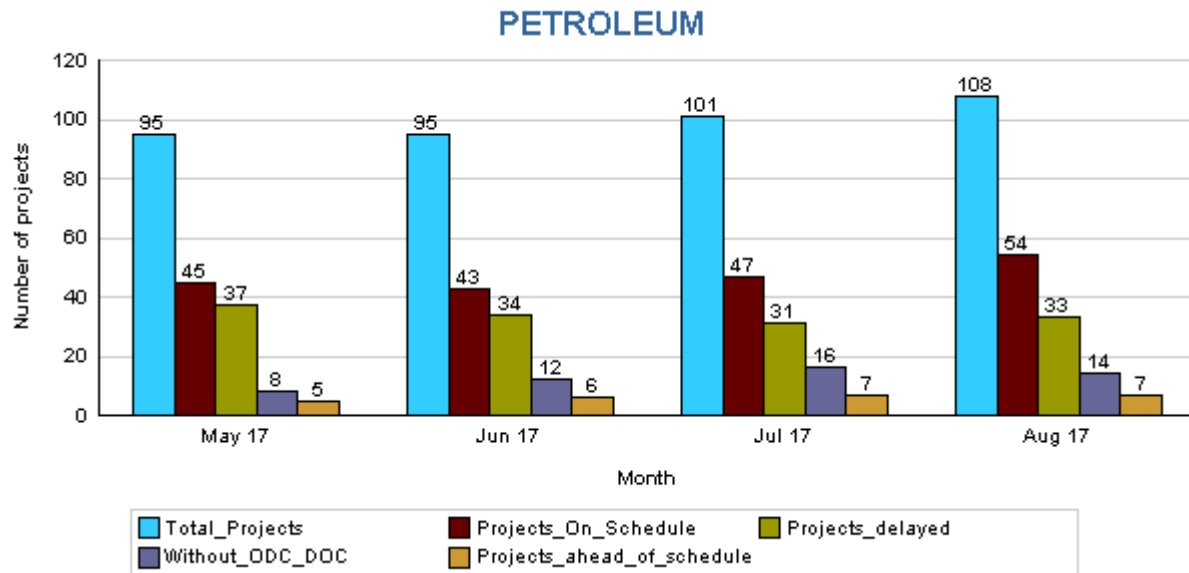


Break-up of 33 Delayed projects in August 2017

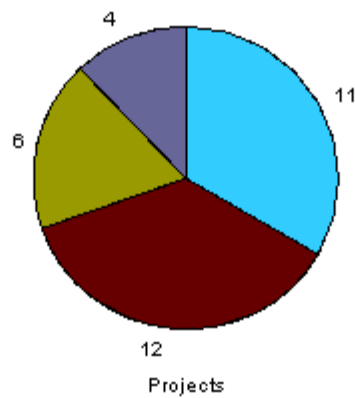


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

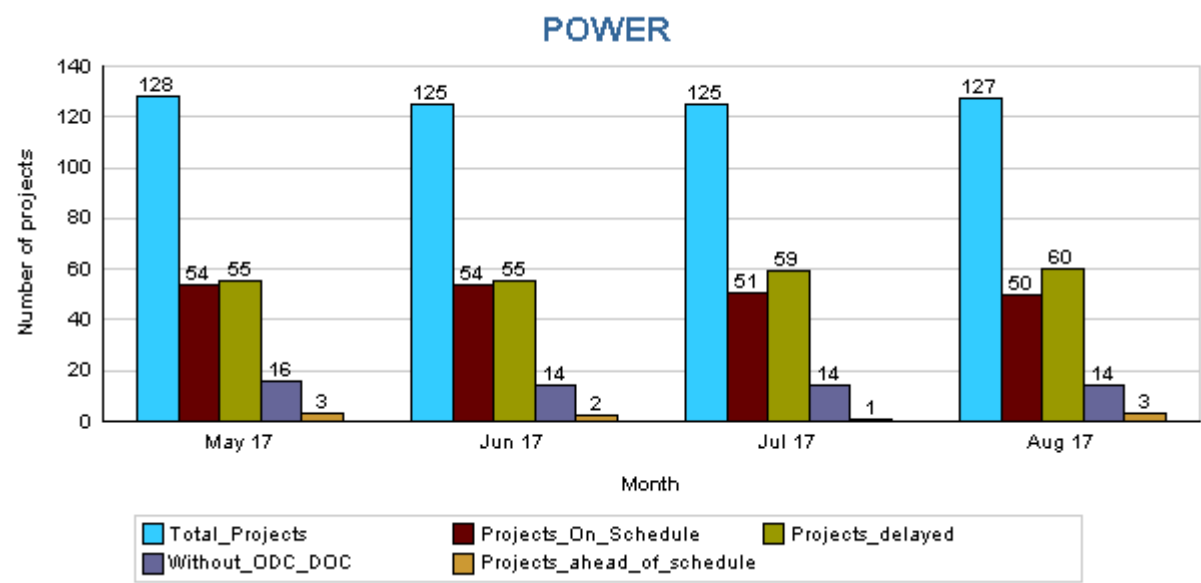


Break-up of 60 Delayed projects in August 2017

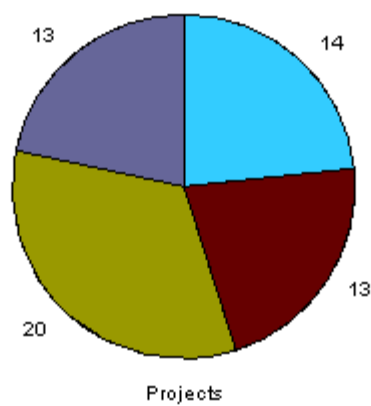


Delay in Months

1-12	13-24	25-60	60 and Above
------	-------	-------	--------------


Graphical Presentation of All Projects w.r.t. Original Schedule

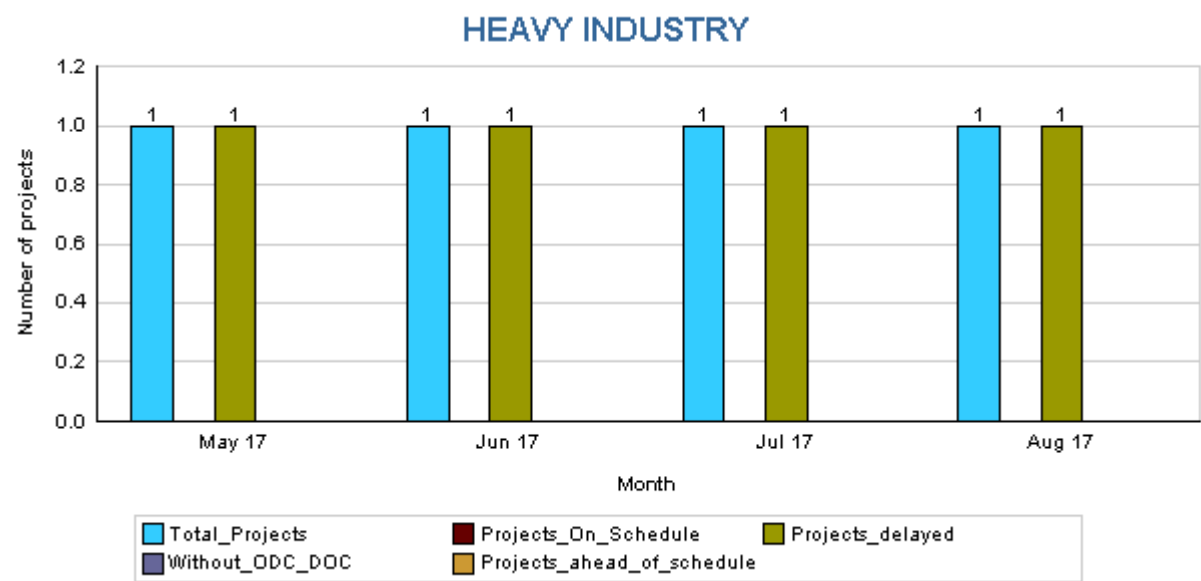


Break-up of 1 Delayed projects in August 2017




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

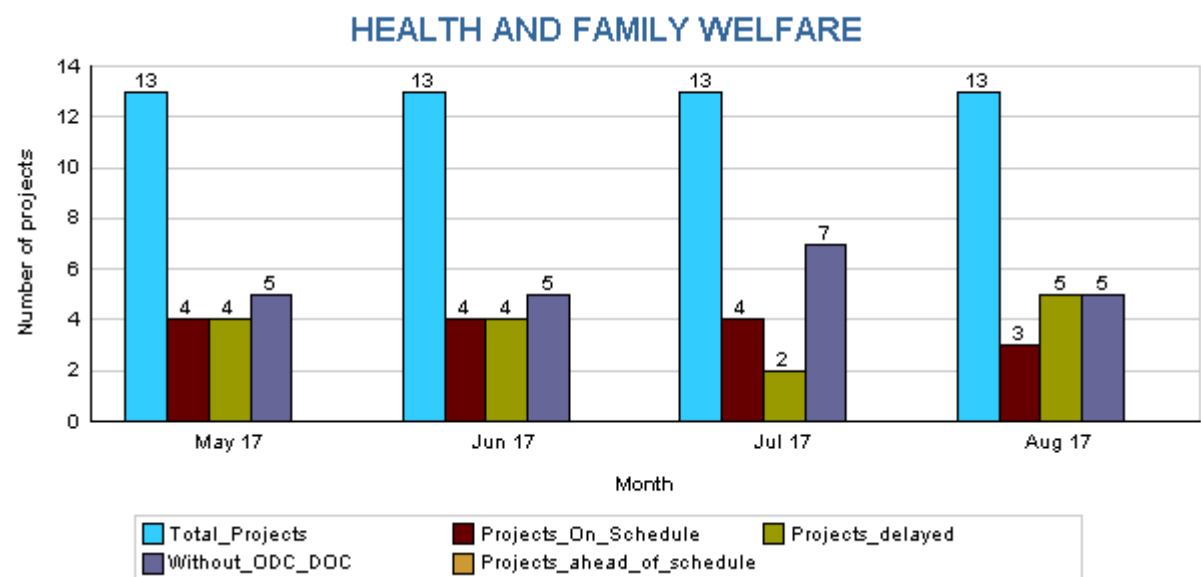


Break-up of 5 Delayed projects in August 2017

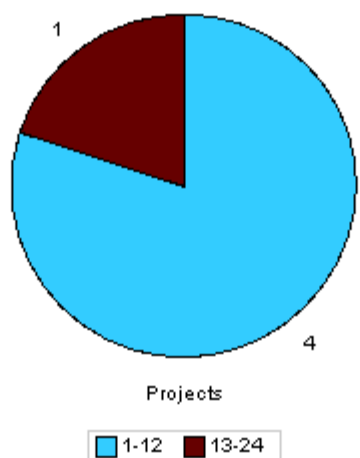


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

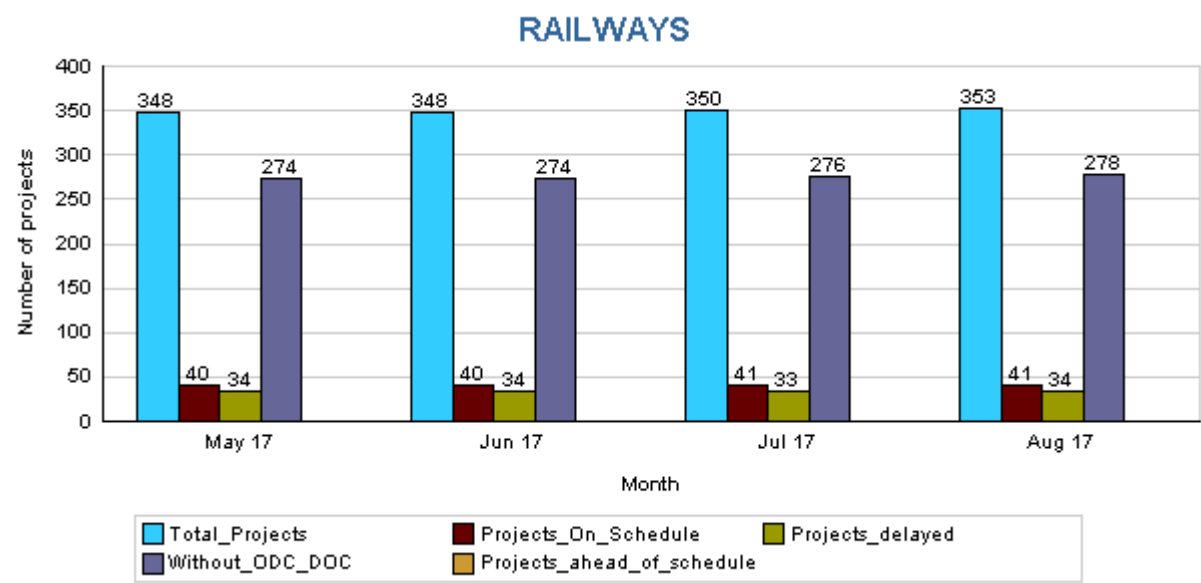


Break-up of 34 Delayed projects in August 2017

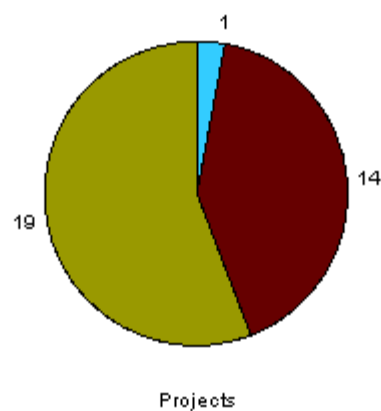


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

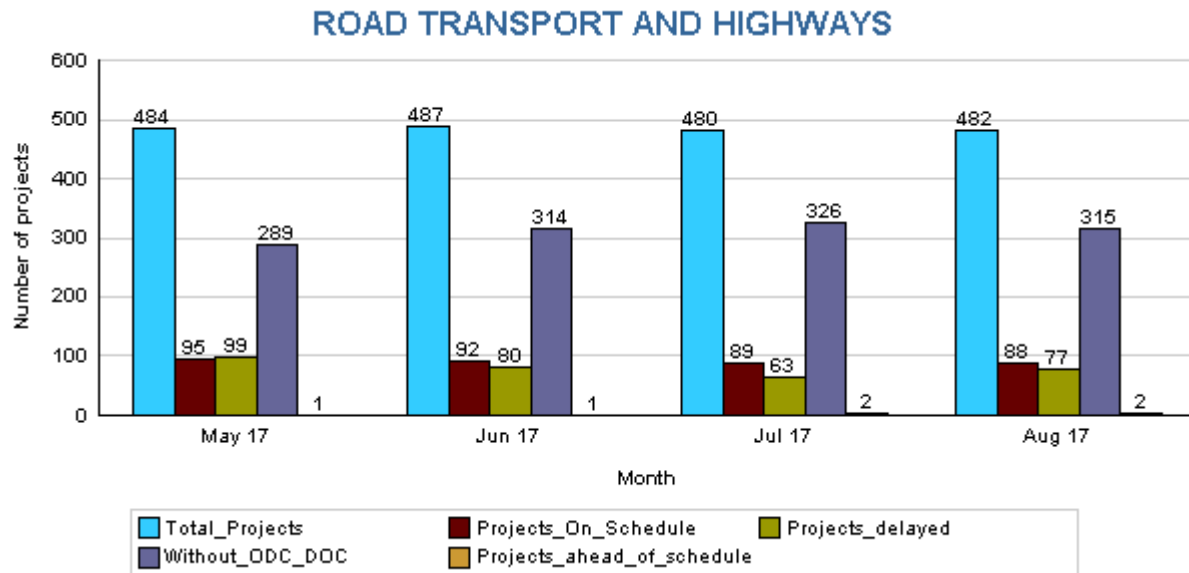


Break-up of 77 Delayed projects in August 2017

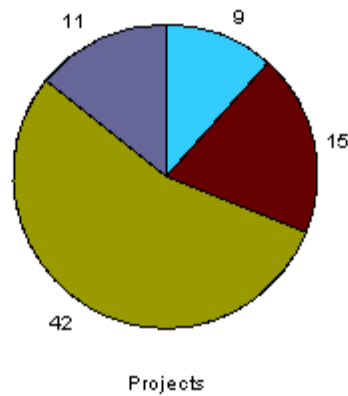


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

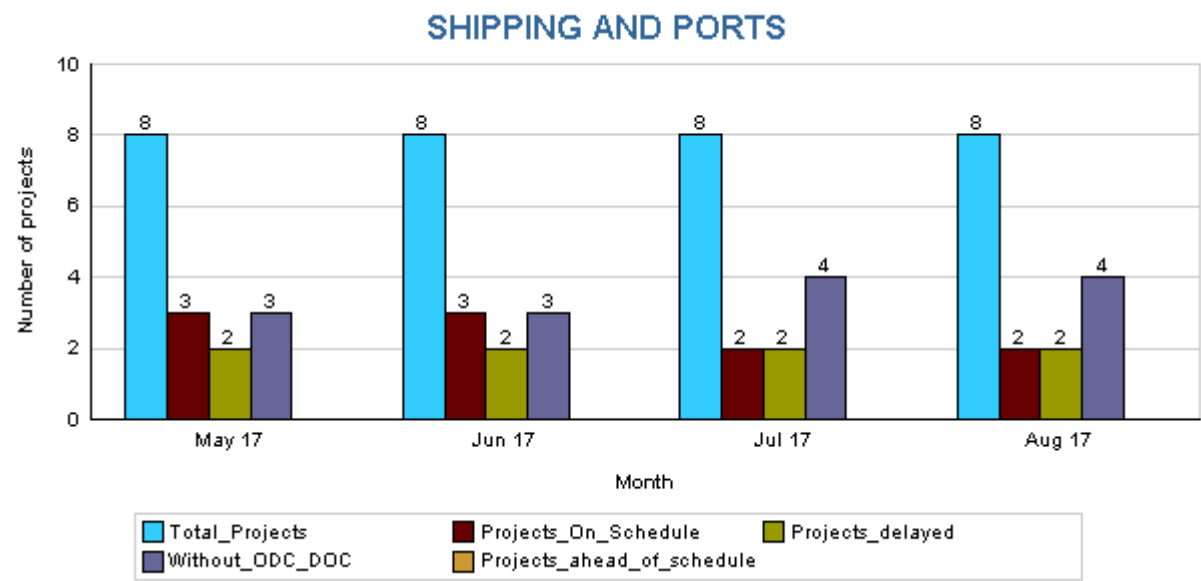


Break-up of 2 Delayed projects in August 2017

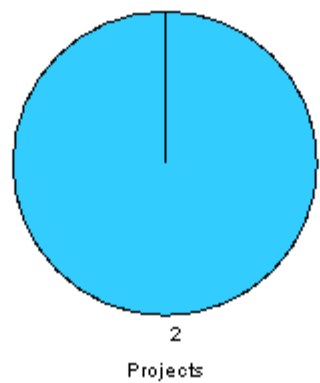


Delay in Months

60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

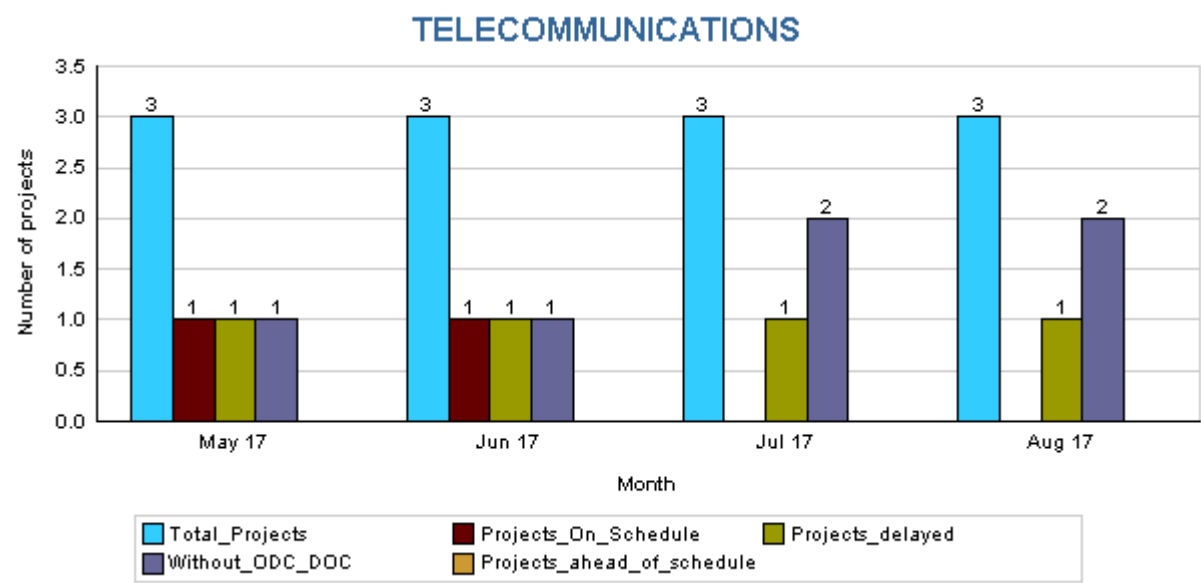


Break-up of 1 Delayed projects in August 2017

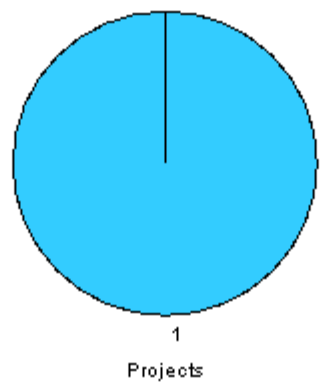


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

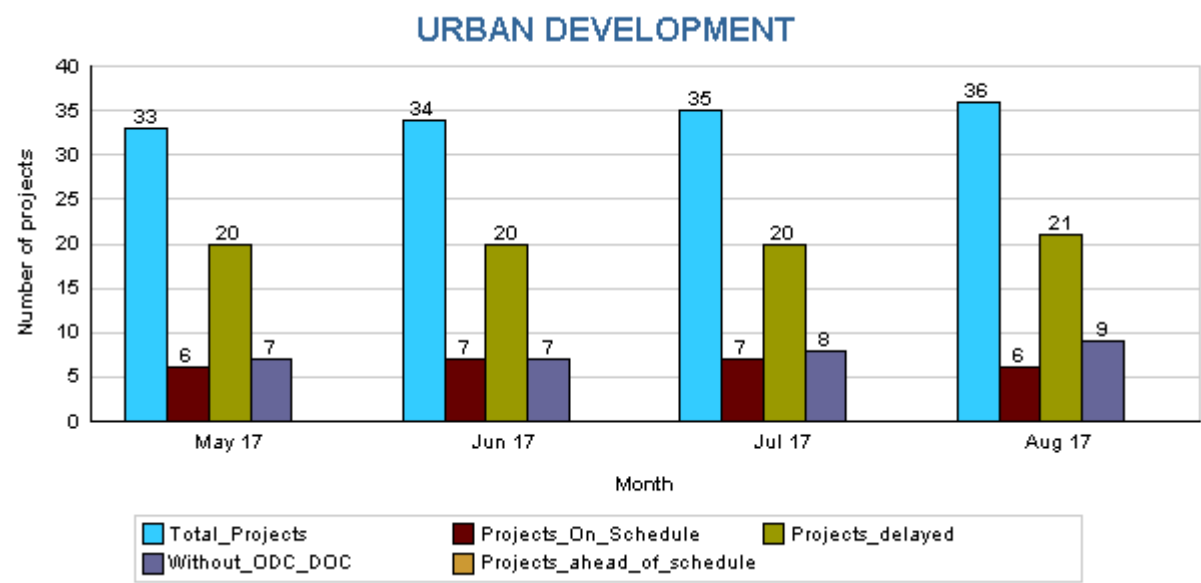


Break-up of 21 Delayed projects in August 2017

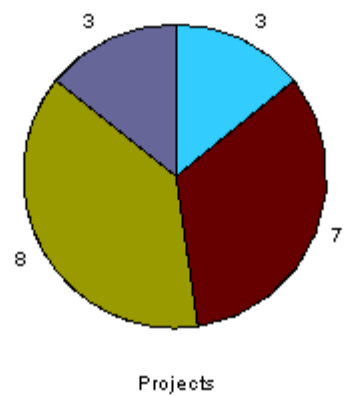

Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

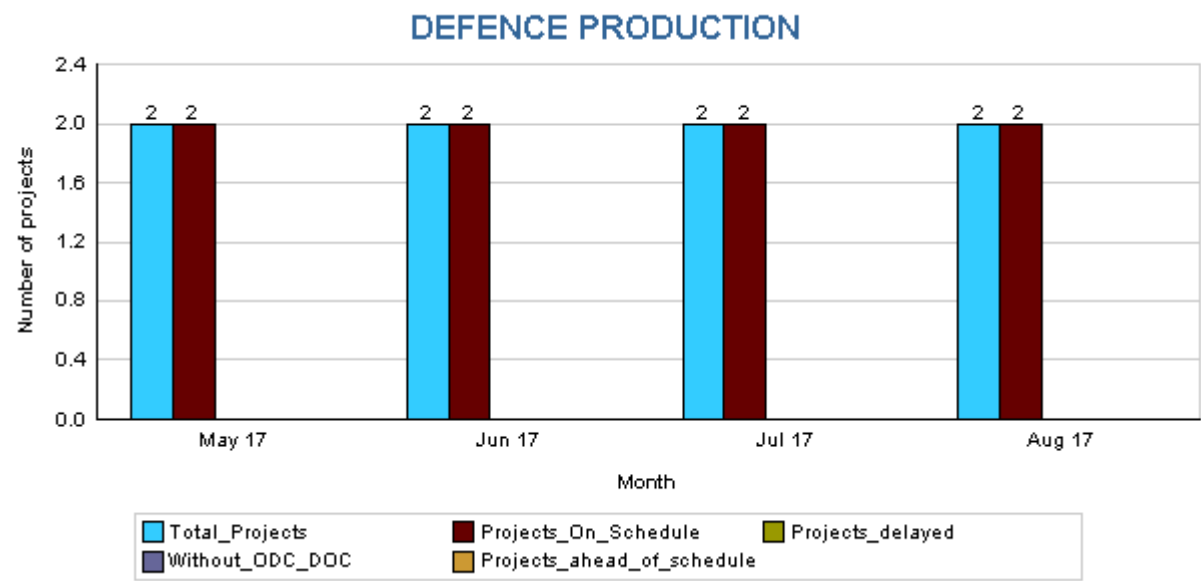

Delay in Months

TABLE-29

<u>Sector wise analysis of projects</u> Rs.150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	404,42.00	52,241.00	46,316.55
CIVIL AVIATION	3	959.68	9,59.68	1,312.86	814.48
COAL	92	88,124.99	882,48.46	88,310.36	21,040.79
FERTILISERS	2	680.64	6,92.29	703.44	466.62
MINES	4	6,773.63	67,73.63	6,773.63	372.63
STEEL	34	57,349.49	577,30.46	57,563.17	38,300.26
PETROLEUM	108	2,08,215.16	2,111,20.11	2,09,608.54	67,811.31
POWER	127	3,44,032.76	3,781,54.11	3,97,114.95	2,30,735.18
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	13	3,637.08	36,37.08	3,649.38	1,751.45
RAILWAYS	353	3,54,063.17	3,581,01.75	4,46,938.49	1,16,071.08
ROAD TRANSPORT AND HIGHWAYS	482	3,17,373.88	3,179,47.90	3,23,746.08	89,417.90
SHIPPING AND PORTS	8	4,117.75	41,31.25	5,085.02	1,875.38
TELECOMMUNICATIONS	3	15,863.43	158,63.43	15,763.43	253.90
URBAN DEVELOPMENT	36	1,45,945.23	1,592,15.64	1,57,932.60	71,466.44
DEFENCE PRODUCTION	2	453.64	4,54.00	469.04	51.37
Grand total	1272	15,89,750.53	16,45,189.79	17,71,039.29	6,89,034.34

TABLE-30

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT , G	10/2009	11,459.00 -	11,459.00	10,443.00	12/2015 11/2016	11/2019	47(O) 36(R)	45/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN , G	10/2009	12,320.00 -	12,320.00	8,074.00	12/2016 03/2017	12/2020	48(O) 45(R)	33/68
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU , G	12/2001	13,171.00 -	22,462.00	22,340.00	12/2008 -	03/2017	-	102/102
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU , G	09/2003	3,492.00 -	6,000.00	5,459.55	09/2010 09/2016	10/2017	85(O) 13(R)	81/87
	Total		40,442.00 -	52,241.00	46,316.55				261/327
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS , G	10/2013	314.61 -	441.33	24.13	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA , G	05/2010	335.61 -	318.00	305.59	05/2012 -	-	-	0/0
7	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM , G	01/2009	309.46 -	553.53	484.76	01/2011 09/2017	09/2017	80(O) 0(R)	0/0
	Total		959.68 -	1,312.86	814.48				0/0
	<u>COAL</u>								
8	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH , G	06/2010	11,816.40 -	11,816.40	2,430.17	03/2023 -	03/2023	0(O) -	11/16
9	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH , G	08/2013	7,612.33 -	7,612.33	1,264.95	03/2023 -	03/2023	0(O) -	2/18
10	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH , G	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023	0(O) -	1/10
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH , G	09/2008	152.43 459.49	459.49	78.39	03/2015 03/2020	03/2020	60(O) 0(R)	2/7
12	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH , G	07/2008	178.44 -	178.44	5.12	03/2014 -	03/2020	72(O) -	1/7
13	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH , G	12/2009	321.50 -	321.50	198.19	03/2014 -	03/2018	48(O) -	0/2
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH , G	11/2009	198.59 -	198.59	169.38	03/2016 -	03/2018	24(O) -	5/7
15	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH , G	04/2012	258.56 -	258.56	149.93	03/2016 -	03/2018	24(O) -	3/6
16	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH , G	12/2013	610.63 -	610.63	29.01	03/2022 -	03/2022	0(O) -	1/7
17	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH , G	05/2014	164.49 -	164.49	45.89	03/2020 -	03/2020	0(O) -	3/6
18	AMERA OC RCE - [N06000123]SECL,CHHATISGARH , G	02/2015	335.97 -	335.97	48.69	03/2018 -	03/2018	0(O) -	1/5

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
19	AMGAON OPENCAS T PROJECT RCE - [N06000135]SECL,CHHATISGARH , G	07/2015	316.10 -	316.10	28.62	03/2020 -	03/2020	0(O) -	0/5
20	DURGAPUR OPENCAS T PROJECT - [N06000136]SECL,CHHATISGARH , G	02/2015	916.24 -	916.24	.71	03/2023 -	03/2023	0(O) -	1/9
21	MADANNAGAR OPENCAS T PROJECT - [N06000140]SECL,CHHATISGARH , G	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/2
22	VIJAY WEST OPENCAS T PROJECT - [N06000158]SECL,CHHATISGARH , G	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/0
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , G	08/2008	706.40 -	706.40	116.67	07/2012 03/2017	03/2021	104(O) 48(R)	2/3
24	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND , G	09/2009	153.82 -	153.82	125.01	03/2014 -	12/2017	45(O) -	4/6
25	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND , G	08/2007	163.51 -	163.51	93.27	03/2011 -	03/2020	108(O) -	2/2
26	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND , G	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84(O) -	2/2
27	PU RNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND , G	07/2008	210.98 -	210.98	205.72	03/2013 -	03/2018	60(O) -	3/3
28	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND , G	08/2008	264.68 -	264.68	153.14	03/2012 -	03/2019	84(O) -	2/3
29	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND , G	12/2009	510.85 -	510.85	341.10	03/2016 -	03/2018	24(O) -	2/3
30	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND , G	06/2009	162.46 -	162.46	80.62	03/2014 -	03/2019	60(O) -	2/2
31	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , G	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
32	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , G	08/2011	1,230.27 -	1,230.27	176.37	04/2015 -	04/2019	48(O) -	1/6
33	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND , G	02/2012	858.11 -	858.11	175.42	03/2020 -	03/2020	0(O) -	4/4
34	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , G	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0(O) -	0/2
35	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , G	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
36	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND , G	08/2010	289.45 -	289.45	151.66	05/2014 -	10/2017	41(O) -	0/8
37	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND , G	10/2012	269.82 -	269.82	144.38	04/2014 -	10/2017	42(O) -	0/10
38	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , G	10/2015	359.69 -	359.69	7.46	03/2022 -	03/2022	0(O) -	0/21
39	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , G	10/2007	259.40 486.57	486.57	294.63	03/2012 03/2018	03/2018	72(O) 0(R)	1/3
40	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH , G	08/2015	1,186.64 -	1,186.64	52.71	03/2023 -	03/2023	0(O) -	3/10
41	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , G	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
42	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , G	12/2014	357.80 -	357.80	114.37	03/2021 -	03/2021	0(O) -	1/7
43	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , G	12/2014	371.04 -	371.04	34.26	03/2021 -	03/2021	0(O) -	1/6

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
44	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , G	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	0/6
45	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH , G	10/2015	488.33 -	488.33	1.13	03/2023 -	03/2023	0(O) -	0/3
46	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH , G	03/2016	869.44 -	869.44	109.31	03/2021 -	03/2021	0(O) -	1/2
47	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH , G	07/2016	409.87 -	409.87	9.72	03/2022 -	03/2022	0(O) -	0/0
48	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , G	09/2014	441.82 -	441.82	174.29	03/2020 -	03/2020	0(O) -	6/11
49	DINESH OCP - [N06000118]WCL,MAHARASHTRA , G	11/2014	611.16 -	611.16	360.21	03/2020 -	03/2020	0(O) -	2/8
50	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , G	09/2014	266.23 -	266.23	138.36	03/2021 -	03/2021	0(O) -	6/12
51	GOKUL - [N06000120]WCL,MAHARASHTRA , G	11/2014	267.67 -	267.67	203.98	03/2018 -	03/2018	0(O) -	6/7
52	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA , G	02/2015	187.94 -	187.94	72.23	03/2023 -	03/2023	0(O) -	6/11
53	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , G	05/2015	295.56 -	295.56	84.95	03/2019 -	03/2019	0(O) -	10/13
54	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , G	06/2015	205.49 -	205.49	65.88	03/2020 -	03/2020	0(O) -	5/10
55	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , G	06/2015	483.69 -	483.69	71.98	03/2021 -	03/2021	0(O) -	2/6
56	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , G	08/2015	727.28 -	727.28	228.99	03/2025 -	03/2025	0(O) -	3/13
57	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , G	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
58	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , G	11/2015	277.65 -	277.65	.13	03/2021 -	03/2021	0(O) -	2/6
59	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , G	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020	0(O) -	2/6
60	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA , G	02/2016	198.68 -	198.68	30.32	03/2019 -	03/2019	0(O) -	2/9
61	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA , G	02/2016	304.52 -	304.52	124.00	03/2019 -	03/2019	0(O) -	1/8
62	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE , G	08/2016	319.76 -	319.76	-	03/2022 -	03/2022	0(O) -	0/3
63	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE , G	09/2016	458.07 -	458.07	-	03/2022 -	03/2022	0(O) -	0/12
64	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE , G	02/2017	328.00 -	328.00	44.86	03/2021 -	03/2021	0(O) -	0/6
65	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA , G	01/2005	302.96 -	302.96	329.80	03/2010 -	03/2018	96(O) -	9/10
66	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , G	12/2007	490.10 -	490.10	272.87	03/2017 -	05/2018	14(O) -	11/11
67	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , G	12/2007	457.77 -	457.77	402.43	03/2013 -	11/2018	68(O) -	8/9
68	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , G	12/2007	172.08 -	172.08	190.68	03/2010 -	03/2019	108(O) -	3/4
69	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , G	08/2008	207.28 -	207.28	215.92	03/2012 -	03/2019	84(O) -	3/5

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
70	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , G	11/2008	479.53 -	479.53	218.28	03/2013 -	03/2019	72(O) -	5/8
71	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , G	05/2014	479.15 -	479.15	21.75	03/2019 -	03/2019	0(O) -	2/9
72	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , G	05/2014	3,756.36 -	3,756.36	673.05	03/2026 -	03/2026	0(O) -	3/15
73	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , G	05/2014	337.66 -	337.66	24.67	03/2019 -	03/2019	0(O) -	3/6
74	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , G	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	2/5
75	GARJANBAHAL OCP - [N06000117]MCL,ODISHA , G	11/2014	1,375.38 -	1,375.38	351.84	03/2021 -	03/2021	0(O) -	1/9
76	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	5.65	09/2019 -	09/2019	0(O) -	0/0
77	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	167.04	12/2019 -	12/2019	0(O) -	0/0
78	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , G	06/2011	5,907.11 -	5,907.11	4,659.77	12/2015 04/2018	04/2018	28(O) 0(R)	16/35
79	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU , G	04/2012	364.75 -	364.75	333.05	10/2014 06/2017	07/2017	-	10/10
80	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU , G	04/2013	1,458.17 709.06	709.06	258.90	06/2015 09/2019	09/2019	51(O) 0(R)	3/7
81	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU , G	05/2016	687.28 -	687.28	681.42	06/2017 -	08/2017	2(O) -	0/0
82	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , G	10/2006	249.03 448.86	448.86	157.97	03/2012 -	03/2019	84(O) -	32/42
83	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , G	12/2008	453.63 -	453.63	-	12/2012 -	-	-	11/44
84	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , G	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132(O) -	0/2
85	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , G	03/2010	209.78 -	209.78	120.55	03/2015 -	03/2018	36(O) -	29/31
86	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , G	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72(O) -	5/6
87	KISTARAM OCP - [N06000089]SCCL,TELANGANA , G	11/2010	242.29 164.04	164.04	.09	03/2015 -	03/2020	60(O) -	0/5
88	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , G	07/2011	162.76 349.28	349.28	1.31	03/2015 -	03/2020	60(O) -	4/29
89	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , G	07/2011	447.06 -	437.51	259.34	03/2015 -	03/2021	72(O) -	5/13
90	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , G	06/2012	365.01 -	365.01	57.64	06/2015 -	03/2018	33(O) -	27/36
91	KALYANKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , G	07/2012	417.33 417.33	417.33	43.97	07/2016 -	03/2020	44(O) -	19/28
92	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , G	11/2012	430.45 415.37	415.37	136.75	03/2016 -	03/2018	24(O) -	33/39
93	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA , G	05/2015	397.09 442.42	442.42	19.94	03/2019 -	03/2019	0(O) -	6/18
94	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12(O) -	0/9

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
95	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA , G	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	1/17
96	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH , G	06/2011	1,131.28 -	1,131.28	427.59	03/2018 -	03/2018	0(O) -	6/10
97	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH , G	07/2016	17,237.00 -	17,237.80	1,107.67	11/2021 -	11/2021	0(O) -	0/0
98	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL , G	11/2015	602.86 -	602.86	263.42	03/2022 -	03/2022	0(O) -	6/12
99	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL , G	08/2012	1,055.05 -	1,055.05	298.37	03/2018 -	09/2018	6(O) -	7/15
	Total		88,124.99 -	88,310.36	21,040.79				392/886
	<u>FERTILISERS</u>								
100	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA , G	10/2014	197.79 209.44	209.44	82.72	11/2016 04/2019	04/2019	29(O) 0(R)	0/0
101	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA , G	02/2016	482.85 -	494.00	383.90	12/2017 -	12/2017	0(O) -	0/1
	Total		680.64 -	703.44	466.62				0/1
	<u>MINES</u>								
102	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA , Private	12/2015	355.13 -	355.13	94.63	11/2016 -	-	-	1/1
103	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA , G	12/2014	5,540.00 -	5,540.00	.31	04/2021 -	04/2021	0(O) -	1/1
104	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA , G	05/2016	534.00 -	534.00	157.34	01/2020 -	01/2020	0(O) -	1/1
105	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 -	344.50	120.35	11/2016 -	-	-	1/1
	Total		6,773.63 -	6,773.63	372.63				4/4
	<u>STEEL</u>								
106	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH , G	07/2011	974.76 -	974.76	510.53	07/2016 -	10/2017	15(O) -	1/1
107	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH , G	07/2011	877.73 -	877.73	745.11	07/2015 -	09/2017	26(O) -	2/2
108	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , G	12/2009	343.00 -	488.40	217.87	10/2016 -	03/2018	17(O) -	0/0
109	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH , G	12/2009	280.00 -	280.00	154.55	09/2016 -	09/2017	12(O) -	1/1
110	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH , G	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
111	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH , G	12/2011	2,858.00 -	2,500.00	564.35	12/2017 -	06/2018	6(O) -	0/0
112	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH , G	08/2015	320.66 -	320.66	11.17	08/2018 -	08/2018	0(O) -	0/0
113	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH , G	07/2015	465.85 -	465.85	20.85	07/2018 -	07/2018	0(O) -	0/0
114	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR , G	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
115	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , G	08/2010	17,265.00 -	17,265.00	17,892.75	03/2013 -	10/2017	55(O) -	35/38
116	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , G	04/2014	188.93 -	188.93	114.04	04/2015 -	-	-	3/5
117	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH , G	01/2010	15,525.00 -	15,525.00	12,559.30	05/2015 12/2017	12/2017	31(O) 0(R)	54/86
118	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH , G	11/2015	818.00 -	818.00	25.74	06/2020 -	06/2020	0(O) -	4/12
119	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT , G	01/2013	175.00 -	175.00	1.83	- -	12/2017	- -	0/0
120	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , G	10/2013	245.67 -	245.67	195.64	05/2016 -	10/2017	17(O) -	2/3
121	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND , G	03/2015	255.19 -	255.19	156.39	03/2018 -	03/2018	0(O) -	1/2
122	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , G	03/2015	1,034.01 -	1,034.01	184.28	10/2017 -	07/2018	9(O) -	0/2
123	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND , G	05/2015	1,154.18 -	1,154.18	402.94	12/2017 -	05/2018	5(O) -	1/2
124	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , G	02/2014	4,749.00 -	4,749.00	64.65	09/2017 -	09/2017	0(O) -	0/0
125	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , G	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21(O) -	0/0
126	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , G	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
127	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , G	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0
128	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , G	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
129	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND , G	11/2016	262.87 -	262.87	35.71	06/2019 -	06/2019	0(O) -	0/1
130	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA , G	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
131	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , G	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
132	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA , G	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0
133	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA , G	04/2015	3,127.30 -	3,127.30	996.15	04/2018 -	02/2019	10(O) -	1/3
134	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN , G	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17(O) -	0/0
135	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA , G	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
136	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA , G	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12(O) -	0/0
137	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA , G	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
138	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH , G	04/2014	1,682.85 -	1,682.85	41.97	09/2018 -	09/2018	0(O) -	0/0
139	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
	Total		57,349.49 -	57,563.17	38,300.26				105/158
	<u>PETROLEUM</u>								
140	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH , G	07/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020	0(O) -	0/0
141	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH , G	09/2016	407.00 -	407.00	25.71	09/2019 -	09/2019	0(O) -	9/27
142	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH , G	03/2016	34,012.00 -	34,012.00	252.02	06/2020 -	06/2020	0(O) -	0/0
143	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH , G	01/2015	342.00 -	342.00	-	03/2021 -	03/2021	0(O) -	0/0
144	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH , G	07/2014	247.00 -	247.00	-	03/2021 -	03/2021	0(O) -	0/0
145	FIELD DEVELOPMENT OF NLP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH , G	04/2017	420.76 -	420.76	-	09/2018 -	09/2018	0(O) -	0/0
146	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH , G	01/2016	247.52 -	247.52	53.32	02/2019 -	12/2018	-2(O) -	2/10
147	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM , G	03/2009	2,465.15 -	2,378.89	1,984.66	03/2013 09/2018	09/2018	66(O) 0(R)	5/15
148	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM , G	06/2010	202.94 341.70	330.35	2.11	01/2014 11/2019	11/2019	70(O) 0(R)	0/2

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
149	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM , G	02/2014	163.88 -	163.88	82.45	07/2016 -	-	-	6/6
150	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM , G	03/2009	228.64 -	209.19	146.86	12/2016 -	03/2018	15(O) -	0/0
151	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018	0(O) -	46/61
152	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM , G	06/2012	150.00 -	259.93	234.99	07/2014 -	09/2017	38(O) -	5/12
153	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM , G	06/2016	423.00 -	423.00	79.24	08/2019 -	08/2019	0(O) -	1/13
154	INDMAX PROJECT AT BONGAIGON REFINERY - [N16000243]IOCL,ASSAM , G	02/2016	2,582.00 -	2,582.00	191.47	11/2019 -	11/2019	0(O) -	0/0
155	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM , G	07/2016	249.85 250.00	244.70	-	05/2020 -	05/2020	0(O) -	0/0
156	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM , G	09/2012	871.35 -	1,200.00	957.00	03/2015 -	-	-	0/5
157	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR , G	07/2015	822.66 -	822.66	216.42	11/2018 -	11/2018	0(O) -	0/0
158	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR , G	05/2016	664.00 -	664.00	98.67	12/2020 -	02/2020	-10(O) -	0/0
159	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR , G	09/2015	324.00 -	324.00	1.35	06/2020 -	06/2020	0(O) -	0/0
160	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH , G	01/2011	141.86 222.81	222.81	174.37	09/2016 02/2017	02/2017	-	12/12
161	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI , G	08/2014	6,086.08 -	5,479.75	2,033.62	05/2019 10/2019	10/2019	5(O) 0(R)	0/0
162	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT , G	09/2011	202.25 -	160.16	105.43	07/2016 06/2018	06/2018	23(O) 0(R)	5/12
163	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT , G	05/2015	1,671.22 567.22	567.22	347.69	11/2019 12/2018	12/2018	-11(O) 0(R)	0/0
164	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT , Central Sector Projects	11/2015	500.00 -	435.00	368.24	03/2017 -	-	-	0/1
165	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	135.88	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
166	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT , G	07/2014	199.95 -	199.95	119.90	03/2018 -	03/2018	0(O) -	15/22
167	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT , G	04/2016	327.78 -	327.78	13.62	04/2018 -	04/2018	0(O) -	14/20
168	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT , G	02/2016	931.00 -	931.00	377.28	07/2017 -	02/2018	7(O) -	0/0
169	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT , G	02/2017	1,162.56 -	1,162.56	159.74	03/2026 -	03/2026	0(O) -	0/0
170	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL,HIMACHAL PRADESH , G	02/2016	356.00 -	356.00	57.85	05/2019 -	12/2018	-5(O) -	1/13
171	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH , G	02/2016	151.00 -	151.00	28.42	09/2019 -	09/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
172	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , G	04/2011	191.96 -	191.96	160.94	05/2015 06/2017	06/2017	-	8/12
173	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND , G	12/2015	658.62 910.23	910.23	-	03/2023 03/2022	03/2022	-12(O) 0(R)	0/0
174	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA , G	02/2012	666.00 838.08	768.25	606.13	11/2015 11/2016	10/2016	-	29/29
175	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA , G	01/2006	993.00 -	1,693.00	1,534.28	01/2012 -	-	-	0/0
176	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	468.00	02/2020 -	02/2020	0(O) -	0/0
177	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA , G	05/2015	224.00 207.00	207.25	33.54	04/2019 -	04/2019	0(O) -	4/8
178	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA , G	10/2015	135.00 171.00	170.70	57.41	03/2019 -	03/2019	0(O) -	3/11
179	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA , G	09/2016	1,810.00 1,810.00	1,810.00	43.02	12/2019 -	12/2019	0(O) -	6/9
180	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA , G	03/2012	16,504.00 -	16,504.00	14,973.16	03/2017 -	-	-	15/16
181	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA , G	10/2015	607.06 714.25	714.25	259.80	10/2017 -	03/2019	17(O) -	35/52
182	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA , G	02/2015	184.00 -	184.00	76.29	12/2017 -	12/2017	0(O) -	0/10
183	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA , G	11/2014	4,588.29 5,245.96	4,588.29	840.60	08/2018 05/2019	05/2019	9(O) 0(R)	0/20
184	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA , G	02/2016	3,313.00 -	3,313.00	59.40	02/2020 -	02/2020	0(O) -	0/0
185	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA , G	05/2015	337.06 -	337.06	12.27	08/2018 -	08/2018	0(O) -	0/0
186	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	173.28	126.24	01/2017 03/2018	03/2018	14(O) 0(R)	0/0
187	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA , G	12/2009	1,584.00 -	1,584.00	1,355.45	03/2017 -	-	-	12/12
188	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA , G	03/2011	861.79 1,256.72	1,256.72	1,158.78	05/2013 12/2017	12/2017	55(O) 0(R)	1/5
189	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA , G	12/2011	2,059.63 -	2,665.65	1,625.39	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
190	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA , G	03/2012	2,592.17 -	2,592.17	1,992.86	05/2014 05/2018	05/2018	48(O) 0(R)	0/21
191	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA , G	06/2014	5,706.47 5,813.25	5,813.25	5,554.21	05/2017 05/2018	05/2018	12(O) 0(R)	7/16
192	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA , G	11/2014	6,068.80 6,068.80	5,296.93	3,995.37	04/2019 03/2019	03/2019	-1(O) 0(R)	0/0
193	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA , G	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018	12(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
194	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA , G	08/2015	2,818.88 -	2,818.88	180.36	03/2019 05/2020	05/2020	14(O) 0(R)	0/0
195	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA , G	05/2015	1,714.00 -	1,417.00	1,046.60	06/2017 -	-	-	0/21
196	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	3,961.54	3,216.59	12/2017 03/2019	03/2019	15(O) 0(R)	0/0
197	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	580.31	04/2018 04/2018	04/2018	0(O) 0(R)	0/0
198	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA , G	05/2016	1,945.00 -	1,945.00	8.38	08/2021 -	08/2021	0(O) -	0/0
199	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA , G	02/2016	554.00 -	554.00	21.03	02/2020 -	02/2020	0(O) -	0/0
200	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA , G	04/2013	449.58 -	449.58	95.55	12/2019 -	12/2019	0(O) -	0/0
201	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA , G	05/2015	193.40 -	193.40	7.03	01/2019 -	01/2019	0(O) -	0/0
202	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA , G	05/2016	212.00 -	212.00	.05	01/2021 -	01/2021	0(O) -	0/0
203	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA , G	05/2016	348.00 -	348.00	.05	01/2021 -	01/2021	0(O) -	0/0
204	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA , G	05/2016	261.00 -	261.00	.05	01/2021 -	01/2021	0(O) -	0/0
205	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	170.15	03/2020 -	03/2020	0(O) -	0/0
206	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE , G	07/2009	3,957.00 -	3,397.00	1,143.75	01/2013 -	12/2018	71(O) -	24/39
207	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE , G	06/2007	736.65 -	571.47	535.39	09/2011 06/2019	06/2019	93(O) 0(R)	0/0
208	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE , G	08/2009	1,793.00 -	1,793.00	1,786.89	12/2016 -	-	-	7/7
209	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE , G	04/2012	600.17 -	600.17	576.09	12/2014 03/2018	03/2018	39(O) 0(R)	0/8
210	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE , G	02/2011	913.00 1,330.00	1,330.00	923.87	06/2018 -	06/2018	0(O) -	0/0
211	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE , G	08/2011	586.00 -	586.00	440.20	08/2015 03/2017	03/2017	-	11/11
212	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE , G	12/2009	309.81 723.40	723.40	372.36	10/2014 03/2018	03/2018	41(O) 0(R)	29/40

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
213	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE , G	07/2011	352.56 -	439.03	126.43	03/2017 -	11/2018	20(O) -	0/0
214	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE , G	05/2013	4,124.35 4,259.59	5,637.00	3,701.21	04/2016 12/2017	12/2017	20(O) 0(R)	0/3
215	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , G	01/2015	1,823.00 -	1,823.00	15.07	12/2020 -	12/2020	0(O) -	0/0
216	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE , G	01/2015	2,321.00 -	2,321.00	51.38	12/2020 -	08/2020	-4(O) -	0/0
217	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE , G	02/2015	890.00 -	887.00	154.97	10/2019 -	10/2019	0(O) -	0/0
218	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE , G	01/2015	690.00 -	690.00	122.14	07/2018 06/2020	06/2020	23(O) 0(R)	10/36
219	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE , G	09/2016	1,879.00 -	1,879.00	148.67	06/2020 -	06/2020	0(O) -	7/24
220	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE , G	11/2016	230.00 -	230.00	11.01	02/2019 -	02/2019	0(O) -	2/13
221	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE , G	05/2016	406.00 -	406.00	.50	10/2020 -	10/2020	0(O) -	0/0
222	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE , G	09/2016	571.66 -	571.66	-	12/2019 -	12/2019	0(O) -	0/0
223	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE , G	07/2015	2,881.40 -	2,881.40	4.85	12/2019 -	12/2019	0(O) -	0/0
224	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE , G	03/2017	2,250.00 -	2,250.00	1.93	12/2019 -	12/2019	0(O) -	0/0
225	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE , G	03/2017	3,212.00 -	3,212.00	.10	12/2020 -	12/2020	0(O) -	0/0
226	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA , G	03/2014	3,150.00 -	3,150.00	1,288.55	09/2017 12/2018	12/2018	15(O) 0(R)	5/6
227	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA , G	03/2014	238.50 -	238.50	167.48	03/2017 10/2017	10/2017	7(O) 0(R)	5/6
228	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA , G	03/2017	2,253.00 -	2,253.00	5.71	12/2019 -	12/2019	0(O) -	0/0
229	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA , G	05/2016	429.00 -	429.00	23.07	01/2019 -	01/2019	0(O) -	0/0
230	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	28.87	12/2019 -	12/2019	0(O) -	0/0
231	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN , G	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
232	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU , G	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
233	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU , G	03/2013	3,110.36 -	3,110.36	2,765.42	11/2015 -	10/2017	23(O) -	51/52

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
234	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU , G	05/2015	257.87 -	257.87	117.68	11/2016 -	02/2018	15(O) -	18/22
235	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects	02/2016	367.11 -	367.11	218.14	04/2017 -	11/2017	7(O) -	20/22
236	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU , G	08/2014	393.00 -	393.00	192.61	04/2018 -	04/2018	0(O) -	0/10
237	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU , G	11/2012	678.00 -	678.00	5.08	02/2017 -	-	-	0/0
238	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU , G	11/2015	390.52 -	390.52	67.52	03/2019 -	04/2019	1(O) -	0/0
239	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU , G	05/2016	4,497.00 -	4,497.00	22.20	12/2018 -	12/2018	0(O) -	0/0
240	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA , G	05/2016	215.38 -	215.38	141.75	06/2017 10/2017	10/2017	4(O) 0(R)	0/0
241	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH , G	07/2015	1,427.94 -	1,427.94	365.49	12/2018 -	12/2018	0(O) -	11/20
242	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	20.22	02/2020 -	02/2020	0(O) -	0/0
243	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL , G	03/2014	3,076.00 4,190.00	4,190.00	1,918.07	09/2017 06/2018	06/2018	9(O) 0(R)	6/7
244	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL , G	08/2014	190.45 -	190.45	104.95	09/2017 -	03/2018	6(O) -	0/0
245	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL , G	03/2015	694.00 -	694.00	155.60	10/2018 -	10/2018	0(O) -	0/0
246	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL , G	04/2016	1,021.00 -	1,021.00	6.09	12/2020 -	12/2020	0(O) -	0/0
247	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL , G	03/2017	1,828.00 -	1,828.00	.10	12/2020 -	12/2020	0(O) -	0/0
	Total		2,08,215.16 -	2,09,608.54	67,811.31				447/840
	<u>POWER</u>								
248	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH , G	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	-	2/2
249	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH , G	03/2015	550.06 -	550.06	461.43	03/2018 -	09/2017	-6(O) -	0/3
250	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH , G	01/2016	207.88 -	207.88	74.23	07/2018 -	07/2018	0(O) -	0/0
251	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH , G	09/2003	6,285.33 -	17,435.15	9,435.49	09/2010 -	-	-	0/0
252	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH , G	12/2004	2,496.90 6,179.96	6,179.96	5,808.04	12/2009 03/2018	03/2018	99(O) 0(R)	18/30
253	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH , G	12/2008	573.99 1,337.76	1,337.76	1,478.76	08/2013 03/2018	03/2018	55(O) 0(R)	32/38

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
254	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM , G	01/2008	4,375.35 6,749.18	6,749.18	6,760.00	09/2011 06/2017	12/2017	75(O) 6(R)	31/37
255	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , G	02/2005	8,692.97 15,095.67	15,095.67	13,653.00	01/2011 05/2018	03/2019	98(O) 10(R)	26/47
256	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR , G	01/2007	5,353.00 7,998.00	5,353.00	5,472.83	05/2014 03/2017	03/2018	46(O) 12(R)	1/18
257	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR , G	03/2010	3,984.03 -	3,984.03	3,290.44	01/2013 -	-	-	1/1
258	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	12,964.60	9,072.44	01/2018 -	08/2018	7(O) -	27/31
259	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR , G	05/2015	436.68 -	602.44	470.78	12/2016 -	12/2017	12(O) -	8/16
260	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR , G	04/2016	790.13 -	790.30	242.89	06/2019 -	06/2019	0(O) -	0/0
261	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH , G	11/2011	2,127.51 2,619.59	2,619.56	2,581.34	07/2014 09/2017	09/2017	38(O) 0(R)	6/8
262	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH , G	12/2011	1,746.65 2,228.71	2,228.71	1,929.61	08/2014 12/2017	12/2017	40(O) 0(R)	7/11
263	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATISGARH - [N18000125]PGCIL,CHHATISGARH , G	03/2012	9,569.76 9,291.03	9,291.03	7,283.96	06/2015 06/2017	09/2017	27(O) 3(R)	27/30
264	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH , G	12/2012	11,846.00 -	11,846.00	8,528.00	06/2017 12/2017	04/2018	10(O) 4(R)	32/40
265	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , G	03/2015	1,394.52 -	1,394.52	14.85	05/2017 06/2019	06/2019	25(O) 0(R)	4/9
266	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI , G	05/2015	780.33 -	780.33	8.20	10/2018 -	10/2018	0(O) -	0/0
267	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT , G	12/2011	552.44 609.44	609.44	501.60	02/2014 03/2016	03/2016	-	10/10
268	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL,GUJARAT , G	10/2015	315.00 -	315.00	14.61	10/2016 -	10/2016	-	2/2
269	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT , G	01/2016	244.19 -	244.19	106.81	07/2018 -	12/2017	-7(O) -	0/0
270	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT , G	07/2016	300.94 -	300.94	18.66	12/2018 -	12/2018	0(O) -	0/0
271	KANDORNA AND BHANWAD WIND FARM - [N18000234]THDCIL,GUJARAT , G	11/2016	415.49 -	415.49	-	03/2017 -	03/2017	-	1/2
272	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT , G	11/2016	330.00 -	330.00	135.14	11/2017 -	11/2017	0(O) -	1/4
273	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH , G	09/2002	3,919.59 -	8,398.75	6,480.33	09/2009 -	12/2018	111(O) -	2/3

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
274	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,HIMACHAL PRADESH , G	12/2005	358.42 -	358.42	-	12/2008 09/2010	-	-	0/15
275	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR , G	01/2009	3,642.04 -	5,882.01	5,021.45	01/2016 -	02/2018	25(O) -	6/6
276	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR , G	10/2014	8,112.12 -	8,112.12	868.78	04/2020 -	05/2023	37(O) -	0/0
277	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR , G	01/2014	1,788.41 -	2,352.57	1,118.12	09/2017 -	09/2018	12(O) -	0/0
278	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , G	02/2014	14,366.58 -	14,366.58	5,214.00	02/2019 02/2020	02/2021	24(O) 12(R)	16/20
279	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND , G	08/2006	2,313.00 4,138.41	4,366.64	3,484.00	12/2011 03/2016	02/2017	-	14/14
280	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND , G	10/2004	4,237.96 4,552.00	4,552.00	1,681.43	10/2017 -	10/2017	0(O) -	0/0
281	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA , G	01/2012	15,166.19 -	15,166.19	14,089.00	01/2017 07/2017	11/2017	10(O) 4(R)	47/48
282	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , G	03/2013	11,638.55 -	11,638.55	8,019.00	09/2017 03/2018	03/2018	6(O) 0(R)	29/41
283	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH , G	03/2015	9,870.51 -	9,870.51	3,245.00	09/2019 -	09/2019	0(O) -	19/19
284	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH , G	01/2016	305.04 -	305.04	148.64	03/2017 10/2017	10/2017	7(O) 0(R)	0/0
285	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH , G	04/2016	287.99 -	287.99	58.44	06/2018 -	06/2018	0(O) -	0/0
286	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	41.04	09/2020 -	09/2020	0(O) -	0/0
287	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , G	12/2007	477.69 738.48	738.48	645.85	09/2010 12/2017	12/2017	87(O) 0(R)	4/8
288	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , G	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 03/2017	03/2017	-	41/41
289	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA , G	03/2012	9,395.18 -	9,395.18	7,988.00	11/2016 12/2017	04/2018	17(O) 4(R)	34/36
290	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM , G	07/1998	368.72 1,329.43	1,329.43	1,259.14	07/2006 11/2017	11/2017	136(O) 0(R)	6/13
291	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE , G	10/2008	4,824.12 5,071.94	5,071.94	4,473.47	10/2012 02/2018	02/2018	64(O) 0(R)	8/11
292	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE , G	02/2009	11,130.19 13,762.80	13,762.80	12,547.20	08/2013 12/2017	12/2017	52(O) 0(R)	22/26
293	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE , G	02/2010	2,144.00 2,932.88	2,932.88	2,552.51	12/2012 02/2018	02/2018	62(O) 0(R)	16/23
294	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , G	02/2010	232.34 -	245.00	238.61	06/2012 -	12/2017	66(O) -	1/4
295	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL,MULTI STATE , G	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	03/2016	-	11/12

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
296	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE , G	07/2010	1,272.80 1,731.10	1,731.10	1,407.97	11/2012 12/2017	12/2017	61(O) 0(R)	10/13
297	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , G	10/2011	487.49 639.46	639.46	485.24	06/2014 03/2018	06/2018	48(O) 3(R)	10/12
298	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE , G	12/2011	297.33 346.79	426.29	355.29	08/2014 12/2017	12/2017	40(O) 0(R)	8/10
299	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE , G	03/2012	198.63 -	198.63	135.16	09/2014 09/2017	09/2017	36(O) 0(R)	0/0
300	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE , G	11/2011	723.63 882.13	882.13	715.86	11/2014 06/2017	12/2017	37(O) 6(R)	7/10
301	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE , G	03/2013	514.20 703.10	703.10	561.70	06/2015 12/2017	12/2017	30(O) 0(R)	7/10
302	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , G	03/2013	2,514.88 -	2,514.88	1,945.36	12/2015 12/2017	03/2018	27(O) 3(R)	15/18
303	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE , G	10/2013	1,364.52 1,891.41	1,891.41	1,144.12	04/2016 09/2017	03/2018	23(O) 6(R)	8/12
304	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE , G	01/2014	374.63 -	374.63	97.92	04/2016 12/2017	12/2017	20(O) 0(R)	0/0
305	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE , G	02/2014	539.82 -	539.82	384.32	06/2016 02/2018	02/2018	20(O) 0(R)	8/11
306	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE , G	02/2014	908.08 969.97	969.97	711.64	06/2016 02/2018	09/2017	15(O) -5(R)	16/18
307	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , G	05/2014	829.98 -	829.98	408.10	08/2016 10/2017	10/2017	14(O) 0(R)	2/4
308	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE , G	05/2014	522.29 550.18	550.18	360.30	11/2016 11/2017	03/2018	16(O) 4(R)	7/12
309	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE , G	03/2014	155.57 206.42	206.42	129.79	03/2016 07/2017	10/2017	19(O) 3(R)	3/6
310	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE , G	06/2014	5,151.37 -	5,151.37	1,407.32	03/2018 -	03/2018	0(O) -	8/12
311	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , G	08/2014	288.49 -	376.09	218.80	02/2017 06/2017	03/2018	13(O) 9(R)	7/12
312	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE , G	02/2014	196.58 225.28	225.28	118.67	02/2016 08/2017	11/2017	21(O) 3(R)	9/17
313	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , G	12/2014	6,517.36 -	6,517.36	3,330.00	04/2018 -	04/2018	0(O) -	3/12
314	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE , G	01/2015	268.80 340.88	340.88	154.86	03/2018 -	03/2018	0(O) -	0/3
315	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE , G	01/2015	871.62 -	871.62	134.51	10/2017 10/2017	06/2018	8(O) 8(R)	0/5

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
316	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE , G	01/2015	203.28 260.03	260.03	159.70	07/2017 -	12/2017	5(O) -	3/5
317	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , G	03/2015	197.40 -	197.40	42.41	03/2018 -	03/2018	0(O) -	0/0
318	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE , G	03/2015	1,071.24 -	1,071.24	452.50	09/2017 -	04/2018	7(O) -	0/0
319	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , G	04/2015	3,705.61 -	3,705.61	1,980.02	04/2018 -	04/2018	0(O) -	4/9
320	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , G	04/2015	1,479.30 -	1,479.30	674.66	04/2017 03/2018	03/2018	11(O) 0(R)	2/8
321	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE , G	07/2015	2,247.37 -	2,247.37	591.47	07/2018 -	07/2018	0(O) -	0/0
322	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE , G	01/2016	1,455.47 -	1,455.47	439.84	07/2018 -	07/2018	0(O) -	0/0
323	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE , G	03/2016	808.63 -	808.63	190.45	01/2018 -	03/2019	14(O) -	0/0
324	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE , G	05/2016	766.21 -	766.21	12.93	11/2018 -	11/2018	0(O) -	0/0
325	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE , G	05/2016	3,519.59 -	3,519.59	345.26	05/2019 -	05/2019	0(O) -	0/0
326	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE , G	05/2016	14,733.37 -	14,733.37	657.13	11/2019 -	11/2019	0(O) -	0/0
327	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE , G	04/2016	810.48 -	810.48	284.67	12/2018 -	12/2018	0(O) -	0/0
328	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE , G	05/2016	167.01 -	167.01	30.90	11/2018 -	11/2018	0(O) -	0/0
329	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE , G	07/2016	150.99 -	150.99	11.40	07/2018 -	07/2018	0(O) -	0/0
330	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE , G	07/2016	333.17 -	333.17	87.99	03/2019 -	03/2019	0(O) -	0/0
331	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE , G	08/2016	431.89 -	431.89	.40	02/2019 -	02/2019	0(O) -	0/0
332	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE , G	08/2016	177.52 -	177.52	10.95	02/2019 -	02/2019	0(O) -	0/0
333	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE , G	09/2016	562.25 -	562.25	18.56	03/2019 -	03/2019	0(O) -	0/0
334	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE , G	03/2017	251.60 -	251.60	-	06/2019 -	06/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
335	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE , G	10/2016	167.75 -	167.75	-	04/2019 -	04/2019	0(O) -	0/0
336	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE , G	03/2017	283.72 -	283.72	7.70	11/2019 -	11/2019	0(O) -	0/0
337	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE , G	10/2016	408.46 -	408.46	40.12	01/2019 -	01/2019	0(O) -	0/0
338	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE , G	10/2016	608.24 -	608.24	5.12	04/2019 -	04/2019	0(O) -	0/0
339	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE , G	02/2017	195.05 -	195.05	-	02/2020 -	02/2020	0(O) -	0/0
340	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE , G	02/2017	322.30 -	322.30	12.97	02/2019 -	02/2019	0(O) -	0/0
341	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE , G	03/2017	162.31 -	162.31	.51	03/2019 -	03/2019	0(O) -	0/0
342	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE , G	02/2017	235.53 -	235.53	5.36	06/2019 -	06/2019	0(O) -	0/0
343	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE , G	03/2017	379.95 -	379.95	19.61	12/2019 -	12/2019	0(O) -	0/0
344	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE , G	02/2017	204.12 -	204.12	7.45	09/2019 -	09/2019	0(O) -	0/0
345	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE , G	02/2017	5,070.13 -	5,070.13	211.58	04/2020 -	04/2020	0(O) -	0/0
346	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE , G	03/2017	337.75 -	337.75	-	06/2019 -	06/2019	0(O) -	0/0
347	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE , G	12/2014	4,754.42 -	4,754.42	341.63	12/2018 -	12/2019	12(O) -	0/0
348	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE , G	12/2014	5,111.33 -	5,111.33	351.70	12/2018 -	12/2019	12(O) -	0/0
349	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 -	1,364.00	515.00	12/2015 -	03/2018	27(O) -	0/0
350	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE , Central Sector Projects	04/2015	2,525.00 -	2,525.00	1,215.00	11/2017 -	11/2017	0(O) -	0/0
351	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , G	02/2014	12,532.44 -	12,532.44	6,184.00	08/2018 -	08/2018	0(O) -	25/30

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
352	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA , G	04/2016	844.64 -	844.64	98.85	04/2019 -	04/2019	0(O) -	0/0
353	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN , G	07/2015	307.18 -	307.18	151.55	11/2017 -	06/2018	7(O) -	0/0
354	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , G	02/2015	302.49 302.00	302.49	270.77	02/2016 -	-	-	1/1
355	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN , G	07/2016	1,429.38 -	1,429.38	95.35	01/2019 -	01/2019	0(O) -	0/0
356	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU , G	05/2005	1,779.29 2,187.32	2,187.32	1,955.46	11/2008 09/2018	09/2018	118(O) 0(R)	20/22
357	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU , G	09/2011	1,940.13 2,702.65	2,702.65	2,323.86	09/2014 06/2017	12/2017	39(O) 6(R)	11/13
358	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU , G	01/2016	162.11 -	162.11	104.56	05/2018 -	12/2017	-5(O) -	0/0
359	50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU , G	09/2017	287.48 -	287.48	.51	03/2018 -	03/2018	0(O) -	0/0
360	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA , G	01/2016	10,598.98 -	10,598.98	982.00	07/2020 -	07/2020	0(O) -	13/18
361	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , G	07/2009	421.01 1,078.31	1,078.31	963.23	07/2013 -	-	-	26/26
362	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA , G	05/2016	409.19 -	409.19	37.13	05/2018 -	05/2018	0(O) -	0/0
363	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , G	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
364	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH , G	09/2014	9,188.98 -	9,188.98	3,043.00	03/2019 -	03/2019	0(O) -	19/27
365	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , G	05/2011	195.42 294.60	294.60	121.55	02/2014 02/2018	12/2018	58(O) 10(R)	2/5
366	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	03/2018	15(O) -	29/34
367	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , G	07/2006	1,657.00 2,978.86	3,939.11	2,307.37	02/2016 09/2019	12/2020	58(O) 15(R)	15/26
368	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND , G	11/2006	2,978.48 -	3,846.30	3,278.00	03/2013 06/2019	06/2019	75(O) 0(R)	3/15
369	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND , G	08/2008	2,491.58 -	2,491.58	1,226.25	06/2013 -	11/2020	89(O) -	7/11
370	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND , G	07/2012	1,527.00 -	1,527.00	147.00	08/2017 -	08/2017	0(O) -	0/15
371	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL , G	04/2010	4,404.57 5,135.01	5,135.01	3,404.34	01/2015 03/2018	03/2018	38(O) 0(R)	12/16
372	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL , G	09/2014	1,381.84 -	1,381.84	287.00	09/2019 -	09/2019	0(O) -	5/7
373	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL , G	04/2007	4,122.00 8,781.30	9,142.58	8,300.00	02/2011 -	03/2016	-	26/26

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
374	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL , G	04/2016	454.11 -	454.11	47.99	04/2018 -	04/2018	0(O) -	0/0
	Total		3,44,032.76 -	3,97,114.95	2,30,735.18				891/1218
	<u>HEAVY INDUSTRY</u>								
375	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE , G	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
376	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM , G	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
377	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI , G	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
378	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI , G	09/2013	444.70 -	444.70	326.30	12/2015 -	-	-	0/0
379	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI , G	11/2013	196.70 -	209.00	170.00	01/2016 -	-	-	0/0
380	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI , G	12/2013	204.44 -	204.44	135.00	05/2017 -	12/2017	7(O) -	0/2
381	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI , G	08/2014	293.65 -	293.65	203.00	05/2017 -	12/2017	7(O) -	0/5
382	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA , G	09/2014	505.58 -	505.58	202.00	03/2018 -	03/2018	0(O) -	0/2
383	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA , G	07/2016	312.99 -	312.99	103.00	08/2018 -	08/2018	0(O) -	0/1
384	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA , G	10/2016	363.99 -	363.99	-	05/2018 08/2019	08/2019	15(O) 0(R)	0/0
385	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB , G	07/2016	152.95 -	152.95	32.00	02/2018 -	08/2018	6(O) -	0/1
386	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH , G	10/2013	159.50 -	159.50	158.65	11/2013 06/2017	06/2017	-	0/8
387	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL , G	12/2014	168.90 -	168.90	101.00	05/2017 -	12/2017	7(O) -	0/3
388	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL , G	08/2016	244.00 -	244.00	66.00	09/2018 -	09/2018	0(O) -	0/0
	Total		3,637.08 -	3,649.38	1,751.45				0/22
	<u>RAILWAYS</u>								
389	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH , G	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106(O) -	0/0
390	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH , G	12/2001	330.00 -	2,125.18	14.17	-	03/2021	-	0/0
391	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH , G	04/2003	136.62 -	376.00	379.85	12/2007 03/2010	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
392	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH , G	07/2006	743.00 -	1,825.00	-	03/2008 06/2008	03/2020	144(O) 141(R)	0/0
393	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH , G	04/2011	283.54 -	759.41	.51	- -	-	-	0/0
394	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , G	04/2013	829.00 -	829.00	.48	- -	-	-	0/1
395	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , G	04/2011	1,313.48 -	1,313.48	8.06	- -	-	-	0/1
396	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , G	03/2012	1,503.71 -	1,503.71	-	- -	03/2020	- -	0/0
397	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH , G	04/2015	3,873.07 -	3,873.07	-	- -	-	-	0/0
398	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH , G	04/2016	4,000.00 -	3,631.00	-	- -	-	-	0/0
399	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH , G	04/2015	3,246.26 -	3,246.26	-	- -	-	-	0/0
400	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH , G	04/2015	2,499.71 -	2,499.71	23.82	03/2021 -	03/2021	0(O) -	0/0
401	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH , G	01/2013	387.70 -	387.70	342.92	03/2018 -	03/2018	0(O) -	0/0
402	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH , G	08/2016	234.50 -	234.50	.14	03/2019 -	03/2019	0(O) -	0/0
403	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM , G	09/1997	1,500.00 -	5,000.00	4,753.99	04/2008 12/2011	06/2018	122(O) 78(R)	0/0
404	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM , G	09/2006	200.00 -	780.00	421.40	- -	03/2019	- -	0/0
405	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM , G	04/1998	227.90 -	509.00	403.86	12/2012 -	05/2016	-	0/0
406	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM , G	04/1996	1,676.31 -	7,000.00	6,995.27	03/2009 -	03/2018	108(O) -	0/0
407	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM , G	04/2011	312.12 -	508.00	477.36	- -	03/2019	- -	0/0
408	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM , G	04/2012	246.07 -	398.93	104.16	- -	03/2019	- -	0/0
409	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM , G	04/2003	971.22 -	966.27	834.11	- -	12/2009	-	0/0
410	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM , G	04/2003	4,300.00 -	4,520.00	4,393.96	- -	08/2015	-	0/0
411	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM , G	04/2007	180.09 -	180.00	157.12	- -	05/2011	-	0/0
412	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM , G	04/2015	2,232.32 -	2,232.32	59.89	- -	03/2021	- -	0/0
413	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM , G	04/2015	870.96 -	870.96	17.53	- -	03/2021	- -	0/0
414	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR , G	04/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
415	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR , G	09/2001	492.98 -	1,320.00	917.84	12/2010 -	-	-	0/0
416	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , G	04/1997	162.87 -	541.00	183.72	-	-	-	0/0
417	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR , G	04/2003	528.65 -	324.66	330.82	-	-	-	0/0
418	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR , G	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
419	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR , G	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
420	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR , G	04/2003	218.19 -	412.05	352.29	-	03/2018	-	0/0
421	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR , G	04/1996	332.92 283.95	477.88	495.40	03/2012 -	-	-	0/0
422	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR , G	09/2006	300.00 -	2,145.00	920.59	-	03/2020	-	0/0
423	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR , G	04/2008	282.92 -	360.00	3.13	-	-	-	0/0
424	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , G	04/2008	490.80 -	490.80	.39	-	-	-	0/0
425	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR , G	04/2008	620.57 -	620.57	-	-	-	-	0/0
426	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR , G	04/2008	445.25 -	445.25	-	-	-	-	0/0
427	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR , G	04/2008	326.20 -	326.20	1.68	-	-	-	0/0
428	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR , G	04/1999	175.69 -	325.00	253.10	-	-	-	0/0
429	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR , G	04/2006	285.07 -	378.56	111.71	-	-	-	0/0
430	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR , G	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
431	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR , G	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
432	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR , G	04/2008	678.62 -	2,393.23	17.17	-	-	-	0/0
433	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR , G	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
434	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR , G	04/2008	304.41 -	304.41	.19	-	-	-	0/0
435	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR , G	04/2008	192.56 -	192.56	.38	-	-	-	0/0
436	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR , G	04/2008	281.30 -	281.30	.58	-	-	-	0/0
437	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , G	04/2004	372.14 -	355.81	283.44	-	-	-	0/0
438	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR , G	04/2009	470.00 -	470.00	40.00	-	-	-	0/0
439	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR , G	04/2013	213.01 -	367.17	13.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
440	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR , G	05/2015	380.00 -	380.00	-	- -	-	-	0/0
441	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR , G	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020	0(O) -	0/1
442	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR , G	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020	0(O) -	1/1
443	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR , G	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
444	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH , G	04/1995	304.00 -	631.78	-	12/2012 -	-	-	0/0
445	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , G	09/2006	324.90 -	516.40	-	03/2010 -	12/2017	93(O) -	0/3
446	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH , G	12/2012	826.57 -	1,160.83	438.97	- -	03/2020	- -	0/1
447	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH , G	03/2007	758.09 -	758.09	-	03/2020 -	03/2020	0(O) -	0/0
448	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH , G	05/2014	207.00 -	207.00	139.85	03/2018 -	03/2018	0(O) -	0/0
449	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , G	04/1999	156.65 -	197.17	56.10	- -	-	-	0/0
450	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI , G	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
451	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT , G	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84(O) -	0/0
452	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT , G	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45(O) -	0/0
453	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT , G	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84(O) -	0/0
454	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT , G	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
455	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT , G	04/2012	567.18 -	975.62	-	- -	03/2020	- -	0/0
456	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT , G	04/2012	376.59 -	644.38	-	- -	12/2020	- -	0/0
457	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT , G	04/2011	439.88 -	845.68	.78	- -	-	-	0/0
458	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , G	04/1994	320.66 -	399.63	-	- -	03/2019	- -	0/0
459	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT , G	04/2013	1,266.89 -	1,266.89	-	- -	12/2020	- -	0/0
460	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , G	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	- -	0/0
461	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , G	04/2010	279.40 -	355.00	323.64	- -	-	-	0/0
462	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT , G	04/2015	1,002.39 -	1,002.39	-	- -	03/2021	- -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
463	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT , G	10/2013	343.00 -	343.00	235.03	03/2019 -	03/2019	0(O) -	0/0
464	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , G	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
465	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , G	04/2012	287.00 -	625.00	4.38	-	-	-	0/0
466	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA , G	04/2013	400.00 -	400.00	-	-	-	-	0/0
467	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA , G	05/2015	400.00 -	400.00	-	-	-	-	0/0
468	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA , G	12/2015	346.32 -	300.00	201.87	03/2019 -	03/2019	0(O) -	0/0
469	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH , G	04/2008	1,046.88 -	2,966.99	-	-	-	-	0/0
470	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , G	03/1995	2,500.00 -	19,565.00	13,536.97	11/2002 -	12/2018	193(O) -	0/0
471	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , G	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99(O) 111(R)	0/0
472	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND , G	04/1997	194.07 -	491.33	-	06/2004 -	-	-	0/0
473	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND , G	04/2002	459.91 -	459.91	221.54	-	-	-	0/0
474	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND , G	03/1997	261.70 -	318.00	-	02/2006 -	12/2019	166(O) -	0/1
475	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND , G	04/2008	167.73 -	167.73	207.11	03/2012 -	-	-	0/0
476	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND , G	04/2010	309.44 -	583.00	-	12/2015 -	-	-	0/0
477	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , G	04/2012	258.20 -	365.00	-	-	12/2017	-	0/0
478	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , G	04/2012	148.77 -	209.00	-	12/2016 -	-	-	0/0
479	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND , G	03/2016	1,724.20 -	1,724.20	-	03/2021 -	03/2021	0(O) -	0/0
480	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA , G	02/1997	295.00 1,289.92	1,289.92	1,493.70	-	01/2017	-	0/1
481	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA , G	04/1997	227.00 -	2,135.00	133.87	-	-	-	0/0
482	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA , G	02/1998	242.42 369.70	1,542.41	927.68	- 05/2009	-	-	0/1
483	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA , G	04/1996	138.00 1,382.78	1,382.78	6.12	-	-	-	0/0
484	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , G	04/2007	482.00 -	874.57	981.70	03/2013 -	-	-	0/0
485	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , G	04/2011	913.00 -	1,801.01	2.55	-	-	-	0/0
486	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , G	04/2007	179.65 -	1,350.91	760.21	-	-	-	0/1
487	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA , G	04/2010	377.93 986.30	986.30	267.65	-	-	-	0/1

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
488	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , G	04/2013	558.00 692.43	692.43	-	- -	- -	-	0/0
489	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , G	04/2011	562.74 -	832.47	.94	- -	- -	-	0/0
490	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , G	04/2011	341.05 -	348.85	.35	- -	- -	-	0/0
491	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA , G	04/2010	2,127.00 -	2,127.00	-	- -	03/2019	- -	0/1
492	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , G	04/2011	146.75 -	167.50	.32	- -	- -	-	0/0
493	GADAG-WADI NL - [N22000299]SWR,KARNATAKA , G	04/2013	1,117.00 1,922.00	1,922.00	3.60	- -	- -	-	0/0
494	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , G	04/2013	327.25 367.77	367.77	.14	- -	- -	-	0/0
495	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , G	04/2012	285.57 279.54	279.54	2.74	01/1999 -	- -	-	0/0
496	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA , G	04/2010	203.40 203.40	273.84	278.08	- -	- -	-	0/0
497	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA , G	03/2015	1,900.00 1,141.00	1,141.00	416.47	- 03/2020	- -	-	0/5
498	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA , G	03/2015	960.00 578.00	578.00	291.26	- 11/2015	03/2020	- 52(R)	0/2
499	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , G	10/1998	550.00 -	1,566.00	235.68	- -	- -	-	0/0
500	KUMBALAM-TURAVUR - [N22000191]SR,KERALA , G	04/2011	252.96 -	252.96	7.16	- -	- -	-	0/0
501	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , G	04/2006	191.72 -	342.85	360.22	- -	- -	-	0/0
502	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , G	04/2010	189.24 -	189.24	6.17	- -	- -	-	0/0
503	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA , G	02/2015	900.00 -	900.00	-	- -	- -	-	0/0
504	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA , G	02/2015	1,000.00 -	1,000.00	-	- -	- -	-	0/0
505	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH , G	04/2001	470.92 727.13	2,713.09	632.05	- -	03/2021	- -	0/0
506	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH , G	04/2005	383.79 -	1,101.16	194.91	- -	- -	-	0/0
507	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , G	09/2007	687.20 -	950.00	-	03/2010 -	03/2018	96(O) -	0/0
508	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH , G	04/2008	603.04 -	1,030.29	628.11	03/2012 -	- -	-	0/0
509	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH , G	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(O) -	1/1
510	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH , G	04/2011	1,485.65 -	1,485.65	-	12/2020 -	12/2020	0(O) -	0/0
511	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH , G	06/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022	0(O) -	0/1
512	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH , G	08/2016	582.13 -	582.13	-	03/2020 -	03/2020	0(O) -	0/1
513	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH , G	12/2015	174.00 -	174.00	90.63	03/2019 -	03/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
514	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA , G	06/1994	663.01 175.30	858.23	688.04	06/1999 -	-	-	0/0
515	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA , G	03/1996	495.44 -	1,781.98	514.44	03/2004 -	03/2020	192(O) -	0/0
516	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA , G	02/1997	514.68 -	2,271.50	812.01	- -	-	-	0/0
517	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA , G	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60(O) -	0/0
518	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA , G	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
519	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , G	04/2008	499.30 -	3,168.29	532.82	- -	-	-	0/0
520	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , G	04/2011	277.70 -	792.89	52.35	- -	-	-	0/0
521	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA , G	04/2011	184.06 -	199.12	142.22	- -	-	-	0/0
522	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA , G	04/2012	297.85 -	540.02	98.02	- -	-	-	0/0
523	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA , G	02/2016	9,968.00 -	9,968.00	-	- -	-	-	0/0
524	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA , G	02/2016	2,425.00 -	2,425.00	-	- -	-	-	0/0
525	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA , G	02/2016	2,750.00 -	2,750.00	-	- -	-	-	0/0
526	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA , G	02/2015	630.00 -	1,272.19	19.48	- -	-	-	0/0
527	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA , G	02/2015	2,326.00 -	2,449.91	.63	- -	-	-	0/0
528	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA , G	02/2015	4,670.00 3,627.00	3,627.47	-	- -	-	-	0/0
529	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA , G	02/2016	1,876.00 -	2,081.27	-	- -	-	-	0/0
530	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA , G	02/2016	854.00 -	1,035.16	-	- -	-	-	0/0
531	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA , G	02/2016	912.00 -	637.95	.35	- -	-	-	0/0
532	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA , G	03/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020	0(O) -	0/0
533	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA , G	04/2015	723.78 -	723.78	-	12/2025 -	12/2025	0(O) -	0/0
534	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA , G	09/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021	0(O) -	0/0
535	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA , G	10/2013	305.00 -	305.00	218.41	03/2019 -	03/2019	0(O) -	0/0
536	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR , G	04/2003	727.56 -	9,658.00	4,927.46	03/2011 -	03/2020	108(O) -	0/0
537	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA , G	04/2010	4,083.02 -	6,000.00	247.67	- -	03/2021	-	0/0
538	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM , G	04/2008	619.34 -	4,600.00	1,565.18	04/2014 -	03/2020	71(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
539	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE , G	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
540	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE , G	02/1996	240.00 -	579.37	537.02	- -	-	-	0/0
541	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , G	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261(O) -	0/0
542	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE , G	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
543	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE , G	04/1997	218.24 236.41	525.00	544.20	- -	03/2019	- -	0/0
544	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE , G	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
545	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE , G	04/1999	744.71 744.71	1,126.79	761.70	- -	-	-	1/1
546	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE , G	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0
547	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , G	03/1998	280.00 -	1,122.00	834.61	- -	-	-	0/6
548	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE , G	04/2000	733.00 -	3,010.00	2,225.72	12/2008 -	03/2019	123(O) -	0/0
549	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , G	04/1998	92.63 -	350.00	316.64	02/2011 -	-	-	0/0
550	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE , G	04/2000	607.09 -	973.33	613.71	12/2012 12/2012	-	-	0/0
551	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE , G	04/2005	230.03 -	718.54	272.77	- -	05/2019	- -	0/0
552	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE , G	12/2006	170.00 -	436.00	439.57	03/2011 -	10/2011	-	0/0
553	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE , G	03/2007	243.78 -	268.78	94.80	- -	08/2017	- -	0/0
554	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE , G	03/2013	295.00 -	477.31	92.43	- -	10/2018	- -	0/0
555	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE , G	04/2007	1,347.26 -	1,347.26	270.58	- -	-	-	0/0
556	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE , G	04/2007	1,640.04 -	1,640.04	331.91	- -	03/2022	- -	0/0
557	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE , G	04/2011	2,082.75 -	2,562.27	177.84	- -	-	-	0/1
558	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE , G	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
559	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE , G	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46(O) -	0/0
560	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , G	04/2010	553.63 -	1,009.00	-	- -	-	-	0/0
561	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE , G	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
562	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE , G	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	- -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
563	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE , G	04/2008	523.52 2,350.00	523.52	2.26	- -	-	-	0/0
564	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE , G	04/2008	822.39 -	1,480.83	-	- -	03/2018	- -	0/1
565	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE , G	04/2007	270.14 -	346.15	253.87	- -	-	-	0/0
566	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE , G	04/2010	242.22 -	471.00	48.76	- -	-	-	0/0
567	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE , G	04/2010	241.52 -	394.28	148.33	- -	-	-	0/0
568	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE , G	04/2011	165.82 -	450.00	117.50	- -	03/2020	- -	0/0
569	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE , G	04/1999	523.17 -	1,871.00	1,071.96	- -	03/2018	- -	0/0
570	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE , G	04/2011	601.43 -	1,500.00	70.29	- -	-	-	0/0
571	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , G	04/1987	406.99 -	319.58	141.88	- -	-	-	0/0
572	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , G	04/2007	450.00 -	290.85	9.31	- -	-	-	0/0
573	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , G	04/2010	172.03 -	260.60	6.42	- -	-	-	0/0
574	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , G	04/2013	915.98 1,130.13	1,130.13	.30	- -	-	-	0/0
575	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE , G	04/2011	248.07 -	234.41	161.17	03/2015 -	-	-	0/0
576	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , G	04/2011	288.35 -	238.36	51.31	- -	-	-	0/0
577	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , G	04/2011	261.38 -	332.14	87.22	- -	-	-	0/0
578	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , G	04/2001	923.52 -	923.52	227.50	- -	-	-	0/0
579	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , G	04/2005	595.91 -	595.91	103.62	- -	-	-	0/0
580	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , G	04/2010	174.56 -	160.97	56.25	- -	-	-	0/0
581	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , G	04/2010	277.28 -	266.00	92.93	- -	-	-	0/0
582	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , G	04/2010	296.44 -	198.88	15.83	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
583	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , G	04/2010	157.94 -	157.94	47.63	- -	11/2018	- -	0/0
584	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , G	04/2007	450.55 -	251.05	15.66	- -	-	-	0/0
585	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , G	04/2010	365.17 -	365.67	1.37	- -	-	-	0/0
586	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , G	04/2011	267.09 -	350.78	98.15	- -	-	-	0/0
587	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , G	04/2011	193.44 -	186.64	150.28	- -	-	-	0/0
588	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , G	04/2011	175.80 -	173.91	18.54	- -	-	-	0/0
589	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE , G	04/2011	299.60 -	269.60	1.11	03/2017 -	-	-	0/0
590	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , G	04/2010	494.54 -	369.69	31.99	- -	-	-	0/0
591	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE , G	04/2000	297.47 -	153.02	52.01	- -	-	-	0/0
592	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE , G	04/2003	337.96 -	186.89	62.73	- -	-	-	0/0
593	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , G	04/2009	493.96 -	681.68	135.79	- -	-	-	0/0
594	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE , G	04/2010	423.66 -	720.59	456.58	03/2017 -	-	-	0/0
595	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , G	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
596	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , G	04/2011	166.89 -	166.89	.02	- -	-	-	0/0
597	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , G	04/2007	98.74 -	381.39	312.12	- -	-	-	0/0
598	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE , G	04/2006	96.16 -	280.00	268.37	- -	-	-	0/0
599	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE , G	04/2012	1,054.35 -	2,200.00	85.33	- -	-	-	0/0
600	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , G	04/2012	923.23 -	923.23	1.11	- -	-	-	0/1
601	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , G	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
602	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , G	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
603	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , G	04/2013	296.00 -	466.65	-	-	-	-	0/0
604	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE , G	04/2007	970.34 -	1,714.49	600.32	-	-	-	0/2
605	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , G	04/2010	337.49 -	792.01	1.13	-	-	-	0/1
606	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE , G	04/2008	2,050.00 -	2,050.00	200.35	-	-	-	0/1
607	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE , G	04/2010	338.54 -	338.54	212.64	-	-	-	0/0
608	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE , G	04/2008	162.96 -	162.96	153.31	-	-	-	0/0
609	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE , G	04/2013	876.00 -	876.00	-	-	-	-	0/0
610	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE , G	04/2007	328.14 -	1,540.00	45.20	-	-	-	0/0
611	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE , G	04/2012	250.93 -	259.23	8.43	-	-	-	0/0
612	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , G	04/2007	313.24 -	554.70	342.00	01/1999 -	-	-	0/0
613	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , G	04/2008	466.48 -	750.00	-	01/1999 -	-	-	0/0
614	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE , G	05/2015	600.00 -	648.00	-	-	02/2019	-	0/0
615	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE , G	03/2015	1,830.00 1,190.92	1,190.92	67.88	-	-	-	0/0
616	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE , G	05/2015	860.43 -	860.43	281.14	-	03/2020	-	0/0
617	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE , G	03/2015	1,618.00 1,614.59	1,614.59	414.20	-	-	-	0/0
618	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE , G	05/2015	720.00 -	678.54	-	-	12/2018	-	0/38
619	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	-	-	-	0/0
620	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE , G	04/2015	2,063.03 -	2,063.03	.14	-	03/2021	-	0/0
621	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE , G	04/2015	636.38 -	636.38	-	-	-	-	0/0
622	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE , G	04/1992	315.64 -	315.00	307.28	-	-	-	0/0
623	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE , G	04/2006	614.54 -	613.00	549.08	-	03/2014	-	0/0
624	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND , G	04/2006	850.00 -	3,000.00	357.19	03/2015 -	03/2020	60(O) -	0/0
625	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND , G	04/2013	4,274.00 -	4,274.00	-	-	03/2020	-	0/0
626	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA , G	04/1994	470.21 -	3,004.90	899.41	-	06/2021	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
627	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA , G	04/1996	301.64 -	1,185.64	-	- 09/2009	03/2019	- 114(R)	0/0
628	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA , G	04/1999	166.16 -	370.00	370.24	02/2009 02/2009	06/2017	-	0/1
629	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA , G	04/1998	183.23 -	1,202.70	-	02/2015 -	12/2019	58(O) -	0/0
630	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA , G	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	12/2017	105(O) 105(R)	1/1
631	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA , G	04/2005	810.78 -	1,928.07	462.42	- -	06/2022	- -	0/0
632	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA , G	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
633	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA , G	03/2011	679.27 -	1,579.27	544.65	- -	03/2021	- -	0/0
634	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA , G	03/2013	858.67 -	843.04	35.75	- -	03/2021	- -	0/0
635	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA , G	03/2006	201.00 -	230.00	242.23	- -	-	-	0/0
636	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA , G	03/2012	155.81 -	238.03	149.99	- -	03/2020	- -	0/0
637	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA , G	03/2011	165.16 -	234.71	224.64	03/2015 -	-	-	0/0
638	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA , G	04/2015	1,547.38 -	1,547.38	28.94	03/2021 -	03/2021	0(O) -	0/0
639	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA , G	04/2015	2,361.74 -	2,361.74	15.51	03/2021 -	03/2021	0(O) -	0/0
640	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA , G	04/2015	701.61 -	701.61	34.88	03/2021 -	03/2021	0(O) -	0/0
641	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA , G	04/2015	1,172.92 -	1,172.92	67.81	03/2021 -	03/2021	0(O) -	0/0
642	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA , G	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020	0(O) -	0/0
643	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA , G	04/1995	524.43 -	939.00	-	12/2021 -	12/2021	0(O) -	0/0
644	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA , G	01/1991	2,335.67 -	2,335.67	-	- -	12/2024	- -	0/0
645	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA , G	03/2006	960.18 -	960.18	-	03/2020 -	03/2020	0(O) -	0/0
646	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA , G	03/2009	942.95 -	942.95	-	03/2019 -	03/2019	0(O) -	0/0
647	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA , G	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0
648	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]JNR,PUNJAB , G	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
649	QADIAN-BEAS - [N22000295]JNR,PUNJAB , G	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
650	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN , G	02/1997	410.08 -	780.98	346.97	- -	-	-	0/0
651	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN , G	04/2008	829.74 -	1,161.64	353.32	03/2015 -	03/2019	48(O) -	0/0
652	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN , G	04/2008	653.19 -	941.04	575.19	03/2014 -	03/2019	60(O) -	0/0
653	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN , G	04/2008	516.23 -	735.00	694.13	03/2014 -	-	-	0/0
654	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN , G	04/2012	246.08 -	348.55	14.66	- -	02/2019	-	0/0
655	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , G	04/2013	236.93 -	276.89	74.21	- -	-	-	0/0
656	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN , G	04/2013	822.00 -	822.00	-	- -	-	-	0/1
657	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , G	04/2013	323.00 -	323.00	-	- -	-	-	0/0
658	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN , G	04/2013	456.00 -	855.16	585.06	- -	05/2018	-	0/0
659	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , G	04/2010	739.65 -	872.22	796.25	- -	-	-	0/1
660	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN , G	04/2011	239.73 -	257.78	30.33	- -	-	-	0/0
661	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , G	04/2011	213.39 -	272.99	63.54	- -	02/2019	-	0/0
662	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , G	04/2012	288.97 -	369.08	144.27	- -	-	-	0/0
663	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , G	04/2013	242.09 -	293.68	76.86	- -	03/2019	-	0/0
664	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN , G	05/2015	873.71 -	873.71	-	- -	-	-	0/0
665	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN , G	01/2011	493.17 -	493.17	383.12	03/2018 -	03/2018	0(O) -	0/0
666	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN , G	04/2012	471.82 -	471.82	19.91	03/2019 -	03/2019	0(O) -	0/0
667	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM , G	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0
668	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU , G	02/1997	155.55 -	870.00	854.91	- -	-	-	0/0
669	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU , G	09/1995	100.00 -	980.00	647.00	- -	-	-	0/0
670	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU , G	04/2006	495.74 -	495.74	386.03	06/2013 -	03/2018	57(O) -	1/4
671	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU , G	09/2007	404.19 -	2,072.50	932.04	- -	-	-	0/0
672	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU , G	09/2006	343.17 -	1,065.00	1,047.11	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
673	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU , G	04/2008	446.87 527.37	527.37	3.34	- 01/2011	-	-	0/0
674	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , G	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
675	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU , G	04/1998	271.24 -	520.00	464.50	- -	-	-	0/0
676	ERODE-PALANI - [N22000199]SR,TAMIL NADU , G	04/2008	288.57 -	603.22	1.63	- -	-	-	0/0
677	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , G	04/2008	164.41 -	302.90	31.98	- -	-	-	0/0
678	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU , G	04/2011	190.10 -	355.96	-	- -	03/2019	-	0/0
679	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA , G	12/1994	124.43 -	1,010.00	919.06	- -	-	-	0/0
680	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA , G	07/1998	125.00 -	480.00	3.48	07/2008 -	-	-	0/0
681	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA , G	04/2006	378.56 -	1,160.47	1.74	- -	03/2022	-	0/1
682	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA , G	04/2012	632.68 -	816.55	-	03/2016 -	12/2018	33(O) -	0/0
683	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , G	04/2013	1,112.00 -	1,112.00	.36	- -	-	-	0/1
684	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA , G	04/2013	616.08 -	616.08	.36	- -	-	-	0/1
685	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA , G	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
686	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA , G	04/2015	728.10 -	728.10	-	12/2024 -	12/2024	0(O) -	0/0
687	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA , G	04/2008	813.34 -	3,451.00	2,316.85	03/2014 -	03/2020	72(O) -	0/0
688	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA , G	04/1999	895.00 -	1,857.00	1,481.71	03/2007 -	04/2016	-	0/0
689	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , G	04/2012	252.00 -	580.00	-	- -	07/2019	- -	2/3
690	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , G	03/1997	677.97 1,062.36	1,679.13	1,706.54	- -	-	-	0/0
691	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH , G	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
692	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , G	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
693	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH , G	04/2006	325.00 -	1,581.53	618.19	03/2010 -	-	-	0/0
694	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH , G	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
695	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH , G	03/2013	307.00 -	308.00	-	- -	-	-	0/0
696	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH , G	03/2008	195.64 -	474.30	388.43	- -	07/2017	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
697	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH , G	03/2012	199.75 -	199.75	211.80	- -	03/2018	- -	0/0
698	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH , G	03/2013	643.00 -	644.00	-	- -	-	-	0/0
699	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , G	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
700	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH , G	04/2013	654.00 -	654.00	-	- -	-	-	0/0
701	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH , G	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
702	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH , G	04/2014	182.92 -	197.73	-	- -	-	-	0/0
703	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH , G	04/1997	836.26 -	1,072.52	1,026.65	- -	-	-	0/0
704	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH , G	03/2015	1,750.00 -	1,295.42	17.78	03/2022 -	03/2022	0(O) -	0/0
705	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH , G	04/2015	524.00 668.00	668.00	-	03/2020 -	03/2020	0(O) -	0/6
706	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH , G	04/2015	750.55 -	943.60	-	12/2024 -	12/2024	0(O) -	0/0
707	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH , G	04/2011	927.01 -	927.01	-	03/2019 -	03/2019	0(O) -	0/0
708	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH , G	04/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025	0(O) -	0/0
709	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH , G	03/2012	1,183.25 -	1,183.25	-	12/2020 -	12/2020	0(O) -	0/0
710	RAMNA - SINGRAULI DOUBLING - [N22000417]EJR,UTTAR PRADESH , G	08/2015	2,436.21 -	2,436.21	33.76	03/2020 -	03/2020	0(O) -	0/0
711	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]EJR,UTTAR PRADESH , G	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12(O) -	0/0
712	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND , G	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
713	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND , G	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0
714	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND , G	04/2011	4,295.30 -	4,295.30	-	12/2026 -	12/2026	0(O) -	0/0
715	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL , G	04/1983	36.80 274.41	614.00	261.36	- -	-	-	0/0
716	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL , G	04/1974	393.46 154.30	1,026.00	182.48	03/2007 03/2007	-	-	0/0
717	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL , G	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
718	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL , G	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	- 111(R)	0/0
719	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL , G	04/2007	1,106.62 -	1,106.62	355.85	12/2010 -	-	-	3/7

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
720	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL, G	03/1984	293.97 -	749.69	-	06/2005 -	-	-	0/0
721	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL, G	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
722	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL, G	04/2010	2,298.42 -	1,655.68	-	03/2014 -	-	-	0/0
723	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL, G	04/2010	3,951.98 -	3,161.58	-	03/2016 -	12/2020	57(O) -	0/0
724	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL, G	04/2010	2,913.51 -	2,619.00	-	03/2016 -	12/2018	33(O) -	0/0
725	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL, G	04/2009	533.38 -	533.38	127.10	12/2011 -	-	-	0/0
726	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL, G	04/2009	611.03 -	611.03	146.31	12/2011 -	-	-	0/0
727	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL, G	04/2004	293.74 -	229.33	140.60	12/2010 -	-	-	0/0
728	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL, G	04/1999	207.52 -	334.87	293.47	12/2012 -	-	-	0/0
729	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL, G	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
730	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL, G	04/2010	267.37 -	434.00	-	- -	-	-	0/0
731	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL, G	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
732	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL, G	04/2010	171.02 -	235.00	237.39	06/2013 -	12/2016	-	0/0
733	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL, G	04/2010	221.42 -	380.00	32.52	- -	-	-	0/0
734	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL, G	04/2011	209.77 -	445.00	319.06	- -	03/2018	-	0/0
735	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL, G	04/2012	283.55 -	330.00	87.65	- -	03/2018	-	0/0
736	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL, G	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
737	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL, G	04/2012	255.64 -	272.20	.64	- -	-	-	0/0
738	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL, G	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
739	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL, G	04/2016	556.31 -	612.00	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
740	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL , G	01/1991	763.18 -	1,428.00	-	12/2021 -	12/2021	0(O) -	0/0
741	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL , G	04/1998	1,027.40 -	2,373.00	-	03/2003 -	-	-	0/0
	Total		3,54,063.17 -	4,46,938.49	1,16,071.08				13/110
	ROAD TRANSPORT AND HIGHWAYS								
742	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,234.53	05/2013 -	12/2017	55(O) -	0/0
743	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50(O) -	0/0
744	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,075.77	05/2014 -	06/2017	-	0/0
745	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
746	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH , G	02/2015	241.61 -	241.61	7.71	02/2017 -	02/2017	-	0/1
747	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	-	0/0
748	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH , G	01/2014	361.30 200.69	207.40	44.08	07/2014 -	-	-	0/1
749	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	-	0/1
750	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/1
751	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	- -	-	-	0/1
752	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	- -	-	-	0/4
753	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
754	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH , G	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	-	0/2
755	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	-	0/4
756	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	-	0/4
757	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
758	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	-	2/4
759	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23(O) -	0/4
760	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
761	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0) - [N24000302]PWD,ANDHRA PRADESH , G	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	-	0/0
762	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	-	0/2
763	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
764	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0
765	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH , G	01/2016	1,134.97 -	1,134.97	151.85	- -	11/2018	- -	0/0
766	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH , G	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	02/2017	-	0/0
767	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH , G	03/2017	648.32 -	503.10	-	03/2020 -	03/2020	0(O) -	0/0
768	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH , G	03/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020	0(O) -	0/0
769	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
770	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0
771	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
772	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	05/2018	0(O) -	1/4
773	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
774	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0(O) -	1/4
775	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/3
776	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
777	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	09/2010	-	0/0
778	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	09/2010	-	0/0
779	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	05/2018	0(O) -	1/4
780	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH , G	01/2016	183.65 -	183.65	-	11/2016 -	11/2016	-	0/0
781	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH , G	01/2016	334.22 -	334.22	-	06/2016 -	06/2016	-	0/4
782	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH , G	04/2016	245.79 -	245.79	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
783	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH , G	04/2016	198.00 -	198.00	-	10/2016 -	10/2016	-	0/4
784	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH , G	11/2015	434.06 -	434.06	-	- -	-	-	0/0
785	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH , G	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36(O) -	0/0
786	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH , G	01/2017	1,253.10 -	1,253.10	-	03/2017 -	-	-	0/0
787	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH , G	03/2017	284.09 -	284.09	-	04/2017 -	-	-	0/0
788	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH , G	02/2017	195.23 -	195.23	-	04/2017 -	-	-	0/0
789	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH , G	02/2017	203.36 -	203.36	-	04/2017 -	-	-	0/0
790	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH , G	01/2017	194.66 -	194.66	-	04/2017 -	-	-	0/0
791	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH , G	02/2017	168.32 -	168.32	-	04/2017 -	-	-	0/0
792	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH , G	02/2017	180.57 -	180.57	-	04/2017 -	-	-	0/0
793	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH , G	02/2017	216.71 -	216.71	-	04/2017 -	-	-	0/0
794	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH , G	02/2017	167.28 -	167.28	-	04/2017 -	-	-	0/0
795	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH , G	01/2017	198.22 -	198.22	-	04/2017 -	-	-	0/0
796	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM , G	12/2003	280.00 -	361.00	-	02/2009 -	12/2017	106(O) -	0/0
797	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM , G	12/2003	199.81 -	385.13	-	04/2009 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
798	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM , G	12/2003	167.64 -	167.64	-	11/2008 -	-	-	0/0
799	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM , G	12/2003	155.04 -	280.13	-	11/2008 -	-	-	0/0
800	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM , G	12/2003	200.00 -	200.00	-	04/2009 -	05/2017	-	0/0
801	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM , G	12/2003	245.00 -	245.00	-	03/2008 -	05/2017	-	0/0
802	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM , G	12/2003	225.00 -	225.00	-	06/2008 -	09/2017	111(O) -	0/0
803	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM , G	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116(O) -	0/0
804	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM , G	12/2003	160.00 -	160.00	-	05/2008 -	05/2017	-	0/0
805	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM , G	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0
806	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM , G	12/2003	217.61 -	309.56	-	04/2010 -	03/2018	95(O) -	0/0
807	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	05/2018	0(O) -	0/4
808	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	06/2018	0(O) -	0/4
809	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	06/2018	0(O) -	0/4
810	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
811	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
812	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O) -	0/4
813	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	-	0/0
814	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	02/2011	-	0/0
815	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	0(O) -	0/0
816	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
817	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	-	12/2018 -	12/2018	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
818	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
819	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	-	-	-	-	0/0
820	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
821	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/4
822	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	-	01/2016 -	01/2016	-	0/4
823	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64(O) -	0/0
824	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	53(O) -	0/0
825	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
826	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	-	03/2014 -	09/2017	42(O) -	0/0
827	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR , G	10/2011	375.09 -	375.09	-	04/2014 -	-	-	0/0
828	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56(O) -	0/0
829	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49(O) -	0/0
830	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	-	-	-	0/0
831	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	08/2016	-	0/0
832	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	10/2016	-	0/0
833	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR , G	08/2015	556.07 -	556.07	-	-	-	-	0/0
834	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR , G	12/2015	1,041.10 -	1,041.10	-	-	04/2019	-	0/0
835	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR , G	08/2015	814.04 -	814.04	-	-	-	-	0/0
836	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR , G	08/2015	322.09 -	322.09	-	-	04/2018	-	0/0
837	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR , G	01/1991	642.41 -	642.41	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
838	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR , G	12/2015	1,167.45 -	1,167.45	-	-	-	-	0/0
839	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR , G	08/2015	399.54 -	399.54	-	-	04/2019	-	0/0
840	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR , G	01/1991	478.35 -	478.35	-	-	-	-	0/0
841	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , G	08/2015	854.80 -	854.80	-	-	12/2017	-	0/0
842	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR , G	08/2015	516.13 -	516.13	-	-	04/2018	-	0/0
843	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	-	-	-	0/0
844	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	-	-	-	0/0
845	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR , G	10/2014	377.64 -	377.64	-	03/2014	-	-	0/0
846	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR , G	10/2013	278.39 -	278.39	-	08/2014	08/2014	-	0/0
847	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR , G	01/2013	322.01 -	322.01	-	08/2014	-	-	0/0
848	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR , G	11/2013	683.83 -	683.83	-	07/2016	-	-	0/0
849	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR , G	02/2014	665.50 -	665.50	-	07/2016	-	-	0/0
850	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR , G	02/2016	178.85 -	178.85	-	05/2016	-	-	0/0
851	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR , G	02/2016	369.77 -	369.77	-	06/2016	06/2016	-	0/0
852	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR , G	02/2016	553.30 -	553.30	-	05/2016	-	-	0/0
853	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR , G	01/2014	1,408.85 -	1,408.85	-	10/2016	-	-	0/0
854	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR , G	03/2015	206.80 -	206.80	-	07/2016	10/2016	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
855	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR , G	08/2015	288.24 -	288.24	-	11/2015 -	-	-	0/0
856	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR , G	05/2015	581.84 -	581.84	-	05/2017 -	-	-	0/0
857	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR , G	08/2016	1,742.01 -	1,742.01	-	12/2016 -	12/2016	-	0/0
858	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR , G	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	0(O) -	0/0
859	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR , G	03/2017	235.48 -	227.77	-	03/2020 -	03/2020	0(O) -	0/0
860	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	03/2015	-	0/0
861	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	03/2015	-	0/0
862	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	03/2015	-	0/0
863	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
864	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
865	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0
866	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
867	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
868	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH , G	02/2013	1,232.00 -	1,232.00	1,090.17	08/2015 -	12/2017	28(O) -	0/0
869	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH , G	12/2015	596.67 -	596.67	-	- -	05/2018	-	0/0
870	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH , G	12/2015	509.13 -	509.13	-	- -	04/2018	-	0/0
871	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH , G	12/2015	726.67 -	726.67	18.03	- -	04/2018	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
872	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I), NEW - [N24000609]NHAI,DELHI , G	09/2015	771.18 -	771.18	450.78	- -	03/2018	- -	0/0
873	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	- -	04/2018	- -	0/1
874	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , G	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
875	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
876	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
877	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	- -	-	-	0/0
878	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	- -	-	-	0/0
879	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	- -	-	-	0/0
880	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63(O) -	2/3
881	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	-	07/2013 -	-	-	0/0
882	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	-	12/2015 -	07/2017	-	0/3
883	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT , G	03/2014	503.16 -	503.16	-	08/2016 -	-	-	0/0
884	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT , G	05/2016	998.18 -	998.18	-	- -	-	-	0/0
885	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT , G	05/2016	834.64 -	834.64	-	- -	-	-	0/0
886	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT , G	05/2016	723.64 -	723.64	-	- -	-	-	0/0
887	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT , G	05/2016	763.08 -	763.08	-	- -	-	-	0/0
888	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT , G	05/2016	425.60 -	425.60	-	- -	-	-	0/0
889	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT , G	05/2016	364.56 -	364.56	-	- -	-	-	0/0
890	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT , G	07/2016	829.97 -	829.97	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
891	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT , G	12/2016	417.19 -	417.19	-	-	-	-	0/0
892	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT , G	01/2017	1,251.11 -	1,251.11	-	-	-	-	0/0
893	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT , G	06/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020	0(O) -	0/0
894	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	480.18	05/2010 -	08/2017	87(O) -	0/0
895	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,882.53	11/2011 -	03/2018	76(O) -	0/0
896	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	08/2017	45(O) -	0/0
897	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA , G	08/2015	723.54 -	723.54	558.12	02/2018 -	02/2018	0(O) -	0/0
898	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA , G	10/2015	562.34 -	562.34	275.35	04/2018 -	04/2018	0(O) -	0/0
899	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA , G	12/2015	602.95 -	602.95	225.80	06/2016 -	06/2018	24(O) -	0/0
900	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA , G	01/2016	574.28 -	574.28	168.65	07/2018 -	07/2018	0(O) -	0/0
901	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	213.57	-	04/2019	-	0/0
902	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	2,137.09	-	01/2018	-	0/0
903	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA , G	11/2015	867.66 -	867.66	542.57	-	05/2018	-	0/0
904	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA , G	05/2015	600.85 -	600.85	193.80	-	05/2018	-	0/0
905	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA , G	08/2016	248.97 -	248.97	-	-	05/2019	-	0/0
906	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA , G	09/2016	1,004.67 -	1,004.67	-	-	05/2019	-	0/0
907	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA , G	03/2017	639.79 -	552.90	-	03/2020 -	03/2020	0(O) -	0/0
908	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,848.95	11/2016 -	02/2018	15(O) -	0/0
909	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH , G	09/2015	934.46 -	934.46	161.96	03/2018 -	03/2018	0(O) -	0/0
910	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH , G	02/2016	273.20 -	273.20	-	-	02/2019	-	0/0
911	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH , G	08/2016	1,583.18 -	1,583.18	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
912	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH , G	09/2016	1,273.71 -	1,273.71	-	- -	-	-	0/0
913	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH , G	10/2016	447.75 -	447.75	-	- -	-	-	0/0
914	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH , G	06/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020	0(O) -	0/0
915	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	1,662.21	07/2015 -	03/2019	44(O) -	0/0
916	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
917	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	11/2017	52(O) -	0/0
918	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,340.87	06/2014 -	12/2017	42(O) -	0/0
919	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR , G	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
920	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , G	12/2015	2,136.97 -	2,136.97	27.62	12/2018 -	12/2018	0(O) -	0/0
921	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	828.06	06/2015 -	12/2017	30(O) -	0/0
922	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND , G	09/2015	341.61 -	341.61	308.23	09/2017 -	09/2017	0(O) -	0/0
923	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND , G	02/2016	997.15 -	997.15	159.68	- -	03/2019	- -	0/0
924	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND , G	07/2016	458.03 -	458.03	-	- -	-	-	0/0
925	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND , G	08/2016	323.72 -	323.72	6.32	- -	08/2018	- -	0/0
926	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND , G	03/2017	165.50 -	172.16	-	03/2020 -	03/2020	0(O) -	0/0
927	4 LANING OF KUTCERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND , G	03/2017	239.68 -	235.90	-	03/2020 -	03/2020	0(O) -	0/0
928	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , G	09/2010	946.00 -	946.00	818.53	- -	12/2017	- -	3/3
929	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
930	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPUR - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24(O) -	0/0
931	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA , G	05/2015	709.00 -	709.00	203.50	09/2017 -	09/2017	0(O) -	0/0
932	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
933	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,283.00	08/2016 -	03/2018	19(O) -	0/0
934	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	478.00	- -	08/2018	- -	0/0
935	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA , G	03/2016	701.40 -	701.40	-	- -	-	-	0/0
936	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA , G	03/2016	870.00 -	870.00	-	- -	-	-	0/0
937	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA , G	05/2014	720.69 -	720.69	99.03	- -	-	-	0/0
938	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA , G	08/2016	1,664.20 -	1,664.20	-	- -	04/2019	- -	0/0
939	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA , G	08/2016	1,167.42 -	1,167.42	5.75	- -	03/2019	- -	0/0
940	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA , G	09/2016	950.69 -	950.69	-	- -	-	-	0/0
941	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI,KARNATAKA , G	03/2017	985.41 -	1,200.00	-	03/2020 -	03/2020	0(O) -	0/0
942	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA , G	03/2017	831.58 -	1,177.00	-	03/2020 -	03/2020	0(O) -	0/0
943	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA , G	03/2017	993.16 -	1,434.00	-	03/2020 -	03/2020	0(O) -	0/0
944	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	-	08/2012 -	-	-	0/0
945	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017	0(O) -	0/0
946	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
947	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA , G	06/2015	845.24 -	845.24	64.50	- -	11/2017	- -	0/0
948	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA , G	04/2016	804.97 -	804.97	-	- -	06/2018	- -	0/0
949	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	-	04/2013 -	09/2017	53(O) -	0/0
950	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	-	05/2013 -	07/2017	-	0/0
951	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	07/2017	-	0/0
952	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	09/2016	-	0/0
953	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
954	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	05/2015	-	0/0
955	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	02/2016	-	0/0
956	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	-	0/0
957	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	05/2017	-	0/0
958	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
959	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	08/2016	-	0/0
960	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	0(O) -	0/0
961	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	04/2015	-	0/0
962	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	02/2015	-	0/0
963	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH , G	03/2015	795.76 -	795.76	-	- -	-	-	0/0
964	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH , G	03/2015	794.30 -	794.30	-	- -	-	-	0/0
965	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , G	02/2015	327.32 -	327.32	142.73	05/2017 -	05/2017	-	0/0
966	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
967	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018	0(O) -	0/0
968	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , G	03/2015	928.83 -	928.83	-	- -	12/2017	- -	0/0
969	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	-	11/2015 -	09/2017	22(O) -	0/0
970	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH , G	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36(O) -	0/0
971	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
972	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH , G	03/2015	810.22 -	810.22	-	- -	-	-	0/0
973	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	- -	01/2019	- -	0/0
974	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	0(O) -	0/0
975	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH , G	08/2016	227.49 -	227.49	-	- -	01/2019	- -	0/0
976	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
977	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,037.05	03/2013 -	12/2017	57(O) -	0/0
978	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA , G	12/2011	942.69 -	942.69	363.09	06/2014 -	03/2018	45(O) -	0/0
979	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,785.50	02/2014 -	03/2018	49(O) -	2/2
980	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA , G	06/2014	260.39 -	260.39	87.43	11/2016 -	11/2016	-	0/2
981	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	- -	10/2017	- -	0/4
982	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	07/2016	-	0/12
983	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	- -	06/2017	-	0/4
984	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	11/2016	-	0/4

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
985	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	- -	-	-	0/0
986	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	65.16	- 03/2013	-	-	0/0
987	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	205.97	- 11/2014	11/2014	-	0/0
988	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
989	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	-	0/0
990	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA , G	09/2015	414.51 -	414.00	-	- -	05/2018	-	0/0
991	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA , G	10/2015	531.13 -	531.13	-	- -	05/2018	-	0/0
992	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	-	0/0
993	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA , G	10/2015	593.26 -	593.26	-	- -	05/2018	-	0/0
994	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA , G	12/2015	649.50 -	649.50	-	- -	03/2019	-	0/0
995	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA , G	08/2015	505.00 -	505.00	-	- -	05/2018	-	0/0
996	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,425.94	07/2017 -	01/2018	6(O) -	0/0
997	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	465.52	11/2016 -	11/2017	12(O) -	0/0
998	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA , G	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
999	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,595.24	01/2018 -	01/2018	0(O) -	0/0
1000	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA , G	04/2010	1,170.52 -	1,170.52	2,082.05	06/2012 -	03/2018	69(O) -	0/0
1001	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA , G	01/2014	292.98 -	292.98	95.60	11/2014 -	11/2014	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1002	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA , G	03/2016	197.69 -	197.69	-	- -	07/2018	- -	0/0
1003	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA , G	03/2016	546.00 -	546.00	-	- -	07/2019	- -	0/0
1004	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA , G	03/2016	591.66 -	591.66	-	- -	07/2019	- -	0/0
1005	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA , G	03/2016	244.00 -	244.00	-	- -	07/2018	- -	0/0
1006	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA , G	03/2016	1,142.62 -	1,142.62	-	- -	-	-	0/0
1007	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA , G	03/2016	1,101.58 -	1,101.58	-	- -	-	-	0/0
1008	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA , G	11/2016	1,071.61 -	1,071.61	-	- -	-	-	0/0
1009	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA , G	11/2016	1,064.88 -	1,064.88	-	- -	-	-	0/0
1010	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA , G	11/2016	400.25 -	400.25	-	- -	03/2019	- -	0/0
1011	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA , G	11/2016	446.17 -	446.17	-	- -	03/2019	- -	0/0
1012	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA , G	11/2016	290.73 -	290.73	-	- -	-	-	0/0
1013	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA , G	01/2017	244.90 -	244.90	10.85	- -	05/2019	- -	0/0
1014	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA , G	02/2017	904.16 -	904.16	-	02/2020 -	02/2020	0(O) -	0/0
1015	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA , G	03/2017	247.02 -	157.49	-	03/2020 -	03/2020	0(O) -	0/0
1016	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA , G	03/2017	744.64 -	982.00	-	03/2020 -	03/2020	0(O) -	0/0
1017	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA , G	03/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020	0(O) -	0/0
1018	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA , G	03/2017	988.34 -	1,043.28	-	03/2020 -	03/2020	0(O) -	0/0
1019	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA , G	03/2017	1,059.73 -	1,071.00	-	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1020	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA , G	03/2017	296.19 -	254.00	-	03/2020 -	05/2019	-10(O) -	0/0
1021	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA , G	03/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020	0(O) -	0/0
1022	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	672.32	01/2014 -	03/2018	50(O) -	0/0
1023	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	02/2011	-	0/0
1024	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA , G	12/2015	479.20 -	479.20	6.14	- -	05/2018	- -	0/0
1025	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
1026	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0
1027	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	10/2010	-	0/0
1028	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
1029	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	09/2017	73(O) -	2/2
1030	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40(O) -	0/0
1031	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49(O) -	0/0
1032	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,095.01	03/2013 -	11/2017	56(O) -	0/0
1033	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	2,447.73	04/2015 -	12/2017	32(O) -	0/0
1034	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	- -	-	-	0/0
1035	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE , G	09/2015	788.51 -	788.51	301.95	03/2018 -	03/2018	0(O) -	0/0
1036	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE , G	09/2016	1,244.10 -	1,244.10	-	- -	-	-	0/0
1037	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1038	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND , G	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36(O) -	0/0
1039	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND , G	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36(O) -	0/0
1040	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND , G	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36(O) -	0/0
1041	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND , G	02/2017	507.68 -	507.68	-	04/2017 -	-	-	0/0
1042	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	-	09/2014 -	-	-	0/0
1043	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	-	06/2014 -	06/2017	-	0/0
1044	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 251.92	218.63	29.27	10/2017 -	10/2017	0(O) -	0/0
1045	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	-	0/0
1046	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , G	01/1991	229.41 265.35	229.41	6.65	05/2018 -	05/2018	0(O) -	0/0
1047	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	-	0/0
1048	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , G	07/2015	1,282.94 -	1,282.94	-	- -	-	-	0/0
1049	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA , G	12/2015	752.28 -	752.28	-	- -	-	-	0/0
1050	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	0(O) -	0/0
1051	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
1052	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA , G	02/2016	1,069.65 -	1,069.65	-	- -	-	-	0/0
1053	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA , G	09/2016	2,510.04 -	2,510.04	-	- -	08/2019	-	0/0
1054	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA , G	10/2016	1,008.96 -	1,008.96	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1055	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA , G	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	-	0/0
1056	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA , G	01/2015	326.63 327.00	327.00	-	04/2018 -	04/2018	0(O) -	0/0
1057	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA , G	02/2015	239.91 240.00	240.00	-	10/2017 -	10/2017	0(O) -	0/0
1058	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA , G	03/2015	226.31 226.00	226.00	-	10/2017 -	10/2017	0(O) -	0/0
1059	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA , G	12/2013	319.80 320.00	320.00	-	05/2016 -	03/2017	-	0/0
1060	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA , G	07/2014	342.05 342.00	342.00	-	01/2017 -	08/2017	7(O) -	0/0
1061	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA , G	08/2013	171.96 172.00	172.00	-	06/2016 -	03/2017	-	0/0
1062	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA , G	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5(O) -	0/0
1063	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA , G	03/2014	162.51 163.00	163.00	-	05/2016 -	03/2017	-	0/0
1064	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA , G	03/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020	0(O) -	0/0
1065	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1066	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1067	4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1068	4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1069	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB , G	01/2014	523.85 -	523.85	236.85	01/2016 -	12/2017	23(O) -	0/0
1070	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1071	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1072	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1073	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1074	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1075	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1076	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1077	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1078	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1079	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB , G	09/2015	273.06 -	273.06	36.58	- -	11/2017	- -	0/0
1080	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , G	09/2014	479.00 -	479.00	396.40	- -	12/2017	- -	0/0
1081	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , G	12/2015	239.23 -	239.23	154.94	12/2017 -	12/2017	0(O) -	0/0
1082	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB , G	10/2015	447.29 -	447.29	41.51	12/2017 -	04/2019	16(O) -	0/0
1083	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1084	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1085	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB , G	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	- -	0/0
1086	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB , G	08/2016	1,169.61 -	1,169.61	-	- -	-	-	0/0
1087	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB , G	03/2017	754.54 -	756.27	-	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1088	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN , G	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
1089	DEOLI KOTA - [N24000148]NHAI, RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	51(O) -	0/0
1090	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN , G	03/2014	240.10 -	240.10	-	03/2016 -	-	-	0/0
1091	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH, RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1092	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH, RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1093	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH, RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
1094	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH, RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
1095	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH, RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1096	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
1097	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN , G	08/2015	538.08 -	538.08	-	02/2018 -	02/2018	0(O) -	0/0
1098	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN , G	09/2014	425.19 -	425.19	-	09/2016 -	09/2017	12(O) -	0/0
1099	JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN , G	08/2015	482.27 -	482.27	-	02/2018 -	02/2018	0(O) -	0/0
1100	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN , G	07/2015	455.60 -	455.60	-	07/2017 -	07/2017	-	0/0
1101	PADI - DAHOD - [N24000353]NHAI, RAJASTHAN , G	11/2014	279.14 -	279.14	-	05/2017 -	-	-	0/0
1102	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN , G	10/2014	264.72 -	264.72	-	04/2017 -	-	-	0/0
1103	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN , G	09/2015	567.51 -	567.51	-	03/2018 -	03/2018	0(O) -	0/0
1104	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH, RAJASTHAN , G	01/1991	269.26 -	269.26	212.72	10/2016 -	10/2016	-	0/0
1105	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH, RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	206.78	05/2016 -	05/2016	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1106	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN , G	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6(O) -	0/0
1107	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	-	08/2016 -	-	-	0/0
1108	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	-	04/2018 -	04/2018	0(O) -	0/0
1109	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1110	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1111	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,130.07	10/2011 -	12/2017	74(O) -	0/0
1112	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN , G	08/2015	275.90 -	275.90	-	- -	02/2018	- -	0/0
1113	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019 -	06/2019	0(O) -	0/0
1114	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019 -	06/2019	0(O) -	0/0
1115	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN , G	06/2016	649.00 -	649.00	-	06/2019 -	06/2019	0(O) -	0/0
1116	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN , G	07/2016	688.70 -	688.70	-	- -	-	-	0/0
1117	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN , G	07/2016	331.46 -	331.46	-	- -	10/2018	- -	0/0
1118	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN , G	08/2016	320.30 -	320.30	-	- -	-	-	0/0
1119	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN , G	09/2016	1,239.82 -	1,239.82	-	- -	-	-	0/0
1120	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN , G	09/2016	1,100.19 -	1,100.19	-	- -	-	-	0/0
1121	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN , G	12/2016	1,031.95 -	1,031.95	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1122	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN , G	04/2017	894.00 -	894.00	-	04/2020 -	04/2020	0(O) -	0/0
1123	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM , G	04/2013	151.59 -	151.59	-	08/2013 -	-	-	0/0
1124	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
1125	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1126	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	-	10/2017 -	10/2017	0(O) -	0/0
1127	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	911.01	03/2013 -	06/2017	-	0/0
1128	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.03	12/2013 -	12/2017	48(O) -	0/0
1129	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU , G	06/2011	600.00 -	600.00	319.76	06/2013 -	-	-	0/0
1130	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55(O) -	0/0
1131	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52(O) -	0/0
1132	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1133	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
1134	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	-	07/2015 -	-	-	0/0
1135	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	08/2015	-	0/0
1136	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU , G	05/2015	1,387.11 -	1,387.11	617.98	11/2017 -	11/2017	0(O) -	0/0
1137	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU , G	06/2015	563.92 -	563.92	87.82	12/2017 -	06/2018	6(O) -	0/0
1138	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU , G	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1139	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU , G	11/2014	563.92 -	563.92	186.50	11/2016 -	08/2017	9(O) -	0/0
1140	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1141	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU , G	02/2016	707.82 -	707.82	129.75	- -	08/2018	- -	0/0
1142	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU , G	02/2016	641.17 -	641.17	37.95	- -	07/2018	- -	0/0
1143	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU , G	03/2017	848.45 -	848.45	-	03/2020 -	03/2020	0(O) -	0/0
1144	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	64.90	07/2016 -	07/2016	-	0/0
1145	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	1,337.00	09/2016 -	03/2018	18(O) -	0/0
1146	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1147	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1148	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1149	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
1150	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1151	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	-	0/4
1152	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	-	0/1
1153	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	-	0/0
1154	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA , G	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1155	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA , G	12/2015	1,423.96 -	1,423.96	454.64	- -	11/2018	- -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1156	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018	0(O) -	0/4
1157	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL, TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	04/2017	-	0/4
1158	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	09/2017	51(O) -	0/0
1159	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	08/2017	48(O) -	0/0
1160	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	564.90	09/2013 -	10/2017	49(O) -	0/0
1161	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47(O) -	0/0
1162	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25(O) -	0/0
1163	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH, UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
1164	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH, UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	03/2016	-	0/0
1165	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH, UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	-	0/0
1166	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH , G	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13(O) -	0/0
1167	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH , G	04/2014	351.34 -	351.34	378.36	01/2016 -	11/2017	22(O) -	0/0
1168	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH , G	09/2015	368.73 -	368.73	197.99	09/2016 -	09/2017	12(O) -	0/0
1169	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH , G	06/2014	301.04 -	301.04	146.23	01/2016 -	-	-	0/0
1170	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH , G	04/2014	495.78 -	495.78	498.08	01/2016 -	11/2017	22(O) -	0/0
1171	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	-	0/0
1172	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD, UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	-	0/0
1173	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP, UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	-	0/0
1174	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1175	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	03/2017	-	0/0
1176	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	-	0/0
1177	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	-	0/0
1178	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH , G	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(O) -	0/0
1179	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH , G	09/2015	664.53 -	664.53	31.87	03/2018 -	03/2018	0(O) -	0/0
1180	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH , G	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(O) -	0/0
1181	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH , G	09/2015	785.78 -	785.78	531.15	03/2018 -	03/2018	0(O) -	0/0
1182	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	120.00	- -	01/2019	- -	0/0
1183	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH , G	12/2015	611.65 -	611.65	208.32	06/2016 -	06/2018	24(O) -	0/0
1184	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH , G	01/2016	815.28 -	815.28	84.46	06/2018 -	06/2018	0(O) -	0/0
1185	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH , G	01/2016	1,027.53 -	1,027.53	142.48	06/2018 -	06/2018	0(O) -	0/0
1186	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH , G	06/2016	667.00 -	667.00	108.23	07/2018 -	06/2018	-1(O) -	0/0
1187	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH , G	12/2015	667.00 -	667.00	147.98	06/2018 -	06/2018	0(O) -	0/0
1188	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	08/2015	-	0/0
1189	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1190	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1191	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH , G	01/2016	683.24 -	683.24	.45	- -	-	-	0/0
1192	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH , G	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0
1193	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH , G	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
1194	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH , G	03/2016	676.73 -	676.73	41.58	- -	04/2019	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1195	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH , G	03/2016	1,404.50 -	1,404.50	2.22	- -	-	-	0/0
1196	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH , G	03/2016	1,396.74 -	1,396.74	-	- -	-	-	0/0
1197	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH , G	03/2016	1,587.49 -	1,587.49	-	- -	04/2019	- -	0/0
1198	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH , G	03/2016	899.00 -	899.00	-	- -	04/2019	- -	0/0
1199	4-LANNING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH , G	03/2016	1,668.00 -	1,668.00	-	- -	-	-	0/0
1200	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH , G	03/2016	1,408.00 -	1,408.00	-	- -	-	-	0/0
1201	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH , G	03/2016	1,737.00 -	1,737.00	-	- -	-	-	0/0
1202	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH , G	08/2016	2,016.00 -	2,016.00	-	- -	04/2019	- -	0/0
1203	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH , G	12/2016	534.55 -	534.55	-	- -	-	-	0/0
1204	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH , G	01/2017	450.68 -	450.68	-	- -	-	-	0/0
1205	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH , G	03/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020	0(O) -	0/0
1206	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH , G	03/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020	0(O) -	0/0
1207	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH , G	03/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020	0(O) -	0/0
1208	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH , G	03/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020	0(O) -	0/0
1209	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND , G	11/2011	478.51 -	478.00	401.67	10/2013 -	12/2017	50(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1210	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND , G	03/2016	720.00 -	720.00	-	-	-	-	0/0
1211	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND , G	03/2016	1,443.00 -	1,443.00	-	-	-	-	0/0
1212	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND , G	11/2012	605.84 -	605.84	547.57	-	07/2018	-	0/0
1213	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,382.75	08/2013 -	12/2017	52(O) -	0/0
1214	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,927.60	08/2013 -	03/2018	55(O) -	0/0
1215	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,678.94	09/2014 -	12/2017	39(O) -	0/0
1216	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	483.91	07/2014 -	03/2018	44(O) -	0/0
1217	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1218	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL , G	01/1991	322.00 -	322.00	56.41	03/2018 -	03/2018	0(O) -	0/0
1219	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL , G	10/2015	361.15 -	361.15	-	-	01/2018	-	0/0
1220	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL , G	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018	0(O) -	0/0
1221	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	2,091.52	-	12/2017	-	0/0
1222	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL , G	03/2016	229.37 -	229.37	28.51	-	11/2018	-	0/0
1223	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL , G	09/2016	767.03 -	767.03	35.56	-	08/2018	-	0/0
	Total		3,17,373.88 -	3,23,746.08	89,417.90				23/182
	SHIPPING AND PORTS								
1224	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA , G	03/2007	245.67 -	409.83	350.68	04/2009 -	-	-	0/0
1225	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96(O) -	0/0
1226	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1227	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141(O) -	0/0
1228	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	235.15	98.60	06/2017 -	-	-	0/1
1229	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017	0(O) -	0/1
1230	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU , G	12/2014	274.85 -	274.85	43.83	04/2017 -	-	-	0/1
1231	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , G	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
	Total		4,117.75 -	5,085.02	1,875.38				0/3
	<u>TELECOMMUNICATIONS</u>								
1232	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI , G	06/2016	418.26 -	418.26	-	06/2017 -	-	-	0/0
1233	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , G	03/2012	13,334.00 -	13,334.00	-	07/2015 -	09/2017	26(O) -	0/0
1234	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		15,863.43 -	15,763.43	253.90				0/70
	<u>URBAN DEVELOPMENT</u>								
1235	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH , G	06/2014	157.84 -	157.84	93.97	03/2017 -	-	-	0/5
1236	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH , G	08/2007	246.90 -	246.90	-	- -	-	-	0/0
1237	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR , G	02/2016	496.18 496.00	496.18	-	06/2017 -	-	-	0/0
1238	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI , G	09/2011	38,585.00 -	38,585.00	30,035.84	03/2016 -	12/2016	-	0/0
1239	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI , G	10/2013	1,219.21 2,230.23	1,219.21	109.75	10/2019 -	03/2020	5(O) -	0/0
1240	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI , G	05/2012	405.01 -	405.01	349.54	12/2014 07/2017	07/2017	-	2/3
1241	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI , G	07/2012	884.30 -	884.30	466.05	12/2015 12/2017	03/2018	27(O) 3(R)	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1242	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI , G	06/2012	4,264.00 -	4,118.00	2,661.40	11/2019 -	11/2019	0(O) -	1/7
1243	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI , G	06/2015	197.33 -	197.33	3.06	- -	04/2019	- -	0/2
1244	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH , G	11/2012	270.83 -	270.83	114.89	11/2014 -	03/2018	40(O) -	0/0
1245	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND , G	09/2012	171.86 -	171.86	38.40	03/2016 -	12/2018	33(O) -	1/6
1246	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA , G	05/2006	6,395.00 13,845.01	13,845.01	14,200.11	06/2011 12/2015	04/2017	-	3/3
1247	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA , G	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1248	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA , G	12/2016	246.31 -	246.31	-	02/2020 -	02/2020	0(O) -	0/0
1249	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA , G	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65(O) 11(R)	0/1
1250	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA , G	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29(O) -	0/0
1251	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA , G	07/2015	154.00 -	154.00	62.77	11/2015 -	12/2017	25(O) -	0/0
1252	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH , G	12/2012	188.87 -	188.87	168.97	12/2015 12/2017	12/2017	24(O) 0(R)	0/0
1253	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC	12/2016	164.00 -	164.00	55.98	01/2018 03/2018	03/2018	2(O) 0(R)	1/10
1254	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA , G	02/2011	241.33 349.33	349.33	218.90	03/2016 12/2017	12/2017	21(O) 0(R)	0/13
1255	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA , G	06/2010	205.00 166.97	170.62	128.00	03/2012 03/2018	03/2018	72(O) 0(R)	11/20
1256	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA , G	12/2012	315.00 -	315.00	300.77	06/2015 -	09/2017	27(O) -	8/8
1257	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA , G	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21(O) -	0/0
1258	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA , G	07/2013	23,136.00 -	23,136.00	-	01/2015 -	-	-	0/0
1259	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44(O) -	0/10
1260	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB , G	02/2014	388.00 -	388.00	251.69	05/2017 08/2017	08/2017	3(O) 0(R)	7/12
1261	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB , G	08/2016	294.00 -	294.00	11.87	04/2019 -	04/2019	0(O) -	0/8

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1262	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN , Central Sector Projects	08/2014	350.02 479.87	350.02	347.68	03/2015 12/2017	12/2017	33(O) 0(R)	0/0
1263	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU , G	04/2014	332.72 -	332.72	248.10	09/2016 -	11/2017	14(O) -	0/0
1264	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU , G	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24(O) -	11/24
1265	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD, TAMIL NADU , G	12/2015	209.00 -	209.00	9.00	- -	-	-	0/6
1266	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL, TAMIL NADU , G	06/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018	0(O) -	0/0
1267	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD, TELANGANA , G	10/2016	209.84 -	209.84	.26	03/2020 -	03/2020	0(O) -	0/5
1268	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH , G	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1269	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND , G	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70(O) -	0/0
1270	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL , G	02/2014	156.57 -	156.57	109.90	08/2016 -	03/2018	19(O) -	7/13
	Total		1,45,945.23 -	1,57,932.60	71,466.44				52/156
	<u>DEFENCE PRODUCTION</u>								
1271	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA , G	12/2016	167.69 168.00	172.99	21.52	05/2018 -	05/2018	0(O) -	1/5
1272	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL, GOA , G	12/2016	285.95 286.00	296.05	29.85	08/2020 -	08/2020	0(O) -	1/3
	Total		453.64 -	469.04	51.37				2/8
	Grand Total		15,89,750.53	17,71,039.29	6,89,034.34				2190/3985


Summary of projects in the Flash Report for the month of August, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1257
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects elevated to the status of Major project during the current month	4
Number of Projects Added in Current Month	12
Number of Projects in Current Month	1272

Brief Analysis


Project Status with respect to Original Schedule: Out of 1272 projects, 12 projects are ahead of schedule, 308 projects are on schedule 296 projects are delayed. 533 projects do not have fixed dates of commissioning. 123 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

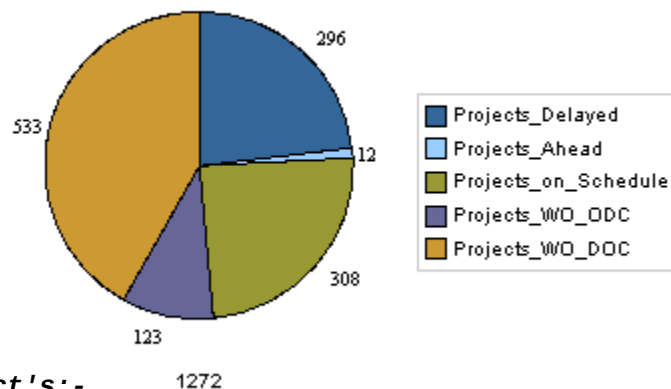

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1272 projects when sanctioned, was of the order of Rs. 1589750.53 crore but this was subsequently revised to Rs. 1771039.29 crore implying a cost overrun of 11.4%. The expenditure incurred on these projects till August, 2017 is Rs. 689034.34 crore, which is 38.9% of the anticipated cost of the projects.

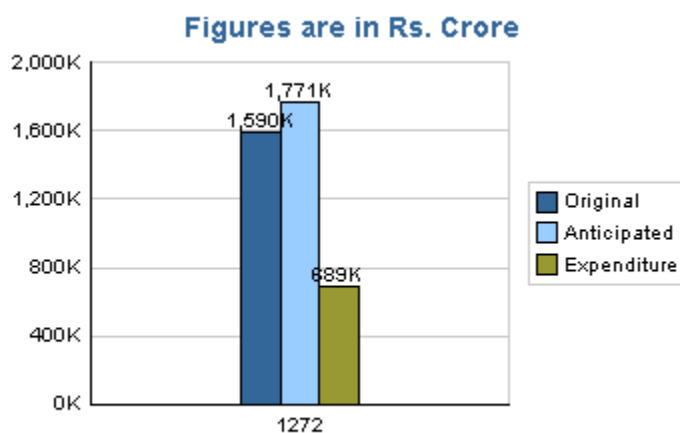

Sector wise current status of projects on the Flash Report

ATOMIC ENERGY

Current Status:


Number of Projects 4

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed. 1 project does not have fixed dates of commissioning.

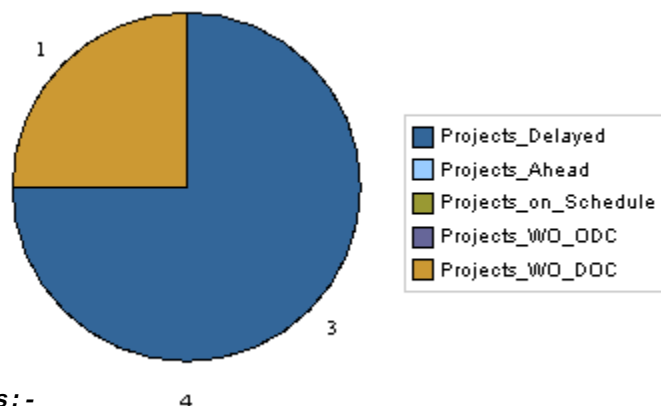


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 52241 crore implying a cost overrun of 29.2%. The expenditure incurred on these projects till August, 2017 is Rs. 46316.55 crore, which is 88.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

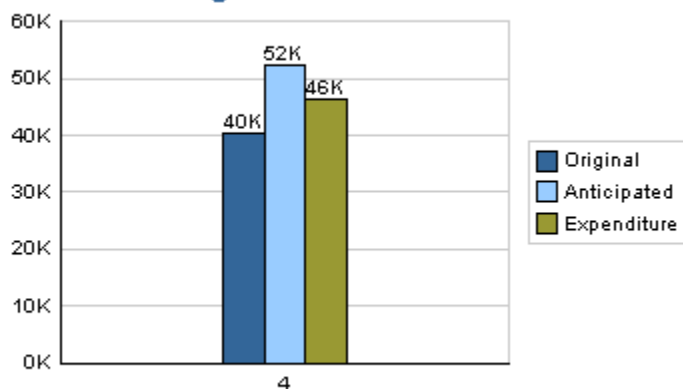

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:


Number of Projects **3**

Number of Projects Delayed **2**

Number of Projects Without Date Of Commissioning **1**

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed. 1 project does not have fixed dates of commissioning.

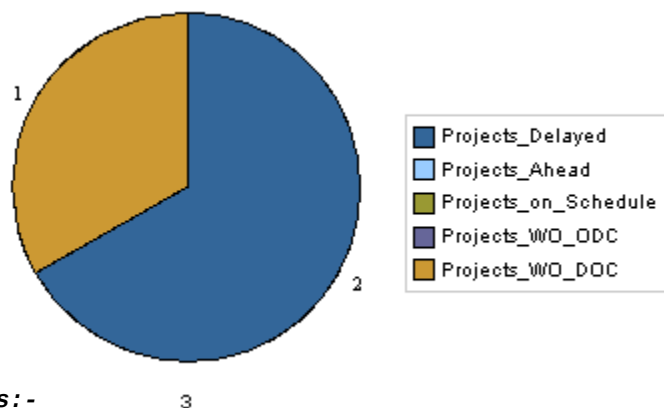


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 959.68 crore but this was subsequently anticipated to Rs. 1312.86 crore implying a cost overrun of 36.8%. The expenditure incurred on these projects till August, 2017 is Rs. 814.48 crore, which is 62% of the anticipated cost of the projects.

Figures are in Rs. Crore

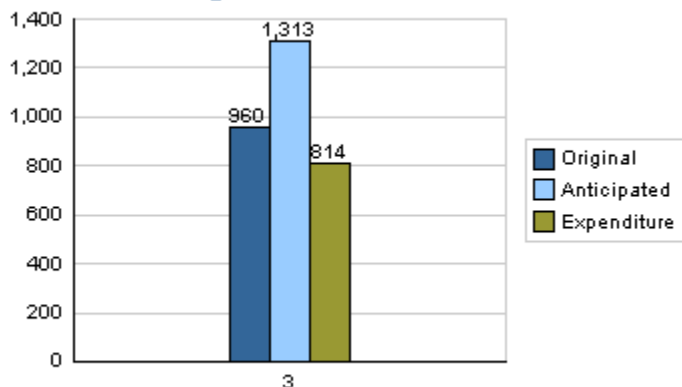

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	92
Number of Projects On Schedule	50
Number of Projects Delayed	39

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 92 projects, 50 projects are on schedule 39 projects are delayed. 3 projects do not have fixed dates of commissioning.

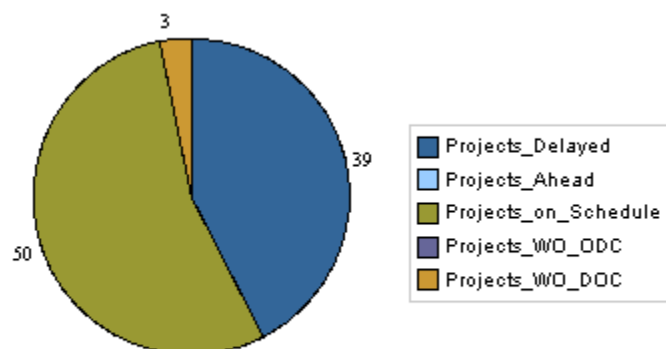


Total No Of Project's:-

92

Investment Scenario

Total original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 88124.99 crore but this was subsequently anticipated to Rs. 88310.36 crore implying a cost overrun of .2%. The expenditure incurred on these projects till August, 2017 is Rs. 21040.79 crore, which is 23.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

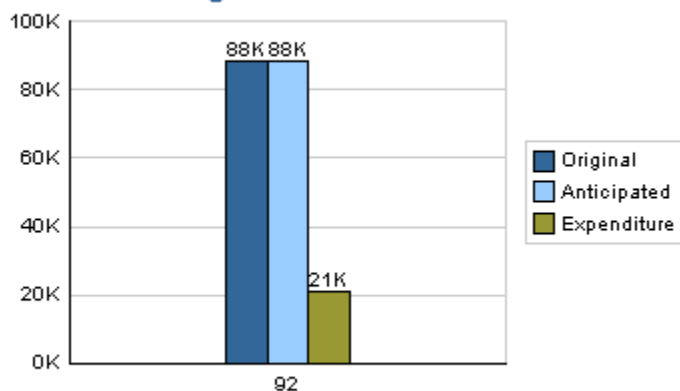

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

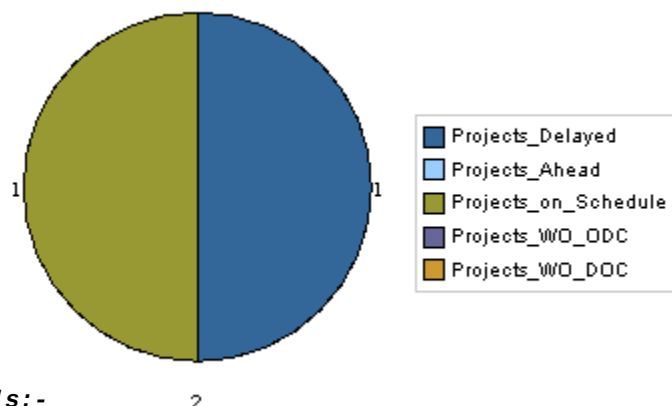


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 703.44 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till August, 2017 is Rs. 466.62 crore, which is 66.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

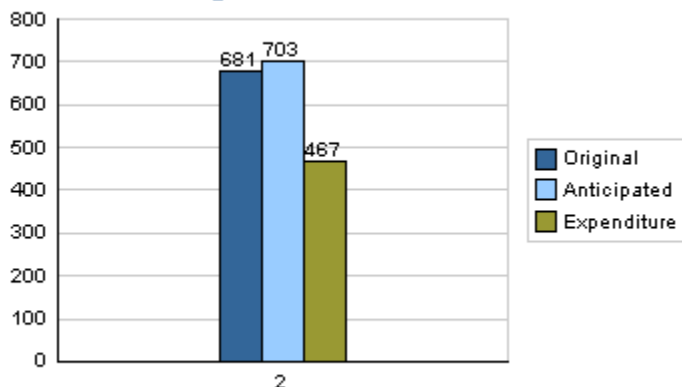

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	4
Number of Projects On Schedule	2

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule 2 projects do not have fixed dates of commissioning.

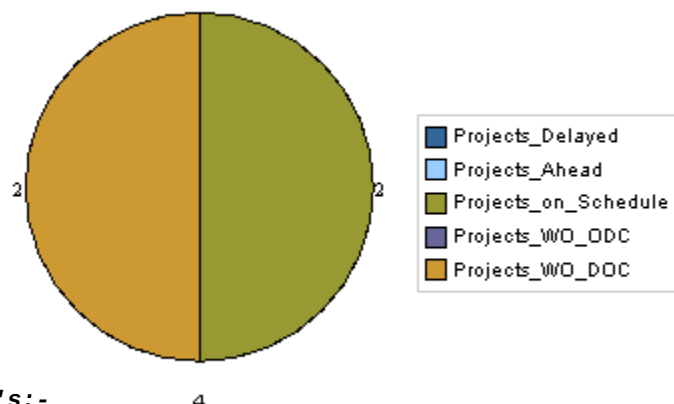


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6773.63 crore but this was subsequently anticipated to Rs. 6773.63 crore The expenditure incurred on these projects till August, 2017 is Rs. 372.63 crore, which is 5.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

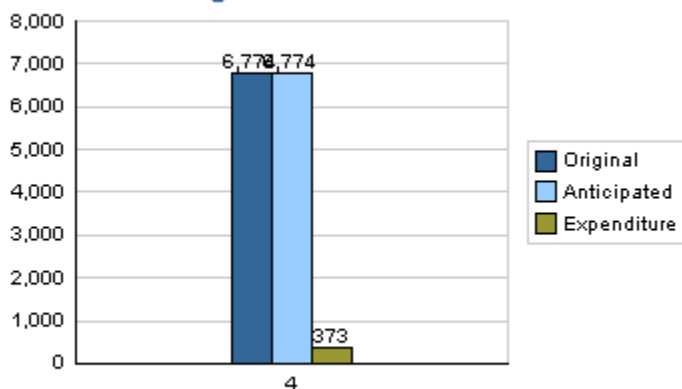

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	34
Number of Projects On Schedule	9
Number of Projects Delayed	17

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 34 projects, 9 projects are on schedule 17 projects are delayed. 7 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

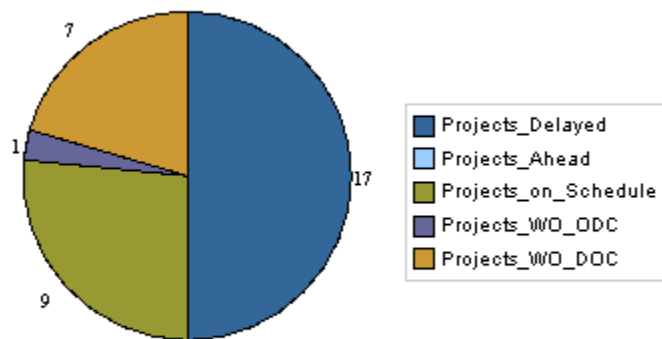


Total No Of Project's:-

34

Investment Scenario

Total original cost of implementation of 34 projects when sanctioned, was of the order of Rs. 57349.49 crore but this was subsequently anticipated to Rs. 57563.17 crore implying a cost overrun of .4%. The expenditure incurred on these projects till August, 2017 is Rs. 38300.26 crore, which is 66.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

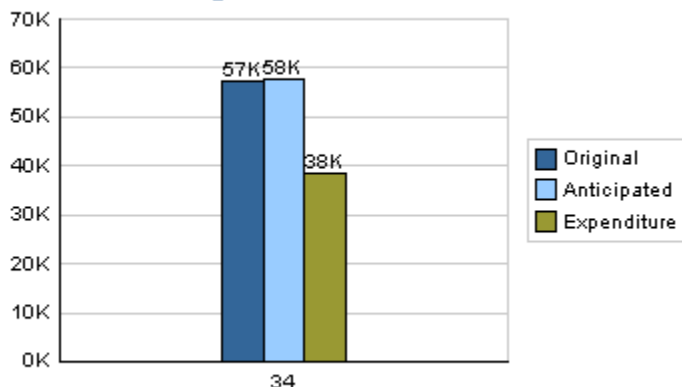

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	108
Number of Projects On Schedule	54
Number of Projects Delayed	33
Number of Projects Ahead	7
Number of Projects Without Date Of Commissioning	14

Brief Analysis

Project Status with respect to Original Schedule: Out of 108 projects, 7 projects are ahead of schedule, 54 projects are on schedule 33 projects are delayed. 14 projects do not have fixed dates of commissioning.

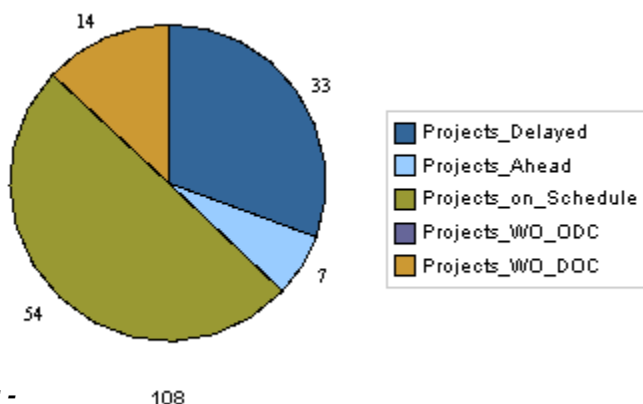


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 108 projects when sanctioned, was of the order of Rs. 208215.16 crore but this was subsequently anticipated to Rs. 209608.54 crore implying a cost overrun of .7%. The expenditure incurred on these projects till August, 2017 is Rs. 67811.31 crore, which is 32.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

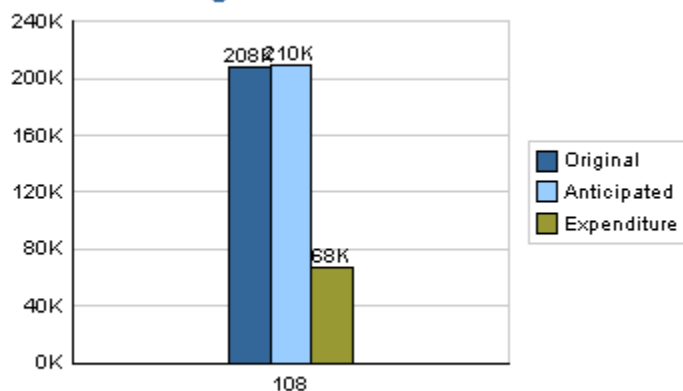

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	127
Number of Projects On Schedule	50
Number of Projects Delayed	60
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	14

Brief Analysis

Project Status with respect to Original Schedule: Out of 127 projects, 3 projects are ahead of schedule, 50 projects are on schedule 60 projects are delayed. 14 projects do not have fixed dates of commissioning.

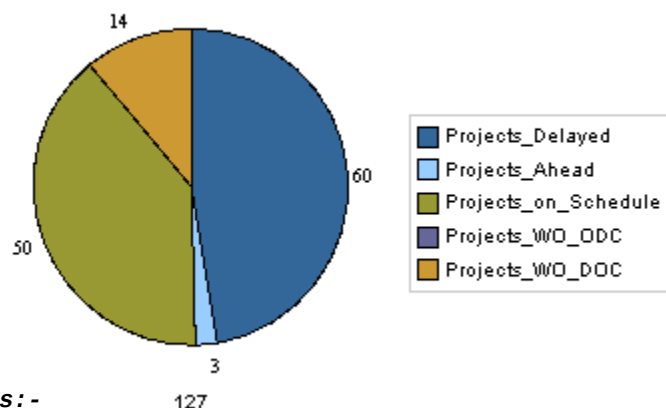


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 344032.76 crore but this was subsequently anticipated to Rs. 397114.95 crore implying a cost overrun of 15.4%. The expenditure incurred on these projects till August, 2017 is Rs. 230735.18 crore, which is 58.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

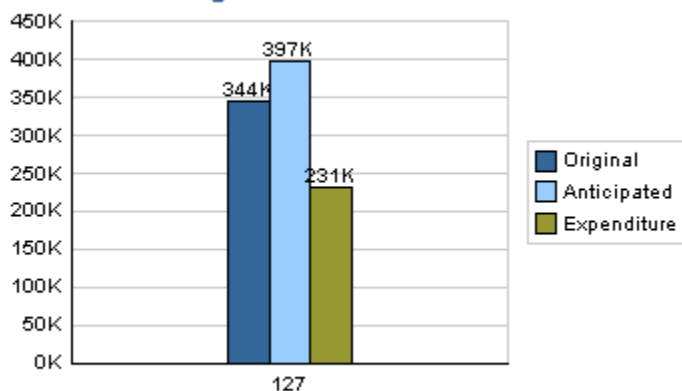

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.



Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till August, 2017 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.

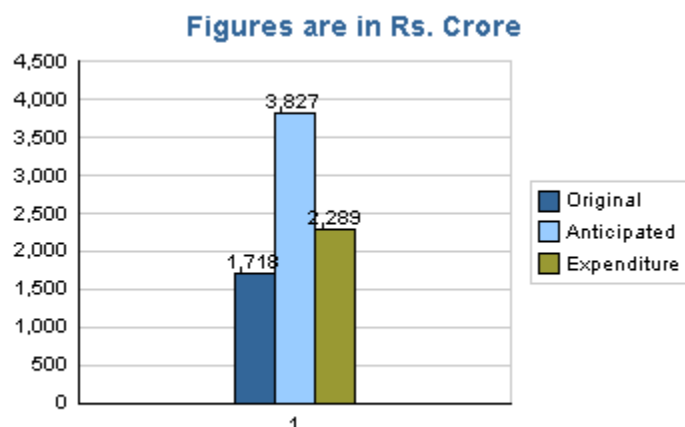

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	13
Number of Projects On Schedule	3
Number of Projects Delayed	5

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 3 projects are on schedule 5 projects are delayed. 5 projects do not have fixed dates of commissioning.

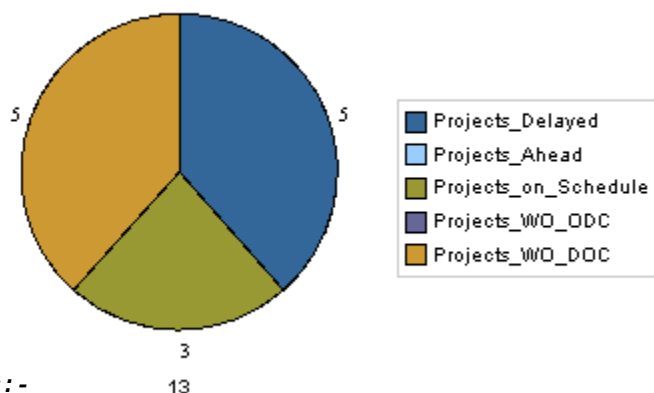


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 3637.08 crore but this was subsequently anticipated to Rs. 3649.38 crore implying a cost overrun of .3%. The expenditure incurred on these projects till August, 2017 is Rs. 1751.45 crore, which is 48% of the anticipated cost of the projects.

Figures are in Rs. Crore

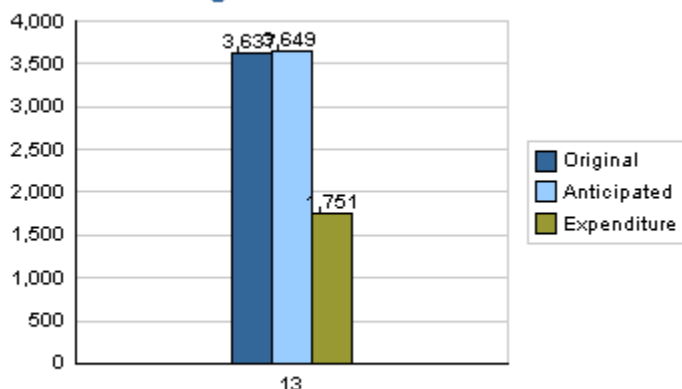

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	353
Number of Projects On Schedule	41
Number of Projects Delayed	34

Number of Projects Without Original Date of Commissioning	55
Number of Projects Without Date Of Commissioning	223

Brief Analysis

Project Status with respect to Original Schedule: Out of 353 projects, 41 projects are on schedule 34 projects are delayed. 223 projects do not have fixed dates of commissioning. 55 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

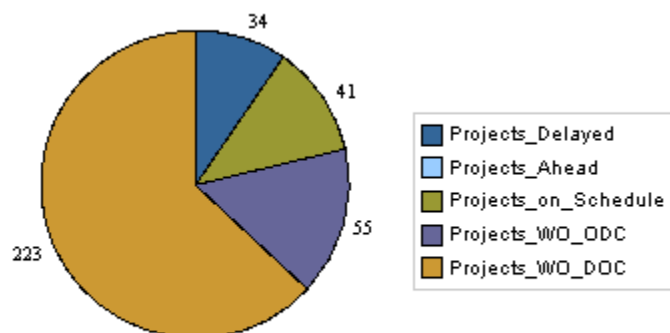


Total No Of Project's:-

353

Investment Scenario

Total original cost of implementation of 353 projects when sanctioned, was of the order of Rs. 354063.17 crore but this was subsequently anticipated to Rs. 446938.49 crore implying a cost overrun of 26.2%. The expenditure incurred on these projects till August, 2017 is Rs. 116071.08 crore, which is 26% of the anticipated cost of the projects.

Figures are in Rs. Crore

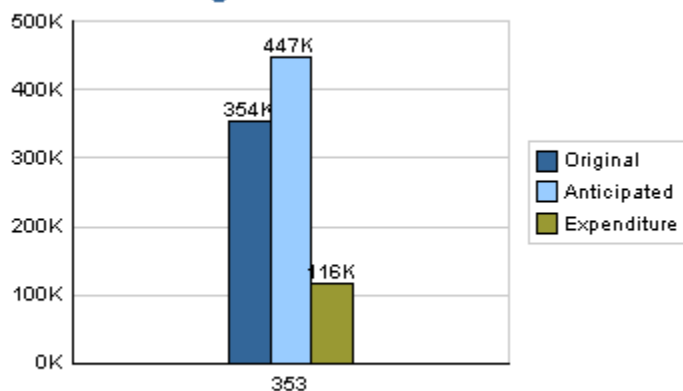

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	482
Number of Projects On Schedule	88
Number of Projects Delayed	77
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	66
Number of Projects Without Date Of Commissioning	249

Brief Analysis

Project Status with respect to Original Schedule: Out of 482 projects, 2 projects are ahead of schedule, 88 projects are on schedule 77 projects are delayed. 249 projects do not have fixed dates of commissioning. 66 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

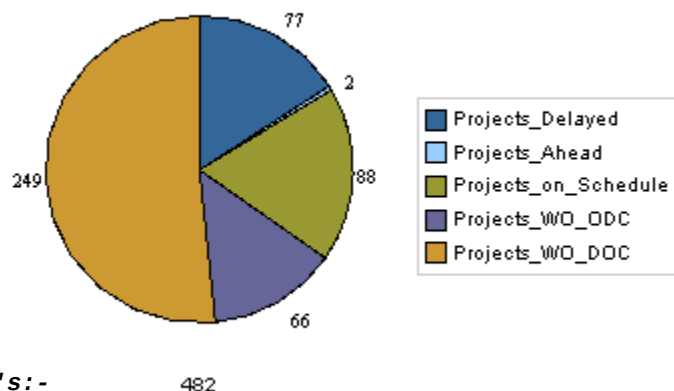


Total No Of Project's:-

482

Investment Scenario

Total original cost of implementation of 482 projects when sanctioned, was of the order of Rs. 317373.88 crore but this was subsequently anticipated to Rs. 323746.08 crore implying a cost overrun of 2%. The expenditure incurred on these projects till August, 2017 is Rs. 89417.9 crore, which is 27.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

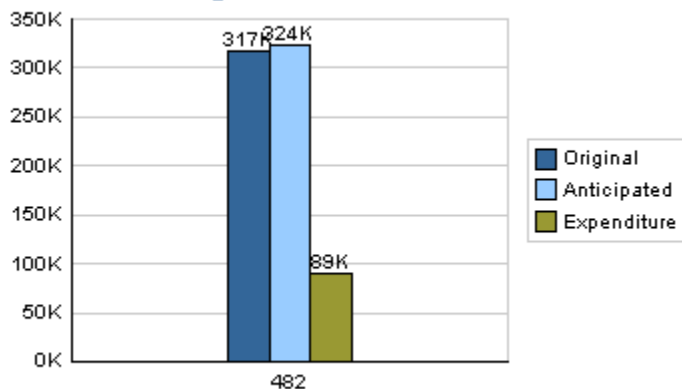

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule 2 projects are delayed. 4 projects do not have fixed dates of commissioning.

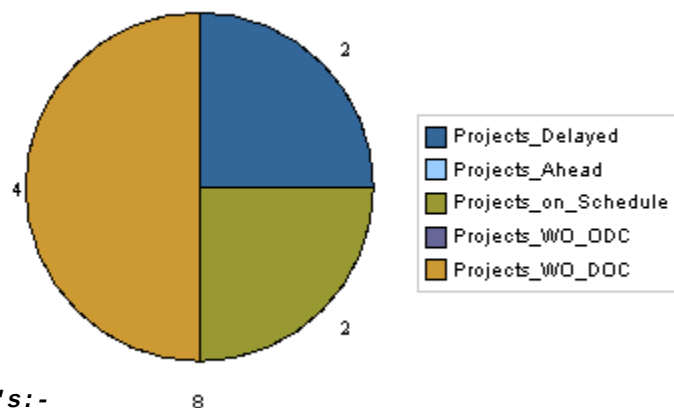


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5085.02 crore implying a cost overrun of 23.5%. The expenditure incurred on these projects till August, 2017 is Rs. 1875.38 crore, which is 36.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

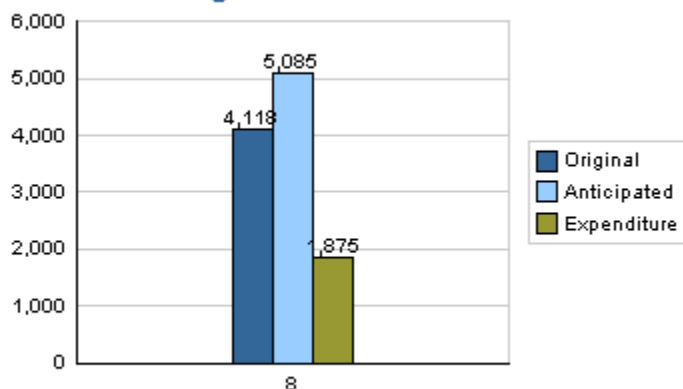

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:


Number of Projects **3**

Number of Projects Delayed **1**

Number of Projects Without Date Of Commissioning **2**

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 1 project is delayed. 2 projects do not have fixed dates of commissioning.

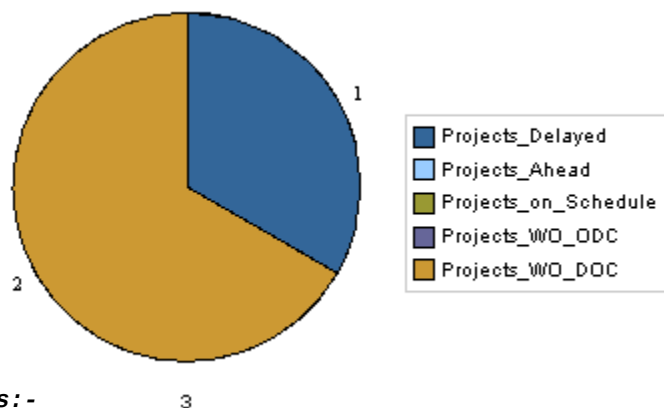


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15863.43 crore but this was subsequently anticipated to Rs. 15763.43 cr The expenditure incurred on these projects till August, 2017 is Rs. 253.9 crore, which is 1.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

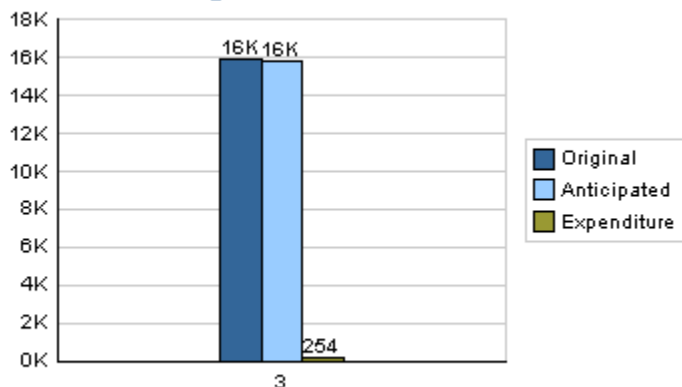

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	36
Number of Projects On Schedule	6
Number of Projects Delayed	21

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 36 projects, 6 projects are on schedule 21 projects are delayed. 8 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

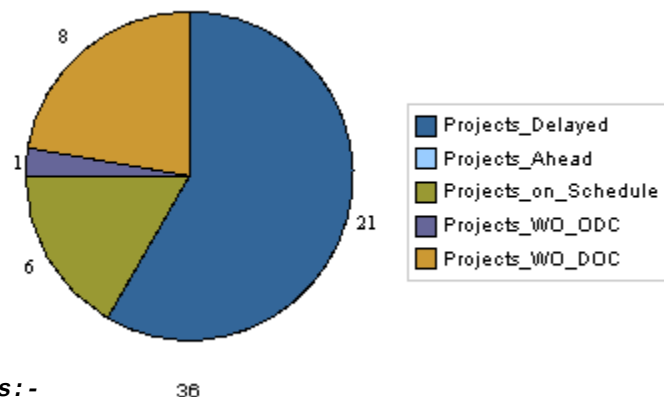


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 36 projects when sanctioned, was of the order of Rs. 145945.23 crore but this was subsequently anticipated to Rs. 157932.6 crore implying a cost overrun of 8.2%. The expenditure incurred on these projects till August, 2017 is Rs. 71466.44 crore, which is 45.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

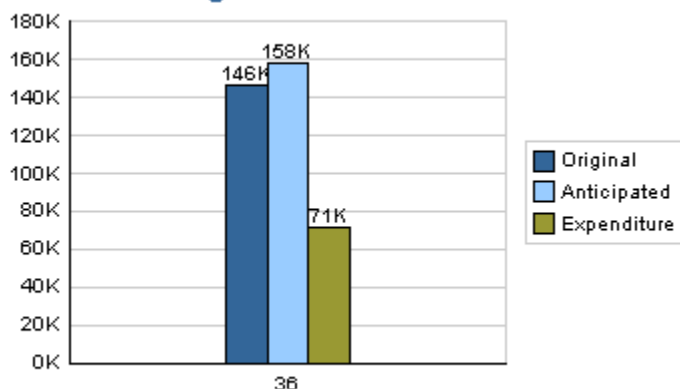

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule

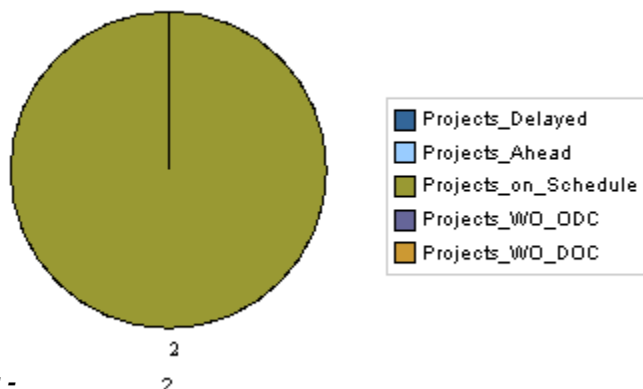


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 469.04 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till August, 2017 is Rs. 51.37 crore, which is 11% of the anticipated cost of the projects.

Figures are in Rs. Crore

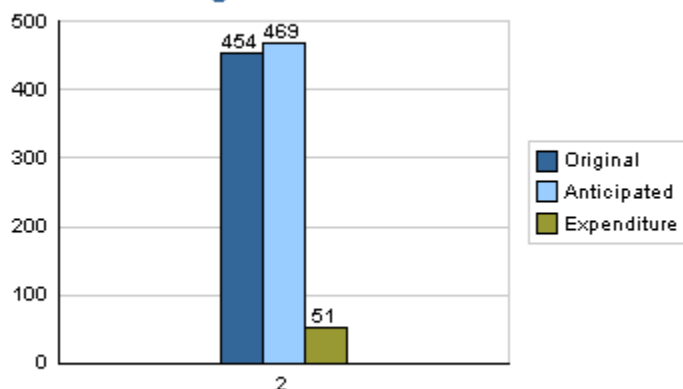

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (AUGUST 2017)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	24.13
2	ANDHRA PRADESH	60	97,457.47	1,01,158.09	10,997.35
3	ARUNACHAL PRADESH	31	16,602.41	32,431.5	17,033.66
4	ASSAM	50	33,769.6	47,399.82	30,027.51
5	BIHAR	78	68,807.61	82,224.21	39,297.92
6	CHHATISGARH	41	94,608.92	96,545.85	57,329.12
7	D & N HAVELI	1	6,086.08	5,479.75	2,033.62
8	DELHI	17	50,925.07	50,831.89	35,132.07
9	GOA	10	4,379.12	4,376.91	438.17
10	GUJARAT	43	39,902.03	42,376.41	15,780.39
11	HARYANA	21	14,081.22	15,967.45	10,743.95
12	HIMACHAL PRADESH	13	15,017.74	21,417.01	8,692.4
13	JAMMU AND KASHMIR	10	27,408.66	47,277.79	29,956.83
14	JHARKHAND	48	46,724.53	50,366.69	16,959.4
15	KARNATAKA	47	79,393.9	97,719.96	43,226.71
16	KERALA	21	37,154.14	38,770.19	17,334.65
17	MADHYA PRADESH	53	55,860.99	60,307.08	16,021.73
18	MAHARASHTRA	113	1,70,980.76	1,80,382.47	59,436.33
19	MANIPUR	2	944.25	9,874.69	4,979.46
20	MEGHALAYA	6	7,108.02	9,025	933.28
21	MIZORAM	5	2,001.2	6,942.57	2,955.14
22	MULTI STATE	180	2,89,659.25	2,74,260.37	80,102.09
23	NAGALAND	7	8,126.79	10,276.79	357.19
24	ODISHA	66	72,116.99	79,775.64	14,900.97
25	PUNJAB	28	15,555.77	15,561.5	3,309.59
26	RAJASTHAN	62	44,007.1	46,166.34	17,230.34
27	SIKKIM	6	2,537.08	5,585.45	893.04
28	TAMIL NADU	57	76,796.39	99,583.49	67,755.52
29	TELANGANA	35	24,832.84	27,489.74	5,730.6
30	TRIPURA	11	4,400.64	9,067.42	5,567.92
31	UTTAR PRADESH	83	1,09,253.66	1,13,086.92	32,116.59
32	UTTARAKHAND	13	16,833.35	20,347.26	7,966.56
33	WEST BENGAL	53	56,102.34	68,521.71	33,770.11
TOTAL		1,272	15,89,750.53	17,71,039.29	6,89,034.34

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(AUGUST 2017)

ATOMIC ENERGY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	13171	-	22340
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	3492	-	5459.55
CIVIL AVIATION						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	484.76
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
4	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	302.96	-	329.8
5	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	190.68
6	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	215.92
7	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	418.97	-	477.74
HEAVY INDUSTRY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	1718	-	2289
PETROLEUM						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1534.28
10	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	150	-	234.99
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	871.35	-	957
POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
12	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	6480.33
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	9435.49
14	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3278
15	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	3642.04	-	5021.45

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(AUGUST 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
16	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	4375.35	6749.18	6760
17	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	573.99	1337.76	1478.76
18	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	232.34	-	238.61
19	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	297.33	346.79	355.29
20	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	-	470.78
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
21	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
22	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	124.43	-	919.06
23	AMRAVATI-NARKHER NL(CR)	CR	06/1994	663.01	175.3	688.04
24	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	2500	-	13536.97
25	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.02
26	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	495.44	-	514.44
27	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	900.05	-	980.99
28	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	514.68	-	812.01
29	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	SWR	02/1997	295	1289.92	1493.7
30	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	386.3	-	967.96
31	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	484.14
32	KARUR-SALEM(NL), SR	SR	02/1997	155.55	-	854.91
33	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	155.74	164.36	874.72
34	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	677.97	1062.36	1706.54
35	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	1500	-	4753.99
36	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	218.24	236.41	544.2
37	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(AUGUST 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
38	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	501.69	335.77	876.49
39	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
40	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	492.98	-	917.84
41	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	242.42	369.7	927.68
42	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	744.71	761.7
43	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72
44	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	625.3	408.76	841.57
45	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	100	-	647
46	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.61
47	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	733	-	2225.72
48	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	1049.69	-	3544.3
49	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	92.63	-	316.64
50	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	607.09	-	613.71
51	JIND-SONEPAT (NL), NR	NR	01/2004	238.56	-	722.65
52	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	470.21	-	899.41
53	RAJATGARH-BARANG(LD), ECOR	RVNL	04/1999	166.16	-	370.24
54	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	727.56	-	4927.46
55	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	352.29
56	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	120	-	210.67
57	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	272.77
58	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	136.62	-	379.85
59	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	332.92	283.95	495.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(AUGUST 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
60	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	404.19	-	932.04
61	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1047.11
62	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	170	-	439.57
63	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	200	-	421.4
64	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	300	-	920.59
65	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	325	-	618.19
66	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	813.34	-	2316.85
67	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	619.34	-	1565.18
68	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	482	-	981.7
69	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	516.23	-	694.13
70	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	167.73	-	207.11
71	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	207.52	-	293.47
72	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	603.04	-	628.11
73	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	1389.62	-	1513.78
74	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29
75	KATAKHAL TO BHAIRABI	NFR	04/1998	227.9	-	403.86
76	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	1676.31	-	6995.27
77	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	388.43
78	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	211.8
79	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	446	-	590.6
80	VIRAMGAM-SURENDRANAGAR (DL)	WR	04/2010	279.4	-	323.64
81	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	456	-	585.06
82	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	739.65	-	796.25

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(AUGUST 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
83	TAMLUK-BASULYA-SUTAHATA DOUBLING	RVNL	04/2010	171.02	-	237.39
84	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.69	-	253.1
85	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	464.5
86	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	-	1481.71
87	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	209.77	-	319.06
88	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	360.22
89	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	523.17	-	1071.96
90	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	312.12	-	477.36
91	WARDHA-NANDED MAHARASHTRA	CR	04/2008	499.3	-	532.82
92	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	423.66	-	456.58
93	PEN ROHA DOUBLING	CR	04/2007	98.74	-	312.12
94	PANVEL PEN DOUBLING	CR	04/2006	96.16	-	268.37
95	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	179.65	-	760.21
96	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	313.24	-	342
97	JHARSUGUDA-RENGALI DOUBLING	ECOR	03/2006	201	-	242.23
98	DELANG-PURI DOUBLING	ECOR	03/2011	165.16	-	224.64
99	HOSADURGA - CHICKJAJUR (28.89 KM)	SWR	04/2010	203.4	203.4	278.08
100	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	836.26	-	1026.65
101	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21
102	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	4300	-	4393.96
ROAD TRANSPORT AND HIGHWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
103	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	340.12
104	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1	NHAI	05/2009	1108	-	3882.53

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(AUGUST 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
	KM)					
105	TALEGAON-AMRAVATI	NHAI	11/2009	567	-	1055.94
106	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	852	-	911.01
107	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2234.53
108	MURADABAD-BAREILY	NHAI	04/2010	1267	-	2664.02
109	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	2037.05
110	NASHRI- CHANANI	NHAI	05/2011	2159	-	3986.82
111	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	1813.76	-	2393.99
112	ROHTAK-BAWAL	NHAI	05/2011	650	-	832.39
113	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1948.72
114	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1329.03
115	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	622.89
116	JORBAT - BARAPANI	NHAI	01/2011	536	-	672.32
117	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	3075.77
118	SRINAGAR TO BANIHAL	NHAI	06/2011	1100.7	-	1340.87
119	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1095.01
120	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2382.75
121	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	998.79	-	1927.6
122	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2678.94
123	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	320.46
124	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1850
125	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	1928.22	-	2447.73
126	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1785.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(AUGUST 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
127	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	1266.6	-	1337
128	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	378.36
129	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	495.78	-	498.08
130	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1425.94
131	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92
132	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	3130.07
133	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	NHAI	07/2015	1393	-	2137.09
134	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	2595.24
135	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2082.05
136	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	2091.52
137	TRICHY - KARUR	NHAI	03/2007	516	-	761.19
SHIPPING AND PORTS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
138	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	245.67	-	350.68
139	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	366.39	-	411.12
STEEL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
140	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	17265	-	17892.75
141	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
142	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64
URBAN DEVELOPMENT						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
143	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	6395	13845.01	14200.11

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Annexure - III

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	51.38	12/2020 -	08/2020
	Total		2,321.00 -	2,321.00	51.38		
	<u>POWER</u>						
2	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	461.43	03/2018 -	09/2017
	Total		550.06 -	550.06	461.43		
	<u>PETROLEUM</u>						
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 6,068.80	5,296.93	3,995.37	04/2019 03/2019	03/2019
4	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 567.22	567.22	347.69	11/2019 12/2018	12/2018
	Total		7,740.02 -	5,864.15	4,343.06		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
5	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	108.23	07/2018 -	06/2018
	Total		667.00 -	667.00	108.23		
	<u>POWER</u>						
6	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	106.81	07/2018 -	12/2017
7	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	104.56	05/2018 -	12/2017
	Total		406.30 -	406.30	211.37		
	<u>PETROLEUM</u>						
8	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	53.32	02/2019 -	12/2018
9	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	57.85	05/2019 -	12/2018
10	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 910.23	910.23	-	03/2023 03/2022	03/2022
11	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	98.67	12/2020 -	02/2020

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,926.14 -	2,177.75	209.84		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
12	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	-	03/2020 -	05/2019
	Total		296.19 -	254.00	.00		
	Grand Total		13,906.71	12,240.26	5,385.31		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	109.31	03/2021 -	03/2021
2	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.13	03/2023 -	03/2023
4	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	48.69	03/2018 -	03/2018
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	351.84	03/2021 -	03/2021
6	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	228.99	03/2025 -	03/2025
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	427.59	03/2018 -	03/2018
8	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	34.26	03/2021 -	03/2021
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	673.05	03/2026 -	03/2026
10	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	7.46	03/2022 -	03/2022
11	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
12	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	65.88	03/2020 -	03/2020
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	263.42	03/2022 -	03/2022
14	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	174.29	03/2020 -	03/2020
15	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
16	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
17	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,264.95	03/2023 -	03/2023
18	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.37	03/2021 -	03/2021
19	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	45.89	03/2020 -	03/2020
20	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	29.01	03/2022 -	03/2022
21	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	72.23	03/2023 -	03/2023
22	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	175.42	03/2020 -	03/2020
24	GOKUL - [N06000120]	11/2014	267.67 -	267.67	203.98	03/2018 -	03/2018
25	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	52.71	03/2023 -	03/2023
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	21.75	03/2019 -	03/2019
27	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	19.94	03/2019 -	03/2019
28	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	5.65	09/2019 -	09/2019
29	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	44.86	03/2021 -	03/2021
30	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	360.21	03/2020 -	03/2020
31	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,107.67	11/2021 -	11/2021
32	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	0.71	03/2023 -	03/2023
33	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
34	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
35	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
36	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	84.95	03/2019 -	03/2019
37	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	30.32	03/2019 -	03/2019
38	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	9.72	03/2022 -	03/2022
39	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,430.17	03/2023 -	03/2023
40	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	0.13	03/2021 -	03/2021
41	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023
42	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	24.67	03/2019 -	03/2019
43	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	167.04	12/2019 -	12/2019
44	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
45	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	71.98	03/2021 -	03/2021
46	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	28.62	03/2020 -	03/2020
47	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	138.36	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
48	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
49	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	-	03/2022 -	03/2022
50	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	124.00	03/2019 -	03/2019
	Total		65,699.36 -	65,745.49	9,109.20		
	<u>DEFENCE PRODUCTION</u>						
51	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	29.85	08/2020 -	08/2020
52	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	21.52	05/2018 -	05/2018
	Total		453.64 -	469.04	51.37		
	<u>FERTILISERS</u>						
53	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	383.90	12/2017 -	12/2017
	Total		482.85 -	494.00	383.90		
	<u>HEALTH AND FAMILY WELFARE</u>						
54	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	202.00	03/2018 -	03/2018
55	NCI AIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	103.00	08/2018 -	08/2018
56	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	66.00	09/2018 -	09/2018
	Total		1,062.57 -	1,062.57	371.00		
	<u>MINES</u>						
57	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	157.34	01/2020 -	01/2020
58	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	0.31	04/2021 -	04/2021
	Total		6,074.00 -	6,074.00	157.65		
	<u>PETROLEUM</u>						
59	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	154.97	10/2019 -	10/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
60	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	4.85	12/2019 -	12/2019
61	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB, HARYANA) - [N16000242]	11/2016	230.00 -	230.00	11.01	02/2019 -	02/2019
62	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	580.31	04/2018 04/2018	04/2018
63	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	20.22	02/2020 -	02/2020
64	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.87	12/2019 -	12/2019
65	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	170.15	03/2020 -	03/2020
66	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	135.88	09/2018 09/2018	09/2018
67	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	468.00	02/2020 -	02/2020
68	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
69	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	1.35	06/2020 -	06/2020
70	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	0.05	01/2021 -	01/2021
71	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018
72	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	6.09	12/2020 -	12/2020
73	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	923.87	06/2018 -	06/2018
74	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	191.47	11/2019 -	11/2019
75	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	252.02	06/2020 -	06/2020
76	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
77	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	15.07	12/2020 -	12/2020
78	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	21.03	02/2020 -	02/2020
79	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	59.40	02/2020 -	02/2020
80	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	8.38	08/2021 -	08/2021
81	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	2,253.00 -	2,253.00	5.71	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
82	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	43.02	12/2019 -	12/2019
83	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	33.54	04/2019 -	04/2019
84	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 -	09/2018
85	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	95.55	12/2019 -	12/2019
86	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	79.24	08/2019 -	08/2019
87	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	0.05	01/2021 -	01/2021
88	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	159.74	03/2026 -	03/2026
89	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
90	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	119.90	03/2018 -	03/2018
91	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	12.27	08/2018 -	08/2018
92	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	22.20	12/2018 -	12/2018
93	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,212.00 -	3,212.00	0.10	12/2020 -	12/2020
94	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	216.42	11/2018 -	11/2018
95	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
96	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	0.50	10/2020 -	10/2020
97	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	28.42	09/2019 -	09/2019
98	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	192.61	04/2018 -	04/2018
99	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	0.05	01/2021 -	01/2021
100	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,250.00 -	2,250.00	1.93	12/2019 -	12/2019
101	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	7.03	01/2019 -	01/2019
102	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	365.49	12/2018 -	12/2018
103	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	57.41	03/2019 -	03/2019
104	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	76.29	12/2017 -	12/2017

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,828.00 -	1,828.00	0.10	12/2020 -	12/2020
106	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	155.60	10/2018 -	10/2018
107	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 -	05/2020
108	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	25.71	09/2019 -	09/2019
109	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	148.67	06/2020 -	06/2020
110	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	-	12/2019 -	12/2019
111	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	327.78	13.62	04/2018 -	04/2018
112	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	23.07	01/2019 -	01/2019
	Total		1,10,562.98 -	1,11,038.75	5,254.26		
	POWER						
113	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	147.00	08/2017 -	08/2017
114	50 MW SOLAR POWER PROJECT - [N18000251]	9/2017	287.48 -	287.48	0.51	03/2018 -	03/2018
115	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	1,407.32	03/2018 -	03/2018
116	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
117	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	1,980.02	04/2018 -	04/2018
118	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	12.97	02/2019 -	02/2019
119	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	5.36	06/2019 -	06/2019
120	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	30.90	11/2018 -	11/2018
121	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	-	04/2019 -	04/2019
122	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	1,681.43	10/2017 -	10/2017
123	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	211.58	04/2020 -	04/2020
124	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	98.85	04/2019 -	04/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
125	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	11.40	07/2018 -	07/2018
126	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	3,330.00	04/2018 -	04/2018
127	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]	4/2015	2,525.00 -	2,525.00	1,215.00	11/2017 -	11/2017
128	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	41.04	09/2020 -	09/2020
129	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	37.13	05/2018 -	05/2018
130	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	0.40	02/2019 -	02/2019
131	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]	11/2016	330.00 -	330.00	135.14	11/2017 -	11/2017
132	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	3,043.00	03/2019 -	03/2019
133	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	74.23	07/2018 -	07/2018
134	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	340.88	154.86	03/2018 -	03/2018
135	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	287.00	09/2019 -	09/2019
136	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
137	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	982.00	07/2020 -	07/2020
138	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.95	02/2019 -	02/2019
139	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.56	03/2019 -	03/2019
140	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	95.35	01/2019 -	01/2019
141	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	47.99	04/2018 -	04/2018
142	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	58.44	06/2018 -	06/2018
143	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	7.45	09/2019 -	09/2019
144	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	3,245.00	09/2019 -	09/2019
145	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	242.89	06/2019 -	06/2019
146	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	12.93	11/2018 -	11/2018
147	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	-	06/2019 -	06/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
148	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	8.20	10/2018 -	10/2018
149	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	284.67	12/2018 -	12/2018
150	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.70	11/2019 -	11/2019
151	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	345.26	05/2019 -	05/2019
152	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	18.66	12/2018 -	12/2018
153	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	0.51	03/2019 -	03/2019
154	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	40.12	01/2019 -	01/2019
155	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	591.47	07/2018 -	07/2018
156	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	5.12	04/2019 -	04/2019
157	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.61	12/2019 -	12/2019
158	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	42.41	03/2018 -	03/2018
159	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	6,184.00	08/2018 -	08/2018
160	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	657.13	11/2019 -	11/2019
161	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	87.99	03/2019 -	03/2019
162	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	439.84	07/2018 -	07/2018
	Total		1,09,911.76 -	1,10,298.05	27,359.39		
	RAILWAYS						
163	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
164	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
165	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	383.12	03/2018 -	03/2018
166	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	67.81	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
167	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	4,295.30	-	12/2026 -	12/2026
168	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	90.63	03/2019 -	03/2019
169	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
170	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
171	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	139.85	03/2018 -	03/2018
172	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	-	03/2020 -	03/2020
173	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
174	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
175	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	218.41	03/2019 -	03/2019
176	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	15.51	03/2021 -	03/2021
177	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	-	03/2021 -	03/2021
178	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	33.76	03/2020 -	03/2020
179	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	-	03/2020 -	03/2020
180	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	0.14	03/2019 -	03/2019
181	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	28.94	03/2021 -	03/2021
182	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
183	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	201.87	03/2019 -	03/2019
184	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020
185	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	-	03/2019 -	03/2019
186	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	23.82	03/2021 -	03/2021
187	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	235.03	03/2019 -	03/2019
188	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	17.78	03/2022 -	03/2022
189	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	34.88	03/2021 -	03/2021
190	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	927.01	-	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
191	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	19.91	03/2019 -	03/2019
192	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	-	12/2024 -	12/2024
193	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.65	-	12/2020 -	12/2020
194	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
195	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	-	12/2025 -	12/2025
196	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	-	12/2021 -	12/2021
197	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
198	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.25	-	12/2020 -	12/2020
199	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	342.92	03/2018 -	03/2018
200	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
201	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	-	12/2021 -	12/2021
202	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
203	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
	Total		50,597.28 -	52,147.82	2,105.54		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
204	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
205	FOUR LANNING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	147.98	06/2018 -	06/2018
206	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
207	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
208	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
209	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	4/2017	388.00 -	447.37	-	10/2017 -	10/2017

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
210	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
211	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
212	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
213	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
214	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
215	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
216	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
217	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017
218	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
219	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
220	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
221	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
222	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
223	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
224	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
225	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
227	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
228	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
229	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	29.27	10/2017 -	10/2017
231	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
232	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
233	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
234	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
235	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
236	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
237	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	2,595.24	01/2018 -	01/2018
238	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
239	TWO LANNING WITH PAVED SHOULDER OF SALASAR- NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
240	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
241	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
242	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
244	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
245	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
246	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
247	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642	3/2015	226.31 226.00	226.00	-	10/2017 -	10/2017
248	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
249	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	301.95	03/2018 -	03/2018
250	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
251	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
252	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
253	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
254	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
255	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
256	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
257	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
258	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
259	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
260	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
261	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	84.46	06/2018 -	06/2018
262	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
263	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
264	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	161.96	03/2018 -	03/2018
265	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	531.15	03/2018 -	03/2018
266	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	558.12	02/2018 -	02/2018
267	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
268	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
269	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	617.98	11/2017 -	11/2017

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
270	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342	5/2015	709.00 -	709.00	203.50	09/2017 -	09/2017
271	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
272	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
273	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
274	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	31.87	03/2018 -	03/2018
275	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	27.62	12/2018 -	12/2018
276	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	154.94	12/2017 -	12/2017
277	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020
278	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	142.48	06/2018 -	06/2018
279	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	168.65	07/2018 -	07/2018
280	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343	9/2015	341.61 -	341.61	308.23	09/2017 -	09/2017
281	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
282	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
283	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
284	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
285	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
286	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
287	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
288	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	2/2015	239.91 240.00	240.00	-	10/2017 -	10/2017
289	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
290	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
291	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	275.35	04/2018 -	04/2018
	Total		63,238.06 -	65,323.22	6,957.80		
	<u>SHIPPING AND PORTS</u>						
292	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
293	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	0.14	12/2017 -	12/2017
	Total		454.50 -	468.33	.14		
	<u>STEEL</u>						
294	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097	2/2014	4,749.00 -	4,749.00	64.65	09/2017 -	09/2017
295	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
296	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	41.97	09/2018 -	09/2018
297	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120	7/2015	465.85 -	465.85	20.85	07/2018 -	07/2018
298	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	156.39	03/2018 -	03/2018
299	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	35.71	06/2019 -	06/2019
300	CENTRAL DISPATCH YARD - [N12000119	8/2015	320.66 -	320.66	11.17	08/2018 -	08/2018
301	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	25.74	06/2020 -	06/2020
302	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
	Total		8,924.42 -	8,924.42	576.54		
	<u>URBAN DEVELOPMENT</u>						
303	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103	12/2016	246.31 -	246.31	-	02/2020 -	02/2020
304	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,118.00	2,661.40	11/2019 -	11/2019
305	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102	8/2016	294.00 -	294.00	11.87	04/2019 -	04/2019
306	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
307	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098	10/2016	209.84 -	209.84	0.26	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
308	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	Total		15,712.15 -	15,566.15	5,210.30		
	Grand Total		4,33,173.57	4,37,611.84	57,537.09		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	03/2017	70.54
	Total		16,663.00 -	28,462.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2017	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
5	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
6	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24
9	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		18,876.68 -	19,914.04			
	<u>DEFENCE PRODUCTION</u>						
12	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	3.16
13	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.53

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		453.64 -	469.04			
	<u>FERTILISERS</u>						
14	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
15	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. [N08000010]	02/2016	482.85 -	494.00	12/2017 -	12/2017	2.31
	Total		680.64 -	703.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
16	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK [N21000005]	11/2013	196.70 -	209.00	01/2016 -	-	6.25
	Total		196.70 -	209.00			
	<u>HEAVY INDUSTRY</u>						
17	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
18	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
20	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
21	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,637.00	04/2016 -	12/2017	36.68
22	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
23	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	222.81	09/2016 -	02/2017	57.06
24	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87
25	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2017	45.83
27	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
28	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	768.25	11/2015 -	10/2016	15.35
29	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	06/2018	45.67
30	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50
31	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
32	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
33	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
34	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) [N16000217]	06/2012	150.00 -	259.93	07/2014 -	09/2017	73.29
35	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
36	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	Total		25,330.13 -	31,941.76			
	<u>POWER</u>						
37	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
38	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
39	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2017	54.59
40	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14
41	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58
42	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
43	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79
44	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	03/2018	38.61

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
45	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	02/2014	908.08 -	969.97	06/2016 -	09/2017	6.82
46	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	03/2018	5.34
47	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	10/2017	32.69
48	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14
49	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	12/2017	54.25
50	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37
51	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	11/2017	14.60
52	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	03/2018	26.82
53	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	12/2017	27.92
54	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01
55	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	245.00	06/2012 -	12/2017	5.45
56	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	12/2018	50.75
57	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96
58	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	88.79
59	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	121.80
60	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51
61	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	12/2017	39.30
62	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73
63	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	06/2018	31.17
64	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	09/2017	23.13
65	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
66	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
67	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37
68	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60
69	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50
70	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93
71	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2019	73.65
72	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,329.43	07/2006 02/2015	11/2017	260.55
73	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	882.13	11/2014 -	12/2017	21.90
75	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	12/2017	36.74
76	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,352.57	09/2017 -	09/2018	31.55
77	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
78	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	10/2017	7.41
79	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	Total		88,811.97 -	1,42,172.89			
	<u>RAILWAYS</u>						
80	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
81	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	-	1,568.48
82	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
83	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	870.00	- -	-	459.31

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
84	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
85	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	1,542.41	- 05/2009	-	536.26
86	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
87	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
88	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
89	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	350.00	02/2011 -	-	277.85
90	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
91	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
92	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	-	210.19
93	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	03/2019	293.06
94	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	2,713.09	- -	03/2021	476.13
95	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	412.05	- -	03/2018	88.85
96	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	- -	-	60.34
97	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
98	HATHUA-BHATNI (N L) (NER) - [220100319	04/2005	230.03 -	718.54	- -	05/2019	212.37
99	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	-	186.92
100	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39
101	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	340.00	03/2009 03/2009	12/2017	154.85
102	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	- -	06/2022	137.80
103	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
104	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51
105	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	03/2018	38.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
106	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	2,072.50	- -	-	412.75
107	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
108	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
109	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
110	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
111	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
112	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
113	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	941.04	03/2014 -	03/2019	44.07
114	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
115	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
116	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	05/2016	123.34
117	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	-	534.55
118	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	-	185.52
119	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
120	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
121	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
122	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
123	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	-	8.18
124	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	-	81.31
125	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	381.39	- -	-	286.26
126	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
127	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
128	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
129	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
130	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
131	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
132	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
133	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
134	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
135	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
136	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
137	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
138	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
139	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
140	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
141	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
142	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
143	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
144	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
145	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
146	MONIGRAM- NIMITTA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
147	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
148	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	-	77.08
149	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
150	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
151	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,271.50	- -	-	341.34
152	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
153	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
154	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33
155	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
156	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
157	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
158	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
159	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64
160	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
161	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
162	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
163	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47
164	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	780.00	- -	03/2019	290.00
165	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	2,145.00	- -	03/2020	615.00
166	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
167	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
168	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119	04/1999	207.52 -	334.87	12/2012 -	-	61.37
169	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2018	317.58
170	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
171	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	360.00	- -	-	27.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
172	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
173	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,679.13	- -	-	147.67
174	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	744.71 -	1,126.79	- -	-	51.31
175	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	780.98	- -	-	90.45
176	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114	04/2008	516.23 -	735.00	03/2014 -	-	42.38
177	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
179	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
180	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
181	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
182	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	06/2017	122.68
183	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
184	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89
185	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
186	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
187	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
188	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
189	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
190	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	491.33	06/2004 -	-	153.17
191	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
192	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) [N22000345	04/1997	836.26 -	1,072.52	- -	-	28.25
193	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	01/2017	337.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
194	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
195	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	-	81.45
196	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
197	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
198	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
199	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
200	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,160.83	- -	03/2020	40.44
201	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	- -	03/2020	52.77
202	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	-	42.11
203	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
204	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322	04/2011	190.10 -	355.96	- -	03/2019	87.25
205	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	-	40.49
206	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324	04/2010	203.40 -	273.84	- -	-	34.63
207	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	648.00	- -	02/2019	8.00
208	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112	04/2008	829.74 -	1,161.64	03/2015 -	03/2019	40.00
209	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	1,010.00	- -	-	711.70
210	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	858.23	06/1999 -	-	29.44
211	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
212	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	308.00	- -	-	.33
213	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	268.78	- -	08/2017	10.26
214	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132	03/2008	195.64 -	474.30	- -	07/2017	142.44
215	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	477.31	- -	10/2018	61.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
216	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
217	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	- -	02/2019	41.64
218	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
219	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
220	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
221	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
222	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
223	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
224	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
225	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
226	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	- -	-	16.87
227	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	855.16	- -	05/2018	87.54
228	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
229	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]	04/2011	239.73 -	257.78	- -	-	7.53
230	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	- -	02/2019	27.93
231	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	- -	-	27.72
232	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	- -	03/2019	21.31
233	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
234	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
235	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
236	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
237	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
238	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41
239	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
240	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
241	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
242	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
243	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
244	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
245	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
246	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
247	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	527.37	- -	-	18.01
248	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
249	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
250	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	- -	03/2018	80.06
251	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
252	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62
253	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
254	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16
255	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	445.00	- -	03/2018	112.14
256	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	330.00	- -	03/2018	16.38
257	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
258	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	302.90	- -	-	84.23
259	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
260	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
261	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	-	94.45
262	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
263	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2020	171.38
264	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
265	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	508.00	- -	03/2019	62.76
266	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
267	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06
268	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,500.00	- -	-	149.41
269	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
270	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
271	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
272	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	- -	-	101.93
273	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	- -	-	5.33
274	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	-	10.94
275	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	-	21.21
276	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
277	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
278	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	08/2015	5.12
279	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	556.31 -	612.00	- -	-	10.01
280	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
281	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
282	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	750.55 -	943.60	12/2024 -	12/2024	25.72
283	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
284	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88
	Total		1,06,335.90 -	2,60,041.87			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
285	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93
286	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
287	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
288	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
289	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
290	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH- 52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
291	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
292	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
293	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
294	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25
295	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
296	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
297	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
298	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
299	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
300	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
301	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
302	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
303	TWO LANE OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
304	FOUR LANE OF GWALIOR-SHIPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
305	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26
306	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	04/2018	.11
307	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	10/2017	.04
308	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	03/2017	.06
309	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	03/2017	.02
310	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	03/2017	.30
311	FOUR LANE OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
312	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
313	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
314	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
315	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
316	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
317	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
318	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
319	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
320	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
321	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
322	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
323	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
324	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54
325	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
326	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
327	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	Total		25,598.69 -	32,656.93			
	<u>SHIPPING AND PORTS</u>						
328	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
329	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	-	18.20
330	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
331	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	-	66.82
332	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
333	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04
334	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
335	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
336	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39
337	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	Total		1,639.71 -	2,211.39			
	<u>URBAN DEVELOPMENT</u>						
338	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	13,845.01	06/2011 -	04/2017	116.50
339	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	12/2017	44.75
340	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2017	30.53
341	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	Total		21,350.59 -	33,518.34			
	Grand Total		3,09,485.22	5,59,295.63			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,000.00	5,459.55	09/2010 09/2016	10/2017	85	71.82	
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	10,443.00	12/2015 11/2016	11/2019	47	0	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,074.00	12/2016 03/2017	12/2020	48	0	
	Total		27,271.00 -	29,779.00	23,976.55					
	<u>CIVIL AVIATION</u>									
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	553.53	484.76	01/2011 09/2017	09/2017	80	78.87	long rainy season
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	24.13	09/2018 -	06/2020	21	40.28	
	Total		624.07 -	994.86	508.89					
	<u>COAL</u>									
6	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU	05/2016	687.28 -	687.28	681.42	06/2017 -	08/2017	2	0	
7	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	151.66	05/2014 -	10/2017	41	0	
8	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	144.38	04/2014 -	10/2017	42	0	
9	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	125.01	03/2014 -	12/2017	45	0	Delay/non-issuance of patta for land/plots allotted to PAFs in area acquired under CBA Act and unjustified demand of villagers for giving possession of land acquired under CBA Act.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL,ODISHA	01/2005	302.96 -	302.96	329.80	03/2010 -	03/2018	96	0	
11	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 486.57	486.57	294.63	03/2012 03/2018	03/2018	72	87.58	forest clearance
12	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	120.55	03/2015 -	03/2018	36	0	
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72	0	
14	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	198.19	03/2014 -	03/2018	48	0	
15	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.38	03/2016 -	03/2018	24	0	
16	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	205.72	03/2013 -	03/2018	60	0	
17	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	341.10	03/2016 -	03/2018	24	0	
18	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	149.93	03/2016 -	03/2018	24	0	land acquisition
19	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	57.64	06/2015 -	03/2018	33	0	
20	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 415.37	415.37	136.75	03/2016 -	03/2018	24	-3.5	
21	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	4,659.77	12/2015 04/2018	04/2018	28	0	
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	272.87	03/2017 -	05/2018	14	0	
23	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	298.37	03/2018 -	09/2018	6	0	Rehabilitation of PAFs: Process of R&R activity delayed due to disputes among villagers for selection of rehab site and resistance by villagers in shifting.
24	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
25	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	402.43	03/2013 -	11/2018	68	0	
26	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 448.86	448.86	157.97	03/2012 -	03/2019	84	80.24	
27	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	190.68	03/2010 -	03/2019	108	0	
28	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	215.92	03/2012 -	03/2019	84	0	
29	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	218.28	03/2013 -	03/2019	72	0	
30	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84	0	
31	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	153.14	03/2012 -	03/2019	84	0	
32	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	80.62	03/2014 -	03/2019	60	0	
33	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
34	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	176.37	04/2015 -	04/2019	48	0	
35	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	258.90	06/2015 09/2019	09/2019	51	-51.37	
36	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	78.39	03/2015 03/2020	03/2020	60	201.44	
37	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.12	03/2014 -	03/2020	72	0	
38	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.27	03/2011 -	03/2020	108	0	
39	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 164.04	164.04	.09	03/2015 -	03/2020	60	-32.3	
40	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 349.28	349.28	1.31	03/2015 -	03/2020	60	114.6	
41	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 417.33	417.33	43.97	07/2016 -	03/2020	44	0	
42	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	116.67	07/2012 03/2017	03/2021	104	0	
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	259.34	03/2015 -	03/2021	72	-2.14	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
44	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	16.86	
	Total		20,618.90 -	20,758.14	11,553.28					
	<u>FERTILISERS</u>									
45	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	82.72	11/2016 04/2019	04/2019	29	5.89	
	Total		197.79 -	209.44	82.72					
	<u>STEEL</u>									
46	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	745.11	07/2015 -	09/2017	26	0	
47	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	154.55	09/2016 -	09/2017	12	0	
48	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	17,892.75	03/2013 -	10/2017	55	0	
49	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	195.64	05/2016 -	10/2017	17	0	
50	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	510.53	07/2016 -	10/2017	15	0	
51	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	12,559.30	05/2015 12/2017	12/2017	31	0	
52	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	12.04	
53	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	217.87	10/2016 -	03/2018	17	42.39	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
54	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	0	
55	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	402.94	12/2017 -	05/2018	5	0	
56	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	564.35	12/2017 -	06/2018	6	-12.53	
57	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	184.28	10/2017 -	07/2018	9	0	
58	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	0	
59	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
60	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	
61	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	996.15	04/2018 -	02/2019	10	0	
62	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	Total		46,224.80 -	46,036.59	35,761.05					
	<u>PETROLEUM</u>									
63	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM	06/2012	150.00 -	259.93	234.99	07/2014 -	09/2017	38	73.29	
64	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	2,765.42	11/2015 -	10/2017	23	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
65	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA	03/2014	238.50 -	238.50	167.48	03/2017 10/2017	10/2017	7	0	
66	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC, TRIPURA	05/2016	215.38 -	215.38	141.75	06/2017 10/2017	10/2017	4	0	
67	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL, TAMIL NADU	02/2016	367.11 -	367.11	218.14	04/2017 -	11/2017	7	0	
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,158.78	05/2013 12/2017	12/2017	55	45.83	
69	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 4,259.59	5,637.00	3,701.21	04/2016 12/2017	12/2017	20	36.68	
70	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU	05/2015	257.87 -	257.87	117.68	11/2016 -	02/2018	15	0	
71	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL, GUJARAT	02/2016	931.00 -	931.00	377.28	07/2017 -	02/2018	7	0	
72	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 -	2,665.65	1,625.39	03/2015 03/2018	03/2018	36	29.42	
73	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 -	600.17	576.09	12/2014 03/2018	03/2018	39	0	
74	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	12/2009	309.81 723.40	723.40	372.36	10/2014 03/2018	03/2018	41	133.5	
75	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	209.19	146.86	12/2016 -	03/2018	15	-8.51	
76	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH	03/2009	181.02 -	173.28	126.24	01/2017 03/2018	03/2018	14	-4.28	
77	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 -	190.45	104.95	09/2017 -	03/2018	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
78	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	1,992.86	05/2014 05/2018	05/2018	48	0	
79	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	5,554.21	05/2017 05/2018	05/2018	12	1.87	
80	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018	12	-27.64	
81	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	105.43	07/2016 06/2018	06/2018	23	-20.81	
82	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 4,190.00	4,190.00	1,918.07	09/2017 06/2018	06/2018	9	36.22	
83	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,984.66	03/2013 09/2018	09/2018	66	-3.5	
84	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	439.03	126.43	03/2017 -	11/2018	20	24.53	
85	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 -	3,397.00	1,143.75	01/2013 -	12/2018	71	-14.15	
86	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	1,288.55	09/2017 12/2018	12/2018	15	0	
87	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	259.80	10/2017 -	03/2019	17	17.66	
88	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	3,961.54	3,216.59	12/2017 03/2019	03/2019	15	-14.25	
89	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	67.52	03/2019 -	04/2019	1	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
90	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	4,588.29	840.60	08/2018 05/2019	05/2019	9	0	
91	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	571.47	535.39	09/2011 06/2019	06/2019	93	-22.42	
92	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	5,479.75	2,033.62	05/2019 10/2019	10/2019	5	-9.96	
93	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	2.11	01/2014 11/2019	11/2019	70	62.78	
94	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	180.36	03/2019 05/2020	05/2020	14	0	
95	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	122.14	07/2018 06/2020	06/2020	23	0	
	Total		58,967.97 -	60,599.99	34,444.14					
	<u>POWER</u>									
96	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 2,619.59	2,619.56	2,581.34	07/2014 09/2017	09/2017	38	23.13	Balance Aurangabad-Boisor line affected due to severe ROW in routing of line through grape garden area being resolved progressively with support from State Govt.
97	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	135.16	09/2014 09/2017	09/2017	36	0	Supply has been completed in package. Presently are only 04 lines balance among which 03 are under construction lines and fourth line is being ROW problem.
98	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 9,291.03	9,291.03	7,283.96	06/2015 06/2017	09/2017	27	-2.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 969.97	969.97	711.64	06/2016 02/2018	09/2017	15	6.82	Project completed except ICT at Parbati PS, held up due to non-availability of shut down (now ant. in Oct'17). Non-availability of down-stream line by HPSEB at Parbati PS shall, however, affect commissioning.
100	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	408.10	08/2016 10/2017	10/2017	14	0	Implementation of balance work affected due to disturbance in J&K.
101	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	129.79	03/2016 07/2017	10/2017	19	32.69	Implementation of balance affected due to delay in equipment supply(Off-shore) & non-readiness of down stream line by State Govt. at Hamirpur.
102	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	148.64	03/2017 10/2017	10/2017	7	0	Work slowed-down to match Gen. project (Gen. project ant. by Nov'17).
103	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,329.43	1,329.43	1,259.14	07/2006 11/2017	11/2017	136	260.55	
104	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	14,089.00	01/2017 07/2017	11/2017	10	0	
105	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	118.67	02/2016 08/2017	11/2017	21	14.6	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
106	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	645.85	09/2010 12/2017	12/2017	87	54.59	Severe ROW problem in balance 02 lines, (400KV D/C Vapi-Navi Mumbai line & LILO at Navi Mumbai). LILO line is being completed using underground cable, however, ROW problem for laying of cable continue. Cable burnt/ damaged by miscreants. Critical. Vapi-Navi Mumbai line now decided to be terminated at Kudus S/stn. Further, its commissioning is linked to readiness of Kudus S/s of MSETCL. Critical.
107	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,760.00	09/2011 06/2017	12/2017	75	54.25	
108	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,547.20	08/2013 12/2017	12/2017	52	23.65	Balance lines (linked to Gen. Proj.) to be completed matching with Generation Project. Kaneng HEP scheduled in Dec'17 and Lower Subhansiri HEP is schedule uncertain.(agitation against big dams).
109	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	245.00	238.61	06/2012 -	12/2017	66	5.45	S/S almost ready since Jun'12. Line completed except 5 kms near Yelahanka, which is held up due to long pending ROW problem (high compensation agitation). Matter taken up with State Govt, MoP. However, issues yet to be resolved.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
110	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,407.97	11/2012 12/2017	12/2017	61	36.01	Down stream 220KV line of state at Daltonganj required matching with readiness of Sasaram - Daltonganj line & Daltonganj sub station anticipated by Dec'17.
111	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,323.86	09/2014 06/2017	12/2017	39	39.3	Balance line affected due to severe ROW problem being faced in Karnataka on Salem PS - Madhugiri line. Issues being addressed by conducting High level meeting with Energy Minister and taking help of Police protection. However, project vary slow.
112	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	426.29	355.29	08/2014 12/2017	12/2017	40	43.37	Implementation affected due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Compensation order issued by State in line with Govt. guidance. Villages-wise compensation rate is to be decided by Distt. Admn. (awaited) for which corridor survey is under progress.
113	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,929.61	08/2014 12/2017	12/2017	40	27.6	Implementation of Kudus (Padghe) S/stn. & associated down stream lines being executed by MSETCL. Critical for commissioning of balance lines under the project.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	715.86	11/2014 06/2017	12/2017	37	21.9	Implementation affected due to severe ROW problem in Uttarakhand in Dehradun-Abdullapur line. Progress of Dulhasti-Kishenpur line, site work affected due to severe ROW at 02 locs. in Doda distt. and disturbance in J&K. State admn. help required to resolved ROW issue (awaited).
115	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	561.70	06/2015 12/2017	12/2017	30	36.74	765KV Bay commissioned in Jan'17 matching with associated line. ICT's ready. Commissioning matching with Generation delayed / down-stream line (under TBCB sch. Apr'19). TBCB line being expedited.
116	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	97.92	04/2016 12/2017	12/2017	20	0	
117	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	159.70	07/2017 -	12/2017	5	27.92	Project commissioned except Bus Reactor at Yelankha As per MoM of 40th SCSPSR held on 19.11.16. Procurement shall be taken up after
118	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	470.78	12/2016 -	12/2017	12	37.96	D
119	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,021.45	01/2016 -	02/2018	25	61.5	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
120	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,473.47	10/2012 02/2018	02/2018	64	5.14	Balance 400kV Wardha – Aurangabad (on 1200KV tower) affected due to delay in implementation arising out of complexities involved (1200KV tower) & severe ROW problem also being encountered, apart from poor performance by executing agency necessitating termination & re-awarding fresh contracts. Work under progress after re-award.
121	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,552.51	12/2012 02/2018	02/2018	62	36.79	Implementation of balance lines affected due to local disturbances & geographical constraints. 01 line in Arunachal Pradesh (Tezu-Namsai line) affected due to compensation issues & land ownership disputes and further their commissioning linked to readiness of down stream system (being implemented under NER comprehensive scheme). Mizoram (Silcher-Melriat line) is affected due to tree cutting. Issue getting resolved with support of state/Dist. Admn.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	384.32	06/2016 02/2018	02/2018	20	0	Implementation affected due to severe ROW problem at singrauli end. Work also affected due to poor performance by executing agency.
123	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	5,808.04	12/2009 03/2018	03/2018	99	147.51	
124	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,337.76	1,337.76	1,478.76	08/2013 03/2018	03/2018	55	133.06	
125	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 5,135.01	5,135.01	3,404.34	01/2015 03/2018	03/2018	38	16.58	Gen. Proj.(Punatsangchu-I HEP in Bhutan) getting delayed. Also line getting completed ahead of Gen. Proj. (now anticipated in 2019-20). Work slowed down to the extent feasible to match Gen. HVDC Bi-pole link from Alipurduar – Agra expected to be commissioned in Sep'17.
126	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,945.36	12/2015 12/2017	03/2018	27	0	Implementation affected due to severe ROW problem & huge forest involvement. forest clearance stage-I for Chattisgarh issued in Jul'17 & working permission awaited. Working permission received in Odisha portion.
127	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	8,019.00	09/2017 03/2018	03/2018	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
128	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,144.12	04/2016 09/2017	03/2018	23	38.61	Implementation affected due to severe ROW problem at Rajarhat end as well as in Jharkhand area. Work in Rajarhat S/stn. area standstill since last 7 - 8 months due to protest agitation by locals who are not allowing to enter in S/stn. Forest clearance (St-I) obtained for Bihar.
129	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	360.30	11/2016 11/2017	03/2018	16	5.34	
130	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	218.80	02/2017 06/2017	03/2018	13	30.37	
131	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	5,353.00	5,472.83	05/2014 03/2017	03/2018	46	0	
132	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	03/2018	15	0	
133	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	674.66	04/2017 03/2018	03/2018	11	0	Work has been slowed-down to match with Generation (ant. by Mar'18). Severe ROW problem in Ajmer – Ajmer line. Matter already taken up with State Govt.
134	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 -	1,364.00	515.00	12/2015 -	03/2018	27	42.83	
135	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTR A	03/2012	9,395.18 -	9,395.18	7,988.00	11/2016 12/2017	04/2018	17	0	
136	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,528.00	06/2017 12/2017	04/2018	10	0	
137	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	452.50	09/2017 -	04/2018	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
138	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	485.24	06/2014 03/2018	06/2018	48	31.17	Balance 400KV Madugiri-Yelhanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the existing contractor has expressed inability to continue the balance work. Balance work under re-tender and award expected by Oct'17.
139	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	134.51	10/2017 10/2017	06/2018	8	0	Gen. project delayed. Work on ATS are being slowed-down to extent possible to match with Generation (ant. by Sep'19).
140	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	151.55	11/2017 -	06/2018	7	0	Generation project delayed (ant. by Jun'19). Forest clearance awaited. Work slowed-down to extent possible to match the generation.
141	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	9,072.44	01/2018 -	08/2018	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
142	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,955.46	11/2008 09/2018	09/2018	118	22.93	Implementation of balance 01 line (Edamon- Muvattupuzha line) is affected due to severe ROW problem (long pending). Compensation to be done on land value, to be finalised by concerned DC with the support of State Govt.. Works under progress after re- award. However stringing & erection work are being affected due to non- availability of Police protection force & about 06 nos. of pending High court case.
143	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,352.57	1,118.12	09/2017 -	09/2018	12	31.55	Implementation affected due to delay in land acquisition of Kargil S/s. Land handed over by DM in Dec'16. Disturbed law & order situation since Jul'16 in Kashmir Valley. Forest clearance required at Govt. of J&K. Tree cutting to be expedited by J&K forest deptt.
144	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,480.33	09/2009 -	12/2018	111	114.28	
145	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	121.55	02/2014 02/2018	12/2018	58	50.75	Power Evacuation Arrangement
146	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	13,653.00	01/2011 05/2018	03/2019	98	73.65	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
147	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	190.45	01/2018 -	03/2019	14	0	Implementation affected due to forest (Tiger reserve) clearance (Stg-I) awaited in Assam portion. Alternate arrangements being made for completion (through contingency scheme) matching with Generation.
148	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,278.00	03/2013 06/2019	06/2019	75	29.14	
149	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	14.85	05/2017 06/2019	06/2019	25	0	Implementation affected due to delayed in land acquisition (land hand over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16).
150	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	341.63	12/2018 -	12/2019	12	0	
151	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	351.70	12/2018 -	12/2019	12	0	
152	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,226.25	06/2013 -	11/2020	89	0	Reasons pending with state government: Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Now the works at various fronts are in progress with intermittent hindrances by villagers. Regular support of Distt. Administration is required.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
153	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	3,939.11	2,307.37	02/2016 09/2019	12/2020	58	137.73	Stoppage of muck dumping for last 13 months at chopra Dumping area.
154	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	5,214.00	02/2019 02/2020	02/2021	24	0	
155	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	868.78	04/2020 -	05/2023	37	0	
	Total		2,01,036.97 -	2,34,794.53	1,67,444.39					
	<u>HEAVY INDUSTRY</u>									
156	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	122.78	
	Total		1,718.00 -	3,827.30	2,289.00					
	<u>HEALTH AND FAMILY WELFARE</u>									
157	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	135.00	05/2017 -	12/2017	7	0	Slow Progress on account of delay in release of fund + stoppage of work by NGT
158	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	203.00	05/2017 -	12/2017	7	0	Delay in release of Funds
159	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	168.90	101.00	05/2017 -	12/2017	7	0	Slow progress on account of labor and material constraints created by the localized unions /goons

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
160	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	32.00	02/2018 -	08/2018	6	0	Progress impacted due to shortage of construction/Building material due to Punjab Govt. Notification banning the mining /querying of aggregate and sand since 18.03.2017, Delay in submission/Mobilizati on of structural drawings by the agency
161	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	-	05/2018 08/2019	08/2019	15	0	
	Total		1,183.93 -	1,183.93	471.00					
	<u>RAILWAYS</u>									
162	NANDYAL- YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106	520.89	
163	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	12/2017	105	154.85	
164	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	516.40	-	03/2010 -	12/2017	93	58.94	
165	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	0	
166	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	386.03	06/2013 -	03/2018	57	0	
167	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	-	03/2010 -	03/2018	96	38.24	
168	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	7,000.00	6,995.27	03/2009 -	03/2018	108	317.58	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
169	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	5,000.00	4,753.99	04/2008 12/2011	06/2018	122	233.33	
170	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	
171	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	13,536.97	11/2002 -	12/2018	193	682.6	
172	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.00	-	03/2016 -	12/2018	33	-10.11	
173	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	12/2018	33	29.06	
174	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,010.00	2,225.72	12/2008 -	03/2019	123	310.64	
175	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	50.68	
176	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,161.64	353.32	03/2015 -	03/2019	48	40	
177	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	941.04	575.19	03/2014 -	03/2019	60	44.07	
178	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	1.06	
179	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	0	
180	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	359.96	
181	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.70	-	02/2015 -	12/2019	58	556.39	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
182	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	318.00	-	02/2006 -	12/2019	166	21.51	
183	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	1,781.98	514.44	03/2004 -	03/2020	192	259.68	
184	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	25.09	
185	JIRIBAM TO IMPHAL (TUPU)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	9,658.00	4,927.46	03/2011 -	03/2020	108	1227.45	
186	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	-	03/2008 06/2008	03/2020	144	145.63	
187	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	2,316.85	03/2014 -	03/2020	72	324.3	
188	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	1,565.18	04/2014 -	03/2020	71	642.73	
189	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	204.95	
190	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84	-2.17	
191	NEW LINE FROM DIMAPUR TO ZUBZA(KOHI) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	357.19	03/2015 -	03/2020	60	252.94	
192	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	-	03/2016 -	12/2020	57	-20	
193	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	
194	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	226.23	
195	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		39,358.15 -	1,06,823.44	48,645.54					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
196	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	480.18	05/2010 -	08/2017	87	0	
197	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	08/2017	45	0	
198	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	08/2017	48	0	
199	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23	0	
200	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	08/2017	9	0	
201	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	342.00	-	01/2017 -	08/2017	7	-01	
202	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 -	09/2017	111	0	
203	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	-	08/2011 -	09/2017	73	0	
204	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	-	04/2013 -	09/2017	53	2.65	
205	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	09/2017	51	0	
206	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	-	03/2014 -	09/2017	42	0	
207	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	-	09/2016 -	09/2017	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
208	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	197.99	09/2016 -	09/2017	12	0	
209	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	-	11/2015 -	09/2017	22	51.83	
210	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	51	0	
211	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	53	0	
212	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	564.90	09/2013 -	10/2017	49	0	
213	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25	0	
214	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	
215	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	11/2017	52	0	
216	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,095.01	03/2013 -	11/2017	56	0	
217	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	0	
218	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	0	
219	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	378.36	01/2016 -	11/2017	22	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
220	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	498.08	01/2016 -	11/2017	22	0	
221	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	465.52	11/2016 -	11/2017	12	0	
222	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	12/2017	106	28.93	
223	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116	0	
224	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63	114.56	
225	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,234.53	05/2013 -	12/2017	55	0	
226	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40	0	
227	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,037.05	03/2013 -	12/2017	57	0	
228	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.03	12/2013 -	12/2017	48	0	
229	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55	0	
230	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52	0	
231	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50	0	
232	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49	0	
233	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,340.87	06/2014 -	12/2017	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
234	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,382.75	08/2013 -	12/2017	52	0	
235	6-LANING OF DHANKUNI- KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,678.94	09/2014 -	12/2017	39	0	
236	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47	0	
237	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	401.67	10/2013 -	12/2017	50	-11	
238	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	828.06	06/2015 -	12/2017	30	0	
239	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	2,447.73	04/2015 -	12/2017	32	0	
240	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	
241	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	236.85	01/2016 -	12/2017	23	0	
242	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,130.07	10/2011 -	12/2017	74	0	
243	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00 -	1,232.00	1,090.17	08/2015 -	12/2017	28	0	
244	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,425.94	07/2017 -	01/2018	6	0	
245	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,848.95	11/2016 -	02/2018	15	0	
246	BRAHMPUTRA BRIDGE, NH NO- 31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	03/2018	95	42.25	
247	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,882.53	11/2011 -	03/2018	76	106.5	
248	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	672.32	01/2014 -	03/2018	50	0	
249	4-LANING OF CHAPRA- HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
250	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,927.60	08/2013 -	03/2018	55	0	
251	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	483.91	07/2014 -	03/2018	44	0	
252	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	363.09	06/2014 -	03/2018	45	0	
253	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,785.50	02/2014 -	03/2018	49	0	
254	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	1,337.00	09/2016 -	03/2018	18	0	
255	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,283.00	08/2016 -	03/2018	19	0	
256	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,082.05	06/2012 -	03/2018	69	0	
257	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	
258	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	0	
259	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	0	
260	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	0	
261	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	87.82	12/2017 -	06/2018	6	0	
262	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13	0	
263	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	225.80	06/2016 -	06/2018	24	0	

[illegible]

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>SHIPPING AND PORTS</u>									
273	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141	300	
274	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	82.72	
	Total		516.39 -	1,269.46	550.92					
	<u>TELECOMMUNICATIONS</u>									
275	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	-	07/2015 -	09/2017	26	0	
	Total		13,334.00 -	13,334.00	.00					
	<u>URBAN DEVELOPMENT</u>									
276	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	251.69	05/2017 08/2017	08/2017	3	0	
277	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	300.77	06/2015 -	09/2017	27	0	
278	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	248.10	09/2016 -	11/2017	14	0	
279	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	168.97	12/2015 12/2017	12/2017	24	0	
280	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	218.90	03/2016 12/2017	12/2017	21	44.75	
281	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24	30.53	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
282	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02 479.87	350.02	347.68	03/2015 12/2017	12/2017	33	0	
283	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD, KERALA	07/2015	154.00 -	154.00	62.77	11/2015 -	12/2017	25	0	
284	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	109.90	08/2016 -	03/2018	19	0	
285	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	114.89	11/2014 -	03/2018	40	0	
286	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 166.97	170.62	128.00	03/2012 03/2018	03/2018	72	-16.77	
287	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	0	
288	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	466.05	12/2015 12/2017	03/2018	27	0	
289	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE 3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD, MADHYA PRADESH	12/2016	164.00 -	164.00	55.98	01/2018 03/2018	03/2018	2	0	
290	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	0	
291	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	38.40	03/2016 -	12/2018	33	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
292	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
293	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
294	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21	0	
295	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	land acquisition
296	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 2,230.23	1,219.21	109.75	10/2019 -	03/2020	5	0	
	Total		60,404.82 -	65,088.18	21,564.62					
	Grand Total		5,37,975.84	6,54,892.71	4,02,226.95					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(August 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82	85
	Total		3,492.00 -	6,000.00				
	<u>CIVIL AVIATION</u>							
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2017	78.87	80
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		624.07 -	994.86				
	<u>COAL</u>							
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60	60
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24	84
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58	72
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	Total		1,242.59 -	2,233.82				
	<u>FERTILISERS</u>							
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29
	Total		197.79 -	209.44				
	<u>HEAVY INDUSTRY</u>							
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIPI) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>PETROLEUM</u>							
11	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217	06/2012	150.00 -	259.93	07/2014 -	09/2017	73.29	38
12	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78	70
13	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50	41
14	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53	20
15	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,256.72	05/2013 -	12/2017	45.83	55
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42	36
18	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22	9
19	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	05/2013	4,124.35 -	5,637.00	04/2016 -	12/2017	36.68	20
20	MH NORTH REDEVELOPMENT PHASE III - [N16000188	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87	12
	Total		17,450.61 -	22,029.58				
	<u>POWER</u>							
21	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165	03/2014	155.57 -	206.42	03/2016 -	10/2017	32.69	19
22	DHUKWAN SMALL HYDRO PROJECT - [N18000189	05/2011	195.42 -	294.60	02/2014 -	12/2018	50.75	58
23	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171	02/2014	196.58 -	225.28	02/2016 -	11/2017	14.60	21
24	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	01/2015	203.28 -	260.03	07/2017 -	12/2017	27.92	5
25	SYSTEM STRENGTHENING XII OF SR - [N18000085	02/2010	232.34 -	245.00	06/2012 -	12/2017	5.45	66
26	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37	13
27	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37	40
28	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,329.43	07/2006 02/2015	11/2017	260.55	136

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
29	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96	12
30	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2017	54.59	87
31	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	06/2018	31.17	48
32	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	12/2017	36.74	30
33	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	03/2018	5.34	16
34	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06	55
35	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	882.13	11/2014 -	12/2017	21.90	37
36	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	02/2014	908.08 -	969.97	06/2016 -	09/2017	6.82	15
37	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83	27
38	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01	61
39	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	03/2018	38.61	23
40	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73	58
41	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60	40
42	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93	118
43	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,352.57	09/2017 -	09/2018	31.55	12
44	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	12/2017	39.30	39
45	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	09/2017	23.13	38
46	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79	62
47	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51	99
48	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14	75

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
49	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50	25
50	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28	111
51	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	12/2017	54.25	75
52	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58	38
53	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14	64
54	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2019	73.65	98
55	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		69,821.30 -	1,03,857.59				
	<u>RAILWAYS</u>							
56	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	12/2017	154.85	105
57	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89	106
58	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39	58
59	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
60	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51	166
61	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
62	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94	93
63	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
64	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
65	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
66	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
67	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06	33

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
68	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	941.04	03/2014 -	03/2019	44.07	60
69	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	03/2018	38.24	96
70	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45	108
71	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64	123
72	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63	144
73	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72
74	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,161.64	03/2015 -	03/2019	40.00	48
75	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94	60
76	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
77	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
78	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
79	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33	122
80	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2018	317.58	108
81	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
82	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		24,810.01 -	93,368.75				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
83	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
84	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25	95
85	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93	106
86	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83	22
87	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50	76

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
88	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65	53
89	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56	63
	Total		5,483.64 -	9,159.30				
	<u>SHIPPING AND PORTS</u>							
90	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00	141
91	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		516.39 -	1,269.46				
	<u>STEEL</u>							
92	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04	12
93	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39	17
	Total		545.61 -	715.40				
	<u>URBAN DEVELOPMENT</u>							
94	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
95	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	349.33	03/2016 -	12/2017	44.75	21
96	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2017	30.53	24
	Total		14,955.59 -	19,673.33				
	Grand Total		1,40,857.60	2,63,338.83				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs.150 Crore and above				(August 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>ATOMIC ENERGY</u>				
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	12/2008 -	03/2017
	Total		13,171.00 -		
	<u>CIVIL AVIATION</u>				
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-
	Total		335.61 -		
	<u>COAL</u>				
3	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	10/2014 06/2017	07/2017
4	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
5	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	Total		1,806.73 -		
	<u>MINES</u>				
6	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 -	11/2016 -	-
7	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 -	11/2016 -	-
	Total		699.63 -		
	<u>STEEL</u>				
8	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
9	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
10	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
11	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
12	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
13	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(August 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	Total		2,025.27 -		
	<u>PETROLEUM</u>				
15	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, KARNATAKA	02/2012	666.00 838.08	11/2015 11/2016	10/2016
16	MARKETING TOP AT KORBA - [N16000186]IOCL, CHHATISGARH	01/2011	141.86 222.81	09/2016 02/2017	02/2017
17	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	08/2015 03/2017	03/2017
18	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	05/2015 06/2017	06/2017
19	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	12/2016 -	-
20	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	03/2017 -	-
21	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	16,504.00 -	03/2017 -	-
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA	01/2006	993.00 -	01/2012 -	-
23	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM	02/2014	163.88 -	07/2016 -	-
24	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL, MAHARASHTRA	05/2015	1,714.00 -	06/2017 -	-
25	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL, GUJARAT	11/2015	500.00 -	03/2017 -	-
26	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN	11/2011	310.00 -	03/2013 -	-
27	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	02/2017 -	-
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		26,697.05 -		
	<u>POWER</u>				
29	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	11/2013 -	03/2016
30	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 609.44	02/2014 03/2016	03/2016
31	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016
32	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL, GUJARAT	10/2015	315.00 -	10/2016 -	10/2016

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(August 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
33	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	02/2017 -	02/2017
34	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	12/2011 03/2016	02/2017
35	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 03/2017	03/2017
36	KANDORNA AND BHANWAD WIND FARM - [N18000234]THDCIL,GUJARAT	11/2016	415.49 -	03/2017 -	03/2017
37	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
38	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,HIMACHAL PRADESH	12/2005	358.42 -	12/2008 09/2010	-
39	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,078.31	07/2013 -	-
40	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
41	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	01/2013 -	-
42	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	02/2016 -	-
	Total		32,127.67 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
43	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 06/2017	06/2017
44	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-
45	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	-
46	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	-
47	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
	Total		1,390.58 -		
	<u>RAILWAYS</u>				
48	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2003	971.22 -	- -	12/2009
49	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011
50	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011
51	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	03/2014
52	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	08/2015
53	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(August 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
54	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	05/2016
55	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016
56	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 1,289.92	- -	01/2017
57	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	06/2017
58	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	07/2017
59	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
60	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-
61	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 175.30	06/1999 -	-
62	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	- -	-
63	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
64	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
65	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
66	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
67	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
68	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
69	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
70	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	-
71	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
72	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-
73	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-
74	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
75	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
76	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
77	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	-
78	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
79	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	- -	-
80	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
81	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007	-
82	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
83	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
84	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
85	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-
86	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
87	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
88	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
89	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
90	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
91	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
92	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
93	KICHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
94	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
95	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
96	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
97	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-
98	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
99	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
100	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-
101	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
102	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
103	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 -	06/2005 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
104	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-
105	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	-
106	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
107	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
108	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN	04/2008	516.23 -	03/2014 -	-
109	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	-
110	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
111	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-
112	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
113	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-
114	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
115	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-
116	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
117	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
118	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-
119	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-
120	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	- -	-
121	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
122	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-
123	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
124	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
125	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR, RAJASTHAN	04/2010	739.65 -	- -	-
126	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-
127	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
128	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
129	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 -	- -	-
130	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
131	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-
132	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 -	12/2015 -	-
133	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
134	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
135	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
136	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
137	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
138	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
139	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
140	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
141	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
142	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
143	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-
144	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-
145	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
146	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
147	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-
148	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-
149	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
150	ATTIPPATTU PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-
151	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 2,350.00	- -	-
152	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
153	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
154	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
155	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
156	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
157	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
158	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
159	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
160	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
161	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	-
162	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
163	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
164	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
165	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
166	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
167	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
168	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
169	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-
170	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-
171	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
172	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
173	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
174	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
175	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
176	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
177	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
178	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
179	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
180	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
181	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
182	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
183	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
184	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
185	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
186	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
187	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
188	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
189	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
190	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-
191	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
192	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
193	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
194	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
195	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	-
196	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	-
197	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
198	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(August 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
199	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
200	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
201	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
202	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
203	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
204	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
205	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
206	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
207	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
208	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
209	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
210	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
211	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
212	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
213	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
214	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
215	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	- -	-
216	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
217	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
218	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
219	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
220	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
221	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
222	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
223	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(August 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
224	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
225	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
226	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
227	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
228	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
229	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
230	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
231	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
232	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
233	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
234	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
235	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
236	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
237	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
238	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
239	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
240	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-
241	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
242	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-
243	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 203.40	- -	-
244	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
245	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
246	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
247	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
248	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(August 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
249	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-
250	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
251	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-
252	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-
253	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-
254	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 -	- -	-
255	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 -	- -	-
256	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-
257	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- -	-
258	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- -	-
259	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	- -	-
260	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
261	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
262	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-
263	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
264	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
265	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
266	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	-
267	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-
268	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
269	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
270	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-
	Total		2,19,204.83 -		

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
271	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	07/2016 -	07/2016
272	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD, ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010
273	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD, ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010
274	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD, MIZORAM	08/2010	195.04 -	10/2010 -	10/2010
275	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD, MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
276	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD, ASSAM	11/2010	470.20 -	02/2011 -	02/2011
277	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
278	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
279	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH, BIHAR	10/2013	278.39 -	08/2014 -	08/2014
280	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH, MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014
281	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD, MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014
282	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP, MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
283	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD, CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015
284	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD, CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
285	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD, CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015
286	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015
287	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP, MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015
288	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH, TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
289	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
290	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015
291	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
292	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
293	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016
294	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016
295	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
296	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
297	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
298	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016
299	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	06/2016
300	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
301	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
302	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016
303	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016
304	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016
305	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016
306	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016
307	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016
308	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
309	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016
310	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016
311	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016
312	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2016
313	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016
314	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016
315	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2016
316	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	11/2016
317	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016
318	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016
319	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	12/2016
320	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016
321	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016
322	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017
323	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017
324	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017
325	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	02/2017
326	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017
327	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
328	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017
329	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017
330	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017
331	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017
332	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017
333	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017
334	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017
335	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017
336	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	04/2017
337	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	05/2017
338	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	05/2017
339	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	05/2017
340	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	05/2017
341	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017
342	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017
343	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017
344	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017
345	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2017
346	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017
347	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	06/2017

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
348	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	06/2017
349	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017
350	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017
351	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	07/2017
352	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017
353	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017
354	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
355	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
356	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
357	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
358	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
359	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
360	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
361	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
362	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
363	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
364	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
365	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
366	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
367	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
368	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
369	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-
370	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
371	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
372	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
373	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
374	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
375	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
376	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
377	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
378	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
379	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
380	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
381	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
382	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
383	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
384	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
385	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
386	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
387	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
388	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
389	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
390	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
391	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
392	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
393	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
394	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
395	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
396	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
397	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
398	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
399	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
400	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
401	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
402	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
403	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
404	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
405	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
406	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
407	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
408	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
409	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
410	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
411	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
412	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
413	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-
414	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-
415	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
416	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
417	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
418	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
419	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
420	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
421	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
422	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
423	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
424	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
425	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
426	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
427	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
428	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
429	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
430	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
431	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-
432	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
433	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
434	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
435	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
436	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
437	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
438	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
439	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
440	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
441	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
442	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
443	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
444	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
445	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
446	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
447	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
448	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
449	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
450	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
451	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
452	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
453	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
454	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
455	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
456	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
457	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
458	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
459	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-
460	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-
461	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
462	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
463	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
464	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
465	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
466	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
467	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
468	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
469	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
470	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
471	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
472	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
473	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
474	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
475	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
476	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
477	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
478	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
479	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
480	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
481	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
482	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
483	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
484	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
485	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
486	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
487	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
488	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
489	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
490	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
491	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
492	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-
493	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	-
494	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
495	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
496	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-
497	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-
498	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
499	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
500	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
501	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
502	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-
503	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
504	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
505	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
506	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
507	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
508	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
509	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
510	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
511	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
512	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
513	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
514	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
515	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
516	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
517	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
518	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
519	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
	Total		1,31,626.68 -		
	<u>SHIPPING AND PORTS</u>				
520	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
521	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-
522	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU	10/2013	198.94 -	06/2017 -	-
523	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU	12/2014	274.85 -	04/2017 -	-
	Total		3,146.86 -		

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(August 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>TELECOMMUNICATIONS</u>				
524	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
525	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	<u>URBAN DEVELOPMENT</u>				
526	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016
527	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 13,845.01	06/2011 12/2015	04/2017
528	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 07/2017	07/2017
529	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
530	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
531	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
532	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
533	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	-
	Total		69,630.93 -		
	Grand Total		5,04,392.27		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above						(August 2017)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00	175.00	1.83	-	12/2017	-	0/0
	Total		175.00	175.00	1.83				0/0
	<u>RAILWAYS</u>								
2	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78	268.78	94.80	-	08/2017	-	0/0
3	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20	365.00	-	-	12/2017	-	0/0
4	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19	412.05	352.29	-	03/2018	-	0/0
5	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75	199.75	211.80	-	03/2018	-	0/0
6	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL, MULTI STATE	04/2008	822.39	1,480.83	-	-	03/2018	-	0/1
7	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77	445.00	319.06	-	03/2018	-	0/0
8	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55	330.00	87.65	-	03/2018	-	0/0
9	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	523.17	1,871.00	1,071.96	-	03/2018	-	0/0
10	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00	855.16	585.06	-	05/2018	-	0/0
11	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00	477.31	92.43	-	10/2018	-	0/0
12	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94	157.94	47.63	-	11/2018	-	0/0
13	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	720.00	678.54	-	-	12/2018	-	0/38
14	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08	348.55	14.66	-	02/2019	-	0/0
15	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39	272.99	63.54	-	02/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(August 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	648.00	-	- -	02/2019	-	0/0
17	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	525.00	544.20	- -	03/2019	-	0/0
18	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	111(R1)	0/0
19	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	03/2019	114(R1)	0/0
20	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	780.00	421.40	- -	03/2019	-	0/0
21	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	399.63	-	- -	03/2019	-	0/0
22	VIRAMGAM-SAMAKHALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	-	0/0
23	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	293.68	76.86	- -	03/2019	-	0/0
24	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
25	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	508.00	477.36	- -	03/2019	-	0/0
26	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	398.93	104.16	- -	03/2019	-	0/0
27	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,127.00	-	- -	03/2019	-	0/1
28	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	355.96	-	- -	03/2019	-	0/0
29	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	718.54	272.77	- -	05/2019	-	0/0
30	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	580.00	-	- -	07/2019	-	2/3
31	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	2,145.00	920.59	- -	03/2020	-	0/0
32	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	975.62	-	- -	03/2020	-	0/0
33	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0
34	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	450.00	117.50	- -	03/2020	-	0/0
35	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	- -	03/2020	-	0/0
36	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,160.83	438.97	- -	03/2020	-	1/1



(August 2017)

[illegible]

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(August 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
57	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP, MAHARASHTRA	03/2015	168.30 -	168.30	13.43	- -	10/2017	-	0/4
58	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	845.24	64.50	- -	11/2017	-	0/0
59	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, PUNJAB	09/2015	273.06 -	273.06	36.58	- -	11/2017	-	0/0
60	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	818.53	- -	12/2017	-	3/3
61	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	479.00	396.40	- -	12/2017	-	0/0
62	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
63	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	1,665.00	2,091.52	- -	12/2017	-	0/0
64	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
65	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	-	- -	01/2018	-	0/0
66	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	1,393.00	2,137.09	- -	01/2018	-	0/0
67	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	275.90	-	- -	02/2018	-	0/0
68	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI, DELHI	09/2015	771.18 -	771.18	450.78	- -	03/2018	-	0/0
69	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHINDEAPAR BRIDGE - [N24000251]NHDP, GOA	03/2015	297.00 -	297.00	38.33	- -	04/2018	-	0/1
70	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
71	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	509.13	-	- -	04/2018	-	0/0
72	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	726.67	18.03	- -	04/2018	-	0/0
73	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	516.13	-	- -	04/2018	-	0/0
74	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	414.00	-	- -	05/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(August 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
75	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	-	- -	05/2018	-	0/0
76	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	-	- -	05/2018	-	0/0
77	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	-	- -	05/2018	-	0/0
78	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	542.57	- -	05/2018	-	0/0
79	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	-	- -	05/2018	-	0/0
80	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	6.14	- -	05/2018	-	0/0
81	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	600.85	193.80	- -	05/2018	-	0/0
82	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0
83	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	197.69	-	- -	07/2018	-	0/0
84	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	37.95	- -	07/2018	-	0/0
85	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	244.00	-	- -	07/2018	-	0/0
86	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	547.57	- -	07/2018	-	0/0
87	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	478.00	- -	08/2018	-	0/0
88	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	129.75	- -	08/2018	-	0/0
89	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	6.32	- -	08/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(August 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
90	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITATION - [N24000620]NHAI, WEST BENGAL	09/2016	767.03	767.03	35.56	-	08/2018	-	0/0
91	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A (NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46	331.46	-	-	10/2018	-	0/0
92	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96	1,423.96	454.64	-	11/2018	-	0/0
93	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97	1,134.97	151.85	-	11/2018	-	0/0
94	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37	229.37	28.51	-	11/2018	-	0/0
95	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20	1,657.20	120.00	-	01/2019	-	0/0
96	FOUR LANING OF BIAORA - DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79	1,583.79	-	-	01/2019	-	0/0
97	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49	227.49	-	-	01/2019	-	0/0
98	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20	273.20	-	-	02/2019	-	0/0
99	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB, SERVICE ROADS, FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA	12/2015	649.50	649.50	-	-	03/2019	-	0/0
100	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15	997.15	159.68	-	03/2019	-	0/0
101	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42	1,167.42	5.75	-	03/2019	-	0/0
102	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25	400.25	-	-	03/2019	-	0/0
103	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17	446.17	-	-	03/2019	-	0/0
104	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72	2,128.72	213.57	-	04/2019	-	0/0
105	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10	1,041.10	-	-	04/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(August 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
106	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
107	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	676.73	41.58	- -	04/2019	-	0/0
108	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	1,587.49	-	- -	04/2019	-	0/0
109	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	899.00	-	- -	04/2019	-	0/0
110	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	-	- -	04/2019	-	0/0
111	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	1,664.20	-	- -	04/2019	-	0/0
112	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	-	0/0
113	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	-	0/0
114	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI, UTTAR PRADESH	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0
115	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	248.97	-	- -	05/2019	-	0/0
116	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA	09/2016	1,004.67 -	1,004.67	-	- -	05/2019	-	0/0
117	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	244.90	10.85	- -	05/2019	-	0/0
118	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
119	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	546.00	-	- -	07/2019	-	0/0
120	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	591.66	-	- -	07/2019	-	0/0
121	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	2,510.04	-	- -	08/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
122	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	-	0/0
	Total		55,026.90 -	55,026.39	9,229.28				3/8
	<u>URBAN DEVELOPMENT</u>								
123	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	3.06	- -	04/2019	-	0/2
	Total		197.33 -	197.33	3.06				0/2
	Grand Total		1,00,302.14	1,20,972.80	21,282.88				6/62

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above				(August 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 09/2017	09/2017	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-	0/0
	Total		959.68 -			0/0
	<u>COAL</u>					
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 -	06/2017 -	08/2017	0/0
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
8	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
9	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH	05/2017	976.95 -	03/2026 -	03/2026	0/0
	Total		20,347.18 -			0/0
	<u>FERTILISERS</u>					
10	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 04/2019	04/2019	0/0
	Total		197.79 -			0/0
	<u>STEEL</u>					
11	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
12	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2017	0/0
13	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
14	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
15	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	03/2018	0/0
16	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
17	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
18	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 -	06/2018	0/0
19	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	07/2018 -	07/2018	0/0
20	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	08/2018	0/0
21	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	08/2018 -	08/2018	0/0
22	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	09/2018 -	09/2018	0/0
23	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
24	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
25	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
26	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
27	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
28	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
29	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
30	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
31	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	Total		15,340.85 -			0/0
	<u>PETROLEUM</u>					
32	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
33	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
34	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	06/2017 10/2017	10/2017	0/0
35	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	07/2017 -	02/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
36	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	12/2016 -	03/2018	0/0
37	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH	03/2009	181.02 -	01/2017 03/2018	03/2018	0/0
38	NEW 250 TMTPL LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 -	09/2017 -	03/2018	0/0
39	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA	12/2015	3,190.69 -	04/2018 04/2018	04/2018	0/0
40	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA	02/2015	2,899.93 -	05/2017 05/2018	05/2018	0/0
41	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 1,330.00	06/2018 -	06/2018	0/0
42	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL, KERALA	05/2015	337.06 -	08/2018 -	08/2018	0/0
43	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC, GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0
44	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC, ANDHRA PRADESH	04/2017	420.76 -	09/2018 -	09/2018	0/0
45	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0
46	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	03/2017 -	11/2018	0/0
47	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]IOCL, BIHAR	07/2015	822.66 -	11/2018 -	11/2018	0/0
48	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT	05/2015	1,671.22 567.22	11/2019 12/2018	12/2018	0/0
49	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU	05/2016	4,497.00 -	12/2018 -	12/2018	0/0
50	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL, MAHARASHTRA	05/2015	193.40 -	01/2019 -	01/2019	0/0
51	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL, ODISHA	05/2016	429.00 -	01/2019 -	01/2019	0/0
52	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA	11/2014	6,068.80 6,068.80	04/2019 03/2019	03/2019	0/0
53	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC, MAHARASHTRA	01/2015	4,619.94 -	12/2017 03/2019	03/2019	0/0
54	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU	11/2015	390.52 -	03/2019 -	04/2019	0/0
55	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	09/2011 06/2019	06/2019	0/0
56	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL, HIMACHAL PRADESH	02/2016	151.00 -	09/2019 -	09/2019	0/0
57	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE	02/2015	890.00 -	10/2019 -	10/2019	0/0
58	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	05/2019 10/2019	10/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
59	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	11/2019 -	11/2019	0/0
60	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	12/2019 -	12/2019	0/0
61	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
62	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	12/2019 -	12/2019	0/0
63	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	2,253.00 -	12/2019 -	12/2019	0/0
64	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,250.00 -	12/2019 -	12/2019	0/0
65	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	12/2019 -	12/2019	0/0
66	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
67	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR	05/2016	664.00 -	12/2020 -	02/2020	0/0
68	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	02/2020 -	02/2020	0/0
69	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	03/2020	0/0
70	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
71	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 250.00	05/2020 -	05/2020	0/0
72	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
73	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	06/2020 -	06/2020	0/0
74	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR	09/2015	324.00 -	06/2020 -	06/2020	0/0
75	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 -	07/2020 -	07/2020	0/0
76	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	12/2020 -	08/2020	0/0
77	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	10/2020 -	10/2020	0/0
78	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
79	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
80	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,212.00 -	12/2020 -	12/2020	0/0
81	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,828.00 -	12/2020 -	12/2020	0/0
82	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
83	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
84	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
85	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 -	08/2021 -	08/2021	0/0
86	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND	12/2015	658.62 910.23	03/2023 03/2022	03/2022	0/0
87	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT	02/2017	1,162.56 -	03/2026 -	03/2026	0/0
88	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
89	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
90	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA	02/2016	554.00 -	02/2020 -	02/2020	0/0
91	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	02/2020 -	02/2020	0/0
	Total		1,34,596.63 -			0/0
	<u>POWER</u>					
92	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 09/2017	09/2017	0/0
93	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 10/2017	10/2017	0/0
94	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	10/2017	0/0
95	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	11/2017 -	11/2017	0/0
96	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	12/2017	0/0
97	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT	01/2016	244.19 -	07/2018 -	12/2017	0/0
98	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	12/2017	0/0
99	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
100	50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU	09/2017	287.48 -	03/2018 -	03/2018	0/0
101	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 -	12/2015 -	03/2018	0/0
102	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	04/2018	0/0
103	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 -	04/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
104	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL, TRIPURA	05/2016	409.19 -	05/2018 -	05/2018	0/0
105	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	11/2017 -	06/2018	0/0
106	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL, MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
107	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL, MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
108	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
109	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL, ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
110	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL, MULTI STATE	07/2016	150.99 -	07/2018 -	07/2018	0/0
111	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
112	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	10/2018 -	10/2018	0/0
113	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
114	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
115	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL, MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
116	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL, GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
117	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
118	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 -	01/2019 -	01/2019	0/0
119	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL, MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
120	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL, MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
121	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
122	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 -	03/2019	0/0
123	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL, MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
124	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL, MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
125	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL, MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
126	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
127	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL, MULTI STATE	10/2016	167.75 -	04/2019 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
128	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
129	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
130	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
131	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
132	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
133	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0
134	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
135	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
136	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
137	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
138	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
139	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
140	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
141	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
142	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 -	09/2020 -	09/2020	0/0
143	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	05/2023	0/0
144	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		79,317.13 -			0/0
	<u>HEAVY INDUSTRY</u>					
145	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
146	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
147	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 08/2019	08/2019	0/0
148	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-	0/0
149	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	-	0/0
150	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	-	0/0
151	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
	Total		1,839.07 -			0/0
	<u>RAILWAYS</u>					
152	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2003	971.22 -	- -	12/2009	0/0
153	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011	0/0
154	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011	0/0
155	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	03/2014	0/0
156	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	08/2015	0/0
157	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016	0/0
158	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	05/2016	0/0
159	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016	0/0
160	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	07/2017	0/0
161	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	08/2017	0/0
162	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	12/2017	0/0
163	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	12/2017	0/0
164	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	12/2017	0/0
165	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	03/2018	0/0
166	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	03/2018	0/0
167	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
168	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	03/2018	0/0
169	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
170	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	- -	03/2018	0/0
171	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
172	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2018	0/0
173	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2018	0/0
174	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0
175	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	05/2018	0/0
176	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2018	0/0
177	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
178	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	10/2018	0/0
179	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	11/2018	0/0
180	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2018	0/0
181	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
182	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2018	0/0
183	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	02/2019	0/0
184	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	02/2019	0/0
185	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	02/2019	0/0
186	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2019	0/0
187	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
188	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	03/2019	0/0
189	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	03/2019	0/0
190	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	- -	03/2019	0/0
191	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
192	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2019	0/0
193	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	03/2019	0/0
194	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
195	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	03/2019	0/0
196	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	03/2019	0/0
197	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	03/2019	0/0
198	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
199	AMBARİ FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	- -	03/2019	0/0
200	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	- -	03/2019	0/0
201	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	- -	03/2019	0/0
202	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
203	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
204	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0
205	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
206	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN	04/2012	471.82 -	03/2019 -	03/2019	0/0
207	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
208	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	03/2019	0/0
209	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
210	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019	0/0
211	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	05/2019	0/0
212	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
213	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	12/2019	0/0
214	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	03/2004 -	03/2020	0/0
215	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
216	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	03/2011 -	03/2020	0/0
217	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
218	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	- -	03/2020	0/0
219	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
220	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	04/2014 -	03/2020	0/0
221	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
222	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2020	0/0
223	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
224	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
225	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
226	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	- -	03/2020	0/0
227	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
228	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	03/2020	0/0
229	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	03/2020	0/0
230	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
231	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
232	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0
233	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
234	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0
235	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
236	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
237	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	- -	12/2020	0/0
238	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
239	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
240	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
241	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	03/2021	0/0
242	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2021	0/0
243	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- -	03/2021	0/0
244	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	03/2021	0/0
245	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	03/2021	0/0
246	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	- -	03/2021	0/0
247	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2021 -	03/2021	0/0
248	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2021 -	03/2021	0/0
249	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2021 -	03/2021	0/0
250	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
251	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2021	0/0
252	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	03/2021	0/0
253	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	03/2021	0/0
254	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0
255	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
256	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	06/2021	0/0
257	TAMLUK DIGHA 88.9 KM WITH MM DESHPAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	763.18 -	12/2021 -	12/2021	0/0
258	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2021	0/0
259	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
260	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	03/2022	0/0
261	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
262	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	06/2022	0/0
263	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
264	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 -	12/2022	0/0
265	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
266	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
267	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	12/2024	0/0
268	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
269	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
270	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
271	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
272	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-	0/0
273	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 175.30	06/1999 -	-	0/0
274	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	-	0/0
275	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
276	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
277	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
278	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
279	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
280	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
281	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
282	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	-	0/0
283	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
284	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-	0/0
285	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-	0/0
286	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
287	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
288	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
289	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	-	0/0
290	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
291	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
292	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
293	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
294	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-	0/0
295	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
296	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
297	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
298	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
299	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
300	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
301	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
302	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
303	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
304	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
305	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
306	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-	0/0
307	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
308	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
309	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-	0/0
310	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
311	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
312	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-	0/0
313	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	-	0/0
314	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
315	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
316	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN	04/2008	516.23 -	03/2014 -	-	0/0
317	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
318	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
319	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
320	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
321	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0
322	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
323	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
324	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
325	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
326	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
327	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-	0/0
328	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	- -	-	0/0
329	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-	0/0
330	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-	0/0
331	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-	0/0
332	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-	0/0
333	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
334	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 -	- -	-	0/0
335	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
336	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
337	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-	0/0
338	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
339	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
340	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
341	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
342	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
343	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
344	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
345	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
346	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
347	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
348	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
349	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
350	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
351	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
352	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
353	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
354	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
355	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-	0/0
356	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 2,350.00	- -	-	0/0
357	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
358	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
359	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
360	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
361	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
362	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
363	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
364	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
365	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
366	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
367	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
368	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
369	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
370	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
371	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
372	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
373	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
374	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-	0/0
375	PLASSEY-JAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-	0/0
376	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
377	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
378	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
379	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
380	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
381	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
382	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
383	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
384	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
385	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
386	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
387	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
388	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
389	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
390	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
391	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
392	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
393	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
394	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
395	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-	0/0
396	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
397	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
398	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
399	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
400	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	-	0/0
401	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	-	0/0
402	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
403	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
404	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
405	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
406	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
407	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
408	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
409	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
410	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
411	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
412	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
413	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
414	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
415	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
416	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
417	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
418	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
419	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
420	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
421	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
422	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
423	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
424	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
425	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
426	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
427	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
428	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
429	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
430	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
431	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
432	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
433	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
434	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
435	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
436	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-	0/0
437	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
438	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-	0/0
439	HOSADURGA - CHICKAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 203.40	- -	-	0/0
440	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
441	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
442	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
443	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
444	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
445	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
446	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
447	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-	0/0
448	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-	0/0
449	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-	0/0
450	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 -	- -	-	0/0
451	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 -	- -	-	0/0
452	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-	0/0
453	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- -	-	0/0
454	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
455	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	- -	-	0/0
456	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
457	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-	0/0
458	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
459	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
460	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
461	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	-	0/0
462	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	- -	-	0/0
463	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
464	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
465	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-	0/0
	Total		3,20,749.38 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
466	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	07/2016	0/0
467	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0
468	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
469	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
470	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
471	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
472	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
473	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
474	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0
475	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
476	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
477	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015	0/0
478	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015	0/0
479	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015	0/0
480	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015	0/0
481	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015	0/0
482	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015	0/0
483	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
484	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015	0/0
485	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
486	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
487	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
488	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0
489	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
490	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016	0/0
491	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
492	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
493	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
494	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
495	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
496	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
497	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
498	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
499	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
500	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH, BIHAR	03/2015	206.80 -	07/2016 -	10/2016	0/0
501	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016	0/0
502	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
503	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH, BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016	0/0
504	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
505	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD, ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
506	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
507	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017	0/0
508	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
509	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD (NH-52B) (NEW NH NO.215) FROM KM 0.00 TO KM 68.30 IN THE STATE - [N24000373]PWD, UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
510	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP, UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
511	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
512	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH, ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017	0/0
513	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH, ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017	0/0
514	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH, ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017	0/0
515	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	04/2009 -	05/2017	0/0
516	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	03/2008 -	05/2017	0/0
517	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 -	05/2017	0/0
518	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
519	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B (EXTN) IN ASSAM - [N24000392]PWD, ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
520	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP, MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
521	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP, MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
522	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
523	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017	0/0
524	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	06/2017	0/0
525	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017	0/0
526	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017	0/0
527	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
528	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
529	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017	0/0
530	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017	0/0
531	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017	0/0
532	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	08/2017	0/0
533	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
534	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	08/2017	0/0
535	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2017	0/0
536	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017	0/0
537	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017	0/0
538	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017	0/0
539	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
540	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
541	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
542	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017	0/0
543	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
544	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017	0/0
545	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017	0/0
546	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
547	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017	0/0
548	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017	0/0
549	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
550	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017	0/0
551	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017	0/0
552	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017	0/0
553	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017	0/0
554	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017	0/0
555	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017	0/0
556	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
557	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
558	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
559	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
560	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017	0/0
561	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017	0/0
562	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017	0/0
563	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017	0/0
564	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	11/2017	0/0
565	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
566	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2017	0/0
567	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2017	0/0
568	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2017	0/0
569	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017	0/0
570	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
571	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2017	0/0
572	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
573	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2017	0/0
574	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
575	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017	0/0
576	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017	0/0
577	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2017	0/0
578	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2017	0/0
579	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2017	0/0
580	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017	0/0
581	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017	0/0
582	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017	0/0
583	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
584	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	12/2017	0/0
585	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
586	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017	0/0
587	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	12/2017	0/0
588	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	12/2017	0/0
589	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
590	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0
591	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	12/2017	0/0
592	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	12/2017	0/0
593	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
594	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
595	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
596	FOUR LANING OF KATHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
597	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
598	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018	0/0
599	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
600	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
601	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
602	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
603	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
604	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	02/2018	0/0
605	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	03/2018	0/0
606	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2018	0/0
607	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	03/2018	0/0
608	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2018	0/0
609	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	03/2018	0/0
610	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	03/2018	0/0
611	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2018	0/0
612	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	03/2018	0/0
613	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
614	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
615	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
616	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
617	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
618	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
619	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
620	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
621	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	03/2018	0/0
622	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
623	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
624	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
625	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
626	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	-	03/2018	0/0
627	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2018	0/0
628	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
629	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2018	0/0
630	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
631	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	-	04/2018	0/0
632	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	-	04/2018	0/0
633	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	-	04/2018	0/0
634	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	-	04/2018	0/0
635	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	04/2018	0/0
636	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 265.35	05/2018 -	05/2018	0/0
637	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	-	05/2018	0/0
638	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	-	05/2018	0/0
639	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	-	05/2018	0/0
640	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	-	05/2018	0/0
641	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	-	05/2018	0/0
642	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	-	05/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
643	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	05/2018	0/0
644	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	- -	05/2018	0/0
645	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	06/2018	0/0
646	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
647	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2018	0/0
648	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	06/2018	0/0
649	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
650	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
651	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
652	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
653	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
654	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
655	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
656	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	06/2018	0/0
657	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
658	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	- -	06/2018	0/0
659	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
660	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
661	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	07/2018	0/0
662	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0
663	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	- -	07/2018	0/0
664	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	- -	07/2018	0/0
665	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	- -	08/2018	0/0
666	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
667	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	08/2018	0/0
668	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	- -	08/2018	0/0
669	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	- -	10/2018	0/0
670	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	- -	11/2018	0/0
671	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	- -	11/2018	0/0
672	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
673	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
674	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHAI, ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
675	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
676	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
677	FOUR LANING OF BIAORA - DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	- -	01/2019	0/0
678	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	- -	01/2019	0/0
679	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	- -	02/2019	0/0
680	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
681	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA	12/2015	649.50 -	- -	03/2019	0/0
682	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
683	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 -	- -	03/2019	0/0
684	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42 -	- -	03/2019	0/0
685	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	- -	03/2019	0/0
686	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	- -	03/2019	0/0
687	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	- -	04/2019	0/0
688	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	- -	04/2019	0/0
689	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
690	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	- -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
691	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	04/2019	0/0
692	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	04/2019	0/0
693	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	04/2019	0/0
694	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	04/2019	0/0
695	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	04/2019	0/0
696	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	05/2019	0/0
697	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	05/2019	0/0
698	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	05/2019	0/0
699	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	05/2019	0/0
700	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	- -	05/2019	0/0
701	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	- -	05/2019	0/0
702	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
703	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
704	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	06/2019	0/0
705	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGOUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0
706	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
707	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
708	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	- -	07/2019	0/0
709	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	- -	07/2019	0/0
710	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	08/2019	0/0
711	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
712	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
713	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
714	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
715	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
716	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	02/2020 -	02/2020	0/0
717	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI, TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
718	FOUR LANNING OF JHANSI-KHAJURAHO SECTION (PKG-I) FROM KM 0.00 TO KM 76.3 (EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI, UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	03/2020	0/0
719	FOUR LANNING OF JHANSI-KHAJURAHO SECTION (PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3 (EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
720	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
721	4-LANNING OF BODHRE-DHULE SECTION (KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
722	4-LANNING OF WARDHA- BUTIBORI SECTION (KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	03/2020	0/0
723	4-LANNING OF YAVATMAL-WARDHA SECTION (KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA	03/2017	988.34 -	03/2020 -	03/2020	0/0
724	4-LANNING OF MAHAGAON-YAVATMAL SECTION (KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	03/2020	0/0
725	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 -	03/2020 -	03/2020	0/0
726	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	03/2020	0/0
727	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
728	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
729	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
730	REHABILITATION AND UPGRADEATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI, ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
731	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI, ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	03/2020	0/0
732	4 LANING OF PISKA MORE TO PALMA SECTION (FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI, JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
733	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI, JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
734	REHABILITATION AND UPGRADEATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
735	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI, UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
736	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI, KARNATAKA	03/2017	985.41 -	03/2020 -	03/2020	0/0
737	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48 (OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI, KARNATAKA	03/2017	831.58 -	03/2020 -	03/2020	0/0
738	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS (KM 189+000 TO KM 260+000 OF NH-48 (O - [N24000675]NHAI, KARNATAKA	03/2017	993.16 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
739	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0
740	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
741	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	06/2020	0/0
742	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
743	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
744	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
745	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
746	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
747	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
748	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
749	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
750	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
751	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
752	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
753	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-	0/0
754	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
755	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
756	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
757	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-	0/0
758	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
759	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
760	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
761	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
762	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
763	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
764	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
765	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
766	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
767	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
768	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
769	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
770	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
771	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
772	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
773	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
774	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
775	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
776	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
777	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
778	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
779	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
780	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
781	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
782	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
783	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
784	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
785	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
786	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
787	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
788	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-	0/0
789	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-	0/0
790	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
791	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
792	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
793	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
794	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
795	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
796	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
797	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
798	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
799	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
800	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
801	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
802	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
803	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
804	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
805	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
806	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-	0/0
807	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
808	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
809	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
810	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
811	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
812	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
813	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
814	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-	0/0
815	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
816	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
817	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
818	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
819	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
820	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
821	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUARI - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
822	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
823	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
824	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
825	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
826	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
827	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
828	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
829	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
830	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
831	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
832	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
833	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
834	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-	0/0
835	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-	0/0
836	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
837	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
838	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
839	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
840	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
841	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0
842	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
843	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
844	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0
845	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
846	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
847	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
848	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
849	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
850	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
851	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
852	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
853	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
854	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
855	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
856	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
857	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
858	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
859	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
860	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
861	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
862	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-	0/0
863	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
864	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
865	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHAI,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
866	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHAI,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
867	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
868	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	-	0/0
869	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
870	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
871	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
872	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
873	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
874	REHABILITATION AND UPGRADE TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
875	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
876	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-	0/0
877	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASTHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
878	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
879	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
880	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
881	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
882	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
883	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
884	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
885	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
886	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
887	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
888	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
889	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
890	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
891	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
892	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
893	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
894	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
	Total		2,95,741.59 -			0/0
	<u>SHIPPING AND PORTS</u>					
895	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	12/2017	0/0
896	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
897	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	12/2018	0/0
898	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
899	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	Total		3,399.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
900	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	09/2017	0/0
901	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	Total		13,752.26 -			0/0
	<u>URBAN DEVELOPMENT</u>					
902	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
903	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	11/2017	0/0
904	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2015 12/2017	12/2017	0/0
905	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000093]CPWD,RAJASTHAN	08/2014	350.02 479.87	03/2015 12/2017	12/2017	0/0
906	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	11/2015 -	12/2017	0/0
907	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	03/2018	0/0
908	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 12/2017	03/2018	0/0
909	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	03/2018	0/0
910	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
911	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
912	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
913	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
914	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 -	02/2020	0/0
915	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
916	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 2,230.23	10/2019 -	03/2020	0/0
917	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
918	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(August 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
919	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	-	0/0
	Total		1,17,189.53 -			0/0
	Grand Total		10,05,148.55			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Annexure - XI

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 969.97	969.97	711.64	06/2016 02/2018	09/2017
	Total		908.08 -	969.97	711.64		
	<u>PETROLEUM</u>						
2	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	51.38	12/2020 -	08/2020
	Total		2,321.00 -	2,321.00	51.38		
	<u>POWER</u>						
3	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	461.43	03/2018 -	09/2017
	Total		550.06 -	550.06	461.43		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	108.23	07/2018 -	06/2018
	Total		667.00 -	667.00	108.23		
	<u>POWER</u>						
5	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	106.81	07/2018 -	12/2017
6	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	104.56	05/2018 -	12/2017
	Total		406.30 -	406.30	211.37		
	<u>PETROLEUM</u>						
7	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	53.32	02/2019 -	12/2018
8	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	57.85	05/2019 -	12/2018

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
9	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	98.67	12/2020 -	02/2020
	Total		1,267.52 -	1,267.52	209.84		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
10	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	-	03/2020 -	05/2019
	Total		296.19 -	254.00	.00		
	Grand Total		6,416.15	6,435.85	1,753.89		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	1/2009	309.46 -	553.53	484.76	01/2011 09/2017	09/2017
	Total		309.46 -	553.53	484.76		
	<u>COAL</u>						
2	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	78.39	03/2015 03/2020	03/2020
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	263.42	03/2022 -	03/2022
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	294.63	03/2012 03/2018	03/2018
5	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	52.71	03/2023 -	03/2023
6	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	258.90	06/2015 09/2019	09/2019
7	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
8	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
10	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	138.36	03/2021 -	03/2021
11	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	360.21	03/2020 -	03/2020
12	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	351.84	03/2021 -	03/2021
13	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
14	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	24.67	03/2019 -	03/2019
15	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	673.05	03/2026 -	03/2026
16	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	21.75	03/2019 -	03/2019
17	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	45.89	03/2020 -	03/2020
18	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	7.46	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	65.88	03/2020 -	03/2020
20	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	19.94	03/2019 -	03/2019
21	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	84.95	03/2019 -	03/2019
22	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	34.26	03/2021 -	03/2021
23	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.37	03/2021 -	03/2021
24	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	48.69	03/2018 -	03/2018
25	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
26	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	72.23	03/2023 -	03/2023
27	GOKUL - [N06000120]	11/2014	267.67 -	267.67	203.98	03/2018 -	03/2018
28	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	124.00	03/2019 -	03/2019
29	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	30.32	03/2019 -	03/2019
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	109.31	03/2021 -	03/2021
31	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
32	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	167.04	12/2019 -	12/2019
33	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	5.65	09/2019 -	09/2019
34	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	4,659.77	12/2015 04/2018	04/2018
35	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,430.17	03/2023 -	03/2023
36	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	174.29	03/2020 -	03/2020
37	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
38	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	44.86	03/2021 -	03/2021
39	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
40	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	-	03/2022 -	03/2022
41	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	9.72	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
42	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,107.67	11/2021 -	11/2021
43	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	427.59	03/2018 -	03/2018
44	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,264.95	03/2023 -	03/2023
45	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	.71	03/2023 -	03/2023
46	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	28.62	03/2020 -	03/2020
47	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
48	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
49	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	228.99	03/2025 -	03/2025
50	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	71.98	03/2021 -	03/2021
51	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	175.42	03/2020 -	03/2020
52	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	.13	03/2021 -	03/2021
53	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.13	03/2023 -	03/2023
54	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	29.01	03/2022 -	03/2022
55	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023
	Total		73,476.47 -	73,307.72	14,400.89		
	<u>DEFENCE PRODUCTION</u>						
56	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	21.52	05/2018 -	05/2018
57	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	29.85	08/2020 -	08/2020
	Total		453.64 -	469.04	51.37		
	<u>FERTILISERS</u>						
58	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	82.72	11/2016 04/2019	04/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	383.90	12/2017 -	12/2017
	Total		680.64 -	703.44	466.62		
	<u>HEALTH AND FAMILY WELFARE</u>						
60	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	202.00	03/2018 -	03/2018
61	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	-	05/2018 08/2019	08/2019
62	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	103.00	08/2018 -	08/2018
63	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	66.00	09/2018 -	09/2018
	Total		1,426.56 -	1,426.56	371.00		
	<u>MINES</u>						
64	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	.31	04/2021 -	04/2021
65	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	157.34	01/2020 -	01/2020
	Total		6,074.00 -	6,074.00	157.65		
	<u>PETROLEUM</u>						
66	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	1,984.66	03/2013 09/2018	09/2018
67	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	571.47	535.39	09/2011 06/2019	06/2019
68	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
69	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI- BONGAIGAON SECTOR PHASE II [N16000259]	9/2016	571.66 -	571.66	-	12/2019 -	12/2019
70	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	.50	10/2020 -	10/2020
71	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	43.02	12/2019 -	12/2019
72	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	57.41	03/2019 -	03/2019
73	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	33.54	04/2019 -	04/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
74	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	1.35	06/2020 -	06/2020
75	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	22.20	12/2018 -	12/2018
76	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	6.09	12/2020 -	12/2020
77	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	28.42	09/2019 -	09/2019
78	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.87	12/2019 -	12/2019
79	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	20.22	02/2020 -	02/2020
80	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	170.15	03/2020 -	03/2020
81	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 -	09/2018
82	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	159.74	03/2026 -	03/2026
83	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 -	05/2020
84	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	23.07	01/2019 -	01/2019
85	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	.05	01/2021 -	01/2021
86	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,828.00 -	1,828.00	.10	12/2020 -	12/2020
87	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,212.00 -	3,212.00	.10	12/2020 -	12/2020
88	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,250.00 -	2,250.00	1.93	12/2019 -	12/2019
89	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	2,253.00 -	2,253.00	5.71	12/2019 -	12/2019
90	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	4.85	12/2019 -	12/2019
91	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
92	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
93	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	.05	01/2021 -	01/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
94	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	.05	01/2021 -	01/2021
95	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	12.27	08/2018 -	08/2018
96	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	59.40	02/2020 -	02/2020
97	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	7.03	01/2019 -	01/2019
98	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	95.55	12/2019 -	12/2019
99	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	21.03	02/2020 -	02/2020
100	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	8.38	08/2021 -	08/2021
101	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	216.42	11/2018 -	11/2018
102	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	252.02	06/2020 -	06/2020
103	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]	5/2016	215.38 -	215.38	141.75	06/2017 10/2017	10/2017
104	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	191.47	11/2019 -	11/2019
105	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	11.01	02/2019 -	02/2019
106	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	-	03/2023 03/2022	03/2022
107	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	148.67	06/2020 -	06/2020
108	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	25.71	09/2019 -	09/2019
109	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	79.24	08/2019 -	08/2019
110	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
111	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	327.78	13.62	04/2018 -	04/2018
112	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	119.90	03/2018 -	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
113	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	365.49	12/2018 -	12/2018
114	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	4,588.29	840.60	08/2018 05/2019	05/2019
115	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	76.29	12/2017 -	12/2017
116	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	192.61	04/2018 -	04/2018
117	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	155.60	10/2018 -	10/2018
118	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	173.28	126.24	01/2017 03/2018	03/2018
119	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	580.31	04/2018 04/2018	04/2018
120	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	3,961.54	3,216.59	12/2017 03/2019	03/2019
121	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	135.88	09/2018 09/2018	09/2018
122	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	468.00	02/2020 -	02/2020
123	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018
124	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	567.22	347.69	11/2019 12/2018	12/2018
125	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	167.48	03/2017 10/2017	10/2017
126	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,479.75	2,033.62	05/2019 10/2019	10/2019
127	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	3,995.37	04/2019 03/2019	03/2019
128	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	122.14	07/2018 06/2020	06/2020
129	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	154.97	10/2019 -	10/2019
130	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	15.07	12/2020 -	12/2020
131	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	5,554.21	05/2017 05/2018	05/2018
132	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018
133	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	372.36	10/2014 03/2018	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
134	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	923.87	06/2018 -	06/2018
135	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	576.09	12/2014 03/2018	03/2018
136	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	1,992.86	05/2014 05/2018	05/2018
137	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,625.39	03/2015 03/2018	03/2018
138	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	1,158.78	05/2013 12/2017	12/2017
139	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	2.11	01/2014 11/2019	11/2019
140	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	180.36	03/2019 05/2020	05/2020
141	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	1,288.55	09/2017 12/2018	12/2018
142	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	4,190.00	1,918.07	09/2017 06/2018	06/2018
143	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	5,637.00	3,701.21	04/2016 12/2017	12/2017
144	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	105.43	07/2016 06/2018	06/2018
	Total		1,67,387.02 -	1,68,146.41	38,478.64		
	<u>POWER</u>						
145	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	645.85	09/2010 12/2017	12/2017
146	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	8,019.00	09/2017 03/2018	03/2018
147	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,547.20	08/2013 12/2017	12/2017
148	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	408.10	08/2016 10/2017	10/2017
149	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	703.10	561.70	06/2015 12/2017	12/2017
150	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	591.47	07/2018 -	07/2018
151	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	674.66	04/2017 03/2018	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	1,980.02	04/2018 -	04/2018
153	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	8.20	10/2018 -	10/2018
154	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	14.85	05/2017 06/2019	06/2019
155	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	42.41	03/2018 -	03/2018
156	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	7/2010	1,272.80 -	1,731.10	1,407.97	11/2012 12/2017	12/2017
157	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	1/2015	268.80 -	340.88	154.86	03/2018 -	03/2018
158	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	3,330.00	04/2018 -	04/2018
159	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	287.00	09/2019 -	09/2019
160	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	6,184.00	08/2018 -	08/2018
161	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	3,043.00	03/2019 -	03/2019
162	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	1,407.32	03/2018 -	03/2018
163	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,278.00	03/2013 06/2019	06/2019
164	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]	4/2015	2,525.00 -	2,525.00	1,215.00	11/2017 -	11/2017
165	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	41.04	09/2020 -	09/2020
166	50 MW SOLAR POWER PROJECT - [N18000251]	9/2017	287.48 -	287.48	.51	03/2018 -	03/2018
167	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	-	06/2019 -	06/2019
168	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	211.58	04/2020 -	04/2020
169	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	7.45	09/2019 -	09/2019
170	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII [N18000245]	3/2017	379.95 -	379.95	19.61	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
171	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	5.36	06/2019 -	06/2019
172	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	.51	03/2019 -	03/2019
173	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	12.97	02/2019 -	02/2019
174	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
175	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	5.12	04/2019 -	04/2019
176	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	40.12	01/2019 -	01/2019
177	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.70	11/2019 -	11/2019
178	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	-	04/2019 -	04/2019
179	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
180	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]	11/2016	330.00 -	330.00	135.14	11/2017 -	11/2017
181	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.56	03/2019 -	03/2019
182	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.95	02/2019 -	02/2019
183	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	.40	02/2019 -	02/2019
184	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	87.99	03/2019 -	03/2019
185	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	11.40	07/2018 -	07/2018
186	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	18.66	12/2018 -	12/2018
187	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	95.35	01/2019 -	01/2019
188	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	1,681.43	10/2017 -	10/2017
189	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	30.90	11/2018 -	11/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
190	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	98.85	04/2019 -	04/2019
191	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	242.89	06/2019 -	06/2019
192	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	58.44	06/2018 -	06/2018
193	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	284.67	12/2018 -	12/2018
194	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	657.13	11/2019 -	11/2019
195	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	345.26	05/2019 -	05/2019
196	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	12.93	11/2018 -	11/2018
197	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	37.13	05/2018 -	05/2018
198	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	47.99	04/2018 -	04/2018
199	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	982.00	07/2020 -	07/2020
200	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	74.23	07/2018 -	07/2018
201	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	439.84	07/2018 -	07/2018
202	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	148.64	03/2017 10/2017	10/2017
203	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	3,245.00	09/2019 -	09/2019
204	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	147.00	08/2017 -	08/2017
205	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	135.16	09/2014 09/2017	09/2017
206	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,329.43	1,259.14	07/2006 11/2017	11/2017
207	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 -	2,187.32	1,955.46	11/2008 09/2018	09/2018
208	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	1,929.61	08/2014 12/2017	12/2017

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
209	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	355.29	08/2014 12/2017	12/2017
210	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,478.76	08/2013 03/2018	03/2018
211	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	2,581.34	07/2014 09/2017	09/2017
212	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	5,808.04	12/2009 03/2018	03/2018
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX [N18000158]	2/2014	539.82 -	539.82	384.32	06/2016 02/2018	02/2018
214	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	97.92	04/2016 12/2017	12/2017
215	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. [N18000080]	2/2010	2,144.00 -	2,932.88	2,552.51	12/2012 02/2018	02/2018
216	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	4/2010	4,404.57 -	5,135.01	3,404.34	01/2015 03/2018	03/2018
217	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	4,473.47	10/2012 02/2018	02/2018
	Total		1,63,808.67 -	1,77,289.16	81,480.72		
	<u>RAILWAYS</u>						
218	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	17.78	03/2022 -	03/2022
219	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	28.94	03/2021 -	03/2021
220	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	15.51	03/2021 -	03/2021
221	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	235.03	03/2019 -	03/2019
222	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	90.63	03/2019 -	03/2019
223	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	201.87	03/2019 -	03/2019
224	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	139.85	03/2018 -	03/2018
225	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	342.92	03/2018 -	03/2018
226	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	19.91	03/2019 -	03/2019
227	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	218.41	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
228	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	383.12	03/2018 -	03/2018
229	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
230	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	-	12/2024 -	12/2024
231	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
232	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	-	12/2021 -	12/2021
233	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	-	12/2021 -	12/2021
234	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	-	03/2021 -	03/2021
235	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
236	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
237	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	67.81	03/2021 -	03/2021
238	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	34.88	03/2021 -	03/2021
239	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	.14	03/2019 -	03/2019
240	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.25	-	12/2020 -	12/2020
241	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	-	03/2019 -	03/2019
242	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	-	03/2020 -	03/2020
243	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	-	03/2020 -	03/2020
244	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020
245	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	-	12/2025 -	12/2025
246	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	4,295.30	-	12/2026 -	12/2026
247	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
248	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	927.01	-	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
249	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
250	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	33.76	03/2020 -	03/2020
251	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
252	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
253	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.65	-	12/2020 -	12/2020
254	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	23.82	03/2021 -	03/2021
255	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
256	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
257	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
258	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
	Total		50,597.28 -	52,147.82	2,105.54		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
259	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
260	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
261	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
262	RHENOK-RORAHTHANG-PAKYONG ON NH 717A - [N24000695]	4/2017	388.00 -	447.37	-	10/2017 -	10/2017
263	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
264	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
265	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
266	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
267	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
268	SIX LANNING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
269	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
270	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
271	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
272	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
273	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
274	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO API/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
275	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
276	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
277	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
278	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
279	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
280	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
281	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
282	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
283	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
284	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
285	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
286	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
287	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
288	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
289	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]	3/2015	226.31 226.00	226.00	-	10/2017 -	10/2017
290	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	2/2015	239.91 240.00	240.00	-	10/2017 -	10/2017
291	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
292	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
293	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	275.35	04/2018 -	04/2018
294	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
295	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	617.98	11/2017 -	11/2017
296	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	558.12	02/2018 -	02/2018
297	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	308.23	09/2017 -	09/2017
298	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00 -	709.00	203.50	09/2017 -	09/2017
299	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
300	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
301	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
302	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
303	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
304	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
305	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
306	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
307	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
308	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	29.27	10/2017 -	10/2017
309	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
310	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	27.62	12/2018 -	12/2018
311	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23 -	239.23	154.94	12/2017 -	12/2017
312	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	161.96	03/2018 -	03/2018
313	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
314	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
315	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
316	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
317	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	531.15	03/2018 -	03/2018
318	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	168.65	07/2018 -	07/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
319	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
320	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
321	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
322	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
323	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
324	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	2,595.24	01/2018 -	01/2018
325	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
326	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	147.98	06/2018 -	06/2018
327	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	142.48	06/2018 -	06/2018
328	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	84.46	06/2018 -	06/2018
329	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	301.95	03/2018 -	03/2018
330	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
331	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
332	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
333	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	31.87	03/2018 -	03/2018
334	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
335	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
336	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
337	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
338	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
339	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
340	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
341	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
342	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
343	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
344	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
345	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017
346	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
	Total		63,238.06 -	65,323.22	6,957.80		
	<u>SHIPPING AND PORTS</u>						
347	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017
348	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
	Total		454.50 -	468.33	.14		
	<u>STEEL</u>						
349	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
350	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	41.97	09/2018 -	09/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
351	CENTRAL DISPATCH YARD - [N12000119]	8/2015	320.66 -	320.66	11.17	08/2018 -	08/2018
352	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]	7/2015	465.85 -	465.85	20.85	07/2018 -	07/2018
353	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	35.71	06/2019 -	06/2019
354	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	25.74	06/2020 -	06/2020
355	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
356	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	156.39	03/2018 -	03/2018
357	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	64.65	09/2017 -	09/2017
358	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	12,559.30	05/2015 12/2017	12/2017
	Total		24,449.42 -	24,449.42	13,135.84		
	<u>URBAN DEVELOPMENT</u>						
359	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	388.00	251.69	05/2017 08/2017	08/2017
360	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	-	02/2020 -	02/2020
361	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB [N28000102]	8/2016	294.00 -	294.00	11.87	04/2019 -	04/2019
362	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	.26	03/2020 -	03/2020
363	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
364	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	12/2016	164.00 -	164.00	55.98	01/2018 03/2018	03/2018
365	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
366	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]	8/2014	350.02 -	350.02	347.68	03/2015 12/2017	12/2017
367	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,661.40	11/2019 -	11/2019
368	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]	6/2010	205.00 -	170.62	128.00	03/2012 03/2018	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
369	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA [N28000068]	2/2011	241.33 -	349.33	218.90	03/2016 12/2017	12/2017
370	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL [N28000059]	12/2012	188.87 -	188.87	168.97	12/2015 12/2017	12/2017
	Total		17,249.37 -	17,176.99	6,381.52		
	Grand Total		5,69,605.09	5,87,535.64	1,64,472.49		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	03/2017	70.54
	Total		16,663.00 -	28,462.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2017	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		17,655.97 -	17,727.42			
	<u>DEFENCE PRODUCTION</u>						
7	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	2.97
8	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.51
	Total		453.64 -	469.04			
	<u>FERTILISERS</u>						
9	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. [N08000010]	02/2016	482.85 -	494.00	12/2017 -	12/2017	2.31
	Total		482.85 -	494.00			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
10	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70 -	209.00	01/2016 -	-	6.25
	Total		196.70 -	209.00			
	<u>HEAVY INDUSTRY</u>						
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
14	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,637.00	04/2016 -	12/2017	36.68
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
17	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
18	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
19	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]	06/2012	150.00 -	259.93	07/2014 -	09/2017	73.29
20	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	Total		12,275.58 -	15,719.05			
	<u>POWER</u>						
21	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
22	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
23	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49	02/2016 -	-	.16
24	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14
25	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37
26	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	245.00	06/2012 -	12/2017	5.45
27	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96
28	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	5.50
29	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	4.12
30	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37
32	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50
33	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,352.57	09/2017 -	09/2018	31.55
34	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
35	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	Total		30,008.31 -	59,469.72			
	<u>RAILWAYS</u>						
36	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
37	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	-	123.75
38	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
39	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	870.00	- -	-	459.31
40	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
41	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	317.21

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
42	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
43	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
44	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
45	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00	02/2011 -	-	277.85
46	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
47	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
48	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
49	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	03/2019	293.06
50	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	- -	03/2021	273.12
51	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	- -	03/2018	88.85
52	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
53	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
54	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	- -	05/2019	212.37
55	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
56	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	12/2017	64.25
58	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	- -	06/2022	137.80
59	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
60	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51
61	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	03/2018	38.24
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50	- -	-	412.75
63	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
64	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
65	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
66	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
67	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
68	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
69	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	941.04	03/2014 -	03/2019	44.07
70	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
71	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
72	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	05/2016	123.34
73	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	-	534.55
74	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	-	185.52
75	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
76	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
77	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
78	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
79	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	-	8.18
80	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	-	81.31
81	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	381.39	- -	-	286.26
82	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
83	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
84	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
85	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
86	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
87	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
88	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
89	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
90	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
91	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
92	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
93	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
94	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
95	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
96	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
97	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
98	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
99	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
100	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	-	77.08
101	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
102	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
103	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	-	341.34
104	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
105	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
106	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33
107	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
108	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
109	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
110	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
111	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64
112	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
113	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
114	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
115	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47
116	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2019	290.00
117	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,145.00	- -	03/2020	615.00
118	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
119	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
120	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
121	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2018	317.58
122	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
123	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	-	27.24
124	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
125	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,679.13	- -	-	58.06
126	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
127	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	780.98	- -	-	90.45
128	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114]	04/2008	516.23 -	735.00	03/2014 -	-	42.38

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
129	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
130	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
131	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
132	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
133	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
134	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	06/2017	122.68
135	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
136	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	488.33
137	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
138	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
139	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
140	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
141	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
142	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	491.33	06/2004 -	-	153.17
143	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
144	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) [N22000345	04/1997	836.26 -	1,072.52	- -	-	28.25
145	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	-	81.45
146	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
147	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
148	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
149	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
150	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,160.83	- -	03/2020	40.44

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
151	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	-	03/2020	52.77
152	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	-	42.11
153	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
154	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	355.96	- -	03/2019	87.25
155	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
156	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]	04/2010	203.40 -	273.84	- -	-	34.63
157	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	648.00	- -	02/2019	8.00
158	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,161.64	03/2015 -	03/2019	40.00
159	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
160	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.23	06/1999 -	-	389.58
161	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
162	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	- -	-	.33
163	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	- -	08/2017	10.26
164	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	- -	07/2017	142.44
165	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	- -	10/2018	61.80
166	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
167	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	- -	02/2019	41.64
168	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
169	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
170	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
171	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
172	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	-	-	27.06
174	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	-	-	23.02
175	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
176	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	-	-	16.87
177	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	-	05/2018	87.54
178	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	-	-	17.92
179	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]	04/2011	239.73 -	257.78	-	-	7.53
180	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	-	02/2019	27.93
181	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	-	-	27.72
182	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	-	03/2019	21.31
183	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
184	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	-	-	62.32
185	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	-	-	82.25
186	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	-	-	162.39
187	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
188	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41
189	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
190	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	-	12/2017	41.36
191	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	-	-	32.26
192	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	-	-	84.98
193	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	-	-	32.80
194	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	-	-	338.91

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
195	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	-	252.66
196	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	-	-	72.37
197	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	-	-	78.78
198	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	-	-	91.71
199	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	-	03/2018	80.06
200	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	-	-	28.14
201	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	-	-	71.62
202	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007	04/2016	107.49
203	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	-	07/2019	130.16
204	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	445.00	-	03/2018	112.14
205	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	330.00	-	03/2018	16.38
206	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	-	-	109.04
207	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	302.90	-	-	84.23
208	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	-	-	78.83
209	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	-	03/2021	46.95
210	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	-	-	94.45
211	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	-	-	63.25
212	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	-	03/2020	171.38
213	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	-	03/2018	257.63
214	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	508.00	-	03/2019	62.76
215	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	-	03/2019	62.12
216	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016	12/2018	29.06

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
217	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,500.00	-	-	149.41
218	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	-	-	51.49
219	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	-	-	27.07
220	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	-	-	101.93
221	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	-	-	5.33
222	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	4,670.00 3,627.00	3,627.47	-	-	.01
223	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	-	-	10.94
224	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	-	-	21.21
225	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014	-	68.57
226	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	-	08/2015	5.12
227	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	-	-	10.01
228	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021	12/2021	87.11
229	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021	12/2021	79.05
230	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	943.60	12/2024	12/2024	25.72
231	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003	-	130.97
	Total		1,05,032.87 -	2,52,794.64			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
232	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009	12/2017	28.93
233	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009	-	92.75
234	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008	-	80.68
235	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009	-	68.99
236	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011	03/2018	106.50

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
237	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266	01/2014	361.30 -	207.40	07/2014 -	-	-42.60
238	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25
239	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
240	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
241	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
242	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
243	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
244	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	.12
245	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	.01
246	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
247	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
248	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
249	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
250	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
251	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
252	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
253	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
254	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
255	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
256	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
257	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
258	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
259	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
260	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
261	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
262	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54
263	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
264	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	Total		23,165.35 -	29,854.53			
	<u>SHIPPING AND PORTS</u>						
265	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
266	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	-	18.20
267	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	.13
268	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	-	66.82
269	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
270	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(August 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
271	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39
272	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	Total		1,261.61 -	1,777.68			
	<u>URBAN DEVELOPMENT</u>						
273	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]	06/2010	205.00 -	170.62	03/2012 -	03/2018	-16.77
274	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	496.18	06/2017 -	-	.04
	Total		701.18 -	666.80			
	Grand Total		2,11,444.63	4,14,638.81			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs.150 Crore and above

(August 2017)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,000.00	5,459.55	09/2010 09/2016	10/2017	85	13
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	10,443.00	12/2015 11/2016	11/2019	47	36
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,074.00	12/2016 03/2017	12/2020	48	45
	Total		27,271.00 -	29,779.00	23,976.55				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	24.13	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	24.13				
	<u>COAL</u>								
5	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU	05/2016	687.28 -	687.28	681.42	06/2017 -	08/2017	2	-
6	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	151.66	05/2014 -	10/2017	41	-
7	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	144.38	04/2014 -	10/2017	42	-
8	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	125.01	03/2014 -	12/2017	45	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	329.80	03/2010 -	03/2018	96	-
10	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	120.55	03/2015 -	03/2018	36	-
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72	-
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	198.19	03/2014 -	03/2018	48	-
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.38	03/2016 -	03/2018	24	-
14	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	205.72	03/2013 -	03/2018	60	-
15	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	341.10	03/2016 -	03/2018	24	-
16	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	149.93	03/2016 -	03/2018	24	-
17	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	57.64	06/2015 -	03/2018	33	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 415.37	415.37	136.75	03/2016 -	03/2018	24	-
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	272.87	03/2017 -	05/2018	14	-
20	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	298.37	03/2018 -	09/2018	6	-
21	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
22	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	402.43	03/2013 -	11/2018	68	-
23	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 448.86	448.86	157.97	03/2012 -	03/2019	84	-
24	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	190.68	03/2010 -	03/2019	108	-
25	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	215.92	03/2012 -	03/2019	84	-
26	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	218.28	03/2013 -	03/2019	72	-
27	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84	-
28	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	153.14	03/2012 -	03/2019	84	-
29	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	80.62	03/2014 -	03/2019	60	-
30	KOYAGUDEM OPENCASST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
31	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	176.37	04/2015 -	04/2019	48	-
32	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.12	03/2014 -	03/2020	72	-
33	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.27	03/2011 -	03/2020	108	-
34	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 164.04	164.04	.09	03/2015 -	03/2020	60	-
35	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 349.28	349.28	1.31	03/2015 -	03/2020	60	-
36	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 417.33	417.33	43.97	07/2016 -	03/2020	44	-
37	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	116.67	07/2012 03/2017	03/2021	104	48
38	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	259.34	03/2015 -	03/2021	72	-
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	-
	Total		12,841.79 -	13,195.91	6,261.59				
	<u>STEEL</u>								
40	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	745.11	07/2015 -	09/2017	26	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	154.55	09/2016 -	09/2017	12	-
42	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	17,892.75	03/2013 -	10/2017	55	-
43	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	195.64	05/2016 -	10/2017	17	-
44	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	510.53	07/2016 -	10/2017	15	-
45	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	-
46	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	217.87	10/2016 -	03/2018	17	-
47	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	-
48	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	402.94	12/2017 -	05/2018	5	-
49	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	564.35	12/2017 -	06/2018	6	-
50	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	184.28	10/2017 -	07/2018	9	-
51	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	-
52	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
53	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
54	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	996.15	04/2018 -	02/2019	10	-
55	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	Total		30,699.80 -	30,511.59	23,201.75				
	<u>PETROLEUM</u>								
56	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]JOCL,ASSAM	06/2012	150.00 -	259.93	234.99	07/2014 -	09/2017	38	-
57	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	2,765.42	11/2015 -	10/2017	23	-
58	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	367.11	218.14	04/2017 -	11/2017	7	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
59	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	117.68	11/2016 -	02/2018	15	-
60	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]JOCL,GUJARAT	02/2016	931.00 -	931.00	377.28	07/2017 -	02/2018	7	-
61	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	209.19	146.86	12/2016 -	03/2018	15	-
62	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 -	190.45	104.95	09/2017 -	03/2018	6	-
63	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	439.03	126.43	03/2017 -	11/2018	20	-
64	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 -	3,397.00	1,143.75	01/2013 -	12/2018	71	-
65	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	259.80	10/2017 -	03/2019	17	-
66	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU	11/2015	390.52 -	390.52	67.52	03/2019 -	04/2019	1	-
	Total		10,542.57 -	10,266.71	5,562.82				
	<u>POWER</u>								
67	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 9,291.03	9,291.03	7,283.96	06/2015 06/2017	09/2017	27	3
68	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	129.79	03/2016 07/2017	10/2017	19	3
69	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	14,089.00	01/2017 07/2017	11/2017	10	4
70	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	118.67	02/2016 08/2017	11/2017	21	3
71	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,760.00	09/2011 06/2017	12/2017	75	6
72	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	245.00	238.61	06/2012 -	12/2017	66	-
73	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,323.86	09/2014 06/2017	12/2017	39	6
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	715.86	11/2014 06/2017	12/2017	37	6
75	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	159.70	07/2017 -	12/2017	5	-
76	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	470.78	12/2016 -	12/2017	12	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above							(August 2017)		
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
77	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,021.45	01/2016 -	02/2018	25	-
78	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,945.36	12/2015 12/2017	03/2018	27	3
79	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,144.12	04/2016 09/2017	03/2018	23	6
80	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	360.30	11/2016 11/2017	03/2018	16	4
81	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	218.80	02/2017 06/2017	03/2018	13	9
82	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	5,353.00	5,472.83	05/2014 03/2017	03/2018	46	12
83	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	03/2018	15	-
84	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 -	1,364.00	515.00	12/2015 -	03/2018	27	-
85	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	7,988.00	11/2016 12/2017	04/2018	17	4
86	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,528.00	06/2017 12/2017	04/2018	10	4
87	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	452.50	09/2017 -	04/2018	7	-
88	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	485.24	06/2014 03/2018	06/2018	48	3
89	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	134.51	10/2017 10/2017	06/2018	8	8
90	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	151.55	11/2017 -	06/2018	7	-
91	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	9,072.44	01/2018 -	08/2018	7	-
92	TRANMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,352.57	1,118.12	09/2017 -	09/2018	12	-
93	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,480.33	09/2009 -	12/2018	111	-
94	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	121.55	02/2014 02/2018	12/2018	58	10
95	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	13,653.00	01/2011 05/2018	03/2019	98	10
96	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	190.45	01/2018 -	03/2019	14	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	341.63	12/2018 -	12/2019	12	-
98	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	351.70	12/2018 -	12/2019	12	-
99	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,226.25	06/2013 -	11/2020	89	-
100	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	3,939.11	2,307.37	02/2016 09/2019	12/2020	58	15
101	NORTH KARANPURA STPP (3X660 MW) - [N18000177]JNTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	5,214.00	02/2019 02/2020	02/2021	24	12
102	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	868.78	04/2020 -	05/2023	37	-
	Total		1,46,231.98 -	1,66,833.45	1,12,611.42				
	<u>HEAVY INDUSTRY</u>								
103	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	2,289.00				
	<u>HEALTH AND FAMILY WELFARE</u>								
104	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	135.00	05/2017 -	12/2017	7	-
105	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	203.00	05/2017 -	12/2017	7	-
106	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	168.90	101.00	05/2017 -	12/2017	7	-
107	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	32.00	02/2018 -	08/2018	6	-
	Total		819.94 -	819.94	471.00				
	<u>RAILWAYS</u>								
108	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106	-
109	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	12/2017	105	105
110	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	516.40	-	03/2010 -	12/2017	93	-
111	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
112	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	386.03	06/2013 -	03/2018	57	-
113	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	-	03/2010 -	03/2018	96	-
114	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	7,000.00	6,995.27	03/2009 -	03/2018	108	-
115	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,000.00	4,753.99	04/2008 12/2011	06/2018	122	78
116	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
117	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	13,536.97	11/2002 -	12/2018	193	-
118	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.00	-	03/2016 -	12/2018	33	-
119	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	12/2018	33	-
120	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,010.00	2,225.72	12/2008 -	03/2019	123	-
121	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	-	111
122	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	03/2019	-	114
123	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
124	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,161.64	353.32	03/2015 -	03/2019	48	-
125	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	941.04	575.19	03/2014 -	03/2019	60	-
126	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	-
127	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	-
128	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	-
129	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.70	-	02/2015 -	12/2019	58	-
130	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	318.00	-	02/2006 -	12/2019	166	-
131	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 -	1,781.98	514.44	03/2004 -	03/2020	192	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
132	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	111
133	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	9,658.00	4,927.46	03/2011 -	03/2020	108	-
134	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	-	03/2008 06/2008	03/2020	144	141
135	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	2,316.85	03/2014 -	03/2020	72	-
136	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	1,565.18	04/2014 -	03/2020	71	-
137	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
138	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84	-
139	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	357.19	03/2015 -	03/2020	60	-
140	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	291.26	- 11/2015	03/2020	-	52
141	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	-	03/2016 -	12/2020	57	-
142	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
143	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	-
144	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	Total		41,808.70 -	1,09,906.41	49,694.03				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
145	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	480.18	05/2010 -	08/2017	87	-
146	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	08/2017	45	-
147	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	08/2017	48	-
148	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23	-
149	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	08/2017	9	-
150	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	342.00	-	01/2017 -	08/2017	7	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
151	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 -	09/2017	111	-
152	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	-	08/2011 -	09/2017	73	-
153	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	-	04/2013 -	09/2017	53	-
154	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	09/2017	51	-
155	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	-	03/2014 -	09/2017	42	-
156	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	-	09/2016 -	09/2017	12	-
157	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	197.99	09/2016 -	09/2017	12	-
158	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	-	11/2015 -	09/2017	22	-
159	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	51	-
160	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	53	-
161	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	564.90	09/2013 -	10/2017	49	-
162	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25	-
163	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
164	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	11/2017	52	-
165	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,095.01	03/2013 -	11/2017	56	-
166	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	-
167	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	-
168	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	378.36	01/2016 -	11/2017	22	-
169	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	498.08	01/2016 -	11/2017	22	-
170	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	465.52	11/2016 -	11/2017	12	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above							(August 2017)		
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
171	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00 -	-	02/2009 -	12/2017	106	-
172	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00 -	-	04/2008 -	12/2017	116	-
173	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	3,237.87 -	-	09/2012 -	12/2017	63	-
174	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00 -	2,234.53	05/2013 -	12/2017	55	-
175	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76 -	-	08/2014 -	12/2017	40	-
176	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55 -	2,037.05	03/2013 -	12/2017	57	-
177	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00 -	1,329.03	12/2013 -	12/2017	48	-
178	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00 -	237.00	05/2013 -	12/2017	55	-
179	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00 -	406.68	08/2013 -	12/2017	52	-
180	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00 -	622.89	10/2013 -	12/2017	50	-
181	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54 -	-	11/2013 -	12/2017	49	-
182	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70 -	1,340.87	06/2014 -	12/2017	42	-
183	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84 -	2,382.75	08/2013 -	12/2017	52	-
184	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18 -	2,678.94	09/2014 -	12/2017	39	-
185	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36 -	320.46	01/2014 -	12/2017	47	-
186	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00 -	401.67	10/2013 -	12/2017	50	-
187	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	1,479.00 -	828.06	06/2015 -	12/2017	30	-
188	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22 -	2,447.73	04/2015 -	12/2017	32	-
189	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00 -	278.17	02/2015 -	12/2017	34	-
190	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85 -	236.85	01/2016 -	12/2017	23	-
191	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70 -	3,130.07	10/2011 -	12/2017	74	-
192	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00 -	1,090.17	08/2015 -	12/2017	28	-
193	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50 -	1,425.94	07/2017 -	01/2018	6	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
194	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,848.95	11/2016 -	02/2018	15	-
195	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	03/2018	95	-
196	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,882.53	11/2011 -	03/2018	76	-
197	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	672.32	01/2014 -	03/2018	50	-
198	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	-
199	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,927.60	08/2013 -	03/2018	55	-
200	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	483.91	07/2014 -	03/2018	44	-
201	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	363.09	06/2014 -	03/2018	45	-
202	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,785.50	02/2014 -	03/2018	49	-
203	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	1,337.00	09/2016 -	03/2018	18	-
204	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,283.00	08/2016 -	03/2018	19	-
205	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,082.05	06/2012 -	03/2018	69	-
206	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
207	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	-
208	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	-
209	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	-
210	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	87.82	12/2017 -	06/2018	6	-
211	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13	-
212	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	225.80	06/2016 -	06/2018	24	-
213	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	208.32	06/2016 -	06/2018	24	-

[illegible]

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(August 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>URBAN DEVELOPMENT</u>								
225	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	300.77	06/2015 -	09/2017	27	-
226	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	248.10	09/2016 -	11/2017	14	-
227	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24	-
228	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	62.77	11/2015 -	12/2017	25	-
229	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	109.90	08/2016 -	03/2018	19	-
230	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	114.89	11/2014 -	03/2018	40	-
231	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	11
232	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	466.05	12/2015 12/2017	03/2018	27	3
233	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	-
234	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	38.40	03/2016 -	12/2018	33	-
235	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
236	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
237	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21	-
238	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-
239	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 2,230.23	1,219.21	109.75	10/2019 -	03/2020	5	-
	Total		58,867.60 -	63,477.34	20,393.40				
	Grand Total		4,11,485.43	5,13,856.29	2,99,971.46				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2019	11459	47
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492	85

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2018	365.01	33
9	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	60
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
11	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
12	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
13	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	11/2018	457.77	68
14	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
15	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	05/2018	490.1	14
16	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2019	207.28	84
17	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72
18	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2018	209.78	36
19	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
20	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
22	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
23	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
24	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
25	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	84
26	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	12/2017	153.82	45
27	KISTARAM OCP	SCCL	11/2010	03/2015	03/2020	242.29	60
28	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
29	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2018	198.59	24
30	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2018	181.19	72
31	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
32	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.4	72
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
37	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2018	210.98	60
38	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
39	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	09/2018	1055.05	6
40	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2017	289.45	41
41	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	10/2017	269.82	42
42	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2018	302.96	96
43	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2018	510.85	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
45	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
46	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	08/2018	152.95	6
47	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	12/2017	293.65	7
48	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	12/2017	168.9	7
49	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	12/2017	204.44	7

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY	IOCL	02/2016	07/2017	02/2018	931	7
52	NEW 250 TMTPL LPG PLANT AT PANAGARH	HPCL	08/2014	09/2017	03/2018	190.45	6
53	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	41
54	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
55	SIX PIPELINE REPLACEMENT PROJECT	ONGC	03/2009	01/2017	03/2018	181.02	14
56	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY	CPCL	02/2016	04/2017	11/2017	367.11	7
57	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	09/2018	2465.15	66
58	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	10/2017	3110.36	23
59	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	03/2018	228.64	15
61	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	06/2020	690	23
62	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	02/2018	257.87	15
63	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY	IOCL	03/2014	03/2017	10/2017	238.5	7
64	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	05/2018	2899.93	12
65	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
66	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
67	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2017	861.79	55
69	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
70	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	23
71	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2019	736.65	93
72	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	11/2018	352.56	20
73	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
74	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
75	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076	9
76	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
77	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2018	2592.17	48
78	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	03/2018	600.17	39
79	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9
80	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	09/2017	150	38

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
81	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
82	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
83	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2017	514.2	30
84	SOLAPUR STPP	NTPC	03/2012	11/2016	04/2018	9395.18	17
85	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.9	99
86	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	12/2017	1940.13	39
87	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657	58
88	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	06/2018	487.49	48
89	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	09/2017	2127.51	38
90	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	55
91	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2017	297.33	40
92	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	40
93	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	02/2018	3642.04	25
94	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	118
95	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2019	8692.97	98
96	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	11/2017	368.72	136
97	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	09/2017	198.63	36
98	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	09/2017	9569.76	27
99	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	10/2017	155.57	19
100	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	75
101	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	12/2017	4375.35	75
102	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	03/2018	288.49	13
103	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	11/2017	196.58	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	05/2023	8112.12	37
105	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	02/2021	14366.58	24
106	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	06/2018	871.62	8
107	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	04/2018	1071.24	7
108	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2018	522.29	16
109	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	12/2017	232.34	66
110	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
111	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	12/2018	195.42	58
112	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	03/2018	5353	46
113	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2017	436.68	12
114	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	03/2018	1479.3	11
115	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	06/2018	307.18	7
116	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	89
117	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955	27
118	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	08/2018	12964.6	7
119	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	03/2018	9750.89	15
120	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
121	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2017	477.69	87
122	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	64
123	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	38
124	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	03/2018	11638.55	6
125	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
126	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144	62

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
127	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	03/2018	1364.52	23
128	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2017	374.63	20
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	02/2018	539.82	20
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	09/2017	908.08	15
131	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION	PGCIL	05/2014	08/2016	10/2017	829.98	14
132	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2017	1272.8	61
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2017	723.63	37
134	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	11/2017	15166.19	10
135	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	04/2018	11846	10
136	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	03/2018	2514.88	27
137	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
138	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	10/2017	305.04	7
139	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
140	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
141	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
142	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	12/2017	1389.62	45
143	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
144	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
145	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2019	829.74	48
146	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
147	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
148	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
149	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2018	632.68	33
150	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
151	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
152	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	99
153	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500	122
154	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
155	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733	123
156	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
157	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2018	495.74	57
158	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
159	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
160	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2018	1676.31	108
161	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
162	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
163	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
164	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
166	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	106
167	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	58
168	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2017	133.41	105
169	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.7	166
170	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.2	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
171	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
172	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144
173	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
174	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
175	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
176	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	MORTH	07/2014	01/2017	08/2017	342.05	7
177	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
178	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
179	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	12/2017	1232	28
180	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
181	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	08/2017	563.92	9
182	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	09/2017	1175	53
183	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	09/2017	1693.75	73
184	ROHTAK-BAWAL	NHAI	05/2011	11/2013	08/2017	650	45
185	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	08/2017	1141	48
186	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2017	1250	48
187	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50
188	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2018	2848	49
189	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	09/2017	574	42
190	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	10/2017	1046	49
191	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2017	485	52

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
192	JORBAT - BARAPANI	NHAI	01/2011	01/2014	03/2018	536	50
193	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2018	575	56
194	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2017	511.54	49
195	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2017	1100.7	42
196	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	03/2018	702.16	44
197	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2017	1479	30
198	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	08/2017	486	87
199	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108	76
200	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU	PWD	03/2015	09/2015	08/2017	309.01	23
201	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
202	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
203	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
204	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
205	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
206	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	12/2017	2498.76	40
207	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
208	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	11/2017	1813.76	52
209	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2018	671.3	64
210	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	10/2017	351.54	53
211	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
212	DEOLI KOTA	NHAI	01/2011	07/2013	10/2017	593	51
213	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	03/2018	1348.2	49
214	MURADABAD-BAREILY	NHAI	04/2010	06/2013	09/2017	1267	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
215	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2017	1724.55	57
216	CUDDAPAH-MYDUKUR-KURN00L KM-167.750-356.502 KM	NHAI	11/2010	05/2013	12/2017	1585	55
217	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	02/2018	1916.79	15
218	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	03/2018	1266.6	18
219	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.1	63
220	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	11/2017	754	56
221	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2017	1078.84	52
222	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	55
223	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2017	1396.18	39
224	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	03/2018	217.61	95
225	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2017	208	116
226	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	09/2017	225	111
227	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2017	478.51	50
228	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2018	942.69	45
229	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	09/2017	425.19	12
230	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	12/2017	523.85	23
231	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2018	563.92	6
232	FOUR LANING OF VARANASI BYPASS	NHAI	05/2015	05/2017	06/2018	261.09	13
233	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	11/2017	351.34	22
234	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	NHAI	09/2015	09/2016	09/2017	368.73	12
235	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	11/2017	495.78	22
236	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2017	291.36	47
237	ETAWAH CHAKERI	NHAI	03/2013	09/2015	10/2017	1573	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
238	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2017	1928.22	32
239	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	01/2018	972.5	6
240	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	11/2017	923.04	12
241	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	03/2018	1655.01	19
242	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	12/2017	1673.7	74
243	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	09/2017	1055	22
244	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	12/2017	280	106
245	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2018	597	6
246	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
247	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
248	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
249	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
250	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96
251	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150	141

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
252	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	06/2018	2858	6
253	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	09/2017	877.73	26
254	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2017	15525	31
255	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	10/2017	245.67	17
256	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSCL	12/2007	12/2016	12/2017	202.61	12
257	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND	HSCL	04/2014	09/2017	12/2018	151.33	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	CULTURE, SHILONG IN MEGALAYA UNDER NLCPR						
258	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HACL	05/2015	03/2017	08/2018	189	17
259	IRRIGATION WORK OF BAGMATI	HACL	10/2005	03/2015	03/2021	956	72
260	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	HACL	12/2007	06/2016	03/2018	253.92	21
261	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HACL	02/2014	12/2016	12/2018	787.29	24
262	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	10/2017	17265	55
263	3RD CONVERTER AND 4TH CASTER	RINL	07/2011	07/2016	10/2017	974.76	15
264	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2018	343	17
265	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	07/2018	1034.01	9
266	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.3	10
267	TURBO BLOWER - 5	RINL	12/2009	09/2016	09/2017	280	12

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
268	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	09/2017	13334	26

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
269	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
270	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AT IISER	CPWD	07/2015	11/2015	12/2017	154	25
271	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	12/2017	350.02	33
272	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2018	216.69	44
273	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
274	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2015	12/2017	188.87	24
275	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	11/2017	332.72	14
276	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI	CPWD	02/2014	08/2016	03/2018	156.57	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NADIA						
277	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	03/2018	270.83	40
278	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2018	171.86	33
279	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	12/2017	241.33	21
280	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	03/2018	205	72
281	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	CPWD	12/2012	06/2015	09/2017	315	27
282	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2018	165.23	65
283	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	03/2018	884.3	27
284	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
285	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
286	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	14600	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

ATOMIC ENERGY

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6000	2508
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291

CIVIL AVIATION

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
8	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
13	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	150	259.93	109.93
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	768.25	102.25

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
20	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
21	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
22	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
23	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	5637	1512.65
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
24	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
25	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	17435.15	11149.82
27	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
28	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
29	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5882.01	2239.97
30	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	426.29	128.96
32	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1337.76	763.77
33	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	2127.51	2619.56	492.05
34	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
35	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	3939.11	2282.11
36	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
37	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
38	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2352.57	564.16
40	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	514.2	703.1	188.9
41	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	723.63	882.13	158.5
42	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
43	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1329.43	960.71
44	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
45	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
46	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9142.58	5020.58
47	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4366.64	2053.64
48	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
49	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
50	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
51	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
52	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
53	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
54	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
55	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	4404.57	5135.01	730.44
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
56	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
57	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	N.A.	36.8	614	577.2
58	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
59	KARUR-SALEM(NL), SR	SR	02/1997	N.A.	155.55	870	714.45
60	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	1542.41	1299.99
62	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
63	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	12/2007	136.62	376	239.38
64	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	810.78	1928.07	1117.29
65	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	340	206.59
66	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
67	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
68	HATHUA-BHATNI (N L) (NER)	NER	04/2005	N.A.	230.03	718.54	488.51
69	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
70	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	412.05	193.86
71	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	470.92	2713.09	2242.17
72	GUDUR-DURGARAJAPATNAM	SCR	04/2011	N.A.	283.54	759.41	475.87
73	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
74	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
75	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
76	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
77	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	280	183.84
78	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	381.39	282.65
79	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
80	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	941.04	287.85
81	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5000	3500
82	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	900.05	1125.89	225.84

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
84	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
85	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
86	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	750	283.52
87	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	554.7	241.46
88	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
89	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
90	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	N.A.	677.97	1679.13	1001.16
91	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
92	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
93	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	7000	5323.69
94	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
95	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
96	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
97	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	2145	1845
98	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	780	580
99	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
100	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
101	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	12/2024	750.55	943.6	193.05
102	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
103	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
104	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	N.A.	4300	4520	220
105	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
107	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	854	1035.16	181.16
108	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	1876	2081.27	205.27
109	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	2326	2449.91	123.91
110	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
111	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
112	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	1500	898.57
113	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
114	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	398.93	152.86
115	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	508	195.88
116	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	523.17	1871	1347.83
117	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
118	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
119	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
120	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
121	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
122	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	302.9	138.49
123	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
124	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	445	235.23
125	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	580	328
126	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1857	962
127	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
128	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1480.83	658.44

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
130	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
131	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
132	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
133	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
134	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
135	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
136	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
137	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
138	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
139	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
140	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
141	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
142	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
143	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
144	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
145	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2562.27	479.52
146	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	1037.15	591.15
147	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	845.68	405.8
148	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79
149	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
150	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	246.08	348.55	102.47
151	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	477.31	182.31

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	474.3	278.66
153	RANCHI-LOHARDAGA(GC), SER	SER	04/1997	06/2004	194.07	491.33	297.26
154	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
155	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
156	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
157	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
158	MUNEERABAD-MAHABOONAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	525	306.76
159	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	155.74	966.98	811.24
160	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	516.4	191.5
161	RAJATGARH-BARANG(LD), ECOR	RVNL	04/1999	02/2009	166.16	370	203.84
162	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	1566	1016
163	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.23	195.22
164	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
165	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1161.64	331.9
166	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	355.96	165.86
167	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
168	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1579.27	900
169	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	N.A.	100	980	880
170	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
171	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
172	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
173	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	N.A.	836.26	1072.52	236.26
174	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	227	2135	1908

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
176	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
177	JALANDHAR-PATHANKOT- JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	19565	17065
179	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650
180	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	516.23	735	218.77
181	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	N.A.	410.08	780.98	370.9
182	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
183	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	436	266
184	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44
185	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
186	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	3010	2277
187	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
188	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
189	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
190	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
191	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
192	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52
193	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
194	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
195	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
196	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
197	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	2966.99	1920.11

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
199	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1825	1082
200	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
201	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
202	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
203	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
204	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
205	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
206	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
207	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
208	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
209	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
210	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	3168.29	2668.99
211	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	509	281.1
212	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
213	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18
214	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
215	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	350	257.37
216	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42
217	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24
218	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
219	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.64	884

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
220	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
221	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
222	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
223	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4)	NHAI	03/2017	03/2020	985.41	1200	214.59
224	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
225	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
226	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
227	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
228	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
229	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
230	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
231	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
232	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
233	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
234	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
235	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
236	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
237	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
238	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
241	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	13845.01	7450.01
242	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108
243	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
244	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492.00	6000.00	2508	85

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	553.53	244.07	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	349.28	186.52	60
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.40	486.57	227.17	72
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	448.86	199.83	84
7	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	09/2017	150.00	259.93	109.93	38
10	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	723.40	413.59	41
11	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2017	861.79	1256.72	394.93	55
12	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	106.78	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	5637.00	1512.65	20
14	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
15	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076.00	4190.00	1114	9
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36
17	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
18	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR) - DRASS- KARGIL-KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2352.57	564.16	12
19	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2017	723.63	882.13	158.5	37
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	11/2017	368.72	1329.43	960.71	136
21	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	408.03	118
22	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	2228.71	482.06	40
23	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955.00	1364.00	409	27
24	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2017	436.68	602.44	165.76	12
25	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.90	6179.96	3683.06	99
26	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	12/2017	1940.13	2702.65	762.52	39
27	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657.00	3939.11	2282.11	58
28	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	06/2018	487.49	639.46	151.97	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	09/2017	2127.51	2619.56	492.05	38
30	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	1337.76	763.77	55
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2017	297.33	426.29	128.96	40
32	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	02/2018	3642.04	5882.01	2239.97	25
33	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	4479.16	111
34	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2017	477.69	738.48	260.79	87
35	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	5071.94	247.82	64
36	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	5135.01	730.44	38
37	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
38	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144.00	2932.88	788.88	62
39	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	03/2018	1364.52	1891.41	526.89	23
40	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	3846.30	867.82	75
41	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	12/2017	4375.35	6749.18	2373.83	75
42	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2017	1272.80	1731.10	458.3	61
43	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2019	8692.97	1,5095.67	6402.7	98
44	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2017	514.20	703.10	188.9	30

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2017)

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2018	632.68	816.55	183.87	33
46	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2019	829.74	1161.64	331.9	48
47	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	811.24	106
48	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
49	MANDARHILL -DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
50	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5000.00	3500	122
51	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
52	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733.00	3010.00	2277	123
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	8930.44	108
54	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	2150	60
55	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
56	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2018	1676.31	7000.00	5323.69	108
57	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
58	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
59	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
60	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.90	516.40	191.5	93
61	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	1202.70	1019.47	58
62	KHURDA ROAD - BARANG 3RD LINE	RVNL	04/2000	03/2009	12/2017	133.41	340.00	206.59	105

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	(DL) (ECOR)								
63	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.20	950.00	262.8	96
64	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
65	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1082	144
66	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	941.04	287.85	60
67	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
68	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34
69	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
70	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	09/2017	1055.00	1601.77	546.77	22
71	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108.00	2288.00	1180	76
72	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.10	3237.87	1728.77	63

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
73	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96
74	ENORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150.00	600.00	450	141

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
75	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2018	343.00	488.40	145.4	17

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
76	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
77	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	1,4600.00	1,9058.00	4458	24
78	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	12/2017	241.33	349.33	108	21

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs.150 Crore and above					(August 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
1	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - PPP (ANNUITY) - [N10000009]	12/2015	344.50 -	344.50	11/2016 -	-	.00	0
	Total		344.50 -	344.50				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
2	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	12/2017	.00	47
3	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	07/2017	.00	50
4	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	10/2017	.00	53
5	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2017	.00	55
6	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2017	.00	52
7	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	08/2017	.00	87
8	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2017	.00	49
9	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
10	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	-	.00	0
11	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	03/2018	.00	50
12	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00 -	567.00	11/2013 -	-	.00	0
13	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2017	.00	50
14	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2017	.00	42
15	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	03/2018	.00	56
16	DEOLI KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	10/2017	.00	51

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above (August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
18	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	-	.00	0
19	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
20	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGOUR PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	06/2019	.00	0
21	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	08/2017	.00	45
22	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00 -	664.00	02/2014 -	-	.00	0
23	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	06/2018	.00	64
24	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	03/2018	.00	44
25	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	11/2017	.00	56
26	FOUR LANING OF MAHUA TO KAGAVADAR OF NH- 8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	06/2019	.00	0
27	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	04/2018	.00	0
28	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36 -	830.36	07/2018 -	07/2018	.00	0
29	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM - PPP (BOT) - [N24000144]	09/2010	852.00 -	852.00	03/2013 -	06/2017	.00	51
30	BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229]	08/2012	867.00 -	867.00	02/2015 -	12/2017	.00	34
31	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	11/2017	.00	12
32	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	0
33	4 LANING OF SOLAPUR YEDISHI SECTION OF NH- 211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	01/2018	.00	6
34	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2018	.00	55
35	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	10/2017	.00	49

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above (August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
36	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	06/2017	.00	36
37	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	09/2017	51.83	22
38	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	12/2017	.00	52
39	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	12/2017	.00	42
40	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	03/2018	106.50	76
41	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	08/2017	.00	48
42	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,206.10	04/2013	09/2017	2.65	53
43	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	12/2017	.00	48
44	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,266.60	09/2016	03/2018	.00	18
45	MURADABAD-BAREILLY - PPP (BOT) - [N24000154]	04/2010	1,267.00	1,267.00	06/2013	09/2017	.00	51
46	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	03/2018	.00	49
47	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	-	08/2018	.00	0
48	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00	1,393.00	-	01/2018	.00	0
49	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	12/2017	.00	39
50	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0
51	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	12/2017	.00	30
52	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	3,237.87	09/2012	12/2017	114.56	63
53	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	06/2017	.00	37
54	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	10/2017	.00	25
55	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	-	01/2019	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above (August 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
56	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00 -	1,585.00	05/2013 -	12/2017	.00	55
57	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	03/2018	.00	19
58	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	- -	01/2019	.00	0
59	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	- -	12/2017	.00	0
60	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	12/2017	.00	74
61	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	09/2017	.00	73
62	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	12/2017	.00	57
63	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	11/2017	.00	52
64	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	01/2018	.00	0
65	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	02/2018	.00	15
66	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	1,928.22	04/2015 -	12/2017	.00	32
67	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	03/2019	.00	44
68	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	07/2017	.00	19
69	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	- -	04/2019	.00	0
70	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	-	.00	0
71	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	- -	05/2019	.00	0
72	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	12/2017	.00	40
73	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	04/2018	.00	49
	Total		83,563.48 -	87,050.12				
	<u>SHIPPING AND PORTS</u>							
74	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	-	18.20	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above					(August 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
75	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66	0
76	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		809.83 -	1,162.94				
	Grand Total		84,717.81	88,557.56				
