

**442th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
August, 2022**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division**

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for August 2022 contains information on the status of the 1526 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, out of 1526 projects, 21 projects are added and 12 projects (6 projects of Road, 5 projects of Petroleum and 1 project of Heavy Industry) are completed. 647 projects are delayed with respect to their original schedules and 71 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 71 projects, 31 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

Sl.No.	Sector	Projects on Monitor	Delayed Projects w.r.t original schedule	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	831	248	23
2	RAILWAYS	173	116	9
3	PETROLEUM	139	88	9
4	COAL	122	37	1
5	POWER	78	53	18
6	WATER RESOURCES	41	30	2
7	HEALTH AND FAMILY WELFARE	28	1	1
8	URBAN DEVELOPMENT	28	13	1
9	CIVIL AVIATION	25	22	1
10	DEPARTMENT OF HIGHER EDUCATION	20	15	1
11	STEEL	9	4	2
12	MINES	7	6	0
13	ATOMIC ENERGY	5	4	0
14	HOME AFFAIRS	5	5	3
15	FINANCE	3	1	0
16	TELECOMMUNICATIONS	3	2	0
17	DPIIT	2	1	0
18	FERTILISERS	1	0	0
19	SHIPPING AND PORTS	1	0	0
20	SOCIAL JUSTICE	1	0	0
21	DEFENCE PRODUCTION	1	1	0
22	COMMERCE	1	0	0
23	DONER	1	0	0
24	RENEWABLE ENERGY	1	0	0
	Total	1526	647	71

3. Total original cost of implementation of the 1526 projects was ₹21,26,460.93 crore and their anticipated completion cost is likely to be ₹25,91,823.45 crore, which reflects overall cost overruns of ₹4,65,362.52 crore (21.88% of original cost). The expenditure incurred on these projects till August 2022 is ₹13,60,645.94 crore, which is 52.49% of the anticipated cost of the projects. The information can be viewed graphically as:

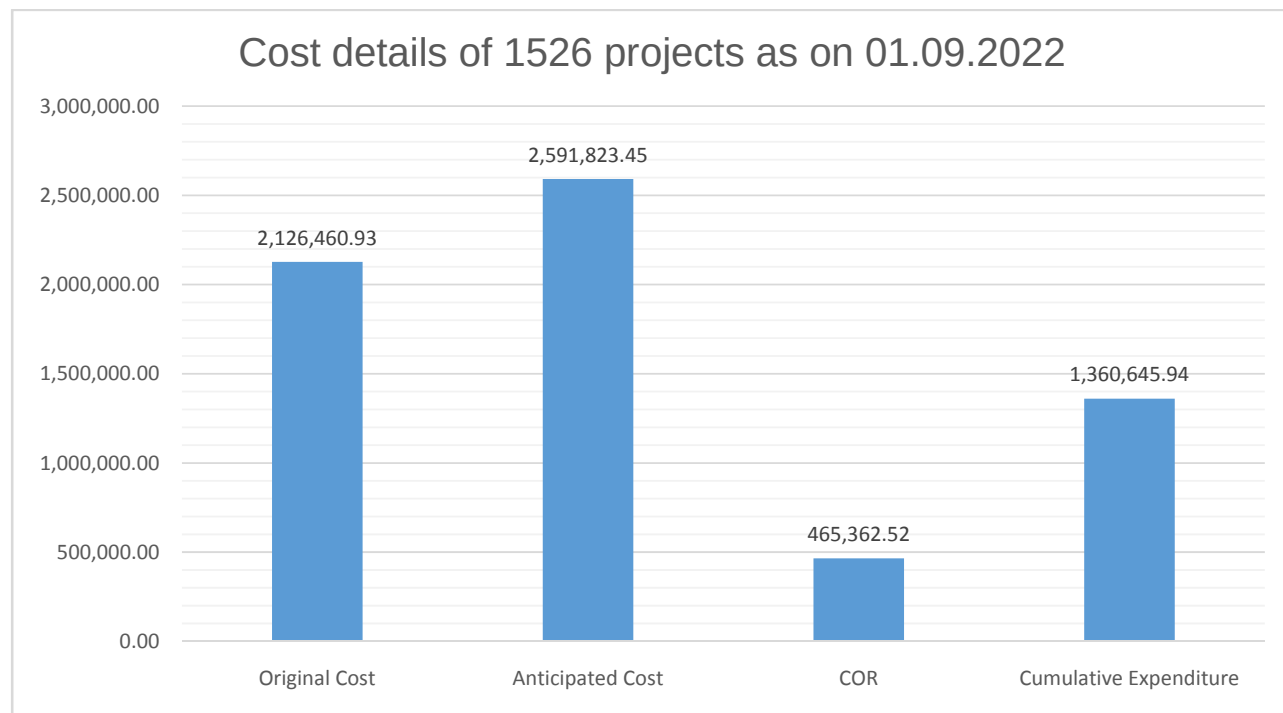


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute terms are at **Table A** and **Table B** respectively.

5. Out of the 1526 projects, 7 projects are ahead of schedule, 265 are on schedule, 647 are delayed, 393 projects reported cost overrun and 219 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 500 if delay is calculated on the basis of latest schedule of completion. Further, for 607 projects neither the year of commissioning nor the tentative gestation period has been reported.


Status of projects (as on 01.09.2022)

(All the figures corresponds to number of project)

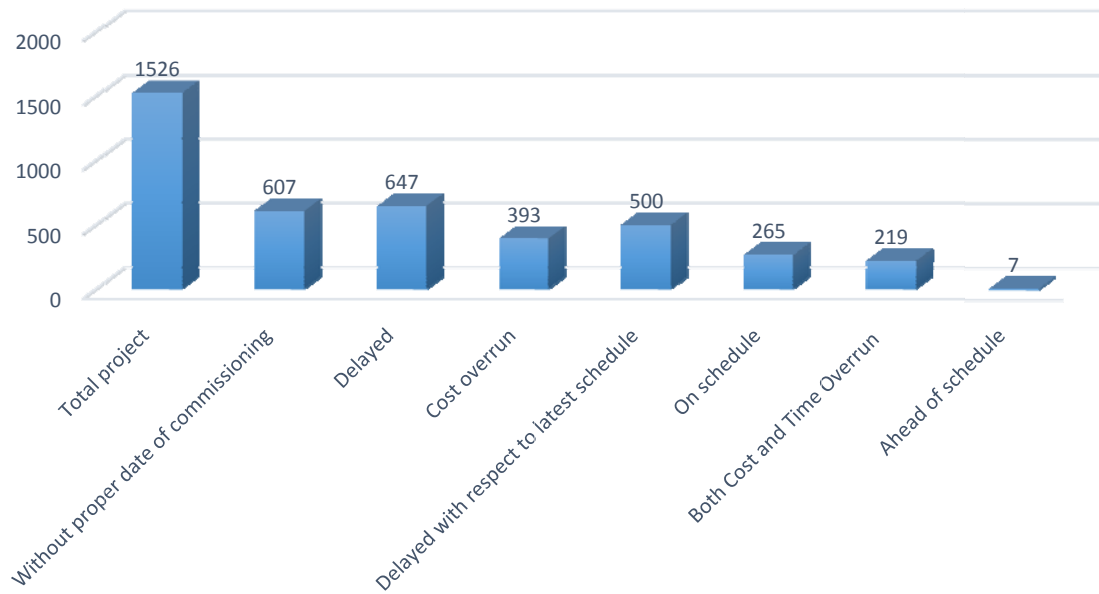


6. Out of 647 delayed projects, 132 (20.40%) projects have overall delay in the range of 1 to 12 months, 118 (18.24%) projects have delay in the range of 13 to 24 months, 273 (42.19%) projects have delay in the range of 25 to 60 months and 124 (19.17%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

Break up of 647 delayed projects in months

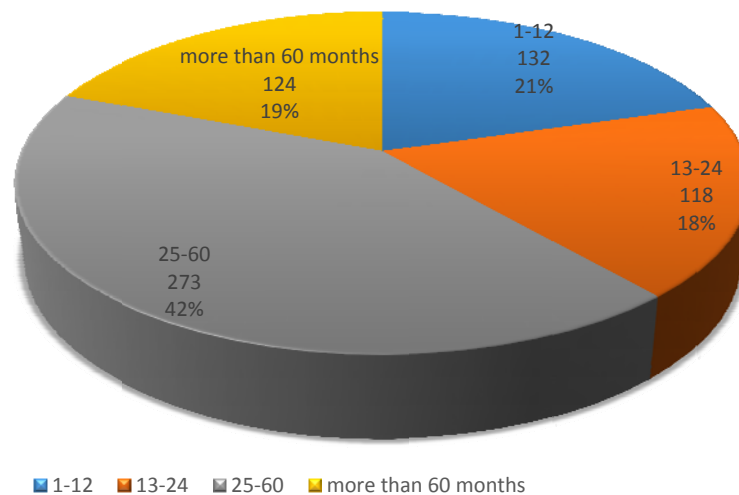

7. The status of online reporting of projects can be viewed month wise as:

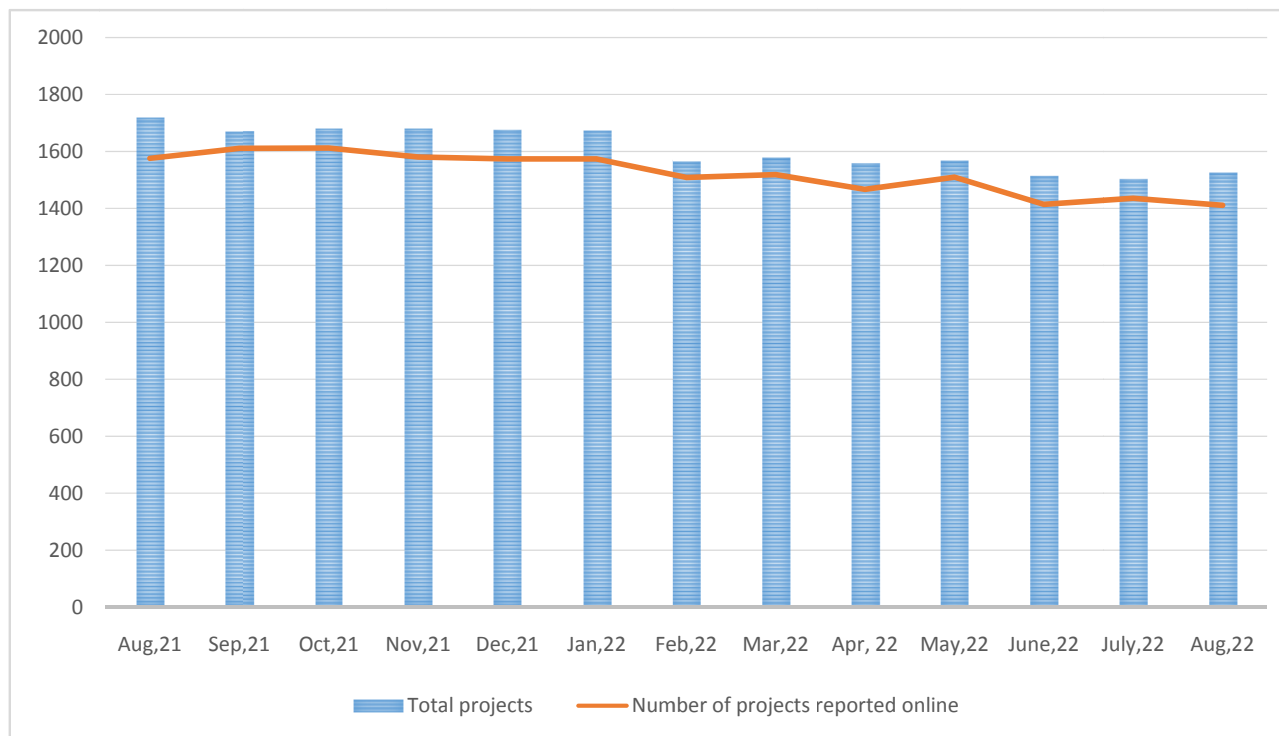

The average time overrun in these 647 delayed projects is 41.64months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment

- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. These sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures may be under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

Table- A

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-09-2022)

SN	PROJECT	DATE OF APPROVAL	COST ORIGINAL (Rs in crore)	COST ANTICIPATED (Rs in crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3,492	7,500	114.78
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11,459	19,220	67.73
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12,320	17,079	38.63
CIVIL AVIATION					
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1,383	2,445	76.79
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417	708	69.63
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346	480	38.72
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	304	351	15.61
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1,142	1,232	7.88
COAL					
9	RANIGANJ MASTER PLAN	08/2009	2,662	5,146	93.35
10	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	480	868	81.09
11	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243	334	37.56
12	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5,907	7,981	35.10
13	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	304	341	12.20
DEPARTMENT OF HIGHER EDUCATION					
14	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	304	334	10.05
DPIIT					
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4,773	5,178	8.49
FINANCE					
16	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/1/2015	209	262	25.36
HEALTH AND FAMILY WELFARE					
17	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414	587	41.63
18	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204	285	39.41
19	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	153	178	16.33
20	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	506	587	16.10

21	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	169	191	13.20
HOME AFFAIRS					
22	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/1/2013	1219.21	1679.02	37.71
23	NSG AT KOLKATA	10/1/2014	162.88	210.83	29.44
24	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	6/1/2019	277.35	290.33	4.68
MINES					
25	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/1/2015	355	581	63.66
26	UTKAL D AND E COAL BLOCK	5/1/2016	534	667.23	24.95
27	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/1/2014	5540	6435.9	16.17
PETROLEUM					
28	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	862	2,001	132.23
29	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678	1,472	117.11
30	LPG TERMINAL AT KOCHI	10/2015	607	1,236	103.60
31	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2,915	5,909	102.71
32	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1,823	3,028	66.09
POWER					
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6,285	19,992	218.08
34	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1,657	4,826	191.23
35	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3,920	10,463	166.94
36	BARH STPP(3X660MW) NTPC	02/2005	8,693	21,312	145.16
37	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2,978	7,103	138.48
RAILWAYS					
38	RAMGANJMUNDI-BHOPAL (NL),WCR	04/2001	425	2,910	585.35
39	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	495	2,980	501.57
40	SEVOK RANGPO, NEFR	04/2008	1,339	7,877	488.06
41	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	09/2006	533	2,650	397.31
42	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	06/2018	229	1,096	378.60
ROAD TRANSPORT AND HIGHWAYS					
43	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	667	3,007	350.75
44	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	06/2016	667	2,328	249.07
45	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	01/2016	815	2,324	185.04
46	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	01/2016	1,028	2,628	155.79
47	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	479	1,082	126.20
STEEL					
48	NMDC INTEGRATED STEEL PLANT	1/1/2010	15525	21940	41.32
TELECOMMUNICATIONS					

49	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/1/2020	431.16	461.42	7.02
URBAN DEVELOPMENT					
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23,136	33,406	44.39
51	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10,773	12,925	19.98
52	NAGPUR METRO RAIL	08/2014	8,680	9,760	12.44
53	PATNA METRO RAIL CORPORATION LIMITED	02/2019	13,366	13,926	4.19
WATER RESOURCES					
54	POLAVARAM IRRIGATION PROJECT	02/2009	10,151	55,549	447.22
55	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	226	399	76.68
56	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254	413	62.63
57	SAIDPUR SEWER NETWORK PATNA	04/2015	269	431	60.52
58	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	214	261	22.24

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns
(COR)(as on 01-09-2022)**

SN	PROJECT	DATE OF APPROVAL	COST ORIGINAL (Rs in crore)	COST ANTICIPATED (Rs in crore)	COR (Rs in crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3,492	7,500	4,008
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11,459	19,220	7,761
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12,320	17,079	4,759
CIVIL AVIATION					
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1,383	2,445	1,062
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417	708	291
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346	480	134
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	304	351	47
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1,142	1,232	90
COAL					
9	RANIGANJ MASTER PLAN	08/2009	2,662	5,146	2,485
10	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	480	868	389
11	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243	334	91
12	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5,907	7,981	2,074
13	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	304	341	37
DEPARTMENT OF HIGHER EDUCation					
14	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	304	334	31
DPIIT					
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4,773	5,178	405
FINANCE					
16	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/1/2015	209	262	53
HEALTH AND FAMILY WELFARE					
17	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414	587	172
18	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204	285	81
19	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	153	178	25
20	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	506	587	81

21	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	169	191	22
HOME AFFAIRS					
22	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/1/2013	1219.21	1679.02	460
23	NSG AT KOLKATA	10/1/2014	162.88	210.83	48
24	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	6/1/2019	277.35	290.33	13
MINES					
25	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/1/2015	355	581	226
26	UTKAL D AND E COAL BLOCK	5/1/2016	534	667.23	133
27	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/1/2014	5540	6435.9	896
PETROLEUM					
28	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	862	2,001	1,140
29	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678	1,472	794
30	LPG TERMINAL AT KOCHI	10/2015	607	1,236	629
31	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2,915	5,909	2,994
32	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1,823	3,028	1,205
POWER					
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6,285	19,992	13,707
34	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1,657	4,826	3,169
35	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3,920	10,463	6,543
36	BARH STPP(3X660MW) NTPC	02/2005	8,693	21,312	12,619
37	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2,978	7,103	4,125
RAILWAYS					
38	RAMGANJMUUNDI-BHOPAL (NL),WCR	04/2001	425	2,910	2,485
39	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	495	2,980	2,485
40	SEVOK RANGPO, NEFR	04/2008	1,339	7,877	6,537
41	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	09/2006	533	2,650	2,117
42	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	06/2018	229	1,096	867
ROAD TRANSPORT AND HIGHWAYS					
43	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	667	3,007	2,340
44	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	06/2016	667	2,328	1,661
45	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	01/2016	815	2,324	1,509
46	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	01/2016	1,028	2,628	1,601
47	HARIDWAR DEHRADUN APPROVED	11/2011	479	1,082	604

	LENGTH 69				
	STEEL				
48	NMDC INTEGRATED STEEL PLANT	1/1/2010	15525	21940	6,415
	TELECOMMUNICATIONS				
49	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/1/2020	431.16	461.42	30
	URBAN DEVELOPMENT				
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23,136	33,406	10,270
51	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10,773	12,925	2,152
52	NAGPUR METRO RAIL	08/2014	8,680	9,760	1,080
53	PATNA METRO RAIL CORPORATION LIMITED	02/2019	13,366	13,926	560
	WATER RESOURCES				
54	POLAVARAM IRRIGATION PROJECT	02/2009	10,151	55,549	45,398
55	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	226	399	173
56	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254	413	159
57	SAIDPUR SEWER NETWORK PATNA	04/2015	269	431	163
58	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	214	261	48

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns
(TOR) (as on 01-09-2022)**

SN	PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING	TOR (in month)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2024	168
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2023	90
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2023	84
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	10/2022	49
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	03/2024	48
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	03/2021	03/2025	48
8	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	12/2022	34
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	12/2024	34
COAL					
10	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2023	144
11	KARTALI (EAST) OCP (2.50 MTY)	07/2008	03/2014	03/2026	144
12	MURAI DIH UG TURN-KEY PROJECT	02/2011	04/2014	10/2025	138
13	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	03/2013	03/2024	132
14	KARMA OCP (1.0MTY)	06/2009	03/2014	03/2023	108
DEPARTMENT OF HIGHER EDUCATION					
15	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	03/2020	02/2023	35
DPIIT					
16	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	01/2023	37
FINANCE					
17	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	10/2022	36
HEALTH AND FAMILY WELFARE					
18	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	09/2021	94
19	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	06/2021	49
20	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	01/2021	44
21	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	12/2021	39
22	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	03/2018	39

	HOME AFFAIRS				
22	NSG AT KOLKATA	10/2014	04/2018	09/2023	65
23	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	12/2022	38
24	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	07/2022	06/2023	11
	MINES				
25	UTKAL D AND E COAL BLOCK	05/2016	01/2020	11/2023	46
26	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	09/2017	06/2019	12/2022	42
27	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2015	11/2020	12/2023	37
	PETROLEUM				
28	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2025	146
29	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2022	115
30	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
31	LPG TERMINAL AT KOCHI	10/2015	10/2017	12/2022	62
32	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	04/2018	05/2023	61
	POWER				
33	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2023	171
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
35	BARH STPP(3X660MW) NTPC	02/2005	10/2011	03/2024	149
36	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	03/2013	12/2024	141
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	03/2025	141
	RAILWAYS				
38	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
39	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2023	228
40	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	03/2009	03/2027	216
41	KHURDA ROAD-BOLANGIR(NL)ECOR	04/1994	03/2009	12/2025	201
42	MANOHARABAD-KOTHPALL NEW LINE(SCR)	04/2006	03/2010	03/2025	180
	ROAD TRANSPORT AND HIGHWAYS				
43	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	09/2011	12/2013	05/2024	125
44	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
45	2 LANNING OF MUZAFFARPUR - SONBARSA	05/2011	11/2013	05/2022	102
46	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013	03/2022	101
47	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	03/2015	01/2016	06/2023	89

	STEEL				
48	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	03/2023	94
	TELECOMMUNICATIONS				
49	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	10/2014	03/2018	11/2022	56
	URBAN DEVELOPMENT				
50	NAGPUR METRO RAIL	08/2014	03/2018	03/2022	48
51	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	09/2022	45
52	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	03/2020	12/2023	45
	WATER RESOURCES				
53	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	03/2024	48
54	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	09/2020	03/2024	42
55	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	03/2020	06/2022	27
56	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	03/2022	04/2024	25
57	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	05/2018	02/2022	03/2024	25

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones (as on 01-09-2022)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.8	351.21	247.98	04/2020	12/2022
	COAL						
2	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	304.13	341.22	139.2	03/2017	12/2022
3	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243	334.27	18.35	04/2018	12/2021
FERTILISERS							
4	AN MELT PROJECT AT RCF TROMBAY	05/2022	187.27	187.27	0.8	09/2024	07/2024
MINES							
5	POTTANGI BAUXITE MINES	05/2018	1437	1381	334.32	12/2024	12/2024
STEEL							
6	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	123.14	12/2023	12/2023
7	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT	02/2022	06/2024	06/2024	207.74	207.74	8.71
8	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP	01/2022	970.18	970.18	76.33	05/2025	05/2025
PETROLEUM							
9	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678	1472	19.51	02/2017	09/2022
10	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711	711	11.12	06/2020	N.A.
11	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	348	437	271.34	01/2021	12/2022
12	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	08/2017	318.8	318.8	210.47	08/2021	03/2023
13	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	08/2018	466	466	343.45	04/2021	09/2022
HEALTH AND FAMILY WELFARE							
14	LGBRIMH-TEZPUR,	07/2012	175.57	179.15	179.15	12/2014	03/2018

	ASSAM						
15	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.5	586.5	11/2013	09/2021
16	CNCI KOLKATA WEST BENGAL	08/2016	244	248	224.92	09/2018	12/2021
17	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	355.15	355.15	321.31	03/2019	12/2021
18	GERIATRICS BLOCK-AIIMS DLEHI	12/2017	156.56	205	145.94	N.A.	01/2022
RAILWAYS							
19	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	2271.5	4805.17	3140.43	03/2021	03/2025
20	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	1510	1547.42	N.A.	03/2024
21	SAKRI-HASANPUR ROAD (NL)	04/1999	325	735.2	413.53	N.A.	12/2024
22	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	04/1997	162.87	614.45	360.11	N.A.	03/2025
23	KHURDA ROAD-BOLANGIR(NL)ECOR	04/1994	2923.13	3791.66	2027.2	03/2009	12/2025
ROAD TRANSPORT AND HIGHWAYS							
24	KANDLA - MUNDRA PORT	01/2011	953.88	953.88	91.63	07/2013	01/2011
25	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	268.08	390.73	386.57	05/2017	06/2022
26	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	191.08	191.08	182.41	08/2015	06/2022
27	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	11/2013	683.83	698.82	717.89	07/2016	06/2022
28	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	01/2014	282.41	319.96	218.75	03/2016	07/2022
TELECOMMUNICATIONS							
29	NETWORK FOR SPECTRUM	03/2012	13334	13334	21545	07/2015	N.A.
30	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	461.42	107.44	06/2021	11/2022
URBAN DEVELOPMENT							
31	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6065.85	07/2017	N.A.
32	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136	33406	22064.15	03/2020	12/2023
33	NAGPUR METRO RAIL	08/2014	8680	9759.79	8524.81	03/2018	03/2022
34	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11420	11420	9009.34	11/2021	03/2023

35	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	1128	1128	69.28	03/2022	06/2024
WATER RESOURCES							
36	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	238.21	12/2019	06/2022
37	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L	03/2017	665.78	665.78	372.23	12/2022	12/2022
38	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	05/2016	211.79	211.79	136.75	12/2021	12/2022
39	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.9	332.7	03/2020	06/2022
40	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	276.1	04/2020	06/2022
COMMERCE							
41	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	0	302.64	30	N.A.
DEPARTMENT OF HIGHER EDUCATION							
42	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	03/2020	808.62	808.62	536.84	07/2022	10/2022
43	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	429.7	242.25	09/2014	12/2022
DPIIT							
44	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773	5178	3032.83	12/2019	01/2023
45	NATIONAL INDUSTRIAL CORRIDOR PROJECT	09/2011	20084	20084	9680.31	03/2027	03/2027
RENEWABLE ENERGY							
46	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	271.9	365	249.96	11/2019	N.A.

N.A.: Not Available.

Table-E

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised
Cost Estimates (as on 01-09-2022)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	0.00	570.11
	COAL				
2	ANANTA OCP EXPANSION PH III	08/2008	228.08	0.00	323.51
3	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	0.00	874.49
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	0.00	7980.79
	HEALTH AND FAMILY WELFARE				
6	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	586.50
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	285.00
8	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	182.10
	HOME AFFAIRS				
11	NSG AT KOLKATA	10/2014	162.88	0.00	176.16
	PETROLEUM				
12	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	09/2017	2677.00	0.00	2943.70
13	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	02/2019	2292.46	0.00	2311.32
14	PIPELINE REPLACEMENT PROJECT (PRP-VI)	05/2019	763.92	0.00	830.87
	POWER				
15	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	0.00	4755.19
16	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	8839.26
17	DEVIKOT SOLAR 90MW	03/2020	501.29	0.00	506.75
	RAILWAYS				
18	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	845.23
19	VIZIANAGARAM -SAMABALPUR 3RD LINE	01/1991	2335.67	0.00	2712.78
20	BHAIRABI SAIRONG, NL, NEFR	04/2008	2393.47	0.00	5330.91
21	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	2271.50	0.00	3140.43
22	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	0.00	12817.81
	ROAD TRANSPORT AND HIGHWAYS				
23	TRICHY - KARUR	03/2007	516.00	0.00	886.96
24	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	02/2008	1673.70	0.00	3326.93
25	PUNE-SATARA(NH-4)	10/2010	1724.55	0.00	2919.69
26	4-LANING OF FARAKA-RAIGANJ	02/2011	1078.84	0.00	2301.82
27	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	07/2010	1987.00	0.00	3116.66
	STEEL				
28	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	262.87	0.00	272.19
	TELECOMMUNICATIONS				
29	NETWORK FOR SPECTRUM	03/2012	13334.00	0.00	21545.00
	URBAN DEVELOPMENT				

30	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	17629.68
31	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39907.57
32	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	6065.85
WATER RESOURCES					
33	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	03/2017	277.42	0.00	298.55

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-09-2022)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	N.A.	N.A.
COAL					
2	ANANTA OCP EXPANSION PH III	08/2008	03/2012	N.A.	N.A.
3	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	09/2020	N.A.	N.A.
4	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	12/2019	N.A.	N.A.
5	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	09/2020	N.A.	N.A.
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
COMMERCE					
7	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
8	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
9	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
10	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
11	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
12	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	06/2020	N.A.	N.A.
PETROLEUM					
20	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	03/2018	08/2022	N.A.	08/2022
21	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
22	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VV SPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	09/2017	06/2021	08/2022	08/2022
23	SWRO II WITH LLPH FACILITIES	09/2019	07/2020	N.A.	N.A.
POWER					
24	EASTERN REGION STRENGTHENING SCHEME - XXIII	07/2020	06/2021	N.A.	04/2022
25	EASTERN REGION STRENGTHENING SCHEME-XII	05/2014	11/2016	N.A.	04/2022
26	EASTERN REGION STRENGTHENING SCHEME-XVIII	03/2017	07/2020	N.A.	08/2022
27	KAWAS SOLAR 56 MW	08/2020	10/2021	01/2023	08/2022

28	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
RAILWAYS					
29	MULTI MODAL LOGISTICS PARK AT KAKINADA	08/2016	03/2019	N.A.	03/2019
30	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	03/2019	N.A.	03/2019
31	ROHTAK-MEHAM HANSI	04/2012	12/2011	N.A.	12/2011
32	ROSA-SITAPUR CANTT- BURHWAL DOUBLING	03/2015	03/2022	N.A.	03/2022
33	SAMBALPUR-TALCHER DOUBLING	03/2011	02/2019	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
34	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	02/2017	04/2017	N.A.	04/2017
35	ETAWAH CHAKERI	03/2013	09/2015	N.A.	01/2016
36	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	03/2016	08/2016	N.A.	08/2016
37	FOUR LANING OF VARANASI BYPASS	05/2015	05/2017	N.A.	05/2019
38	GHAZIABAD-ALIGARH NH-91	02/2011	08/2013	N.A.	08/2013
TELECOMMUNICATIONS					
40	NETWORK FOR SPECTRUM	03/2012	07/2015	N.A.	N.A.
URBAN DEVELOPMENT					
41	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	06/2016	03/2018	02/2021	N.A.
42	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
43	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	06/2015	04/2019	N.A.	N.A.
44	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	05/2017	12/2020	09/2021	N.A.
45	DELHI MRTS PHASE-III	09/2011	03/2016	08/2021	N.A.
WATER RESOURCES					
46	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	05/2017	05/2020	N.A.	N.A.
47	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	12/2022	N.A.

N.A.: Not Available.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	831	23
2	RAILWAYS	173	9
3	PETROLEUM	139	9
4	COAL	122	1
5	POWER	78	18
6	WATER RESOURCES	41	2
7	HEALTH AND FAMILY WELFARE	28	1
8	URBAN DEVELOPMENT	28	1
9	CIVIL AVIATION	25	1
10	DEPARTMENT OF HIGHER EDUCATION	20	1
11	STEEL	9	2
12	MINES	7	0
13	ATOMIC ENERGY	5	0
14	HOME AFFAIRS	5	3
15	FINANCE	3	0
16	TELECOMMUNICATIONS	3	0
17	DPIIT	2	0
18	FERTILISERS	1	0
19	SHIPPING AND PORTS	1	0
20	SOCIAL JUSTICE	1	0
21	DEFENCE PRODUCTION	1	0
22	COMMERCE	1	0
23	DONER	1	0
24	RENEWABLE ENERGY	1	0
	Total	1526	71

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2022-2023				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2022			
	<u>PETROLEUM</u>			
1	PARADIP LPG IMPORT FACILITY (INDIAN OIL CORPORATION LIMITED) - [N16000196]	690.00	07/2018	625.28
2	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI Central Sector Projects(GAS AUTHORITY OF INDIA LIMITED) - [N16000288]	287.49	04/2022	215.02
3	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND (INDIAN OIL CORPORATION LIMITED) - [N16000304]	236.00	06/2020	248.03
4	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU (INDIAN OIL CORPORATION LIMITED) - [N16000305]	466.43	10/2020	323.49
5	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000308]	315.00	12/2021	232.80
6	LPG BP PROJECT MOTIHARI (INDIAN OIL CORPORATION LIMITED) - [N16000317]	206.50	03/2021	180.57
7	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000337]	189.00	01/2021	189.22
8	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR (INDIAN OIL CORPORATION LIMITED) - [N16000344]	522.00	03/2021	443.99
9	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000380]	380.00	11/2021	366.58
	<u>POWER</u>			
10	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000066]	11,130.19	08/2013	12,394.95
11	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000188]	1,394.52	05/2017	587.21
12	EASTERN REGION STRENGTHENING SCHEME XX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000268]	358.83	05/2020	264.46
13	JETSAR SOLAR 160 MW EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000287]	702.28	03/2021	631.69
14	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000309]	496.11	06/2020	322.28
15	WESTERN REGION SYSTEM STRENGTHENING - XX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000310]	226.98	08/2021	129.97
16	SOUTHERN REGION SYSTEM STRENGTHENING - XXV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000311]	154.72	07/2021	95.53
17	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000312]	2,578.47	12/2020	1,797.70
18	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000318]	221.36	03/2021	123.44

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
19	4 LANING OF NAGPUR-BETUL PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000155]	2,498.76	08/2014	2,531.46
20	NASHRI- CHANANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000162]	2,159.00	06/2015	4,729.68
21	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000233]	1,266.60	09/2016	1,446.45
22	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000367]	495.78	01/2016	833.76
23	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000460]	611.65	06/2016	1,816.57
24	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000547]	1,404.50	-	2,977.58
25	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000599]	2,016.00	04/2019	3,026.14
26	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000637]	534.55	-	433.62
27	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000648]	450.68	-	730.06
28	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000672]	2,064.99	03/2020	2,118.76
29	VARANASI RING ROAD PKG - I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000740]	450.77	-	992.12
30	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001163]	329.01	02/2017	233.73
	May,2022			
	<u>COAL</u>			
31	MANIKPUR OC EXPANSION (3.5 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000081]	321.50	03/2014	225.36
	<u>PETROLEUM</u>			
32	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000316]	161.50	06/2020	149.10
33	220 KV GRID SUPPLY EPC(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000407]	303.40	03/2021	199.17
	<u>POWER</u>			
34	BRBCL-NABINAGAR TPP- JV (4X250 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000190]	5,353.00	07/2012	8,839.26
35	NPGCPL-NABINAGAR STPP - JV (3X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000192]	12,964.60	05/2018	15,763.67

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
36	PAKRI BARWADIH COAL MINING PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000225]	4,237.96	10/2017	3,409.94
37	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL (NATIONAL THERMAL POWER CORPORATION) - [N18000276]	1,885.13	12/2018	2,050.89
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
38	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000327]	394.00	06/2018	380.00
39	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000554]	870.00	03/2019	283.38
40	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000867]	216.00	11/2018	117.19
41	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000882]	218.70	11/2020	103.81
42	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000889]	279.70	08/2017	331.86
43	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000923]	464.07	11/2018	319.88
44	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000959]	341.79	05/2018	226.00
45	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000976]	210.50	-	145.79
	<u>PETROLEUM</u>			
46	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000359]	3,660.71	05/2021	3,637.73
	<u>POWER</u>			
47	RAMAGUNDAM FLOATING SOLAR 100 MW EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000284]	401.90	04/2021	321.18
48	KAYAMKULAM SOLAR 70 MW EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000288]	403.62	06/2021	245.53
	<u>RAILWAYS</u>			
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) (SOUTHERN RAILWAY) - [220100262]	303.98	03/2020	727.62
50	DHASA-JETALSAR (GC) (RAIL VIKAS NIGAM LTD.) - [N22000141]	644.38	03/2021	980.39

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
51	ARA-BHABHUA ROAD (NL) (EAST CENTRAL RAILWAYS) - [N22000166]	633.87	-	0.40
52	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) (EAST CENTRAL RAILWAYS) - [N22000175]	678.62	-	3.20
53	KURUPPANTHARA-CHINGAVANAM (SOUTHERN RAILWAY) - [N22000190]	270.14	-	702.85
54	BHADRACHALAM ROAD-SATTUPALLI (SOUTH CENTRAL RAILWAY) - [N22000287]	704.31	03/2020	903.18
55	YELAHANKA-PENUKONDA (SOUTH WESTERN RAILWAY) - [N22000328]	860.43	03/2020	1,062.99
56	ARSIKERE-TUMKUR (SOUTH WESTERN RAILWAY) - [N22000332]	578.00	03/2020	681.32
57	DUVVADA-VIJAYAWADA (SOUTH CENTRAL RAILWAY) - [N22000366]	3,873.07	-	0.07
58	DIGARU-HOJAI (102 KM) (NORTH EAST FRONTIER RAILWAY) - [N22000389]	870.96	03/2021	1,829.49
59	SECUNDERABAD-MAHABUBNAGAR DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000403]	773.94	12/2024	1,275.94
60	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT (SOUTH EAST CENTRAL RAILWAY) - [N22000438]	585.93	02/2019	1,222.59
61	JALANDHAR-PATHANKOT-JAMMU TAWI (NORTHERN RAILWAY) - [N22000492]	625.00	03/2016	838.77
62	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW (RAIL INDIA TECHNICAL AND ECONOMIC SERVICE) - [N22000498]	393.98	03/2020	388.49
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
63	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000125]	1,509.10	09/2012	3,684.44
64	MUZAFFARNAGAR-HARIDWAR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000201]	754.00	03/2013	1,364.18
65	2 LANING WITH PS OF GULABPURA - UNIARA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000423]	597.00	10/2017	587.64
66	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000443]	991.59	06/2018	1,154.00
67	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000468]	795.76	-	669.94
68	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000469]	794.30	-	669.35
69	FOUR LANING OF YADGIRI - WARANGAL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000486]	1,423.96	11/2018	975.10
70	FOUR LANING OF JABALPUR - LAKHNADON (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000489]	928.83	-	867.83
71	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000504]	810.22	-	742.47
72	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 () (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000563]	1,668.00	-	946.08
73	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL- SANCHI SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000605]	227.49	01/2019	193.99

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
74	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000660]	296.19	03/2020	254.85
75	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000663]	1,989.00	03/2020	772.56
76	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. Central Sector Projects(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000702]	639.97	10/2017	485.05
77	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 Central Sector Projects(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000705]	374.40	09/2017	215.49
78	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 Central Sector Projects(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000706]	990.61	09/2017	681.43
79	4-LANNING OF OTTANCHATRAM BYPASS Central Sector Projects(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000707]	244.27	09/2017	178.41
80	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000793]	925.40	-	1,136.70
81	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000836]	275.12	-	153.00
82	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000842]	199.90	-	124.52
83	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000843]	196.05	-	143.03
84	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000846]	198.05	-	123.94
85	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000848]	181.78	-	174.02
86	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001240]	370.36	08/2022	271.81
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
87	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND (CPWD OF HIGHER EDUCATION) - [N28000065]	270.83	11/2014	235.32
	July,2022			
	<u>FERTILISERS</u>			
88	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY (RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000018]	426.72	04/2020	366.30
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
89	SAMBHU KI BHURJ SOLAR 250 MW EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000285]	1,522.71	09/2021	1,315.75
90	FATEHGARH SOLAR 296MW EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000289]	1,749.31	09/2021	1,441.61
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
91	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422- KM 242.300 CHILPI- KAWARDHA SECTION. EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000281]	291.05	-	257.85
92	REHABILITATION AND UPGADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001091]	536.65	12/2019	573.95
93	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001229]	379.16	11/2017	332.92
	August,2022			
	<u>PETROLEUM</u>			
94	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) (OIL INDIA LIMITED) - [N16000258]	406.00	10/2020	314.00
95	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II (OIL INDIA LIMITED) - [N16000259]	571.66	12/2019	511.00
96	DOBHI-DURGAPUR PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000273]	2,433.00	12/2020	2,250.60
97	LAB REVAMP AT GUJARAT REFINERY Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000377]	403.00	04/2022	279.12
98	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000397]	640.00	12/2021	424.30
	<u>HEAVY INDUSTRY</u>			
99	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) (NATRIP IMPLEMENTATION SOCIETY) - [N20000001]	1,718.00	09/2011	3,496.57
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
100	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000131]	1,693.75	08/2011	2,848.49
101	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000328]	369.00	03/2018	322.69
102	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000869]	517.57	10/2018	438.74

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
103	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000972]	175.06	-	102.00
104	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000973]	176.12	-	102.99
105	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24001319]	257.96	01/2022	122.81

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2022-2023				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2022			
	<u>STEEL</u>			
1	SCREENING PLANT III AT KIRANDUL (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000128]	2,092.97	08/2024	0.00
	<u>RAILWAYS</u>			
2	ANGAMALI-SABARIMALA (N.L.)(SR) (SOUTHERN RAILWAY) - [220100252]	1,566.00	-	264.30
3	DEOGHAR - SULTANGANJ (INL), ER (EASTERN RAILWAYS) - [220100273]	607.09	02/2013	633.43
4	BANGLORE - SATYAMANGALAM (NL)(SWR) (SOUTH WESTERN RAILWAY) - [220100274]	1,382.78	03/2002	7.35
5	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP (NORTH EASTERN RAILWAY) - [N22000130]	307.00	-	0.00
6	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP (NORTH EASTERN RAILWAY) - [N22000136]	643.00	-	0.00
7	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) (WESTERN RAILWAY) - [N22000143]	320.66	03/2019	540.09
8	PUSHKAR-MERTA (NORTH WESTERN RAILWAY) - [N22000151]	323.00	-	0.00
9	BIHTA-AURANGABAD (NL) (EAST CENTRAL RAILWAYS) - [N22000170]	326.20	-	2.88
10	CHHAPRA-MUZAFFARPUR (NL) (EAST CENTRAL RAILWAYS) - [N22000172]	378.56	-	387.43
11	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR (SOUTHERN RAILWAY) - [N22000186]	839.00	-	0.63
12	KUMBALAM-TURAVUR (SOUTHERN RAILWAY) - [N22000191]	252.96	-	256.71
13	DIMAPUR-TIZIT NL (NORTH EAST FRONTIER RAILWAY) - [N22000196]	4,274.00	03/2020	0.00
14	ERNAKULAM-KUMBALAM (SOUTHERN RAILWAY) - [N22000204]	189.24	-	268.76
15	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR (METROPOLITAN RAPID TRANSPORT PROJECTS) - [N22000212]	573.78	-	0.00
16	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG(EASTERN RAILWAYS) - [N22000216]	406.99	03/2006	149.04
17	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3(EASTERN RAILWAYS) - [N22000224]	923.52	03/2016	606.83
18	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL (EASTERN RAILWAYS) - [N22000228]	277.28	03/2016	212.86

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
19	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL(EASTERN RAILWAYS) - [N22000240]	494.54	03/2005	30.12
20	MANUGURU-RAMAGUNDAM (SOUTH CENTRAL RAILWAY) - [N22000259]	1,112.00	-	0.92
21	GUDUR-DURGARAJPATNAM (SOUTH CENTRAL RAILWAY) - [N22000265]	761.37	-	0.53
22	GRADE SEPERATOR AT DAYABASTI (NORTHERN RAILWAY) - [N22000269]	156.65	-	116.87
23	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL (SOUTH WESTERN RAILWAY) - [N22000276]	558.00	-	0.00
24	SRINIVASA-PURA-MADANAPALLI NL (SOUTH WESTERN RAILWAY) - [N22000277]	296.00	-	0.00
25	WHITE FIELD-KOLAR NL (SOUTH WESTERN RAILWAY) - [N22000280]	348.85	-	0.36
26	CUMBUM-PRODDATUR (SOUTH CENTRAL RAILWAY) - [N22000282]	829.00	-	1.01
27	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I (SOUTH CENTRAL RAILWAY) - [N22000288]	2,132.77	03/2014	347.10
28	CHIKBALLA-PUR-GOWRIBIDANUR NL (SOUTH WESTERN RAILWAY) - [N22000300]	327.25	-	0.00
29	INDORE - MANMAD VIA MALEGAON (368 KM) (CENTRAL RAILWAYS) - [N22000353]	9,968.00	03/2024	0.00
30	PUNE-NASIK (265 KM) (CENTRAL RAILWAYS) - [N22000354]	2,425.00	03/2024	0.00
31	VAIBHAVWADI - KOLHAPUR (107 KM) (CENTRAL RAILWAYS) - [N22000355]	2,750.00	03/2024	0.00
32	KONDAPALLI-KOTHAGUDEM (SOUTH CENTRAL RAILWAY) - [N22000364]	723.00	-	0.00
33	DIGHI PORT NEW LINE (RAIL VIKAS NIGAM LTD.) - [N22000408]	723.78	12/2025	0.19
34	PALAKKAD - SETTING UP OF RAIL COACH FACTORY (SOUTHERN RAILWAY) - [N22000443]	550.00	03/2016	0.00
35	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. (NORTH EASTERN RAILWAY) - [N22000457]	1,900.00	01/2022	0.00
36	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE (NORTH EASTERN RAILWAY) - [N22000460]	1,343.00	01/2018	0.00
37	ETAH - KASGANJ - NEW LINE (NORTH EASTERN RAILWAY) - [N22000462]	276.90	04/2017	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
38	FOUR LANING OF PATNA - GAYA - DHOBI SECTION OF NH-83 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000355]	1,027.00	04/2018	0.00
39	WIDENING OF PIPLI-BHAVNAGAR-SECTION PACKAGE 1 FROM KM 136/025 TO 169/328 (DESIGN CHAINAGE KM 136/000(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000816]	799.48	-	0.00
40	UPGRADATION TO 4 LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR-BHUJ UP TO AIRPORT (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000817]	894.24	-	0.00
41	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 323.00 TO KM 355.00 (SAPNA TO PADRA SECTI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000818]	1,671.41	-	0.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
42	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 292.00 TO KM 323.00 (MANUBAR TO SANPA SEC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000819]	1,431.74	-	0.00
	July,2022			
	<u>RAILWAYS</u>			
43	PALAKKAD - SETTING UP OF RAIL COACH FACTORY (SOUTHERN RAILWAY) - [N22000443]	550.00	03/2016	0.00

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1505
No of Projects Completed/Dropped/Frozen in Current Month	12
No of Projects added in Current Month	21
No of Projects Elevated in Current Month	12
No of Projects in Current Month	1526

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	647 (42.40%)	7 (.46%)	265 (17.37%)	118 (7.73%)	489 (32.04%)	1526
Latest Approved (Date)	500 (32.77%)	15 (.98%)	431 (28.24%)	91 (5.96%)	489 (32.04%)	1526

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1220	17,50,693.80	19,19,092.58	9,13,866.27	47.60	1,68,398.78	9.60
Project with Revision in Cost	306	6,23,756.33	6,72,730.87	4,46,779.67	66.40	48,974.54	7.90
Total	1,526	23,74,450.13	25,91,823.45	13,60,645.94	52.50	2,17,373.32	9.15
Original Cost of All Projects							
Original Cost	1,526	21,26,460.93	25,91,823.45	13,60,645.94	52.50	4,65,362.52	21.88

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	647	9,57,839.23	12,60,856.62	7,54,269.22	59.80	3,03,017.39	31.64
Latest Approved (RCE)	500	7,74,855.61	9,01,262.99	5,37,790.06	59.70	1,26,407.38	16.31

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	71	1,30,917.79	2,01,415.96	1,49,838.76	74.40	70,498.17	53.80
Total	71	1,30,917.79	2,01,415.96	1,49,838.76	74.39	70,498.17	53.85

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,269.00	14.16	3	27,271.00	43,799.00	60.61
2	CIVIL AVIATION	25	15,984.85	17,572.54	9.93	5	3,592.30	5,216.27	45.21
3	COAL	122	1,68,218.93	1,72,645.43	2.63	8	27,350.03	32,525.64	18.92
4	FINANCE	3	786.27	831.04	5.69	1	209.00	262.00	25.36
5	FERTILISERS	1	187.27	187.27	0.00	0	0.00	0.00	0.00
6	MINES	7	7,333.99	8,585.77	17.07	3	4,992.00	6,303.23	26.27
7	STEEL	9	23,919.19	30,334.19	26.82	1	15,525.00	21,940.00	41.32
8	PETROLEUM	139	3,66,013.55	3,86,263.94	5.53	28	66,663.55	91,460.94	37.20
9	POWER	78	1,82,940.83	2,35,941.73	28.97	24	79,676.96	1,33,194.91	67.17
10	HEALTH AND FAMILY WELFARE	28	13,696.26	14,200.97	3.69	13	4,456.80	5,069.51	13.75
11	RAILWAYS	173	3,72,761.45	6,19,569.99	66.21	131	1,94,983.24	4,48,395.49	129.97
12	ROAD TRANSPORT AND HIGHWAYS	831	4,92,741.89	5,40,815.51	9.76	153	1,20,587.37	1,73,392.57	43.79
13	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
14	TELECOMMUNICATIONS	3	14,013.36	14,043.62	0.22	1	431.16	461.42	7.02
15	URBAN DEVELOPMENT	28	2,84,811.01	3,05,228.48	7.17	8	1,14,518.89	1,35,015.56	17.90
16	WATER RESOURCES	41	23,466.28	69,354.43	195.55	8	12,225.19	58,202.82	376.09
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
18	DEFENCE PRODUCTION	1	246.31	200.00	-18.80	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	20	9,449.72	9,347.30	-1.08	1	303.90	334.45	10.05
21	HOME AFFAIRS	5	2,025.73	2,546.47	25.71	3	1,659.44	2,180.18	31.38

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	8.49
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	RENEWABLE ENERGY	1	271.90	365.00	34.24	1	271.90	365.00	34.24
Total		1526	21,26,460.93	25,91,823.45	21.88	393	6,79,490.73	11,63,296.99	71.20

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

[illegible]

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
Total		1526	21,26,460.93	25,91,823.45	21.88	393	6,79,490.73	11,63,296.99	71.20

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,269.00	14.16	4	67,120.00	83,648.00	36 - 168
2	CIVIL AVIATION	25	15,984.85	17,572.54	9.93	22	14,858.31	16,482.28	4 - 49
3	COAL	122	1,68,218.93	1,72,645.43	2.63	37	38,126.49	40,392.68	12 - 147
4	FINANCE	3	786.27	831.04	5.69	1	209.00	262.00	36 - 36
5	FERTILISERS	1	187.27	187.27	0.00	0	0.00	0.00	-
6	MINES	7	7,333.99	8,585.77	17.07	6	5,896.99	7,204.77	30 - 46
7	STEEL	9	23,919.19	30,334.19	26.82	4	19,728.88	26,143.88	13 - 94
8	PETROLEUM	139	3,66,013.55	3,86,263.94	5.53	88	1,73,603.38	1,87,965.25	2 - 146
9	POWER	78	1,82,940.83	2,35,941.73	28.97	53	1,39,272.91	1,91,717.74	2 - 171
10	HEALTH AND FAMILY WELFARE	28	13,696.26	14,200.97	3.69	1	1,351.00	1,471.04	11 - 11
11	RAILWAYS	173	3,72,761.45	6,19,569.99	66.21	116	1,76,306.09	3,11,937.08	3 - 276
12	ROAD TRANSPORT AND HIGHWAYS	831	4,92,741.89	5,40,815.51	9.76	248	1,40,679.89	1,54,242.88	1 - 125
13	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
14	TELECOMMUNICATIONS	3	14,013.36	14,043.62	0.22	2	679.36	709.62	17 - 56
15	URBAN DEVELOPMENT	28	2,84,811.01	3,05,228.48	7.17	13	1,45,209.38	1,57,552.40	3 - 49
16	WATER RESOURCES	41	23,466.28	69,354.43	195.55	30	19,855.50	65,407.94	6 - 48
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
18	DEFENCE PRODUCTION	1	246.31	200.00	-18.80	1	246.31	200.00	32 - 32
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	20	9,449.72	9,347.30	-1.08	15	7,897.01	7,794.59	3 - 99
21	HOME AFFAIRS	5	2,025.73	2,546.47	25.71	5	2,025.73	2,546.47	5 - 65
22	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37 - 37
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
24	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	-
Total		1526	21,26,460.93	25,91,823.45	21.88	647	9,57,839.23	12,60,856.62	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	66	1,12,846.32	1,64,854.74	46.09	31	89,785.90	1,39,322.98	4 - 216
2	ARUNACHAL PRADESH	42	23,572.02	37,508.36	59.12	15	10,242.31	24,120.75	7 - 155
3	ASSAM	50	51,277.81	61,098.00	19.15	16	8,656.59	12,482.48	1 - 89
4	BIHAR	79	97,760.92	1,21,511.70	24.29	44	50,261.65	67,850.81	3 - 149
5	GOA	11	5,588.46	5,629.50	0.73	2	559.59	590.14	24 - 35
6	GUJARAT	59	1,08,793.95	1,22,941.89	13.00	21	48,193.11	62,211.58	3 - 144
7	HARYANA	30	58,831.75	61,266.98	4.14	14	10,946.56	11,557.17	5 - 43
8	HIMACHAL PRADESH	19	22,091.98	33,807.28	53.03	5	9,083.49	16,356.02	10 - 171
9	JAMMU AND KASHMIR	27	47,696.67	82,076.18	72.08	9	17,136.00	51,648.26	3 - 247
10	KARNATAKA	50	81,951.07	90,498.98	10.43	27	46,837.48	49,353.50	4 - 129
11	KERALA	15	15,893.03	19,006.36	19.59	4	3,596.80	4,806.66	24 - 66
12	MADHYA PRADESH	67	60,727.92	68,770.29	13.24	42	46,845.88	53,889.18	12 - 116
13	MAHARASHTRA	224	1,89,111.93	2,11,359.02	11.76	59	86,789.22	1,08,235.28	9 - 228
14	MANIPUR	28	12,848.47	22,717.09	76.81	11	7,644.48	17,513.10	3 - 153
15	MEGHALAYA	13	5,093.36	12,456.56	144.56	3	948.46	893.84	12 - 99
16	MIZORAM	25	12,450.29	17,404.99	39.80	9	6,557.52	10,691.50	43 - 117
17	NAGALAND	37	12,630.26	17,014.38	34.71	11	5,099.23	9,435.71	4 - 132
18	ODISHA	79	1,15,014.68	1,24,251.75	8.03	42	51,565.82	60,212.54	6 - 201
19	PUNJAB	23	17,390.42	18,541.79	6.62	9	4,753.34	4,621.82	3 - 108
20	RAJASTHAN	41	54,162.68	59,548.71	9.94	17	28,404.27	33,198.59	2 - 84
21	SIKKIM	21	14,350.32	21,030.43	46.55	12	11,241.38	17,778.82	3 - 96
22	TAMIL NADU	62	2,02,260.40	2,23,144.21	10.33	27	71,874.20	80,587.23	2 - 168
23	TRIPURA	18	4,666.82	4,808.15	3.03	10	2,656.06	2,795.16	5 - 30
24	UTTAR PRADESH	93	1,24,370.16	1,39,066.47	11.82	42	82,912.24	93,587.40	5 - 66
25	WEST BENGAL	62	63,606.38	75,703.23	19.02	36	34,560.32	41,331.51	5 - 141
26	A & N ISLANDS	10	3,043.24	3,314.60	8.92	4	1,309.00	1,599.70	35 - 53
27	DELHI	27	81,077.58	84,083.09	3.71	10	34,529.11	35,375.11	6 - 56
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATISGARH	40	76,020.96	1,02,152.00	34.37	22	34,951.61	45,010.06	3 - 144
30	JHARKHAND	48	73,691.13	80,705.52	9.52	19	41,679.09	44,588.54	3 - 144
31	UTTARAKHAND	29	35,446.38	54,833.80	54.70	14	28,036.00	45,440.45	3 - 141
32	TELANGANA	44	32,353.76	34,700.38	7.25	17	17,795.32	19,601.18	10 - 180
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	27 - 27
34	MULTI STATE	78	3,07,011.58	4,13,054.73	34.54	42	62,040.93	93,689.22	3 - 276
Total		1526	21,26,460.93	25,91,823.45	21.88	647	9,57,839.23	12,60,856.62	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissionin

TABLE-9

Extent of time overrun in projects with respect to latest schedule						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,269.00	0.50	4	82,988.00	83,648.00	36 - 168
2	CIVIL AVIATION	25	16,322.76	17,572.54	7.66	7	4,382.29	5,534.29	4 - 48
3	COAL	122	1,68,359.96	1,72,645.43	2.55	34	36,534.62	38,659.90	12 - 147
4	FINANCE	3	778.04	831.04	6.81	0	0.00	0.00	-
5	FERTILISERS	1	187.27	187.27	0.00	0	0.00	0.00	-
6	MINES	7	8,585.77	8,585.77	0.00	1	255.37	255.37	30 - 30
7	STEEL	9	30,334.19	30,334.19	0.00	3	4,203.88	4,203.88	13 - 74
8	PETROLEUM	139	3,79,470.22	3,86,263.94	1.79	40	80,019.92	85,378.29	0 - 67
9	POWER	78	2,15,233.13	2,35,941.73	9.62	38	1,29,384.58	1,44,339.13	0 - 149
10	HEALTH AND FAMILY WELFARE	28	13,711.40	14,200.97	3.57	1	1,351.00	1,471.04	11 - 11
11	RAILWAYS	173	4,74,776.22	6,19,569.99	30.50	98	1,51,364.78	2,38,747.98	0 - 276
12	ROAD TRANSPORT AND HIGHWAYS	831	5,23,824.24	5,40,815.51	3.24	218	1,43,166.24	1,44,639.59	0 - 121
13	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
14	TELECOMMUNICATIONS	3	14,043.62	14,043.62	0.00	2	709.62	709.62	17 - 56
15	URBAN DEVELOPMENT	28	2,84,811.01	3,05,228.48	7.17	9	1,18,219.18	1,30,562.20	3 - 49
16	WATER RESOURCES	41	69,354.43	69,354.43	0.00	29	9,859.07	9,859.07	6 - 42
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
18	DEFENCE PRODUCTION	1	210.00	200.00	-4.76	1	210.00	200.00	32 - 32
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	20	9,425.47	9,347.30	-0.83	11	5,774.62	5,696.45	3 - 66
21	HOME AFFAIRS	5	2,025.73	2,546.47	25.71	3	1,659.44	2,180.18	11 - 65
22	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37 - 37
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
24	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	-
Total		1526	23,74,450.13	25,91,823.45	9.15	500	7,74,855.61	9,01,262.99	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,269.00	0.50	1	6,840.00	7,500.00	9.65
2	CIVIL AVIATION	25	16,322.76	17,572.54	7.66	3	2,871.27	4,157.33	44.79
3	COAL	122	1,68,359.96	1,72,645.43	2.55	5	26,513.45	31,548.15	18.99
4	FINANCE	3	778.04	831.04	6.81	1	209.00	262.00	25.36
5	FERTILISERS	1	187.27	187.27	0.00	0	0.00	0.00	0.00
6	MINES	7	8,585.77	8,585.77	0.00	0	0.00	0.00	0.00
7	STEEL	9	30,334.19	30,334.19	0.00	0	0.00	0.00	0.00
8	PETROLEUM	139	3,79,470.22	3,86,263.94	1.79	7	35,742.57	48,005.29	34.31
9	POWER	78	2,15,233.13	2,35,941.73	9.62	20	56,341.34	77,566.99	37.67
10	HEALTH AND FAMILY WELFARE	28	13,711.40	14,200.97	3.57	13	4,456.80	5,069.51	13.75
11	RAILWAYS	173	4,74,776.22	6,19,569.99	30.50	114	1,87,481.71	3,37,599.09	80.07
12	ROAD TRANSPORT AND HIGHWAYS	831	5,23,824.24	5,40,815.51	3.24	136	90,714.91	1,22,721.17	35.28
13	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
14	TELECOMMUNICATIONS	3	14,043.62	14,043.62	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	28	2,84,811.01	3,05,228.48	7.17	8	1,14,518.89	1,35,015.56	17.90
16	WATER RESOURCES	41	69,354.43	69,354.43	0.00	0	0.00	0.00	0.00
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
18	DEFENCE PRODUCTION	1	210.00	200.00	-4.76	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	20	9,425.47	9,347.30	-0.83	0	0.00	0.00	0.00
21	HOME AFFAIRS	5	2,025.73	2,546.47	25.71	3	1,659.44	2,180.18	31.38
22	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	8.49
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	RENEWABLE ENERGY	1	271.90	365.00	34.24	1	271.90	365.00	34.24
Total		1526	23,74,450.13	25,91,823.45	9.15	313	5,32,394.28	7,77,168.27	45.98

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,269.00	0.50	1	6,840.00	7,500.00	168- 168
2	CIVIL AVIATION	25	16,322.76	17,572.54	7.66	2	2,525.00	3,677.00	24- 48
3	COAL	122	1,68,359.96	1,72,645.43	2.55	3	20,378.26	23,252.65	24- 132
4	FINANCE	3	778.04	831.04	6.81	0	0.00	0.00	0- 0
5	FERTILISERS	1	187.27	187.27	0.00	0	0.00	0.00	0- 0
6	MINES	7	8,585.77	8,585.77	0.00	0	0.00	0.00	0- 0
7	STEEL	9	30,334.19	30,334.19	0.00	0	0.00	0.00	0- 0
8	PETROLEUM	139	3,79,470.22	3,86,263.94	1.79	3	21,480.54	26,838.91	20- 32
9	POWER	78	2,15,233.13	2,35,941.73	9.62	12	51,034.42	66,506.02	12- 141
10	HEALTH AND FAMILY WELFARE	28	13,711.40	14,200.97	3.57	1	1,351.00	1,471.04	11- 11
11	RAILWAYS	173	4,74,776.22	6,19,569.99	30.50	65	97,064.36	1,85,007.40	3- 276
12	ROAD TRANSPORT AND HIGHWAYS	831	5,23,824.24	5,40,815.51	3.24	39	25,130.38	29,767.58	15- 105
13	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	3	14,043.62	14,043.62	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	28	2,84,811.01	3,05,228.48	7.17	2	33,909.00	46,331.22	45- 45
16	WATER RESOURCES	41	69,354.43	69,354.43	0.00	0	0.00	0.00	0- 0
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	210.00	200.00	-4.76	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	20	9,425.47	9,347.30	-0.83	0	0.00	0.00	0- 0
21	HOME AFFAIRS	5	2,025.73	2,546.47	25.71	3	1,659.44	2,180.18	11- 65
22	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37- 37
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	0- 0
Total		1526	23,74,450.13	25,91,823.45	9.15	132	2,66,145.40	3,97,710.00	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,269.00	14.16	3	27,271.00	43,799.00	84- 168
2	CIVIL AVIATION	25	15,984.85	17,572.54	9.93	5	3,592.30	5,216.27	24- 49
3	COAL	122	1,68,218.93	1,72,645.43	2.63	6	21,214.84	24,230.14	24- 132
4	FINANCE	3	786.27	831.04	5.69	1	209.00	262.00	36- 36
5	FERTILISERS	1	187.27	187.27	0.00	0	0.00	0.00	0- 0
6	MINES	7	7,333.99	8,585.77	17.07	3	4,992.00	6,303.23	33- 46
7	STEEL	9	23,919.19	30,334.19	26.82	1	15,525.00	21,940.00	94- 94
8	PETROLEUM	139	3,66,013.55	3,86,263.94	5.53	25	52,886.08	70,624.95	6- 146
9	POWER	78	1,82,940.83	2,35,941.73	28.97	22	73,662.78	1,26,624.66	9- 171
10	HEALTH AND FAMILY WELFARE	28	13,696.26	14,200.97	3.69	1	1,351.00	1,471.04	11- 11
11	RAILWAYS	173	3,72,761.45	6,19,569.99	66.21	86	1,26,859.22	2,63,046.48	3- 276
12	ROAD TRANSPORT AND HIGHWAYS	831	4,92,741.89	5,40,815.51	9.76	52	38,177.88	53,059.21	17- 125
13	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	3	14,013.36	14,043.62	0.22	1	431.16	461.42	17- 17
15	URBAN DEVELOPMENT	28	2,84,811.01	3,05,228.48	7.17	2	33,909.00	46,331.22	45- 45
16	WATER RESOURCES	41	23,466.28	69,354.43	195.55	6	11,730.79	57,372.71	18- 48
17	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	246.31	200.00	-18.80	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	20	9,449.72	9,347.30	-1.08	1	303.90	334.45	35- 35
21	HOME AFFAIRS	5	2,025.73	2,546.47	25.71	3	1,659.44	2,180.18	11- 65
22	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37- 37
23	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	0- 0
Total		1526	21,26,460.93	25,91,823.45	21.88	219	4,18,548.39	7,28,434.96	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

List of projects completed/dropped/Frozen during current month					Rs. 150		Crore and above	
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	
	HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1,718.00	09/2011	3,558.60	N.A.	3,496.57	
	PETROLEUM							
2	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	05/2016	406.00	10/2020	340.00	06/2022	314.00	
3	DOBHI-DURGAPUR PIPELINE PROJECT	03/2017	2,433.00	12/2020	2,433.00	08/2022	2,250.60	
4	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	09/2016	571.66	12/2019	510.00	08/2022	511.00	
5	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	07/2020	640.00	12/2021	640.00	07/2022	424.30	
6	LAB REVAMP AT GUJARAT REFINERY Central Sector Projects	10/2019	403.00	04/2022	403.00	N.A.	279.12	
	RAILWAYS							
7	BOWAICHANDI-ARAMBAGH	04/2010	267.37	N.A.	620.00	03/2025	42.11	
8	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	02/2012	550.00	03/2016	550.00	03/2016	0.00	
9	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	1,027.40	03/2003	2,373.00	03/2030	485.05	
	ROAD TRANSPORT AND HIGHWAYS							
10	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S EPC	10/2014	369.00	03/2018	369.00	03/2018	322.69	
11	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	08/2017	517.57	10/2018	423.93	06/2021	438.74	
12	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	02/2017	176.12	N.A.	176.12	04/2022	102.99	
13	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 EPC	06/2020	257.96	01/2022	257.96	01/2022	122.81	
14	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	02/2017	175.06	N.A.	175.06	04/2022	102.00	
15	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 PPP (BOT)	02/2009	1,693.75	08/2011	1,693.75	05/2022	2,848.49	

List of projects completed/dropped/Frozen during current month							Rs. 150	Core and above
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	

TABLE-14

List of projects added						Rs. 150		Core and above	(August 2022)
			Original		Anticipated				
Sl.No	Project	DOA	Cost	DOC	Cost	DOC			
	<u>COAL</u>								
1	SINGHORI DEEP OC Central Sector Projects	5/2022	421.84	3/2029	421.84	3/2029			
2	MAKARDHOKDA I EXPANSION OC Central Sector Projects	6/2022	497.06	3/2026	497.06	3/2026			
3	BHATADI EXPANSION OC Central Sector Projects	2/2020	729.86	3/2028	729.86	3/2028			
	<u>MINES</u>								
4	POTTANGI BAUXITE MINES Central Sector Projects	5/2018	1,437.00	12/2024	1,381.00	12/2024			
	<u>PETROLEUM</u>								
5	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI Central Sector Projects	5/2022	423.39	3/2024	423.39	3/2024			
6	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI Central Sector Projects	1/2022	389.00	9/2024	389.00	9/2024			
7	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT Central Sector Projects	1/2022	328.00	9/2024	328.00	9/2024			
	<u>POWER</u>								
8	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION Central Sector Projects	11/2018	173.94	11/2021	173.94	9/2022			

List of projects added Rs. 150 Crore and above					(August 2022)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
9	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH EPC	7/2015	197.16	10/2018	197.16	10/2018
10	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	167.28	4/2017	167.28	4/2017
11	DABOKA KATHKATI PACKAGE-6 EPC	9/2021	625.64	7/2024	625.64	7/2024
12	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 EPC	4/2022	170.95	7/2024	170.95	7/2024
13	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 EPC	2/2022	191.33	8/2022	191.33	8/2022
14	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR EPC	2/2022	184.15	8/2022	184.15	8/2022
15	IMPHAL - KHONGSANG PKG-4 EPC	8/2021	579.63	12/2023	579.63	12/2023
16	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 EPC	3/2022	215.27	7/2024	215.27	7/2024
17	DEVELOPMENT OF MULTIMODAL LOGISTICS PARK AT BANGALORE AND EXTERNAL CONNECTIVITY TO THE MULTI MODEL L EPC	6/2022	1,769.70	3/2025	1,769.70	3/2025
18	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00)	3/2016	429.52	8/2016	429.52	8/2016
19	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	323.98	9/2018	323.98	9/2018
20	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	256.66	/	256.66	3/2024
21	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH EPC	11/2021	223.35	2/2022	223.35	2/2022

TABLE-15

Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		5919	
Achieved up to month		2920	

TABLE-16

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(August 2022)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. AAI EPC	255.69	255.69	09/2021	03/2023	09/2023	6
	<u>COAL</u>						
2	MADHUBAND NLW WASHERY BCCL	289.45	302.00	05/2014	08/2022	09/2022	1
	<u>STEEL</u>						
3	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL SAIL	262.87	262.87	06/2019	08/2022	09/2022	1
4	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	21,940.00	05/2015	09/2022	03/2023	6
	<u>PETROLEUM</u>						
5	IRUGUR-DEVANGONTHI POL PIPELINE BPCL	678.00	1,472.00	02/2017	08/2022	09/2022	1
6	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR IOCL	1,823.00	3,027.90	03/2021	08/2022	10/2022	2
7	KOYALI AHMEDNAGAR SOLAPUR PIPELINE IOCL	1,945.00	2,145.00	02/2022	10/2022	12/2022	2
8	PARADIP SOMNATHPUR HALDIA PIPELINE IOCL	1,297.50	1,297.50	10/2021	10/2022	12/2022	2
9	HASSAN CHERLAPALLI LPG PIPELINE HPCL	2,166.38	2,166.38	06/2022	08/2022	10/2022	2
10	RUF PITCH LOADING GANTRY HPCL EPC	332.61	332.61	11/2022	12/2022	03/2023	3
11	MUZAFFARPUR-MOTIHARI LPG PIPELINE IOCL	403.00	403.00	08/2022	08/2022	12/2022	4
12	SULPHUR FORMING UNIT IN SRU HPCL EPC	210.94	210.94	08/2021	07/2022	12/2022	5
13	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA IOCL	14,810.00	14,810.00	04/2023	04/2023	07/2024	15
	<u>POWER</u>						
14	AMELIA COAL MINE THDCIL Central Sector Projects	2,104.21	1,587.16	09/2020	08/2022	09/2022	1
15	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT PGCIL	1,031.00	1,143.00	08/2021	09/2022	10/2022	1

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (August 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII PGCIL	379.95	379.95	12/2019	09/2022	11/2022	2
17	NAITWAR MORI HEP SJVN	648.33	947.89	12/2021	10/2022	12/2022	2
18	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA PGCIL	267.33	267.33	03/2022	09/2022	11/2022	2
19	BARH STPP(3X660MW) NTPC NTPC	8,692.97	21,312.11	10/2011	12/2023	03/2024	3
20	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO PGCIL	197.40	197.40	03/2018	09/2022	12/2022	3
21	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ PGCIL	322.30	322.30	02/2019	09/2022	12/2022	3
22	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	09/2022	12/2022	3
23	NOKHRA NTPC EPC	1,722.14	1,803.19	09/2021	10/2022	01/2023	3
24	CHHATTARGARH 150 MW NTPC EPC	599.99	599.99	07/2022	05/2023	08/2023	3
25	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD PGCIL PPP (BOT)	562.86	562.86	01/2021	09/2022	12/2022	3
26	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION PGCIL	241.38	241.38	11/2021	09/2022	12/2022	3
27	KALPI SOLAR POWER PROJECT NHPC Joint Venture	314.64	337.77	03/2022	09/2022	12/2022	3
28	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,998.00	11/2020	02/2023	06/2023	4
29	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) NTPC EPC	674.92	674.92	09/2022	03/2023	08/2023	5
30	BIKANER SOLAR POWER PROJECT SJVN EPC	5,491.89	6,023.89	05/2024	09/2023	05/2024	8
31	NORTH KARANPURA STPP (3X660 MW) NTPC	14,366.58	17,007.00	06/2019	01/2024	12/2024	11
	<u>HEALTH AND FAMILY WELFARE</u>						
32	AIIMS BILASPUR NBCC FOR HEALTH	1,351.00	1,471.04	09/2021	06/2022	08/2022	2
	<u>RAILWAYS</u>						

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (August 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
33	BOINCHI-SHAKTIGARH 3RD LINE ER	175.80	495.10	N.A.	08/2022	09/2022	1
34	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	37,012.26	11/2002	04/2023	06/2023	2
35	MADURAI-BODINAYAKKANUR SR	164.41	591.00	N.A.	07/2022	09/2022	2
36	SAMBALPUR - TITLAGARH - DOUBLING RVNL	948.04	2,009.00	03/2020	07/2022	09/2022	2
37	RAIPUR - TITLAGARH - DOUBLING RVNL	1,402.02	1,300.00	03/2020	07/2022	09/2022	2
38	PUNE-MIRAJ-LONDA (467 KM) CR	3,627.47	4,670.00	03/2024	03/2023	03/2024	12
39	AHMEDNAGAR-PARLI VAIJNATH(NL) CR CR	2,271.50	4,805.17	03/2021	03/2023	03/2025	24
40	KALYAN-KASARA 3RD LINE CR	792.89	1,387.52	03/2021	03/2023	03/2025	24
41	DAUND - MANMAD (236 KM) CR	1,876.00	2,081.27	03/2023	03/2023	03/2025	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
42	FOUR LANING OF SIMGA - SARAGAON NHAI	596.67	819.35	05/2018	07/2022	08/2022	1
43	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 NHIDCL	290.05	290.05	11/2017	08/2022	09/2022	1
44	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A MoRTH	188.80	188.80	05/2019	08/2022	09/2022	1
45	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 NHAI EPC	594.75	606.75	11/2019	11/2022	12/2022	1
46	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) NHAI	1,071.61	1,048.10	N.A.	07/2022	09/2022	2
47	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) NHAI	1,532.62	1,827.00	03/2021	06/2022	08/2022	2
48	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA MoRTH	214.23	214.23	08/2018	09/2022	11/2022	2
49	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T MoRTH	281.45	319.96	N.A.	07/2022	09/2022	2
50	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO MoRTH	423.79	423.79	01/2018	08/2022	10/2022	2
51	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 MoRTH EPC	319.68	404.10	N.A.	08/2022	11/2022	3

List of projects reporting additional delayed Rs. 150 Crore and above							(August 2022)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
52	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P MoRTH	178.85	225.06	05/2016	08/2022	11/2022	3
53	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C NHAI	1,184.71	1,310.00	03/2020	06/2022	09/2022	3
54	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) MoRTH	159.12	159.12	01/2016	06/2022	09/2022	3
55	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP MoRTH EPC	165.67	165.67	11/2015	06/2022	10/2022	4
56	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P MoRTH	553.30	587.41	05/2016	07/2022	11/2022	4
57	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM NHIDCL	284.09	284.09	04/2017	08/2022	12/2022	4
58	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV NHAI	894.00	929.32	04/2020	08/2022	12/2022	4
59	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER NHAI	946.00	1,046.56	06/2018	07/2022	12/2022	5
60	FOUR LANING WITH PS TALEBANI -SMBALPUR NHAI	752.28	752.28	N.A.	06/2022	11/2022	5
61	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS NHAI	809.07	1,065.70	N.A.	07/2022	12/2022	5
62	4-LANNING OF THALSERRY -MAHE BYPASS NHAI Central Sector Projects	1,124.11	1,309.79	09/2017	09/2022	03/2023	6
63	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) NHIDCL EPC	262.84	262.84	05/2023	05/2023	01/2024	8
64	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) NHAI	1,261.98	2,145.96	N.A.	06/2023	06/2024	12
	<u>URBAN DEVELOPMENT</u>						
65	AHMEDABAD METRO RAIL PROJECT PHASE 1 MEGA	10,773.00	12,925.22	12/2018	08/2022	09/2022	1
	<u>WATER RESOURCES</u>						

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (August 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
66	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH UPJalNigam	206.05	206.05	10/2021	07/2022	08/2022	1
67	I AND D AND STP AT CHAPPRA BUIDCO	236.15	236.15	12/2020	08/2022	10/2022	2
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
68	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR CPWD EDUCATION	392.51	392.51	06/2022	02/2023	04/2023	2
	<u>HOME AFFAIRS</u>						
69	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD FOR MHA	1,219.21	1,679.02	10/2019	09/2022	12/2022	3
70	NSG AT KOLKATA CPWD FOR MHA Central Sector Projects	162.88	210.83	04/2018	06/2023	09/2023	3
71	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI CPWD FOR MHA EPC	277.35	290.33	07/2022	03/2023	06/2023	3

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,326,09.00	1,33,269.00	78,003.54
CIVIL AVIATION	25	15,984.85	163,22.76	17,572.54	8,329.57
COAL	122	1,68,218.93	1,683,59.96	1,72,645.43	62,007.26
FINANCE	3	786.27	7,78.04	831.04	662.05
FERTILISERS	1	187.27	1,87.27	187.27	0.80
MINES	7	7,333.99	85,85.77	8,585.77	2,634.75
STEEL	9	23,919.19	303,34.19	30,334.19	23,716.27
PETROLEUM	139	3,66,013.55	3,794,70.22	3,86,263.94	1,36,450.20
POWER	78	1,82,940.83	2,152,33.13	2,35,941.73	1,39,404.28
HEALTH AND FAMILY WELFARE	28	13,696.26	137,11.40	14,200.97	10,357.53
RAILWAYS	173	3,72,761.45	4,747,76.22	6,19,569.99	3,43,528.75
ROAD TRANSPORT AND HIGHWAYS	831	4,92,741.89	5,238,24.24	5,40,815.51	3,21,001.00
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	2,160.50
TELECOMMUNICATIONS	3	14,013.36	140,43.62	14,043.62	21,826.52
URBAN DEVELOPMENT	28	2,84,811.01	2,848,11.01	3,05,228.48	1,66,037.24
WATER RESOURCES	41	23,466.28	693,54.43	69,354.43	25,328.42
SOCIAL JUSTICE	1	170.99	1,70.99	170.99	73.80
DEFENCE PRODUCTION	1	246.31	2,10.00	200.00	181.63
COMMERCE	1	302.64	3,02.64	302.64	30.00
DEPARTMENT OF HIGHER EDUCATION	20	9,449.72	94,25.47	9,347.30	4,408.99
HOME AFFAIRS	5	2,025.73	20,25.73	2,546.47	1,391.41
DPIIT	2	24,857.00	248,57.00	25,262.00	12,713.14
DONER	1	151.33	1,51.33	151.33	148.33
RENEWABLE ENERGY	1	271.90	2,71.90	365.00	249.96
Grand total	1526	21,26,460.93	23,74,450.13	25,91,823.45	13,60,645.94

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	66	1,12,846.32	1,64,854.74	46.09	7	39,091.22	91,655.24	17 - 216
2	ARUNACHAL PRADESH	42	23,572.02	37,508.36	59.12	4	6,882.14	20,760.58	64 - 155
3	ASSAM	50	51,277.81	61,098.00	19.15	9	6,605.26	10,649.08	34 - 89
4	BIHAR	79	97,760.92	1,21,511.70	24.29	12	15,592.91	33,619.77	36 - 149
5	GOA	11	5,588.46	5,629.50	0.73	1	303.90	334.45	35 - 35
6	GUJARAT	59	1,08,793.95	1,22,941.89	13.00	13	30,584.05	44,602.52	9 - 144
7	HARYANA	30	58,831.75	61,266.98	4.14	4	3,219.77	3,830.38	28 - 41
8	HIMACHAL PRADESH	19	22,091.98	33,807.28	53.03	3	6,205.05	13,477.58	11 - 171
9	JAMMU AND KASHMIR	27	47,696.67	82,076.18	72.08	1	2,500.00	37,012.26	247 - 247
10	KARNATAKA	50	81,951.07	90,498.98	10.43	8	5,924.50	8,784.25	7 - 129
11	KERALA	15	15,893.03	19,006.36	19.59	3	2,843.17	4,053.03	44 - 66
12	MADHYA PRADESH	67	60,727.92	68,770.29	13.24	11	13,261.98	20,911.39	21 - 55
13	MAHARASHTRA	224	1,89,111.93	2,11,359.02	11.76	19	48,090.43	69,626.78	9 - 228
14	MANIPUR	28	12,848.47	22,717.09	76.81	1	4,454.17	14,322.79	153 - 153
15	MEGHALAYA	13	5,093.36	12,456.56	144.56	0	0.00	0.00	-
16	MIZORAM	25	12,450.29	17,404.99	39.80	1	2,393.47	6,527.45	117 - 117
17	NAGALAND	37	12,630.26	17,014.38	34.71	1	2,326.52	6,663.00	132 - 132
18	ODISHA	79	1,15,014.68	1,24,251.75	8.03	17	19,377.91	28,024.63	6 - 201
19	PUNJAB	23	17,390.42	18,541.79	6.62	0	0.00	0.00	-
20	RAJASTHAN	41	54,162.68	59,548.71	9.94	2	13,214.00	18,008.32	32 - 84
21	SIKKIM	21	14,350.32	21,030.43	46.55	1	1,339.48	7,876.92	96 - 96
22	TAMIL NADU	62	2,02,260.40	2,23,144.21	10.33	9	12,292.60	22,251.10	33 - 168
23	TRIPURA	18	4,666.82	4,808.15	3.03	1	569.63	708.73	30 - 30
24	UTTAR PRADESH	93	1,24,370.16	1,39,066.47	11.82	20	32,870.42	43,651.63	9 - 66
25	WEST BENGAL	62	63,606.38	75,703.23	19.02	16	17,843.75	24,636.21	18 - 141
26	A & N ISLANDS	10	3,043.24	3,314.60	8.92	2	655.03	945.73	35 - 49
27	DELHI	27	81,077.58	84,083.09	3.71	4	6,573.36	7,498.56	11 - 38
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATISGARH	40	76,020.96	1,02,152.00	34.37	9	26,195.99	36,373.79	33 - 94
30	JHARKHAND	48	73,691.13	80,705.52	9.52	5	15,718.07	18,627.52	13 - 100
31	UTTARAKHAND	29	35,446.38	54,833.80	54.70	5	23,991.39	41,395.84	3 - 141
32	TELANGANA	44	32,353.76	34,700.38	7.25	3	12,392.14	14,198.00	31 - 180
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	27 - 27
34	MULTI STATE	78	3,07,011.58	4,13,054.73	34.54	26	44,889.81	76,927.10	12 - 276
Total		1526	21,26,460.93	25,91,823.45	21.88	219	4,18,548.39	7,28,434.96	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	145	7
2	RAILWAYS	118	7
3	PETROLEUM	58	6
4	POWER	39	7
5	COAL	34	0
6	URBAN DEVELOPMENT	22	1
7	ATOMIC ENERGY	5	0
8	CIVIL AVIATION	5	0
9	STEEL	4	1
10	HEALTH AND FAMILY WELFARE	3	1
11	MINES	2	0
12	DPIIT	2	0
13	SHIPPING AND PORTS	1	0
14	TELECOMMUNICATIONS	1	0
15	WATER RESOURCES	1	0
16	HOME AFFAIRS	1	1
	Total	441	31

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2022-2023				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2022			
	<u>POWER</u>			
1	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000066]	11,130.19	08/2013	12,394.95
2	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000188]	1,394.52	05/2017	587.21
3	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000312]	2,578.47	12/2020	1,797.70
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
4	4 LANING OF NAGPUR-BETUL PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000155]	2,498.76	08/2014	2,531.46
5	NASHRI- CHANANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000162]	2,159.00	06/2015	4,729.68
6	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000233]	1,266.60	09/2016	1,446.45
7	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000547]	1,404.50	-	2,977.58
8	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000599]	2,016.00	04/2019	3,026.14
9	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000672]	2,064.99	03/2020	2,118.76
	May,2022			
	<u>POWER</u>			
10	BRBCL-NABINAGAR TPP- JV (4X250 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000190]	5,353.00	07/2012	8,839.26
11	NPGCPL-NABINAGAR STPP - JV (3X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000192]	12,964.60	05/2018	15,763.67
12	PAKRI BARWADIH COAL MINING PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000225]	4,237.96	10/2017	3,409.94
13	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL (NATIONAL THERMAL POWER CORPORATION) - [N18000276]	1,885.13	12/2018	2,050.89
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
14	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000554]	870.00	03/2019	283.38

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	June,2022			
	<u>PETROLEUM</u>			
15	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000359]	3,660.71	05/2021	3,637.73
	<u>RAILWAYS</u>			
16	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) (SOUTHERN RAILWAY) - [220100262]	303.98	03/2020	727.62
17	YELAHANKA-PENUKONDA (SOUTH WESTERN RAILWAY) - [N22000328]	860.43	03/2020	1,062.99
18	DUVVADA-VIJAYAWADA (SOUTH CENTRAL RAILWAY) - [N22000366]	3,873.07	-	0.07
19	DIGARU-HOJAI (102 KM) (NORTH EAST FRONTIER RAILWAY) - [N22000389]	870.96	03/2021	1,829.49
20	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT (SOUTH EAST CENTRAL RAILWAY) - [N22000438]	585.93	02/2019	1,222.59
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
21	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000125]	1,509.10	09/2012	3,684.44
22	MUZAFFARNAGAR-HARIDWAR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000201]	754.00	03/2013	1,364.18
23	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000443]	991.59	06/2018	1,154.00
24	FOUR LANING OF YADGIRI - WARANGAL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000486]	1,423.96	11/2018	975.10
25	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 ((NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000563]	1,668.00	-	946.08
26	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000663]	1,989.00	03/2020	772.56
27	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000793]	925.40	-	1,136.70
	July,2022			
	<u>POWER</u>			
28	SAMBHU KI BHURJ SOLAR 250 MW EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000285]	1,522.71	09/2021	1,315.75
29	FATEHGARH SOLAR 296MW EPC(NATIONAL THERMAL POWER CORPORATION) - [N18000289]	1,749.31	09/2021	1,441.61
	August,2022			
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
30	DOBHI-DURGAPUR PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000273]	2,433.00	12/2020	2,250.60
	<u>HEAVY INDUSTRY</u>			
31	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) (NATRIIP IMPLEMENTATION SOCIETY) - [N20000001]	1,718.00	09/2011	3,496.57
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
32	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000131]	1,693.75	08/2011	2,848.49

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2022-2023				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2022			
	<u>STEEL</u>			
1	SCREENING PLANT III AT KIRANDUL (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000128]	2,092.97	08/2024	0.00
	<u>RAILWAYS</u>			
2	ANGAMALI-SABARIMALA (N.L.)(SR) (SOUTHERN RAILWAY) - [220100252]	1,566.00	-	264.30
3	DEOGHAR - SULTANGANJ (INL), ER (EASTERN RAILWAYS) - [220100273]	607.09	02/2013	633.43
4	BANGLORE - SATYAMANGALAM (NL)(SWR) (SOUTH WESTERN RAILWAY) - [220100274]	1,382.78	03/2002	7.35
5	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP (NORTH EASTERN RAILWAY) - [N22000130]	307.00	-	0.00
6	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) (WESTERN RAILWAY) - [N22000143]	320.66	03/2019	540.09
7	BIHTA-AURANGABAD (NL) (EAST CENTRAL RAILWAYS) - [N22000170]	326.20	-	2.88
8	CHHAPRA-MUZAFFARPUR (NL) (EAST CENTRAL RAILWAYS) - [N22000172]	378.56	-	387.43
9	DIMAPUR-TIZIT NL (NORTH EAST FRONTIER RAILWAY) - [N22000196]	4,274.00	03/2020	0.00
10	MANUGURU-RAMAGUNDAM (SOUTH CENTRAL RAILWAY) - [N22000259]	1,112.00	-	0.92
11	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I (SOUTH CENTRAL RAILWAY) - [N22000288]	2,132.77	03/2014	347.10
12	INDORE - MANMAD VIA MALEGAON (368 KM) (CENTRAL RAILWAYS) - [N22000353]	9,968.00	03/2024	0.00
13	PUNE-NASIK (265 KM) (CENTRAL RAILWAYS) - [N22000354]	2,425.00	03/2024	0.00
14	VAIBHAVWADI -KOLHAPUR (107 KM) (CENTRAL RAILWAYS) - [N22000355]	2,750.00	03/2024	0.00
15	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. (NORTH EASTERN RAILWAY) - [N22000457]	1,900.00	01/2022	0.00
16	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE (NORTH EASTERN RAILWAY) - [N22000460]	1,343.00	01/2018	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	FOUR LANING OF PATNA - GAYA - DHOBI SECTION OF NH-83 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000355]	1,027.00	04/2018	0.00
18	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 323.00 TO KM 355.00 (SAPNA TO PADRA SECTI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000818]	1,671.41	-	0.00

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during

2022-2023

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
19	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 292.00 TO KM 323.00 (MANUBAR TO SANPA SEC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000819]	1,431.74	-	0.00

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	438
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	2
No of Projects in Current Month	441

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	229 (51.93%)	3 (.68%)	74 (16.78%)	45 (10.20%)	90 (20.41%)	441
Latest Approved (Date)	175 (39.68%)	5 (1.13%)	135 (30.61%)	36 (8.16%)	90 (20.41%)	441

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	326	13,75,404.53	15,37,548.29	7,27,386.82	47.30	1,62,143.76	11.80
Project with Revision in Cost	115	5,38,512.69	5,90,562.49	3,93,207.77	66.60	52,049.80	9.70
Total	441	19,13,917.22	21,28,110.78	11,20,594.59	52.66	2,14,193.56	11.19
Original Cost of All Projects							
Original Cost	441	16,73,812.55	21,28,110.78	11,20,594.59	52.66	4,54,298.23	27.14

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	229	7,86,428.32	10,82,797.81	6,61,896.60	61.10	2,96,369.49	37.69
Latest Approved (RCE)	175	6,37,069.19	7,60,384.22	4,64,766.88	61.10	1,23,315.03	19.36

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	31	1,16,943.88	1,85,826.74	1,39,788.12	75.20	68,882.86	58.90
Total	31	1,16,943.88	1,85,826.74	1,39,788.12	75.22	68,882.86	58.90

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 1000 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,269.00	14.16	3	27,271.00	43,799.00	60.61
2	CIVIL AVIATION	5	7,613.90	8,765.90	15.13	2	2,525.00	3,677.00	45.62
3	COAL	34	1,25,582.49	1,30,141.72	3.63	3	25,805.84	30,365.07	17.67
4	MINES	2	5,540.00	6,436.00	16.17	1	4,103.00	5,055.00	23.20
5	STEEL	4	21,558.98	27,973.98	29.76	1	15,525.00	21,940.00	41.32
6	PETROLEUM	58	3,31,821.50	3,51,042.43	5.79	16	61,906.61	85,674.54	38.39
7	POWER	39	1,66,123.56	2,18,485.46	31.52	16	75,914.52	1,28,793.47	69.66
8	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.04	2.62	1	1,351.00	1,471.04	8.89
9	RAILWAYS	118	3,42,359.50	5,86,710.46	71.37	92	1,80,691.74	4,25,688.73	135.59
10	ROAD TRANSPORT AND HIGHWAYS	145	2,14,725.95	2,57,498.05	19.92	65	81,909.02	1,26,399.00	54.32
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	7	1,14,321.56	1,34,795.56	17.91
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
15	HOME AFFAIRS	1	1,219.21	1,679.02	37.71	1	1,219.21	1,679.02	37.71
16	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	8.49
Total		441	16,73,812.55	21,28,110.78	27.14	210	6,07,467.54	10,70,064.30	76.15

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	18	93,955.97	1,46,015.65	55.41	9	44,306.33	99,338.01	124.21
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	2	8,264.33	22,029.33	166.56
3	ASSAM	9	34,555.07	43,143.49	24.85	5	16,954.52	26,712.94	57.56
4	BIHAR	25	73,609.59	95,173.80	29.30	13	30,003.94	52,203.65	73.99
5	GUJARAT	23	86,838.75	1,00,505.66	15.74	11	32,261.38	46,587.34	44.41
6	HARYANA	13	51,014.43	51,953.20	1.84	8	9,730.19	10,668.96	9.65
7	HIMACHAL PRADESH	10	18,720.95	30,436.25	62.58	5	9,650.78	21,366.08	121.39
8	JAMMU AND KASHMIR	13	41,767.84	76,147.35	82.31	1	2,500.00	37,012.26	1380.49
9	KARNATAKA	20	70,060.07	78,338.37	11.82	12	17,935.83	26,214.13	46.16
10	KERALA	7	11,881.63	14,904.84	25.44	6	10,449.73	13,472.94	28.93
11	MADHYA PRADESH	17	37,488.68	44,494.72	18.69	7	11,608.43	19,131.52	64.81
12	MAHARASHTRA	39	1,13,200.73	1,38,716.38	22.54	19	65,111.59	90,694.63	39.29
13	MANIPUR	1	4,454.17	14,322.79	221.56	1	4,454.17	14,322.79	221.56
14	MEGHALAYA	1	906.46	8,324.28	818.33	1	906.46	8,324.28	818.33
15	MIZORAM	1	2,393.47	6,527.45	172.72	1	2,393.47	6,527.45	172.72
16	NAGALAND	1	2,326.52	6,663.00	186.39	1	2,326.52	6,663.00	186.39
17	ODISHA	37	95,429.38	1,03,286.41	8.23	11	18,569.16	26,482.19	42.61
18	PUNJAB	7	8,647.82	9,958.16	15.15	2	2,557.95	3,868.29	51.23
19	RAJASTHAN	17	42,922.04	47,915.51	11.63	2	13,284.17	18,277.64	37.59
20	SIKKIM	2	7,087.52	13,624.96	92.24	1	1,339.48	7,876.92	488.06
21	TAMIL NADU	28	1,83,861.78	2,04,908.53	11.45	13	40,166.77	61,608.52	53.38
22	UTTAR PRADESH	38	1,01,053.19	1,15,582.36	14.38	20	39,711.12	54,612.49	37.52
23	WEST BENGAL	19	47,030.89	58,626.37	24.66	10	23,280.95	34,892.43	49.88
24	DELHI	7	74,527.86	76,909.38	3.20	3	44,577.21	47,037.93	5.52
25	CHHATISGARH	17	64,949.58	90,625.43	39.53	7	25,757.63	51,535.50	100.08
26	JHARKHAND	14	58,448.62	65,336.45	11.78	4	16,682.83	23,570.66	41.29
27	UTTARAKHAND	9	28,781.19	47,795.15	66.06	7	25,870.41	44,884.37	73.50
28	TELANGANA	3	16,188.46	17,677.00	9.20	2	11,759.46	13,248.00	12.66
29	MULTI STATE	42	2,91,726.97	3,96,449.92	35.90	26	75,052.73	1,80,900.05	141.03
Total		441	16,73,812.55	21,28,110.78	27.14	210	6,07,467.54	10,70,064.30	76.15

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,269.00	14.16	4	67,120.00	83,648.00	36 - 168
2	CIVIL AVIATION	5	7,613.90	8,765.90	15.13	5	7,613.90	8,765.90	12 - 48
3	COAL	34	1,25,582.49	1,30,141.72	3.63	6	25,542.64	28,028.19	12 - 61
4	MINES	2	5,540.00	6,436.00	16.17	1	4,103.00	5,055.00	33 - 33
5	STEEL	4	21,558.98	27,973.98	29.76	3	19,466.01	25,881.01	13 - 94
6	PETROLEUM	58	3,31,821.50	3,51,042.43	5.79	37	1,54,025.69	1,67,500.10	2 - 146
7	POWER	39	1,66,123.56	2,18,485.46	31.52	29	1,28,406.42	1,80,236.32	2 - 171
8	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.04	2.62	1	1,351.00	1,471.04	11 - 11
9	RAILWAYS	118	3,42,359.50	5,86,710.46	71.37	89	1,62,351.79	2,95,048.47	3 - 276
10	ROAD TRANSPORT AND HIGHWAYS	145	2,14,725.95	2,57,498.05	19.92	39	55,395.21	67,505.46	17 - 125
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	-
13	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	12	1,44,909.41	1,57,252.43	3 - 49
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	48 - 48
15	HOME AFFAIRS	1	1,219.21	1,679.02	37.71	1	1,219.21	1,679.02	38 - 38
16	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37 - 37
Total		441	16,73,812.55	21,28,110.78	27.14	229	7,86,428.32	10,82,797.81	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	93,955.97	1,46,015.65	55.41	11	81,796.25	1,31,278.62	17 - 216
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	9	34,555.07	43,143.49	24.85	4	4,588.52	7,744.94	36 - 89
4	BIHAR	25	73,609.59	95,173.80	29.30	13	36,202.30	53,596.43	15 - 149
5	GUJARAT	23	86,838.75	1,00,505.66	15.74	10	41,424.50	55,296.85	3 - 144
6	HARYANA	13	51,014.43	51,953.20	1.84	4	7,301.66	7,581.66	7 - 41
7	HIMACHAL PRADESH	10	18,720.95	30,436.25	62.58	4	8,690.98	15,963.51	11 - 171
8	JAMMU AND KASHMIR	13	41,767.84	76,147.35	82.31	5	16,018.45	50,530.71	48 - 247
9	KARNATAKA	20	70,060.07	78,338.37	11.82	9	38,922.69	41,348.30	4 - 129
10	KERALA	7	11,881.63	14,904.84	25.44	3	2,843.17	4,053.03	44 - 66
11	MADHYA PRADESH	17	37,488.68	44,494.72	18.69	14	33,415.10	40,421.14	12 - 116
12	MAHARASHTRA	39	1,13,200.73	1,38,716.38	22.54	21	68,371.08	89,257.06	9 - 228
13	MANIPUR	1	4,454.17	14,322.79	221.56	1	4,454.17	14,322.79	153 - 153
14	MEGHALAYA	1	906.46	8,324.28	818.33	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	6,527.45	172.72	1	2,393.47	6,527.45	117 - 117
16	NAGALAND	1	2,326.52	6,663.00	186.39	1	2,326.52	6,663.00	132 - 132
17	ODISHA	37	95,429.38	1,03,286.41	8.23	20	43,303.06	50,656.87	10 - 201
18	PUNJAB	7	8,647.82	9,958.16	15.15	1	1,069.59	1,069.59	38 - 38
19	RAJASTHAN	17	42,922.04	47,915.51	11.63	9	23,265.78	28,024.78	2 - 84
20	SIKKIM	2	7,087.52	13,624.96	92.24	2	7,087.52	13,624.96	16 - 96
21	TAMIL NADU	28	1,83,861.78	2,04,908.53	11.45	14	63,419.46	72,617.70	2 - 168
22	UTTAR PRADESH	38	1,01,053.19	1,15,582.36	14.38	20	74,219.14	84,613.63	5 - 54
23	WEST BENGAL	19	47,030.89	58,626.37	24.66	10	26,761.59	33,077.05	5 - 141
24	DELHI	7	74,527.86	76,909.38	3.20	5	33,248.86	34,034.47	6 - 38
25	CHHATISGARH	17	64,949.58	90,625.43	39.53	7	28,310.02	37,913.28	13 - 94
26	JHARKHAND	14	58,448.62	65,336.45	11.78	5	37,023.06	39,663.48	24 - 74
27	UTTARAKHAND	9	28,781.19	47,795.15	66.06	5	24,726.84	41,831.73	3 - 141
28	TELANGANA	3	16,188.46	17,677.00	9.20	2	11,759.46	13,248.00	31 - 180
29	MULTI STATE	42	2,91,726.97	3,96,449.92	35.90	27	57,199.75	87,844.35	7 - 276
Total		441	16,73,812.55	21,28,110.78	27.14	229	7,86,428.32	10,82,797.81	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

Extent of time overrun in projects with respect to latest schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,269.00	0.50	4	82,988.00	83,648.00	36 - 168
2	CIVIL AVIATION	5	7,613.90	8,765.90	15.13	2	2,525.00	3,677.00	24 - 48
3	COAL	34	1,25,582.61	1,30,141.72	3.63	6	25,542.64	28,028.19	12 - 61
4	MINES	2	6,436.00	6,436.00	0.00	0	0.00	0.00	-
5	STEEL	4	27,973.98	27,973.98	0.00	2	3,941.01	3,941.01	13 - 74
6	PETROLEUM	58	3,44,573.43	3,51,042.43	1.88	15	69,549.97	74,885.97	0 - 67
7	POWER	39	1,98,291.02	2,18,485.46	10.18	21	1,22,244.25	1,36,865.75	0 - 149
8	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.04	2.62	1	1,351.00	1,471.04	11 - 11
9	RAILWAYS	118	4,44,008.37	5,86,710.46	32.14	74	1,38,770.58	2,23,525.04	3 - 276
10	ROAD TRANSPORT AND HIGHWAYS	145	2,40,420.78	2,57,498.05	7.10	40	66,245.32	67,222.97	0 - 116
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	-
13	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	8	1,17,919.21	1,30,262.23	3 - 49
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	-
15	HOME AFFAIRS	1	1,219.21	1,679.02	37.71	1	1,219.21	1,679.02	38 - 38
16	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37 - 37
Total		441	19,13,917.22	21,28,110.78	11.19	175	6,37,069.19	7,60,384.22	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,269.00	0.50	1	6,840.00	7,500.00	9.65
2	CIVIL AVIATION	5	7,613.90	8,765.90	15.13	2	2,525.00	3,677.00	45.62
3	COAL	34	1,25,582.61	1,30,141.72	3.63	3	25,805.84	30,365.07	17.67
4	MINES	2	6,436.00	6,436.00	0.00	0	0.00	0.00	0.00
5	STEEL	4	27,973.98	27,973.98	0.00	0	0.00	0.00	0.00
6	PETROLEUM	58	3,44,573.43	3,51,042.43	1.88	2	33,294.00	45,232.00	35.86
7	POWER	39	1,98,291.02	2,18,485.46	10.18	12	52,454.06	73,165.55	39.49
8	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.04	2.62	1	1,351.00	1,471.04	8.89
9	RAILWAYS	118	4,44,008.37	5,86,710.46	32.14	80	1,75,288.94	3,18,637.06	81.78
10	ROAD TRANSPORT AND HIGHWAYS	145	2,40,420.78	2,57,498.05	7.10	36	49,621.13	75,303.81	51.76
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	7	1,14,321.56	1,34,795.56	17.91
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
15	HOME AFFAIRS	1	1,219.21	1,679.02	37.71	1	1,219.21	1,679.02	37.71
16	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	8.49
Total		441	19,13,917.22	21,28,110.78	11.19	146	4,67,493.74	6,97,004.11	49.09

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,32,609.00	1,33,269.00	0.50	1	6,840.00	7,500.00	168- 168
2	CIVIL AVIATION	5	7,613.90	8,765.90	15.13	2	2,525.00	3,677.00	24- 48
3	COAL	34	1,25,582.61	1,30,141.72	3.63	2	19,898.73	22,384.28	24- 60
4	MINES	2	6,436.00	6,436.00	0.00	0	0.00	0.00	0- 0
5	STEEL	4	27,973.98	27,973.98	0.00	0	0.00	0.00	0- 0
6	PETROLEUM	58	3,44,573.43	3,51,042.43	1.88	1	20,928.00	26,264.00	32- 32
7	POWER	39	1,98,291.02	2,18,485.46	10.18	10	50,199.92	65,338.47	14- 141
8	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.04	2.62	1	1,351.00	1,471.04	11- 11
9	RAILWAYS	118	4,44,008.37	5,86,710.46	32.14	51	90,980.43	1,76,231.91	3- 276
10	ROAD TRANSPORT AND HIGHWAYS	145	2,40,420.78	2,57,498.05	7.10	9	12,296.31	14,634.14	17- 105
11	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	2	33,909.00	46,331.22	45- 45
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
15	HOME AFFAIRS	1	1,219.21	1,679.02	37.71	1	1,219.21	1,679.02	38- 38
16	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37- 37
Total		441	19,13,917.22	21,28,110.78	11.19	81	2,44,920.60	3,70,689.08	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,33,269.00	14.16	3	27,271.00	43,799.00	84- 168
2	CIVIL AVIATION	5	7,613.90	8,765.90	15.13	2	2,525.00	3,677.00	24- 48
3	COAL	34	1,25,582.49	1,30,141.72	3.63	2	19,898.73	22,384.28	24- 60
4	MINES	2	5,540.00	6,436.00	16.17	1	4,103.00	5,055.00	33- 33
5	STEEL	4	21,558.98	27,973.98	29.76	1	15,525.00	21,940.00	94- 94
6	PETROLEUM	58	3,31,821.50	3,51,042.43	5.79	14	48,717.34	65,568.75	10- 146
7	POWER	39	1,66,123.56	2,18,485.46	31.52	15	70,422.63	1,22,769.58	14- 171
8	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.04	2.62	1	1,351.00	1,471.04	11- 11
9	RAILWAYS	118	3,42,359.50	5,86,710.46	71.37	69	1,18,974.54	2,52,168.24	3- 276
10	ROAD TRANSPORT AND HIGHWAYS	145	2,14,725.95	2,57,498.05	19.92	19	24,212.05	36,322.30	17- 125
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	13,334.00	0.00	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	2	33,909.00	46,331.22	45- 45
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	48- 48
15	HOME AFFAIRS	1	1,219.21	1,679.02	37.71	1	1,219.21	1,679.02	38- 38
16	DPIIT	2	24,857.00	25,262.00	1.63	1	4,773.00	5,178.00	37- 37
Total		441	16,73,812.55	21,28,110.78	27.14	132	3,83,052.54	6,83,892.30	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

<u>List of projects completed/dropped/Frozen during current month</u>					Rs. 1000		Crore and above	
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	
	<u>HEAVY INDUSTRY</u>							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1,718.00	09/2011	3,558.60	N.A.	3,496.57	
	<u>PETROLEUM</u>							
2	DOBHI-DURGAPUR PIPELINE PROJECT	03/2017	2,433.00	12/2020	2,433.00	08/2022	2,250.60	
	<u>RAILWAYS</u>							
3	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	1,027.40	03/2003	2,373.00	03/2030	485.05	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
4	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 PPP (BOT)	02/2009	1,693.75	08/2011	1,693.75	05/2022	2,848.49	

TABLE-32

List of projects added Rs. 1000 Crore and above					(August 2022)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>MINES</u>					
1	POTTANGI BAUXITE MINES Central Sector Projects	5/2018	1,437.00	12/2024	1,381.00	12/2024
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
2	DEVELOPMENT OF MULTIMODAL LOGISTICS PARK AT BANGALORE AND EXTERNAL CONNECTIVITY TO THE MULTI MODEL L EPC	6/2022	1,769.70	3/2025	1,769.70	3/2025

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2780	
Achieved up to month	1681	

TABLE-34

List of projects reporting additional delayed Rs. 1000 Crore and above							(August 2022)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>STEEL</u>						
1	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	21,940.00	05/2015	09/2022	03/2023	6
	<u>PETROLEUM</u>						
2	IRUGUR-DEVANGONTHI POL PIPELINE BPCL	678.00	1,472.00	02/2017	08/2022	09/2022	1
3	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR IOCL	1,823.00	3,027.90	03/2021	08/2022	10/2022	2
4	KOYALI AHMEDNAGAR SOLAPUR PIPELINE IOCL	1,945.00	2,145.00	02/2022	10/2022	12/2022	2
5	PARADIP SOMNATHPUR HALDIA PIPELINE IOCL	1,297.50	1,297.50	10/2021	10/2022	12/2022	2
6	HASSAN CHERLAPALLI LPG PIPELINE HPCL	2,166.38	2,166.38	06/2022	08/2022	10/2022	2
7	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA IOCL	14,810.00	14,810.00	04/2023	04/2023	07/2024	15
	<u>POWER</u>						
8	AMELIA COAL MINE THDCIL Central Sector Projects	2,104.21	1,587.16	09/2020	08/2022	09/2022	1
9	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT PGCIL	1,031.00	1,143.00	08/2021	09/2022	10/2022	1
10	BARH STPP(3X660MW) NTPC	8,692.97	21,312.11	10/2011	12/2023	03/2024	3
11	NOKHRA NTPC EPC	1,722.14	1,803.19	09/2021	10/2022	01/2023	3
12	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,998.00	11/2020	02/2023	06/2023	4
13	BIKANER SOLAR POWER PROJECT SJVN EPC	5,491.89	6,023.89	05/2024	09/2023	05/2024	8
14	NORTH KARANPURA STPP (3X660 MW) NTPC	14,366.58	17,007.00	06/2019	01/2024	12/2024	11
	<u>HEALTH AND FAMILY WELFARE</u>						
15	AIIMS BILASPUR NBCC FOR HEALTH	1,351.00	1,471.04	09/2021	06/2022	08/2022	2
	<u>RAILWAYS</u>						

List of projects reporting additional delayed Rs. 1000 Crore and above (August 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	37,012.26	11/2002	04/2023	06/2023	2
17	SAMBALPUR - TITLAGARH - DOUBLING RVNL	948.04	2,009.00	03/2020	07/2022	09/2022	2
18	RAIPUR - TITLAGARH - DOUBLING RVNL	1,402.02	1,300.00	03/2020	07/2022	09/2022	2
19	PUNE-MIRAJ-LONDA (467 KM) CR	3,627.47	4,670.00	03/2024	03/2023	03/2024	12
20	AHMEDNAGAR-PARLI VAIJNATH(NL) CR CR	2,271.50	4,805.17	03/2021	03/2023	03/2025	24
21	KALYAN-KASARA 3RD LINE CR	792.89	1,387.52	03/2021	03/2023	03/2025	24
22	DAUND - MANMAD (236 KM) CR	1,876.00	2,081.27	03/2023	03/2023	03/2025	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
23	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) NHAI	1,071.61	1,048.10	N.A.	07/2022	09/2022	2
24	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) NHAI	1,532.62	1,827.00	03/2021	06/2022	08/2022	2
25	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C NHAI	1,184.71	1,310.00	03/2020	06/2022	09/2022	3
26	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER NHAI	946.00	1,046.56	06/2018	07/2022	12/2022	5
27	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS NHAI	809.07	1,065.70	N.A.	07/2022	12/2022	5
28	4-LANNING OF THALSERRY -MAHE BYPASS NHAI Central Sector Projects	1,124.11	1,309.79	09/2017	09/2022	03/2023	6
29	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) NHAI	1,261.98	2,145.96	N.A.	06/2023	06/2024	12
	<u>URBAN DEVELOPMENT</u>						
30	AHMEDABAD METRO RAIL PROJECT PHASE 1 MEGA	10,773.00	12,925.22	12/2018	08/2022	09/2022	1
	<u>HOME AFFAIRS</u>						
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD FOR MHA	1,219.21	1,679.02	10/2019	09/2022	12/2022	3

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above (August 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)

TABLE-35

<u>Sector wise analysis of projects</u> Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,326,09.00	1,33,269.00	78,003.54
CIVIL AVIATION	5	7,613.90	76,13.90	8,765.90	3,287.72
COAL	34	1,25,582.49	1,255,82.61	1,30,141.72	48,754.61
MINES	2	5,540.00	64,36.00	6,436.00	1,820.63
STEEL	4	21,558.98	279,73.98	27,973.98	23,107.60
PETROLEUM	58	3,31,821.50	3,445,73.43	3,51,042.43	1,21,986.52
POWER	39	1,66,123.56	1,982,91.02	2,18,485.46	1,31,215.90
HEALTH AND FAMILY WELFARE	3	4,583.00	45,83.00	4,703.04	2,133.71
RAILWAYS	118	3,42,359.50	4,440,08.37	5,86,710.46	3,26,139.10
ROAD TRANSPORT AND HIGHWAYS	145	2,14,725.95	2,404,20.78	2,57,498.05	1,61,276.96
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	2,160.50
TELECOMMUNICATIONS	1	13,334.00	133,34.00	13,334.00	21,545.00
URBAN DEVELOPMENT	22	2,82,232.24	2,822,32.24	3,02,627.04	1,64,875.57
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	20,538.05
HOME AFFAIRS	1	1,219.21	12,19.21	1,679.02	1,036.04
DPIIT	2	24,857.00	248,57.00	25,262.00	12,713.14
Grand total	441	16,73,812.55	19,13,917.22	21,28,110.78	11,20,594.59


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	93,955.97	1,46,015.65	55.41	6	38,514.74	90,969.11	17 - 216
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	9	34,555.07	43,143.49	24.85	4	4,588.52	7,744.94	36 - 89
4	BIHAR	25	73,609.59	95,173.80	29.30	7	13,385.74	30,779.87	36 - 149
5	GUJARAT	23	86,838.75	1,00,505.66	15.74	8	27,999.18	41,871.53	12 - 144
6	HARYANA	13	51,014.43	51,953.20	1.84	1	2,128.72	2,408.72	41 - 41
7	HIMACHAL PRADESH	10	18,720.95	30,436.25	62.58	3	6,205.05	13,477.58	11 - 171
8	JAMMU AND KASHMIR	13	41,767.84	76,147.35	82.31	1	2,500.00	37,012.26	247 - 247
9	KARNATAKA	20	70,060.07	78,338.37	11.82	4	4,744.25	7,169.86	33 - 129
10	KERALA	7	11,881.63	14,904.84	25.44	3	2,843.17	4,053.03	44 - 66
11	MADHYA PRADESH	17	37,488.68	44,494.72	18.69	7	11,608.43	19,131.52	21 - 55
12	MAHARASHTRA	39	1,13,200.73	1,38,716.38	22.54	13	44,376.10	65,262.08	9 - 228
13	MANIPUR	1	4,454.17	14,322.79	221.56	1	4,454.17	14,322.79	153 - 153
14	MEGHALAYA	1	906.46	8,324.28	818.33	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	6,527.45	172.72	1	2,393.47	6,527.45	117 - 117
16	NAGALAND	1	2,326.52	6,663.00	186.39	1	2,326.52	6,663.00	132 - 132
17	ODISHA	37	95,429.38	1,03,286.41	8.23	9	16,169.10	23,522.91	23 - 201
18	PUNJAB	7	8,647.82	9,958.16	15.15	0	0.00	0.00	-
19	RAJASTHAN	17	42,922.04	47,915.51	11.63	1	12,320.00	17,079.00	84 - 84
20	SIKKIM	2	7,087.52	13,624.96	92.24	1	1,339.48	7,876.92	96 - 96
21	TAMIL NADU	28	1,83,861.78	2,04,908.53	11.45	6	11,401.69	20,994.93	33 - 168
22	UTTAR PRADESH	38	1,01,053.19	1,15,582.36	14.38	12	29,690.76	40,085.25	9 - 54
23	WEST BENGAL	19	47,030.89	58,626.37	24.66	7	15,479.39	21,810.85	55 - 141
24	DELHI	7	74,527.86	76,909.38	3.20	2	5,992.21	6,857.02	37 - 38
25	CHHATISGARH	17	64,949.58	90,625.43	39.53	5	24,001.00	33,706.28	33 - 94
26	JHARKHAND	14	58,448.62	65,336.45	11.78	1	14,366.58	17,007.00	66 - 66
27	UTTARAKHAND	9	28,781.19	47,795.15	66.06	4	23,343.06	40,447.95	3 - 141
28	TELANGANA	3	16,188.46	17,677.00	9.20	2	11,759.46	13,248.00	31 - 180
29	MULTI STATE	42	2,91,726.97	3,96,449.92	35.90	21	42,836.42	73,870.02	12 - 276
Total		441	16,73,812.55	21,28,110.78	27.14	132	3,83,052.54	6,83,892.30	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

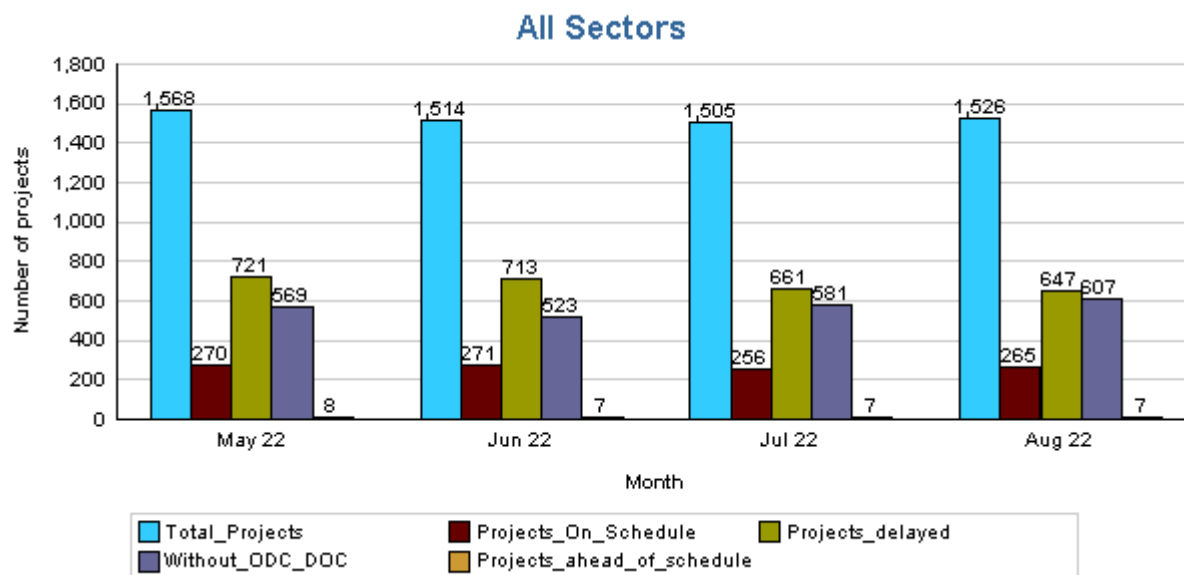

Break-up of 647 Delayed projects in August 2022

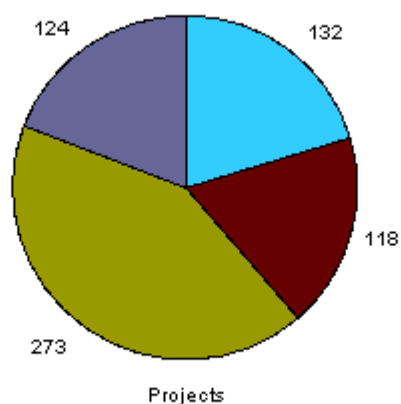


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of WATER RESOURCES Sector

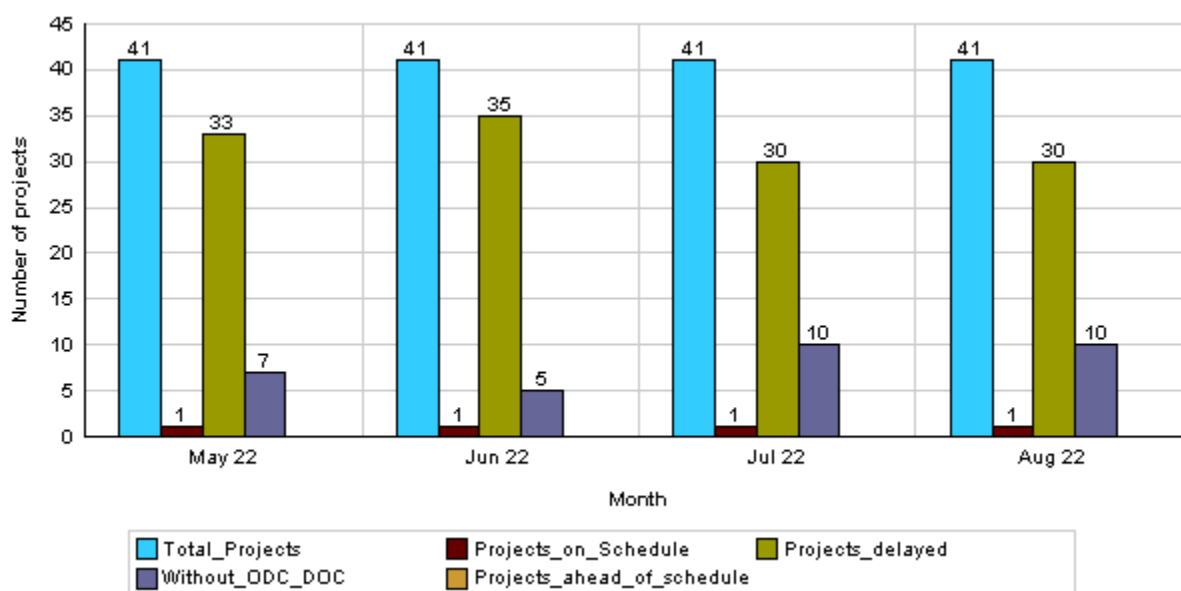


Break-up of 30 Delayed projects in August 2022

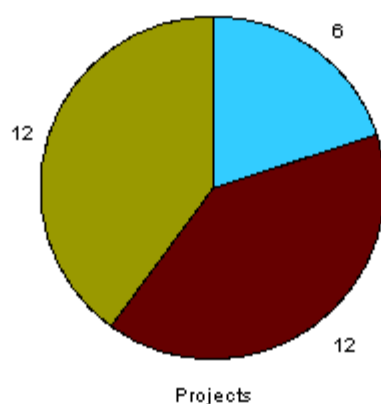


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	6	12	12	0

Graphical Presentation of URBAN DEVELOPMENT Sector

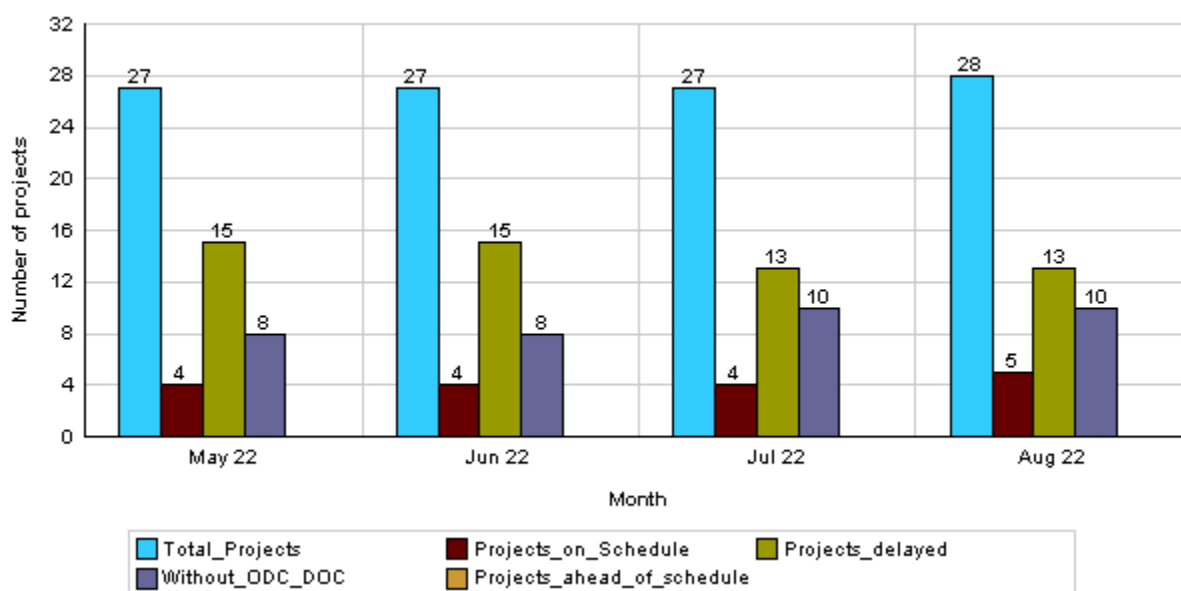


Break-up of 13 Delayed projects in August 2022

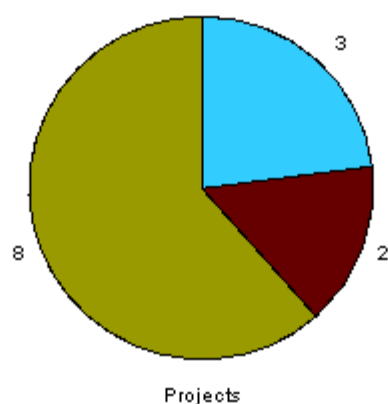


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of TELECOMMUNICATIONS Sector

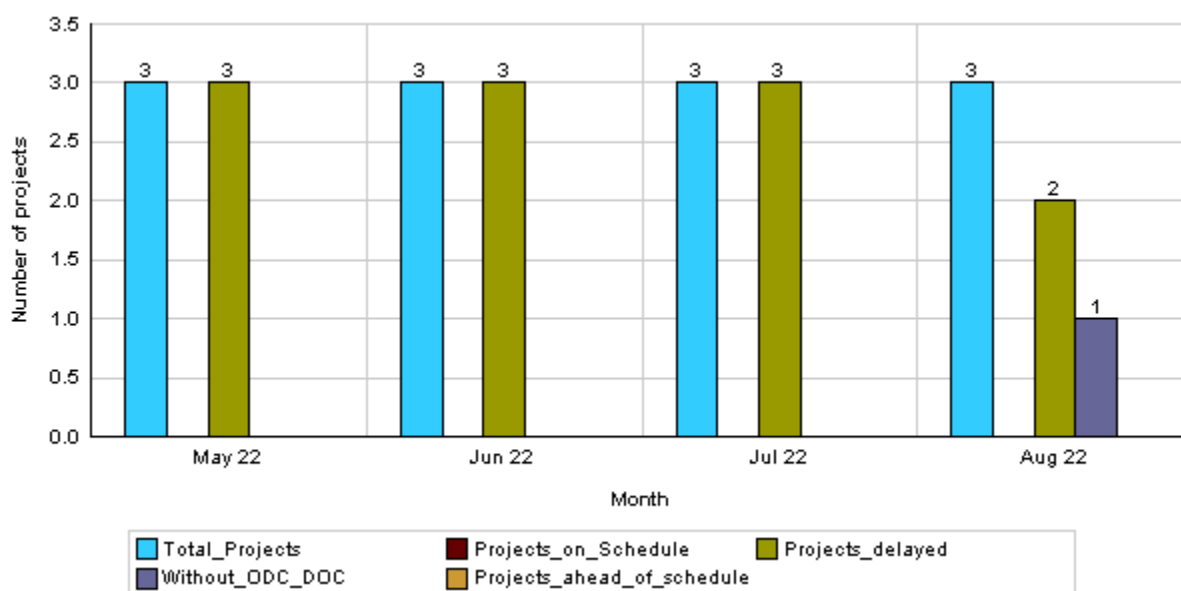


Break-up of 2 Delayed projects in August 2022

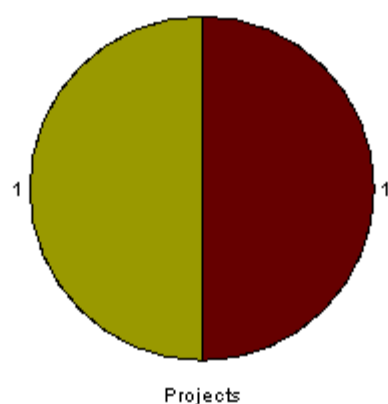


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	1	1	0

Graphical Presentation of STEEL Sector

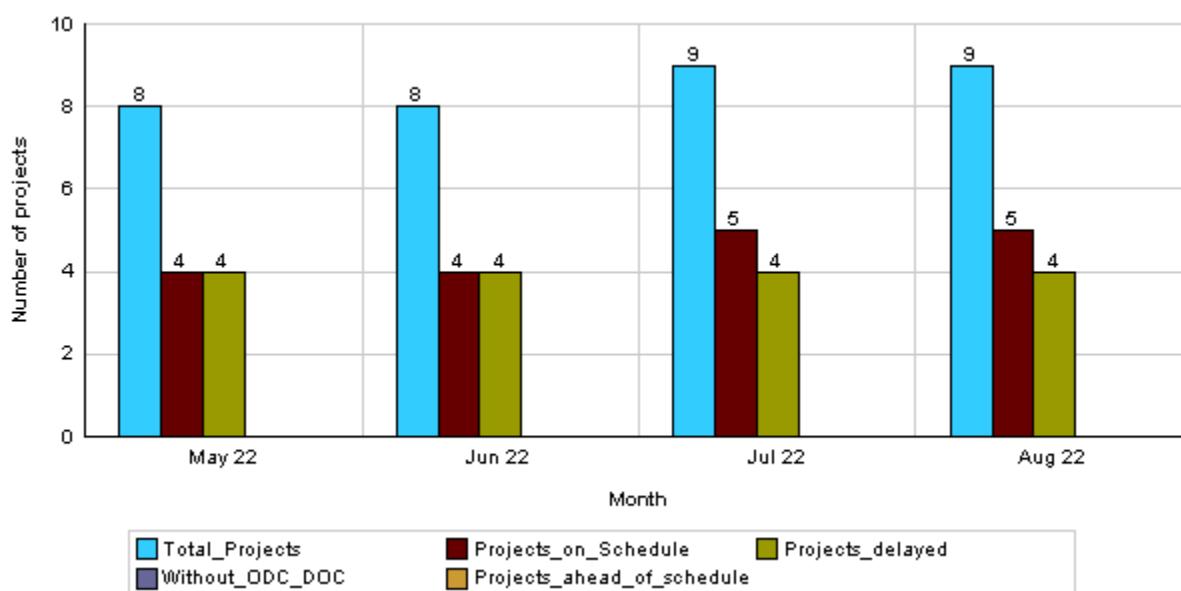


Break-up of 4 Delayed projects in August 2022

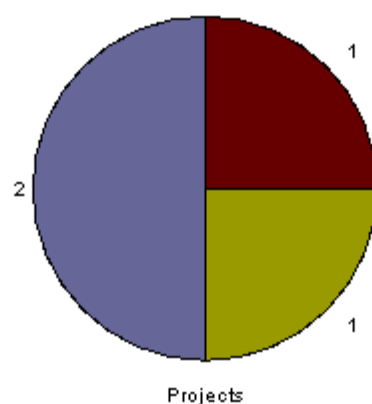

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	1	1	1	2

Graphical Presentation of SHIPPING AND PORTS Sector

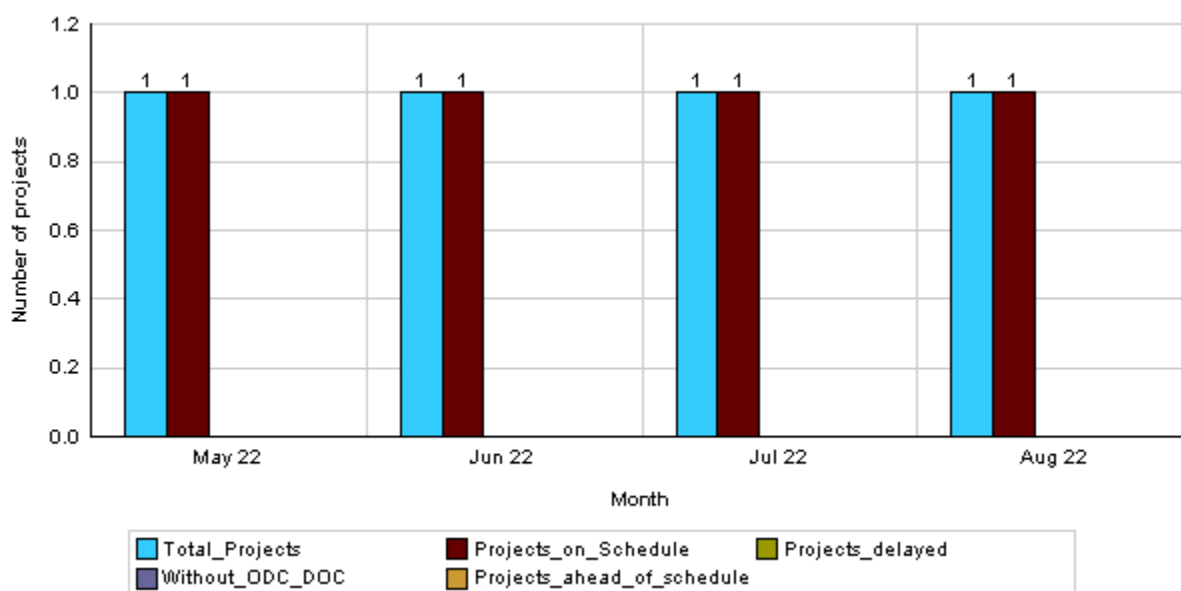


Break-up of 0 Delayed projects in August 2022


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12				
13-24				
25-60				
MORE THAN 60				

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

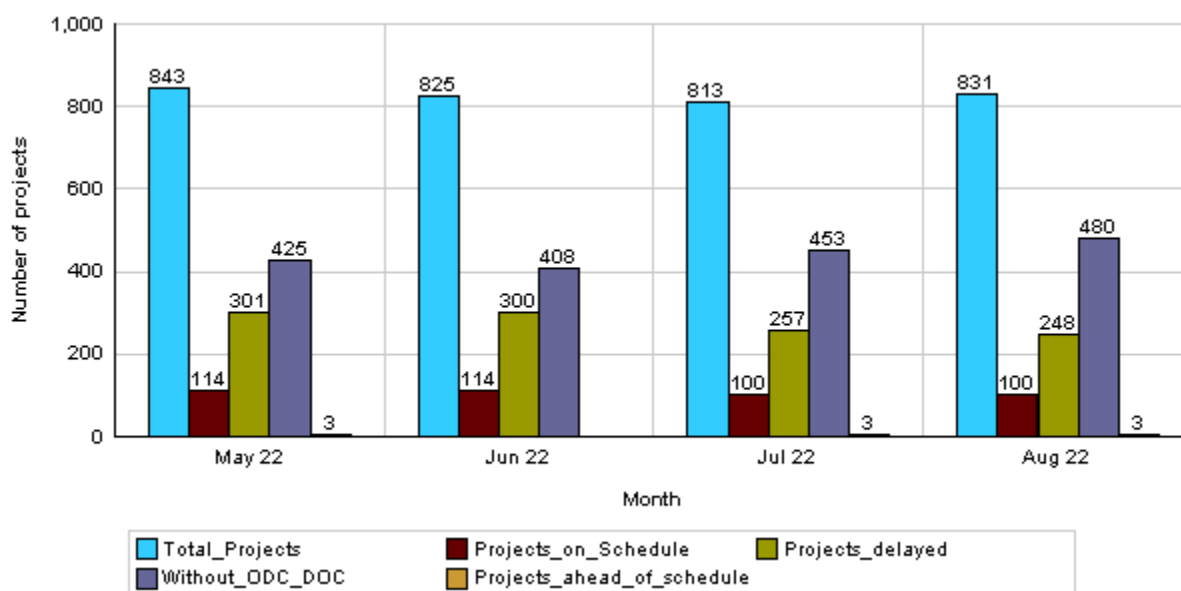


Break-up of 248 Delayed projects in August 2022

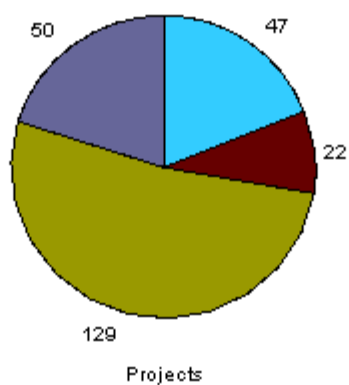

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RENEWABLE ENERGY Sector

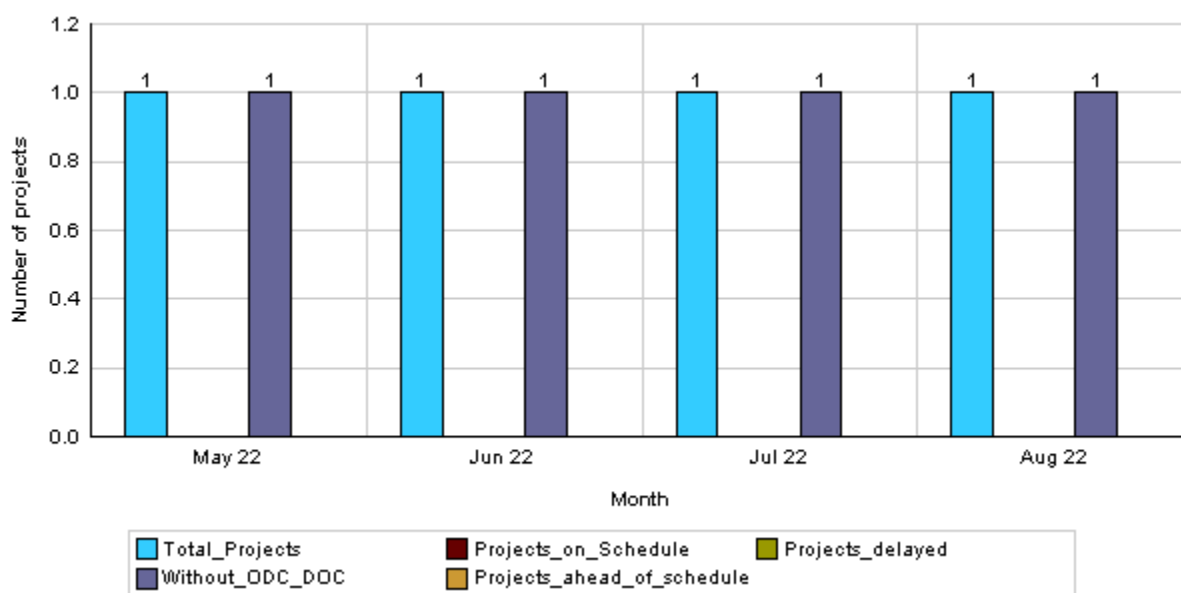


Break-up of 0 Delayed projects in August 2022


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of RAILWAYS Sector

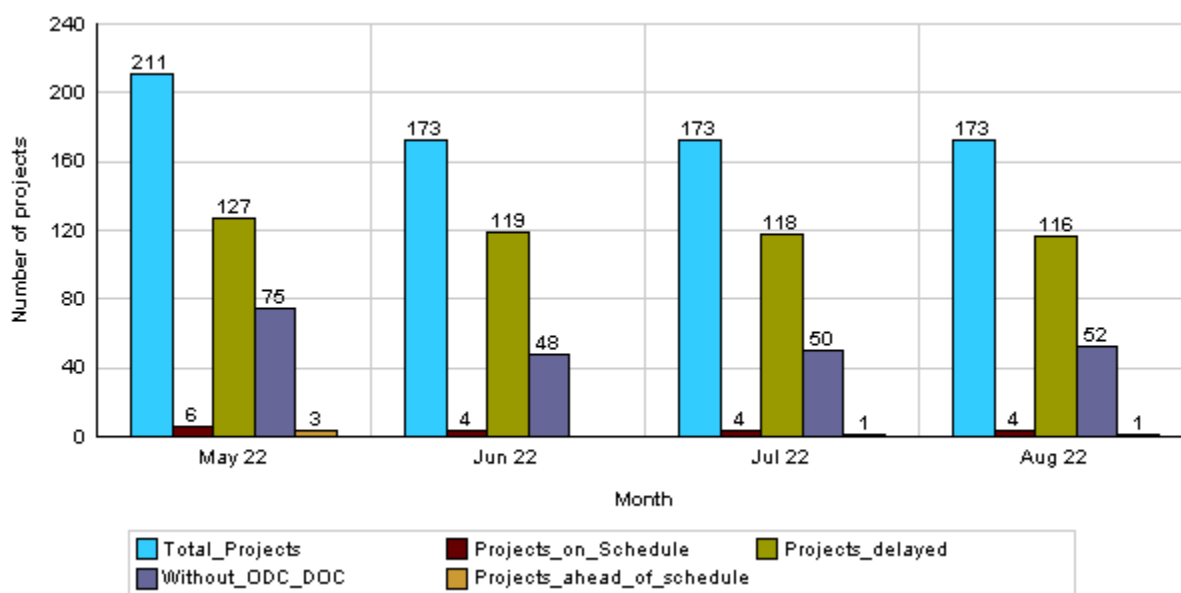


Break-up of 116 Delayed projects in August 2022

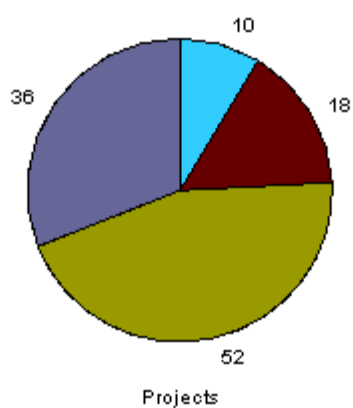


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

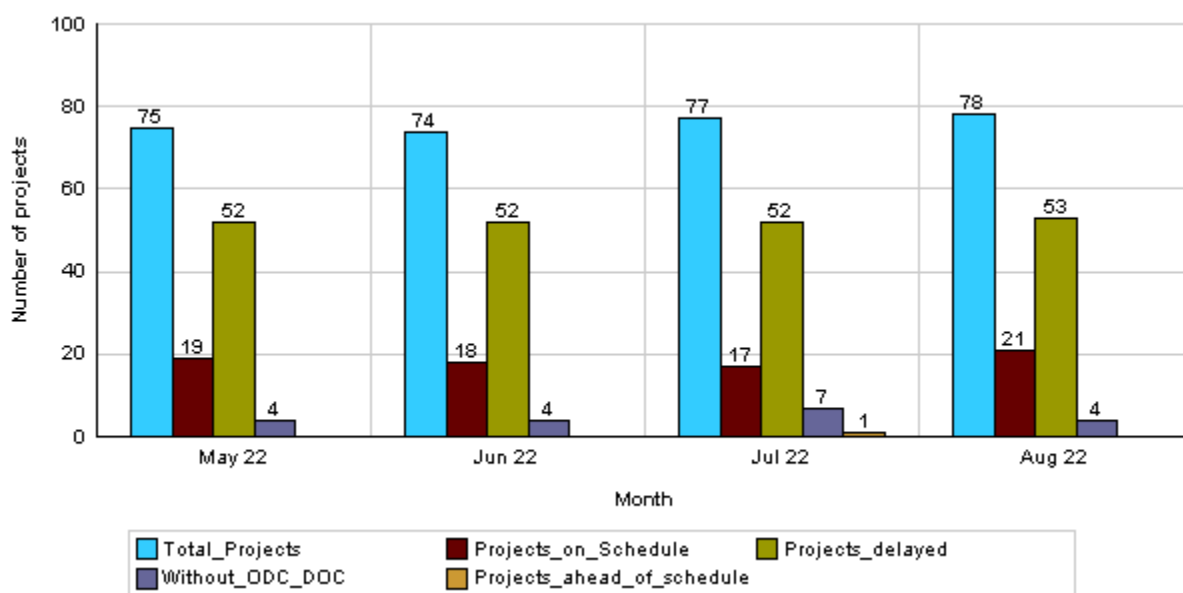


Break-up of 53 Delayed projects in August 2022

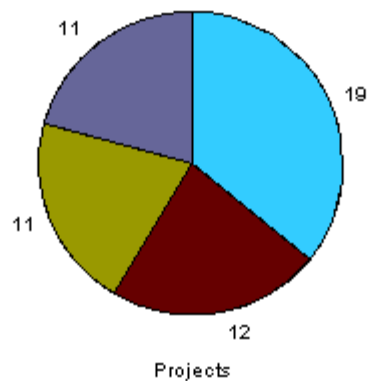


Delay in Months

Delay in Months	Count
1-12	19
13-24	12
25-60	11
MORE THAN 60	11

Graphical Presentation of PETROLEUM Sector

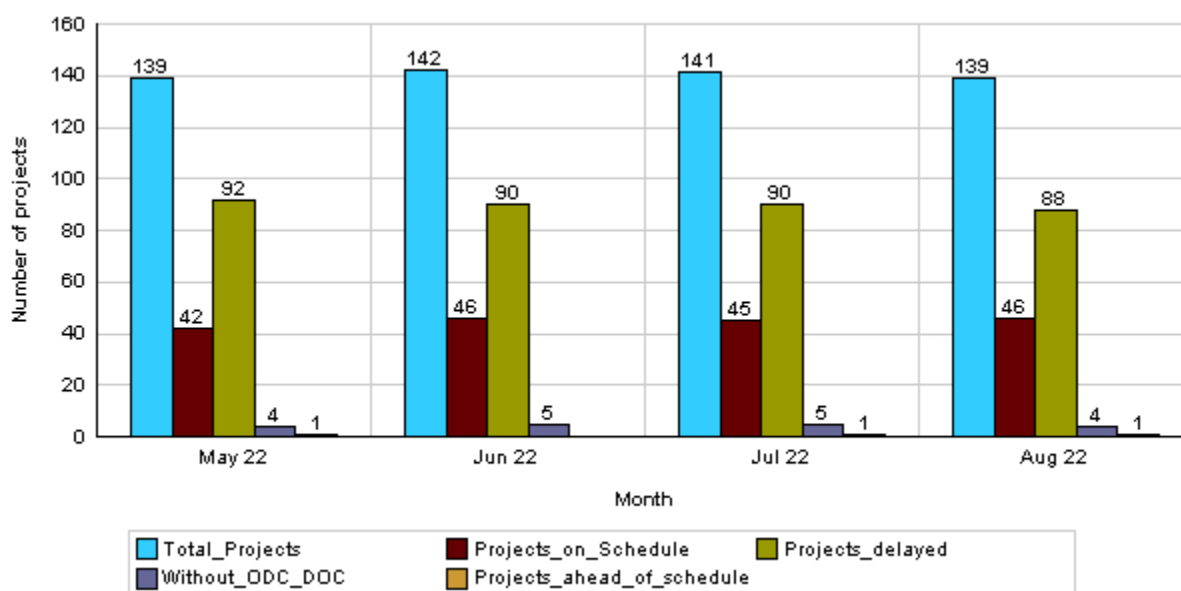


Break-up of 88 Delayed projects in August 2022

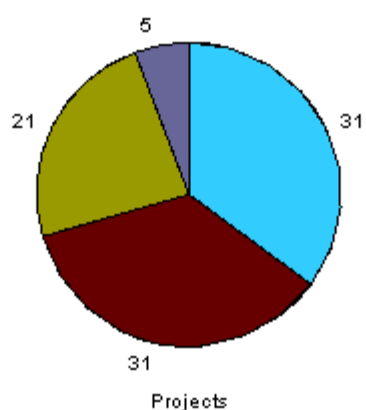


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	31	31	21	5

Graphical Presentation of MINES Sector

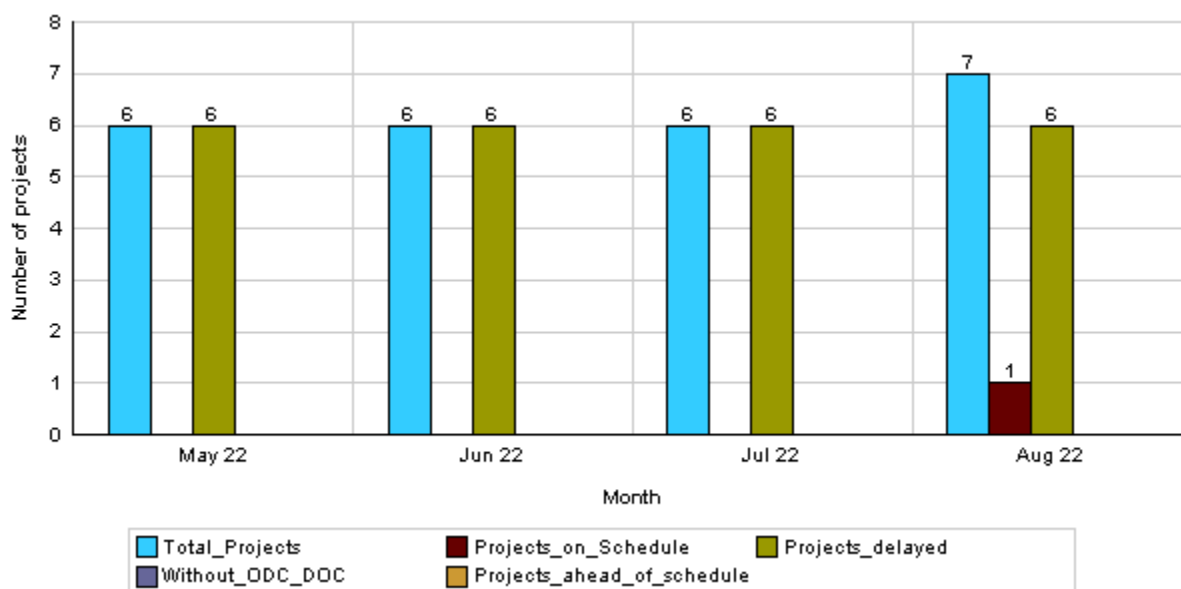


Break-up of 6 Delayed projects in August 2022




Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of HOME AFFAIRS Sector

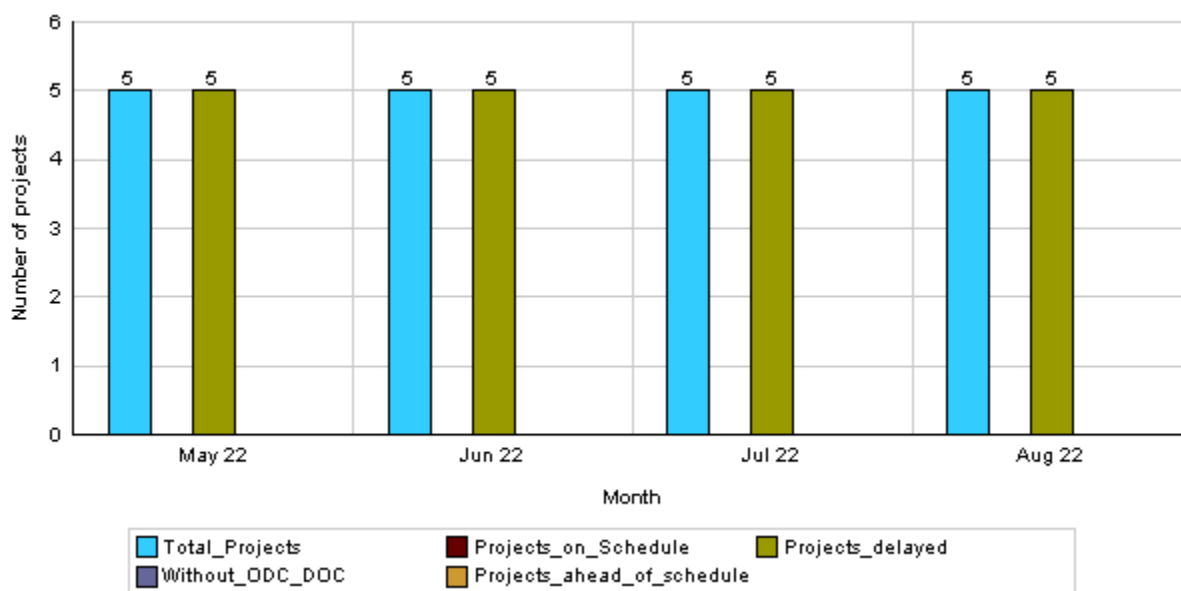


Break-up of 5 Delayed projects in August 2022

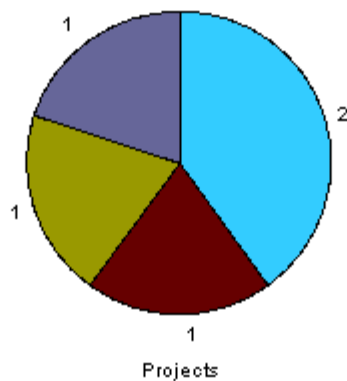


Delay in Months

Delay in Months	Number of Projects
1-12	2
13-24	1
25-60	1
MORE THAN 60	1

Graphical Presentation of DEPARTMENT OF HIGHER EDUCATION Sector

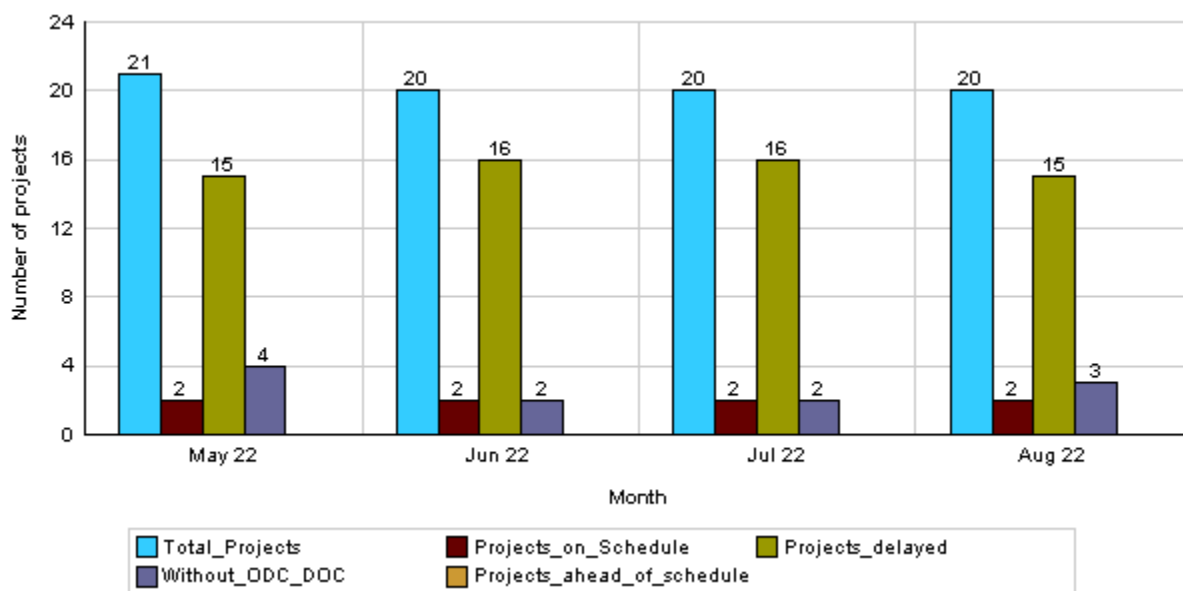


Break-up of 15 Delayed projects in August 2022

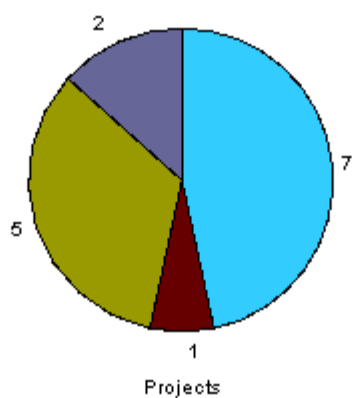

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	7	1	5	2

Graphical Presentation of HEAVY INDUSTRY Sector

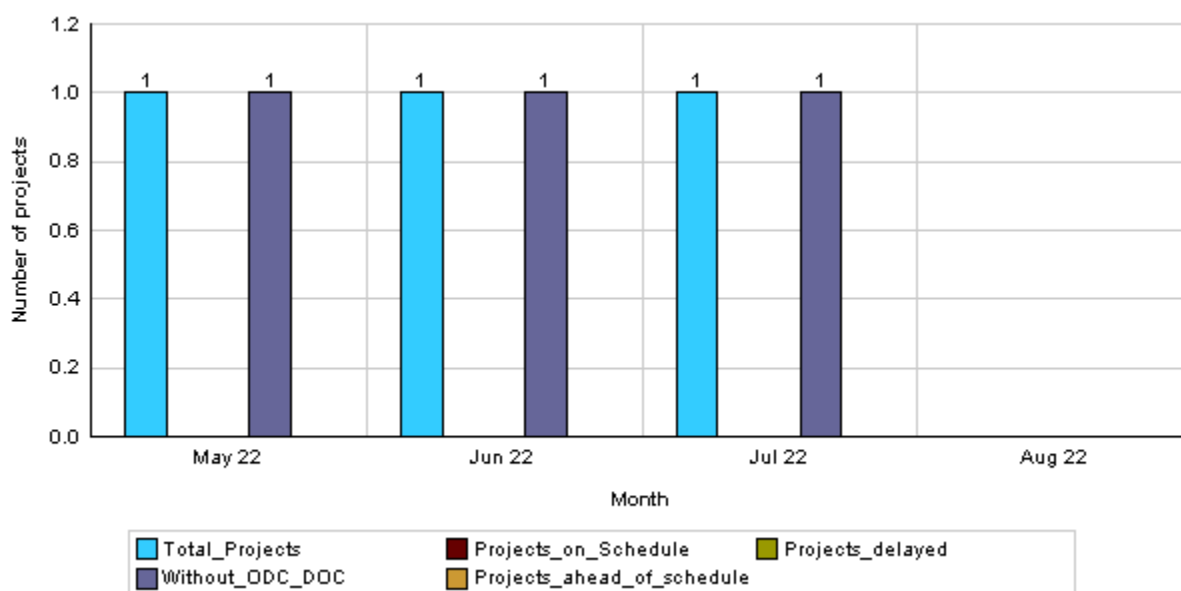


Break-up of 0 Delayed projects in August 2022


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12				
13-24				
25-60				
MORE THAN 60				

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

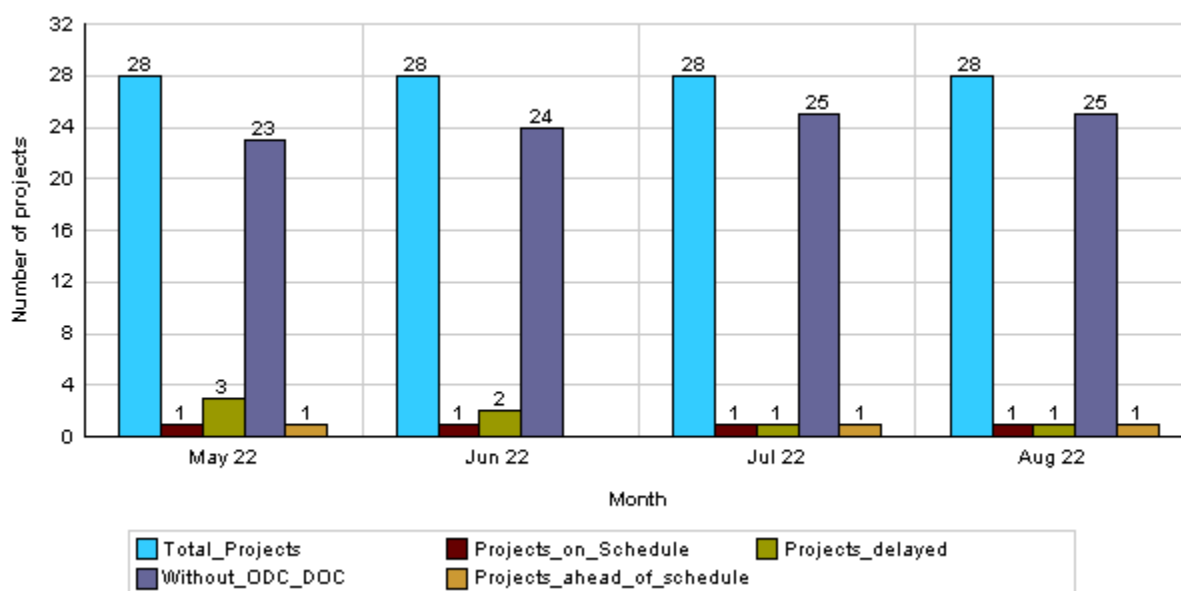


Break-up of 1 Delayed projects in August 2022

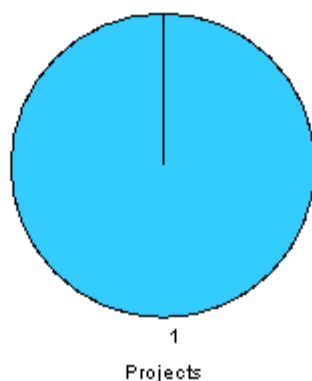


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of FINANCE Sector

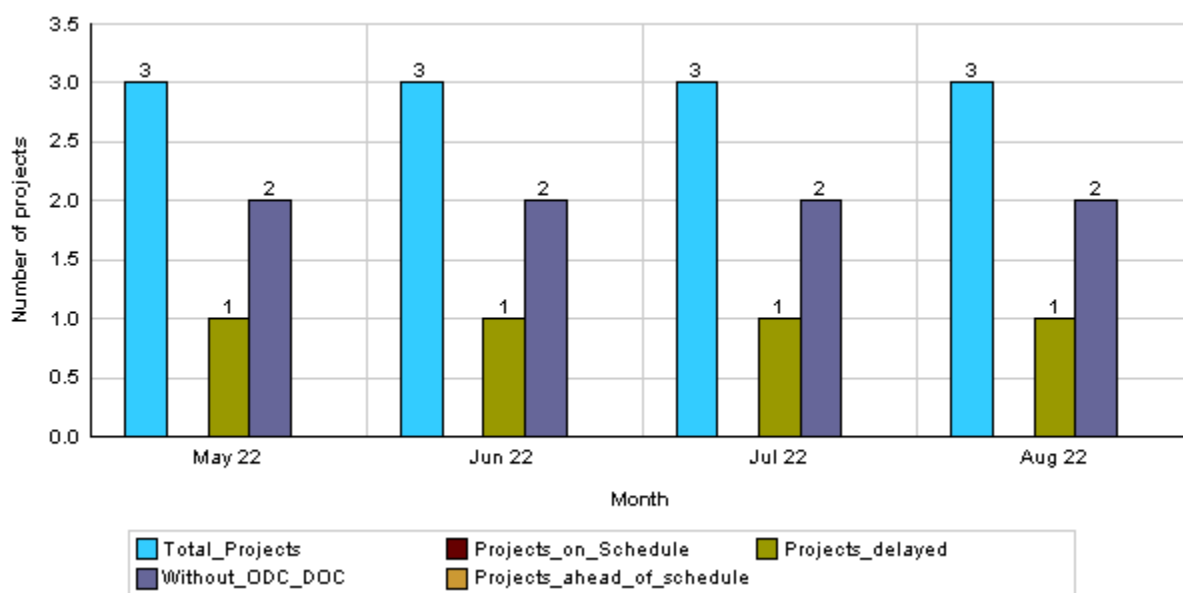


Break-up of 1 Delayed projects in August 2022

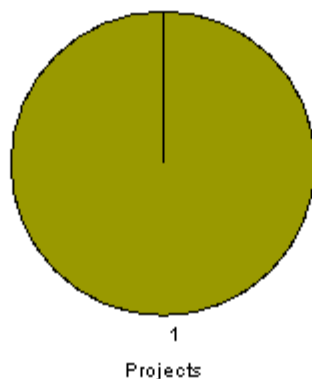

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	0	1	0

Graphical Presentation of FERTILISERS Sector

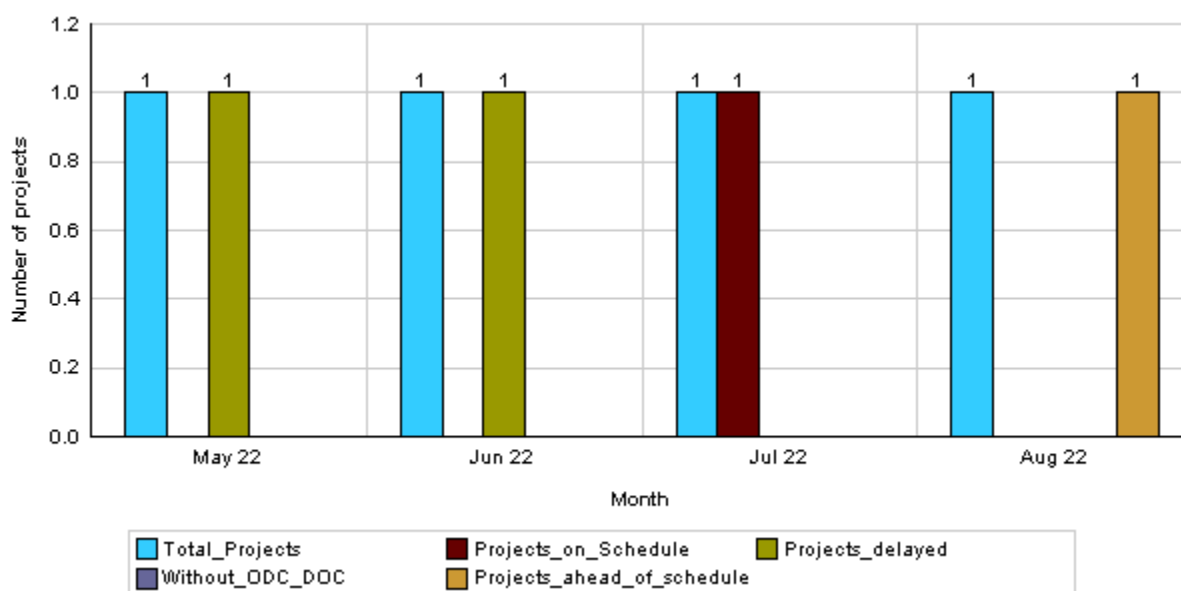


Break-up of 0 Delayed projects in August 2022


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	0	0
MORE THAN 60	0	0	0	0

Graphical Presentation of DPIIT Sector

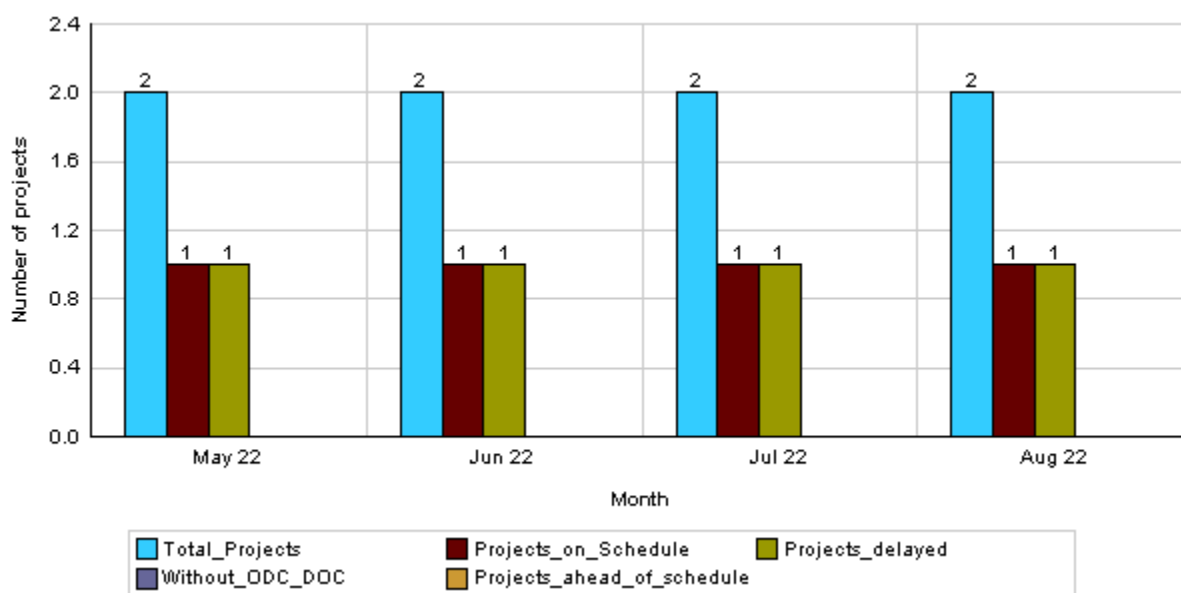


Break-up of 1 Delayed projects in August 2022

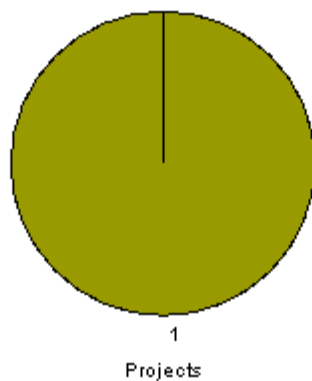

Delay in Months

Delay in Months	Count
1-12	0
13-24	0
25-60	1
MORE THAN 60	0

Graphical Presentation of DONER Sector

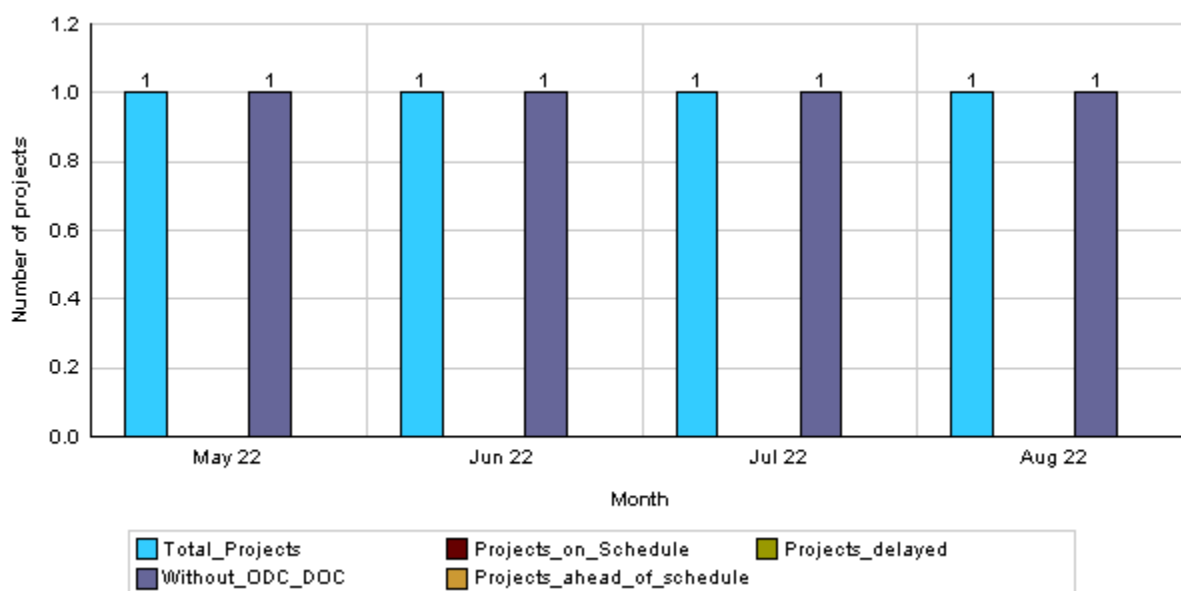


Break-up of 0 Delayed projects in August 2022


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of DEFENCE PRODUCTION Sector

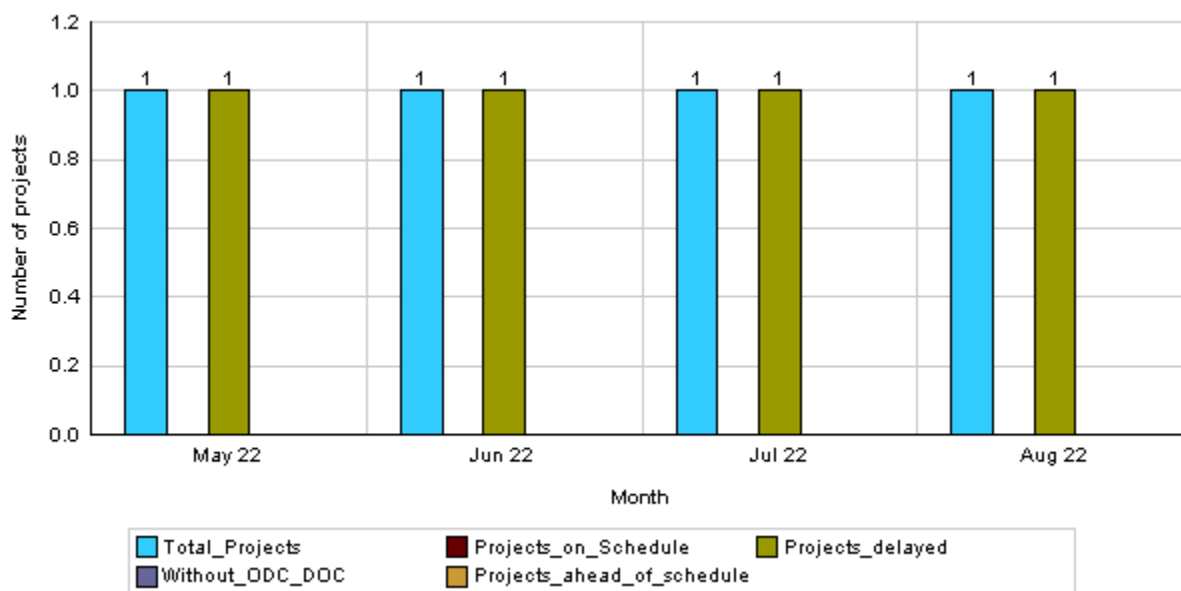


Break-up of 1 Delayed projects in August 2022

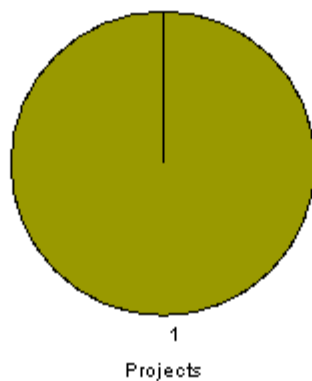

Delay in Months

Delay in Months	Count
1-12	0
13-24	0
25-60	1
MORE THAN 60	0

Graphical Presentation of COMMERCE Sector

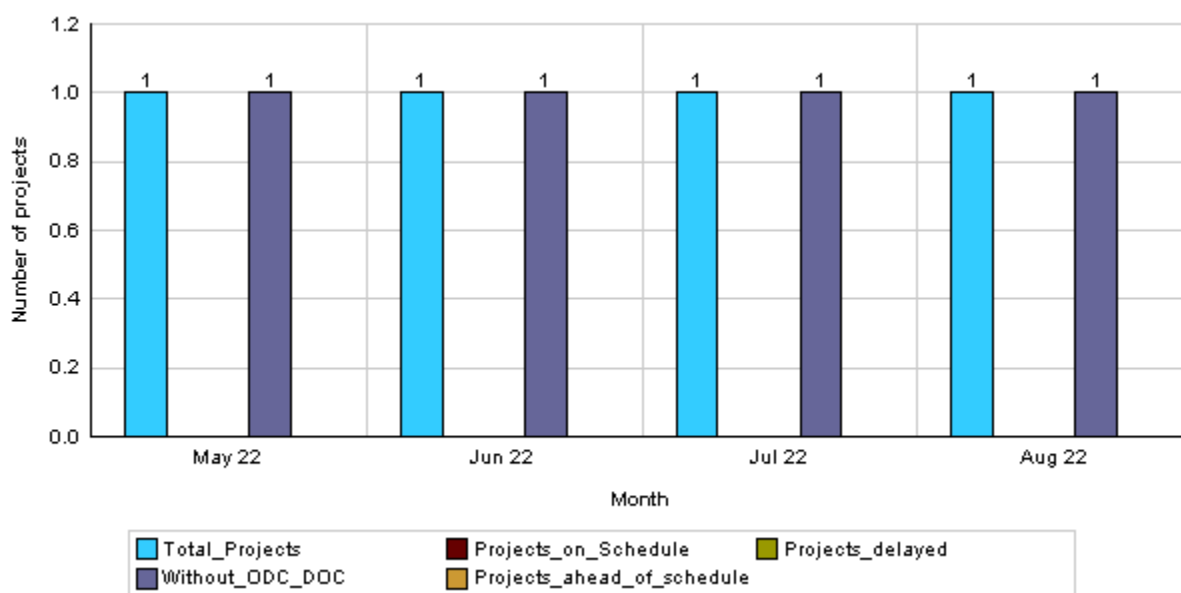


Break-up of 0 Delayed projects in August 2022


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12				
13-24				
25-60				
MORE THAN 60				

Graphical Presentation of COAL Sector

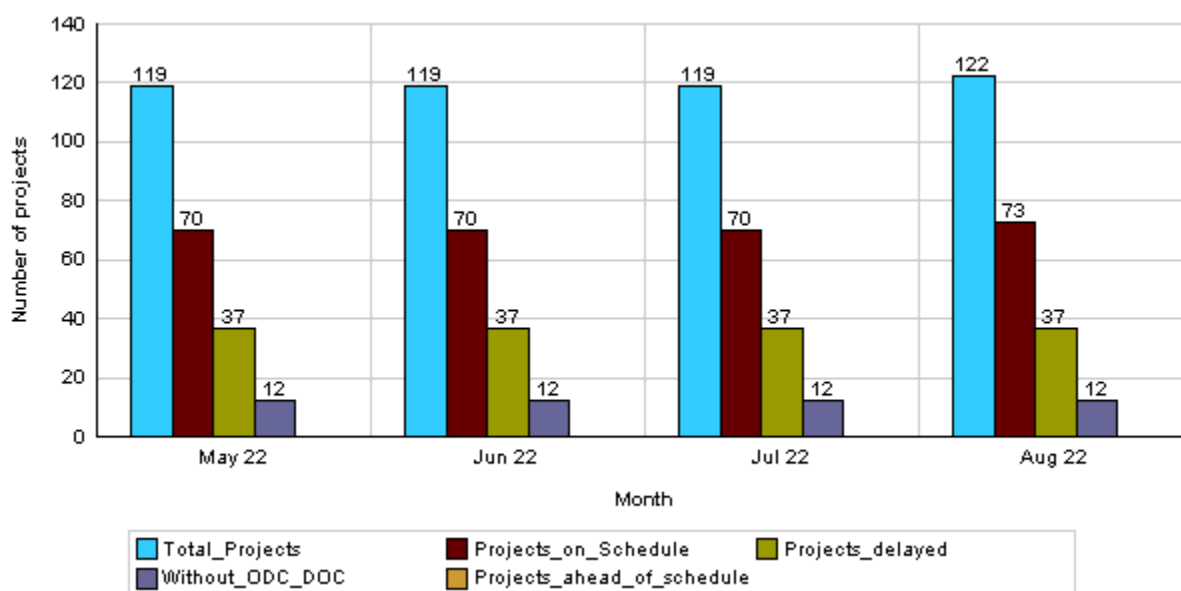


Break-up of 37 Delayed projects in August 2022

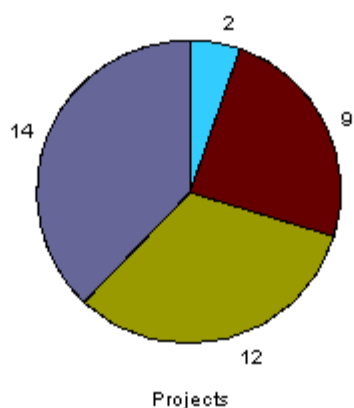


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	2	9	12	14

Graphical Presentation of CIVIL AVIATION Sector

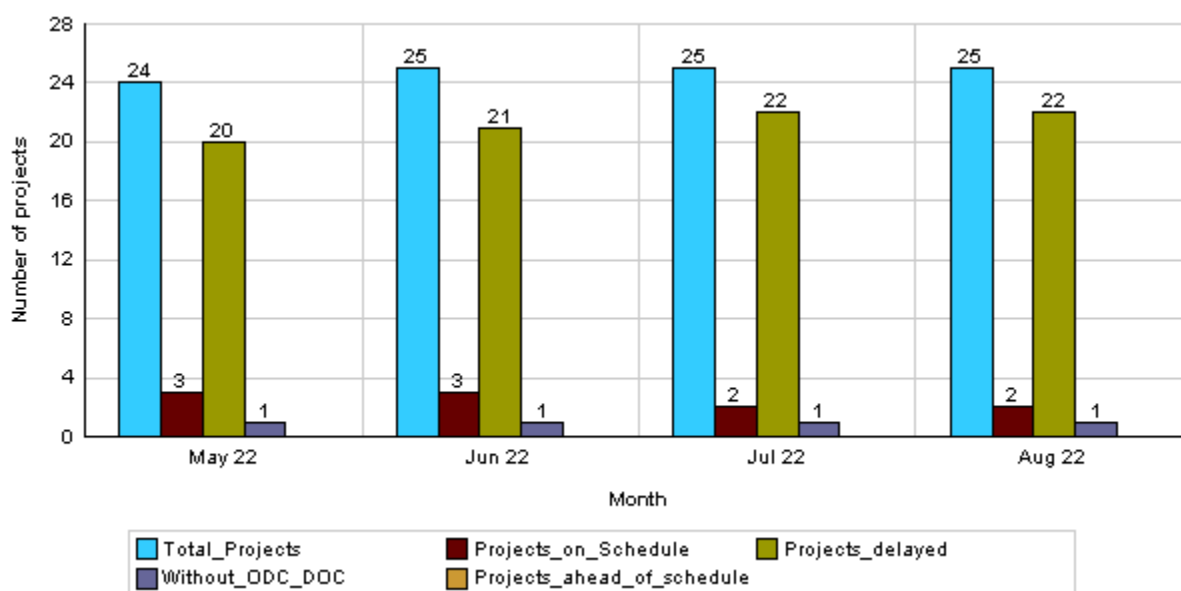


Break-up of 22 Delayed projects in August 2022

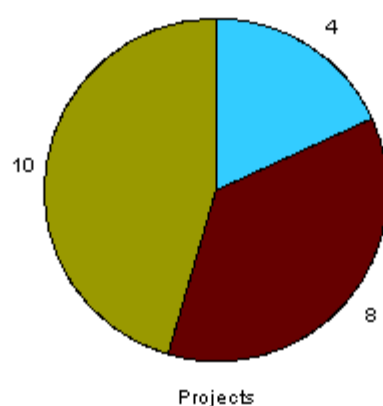


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

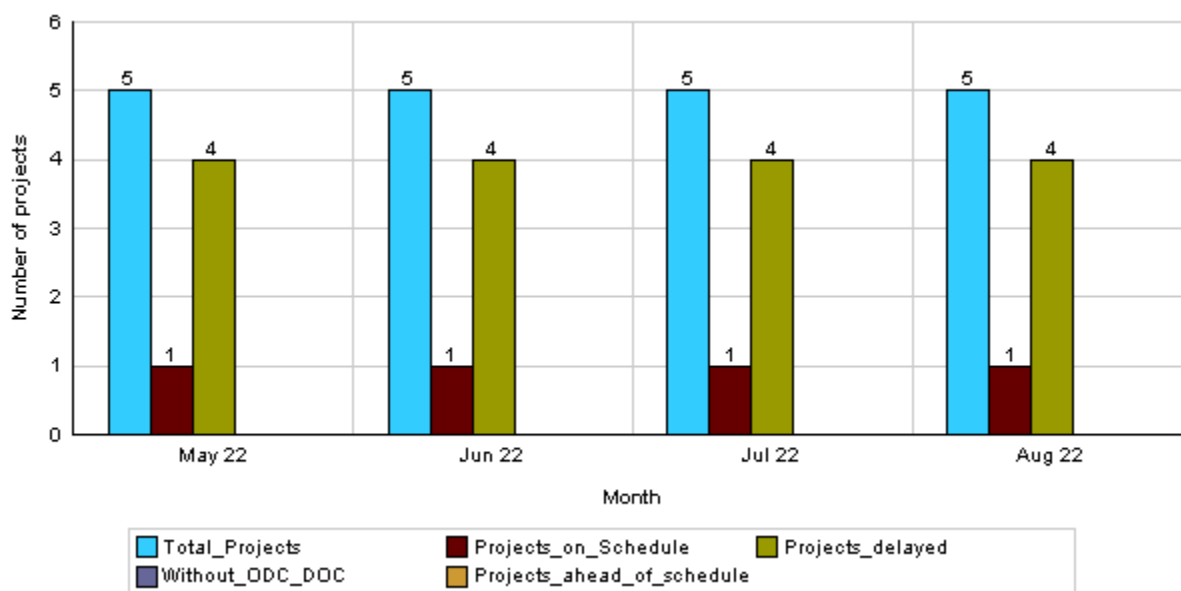

Break-up of 4 Delayed projects in August 2022

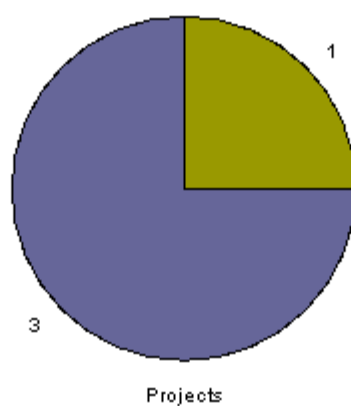

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	0	0	1	3

Detail of ongoing Projects Costing Rs		150	Crore and above.			(August 2022)
		(All Cost/ Expenditure in Rs. Crore)				
Sl.No	Project	Date of Approval (month / year)	Original / Revised / Anticipated Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]	Miles tones Achieved / Total
	ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044],BHAVNI,TAMIL NADU	9/2003	9/2010 (10/2022) [9/2024]	3,492.00 (6,840.00) [7,500.00]	6,433.54 (4,008.00) [168]	83/87
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027],NPCIL,RAJASTHAN	10/2009	12/2016 (-) [12/2023]	12,320.00 (17,079.00) [17,079.00]	14,876.00 (4,759.00) [84]	55/68
3	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029],NPCIL,TAMIL NADU	6/2017	9/2027 (-) [9/2027]	49,621.00 (-) [49,621.00]	6,216.00 (0.00) [0]	16/80
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028],NPCIL,TAMIL NADU	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	31,955.00 (0.00) [36]	32/76
5	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010],NPCIL,GUJARAT	10/2009	12/2015 (-) [6/2023]	11,459.00 (19,220.00) [19,220.00]	18,523.00 (7,761.00) [90]	64/70
	CIVIL AVIATION					
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076],AAI,DELHI	11/2016	4/2020 (12/2022) [12/2022]	303.80 (351.21) [351.21]	247.98 (47.41) [32]	0/0
7	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 - [N04000098],AAI,MADHYA PRADESH	10/2021	8/2023 (-) [8/2023]	446.12 (-) [446.12]	40.91 (0.00) [0]	0/1
8	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086],AAI,TELANGANA	5/2020	5/2022 (3/2023) [3/2023]	353.61 (-) [353.61]	175.15 (0.00) [10]	2/4
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079],AAI,MAHARASHTRA	3/2017	4/2021 (8/2023) [8/2023]	475.39 (-) [475.39]	248.29 (0.00) [28]	3/10
10	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081],AAI,WEST BENGAL	1/2019	11/2021 (4/2023) [4/2023]	389.71 (-) [389.71]	325.34 (0.00) [17]	0/2
11	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080],AAI,WEST BENGAL	1/2016	3/2020 (3/2024) [3/2024]	458.00 (-) [458.00]	190.85 (0.00) [48]	0/2
12	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085],AAI,UTTARAKHAND	7/2018	9/2020 (12/2022) [12/2022]	456.86 (-) [456.86]	376.59 (0.00) [27]	1/1
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084],AAI,TRIPURA	9/2015	6/2019 (12/2021) [12/2021]	438.28 (-) [402.00]	405.76 (-36.28) [0]	1/1
14	EXTENSION OF RUNWAY WITH	6/2017	12/2020	255.68	202.60	0/1

	BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM - [N04000096],AAI,MAHARASHTRA		(-) [9/2023]	(-) [255.68]	(0.00) [33]	
15	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091],AAI,ANDHRA PRADESH	4/2020	3/2023 (-) [7/2023]	611.80 (-) [611.80]	167.35 (0.00) [4]	6/14
16	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. - [N04000093],AAI,GUJARAT	8/2018	2/2021 (-) [12/2022]	353.25 (-) [353.25]	143.30 (0.00) [22]	0/1
17	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083],AAI,ASSAM	12/2016	3/2021 (-) [3/2025]	1,142.00 (-) [1,232.00]	426.51 (90.00) [48]	0/1
18	UPGRADATION OF JABALPUR AIRPORT - [N04000087],AAI,MADHYA PRADESH	6/2016	6/2021 (3/2023) [3/2023]	412.24 (-) [412.24]	284.51 (0.00) [21]	0/1
19	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092],AAI,ARUNACHAL PRADESH	2/2019	8/2022 (3/2023) [3/2023]	645.63 (-) [645.63]	519.30 (0.00) [7]	0/3
20	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078],AAI,LADAKH	7/2018	9/2021 (12/2023) [12/2023]	346.27 (-) [480.33]	192.21 (134.06) [27]	2/4
21	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077],AAI,UTTAR PRADESH	6/2018	9/2021 (-) [9/2023]	1,383.00 (-) [2,445.00]	797.96 (1,062.00) [24]	0/2
22	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 - [N04000094],AAI,UTTAR PRADESH	3/2021	12/2022 (-) [12/2022]	242.14 (-) [242.14]	57.40 (0.00) [0]	0/2
23	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073],AAI,A & N ISLANDS	10/2013	9/2018 (10/2022) [10/2022]	417.23 (707.73) [707.73]	570.11 (290.50) [49]	0/6
24	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090],AAI,TAMIL NADU	6/2019	3/2022 (12/2023) [3/2024]	380.87 (-) [380.87]	68.90 (0.00) [24]	8/21
25	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088],AAI,GUJARAT	1/2018	8/2022 (8/2023) [8/2023]	1,405.00 (-) [1,405.00]	681.21 (0.00) [12]	2/15
26	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. - [N04000095],AAI,GOA	11/2017	9/2021 (-) [9/2023]	255.69 (-) [255.69]	27.32 (0.00) [24]	0/1
27	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089],AAI,ANDHRA PRADESH	8/2017	2/2020 (12/2022) [12/2022]	177.10 (-) [177.10]	137.92 (0.00) [34]	1/4
28	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082],AAI,BIHAR	5/2018	10/2022 (3/2024) [3/2024]	1,216.90 (-) [1,216.90]	333.86 (0.00) [17]	0/3
29	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074],AAI,TAMIL NADU	6/2018	2/2022 (12/2024) [12/2024]	2,467.00 (-) [2,467.00]	1,048.18 (0.00) [34]	5/12
30	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI -	8/2018	10/2021 (4/2023) [4/2023]	951.28 (-) [951.28]	660.06 (0.00) [18]	3/14

	[N04000075],AAI,TAMIL NADU					
	COAL					
31	MURAI DIH UG TURN-KEY PROJECT - [N06000096],BCCL,JHARKHAND	2/2011	4/2014 (-) [10/2025]	339.88 (-) [339.88]	130.52 (0.00) [138]	4/7
32	MADHUBAND NLW WASHERY - [N06000126],BCCL,JHARKHAND	8/2010	5/2014 (-) [9/2022]	289.45 (302.00) [302.00]	296.38 (12.55) [100]	0/8
33	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106],BCCL,JHARKHAND	2/2014	3/2021 (-) [3/2023]	555.52 (-) [555.52]	20.01 (0.00) [24]	0/2
34	MOONIDIH XV SEAM UG - [N06000098],BCCL,JHARKHAND	8/2011	3/2019 (-) [4/2024]	1,230.27 (-) [1,230.27]	538.38 (0.00) [61]	2/6
35	2.0 MTPA BHOJUDI H NLW WASHERY - [N06000195],BCCL,WEST BENGAL	12/2015	3/2017 (-) [12/2022]	304.13 (341.22) [341.22]	139.20 (37.09) [69]	0/0
36	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194],BCCL,JHARKHAND	10/2015	4/2018 (-) [6/2023]	243.00 (334.27) [334.27]	44.58 (91.27) [62]	0/0
37	EPR PUNDI OCP - [N06000242],CCL,JHARKHAND	11/2020	3/2024 (-) [3/2024]	713.35 (-) [713.35]	233.94 (0.00) [0]	0/0
38	EXPANSION PROJECT AMRAPALI OCP - [N06000217],CCL,JHARKHAND	8/2020	3/2028 (-) [3/2028]	5,136.15 (-) [5,136.15]	331.85 (0.00) [0]	0/0
39	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216],CCL,JHARKHAND	8/2020	3/2028 (-) [3/2028]	7,254.37 (-) [7,254.37]	782.87 (0.00) [0]	0/0
40	EXPANSION OF KARO OCP - [N06000246],CCL,JHARKHAND	1/2022	3/2026 (-) [3/2026]	908.47 (-) [908.47]	99.05 (0.00) [0]	0/0
41	TETARIAKHAR EXPANSION OCP - [N06000186],CCL,JHARKHAND	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	48.22 (0.00) [0]	1/1
42	CHANDRAGUPT OCP - [N06000238],CCL,JHARKHAND	8/2020	3/2032 (-) [3/2032]	973.50 (-) [973.50]	204.84 (0.00) [0]	0/0
43	SIRKA OCP - [N06000239],CCL,JHARKHAND	5/2020	3/2025 (-) [3/2025]	222.82 (-) [222.82]	136.52 (0.00) [0]	0/0
44	CHURI BENTI UG (0.81 MTY) - [N06000083],CCL,JHARKHAND	8/2007	3/2011 (-) [3/2023]	163.51 (-) [163.51]	133.41 (0.00) [144]	7/7
45	KOTRE BASANTPUR PACHMO OCP - [N06000237],CCL,JHARKHAND	8/2020	3/2032 (-) [3/2032]	861.06 (-) [861.06]	137.75 (0.00) [0]	0/0
46	JHARKHAND LAIYO OCP - [N06000240],CCL,JHARKHAND	8/2020	3/2031 (-) [3/2031]	764.57 (-) [764.57]	152.91 (0.00) [0]	0/0
47	EPR TAPIN SOUTH OCP - [N06000241],CCL,JHARKHAND	11/2020	3/2025 (-) [3/2025]	230.41 (-) [230.41]	18.14 (0.00) [0]	0/0
48	UCE OF EPR OF NORTH URIMARI OCP - [N06000218],CCL,JHARKHAND	7/2021	3/2026 (-) [3/2026]	778.80 (-) [778.80]	508.97 (0.00) [0]	0/0
49	KARMA OCP (1.0MTY) - [N06000088],CCL,JHARKHAND	6/2009	3/2014 (-) [3/2023]	162.46 (-) [162.46]	93.61 (0.00) [108]	7/7
50	EPR ROHINI KARKATA OCP - [N06000243],CCL,JHARKHAND	1/2021	3/2025 (-) [3/2025]	1,020.42 (-) [1,020.42]	81.23 (0.00) [0]	0/0
51	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087],CCL,JHARKHAND	12/2009	3/2016 (-)	510.85 (-)	487.40 (0.00)	7/7

			[3/2023]	[510.85]	[84]	
52	EXPANSION OF KONAR OCP - [N06000245],CCL,JHARKHAND	1/2022	3/2032 (-) [3/2032]	799.34 (-) [799.34]	263.19 (0.00) [0]	0/0
53	EXPANSION OF ASHOK OCP - [N06000247],CCL,JHARKHAND	5/2021	3/2026 (-) [3/2026]	2,898.28 (-) [2,898.28]	186.45 (0.00) [0]	0/0
54	RANIGANJ MASTER PLAN - [N06000163],ECL, WEST BENGAL	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	648.15 (2,484.75) [60]	1/19
55	HURA - C OC (3 MTY) - [N06000143],ECL,JHARKHAND	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	263.24 (0.00) [0]	4/22
56	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191],ECL, WEST BENGAL	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	11.09 (0.00) [0]	0/0
57	TILABONI UG MINE - [N06000172],ECL, WEST BENGAL	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	6.04 (0.00) [0]	2/27
58	SONEPUR BAZARI EXPANSION OC - [N06000220],ECL, WEST BENGAL	7/2021	3/2029 (-) [3/2029]	5,365.88 (5,366.00) [5,365.88]	170.95 (0.00) [0]	0/0
59	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223],ECL, WEST BENGAL	4/2020	3/2029 (-) [3/2029]	1,210.12 (-) [1,210.12]	152.04 (0.00) [0]	0/0
60	BONJEME HARI EXPANSION OCP - [N06000244],ECL, WEST BENGAL	8/2021	3/2025 (-) [3/2025]	570.12 (-) [570.12]	0.23 (0.00) [0]	0/0
61	SIDULI MINE (OC AND UG) - [N06000165],ECL, WEST BENGAL	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	2.00 (0.00) [0]	4/22
62	MOHANPUR EXPANSION OC PHASE II - [N06000236],ECL, WEST BENGAL	11/2020	3/2025 (-) [3/2025]	888.99 (-) [888.99]	13.41 (0.00) [0]	0/0
63	NAKRAKONDA KUMARDIH B OCP - [N06000170],ECL, WEST BENGAL	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	37.77 (0.00) [0]	2/22
64	CHITRA EAST (RCE) OCP - [N06000169],ECL,JHARKHAND	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	168.07 (0.00) [0]	0/17
65	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185],ECL, WEST BENGAL	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	2.14 (0.00) [0]	0/22
66	GOPALJI-KANIHA OCP - [N06000229],MCL,ODISHA	8/2020	3/2028 (-) [3/2028]	8,416.19 (-) [8,416.19]	1,280.15 (0.00) [0]	0/0
67	GARJANBAHAL OCP - [N06000117],MCL,ODISHA	11/2014	3/2021 (-) [3/2026]	1,375.38 (-) [1,375.38]	734.15 (0.00) [60]	9/10
68	SUBHADRA OCP - [N06000249],MCL,ODISHA	5/2021	3/2027 (3/2029) [0/0]	1,693.81 (-) [1,693.81]	543.47 (0.00) [0]	0/0
69	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112],MCL,ODISHA	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	251.54 (0.00) [60]	3/9
70	BALARAM EXPANSION OCP - [N06000230],MCL,ODISHA	8/2020	3/2029 (-) [3/2029]	3,504.21 (-) [3,504.21]	620.60 (0.00) [0]	0/0
71	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171],MCL,ODISHA	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,355.67 (0.00) [0]	3/9
72	SIARMAL OCP (40.00MTY) - [N06000113],MCL,ODISHA	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	2,803.48 (0.00) [0]	11/15

73	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167],MCL,ODISHA	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	934.50 (0.00) [0]	4/12
74	ANANTA OCP EXPANSION PH III - [N06000225],MCL,ODISHA	8/2008	3/2012 (-) [0/0]	228.08 (-) [314.71]	323.51 (86.63) [0]	0/0
75	KULDA EXPANSION OCP- 15 MTY - [N06000248],MCL,ODISHA	6/2014	3/2018 (-) [3/2026]	348.16 (-) [348.16]	162.94 (0.00) [96]	0/0
76	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068],MCL,ODISHA	11/2008	3/2013 (-) [3/2024]	479.53 (-) [868.37]	874.49 (388.84) [132]	6/9
77	BHUBANESWARI EXPANSION OCP - [N06000227],MCL,ODISHA	8/2020	3/2031 (-) [3/2031]	3,145.45 (-) [3,145.45]	840.23 (0.00) [0]	0/0
78	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095],NLC,TAMIL NADU	6/2011	12/2015 (-) [2/2021]	5,907.11 (-) [7,980.79]	7,457.04 (2,073.68) [0]	35/35
79	TALABIRA II AND III OCP - [N06000189],NLC,ODISHA	7/2017	1/2027 (-) [1/2027]	2,401.07 (-) [2,401.07]	918.18 (0.00) [0]	19/22
80	PACHWARA SOUTH COAL BLOCK - [N06000193],NLC,JHARKHAND	7/2013	9/2028 (-) [9/2028]	1,795.01 (-) [1,795.01]	40.80 (0.00) [0]	5/11
81	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188],NLC,RAJASTHAN	3/2015	9/2020 (-) [0/0]	2,196.30 (-) [2,196.30]	112.92 (0.00) [0]	0/0
82	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144],NLC,RAJASTHAN	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]	0/0
83	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152],NLC,UTTAR PRADESH	7/2016	11/2021 (-) [11/2023]	17,237.00 (-) [17,237.80]	13,965.29 (0.80) [24]	21/48
84	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138],NLC,TAMIL NADU	4/2013	6/2015 (-) [9/2027]	1,458.17 (-) [709.06]	526.60 (-749.11) [147]	5/7
85	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187],NLC,RAJASTHAN	3/2015	9/2020 (-) [0/0]	2,112.60 (-) [2,112.60]	93.05 (0.00) [0]	0/0
86	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145],NLC,RAJASTHAN	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]	0/0
87	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159],NCL,MADHYA PRADESH	5/2017	3/2021 (-) [3/2023]	1,783.09 (-) [1,783.09]	1,197.65 (0.00) [24]	5/9
88	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184],NCL,MADHYA PRADESH	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	6.55 (0.00) [0]	1/7
89	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196],NCL,MADHYA PRADESH	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	36.27 (0.00) [0]	0/8
90	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192],NCL,MULTI STATE	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	138.51 (0.00) [0]	0/6
91	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162],NCL,MADHYA PRADESH	11/2017	3/2022 (-) [3/2023]	1,255.17 (-) [1,255.17]	846.30 (0.00) [12]	5/9
92	KHADIA EXPANSION OCP - [N06000208],NCL,UTTAR PRADESH	6/2021	3/2025 (-)	491.67 (-)	6.16 (0.00)	0/5

			[3/2025]	[491.67]	[0]	
93	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II - [N06000212],SCCL,TELANGANA	3/2019	3/2021 (-) [3/2023]	473.22 (-) [473.22]	392.38 (0.00) [24]	3/4
94	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210],SCCL,TELANGANA	11/2015	3/2023 (-) [3/2023]	489.62 (-) [489.62]	341.71 (0.00) [0]	0/3
95	RCE OF KISTARAM OPENCAST PROJECT - [N06000215],SCCL,TELANGANA	3/2017	3/2021 (-) [3/2023]	164.04 (-) [164.04]	143.08 (0.00) [24]	0/1
96	RCE OF INDARAM OPENCAST PROJECT - [N06000211],SCCL,TELANGANA	8/2017	3/2021 (-) [3/2023]	349.28 (-) [349.28]	323.72 (0.00) [24]	1/5
97	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213],SCCL,TELANGANA	3/2016	3/2020 (-) [3/2023]	384.32 (-) [384.32]	171.52 (0.00) [36]	0/3
98	VENKATESH KHANI COAL MINE - [N06000204],SCCL,TELANGANA	10/2020	3/2023 (-) [3/2024]	484.51 (-) [484.51]	36.25 (0.00) [12]	2/8
99	NAINI COAL MINE - [N06000203],SCCL,ODISHA	3/2020	3/2024 (-) [3/2024]	494.30 (-) [494.30]	282.84 (0.00) [0]	1/7
100	GODAVARIKHANI COAL MINE - [N06000202],SCCL,TELANGANA	7/2019	3/2023 (-) [3/2023]	438.98 (-) [438.98]	123.02 (0.00) [0]	6/11
101	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214],SCCL,TELANGANA	8/2017	3/2020 (-) [3/2024]	442.42 (-) [442.42]	129.91 (0.00) [48]	0/1
102	KAKATHIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161],SCCL,TELANGANA	3/2017	3/2022 (-) [3/2024]	413.84 (-) [413.84]	346.68 (0.00) [24]	7/11
103	SRP OC-II EXPANSION PROJECT - [N06000173],SCCL,TELANGANA	11/2016	3/2018 (-) [3/2024]	272.73 (-) [272.73]	153.75 (0.00) [72]	2/6
104	BATURA HIGHWALL PROJECT - [N06000134],SECL,MADHYA PRADESH	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	2.24 (0.00) [0]	1/10
105	AMGAON OPENCAST PROJECT RCE - [N06000135],SECL,CHHATISGARH	7/2015	3/2020 (-) [3/2023]	316.10 (-) [316.10]	154.35 (0.00) [36]	3/6
106	AMERA OC RCE - [N06000123],SECL,CHHATISGARH	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	48.55 (0.00) [60]	1/7
107	KUSMUNDA EXPN.OCP(SECL)(15- 50)MTY - [N06000008],SECL,CHHATISGARH	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	3,646.22 (0.00) [0]	13/22
108	AMRITDHARA OC PROJECT - [N06000122],SECL,MADHYA PRADESH	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]	3/10
109	PELMA OCP(15.00MTY) - [N06000045],SECL,CHHATISGARH	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	11.18 (0.00) [0]	1/12
110	KARTALI (EAST) OCP (2.50 MTY) - [N06000076],SECL,CHHATISGARH	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	16.13 (0.00) [144]	3/9
111	DURGAPUR OPENCAST PROJECT - [N06000136],SECL,CHHATISGARH	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	13.24 (0.00) [0]	2/12
112	AMADAND OPENCAST EXPANSION PROJECT - [N06000148],SECL,MADHYA PRADESH	3/2016	3/2021 (3/2025) [3/2025]	869.44 (-) [869.44]	163.63 (0.00) [48]	4/6
113	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232],SECL,CHHATISGARH	7/2016	3/2020 (-)	459.49 (-)	215.67 (0.00)	0/0

			[3/2022]	[459.49]	[0]	
114	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124],SECL,MADHYA PRADESH	12/2014	3/2021 (-) [3/2024]	357.80 (-) [357.80]	86.97 (0.00) [36]	4/10
115	KANCHAN OC EXPANSION - [N06000125],SECL,MADHYA PRADESH	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	87.70 (0.00) [36]	5/9
116	MAHAMAYA OPENCAST PROJECT - [N06000164],SECL,CHHATISGARH	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	79.53 (0.00) [0]	2/4
117	VIJAY WEST OPENCAST PROJECT - [N06000158],SECL,CHHATISGARH	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	87.36 (0.00) [0]	2/2
118	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199],SECL,CHHATISGARH	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]	0/0
119	DIPKA OC EXPANSION 40 MTY - [N06000200],SECL,CHHATISGARH	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	1,990.07 (0.00) [0]	0/0
120	JAMPALI OCP RCE - [N06000198],SECL,CHHATISGARH	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	182.09 (0.00) [0]	0/0
121	BAROUD OC EXPANSION (3-10 MTY) - [N06000197],SECL,CHHATISGARH	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	446.28 (0.00) [0]	0/0
122	RAMPUR BATURA OC (4.0 MTY) - [N06000233],SECL,MADHYA PRADESH	7/2019	3/2026 (-) [3/2026]	1,248.93 (-) [1,248.93]	297.19 (0.00) [0]	0/0
123	MADANNAGAR OPENCAST PROJECT - [N06000140],SECL,CHHATISGARH	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]	2/6
124	GEVRA EXPANSION OCP (SECL) (35- 70) MTY - [060100093],SECL,CHHATISGARH	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	5,180.64 (0.00) [0]	15/21
125	JHIRIA WEST OPENCAST PROJECT - [N06000166],SECL,CHHATISGARH	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	2.67 (0.00) [0]	3/5
126	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207],SECL,MADHYA PRADESH	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]	0/0
127	CHHAL OC SEAM -III (6.00 MTY) - [N06000104],SECL,CHHATISGARH	12/2013	3/2022 (3/2025) [3/2025]	610.63 (-) [610.63]	234.80 (0.00) [36]	4/11
128	BHANEGAON OC (1MTY) - [N06000221],WCL,MAHARASHTRA	2/2017	3/2023 (-) [3/2023]	409.68 (-) [409.68]	93.68 (0.00) [0]	0/1
129	GANDHIGRAM UG MINE - [N06000183],WCL,MADHYA PRADESH	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	21.89 (0.00) [0]	2/7
130	RPR FOR JAMUNIA UG - [N06000228],WCL,MADHYA PRADESH	8/2020	3/2026 (-) [3/2026]	281.25 (-) [281.25]	22.91 (0.00) [0]	0/4
131	TAWA III UG MINE - [N06000250],WCL,MADHYA PRADESH	12/2021	3/2027 (-) [3/2027]	324.25 (-) [324.25]	10.20 (0.00) [0]	0/5
132	NEW MAJRI UG TO OC - [N06000128],WCL,MAHARASHTRA	5/2015	3/2019 (-) [3/2022]	295.56 (-) [295.56]	220.94 (0.00) [0]	12/13
133	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157],WCL,MULTI STATE	2/2017	3/2021 (-) [9/2023]	328.00 (-) [328.00]	302.91 (0.00) [30]	5/6
134	UKNI DEEP OC - [N06000179],WCL,MAHARASHTRA	11/2018	3/2021 (-)	318.14 (-)	237.84 (0.00)	1/4

			[9/2022]	[318.14]	[18]	
135	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226],WCL,MAHARASHTRA	9/2018	3/2024 (-) [3/2024]	313.34 (-) [313.34]	169.46 (0.00) [0]	0/1
136	AMALGAMATED YEKONA-I YEKONA-II - [N06000132],WCL,MAHARASHTRA	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	465.37 (0.00) [0]	9/13
137	GAURI PAUNI EXPANSION OC - [N06000235],WCL,MAHARASHTRA	8/2020	3/2029 (-) [3/2029]	337.38 (-) [337.38]	48.04 (0.00) [0]	1/7
138	SINGHORI DEEP OC - [N06000252],WCL,MAHARASHTRA	5/2022	3/2029 (-) [3/2029]	421.84 (-) [421.84]	86.08 (0.00) [0]	0/0
139	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231],WCL,MAHARASHTRA	11/2020	3/2026 (-) [3/2026]	826.80 (-) [826.80]	314.10 (0.00) [0]	0/4
140	MAKARDHOKDA I EXPANSION OC - [N06000253],WCL,MAHARASHTRA	6/2022	3/2026 (-) [3/2026]	497.06 (-) [497.06]	135.18 (0.00) [0]	0/0
141	BHATADI EXPASION OC (0.975 MTY) - [N06000234],WCL,MAHARASHTRA	2/2016	3/2019 (-) [9/2026]	327.41 (-) [327.41]	176.39 (0.00) [90]	0/1
142	BELLORA-NAIGAON DEEP OC - [N06000180],WCL,MAHARASHTRA	11/2018	3/2021 (9/2022) [9/2022]	252.71 (-) [252.71]	108.78 (0.00) [18]	0/3
143	SASTI EXPANSION OC - [N06000206],WCL,MAHARASHTRA	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	52.55 (0.00) [0]	2/7
144	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154],WCL,MULTI STATE	8/2016	3/2022 (-) [3/2022]	319.76 (319.76) [319.76]	259.10 (0.00) [0]	0/3
145	DHANKASA UG (RECAST) (1 MTY) - [N06000224],WCL,MADHYA PRADESH	2/2020	3/2025 (-) [3/2025]	289.30 (-) [289.30]	40.60 (0.00) [0]	0/5
146	BHATADI EXPANSION OC - [N06000254],WCL,MAHARASHTRA	2/2020	3/2028 (-) [3/2028]	729.86 (-) [729.86]	149.25 (0.00) [0]	0/0
147	ADASA UG TO OC (1.50 MTY) - [N06000219],WCL,MAHARASHTRA	11/2018	3/2024 (-) [3/2024]	333.43 (-) [333.43]	173.40 (0.00) [0]	0/4
148	GHONSA EXPANSION DEEP OC - [N06000205],WCL,MAHARASHTRA	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	57.00 (0.00) [0]	0/7
149	VISHNUPURI UG TO OC MINE - [N06000178],WCL,MADHYA PRADESH	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]	0/7
150	SAONER UG MINE I EXPANSION - [N06000251],WCL,MAHARASHTRA	1/2022	3/2028 (-) [3/2028]	253.51 (-) [253.51]	24.86 (0.00) [0]	0/5
151	DHUPTALA OC(SASTI UG TO OC) - [N06000209],WCL,MAHARASHTRA	2/2019	3/2028 (-) [3/2028]	720.87 (-) [720.87]	131.28 (0.00) [0]	0/6
152	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222],WCL,MAHARASHTRA	2/2020	3/2027 (-) [3/2027]	1,184.33 (-) [1,184.33]	511.36 (0.00) [0]	1/8
	COMMERCE					
153	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003],NBCC FOR COMMER,DELHI	6/2018	10/2020 (-) [0/0]	302.64 (-) [302.64]	30.00 (0.00) [0]	0/0
	DEFENCE PRODUCTION					
154	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (8/2022)	246.31 (210.00)	181.63 (-46.31)	9/10

	- [N28000103],CPWD FOR DEFENC,KARNATAKA		[10/2022]	[200.00]	[32]	
	<u>DEPARTMENT OF HIGHER EDUCATION</u>					
155	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL - [N42000010],CPWD,KARNATAKA	8/2021	2/2024 (-) [2/2024]	316.25 (-) [316.25]	0.00 (0.00) [0]	1/2
156	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006],CPWD EDUCATION,KARNATAKA	7/2019	3/2022 (10/2022) [10/2022]	851.00 (851.00) [851.00]	466.32 (0.00) [7]	6/12
157	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140],CPWD EDUCATION,KERALA	7/2019	3/2021 (-) [3/2023]	753.63 (-) [753.63]	291.95 (0.00) [24]	2/11
158	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075],CPWD EDUCATION,KERALA	1/2010	10/2012 (-) [10/2012]	165.23 (-) [165.23]	136.31 (0.00) [0]	8/8
159	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005],CPWD EDUCATION,ANDHRA PRADESH	2/2019	6/2020 (-) [11/2022]	655.34 (-) [655.34]	469.33 (0.00) [29]	0/110
160	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009],CPWD EDUCATION,BIHAR	9/2018	9/2020 (-) [11/2022]	375.00 (-) [375.00]	175.10 (0.00) [26]	3/7
161	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130],CPWD EDUCATION,JAMMU AND KASHMIR	3/2019	7/2022 (10/2022) [10/2022]	424.93 (-) [424.93]	209.30 (0.00) [3]	0/14
162	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131],CPWD EDUCATION,JAMMU AND KASHMIR	1/2018	4/2023 (-) [4/2023]	676.00 (-) [676.00]	0.15 (0.00) [0]	0/1
163	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126],CPWD EDUCATION,ODISHA	1/2019	3/2022 (-) [1/2023]	790.79 (-) [790.79]	394.21 (0.00) [10]	1/5
164	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008],CPWD EDUCATION,HIMACHAL PRADESH	9/2018	6/2022 (4/2023) [4/2023]	392.51 (-) [392.51]	106.00 (0.00) [10]	0/2
165	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141],CPWD EDUCATION,CHHATISGARH	3/2020	7/2022 (-) [10/2022]	808.62 (-) [808.62]	536.84 (0.00) [3]	0/0
166	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120],CPWD EDUCATION,PUNJAB	1/2018	5/2020 (-) [12/2022]	430.00 (-) [387.83]	258.31 (-42.17) [31]	3/5
167	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. -	5/2019	3/2020 (-) [2/2023]	303.90 (334.45) [334.45]	140.00 (30.55) [35]	3/8

	[N42000002],CPWD EDUCATION,GOA					
168	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB - [N28000142],CPWD EDUCATION,PUNJAB	10/2019	5/2022 (-) [3/2023]	348.24 (-) [348.24]	81.58 (0.00) [10]	1/8
169	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146],CPWD EDUCATION,WEST BENGAL	3/2020	6/2020 (-) [12/2022]	193.83 (-) [193.83]	64.30 (0.00) [30]	0/14
170	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100],CPWD EDUCATION,BIHAR	2/2016	6/2017 (6/2022) [12/2022]	496.18 (496.00) [460.00]	342.91 (-36.18) [66]	3/6
171	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007],CPWD EDUCATION,ANDHRA PRADESH	9/2019	9/2022 (-) [7/2023]	588.72 (-) [588.72]	281.71 (0.00) [10]	4/9
172	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067],CPWD EDUCATION,JHARKHAND	9/2012	3/2016 (7/2022) [7/2022]	171.86 (171.86) [171.86]	151.07 (0.00) [0]	4/6
173	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117],CPWD EDUCATION,MAHARASHTRA	1/2018	7/2020 (-) [7/2020]	223.37 (-) [223.37]	61.35 (0.00) [0]	5/14
174	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001],RITES OF HIGHER,MEGHALAYA	9/2013	9/2014 (12/2022) [12/2022]	484.32 (429.70) [429.70]	242.25 (-54.62) [99]	0/0
	<u>DONER</u>					
175	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103],HSCL FOR DONER,MEGHALAYA	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	148.33 (0.00) [0]	12/15
	<u>DPIIT</u>					
176	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001],DMIC FOR DPIIT,MULTI STATE	9/2011	3/2027 (3/2027) [3/2027]	20,084.00 (20,084.00) [20,084.00]	9,680.31 (0.00) [0]	0/0
177	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002],IICC FOR DPIIT,DELHI	11/2017	12/2019 (-) [1/2023]	4,773.00 (-) [5,178.00]	3,032.83 (405.00) [37]	0/0
	<u>FERTILISERS</u>					
178	AN MELT PROJECT AT RCF TROMBAY - [N08000019],RCF,MAHARASHTRA	5/2022	9/2024 (-) [7/2024]	187.27 (-) [187.27]	0.80 (0.00) [-2]	0/0
	<u>FINANCE</u>					
179	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109],CPWD FOR FINANC,TAMIL NADU	11/2017	11/2021 (-) [0/0]	348.77 (-) [348.77]	270.69 (0.00) [0]	3/8
180	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS.	12/2015	10/2019 (10/2022)	209.00 (-)	208.93 (53.00)	2/6

	FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089],CPWD FOR FINANC,TAMIL NADU		[10/2022]	[262.00]	[36]	
181	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA - [N07000001],NPCC,DELHI	7/2018	4/2022 (-) [4/2022]	228.50 (220.27) [220.27]	182.43 (-8.23) [0]	6/15
	HEALTH AND FAMILY WELFARE					
182	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127],CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	6/2021 (-) [6/2021]	260.00 (-) [260.00]	25.38 (0.00) [0]	0/0
183	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029],CPWD FOR HEALTH,JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	667.78 (0.00) [0]	0/0
184	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098],CPWD FOR HEALTH,TELANGANA	10/2016	3/2020 (-) [0/0]	209.84 (-) [209.84]	228.52 (0.00) [0]	1/5
185	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139],CPWD FOR HEALTH,PONDICHERRY	3/2018	9/2020 (-) [0/0]	195.00 (-) [195.00]	16.41 (0.00) [0]	0/33
186	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112],CPWD FOR HEALTH,KERALA	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	88.39 (0.00) [0]	2/7
187	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150],CPWD FOR HEALTH,JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	303.17 (0.00) [-16]	0/0
188	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027],HITES,ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (890.14) [860.00]	528.81 (-15.00) [0]	0/0
189	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026],HITES,PUNJAB	7/2016	6/2020 (-) [0/0]	703.00 (-) [635.00]	575.00 (-68.00) [0]	0/0
190	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025],HITES,UTTAR PRADESH	7/2016	4/2020 (-) [0/0]	785.00 (-) [760.00]	672.98 (-25.00) [0]	0/0
191	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020],HSCC,ANDHRA PRADESH	3/2018	/ (-) [7/2022]	601.02 (-) [601.02]	578.84 (0.00) [0]	0/0
192	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024],HSCC,WEST BENGAL	4/2018	/ (-) [12/2021]	651.99 (-) [651.99]	622.18 (0.00) [0]	0/0
193	AIIMS - OPD(NEW) - [N21000009],HSCC,DELHI	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]	5/5
194	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023],HSCC,MAHARASHTRA	3/2018	/ (-) [12/2021]	582.99 (-) [582.99]	562.03 (0.00) [0]	0/0

195	NEIGRIHMS SHILLONG MEGHALYA - [N21000013],HSCC,MEGHALAYA	10/2016	5/2018 (-) [6/2022]	363.99 (-) [363.99]	299.13 (0.00) [0]	0/0
196	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019],HSCC,DELHI	12/2017	/ (-) [1/2022]	156.56 (-) [205.00]	145.94 (48.44) [0]	0/0
197	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012],HSCC,PUNJAB	7/2016	2/2018 (-) [4/2021]	152.95 (-) [177.92]	171.90 (24.97) [0]	1/1
198	LHMC NEW DELHI-RE- DEVELOPMENT - [N21000003],HSCC,DELHI	2/2013	11/2013 (-) [9/2021]	414.11 (-) [586.50]	586.50 (172.39) [0]	0/0
199	LGBRIMH-TEZPUR, ASSAM - [N21000007],HSCC,ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [179.15]	179.15 (3.58) [0]	0/0
200	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022],HSCC,GOA	1/2018	/ (-) [5/2021]	249.01 (-) [249.07]	244.64 (0.06) [0]	0/0
201	AIIMS - MOTHER AND CHILD BLOCK - [N21000008],HSCC,DELHI	12/2013	5/2017 (-) [6/2021]	204.44 (-) [285.00]	285.00 (80.56) [0]	2/2
202	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010],HSCC,WEST BENGAL	12/2014	5/2017 (-) [1/2021]	168.90 (-) [191.20]	182.10 (22.30) [0]	3/3
203	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018],HSCC,WEST BENGAL	8/2017	3/2019 (-) [12/2021]	355.15 (-) [355.15]	321.31 (0.00) [0]	0/0
204	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011],HSCC,HARYANA	9/2014	3/2018 (-) [4/2020]	505.58 (-) [586.96]	586.96 (81.38) [0]	2/2
205	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016],HSCC,MAHARASHTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	259.46 (0.00) [0]	0/0
206	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017],HSCC,ANDHRA PRADESH	8/2017	3/2019 (-) [2/2021]	272.19 (-) [280.00]	268.59 (7.81) [0]	0/0
207	CNCI KOLKATA WEST BENGAL - [N21000015],HSCC,WEST BENGAL	8/2016	9/2018 (-) [12/2021]	244.00 (-) [248.00]	224.92 (4.00) [0]	0/0
208	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021],HSCC,UTTAR PRADESH	3/2018	/ (-) [5/2021]	268.84 (-) [284.67]	269.92 (15.83) [0]	0/0
209	AIIMS BILASPUR - [N21000028],NBCC FOR HEALTH,HIMACHAL PRADESH	4/2018	9/2021 (-) [8/2022]	1,351.00 (-) [1,471.04]	1,162.76 (120.04) [11]	2/4
HOME AFFAIRS						
210	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" - [N28000147],CPWD FOR MHA,HARYANA	1/2020	10/2023 (3/2024) [3/2024]	166.98 (166.98) [166.98]	17.41 (0.00) [5]	0/12
211	NSG AT KOLKATA - [N28000104],CPWD FOR MHA,WEST BENGAL	10/2014	4/2018 (-) [9/2023]	162.88 (-) [210.83]	176.16 (47.95) [65]	6/7
212	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071],CPWD FOR MHA,DELHI	10/2013	10/2019 (-) [12/2022]	1,219.21 (-) [1,679.02]	1,036.04 (459.81) [38]	1/7

213	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003],CPWD FOR MHA,UTTAR PRADESH	5/2019	1/2022 (3/2023) [3/2023]	199.31 (-) [199.31]	98.57 (0.00) [14]	3/6
214	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002],CPWD FOR MHA,DELHI	6/2019	7/2022 (-) [6/2023]	277.35 (-) [290.33]	63.23 (12.98) [11]	3/6
	MINES					
215	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015],CPWD,WEST BENGAL	4/2019	4/2022 (-) [10/2024]	255.37 (-) [255.37]	26.26 (0.00) [30]	0/1
216	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012],NALCO,ODISHA	12/2015	11/2020 (12/2023) [12/2023]	355.00 (581.00) [581.00]	96.18 (226.00) [37]	3/3
217	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013],NALCO,ODISHA	11/2017	4/2021 (12/2023) [12/2023]	483.00 (483.00) [483.00]	59.47 (0.00) [32]	2/2
218	UTKAL D AND E COAL BLOCK - [N10000011],NALCO,ODISHA	5/2016	1/2020 (11/2023) [11/2023]	534.00 (667.23) [667.23]	497.21 (133.23) [46]	3/3
219	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010],NALCO,ODISHA	12/2014	4/2021 (1/2024) [1/2024]	4,103.00 (5,055.00) [5,055.00]	1,486.31 (952.00) [33]	4/4
220	POTTANGI BAUXITE MINES - [N10000016],NALCO,ODISHA	5/2018	12/2024 (12/2024) [12/2024]	1,437.00 (1,381.00) [1,381.00]	334.32 (-56.00) [0]	0/0
221	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014],NALCO,TAMIL NADU	9/2017	6/2019 (12/2022) [12/2022]	166.62 (163.17) [163.17]	135.00 (-3.45) [42]	1/1
	PETROLEUM					
222	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374],BPCL,ODISHA	8/2019	8/2022 (6/2023) [6/2023]	1,607.00 (-) [1,607.00]	507.46 (0.00) [10]	9/28
223	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI - [N16000452],BPCL,MAHARASHTRA	5/2022	3/2024 (-) [3/2024]	423.39 (-) [423.39]	36.46 (0.00) [0]	0/0
224	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410],BPCL,MAHARASHTRA	8/2020	3/2023 (-) [3/2023]	697.00 (-) [697.00]	486.80 (0.00) [0]	5/10
225	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442],BPCL,MAHARASHTRA	4/2021	6/2024 (-) [6/2024]	1,164.69 (-) [1,164.69]	58.88 (0.00) [0]	0/0
226	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373],BPCL,JHARKHAND	11/2018	6/2022 (3/2023) [3/2023]	248.55 (-) [248.55]	180.31 (0.00) [9]	7/16
227	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364],BPCL,ANDHRA PRADESH	7/2017	2/2021 (-) [3/2023]	580.20 (-) [580.20]	393.95 (0.00) [25]	6/16

228	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234],BPCL,TAMIL NADU	11/2012	2/2017 (8/2022) [9/2022]	678.00 (1,472.00) [1,472.00]	19.51 (794.00) [67]	0/0
229	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314],BPCL,KERALA	12/2015	6/2019 (2/2023) [2/2023]	1,112.00 (1,507.24) [1,507.24]	972.00 (395.24) [44]	1/3
230	CBR 9 MMTA PROJECT - [N16000434],CPCL,TAMIL NADU	1/2021	6/2025 (-) [6/2025]	31,580.00 (-) [31,580.00]	698.40 (0.00) [0]	9/50
231	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285],GAIL,MULTI STATE	6/2009	12/2012 (2/2025) [2/2025]	2,915.00 (5,909.00) [5,909.00]	3,570.80 (2,994.00) [146]	26/42
232	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272],GAIL,ODISHA	3/2017	12/2020 (11/2022) [11/2022]	1,933.00 (2,105.70) [2,105.70]	1,811.30 (172.70) [23]	21/24
233	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289],GAIL,ODISHA	7/2017	7/2022 (-) [8/2023]	243.53 (-) [243.53]	195.96 (0.00) [13]	10/10
234	DHAMRA HALDIA PIPELINE PROJECT - [N16000391],GAIL,MULTI STATE	3/2020	11/2022 (6/2023) [6/2023]	1,030.65 (-) [1,030.65]	448.70 (0.00) [7]	9/12
235	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389],GAIL,JHARKHAND	10/2017	10/2022 (-) [8/2023]	221.45 (-) [221.45]	129.91 (0.00) [10]	9/9
236	BARAUNI-GUWAHATI PIPELINE - [N16000334],GAIL,MULTI STATE	6/2018	12/2021 (6/2023) [6/2023]	3,308.00 (-) [3,308.00]	2,819.70 (0.00) [18]	18/20
237	BOKARO-ANGUL PIPELINE PROJECT - [N16000274],GAIL,MULTI STATE	3/2017	12/2020 (11/2022) [11/2022]	3,437.00 (-) [3,048.00]	2,444.60 (-389.00) [23]	21/24
238	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327],GAIL,BIHAR	10/2017	10/2022 (-) [10/2023]	359.25 (-) [359.25]	228.18 (0.00) [12]	10/10
239	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349],GAIL,GUJARAT	9/2018	2/2021 (-) [10/2022]	225.54 (-) [247.90]	154.74 (22.36) [20]	6/8
240	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388],GAIL,MULTI STATE	9/2019	7/2022 (7/2023) [7/2023]	2,658.34 (-) [2,658.34]	918.30 (0.00) [12]	11/14
241	60 KTA POLYPROPYLENE PROJECT - [N16000429],GAIL,UTTAR PRADESH	3/2019	4/2024 (-) [4/2024]	910.56 (-) [910.56]	213.00 (0.00) [0]	10/17
242	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398],GAIL,MULTI STATE	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	2,903.70 (0.00) [0]	18/29
243	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329],GAIL,JHARKHAND	10/2017	10/2022 (-) [3/2023]	226.45 (-) [226.45]	179.25 (0.00) [5]	19/19
244	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355],GAIL,HARYANA	8/2018	8/2020 (6/2022) [12/2022]	286.42 (327.00) [327.01]	255.10 (40.59) [28]	14/16
245	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328],GAIL,ODISHA	7/2017	7/2022 (-) [8/2023]	182.20 (-) [182.20]	115.16 (0.00) [13]	9/9
246	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430],GAIL,MAHARASHTRA	5/2019	4/2025 (-) [4/2025]	8,797.00 (-) [8,797.00]	397.00 (0.00) [0]	14/20
247	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275],GAIL,WEST BENGAL	3/2017	12/2020 (6/2023) [6/2023]	1,740.00 (-) [1,740.00]	1,084.40 (0.00) [30]	15/24

248	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390],GAIL,UTTAR PRADESH	8/2018	4/2021 (12/2022) [12/2022]	217.92 (-) [217.92]	126.20 (0.00) [20]	12/14
249	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385],HPCL,HARYANA	9/2018	9/2026 (-) [2/2027]	520.00 (-) [520.00]	275.43 (0.00) [5]	43/52
250	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402],HPCL,PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,421.46]	502.70 (0.00) [0]	16/22
251	SWRO II WITH LLPH FACILITIES - [N16000378],HPCL,ANDHRA PRADESH	9/2019	7/2020 (-) [0/0]	196.26 (-) [196.26]	125.93 (0.00) [0]	1/5
252	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413],HPCL,CHHATISGARH	3/2021	3/2024 (-) [3/2024]	456.00 (-) [456.00]	113.39 (0.00) [0]	14/62
253	EXTENSION OF VISAKH- VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296],HPCL,MULTI STATE	9/2017	6/2021 (8/2022) [8/2022]	2,677.00 (3,185.00) [3,185.00]	2,943.70 (508.00) [14]	26/26
254	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392],HPCL,WEST BENGAL	3/2019	3/2031 (-) [8/2031]	5,830.20 (-) [5,830.20]	301.79 (0.00) [5]	31/50
255	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432],HPCL,ANDHRA PRADESH	9/2021	6/2024 (-) [6/2024]	160.00 (-) [160.00]	0.13 (0.00) [0]	2/13
256	VISAKH REFINERY MODERNISATION PROJECT - [N16000235],HPCL,ANDHRA PRADESH	7/2016	7/2020 (-) [3/2023]	20,928.00 (-) [26,264.00]	20,025.46 (5,336.00) [32]	100/111
257	NEW LPG PLANT AT VARANASI - [N16000447],HPCL,UTTAR PRADESH	8/2017	5/2024 (-) [5/2024]	194.62 (-) [194.62]	61.25 (0.00) [0]	0/20
258	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369],HPCL,KARNATAKA	12/2018	12/2022 (12/2023) [12/2023]	854.00 (-) [854.00]	235.86 (0.00) [12]	15/19
259	BARMER PALANPUR PIPELINE - [N16000384],HPCL,MULTI STATE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	567.76 (0.00) [0]	18/20
260	RUF PITCH LOADING GANTRY - [N16000406],HPCL,ANDHRA PRADESH	10/2020	11/2022 (-) [3/2023]	332.61 (-) [332.61]	32.33 (0.00) [4]	6/12
261	BHATINDA SANGRUR PIPELINE - [N16000440],HPCL,PUNJAB	11/2021	4/2024 (-) [4/2024]	367.00 (-) [367.00]	7.07 (0.00) [0]	0/0
262	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315],HPCL,MAHARASHTRA	6/2017	6/2020 (-) [9/2022]	249.26 (-) [249.26]	249.10 (0.00) [27]	7/12
263	SULPHUR FORMING UNIT IN SRU - [N16000408],HPCL,ANDHRA PRADESH	10/2020	8/2021 (-) [12/2022]	210.94 (-) [210.94]	139.97 (0.00) [16]	1/6
264	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387],HPCL,UTTAR PRADESH	3/2019	3/2029 (-) [8/2029]	3,450.20 (-) [3,450.20]	763.70 (0.00) [5]	34/64
265	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367],HPCL,KARNATAKA	6/2019	6/2022 (-) [10/2022]	2,166.38 (-) [2,166.38]	1,762.67 (0.00) [4]	17/18

266	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI - [N16000438],IISCO,TAMIL NADU	1/2022	7/2024 (-) [7/2024]	827.00 (-) [827.00]	63.86 (0.00) [0]	0/0
267	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326],IOCL,GUJARAT	10/2017	2/2020 (7/2022) [9/2022]	906.00 (-) [906.00]	423.21 (0.00) [31]	7/8
268	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM - [N16000441],IOCL,ASSAM	3/2022	7/2026 (-) [7/2026]	277.00 (-) [277.00]	0.00 (0.00) [0]	0/0
269	R and D CAMPUS II AT FARIDABAD - [N16000375],IOCL,HARYANA	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (3,219.94) [2,281.94]	804.64 (0.00) [7]	4/7
270	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414],IOCL,ASSAM	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	49.33 (0.00) [0]	4/10
271	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324],IOCL,BIHAR	12/2017	10/2020 (8/2022) [8/2023]	199.36 (-) [199.36]	118.68 (0.00) [34]	2/2
272	SITARGANJ LPG PROJECT - [N16000282],IOCL,UTTARAKHAND	2/2017	2/2020 (10/2022) [10/2022]	160.10 (-) [160.10]	115.53 (0.00) [32]	19/26
273	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382],IOCL,GUJARAT	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	1,472.17 (0.00) [0]	6/11
274	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403],IOCL,TAMIL NADU	10/2020	9/2023 (-) [2/2024]	921.00 (-) [921.00]	61.75 (0.00) [5]	0/0
275	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424],IOCL,BIHAR	6/2019	2/2028 (8/2029) [8/2029]	347.00 (-) [347.00]	125.47 (0.00) [18]	0/0
276	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393],IOCL,WEST BENGAL	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	309.35 (0.00) [0]	4/6
277	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395],IOCL,ODISHA	1/2020	7/2022 (-) [3/2023]	202.16 (-) [202.16]	129.65 (0.00) [8]	3/4
278	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI - [N16000453],IOCL,BIHAR	1/2022	9/2024 (-) [9/2024]	389.00 (-) [389.00]	0.00 (0.00) [0]	0/0
279	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342],IOCL,ANDHRA PRADESH	8/2018	4/2021 (9/2022) [9/2022]	466.00 (-) [466.00]	343.45 (0.00) [17]	0/0
280	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412],IOCL,HARYANA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	818.04 (0.00) [0]	8/9
281	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333],IOCL,UTTAR PRADESH	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	614.47 (0.00) [0]	3/3

282	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363],IOCL,HARYANA	12/2018	6/2021 (7/2022) [3/2023]	278.60 (-) [278.60]	160.73 (0.00) [21]	3/5
283	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT - [N16000336],IOCL,GUJARAT	3/2018	/ (3/2023) [3/2023]	588.20 (-) [730.20]	303.77 (142.00) [-]	13/17
284	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376],IOCL,HARYANA	8/2019	12/2021 (1/2023) [1/2023]	1,255.00 (-) [1,255.00]	661.56 (0.00) [13]	5/7
285	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321],IOCL,HARYANA	4/2018	2/2020 (2/2023) [2/2023]	206.63 (340.76) [340.76]	220.01 (134.13) [36]	6/7
286	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE - [N16000451],IOCL,TAMIL NADU	3/2022	11/2024 (-) [11/2024]	564.00 (-) [564.00]	0.00 (0.00) [0]	0/0
287	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418],IOCL,TAMIL NADU	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	234.49 (0.00) [0]	0/0
288	KHARAGPUR LPG BOTTLING PLANT - [N16000300],IOCL,WEST BENGAL	4/2017	4/2020 (10/2022) [10/2022]	163.02 (207.36) [207.36]	152.03 (44.34) [30]	21/26
289	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353],IOCL,HARYANA	10/2018	2/2020 (7/2022) [12/2022]	598.00 (753.89) [753.89]	602.73 (155.89) [34]	4/5
290	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303],IOCL,UTTAR PRADESH	8/2017	8/2021 (3/2023) [3/2023]	318.80 (-) [318.80]	210.47 (0.00) [19]	0/0
291	LPG BP PROJECT JODHPUR - [N16000318],IOCL,RAJASTHAN	3/2018	/ (3/2023) [3/2023]	229.80 (-) [229.80]	130.21 (0.00) [-]	18/26
292	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416],IOCL,JHARKHAND	10/2018	12/2029 (3/2030) [3/2030]	613.00 (-) [613.00]	191.24 (0.00) [3]	0/0
293	PARADIP HYDERABAD PIPELINE - [N16000194],IOCL,MULTI STATE	1/2015	12/2020 (2/2023) [12/2022]	2,321.00 (3,338.00) [3,338.00]	3,250.17 (1,017.00) [24]	5/5
294	LPG BP PROJECT KHORDHA - [N16000283],IOCL,ODISHA	12/2016	12/2019 (1/2023) [1/2023]	161.59 (-) [161.59]	101.66 (0.00) [37]	18/26
295	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352],IOCL,HARYANA	1/2019	1/2021 (8/2022) [11/2022]	909.00 (-) [909.00]	680.30 (0.00) [22]	5/6
296	LPG TERMINAL AT KOCHI - [N16000171],IOCL,KERALA	10/2015	10/2017 (3/2022) [12/2022]	607.06 (1,236.00) [1,236.00]	684.72 (628.94) [62]	46/52
297	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY - [N16000446],IOCL,MAHARASHTRA	9/2021	10/2023 (-) [10/2023]	378.00 (-) [378.00]	60.31 (0.00) [0]	0/0
298	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405],IOCL,TAMIL NADU	10/2020	12/2023 (-) [2/2024]	1,398.00 (-) [1,398.00]	290.30 (0.00) [2]	0/0

299	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435],IOCL,RAJASTHAN	12/2021	10/2024 (-) [10/2024]	9,028.00 (-) [9,028.00]	58.89 (0.00) [0]	0/0
300	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415],IOCL,BIHAR	10/2018	8/2027 (2/2029) [2/2029]	176.00 (-) [176.00]	110.40 (0.00) [18]	0/0
301	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340],IOCL,HARYANA	8/2018	8/2020 (4/2022) [12/2022]	1,636.00 (-) [1,636.00]	1,097.83 (0.00) [28]	6/7
302	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332],IOCL,WEST BENGAL	3/2018	9/2022 (2/2023) [2/2023]	3,712.00 (3,696.00) [3,696.00]	2,638.70 (-16.00) [5]	3/3
303	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350],IOCL,ANDHRA PRADESH	10/2018	10/2021 (9/2022) [9/2022]	316.20 (-) [316.20]	183.14 (0.00) [11]	0/0
304	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162],IOCL,TAMIL NADU	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]	0/0
305	CGD PROJECT AT SALEM DISTRICT - [N16000419],IOCL,TAMIL NADU	10/2018	3/2030 (-) [3/2030]	1,304.00 (-) [1,304.00]	65.64 (0.00) [0]	0/0
306	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425],IOCL,BIHAR	6/2019	2/2028 (8/2029) [8/2029]	2,996.00 (-) [2,996.00]	395.60 (0.00) [18]	0/0
307	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249],IOCL,MAHARASHTRA	5/2016	2/2022 (8/2022) [12/2022]	1,945.00 (2,145.00) [2,145.00]	1,801.97 (200.00) [10]	5/5
308	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422],IOCL,BIHAR	6/2019	2/2028 (8/2029) [8/2029]	439.00 (-) [439.00]	147.85 (0.00) [18]	0/0
309	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368],IOCL,ODISHA	6/2019	9/2022 (3/2023) [3/2023]	371.00 (427.10) [427.10]	99.98 (56.10) [6]	6/8
310	CGD PROJECT AT REWA DISTRICT - [N16000417],IOCL,MADHYA PRADESH	10/2018	2/2027 (9/2028) [9/2028]	177.00 (-) [177.00]	82.58 (0.00) [19]	0/0
311	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409],IOCL,GUJARAT	9/2020	9/2024 (-) [8/2024]	18,936.00 (-) [18,936.00]	1,433.13 (0.00) [-1]	9/15
312	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323],IOCL,UTTAR PRADESH	8/2017	8/2020 (11/2022) [11/2022]	255.40 (-) [255.40]	188.28 (0.00) [27]	3/3
313	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427],IOCL,MULTI STATE	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	154.30 (0.00) [0]	0/0
314	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345],IOCL,ODISHA	10/2018	10/2021 (7/2022) [12/2022]	1,297.50 (-) [1,297.50]	1,004.24 (0.00) [14]	1/1
315	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343],IOCL,ANDHRA PRADESH	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	150.41 (0.00) [10]	0/0
316	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED	1/2022	9/2024 (-)	328.00 (-)	1.55 (0.00)	0/0

	FACILITIES AT GUJARAT - [N16000454],IOCL,GUJARAT		[9/2024]	[328.00]	[0]	
317	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383],IOCL,HARYANA	9/2019	7/2021 (3/2022) [6/2023]	164.69 (-) [164.69]	81.34 (0.00) [23]	4/9
318	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386],IOCL,BIHAR	1/2020	4/2023 (-) [7/2024]	14,810.00 (-) [14,810.00]	3,834.49 (0.00) [15]	4/7
319	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361],IOCL,ODISHA	11/2018	9/2021 (12/2022) [12/2022]	462.30 (543.00) [543.00]	291.80 (80.70) [15]	4/5
320	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253],IOCL,TAMIL NADU	5/2016	12/2018 (11/2023) [11/2023]	4,497.00 (6,025.00) [6,025.00]	4,938.92 (1,528.00) [59]	5/5
321	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396],IOCL,ODISHA	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	1,266.59 (0.00) [0]	7/12
322	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423],IOCL,BIHAR	6/2019	12/2029 (3/2030) [3/2030]	163.00 (-) [163.00]	42.34 (0.00) [3]	0/0
323	LPG BP PROJECT CHITTOOR - [N16000381],IOCL,ANDHRA PRADESH	7/2019	7/2022 (6/2023) [6/2023]	167.00 (-) [167.00]	47.33 (0.00) [11]	0/5
324	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426],IOCL,MULTI STATE	6/2019	12/2029 (3/2030) [3/2030]	169.00 (-) [169.00]	48.73 (0.00) [3]	0/0
325	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411],IOCL,GUJARAT	10/2020	8/2023 (-) [8/2023]	1,614.00 (-) [1,614.00]	173.85 (0.00) [0]	0/0
326	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268],IOCL,MAHARASHTRA	5/2016	1/2021 (-) [12/2022]	348.00 (437.00) [437.00]	271.34 (89.00) [23]	0/0
327	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420],IOCL,ANDHRA PRADESH	6/2019	8/2027 (3/2030) [3/2030]	2,880.00 (-) [2,880.00]	139.21 (0.00) [31]	0/0
328	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351],IOCL,TELANGANA	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	193.17 (0.00) [16]	0/0
329	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338],IOCL,ODISHA	4/2018	10/2021 (7/2022) [12/2022]	5,654.00 (-) [5,654.00]	3,885.24 (0.00) [14]	9/10
330	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE - [N16000437],IOCL,KARNATAKA	1/2022	7/2025 (-) [7/2025]	463.00 (-) [463.00]	19.27 (0.00) [0]	0/0
331	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421],IOCL,BIHAR	6/2019	12/2029 (3/2030) [3/2030]	988.00 (-) [988.00]	57.14 (0.00) [3]	0/0
332	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400],IOCL,GUJARAT	6/2020	12/2022 (-) [12/2022]	1,378.00 (-) [1,378.00]	441.50 (0.00) [0]	0/0
333	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-)	403.00 (-)	213.43 (0.00)	0/2

	- [N16000399],IOCL,BIHAR		[12/2022]	[403.00]	[4]	
334	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362],IOCL,ODISHA	5/2019	8/2021 (9/2022) [3/2024]	3,361.00 (-) [3,361.00]	2,258.02 (0.00) [31]	7/11
335	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193],IOCL,MULTI STATE	1/2015	3/2021 (6/2022) [10/2022]	1,823.00 (3,027.90) [3,027.90]	2,446.06 (1,204.90) [19]	5/5
336	NORTH EAST GAS GRID - [N16000439],IGGL,MULTI STATE	11/2020	3/2024 (3/2024) [3/2024]	9,265.00 (9,265.00) [9,265.00]	2,431.15 (0.00) [0]	9/18
337	DEVANGONTHI MARKETING TERMINAL - [N16000401],MANGALORE REFIN,KARNATAKA	6/2020	6/2023 (1/2024) [1/2024]	200.00 (304.00) [304.00]	41.00 (104.00) [7]	3/6
338	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394],NRL,ASSAM	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	3,273.73 (-1,170.00) [0]	6/20
339	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379],NRL,ASSAM	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	1,929.71 (6,602.00) [0]	7/14
340	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357],ONGC,MAHARASHTRA	2/2019	5/2021 (12/2022) [12/2022]	2,292.46 (-) [2,292.46]	2,311.32 (0.00) [19]	5/6
341	CREATION OF GAS DEHYDRATION FACILITIES - [N16000443],ONGC,TRIPURA	3/2022	5/2024 (-) [5/2024]	209.33 (-) [209.33]	0.00 (0.00) [0]	1/2
342	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) - [N16000445],ONGC,JHARKHAND	11/2019	1/2024 (-) [1/2024]	431.00 (-) [431.00]	29.95 (0.00) [0]	1/3
343	REDEVELOPMENT OF LINCH FIELD - [N16000428],ONGC,GUJARAT	4/2021	3/2025 (-) [3/2025]	631.03 (-) [631.03]	212.55 (0.00) [0]	0/2
344	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247],ONGC,ANDHRA PRADESH	3/2016	6/2020 (5/2023) [5/2023]	34,012.00 (-) [31,040.00]	19,243.11 (-2,972.00) [35]	15/20
345	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128],ONGC,MAHARASHTRA	3/2011	5/2013 (12/2022) [12/2022]	861.79 (2,001.34) [2,001.34]	1,680.76 (1,139.55) [115]	7/8
346	REDEVELOPMENT OF NANDASAN FIELD - [N16000404],ONGC,GUJARAT	2/2020	8/2022 (2/2023) [2/2023]	444.87 (-) [444.87]	338.56 (0.00) [6]	5/6
347	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213],ONGC,MAHARASHTRA	12/2015	4/2018 (5/2023) [5/2023]	3,190.69 (3,375.90) [3,375.90]	2,911.17 (185.21) [61]	13/15
348	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD - [N16000444],ONGC,GUJARAT	1/2022	11/2024 (-) [11/2024]	621.40 (-) [621.40]	72.69 (0.00) [0]	0/2
349	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241],ONGC,TAMIL NADU	11/2015	3/2019 (9/2021) [12/2022]	650.82 (-) [650.82]	462.08 (0.00) [45]	4/6
350	REDEVELOPMENT OF SANTHAL FIELD - [N16000279],ONGC,GUJARAT	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [1,162.56]	915.64 (0.00) [0]	9/10
351	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-)	218.38 (-)	35.16 (0.00)	3/5

	- [N16000433],ONGC,ASSAM		[2/2023]	[218.38]	[0]	
352	HEERA REDEVELOPMENT - PHASE III - [N16000360],ONGC,MAHARASHTRA	6/2019	3/2022 (3/2023) [3/2023]	2,494.68 (-) [2,494.68]	2,141.49 (0.00) [12]	5/6
353	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370],ONGC,MAHARASHTRA	5/2019	12/2020 (12/2022) [12/2022]	763.92 (-) [829.58]	830.87 (65.66) [24]	4/5
354	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358],ONGC,MAHARASHTRA	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	2,816.87 (747.87) [14]	4/6
355	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431],ONGC,GUJARAT	8/2021	2/2026 (-) [2/2026]	885.63 (-) [885.63]	231.36 (0.00) [0]	0/2
356	PIPELINE REPLACEMENT PROJECT - VII - [N16000436],ONGC,MAHARASHTRA	1/2022	5/2024 (-) [5/2024]	3,183.58 (-) [3,183.58]	123.40 (0.00) [0]	4/5
357	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239],ONGC,JHARKHAND	12/2015	3/2023 (3/2022) [3/2023]	823.27 (1,137.79) [1,137.79]	848.08 (314.52) [0]	9/11
358	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331],OIL,ASSAM	1/2018	2/2020 (12/2022) [12/2022]	543.91 (-) [638.60]	423.10 (94.69) [34]	1/14
359	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING - [N16000450],OIL,ASSAM	12/2020	7/2024 (-) [7/2024]	430.76 (-) [430.76]	8.66 (0.00) [0]	0/0
360	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT - [N16000449],OIL,ASSAM	6/2021	12/2024 (-) [12/2024]	860.00 (-) [860.00]	20.10 (0.00) [0]	0/0
	POWER					
361	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172],CVPPPL,JAMMU AND KASHMIR	10/2014	4/2020 (7/2025) [7/2025]	8,112.12 (-) [8,112.12]	2,449.04 (0.00) [63]	0/0
362	KIRU HYDRO ELECTRIC PROJECT - [N18000278],CVPPPL,JAMMU AND KASHMIR	3/2019	/ (8/2024) [7/2025]	4,287.59 (-) [4,287.59]	793.45 (0.00) [-]	0/0
363	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221],NHPC,ARUNACHAL PRADESH	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	16,222.78 (13,707.10) [155]	0/0
364	RATLE HE PROJECT - [N18000324],NHPC,JAMMU AND KASHMIR	2/2021	2/2026 (2/2026) [2/2026]	5,281.94 (5,281.94) [5,281.94]	43.55 (0.00) [0]	0/0
365	TEESTA VI HE PROJECT - [N18000325],NHPC,SIKKIM	3/2019	3/2024 (-) [7/2025]	5,748.04 (-) [5,748.04]	1,748.06 (0.00) [16]	0/0
366	PARBATI HEP (4X200 MW) (NHPC) II - [180100210],NHPC,HIMACHAL PRADESH	9/2002	9/2009 (12/2023) [12/2023]	3,919.59 (10,463.03) [10,463.03]	10,010.30 (6,543.44) [171]	5/5
367	RANGIT IV HE PROJECT - [N18000326],NHPC,SIKKIM	3/2021	5/2024 (8/2024) [8/2024]	938.29 (938.29) [938.29]	315.06 (0.00) [3]	0/0
368	KALPI SOLAR POWER PROJECT - [N18000323],NHPC,UTTAR PRADESH	7/2020	3/2022 (12/2022) [12/2022]	314.64 (335.36) [337.77]	218.26 (23.13) [9]	0/0
369	DEVIKOT SOLAR 90MW - [N18000280],NTPC,UTTAR PRADESH	3/2020	9/2021 (1/2023) [9/2022]	501.29 (-) [524.83]	506.75 (23.54) [12]	0/0

370	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296],NTPC,GUJARAT	5/2021	9/2022 (-) [8/2023]	674.92 (-) [674.92]	76.91 (0.00) [11]	0/0
371	BARH STPP(3X660MW) NTPC - [180100242],NTPC,BIHAR	2/2005	10/2011 (7/2023) [3/2024]	8,692.97 (21,312.11) [21,312.11]	20,184.00 (12,619.14) [149]	35/49
372	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322],NTPC,RAJASTHAN	3/2022	8/2023 (10/2023) [10/2023]	1,426.94 (-) [1,426.94]	49.14 (0.00) [2]	0/0
373	DAYAPAR WIND ENERGY PROJECT 150MW - [N18000319],NTPC,GUJARAT	11/2021	5/2023 (-) [5/2023]	937.80 (-) [937.80]	102.21 (0.00) [0]	0/0
374	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014],NTPC,UTTARAKHAND	11/2006	3/2013 (12/2021) [12/2024]	2,978.48 (5,867.38) [7,103.00]	5,489.00 (4,124.52) [141]	8/15
375	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212],NTPC,TELANGANA	1/2016	11/2020 (7/2022) [6/2023]	10,598.98 (-) [10,998.00]	9,540.00 (399.02) [31]	32/39
376	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321],NTPC,RAJASTHAN	3/2022	8/2023 (10/2023) [10/2023]	1,409.52 (-) [1,409.52]	50.84 (0.00) [2]	0/0
377	CHHATTARGARH 150 MW - [N18000294],NTPC,RAJASTHAN	2/2021	7/2022 (-) [8/2023]	599.99 (-) [599.99]	170.95 (0.00) [13]	0/0
378	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286],NTPC,RAJASTHAN	3/2020	9/2021 (1/2023) [1/2023]	1,782.00 (-) [1,782.00]	1,146.84 (0.00) [16]	0/0
379	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320],NTPC,RAJASTHAN	3/2022	8/2023 (10/2023) [10/2023]	1,352.71 (-) [1,352.71]	41.85 (0.00) [2]	0/0
380	PATRATU STPP-I (3X800MW) - [N18000275],NTPC,JHARKHAND	11/2017	3/2023 (-) [3/2025]	18,668.00 (-) [18,668.00]	8,846.25 (0.00) [24]	4/23
381	GUJARAT 200 MW (GUVNL TENDER) - [N18000295],NTPC,GUJARAT	1/2021	7/2022 (10/2022) [8/2023]	842.27 (-) [842.27]	92.08 (0.00) [13]	0/0
382	ANTA SOLAR 90 MW - [N18000292],NTPC,RAJASTHAN	1/2021	3/2022 (12/2023) [3/2023]	382.22 (-) [382.22]	36.61 (0.00) [12]	0/0
383	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142],NTPC,UTTARAKHAND	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,527.00]	149.93 (0.00) [0]	0/15
384	DEVIKOT SOLAR 150MW - [N18000281],NTPC,UTTAR PRADESH	1/2020	9/2021 (11/2022) [9/2022]	798.24 (-) [852.90]	637.22 (54.66) [12]	0/0
385	ETTAYAPURAM SOLAR 230MW - [N18000290],NTPC,TAMIL NADU	3/2020	9/2021 (11/2022) [10/2022]	1,316.22 (-) [1,316.22]	1,059.63 (0.00) [13]	0/0
386	KAWAS SOLAR 56 MW - [N18000283],NTPC,GUJARAT	8/2020	10/2021 (1/2023) [8/2022]	261.80 (-) [293.03]	243.32 (31.23) [10]	0/0
387	NOKHRA - [N18000282],NTPC,UTTAR PRADESH	3/2020	9/2021 (1/2023) [1/2023]	1,722.14 (-) [1,803.19]	1,193.45 (81.05) [16]	0/0
388	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277],NTPC,WEST BENGAL	12/2016	11/2018 (12/2022) [12/2022]	529.68 (633.80) [679.00]	549.68 (149.32) [49]	12/20
389	BHENSARA 320 MW - [N18000293],NTPC,RAJASTHAN	1/2021	7/2022 (-) [8/2023]	1,221.73 (-) [1,221.73]	146.13 (0.00) [13]	0/0
390	NORTH KARANPURA STPP (3X660 MW) - [N18000177],NTPC,JHARKHAND	2/2014	6/2019 (10/2022) [12/2024]	14,366.58 (-) [17,007.00]	13,203.00 (2,640.42) [66]	31/46

391	RAMMAM-III HEPP (3X40 MW) - [N18000178],NTPC,WEST BENGAL	9/2014	9/2019 (12/2024) [7/2025]	1,381.84 (-) [1,803.00]	809.11 (421.16) [70]	6/10
392	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264],PGCIL,MULTI STATE	8/2017	2/2020 (-) [4/2023]	1,931.39 (-) [2,635.55]	1,891.34 (704.16) [38]	0/0
393	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308],PGCIL,MULTI STATE	2/2019	12/2020 (-) [3/2023]	572.98 (-) [572.98]	293.86 (0.00) [27]	0/0
394	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299],PGCIL,BIHAR	5/2021	4/2023 (-) [4/2023]	179.29 (-) [179.29]	79.99 (0.00) [0]	0/0
395	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR- LEH TRANSMISSION SYSTEM - [N18000330],PGCIL,MULTI STATE	3/2022	12/2024 (-) [12/2024]	288.71 (-) [288.71]	0.00 (0.00) [0]	0/0
396	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000331],PGCIL,MULTI STATE	2/2022	9/2023 (-) [9/2023]	359.47 (-) [359.47]	9.29 (0.00) [0]	0/0
397	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C - [N18000338],PGCIL,MULTI STATE	7/2022	3/2025 (-) [3/2025]	186.19 (-) [186.19]	0.00 (0.00) [0]	0/0
398	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM - [N18000328],PGCIL,MULTI STATE	2/2022	4/2025 (-) [4/2025]	318.12 (-) [318.12]	45.42 (0.00) [0]	0/0
399	EASTERN REGION STRENGTHENING SCHEME -XVIII - [N18000258],PGCIL,MULTI STATE	3/2017	7/2020 (-) [8/2022]	3,500.00 (3,500.00) [3,994.00]	3,160.77 (494.00) [25]	0/0
400	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316],PGCIL,MULTI STATE	5/2021	3/2023 (-) [3/2023]	576.42 (-) [576.42]	54.00 (0.00) [0]	0/0
401	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315],PGCIL,MULTI STATE	7/2020	6/2021 (-) [4/2022]	239.89 (-) [239.89]	163.02 (0.00) [0]	0/0
402	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305],PGCIL,RAJASTHAN	6/2021	12/2022 (-) [12/2023]	713.82 (-) [713.82]	323.37 (0.00) [12]	0/0
403	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262],PGCIL,TAMIL NADU	5/2017	7/2019 (-) [12/2022]	186.17 (-) [219.66]	172.19 (33.49) [41]	0/0
404	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303],PGCIL,RAJASTHAN	3/2021	12/2022 (-) [9/2023]	353.85 (-) [353.85]	134.19 (0.00) [9]	0/0
405	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184],PGCIL,MULTI STATE	3/2015	3/2018 (-) [12/2022]	197.40 (-) [197.40]	195.47 (0.00) [57]	0/0

406	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249],PGCIL,MULTI STATE	12/2014	12/2018 (-) [3/2024]	4,754.42 (-) [9,129.32]	4,251.79 (4,374.90) [63]	0/0
407	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD - [N18000314],PGCIL,RAJASTHAN	1/2020	1/2021 (-) [12/2022]	562.86 (-) [562.86]	374.60 (0.00) [23]	0/0
408	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B - [N18000337],PGCIL,MULTI STATE	7/2022	6/2023 (-) [6/2023]	4,546.26 (-) [4,546.26]	21.50 (0.00) [0]	0/0
409	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327],PGCIL,ASSAM	3/2019	3/2023 (-) [3/2023]	1,326.00 (-) [1,326.00]	1,054.46 (0.00) [0]	0/0
410	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317],PGCIL,MULTI STATE	11/2018	11/2021 (-) [12/2022]	241.38 (-) [241.38]	223.80 (0.00) [13]	0/0
411	EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244],PGCIL,MULTI STATE	2/2017	6/2019 (-) [12/2022]	235.53 (-) [235.53]	164.87 (0.00) [42]	0/0
412	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242],PGCIL,MULTI STATE	2/2017	2/2019 (-) [12/2022]	322.30 (-) [322.30]	210.54 (0.00) [46]	0/0
413	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332],PGCIL,MULTI STATE	5/2022	11/2023 (-) [11/2023]	1,666.00 (-) [1,666.00]	0.00 (0.00) [0]	0/0
414	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION - [N18000339],PGCIL,MULTI STATE	11/2018	11/2021 (-) [9/2022]	173.94 (-) [173.94]	114.48 (0.00) [10]	0/0
415	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304],PGCIL,RAJASTHAN	3/2021	12/2022 (-) [12/2022]	1,340.81 (-) [1,340.81]	626.81 (0.00) [0]	0/0
416	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245],PGCIL,MULTI STATE	3/2017	12/2019 (-) [11/2022]	379.95 (-) [379.95]	266.47 (0.00) [35]	0/0
417	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164],PGCIL,MULTI STATE	5/2014	11/2016 (-) [4/2022]	522.29 (-) [546.36]	481.89 (24.07) [0]	10/12
418	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250],PGCIL,MULTI STATE	12/2014	12/2018 (-) [1/2024]	5,111.33 (-) [6,700.00]	4,097.84 (1,588.67) [61]	0/0
419	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302],PGCIL,HARYANA	1/2019	3/2022 (-) [11/2022]	267.33 (-) [267.33]	86.32 (0.00) [8]	0/0
420	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307],PGCIL,RAJASTHAN	6/2021	12/2022 (-) [8/2023]	1,006.00 (-) [1,006.00]	660.83 (0.00) [8]	0/0

421	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. - [N18000329],PGCIL,MULTI STATE	3/2022	3/2023 (-) [3/2023]	176.22 (-) [176.22]	2.28 (0.00) [0]	0/0
422	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313],PGCIL,MULTI STATE	9/2015	12/2017 (-) [12/2022]	167.31 (-) [167.31]	129.26 (0.00) [60]	0/0
423	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306],PGCIL,RAJASTHAN	6/2021	12/2022 (-) [8/2023]	1,562.00 (-) [1,562.00]	500.90 (0.00) [8]	0/0
424	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300],PGCIL,RAJASTHAN	5/2021	9/2022 (-) [1/2023]	1,184.88 (-) [1,184.88]	80.70 (0.00) [4]	0/0
425	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301],PGCIL,GUJARAT	10/2019	8/2021 (-) [10/2022]	1,031.00 (-) [1,143.00]	985.61 (112.00) [14]	0/0
426	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291],SJVN,HIMACHAL PRADESH	10/2020	11/2025 (-) [11/2025]	687.97 (-) [687.97]	285.25 (0.00) [0]	2/11
427	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194],SJVN,BIHAR	3/2019	1/2024 (-) [1/2024]	10,439.09 (-) [10,439.09]	5,935.72 (0.00) [0]	16/27
428	PARASAN SOLAR POWER PROJECT - [N18000298],SJVN,UTTAR PRADESH	8/2021	12/2022 (-) [12/2022]	392.30 (-) [392.30]	397.04 (0.00) [0]	0/5
429	GURHAH SOLAR POWER PROJECT - [N18000334],SJVN,UTTAR PRADESH	5/2022	8/2023 (-) [8/2023]	466.82 (-) [466.82]	42.58 (0.00) [0]	0/0
430	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279],SJVN,HIMACHAL PRADESH	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	810.74 (0.00) [0]	2/10
431	BIKANER SOLAR POWER PROJECT - [N18000335],SJVN,MAHARASHTRA	4/2022	5/2024 (-) [5/2024]	5,491.89 (532.00) [6,023.89]	791.28 (532.00) [0]	0/0
432	Bagodara Solar Power Project - [N18000297],SJVN,GUJARAT	5/2021	10/2022 (-) [10/2022]	339.35 (-) [339.35]	45.45 (0.00) [0]	0/5
433	NAITWAR MORI HEP - [N18000265],SJVN,UTTARAKHAND	10/2017	12/2021 (-) [12/2022]	648.33 (-) [947.89]	915.31 (299.56) [12]	16/32
434	GUJRAI SOLAR POWER PROJECT - [N18000336],SJVN,UTTAR PRADESH	6/2022	8/2023 (-) [8/2023]	279.94 (-) [279.94]	28.39 (0.00) [0]	0/0
435	KHURJA SUPER THERMAL POWER PROJECT - [N18000272],THDCIL,UTTAR PRADESH	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	5,031.01 (0.00) [11]	5/13
436	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010],THDCIL,UTTARAKHAND	7/2006	2/2016 (6/2022) [10/2023]	1,657.00 (-) [4,825.60]	4,755.19 (3,168.60) [92]	26/34
437	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042],THDCIL,UTTARAKHAND	8/2008	6/2013 (-) [3/2025]	2,491.58 (3,860.35) [3,860.35]	2,640.57 (1,368.77) [141]	10/25
438	AMELIA COAL MINE	1/2017	9/2020	2,104.21	742.49	19/25

	- [N18000252], THDCIL, MADHYA PRADESH		(-) [9/2022]	(-) [1,587.16]	(-517.05) [24]	
	RAILWAYS					
439	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181], CR, MAHARASHTRA	2/1997	3/2021 (-) [3/2025]	2,271.50 (-) [4,805.17]	3,140.43 (2,533.67) [48]	0/0
440	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356], CR, MAHARASHTRA	2/2015	3/2022 (-) [3/2024]	1,272.19 (-) [1,384.72]	629.92 (112.53) [24]	0/0
441	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250], CR, MAHARASHTRA	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	365.59 (0.00) [24]	0/0
442	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362], CR, MAHARASHTRA	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	313.34 (0.00) [12]	0/0
443	DAUND - MANMAD (236 KM) - [N22000360], CR, MAHARASHTRA	2/2016	3/2023 (-) [3/2025]	1,876.00 (-) [2,081.27]	881.45 (205.27) [24]	0/0
444	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361], CR, MAHARASHTRA	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	542.40 (0.00) [24]	0/0
445	KALYAN-KASARA 3RD LINE - [N22000233], CR, MAHARASHTRA	4/2011	3/2021 (-) [3/2025]	792.89 (-) [1,387.52]	464.66 (594.63) [48]	0/0
446	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358], CR, MAHARASHTRA	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	657.66 (0.00) [12]	0/0
447	PUNE-MIRAJ-LONDA (467 KM) - [N22000359], CR, MAHARASHTRA	2/2015	3/2024 (-) [3/2024]	3,627.47 (3,627.00) [4,670.00]	2,229.23 (1,042.53) [0]	0/0
448	WARDHA-NANDED MAHARASHTRA - [N22000231], CR, MAHARASHTRA	4/2008	3/2023 (-) [3/2024]	3,168.29 (-) [3,445.48]	1,543.90 (277.19) [12]	0/0
449	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428], CCOI, GUJARAT	10/2013	3/2019 (-) [3/2019]	343.00 (-) [343.00]	222.83 (0.00) [0]	0/0
450	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431], CCOI, ANDHRA PRADESH	8/2016	3/2019 (-) [3/2019]	234.50 (-) [235.00]	14.14 (0.50) [0]	0/0
451	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464], DFCC, MULTI STATE	11/2007	3/2020 (-) [0/0]	16,592.00 (51,101.00) [51,101.00]	47,476.00 (34,509.00) [0]	0/0
452	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346], DFCC, MULTI STATE	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [51,219.00]	31,304.00 (39,630.00) [0]	0/0
453	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222], ECR, JHARKHAND	3/1999	/ (-) [7/2022]	1,033.07 (3,020.95) [3,800.00]	3,787.71 (2,766.93) [0]	0/0
454	SAKRI-HASANPUR ROAD (NL) - [N22000171], ECR, BIHAR	4/1999	/ (-) [12/2024]	325.00 (735.20) [735.20]	413.53 (410.20) [-]	0/0
455	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240], ECR, BIHAR	4/1997	3/2012 (-) [6/2023]	324.73 (967.29) [1,110.00]	1,112.02 (785.27) [135]	0/0
456	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472], ECR, BIHAR	4/2016	3/2021 (-) [12/2024]	744.04 (1,215.54) [1,215.54]	685.28 (471.50) [45]	0/0
457	HAJIPUR-SAGAULI VIA VAISHALI (NL), ECR - [220100303], ECR, BIHAR	4/2003	/ (-) [12/2024]	528.65 (2,066.78) [2,066.78]	1,661.76 (1,538.13) [-]	0/0
458	HAJIPUR - BACHAWARA - [N22000334], ECR, MULTI STATE	5/2015	3/2019 (-) [7/2022]	678.54 (678.54) [1,010.00]	1,038.66 (331.46) [0]	0/38

459	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA- BARDIBAS(NEPAL) GC - [N22000181], ECR, BIHAR	4/2009	3/2020 (-) [3/2025]	548.00 (548.00) [783.83]	540.74 (235.83) [60]	0/0
460	KIUL - GAYA DOUBLING PROJECT - [N22000349], ECR, BIHAR	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	1,153.56 (0.00) [36]	0/1
461	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476], ECR, BIHAR	4/1991	/ (-) [3/2024]	329.39 (1,483.14) [1,510.00]	1,547.42 (1,180.61) [-]	0/0
462	SAMASTIPUR-DARBANGHA - [N22000329], ECR, BIHAR	5/2015	/ (-) [12/2024]	380.00 (519.33) [519.33]	346.79 (139.33) [-]	0/0
463	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419], ECR, UTTAR PRADESH	8/2015	3/2019 (-) [3/2023]	528.57 (-) [528.57]	436.16 (0.00) [48]	0/0
464	RAMNA - SINGRAULI DOUBLING - [N22000417], ECR, UTTAR PRADESH	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,953.80 (0.00) [48]	0/0
465	SAKRI-NIRMALI AND JHANJHARPUR- LAUKAHABAZAR AND SAHARSA- FORBESGANJ (GC) - [N22000180], ECR, BIHAR	4/2004	/ (-) [3/2024]	372.14 (1,470.50) [1,700.00]	1,758.02 (1,327.86) [-]	0/0
466	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350], ECR, BIHAR	12/2015	3/2020 (-) [12/2023]	1,491.47 (-) [1,491.47]	660.90 (0.00) [45]	1/1
467	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473], ECR, BIHAR	4/2016	3/2021 (-) [3/2024]	731.64 (1,185.73) [1,185.73]	624.19 (454.09) [36]	0/0
468	ARARIA-SUPAUL (NL) - [N22000177], ECR, BIHAR	4/2008	/ (-) [12/2025]	1,605.17 (1,605.17) [1,605.17]	213.88 (0.00) [-]	0/0
469	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257], ECR, BIHAR	4/1997	/ (-) [3/2025]	162.87 (614.45) [614.45]	360.11 (451.58) [-]	0/0
470	KODERMA-TILAIYA (NL), ECR - [220100305], ECR, JHARKHAND	4/2002	/ (-) [3/2024]	459.91 (1,625.87) [1,625.87]	1,136.40 (1,165.96) [-]	0/0
471	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328], ECR, ODISHA	4/2005	6/2021 (-) [3/2025]	810.78 (1,928.07) [1,928.07]	1,027.78 (1,117.29) [45]	0/0
472	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381], ECR, ODISHA	4/2015	12/2018 (-) [3/2025]	1,172.92 (-) [1,172.92]	825.47 (0.00) [75]	0/0
473	BHADRAK - NERGUNDI 3RD LINE - [N22000316], ECR, ODISHA	3/2013	10/2020 (-) [3/2024]	843.04 (-) [843.04]	439.50 (0.00) [41]	0/0
474	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380], ECR, ODISHA	4/2015	11/2018 (-) [3/2025]	701.61 (-) [810.02]	179.43 (108.41) [76]	0/0
475	SAMBALPUR-TALCHER DOUBLING - [N22000315], ECR, ODISHA	3/2011	2/2019 (-) [0/0]	1,111.99 (-) [1,539.28]	1,152.38 (427.29) [0]	0/0
476	KIRANDUL - JAGDALPUR DOUBLING - [N22000318], ECR, CHHATISGARH	12/2012	3/2020 (-) [3/2024]	1,160.00 (-) [1,160.83]	1,095.89 (0.83) [48]	1/1
477	KHURDA ROAD-BOLANGIR(NL) ECR - [220100284], ECR, ODISHA	4/1994	3/2009 (12/2025) [12/2025]	2,923.13 (-) [3,791.66]	2,027.20 (868.53) [201]	0/0
478	JAGDALPUR-KORAPUT DOUBLING	4/2015	3/2022	1,547.38	834.54	0/0

	- [N22000376],ECOR,ODISHA		(-) [3/2024]	(-) [1,547.38]	(0.00) [24]	
479	KOTTAVALSA - KORAPUT DOUBLING - [N22000377],ECOR,ANDHRA PRADESH	4/2015	3/2022 (-) [3/2026]	2,499.71 (-) [2,499.71]	992.84 (0.00) [48]	0/0
480	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379],ECOR,ODISHA	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	729.38 (0.00) [48]	0/0
481	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302],ER,WEST BENGAL	4/2012	/ (-) [12/2022]	255.64 (-) [272.20]	328.63 (16.56) [-]	0/0
482	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272],ER,WEST BENGAL	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	906.01 (430.57) [72]	0/0
483	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238],ER,MULTI STATE	4/2011	/ (-) [9/2022]	175.80 (-) [495.10]	376.37 (319.30) [-]	0/0
484	BANDEL-BOINCHI 3RD LINE - [N22000221],ER,MULTI STATE	4/2011	/ (9/2021) [5/2022]	288.35 (-) [402.48]	548.37 (114.13) [0]	0/0
485	PIRPAINTI-JASIDIH - [N22000219],ER,MULTI STATE	4/2013	3/2022 (-) [3/2023]	915.98 (-) [2,137.81]	558.15 (1,221.83) [12]	0/0
486	MONIGRAM- NIMTITA - [N22000301],ER,MULTI STATE	4/2012	/ (-) [3/2023]	250.93 (-) [310.70]	470.90 (59.77) [-]	0/0
487	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI- SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229],ER,MULTI STATE	4/2010	3/2017 (-) [10/2022]	365.17 (-) [439.30]	525.35 (74.13) [67]	0/0
488	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489],IRCON,CHHATISGARH	4/2013	9/2018 (-) [12/2023]	3,055.00 (-) [3,500.00]	2,945.30 (445.00) [63]	0/1
489	GEVRA ROAD PENDRA ROAD - [N22000488],IRCON,CHHATISGARH	2/2014	3/2022 (-) [12/2024]	2,288.00 (-) [4,970.11]	1,509.87 (2,682.11) [33]	0/1
490	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418],IRCON,ODISHA	4/2016	3/2020 (-) [12/2025]	5,200.00 (-) [5,200.00]	0.00 (0.00) [69]	0/0
491	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108],KOMRCL,WEST BENGAL	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]	0/0
492	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164],MRTP,MAHARASHTRA	3/1996	3/2004 (-) [3/2023]	495.44 (-) [2,980.41]	1,991.80 (2,484.97) [228]	0/0
493	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028],MRTP,TAMIL NADU	4/2006	6/2013 (-) [12/2022]	495.74 (-) [774.51]	552.70 (278.77) [114]	1/4
494	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092],MRTP,MAHARASHTRA	4/2008	3/2014 (-) [0/0]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]	0/0
495	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135],MRTP,WEST BENGAL	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [0]	0/0
496	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND	4/2010	/ (3/2026) [12/2027]	2,030.50 (746.83) [746.83]	22.79 (-1,283.67) [-]	0/0

	TANPUR-BANSI PAHARPUR - [N22000158],NCR,MULTI STATE					
497	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495],NCR,UTTAR PRADESH	3/2018	3/2023 (-) [3/2026]	4,329.53 (-) [4,329.53]	109.37 (0.00) [36]	0/0
498	JHANSI BINA DOUBLING - [N22000496],NCR,UTTAR PRADESH	9/2016	3/2021 (-) [12/2023]	2,001.00 (2,001.00) [2,001.00]	1,043.73 (0.00) [33]	2/6
499	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148],NCR,MULTI STATE	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	799.75 (932.64) [33]	0/5
500	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206],NFR,MULTI STATE	4/2010	3/2020 (-) [3/2024]	242.22 (-) [471.00]	77.45 (228.78) [48]	0/0
501	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288],NFR,MANIPUR	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [14,322.79]	12,817.81 (9,868.62) [153]	0/0
502	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205],NFR,MEGHALAYA	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [8,324.28]	266.07 (7,417.82) [0]	0/0
503	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207],NFR,MULTI STATE	4/2010	/ (-) [3/2023]	241.52 (-) [401.65]	342.82 (160.13) [-]	0/0
504	AGARTALA-AKHAURA NL - [N22000195],NFR,TRIPURA	4/2012	3/2020 (-) [9/2022]	569.63 (-) [708.73]	380.92 (139.10) [30]	2/3
505	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087],NFR,BIHAR	9/2006	3/2019 (-) [12/2023]	532.87 (-) [2,650.00]	1,255.18 (2,117.13) [57]	0/0
506	MURKONGSELEK-PASIGHAT NL - [N22000208],NFR,MULTI STATE	4/2011	3/2020 (-) [10/2024]	414.84 (-) [983.55]	344.80 (568.71) [55]	0/0
507	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124],NFR,NAGALAND	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	1,781.77 (4,336.48) [132]	0/0
508	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086],NFR,ASSAM	9/2006	3/2019 (-) [3/2024]	385.20 (-) [1,145.79]	990.86 (760.59) [60]	0/0
509	BHAIRABI SAIRONG, NL, NEFR - [N22000100],NFR,MIZORAM	4/2008	3/2014 (-) [12/2023]	2,393.47 (-) [6,527.45]	5,330.91 (4,133.98) [117]	0/0
510	BONGAIGAON-GOALPARA- GUWAHATI (176 KM) - [N22000388],NFR,ASSAM	4/2015	3/2022 (-) [3/2025]	2,232.32 (-) [4,059.65]	2,380.05 (1,827.33) [36]	0/0
511	SEVOK RANGPO, NEFR - [N22000102],NFR,SIKKIM	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [7,876.92]	3,408.77 (6,537.44) [96]	0/0
512	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING - [N22000183],NFR,MULTI STATE	4/2013	3/2019 (-) [12/2023]	1,798.00 (-) [2,047.51]	1,050.40 (249.51) [57]	0/0
513	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459],NER,UTTAR PRADESH	4/2017	4/2017 (-) [10/2022]	150.00 (-) [341.66]	0.74 (191.66) [66]	0/0
514	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347],NER,UTTAR PRADESH	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [2,000.00]	1,832.40 (704.58) [0]	0/0
515	CHHAPRA-BALLIA UP - [N22000134],NER,MULTI STATE	3/2013	1/2019 (-) [0/0]	295.00 (-) [800.00]	687.13 (505.00) [0]	0/0
516	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468],NER,UTTAR PRADESH	4/2016	/ (-) [12/2023]	602.50 (-) [800.00]	185.52 (197.50) [-]	0/0

517	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470],NER,UTTAR PRADESH	4/2016	12/2019 (-) [0/0]	1,177.96 (-) [1,028.95]	866.28 (-149.01) [0]	0/0
518	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456],NER,UTTAR PRADESH	4/2016	4/2016 (-) [0/0]	213.00 (-) [213.35]	141.72 (0.35) [0]	0/0
519	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469],NER,UTTAR PRADESH	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	362.14 (-233.29) [0]	0/0
520	DAUSA-GANGAPUR CITY(NL),NWR - [220100184],NWR,RAJASTHAN	2/1997	2/2019 (-) [6/2022]	410.08 (-) [860.41]	837.18 (450.33) [0]	0/0
521	PHULERA - DIGANA DOUBLING - [N22000326],NWR,MULTI STATE	5/2015	3/2020 (-) [10/2022]	600.00 (-) [701.81]	476.01 (101.81) [31]	0/0
522	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466],NWR,RAJASTHAN	8/2018	8/2022 (-) [11/2022]	808.85 (-) [808.85]	638.86 (0.00) [3]	0/0
523	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281],NR,DELHI	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	133.78 (123.32) [-]	0/0
524	NANGALDAM-TALWARA(NL),NR - [220100188],NR,MULTI STATE	3/1981	7/2012 (-) [11/2024]	450.00 (-) [2,017.96]	845.23 (1,567.96) [148]	0/0
525	ROHTAK-MEHAM HANSI - [N22000272],NR,HARYANA	4/2012	12/2011 (-) [12/2011]	287.00 (-) [893.45]	686.20 (606.45) [0]	0/0
526	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274],NR,MULTI STATE	4/2007	/ (-) [9/2023]	336.91 (-) [791.39]	572.99 (454.48) [-]	0/0
527	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502],NR,PUNJAB	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	190.00 (0.00) [108]	0/0
528	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133],NR,JAMMU AND KASHMIR	3/1995	11/2002 (6/2023) [6/2023]	2,500.00 (37,012.26) [37,012.26]	30,671.82 (34,512.26) [247]	0/0
529	CHANDIGARH-BADDI - [N22000467],NR,MULTI STATE	4/2007	3/2023 (-) [12/2025]	328.14 (-) [1,540.13]	242.09 (1,211.99) [33]	0/0
530	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463],NHSRCL,MULTI STATE	12/2015	12/2023 (-) [0/0]	1,08,000.00 (-) [1,08,000.00]	30,489.68 (0.00) [0]	0/2
531	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394],RITES,TELANGANA	3/2015	3/2021 (12/2022) [0/0]	636.38 (998.06) [998.06]	900.29 (361.68) [0]	3/3
532	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413],RVNL,UTTAR PRADESH	3/2012	12/2020 (-) [9/2022]	1,183.25 (-) [2,203.53]	2,075.59 (1,020.28) [21]	0/0
533	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327],RVNL,ODISHA	4/2000	3/2009 (3/2009) [12/2022]	133.41 (207.00) [433.00]	455.39 (299.59) [165]	1/1
534	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401],RVNL,UTTAR PRADESH	4/2015	3/2022 (-) [12/2022]	943.60 (-) [1,500.00]	1,127.95 (556.40) [9]	0/0
535	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110],RVNL,WEST BENGAL	4/2010	3/2016 (-) [3/2026]	3,951.98 (-) [4,259.48]	3,496.68 (307.50) [120]	0/0

536	BINA - KOTA DOUBLING WITH RE - [N22000414],RVNL,MADHYA PRADESH	4/2011	12/2020 (-) [9/2022]	1,485.85 (-) [1,835.83]	2,340.59 (349.98) [21]	0/0
537	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109],RVNL, WEST BENGAL	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	305.05 (435.44) [141]	0/0
538	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404],RVNL,UTTAR PRADESH	4/2011	3/2019 (-) [3/2023]	927.01 (-) [1,457.79]	1,408.80 (530.78) [48]	0/0
539	VIJAYAWADA-GUDUR - [N22000369],RVNL,ANDHRA PRADESH	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	4,099.98 (302.42) [0]	0/0
540	RAIPUR - TITLAGARH - DOUBLING - [N22000411],RVNL,CHHATISGARH	3/2007	3/2020 (-) [9/2022]	1,402.02 (-) [1,300.00]	1,405.40 (-102.02) [30]	0/0
541	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111],RVNL, WEST BENGAL	4/2010	3/2016 (-) [7/2025]	2,913.51 (-) [4,834.54]	1,839.89 (1,921.03) [112]	0/0
542	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409],RVNL,ODISHA	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	2,712.78 (992.05) [24]	0/0
543	VIJAYWADA-GUDUGOLANU- BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313],RVNL,ANDHRA PRADESH	3/2012	3/2020 (-) [6/2022]	1,503.71 (-) [3,633.12]	4,271.59 (2,129.41) [0]	0/0
544	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451],RVNL,TAMIL NADU	2/2015	3/2020 (-) [12/2022]	760.00 (-) [1,536.00]	1,664.15 (776.00) [33]	0/0
545	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501],RVNL,UTTAR PRADESH	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	3,492.37 (0.00) [0]	0/0
546	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325],RVNL,ODISHA	4/1998	2/2015 (-) [9/2022]	1,202.70 (-) [2,440.53]	2,202.65 (1,237.83) [91]	0/0
547	BANASPANI- JAKHPURA - DOUBLING - [N22000412],RVNL,ODISHA	3/2009	3/2019 (-) [3/2023]	942.95 (-) [1,552.26]	1,445.70 (609.31) [48]	0/0
548	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449],RVNL,TAMIL NADU	2/2015	3/2022 (-) [5/2023]	1,700.00 (-) [1,305.00]	1,284.85 (-395.00) [14]	0/0
549	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410],RVNL,ODISHA	3/2006	3/2020 (-) [9/2022]	948.04 (-) [2,009.00]	2,350.49 (1,060.96) [30]	0/0
550	BHANUPALI-BILASPUR BERI NL - [N22000273],RVNL,HIMACHAL PRADESH	4/2008	12/2026 (-) [3/2025]	2,966.99 (-) [6,753.42]	2,374.44 (3,786.43) [-21]	0/0
551	PALANPUR-SAMAKHAYALI (DL) - [N22000144],RVNL,GUJARAT	4/2013	12/2021 (-) [12/2022]	1,548.66 (-) [2,538.01]	2,375.23 (989.35) [12]	0/0
552	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405],RVNL,UTTAR PRADESH	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	1,267.55 (0.00) [21]	0/0
553	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407],RVNL,MAHARASHTRA	3/2009	3/2020 (-) [7/2022]	713.48 (-) [2,725.00]	3,066.34 (2,011.52) [0]	0/0
554	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213],RVNL,TELANGANA	4/2012	3/2016 (-) [9/2022]	632.68 (-) [950.00]	626.34 (317.32) [78]	0/0

555	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297],RVNL,KARNATAKA	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [3,300.00]	2,799.96 (1,173.00) [0]	0/1
556	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406],RVNL,UTTARAKHAND	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [24,659.00]	8,453.89 (8,443.00) [3]	0/0
557	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205],SCR,MULTI STATE	4/1997	3/2000 (-) [3/2023]	1,723.00 (1.00) [3,421.35]	2,206.22 (1,698.35) [276]	0/0
558	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432],SCR,TELANGANA	4/2017	3/2022 (-) [0/0]	119.73 (185.00) [242.28]	56.14 (122.55) [0]	0/0
559	BHADRACHALAM-KOVVUR - [N22000264],SCR,MULTI STATE	4/2012	/ (-) [0/0]	923.23 (-) [923.23]	2.46 (0.00) [0]	1/1
560	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032],SCR,TELANGANA	4/2006	3/2010 (-) [3/2025]	1,160.48 (-) [2,250.00]	784.26 (1,089.52) [180]	1/1
561	GUNTUR-GUNTAKAL - [N22000368],SCR,ANDHRA PRADESH	4/2016	3/2022 (-) [3/2025]	3,631.00 (-) [3,887.48]	1,755.92 (256.48) [36]	0/0
562	KAZIPET-BALHRSHA - [N22000367],SCR,MULTI STATE	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,875.71 (0.00) [36]	0/0
563	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261],SCR,MULTI STATE	4/2012	3/2023 (-) [3/2025]	1,856.95 (-) [1,952.68]	918.80 (95.73) [24]	0/0
564	NADIKUDE-SRI KALAHASTI - [N22000286],SCR,ANDHRA PRADESH	4/2011	3/2021 (-) [3/2026]	2,288.70 (-) [2,288.70]	1,274.68 (0.00) [60]	0/1
565	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265],SCR,ANDHRA PRADESH	12/2001	3/2009 (-) [3/2027]	1,045.20 (-) [2,120.16]	1,095.80 (1,074.96) [216]	0/0
566	ANUPPUR-KATNI - [N22000485],SECR,MADHYA PRADESH	4/2015	12/2021 (12/2023) [12/2023]	1,370.00 (-) [1,370.94]	918.24 (0.94) [24]	0/0
567	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480],SECR,MAHARASHTRA	6/2018	12/2021 (-) [12/2024]	229.00 (-) [1,096.00]	88.40 (867.00) [36]	0/1
568	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420],SECR,MAHARASHTRA	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (-) [3,176.60]	1,902.75 (1,268.09) [9]	0/1
569	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484],SECR,CHHATISGARH	4/2015	3/2021 (12/2023) [12/2023]	1,973.00 (2,135.34) [2,135.34]	1,106.76 (162.34) [33]	0/1
570	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506],SER,MULTI STATE	3/2019	5/2023 (-) [12/2024]	1,866.31 (-) [1,866.31]	610.05 (0.00) [19]	0/0
571	BONDAMUNDA RANCHI DOUBLING - [N22000396],SER,JHARKHAND	3/2016	3/2021 (-) [3/2024]	1,724.20 (-) [1,724.20]	1,358.49 (0.00) [36]	0/0
572	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508],SER,JHARKHAND	4/2018	6/2022 (-) [12/2025]	428.65 (-) [472.50]	6.00 (43.85) [42]	0/0
573	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395],SER,ODISHA	11/2015	3/2020 (-) [10/2022]	969.83 (-) [1,312.97]	1,264.07 (343.14) [31]	0/0
574	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510],SER,WEST BENGAL	4/2018	6/2022 (-) [12/2023]	338.00 (-) [393.83]	34.60 (55.83) [18]	0/0
575	TALGARIA TO BOKARO N/CABIN	4/2018	12/2021	390.39	259.72	0/0

	DOUBLING(38 KM) - [N22000509],SER,JHARKHAND		(-) [1/2023]	(-) [511.75]	(121.36) [13]	
576	HUBLI- CHIKJAJUR - [N22000325],SWR,KARNATAKA	3/2015	3/2020 (-) [12/2022]	1,156.94 (-) [1,954.21]	1,381.52 (797.27) [33]	3/5
577	BAGALKOT-KUDACHI NL - [N22000258],SWR,KARNATAKA	4/2010	3/2016 (-) [12/2026]	986.30 (1,378.00) [1,530.09]	332.27 (543.79) [129]	1/1
578	TUMKUR-CHITRADURGA- DAVENGERE NL - [N22000256],SWR,KARNATAKA	4/2011	/ (-) [3/2025]	1,801.01 (-) [2,000.97]	104.48 (199.96) [-]	0/0
579	GADAG-WADI NL - [N22000299],SWR,KARNATAKA	4/2013	12/2018 (-) [6/2025]	2,841.84 (-) [2,841.84]	490.24 (0.00) [78]	0/0
580	HUBLI-ANKOLA(NL),SWR - [220100193],SWR,KARNATAKA	4/1997	/ (-) [3/2028]	2,315.00 (-) [5,174.30]	158.25 (2,859.30) [-]	0/0
581	HOTGI-KUDGI-GADAG - [N22000333],SWR,MULTI STATE	3/2015	3/2019 (-) [2/2024]	1,614.59 (-) [1,878.00]	1,611.28 (263.41) [59]	0/0
582	RAYADURGA-TUMKUR NL - [N22000279],SWR,MULTI STATE	4/2007	/ (-) [12/2025]	2,062.30 (-) [2,404.03]	1,108.14 (341.73) [-]	2/2
583	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486],SWR,KARNATAKA	3/1996	3/2017 (-) [3/2026]	644.78 (889.00) [826.18]	499.13 (181.40) [108]	0/0
584	SHIMOGA-HARIHAR NL - [N22000278],SWR,KARNATAKA	4/2011	3/2016 (-) [3/2026]	832.47 (-) [832.47]	0.94 (0.00) [120]	0/0
585	MARIKUPPAM - KUPPAM - [N22000308],SWR,KARNATAKA	4/2012	3/2016 (-) [3/2024]	279.54 (-) [279.54]	36.45 (0.00) [96]	0/0
586	TIDIVANAM-NAGARI (NL) - [N22000085],SR,TAMIL NADU	9/2006	/ (-) [12/2025]	582.83 (-) [3,500.79]	622.53 (2,917.96) [-]	0/0
587	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215],SR,MULTI STATE	4/2011	3/2019 (-) [12/2027]	120.70 (-) [2,084.48]	321.37 (1,963.78) [105]	0/0
588	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399],SR,KERALA	2/2015	/ (-) [3/2024]	1,431.90 (-) [1,431.90]	1,019.34 (0.00) [-]	0/0
589	MAYLADUTHURAI-THIRUVARUR- KARAIKUDI-THIRU 'PONDII'- AGASTIYAMPALLI - [N22000079],SR,TAMIL NADU	9/2007	2/2019 (-) [3/2025]	724.69 (-) [3,081.20]	1,774.56 (2,356.51) [73]	0/0
590	MADURAI-BODINAYAKKANUR - [N22000201],SR,TAMIL NADU	4/2008	/ (9/2022) [9/2022]	164.41 (-) [591.00]	464.44 (426.59) [-]	0/0
591	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400],SR,KERALA	2/2015	/ (-) [3/2025]	1,000.00 (1,281.63) [1,339.00]	0.91 (339.00) [-]	0/0
592	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232],WCR,MULTI STATE	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,427.33 (8,000.84) [202]	1/9
593	KATNI-BINA 3RD LINE (263 KM) - [N22000415],WCR,MADHYA PRADESH	6/2016	3/2022 (3/2024) [3/2024]	2,478.23 (2,938.00) [2,938.00]	1,450.69 (459.77) [24]	6/17
594	KATNI GRADE SEPARATOR/BYE PASS - [N22000416],WCR,MADHYA PRADESH	8/2016	3/2022 (-) [9/2024]	582.13 (-) [1,247.64]	704.97 (665.51) [30]	1/1
595	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351],WCR,MADHYA	12/2015	3/2020 (-) [10/2024]	1,763.93 (2,445.30) [2,445.30]	1,720.50 (681.37) [55]	1/1

	PRADESH					
596	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314],WCR,MADHYA PRADESH	4/2001	3/2021 (3/2024) [3/2024]	424.60 (-) [2,909.99]	1,658.34 (2,485.39) [36]	4/15
597	SURENDRA NAGAR RAJKOT - [N22000392],WR,GUJARAT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,042.12) [1,119.12]	962.02 (116.73) [21]	0/0
598	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120],WR,MADHYA PRADESH	4/2008	3/2022 (3/2026) [3/2026]	3,503.69 (5,839.02) [6,383.82]	2,529.21 (2,880.13) [48]	0/0
599	VIRAMGAM-SAMAKHIALI (DL) - [N22000145],WR,GUJARAT	4/2011	3/2021 (12/2022) [12/2022]	1,037.15 (1,125.53) [1,394.02]	1,300.17 (356.87) [21]	0/0
600	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123],WR,GUJARAT	4/2008	3/2012 (3/2024) [3/2024]	318.24 (322.19) [1,083.17]	252.70 (764.93) [144]	0/0
601	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503],WR,MADHYA PRADESH	4/2017	3/2022 (3/2026) [3/2026]	495.18 (495.18) [495.18]	1.01 (0.00) [48]	0/0
602	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436],WR,GUJARAT	3/2012	/ (-) [3/2024]	248.26 (-) [528.49]	127.92 (280.23) [-]	0/0
603	CHOTTAUDEPUR-DHAR(NL) - [N22000138],WR,MULTI STATE	4/2007	3/2022 (12/2024) [12/2024]	1,347.26 (1,524.68) [1,524.68]	1,063.17 (177.42) [33]	0/0
604	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493],WR,MADHYA PRADESH	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [640.75]	497.73 (-59.25) [33]	0/0
605	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139],WR,MULTI STATE	4/2007	3/2022 (3/2025) [3/2025]	1,640.04 (1,873.10) [1,873.10]	908.51 (233.06) [36]	0/0
606	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505],WR,GUJARAT	4/2018	3/2024 (12/2024) [12/2024]	537.31 (537.31) [584.31]	2.44 (47.00) [9]	0/0
607	MIYAGAM-KARJAN-DABHOI- SAMLAYA (GC) - [N22000142],WR,GUJARAT	4/2011	/ (10/2025) [10/2025]	844.10 (844.10) [844.10]	390.14 (0.00) [-]	0/0
608	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434],WR,MAHARASHTRA	3/2010	/ (-) [3/2024]	265.88 (-) [311.36]	0.00 (45.48) [-]	0/0
609	AHMEDABAD-HIMMATNAGAR- UDAIPUR (WR) - [N22000121],WR,GUJARAT	4/2008	3/2020 (3/2024) [3/2024]	829.74 (1,631.75) [2,448.99]	2,142.58 (1,619.25) [48]	0/0
610	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504],WR,GUJARAT	4/2017	3/2020 (12/2024) [12/2024]	692.25 (692.26) [692.26]	8.51 (0.01) [57]	0/0
611	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435],WR,MAHARASHTRA	3/2012	/ (-) [3/2024]	217.38 (-) [393.62]	219.72 (176.24) [-]	0/0
	RENEWABLE ENERGY					
612	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118],CPWD R ENERGY,DELHI	10/2017	11/2019 (-) [0/0]	271.90 (-) [365.00]	249.96 (93.10) [0]	0/0
	ROAD TRANSPORT AND HIGHWAYS					
613	MUL TO CHANDRAPUR - [N24001117],MoRTH,MAHARASHTRA	12/2016	7/2019 (-) [6/2022]	162.34 (-) [162.34]	66.99 (0.00) [0]	1/4
614	RECONSTRUCTION WITH	12/2017	12/2019	200.34	141.39	0/0

	GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773],MoRTH,UTTARAKHAND		(-) [0/0]	(-) [200.34]	(0.00) [0]	
615	AJANTHA TO BULDHANA - [N24001008],MoRTH,A & N ISLANDS	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	260.08 (0.00) [0]	0/4
616	WARDHA TO ARVI - [N24001150],MoRTH,MAHARASHTRA	2/2018	4/2020 (-) [3/2022]	313.58 (-) [313.58]	229.05 (0.00) [0]	0/4
617	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197],MoRTH,GUJARAT	3/2018	6/2021 (-) [6/2022]	351.00 (270.00) [270.00]	197.00 (-81.00) [0]	3/4
618	SHIROD SHAHPURER TO NANDED - [N24001041],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [2/2022]	211.34 (-) [211.34]	136.33 (0.00) [0]	2/4
619	SATARA MURVAD PILLOV PANDHARPUR - [N24001095],MoRTH,MAHARASHTRA	1/2017	/ (-) [6/2022]	388.44 (-) [388.44]	213.91 (0.00) [0]	0/0
620	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242],MoRTH,RAJASTHAN	8/2020	11/2020 (-) [0/0]	196.23 (-) [196.00]	84.00 (-0.23) [0]	2/4
621	SILLOD TO FARDAPUR - [N24001125],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [6/2022]	337.46 (-) [337.46]	262.43 (0.00) [0]	0/4
622	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000],MoRTH,BIHAR	3/2018	/ (3/2022) [3/2022]	153.24 (-) [153.24]	115.69 (0.00) [0]	0/0
623	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514],MoRTH,GOA	12/2015	/ (-) [3/2022]	773.98 (-) [773.98]	413.42 (0.00) [0]	0/0
624	WAKED TO TALEGAON - [N24001135],MoRTH,MAHARASHTRA	2/2016	2/2019 (-) [11/2021]	1,244.75 (1,245.00) [1,244.75]	911.66 (0.00) [0]	0/0
625	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909],MoRTH,PUNJAB	10/2017	10/2019 (-) [12/2022]	1,069.59 (-) [1,069.59]	739.08 (0.00) [38]	0/1
626	DEULGAON SAKARSHA TO MEHKAR - [N24001076],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	146.73 (0.00) [0]	0/0
627	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248],MoRTH,TELANGANA	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.96 (0.00) [0]	0/0
628	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258],MoRTH,GOA	3/2015	/ (-) [12/2021]	184.05 (-) [184.05]	118.37 (0.00) [0]	2/4
629	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896],MoRTH,MADHYA PRADESH	1/2017	9/2019 (9/2021) [9/2021]	373.82 (-) [373.82]	244.81 (0.00) [0]	0/0

630	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282],MoRTH,ANDHRA PRADESH	1/2014	11/2014 (-) [11/2014]	195.45 (-) [195.45]	0.00 (0.00) [0]	0/4
631	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH- 81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874],MoRTH,WEST BENGAL	3/2016	11/2018 (3/2022) [3/2023]	271.17 (291.20) [291.20]	125.25 (20.03) [52]	0/0
632	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259],MoRTH,GOA	3/2015	/ (2/2019) [1/2020]	280.16 (-) [290.59]	243.00 (10.43) [0]	3/4
633	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382],MoRTH,HIMACHAL PRADESH	8/2020	3/2021 (-) [0/0]	242.80 (-) [242.80]	41.61 (0.00) [0]	0/0
634	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243],MoRTH,ASSAM	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	93.86 (0.00) [0]	0/0
635	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992],MoRTH,TELANGANA	2/2018	4/2020 (7/2020) [7/2020]	426.52 (-) [426.52]	398.81 (0.00) [0]	0/0
636	HELWAK TO KARAD - [N24001055],MoRTH,MAHARASHTRA	2/2017	7/2019 (-) [7/2021]	416.99 (-) [416.99]	225.83 (0.00) [0]	0/4
637	MALEGAON TO RISOD - [N24001089],MoRTH,MAHARASHTRA	2/2018	12/2019 (-) [10/2020]	303.24 (303.00) [303.24]	198.53 (0.00) [0]	0/4
638	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774],MoRTH,UTTARAKHAND	12/2017	12/2019 (-) [0/0]	248.22 (-) [248.22]	146.17 (0.00) [0]	0/0
639	BODHWAD TO STATE BORDER - [N24001086],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [11/2020]	178.26 (-) [178.26]	159.96 (0.00) [0]	0/4
640	WIDENING TO 2 LANE, RE- ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306],MoRTH,MIZORAM	11/2010	3/2011 (12/2022) [0/0]	624.41 (1,109.88) [992.67]	1,021.46 (368.26) [0]	0/0
641	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943],MoRTH,BIHAR	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	234.43 (0.00) [0]	0/0
642	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781],MoRTH,UTTARAKHAND	5/2018	5/2020 (10/2022) [10/2022]	248.00 (-) [248.00]	111.85 (0.00) [29]	0/0
643	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 -	1/2017	1/2021 (-) [4/2022]	205.95 (-) [205.95]	164.98 (0.00) [0]	0/0

	[N24001182],MoRTH,MIZORAM					
644	MHASWAD TO TEMBHURNI - [N24001099],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [9/2022]	488.60 (-) [488.60]	240.92 (0.00) [38]	0/4
645	SHIVUR TO YEOLA - [N24001059],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [3/2022]	181.08 (-) [181.08]	97.86 (0.00) [0]	0/4
646	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	543.05 (-) [543.05]	241.22 (0.00) [0]	0/0
647	CHIMUR TO WARORA - [N24001105],MoRTH,MAHARASHTRA	11/2016	3/2019 (-) [6/2022]	467.70 (-) [467.70]	223.35 (0.00) [0]	0/4
648	JAHIRABAD TO LATUR - [N24001040],MoRTH,MAHARASHTRA	1/2017	11/2019 (-) [3/2022]	461.96 (-) [461.96]	329.59 (0.00) [0]	2/4
649	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963],MoRTH,ANDHRA PRADESH	1/2018	8/2018 (1/2022) [1/2022]	418.03 (386.99) [386.99]	361.50 (-31.04) [0]	4/4
650	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937],MoRTH,ANDHRA PRADESH	3/2018	8/2018 (8/2022) [8/2022]	289.67 (234.73) [234.73]	262.20 (-54.94) [48]	3/4
651	PATRADEVI TO KARASWADA 4L - [N24001004],MoRTH,GOA	3/2017	5/2020 (-) [6/2022]	634.32 (-) [634.32]	347.93 (0.00) [0]	1/4
652	SELDOH TO PANVAR - [N24001097],MoRTH,MAHARASHTRA	7/2018	5/2020 (-) [12/2022]	404.33 (404.00) [404.33]	114.51 (0.00) [31]	0/4
653	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380],MoRTH,TAMIL NADU	8/2020	2/2021 (-) [0/0]	302.62 (-) [302.62]	166.72 (0.00) [0]	2/4
654	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	394.27 (-) [394.27]	158.24 (0.00) [0]	0/0
655	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912],MoRTH,ODISHA	8/2016	2/2017 (11/2022) [0/0]	287.70 (-) [287.70]	229.52 (0.00) [0]	0/0
656	TAKARKHED TO JALNA - [N24001085],MoRTH,MAHARASHTRA	9/2017	6/2019 (-) [11/2020]	417.90 (418.00) [417.90]	275.39 (0.00) [0]	0/4
657	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584],MoRTH,MAHARASHTRA	3/2016	/ (-) [7/2021]	1,142.62 (1,907.03) [1,142.62]	978.04 (0.00) [0]	0/0
658	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181],MoRTH,MIZORAM	8/2010	9/2014 (10/2022) [0/0]	186.96 (-) [322.24]	312.50 (135.28) [0]	0/0

659	REHABILITATION AND UPGRADATION OF DHINDI- DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965],MoRTH,ANDHRA PRADESH	1/2016	5/2016 (7/2022) [7/2022]	386.09 (316.06) [316.06]	224.62 (-70.03) [0]	3/4
660	KATOL TO WARUD - [N24001019],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [1/2020]	463.62 (664.00) [463.62]	265.78 (0.00) [0]	0/4
661	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585],MoRTH,MAHARASHTRA	3/2016	/ (-) [3/2023]	1,101.58 (-) [1,101.58]	395.64 (0.00) [-]	0/0
662	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334],MoRTH,KARNATAKA	3/2015	11/2015 (12/2021) [10/2022]	165.67 (-) [165.67]	124.52 (0.00) [83]	0/0
663	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998],MoRTH,TELANGANA	1/2019	/ (1/2023) [1/2023]	193.19 (249.72) [249.72]	184.91 (56.53) [-]	0/0
664	RISOD TO HINGOLI - [N24001149],MoRTH,MAHARASHTRA	2/2018	12/2019 (-) [3/2022]	355.99 (-) [355.99]	247.60 (0.00) [0]	0/0
665	CHIKALI TO DHAD - [N24001061],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [6/2022]	189.46 (189.00) [189.46]	111.73 (0.00) [0]	0/4
666	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [6/2019]	406.51 (-) [406.51]	340.26 (0.00) [0]	0/0
667	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211],MoRTH,UTTAR PRADESH	11/2018	/ (-) [9/2022]	281.45 (-) [319.96]	202.69 (38.51) [-]	0/0
668	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872],MoRTH,MADHYA PRADESH	3/2018	8/2018 (8/2021) [10/2022]	166.21 (-) [174.90]	154.26 (8.69) [50]	0/0
669	KHERDA TO NAGZARI - [N24001072],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [9/2020]	181.30 (-) [181.30]	137.37 (0.00) [0]	0/4
670	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950],MoRTH,RAJASTHAN	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	147.79 (0.00) [0]	3/4
671	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252],MoRTH,MAHARASHTRA	3/2015	/ (-) [6/2019]	168.30 (-) [168.30]	100.56 (0.00) [0]	0/4
672	MANGAON TO DIGHI PORT - [N24001024],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2022]	457.52 (-) [457.52]	392.92 (0.00) [0]	2/4
673	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR- KARNOHAL SECTION (KM 141.000 TO K - [N24001447],MoRTH,HIMACHAL PRADESH	8/2020	12/2024 (-) [12/2024]	371.93 (-) [371.93]	0.00 (0.00) [0]	0/0

674	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376],MoRTH,ARUNACHAL PRADESH	3/2021	3/2027 (-) [3/2027]	182.55 (-) [182.55]	24.82 (0.00) [0]	0/0
675	SATARA TO MHASWAD - [N24001092],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [9/2022]	653.46 (-) [653.46]	287.45 (0.00) [38]	0/4
676	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772],MoRTH,UTTARAKHAND	12/2017	12/2019 (-) [0/0]	257.34 (-) [257.34]	156.63 (0.00) [0]	0/0
677	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208],MoRTH,UTTAR PRADESH	3/2018	8/2020 (-) [10/2022]	288.30 (-) [323.36]	237.25 (35.06) [26]	0/0
678	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984],MoRTH,TELANGANA	1/2017	12/2019 (12/2019) [12/2019]	283.00 (-) [283.00]	250.42 (0.00) [0]	0/0
679	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391],MoRTH,PUNJAB	11/2015	/ (-) [0/0]	889.24 (-) [904.82]	849.98 (15.58) [0]	0/1
680	SALAIKHURD TO TIRORA - [N24001042],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [3/2022]	415.25 (415.25) [415.25]	273.34 (0.00) [0]	0/4
681	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516],MoRTH,GOA	12/2015	/ (-) [3/2022]	819.95 (-) [819.95]	423.47 (0.00) [0]	0/0
682	SANGOLA TO JATH - [N24001052],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [3/2022]	257.38 (257.00) [257.38]	166.31 (0.00) [0]	0/4
683	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892],MoRTH,MADHYA PRADESH	11/2017	7/2018 (8/2021) [10/2022]	249.05 (-) [249.05]	219.86 (0.00) [51]	0/0
684	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916],MoRTH,ODISHA	3/2018	8/2018 (11/2022) [11/2022]	214.23 (-) [214.23]	138.74 (0.00) [51]	0/0
685	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151],MoRTH,MADHYA PRADESH	11/2017	3/2018 (6/2021) [10/2022]	392.33 (-) [428.55]	404.69 (36.22) [55]	0/0
686	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913],MoRTH,ODISHA	9/2016	2/2017 (11/2022) [0/0]	295.67 (-) [295.67]	203.61 (0.00) [0]	0/0
687	INDAPAU TO AGARDANDA - [N24001025],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [2/2022]	355.17 (-) [355.17]	270.78 (0.00) [0]	3/4
688	REHABILITATION AND UP GRADATION OF NH-544E FROM KM	3/2020	3/2021 (4/2022)	207.79 (-)	134.98 (0.00)	3/4

	56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384],MoRTH,ANDHRA PRADESH		[4/2022]	[207.79]	[0]	
689	KUNDRAL TO WAZAR - [N24001077],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [12/2020]	225.25 (225.00) [225.25]	199.34 (0.00) [0]	2/4
690	PAHUR TO BODHWAD - [N24001084],MoRTH,MAHARASHTRA	1/2017	5/2020 (-) [2/2022]	244.93 (-) [244.93]	167.44 (0.00) [0]	0/4
691	NASHIK TO PETH - [N24001121],MoRTH,MAHARASHTRA	12/2015	11/2018 (-) [4/2021]	289.60 (-) [289.60]	210.10 (0.00) [0]	0/4
692	SHEGAON TO DEORI PHATA - [N24001010],MoRTH,MAHARASHTRA	2/2017	5/2019 (-) [11/2020]	373.10 (373.00) [373.10]	320.45 (0.00) [0]	0/4
693	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883],MoRTH,WEST BENGAL	3/2018	10/2020 (3/2022) [3/2023]	254.30 (-) [254.30]	130.87 (0.00) [29]	0/0
694	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887],MoRTH,WEST BENGAL	6/2016	8/2019 (8/2022) [3/2023]	236.78 (-) [263.26]	91.29 (26.48) [43]	0/0
695	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156],MoRTH,KARNATAKA	1/2017	9/2017 (-) [7/2022]	166.67 (-) [264.34]	181.38 (97.67) [0]	0/0
696	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178],MoRTH,NAGALAND	11/2016	9/2019 (-) [11/2020]	336.25 (-) [369.96]	309.98 (33.71) [0]	0/0
697	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064],MoRTH,MAHARASHTRA	3/2018	2/2020 (-) [6/2021]	217.14 (217.00) [217.14]	153.92 (0.00) [0]	0/4
698	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444],MoRTH,GOA	10/2015	/ (9/2022) [12/2022]	936.40 (-) [936.40]	611.47 (0.00) [-]	0/0
699	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886],MoRTH,MADHYA PRADESH	1/2017	3/2017 (12/2021) [11/2022]	205.05 (-) [205.05]	137.88 (0.00) [68]	0/0
700	WAKAN PALI KHOPOLI - [N24001026],MoRTH,MAHARASHTRA	1/2017	5/2019 (-) [9/2022]	376.19 (-) [376.19]	113.66 (0.00) [40]	1/4
701	MANSAR TO SALAIKHURD - [N24001035],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [6/2021]	418.36 (-) [418.36]	263.13 (0.00) [0]	0/4
702	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914],MoRTH,ODISHA	12/2016	8/2018 (11/2022) [11/2022]	223.50 (-) [223.50]	132.37 (0.00) [51]	0/0
703	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195],MoRTH,ARUNACHAL	11/2016	/ (-) [3/2022]	243.89 (-) [243.89]	232.72 (0.00) [0]	0/0

	PRADESH					
704	PARLI PIMPLA DAHIGUDA - [N24001138], MoRTH, MAHARASHTRA	2/2017	6/2019 (-) [6/2022]	205.72 (206.00) [205.72]	85.71 (0.00) [0]	1/4
705	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175], MoRTH, NAGALAND	10/2016	12/2020 (9/2021) [0/0]	167.62 (-) [167.62]	142.40 (0.00) [0]	0/0
706	SHAHPUR PATGAON SECTION I - [N24001027], MoRTH, MAHARASHTRA	1/2018	12/2019 (-) [6/2022]	150.79 (-) [150.79]	59.88 (0.00) [0]	1/4
707	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161], MoRTH, KARNATAKA	12/2017	1/2019 (7/2021) [7/2022]	297.30 (-) [318.28]	246.53 (20.98) [0]	0/0
708	SAKOLI TO BHANDARA - [N24001118], MoRTH, MAHARASHTRA	1/2017	6/2019 (-) [6/2022]	362.96 (-) [362.96]	215.12 (0.00) [0]	0/4
709	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415], MoRTH, MIZORAM	8/2010	10/2010 (12/2022) [0/0]	195.04 (434.65) [377.99]	400.65 (182.95) [0]	0/0
710	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777], MoRTH, UTTARAKHAND	11/2017	11/2019 (-) [0/0]	283.51 (-) [283.51]	196.03 (0.00) [0]	0/0
711	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881], MoRTH, MADHYA PRADESH	11/2017	2/2018 (9/2021) [11/2022]	184.62 (-) [184.62]	141.48 (0.00) [57]	0/0
712	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870], MoRTH, MADHYA PRADESH	3/2018	3/2018 (10/2021) [10/2022]	162.56 (-) [162.56]	137.52 (0.00) [55]	0/0
713	UPGRADATION OF PAWAI-SALEHA- JASSO-NAGOD ROAD TO 2L + PS - [N24000888], MoRTH, MADHYA PRADESH	3/2018	3/2018 (9/2021) [12/2022]	214.69 (-) [214.69]	90.24 (0.00) [57]	0/0
714	NILAJPHATA TO BHANDARA - [N24001043], MoRTH, MAHARASHTRA	1/2018	5/2020 (-) [9/2022]	420.63 (421.00) [420.63]	209.61 (0.00) [28]	0/4
715	SHIRUR TO KHARDA - [N24001123], MoRTH, MAHARASHTRA	2/2017	6/2019 (-) [9/2022]	381.77 (-) [381.77]	186.62 (0.00) [39]	0/4
716	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997], MoRTH, TELANGANA	3/2018	7/2019 (6/2022) [6/2022]	192.67 (-) [192.67]	171.04 (0.00) [0]	0/0
717	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177], MoRTH, TRIPURA	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	136.98 (0.00) [0]	0/0
718	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885], MoRTH, WEST BENGAL	3/2016	8/2019 (11/2022) [3/2023]	160.27 (-) [213.97]	47.17 (53.70) [43]	0/0
719	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (9/2021)	217.22 (-)	206.89 (9.66)	0/0

	- [N24000890],MoRTH,MADHYA PRADESH		[10/2022]	[226.88]	[50]	
720	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421],MoRTH,UTTAR PRADESH	7/2018	2/2024 (-) [2/2024]	1,948.25 (-) [1,948.25]	509.41 (0.00) [0]	0/0
721	MAHAD TO RAIGAD FORT - [N24001038],MoRTH,MAHARASHTRA	7/2018	5/2020 (-) [12/2022]	237.40 (-) [237.40]	31.41 (0.00) [31]	0/4
722	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915],MoRTH,ODISHA	12/2016	4/2018 (11/2022) [11/2022]	206.88 (-) [206.88]	134.11 (0.00) [55]	0/0
723	TALEGAON TO GONAPUR - [N24001096],MoRTH,MAHARASHTRA	1/2018	3/2019 (-) [3/2022]	264.41 (264.00) [264.41]	189.64 (0.00) [0]	0/0
724	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966],MoRTH,ANDHRA PRADESH	1/2016	8/2016 (6/2022) [6/2022]	348.95 (-) [348.95]	274.08 (0.00) [0]	3/4
725	DAHEGAON TO KUHI - [N24001017],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [9/2020]	228.89 (229.00) [228.89]	154.82 (0.00) [0]	3/4
726	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247],MoRTH,TELANGANA	10/2014	2/2017 (12/2022) [12/2022]	295.47 (-) [295.47]	214.36 (0.00) [70]	0/1
727	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933],MoRTH,ANDHRA PRADESH	2/2017	11/2017 (6/2022) [6/2022]	429.43 (373.05) [373.05]	338.66 (-56.38) [0]	3/4
728	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	347.78 (-) [347.78]	223.07 (0.00) [0]	0/0
729	KOLHA TO NASRATPUR - [N24001111],MoRTH,MAHARASHTRA	4/2016	4/2019 (-) [6/2022]	281.78 (282.00) [281.78]	73.92 (0.00) [0]	0/4
730	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988],MoRTH,TELANGANA	1/2018	12/2019 (11/2020) [11/2020]	230.03 (-) [230.03]	222.85 (0.00) [0]	0/0
731	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224],MoRTH,CHHATISGARH	3/2017	1/2018 (-) [10/2022]	423.79 (-) [423.79]	302.65 (0.00) [57]	0/0
732	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221],MoRTH,CHHATISGARH	1/2016	10/2016 (-) [12/2022]	624.98 (-) [731.50]	471.29 (106.52) [74]	0/0
733	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 -	12/2015	2/2020 (8/2021) [9/2022]	957.54 (-) [927.73]	784.39 (-29.81) [31]	0/0

	[N24000478],MoRTH,MADHYA PRADESH					
734	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645],MoRTH,ODISHA	8/2013	6/2016 (9/2022) [9/2022]	171.96 (172.00) [172.00]	108.00 (0.04) [75]	0/0
735	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160],MoRTH,KARNATAKA	9/2017	10/2018 (4/2021) [4/2021]	191.60 (-) [191.60]	108.94 (0.00) [0]	0/0
736	MEHKAR TO AJISPUR - [N24001048],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2022]	232.77 (-) [232.77]	151.60 (0.00) [0]	0/0
737	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993],MoRTH,TELANGANA	3/2018	9/2020 (6/2022) [6/2022]	322.81 (-) [322.81]	294.69 (0.00) [0]	0/0
738	WARDHA TO HINGAGHAT - [N24001098],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [7/2021]	216.90 (217.00) [216.90]	160.37 (0.00) [0]	1/4
739	PALPHATA TO PHULAMBARI - [N24001060],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [3/2022]	227.19 (227.00) [227.19]	141.92 (0.00) [0]	0/4
740	KARAD TO VITA - [N24001049],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [3/2022]	344.85 (245.00) [344.85]	260.80 (0.00) [0]	0/4
741	KHAMGAON TO SHEGAON - [N24001009],MoRTH,MAHARASHTRA	2/2017	5/2019 (-) [9/2019]	203.21 (203.00) [203.21]	163.81 (0.00) [0]	0/0
742	VADPALE TO BHOGAN KHURD - [N24001115],MoRTH,MAHARASHTRA	1/2017	11/2019 (-) [6/2022]	1,598.47 (1,560.00) [1,598.47]	1,246.19 (0.00) [0]	1/4
743	KHAMGAON TO DEULGAON SAKARSHA - [N24001074],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [3/2020]	249.29 (-) [249.29]	146.41 (0.00) [0]	0/0
744	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387],MoRTH,KARNATAKA	1/2017	9/2017 (4/2021) [12/2022]	264.34 (-) [264.34]	181.38 (0.00) [63]	0/0
745	PANCHARAL TO MANDANGHAR - [N24001107],MoRTH,MAHARASHTRA	7/2018	5/2020 (-) [12/2022]	381.08 (302.00) [381.08]	21.02 (0.00) [31]	0/4
746	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422],MoRTH,HIMACHAL PRADESH	2/2021	9/2021 (-) [0/0]	345.89 (-) [345.89]	88.41 (0.00) [0]	0/0
747	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216],MoRTH,JHARKHAND	12/2016	9/2021 (6/2022) [0/0]	196.00 (-) [196.00]	141.64 (0.00) [0]	3/4
748	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411],MoRTH,RAJASTHAN	12/2020	10/2021 (-) [0/0]	379.23 (-) [379.23]	46.00 (0.00) [0]	0/0
749	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM	11/2016	8/2017 (6/2022) [6/2022]	376.25 (-) [376.25]	365.44 (0.00) [0]	3/4

	KM84/550 - 124/200 OF NH2 - [N24000968],MoRTH,ANDHRA PRADESH					
750	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928],MoRTH,ANDHRA PRADESH	10/2015	12/2015 (1/2021) [1/2021]	333.21 (-) [353.43]	341.76 (20.22) [0]	3/3
751	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307],MoRTH,TRIPURA	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	107.81 (38.51) [0]	0/0
752	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222],MoRTH,CHHATISGARH	3/2016	7/2016 (-) [12/2022]	452.94 (-) [435.61]	126.17 (-17.33) [77]	0/0
753	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408],MoRTH,ASSAM	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	2.54 (0.00) [0]	0/0
754	4L+PS OF NH -58 FROM BEAWAR- GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG- II. - [N24001412],MoRTH,RAJASTHAN	12/2020	10/2021 (-) [0/0]	339.65 (-) [339.65]	63.00 (0.00) [0]	0/0
755	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228],MoRTH,CHHATISGARH	11/2017	5/2019 (-) [9/2022]	188.80 (-) [188.80]	125.56 (0.00) [40]	0/0
756	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939],MoRTH,ANDHRA PRADESH	3/2018	11/2018 (1/2022) [1/2022]	504.19 (504.00) [504.19]	495.73 (0.00) [0]	4/4
757	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904],MoRTH,HARYANA	1/2017	3/2019 (-) [10/2022]	247.25 (-) [247.25]	195.15 (0.00) [43]	0/1
758	MALEWADA TO CHIMUR - [N24001104],MoRTH,MAHARASHTRA	10/2016	6/2019 (-) [6/2022]	322.55 (-) [322.55]	213.50 (0.00) [0]	2/4
759	TALGAON TO KALMATH - [N24001136],MoRTH,MAHARASHTRA	10/2016	3/2020 (-) [10/2020]	904.70 (1,428.09) [904.70]	969.90 (0.00) [0]	2/4
760	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD - [N24000964],MoRTH,ANDHRA PRADESH	8/2016	1/2017 (12/2022) [12/2022]	350.61 (-) [350.61]	325.56 (0.00) [71]	3/4
761	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578],MoRTH,BIHAR	2/2016	5/2016 (3/2022) [11/2022]	553.30 (587.41) [587.41]	553.81 (34.11) [78]	0/0
762	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141],MoRTH,UTTAR	3/2016	1/2020 (-) [0/0]	240.30 (240.00) [240.30]	200.00 (0.00) [0]	0/0

	PRADESH					
763	WADIGODRI TO DHANGRIIMPRI - [N24001063],MoRTH,MAHARASHTRA	3/2018	2/2020 (-) [1/2021]	194.23 (194.00) [194.23]	134.91 (0.00) [0]	0/4
764	PEN TO KHOPOLI - [N24001106],MoRTH,MAHARASHTRA	3/2018	3/2018 (-) [6/2022]	301.39 (302.00) [301.39]	147.64 (0.00) [0]	0/4
765	KALMATH TO ZARAP - [N24001137],MoRTH,MAHARASHTRA	9/2016	3/2020 (-) [3/2020]	1,338.13 (2,617.44) [1,338.13]	1,346.39 (0.00) [0]	3/5
766	NALDURG TO AKKALKOT - [N24001051],MoRTH,MAHARASHTRA	2/2018	12/2019 (-) [12/2020]	274.50 (275.00) [274.50]	143.39 (0.00) [0]	0/4
767	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388],MoRTH,KARNATAKA	3/2019	12/2019 (12/2022) [12/2023]	423.15 (-) [423.15]	216.18 (0.00) [48]	0/0
768	CHALISGAON TO NANDGAON - [N24001108],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [3/2021]	206.97 (207.00) [206.97]	145.87 (0.00) [0]	0/4
769	FARDAPUR TO JALGAON - [N24001126],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [6/2022]	456.45 (-) [456.45]	425.07 (0.00) [0]	0/4
770	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332],MoRTH,MAHARASHTRA	1/2015	/ (-) [9/2022]	225.81 (-) [225.81]	114.55 (0.00) [-]	0/0
771	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574],MoRTH,BIHAR	11/2013	7/2016 (6/2022) [6/2022]	683.83 (698.82) [698.82]	717.89 (14.99) [0]	0/0
772	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 - [N24001441],MoRTH,MEGHALAYA	8/2020	2/2022 (-) [0/0]	302.88 (-) [302.88]	9.20 (0.00) [0]	0/0
773	ARDHAPUR TO HIMAYATNAGAR - [N24001079],MoRTH,MAHARASHTRA	12/2017	6/2020 (-) [6/2022]	426.06 (426.00) [426.06]	247.48 (0.00) [0]	1/4
774	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR - [N24001454],MoRTH,TAMIL NADU	2/2022	8/2022 (-) [8/2022]	184.15 (-) [184.15]	0.00 (0.00) [0]	0/0
775	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD- SAMSHABAD SECTION OF NH - [N24000987],MoRTH,TELANGANA	1/2018	5/2020 (12/2022) [12/2022]	283.15 (-) [283.15]	201.27 (0.00) [31]	0/0
776	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511],MoRTH,UTTAR PRADESH	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	141.33 (0.00) [0]	0/0
777	REHABILITAITON AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970],MoRTH,ANDHRA	1/2017	1/2018 (12/2022) [12/2022]	576.48 (686.13) [686.13]	503.77 (109.65) [59]	3/4

	PRADESH					
778	BAMNI TO NAVEGAON - [N24001110], MoRTH, MAHARASHTRA	9/2017	4/2020 (-) [3/2021]	241.69 (242.00) [241.69]	172.01 (0.00) [0]	1/4
779	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821], MoRTH, A & N ISLANDS	11/2017	11/2019 (-) [0/0]	257.34 (-) [238.00]	214.90 (-19.34) [0]	0/0
780	NAIGAONBANDI TO MANGRULPIR - [N24001094], MoRTH, MAHARASHTRA	12/2017	3/2019 (-) [12/2021]	244.04 (244.00) [244.04]	177.32 (0.00) [0]	0/0
781	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985], MoRTH, TELANGANA	1/2017	5/2019 (10/2020) [10/2020]	359.27 (-) [359.27]	311.81 (0.00) [0]	0/0
782	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412], MoRTH, MADHYA PRADESH	1/2012	4/2015 (-) [0/0]	410.72 (-) [410.72]	392.45 (0.00) [0]	0/0
783	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308], MoRTH, MIZORAM	8/2010	10/2010 (12/2022) [0/0]	193.69 (374.59) [327.92]	347.48 (134.23) [0]	0/0
784	AKOLA TO AKOT - [N24001003], MoRTH, MAHARASHTRA	1/2017	6/2019 (-) [9/2022]	313.95 (-) [313.95]	142.29 (0.00) [39]	0/4
785	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290], MoRTH, ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	342.55 (-) [342.55]	264.65 (0.00) [0]	0/0
786	CHIKLI TO TAKARKHED - [N24001083], MoRTH, MAHARASHTRA	3/2018	12/2019 (-) [12/2020]	393.10 (393.00) [393.10]	253.71 (0.00) [0]	2/4
787	KARAD TO TAGAON - [N24001053], MoRTH, MAHARASHTRA	1/2017	6/2019 (-) [12/2022]	537.81 (538.00) [537.81]	237.00 (0.00) [42]	0/4
788	PARSHURAM GHAT TO ARAWALI - [N24001133], MoRTH, MAHARASHTRA	4/2016	12/2019 (-) [9/2022]	983.14 (2,226.11) [983.14]	806.99 (0.00) [33]	1/4
789	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210], MoRTH, UTTAR PRADESH	3/2018	/ (-) [7/2022]	306.59 (-) [306.59]	218.06 (0.00) [0]	0/0
790	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176], MoRTH, NAGALAND	10/2016	12/2020 (9/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]	0/0
791	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925], MoRTH, GUJARAT	10/2018	5/2019 (-) [5/2022]	400.76 (394.44) [394.44]	215.03 (-6.32) [0]	2/4
792	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 -	2/2018	6/2020 (1/2021) [1/2021]	206.13 (-) [206.13]	185.75 (0.00) [0]	0/0

	[N24000989],MoRTH,TELANGANA					
793	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531],MoRTH,BIHAR	1/1991	/ (11/2022) [11/2022]	319.68 (404.10) [404.10]	400.67 (84.42) [-]	0/0
794	WASHIM TO DASTAPUR - [N24001068],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [9/2020]	165.51 (-) [165.51]	133.93 (0.00) [0]	1/4
795	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152],MoRTH,ASSAM	9/2018	9/2021 (12/2022) [12/2022]	160.00 (-) [160.00]	138.51 (0.00) [15]	0/0
796	KAJI TO KUSALAM - [N24001037],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [6/2022]	554.78 (-) [554.78]	317.29 (0.00) [0]	2/4
797	INDAPUR TO VADPALE - [N24001114],MoRTH,MAHARASHTRA	1/2017	12/2019 (-) [6/2022]	1,202.52 (1,203.00) [1,202.52]	929.67 (0.00) [0]	1/4
798	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385],MoRTH,ANDHRA PRADESH	6/2020	5/2021 (12/2022) [12/2022]	221.40 (-) [221.40]	90.53 (0.00) [19]	2/4
799	KOLDE TO KHETIYA - [N24001090],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2022]	509.18 (-) [509.18]	283.13 (0.00) [0]	0/4
800	KALMAB TO RALEGAON - [N24001044],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [8/2020]	467.78 (-) [467.78]	467.78 (0.00) [0]	0/4
801	LATUR TO PANGAON - [N24001066],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [12/2020]	336.47 (336.00) [336.47]	203.39 (0.00) [0]	0/4
802	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527],MoRTH,ODISHA	12/2011	8/2015 (6/2022) [6/2022]	191.08 (-) [191.08]	182.41 (0.00) [0]	0/0
803	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372],MoRTH,ARUNACHAL PRADESH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	176.69 (0.00) [0]	0/0
804	MANGRUPHIR TO MAHAN - [N24001087],MoRTH,MAHARASHTRA	3/2018	11/2019 (-) [2/2022]	222.13 (222.00) [222.13]	156.87 (0.00) [0]	0/4
805	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931],MoRTH,ANDHRA PRADESH	11/2016	5/2017 (8/2022) [8/2022]	290.15 (290.15) [290.15]	188.56 (0.00) [63]	3/4
806	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907],MoRTH,PUNJAB	3/2018	8/2020 (-) [12/2022]	293.10 (-) [293.10]	256.89 (0.00) [28]	0/1
807	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG -	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	151.70 (0.00) [0]	0/0

	[N24000776],MoRTH,UTTARAKHAND					
808	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257],MoRTH,GOA	3/2015	/ (12/2021) [3/2022]	298.33 (354.43) [298.33]	349.92 (0.00) [0]	0/4
809	BHOKAR TO SARSAM - [N24001128],MoRTH,MAHARASHTRA	2/2017	7/2019 (-) [11/2020]	295.09 (-) [295.99]	186.27 (0.90) [0]	0/4
810	GADCHIROLI TO MUL - [N24001116],MoRTH,MAHARASHTRA	12/2016	6/2019 (-) [3/2022]	484.15 (-) [484.15]	349.78 (0.00) [0]	2/4
811	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201],MoRTH,BIHAR	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	535.86 (0.00) [0]	0/0
812	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159],MoRTH,KARNATAKA	1/2018	7/2018 (3/2021) [6/2022]	159.70 (-) [159.70]	122.11 (0.00) [0]	0/0
813	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369],MoRTH,KERALA	2/2017	8/2017 (3/2022) [0/0]	294.28 (296.53) [296.53]	211.30 (2.25) [0]	0/0
814	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383],MoRTH,HIMACHAL PRADESH	8/2020	4/2021 (-) [0/0]	349.20 (-) [349.20]	206.92 (0.00) [0]	0/0
815	NANDGAON TO MORSHI - [N24001014],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [11/2019]	385.87 (386.00) [385.87]	258.29 (0.00) [0]	0/0
816	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983],MoRTH,TELANGANA	1/2017	10/2019 (10/2019) [10/2019]	196.52 (-) [196.52]	121.70 (0.00) [0]	0/0
817	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236],MoRTH,TAMIL NADU	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	276.41 (0.00) [0]	3/4
818	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 - [N24001455],MoRTH,TAMIL NADU	2/2022	8/2022 (-) [8/2022]	191.33 (-) [191.33]	0.00 (0.00) [0]	0/0
819	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	421.48 (-) [421.48]	147.23 (0.00) [0]	0/0
820	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779],MoRTH,UTTARAKHAND	2/2018	2/2020 (10/2022) [10/2022]	418.88 (-) [418.88]	264.67 (0.00) [32]	0/0
821	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF	1/2017	5/2019 (8/2019) [8/2019]	244.54 (-) [244.54]	169.89 (0.00) [0]	0/0

	THIRUMALAGIRI TO SURYAPET SE - [N24000982],MoRTH,TELANGANA					
822	OMREGA TO AUSA - [N24001067],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [9/2021]	272.04 (272.00) [272.04]	272.04 (0.00) [0]	0/4
823	JALGAON TO BHADGAON - [N24001045],MoRTH,MAHARASHTRA	1/2018	11/2019 (-) [1/2021]	307.54 (308.00) [307.54]	221.49 (0.00) [0]	0/4
824	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU- GONDIGUDA SECT - [N24001386],MoRTH,ANDHRA PRADESH	8/2020	3/2021 (3/2023) [3/2023]	222.61 (-) [222.61]	42.15 (0.00) [24]	1/4
825	REHABILITATION AND UP- GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875],MoRTH,MADHYA PRADESH	2/2018	3/2018 (3/2022) [5/2023]	169.63 (-) [169.63]	89.32 (0.00) [62]	0/0
826	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778],MoRTH,UTTARAKHAND	11/2017	11/2019 (10/2020) [10/2020]	266.52 (-) [266.52]	153.44 (0.00) [0]	0/0
827	NAGBHID TO ARMORI - [N24001119],MoRTH,MAHARASHTRA	9/2016	7/2019 (-) [11/2019]	269.05 (-) [269.05]	200.00 (0.00) [0]	0/4
828	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC - [N24001373],MoRTH,ARUNACHAL PRADESH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	141.82 (0.00) [0]	0/0
829	PATGAON KHOPOLI SECTION I - [N24001028],MoRTH,MAHARASHTRA	1/2018	12/2019 (-) [3/2022]	170.00 (-) [170.00]	125.80 (0.00) [0]	0/4
830	HIMAYATNAGAR TO PHULSAWANGI - [N24001081],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [6/2022]	294.87 (295.00) [294.87]	163.51 (0.00) [0]	1/4
831	REHABILITATION AND UPGRADATION OF LOSARI- MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967],MoRTH,ANDHRA PRADESH	3/2016	9/2016 (7/2022) [7/2022]	444.84 (-) [444.84]	396.31 (0.00) [0]	3/4
832	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [3/2022]	336.21 (336.00) [336.21]	234.29 (0.00) [0]	0/4
833	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDA-SAGWARA) SECTION OF NH- 927A. PKG-- [N24001413],MoRTH,RAJASTHAN	2/2021	11/2021 (-) [0/0]	240.99 (-) [240.99]	12.16 (0.00) [0]	0/0
834	AHMEDNAGAR TO BARAMATI - [N24001100],MoRTH,MAHARASHTRA	1/2017	8/2019 (-) [8/2021]	955.40 (-) [955.40]	492.20 (0.00) [0]	0/4
835	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880],MoRTH,WEST BENGAL	2/2018	9/2020 (3/2022) [3/2023]	426.18 (-) [426.18]	284.89 (0.00) [30]	0/0

836	TASGAON TO SHIRDHON - [N24001054], MoRTH, MAHARASHTRA	1/2017	11/2019 (-) [7/2019]	195.64 (196.00) [195.64]	116.92 (0.00) [0]	0/4
837	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898], MoRTH, MADHYA PRADESH	1/2016	7/2018 (5/2021) [9/2022]	809.16 (-) [809.16]	635.00 (0.00) [50]	0/0
838	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301], MoRTH, ANDHRA PRADESH	3/2015	10/2015 (6/2021) [6/2021]	271.45 (-) [271.45]	234.26 (0.00) [0]	4/4
839	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375], MoRTH, ARUNACHAL PRADESH	6/2020	3/2027 (-) [3/2027]	496.47 (-) [496.47]	32.23 (0.00) [0]	0/0
840	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH. 485+2 - [N24001158], MoRTH, KARNATAKA	3/2018	6/2019 (1/2022) [3/2023]	159.97 (-) [242.61]	94.29 (82.64) [45]	0/0
841	BARELA-MANDLA SECTION OF NH- 12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378], MoRTH, MADHYA PRADESH	6/2015	/ (3/2021) [9/2022]	390.51 (-) [390.51]	314.69 (0.00) [-]	0/0
842	MANJUSUMBA TO CHUMBALI - [N24001031], MoRTH, MAHARASHTRA	1/2017	8/2019 (-) [3/2022]	228.54 (-) [228.54]	161.24 (0.00) [0]	2/4
843	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM. 7.950 (UPPAL) TO KM. 14.200 OF NH-163 TO DE-CONGES - [N24000994], MoRTH, TELANGANA	3/2018	7/2020 (5/2023) [5/2023]	626.76 (-) [626.76]	227.71 (0.00) [34]	0/0
844	JALGAON TO NANDURA - [N24001088], MoRTH, MAHARASHTRA	3/2018	12/2019 (-) [11/2020]	177.84 (177.00) [177.84]	110.20 (0.00) [0]	0/0
845	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409], MoRTH, RAJASTHAN	7/2020	9/2021 (-) [0/0]	319.09 (-) [319.09]	15.53 (0.00) [0]	0/4
846	MANTHA TALUKAS BORDER TO PARTUR - [N24001033], MoRTH, MAHARASHTRA	1/2017	7/2019 (-) [3/2022]	486.19 (-) [486.19]	315.19 (0.00) [0]	2/4
847	NASRATPUR TO BARASGAON - [N24001112], MoRTH, MAHARASHTRA	7/2016	9/2019 (-) [6/2022]	406.54 (407.00) [406.54]	193.70 (0.00) [0]	2/4
848	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940], MoRTH, ANDHRA PRADESH	3/2016	5/2016 (11/2022) [11/2022]	995.09 (995.00) [995.09]	643.29 (0.00) [78]	3/4
849	DASTAPUR TO KARANJA - [N24001070], MoRTH, MAHARASHTRA	3/2018	12/2019 (-) [9/2020]	182.63 (-) [182.63]	137.99 (0.00) [0]	2/4
850	ARNI TO NAIGAINBANDI - [N24001093], MoRTH, MAHARASHTRA	12/2017	12/2019 (-) [6/2022]	309.94 (310.00) [309.94]	207.17 (0.00) [0]	0/0

851	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891],MoRTH,MADHYA PRADESH	3/2018	3/2018 (10/2021) [10/2022]	233.04 (-) [233.04]	184.37 (0.00) [55]	0/0
852	AHMADPUR TO PIMPLA - [N24001029],MoRTH,MAHARASHTRA	1/2017	8/2019 (-) [6/2022]	422.38 (-) [422.38]	243.81 (0.00) [0]	2/4
853	PUNE TO MALE VILLAGE - [N24001078],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [4/2022]	228.31 (-) [228.31]	100.97 (0.00) [0]	0/0
854	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	450.65 (-) [450.65]	117.78 (0.00) [0]	0/0
855	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294],MoRTH,ARUNACHAL PRADESH	3/2019	3/2027 (-) [3/2027]	560.39 (-) [560.39]	307.44 (0.00) [0]	0/0
856	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194],MoRTH,ARUNACHAL PRADESH	9/2011	/ (12/2021) [12/2021]	1,979.00 (-) [2,036.90]	1,251.08 (57.90) [0]	0/0
857	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899],MoRTH,MADHYA PRADESH	3/2016	6/2019 (4/2021) [9/2022]	877.79 (-) [949.54]	807.22 (71.75) [39]	0/0
858	MORSHI TO ACHALPUR - [N24001015],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [12/2020]	341.16 (341.00) [341.16]	247.86 (0.00) [0]	0/0
859	UPGRADATION OF ADHALGAON- JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH - [N24001448],MoRTH,MAHARASHTRA	11/2021	2/2022 (-) [2/2022]	223.35 (-) [223.35]	0.00 (0.00) [0]	0/0
860	NANDED TO JALKOT - [N24001069],MoRTH,MAHARASHTRA	12/2017	9/2019 (-) [6/2022]	456.93 (457.00) [456.93]	456.93 (0.00) [0]	1/4
861	OSMANNAGAR TO KUNDRALE - [N24001075],MoRTH,MAHARASHTRA	9/2017	8/2020 (-) [6/2022]	344.25 (344.00) [344.25]	177.10 (0.00) [0]	0/4
862	KARWANDI TO RAJURI - [N24001058],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [6/2022]	276.95 (277.00) [276.95]	160.17 (0.00) [0]	0/4
863	ANJANGAON TO MAH/MP BORDER - [N24001007],MoRTH,MADHYA PRADESH	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	326.56 (0.00) [0]	0/4
864	KOTHARI TO DHANORA - [N24001073],MoRTH,MAHARASHTRA	9/2018	8/2020 (-) [9/2022]	301.38 (301.00) [301.38]	195.29 (0.00) [25]	0/0
865	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370],MoRTH,KERALA	2/2017	9/2017 (1/2022) [0/0]	380.76 (372.87) [372.87]	312.49 (-7.89) [0]	0/0
866	AURANGABAD TO SILLOD - [N24001124],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [6/2022]	456.32 (-) [456.32]	341.63 (0.00) [0]	0/4

867	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941],MoRTH,PUNJAB	3/2018	8/2020 (-) [10/2022]	293.64 (-) [293.64]	283.78 (0.00) [26]	0/0
868	CHIKALI TO KHAMGAON - [N24001012],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [1/2020]	548.03 (548.00) [548.03]	406.13 (0.00) [0]	0/4
869	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877],MoRTH,UTTAR PRADESH	11/2016	/ (-) [7/2022]	326.99 (327.00) [326.99]	281.05 (0.00) [0]	0/0
870	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926],MoRTH,GUJARAT	8/2017	3/2018 (-) [12/2022]	962.43 (-) [962.43]	594.81 (0.00) [57]	3/4
871	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917],MoRTH,ODISHA	3/2018	8/2018 (10/2022) [10/2022]	199.16 (-) [199.16]	101.34 (0.00) [50]	0/0
872	BHADGAON TO CHALISGAON - [N24001047],MoRTH,MAHARASHTRA	1/2018	11/2019 (-) [12/2020]	259.55 (260.00) [259.55]	215.68 (0.00) [0]	0/0
873	BHOGAN KHURD TO KASHEDI - [N24001132],MoRTH,MAHARASHTRA	9/2017	6/2021 (-) [9/2022]	743.21 (743.00) [743.21]	475.80 (0.00) [15]	1/4
874	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239],MoRTH,TAMIL NADU	3/2018	6/2019 (-) [0/0]	240.38 (212.74) [240.38]	171.85 (0.00) [0]	3/4
875	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254],MoRTH,MAHARASHTRA	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	303.72 (0.00) [0]	3/4
876	KUSUMBA TO MALEGAON - [N24001109],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [7/2021]	243.45 (244.00) [243.45]	170.25 (0.00) [0]	0/4
877	MEHKAR TO CHIKALI - [N24001011],MoRTH,MAHARASHTRA	2/2017	5/2019 (-) [3/2020]	322.48 (322.00) [322.48]	230.03 (0.00) [0]	0/4
878	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910],MoRTH,PUNJAB	3/2018	11/2020 (-) [12/2022]	170.57 (192.48) [170.57]	87.84 (0.00) [25]	0/1
879	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226],MoRTH,CHHATISGARH	12/2014	3/2015 (-) [3/2023]	496.02 (-) [496.02]	240.11 (0.00) [96]	0/0
880	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172],MoRTH,KARNATAKA	1/2017	8/2017 (1/2021) [7/2022]	291.49 (-) [291.49]	217.77 (0.00) [0]	0/0
881	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980],MoRTH,TELANGANA	10/2016	2/2019 (6/2022) [6/2022]	298.32 (-) [298.32]	142.58 (0.00) [0]	0/0
882	CONSTRUCTION OF 2 LANE ROAD	3/2019	3/2027	403.68	224.20	0/0

	OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289],MoRTH,ARUNACHAL PRADESH		(-) [3/2027]	(-) [403.68]	(0.00) [0]	
883	PANDHARPUR TO SANGOLA - [N24001102],MoRTH,MAHARASHTRA	7/2017	7/2019 (-) [3/2022]	218.38 (-) [218.38]	175.69 (0.00) [0]	0/4
884	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775],MoRTH,UTTARAKHAND	6/2017	6/2019 (10/2022) [10/2022]	282.08 (-) [282.08]	206.46 (0.00) [40]	0/0
885	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT - [N24001427],MoRTH,GUJARAT	6/2020	4/2023 (-) [4/2023]	166.21 (-) [166.21]	53.63 (0.00) [0]	2/4
886	JINTUR TO PARBHANI - [N24001039],MoRTH,MAHARASHTRA	1/2017	/ (-) [9/2022]	356.66 (-) [356.66]	162.29 (0.00) [-]	0/4
887	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929],MoRTH,ANDHRA PRADESH	9/2016	2/2017 (2/2022) [2/2022]	372.68 (309.37) [309.37]	274.73 (-63.31) [0]	4/4
888	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382],MoRTH,BIHAR	1/1991	/ (6/2022) [3/2023]	675.00 (780.77) [780.77]	453.21 (105.77) [-]	0/0
889	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576],MoRTH,BIHAR	2/2016	5/2016 (6/2022) [11/2022]	178.85 (225.06) [225.06]	212.91 (46.21) [78]	0/0
890	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217],MoRTH,CHHATISGARH	1/2016	8/2016 (-) [12/2022]	497.14 (-) [572.66]	280.46 (75.52) [76]	0/0
891	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179],MoRTH,NAGALAND	3/2017	11/2020 (12/2022) [9/2022]	217.35 (-) [217.35]	173.98 (0.00) [22]	0/0
892	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610],MoRTH,BIHAR	8/2016	12/2016 (6/2022) [5/2022]	1,742.01 (-) [1,742.01]	1,845.15 (0.00) [0]	0/0
893	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579],MoRTH,BIHAR	1/2014	10/2016 (3/2022) [3/2023]	1,408.85 (2,138.16) [2,138.16]	1,412.08 (729.31) [77]	0/0
894	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130],MoRTH,UTTARAKHAND	8/2016	12/2017 (1/2021) [1/2021]	234.88 (-) [234.88]	174.51 (0.00) [0]	0/0
895	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT -	5/2018	5/2018 (7/2022) [7/2022]	171.60 (-) [171.60]	82.13 (0.00) [0]	0/0

	[N24001168],MoRTH,KARNATAKA					
896	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180],MoRTH,NAGALAND	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	174.77 (0.00) [0]	0/0
897	SARAD VANI PIMPALGAON - [N24001103],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2021]	250.46 (-) [250.46]	174.16 (0.00) [0]	0/4
898	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219],MoRTH,CHHATISGARH	1/2016	9/2016 (-) [3/2023]	476.20 (544.00) [544.00]	452.11 (67.80) [78]	0/0
899	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410],MoRTH,RAJASTHAN	8/2020	12/2020 (-) [0/0]	216.72 (-) [216.72]	81.28 (0.00) [0]	2/4
900	RALEGAON TO RAMTIRTH - [N24001046],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2022]	210.81 (-) [210.81]	210.81 (0.00) [0]	0/4
901	VITA TO NAGAJ - [N24001050],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [6/2022]	304.58 (305.00) [304.58]	142.11 (0.00) [0]	0/4
902	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934],MoRTH,ANDHRA PRADESH	3/2018	8/2018 (7/2022) [7/2022]	228.32 (202.83) [202.83]	170.97 (-25.49) [0]	3/4
903	WADI TO ASOLA - [N24001022],MoRTH,MAHARASHTRA	1/2017	9/2019 (-) [12/2022]	363.82 (364.00) [363.82]	109.56 (0.00) [39]	1/4
904	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [3/2022]	223.46 (-) [223.46]	68.00 (0.00) [0]	0/0
905	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958],MoRTH,RAJASTHAN	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	330.30 (0.00) [0]	3/4
906	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056],MoRTH,MAHARASHTRA	2/2017	7/2019 (-) [3/2022]	422.02 (422.00) [422.02]	302.13 (0.00) [0]	0/0
907	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209],MoRTH,UTTAR PRADESH	3/2016	9/2020 (-) [12/2021]	296.50 (-) [296.50]	259.77 (0.00) [0]	0/0
908	MORSHI TO MAH/MP BORDER - [N24001016],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [12/2019]	471.61 (472.00) [471.61]	321.02 (0.00) [0]	0/0
909	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241],MoRTH,RAJASTHAN	3/2020	8/2020 (-) [0/0]	255.23 (-) [255.23]	89.00 (0.00) [0]	3/4
910	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780],MoRTH,UTTARAKHAND	2/2018	/ (10/2022) [10/2022]	293.68 (-) [293.68]	185.08 (0.00) [-]	0/0
911	PARBHANI TO GANGKHED - [N24001065],MoRTH,MAHARASHTRA	3/2018	12/2019 (-)	238.19 (238.00)	190.37 (0.00)	0/4

			[3/2022]	[238.19]	[0]	
912	AKOT TO ANJANGAON - [N24001006],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [11/2020]	245.77 (246.00) [245.77]	220.54 (0.00) [0]	0/4
913	NAGAJ TO VAIJAPUR - [N24001023],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [12/2020]	376.72 (377.00) [376.72]	273.87 (0.00) [0]	0/4
914	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164],MoRTH,KARNATAKA	10/2016	3/2017 (3/2021) [6/2022]	396.96 (-) [396.96]	272.96 (0.00) [0]	0/0
915	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981],MoRTH,TELANGANA	10/2016	3/2019 (4/2023) [4/2023]	248.83 (-) [248.83]	149.11 (0.00) [49]	0/0
916	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991],MoRTH,TELANGANA	2/2018	11/2019 (6/2022) [6/2022]	220.28 (-) [220.28]	193.45 (0.00) [0]	0/0
917	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245],MoRTH,TELANGANA	1/2014	3/2016 (9/2019) [9/2019]	270.00 (-) [270.00]	7.65 (0.00) [0]	1/4
918	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) - [N24001442],MoRTH,SIKKIM	10/2021	5/2024 (-) [5/2024]	385.15 (-) [385.15]	8.95 (0.00) [0]	0/0
919	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513],MoRTH,MADHYA PRADESH	3/2015	8/2017 (6/2021) [12/2022]	511.83 (-) [511.83]	432.54 (0.00) [64]	0/0
920	BARASGAON TO RAHATEE - [N24001113],MoRTH,MAHARASHTRA	7/2016	9/2018 (-) [3/2022]	289.11 (290.00) [289.11]	144.69 (0.00) [0]	0/4
921	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173],MoRTH,KARNATAKA	2/2017	5/2019 (5/2023) [5/2023]	157.32 (187.61) [157.32]	24.20 (0.00) [48]	0/0
922	KANTE TO WAKED - [N24001134],MoRTH,MAHARASHTRA	3/2016	11/2019 (-) [12/2022]	1,230.02 (1,230.00) [1,230.02]	664.06 (0.00) [37]	1/4
923	DEORI TO AMGAON - [N24001032],MoRTH,MAHARASHTRA	1/2017	5/2019 (-) [6/2022]	409.62 (410.00) [409.62]	290.44 (0.00) [0]	0/4
924	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392],MoRTH,ASSAM	11/2010	5/2017 (6/2022) [6/2022]	268.08 (-) [390.73]	386.57 (122.65) [0]	0/0
925	CONSTRUCTION OF RING ROAD FOR RAEARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331],MoRTH,UTTAR PRADESH	1/2014	3/2016 (-) [7/2022]	282.41 (-) [319.96]	218.75 (37.55) [0]	0/0
926	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05	3/2019	3/2027 (-) [3/2027]	486.70 (-) [486.70]	201.16 (0.00) [0]	0/0

	(PACKAGE - [N24001293],MoRTH,ARUNACHAL PRADESH					
927	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207],MoRTH,UTTAR PRADESH	3/2018	1/2021 (-) [0/0]	185.18 (-) [185.18]	84.07 (0.00) [0]	0/0
928	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782],MoRTH,UTTARAKHAND	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]	0/0
929	BHANDARA TO GHOTITOK - [N24001018],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [12/2019]	392.83 (393.00) [392.83]	274.75 (0.00) [0]	0/0
930	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876],MoRTH,WEST BENGAL	1/2017	9/2019 (3/2022) [12/2022]	396.86 (-) [396.86]	282.77 (0.00) [39]	0/0
931	DIGRAS DARWAH KARANJA - [N24001013],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [3/2022]	391.06 (391.00) [391.06]	256.99 (0.00) [0]	0/0
932	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969],MoRTH,ANDHRA PRADESH	1/2017	9/2017 (12/2022) [12/2022]	263.45 (263.45) [263.45]	127.85 (0.00) [63]	1/4
933	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT - [N24001423],MoRTH,UTTAR PRADESH	4/2021	3/2022 (-) [9/2023]	309.48 (-) [309.48]	27.13 (0.00) [18]	0/0
934	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894],MoRTH,MADHYA PRADESH	2/2018	3/2018 (11/2021) [6/2022]	279.44 (-) [279.44]	231.61 (0.00) [0]	0/0
935	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639],MoRTH,ODISHA	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	183.94 (0.50) [0]	0/0
936	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206],MoRTH,UTTAR PRADESH	3/2018	4/2020 (-) [8/2022]	263.89 (-) [242.05]	190.01 (-21.84) [28]	0/0
937	PARTUR TO MAJALGAON - [N24001034],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [6/2022]	420.57 (-) [420.57]	270.28 (0.00) [0]	2/4
938	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014- 15-775) - [N24001166],MoRTH,KARNATAKA	3/2015	1/2016 (12/2021) [9/2022]	159.12 (-) [159.12]	123.72 (0.00) [80]	0/0
939	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W - [N24001424],MoRTH,UTTAR	3/2021	3/2022 (-) [9/2023]	185.09 (-) [185.09]	3.58 (0.00) [18]	0/0

	PRADESH					
940	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218],MoRTH,CHHATISGARH	11/2015	6/2017 (-) [12/2022]	335.32 (-) [335.32]	277.98 (0.00) [66]	0/0
941	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374],MoRTH,ARUNACHAL PRADESH	6/2020	3/2027 (-) [3/2027]	437.60 (-) [437.60]	41.92 (0.00) [0]	0/0
942	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 - [N24000422],MoRTH,ANDHRA PRADESH	3/2015	9/2015 (-) [9/2015]	309.01 (-) [309.01]	0.00 (0.00) [0]	0/0
943	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932],MoRTH,ANDHRA PRADESH	1/2017	8/2017 (8/2022) [8/2022]	319.28 (319.28) [319.28]	241.94 (0.00) [60]	4/4
944	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990],MoRTH,TELANGANA	2/2018	11/2019 (3/2022) [3/2022]	294.13 (-) [294.13]	174.27 (0.00) [0]	0/0
945	KARASWADA TO BAMBOLIM - [N24001005],MoRTH,GOA	3/2017	12/2019 (-) [3/2022]	852.67 (-) [852.67]	234.18 (0.00) [0]	1/4
946	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381],MoRTH,HIMACHAL PRADESH	8/2020	4/2021 (-) [0/0]	272.98 (-) [272.98]	57.24 (0.00) [0]	0/0
947	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165],MoRTH,KARNATAKA	11/2016	3/2017 (3/2021) [9/2022]	314.90 (-) [314.90]	206.30 (0.00) [66]	0/0
948	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198],MoRTH,MADHYA PRADESH	1/2019	3/2021 (11/2021) [12/2022]	264.50 (-) [264.50]	179.94 (0.00) [21]	0/0
949	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162],MoRTH,KARNATAKA	3/2018	10/2018 (4/2021) [4/2021]	325.86 (-) [386.41]	347.42 (60.55) [0]	0/0
950	AMD1 TO SAONER - [N24001021],MoRTH,MAHARASHTRA	1/2017	6/2019 (-) [2/2020]	396.91 (397.00) [396.91]	289.79 (0.00) [0]	3/4
951	JALKOT TO TOGRI - [N24001071],MoRTH,MAHARASHTRA	7/2018	8/2020 (-) [3/2022]	299.92 (300.00) [299.92]	186.89 (0.00) [0]	0/4
952	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922],MoRTH,GUJARAT	12/2017	11/2018 (6/2021) [9/2022]	867.97 (913.49) [913.49]	700.54 (45.52) [46]	3/4
953	IMPROVEMENTS AND	8/2016	2/2017	175.50	164.41	0/0

	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157],MoRTH,KARNATAKA		(12/2020) [8/2022]	(241.60) [241.60]	(66.10) [66]	
954	KARAD PATAN CHIPLUN GUHAGAR - [N24001057],MoRTH,MAHARASHTRA	2/2017	6/2019 (-) [9/2022]	407.19 (407.00) [407.19]	323.02 (0.00) [39]	0/4
955	SARSAM TO KOTHARI - [N24001002],MoRTH,MAHARASHTRA	2/2016	7/2019 (-) [9/2022]	545.64 (-) [545.64]	216.28 (0.00) [38]	0/4
956	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893],MoRTH,MADHYA PRADESH	11/2017	2/2018 (3/2022) [10/2022]	254.17 (-) [254.17]	197.45 (0.00) [56]	0/0
957	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080],MoRTH,MAHARASHTRA	3/2018	12/2019 (-) [4/2022]	256.15 (-) [256.15]	100.31 (0.00) [0]	0/0
958	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986],MoRTH,TELANGANA	1/2017	5/2019 (7/2021) [7/2021]	300.00 (-) [300.00]	217.68 (0.00) [0]	0/0
959	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996],MoRTH,TELANGANA	1/2017	10/2019 (6/2021) [6/2021]	605.08 (-) [605.08]	411.93 (0.00) [0]	0/0
960	PIMPLA TO MANJARUMBHA - [N24001030],MoRTH,MAHARASHTRA	1/2017	8/2019 (-) [6/2022]	595.77 (-) [595.77]	332.72 (0.00) [0]	2/4
961	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820],MoRTH,A & N ISLANDS	11/2017	11/2019 (-) [10/2022]	237.80 (-) [238.00]	94.55 (0.20) [35]	0/0
962	PAITHAN TO SHIRUR - [N24001122],MoRTH,MAHARASHTRA	3/2017	6/2019 (-) [12/2022]	341.80 (-) [341.80]	203.09 (0.00) [42]	0/4
963	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475],MoRTH,MADHYA PRADESH	11/2015	1/2020 (6/2021) [9/2022]	628.45 (-) [628.45]	467.04 (0.00) [32]	0/0
964	KURUDWADI TO PANDHARPUR - [N24001101],MoRTH,MAHARASHTRA	1/2017	7/2019 (-) [3/2022]	307.63 (-) [307.63]	197.27 (0.00) [0]	0/4
965	4-LANING OF DERGAON TOWN - [N24001435],NHIDCL,ASSAM	3/2020	6/2022 (-) [6/2022]	287.63 (-) [287.63]	89.55 (0.00) [0]	0/4
966	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356],NHIDCL,MIZORAM	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	52.09 (0.00) [0]	0/4
967	MARAM - PEREN PKG-3 - [N24001439],NHIDCL,MANIPUR	8/2021	5/2023 (-) [11/2023]	467.41 (-) [467.41]	20.74 (0.00) [6]	0/4
968	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438],NHIDCL,ASSAM	12/2015	12/2018 (-) [12/2022]	289.99 (-) [289.99]	120.17 (0.00) [48]	2/4
969	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326],NHIDCL,ARUNACHAL	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	0.00 (0.00) [0]	2/4

	PRADESH					
970	DEMBUEN - BRUNI - [N24001321],NHIDCL,ARUNACHAL PRADESH	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	167.37 (0.00) [0]	2/4
971	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196],NHIDCL,ASSAM	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	98.01 (0.00) [0]	2/4
972	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745],NHIDCL,A & N ISLANDS	3/2017	12/2017 (-) [3/2022]	409.85 (-) [409.85]	70.00 (0.00) [0]	2/4
973	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767],NHIDCL,SIKKIM	3/2017	/ (-) [4/2023]	375.80 (-) [375.80]	96.70 (0.00) [-]	2/4
974	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246],NHIDCL,ASSAM	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	52.00 (0.00) [0]	1/4
975	TAMENGLONG - MAHUR PKG-1 - [N24001402],NHIDCL,MANIPUR	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	14.79 (0.00) [0]	0/4
976	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264],NHIDCL,JAMMU AND KASHMIR	7/2020	4/2022 (-) [12/2022]	228.39 (-) [228.39]	14.76 (0.00) [8]	1/4
977	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278],NHIDCL,MIZORAM	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	81.09 (0.00) [0]	1/4
978	IMPROVEMENT/WIDENING TO 2- LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314],NHIDCL,MEGHALAYA	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	327.61 (0.00) [0]	1/4
979	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320],NHIDCL,ASSAM	6/2015	6/2018 (-) [3/2023]	463.49 (-) [801.54]	185.26 (338.05) [57]	2/4
980	IMPHAL - KHONGSANG PKG-2 - [N24001353],NHIDCL,MANIPUR	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	21.30 (0.00) [0]	0/4
981	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858],NHIDCL,MIZORAM	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	271.82 (0.00) [46]	1/4
982	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (12/2022) [12/2022]	184.88 (-) [184.88]	57.76 (0.00) [8]	2/4
983	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685],NHIDCL,ARUNACHAL PRADESH	2/2017	4/2017 (-) [4/2017]	167.28 (-) [167.28]	0.00 (0.00) [0]	2/4

984	DABOKA KATHKATI PACKAGE-5 - [N24001366],NHIDCL,ASSAM	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	8.28 (0.00) [0]	0/4
985	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE- BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245],NHIDCL,ARUNACHAL PRADESH	9/2020	5/2022 (-) [1/2023]	353.90 (-) [353.90]	34.28 (0.00) [8]	1/4
986	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360],NHIDCL,MEGHALAYA	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	87.95 (0.00) [0]	1/4
987	REHABILITATION OF SECTION FROM KM 298.00 TO KM 330.662 PKG-8 - [N24001433],NHIDCL,A & N ISLANDS	4/2021	7/2023 (-) [7/2023]	154.61 (-) [154.61]	0.00 (0.00) [0]	0/4
988	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270],NHIDCL,MANIPUR	3/2020	6/2022 (-) [12/2022]	292.24 (-) [292.24]	98.42 (0.00) [6]	2/4
989	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741],NHIDCL,UTTARAKHAND	3/2018	5/2018 (-) [12/2022]	274.31 (-) [274.31]	143.41 (0.00) [55]	3/4
990	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (4/2022) [12/2022]	228.71 (-) [228.71]	67.40 (0.00) [8]	2/4
991	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743],NHIDCL,UTTARAKHAND	3/2018	5/2018 (-) [12/2022]	417.24 (-) [417.24]	295.36 (0.00) [55]	3/4
992	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865],NHIDCL,MIZORAM	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	182.20 (0.00) [48]	1/4
993	IMPROVEMENT/WIDENING TO 2- LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903],NHIDCL,MEGHALAYA	3/2019	5/2019 (-) [9/2022]	306.28 (-) [306.28]	165.99 (0.00) [40]	2/4
994	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695],NHIDCL,SIKKIM	4/2017	10/2017 (6/2022) [6/2022]	388.00 (447.37) [530.67]	316.99 (142.67) [0]	4/4
995	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250],NHIDCL,ASSAM	8/2020	3/2022 (-) [11/2022]	278.46 (-) [278.46]	120.18 (0.00) [8]	3/4
996	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259],NHIDCL,NAGALAND	9/2020	4/2022 (-) [3/2023]	315.63 (-) [315.63]	12.23 (0.00) [11]	1/4
997	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389],NHIDCL,NAGALAND	3/2020	6/2022 (-) [12/2022]	206.53 (-) [206.53]	95.95 (0.00) [6]	3/4
998	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4- LANING FROM (- [N24001313],NHIDCL,MEGHALAYA	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.79 (0.00) [0]	0/4

999	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274],NHIDCL,MANIPUR	8/2020	4/2022 (-) [2/2023]	379.39 (-) [379.39]	22.07 (0.00) [10]	0/4
1000	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284],NHIDCL,NAGALAND	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	64.96 (0.00) [0]	1/4
1001	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322],NHIDCL,SIKKIM	9/2020	5/2022 (-) [12/2022]	183.31 (-) [183.31]	87.22 (0.00) [7]	0/4
1002	IMPHAL – MOREH (PACKAGE 4) - [N24001399],NHIDCL,MANIPUR	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	46.79 (0.00) [0]	0/4
1003	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763],NHIDCL,NAGALAND	3/2018	9/2018 (-) [12/2022]	215.79 (-) [215.79]	86.37 (0.00) [51]	1/4
1004	KHELLANI-KHANABAL PKG-5 - [N24001396],NHIDCL,JAMMU AND KASHMIR	7/2021	2/2023 (-) [2/2023]	497.09 (-) [497.09]	25.62 (0.00) [0]	0/4
1005	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262],NHIDCL,SIKKIM	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	115.75 (0.00) [0]	1/4
1006	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327],NHIDCL,SIKKIM	8/2020	5/2022 (-) [12/2022]	292.80 (-) [292.80]	52.83 (0.00) [7]	1/4
1007	DABOKA KATHKATI PACKAGE-2 - [N24001364],NHIDCL,ASSAM	3/2021	1/2024 (-) [1/2023]	335.88 (-) [335.88]	70.36 (0.00) [-12]	2/4
1008	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757],NHIDCL,NAGALAND	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	141.12 (0.00) [0]	0/4
1009	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616],NHIDCL,ARUNACHAL PRADESH	4/2016	/ (-) [9/2022]	245.79 (-) [245.79]	224.65 (0.00) [-]	3/4
1010	MERANGKONG-TAMLU-MON (MTM) PKG-5 - [N24001438],NHIDCL,NAGALAND	7/2021	12/2023 (-) [12/2023]	161.73 (-) [161.73]	11.38 (0.00) [0]	0/4
1011	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337],NHIDCL,SIKKIM	10/2020	11/2023 (-) [5/2024]	493.42 (-) [493.42]	12.26 (0.00) [6]	1/4
1012	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765],NHIDCL,NAGALAND	3/2018	9/2018 (-) [9/2018]	323.98 (-) [323.98]	0.00 (0.00) [0]	0/4
1013	KARGIL-ZANSKR PACKAGE-8 - [N24001348],NHIDCL,LADAKH	3/2021	1/2023 (-) [1/2023]	398.37 (-) [398.37]	28.25 (0.00) [0]	1/4

1014	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355],NHIDCL,MIZORAM	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	129.85 (0.00) [0]	0/4
1015	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 - [N24001451],NHIDCL,ASSAM	3/2022	7/2024 (-) [7/2024]	215.27 (-) [215.27]	0.00 (0.00) [0]	0/4
1016	REHABILITATION AND UP- GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267],NHIDCL,TRIPURA	3/2020	7/2022 (3/2023) [3/2023]	178.43 (-) [178.43]	28.82 (0.00) [8]	1/4
1017	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (12/2022) [12/2022]	294.04 (-) [294.04]	109.59 (0.00) [8]	3/4
1018	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323],NHIDCL,ASSAM	10/2014	11/2018 (-) [9/2022]	588.95 (-) [873.91]	559.13 (284.96) [46]	3/4
1019	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762],NHIDCL,NAGALAND	3/2018	9/2018 (-) [6/2022]	215.12 (-) [215.12]	127.87 (0.00) [0]	3/4
1020	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753],NHIDCL,NAGALAND	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	199.63 (0.00) [50]	2/4
1021	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679],NHIDCL,ARUNACHAL PRADESH	2/2017	4/2017 (-) [11/2022]	195.23 (-) [252.79]	180.00 (57.56) [67]	3/4
1022	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392],NHIDCL,ARUNACHAL PRADESH	8/2020	4/2022 (12/2022) [12/2022]	199.03 (-) [199.03]	70.58 (0.00) [8]	2/4
1023	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279],NHIDCL,MIZORAM	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	134.55 (0.00) [0]	1/4
1024	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH- 144A FROM GANESH VIHA - [N24000868],NHIDCL,JAMMU AND KASHMIR	3/2018	7/2019 (-) [12/2022]	253.44 (-) [253.44]	112.59 (0.00) [41]	2/4
1025	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282],NHIDCL,NAGALAND	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	96.39 (0.00) [0]	1/4
1026	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357],NHIDCL,MIZORAM	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	163.89 (0.00) [0]	0/4
1027	KARGIL-ZANSKR PACKAGE-2 - [N24001344],NHIDCL,LADAKH	3/2021	1/2023 (-) [1/2023]	404.89 (-) [404.89]	1.98 (0.00) [0]	0/4
1028	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF	3/2020	7/2022 (3/2023) [7/2022]	154.51 (-) [154.51]	11.92 (0.00) [0]	2/4

	KAILASHAHAR-KURTI BRIDGE - [N24001265],NHIDCL,TRIPURA					
1029	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286],NHIDCL,NAGALAND	3/2020	6/2022 (-) [10/2022]	278.95 (-) [278.95]	128.23 (0.00) [4]	2/4
1030	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759],NHIDCL,NAGALAND	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	134.89 (0.00) [0]	3/4
1031	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749],NHIDCL,A & N ISLANDS	3/2018	10/2018 (-) [6/2022]	234.27 (-) [234.27]	11.03 (0.00) [0]	2/4
1032	2-LANING FROM JOLAIBARI - BELONIA - [N24001317],NHIDCL,TRIPURA	6/2020	1/2022 (-) [12/2022]	201.99 (-) [201.99]	49.65 (0.00) [11]	1/4
1033	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255],NHIDCL,NAGALAND	9/2020	10/2022 (-) [12/2023]	277.44 (-) [277.44]	55.34 (0.00) [14]	2/4
1034	KEIFANG - TUVAI PKG-1 - [N24001440],NHIDCL,MIZORAM	9/2021	5/2023 (-) [5/2023]	492.94 (-) [492.94]	19.53 (0.00) [0]	0/4
1035	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760],NHIDCL,NAGALAND	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	157.06 (0.00) [0]	3/4
1036	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309],NHIDCL,TRIPURA	11/2020	6/2022 (-) [12/2022]	159.13 (-) [159.13]	30.58 (0.00) [6]	1/4
1037	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342],NHIDCL,JAMMU AND KASHMIR	3/2021	12/2022 (-) [12/2022]	260.40 (-) [260.40]	8.26 (0.00) [0]	1/4
1038	TAMENGLONG - MAHUR PKG-2 - [N24001403],NHIDCL,MANIPUR	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	58.46 (0.00) [0]	0/4
1039	LADDA - BASAI - [N24001316],NHIDCL,ARUNACHAL PRADESH	2/2021	4/2023 (-) [2/2024]	445.96 (-) [445.96]	2.94 (0.00) [10]	0/4
1040	IMPROVEMENT/WIDENING TO 2- LANE WITH PAVED SHOULDER / 4- LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335],NHIDCL,MEGHALAYA	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	44.52 (0.00) [0]	0/4
1041	IMPROVEMENT/WIDENING TO 2- LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334],NHIDCL,MEGHALAYA	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	175.18 (0.00) [0]	1/4
1042	CHURACHANPUR TUIVAI PKG-3 - [N24001405],NHIDCL,MANIPUR	7/2021	10/2023 (-) [8/2023]	673.27 (-) [673.27]	106.28 (0.00) [-2]	0/4
1043	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI- RONGARA) [N24001339],NHIDCL,MEGHALAYA	10/2020	4/2022 (-) [4/2023]	157.86 (-) [157.86]	81.82 (0.00) [12]	2/4
1044	MARIAM - PEREN (PKG 1B) - [N24001350],NHIDCL,MANIPUR	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	45.41 (0.00) [0]	1/4

1045	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252],NHIDCL,SIKKIM	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	84.58 (0.00) [0]	1/4
1046	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338],NHIDCL,SIKKIM	10/2020	12/2023 (11/2024) [11/2024]	816.79 (-) [816.79]	15.85 (0.00) [11]	0/4
1047	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251],NHIDCL,SIKKIM	3/2019	4/2022 (-) [5/2023]	402.94 (-) [402.94]	118.12 (0.00) [13]	2/4
1048	MANU-SIMLUNG (PKG 4) - [N24001363],NHIDCL,TRIPURA	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	24.72 (0.00) [0]	1/4
1049	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249],NHIDCL,TRIPURA	6/2020	1/2022 (8/2022) [8/2022]	347.36 (-) [347.36]	154.53 (0.00) [7]	3/4
1050	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336],NHIDCL,SIKKIM	8/2020	4/2023 (9/2023) [9/2023]	230.45 (-) [230.45]	32.58 (0.00) [5]	1/4
1051	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866],NHIDCL,JAMMU AND KASHMIR	3/2018	8/2018 (-) [5/2022]	404.17 (-) [404.17]	296.31 (0.00) [0]	2/4
1052	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690],NHIDCL,ARUNACHAL PRADESH	1/2017	4/2017 (-) [8/2022]	198.22 (-) [252.05]	171.06 (53.83) [64]	3/4
1053	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761],NHIDCL,NAGALAND	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	195.15 (0.00) [0]	2/4
1054	GOHA-KHELLANI PKG-3 - [N24001397],NHIDCL,JAMMU AND KASHMIR	2/2021	3/2023 (-) [3/2023]	431.28 (-) [431.28]	43.78 (0.00) [0]	0/4
1055	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861],NHIDCL,MIZORAM	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	201.83 (0.00) [43]	1/4
1056	DABOKA KATHKATI PACKAGE-6 - [N24001450],NHIDCL,ASSAM	9/2021	7/2024 (-) [7/2024]	625.64 (-) [625.64]	0.00 (0.00) [0]	0/4
1057	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322],NHIDCL,ASSAM	3/2015	11/2018 (-) [8/2022]	168.39 (-) [259.79]	158.07 (91.40) [45]	4/4
1058	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277],NHIDCL,MIZORAM	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	60.68 (0.00) [0]	1/4
1059	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER	4/2017	9/2019 (-)	404.29 (-)	145.96 (0.00)	0/4

	CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864],NHIDCL,MIZORAM		[4/2024]	[404.29]	[55]	
1060	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946],NHIDCL,ARUNACHAL PRADESH	3/2017	/ (-) [3/2024]	1,718.59 (-) [1,718.59]	543.26 (0.00) [-]	2/4
1061	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431],NHIDCL,ASSAM	1/1991	/ (-) [11/2022]	520.01 (-) [520.01]	214.57 (0.00) [-]	3/4
1062	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329],NHIDCL,TRIPURA	3/2020	7/2022 (-) [1/2023]	165.54 (-) [165.54]	37.19 (0.00) [6]	2/4
1063	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755],NHIDCL,NAGALAND	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	137.74 (0.00) [0]	2/4
1064	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855],NHIDCL,UTTARAKHAND	3/2018	7/2018 (-) [3/2024]	1,383.78 (-) [1,383.78]	362.22 (0.00) [68]	2/5
1065	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902],NHIDCL,ASSAM	10/2017	/ (-) [4/2023]	818.00 (-) [818.00]	350.68 (0.00) [-]	2/4
1066	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361],NHIDCL,SIKKIM	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	19.69 (0.00) [0]	1/4
1067	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248],NHIDCL,ASSAM	8/2020	4/2022 (-) [4/2023]	208.84 (-) [208.84]	27.93 (0.00) [12]	1/4
1068	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752],NHIDCL,NAGALAND	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	365.94 (0.00) [0]	3/4
1069	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582],NHIDCL,ASSAM	1/2016	1/2016 (-) [7/2022]	294.17 (-) [385.57]	229.26 (91.40) [0]	3/4
1070	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754],NHIDCL,NAGALAND	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	212.37 (0.00) [0]	2/4
1071	SENAPATI- IMPHAL PKG-5B - [N24001400],NHIDCL,MANIPUR	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]	0/4
1072	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680],NHIDCL,ARUNACHAL PRADESH	2/2017	4/2017 (-) [10/2022]	203.36 (-) [263.31]	172.68 (59.95) [66]	3/4
1073	CONSTRUCTION OF TWO LANE	3/2020	7/2022	281.78	163.52	2/4

	WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283],NHIDCL,MIZORAM		(-) [7/2022]	(-) [281.78]	(0.00) [0]	
1074	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367],NHIDCL,ASSAM	3/2021	12/2022 (-) [1/2023]	636.42 (-) [418.49]	96.45 (-217.93) [1]	1/4
1075	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949],NHIDCL,ARUNACHAL PRADESH	12/2016	/ (-) [12/2022]	188.78 (-) [188.78]	142.23 (0.00) [-]	3/4
1076	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686],NHIDCL,NAGALAND	3/2016	8/2016 (-) [0/0]	373.07 (-) [387.00]	364.31 (13.93) [0]	3/4
1077	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332],NHIDCL,ASSAM	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	46.43 (0.00) [0]	1/4
1078	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331],NHIDCL,ASSAM	3/2020	6/2022 (-) [3/2023]	261.13 (-) [261.13]	45.67 (0.00) [9]	1/4
1079	IMPHAL - KHONGSANG PKG-4 - [N24001453],NHIDCL,MANIPUR	8/2021	12/2023 (-) [12/2023]	579.63 (-) [579.63]	0.00 (0.00) [0]	0/4
1080	TAMENGLONG - MAHUR PKG-3 - [N24001354],NHIDCL,MANIPUR	3/2021	12/2022 (-) [4/2023]	234.08 (-) [234.08]	32.64 (0.00) [4]	1/4
1081	PEREN-DIMAPUR PKG-5 - [N24001407],NHIDCL,NAGALAND	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	0.00 (0.00) [0]	0/0
1082	DABOKA KATHKATI PACKAGE-4 - [N24001365],NHIDCL,ASSAM	2/2021	12/2023 (-) [12/2022]	260.07 (-) [260.07]	109.24 (0.00) [-12]	3/4
1083	TLABUNG - LUNGLEI PKG-A - [N24001358],NHIDCL,MIZORAM	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	36.21 (0.00) [0]	0/4
1084	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333],NHIDCL,ASSAM	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	256.92 (0.00) [0]	2/4
1085	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247],NHIDCL,TRIPURA	3/2020	1/2022 (-) [10/2022]	247.76 (-) [247.76]	67.01 (0.00) [9]	2/4
1086	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863],NHIDCL,MIZORAM	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	234.73 (0.00) [45]	1/4
1087	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948],NHIDCL,ARUNACHAL PRADESH	9/2016	/ (-) [3/2023]	568.92 (-) [568.92]	390.60 (0.00) [-]	0/4
1088	KHELLANI-KHANABAL PKG-4 - [N24001395],NHIDCL,JAMMU AND KASHMIR	7/2021	8/2023 (-) [8/2023]	859.67 (-) [859.67]	25.50 (0.00) [0]	0/4
1089	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA- KHUPA-HAYULIANG SECTION OF NH-	8/2020	4/2022 (-) [1/2023]	301.06 (-) [301.06]	45.78 (0.00) [9]	1/4

	113 FROM CH.68. - [N24001244],NHIDCL,ARUNACHAL PRADESH					
1090	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683],NHIDCL,ARUNACHAL PRADESH	2/2017	4/2017 (11/2023) [11/2023]	180.57 (244.10) [180.57]	18.01 (0.00) [79]	1/4
1091	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253],NHIDCL,JAMMU AND KASHMIR	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	550.00 (0.00) [0]	2/4
1092	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742],NHIDCL,UTTARAKHAND	3/2018	6/2018 (-) [12/2022]	403.36 (-) [403.36]	230.60 (0.00) [54]	3/4
1093	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271],NHIDCL,MANIPUR	6/2020	8/2022 (-) [12/2022]	365.53 (-) [365.53]	118.82 (0.00) [4]	2/4
1094	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368],NHIDCL,ASSAM	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]	0/4
1095	KARGIL-ZANSKR PACKAGE-1 - [N24001343],NHIDCL,LADAKH	3/2021	1/2023 (-) [1/2023]	384.23 (-) [384.23]	21.95 (0.00) [0]	1/4
1096	JOGIGHOPA BRIDGE - [N24001434],NHIDCL,ASSAM	8/2021	11/2024 (-) [11/2024]	746.76 (-) [746.76]	9.76 (0.00) [0]	0/4
1097	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768],NHIDCL,SIKKIM	11/2017	11/2017 (-) [9/2022]	290.05 (-) [290.05]	175.49 (0.00) [58]	3/4
1098	MARIAM - PEREN PKG-2B - [N24001351],NHIDCL,MANIPUR	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	27.58 (0.00) [0]	1/4
1099	IMPHAL - KHONGSANG PKG-3 - [N24001401],NHIDCL,MANIPUR	7/2021	3/2023 (-) [9/2023]	467.00 (-) [467.00]	50.90 (0.00) [6]	0/4
1100	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269],NHIDCL,ASSAM	3/2020	3/2022 (-) [12/2022]	216.49 (-) [216.49]	65.59 (0.00) [9]	2/4
1101	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688],NHIDCL,NAGALAND	3/2016	8/2016 (-) [8/2016]	429.52 (-) [429.52]	0.00 (0.00) [0]	3/4
1102	TAMENGLONG - MAHUR PKG-5 - [N24001436],NHIDCL,MANIPUR	8/2021	5/2023 (-) [5/2023]	477.86 (-) [477.86]	14.26 (0.00) [0]	0/4
1103	KHELLANI-KHANABAL PKG-1 - [N24001323],NHIDCL,JAMMU AND KASHMIR	3/2021	9/2022 (-) [9/2022]	486.45 (-) [486.45]	15.88 (0.00) [0]	2/4
1104	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285],NHIDCL,NAGALAND	3/2020	12/2021 (-) [0/0]	330.78 (-) [330.78]	98.59 (0.00) [0]	1/4
1105	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-)	4,997.04 (-)	364.26 (0.00)	1/4

	- [N24001326],NHIDCL,ASSAM		[9/2028]	[4,997.04]	[0]	
1106	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268],NHIDCL,MANIPUR	3/2019	7/2022 (-) [3/2023]	471.00 (-) [471.00]	251.05 (0.00) [8]	3/4
1107	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276],NHIDCL,MANIPUR	8/2020	4/2022 (-) [0/0]	228.97 (-) [228.97]	0.00 (0.00) [0]	0/4
1108	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308],NHIDCL,TRIPURA	11/2020	7/2022 (11/2022) [12/2022]	332.14 (-) [332.14]	56.56 (0.00) [5]	2/4
1109	KARGIL-ZANSKR PACKAGE-7 - [N24001347],NHIDCL,LADAKH	1/2021	6/2024 (-) [6/2024]	308.86 (-) [308.86]	80.00 (0.00) [0]	2/4
1110	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583],NHIDCL,ASSAM	1/2016	1/2016 (-) [12/2022]	252.00 (-) [330.30]	141.13 (78.30) [83]	2/4
1111	KHELLANI-KHANABAL PKG-3 - [N24001341],NHIDCL,JAMMU AND KASHMIR	3/2021	12/2022 (-) [12/2022]	398.51 (-) [398.51]	24.74 (0.00) [0]	1/4
1112	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678],NHIDCL,ARUNACHAL PRADESH	3/2017	4/2017 (-) [12/2022]	284.09 (-) [284.09]	188.40 (0.00) [68]	3/4
1113	IMPHAL – MOREH PACKAGE- 3 - [N24001352],NHIDCL,MANIPUR	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	112.33 (0.00) [0]	2/4
1114	KARGIL-ZANSKR PACKAGE-6 - [N24001346],NHIDCL,LADAKH	1/2021	5/2024 (-) [5/2024]	239.81 (-) [239.81]	81.30 (0.00) [0]	2/4
1115	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362],NHIDCL,SIKKIM	12/2020	2/2024 (2/2024) [2/2024]	410.60 (-) [410.60]	21.94 (0.00) [0]	0/4
1116	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256],NHIDCL,JAMMU AND KASHMIR	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	678.90 (0.00) [0]	1/7
1117	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312],NHIDCL,MANIPUR	3/2020	6/2022 (-) [12/2022]	167.95 (-) [167.95]	77.77 (0.00) [6]	3/4
1118	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319],NHIDCL,ASSAM	6/2015	6/2018 (-) [6/2018]	437.39 (-) [437.39]	0.00 (0.00) [0]	1/4
1119	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305],NHIDCL,ASSAM	5/2015	5/2018 (-) [7/2022]	454.89 (-) [814.56]	391.87 (359.67) [0]	3/4
1120	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771],NHIDCL,MEGHALAYA	4/2017	/ (-) [11/2022]	553.51 (-) [553.51]	232.58 (0.00) [-]	2/4

1121	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328],NHIDCL,ASSAM	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	188.31 (0.00) [0]	2/4
1122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758],NHIDCL,NAGALAND	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	136.85 (0.00) [0]	0/4
1123	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 - [N24001452],NHIDCL,ASSAM	4/2022	7/2024 (-) [7/2024]	170.95 (-) [170.95]	0.00 (0.00) [0]	0/4
1124	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG-4A) - [N24001272],NHIDCL,MANIPUR	3/2020	6/2022 (-) [12/2022]	167.95 (-) [167.95]	77.72 (0.00) [6]	2/4
1125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756],NHIDCL,NAGALAND	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	119.22 (0.00) [48]	2/4
1126	KHELLANI-KHANABAL PKG-2 - [N24001394],NHIDCL,JAMMU AND KASHMIR	7/2021	2/2023 (-) [2/2023]	512.43 (-) [512.43]	9.78 (0.00) [0]	0/4
1127	TAMENGLONG - MAHUR PKG-6 - [N24001437],NHIDCL,MANIPUR	9/2021	5/2023 (-) [5/2023]	311.18 (-) [311.18]	22.84 (0.00) [0]	0/4
1128	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280],NHIDCL,NAGALAND	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	94.03 (0.00) [0]	1/4
1129	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857],NHIDCL,MIZORAM	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	220.92 (0.00) [43]	1/4
1130	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944],NHIDCL,ARUNACHAL PRADESH	12/2016	/ (-) [12/2022]	200.44 (-) [200.44]	135.92 (0.00) [-]	3/4
1131	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823],NHIDCL,ASSAM	3/2015	1/2016 (-) [6/2023]	829.00 (-) [1,307.50]	411.51 (478.50) [89]	2/3
1132	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744],NHIDCL,A & N ISLANDS	3/2015	10/2018 (-) [3/2023]	262.97 (-) [262.97]	30.00 (0.00) [53]	1/4
1133	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254],NHIDCL,SIKKIM	3/2020	6/2022 (-) [12/2022]	242.97 (-) [242.97]	68.35 (0.00) [6]	2/4
1134	TWO-LANING OF HAYULIANG-HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979],NHIDCL,ARUNACHAL PRADESH	1/2017	/ (-) [3/2024]	256.66 (-) [256.66]	0.00 (0.00) [-]	1/4
1135	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258],NHIDCL,NAGALAND	8/2020	4/2022 (-) [6/2023]	202.36 (-) [202.36]	15.41 (0.00) [14]	1/4

1136	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769],NHIDCL,SIKKIM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	62.92 (0.00) [0]	1/4
1137	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862],NHIDCL,MIZORAM	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	237.48 (0.00) [43]	1/4
1138	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281],NHIDCL,MIZORAM	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	98.32 (0.00) [0]	0/4
1139	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263],NHIDCL,TRIPURA	6/2020	1/2022 (-) [0/0]	277.50 (-) [277.50]	140.76 (0.00) [0]	1/4
1140	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287],NHIDCL,NAGALAND	4/2020	12/2021 (-) [0/0]	330.80 (-) [330.80]	63.26 (0.00) [0]	1/4
1141	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859],NHIDCL,MIZORAM	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	234.97 (0.00) [45]	1/4
1142	MARIAM - PEREN PKG-1A - [N24001349],NHIDCL,MANIPUR	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	13.88 (0.00) [0]	0/4
1143	TADADEGE - HENKAR - [N24001315],NHIDCL,ARUNACHAL PRADESH	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	24.48 (0.00) [0]	0/4
1144	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG-4B) - [N24001273],NHIDCL,MANIPUR	7/2020	8/2022 (-) [11/2022]	177.76 (-) [177.76]	70.23 (0.00) [3]	2/4
1145	KARGIL-ZANSKR PACKAGE-5 - [N24001330],NHIDCL,LADAKH	8/2020	12/2023 (-) [12/2023]	169.79 (-) [169.79]	103.72 (0.00) [0]	3/4
1146	TLABUNG - LUNGLEI PKG-B - [N24001359],NHIDCL,MIZORAM	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	33.38 (0.00) [0]	0/4
1147	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764],NHIDCL,NAGALAND	3/2018	9/2018 (-) [6/2023]	272.89 (-) [272.89]	103.64 (0.00) [57]	0/4
1148	DOGINALA - GAU - [N24001320],NHIDCL,ARUNACHAL PRADESH	12/2020	9/2022 (-) [4/2023]	242.30 (-) [242.30]	15.04 (0.00) [7]	0/4
1149	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325],NHIDCL,SIKKIM	9/2020	5/2023 (-) [1/2024]	262.84 (-) [262.84]	129.59 (0.00) [8]	1/4
1150	KHELLANI-KHANABAL PKG-6 - [N24001324],NHIDCL,JAMMU AND KASHMIR	2/2021	9/2022 (-) [9/2022]	285.28 (-) [285.28]	70.27 (0.00) [0]	2/4
1151	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311],NHIDCL,TRIPURA	11/2020	7/2022 (2/2023) [7/2022]	206.78 (-) [206.78]	43.98 (0.00) [0]	3/4
1152	UP-GRADATION TO 2-LANE WITH	7/2020	4/2022	210.79	20.59	2/4

	PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266],NHIDCL,JAMMU AND KASHMIR		(-) [12/2022]	(-) [210.79]	(0.00) [8]	
1153	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746],NHIDCL,A & N ISLANDS	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	159.49 (0.00) [0]	3/4
1154	MARIAM - PEREN (PKG 2A) - [N24001398],NHIDCL,MANIPUR	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	68.82 (0.00) [0]	0/4
1155	PEREN-DIMAPUR SECTION PKG-2 - [N24001406],NHIDCL,NAGALAND	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	52.94 (0.00) [0]	0/4
1156	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAPOKPI SECTIO - [N24001275],NHIDCL,MANIPUR	8/2020	4/2022 (-) [0/0]	268.98 (-) [268.98]	22.08 (0.00) [0]	0/4
1157	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318],NHIDCL,TRIPURA	9/2020	4/2022 (-) [10/2022]	173.17 (-) [173.17]	21.34 (0.00) [6]	1/4
1158	TAMENGLONG - MAHUR PKG-4 - [N24001404],NHIDCL,MANIPUR	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	16.45 (0.00) [0]	0/4
1159	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748],NHIDCL,A & N ISLANDS	2/2018	10/2018 (-) [12/2022]	391.00 (-) [391.00]	22.17 (0.00) [50]	1/4
1160	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687],NHIDCL,NAGALAND	3/2016	8/2016 (-) [0/0]	396.52 (-) [396.52]	321.87 (0.00) [0]	3/4
1161	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310],NHIDCL,TRIPURA	11/2020	7/2022 (-) [12/2022]	280.91 (-) [280.91]	148.65 (0.00) [5]	3/4
1162	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261],NHIDCL,SIKKIM	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	50.95 (0.00) [0]	1/4
1163	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260],NHIDCL,NAGALAND	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	84.56 (0.00) [0]	2/4
1164	KARGIL-ZANSKR PACKAGE-3 - [N24001345],NHIDCL,LADAKH	8/2020	1/2023 (-) [1/2023]	381.01 (-) [381.01]	16.77 (0.00) [0]	1/4
1165	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122],NHAI,HARYANA	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [0]	0/0
1166	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN - [N24001425],NHAI,KARNATAKA	3/2021	11/2021 (-) [11/2023]	1,100.88 (1,100.88) [1,100.88]	261.90 (0.00) [24]	0/4
1167	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF	5/2020	7/2023 (-) [7/2023]	691.52 (-) [691.52]	113.57 (0.00) [0]	1/4

	DSIR ZONE OF AHMEDAB - [N24001445],NHAI,GUJARAT					
1168	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431],NHAI,TAMIL NADU	3/2018	10/2020 (-) [12/2023]	1,872.68 (-) [1,872.68]	0.00 (0.00) [38]	0/0
1169	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720],NHAI,ANDHRA PRADESH	12/2017	/ (-) [5/2022]	357.00 (-) [357.00]	0.00 (0.00) [0]	0/0
1170	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722],NHAI,UTTAR PRADESH	12/2017	/ (-) [5/2019]	305.00 (-) [305.00]	0.00 (0.00) [0]	0/0
1171	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638],NHAI,UTTARAKHAND	11/2012	7/2018 (2/2022) [5/2022]	605.84 (1,023.23) [1,023.23]	981.05 (417.39) [0]	3/4
1172	FOUR LANING OF BARHI- HAZARIBAGH NH-33 - [N24000607],NHAI,JHARKHAND	8/2016	8/2018 (-) [5/2022]	323.72 (-) [355.24]	327.54 (31.52) [0]	0/0
1173	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214],NHAI,MADHYA PRADESH	12/2017	/ (-) [10/2022]	217.96 (-) [884.00]	797.00 (666.04) [-]	3/4
1174	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182],NHAI,MULTI STATE	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	3,379.45 (531.45) [105]	0/0
1175	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490],NHAI,KARNATAKA	3/2015	8/2018 (-) [6/2022]	1,388.00 (-) [1,388.00]	1,255.00 (0.00) [0]	0/0
1176	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306],NHAI,UTTAR PRADESH	10/2020	3/2023 (-) [1/2024]	724.60 (-) [724.60]	680.12 (0.00) [10]	0/1
1177	ISMAILABAD-NARNAUL PKG-4 - [N24001192],NHAI,HARYANA	1/2019	/ (5/2022) [5/2022]	1,018.79 (1,072.08) [1,072.08]	1,023.71 (53.29) [0]	3/4
1178	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557],NHAI,TAMIL NADU	2/2016	7/2018 (-) [3/2022]	641.17 (-) [641.17]	430.39 (0.00) [0]	0/0
1179	SIX LANNING OF NELLORE- CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183],NHAI,ANDHRA PRADESH	11/2011	5/2014 (-) [5/2022]	1,535.00 (-) [1,535.00]	3,287.35 (0.00) [0]	0/0
1180	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138],NHAI,KARNATAKA	9/2010	6/2018 (12/2022) [12/2022]	946.00 (1,046.56) [1,046.56]	822.13 (100.56) [54]	3/4
1181	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521],NHAI,BIHAR	8/2015	/ (3/2022) [5/2022]	854.80 (-) [1,038.56]	1,065.19 (183.76) [0]	3/4
1182	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594],NHAI,JHARKHAND	7/2016	/ (-) [6/2022]	458.03 (-) [486.00]	487.99 (27.97) [0]	0/0
1183	SIX LANING OF NH-140 FROM	3/2018	/	1,550.98	1,673.32	0/0

	CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809],NHAI,ANDHRA PRADESH		(-) [9/2022]	(-) [1,550.98]	(0.00) [-]	
1184	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825],NHAI,TELANGANA	3/2018	/ (3/2021) [2/2023]	828.29 (1,140.50) [828.29]	287.90 (0.00) [-]	0/0
1185	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350],NHAI,TAMIL NADU	6/2015	12/2017 (-) [5/2023]	563.92 (-) [563.92]	63.30 (0.00) [65]	0/0
1186	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801],NHAI,GUJARAT	2/2018	/ (6/2021) [9/2022]	1,052.21 (-) [1,361.00]	503.77 (308.79) [-]	2/4
1187	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566],NHAI,KERALA	4/2016	6/2018 (12/2021) [7/2022]	804.97 (-) [804.97]	615.73 (0.00) [0]	0/0
1188	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552],NHAI,KARNATAKA	3/2016	3/2019 (3/2023) [3/2023]	701.40 (-) [701.40]	156.33 (0.00) [48]	2/4
1189	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728],NHAI,MADHYA PRADESH	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	538.44 (0.00) [0]	0/0
1190	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784],NHAI,KERALA	2/2018	/ (-) [1/2024]	1,424.77 (1,862.77) [1,862.77]	192.01 (438.00) [-]	0/0
1191	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724],NHAI,BIHAR	1/2018	/ (-) [4/2024]	895.39 (-) [895.39]	1,369.90 (0.00) [-]	0/0
1192	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161],NHAI,JAMMU AND KASHMIR	7/2010	7/2015 (-) [5/2022]	1,987.00 (-) [1,987.00]	3,116.66 (0.00) [0]	9/10
1193	MEERUT-BULANDSHAHR - [N24000539],NHAI,UTTAR PRADESH	1/2016	/ (-) [3/2022]	683.24 (-) [987.94]	0.00 (304.70) [0]	0/2
1194	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635],NHAI,GUJARAT	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	199.86 (0.00) [0]	0/3
1195	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694],NHAI,TAMIL NADU	3/2016	7/2016 (-) [3/2022]	641.17 (-) [641.17]	430.39 (0.00) [0]	0/0
1196	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437],NHAI,WEST BENGAL	10/2015	/ (-) [2/2021]	361.15 (416.00) [363.93]	276.71 (2.78) [0]	0/0
1197	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733],NHAI,ODISHA	1/2018	/ (-) [3/2023]	633.68 (-) [633.68]	320.00 (0.00) [-]	0/1
1198	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO	10/2015	5/2018 (-) [12/2022]	531.13 (480.35) [777.03]	766.05 (245.90) [55]	0/0

	KM 7.422 (- [N24000435],NHAI,MAHARASHTRA					
1199	SIX LANING OF CHANDIKHOL- JAGATPUR-BHUBANESWAR - [N24000205],NHAI,ODISHA	12/2011	6/2014 (-) [2/2023]	1,047.00 (-) [1,047.00]	1,855.00 (0.00) [104]	0/0
1200	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507],NHAI,BIHAR	12/2015	/ (-) [3/2023]	1,167.45 (-) [1,182.94]	399.40 (15.49) [-]	0/0
1201	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445],NHAI,RAJASTHAN	8/2014	4/2018 (-) [9/2022]	822.90 (-) [822.90]	844.08 (0.00) [53]	0/0
1202	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544],NHAI,UTTAR PRADESH	3/2016	4/2019 (-) [3/2019]	676.73 (-) [676.73]	986.47 (0.00) [0]	0/0
1203	6-LANING OF DHANKUNI- KHARAGPUR SECTION - [N24000206],NHAI,WEST BENGAL	4/2012	9/2014 (-) [8/2021]	1,396.18 (-) [1,396.18]	1,396.18 (0.00) [0]	0/0
1204	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300],NHAI,ANDHRA PRADESH	11/2019	2/2021 (4/2021) [2/2023]	1,226.88 (1,240.13) [1,321.60]	678.20 (94.72) [24]	0/0
1205	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451],NHAI,MAHARASHTRA	8/2015	5/2018 (-) [3/2022]	505.00 (-) [504.00]	550.48 (-1.00) [0]	0/1
1206	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234],NHAI,MADHYA PRADESH	2/2019	3/2020 (-) [8/2022]	996.27 (-) [996.27]	965.00 (0.00) [29]	2/3
1207	AHMEDABAD TO VADODARA SECTION - [N24000222],NHAI,GUJARAT	1/2013	12/2015 (11/2018) [11/2018]	2,125.24 (-) [2,125.24]	437.87 (0.00) [0]	3/3
1208	PUNE-SATARA(NH-4) - [N24000156],NHAI,MAHARASHTRA	10/2010	3/2013 (-) [9/2022]	1,724.55 (-) [1,724.55]	2,919.69 (0.00) [114]	0/0
1209	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619],NHAI,ODISHA	9/2016	8/2019 (-) [6/2023]	2,510.04 (-) [2,510.04]	658.95 (0.00) [46]	0/0
1210	4 LANING OF BAHARAGORA - SINGHARA - [N24000427],NHAI,ODISHA	7/2015	/ (-) [8/2022]	1,282.94 (-) [1,282.94]	705.46 (0.00) [-]	0/0
1211	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570],NHAI,GUJARAT	5/2016	/ (-) [12/2022]	763.08 (-) [763.08]	408.37 (0.00) [-]	2/2
1212	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709],NHAI,MADHYA PRADESH	12/2017	/ (-) [3/2023]	950.27 (-) [950.27]	454.01 (0.00) [-]	4/4
1213	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION - [N24001444],NHAI,GUJARAT	5/2020	1/2024 (-) [1/2024]	882.00 (-) [882.00]	0.02 (0.00) [0]	0/4

1214	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTION - [N24000711],NHAI,RAJASTHAN	12/2017	/ (-) [12/2023]	1,308.73 (-) [1,308.73]	221.14 (0.00) [-]	0/0
1215	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697],NHAI,TAMIL NADU	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	742.16 (0.00) [0]	0/0
1216	DEVELOPMENT OF MULTIMODAL LOGISTICS PARK AT BANGALORE AND EXTERNAL CONNECTIVITY TO THE MULTI MODEL L - [N24001449],NHAI,KARNATAKA	6/2022	3/2025 (-) [3/2025]	1,769.70 (-) [1,769.70]	4.20 (0.00) [0]	0/0
1217	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449],NHAI,HARYANA	7/2015	4/2019 (-) [9/2022]	2,128.72 (2,408.72) [2,408.72]	1,865.00 (280.00) [41]	0/0
1218	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654],NHAI,UTTAR PRADESH	3/2017	3/2020 (-) [9/2022]	1,184.71 (-) [1,310.00]	1,309.30 (125.29) [30]	3/4
1219	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185],NHAI,BIHAR	9/2011	3/2014 (-) [12/2022]	574.00 (-) [574.00]	768.92 (0.00) [105]	0/0
1220	JUNAGADH BYPASS - [N24000701],NHAI,GUJARAT	10/2017	10/2017 (-) [7/2022]	232.49 (373.10) [232.49]	228.82 (0.00) [0]	0/0
1221	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783],NHAI,KARNATAKA	2/2018	/ (-) [12/2023]	486.78 (-) [486.78]	171.98 (0.00) [-]	3/3
1222	ISMAILABAD-NARNAUL PKG-2 - [N24001190],NHAI,HARYANA	1/2019	/ (4/2022) [4/2022]	1,243.45 (1,407.35) [1,407.35]	1,355.53 (163.90) [0]	0/4
1223	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601],NHAI,PUNJAB	8/2016	/ (-) [5/2021]	1,169.61 (-) [2,280.00]	1,330.39 (1,110.39) [0]	0/0
1224	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569],NHAI,GUJARAT	5/2016	/ (-) [8/2022]	723.64 (-) [723.64]	528.22 (0.00) [-]	2/2
1225	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841],NHAI,HARYANA	3/2018	/ (-) [4/2022]	795.50 (-) [922.64]	820.70 (127.14) [0]	0/0
1226	FOUR LANING OF PARWANOO - SOLAN - [N24000479],NHAI,HIMACHAL PRADESH	9/2015	3/2018 (3/2021) [12/2022]	934.46 (-) [1,543.51]	1,472.50 (609.05) [57]	0/0
1227	INDORE-DEWAS(NH-3) - [N24000159],NHAI,MADHYA PRADESH	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]	3/3
1228	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463],NHAI,WEST BENGAL	12/2015	6/2018 (-) [1/2023]	1,083.00 (1,414.01) [1,414.01]	1,000.57 (331.01) [55]	0/0
1229	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704],NHAI,KERALA	9/2017	9/2017 (5/2021) [3/2023]	1,124.11 (-) [1,309.79]	1,162.72 (185.68) [66]	0/0
1230	SRINAGAR TO BANIHAL - [N24000189],NHAI,JAMMU AND	6/2011	6/2014 (-)	1,100.70 (-)	2,935.64 (0.00)	3/4

	KASHMIR		[9/2022]	[1,100.70]	[99]	
1231	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448],NHAI,HARYANA	1/2016	7/2018 (-) [7/2019]	574.28 (-) [537.16]	485.00 (-37.12) [0]	0/0
1232	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493],NHAI,UTTAR PRADESH	1/2016	6/2018 (12/2022) [6/2022]	1,027.53 (2,950.04) [2,628.31]	2,588.02 (1,600.78) [0]	0/1
1233	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675],NHAI,KARNATAKA	3/2017	3/2020 (-) [6/2022]	993.16 (-) [1,434.00]	1,319.54 (440.84) [0]	0/0
1234	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739],NHAI,ODISHA	1/2018	/ (-) [6/2023]	503.88 (-) [503.88]	159.77 (0.00) [-]	0/0
1235	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301],NHAI,ANDHRA PRADESH	11/2019	2/2021 (-) [7/2024]	1,601.10 (-) [1,601.10]	612.83 (0.00) [41]	0/0
1236	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737],NHAI,ODISHA	1/2018	/ (-) [7/2022]	1,522.00 (-) [1,522.00]	636.05 (0.00) [0]	0/0
1237	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551],NHAI,UTTAR PRADESH	3/2016	4/2019 (12/2021) [9/2022]	1,587.49 (3,150.00) [3,063.99]	2,904.36 (1,476.50) [41]	0/0
1238	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378],NHAI,MAHARASHTRA	2/2019	11/2019 (-) [12/2022]	362.46 (362.46) [361.70]	304.45 (-0.76) [37]	0/0
1239	FOUR LANING OF VARANASI BYPASS - [N24000356],NHAI,UTTAR PRADESH	5/2015	5/2017 (-) [5/2019]	261.09 (839.00) [261.09]	240.96 (0.00) [0]	0/0
1240	KANDLA - MUNDRA PORT - [N24000175],NHAI,GUJARAT	1/2011	7/2013 (-) [7/2013]	953.88 (-) [953.88]	91.63 (0.00) [0]	0/0
1241	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826],NHAI,TAMIL NADU	3/2018	/ (-) [12/2022]	505.35 (-) [505.35]	255.05 (0.00) [-]	0/0
1242	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810],NHAI,ANDHRA PRADESH	3/2018	/ (-) [5/2022]	565.09 (-) [565.09]	713.85 (0.00) [0]	0/0
1243	ISMAILABAD-NARNAUL PKG-1 - [N24001193],NHAI,HARYANA	1/2019	/ (5/2022) [5/2022]	996.65 (1,173.65) [1,173.65]	1,115.31 (177.00) [0]	3/4
1244	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790],NHAI,WEST BENGAL	3/2018	/ (-) [6/2024]	1,261.98 (2,145.96) [2,145.96]	199.05 (883.98) [-]	0/0
1245	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786],NHAI,UTTAR PRADESH	2/2018	/ (-) [8/2022]	670.50 (1,248.00) [670.50]	1,147.08 (0.00) [-]	0/0

1246	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454],NHAI,MAHARASHTRA	6/2014	11/2016 (-) [12/2022]	923.04 (-) [923.04]	869.13 (0.00) [73]	0/0
1247	4-LANING OF BRAHAMPORE-FARAKA - [N24000203],NHAI,WEST BENGAL	2/2011	8/2013 (-) [6/2023]	998.79 (-) [998.79]	2,004.66 (0.00) [118]	3/4
1248	ISMAILABAD-NARNAUL PKG-5 - [N24001186],NHAI,HARYANA	1/2019	/ (5/2022) [5/2022]	1,051.91 (1,118.07) [1,118.07]	1,031.96 (66.16) [0]	3/4
1249	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662],NHAI,PUNJAB	3/2017	3/2020 (3/2023) [3/2023]	754.54 (756.27) [665.19]	528.73 (-89.35) [36]	3/4
1250	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232],NHAI,MADHYA PRADESH	2/2019	3/2020 (-) [8/2022]	847.00 (-) [847.00]	908.00 (0.00) [29]	2/3
1251	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR- PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814],NHAI,CHHATISGARH	3/2018	/ (7/2022) [7/2022]	1,029.96 (1,632.70) [16,732.70]	468.76 (15,702.74) [0]	0/0
1252	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710],NHAI,TAMIL NADU	12/2017	/ (-) [12/2022]	379.90 (-) [379.90]	261.83 (0.00) [-]	0/0
1253	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808],NHAI,ARUNACHAL PRADESH	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]	0/0
1254	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH- 209(EXISTING CHAINAGE FROM - [N24000622],NHAI,KARNATAKA	9/2016	8/2019 (-) [6/2022]	950.69 (-) [1,108.00]	1,529.21 (157.31) [0]	0/0
1255	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH- 29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806],NHAI,UTTAR PRADESH	2/2018	/ (-) [3/2023]	972.77 (1,603.94) [1,441.00]	494.71 (468.23) [-]	0/0
1256	FOUR LANNING OF NERCHOWK- PANDOH BYPASS SECTION OF NH- 21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613],NHAI,HIMACHAL PRADESH	9/2016	/ (-) [3/2023]	1,273.71 (-) [1,273.71]	1,092.03 (0.00) [-]	0/0
1257	FOUR LANING OF BHAVNAGAR- TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567],NHAI,GUJARAT	5/2016	/ (-) [8/2024]	998.18 (-) [998.18]	781.17 (0.00) [-]	2/2
1258	FOUR LANNING OF VIKRAVANDI- SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652],NHAI,TAMIL NADU	3/2017	3/2020 (-) [12/2022]	848.45 (-) [848.45]	252.08 (0.00) [33]	0/0
1259	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED	2/2018	/ (10/2021)	741.86 (649.00)	185.59 (-92.86)	0/0

	SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795],NHAI,RAJASTHAN		[12/2022]	[649.00]	[-]	
1260	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811],NHAI,ANDHRA PRADESH	3/2018	/ (-) [6/2022]	314.43 (-) [314.43]	85.61 (0.00) [0]	0/0
1261	PANIKHOLI-RIMOLI - [N24000197],NHAI,ODISHA	3/2012	9/2014 (-) [6/2022]	1,410.00 (-) [1,410.00]	0.00 (0.00) [0]	0/0
1262	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671],NHAI,ODISHA	3/2017	3/2020 (-) [3/2022]	1,288.07 (-) [1,420.00]	1,105.15 (131.93) [0]	0/0
1263	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606],NHAI,HIMACHAL PRADESH	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	0.00 (0.00) [0]	0/0
1264	INDORE-JHABUA-GUJRAT/MP - [N24000136],NHAI,MADHYA PRADESH	10/2010	4/2013 (-) [12/2022]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [116]	4/4
1265	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571],NHAI,GUJARAT	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]	0/0
1266	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731],NHAI,ODISHA	1/2018	/ (-) [7/2022]	953.09 (-) [953.09]	664.48 (0.00) [0]	0/0
1267	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550],NHAI,ODISHA	2/2016	/ (-) [10/2022]	1,069.65 (-) [1,069.65]	856.21 (0.00) [-]	0/0
1268	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851],NHAI,MAHARASHTRA	3/2018	/ (-) [10/2023]	1,162.92 (1,182.87) [1,182.87]	84.54 (19.95) [-]	0/0
1269	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789],NHAI,KARNATAKA	2/2018	/ (-) [9/2022]	2,177.80 (-) [2,450.00]	2,691.86 (272.20) [-]	0/0
1270	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515],NHAI,WEST BENGAL	4/2014	/ (-) [12/2023]	1,665.00 (-) [2,360.65]	4,521.55 (695.65) [-]	0/0
1271	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696],NHAI,BIHAR	8/2017	8/2017 (8/2023) [8/2023]	950.64 (1,161.00) [1,168.33]	503.74 (217.69) [72]	0/0
1272	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488],NHAI,JAMMU AND KASHMIR	12/2015	12/2018 (12/2022) [12/2022]	2,136.97 (2,288.97) [2,136.97]	1,921.25 (0.00) [48]	3/4
1273	FOUR LANING OF MADURAI-CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827],NHAI,TAMIL NADU	3/2018	/ (-) [9/2022]	628.71 (-) [628.71]	448.26 (0.00) [-]	0/0

1274	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485],NHAI,ODISHA	12/2015	/ (-) [11/2022]	752.28 (-) [752.28]	379.01 (0.00) [-]	0/1
1275	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT- SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665],NHAI,BIHAR	3/2017	3/2020 (12/2018) [3/2023]	672.89 (736.01) [830.31]	31.82 (157.42) [36]	0/0
1276	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419],NHAI,PUNJAB	2/2021	4/2024 (-) [4/2024]	1,269.96 (-) [1,269.96]	0.00 (0.00) [0]	0/0
1277	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510],NHAI,CHHATISGARH	12/2015	4/2018 (-) [12/2021]	726.67 (1,103.55) [1,096.52]	538.73 (369.85) [0]	0/0
1278	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224],NHAI,MULTI STATE	10/2012	4/2015 (5/2022) [5/2022]	1,928.22 (-) [1,928.22]	1,890.04 (0.00) [0]	4/4
1279	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822],NHAI,TELANGANA	3/2018	/ (-) [10/2021]	950.63 (-) [950.63]	764.27 (0.00) [0]	0/0
1280	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA- SAMANA-PATRAN ROAD (SH-1 - [N24001414],NHAI,PUNJAB	12/2020	1/2024 (4/2024) [1/2024]	733.00 (-) [733.00]	0.00 (0.00) [0]	0/0
1281	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232],NHAI,HIMACHAL PRADESH	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,660.92 (0.00) [0]	0/0
1282	GHAZIABAD-ALIGARH NH-91 - [N24000170],NHAI,UTTAR PRADESH	2/2011	8/2013 (-) [8/2013]	1,141.00 (-) [1,141.00]	1,715.00 (0.00) [0]	0/0
1283	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506],NHAI,BIHAR	1/1991	/ (-) [12/2022]	642.41 (-) [681.67]	673.94 (39.26) [-]	3/4
1284	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785],NHAI,TAMIL NADU	2/2018	/ (-) [12/2022]	1,166.26 (1,296.93) [1,422.13]	444.08 (255.87) [-]	0/0
1285	4-LANNING OF STHIYATHOPU- CHOLOPURAM - [N24000708],NHAI,TAMIL NADU	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	929.50 (0.00) [0]	0/0
1286	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590],NHAI,BIHAR	5/2015	5/2017 (-) [9/2024]	581.84 (-) [581.84]	0.00 (0.00) [88]	0/0
1287	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426],NHAI,RAJASTHAN	11/2012	8/2016 (-) [5/2022]	530.07 (-) [530.07]	558.12 (0.00) [0]	0/0
1288	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592],NHAI,GUJARAT	7/2016	/ (-) [12/2022]	829.97 (-) [829.97]	329.71 (0.00) [-]	0/0
1289	FOUR LANNING OF JHANSI- KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653],NHAI,UTTAR PRADESH	3/2017	3/2020 (-) [8/2022]	1,373.28 (-) [1,405.27]	1,401.96 (31.99) [29]	3/4

1290	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854],NHAI,JHARKHAND	3/2018	/ (2/2023) [2/2023]	1,005.08 (-) [1,005.08]	0.00 (0.00) [-]	0/0
1291	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589],NHAI,RAJASTHAN	6/2016	6/2019 (5/2022) [3/2022]	649.00 (-) [649.00]	724.30 (0.00) [0]	0/0
1292	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428],NHAI,TAMIL NADU	3/2018	11/2021 (-) [11/2023]	998.70 (-) [998.70]	0.00 (0.00) [24]	0/0
1293	KRISHNANAGAR-BERHAMPUR - [N24000209],NHAI,WEST BENGAL	2/2012	7/2014 (-) [0/0]	702.16 (-) [702.16]	0.00 (0.00) [0]	0/4
1294	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549],NHAI,UTTAR PRADESH	3/2016	/ (-) [9/2022]	1,396.74 (4,041.80) [1,396.74]	3,704.91 (0.00) [-]	0/0
1295	ISMAILABAD-NARNAUL PKG-3 - [N24001191],NHAI,HARYANA	1/2019	/ (5/2022) [5/2022]	889.36 (986.10) [986.10]	949.40 (96.74) [0]	3/4
1296	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833],NHAI,GUJARAT	3/2018	/ (-) [6/2022]	1,437.64 (-) [1,437.64]	564.11 (0.00) [0]	0/0
1297	NAGPUR RING ROAD PACKAGE-2 - [N24000560],NHAI,MAHARASHTRA	3/2016	7/2019 (10/2023) [10/2023]	591.66 (-) [591.66]	332.33 (0.00) [51]	0/0
1298	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342],NHAI,KARNATAKA	5/2015	9/2017 (-) [9/2019]	709.00 (-) [709.00]	541.35 (0.00) [0]	0/0
1299	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302],NHAI,TAMIL NADU	7/2020	12/2021 (-) [0/0]	3,426.00 (-) [5,852.00]	0.00 (2,426.00) [0]	0/0
1300	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849],NHAI,MAHARASHTRA	3/2018	/ (2/2022) [2/2022]	289.21 (-) [289.21]	240.40 (0.00) [0]	4/4
1301	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831],NHAI,MULTI STATE	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]	0/0
1302	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633],NHAI,ODISHA	10/2016	/ (-) [3/2022]	1,008.96 (-) [1,008.96]	1,148.36 (0.00) [0]	0/0
1303	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565],NHAI,UTTAR PRADESH	3/2016	/ (12/2021) [12/2021]	1,737.00 (2,421.37) [2,421.37]	1,877.96 (684.37) [0]	4/4
1304	FOUR LANING OF SIMGA - SARAGAON - [N24000495],NHAI,CHHATISGARH	12/2015	5/2018 (3/2022) [8/2022]	596.67 (819.35) [819.35]	439.27 (222.68) [51]	0/0
1305	ADDITIONAL FACILITY FOR 4-LANE	12/2017	/	207.00	0.00	0/0

	DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721],NHAI,UTTAR PRADESH		(-) [9/2021]	(-) [207.00]	(0.00) [0]	
1306	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 - [N24001443],NHAI,GUJARAT	5/2020	3/2024 (-) [3/2024]	690.30 (-) [690.30]	62.72 (0.00) [0]	0/4
1307	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659],NHAI,MAHARASHTRA	3/2017	3/2017 (-) [6/2022]	1,059.73 (-) [1,071.00]	0.00 (11.27) [0]	0/0
1308	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629],NHAI,MAHARASHTRA	11/2016	3/2019 (-) [6/2022]	400.25 (-) [400.25]	259.11 (0.00) [0]	0/0
1309	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233],NHAI,MADHYA PRADESH	3/2019	5/2020 (-) [8/2022]	1,047.00 (-) [1,047.00]	879.00 (0.00) [27]	2/3
1310	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692],NHAI,HIMACHAL PRADESH	6/2017	6/2020 (-) [6/2023]	2,485.93 (-) [2,485.93]	1,208.03 (0.00) [36]	0/0
1311	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631],NHAI,MAHARASHTRA	11/2016	/ (5/2017) [9/2022]	290.73 (-) [359.60]	339.75 (68.87) [-]	3/4
1312	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231],NHAI,MADHYA PRADESH	2/2019	12/2019 (-) [8/2022]	990.97 (-) [990.97]	1,020.00 (0.00) [32]	2/3
1313	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415],NHAI,PUNJAB	12/2020	4/2024 (-) [4/2024]	881.00 (-) [881.00]	0.00 (0.00) [0]	0/0
1314	4-LANING OF FARAKA-RAIGANJ - [N24000202],NHAI,WEST BENGAL	2/2011	8/2013 (-) [3/2022]	1,078.84 (-) [1,078.84]	2,301.82 (0.00) [0]	3/4
1315	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453],NHAI,MAHARASHTRA	1/2015	7/2017 (-) [10/2019]	972.50 (-) [972.50]	1,492.00 (0.00) [0]	0/0
1316	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726],NHAI,JHARKHAND	1/2018	/ (-) [9/2022]	1,155.16 (-) [950.49]	539.74 (-204.67) [-]	0/0
1317	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379],NHAI,MAHARASHTRA	2/2019	11/2019 (-) [12/2022]	594.75 (594.75) [606.75]	410.81 (12.00) [37]	0/0
1318	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730],NHAI,MAHARASHTRA	1/2018	/ (6/2022) [6/2022]	621.00 (595.00) [595.00]	595.00 (-26.00) [0]	2/3
1319	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188],NHAI,BIHAR	5/2011	11/2013 (-) [5/2022]	511.54 (-) [591.00]	576.99 (79.46) [0]	0/0

1320	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303],NHAI,BIHAR	10/2013	12/2020 (-) [12/2022]	649.90 (-) [649.90]	155.54 (0.00) [24]	0/0
1321	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847],NHAI,MAHARASHTRA	3/2018	/ (2/2022) [3/2022]	291.53 (-) [291.53]	264.99 (0.00) [0]	4/4
1322	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620],NHAI,WEST BENGAL	9/2016	8/2018 (-) [3/2022]	767.03 (-) [767.03]	613.08 (0.00) [0]	0/0
1323	ISMAILABAD-NARNAUL PKG-8 - [N24001189],NHAI,HARYANA	1/2019	/ (3/2022) [3/2022]	1,033.19 (1,044.32) [1,044.32]	911.58 (11.13) [0]	0/4
1324	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362],NHAI,UTTAR PRADESH	9/2015	9/2016 (-) [11/2018]	368.73 (503.36) [368.73]	488.83 (0.00) [0]	4/4
1325	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699],NHAI,ODISHA	7/2017	7/2017 (-) [10/2022]	476.56 (-) [476.56]	275.93 (0.00) [63]	0/0
1326	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798],NHAI,UTTAR PRADESH	3/2018	/ (-) [5/2022]	2,140.93 (-) [2,140.93]	1,877.63 (0.00) [0]	0/0
1327	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603],NHAI,KARNATAKA	8/2016	3/2019 (6/2023) [6/2023]	1,167.42 (-) [870.00]	380.24 (-297.42) [51]	0/4
1328	NAGPUR RING ROAD PACKAGE-1 - [N24000558],NHAI,MAHARASHTRA	3/2016	7/2019 (7/2023) [7/2023]	546.00 (-) [546.00]	347.64 (0.00) [48]	2/3
1329	TRICHY - KARUR - [N24000528],NHAI,TAMIL NADU	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]	0/0
1330	4-laning of Khammam-Ashwaraopet section of NH-365BB - [N24000751],NHAI,TELANGANA	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]	0/0
1331	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713],NHAI,MAHARASHTRA	12/2017	/ (-) [0/0]	404.94 (495.92) [404.94]	427.22 (0.00) [0]	0/0
1332	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630],NHAI,MAHARASHTRA	11/2016	3/2019 (-) [12/2022]	446.17 (-) [446.17]	242.52 (0.00) [45]	0/0
1333	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 - [N24001432],NHAI,ASSAM	12/2021	8/2024 (-) [8/2024]	300.00 (-) [300.00]	29.81 (0.00) [0]	0/0
1334	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177],NHAI,TAMIL NADU	9/2011	8/2013 (-) [7/2022]	485.00 (-) [485.00]	293.45 (0.00) [0]	0/0
1335	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418],NHAI,PUNJAB	12/2020	4/2024 (-) [4/2024]	1,094.46 (-) [1,094.46]	0.00 (0.00) [0]	0/0

1336	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230],NHAI,MAHARASHTRA	5/2013	2/2014 (-) [10/2022]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [104]	2/2
1337	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723],NHAI,BIHAR	1/2018	/ (12/2019) [6/2023]	573.70 (644.50) [726.99]	222.51 (153.29) [-]	0/0
1338	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718],NHAI,ANDHRA PRADESH	12/2017	/ (7/2021) [0/0]	328.67 (416.07) [416.07]	330.31 (87.40) [0]	0/0
1339	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178],NHAI,ANDHRA PRADESH	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]	0/0
1340	PATNA-MUZZAFFARPUR - [N24000165],NHAI,BIHAR	8/2010	2/2013 (12/2022) [3/2023]	671.30 (-) [671.30]	1,587.77 (0.00) [121]	3/4
1341	4-LANNING OF CHUTMALPUR- GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH- 73) TO KM 17.900 - [N24000562],NHAI,UTTARAKHAND	3/2016	/ (3/2022) [3/2022]	1,443.00 (2,330.79) [2,330.79]	1,246.85 (887.79) [0]	3/3
1342	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602],NHAI,KARNATAKA	8/2016	4/2020 (-) [8/2022]	1,664.20 (-) [1,664.20]	1,301.27 (0.00) [28]	3/4
1343	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668],NHAI,ANDHRA PRADESH	3/2017	3/2020 (-) [3/2022]	1,041.62 (-) [1,187.10]	975.08 (145.48) [0]	0/0
1344	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835],NHAI,HARYANA	3/2018	/ (-) [8/2023]	1,484.30 (-) [1,484.30]	889.47 (0.00) [-]	0/0
1345	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693],NHAI,GUJARAT	6/2017	6/2020 (-) [10/2021]	1,958.88 (2,047.39) [1,993.81]	1,116.85 (34.93) [0]	3/3
1346	ETAWAH CHAKERI - [N24000219],NHAI,UTTAR PRADESH	3/2013	9/2015 (-) [1/2016]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]	0/0
1347	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172],NHAI,TAMIL NADU	9/2011	12/2013 (5/2024) [5/2024]	1,250.00 (1,380.73) [1,380.73]	1,354.65 (130.73) [125]	0/0
1348	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377],NHAI,MAHARASHTRA	2/2019	11/2019 (1/2022) [12/2022]	731.89 (731.89) [732.34]	530.71 (0.45) [37]	0/0
1349	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651],NHAI,MAHARASHTRA	2/2017	2/2020 (3/2022) [3/2022]	904.16 (-) [904.16]	0.00 (0.00) [0]	0/0
1350	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199],NHAI,MADHYA PRADESH	10/2019	/ (-) [8/2022]	743.88 (-) [743.89]	721.00 (0.01) [-]	2/3
1351	FOUR LANING OF FORBESGANJ -	8/2015	4/2018	322.09	181.18	0/0

	JOGBANI - [N24000501],NHAI,BIHAR		(-) [6/2022]	(-) [322.09]	(0.00) [0]	
1352	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655],NHAI,MAHARASHTRA	3/2017	3/2020 (-) [11/2022]	247.02 (-) [157.49]	31.97 (-89.53) [32]	0/0
1353	2-LANNING WITH PS MOTIHARI- RAXAUL - [N24000186],NHAI,BIHAR	10/2011	4/2014 (-) [11/2022]	375.09 (-) [375.09]	494.33 (0.00) [103]	0/0
1354	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522],NHAI,BIHAR	8/2015	4/2018 (-) [1/2021]	516.13 (-) [649.27]	638.53 (133.14) [0]	4/4
1355	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208],NHAI,UTTAR PRADESH	7/2012	1/2014 (-) [12/2019]	291.36 (480.31) [469.31]	470.89 (177.95) [0]	0/0
1356	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462],NHAI,KARNATAKA	5/2014	8/2016 (12/2022) [12/2022]	1,655.01 (2,639.00) [2,639.00]	1,710.83 (983.99) [76]	3/4
1357	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471],NHAI,JAMMU AND KASHMIR	12/2015	6/2019 (-) [12/2023]	2,168.66 (-) [2,168.66]	1,190.60 (0.00) [54]	0/0
1358	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736],NHAI,ODISHA	1/2018	/ (-) [6/2023]	686.65 (-) [686.65]	254.00 (0.00) [-]	0/0
1359	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416],NHAI,PUNJAB	12/2020	1/2024 (-) [4/2024]	989.66 (-) [989.66]	0.00 (0.00) [3]	0/0
1360	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815],NHAI,GUJARAT	3/2018	/ (-) [6/2022]	2,702.05 (-) [2,043.00]	2,043.00 (-659.05) [0]	0/0
1361	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719],NHAI,ANDHRA PRADESH	12/2017	/ (-) [6/2022]	1,323.15 (-) [1,323.15]	1,254.88 (0.00) [0]	0/0
1362	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498],NHAI,UTTAR PRADESH	6/2016	7/2018 (12/2021) [9/2022]	667.00 (2,405.30) [2,328.27]	2,126.16 (1,661.27) [50]	0/1
1363	2-LANING OF KRISHNAGIRI- TINDIVANAM (APPROVED LENH 170 KM) - [N24000213],NHAI,TAMIL NADU	4/2012	4/2014 (-) [3/2023]	624.00 (526.09) [526.09]	189.10 (-97.91) [107]	0/0
1364	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834],NHAI,GUJARAT	3/2018	/ (-) [6/2022]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]	0/0
1365	4L OF ADDAHOLE TO BANTWAL CROSS SECTION - [N24001426],NHAI,KARNATAKA	3/2021	10/2021 (-) [9/2023]	317.90 (317.90) [317.90]	127.41 (0.00) [23]	1/4
1366	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799],NHAI,ANDHRA PRADESH	2/2018	/ (11/2021) [8/2022]	1,959.00 (2,909.00) [1,959.00]	1,412.01 (0.00) [-]	0/0
1367	REHABILITATION AND UP-	1/2018	/	668.86	505.36	0/0

	GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732],NHAI,ODISHA		(-) [3/2022]	(-) [668.86]	(0.00) [0]	
1368	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634],NHAI,HIMACHAL PRADESH	10/2016	/ (-) [7/2022]	447.75 (-) [447.75]	1,402.07 (0.00) [0]	0/0
1369	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656],NHAI,MAHARASHTRA	3/2017	3/2020 (7/2022) [7/2024]	744.64 (-) [982.00]	0.00 (237.36) [52]	0/0
1370	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830],NHAI,TAMIL NADU	3/2018	/ (-) [1/2024]	2,065.96 (-) [2,169.00]	0.00 (103.04) [-]	0/0
1371	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712],NHAI,UTTAR PRADESH	12/2017	/ (-) [3/2021]	1,232.21 (-) [1,087.00]	1,084.94 (-145.21) [0]	0/0
1372	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800],NHAI,UTTAR PRADESH	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,228.92 (211.43) [0]	0/0
1373	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792],NHAI,UTTAR PRADESH	3/2018	/ (-) [12/2022]	809.07 (1,065.70) [1,065.70]	1,049.98 (256.63) [-]	0/0
1374	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824],NHAI,TELANGANA	3/2018	/ (-) [10/2022]	857.62 (-) [857.62]	561.95 (0.00) [-]	0/0
1375	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459],NHAI,KERALA	6/2015	/ (1/2020) [1/2020]	845.24 (-) [941.00]	910.78 (95.76) [0]	0/0
1376	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212],NHAI,UTTARAKHAND	11/2011	10/2013 (3/2022) [3/2022]	478.51 (1,082.40) [1,082.40]	315.11 (603.89) [0]	0/0
1377	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627],NHAI,MAHARASHTRA	11/2016	/ (12/2021) [9/2022]	1,071.61 (-) [1,048.10]	1,251.13 (-23.51) [-]	3/4
1378	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304],NHAI,BIHAR	10/2013	11/2020 (-) [11/2022]	446.97 (-) [446.97]	170.57 (0.00) [24]	0/0
1379	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432],NHAI,MAHARASHTRA	9/2015	5/2018 (11/2020) [11/2020]	414.51 (414.00) [414.00]	399.23 (-0.51) [0]	1/1
1380	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738],NHAI,ODISHA	1/2018	/ (-) [3/2023]	999.00 (-) [999.00]	309.51 (0.00) [-]	0/0
1381	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555],NHAI,TAMIL NADU	2/2016	8/2018 (-) [3/2022]	707.82 (-) [707.82]	449.52 (0.00) [0]	0/0

1382	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429],NHAI,TAMIL NADU	3/2018	11/2021 (-) [11/2023]	1,294.47 (-) [1,294.47]	0.00 (0.00) [24]	0/0
1383	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828],NHAI,TAMIL NADU	3/2018	/ (8/2023) [8/2023]	633.55 (664.10) [736.33]	68.39 (102.78) [-]	0/0
1384	FOUR LANING OF PATNA TO KOILWAR - [N24000473],NHAI,BIHAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]	0/0
1385	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176],NHAI,TAMIL NADU	5/2010	5/2013 (-) [5/2022]	374.00 (-) [166.90]	98.45 (-207.10) [0]	0/0
1386	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716],NHAI,ODISHA	12/2017	/ (-) [10/2022]	417.51 (-) [417.51]	320.13 (0.00) [-]	0/0
1387	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556],NHAI,UTTAR PRADESH	3/2016	4/2019 (6/2022) [6/2022]	899.00 (1,376.86) [1,376.86]	909.36 (477.86) [0]	3/4
1388	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564],NHAI,UTTAR PRADESH	3/2016	/ (7/2022) [7/2022]	1,408.00 (1,330.02) [1,330.02]	679.90 (-77.98) [0]	1/4
1389	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715],NHAI,ODISHA	12/2017	/ (-) [6/2023]	686.65 (-) [686.65]	316.00 (0.00) [-]	0/0
1390	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499],NHAI,UTTAR PRADESH	12/2015	6/2018 (12/2021) [12/2022]	667.00 (3,192.10) [3,006.53]	2,989.89 (2,339.53) [54]	0/0
1391	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802],NHAI,UTTAR PRADESH	3/2018	/ (-) [12/2021]	1,025.80 (-) [677.07]	222.94 (-348.73) [0]	0/0
1392	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG - [N24001446],NHAI,GUJARAT	5/2020	12/2023 (-) [12/2023]	894.00 (-) [894.00]	213.55 (0.00) [0]	1/4
1393	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717],NHAI,JAMMU AND KASHMIR	12/2017	/ (10/2018) [3/2024]	1,471.75 (-) [1,339.00]	1,236.41 (-132.75) [-]	2/3
1394	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852],NHAI,HIMACHAL PRADESH	3/2018	/ (11/2022) [11/2022]	478.74 (-) [1,135.08]	905.95 (656.34) [-]	0/0
1395	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340],NHAI,MADHYA PRADESH	11/2019	7/2021 (-) [7/2023]	716.00 (-) [716.00]	0.00 (0.00) [24]	0/0

1396	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477],NHAI,RAJASTHAN	2/2008	10/2011 (-) [6/2022]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]	0/0
1397	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213],NHAI,MADHYA PRADESH	12/2017	/ (-) [8/2022]	1,094.97 (-) [1,094.97]	1,097.00 (0.00) [-]	3/4
1398	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691],NHAI,RAJASTHAN	4/2017	4/2020 (-) [12/2022]	894.00 (-) [929.32]	880.00 (35.32) [32]	0/0
1399	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417],NHAI,PUNJAB	12/2020	4/2024 (-) [4/2024]	1,234.40 (-) [1,234.40]	0.00 (0.00) [0]	0/0
1400	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812],NHAI,ANDHRA PRADESH	3/2018	/ (-) [5/2022]	557.30 (-) [557.30]	460.93 (0.00) [0]	0/0
1401	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844],NHAI,ODISHA	3/2018	/ (-) [9/2022]	806.11 (-) [806.11]	665.33 (0.00) [-]	0/0
1402	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829],NHAI,TAMIL NADU	3/2018	/ (-) [12/2022]	1,016.92 (1,282.30) [1,308.88]	492.86 (291.96) [-]	0/0
1403	4-LANNING OF CHAPRA-HAJIPUR - [N24000187],NHAI,BIHAR	1/2011	7/2013 (12/2022) [0/0]	575.00 (-) [575.00]	517.32 (0.00) [0]	2/3
1404	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787],NHAI,KARNATAKA	2/2018	/ (-) [10/2022]	1,995.34 (-) [2,400.00]	3,568.04 (404.66) [-]	0/0
1405	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796],NHAI,UTTAR PRADESH	3/2018	/ (-) [10/2022]	1,117.84 (-) [1,117.84]	84.10 (0.00) [-]	0/0
1406	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714],NHAI,BIHAR	12/2017	/ (-) [10/2024]	2,598.00 (-) [1,962.50]	689.57 (-635.50) [-]	0/0
1407	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149],NHAI,KERALA	2/2010	8/2012 (-) [3/2022]	617.00 (-) [617.00]	0.00 (0.00) [0]	0/0
1408	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480],NHAI,BIHAR	12/2015	4/2019 (7/2022) [12/2022]	1,041.10 (567.00) [639.58]	492.38 (-401.52) [44]	0/0
1409	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735],NHAI,ODISHA	1/2018	/ (-) [10/2022]	564.66 (-) [564.66]	452.72 (0.00) [-]	0/1
1410	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649],NHAI,GUJARAT	1/2017	/ (6/2021) [9/2022]	1,251.11 (-) [1,361.00]	503.77 (109.89) [-]	2/4

1411	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807],NHAI,ANDHRA PRADESH	3/2018	3/2021 (-) [8/2022]	1,532.62 (-) [1,827.00]	1,306.69 (294.38) [17]	4/4
1412	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600],NHAI,PUNJAB	8/2016	9/2019 (-) [5/2022]	1,388.34 (-) [1,588.29]	739.00 (199.95) [0]	0/0
1413	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813],NHAI,BIHAR	3/2018	/ (-) [6/2023]	496.20 (-) [537.17]	156.46 (40.97) [-]	0/0
1414	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212],NHAI,MADHYA PRADESH	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	689.00 (183.02) [-]	2/4
1415	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832],NHAI,MULTI STATE	3/2018	/ (-) [0/0]	998.70 (-) [962.00]	0.00 (-36.70) [0]	0/0
1416	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441],NHAI,MAHARASHTRA	10/2015	5/2018 (12/2022) [6/2022]	593.26 (-) [717.24]	662.98 (123.98) [0]	0/1
1417	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666],NHAI,BIHAR	3/2017	3/2020 (-) [5/2022]	235.48 (-) [227.77]	11.00 (-7.71) [0]	0/0
1418	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839],NHAI,HARYANA	3/2018	/ (-) [2/2022]	634.70 (-) [925.96]	823.04 (291.26) [0]	0/0
1419	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483],NHAI,PUNJAB	9/2014	/ (3/2023) [3/2023]	479.00 (479.00) [479.00]	456.80 (0.00) [-]	3/4
1420	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559],NHAI,UTTARAKHAND	3/2016	/ (9/2022) [9/2022]	720.00 (793.63) [793.63]	326.96 (73.63) [-]	2/4
1421	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298],NHAI,ANDHRA PRADESH	9/2018	1/2020 (8/2021) [7/2022]	597.67 (570.98) [570.98]	509.41 (-26.69) [0]	0/0
1422	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628],NHAI,MAHARASHTRA	11/2016	/ (8/2022) [11/2022]	1,064.88 (-) [1,021.00]	627.92 (-43.88) [-]	2/4
1423	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482],NHAI,BIHAR	8/2015	/ (-) [9/2022]	814.04 (-) [825.17]	1,018.46 (11.13) [-]	3/4
1424	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299],NHAI,ANDHRA PRADESH	9/2018	2/2019 (4/2021) [5/2022]	617.41 (655.64) [668.45]	562.93 (51.04) [0]	0/0
1425	ISMAILABAD-NARNAUL PKG-6	1/2019	/	1,120.06	1,127.92	3/4

	- [N24001187],NHAI,HARYANA		(7/2022) [7/2022]	(1,206.48) [1,206.48]	(86.42) [0]	
1426	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENMORE PORT CONNECTIVITY - [N24000173],NHAI,TAMIL NADU	6/2011	6/2013 (-) [2/2022]	600.00 (-) [600.00]	2.98 (0.00) [0]	0/0
1427	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- - [N24001420],NHAI,PUNJAB	2/2021	4/2024 (-) [4/2024]	853.66 (-) [853.66]	0.00 (0.00) [0]	0/0
1428	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305],NHAI,BIHAR	10/2013	11/2020 (-) [11/2022]	464.09 (-) [464.09]	174.53 (0.00) [24]	0/0
1429	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430],NHAI,TAMIL NADU	3/2018	1/2022 (-) [1/2024]	2,120.40 (-) [2,120.40]	0.00 (0.00) [24]	0/0
1430	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442],NHAI,MAHARASHTRA	12/2015	3/2019 (12/2022) [12/2022]	649.50 (-) [649.50]	277.75 (0.00) [45]	0/4
1431	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491],NHAI,UTTAR PRADESH	1/2016	6/2018 (12/2021) [12/2022]	815.28 (2,603.99) [2,323.88]	2,223.06 (1,508.60) [54]	0/0
1432	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734],NHAI,ODISHA	1/2018	/ (-) [10/2022]	614.48 (-) [614.48]	440.00 (0.00) [-]	0/0
1433	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674],NHAI,KARNATAKA	3/2017	3/2020 (-) [6/2022]	831.58 (-) [1,177.00]	912.41 (345.42) [0]	0/0
1434	ISMAILABAD-NARNAUL PKG-7 - [N24001188],NHAI,HARYANA	1/2019	/ (6/2022) [6/2022]	1,137.42 (1,238.29) [1,238.29]	1,185.04 (100.87) [0]	3/4
1435	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636],NHAI,RAJASTHAN	12/2016	/ (-) [3/2022]	1,031.95 (-) [1,031.95]	1,518.41 (0.00) [0]	0/0
1436	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804],NHAI,TELANGANA	3/2018	/ (-) [12/2021]	802.65 (-) [802.65]	527.89 (0.00) [0]	0/0
1437	FOUR LANNING OF DARAH JHALWAR TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703],NHAI,RAJASTHAN	10/2017	10/2017 (-) [5/2022]	964.17 (1,140.64) [1,198.64]	1,053.15 (234.47) [0]	0/0
1438	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371],NHAI,BIHAR	10/2019	2/2020 (-) [8/2023]	1,101.99 (-) [1,101.99]	424.90 (0.00) [42]	0/4
1439	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 -	11/2017	1/2019 (-) [1/2019]	2,159.00 (2,262.00) [2,262.00]	1,978.74 (103.00) [0]	0/0

	[N24001185],NHAI,UTTAR PRADESH					
1440	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725],NHAI,JHARKHAND	1/2018	/ (-) [3/2023]	273.46 (-) [276.17]	175.09 (2.71) [-]	0/0
1441	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360],NHAI,UTTAR PRADESH	4/2014	1/2016 (-) [1/2019]	351.34 (589.04) [417.68]	545.12 (66.34) [0]	0/0
1442	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803],NHAI,UTTAR PRADESH	3/2018	/ (-) [10/2021]	1,115.28 (-) [770.04]	332.69 (-345.24) [0]	0/0
1443	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853],NHAI,MAHARASHTRA	3/2018	/ (-) [6/2022]	642.13 (-) [807.00]	760.42 (164.87) [0]	0/0
	<u>SHIPPING AND PORTS</u>					
1444	JAL MARG VIKAS PROJECT - [N25000072],IWAI,MULTI STATE	1/2018	3/2023 (-) [3/2023]	5,369.18 (4,633.81) [4,633.81]	2,160.50 (-735.37) [0]	2/7
	<u>SOCIAL JUSTICE</u>					
1445	CENTRE FOR DISABILITY SPORTS - [N38000001],CPWD,MADHYA PRADESH	2/2019	3/2024 (-) [3/2024]	170.99 (-) [170.99]	73.80 (0.00) [0]	1/5
	<u>STEEL</u>					
1446	NMDC INTEGRATED STEEL PLANT - [N12000086],NMDC,CHHATISGARH	1/2010	5/2015 (3/2023) [3/2023]	15,525.00 (21,940.00) [21,940.00]	21,019.89 (6,415.00) [94]	77/86
1447	SCREENING PLANT-III AT KIRANDUL - [N12000127],NMDC,CHHATISGARH	3/2021	8/2024 (-) [8/2024]	2,092.97 (-) [2,092.97]	396.60 (0.00) [0]	0/5
1448	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124],NMDC,CHHATISGARH	11/2015	6/2023 (-) [7/2024]	2,907.00 (-) [2,907.00]	908.39 (0.00) [13]	3/8
1449	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118],SAIL,JHARKHAND	11/2016	6/2019 (6/2022) [9/2022]	262.87 (-) [262.87]	272.19 (0.00) [39]	1/1
1450	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095],SAIL,JHARKHAND	3/2015	10/2017 (12/2021) [12/2023]	1,034.01 (-) [1,034.01]	782.72 (0.00) [74]	0/2
1451	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122],SAIL,ODISHA	11/2020	5/2023 (-) [5/2023]	377.18 (-) [377.18]	128.30 (0.00) [0]	0/1
1452	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT - [N12000126],SAIL,JHARKHAND	2/2022	6/2024 (-) [6/2024]	207.74 (-) [207.74]	8.71 (0.00) [0]	0/0
1453	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123],SAIL,CHHATISGARH	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	123.14 (0.00) [0]	0/0
1454	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125],SAIL,ODISHA	1/2022	5/2025 (-) [5/2025]	970.18 (-) [970.18]	76.33 (0.00) [0]	0/1
	<u>TELECOMMUNICATIONS</u>					
1455	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART -	3/2020	6/2021 (11/2021) [11/2022]	431.16 (461.42) [461.42]	107.44 (30.26) [17]	0/0

	[N26000114],BSNL,MULTI STATE					
1456	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115],CPWD FOR TELECO,DELHI	10/2014	3/2018 (-) [11/2022]	248.20 (-) [248.20]	174.08 (0.00) [56]	3/5
1457	NETWORK FOR SPECTRUM - [N26000101],DOT,MULTI STATE	3/2012	7/2015 (-) [6/2022]	13,334.00 (-) [13,334.00]	21,545.00 (0.00) [0]	0/0
	URBAN DEVELOPMENT					
1458	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137],MEGA,GUJARAT	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	763.91 (0.00) [0]	0/1
1459	SURAT METRO RAIL PROJECT - [N28000138],MEGA,GUJARAT	3/2019	3/2024 (-) [6/2024]	12,020.32 (-) [12,020.32]	814.67 (0.00) [3]	0/1
1460	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122],MEGA,GUJARAT	11/2014	12/2018 (-) [9/2022]	10,773.00 (-) [12,925.22]	10,816.18 (2,152.22) [45]	0/1
1461	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151],BMRCL,KARNATAKA	6/2021	6/2026 (-) [6/2026]	14,788.10 (-) [14,788.10]	2,942.84 (0.00) [0]	0/76
1462	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058],BMRCL,KARNATAKA	2/2014	2/2021 (-) [3/2025]	26,405.14 (-) [26,405.14]	22,869.55 (0.00) [49]	163/249
1463	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149],CPWD,CHHATISGARH	5/2019	9/2020 (-) [11/2023]	299.97 (-) [299.97]	69.08 (0.00) [38]	2/6
1464	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129],CPWD,DELHI	10/2016	3/2022 (6/2024) [6/2024]	1,128.00 (-) [1,128.00]	69.28 (0.00) [27]	0/0
1465	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128],CPWD,DELHI	10/2016	7/2021 (-) [6/2024]	1,180.00 (-) [1,100.80]	36.69 (-79.20) [35]	0/6
1466	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087],CPWD,DELHI	6/2015	4/2019 (-) [4/2022]	197.33 (-) [220.00]	113.34 (22.67) [0]	2/2
1467	CONSTRUCTION OF NEW NACIN CAMPUS, PALASAMIDRAM, ANDHRA PRADESH - [N28000152],CPWD,ANDHRA PRADESH	2/2022	8/2024 (-) [8/2024]	702.47 (-) [702.47]	1.16 (0.00) [0]	0/0
1468	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110],CPWD,DELHI	10/2016	3/2021 (-) [0/0]	422.00 (-) [422.00]	221.22 (0.00) [0]	0/0
1469	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114],CPWD,DELHI	10/2016	8/2020 (-) [0/0]	392.00 (-) [392.00]	242.43 (0.00) [0]	2/5
1470	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084],CMRL,TAMIL NADU	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [18,380.00]	17,629.68 (3,780.00) [0]	24/24
1471	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097],CMRL,TAMIL NADU	6/2016	3/2018 (2/2021) [0/0]	3,770.00 (-) [3,770.00]	2,549.19 (0.00) [0]	21/21
1472	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-)	24,948.65 (-)	4,071.69 (0.00)	0/1

	- [N28000135],DMRC,DELHI		[9/2025]	[24,948.65]	[6]	
1473	DELHI MRTS PHASE-III - [N28000056],DMRC,DELHI	9/2011	3/2016 (8/2021) [0/0]	38,585.00 (-) [40,180.91]	39,907.57 (1,595.91) [0]	1/1
1474	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136],DMRC,DELHI	5/2017	12/2020 (9/2021) [0/0]	565.00 (-) [565.00]	514.44 (0.00) [0]	1/1
1475	KOCHI METRO RAIL PROJECT - [N28000081],KMRCL,KERALA	7/2012	7/2017 (9/2020) [0/0]	5,181.79 (-) [6,218.14]	6,065.85 (1,036.35) [0]	0/0
1476	KANPUR METRO RAIL PROJECT - [N28000144],LMRCL,UTTAR PRADESH	5/2019	3/2024 (-) [11/2024]	11,076.48 (-) [11,076.48]	3,461.78 (0.00) [8]	0/0
1477	AGRA METRO RAIL PROJECT - [N28000145],LMRCL,UTTAR PRADESH	5/2019	3/2024 (-) [12/2025]	8,379.62 (-) [8,379.62]	1,143.47 (0.00) [21]	0/0
1478	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121],MMRC,MAHARASHTRA	12/2016	11/2021 (3/2023) [3/2023]	11,420.00 (-) [11,420.00]	9,009.34 (0.00) [16]	0/0
1479	MUMBAI METRO LINE 3 (COLABA- BANDRA-SEEPZ) - [N28000086],MMRCL,MAHARASHTRA	7/2013	3/2020 (-) [12/2023]	23,136.00 (-) [33,406.00]	22,064.15 (10,270.00) [45]	0/0
1480	INDORE METRO RAIL - [N28000125],MPMRCL,MADHYA PRADESH	11/2018	2/2023 (7/2025) [7/2025]	7,500.80 (-) [7,500.80]	261.39 (0.00) [29]	0/0
1481	BHOPAL METRO RAIL - [N28000124],MPMRCL,MADHYA PRADESH	11/2018	2/2023 (5/2025) [5/2025]	6,941.40 (-) [6,941.40]	244.26 (0.00) [27]	0/0
1482	NAGPUR METRO RAIL - [N28000085],NMRCL,MAHARASHTRA	8/2014	3/2018 (-) [3/2022]	8,680.00 (-) [9,759.79]	8,524.81 (1,079.79) [0]	0/0
1483	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105],NBCC,DELHI	7/2016	/ (-) [3/2023]	2,694.00 (-) [2,694.00]	1,292.02 (0.00) [-]	0/9
1484	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134],NCRTC,MULTI STATE	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	9,900.05 (0.00) [0]	0/8
1485	PATNA METRO RAIL CORPORATION LIMITED - [N28000148],PATNA METRO RAI,BIHAR	2/2019	6/2024 (-) [6/2024]	13,365.77 (-) [13,925.50]	437.20 (559.73) [0]	0/0
	<u>WATER RESOURCES</u>					
1486	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001],BPB,MAHARASHTRA	3/2017	12/2019 (12/2022) [0/0]	233.57 (-) [233.57]	196.88 (0.00) [0]	0/0
1487	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044],BUIDCO,BIHAR	3/2017	5/2021 (-) [10/2022]	277.42 (-) [277.42]	298.55 (0.00) [17]	0/0
1488	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027],BUIDCO,BIHAR	10/2017	9/2020 (-) [3/2024]	254.13 (413.29) [413.29]	0.07 (159.16) [42]	0/0
1489	SAIDPUR SEWER NETWORK PATNA - [N30000039],BUIDCO,BIHAR	4/2015	1/2021 (-) [6/2022]	268.63 (431.21) [431.21]	432.61 (162.58) [0]	0/0
1490	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036],BUIDCO,BIHAR	3/2018	10/2021 (-) [12/2023]	294.02 (-) [294.02]	90.96 (0.00) [26]	0/0
1491	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035],BUIDCO,BIHAR	3/2018	8/2021 (-) [8/2023]	305.19 (-) [305.19]	146.80 (0.00) [24]	0/0
1492	SEWERAGE SYSTEM AND STP FOR	8/2017	6/2022	824.00	140.17	0/0

	DIGHA ZONE, PATNA - [N30000051],BUIDCO,BIHAR		(-) [12/2022]	(-) [824.00]	(0.00) [6]	
1493	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040],BUIDCO,BIHAR	5/2017	4/2021 (-) [9/2022]	356.37 (-) [356.37]	215.30 (0.00) [17]	0/0
1494	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050],BUIDCO,BIHAR	8/2017	6/2022 (-) [12/2022]	578.89 (-) [578.89]	16.55 (0.00) [6]	0/0
1495	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043],BUIDCO,BIHAR	5/2017	11/2020 (-) [5/2022]	191.62 (-) [191.62]	94.08 (0.00) [0]	0/0
1496	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026],BUIDCO,BIHAR	3/2018	7/2021 (-) [3/2023]	230.06 (-) [230.06]	137.93 (0.00) [20]	0/0
1497	I AND D AND STP AT CHAPPRA - [N30000028],BUIDCO,BIHAR	11/2018	12/2020 (-) [10/2022]	236.15 (-) [236.15]	80.59 (0.00) [22]	0/0
1498	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037],BUIDCO,BIHAR	12/2014	3/2020 (-) [6/2022]	225.77 (398.90) [398.90]	332.70 (173.13) [0]	0/0
1499	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016],DJB,DELHI	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	205.76 (0.00) [10]	0/0
1500	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014],DJB,DELHI	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	372.23 (0.00) [0]	0/0
1501	REHABILITATION AND UP- GRADATION OF PHASE I STP 182 MLD R2 - [N30000015],DJB,DELHI	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	136.75 (0.00) [12]	0/0
1502	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018],DJB,DELHI	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]	0/0
1503	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017],DJB,DELHI	12/2018	1/2021 (-) [3/2022]	515.07 (-) [515.07]	388.08 (0.00) [0]	0/0
1504	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034],KMDA,WEST BENGAL	8/2017	9/2022 (-) [12/2024]	307.12 (-) [307.12]	0.00 (0.00) [27]	0/0
1505	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030],KMDA,WEST BENGAL	3/2019	4/2022 (-) [12/2024]	287.53 (-) [287.53]	0.00 (0.00) [32]	0/0
1506	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045],KMDA,WEST BENGAL	8/2017	12/2021 (-) [9/2023]	185.22 (-) [185.22]	36.83 (0.00) [21]	0/0
1507	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048],KMDA,WEST BENGAL	1/2018	12/2021 (-) [9/2023]	172.10 (-) [172.10]	36.83 (0.00) [21]	0/0
1508	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032],KMDA,WEST BENGAL	5/2018	2/2022 (-) [3/2024]	198.43 (224.69) [224.69]	0.00 (26.26) [25]	0/0
1509	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (-)	274.76 (-)	238.21 (0.00)	0/0

	- [N30000046],KMDA,WEST BENGAL		[6/2022]	[274.76]	[0]	
1510	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033],KMDA,WEST BENGAL	3/2018	6/2022 (-) [3/2024]	165.16 (-) [165.16]	0.00 (0.00) [21]	0/0
1511	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031],KMDA,WEST BENGAL	12/2018	4/2022 (-) [12/2024]	234.31 (-) [234.31]	0.00 (0.00) [32]	0/0
1512	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047],KMDA,WEST BENGAL	12/2014	4/2020 (-) [6/2022]	272.32 (-) [272.32]	276.10 (0.00) [0]	0/0
1513	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N30000042],KMDA,WEST BENGAL	5/2018	2/2022 (-) [3/2024]	160.00 (154.73) [154.73]	10.35 (-5.27) [25]	0/0
1514	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029],KMDA,WEST BENGAL	1/2019	4/2022 (-) [12/2024]	384.96 (-) [384.96]	0.00 (0.00) [32]	0/0
1515	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049],KMDA,WEST BENGAL	10/2017	12/2021 (-) [9/2023]	164.93 (-) [164.93]	36.83 (0.00) [21]	0/0
1516	POLAVARAM IRRIGATION PROJECT - [N30000002],PPA,ANDHRA PRADESH	2/2009	3/2020 (3/2024) [3/2024]	10,151.04 (55,548.87) [55,548.87]	20,538.05 (45,397.83) [48]	4/19
1517	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008],UPJalNigam,UTTAR PRADESH	10/2017	3/2022 (-) [4/2024]	213.62 (261.12) [261.12]	0.00 (47.50) [25]	0/0
1518	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025],UPJalNigam,UTTAR PRADESH	3/2019	7/2021 (-) [4/2024]	298.12 (213.91) [213.91]	0.00 (-84.21) [33]	0/0
1519	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006],UPJalNigam,UTTAR PRADESH	5/2017	9/2021 (-) [12/2022]	767.59 (-) [767.59]	198.68 (0.00) [15]	0/0
1520	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021],UPJalNigam,UTTAR PRADESH	1/2019	12/2021 (-) [6/2023]	231.79 (234.03) [234.03]	28.37 (2.24) [18]	0/0
1521	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024],UPJalNigam,UTTAR PRADESH	2/2019	6/2022 (-) [4/2024]	681.78 (690.71) [690.71]	0.00 (8.93) [22]	0/0
1522	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022],UPJalNigam,UTTAR PRADESH	1/2019	10/2021 (-) [8/2022]	206.05 (-) [206.05]	110.89 (0.00) [10]	0/0
1523	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010],UPJalNigam,UTTAR PRADESH	3/2018	9/2021 (-) [9/2022]	967.23 (-) [967.23]	161.48 (0.00) [12]	0/0
1524	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH -	3/2019	8/2021 (-) [3/2024]	271.39 (-) [271.39]	0.00 (0.00) [31]	0/0

	[N30000013],UPJalNigam,UTTAR PRADESH					
1525	MATHURA SEWERAGE SCHEME - [N30000019],UPJalNigam,UTTAR PRADESH	12/2017	12/2020 (-) [6/2022]	460.45 (-) [460.45]	278.49 (0.00) [0]	0/0
1526	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004],UKJalNigam,UTTARAKHA ND	3/2017	11/2019 (-) [2/2022]	158.00 (-) [158.00]	91.30 (0.00) [0]	0/0
	Total			21,26,460.93 (6,23,756.33) [25,91,823.45]	13,60,645.94 (4,65,362.52)	2920/6021


Summary of projects in the Flash Report for the month of August, 2022

Project Implementation - Current Status:

Number of Projects in Previous Month	1505
Number of Projects completed/dropped/frozen in Current Month	15
	0
Number of Projects Added in Current Month	21
Number of Projects in Current Month	1526

Brief Analysis

Project Status with respect to Original Schedule: Out of 1526 projects, 7 projects are ahead of schedule, 265 projects are on schedule 647 projects are delayed. 489 projects do not have fixed dates of commissioning. 118 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

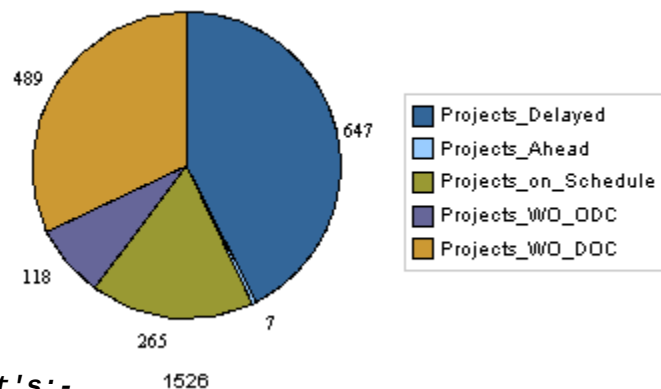


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1526 projects when sanctioned, was of the order of Rs. 2126460.93 crore but this was subsequently revised to Rs. 2591823.45 crore implying a cost overrun of 21.9%. The expenditure incurred on these projects till August, 2022 is Rs. 1360645.94 crore, which is 52.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

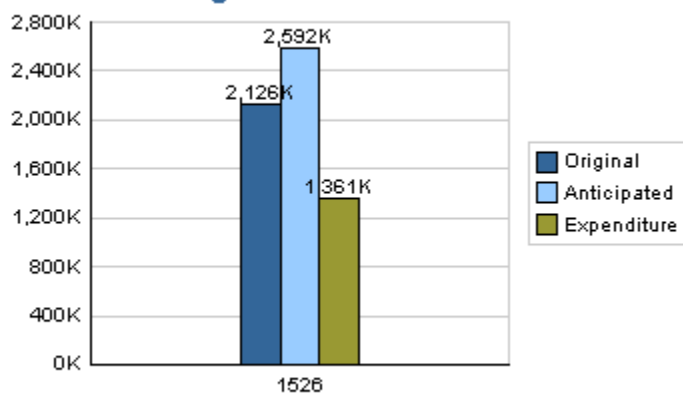

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	30

Number of Projects Without Date Of Commissioning 10

Brief Analysis

Project Status with respect to Original Schedule: Out of 41 projects, 1 project is on schedule 30 projects are delayed. 10 projects do not have fixed dates of commissioning.

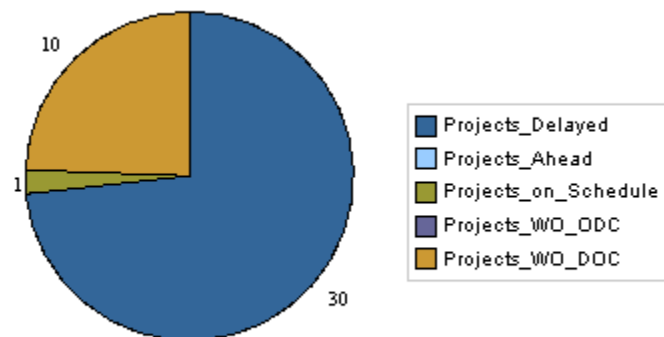


Total No Of Project's:-

41

Investment Scenario

Total original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 23466.28 crore but this was subsequently anticipated to Rs. 69354.43 crore implying a cost overrun of 195.5%. The expenditure incurred on these projects till August, 2022 is Rs. 25328.42 crore, which is 36.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

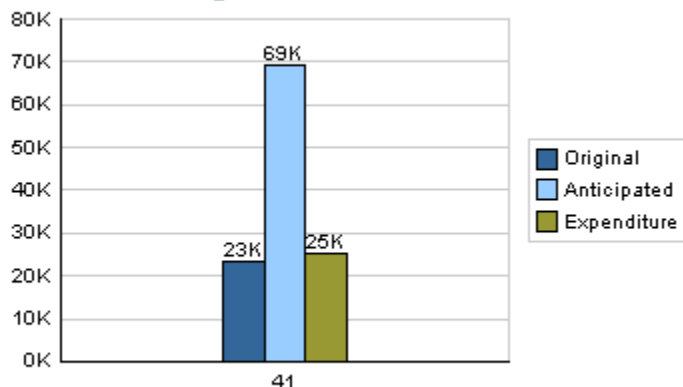

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	28
Number of Projects On Schedule	5
Number of Projects Delayed	13

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	9

Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 5 projects are on schedule 13 projects are delayed. 9 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

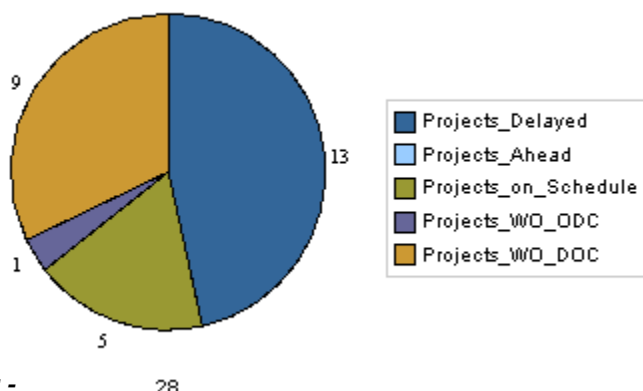


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 284811.01 crore but this was subsequently anticipated to Rs. 305228.48 crore implying a cost overrun of 7.2%. The expenditure incurred on these projects till August, 2022 is Rs. 166037.24 crore, which is 54.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

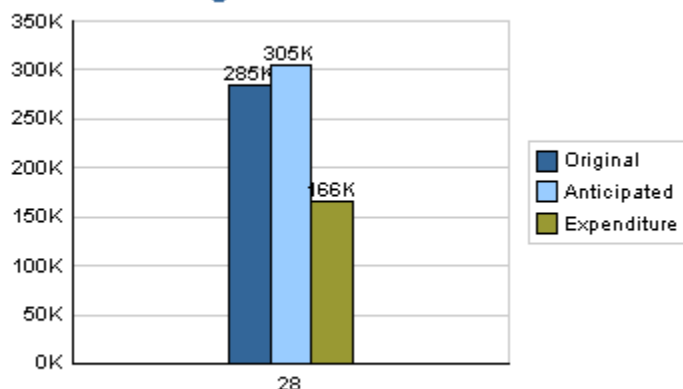

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed. 1 project does not have fixed dates of commissioning.

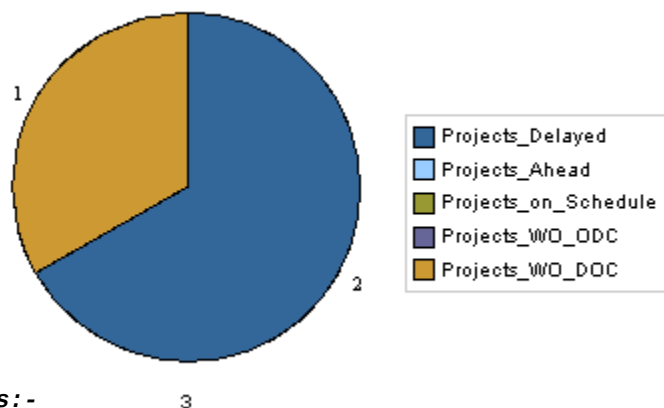


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14013.36 crore but this was subsequently anticipated to Rs. 14043.62 crore implying a cost overrun of .2%. The expenditure incurred on these projects till August, 2022 is Rs. 21826.52 crore, which is 155.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

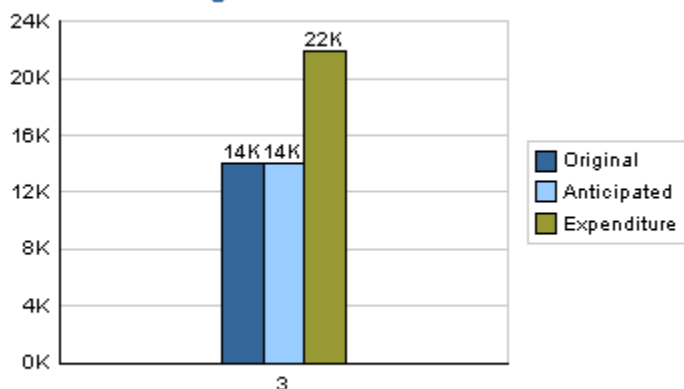

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	5
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 5 projects are on schedule 4 projects are delayed.

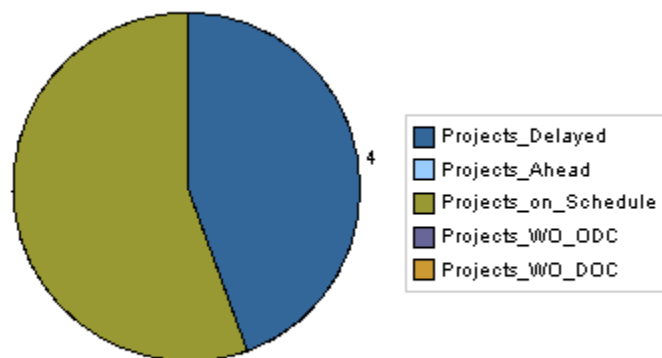


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 23919.19 crore but this was subsequently anticipated to Rs. 30334.19 crore implying a cost overrun of 26.8%. The expenditure incurred on these projects till August, 2022 is Rs. 23716.27 crore, which is 78.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

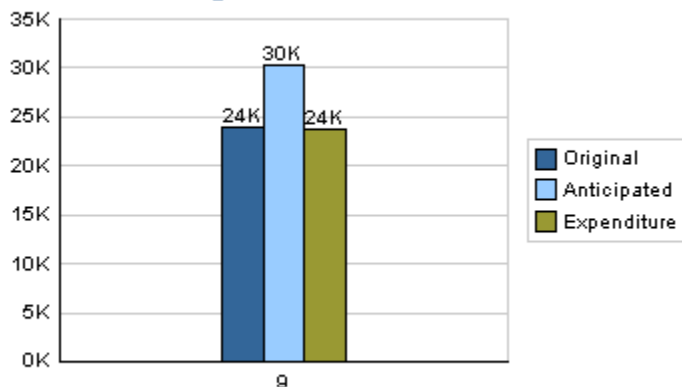

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule

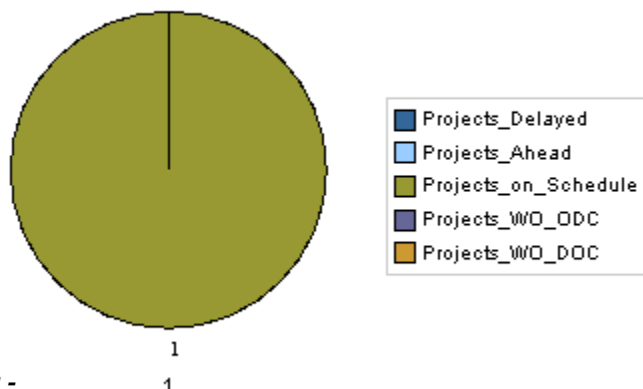


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 5369.18 crore but this was subsequently anticipated to Rs. 4633.81 cr The expenditure incurred on these projects till August, 2022 is Rs. 2160.5 crore, which is 46.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

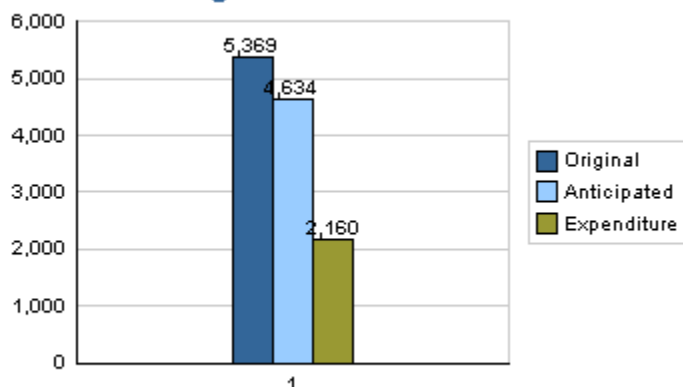

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	831
Number of Projects On Schedule	100
Number of Projects Delayed	248
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	87
Number of Projects Without Date Of Commissioning	393

Brief Analysis

Project Status with respect to Original Schedule: Out of 831 projects, 3 projects are ahead of schedule, 100 projects are on schedule 248 projects are delayed. 393 projects do not have fixed dates of commissioning. 87 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

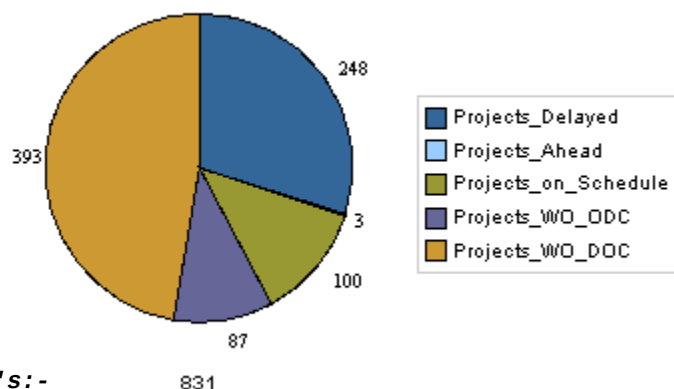

Investment Scenario

Total original cost of implementation of 831 projects when sanctioned, was of the order of Rs. 492741.89 crore but this was subsequently anticipated to Rs. 540815.51 crore implying a cost overrun of 9.8%. The expenditure incurred on these projects till August, 2022 is Rs. 321001 crore, which is 59.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

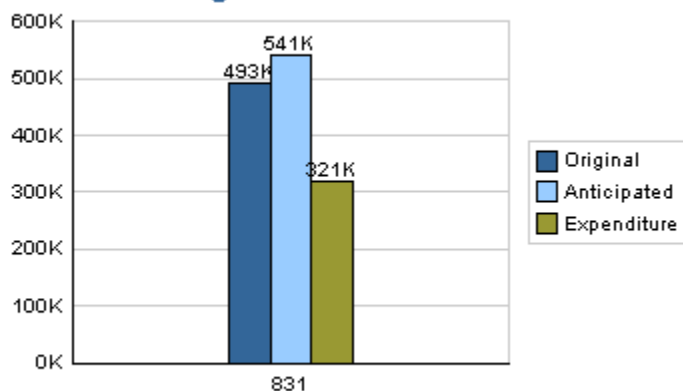

Sector wise current status of projects on the Flash Report

RENEWABLE ENERGY


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

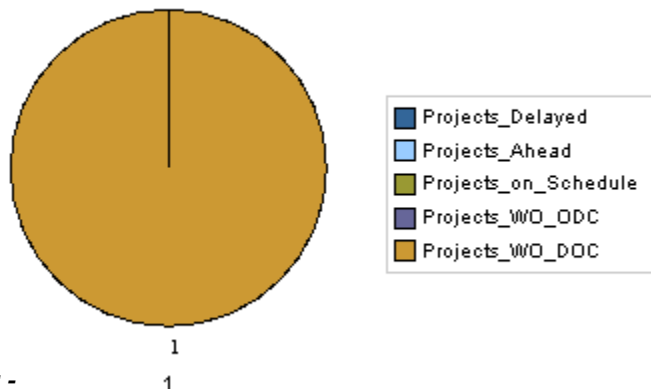


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 271.9 crore but this was subsequently anticipated to Rs. 365 crore implying a cost overrun of 34.2%. The expenditure incurred on these projects till August, 2022 is Rs. 249.96 crore, which is 68.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

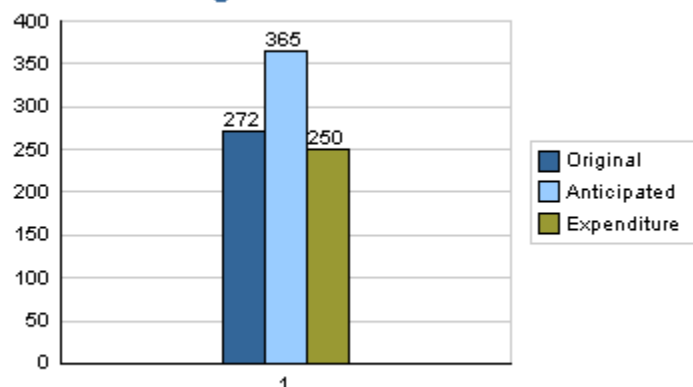

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	173
Number of Projects On Schedule	4
Number of Projects Delayed	116
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	25

Brief Analysis

Project Status with respect to Original Schedule: Out of 173 projects, 1 project is ahead of schedule, 4 projects are on schedule 116 projects are delayed. 25 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

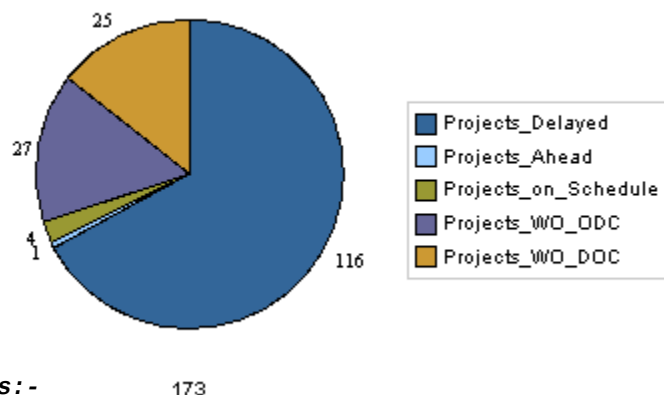


Total No Of Project's:-

173

Investment Scenario

Total original cost of implementation of 173 projects when sanctioned, was of the order of Rs. 372761.45 crore but this was subsequently anticipated to Rs. 619569.99 crore implying a cost overrun of 66.2%. The expenditure incurred on these projects till August, 2022 is Rs. 343528.75 crore, which is 55.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

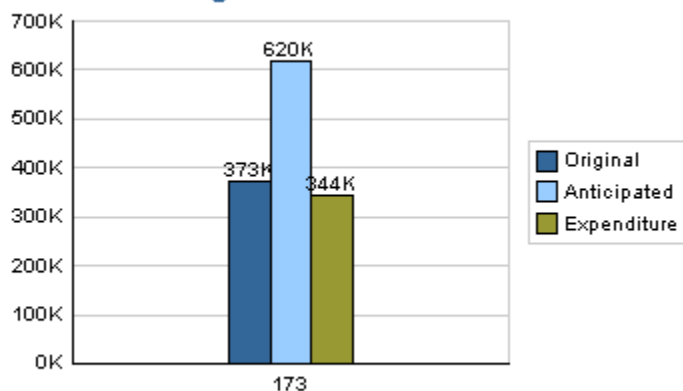

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	78
Number of Projects On Schedule	21
Number of Projects Delayed	53

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 21 projects are on schedule 53 projects are delayed. 3 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

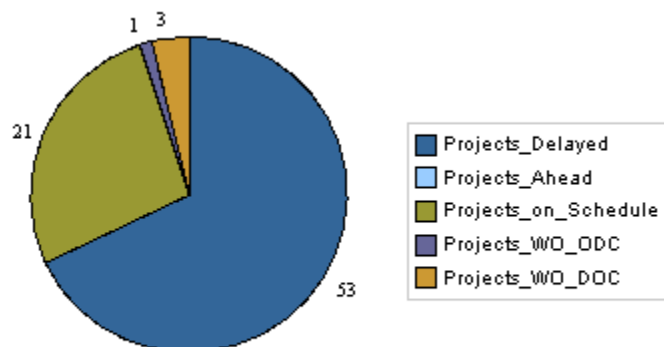


Total No Of Project's:-

78

Investment Scenario

Total original cost of implementation of 78 projects when sanctioned, was of the order of Rs. 182940.83 crore but this was subsequently anticipated to Rs. 235941.73 crore implying a cost overrun of 29%. The expenditure incurred on these projects till August, 2022 is Rs. 139404.28 crore, which is 59.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

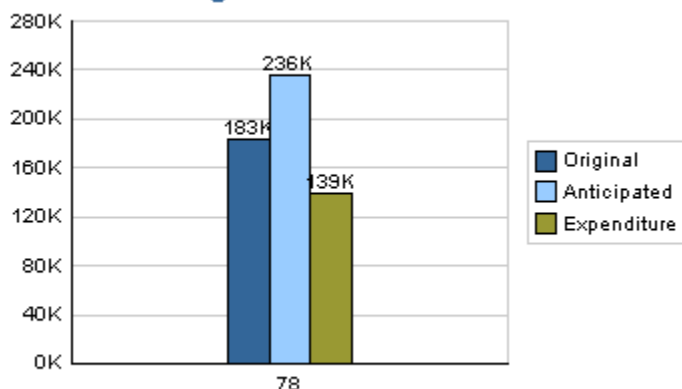

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	139
Number of Projects On Schedule	46
Number of Projects Delayed	88
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 139 projects, 1 project is ahead of schedule, 46 projects are on schedule 88 projects are delayed. 2 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

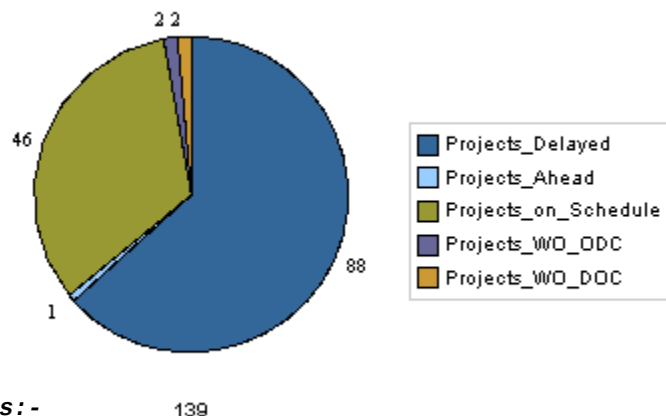


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 139 projects when sanctioned, was of the order of Rs. 366013.55 crore but this was subsequently anticipated to Rs. 386263.94 crore implying a cost overrun of 5.5%. The expenditure incurred on these projects till August, 2022 is Rs. 136450.2 crore, which is 35.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

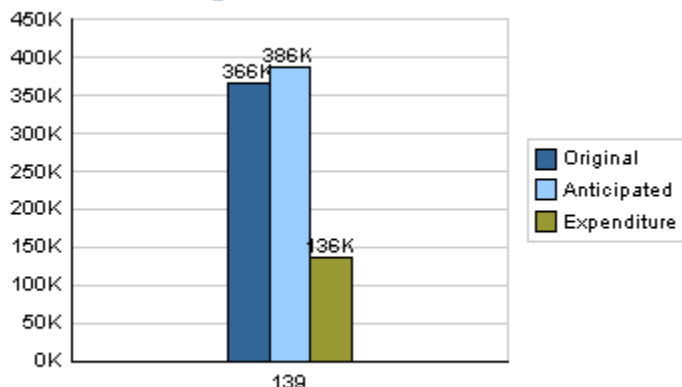

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	7
Number of Projects On Schedule	1
Number of Projects Delayed	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 1 project is on schedule 6 projects are delayed.

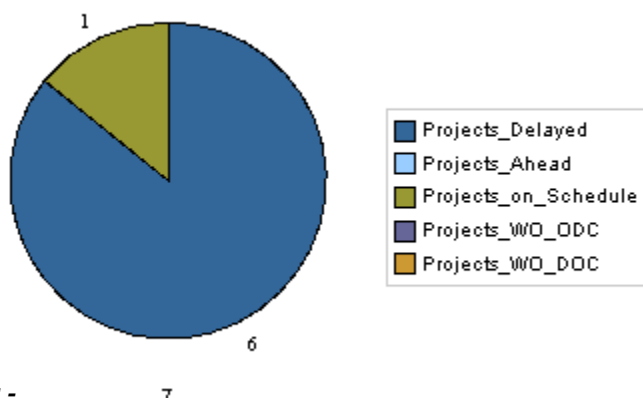


Total No Of Project's:-

7

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 7333.99 crore but this was subsequently anticipated to Rs. 8585.77 crore implying a cost overrun of 17.1%. The expenditure incurred on these projects till August, 2022 is Rs. 2634.75 crore, which is 30.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

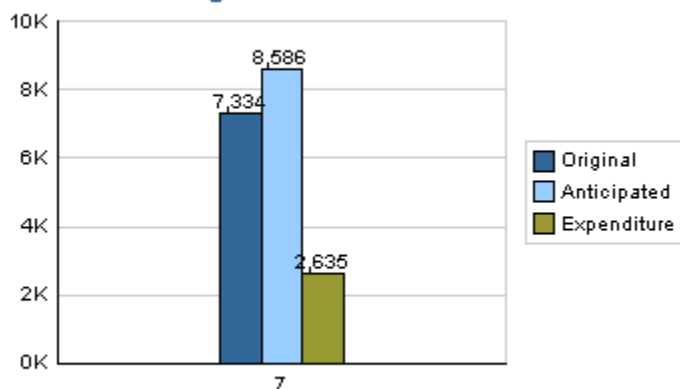

Sector wise current status of projects on the Flash Report


HOME AFFAIRS

Current Status:

Number of Projects	5
Number of Projects Delayed	5

Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 5 projects are delayed.

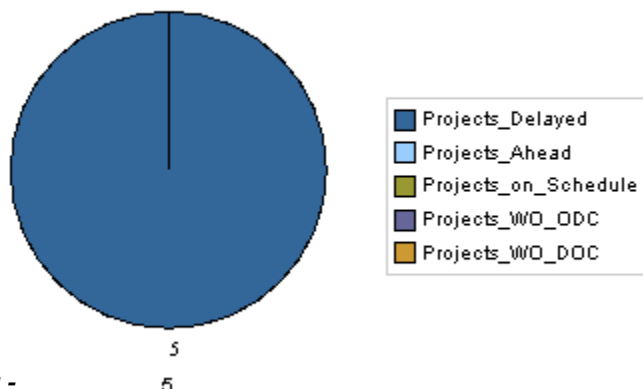

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 2025.73 crore but this was subsequently anticipated to Rs. 2546.47 crore implying a cost overrun of 25.7%. The expenditure incurred on these projects till August, 2022 is Rs. 1391.41 crore, which is 54.6% of the anticipated cost of the projects.

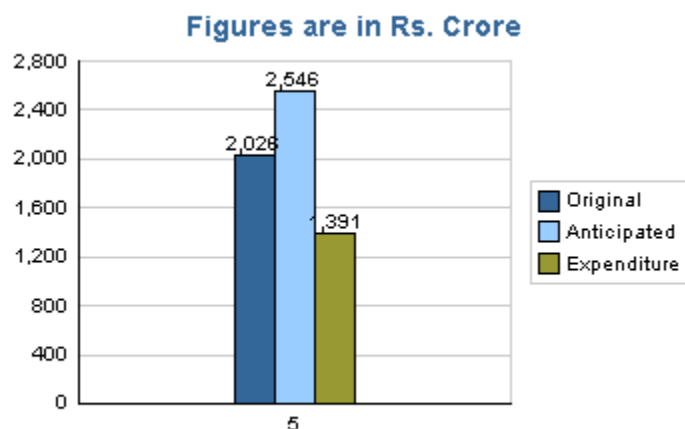

Sector wise current status of projects on the Flash Report

DEPARTMENT OF HIGHER EDUCATION


Current Status:

Number of Projects	20
Number of Projects On Schedule	2
Number of Projects Delayed	15

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 2 projects are on schedule 15 projects are delayed. 3 projects do not have fixed dates of commissioning.

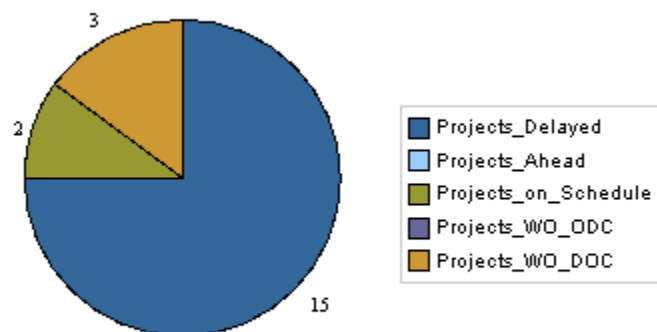


Total No Of Project's:-

20

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 9449.72 crore but this was subsequently anticipated to Rs. 9347.3 cr The expenditure incurred on these projects till August, 2022 is Rs. 4408.99 crore, which is 47.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

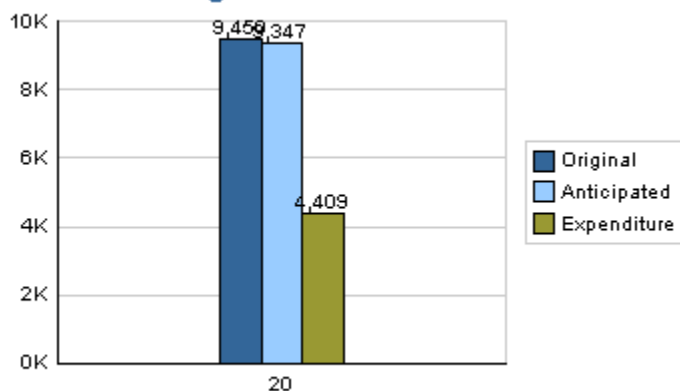


Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY

Current Status:

Brief Analysis





Total No Of Project's:-

Investment Scenario



Figures are in Rs. Crore



0

.

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	28
Number of Projects On Schedule	1
Number of Projects Delayed	1
Number of Projects Ahead	1

Number of Projects Without Date Of Commissioning 25

Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 1 project is ahead of schedule, 1 project is on schedule 1 project is delayed. 25 projects do not have fixed dates of commissioning.

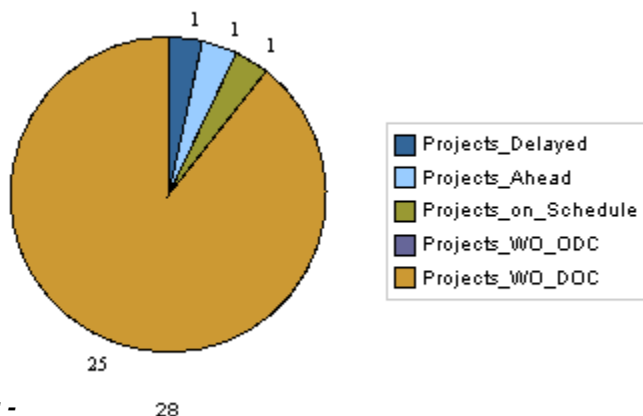


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 13696.26 crore but this was subsequently anticipated to Rs. 14200.97 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till August, 2022 is Rs. 10357.53 crore, which is 72.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

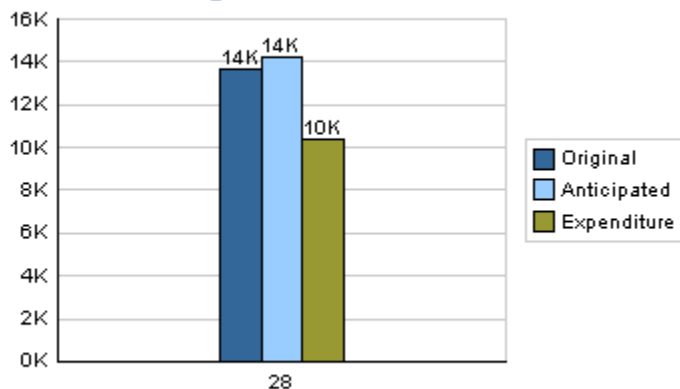

Sector wise current status of projects on the Flash Report

FINANCE

Current Status:


Number of Projects **3**

Number of Projects Delayed **1**

Number of Projects Without Date Of Commissioning **2**

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 1 project is delayed. 2 projects do not have fixed dates of commissioning.

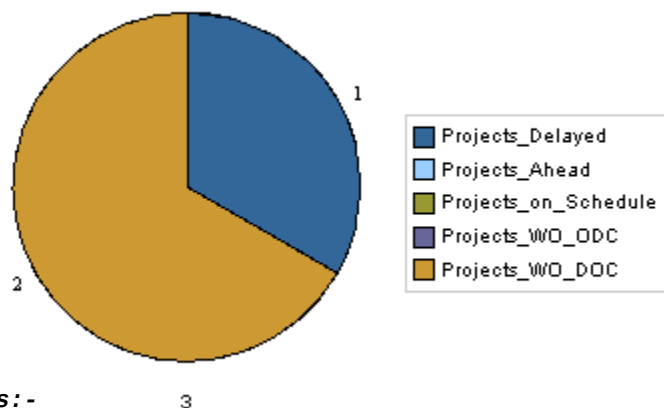


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 786.27 crore but this was subsequently anticipated to Rs. 831.04 crore implying a cost overrun of 5.7%. The expenditure incurred on these projects till August, 2022 is Rs. 662.05 crore, which is 79.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

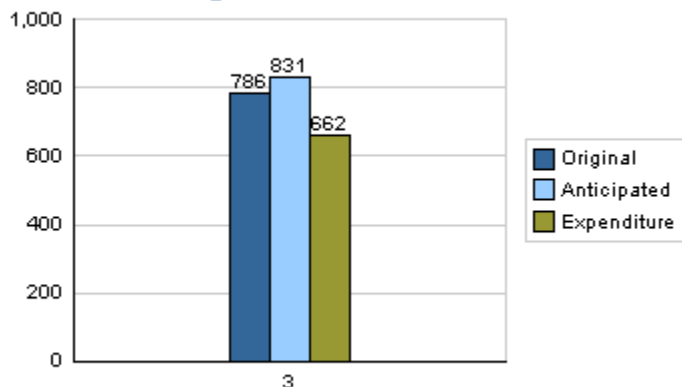

Sector wise current status of projects on the Flash Report

FERTILISERS


Current Status:

Number of Projects 1

Number of Projects Ahead 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is ahead of schedule,




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 187.27 crore but this was subsequently anticipated to Rs. 187.27 crore. The expenditure incurred on these projects till August, 2022 is Rs. .8 crore, which is .4% of the anticipated cost of the projects.

Figures are in Rs. Crore

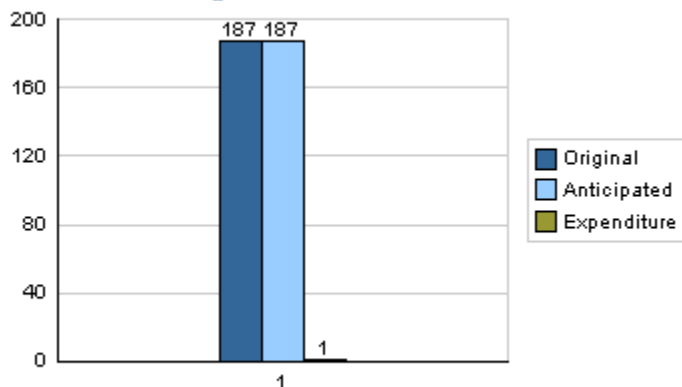

Sector wise current status of projects on the Flash Report


DPIIT

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

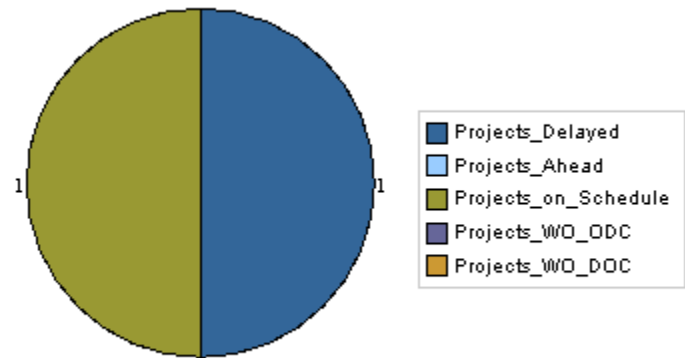


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 24857 crore but this was subsequently anticipated to Rs. 25262 crore implying a cost overrun of 1.6%. The expenditure incurred on these projects till August, 2022 is Rs. 12713.14 crore, which is 50.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

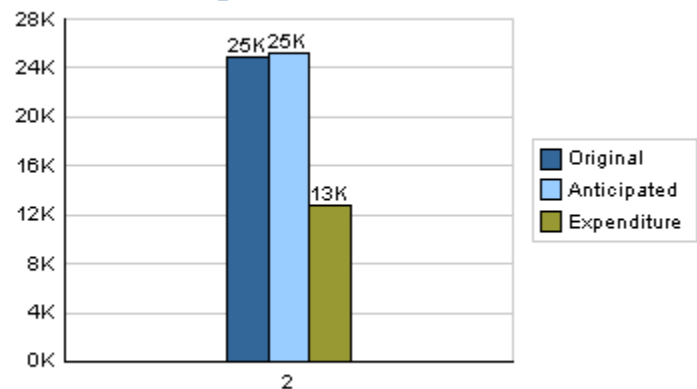

Sector wise current status of projects on the Flash Report

DONER


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 151.33 crore but this was subsequently anticipated to Rs. 151.33 crore. The expenditure incurred on these projects till August, 2022 is Rs. 148.33 crore, which is 98% of the anticipated cost of the projects.

Figures are in Rs. Crore

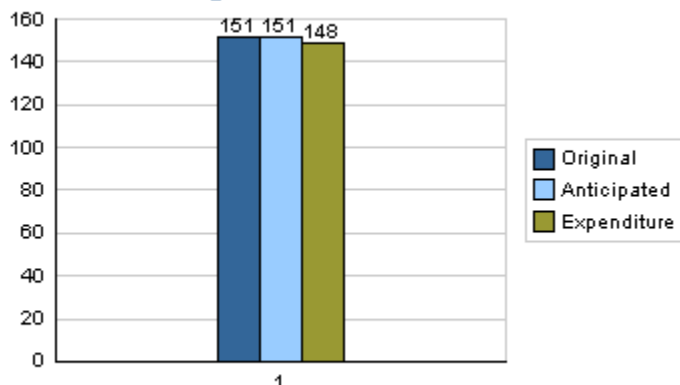

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

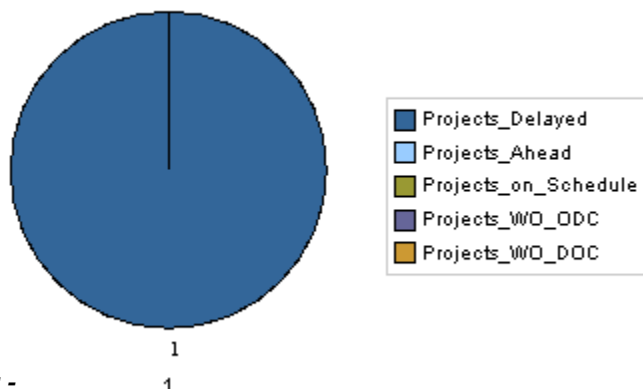


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 246.31 crore but this was subsequently anticipated to Rs. 200 cr. The expenditure incurred on these projects till August, 2022 is Rs. 181.63 crore, which is 90.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

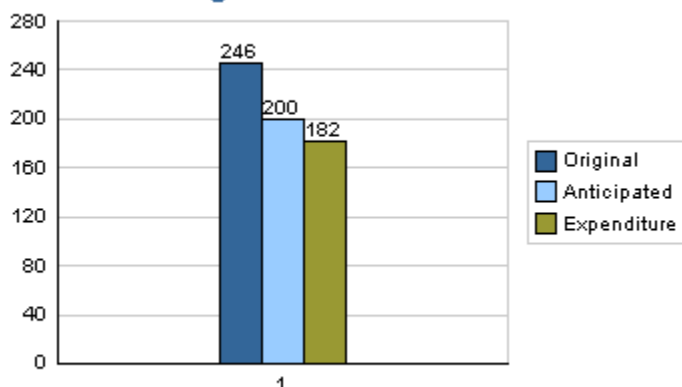

Sector wise current status of projects on the Flash Report

COMMERCE


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

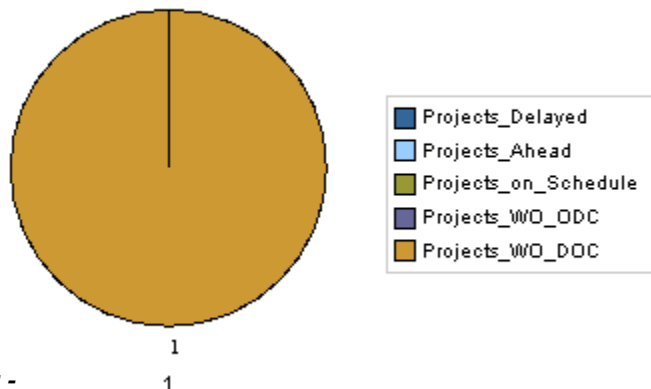


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 302.64 crore but this was subsequently anticipated to Rs. 302.64 crore. The expenditure incurred on these projects till August, 2022 is Rs. 30 crore, which is 9.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

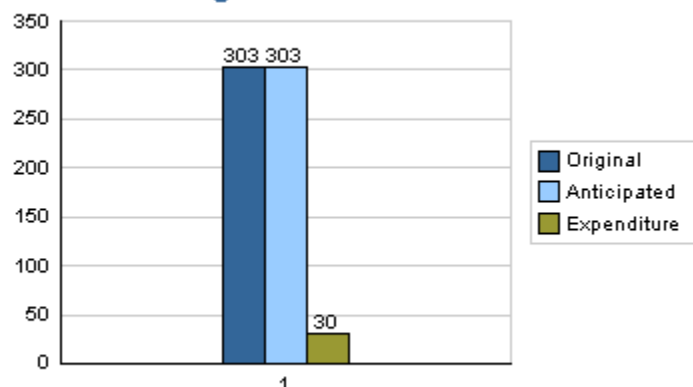

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	122
Number of Projects On Schedule	73
Number of Projects Delayed	37

Number of Projects Without Date Of Commissioning 12

Brief Analysis

Project Status with respect to Original Schedule: Out of 122 projects, 73 projects are on schedule 37 projects are delayed. 12 projects do not have fixed dates of commissioning.

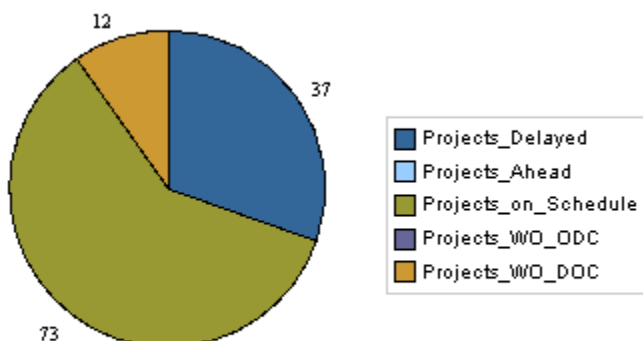


Total No Of Project's:-

122

Investment Scenario

Total original cost of implementation of 122 projects when sanctioned, was of the order of Rs. 168218.93 crore but this was subsequently anticipated to Rs. 172645.43 crore implying a cost overrun of 2.6%. The expenditure incurred on these projects till August, 2022 is Rs. 62007.26 crore, which is 35.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

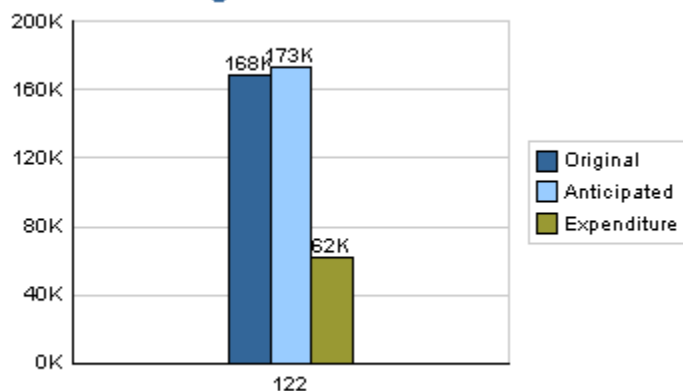

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	25
Number of Projects On Schedule	2
Number of Projects Delayed	22

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 25 projects, 2 projects are on schedule 22 projects are delayed. 1 project does not have fixed dates of commissioning.

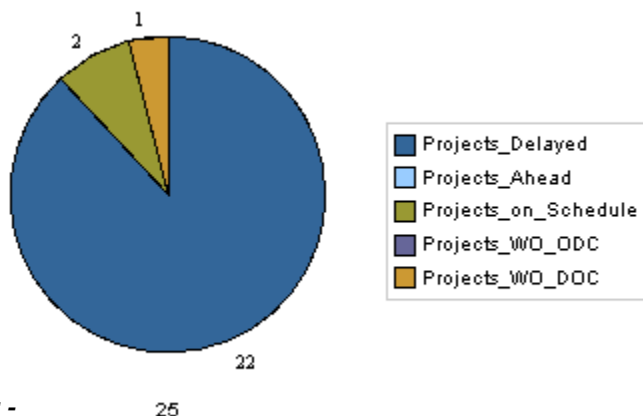


Total No Of Project's:-

25

Investment Scenario

Total original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 15984.85 crore but this was subsequently anticipated to Rs. 17572.54 crore implying a cost overrun of 9.9%. The expenditure incurred on these projects till August, 2022 is Rs. 8329.57 crore, which is 47.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

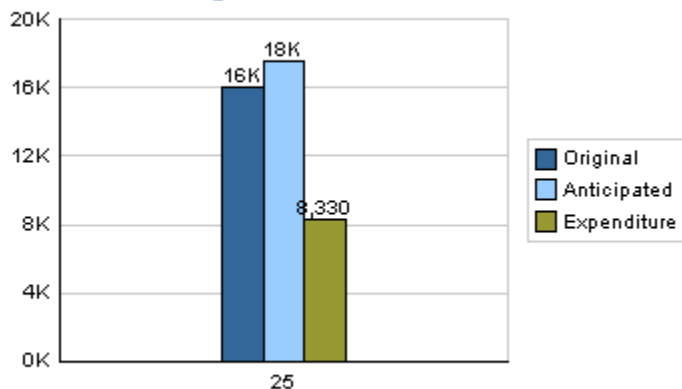

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 1 project is on schedule 4 projects are delayed.

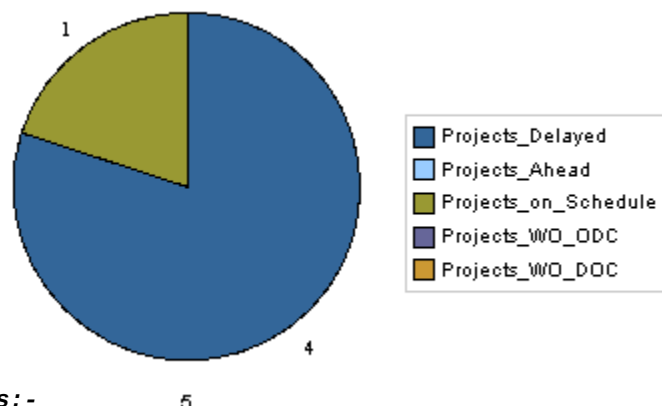


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 116741 crore but this was subsequently anticipated to Rs. 133269 crore implying a cost overrun of 14.2%. The expenditure incurred on these projects till August, 2022 is Rs. 78003.54 crore, which is 58.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

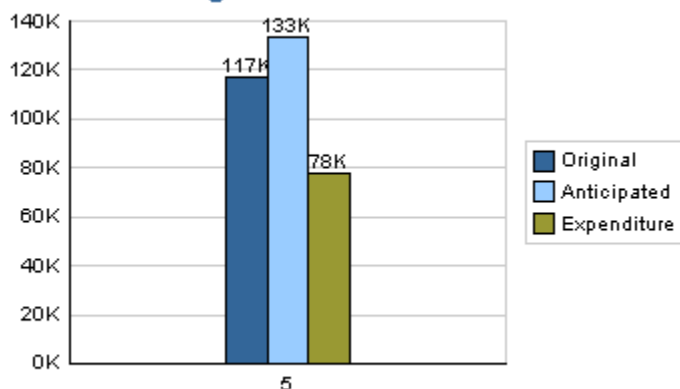

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (AUGUST 2022)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	10	3,043.24	3,314.6	1,432.33
2	ANDHRA PRADESH	66	1,12,846.32	1,64,854.74	97,257.14
3	ARUNACHAL PRADESH	42	23,572.02	37,508.36	23,290.38
4	ASSAM	50	51,277.81	61,098	16,361.51
5	BIHAR	79	97,760.92	1,21,511.7	65,888.7
6	CHHATISGARH	40	76,020.96	1,02,152	47,262.42
7	DELHI	27	81,077.58	84,083.09	54,039.03
8	GOA	11	5,588.46	5,629.5	3,153.72
9	GUJARAT	59	1,08,793.95	1,22,941.89	57,135.13
10	HARYANA	30	58,831.75	61,266.98	21,283.42
11	HIMACHAL PRADESH	19	22,091.98	33,807.28	22,910.55
12	JAMMU AND KASHMIR	27	47,696.67	82,076.18	47,435.8
13	JHARKHAND	48	73,691.13	80,705.52	38,445.33
14	KARNATAKA	50	81,951.07	90,498.98	53,790.32
15	KERALA	15	15,893.03	19,006.36	12,664.5
16	LADAKH	8	2,633.23	2,767.29	526.18
17	MADHYA PRADESH	67	60,727.92	68,770.29	33,202.42
18	MAHARASHTRA	224	1,89,111.93	2,11,359.02	1,30,828.12
19	MANIPUR	28	12,848.47	22,717.09	14,229.44
20	MEGHALAYA	13	5,093.36	12,456.56	2,252.42
21	MIZORAM	25	12,450.29	17,404.99	10,281
22	MULTI STATE	78	3,07,011.58	4,13,054.73	2,21,390.85
23	NAGALAND	37	12,630.26	17,014.38	6,392.63
24	ODISHA	79	1,15,014.68	1,24,251.75	57,753.36
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	23	17,390.42	18,541.79	7,059.05
27	RAJASTHAN	41	54,162.68	59,548.71	31,456.83
28	SIKKIM	21	14,350.32	21,030.43	6,942.65
29	TAMIL NADU	62	2,02,260.4	2,23,144.21	98,308.31
30	TELANGANA	44	32,353.76	34,700.38	21,160.74
31	TRIPURA	18	4,666.82	4,808.15	1,847.18
32	UTTAR PRADESH	93	1,24,370.16	1,39,066.47	89,797.98
33	UTTARAKHAND	29	35,446.38	54,833.8	28,776.8
34	WEST BENGAL	62	63,606.38	75,703.23	36,073.29
TOTAL		1,526	21,26,460.93	25,91,823.45	13,60,645.94

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
1	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	868.37	874.49	03/2013 -	03/2024
2	ANANTA OCP EXPANSION PH III - [N06000225]	8/2008	228.08 -	314.71	323.51	03/2012 -	-
	<u>Neyveli Lignite Corporation</u>						
3	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	7,980.79	7,457.04	12/2015 -	02/2021
	Total		6,614.72 -	9,163.87	8,655.04		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
4	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	228.52	03/2020 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>						
5	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	586.50	586.50	11/2013 -	09/2021
6	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	285.00	285.00	05/2017 -	06/2021
7	LGBRIMH-TEZPUR, ASSAM - [N21000007]	7/2012	175.57 -	179.15	179.15	12/2014 -	03/2018
8	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	586.96	586.96	03/2018 -	04/2020
10	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	171.90	02/2018 -	04/2021
11	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]	3/2018	268.84 -	284.67	269.92	- -	05/2021
12	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	182.10	05/2017 -	01/2021
	Total		2,393.88 -	2,826.24	2,789.81		
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
13	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	210.83	176.16	04/2018 -	09/2023
	Total		162.88 -	210.83	176.16		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Oil & Natural Gas Corporation Limited</u>						
14	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	2,311.32	05/2021 12/2022	12/2022
15	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	829.58	830.87	12/2020 12/2022	12/2022
	Total		3,056.38 -	3,122.04	3,142.19		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
16	DEVIKOT SOLAR 90MW - [N18000280]	3/2020	501.29 -	524.83	506.75	09/2021 01/2023	09/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						
17	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	915.31	12/2021 -	12/2022
18	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	392.30 -	392.30	397.04	12/2022 -	12/2022
	<u>Thdc India Limited</u>						
19	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	4,825.60	4,755.19	02/2016 06/2022	10/2023
	Total		3,198.92 -	6,690.62	6,574.29		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
20	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,805.17	3,140.43	03/2021 -	03/2025
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
21	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	51,219.00	31,304.00	- -	-
	<u>East Central Railways</u>						
22	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,800.00	3,787.71	- -	07/2022
23	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	4/1997	324.73 -	1,110.00	1,112.02	03/2012 -	06/2023
24	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	4/2004	372.14 -	1,700.00	1,758.02	- -	03/2024
25	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,510.00	1,547.42	- -	03/2024
26	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	1,010.00	1,038.66	03/2019 -	07/2022
	<u>East Coast Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
27	SAMBALPUR-TALCHER DOUBLING - [N22000315]	3/2011	1,111.99 -	1,539.28	1,152.38	02/2019 -	-
	<u>Eastern Railways</u>						
28	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	4/2010	365.17 -	439.30	525.35	03/2017 -	10/2022
29	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	470.90	- -	03/2023
30	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	402.48	548.37	- 09/2021	05/2022
31	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	495.10	376.37	- -	09/2022
32	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	4/2012	255.64 -	272.20	328.63	- -	12/2022
	<u>Metropolitan Rapid Transport Projects</u>						
33	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	2,980.41	1,991.80	03/2004 -	03/2023
34	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	774.51	552.70	06/2013 -	12/2022
35	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-
	<u>North East Frontier Railway</u>						
36	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	6,527.45	5,330.91	03/2014 -	12/2023
37	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	14,322.79	12,817.81	03/2011 -	12/2023
38	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,145.79	990.86	03/2019 -	03/2024
39	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	7,876.92	3,408.77	12/2015 -	12/2023
40	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	9/2006	532.87 -	2,650.00	1,255.18	03/2019 -	12/2023
41	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	401.65	342.82	- -	03/2023
42	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	4,059.65	2,380.05	03/2022 -	03/2025
	<u>North Eastern Railway</u>						
43	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	800.00	687.13	01/2019 -	-
44	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	2,000.00	1,832.40	03/2022 -	03/2022
	<u>North Western Railway</u>						
45	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	860.41	837.18	02/2019 -	06/2022
	<u>Northern Railway</u>						
46	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	686.20	12/2011 -	12/2011

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
47	NANGALDAM-TALWARA(NL),NR - [220100188	3/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024
48	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274	4/2007	336.91 -	791.39	572.99	- -	09/2023
	<u>Rail Vikas Nigam Ltd.</u>						
49	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	1,202.70 -	2,440.53	2,202.65	02/2015 -	09/2022
50	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	2/2015	760.00 -	1,536.00	1,664.15	03/2020 -	12/2022
51	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,835.83	2,340.59	12/2020 -	09/2022
52	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	2,203.53	2,075.59	12/2020 -	09/2022
53	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	1,552.26	1,445.70	03/2019 -	03/2023
54	RAIPUR - TITLAGARH - DOUBLING - [N22000411	3/2007	1,402.02 -	1,300.00	1,405.40	03/2020 -	09/2022
55	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	2,009.00	2,350.49	03/2020 -	09/2022
56	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	1/1991	2,335.67 -	3,327.72	2,712.78	12/2024 -	12/2026
57	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	2,725.00	3,066.34	03/2020 -	07/2022
58	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	1,457.79	1,408.80	03/2019 -	03/2023
59	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	4/2015	943.60 -	1,500.00	1,127.95	03/2022 -	12/2022
60	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.68	4,099.98	12/2023 -	12/2023
61	PALANPUR-SAMAKHAYALI (DL) - [N22000144	4/2013	1,548.66 -	2,538.01	2,375.23	12/2021 -	12/2022
62	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	3/2012	1,503.71 -	3,633.12	4,271.59	03/2020 -	06/2022
63	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00 -	3,300.00	2,799.96	03/2023 -	03/2023
64	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	4/2000	133.41 207.00	433.00	455.39	03/2009 03/2009	12/2022
	<u>South Central Railway</u>						
65	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	1,095.80	03/2009 -	03/2027
66	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	4/1997	1,723.00 1.00	3,421.35	2,206.22	03/2000 -	03/2023
	<u>South Eastern Railway</u>						
67	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.97	1,264.07	03/2020 -	10/2022
	<u>South Western Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
68	HUBLI- CHIKAJUR - [N22000325 <u>Southern Railway</u>	3/2015	1,156.94 -	1,954.21	1,381.52	03/2020 -	12/2022
69	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'- AGASTIYAMPALLI - [N22000079	9/2007	724.69 -	3,081.20	1,774.56	02/2019 -	03/2025
70	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	4/2011	120.70 -	2,084.48	321.37	03/2019 -	12/2027
71	MADURAI-BODINAYAKKANUR - [N22000201	4/2008	164.41 -	591.00	464.44	- 09/2022	09/2022
72	TIDIVANAM-NAGARI (NL) - [N22000085 <u>West Central Railway</u>	9/2006	582.83 -	3,500.79	622.53	- -	12/2025
73	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,658.34	03/2021 03/2024	03/2024
74	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	8/2016	582.13 -	1,247.64	704.97	03/2022 -	09/2024
75	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232 <u>Western Railway</u>	9/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025
76	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	2,448.99	2,142.58	03/2020 03/2024	03/2024
77	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435	3/2012	217.38 -	393.62	219.72	- -	03/2024
78	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	4/2011	1,037.15 -	1,394.02	1,300.17	03/2021 12/2022	12/2022
	Total		70,795.32 -	1,95,339.97	1,40,901.22		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
79	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	386.57	05/2017 06/2022	06/2022
80	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574	11/2013	683.83 -	698.82	717.89	07/2016 06/2022	06/2022
81	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	404.69	03/2018 06/2021	10/2022
82	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	322.24	312.50	09/2014 10/2022	-
83	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	3/2018	325.86 -	386.41	347.42	10/2018 04/2021	04/2021
84	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156	1/2017	166.67 -	264.34	181.38	09/2017 -	07/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	341.76	12/2015 01/2021	01/2021
86	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610	8/2016	1,742.01 -	1,742.01	1,845.15	12/2016 06/2022	05/2022
	<u>National Highways Authority Of India</u>						
87	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	10/2022
88	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	2,919.69	03/2013 -	09/2022
89	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	12/2022
90	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	3,116.66	07/2015 -	05/2022
91	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	08/2013
92	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022
93	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	3/2018	642.13 -	807.00	760.42	- -	06/2022
94	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	3/2018	478.74 -	1,135.08	905.95	- 11/2022	11/2022
95	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	9/2017	1,124.11 -	1,309.79	1,162.72	09/2017 05/2021	03/2023
96	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	1,319.54	03/2020 -	06/2022
97	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	912.41	03/2020 -	06/2022
98	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	1,309.30	03/2020 -	09/2022
99	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,405.27	1,401.96	03/2020 -	08/2022
100	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	01/2016
101	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,855.00	06/2014 -	02/2023
102	4-LANING OF BRAHAMPORE-FARAKA - [N24000203	2/2011	998.79 -	998.79	2,004.66	08/2013 -	06/2023
103	4-LANING OF FARAKA-RAIGANJ - [N24000202	2/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	03/2022
104	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	2,935.64	06/2014 -	09/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	591.00	576.99	11/2013 -	05/2022
106	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	494.33	04/2014 -	11/2022
107	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	768.92	03/2014 -	12/2022
108	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	3,287.35	05/2014 -	05/2022
109	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589	6/2016	649.00 -	649.00	724.30	06/2019 05/2022	03/2022
110	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	986.47	04/2019 -	03/2019
111	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	886.96	07/2008 -	-
112	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	8/2015	516.13 -	649.27	638.53	04/2018 -	01/2021
113	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521	8/2015	854.80 -	1,038.56	1,065.19	- 03/2022	05/2022
114	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	2,360.65	4,521.55	- -	12/2023
115	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	1/1991	642.41 -	681.67	673.94	- -	12/2022
116	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	8/2015	814.04 -	825.17	1,018.46	- -	09/2022
117	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	1,543.51	1,472.50	03/2018 03/2021	12/2022
118	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	3/2018	795.50 -	922.64	820.70	- -	04/2022
119	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	3/2018	634.70 -	925.96	823.04	- -	02/2022
120	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810	3/2018	565.09 -	565.09	713.85	- -	05/2022
121	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809	3/2018	1,550.98 -	1,550.98	1,673.32	- -	09/2022
122	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	3/2018	1,120.57 -	1,332.00	1,228.92	- -	-
123	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	2/2018	2,177.80 -	2,450.00	2,691.86	- -	09/2022
124	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	2/2018	1,995.34 -	2,400.00	3,568.04	- -	10/2022
125	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724	1/2018	895.39 -	895.39	1,369.90	- -	04/2024

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
126	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636	12/2016	1,031.95 -	1,031.95	1,518.41	- -	03/2022
127	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232	2/2019	847.00 -	847.00	908.00	03/2020 -	08/2022
128	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231	2/2019	990.97 -	990.97	1,020.00	12/2019 -	08/2022
129	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	797.00	- -	10/2022
130	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213	12/2017	1,094.97 -	1,094.97	1,097.00	- -	08/2022
131	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	689.00	- -	11/2022
132	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634	10/2016	447.75 -	447.75	1,402.07	- -	07/2022
133	REHABILITAION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633	10/2016	1,008.96 -	1,008.96	1,148.36	- -	03/2022
134	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	359.60	339.75	- 05/2017	09/2022
135	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627	11/2016	1,071.61 -	1,048.10	1,251.13	- 12/2021	09/2022
136	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,529.21	08/2019 -	06/2022
137	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	8/2016	323.72 -	355.24	327.54	08/2018 -	05/2022
138	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	8/2016	1,169.61 -	2,280.00	1,330.39	- -	05/2021
139	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594	7/2016	458.03 -	486.00	487.99	- -	06/2022
140	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	06/2022
141	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	6/2015	845.24 -	941.00	910.78	- 01/2020	01/2020
142	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019
143	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451	8/2015	505.00 -	504.00	550.48	05/2018 -	03/2022
144	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	844.08	04/2018 -	09/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
145	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	717.24	662.98	05/2018 12/2022	06/2022
146	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	777.03	766.05	05/2018 -	12/2022
147	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	558.12	08/2016 -	05/2022
148	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.53	10/2013 -	-
149	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	1,587.77	02/2013 12/2022	03/2023
150	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-
	Total		65,350.34 -	74,214.19	93,535.92		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
151	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	272.19	06/2019 06/2022	09/2022
	Total		262.87 -	262.87	272.19		
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
152	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	13,334.00	21,545.00	07/2015 -	06/2022
	Total		13,334.00 -	13,334.00	21,545.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
153	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,925.22	10,816.18	12/2018 -	09/2022
	<u>Chennai Metro Rail Ltd</u>						
154	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	2/2009	14,600.00 -	18,380.00	17,629.68	12/2015 -	-
	<u>Delhi Metro Rail Corporation</u>						
155	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	40,180.91	39,907.57	03/2016 08/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>						
156	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	6,218.14	6,065.85	07/2017 09/2020	-
	Total		69,139.79 -	77,704.27	74,419.28		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
157	SAIDPUR SEWER NETWORK PATNA - [N30000039]	4/2015	268.63 -	431.21	432.61	01/2021 -	06/2022
158	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	298.55	05/2021 -	10/2022
	<u>Kolkata Metropolitan Development Authority</u>						
159	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]	12/2014	272.32 -	272.32	276.10	04/2020 -	06/2022
	Total		818.37 -	980.95	1,007.26		
	Grand Total		2,35,127.47	3,83,849.85	3,53,018.36		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
1	AN MELT PROJECT AT RCF TROMBAY - [N08000019	5/2022	187.27	187.27	.80	09/2024	07/2024
	Total		187.27	187.27	.80		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150	3/2019	1,828.00	1,828.00	303.17	09/2025	05/2024
	Total		1,828.00	1,828.00	303.17		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 3,338.00	3,338.00	3,250.17	12/2020 02/2023	12/2022
4	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409	9/2020	18,936.00	18,936.00	1,433.13	09/2024	08/2024
	Total		21,257.00	22,274.00	4,683.30		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
5	DEVIKOT SOLAR 90MW - [N18000280	3/2020	501.29	524.83	506.75	09/2021 01/2023	09/2022
6	DEVIKOT SOLAR 150MW - [N18000281	1/2020	798.24	852.90	637.22	09/2021 11/2022	09/2022
7	ANTA SOLAR 90 MW - [N18000292	1/2021	382.22	382.22	36.61	03/2022 12/2023	03/2023
8	ETTAYAPURAM SOLAR 230MW - [N18000290	3/2020	1,316.22	1,316.22	1,059.63	09/2021 11/2022	10/2022
9	KAWAS SOLAR 56 MW - [N18000283	8/2020	261.80	293.03	243.32	10/2021 01/2023	08/2022
	Total		3,259.77	3,369.20	2,483.53		
	<u>RAILWAYS</u>						
	<u>Rail Vikas Nigam Ltd.</u>						
10	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99	6,753.42	2,374.44	12/2026	03/2025

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		2,966.99 -	6,753.42	2,374.44		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
11	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179	3/2017	217.35 -	217.35	173.98	11/2020 12/2022	09/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
12	DABOKA KATHKATI PACKAGE-2 - [N24001364	3/2021	335.88 -	335.88	70.36	01/2024 -	01/2023
13	DABOKA KATHKATI PACKAGE-4 - [N24001365	2/2021	260.07 -	260.07	109.24	12/2023 -	12/2022
14	CHURACHANPUR TUIVAI PKG-3 - [N24001405	7/2021	673.27 -	673.27	106.28	10/2023 -	08/2023
	<u>National Highways Authority Of India</u>						
15	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 04/2024	01/2024
	Total		2,219.57 -	2,219.57	459.86		
	Grand Total		31,718.60	36,631.46	10,305.10		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	6,216.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	6,216.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 - [N04000094]	3/2021	242.14 -	242.14	57.40	12/2022 -	12/2022
3	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 - [N04000098]	10/2021	446.12 -	446.12	40.91	08/2023 -	08/2023
	Total		688.26 -	688.26	98.31		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
4	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]	8/2020	7,254.37 -	7,254.37	782.87	03/2028 -	03/2028
5	SIRKA OCP - [N06000239]	5/2020	222.82 -	222.82	136.52	03/2025 -	03/2025
6	JHARKHAND LAIYO OCP - [N06000240]	8/2020	764.57 -	764.57	152.91	03/2031 -	03/2031
7	KOTRE BASANTPUR PACHMO OCP - [N06000237]	8/2020	861.06 -	861.06	137.75	03/2032 -	03/2032
8	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]	7/2021	778.80 -	778.80	508.97	03/2026 -	03/2026
9	EPR PUNDI OCP - [N06000242]	11/2020	713.35 -	713.35	233.94	03/2024 -	03/2024
10	CHANDRAGUPT OCP - [N06000238]	8/2020	973.50 -	973.50	204.84	03/2032 -	03/2032
11	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	48.22	03/2023 -	03/2023
12	EXPANSION PROJECT AMRAPALI OCP - [N06000217]	8/2020	5,136.15 -	5,136.15	331.85	03/2028 -	03/2028
13	EPR ROHINI KARKATA OCP - [N06000243]	1/2021	1,020.42 -	1,020.42	81.23	03/2025 -	03/2025
14	EXPANSION OF ASHOK OCP - [N06000247]	5/2021	2,898.28 -	2,898.28	186.45	03/2026 -	03/2026
15	EXPANSION OF KONAR OCP - [N06000245]	1/2022	799.34 -	799.34	263.19	03/2032 -	03/2032
16	EPR TAPIN SOUTH OCP - [N06000241]	11/2020	230.41 -	230.41	18.14	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
17	EXPANSION OF KARO OCP - [N06000246]	1/2022	908.47 -	908.47	99.05	03/2026 -	03/2026
	<u>Eastern Coal Fields Limited</u>						
18	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	6.04	03/2027 -	03/2027
19	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]	4/2020	1,210.12 -	1,210.12	152.04	03/2029 -	03/2029
20	MOHANPUR EXPANSION OC PHASE II - [N06000236]	11/2020	888.99 -	888.99	13.41	03/2025 -	03/2025
21	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	168.07	03/2024 -	03/2024
22	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	2.00	03/2026 -	03/2026
23	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	2.14	03/2027 -	03/2027
24	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	37.77	03/2029 -	03/2029
25	SONEPUR BAZARI EXPANSION OC - [N06000220]	7/2021	5,365.88 5,366.00	5,365.88	170.95	03/2029 -	03/2029
26	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	11.09	03/2025 -	03/2025
27	BONJEMEhari EXPANSION OCP - [N06000244]	8/2021	570.12 -	570.12	0.23	03/2025 -	03/2025
	<u>Mahanadi Coal Fields Limited</u>						
28	BALARAM EXPANSION OCP - [N06000230]	8/2020	3,504.21 -	3,504.21	620.60	03/2029 -	03/2029
29	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,803.48	03/2026 -	03/2026
30	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	934.50	03/2027 -	03/2027
31	GOPALJI-KANIHA OCP - [N06000229]	8/2020	8,416.19 -	8,416.19	1,280.15	03/2028 -	03/2028
32	BHUBANESWARI EXPANSION OCP - [N06000227]	8/2020	3,145.45 -	3,145.45	840.23	03/2031 -	03/2031
33	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,355.67	03/2029 -	03/2029
	<u>Neyveli Lignite Corporation</u>						
34	PACHWARA SOUTH COAL BLOCK - [N06000193]	7/2013	1,795.01 -	1,795.01	40.80	09/2028 -	09/2028
35	TALABIRA II AND III OCP - [N06000189]	7/2017	2,401.07 -	2,401.07	918.18	01/2027 -	01/2027
	<u>Northern Coal Fields Limited</u>						
36	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	6.55	03/2023 -	03/2023
37	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	138.51	03/2024 -	03/2024
38	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	6.16	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
39	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	36.27	03/2025 -	03/2025
	<u>Singareni Colliers Company Limited</u>						
40	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210]	11/2015	489.62 -	489.62	341.71	03/2023 -	03/2023
41	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	123.02	03/2023 -	03/2023
42	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	282.84	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
43	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,646.22	03/2023 -	03/2023
44	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
45	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
46	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	79.53	03/2026 -	03/2026
47	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	13.24	03/2023 -	03/2023
48	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	2.67	03/2026 -	03/2026
49	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,990.07	03/2029 -	03/2029
50	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	5,180.64	03/2023 -	03/2023
51	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	11.18	03/2023 -	03/2023
52	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
53	RAMPUR BATURA OC (4.0 MTY) - [N06000233]	7/2019	1,248.93 -	1,248.93	297.19	03/2026 -	03/2026
54	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
55	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	446.28	03/2029 -	03/2029
56	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	182.09	03/2024 -	03/2024
57	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	87.36	03/2026 -	03/2026
	<u>Western Coal Fields Limited</u>						
58	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
59	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
60	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226]	9/2018	313.34 -	313.34	169.46	03/2024 -	03/2024
61	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	465.37	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	BHATADI EXPANSION OC - [N06000254]	2/2020	729.86 -	729.86	149.25	03/2028 -	03/2028
63	SINGHORI DEEP OC - [N06000252]	5/2022	421.84 -	421.84	86.08	03/2029 -	03/2029
64	MAKARDHOKDA I EXPANSION OC - [N06000253]	6/2022	497.06 -	497.06	135.18	03/2026 -	03/2026
65	SAONER UG MINE I EXPANSION - [N06000251]	1/2022	253.51 -	253.51	24.86	03/2028 -	03/2028
66	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]	2/2020	1,184.33 -	1,184.33	511.36	03/2027 -	03/2027
67	ADASA UG TO OC (1.50 MTY) - [N06000219]	11/2018	333.43 -	333.43	173.40	03/2024 -	03/2024
68	TAWA III UG MINE - [N06000250]	12/2021	324.25 -	324.25	10.20	03/2027 -	03/2027
69	RPR FOR JAMUNIA UG - [N06000228]	8/2020	281.25 -	281.25	22.91	03/2026 -	03/2026
70	DHANKASA UG (RECAST) (1 MTY) - [N06000224]	2/2020	289.30 -	289.30	40.60	03/2025 -	03/2025
71	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	131.28	03/2028 -	03/2028
72	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	21.89	03/2026 -	03/2026
73	GAURI PAUNI EXPANSION OC - [N06000235]	8/2020	337.38 -	337.38	48.04	03/2029 -	03/2029
74	BHANEAGAON OC (1MTY) - [N06000221]	2/2017	409.68 -	409.68	93.68	03/2023 -	03/2023
75	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
76	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231]	11/2020	826.80 -	826.80	314.10	03/2026 -	03/2026
	Total		1,15,252.04 -	1,15,252.04	27,924.96		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Central Public Works Department</u>						
77	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL - [N42000010]	8/2021	316.25 -	316.25	-	02/2024 -	02/2024
	<u>Cpwd Of Higher Education</u>						
78	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	0.15	04/2023 -	04/2023
	Total		992.25 -	992.25	.15		
	<u>DPIIT</u>						
	<u>Dmic For Dpiit</u>						
79	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001]	9/2011	20,084.00 -	20,084.00	9,680.31	03/2027 03/2027	03/2027

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		20,084.00 -	20,084.00	9,680.31		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
80	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029	3/2019	1,404.00 -	1,404.00	667.78	09/2023 -	09/2023
	Total		1,404.00 -	1,404.00	667.78		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
81	POTTANGI BAUXITE MINES - [N10000016	5/2018	1,437.00 -	1,381.00	334.32	12/2024 12/2024	12/2024
	Total		1,437.00 -	1,381.00	334.32		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
82	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410	8/2020	697.00 -	697.00	486.80	03/2023 -	03/2023
83	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442	4/2021	1,164.69 -	1,164.69	58.88	06/2024 -	06/2024
84	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI - [N16000452	5/2022	423.39 -	423.39	36.46	03/2024 -	03/2024
	<u>Chennai Petroleum Corporation Limited</u>						
85	CBR 9 MMTPA PROJECT - [N16000434	1/2021	31,580.00 -	31,580.00	698.40	06/2025 -	06/2025
	<u>Gas Authority Of India Limited</u>						
86	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430	5/2019	8,797.00 -	8,797.00	397.00	04/2025 -	04/2025
87	60 KTA POLYPROPYLENE PROJECT - [N16000429	3/2019	910.56 -	910.56	213.00	04/2024 -	04/2024
88	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398	6/2020	7,844.25 -	7,844.25	2,903.70	05/2023 -	05/2023
	<u>Hindustan Petroleum Corporation Limited</u>						
89	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402	5/2020	1,421.46 -	1,421.46	502.70	02/2023 -	02/2023
90	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432	9/2021	160.00 -	160.00	0.13	06/2024 -	06/2024
91	BARMER PALANPUR PIPELINE - [N16000384	11/2019	776.00 -	776.00	567.76	11/2022 -	11/2022
92	NEW LPG PLANT AT VARANASI - [N16000447	8/2017	194.62 -	194.62	61.25	05/2024 -	05/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
93	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	113.39	03/2024 -	03/2024
94	BHATINDA SANGRUR PIPELINE - [N16000440]	11/2021	367.00 -	367.00	7.07	04/2024 -	04/2024
	<u>Indian Iron Steel Company</u>						
95	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI - [N16000438]	1/2022	827.00 -	827.00	63.86	07/2024 -	07/2024
	<u>Indian Oil Corporation Limited</u>						
96	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	614.47	08/2022 -	08/2022
97	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE - [N16000437]	1/2022	463.00 -	463.00	19.27	07/2025 -	07/2025
98	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	65.64	03/2030 -	03/2030
99	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI - [N16000453]	1/2022	389.00 -	389.00	-	09/2024 -	09/2024
100	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	1,266.59	01/2024 -	01/2024
101	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT - [N16000454]	1/2022	328.00 -	328.00	1.55	09/2024 -	09/2024
102	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	818.04	09/2024 -	09/2024
103	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	309.35	01/2023 -	01/2023
104	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]	12/2021	9,028.00 -	9,028.00	58.89	10/2024 -	10/2024
105	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY - [N16000446]	9/2021	378.00 -	378.00	60.31	10/2023 -	10/2023
106	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	173.85	08/2023 -	08/2023
107	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	1,472.17	05/2023 -	05/2023
108	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	441.50	12/2022 -	12/2022
109	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	49.33	10/2023 -	10/2023
110	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM - [N16000441]	3/2022	277.00 -	277.00	-	07/2026 -	07/2026
111	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	154.30	02/2028 -	02/2028
112	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE - [N16000451]	3/2022	564.00 -	564.00	-	11/2024 -	11/2024
113	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	234.49	03/2030 -	03/2030
	<u>Indradhanush Gas Grid Ltd</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
114	NORTH EAST GAS GRID - [N16000439]	11/2020	9,265.00 -	9,265.00	2,431.15	03/2024 03/2024	03/2024
	<u>Numaligarh Refinery Limited</u>						
115	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	18,968.00	1,929.71	10/2024 -	10/2024
116	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	3,273.73	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
117	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	848.08	03/2023 03/2022	03/2023
118	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	212.55	03/2025 -	03/2025
119	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD - [N16000444]	1/2022	621.40 -	621.40	72.69	11/2024 -	11/2024
120	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) - [N16000445]	11/2019	431.00 -	431.00	29.95	01/2024 -	01/2024
121	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON - [N16000433]	8/2021	218.38 -	218.38	35.16	02/2023 -	02/2023
122	PIPELINE REPLACEMENT PROJECT - VII - [N16000436]	1/2022	3,183.58 -	3,183.58	123.40	05/2024 -	05/2024
123	CREATION OF GAS DEHYDRATION FACILITIES - [N16000443]	3/2022	209.33 -	209.33	-	05/2024 -	05/2024
124	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]	8/2021	885.63 -	885.63	231.36	02/2026 -	02/2026
125	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	915.64	03/2026 -	03/2026
	<u>Oil India Limited</u>						
126	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT - [N16000449]	6/2021	860.00 -	860.00	20.10	12/2024 -	12/2024
127	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION, PROCESSING - [N16000450]	12/2020	430.76 -	430.76	8.66	07/2024 -	07/2024
	Total		1,71,748.91 -	1,77,495.43	21,982.33		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
128	RATLE HE PROJECT - [N18000324]	2/2021	5,281.94 -	5,281.94	43.55	02/2026 02/2026	02/2026
	<u>National Thermal Power Corporation</u>						
129	DAYAPAR WIND ENERGY PROJECT 150MW - [N18000319]	11/2021	937.80 -	937.80	102.21	05/2023 -	05/2023
	<u>Power Grid Corporation Of India Limited</u>						
130	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]	3/2021	1,340.81 -	1,340.81	626.81	12/2022 -	12/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
131	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316]	5/2021	576.42 -	576.42	54.00	03/2023 -	03/2023
132	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM - [N18000330]	3/2022	288.71 -	288.71	-	12/2024 -	12/2024
133	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. - [N18000329]	3/2022	176.22 -	176.22	2.28	03/2023 -	03/2023
134	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000331]	2/2022	359.47 -	359.47	9.29	09/2023 -	09/2023
135	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B - [N18000337]	7/2022	4,546.26 -	4,546.26	21.50	06/2023 -	06/2023
136	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C - [N18000338]	7/2022	186.19 -	186.19	-	03/2025 -	03/2025
137	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332]	5/2022	1,666.00 -	1,666.00	-	11/2023 -	11/2023
138	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299]	5/2021	179.29 -	179.29	79.99	04/2023 -	04/2023
139	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327]	3/2019	1,326.00 -	1,326.00	1,054.46	03/2023 -	03/2023
140	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM - [N18000328]	2/2022	318.12 -	318.12	45.42	04/2025 -	04/2025
	<u>Satluj Jal Vidyut Nigam Limited</u>						
141	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	5,935.72	01/2024 -	01/2024
142	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	285.25	11/2025 -	11/2025
143	GUJRAI SOLAR POWER PROJECT - [N18000336]	6/2022	279.94 -	279.94	28.39	08/2023 -	08/2023
144	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	810.74	01/2026 -	01/2026
145	GURHAH SOLAR POWER PROJECT - [N18000334]	5/2022	466.82 -	466.82	42.58	08/2023 -	08/2023
146	BIKANER SOLAR POWER PROJECT - [N18000335]	4/2022	5,491.89 532.00	6,023.89	791.28	05/2024 -	05/2024
147	Bagodara Solar Power Project - [N18000297]	5/2021	339.35 -	339.35	45.45	10/2022 -	10/2022
148	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	392.30 -	392.30	397.04	12/2022 -	12/2022
	Total		37,091.15 -	37,623.15	10,375.96		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
149	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	4,670.00	2,229.23	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
150	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00 -	3,300.00	2,799.96	03/2023 -	03/2023
151	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501	6/2016	3,677.76 -	3,677.76	3,492.37	12/2023 -	12/2023
152	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.68	4,099.98	12/2023 -	12/2023
	Total		12,678.49 -	15,196.44	12,621.54		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
153	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	174.77	12/2022 -	12/2022
154	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294	3/2019	560.39 -	560.39	307.44	03/2027 -	03/2027
155	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297	3/2019	450.65 -	450.65	117.78	03/2027 -	03/2027
156	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291	3/2019	421.48 -	421.48	147.23	03/2027 -	03/2027
157	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR - [N24001454	2/2022	184.15 -	184.15	-	08/2022 -	08/2022
158	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290	3/2019	342.55 -	342.55	264.65	03/2027 -	03/2027
159	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293	3/2019	486.70 -	486.70	201.16	03/2027 -	03/2027
160	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292	3/2019	543.05 -	543.05	241.22	03/2027 -	03/2027
161	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375	6/2020	496.47 -	496.47	32.23	03/2027 -	03/2027
162	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408	2/2021	925.47 -	925.47	2.54	07/2025 -	07/2025
163	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	236.18	107.81	12/2022 -	12/2022
164	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC - [N24001373	1/2020	358.26 -	358.26	141.82	02/2024 -	02/2024
165	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376	3/2021	182.55 -	182.55	24.82	03/2027 -	03/2027

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
166	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K - [N24001447	8/2020	371.93 -	371.93	-	12/2024 -	12/2024
167	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) - [N24001442	10/2021	385.15 -	385.15	8.95	05/2024 -	05/2024
168	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374	6/2020	437.60 -	437.60	41.92	03/2027 -	03/2027
169	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372	2/2021	588.09 -	588.09	176.69	03/2024 -	03/2024
170	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT - [N24001427	6/2020	166.21 -	166.21	53.63	04/2023 -	04/2023
171	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289	3/2019	403.68 -	403.68	224.20	03/2027 -	03/2027
172	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295	3/2019	347.78 -	347.78	223.07	03/2027 -	03/2027
173	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421	7/2018	1,948.25 -	1,948.25	509.41	02/2024 -	02/2024
174	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 - [N24001455	2/2022	191.33 -	191.33	-	08/2022 -	08/2022
175	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296	3/2019	394.27 -	394.27	158.24	03/2027 -	03/2027
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
176	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	550.00	12/2023 -	12/2023
177	KARGIL-ZANSKR PACKAGE-7 - [N24001347	1/2021	308.86 -	308.86	80.00	06/2024 -	06/2024
178	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334	11/2020	445.51 -	445.51	175.18	12/2023 -	12/2023
179	MARIAM - PEREN (PKG 2A) - [N24001398	7/2021	204.58 -	204.58	68.82	03/2023 -	03/2023
180	KHELLANI-KHANABAL PKG-5 - [N24001396	7/2021	497.09 -	497.09	25.62	02/2023 -	02/2023
181	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 - [N24001452	4/2022	170.95 -	170.95	-	07/2024 -	07/2024
182	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333	9/2019	761.54 -	761.54	256.92	05/2023 -	05/2023
183	TLABUNG - LUNGLEI PKG-A - [N24001358	3/2021	698.44 -	698.44	36.21	12/2022 -	12/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
184	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277	9/2020	275.02 -	275.02	60.68	10/2022 -	10/2022
185	DABOKA KATHKATI PACKAGE-6 - [N24001450	9/2021	625.64 -	625.64	-	07/2024 -	07/2024
186	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328	12/2020	804.00 -	804.00	188.31	08/2023 -	08/2023
187	KHELLANI-KHANABAL PKG-6 - [N24001324	2/2021	285.28 -	285.28	70.27	09/2022 -	09/2022
188	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261	8/2020	311.00 -	311.00	50.95	04/2023 -	04/2023
189	KARGIL-ZANSKR PACKAGE-3 - [N24001345	8/2020	381.01 -	381.01	16.77	01/2023 -	01/2023
190	TAMENGLONG - MAHUR PKG-4 - [N24001404	7/2021	198.77 -	198.77	16.45	03/2023 -	03/2023
191	KEIFANG - TUVAI PKG-1 - [N24001440	9/2021	492.94 -	492.94	19.53	05/2023 -	05/2023
192	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	52.00	12/2022 -	12/2022
193	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326	11/2020	4,997.04 -	4,997.04	364.26	09/2028 -	09/2028
194	TAMENGLONG - MAHUR PKG-6 - [N24001437	9/2021	311.18 -	311.18	22.84	05/2023 -	05/2023
195	KHELLANI-KHANABAL PKG-2 - [N24001394	7/2021	512.43 -	512.43	9.78	02/2023 -	02/2023
196	DEMBUEN - BRUNI - [N24001321	12/2020	606.63 -	606.63	167.37	03/2023 -	03/2023
197	KHELLANI-KHANABAL PKG-1 - [N24001323	3/2021	486.45 -	486.45	15.88	09/2022 -	09/2022
198	KARGIL-ZANSKR PACKAGE-2 - [N24001344	3/2021	404.89 -	404.89	1.98	01/2023 -	01/2023
199	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357	3/2021	674.71 -	674.71	163.89	06/2023 -	06/2023
200	TAMENGLONG - MAHUR PKG-5 - [N24001436	8/2021	477.86 -	477.86	14.26	05/2023 -	05/2023
201	MARIAM - PEREN PKG-2B - [N24001351	2/2021	232.26 -	232.26	27.58	12/2022 -	12/2022
202	JOGIGHOPA BRIDGE - [N24001434	8/2021	746.76 -	746.76	9.76	11/2024 -	11/2024
203	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356	3/2021	233.25 -	233.25	52.09	12/2022 -	12/2022
204	KARGIL-ZANSKR PACKAGE-1 - [N24001343	3/2021	384.23 -	384.23	21.95	01/2023 -	01/2023
205	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
206	REHABILITATION OF SECTION FROM KM 298.00 TO KM 330.662 PKG-8 - [N24001433	4/2021	154.61 -	154.61	-	07/2023 -	07/2023
207	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360	3/2021	260.21 -	260.21	87.95	12/2022 -	12/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
208	DABOKA KATHKATI PACKAGE-5 - [N24001366]	3/2021	288.85 -	288.85	8.28	01/2023 -	01/2023
209	SENAPATI- IMPHAL PKG-5B - [N24001400]	3/2021	211.70 -	211.70	-	01/2023 -	01/2023
210	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	21.30	12/2022 -	12/2022
211	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	327.61	12/2023 -	12/2023
212	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 - [N24001451]	3/2022	215.27 -	215.27	-	07/2024 -	07/2024
213	TAMENGLONG - MAHUR PKG-1 - [N24001402]	7/2021	185.80 -	185.80	14.79	03/2023 -	03/2023
214	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	129.85	12/2022 -	12/2022
215	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	28.25	01/2023 -	01/2023
216	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]	7/2021	258.52 -	258.52	52.94	03/2023 -	03/2023
217	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	19.69	09/2023 -	09/2023
218	MERANGKONG-TAMLU-MON (MTM) PKG-5 - [N24001438]	7/2021	161.73 -	161.73	11.38	12/2023 -	12/2023
219	KHELLANI-KHANABAL PKG-4 - [N24001395]	7/2021	859.67 -	859.67	25.50	08/2023 -	08/2023
220	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]	7/2020	345.38 -	345.38	115.75	04/2023 -	04/2023
221	IMPHAL - KHONGSANG PKG-4 - [N24001453]	8/2021	579.63 -	579.63	-	12/2023 -	12/2023
222	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	678.90	09/2026 -	09/2026
223	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	410.60	21.94	02/2024 02/2024	02/2024
224	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	81.30	05/2024 -	05/2024
225	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	33.38	01/2023 -	01/2023
226	IMPHAL - MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	112.33	12/2022 -	12/2022
227	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	24.74	12/2022 -	12/2022
228	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	103.72	12/2023 -	12/2023
229	GOHA-KHELLANI PKG-3 - [N24001397]	2/2021	431.28 -	431.28	43.78	03/2023 -	03/2023
230	PEREN-DIMAPUR PKG-5 - [N24001407]	2/2021	207.33 -	207.33	-	03/2023 -	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
231	IMPHAL – MOREH (PACKAGE 4) - [N24001399]	3/2021	277.99 -	277.99	46.79	01/2023 -	01/2023
232	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	24.72	12/2022 -	12/2022
233	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	84.58	04/2023 -	04/2023
234	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	24.48	03/2023 -	03/2023
235	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	45.41	12/2022 -	12/2022
236	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	13.88	12/2022 -	12/2022
237	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	171.79	12/2023 -	12/2023
238	TAMENGLONG - MAHUR PKG-2 - [N24001403]	7/2021	483.87 -	483.87	58.46	03/2023 -	03/2023
239	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]	3/2021	260.40 -	260.40	8.26	12/2022 -	12/2022
240	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]	11/2020	284.21 -	284.21	44.52	12/2023 -	12/2023
	<u>National Highways Authority Of India</u>						
241	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 - [N24001432]	12/2021	300.00 -	300.00	29.81	08/2024 -	08/2024
242	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
243	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
244	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 - [N24001443]	5/2020	690.30 -	690.30	62.72	03/2024 -	03/2024
245	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB - [N24001445]	5/2020	691.52 -	691.52	113.57	07/2023 -	07/2023
246	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
247	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
248	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420]	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
249	DEVELOPMENT OF MULTIMODAL LOGISTICS PARK AT BANGALORE AND EXTERNAL CONNECTIVITY TO THE MULTI MODEL L - [N24001449]	6/2022	1,769.70 -	1,769.70	4.20	03/2025 -	03/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
250	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION - [N24001444	5/2020	882.00 -	882.00	0.02	01/2024 -	01/2024
251	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 04/2024	01/2024
252	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAGE - [N24001446	5/2020	894.00 -	894.00	213.55	12/2023 -	12/2023
	Total		59,917.38 -	59,955.89	8,589.07		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
253	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	2,160.50	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	2,160.50		
	<u>SOCIAL JUSTICE</u>						
	<u>Central Public Works Department</u>						
254	CENTRE FOR DISABILITY SPORTS - [N38000001	2/2019	170.99 -	170.99	73.80	03/2024 -	03/2024
	Total		170.99 -	170.99	73.80		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
255	SCREENING PLANT-III AT KIRANDUL - [N12000127	3/2021	2,092.97 -	2,092.97	396.60	08/2024 -	08/2024
	<u>Steel Authority Of India Limited (Sail)</u>						
256	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	123.14	12/2023 -	12/2023
257	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	128.30	05/2023 -	05/2023
258	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125	1/2022	970.18 -	970.18	76.33	05/2025 -	05/2025
259	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT - [N12000126	2/2022	207.74 -	207.74	8.71	06/2024 -	06/2024
	Total		4,190.31 -	4,190.31	733.08		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
260	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	763.91	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Bangalore Metro Rail Corporation Limited</u>						
261	BANGALORE METRO RAIL PROJECT LIMITED, PHASE. 2A AND 2B - [N28000151]	6/2021	14,788.10 -	14,788.10	2,942.84	06/2026 -	06/2026
	<u>Central Public Works Department</u>						
262	CONSTRUCTION OF NEW NACIN CAMPUS, PALASAMIDRAM, ANDHRA PRADESH - [N28000152]	2/2022	702.47 -	702.47	1.16	08/2024 -	08/2024
	<u>National Capital Region Transport Corp</u>						
263	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	9,900.05	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
264	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,925.50	437.20	06/2024 -	06/2024
	Total		64,514.51 -	65,074.24	14,045.16		
	<u>WATER RESOURCES</u>						
	<u>Delhi Jal Board</u>						
265	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	372.23	12/2022 -	12/2022
	Total		665.78 -	665.78	372.23		
	Grand Total		5,45,825.25	5,54,428.59	1,15,875.50		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	7,500.00	6,433.54	09/2010 -	09/2024	114.78
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	19,220.00	18,523.00	12/2015 -	06/2023	67.73
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	14,876.00	12/2016 -	12/2023	38.63
	Total		27,271.00 -	43,799.00	39,832.54			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 -	707.73	570.11	09/2018 -	10/2022	69.63
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]	11/2016	303.80 -	351.21	247.98	04/2020 -	12/2022	15.61
6	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 -	2,445.00	797.96	09/2021 -	09/2023	76.79
7	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	192.21	09/2021 -	12/2023	38.72
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	426.51	03/2021 -	03/2025	7.88
	Total		3,592.30 -	5,216.27	2,234.77			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
9	MADHUBAND NLW WASHERY - [N06000126]	08/2010	289.45 -	302.00	296.38	05/2014 -	09/2022	4.34
10	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	44.58	04/2018 -	06/2023	37.56
11	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	139.20	03/2017 -	12/2022	12.20
	<u>Eastern Coal Fields Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	648.15	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>							
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	868.37	874.49	03/2013 -	03/2024	81.09
14	ANANTA OCP EXPANSION PH III - [N06000225]	08/2008	228.08 -	314.71	323.51	03/2012 -	-	37.98
	<u>Neyveli Lignite Corporation</u>							
15	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,457.04	12/2015 -	02/2021	35.10
16	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	13,965.29	11/2021 -	11/2023	.00
	Total		27,350.03 -	32,525.64	23,748.64			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
17	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]	05/2019	303.90 -	334.45	140.00	03/2020 -	02/2023	10.05
	Total		303.90 -	334.45	140.00			
	<u>DPIIT</u>							
	<u>Iicc For Dpiit</u>							
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	3,032.83	12/2019 -	01/2023	8.49
	Total		4,773.00 -	5,178.00	3,032.83			
	<u>FINANCE</u>							
	<u>Cpwd For Finance</u>							
19	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE- IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	262.00	208.93	10/2019 -	10/2022	25.36
	Total		209.00 -	262.00	208.93			
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	586.50	586.50	11/2013 -	09/2021	41.63
21	LGBRIMH-TEZPUR, ASSAM - [N21000007]	07/2012	175.57 -	179.15	179.15	12/2014 -	03/2018	2.04

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
22	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	285.00	285.00	05/2017 -	06/2021	39.41
23	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68
24	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	182.10	05/2017 -	01/2021	13.20
25	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	586.96	586.96	03/2018 -	04/2020	16.10
26	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	171.90	02/2018 -	04/2021	16.33
27	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	12/2021	1.64
28	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	280.00	268.59	03/2019 -	02/2021	2.87
29	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	205.00	145.94	- -	01/2022	30.94
30	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]	03/2018	268.84 -	284.67	269.92	- -	05/2021	5.89
31	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	244.64	- -	05/2021	.02
	<u>Nbcc For Health</u>							
32	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.04	1,162.76	09/2021 -	08/2022	8.89
	Total		4,456.80 -	5,069.51	4,608.14			
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
33	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,679.02	1,036.04	10/2019 -	12/2022	37.71
34	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	210.83	176.16	04/2018 -	09/2023	29.44
35	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI [N45000002]	06/2019	277.35 -	290.33	63.23	07/2022 -	06/2023	4.68
	Total		1,659.44 -	2,180.18	1,275.43			
	<u>MINES</u>							
	<u>National Aluminum Company Limited (Nalco)</u>							
36	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	4,103.00 5,055.00	5,055.00	1,486.31	04/2021 -	01/2024	23.20

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
37	UTKAL D AND E COAL BLOCK - [N10000011]	05/2016	534.00 -	667.23	497.21	01/2020 -	11/2023	24.95
38	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	581.00	96.18	11/2020 -	12/2023	63.66
	Total		4,992.00 -	6,303.23	2,079.70			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
39	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.51	02/2017 -	09/2022	117.11
40	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	972.00	06/2019 -	02/2023	35.54
	<u>Gas Authority Of India Limited</u>							
41	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	03/2017	1,933.00 -	2,105.70	1,811.30	12/2020 -	11/2022	8.93
42	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,570.80	12/2012 -	02/2025	102.71
43	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 -	247.90	154.74	02/2021 -	10/2022	9.91
44	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	255.10	08/2020 -	12/2022	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
45	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	20,025.46	07/2020 -	03/2023	25.50
46	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,185.00	2,943.70	06/2021 -	08/2022	18.98
	<u>Indian Oil Corporation Limited</u>							
47	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	684.72	10/2017 -	12/2022	103.60
48	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,446.06	03/2021 -	10/2022	66.09
49	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	3,250.17	12/2020 -	12/2022	43.82
50	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	05/2016	1,945.00 -	2,145.00	1,801.97	02/2022 -	12/2022	10.28
51	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	4,938.92	12/2018 -	11/2023	33.98

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
52	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268	05/2016	348.00 -	437.00	271.34	01/2021 -	12/2022	25.57
53	KHARAGPUR LPG BOTTLING PLANT - [N16000300	04/2017	163.02 -	207.36	152.03	04/2020 -	10/2022	27.20
54	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321	04/2018	206.63 -	340.76	220.01	02/2020 -	02/2023	64.91
55	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336	03/2018	588.20 -	730.20	303.77	- -	03/2023	24.14
56	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353	10/2018	598.00 -	753.89	602.73	02/2020 -	12/2022	26.07
57	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361	11/2018	462.30 -	543.00	291.80	09/2021 -	12/2022	17.46
58	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368	06/2019	371.00 -	427.10	99.98	09/2022 -	03/2023	15.12
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
59	DEVANGONTHI MARKETING TERMINAL - [N16000401	06/2020	200.00 -	304.00	41.00	06/2023 -	01/2024	52.00
	<u>Numaligarh Refinery Limited</u>							
60	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379	01/2019	12,366.00 -	18,968.00	1,929.71	10/2024 -	10/2024	53.39
	<u>Oil & Natural Gas Corporation Limited</u>							
61	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	2,001.34	1,680.76	05/2013 -	12/2022	132.23
62	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,375.90	2,911.17	04/2018 -	05/2023	5.80
63	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239	12/2015	823.27 -	1,137.79	848.08	03/2023 -	03/2023	38.20
64	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	04/2019	3,228.80 -	3,976.67	2,816.87	03/2022 -	05/2023	23.16
65	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	05/2019	763.92 -	829.58	830.87	12/2020 -	12/2022	8.60
	<u>Oil India Limited</u>							
66	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	638.60	423.10	02/2020 -	12/2022	17.41
	Total		66,663.55 -	91,460.94	56,297.67			
	<u>POWER</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>National Hydro-Electric Power Corporation</u>							
67	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	09/2002	3,919.59 -	10,463.03	10,010.30	09/2009 -	12/2023	166.94
68	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,992.43	16,222.78	09/2010 -	08/2023	218.08
69	KALPI SOLAR POWER PROJECT - [N18000323]	07/2020	314.64 -	337.77	218.26	03/2022 -	12/2022	7.35
	<u>National Thermal Power Corporation</u>							
70	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	7,103.00	5,489.00	03/2013 -	12/2024	138.48
71	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	13,203.00	06/2019 -	12/2024	18.38
72	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	809.11	09/2019 -	07/2025	30.48
73	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	21,312.11	20,184.00	10/2011 -	03/2024	145.16
74	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	9,540.00	11/2020 -	06/2023	3.76
75	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	679.00	549.68	11/2018 -	12/2022	28.19
76	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 -	524.83	506.75	09/2021 -	09/2022	4.70
77	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 -	852.90	637.22	09/2021 -	09/2022	6.85
78	NOKHRA - [N18000282]	03/2020	1,722.14 -	1,803.19	1,193.45	09/2021 -	01/2023	4.71
79	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	243.32	10/2021 -	08/2022	11.93
	<u>Power Grid Corporation Of India Limited</u>							
80	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	481.89	11/2016 -	04/2022	4.61
81	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	4,251.79	12/2018 -	03/2024	92.02
82	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	4,097.84	12/2018 -	01/2024	31.08
83	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,160.77	07/2020 -	08/2022	14.11
84	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	172.19	07/2019 -	12/2022	17.99
85	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 -	2,635.55	1,891.34	02/2020 -	04/2023	36.46

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
86	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]	10/2019	1,031.00 -	1,143.00	985.61	08/2021 -	10/2022	10.86
	<u>Satluj Jal Vidyut Nigam Limited</u>							
87	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	915.31	12/2021 -	12/2022	46.20
88	BIKANER SOLAR POWER PROJECT - [N18000335]	04/2022	5,491.89 532.00	6,023.89	791.28	05/2024 -	05/2024	9.69
	<u>Thdc India Limited</u>							
89	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,640.57	06/2013 -	03/2025	54.94
90	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,755.19	02/2016 -	10/2023	191.23
	Total		79,676.96 -	1,33,194.91	102,950.65			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
91	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	1,543.90	03/2023 -	03/2024	8.75
92	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	464.66	03/2021 -	03/2025	75.00
93	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,805.17	3,140.43	03/2021 -	03/2025	111.54
94	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,384.72	629.92	03/2022 -	03/2024	8.85
95	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	4,670.00	2,229.23	03/2024 -	03/2024	28.74
96	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	881.45	03/2023 -	03/2025	10.94
	<u>Container Corporation Of India</u>							
97	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	03/2019	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
98	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	51,219.00	31,304.00	- -	-	341.96
99	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	47,476.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
100	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,800.00	3,787.71	- -	07/2022	267.84
101	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,661.76	- -	12/2024	290.95
102	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,110.00	1,112.02	03/2012 -	06/2023	241.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
103	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	614.45	360.11	- -	03/2025	277.26
104	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00 -	519.33	346.79	- -	12/2024	36.67
105	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	1,010.00	1,038.66	03/2019 -	07/2022	48.85
106	KODERMA-TILAIYA (NL), ECR - [220100305	04/2002	459.91 -	1,625.87	1,136.40	- -	03/2024	253.52
107	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00 -	735.20	413.53	- -	12/2024	126.22
108	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14 -	1,700.00	1,758.02	- -	03/2024	356.82
109	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	783.83	540.74	03/2020 -	03/2025	43.03
110	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	685.28	03/2021 -	12/2024	63.37
111	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	624.19	03/2021 -	03/2024	62.06
112	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,510.00	1,547.42	- -	03/2024	358.42
	<u>East Coast Railway</u>							
113	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	1,027.78	06/2021 -	03/2025	137.80
114	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	2,027.20	03/2009 -	12/2025	29.71
115	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	1,152.38	02/2019 -	-	38.43
116	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	1,095.89	03/2020 -	03/2024	.07
117	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	179.43	11/2018 -	03/2025	15.45
	<u>Eastern Railways</u>							
118	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	906.01	03/2019 12/2009	03/2025	36.22
119	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	525.35	03/2017 -	10/2022	20.30
120	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	376.37	- -	09/2022	181.63
121	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	470.90	- -	03/2023	23.82
122	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	328.63	- -	12/2022	6.48

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
123	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	558.15	03/2022 -	03/2023	133.39
124	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	402.48	548.37	- -	05/2022	39.58
	<u>Indian Railway Construction Company Limited</u>							
125	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	1,509.87	03/2022 -	12/2024	117.23
126	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,500.00	2,945.30	09/2018 -	12/2023	14.57
	<u>Metropolitan Rapid Transport Projects</u>							
127	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,991.80	03/2004 -	03/2023	501.57
128	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	774.51	552.70	06/2013 -	12/2022	56.23
129	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	75.91
	<u>North Central Railway</u>							
130	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	799.75	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>							
131	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	6,527.45	5,330.91	03/2014 -	12/2023	172.72
132	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.79	12,817.81	03/2011 -	12/2023	221.56
133	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,145.79	990.86	03/2019 -	03/2024	197.45
134	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,650.00	1,255.18	03/2019 -	12/2023	397.31
135	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	6,663.00	1,781.77	03/2015 -	03/2026	186.39
136	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	7,876.92	3,408.77	12/2015 -	12/2023	488.06
137	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,047.51	1,050.40	03/2019 -	12/2023	13.88
138	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	708.73	380.92	03/2020 -	09/2022	24.42
139	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	8,324.28	266.07	03/2021 -	-	818.33
140	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	77.45	03/2020 -	03/2024	94.45
141	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	401.65	342.82	- -	03/2023	66.30

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
142	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	983.55	344.80	03/2020 -	10/2024	137.09
143	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	4,059.65	2,380.05	03/2022 -	03/2025	81.86
	<u>North Eastern Railway</u>							
144	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	800.00	687.13	01/2019 -	-	171.19
145	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	2,000.00	1,832.40	03/2022 -	03/2022	54.39
146	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	141.72	04/2016 -	-	.16
147	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	0.74	04/2017 -	10/2022	127.77
148	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	800.00	185.52	- -	12/2023	32.78
	<u>North Western Railway</u>							
149	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	837.18	02/2019 -	06/2022	109.82
150	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	476.01	03/2020 -	10/2022	16.97
	<u>Northern Railway</u>							
151	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	686.20	12/2011 -	12/2011	211.31
152	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	572.99	- -	09/2023	134.90
153	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	133.78	- -	09/2023	41.71
154	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024	348.44
155	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	37,012.26	30,671.82	11/2002 -	06/2023	1,380.49
156	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.09	03/2023 -	12/2025	369.35
	<u>Rail India Technical And Economic Service</u>							
157	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	03/2015	636.38 -	998.06	900.29	03/2021 -	-	56.83
	<u>Rail Vikas Nigam Ltd.</u>							
158	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	2,202.65	02/2015 -	09/2022	102.92
159	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	455.39	03/2009 03/2009	12/2022	224.56
160	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,834.54	1,839.89	03/2016 -	07/2025	65.94

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
161	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	2,374.44	12/2026 -	03/2025	127.62
162	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,300.00	2,799.96	03/2023 -	03/2023	55.15
163	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	3,496.68	03/2016 -	03/2026	7.78
164	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	305.05	03/2014 -	12/2025	18.95
165	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,633.12	4,271.59	03/2020 -	06/2022	141.61
166	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	2,538.01	2,375.23	12/2021 -	12/2022	63.88
167	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	626.34	03/2016 -	09/2022	50.15
168	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	4,099.98	12/2023 -	12/2023	9.32
169	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,500.00	1,127.95	03/2022 -	12/2022	58.97
170	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,457.79	1,408.80	03/2019 -	03/2023	57.26
171	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	24,659.00	8,453.89	12/2024 -	03/2025	52.07
172	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	3,066.34	03/2020 -	07/2022	281.93
173	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	2,712.78	12/2024 -	12/2026	42.47
174	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	2,350.49	03/2020 -	09/2022	111.91
175	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,552.26	1,445.70	03/2019 -	03/2023	64.62
176	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	2,203.53	2,075.59	12/2020 -	09/2022	86.23
177	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	2,340.59	12/2020 -	09/2022	23.55
178	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,664.15	03/2020 -	12/2022	102.11
<u>South Central Railway</u>								
179	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,095.80	03/2009 -	03/2027	102.85
180	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	2,250.00	784.26	03/2010 -	03/2025	93.89
181	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	918.80	03/2023 -	03/2025	5.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
182	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [N220100205	04/1997	1,723.00 1.00	3,421.35	2,206.22	03/2000 -	03/2023	98.57
183	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	1,755.92	03/2022 -	03/2025	7.06
184	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	242.28	56.14	03/2022 -	-	102.36
	<u>South East Central Railway</u>							
185	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	3,176.60	1,902.75	03/2023 -	12/2023	66.44
186	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	88.40	12/2021 -	12/2024	378.60
187	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	04/2015	1,973.00 -	2,135.34	1,106.76	03/2021 -	12/2023	8.23
188	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	918.24	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>							
189	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.97	1,264.07	03/2020 -	10/2022	35.38
190	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508	04/2018	428.65 -	472.50	6.00	06/2022 -	12/2025	10.23
191	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509	04/2018	390.39 -	511.75	259.72	12/2021 -	01/2023	31.09
192	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510	04/2018	338.00 -	393.83	34.60	06/2022 -	12/2023	16.52
	<u>South Western Railway</u>							
193	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	1,801.01 -	2,000.97	104.48	- -	03/2025	11.10
194	BAGALKOT-KUDACHI NL - [N22000258	04/2010	986.30 -	1,530.09	332.27	03/2016 -	12/2026	55.13
195	RAYADURGA-TUMKUR NL - [N22000279	04/2007	2,062.30 -	2,404.03	1,108.14	- -	12/2025	16.57
196	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	2,315.00 -	5,174.30	158.25	- -	03/2028	123.51
197	HUBLI- CHIKJAJUR - [N22000325	03/2015	1,156.94 -	1,954.21	1,381.52	03/2020 -	12/2022	68.91
198	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,878.00	1,611.28	03/2019 -	02/2024	16.31
199	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	826.18	499.13	03/2017 -	03/2026	28.13
	<u>Southern Railway</u>							
200	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU PONDY-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	3,081.20	1,774.56	02/2019 -	03/2025	325.17

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
201	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,500.79	622.53	- -	12/2025	500.65
202	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	591.00	464.44	- -	09/2022	259.47
203	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,084.48	321.37	03/2019 -	12/2027	1,626.99
204	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	0.91	- -	03/2025	33.90
	<u>West Central Railway</u>							
205	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,658.34	03/2021 -	03/2024	585.35
206	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	3,230.57
207	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,445.30	1,720.50	03/2020 -	10/2024	38.63
208	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,938.00	1,450.69	03/2022 -	03/2024	18.55
209	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	704.97	03/2022 -	09/2024	114.32
	<u>Western Railway</u>							
210	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,383.82	2,529.21	03/2022 -	03/2026	82.20
211	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	1,083.17	252.70	03/2012 -	03/2024	240.36
212	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,448.99	2,142.58	03/2020 -	03/2024	195.15
213	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	1,063.17	03/2022 -	12/2024	13.17
214	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	04/2007	1,640.04 -	1,873.10	908.51	03/2022 -	03/2025	14.21
215	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,394.02	1,300.17	03/2021 -	12/2022	34.41
216	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,119.12	962.02	03/2021 -	12/2022	11.65
217	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM [N22000434]	03/2010	265.88 -	311.36	-	- -	03/2024	17.11
218	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]	03/2012	217.38 -	393.62	219.72	- -	03/2024	81.07
219	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]	03/2012	248.26 -	528.49	127.92	- -	03/2024	112.88
220	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]	04/2017	692.25 -	692.26	8.51	03/2020 -	12/2024	.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
221	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	04/2018	537.31 -	584.31	2.44	03/2024 -	12/2024	8.75
	Total		1,94,983.24 -	4,48,395.49	283,974.69			
	<u>RENEWABLE ENERGY</u>							
	<u>Cpwd For Renewable Energy</u>							
222	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	365.00	249.96	11/2019 -	-	34.24
	Total		271.90 -	365.00	249.96			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
223	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	1,021.46	03/2011 -	-	58.98
224	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	347.48	10/2010 -	-	69.30
225	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]	01/2014	282.41 -	319.96	218.75	03/2016 -	07/2022	13.30
226	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	243.00	- -	01/2020	3.72
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]	01/1991	675.00 -	780.77	453.21	- -	03/2023	15.67
228	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	386.57	05/2017 -	06/2022	45.75
229	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	849.98	- -	-	1.75
230	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	400.65	10/2010 -	-	93.80
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	404.10	400.67	- -	11/2022	26.41
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000574]	11/2013	683.83 -	698.82	717.89	07/2016 -	06/2022	2.19

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
233	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000576	02/2016	178.85 -	225.06	212.91	05/2016 -	11/2022	25.84
234	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000578	02/2016	553.30 -	587.41	553.81	05/2016 -	11/2022	6.16
235	FOUR LANEING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579	01/2014	1,408.85 -	2,138.16	1,412.08	10/2016 -	03/2023	51.77
236	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	.26
237	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	108.00	06/2016 -	09/2022	.02
238	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	-	- -	-	.06
239	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	94.55	11/2019 -	10/2022	.08
240	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	174.90	154.26	08/2018 -	10/2022	5.23
241	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	125.25	11/2018 -	03/2023	7.39
242	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	47.17	08/2019 -	03/2023	33.51
243	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	91.29	08/2019 -	03/2023	11.18
244	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	206.89	08/2018 -	10/2022	4.45
245	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	03/2016	877.79 -	949.54	807.22	06/2019 -	09/2022	8.17
246	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922	12/2017	867.97 -	913.49	700.54	11/2018 -	09/2022	5.24
247	FOUR LANEING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	341.76	12/2015 -	01/2021	6.07
248	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	01/2017	576.48 -	686.13	503.77	01/2018 -	12/2022	19.02
249	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998	01/2019	193.19 -	249.72	184.91	- -	01/2023	29.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
250	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	186.27	07/2019 -	11/2020	.31
251	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	404.69	03/2018 -	10/2022	9.23
252	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]	01/2017	166.67 -	264.34	181.38	09/2017 -	07/2022	58.60
253	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]	08/2016	175.50 -	241.60	164.41	02/2017 -	08/2022	37.66
254	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]	03/2018	159.97 -	242.61	94.29	06/2019 -	03/2023	51.66
255	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]	12/2017	297.30 -	318.28	246.53	01/2019 -	07/2022	7.06
256	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	03/2018	325.86 -	386.41	347.42	10/2018 -	04/2021	18.58
257	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]	11/2016	336.25 -	369.96	309.98	09/2019 -	11/2020	10.03
258	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	322.24	312.50	09/2014 -	-	72.36
259	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	1,251.08	-	12/2021	2.93
260	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208]	03/2018	288.30 -	323.36	237.25	08/2020 -	10/2022	12.16
261	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]	11/2018	281.45 -	319.96	202.69	-	09/2022	13.68
262	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	280.46	08/2016 -	12/2022	15.19
263	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	452.11	09/2016 -	03/2023	14.24
264	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	471.29	10/2016 -	12/2022	17.04
265	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	01/2017	197.67 -	236.18	107.81	12/2022 -	12/2022	19.48

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
266	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369	02/2017	294.28 -	296.53	211.30	08/2017 -	-	.76
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
267	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	05/2015	454.89 -	814.56	391.87	05/2018 -	07/2022	79.07
268	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320	06/2015	463.49 -	801.54	185.26	06/2018 -	03/2023	72.94
269	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	03/2015	168.39 -	259.79	158.07	11/2018 -	08/2022	54.28
270	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	873.91	559.13	11/2018 -	09/2022	48.38
271	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582	01/2016	294.17 -	385.57	229.26	01/2016 -	07/2022	31.07
272	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583	01/2016	252.00 -	330.30	141.13	01/2016 -	12/2022	31.07
273	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	180.00	04/2017 -	11/2022	29.48
274	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	172.68	04/2017 -	10/2022	29.48
275	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	364.31	08/2016 -	-	3.73
276	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	171.06	04/2017 -	08/2022	27.16
277	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	530.67	316.99	10/2017 -	06/2022	36.77
278	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823	03/2015	829.00 -	1,307.50	411.51	01/2016 -	06/2023	57.72
	<u>National Highways Authority Of India</u>							
279	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
280	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138	09/2010	946.00 -	1,046.56	822.13	06/2018 -	12/2022	10.63
281	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	09/2011	1,250.00 -	1,380.73	1,354.65	12/2013 -	05/2024	10.46

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
282	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66
283	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	576.99	11/2013 -	05/2022	15.53
284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	470.89	01/2014 -	12/2019	61.08
285	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]	11/2011	478.51 -	1,082.40	315.11	10/2013 -	03/2022	126.20
286	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 -	417.68	545.12	01/2016 -	01/2019	18.88
287	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	777.03	766.05	05/2018 -	12/2022	46.30
288	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	276.71	- -	02/2021	.77
289	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	717.24	662.98	05/2018 -	06/2022	20.90
290	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]	07/2015	2,128.72 -	2,408.72	1,865.00	04/2019 -	09/2022	13.15
291	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	910.78	- -	01/2020	11.33
292	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	05/2014	1,655.01 -	2,639.00	1,710.83	08/2016 -	12/2022	59.46
293	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,414.01	1,000.57	06/2018 -	01/2023	30.56
294	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	09/2015	934.46 -	1,543.51	1,472.50	03/2018 -	12/2022	65.18
295	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	1,018.46	- -	09/2022	1.37
296	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	01/2016	815.28 -	2,323.88	2,223.06	06/2018 -	12/2022	185.04
297	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	01/2016	1,027.53 -	2,628.31	2,588.02	06/2018 -	06/2022	155.79
298	FOUR LANING OF SIMGA - SARAGAON - [N24000495]	12/2015	596.67 -	819.35	439.27	05/2018 -	08/2022	37.32
299	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	06/2016	667.00 -	2,328.27	2,126.16	07/2018 -	09/2022	249.07
300	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	3,006.53	2,989.89	06/2018 -	12/2022	350.75
301	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	673.94	- -	12/2022	6.11
302	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	399.40	- -	03/2023	1.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
303	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67 -	1,096.52	538.73	04/2018 -	12/2021	50.90
304	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,521.55	-	12/2023	41.78
305	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,065.19	-	05/2022	21.50
306	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	638.53	04/2018 -	01/2021	25.80
307	MEERUT-BULANDSHAHAHAR - [N24000539]	01/2016	683.24 -	987.94	-	-	03/2022	44.60
308	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	3,063.99	2,904.36	04/2019 -	09/2022	93.01
309	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	03/2016	899.00 -	1,376.86	909.36	04/2019 -	06/2022	53.15
310	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]	03/2016	720.00 -	793.63	326.96	-	09/2022	10.23
311	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]	03/2016	1,443.00 -	2,330.79	1,246.85	-	03/2022	61.52
312	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]	03/2016	1,737.00 -	2,421.37	1,877.96	-	12/2021	39.40
313	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]	07/2016	458.03 -	486.00	487.99	-	06/2022	6.11
314	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	1,588.29	739.00	09/2019 -	05/2022	14.40
315	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,330.39	-	05/2021	94.94
316	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	355.24	327.54	08/2018 -	05/2022	9.74
317	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,529.21	08/2019 -	06/2022	16.55
318	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	359.60	339.75	-	09/2022	23.69
319	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	1,023.23	981.05	07/2018 -	05/2022	68.89
320	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]	01/2017	1,251.11 -	1,361.00	503.77	-	09/2022	8.78

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
321	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	03/2017	1,373.28 -	1,405.27	1,401.96	03/2020 -	08/2022	2.33
322	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	1,309.30	03/2020 -	09/2022	10.58
323	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	-	03/2020 -	07/2024	31.88
324	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	-	03/2017 -	06/2022	1.06
325	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	830.31	31.82	03/2020 -	03/2023	23.39
326	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	975.08	03/2020 -	03/2022	13.97
327	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	1,105.15	03/2020 -	03/2022	10.24
328	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	912.41	03/2020 -	06/2022	41.54
329	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	1,319.54	03/2020 -	06/2022	44.39
330	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	880.00	04/2020 -	12/2022	3.95
331	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	10/2021	1.78
332	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	08/2017	950.64 -	1,168.33	503.74	08/2017 -	08/2023	22.90
333	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703	10/2017	964.17 -	1,198.64	1,053.15	10/2017 -	05/2022	24.32
334	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,309.79	1,162.72	09/2017 -	03/2023	16.52
335	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718	12/2017	328.67 -	416.07	330.31	-	-	26.59
336	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG -I - [N24000723	01/2018	573.70 -	726.99	222.51	-	06/2023	26.72
337	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	175.09	-	03/2023	.99
338	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,862.77	192.01	-	01/2024	30.74

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
339	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 -	1,422.13	444.08	- -	12/2022	21.94
340	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 -	2,400.00	3,568.04	- -	10/2022	20.28
341	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 -	2,450.00	2,691.86	- -	09/2022	12.50
342	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]	03/2018	1,261.98 -	2,145.96	199.05	- -	06/2024	70.05
343	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]	03/2018	809.07 -	1,065.70	1,049.98	- -	12/2022	31.72
344	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 -	1,332.00	1,228.92	- -	-	18.87
345	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 -	1,361.00	503.77	- -	09/2022	29.35
346	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]	02/2018	972.77 -	1,441.00	494.71	- -	03/2023	48.13
347	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	1,827.00	1,306.69	03/2021 -	08/2022	19.21
348	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 -	537.17	156.46	- -	06/2023	8.26
349	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 -	16,732.70	468.76	- -	07/2022	1,524.60
350	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]	03/2018	633.55 -	736.33	68.39	- -	08/2023	16.22
351	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,308.88	492.86	- -	12/2022	28.71
352	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96 -	2,169.00	-	- -	01/2024	4.99
353	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 -	1,296.00	-	- -	-	.12
354	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	925.96	823.04	- -	02/2022	45.89

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
355	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 -	922.64	820.70	- -	04/2022	15.98
356	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]	03/2018	1,162.92 -	1,182.87	84.54	- -	10/2023	1.72
357	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]	03/2018	478.74 -	1,135.08	905.95	- -	11/2022	137.10
358	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	03/2018	642.13 -	807.00	760.42	- -	06/2022	25.68
359	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]	11/2017	2,159.00 -	2,262.00	1,978.74	01/2019 -	01/2019	4.77
360	ISMAILABAD-NARNAUL PKG-5 - [N24001186]	01/2019	1,051.91 -	1,118.07	1,031.96	- -	05/2022	6.29
361	ISMAILABAD-NARNAUL PKG-6 - [N24001187]	01/2019	1,120.06 -	1,206.48	1,127.92	- -	07/2022	7.72
362	ISMAILABAD-NARNAUL PKG-7 - [N24001188]	01/2019	1,137.42 -	1,238.29	1,185.04	- -	06/2022	8.87
363	ISMAILABAD-NARNAUL PKG-8 - [N24001189]	01/2019	1,033.19 -	1,044.32	911.58	- -	03/2022	1.08
364	ISMAILABAD-NARNAUL PKG-2 - [N24001190]	01/2019	1,243.45 -	1,407.35	1,355.53	- -	04/2022	13.18
365	ISMAILABAD-NARNAUL PKG-3 - [N24001191]	01/2019	889.36 -	986.10	949.40	- -	05/2022	10.88
366	ISMAILABAD-NARNAUL PKG-4 - [N24001192]	01/2019	1,018.79 -	1,072.08	1,023.71	- -	05/2022	5.23
367	ISMAILABAD-NARNAUL PKG-1 - [N24001193]	01/2019	996.65 -	1,173.65	1,115.31	- -	05/2022	17.76
368	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]	10/2019	743.88 -	743.89	721.00	- -	08/2022	.00
369	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]	12/2017	656.98 -	840.00	689.00	- -	11/2022	27.86
370	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]	12/2017	217.96 -	884.00	797.00	- -	10/2022	305.58
371	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]	09/2018	617.41 -	668.45	562.93	02/2019 -	05/2022	8.27
372	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]	11/2019	1,226.88 -	1,321.60	678.20	02/2021 -	02/2023	7.72

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
373	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]	07/2020	3,426.00 -	5,852.00	-	12/2021 -	-	70.81
374	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]	02/2019	731.89 -	732.34	530.71	11/2019 -	12/2022	.06
375	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]	02/2019	594.75 -	606.75	410.81	11/2019 -	12/2022	2.02
	Total		1,20,587.37 -	1,73,392.57	112,665.13			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
376	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	21,019.89	05/2015 -	03/2023	41.32
	Total		15,525.00 -	21,940.00	21,019.89			
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
377	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]	03/2020	431.16 431.00	461.42	107.44	06/2021 -	11/2022	7.02
	Total		431.16 -	461.42	107.44			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
378	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,925.22	10,816.18	12/2018 -	09/2022	19.98
	<u>Central Public Works Department</u>							
379	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33 -	220.00	113.34	04/2019 -	-	11.49
	<u>Chennai Metro Rail Ltd</u>							
380	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	18,380.00	17,629.68	12/2015 -	-	25.89
	<u>Delhi Metro Rail Corporation</u>							
381	DELHI MRTS PHASE-III - [N28000056]	09/2011	38,585.00 -	40,180.91	39,907.57	03/2016 -	-	4.14
	<u>Kochi Metro Rail Corporation Ltd</u>							
382	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	6,065.85	07/2017 -	-	20.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Mumbai Metro Rail Corporation Ltd</u>							
383	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	22,064.15	03/2020 -	12/2023	44.39
	<u>Nagpur Metro Rail Corporation Ltd</u>							
384	NAGPUR METRO RAIL - [N28000085]	08/2014	8,680.00 -	9,759.79	8,524.81	03/2018 -	03/2022	12.44
	<u>Patna Metro Rail Corporation</u>							
385	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 -	13,925.50	437.20	06/2024 -	06/2024	4.19
	Total		1,14,518.89 -	1,35,015.56	105,558.78			
	<u>WATER RESOURCES</u>							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
386	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	413.29	0.07	09/2020 -	03/2024	62.63
387	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	398.90	332.70	03/2020 -	06/2022	76.68
388	SAIDPUR SEWER NETWORK PATNA - [N30000039]	04/2015	268.63 -	431.21	432.61	01/2021 -	06/2022	60.52
	<u>Kolkata Metropolitan Development Authority</u>							
389	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	03/2024	13.23
	<u>Polavaram Project Authority</u>							
390	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	20,538.05	03/2020 -	03/2024	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
391	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	04/2024	22.24
392	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	28.37	12/2021 -	06/2023	.97
393	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	1.31
	Total		12,225.19 -	58,202.82	21,331.80			
	Grand Total		6,79,490.73	11,63,296.99	781,316.99			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 6,840.00	7,500.00	6,433.54	09/2010 10/2022	09/2024	168	114.78	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 19,220.00	19,220.00	18,523.00	12/2015 -	06/2023	90	67.73	
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	31,955.00	11/2020 -	11/2023	36	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	14,876.00	12/2016 -	12/2023	84	38.63	
	Total		67,120.00 -	83,648.00	71,787.54					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	417.23 707.73	707.73	570.11	09/2018 10/2022	10/2022	49	69.63	Nil
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	303.80 351.21	351.21	247.98	04/2020 12/2022	12/2022	32	15.61	Nil
7	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI, UTTARAKHAND	07/2018	456.86 -	456.86	376.59	09/2020 12/2022	12/2022	27	0	Nil

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
8	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	137.92	02/2020 12/2022	12/2022	34	0	1. A portion of the site measuring 3.40 acres is not available due to write petition between land owner & State Govt., which is fouling in the Runway extension and Basic Strip due to which the work will be delayed further. 2. High mast transmission towers in the approach path of Runway 08 to be shifted by APTRANSCO (Govt. of AP undertaking) for final commissioning of the Project and this part of the work is yet to physically start. However work order is placed by State Government and agency mobilizing Men, materials & Machinery for the work.
9	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. - [N04000093]AAI,GUJARAT	08/2018	353.25 -	353.25	143.30	02/2021 -	12/2022	22	0	Nil
10	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]AAI,TELANGANA	05/2020	353.61 -	353.61	175.15	05/2022 03/2023	03/2023	10	0	Nil
11	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24 -	412.24	284.51	06/2021 03/2023	03/2023	21	0	Nil
12	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH	02/2019	645.63 -	645.63	519.30	08/2022 03/2023	03/2023	7	0	Acquisition of 2.604 Ha of Assam land, Land acquisition for Kokila River diversion and ultimate development at 26 side of runway of Hollongi Airport ,Solar powered obstruction light to be installed on hill tops in the vicinity of Airport,C/o Boundary wall.
13	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	660.06	10/2021 04/2023	04/2023	18	0	Nil
14	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	389.71	325.34	11/2021 04/2023	04/2023	17	0	2

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
15	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH	04/2020	611.80 -	611.80	167.35	03/2023 -	07/2023	4	0	Nil
16	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39 -	475.39	248.29	04/2021 08/2023	08/2023	28	0	Nil
17	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	1,405.00	681.21	08/2022 08/2023	08/2023	12	0	1) Relocation of Juna Hirasar village 2) Relocation of wind mills, Lowering of Pylon mast & Cell phone mast, Lowering of obstacles outside airport.
18	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	2,445.00	797.96	09/2021 -	09/2023	24	76.79	
19	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. - [N04000095]AAI,GOA	11/2017	255.69 -	255.69	27.32	09/2021 -	09/2023	24	0	Consent to Establish received from GSPCB on 18.04.2022. Issue resolved.
20	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM - [N04000096]AAI,MAHARASHTRA	06/2017	255.68 -	255.68	202.60	12/2020 -	09/2023	33	0	Process of acquisition of land is in progress by State Government.
21	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH	07/2018	346.27 -	480.33	192.21	09/2021 12/2023	12/2023	27	38.72	Nil
22	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	458.00 -	458.00	190.85	03/2020 03/2024	03/2024	48	0	Nil
23	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	333.86	10/2022 03/2024	03/2024	17	0	AUGUMENTATION OF STORM WATER DRAINAGE SYSTEM FOR CONNECTIONG NEW STORM WATER SYSTEM OF AIRPORT WITH ENLARGED CAPACITY.
24	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	68.90	03/2022 12/2023	03/2024	24	0	Nil
25	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	1,048.18	02/2022 12/2024	12/2024	34	0	Nil

Details of Delayed Projects w.r.t. Original Schedule

[illegible]

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
36	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	5,146.48	648.15	08/2019 -	08/2024	60	93.35	i). Approval of Deptt. of IC& E, Govt. of WB regarding utilization of further 100.32 acres vested land which was identified and finalized by ADDA for this rehabilitation project. ii). To expedite shifting of families at the Bijaynagar site where construction of 160 flats has already been completed with infrastructural developments/amenities. iii). Approval of revised R&R package by Cabinet of State Govt. of West Bengal before sending to Ministry of Coal, GOI for obtaining competent approval. iv). Publication of final figure of Demographic survey report for non-ECL households by ADDA. v). Finalization and publication of valuation report for Legal Title Holder households by ADDA.
	<u>Mahanadi Coal Fields Limited</u>									
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	868.37	874.49	03/2013 -	03/2024	132	81.09	
38	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	251.54	03/2019 -	03/2024	60	0	
39	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38 -	1,375.38	734.15	03/2021 -	03/2026	60	0	
40	KULDA EXPANSION OCP- 15 MTY - [N06000248]MCL, ODISHA	06/2014	348.16 -	348.16	162.94	03/2018 -	03/2026	96	0	
	<u>Neyveli Lignite Corporation</u>									
41	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	13,965.29	11/2021 -	11/2023	24	0	1. Acquisition of Balance 4.7689 ha of pocket land in main plant area. 2. Acquisition of Balance 13.69415 ha of Railway siding land. 3. PPA with UP Govt. for balance 25% power allocated by MoP(Gol).
42	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	709.06	526.60	06/2015 -	09/2027	147	-51.37	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Northern Coal Fields Limited</u>									
43	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09	1,783.09	1,197.65	03/2021	03/2023	24	0	
44	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17	1,255.17	846.30	03/2022	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
45	RCE OF INDARAM OPENCAST PROJECT - [N06000211]SCCL,TELANGANA	08/2017	349.28	349.28	323.72	03/2021	03/2023	24	0	
46	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II - [N06000212]SCCL,TELANGANA	03/2019	473.22	473.22	392.38	03/2021	03/2023	24	0	
47	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213]SCCL,TELANGANA	03/2016	384.32	384.32	171.52	03/2020	03/2023	36	0	
48	RCE OF KISTARAM OPENCAST PROJECT - [N06000215]SCCL,TELANGANA	03/2017	164.04	164.04	143.08	03/2021	03/2023	24	0	
49	KAKATYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84	413.84	346.68	03/2022	03/2024	24	0	
50	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73	272.73	153.75	03/2018	03/2024	72	0	
51	VENKATESH KHANI COAL MINE - [N06000204]SCCL,TELANGANA	10/2020	484.51	484.51	36.25	03/2023	03/2024	12	0	
52	RCE OF KAKATHYAKHANI OC - 2 PROJECT - [N06000214]SCCL,TELANGANA	08/2017	442.42	442.42	129.91	03/2020	03/2024	48	0	
	<u>South-Eastern Coal Fields Limited</u>									
53	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97	335.97	48.55	03/2018	03/2023	60	0	
54	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10	316.10	154.35	03/2020	03/2023	36	0	
55	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80	357.80	86.97	03/2021	03/2024	36	0	
56	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04	371.04	87.70	03/2021	03/2024	36	0	
57	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63	610.63	234.80	03/2022	03/2025	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
58	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	163.63	03/2021 03/2025	03/2025	48	0	
59	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	16.13	03/2014 -	03/2026	144	0	
	<u>Western Coal Fields Limited</u>									
60	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA	11/2018	318.14 -	318.14	237.84	03/2021 -	09/2022	18	0	
61	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	108.78	03/2021 09/2022	09/2022	18	0	
62	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	302.91	03/2021 -	09/2023	30	0	
63	BHATADI EXPASION OC (0.975 MTY) - [N06000234]WCL,MAHARASHTRA	02/2016	327.41 -	327.41	176.39	03/2019 -	09/2026	90	0	
	Total		38,126.49 -	40,392.68	24,405.94					
	<u>FINANCE</u>									
	<u>Cpwd For Finance</u>									
64	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU	12/2015	209.00 -	262.00	208.93	10/2019 10/2022	10/2022	36	25.36	
	Total		209.00 -	262.00	208.93					
	<u>MINES</u>									
	<u>Central Public Works Department</u>									
65	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]CPWD,WEST BENGAL	04/2019	255.37 -	255.37	26.26	04/2022 -	10/2024	30	0	
	<u>National Aluminum Company Limited (Nalco)</u>									
66	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2022	12/2022	42	-2.07	Extension of NFR (Noted For Record)is pending with TANGEDCO.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
67	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 667.23	667.23	497.21	01/2020 11/2023	11/2023	46	24.95	1) Balance Land Acquisition of Utkal E: IDCO to execute the lease deed with NALCO. 2) Stage - II Forest Clearance of Utkal E: MOEF&CC, GOI on 29.12.2021 has asked to submit a new Soil Moisture Conservation scheme prepared by M/s CMPDIL. The scheme has been prepared and submitted to DFO Angul for approval.
68	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 581.00	581.00	96.18	11/2020 12/2023	12/2023	37	63.66	
69	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	483.00	59.47	04/2021 12/2023	12/2023	32	0	
70	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	4,103.00 5,055.00	5,055.00	1,486.31	04/2021 01/2024	01/2024	33	23.2	
	Total		5,896.99 -	7,204.77	2,300.43					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
71	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	21,019.89	05/2015 03/2023	03/2023	94	41.32	
72	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH	11/2015	2,907.00 -	2,907.00	908.39	06/2023 -	07/2024	13	0	
	<u>Steel Authority Of India Limited (SAIL)</u>									
73	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	272.19	06/2019 06/2022	09/2022	39	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
74	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	782.72	10/2017 12/2021	12/2023	74	0	
	Total		19,728.88 -	26,143.88	22,983.19					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
75	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	19.51	02/2017 08/2022	09/2022	67	117.11	Delay due to RoU issues in Tamil Nadu (TN) portion due to local resistance and lack of support / clarity from TN Govt. including delay in release of GO on land and crop compensation which was released in Feb 2020.Detailed Engineering Survey and other ROU activities could not be done due to local protests. TIDCO has been nominated as Nodal Agency for resolving ROU issues in Oct 2021. Pipeline route is being discussed with TIDCO officials.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
76	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	972.00	06/2019 02/2023	02/2023	44	35.54	Kerala State: Delays in release of Kerala GO on compensation, RoU acquisition, permission from Chalakudy Municipality etc. Major Project activities started only after Kerala GO on compensation to landowners which was released in Jan 2019. Tamil Nadu State: Project work was stalled since Dec'2014 after denial of permissions from SH authorities to lay pipeline along roads. Local resistance and lack of support / clarity from Tamil Nadu Govt. including delay in release of GO on land and crop compensation resulted in delays. GO was released in Feb 2020. Competent Authority was appointed in May 2021. TIDCO has been nominated as Nodal Agency for resolving ROU issues in Oct 2021. ROU acquisition activities has been started in section up to Coimbatore (42 KM).
77	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	393.95	02/2021 -	03/2023	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
78	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	248.55	180.31	06/2022 03/2023	03/2023	9	0	Activities on 18 acres of land out of 70 acres were on hold due to Status Quo order by Hon'ble court of Ranchi- Jharkhand (Land of 10 acres since 24.09.2019 and land of 8 acres since 04.07.2020). High Court has given verdict for 10 acres of land on 03.09.2021 directing State Government to determine appropriate compensation of land and to hand over possession of same to BPCL on payment of proportionate compensation to petitioners. BPCL has deposited the said compensation amount. Work re-commenced after clearance from the govt in April-2022. Second petition with respect to 8 acres of land yet to be taken up for hearing.
79	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374]BPCL,ODISHA	08/2019	1,607.00 -	1,607.00	507.46	08/2022 06/2023	06/2023	10	0	
	<u>Gas Authority Of India Limited</u>									
80	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	247.90	154.74	02/2021 -	10/2022	20	9.91	Nil
81	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 2,105.70	2,105.70	1,811.30	12/2020 11/2022	11/2022	23	8.93	1) Delay in grant of Forest permission in Odisha.(13 Km) 2) Unprecedented flood leading to inundation of RoU. 3) RoU related issues/encumbrance/resistance.
82	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00 -	3,048.00	2,444.60	12/2020 11/2022	11/2022	23	-11.32	1) Delay in receipt of Forest permission in Odisha.(65 Km) 2) Other RoU related issues/encumbrance/resistance.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
83	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.00	327.01	255.10	08/2020 06/2022	12/2022	28	14.17	Stiff resistance from Farmers (From Ch 113 to 133.9 in patches ~ 9 Km) is being faced demanding higher compensation in Hissar district
84	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 -	217.92	126.20	04/2021 12/2022	12/2022	20	0	
85	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]GAIL,JHARKHAND	10/2017	226.45 -	226.45	179.25	10/2022 -	03/2023	5	0	NIL
86	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	1,084.40	12/2020 06/2023	06/2023	30	0	Non – availability of RoU in West Bengal.
87	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 -	3,308.00	2,819.70	12/2021 06/2023	06/2023	18	0	Delay in RoU acquisition in West Bengal.
88	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE	03/2020	1,030.65 -	1,030.65	448.70	11/2022 06/2023	06/2023	7	0	Delay in RoU acquisition in West Bengal.
89	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE	09/2019	2,658.34 -	2,658.34	918.30	07/2022 07/2023	07/2023	12	0	
90	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 -	243.53	195.96	07/2022 -	08/2023	13	0	
91	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20 -	182.20	115.16	07/2022 -	08/2023	13	0	NIL
92	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]GAIL,JHARKHAND	10/2017	221.45 -	221.45	129.91	10/2022 -	08/2023	10	0	NIL
93	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	359.25	228.18	10/2022 -	10/2023	12	0	NIL
94	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,570.80	12/2012 02/2025	02/2025	146	102.71	Non - availability of hindrance free RoU in Tamil Nadu.
	<u>Hindustan Petroleum Corporation Limited</u>									
95	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 3,185.00	3,185.00	2,943.70	06/2021 08/2022	08/2022	14	18.98	Nil

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
96	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	249.10	06/2020 -	09/2022	27	0	
97	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA	06/2019	2,166.38 -	2,166.38	1,762.67	06/2022 -	10/2022	4	0	
98	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	210.94	139.97	08/2021 -	12/2022	16	0	
99	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 -	26,264.00	20,025.46	07/2020 -	03/2023	32	25.5	
100	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH	10/2020	332.61 -	332.61	32.33	11/2022 -	03/2023	4	0	
101	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA	12/2018	854.00 -	854.00	235.86	12/2022 12/2023	12/2023	12	0	
102	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	275.43	09/2026 -	02/2027	5	0	
103	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	763.70	03/2029 -	08/2029	5	0	
104	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL	03/2019	5,830.20 -	5,830.20	301.79	03/2031 -	08/2031	5	0	
	<u>Indian Oil Corporation Limited</u>									
105	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	423.21	02/2020 07/2022	09/2022	31	0	
106	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	343.45	04/2021 09/2022	09/2022	17	0	
107	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	316.20	183.14	10/2021 09/2022	09/2022	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
108	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,446.06	03/2021 06/2022	10/2022	19	66.09	
109	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	115.53	02/2020 10/2022	10/2022	32	0	
110	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 207.36	207.36	152.03	04/2020 10/2022	10/2022	30	27.2	
111	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	188.28	08/2020 11/2022	11/2022	27	0	
112	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	680.30	01/2021 08/2022	11/2022	22	0	
113	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	684.72	10/2017 03/2022	12/2022	62	103.6	
114	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 3,338.00	3,338.00	3,250.17	12/2020 02/2023	12/2022	24	43.82	
115	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 2,145.00	2,145.00	1,801.97	02/2022 08/2022	12/2022	10	10.28	1. Stiff resistance in opening of RoU in Maharashtra due to demand of exorbitant compensation and diversion of route. As on date, work is hampered in 6.15 Km of RoU in different stretches in Dhule (0.20 Km), Ahmednagar (3.0 Km), Beed (0.38 Km), Osmanabad (0.56 km) and Solapur (2.0 Km) districts.
116	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	271.34	01/2021 -	12/2022	23	25.57	
117	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA	04/2018	5,654.00 -	5,654.00	3,885.24	10/2021 07/2022	12/2022	14	0	
118	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	1,097.83	08/2020 04/2022	12/2022	28	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
119	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	1,004.24	10/2021 07/2022	12/2022	14	0	
120	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 753.89	753.89	602.73	02/2020 07/2022	12/2022	34	26.07	
121	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 543.00	543.00	291.80	09/2021 12/2022	12/2022	15	17.46	
122	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	403.00	213.43	08/2022 -	12/2022	4	0	Delay in purchase of land at 3 locations (Muzaffarpur 2 , East Champaran-1) for installation of sectionalizing valves due to poor response of EOI publications and high rates demanded by private landowners. Regular follow-up is being maintained with State Administration for providing assistance in resolution of issue. Letter sent to DM Muzaffarpur and DM East Champaran on 25.05.2022. Meeting held with DM Muzaffarpur on 04.06.2022. Meeting held with DM East Champaran on 25.06.2022.
123	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	101.66	12/2019 01/2023	01/2023	37	0	
124	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	1,255.00	661.56	12/2021 01/2023	01/2023	13	0	
125	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 340.76	340.76	220.01	02/2020 02/2023	02/2023	36	64.91	
126	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL	03/2018	3,712.00 3,696.00	3,696.00	2,638.70	09/2022 02/2023	02/2023	5	-43	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
127	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	150.41	04/2022 -	02/2023	10	0	
128	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	210.47	08/2021 03/2023	03/2023	19	0	
129	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	160.73	06/2021 07/2022	03/2023	21	0	
130	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 427.10	427.10	99.98	09/2022 03/2023	03/2023	6	15.12	
131	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	202.16	129.65	07/2022 -	03/2023	8	0	
132	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	47.33	07/2022 06/2023	06/2023	11	0	
133	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	81.34	07/2021 03/2022	06/2023	23	0	
134	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,219.94	2,281.94	804.64	12/2022 07/2023	07/2023	7	0	
135	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	118.68	10/2020 08/2022	08/2023	34	0	
136	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	193.17	04/2022 -	08/2023	16	0	
137	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	4,938.92	12/2018 11/2023	11/2023	59	33.98	1. Delay in finalization of Market value of land for payment of enhanced compensation. Till date, Market value for 340 villages out of total 665 villages received.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
138	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	61.75	09/2023 -	02/2024	5	0	
139	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	1,398.00	290.30	12/2023 -	02/2024	2	0	
140	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA	05/2019	3,361.00 -	3,361.00	2,258.02	08/2021 09/2022	03/2024	31	0	
141	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR	01/2020	14,810.00 -	14,810.00	3,834.49	04/2023 -	07/2024	15	0	
142	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH	10/2018	177.00 -	177.00	82.58	02/2027 09/2028	09/2028	19	0	
143	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR	10/2018	176.00 -	176.00	110.40	08/2027 02/2029	02/2029	18	0	
144	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR	06/2019	439.00 -	439.00	147.85	02/2028 08/2029	08/2029	18	0	
145	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR	06/2019	347.00 -	347.00	125.47	02/2028 08/2029	08/2029	18	0	
146	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	2,996.00	395.60	02/2028 08/2029	08/2029	18	0	
147	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND	10/2018	613.00 -	613.00	191.24	12/2029 03/2030	03/2030	3	0	
148	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	2,880.00	139.21	08/2027 03/2030	03/2030	31	0	
149	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR	06/2019	988.00 -	988.00	57.14	12/2029 03/2030	03/2030	3	0	
150	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR	06/2019	163.00 -	163.00	42.34	12/2029 03/2030	03/2030	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]OCL,MULTI STATE	06/2019	169.00 -	169.00	48.73	12/2029 03/2030	03/2030	3	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
152	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA	06/2020	200.00 304.00	304.00	41.00	06/2023 01/2024	01/2024	7	52	
	<u>Oil & Natural Gas Corporation Limited</u>									
153	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 2,001.34	2,001.34	1,680.76	05/2013 12/2022	12/2022	115	132.23	
154	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	462.08	03/2019 09/2021	12/2022	45	0	Facilities: Grant of CTE is awaited from TNPCB, Govt of Tamil Nadu. Drilling: * Public hearing for grant of Environmental Clearance (EC) and site access issues have delayed drilling of balance wells.
155	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	2,292.46	2,311.32	05/2021 12/2022	12/2022	19	0	
156	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	829.58	830.87	12/2020 12/2022	12/2022	24	8.6	
157	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT	02/2020	444.87 -	444.87	338.56	08/2022 02/2023	02/2023	6	0	
158	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	06/2019	2,494.68 -	2,494.68	2,141.49	03/2022 03/2023	03/2023	12	0	
159	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,911.17	04/2018 05/2023	05/2023	61	5.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
160	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	31,040.00	19,243.11	06/2020 05/2023	05/2023	35	-8.74	
161	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	2,816.87	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									
162	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	638.60	423.10	02/2020 12/2022	12/2022	34	17.41	
	Total		1,73,603.38 -	1,87,965.25	1,12,463.71					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
163	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	2,449.04	04/2020 07/2025	07/2025	63	0	Signing of PPA for 1000MW Pakal Dul HE Projects – Pending with J&K Govt.
	<u>National Hydro-Electric Power Corporation</u>									
164	KALPI SOLAR POWER PROJECT - [N18000323]NHPC,UTTAR PRADESH	07/2020	314.64 335.36	337.77	218.26	03/2022 12/2022	12/2022	9	7.35	
165	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	16,222.78	09/2010 08/2023	08/2023	155	218.08	
166	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 10,463.03	10,463.03	10,010.30	09/2009 12/2023	12/2023	171	166.94	
167	RANGIT IV HE PROJECT - [N18000326]NHPC,SIKKIM	03/2021	938.29 938.29	938.29	315.06	05/2024 08/2024	08/2024	3	0	
168	TEESTA VI HE PROJECT - [N18000325]NHPC,SIKKIM	03/2019	5,748.04 -	5,748.04	1,748.06	03/2024 -	07/2025	16	0	
	<u>National Thermal Power Corporation</u>									
169	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	293.03	243.32	10/2021 01/2023	08/2022	10	11.93	
170	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	524.83	506.75	09/2021 01/2023	09/2022	12	4.7	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
171	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	852.90	637.22	09/2021 11/2022	09/2022	12	6.85	
172	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	1,316.22	1,059.63	09/2021 11/2022	10/2022	13	0	
173	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	679.00	549.68	11/2018 12/2022	12/2022	49	28.19	None
174	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	1,803.19	1,193.45	09/2021 01/2023	01/2023	16	4.71	
175	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	1,782.00	1,146.84	09/2021 01/2023	01/2023	16	0	
176	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	382.22	36.61	03/2022 12/2023	03/2023	12	0	
177	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,998.00	9,540.00	11/2020 07/2022	06/2023	31	3.76	
178	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	1,221.73	146.13	07/2022 -	08/2023	13	0	
179	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	599.99	170.95	07/2022 -	08/2023	13	0	
180	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	842.27	92.08	07/2022 10/2022	08/2023	13	0	
181	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]NTPC,GUJARAT	05/2021	674.92 -	674.92	76.91	09/2022 -	08/2023	11	0	
182	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320]NTPC,RAJASTHAN	03/2022	1,352.71 -	1,352.71	41.85	08/2023 10/2023	10/2023	2	0	
183	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321]NTPC,RAJASTHAN	03/2022	1,409.52 -	1,409.52	50.84	08/2023 10/2023	10/2023	2	0	
184	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322]NTPC,RAJASTHAN	03/2022	1,426.94 -	1,426.94	49.14	08/2023 10/2023	10/2023	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
185	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	20,184.00	10/2011 07/2023	03/2024	149	145.16	Bakhtiyarpur ROR line: Acquisition of 12.241 Acres supplementary land is under process. Land award has been done. Payment to landowner is done for 6.54acres, balance in progress. However, few Raiyats are unwilling to accept the compensation as the award has been issued based on reduced circle rate. State Govt support required to Railways for acquisition / possession of said Land. Support of Ministry of Railways is required for timely completion of above works.
186	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	7,103.00	5,489.00	03/2013 12/2021	12/2024	141	138.48	
187	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	17,007.00	13,203.00	06/2019 10/2022	12/2024	66	18.38	1.Maintaining Law & order and resolution of following issue: 1.Acquisition of Land by CCL for external CHP. 2.Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. 3.Readiness of ATS Lines by NKT.L.
188	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	18,668.00	8,846.25	03/2023 -	03/2025	24	0	Readiness of Start-up power and ATS matching with commissioning schedule of the project Expeditious Award of construction of power evacuation and start-up power line is required. Transfer & possession of balance land. Physical possession of encumbrance free land for Ash Mound-I.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
189	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,803.00	809.11	09/2019 12/2024	07/2025	70	30.48	Support required from Govt. of WB for shifting of homesteads in PH to Surge Shaft Road. Resolution of disputes of villagers with District Administration -
	<u>Power Grid Corporation Of India Limited</u>									
190	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,160.77	07/2020 -	08/2022	25	14.11	
191	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION - [N18000339]PGCIL, MULTI STATE	11/2018	173.94 -	173.94	114.48	11/2021 -	09/2022	10	0	
192	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]PGCIL, GUJARAT	10/2019	1,031.00 -	1,143.00	985.61	08/2021 -	10/2022	14	10.86	
193	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	379.95	266.47	12/2019 -	11/2022	35	0	
194	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302]PGCIL, HARYANA	01/2019	267.33 -	267.33	86.32	03/2022 -	11/2022	8	0	
195	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	197.40	195.47	03/2018 -	12/2022	57	0	
196	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	322.30	210.54	02/2019 -	12/2022	46	0	
197	EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	235.53	164.87	06/2019 -	12/2022	42	0	
198	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 -	219.66	172.19	07/2019 -	12/2022	41	17.99	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
199	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL,MULTI STATE	09/2015	167.31 -	167.31	129.26	12/2017 -	12/2022	60	0	
200	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD - [N18000314]PGCIL,RAJASTHAN	01/2020	562.86 -	562.86	374.60	01/2021 -	12/2022	23	0	
201	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL,MULTI STATE	11/2018	241.38 -	241.38	223.80	11/2021 -	12/2022	13	0	
202	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL,RAJASTHAN	05/2021	1,184.88 -	1,184.88	80.70	09/2022 -	01/2023	4	0	
203	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308]PGCIL,MULTI STATE	02/2019	572.98 -	572.98	293.86	12/2020 -	03/2023	27	0	
204	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	2,635.55	1,891.34	02/2020 -	04/2023	38	36.46	
205	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN	06/2021	1,562.00 -	1,562.00	500.90	12/2022 -	08/2023	8	0	
206	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN	06/2021	1,006.00 -	1,006.00	660.83	12/2022 -	08/2023	8	0	
207	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303]PGCIL,RAJASTHAN	03/2021	353.85 -	353.85	134.19	12/2022 -	09/2023	9	0	
208	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305]PGCIL,RAJASTHAN	06/2021	713.82 -	713.82	323.37	12/2022 -	12/2023	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
209	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,700.00	4,097.84	12/2018 -	01/2024	61	31.08	
210	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	4,251.79	12/2018 -	03/2024	63	92.02	
	<u>Satluj Jal Vidyut Nigam Limited</u>									
211	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	947.89	915.31	12/2021 -	12/2022	12	46.2	1. Stay imposed by Hon'ble High Court of Uttarakhand on all construction activities within 200 m of the river. 2. Agitation by locals in project area. 3. Delay due to Covid-19 pandemic. 4. Geological challenges. 5. Change in Design and scope of work.6. Settlement of long stretch of road on Vikasnagar – Uttarkashi highway in Sept., 2021 affected the supply of construction material which resulted in slow progress
	<u>Thdc India Limited</u>									
212	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 -	1,587.16	742.49	09/2020 -	09/2022	24	-24.57	(i) Handing over of balance 79 Ha (out of 139 Ha) priority-I Forest land after tree felling needs to be expedited by Forest dept. (ii) Disposal of pending cases & payment of Compensation to balance PAFs and handing over of balance 116.35 Ha Private/ Tenancy land is pending with Dist Admin, Singrauli. (iii) Shifting of Govt. buildings such as schools, Anganwadi etc., private houses and felling of trees in Govt. land of Coal Block (178.13 Ha.) pending by District Administration/Forest dept.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
213	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	4,825.60	4,755.19	02/2016 06/2022	10/2023	92	191.23	• Pending transfer of additional 4.916 hectare forest land and permission for mining in Tehri district.
214	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	5,031.01	09/2023 -	08/2024	11	0	• Law & Order Issues in taking possession of small patches of land within boundary of already acquired 1201 Acre land. • Signing of Lease deed by UPSIDC is getting delayed due to Court case filed by PAFs.
215	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	2,640.57	06/2013 -	03/2025	141	54.94	• All Law & order issues have been resolved in Aug'21 with the support of GoUK/ District Administration, Chamoli.
	Total		1,39,272.91 -	1,91,717.74	1,27,440.03					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Nbcc For Health</u>									
216	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.04	1,162.76	09/2021 -	08/2022	11	8.89	
	Total		1,351.00 -	1,471.04	1,162.76					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
217	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	3,445.48	1,543.90	03/2023 -	03/2024	12	8.75	
218	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	365.59	03/2022 -	03/2024	24	0	
219	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,384.72	629.92	03/2022 -	03/2024	24	8.85	
220	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	657.66	03/2023 -	03/2024	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
221	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	542.40	03/2022 -	03/2024	24	0	
222	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	313.34	03/2023 -	03/2024	12	0	
223	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,805.17	3,140.43	03/2021 -	03/2025	48	111.54	
224	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,387.52	464.66	03/2021 -	03/2025	48	75	
225	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	2,081.27	881.45	03/2023 -	03/2025	24	10.94	
<u>East Central Railways</u>										
226	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	1,153.56	03/2020 -	03/2023	36	0	
227	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	436.16	03/2019 -	03/2023	48	0	
228	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	1,110.00	1,112.02	03/2012 -	06/2023	135	241.82	
229	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	660.90	03/2020 -	12/2023	45	0	
230	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,953.80	03/2020 -	03/2024	48	0	
231	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	624.19	03/2021 -	03/2024	36	62.06	
232	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	685.28	03/2021 -	12/2024	45	63.37	
233	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 548.00	783.83	540.74	03/2020 -	03/2025	60	43.03	
<u>East Coast Railway</u>										
234	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	439.50	10/2020 -	03/2024	41	0	
235	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGAR H	12/2012	1,160.00 -	1,160.83	1,095.89	03/2020 -	03/2024	48	.07	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
236	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	834.54	03/2022 -	03/2024	24	0	
237	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	1,027.78	06/2021 -	03/2025	45	137.8	Acquisition of balance 575.620 Ac. of Private land & 185.94 Ac. of Govt. land Balance 12924 nos. of trees to be cut out of 30734 nos. Shifting/modification of EHT/HT/LT power line crossings bet. Km. 43.50-43.98, 44.60-44.72, 45.695-45.800, 46.240, 46.550, 47.50, 48.24-48.38, 51.10, 51.54-52.00, 52.220 by TP Central Odisha Distribution Ltd.(TPCODL).
238	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	179.43	11/2018 -	03/2025	76	15.45	
239	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	825.47	12/2018 -	03/2025	75	0	
240	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	2,027.20	03/2009 12/2025	12/2025	201	29.71	Complete handover of private land by state govt as per MOU has not been made till date. 150.74acres of balance private land yet to be handed over by State Govt. of Odisha. Pending Stage-I forest clearance & working permission between Km.112-180 needs to be sanctioned for early taking up the construction works in forest land.
241	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	992.84	03/2022 -	03/2026	48	0	
242	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	729.38	03/2022 03/2026	03/2026	48	0	
	<u>Eastern Railways</u>									
243	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	525.35	03/2017 -	10/2022	67	20.3	Baruipara – Furfura (12.30 Km) New line - Work could not be started due to non-availability of land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
244	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	558.15	03/2022 -	03/2023	12	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
245	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [N22000272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	906.01	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30KM between Kamarpukur and Jairambati in Hooghly district is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non-availability of land.
	<u>Indian Railway Construction Company Limited</u>									
246	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON, CHHATISGARH	04/2013	3,055.00 -	3,500.00	2,945.30	09/2018 -	12/2023	63	14.57	
247	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON, CHHATISGARH	02/2014	2,288.00 -	4,970.11	1,509.87	03/2022 -	12/2024	33	117.23	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
248	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	5,200.00	-	03/2020 -	12/2025	69	0	
	<u>Metropolitan Rapid Transport Projects</u>									
249	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	774.51	552.70	06/2013 -	12/2022	114	56.23	
250	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,991.80	03/2004 -	03/2023	228	501.57	
	<u>North Central Railway</u>									
251	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 2,001.00	2,001.00	1,043.73	03/2021 -	12/2023	33	0	
252	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	799.75	03/2022 -	12/2024	33	32.02	
253	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	109.37	03/2023 -	03/2026	36	0	
	<u>North East Frontier Railway</u>									
254	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	708.73	380.92	03/2020 -	09/2022	30	24.42	
255	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	14,322.79	12,817.81	03/2011 -	12/2023	153	221.56	
256	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,650.00	1,255.18	03/2019 -	12/2023	57	397.31	
257	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	6,527.45	5,330.91	03/2014 -	12/2023	117	172.72	
258	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	7,876.92	3,408.77	12/2015 -	12/2023	96	488.06	
259	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	2,047.51	1,050.40	03/2019 -	12/2023	57	13.88	
260	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,145.79	990.86	03/2019 -	03/2024	60	197.45	
261	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	471.00	77.45	03/2020 -	03/2024	48	94.45	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
272	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	2,440.53	2,202.65	02/2015 -	09/2022	91	102.92	
273	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	950.00	626.34	03/2016 -	09/2022	78	50.15	
274	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	2,009.00	2,350.49	03/2020 -	09/2022	30	111.91	
275	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,405.40	03/2020 -	09/2022	30	-7.28	
276	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	2,203.53	2,075.59	12/2020 -	09/2022	21	86.23	
277	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	2,340.59	12/2020 -	09/2022	21	23.55	
278	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	433.00	455.39	03/2009 03/2009	12/2022	165	224.56	
279	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	2,538.01	2,375.23	12/2021 -	12/2022	12	63.88	
280	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	1,500.00	1,127.95	03/2022 -	12/2022	9	58.97	
281	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL, TAMIL NADU	02/2015	760.00 -	1,536.00	1,664.15	03/2020 -	12/2022	33	102.11	
282	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	1,457.79	1,408.80	03/2019 -	03/2023	48	57.26	
283	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,552.26	1,445.70	03/2019 -	03/2023	48	64.62	
284	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL, TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,284.85	03/2022 -	05/2023	14	-23.24	
285	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,267.55	03/2023 -	12/2024	21	0	
286	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	24,659.00	8,453.89	12/2024 -	03/2025	3	52.07	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
287	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,834.54	1,839.89	03/2016 -	07/2025	112	65.94	
288	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	305.05	03/2014 -	12/2025	141	18.95	
289	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	3,496.68	03/2016 -	03/2026	120	7.78	
290	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	3,327.72	2,712.78	12/2024 -	12/2026	24	42.47	
	<u>South Central Railway</u>									
291	MUNEERABAD- MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,206.22	03/2000 -	03/2023	276	98.57	
292	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	2,063.03	1,875.71	03/2021 -	03/2024	36	0	
293	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48 -	2,250.00	784.26	03/2010 -	03/2025	180	93.89	
294	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 -	1,952.68	918.80	03/2023 -	03/2025	24	5.16	
295	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,755.92	03/2022 -	03/2025	36	7.06	
296	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	1,274.68	03/2021 -	03/2026	60	0	
297	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,095.80	03/2009 -	03/2027	216	102.85	
	<u>South East Central Railway</u>									
298	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR, MAHARASHTRA	09/2016	1,908.51 -	3,176.60	1,902.75	03/2023 12/2023	12/2023	9	66.44	
299	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR, CHHATTISGARH	04/2015	1,973.00 2,135.34	2,135.34	1,106.76	03/2021 12/2023	12/2023	33	8.23	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
300	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	918.24	12/2021 12/2023	12/2023	24	.07	
301	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	88.40	12/2021 -	12/2024	36	378.6	
	<u>South Eastern Railway</u>									
302	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.97	1,264.07	03/2020 -	10/2022	31	35.38	
303	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	511.75	259.72	12/2021 -	01/2023	13	31.09	
304	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	393.83	34.60	06/2022 -	12/2023	18	16.52	
305	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	1,358.49	03/2021 -	03/2024	36	0	
306	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	1,866.31	610.05	05/2023 -	12/2024	19	0	
307	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	472.50	6.00	06/2022 -	12/2025	42	10.23	
	<u>South Western Railway</u>									
308	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,954.21	1,381.52	03/2020 -	12/2022	33	68.91	
309	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,878.00	1,611.28	03/2019 -	02/2024	59	16.31	
310	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	36.45	03/2016 -	03/2024	96	0	Out of 28.54 Ha of land in Karnataka, GoK has handed over only 8.42 Ha of land. Balance 20.12 Ha to be handed over by GoK to Rlys. Out of 99.68 Ha of land in Andhra Pradesh, GoAP has handed over 33.41 Ha of land only. Balance 66.27 Ha of land to be handed over by GoAP to Railways.
311	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	490.24	12/2018 -	06/2025	78	0	Out of 1611.2 Ha of land, 1144.09 Ha of land has been handed over by GoK. For balance 467.03 Ha, land acquisition by GoK is in progress as land to be given free by GoK.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
312	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2026	120	0	GoK have not initiated land acquisition process, although requisition to acquire land for 1000 acres has been submitted by the Railways in the year 2013 & GoK have not released any funds to concerned DCs for this purpose. Hence work could not be commenced till date.
313	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	826.18	499.13	03/2017 -	03/2026	108	28.13	Out of 132.35 Ha of land, 63.58 Ha of land only handed over by GoK. Balance 67.69 Ha of land yet to be acquired & handed over to Railways by GoK.
314	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 1,378.00	1,530.09	332.27	03/2016 -	12/2026	129	55.13	Out of 995.14 Ha of land, 703.4 Ha of land has been handed over by GOK. For balance 278.72 Ha, land acquisition by GOK is in progress as land to be given free by GOK.
	<u>Southern Railway</u>									
315	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,081.20	1,774.56	02/2019 -	03/2025	73	325.17	
316	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,084.48	321.37	03/2019 -	12/2027	105	1626.99	
	<u>West Central Railway</u>									
317	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,658.34	03/2021 03/2024	03/2024	36	585.35	
318	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 2,938.00	2,938.00	1,450.69	03/2022 03/2024	03/2024	24	18.55	
319	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	704.97	03/2022 -	09/2024	30	114.32	
320	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	1,720.50	03/2020 -	10/2024	55	38.63	
321	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	202	3230.57	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Western Railway</u>									
322	VIRAMGAM-SAMAKHALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,125.53	1,394.02	1,300.17	03/2021 12/2022	12/2022	21	34.41	
323	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,042.12	1,119.12	962.02	03/2021 12/2022	12/2022	21	11.65	
324	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	640.75	497.73	06/2020 03/2023	03/2023	33	-8.46	
325	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,631.75	2,448.99	2,142.58	03/2020 03/2024	03/2024	48	195.15	
326	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 322.19	1,083.17	252.70	03/2012 03/2024	03/2024	144	240.36	
327	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,524.68	1,524.68	1,063.17	03/2022 12/2024	12/2024	33	13.17	
328	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 692.26	692.26	8.51	03/2020 12/2024	12/2024	57	0	
329	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT	04/2018	537.31 537.31	584.31	2.44	03/2024 12/2024	12/2024	9	8.75	
330	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,873.10	1,873.10	908.51	03/2022 03/2025	03/2025	36	14.21	
331	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	6,383.82	2,529.21	03/2022 03/2026	03/2026	48	82.2	
332	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 495.18	495.18	1.01	03/2022 03/2026	03/2026	48	0	
	Total		1,76,306.09 -	3,11,937.08	1,78,060.81					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
333	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 290.15	290.15	188.56	05/2017 08/2022	08/2022	63	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
334	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 319.28	319.28	241.94	08/2017 08/2022	08/2022	60	0	
335	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 234.73	234.73	262.20	08/2018 08/2022	08/2022	48	-18.97	
336	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 241.60	241.60	164.41	02/2017 12/2020	08/2022	66	37.66	
337	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	190.01	04/2020 -	08/2022	28	-8.28	
338	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	467.04	01/2020 06/2021	09/2022	32	0	
339	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	927.73	784.39	02/2020 08/2021	09/2022	31	-3.11	
340	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	172.00	108.00	06/2016 09/2022	09/2022	75	.02	
341	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	635.00	07/2018 05/2021	09/2022	50	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
342	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	949.54	807.22	06/2019 04/2021	09/2022	39	8.17	
343	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 913.49	913.49	700.54	11/2018 06/2021	09/2022	46	5.24	Delay in obtaining utility shifting estimate from the concern department,obtaining forest clearance and tree cutting operation,obtaining approval for GAD and finalization of COS
344	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	545.64	216.28	07/2019 -	09/2022	38	0	
345	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	313.95	142.29	06/2019 -	09/2022	39	0	
346	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	376.19	113.66	05/2019 -	09/2022	40	0	
347	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	420.63	209.61	05/2020 -	09/2022	28	0	
348	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	323.02	06/2019 -	09/2022	39	0	
349	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	301.38	195.29	08/2020 -	09/2022	25	0	
350	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	653.46	287.45	07/2019 -	09/2022	38	0	
351	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	488.60	240.92	07/2019 -	09/2022	38	0	
352	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	381.77	186.62	06/2019 -	09/2022	39	0	
353	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	743.21	475.80	06/2021 -	09/2022	15	0	
354	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 2,226.11	983.14	806.99	12/2019 -	09/2022	33	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
355	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STATE - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	314.90	206.30	03/2017 03/2021	09/2022	66	0	
356	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	159.12	123.72	01/2016 12/2021	09/2022	80	0	
357	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	125.56	05/2019 -	09/2022	40	0	
358	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	165.67	124.52	11/2015 12/2021	10/2022	83	0	
359	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	282.08	206.46	06/2019 10/2022	10/2022	40	0	
360	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	418.88	264.67	02/2020 10/2022	10/2022	32	0	
361	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	248.00	111.85	05/2020 10/2022	10/2022	29	0	
362	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	238.00	94.55	11/2019 -	10/2022	35	.08	
363	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	10/2022	55	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
364	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	174.90	154.26	08/2018 08/2021	10/2022	50	5.23	
365	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	206.89	08/2018 09/2021	10/2022	50	4.45	
366	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	184.37	03/2018 10/2021	10/2022	55	0	
367	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	219.86	07/2018 08/2021	10/2022	51	0	
368	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	197.45	02/2018 03/2022	10/2022	56	0	
369	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	195.15	03/2019 -	10/2022	43	0	"On account of delay in getting approval of GAD and other various approvals from Railway authorities. At present there is no issue."
370	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	199.16	101.34	08/2018 10/2022	10/2022	50	0	
371	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	293.64	283.78	08/2020 -	10/2022	26	0	COVID and delay in design approval by Railway
372	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	428.55	404.69	03/2018 06/2021	10/2022	55	9.23	
373	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	323.36	237.25	08/2020 -	10/2022	26	12.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
374	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	302.65	01/2018 -	10/2022	57	0	
375	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 225.06	225.06	212.91	05/2016 06/2022	11/2022	78	25.84	
376	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 587.41	587.41	553.81	05/2016 03/2022	11/2022	78	6.16	
377	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	141.48	02/2018 09/2021	11/2022	57	0	
378	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	137.88	03/2017 12/2021	11/2022	68	0	
379	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	223.50	132.37	08/2018 11/2022	11/2022	51	0	
380	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	206.88	134.11	04/2018 11/2022	11/2022	55	0	
381	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	214.23	138.74	08/2018 11/2022	11/2022	51	0	
382	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	643.29	05/2016 11/2022	11/2022	78	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
383	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	295.47	214.36	02/2017 12/2022	12/2022	70	0	
384	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	432.54	08/2017 06/2021	12/2022	64	0	
385	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 -	396.86	282.77	09/2019 03/2022	12/2022	39	0	
386	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	90.24	03/2018 09/2021	12/2022	57	0	
387	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	293.10	256.89	08/2020 -	12/2022	28	0	"Delay due to approval of revised estimate which has now been approved in Feb, 2021. Possession of land in approx. 200 mtr. yet to be handed over by CALA, Budhlada."
388	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	739.08	10/2019 -	12/2022	38	0	Work in progress. Work in District Hoshiarpur held up due LA issue. DC has submitted report to FCR on 23.06.2021. The Change of Scope as per existing ROW submitted on 10.01.2022 to RO, MORT&H for approval. The agency has terminated the agreement and issued termination notice vide their letter dated 27.06.2022
389	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	87.84	11/2020 -	12/2022	25	0	LA issue for ROB in Km 12

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
390	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	962.43	594.81	03/2018 -	12/2022	57	0	Delay in Approval of GAD & Construction drawing, Delay in Approvals of Mix Design, Proof Consultant, Construction Material and steel etc from Authority
391	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	325.56	01/2017 12/2022	12/2022	71	0	Delay in LA
392	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 263.45	263.45	127.85	09/2017 12/2022	12/2022	63	0	LA issues
393	REHABILITATION AND UPGRADEMENT OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 686.13	686.13	503.77	01/2018 12/2022	12/2022	59	19.02	
394	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	283.15	201.27	05/2020 12/2022	12/2022	31	0	
395	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	363.82	109.56	09/2019 -	12/2022	39	0	
396	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	237.40	31.41	05/2020 -	12/2022	31	0	
397	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	237.00	06/2019 -	12/2022	42	0	
398	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	404.33	114.51	05/2020 -	12/2022	31	0	
399	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	381.08	21.02	05/2020 -	12/2022	31	0	
400	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	341.80	203.09	06/2019 -	12/2022	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
401	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	1,230.02	664.06	11/2019 -	12/2022	37	0	
402	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	160.00	138.51	09/2021 12/2022	12/2022	15	0	
403	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	179.94	03/2021 11/2021	12/2022	21	0	
404	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	572.66	280.46	08/2016 -	12/2022	76	15.19	
405	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	277.98	06/2017 -	12/2022	66	0	
406	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	731.50	471.29	10/2016 -	12/2022	74	17.04	
407	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	435.61	126.17	07/2016 -	12/2022	77	-3.83	
408	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	90.53	05/2021 12/2022	12/2022	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
409	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	264.34	181.38	09/2017 04/2021	12/2022	63	0	
410	FOUR LANEING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	2,138.16	1,412.08	10/2016 03/2022	03/2023	77	51.77	
411	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	125.25	11/2018 03/2022	03/2023	52	7.39	
412	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 -	426.18	284.89	09/2020 03/2022	03/2023	30	0	
413	DEVELOPMENT OF 4-LANEING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 -	254.30	130.87	10/2020 03/2022	03/2023	29	0	
414	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 -	213.97	47.17	08/2019 11/2022	03/2023	43	33.51	
415	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 -	263.26	91.29	08/2019 08/2022	03/2023	43	11.18	
416	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	242.61	94.29	06/2019 01/2022	03/2023	45	51.66	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
417	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	544.00	452.11	09/2016 -	03/2023	78	14.24	
418	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	240.11	03/2015 -	03/2023	96	0	
419	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	42.15	03/2021 03/2023	03/2023	24	0	
420	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	248.83	149.11	03/2019 04/2023	04/2023	49	0	
421	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	89.32	03/2018 03/2022	05/2023	62	0	
422	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	626.76	227.71	07/2020 05/2023	05/2023	34	0	
423	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 187.61	157.32	24.20	05/2019 05/2023	05/2023	48	0	
424	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT - [N24001423]MoRTH,UTTAR PRADESH	04/2021	309.48 -	309.48	27.13	03/2022 -	09/2023	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
425	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W - [N24001424]MoRTH,UTTAR PRADESH	03/2021	185.09 -	185.09	3.58	03/2022 -	09/2023	18	0	
426	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	423.15	216.18	12/2019 12/2022	12/2023	48	0	
427	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	217.35	173.98	11/2020 12/2022	09/2022	22	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
428	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	259.79	158.07	11/2018 -	08/2022	45	54.28	
429	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	252.05	171.06	04/2017 -	08/2022	64	27.16	
430	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA	06/2020	347.36 -	347.36	154.53	01/2022 08/2022	08/2022	7	0	
431	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	873.91	559.13	11/2018 -	09/2022	46	48.38	
432	CONSTRUCT ION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	119.22	09/2018 -	09/2022	48	0	
433	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	175.49	11/2017 -	09/2022	58	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
434	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	165.99	05/2019 -	09/2022	40	0	
435	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	263.31	172.68	04/2017 -	10/2022	66	29.48	
436	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA	03/2020	247.76 -	247.76	67.01	01/2022 -	10/2022	9	0	
437	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND	03/2020	278.95 -	278.95	128.23	06/2022 -	10/2022	4	0	
438	2-LANING OF KHOWAI - AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]NHIDCL,TRIPURA	09/2020	173.17 -	173.17	21.34	04/2022 -	10/2022	6	0	
439	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	252.79	180.00	04/2017 -	11/2022	67	29.48	
440	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	199.63	09/2018 -	11/2022	50	0	
441	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM	08/2020	278.46 -	278.46	120.18	03/2022 -	11/2022	8	0	
442	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL,MANIPUR	07/2020	177.76 -	177.76	70.23	08/2022 -	11/2022	3	0	
443	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	289.99	120.17	12/2018 -	12/2022	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
444	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	330.30	141.13	01/2016 -	12/2022	83	31.07	
445	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	284.09	188.40	04/2017 -	12/2022	68	0	
446	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL, UTTARAKHAND	03/2018	274.31 -	274.31	143.41	05/2018 -	12/2022	55	0	
447	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL, UTTARAKHAND	03/2018	403.36 -	403.36	230.60	06/2018 -	12/2022	54	0	
448	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL, UTTARAKHAND	03/2018	417.24 -	417.24	295.36	05/2018 -	12/2022	55	0	
449	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS	02/2018	391.00 -	391.00	22.17	10/2018 -	12/2022	50	0	
450	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	86.37	09/2018 -	12/2022	51	0	
451	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL, JAMMU AND KASHMIR	03/2018	253.44 -	253.44	112.59	07/2019 -	12/2022	41	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
452	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM	03/2020	242.97 -	242.97	68.35	06/2022 -	12/2022	6	0	
453	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR	07/2020	228.39 -	228.39	14.76	04/2022 -	12/2022	8	0	
454	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR	07/2020	210.79 -	210.79	20.59	04/2022 -	12/2022	8	0	
455	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 1B) - [N24001269]NHIDCL,ASSAM	03/2020	216.49 -	216.49	65.59	03/2022 -	12/2022	9	0	
456	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL,MANIPUR	03/2020	292.24 -	292.24	98.42	06/2022 -	12/2022	6	0	
457	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL,MANIPUR	06/2020	365.53 -	365.53	118.82	08/2022 -	12/2022	4	0	
458	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL,MANIPUR	03/2020	167.95 -	167.95	77.72	06/2022 -	12/2022	6	0	
459	KAILASHAHAR TO KHOWAI PKG- 5 - [N24001308]NHIDCL,TRIPURA	11/2020	332.14 -	332.14	56.56	07/2022 11/2022	12/2022	5	0	
460	KAILASHAHAR TO KHOWAI PKG- 4 - [N24001309]NHIDCL,TRIPURA	11/2020	159.13 -	159.13	30.58	06/2022 -	12/2022	6	0	
461	KAILASHAHAR TO KHOWAI PKG- 3 - [N24001310]NHIDCL,TRIPURA	11/2020	280.91 -	280.91	148.65	07/2022 -	12/2022	5	0	
462	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]NHIDCL,MANIPUR	03/2020	167.95 -	167.95	77.77	06/2022 -	12/2022	6	0	
463	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA	06/2020	201.99 -	201.99	49.65	01/2022 -	12/2022	11	0	
464	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]NHIDCL,SIKKIM	09/2020	183.31 -	183.31	87.22	05/2022 -	12/2022	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
465	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]NHIDCL,SIKKIM	08/2020	292.80 -	292.80	52.83	05/2022 -	12/2022	7	0	
466	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]NHIDCL,NAGALAND	03/2020	206.53 -	206.53	95.95	06/2022 -	12/2022	6	0	
467	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390]NHIDCL,ARUNACHAL PRADESH	08/2020	228.71 -	228.71	67.40	04/2022 04/2022	12/2022	8	0	
468	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]NHIDCL,ARUNACHAL PRADESH	08/2020	294.04 -	294.04	109.59	04/2022 12/2022	12/2022	8	0	
469	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]NHIDCL,ARUNACHAL PRADESH	08/2020	199.03 -	199.03	70.58	04/2022 12/2022	12/2022	8	0	
470	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]NHIDCL,ARUNACHAL PRADESH	08/2020	184.88 -	184.88	57.76	04/2022 12/2022	12/2022	8	0	
471	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH	08/2020	301.06 -	301.06	45.78	04/2022 -	01/2023	9	0	
472	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH	09/2020	353.90 -	353.90	34.28	05/2022 -	01/2023	8	0	
473	2-LANING OF KHOWAI - AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]NHIDCL,TRIPURA	03/2020	165.54 -	165.54	37.19	07/2022 -	01/2023	6	0	
474	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM	03/2021	636.42 -	418.49	96.45	12/2022 -	01/2023	1	-34.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
475	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL, MANIPUR	08/2020	379.39 -	379.39	22.07	04/2022 -	02/2023	10	0	
476	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	801.54	185.26	06/2018 -	03/2023	57	72.94	
477	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL, A & N ISLANDS	03/2015	262.97 -	262.97	30.00	10/2018 -	03/2023	53	0	
478	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL, NAGALAND	09/2020	315.63 -	315.63	12.23	04/2022 -	03/2023	11	0	
479	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL, TRIPURA	03/2020	178.43 -	178.43	28.82	07/2022 03/2023	03/2023	8	0	
480	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL, MANIPUR	03/2019	471.00 -	471.00	251.05	07/2022 -	03/2023	8	0	
481	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]NHIDCL, ASSAM	03/2020	261.13 -	261.13	45.67	06/2022 -	03/2023	9	0	
482	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL, MIZORAM	04/2017	519.09 -	519.09	220.92	09/2019 -	04/2023	43	0	
483	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL, MIZORAM	04/2017	473.18 -	473.18	201.83	09/2019 -	04/2023	43	0	
484	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL, MIZORAM	04/2017	537.82 -	537.82	237.48	09/2019 -	04/2023	43	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
485	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL, ASSAM	08/2020	208.84 -	208.84	27.93	04/2022 -	04/2023	12	0	
486	DOGINALA - GAU - [N24001320]NHIDCL, ARUNACHAL PRADESH	12/2020	242.30 -	242.30	15.04	09/2022 -	04/2023	7	0	
487	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]NHIDCL, MEGHALAYA	10/2020	157.86 -	157.86	81.82	04/2022 -	04/2023	12	0	
488	TAMENGLONG - MAHUR PKG-3 - [N24001354]NHIDCL, MANIPUR	03/2021	234.08 -	234.08	32.64	12/2022 -	04/2023	4	0	
489	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL, SIKKIM	03/2019	402.94 -	402.94	118.12	04/2022 -	05/2023	13	0	
490	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL, NAGALAND	03/2018	272.89 -	272.89	103.64	09/2018 -	06/2023	57	0	
491	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM	03/2015	829.00 -	1,307.50	411.51	01/2016 -	06/2023	89	57.72	
492	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL, MIZORAM	04/2017	642.96 -	642.96	234.97	09/2019 -	06/2023	45	0	
493	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL, MIZORAM	04/2017	518.53 -	518.53	234.73	09/2019 -	06/2023	45	0	
494	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL, NAGALAND	08/2020	202.36 -	202.36	15.41	04/2022 -	06/2023	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
495	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	271.82	09/2019 -	07/2023	46	0	
496	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	182.20	09/2019 -	09/2023	48	0	
497	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]NHIDCL,SIKKIM	08/2020	230.45 -	230.45	32.58	04/2023 09/2023	09/2023	5	0	
498	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR	07/2021	467.00 -	467.00	50.90	03/2023 -	09/2023	6	0	
499	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 244.10	180.57	18.01	04/2017 11/2023	11/2023	79	0	
500	MARAM - PEREN PKG-3 - [N24001439]NHIDCL,MANIPUR	08/2021	467.41 -	467.41	20.74	05/2023 -	11/2023	6	0	
501	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND	09/2020	277.44 -	277.44	55.34	10/2022 -	12/2023	14	0	
502	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]NHIDCL,SIKKIM	09/2020	262.84 -	262.84	129.59	05/2023 -	01/2024	8	0	
503	LADDA - BASAI - [N24001316]NHIDCL,ARUNACHAL PRADESH	02/2021	445.96 -	445.96	2.94	04/2023 -	02/2024	10	0	
504	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	362.22	07/2018 -	03/2024	68	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
505	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	145.96	09/2019 -	04/2024	55	0	
506	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]NHIDCL,SIKKIM	10/2020	493.42 -	493.42	12.26	11/2023 -	05/2024	6	0	
507	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]NHIDCL,SIKKIM	10/2020	816.79 -	816.79	15.85	12/2023 11/2024	11/2024	11	0	
	<u>National Highways Authority Of India</u>									
508	FOUR LANNING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 819.35	819.35	439.27	05/2018 03/2022	08/2022	51	37.32	
509	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	1,664.20	1,301.27	04/2020 -	08/2022	28	0	Stoppage of work by the villagers for demand of structures at Bandiwad, Shiraguppi, Talakal and Halligudi villages. Now the issues of all villages resolved except Shiraguppi. Work is in progress. Further the project is delayed due to COVID-19 pandemic also.
510	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,405.27	1,401.96	03/2020 -	08/2022	29	2.33	
511	FOUR LANNING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,827.00	1,306.69	03/2021 -	08/2022	17	19.21	
512	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	1,020.00	12/2019 -	08/2022	32	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
513	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	908.00	03/2020 -	08/2022	29	0	
514	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	879.00	05/2020 -	08/2022	27	0	
515	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	996.27	965.00	03/2020 -	08/2022	29	0	
516	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,919.69	03/2013 -	09/2022	114	0	
517	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,935.64	06/2014 -	09/2022	99	0	
518	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	09/2022	53	0	
519	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 2,408.72	2,408.72	1,865.00	04/2019 -	09/2022	41	13.15	
520	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,405.30	2,328.27	2,126.16	07/2018 12/2021	09/2022	50	249.07	
521	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 3,150.00	3,063.99	2,904.36	04/2019 12/2021	09/2022	41	93.01	
522	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	1,309.30	03/2020 -	09/2022	30	10.58	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
523	WIDENING OF KHEDE-SINAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	10/2022	104	0	
524	REHABILITATION AND UPGRADE OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	275.93	07/2017 -	10/2022	63	0	
525	2-LANING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	494.33	04/2014 -	11/2022	103	0	
526	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	157.49	31.97	03/2020 -	11/2022	32	-36.24	
527	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	446.97	170.57	11/2020 -	11/2022	24	0	Project Not Delayed.
528	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	464.09	174.53	11/2020 -	11/2022	24	0	
529	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	12/2022	116	0	
530	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 1,046.56	1,046.56	822.13	06/2018 12/2022	12/2022	54	10.63	Change in demand time to time by local as well as public representative for flyover like Kundapur, Pumpwell etc
531	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	18.66	
532	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	768.92	03/2014 -	12/2022	105	0	
533	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 480.35	777.03	766.05	05/2018 -	12/2022	55	46.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
534	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	277.75	03/2019 12/2022	12/2022	45	0	
535	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	869.13	11/2016 -	12/2022	73	0	
536	4-LANING OF GOA/KARNATKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATKA	05/2014	1,655.01 2,639.00	2,639.00	1,710.83	08/2016 12/2022	12/2022	76	59.46	"a) Due to non-availability of work front on account of non-disbursement of land compensation to the land owners, since the land owners are not coming forward to accept the LA compensation as many of the land owners are out of country. However, the action has been taken to issue the 3E notification. The same is under implementation by the district administration. b) Frequent transfer of SLAO delays in disbursement of compensation. 1. Due to non-availability of work front on account of non-disbursement of land compensation to the land owners, since the land owners are not coming forward to accept the LA compensation as many of the land owners are out of country. However, the action has been taken to issue the 3E notification. The same is under implementation by the district administration 2. Frequent transfer of SLAO delays in disbursement of compensation. 3)VIP's and Local Publics are demanding for additional sections and facilities. This also major cause for delay of the project

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
537	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	1,543.51	1,472.50	03/2018 03/2021	12/2022	57	65.18	
538	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 567.00	639.58	492.38	04/2019 07/2022	12/2022	44	-38.57	Nil
539	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,288.97	2,136.97	1,921.25	12/2018 12/2022	12/2022	48	0	
540	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,603.99	2,323.88	2,223.06	06/2018 12/2021	12/2022	54	185.04	
541	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,192.10	3,006.53	2,989.89	06/2018 12/2021	12/2022	54	350.75	
542	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	242.52	03/2019 -	12/2022	45	0	
543	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	252.08	03/2020 -	12/2022	33	0	
544	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	880.00	04/2020 -	12/2022	32	3.95	
545	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	649.90	155.54	12/2020 -	12/2022	24	0	Project Not Delayed.
546	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	732.34	530.71	11/2019 01/2022	12/2022	37	.06	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
547	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	361.70	304.45	11/2019 -	12/2022	37	-21	
548	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	606.75	410.81	11/2019 -	12/2022	37	2.02	
549	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 1,414.01	1,414.01	1,000.57	06/2018 -	01/2023	55	30.56	bin naguri 5.1 km land acquisition issue
550	SIX LANING OF CHANDIKHOL- JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,855.00	06/2014 -	02/2023	104	0	
551	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI, ANDHRA PRADESH	11/2019	1,226.88 1,240.13	1,321.60	678.20	02/2021 04/2021	02/2023	24	7.72	
552	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	1,587.77	02/2013 12/2022	03/2023	121	0	
553	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 526.09	526.09	189.10	04/2014 -	03/2023	107	-15.69	
554	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI, KARNATAKA	03/2016	701.40 -	701.40	156.33	03/2019 03/2023	03/2023	48	0	NA
555	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 756.27	665.19	528.73	03/2020 03/2023	03/2023	36	-11.84	
556	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 736.01	830.31	31.82	03/2020 12/2018	03/2023	36	23.39	Procedural delay in Land Acquisition. Now, disbursement to land owner is under progress and possession of land received.
557	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI, KERALA	09/2017	1,124.11 -	1,309.79	1,162.72	09/2017 05/2021	03/2023	66	16.52	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
558	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	63.30	12/2017 -	05/2023	65	0	
559	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	2,004.66	08/2013 -	06/2023	118	0	
560	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	380.24	03/2019 06/2023	06/2023	51	-25.48	
561	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	2,510.04	658.95	08/2019 -	06/2023	46	0	
562	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	1,208.03	06/2020 -	06/2023	36	0	
563	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	347.64	07/2019 07/2023	07/2023	48	0	Nil
564	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	716.00	-	07/2021 -	07/2023	24	0	
565	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	1,168.33	503.74	08/2017 08/2023	08/2023	72	22.9	Delay in providing the vacant access and Right of way to the site and adverse law and order situation in an around the project area.
566	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	1,101.99	424.90	02/2020 -	08/2023	42	0	
567	4L OF ADDAHOLE TO BANTWAL CROSS SECTION - [N24001426]NHAI,KARNATAKA	03/2021	317.90 317.90	317.90	127.41	10/2021 -	09/2023	23	0	NA
568	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	332.33	07/2019 10/2023	10/2023	51	0	Nil
569	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN - [N24001425]NHAI,KARNATAKA	03/2021	1,100.88 1,100.88	1,100.88	261.90	11/2021 -	11/2023	24	0	NA

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
570	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428]NHAI,TAMIL NADU	03/2018	998.70 -	998.70	-	11/2021 -	11/2023	24	0	
571	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429]NHAI,TAMIL NADU	03/2018	1,294.47 -	1,294.47	-	11/2021 -	11/2023	24	0	
572	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	1,190.60	06/2019 -	12/2023	54	0	
573	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431]NHAI,TAMIL NADU	03/2018	1,872.68 -	1,872.68	-	10/2020 -	12/2023	38	0	
574	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 -	724.60	680.12	03/2023 -	01/2024	10	0	
575	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430]NHAI,TAMIL NADU	03/2018	2,120.40 -	2,120.40	-	01/2022 -	01/2024	24	0	
576	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	989.66	-	01/2024 -	04/2024	3	0	
577	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 1,380.73	1,380.73	1,354.65	12/2013 05/2024	05/2024	125	10.46	
578	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	982.00	-	03/2020 07/2022	07/2024	52	31.88	Nil

Details of Delayed Projects w.r.t. Original Schedule

[illegible]

Details of Delayed Projects w.r.t. Original Schedule

[illegible]

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>WATER RESOURCES</u>									
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
596	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO, BIHAR	05/2017	356.37 -	356.37	215.30	04/2021 -	09/2022	17	0	
597	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO, BIHAR	11/2018	236.15 -	236.15	80.59	12/2020 -	10/2022	22	0	
598	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO, BIHAR	03/2017	277.42 -	277.42	298.55	05/2021 -	10/2022	17	0	
599	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO, BIHAR	08/2017	578.89 -	578.89	16.55	06/2022 -	12/2022	6	0	
600	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO, BIHAR	08/2017	824.00 -	824.00	140.17	06/2022 -	12/2022	6	0	
601	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO, BIHAR	03/2018	230.06 -	230.06	137.93	07/2021 -	03/2023	20	0	
602	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19 -	305.19	146.80	08/2021 -	08/2023	24	0	
603	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO, BIHAR	03/2018	294.02 -	294.02	90.96	10/2021 -	12/2023	26	0	
604	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 413.29	413.29	.07	09/2020 -	03/2024	42	62.63	
	<u>Delhi Jal Board</u>									
605	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI	05/2016	211.79 -	211.79	136.75	12/2021 -	12/2022	12	0	
606	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI	05/2016	239.11 -	239.11	205.76	02/2022 -	12/2022	10	0	
	<u>Kolkata Metropolitan Development Authority</u>									
607	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	185.22	36.83	12/2021 -	09/2023	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
626	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD FOR DEFENC, KARNATAKA	12/2016	246.31 210.00	200.00	181.63	02/2020 08/2022	10/2022	32	-18.8	
	Total		246.31 -	200.00	181.63					
	<u>DEPARTMENT OF HIGHER EDUCATION</u>									
	<u>Cpwd Of Higher Education</u>									
627	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION, JAMMU AND KASHMIR	03/2019	424.93 -	424.93	209.30	07/2022 10/2022	10/2022	3	0	
628	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION, CHHATTISGARH	03/2020	808.62 -	808.62	536.84	07/2022 -	10/2022	3	0	
629	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION, KARNATAKA	07/2019	851.00 851.00	851.00	466.32	03/2022 10/2022	10/2022	7	0	
630	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION, ANDHRA PRADESH	02/2019	655.34 -	655.34	469.33	06/2020 -	11/2022	29	0	
631	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION, BIHAR	09/2018	375.00 -	375.00	175.10	09/2020 -	11/2022	26	0	
632	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION, BIHAR	02/2016	496.18 496.00	460.00	342.91	06/2017 06/2022	12/2022	66	-7.29	
633	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION, PUNJAB	01/2018	430.00 -	387.83	258.31	05/2020 -	12/2022	31	-9.81	Nil

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
634	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION, WEST BENGAL	03/2020	193.83 -	193.83	64.30	06/2020 -	12/2022	30	0	
635	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION, ODISHA	01/2019	790.79 -	790.79	394.21	03/2022 -	01/2023	10	0	
636	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION, GOA	05/2019	303.90 334.45	334.45	140.00	03/2020 -	02/2023	35	10.05	
637	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION, KERALA	07/2019	753.63 -	753.63	291.95	03/2021 -	03/2023	24	0	
638	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION, PUNJAB	10/2019	348.24 -	348.24	81.58	05/2022 -	03/2023	10	0	
639	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION, HIMACHAL PRADESH	09/2018	392.51 -	392.51	106.00	06/2022 04/2023	04/2023	10	0	The land provided by the Government of Himachal Pradesh is not free from encumbrances such as the buildings vacated by (6th IRBN) partially handed over to CPWD by the concerned Agriculture Department. The land has not been demarcated at certain locations which is hampering in the construction of the Campus Buildings and Boundary wall. Existing road connects to the Gujjar Colony, Naurangabad is passing through the middle of land allocated to IIM Sirmaur. Work of various services, road & development is held up due to this.

Details of Delayed Projects w.r.t. Original Schedule

[illegible]

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
647	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	5,178.00	3,032.83	12/2019 -	01/2023	37	8.49	
	Total		4,773.00 -	5,178.00	3,032.83					
	Grand Total		9,57,839.23	12,60,856.62	7,54,269.22					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(August 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	7,500.00	6,433.54	09/2010 -	09/2024	114.78	168
	<u>Nuclear Power Corporation Of India Limited</u>								
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00 -	17,079.00	14,876.00	12/2016 -	12/2023	38.63	84
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	19,220.00	18,523.00	12/2015 -	06/2023	67.73	90
	Total		27,271.00 -	43,799.00	39,832.54				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]	11/2016	303.80 -	351.21	247.98	04/2020 -	12/2022	15.61	32
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	192.21	09/2021 -	12/2023	38.72	27
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	570.11	09/2018 -	10/2022	69.63	49
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	426.51	03/2021 -	03/2025	7.88	48
8	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 -	2,445.00	797.96	09/2021 -	09/2023	76.79	24
	Total		3,592.30 -	5,216.27	2,234.77				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
9	MADHUBAND NLW WASHERY - [N06000126]	08/2010	289.45 -	302.00	296.38	05/2014 -	09/2022	4.34	100
10	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	44.58	04/2018 -	06/2023	37.56	62
11	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	139.20	03/2017 -	12/2022	12.20	69
	<u>Eastern Coal Fields Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
12	RANIGANJ MASTER PLAN - [N06000163 <u>Mahanadi Coal Fields Limited</u>	08/2009	2,661.73 -	5,146.48	648.15	08/2019 -	08/2024	93.35	60
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068 <u>Neyveli Lignite Corporation</u>	11/2008	479.53 -	868.37	874.49	03/2013 -	03/2024	81.09	132
14	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152	07/2016	17,237.00 -	17,237.80	13,965.29	11/2021 -	11/2023	.00	24
	Total		21,214.84 -	24,230.14	15,968.09				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								
15	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002	05/2019	303.90 -	334.45	140.00	03/2020 -	02/2023	10.05	35
	Total		303.90 -	334.45	140.00				
	<u>DPIIT</u>								
	<u>licc For Dpiit</u>								
16	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002	11/2017	4,773.00 -	5,178.00	3,032.83	12/2019 -	01/2023	8.49	37
	Total		4,773.00 -	5,178.00	3,032.83				
	<u>FINANCE</u>								
	<u>Cpwd For Finance</u>								
17	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089	12/2015	209.00 -	262.00	208.93	10/2019 -	10/2022	25.36	36
	Total		209.00 -	262.00	208.93				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Nbcc For Health</u>								
18	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.04	1,162.76	09/2021 -	08/2022	8.89	11
	Total		1,351.00 -	1,471.04	1,162.76				
	<u>HOME AFFAIRS</u>								
	<u>Cpwd For Mha</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
19	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	210.83	176.16	04/2018 -	09/2023	29.44	65
20	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002	06/2019	277.35 -	290.33	63.23	07/2022 -	06/2023	4.68	11
21	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,679.02	1,036.04	10/2019 -	12/2022	37.71	38
	Total		1,659.44 -	2,180.18	1,275.43				
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
22	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	581.00	96.18	11/2020 -	12/2023	63.66	37
23	UTKAL D AND E COAL BLOCK - [N10000011	05/2016	534.00 -	667.23	497.21	01/2020 -	11/2023	24.95	46
24	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT [N10000010	12/2014	4,103.00 5,055.00	5,055.00	1,486.31	04/2021 -	01/2024	23.20	33
	Total		4,992.00 -	6,303.23	2,079.70				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
25	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	19.51	02/2017 -	09/2022	117.11	67
26	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	972.00	06/2019 -	02/2023	35.54	44
	<u>Gas Authority Of India Limited</u>								
27	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 -	247.90	154.74	02/2021 -	10/2022	9.91	20
28	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	255.10	08/2020 -	12/2022	14.17	28
29	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272	03/2017	1,933.00 -	2,105.70	1,811.30	12/2020 -	11/2022	8.93	23
30	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,570.80	12/2012 -	02/2025	102.71	146
	<u>Hindustan Petroleum Corporation Limited</u>								
31	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,185.00	2,943.70	06/2021 -	08/2022	18.98	14

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
32	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	20,025.46	07/2020 -	03/2023	25.50	32
	<u>Indian Oil Corporation Limited</u>								
33	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	04/2017	163.02 -	207.36	152.03	04/2020 -	10/2022	27.20	30
34	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	04/2018	206.63 -	340.76	220.01	02/2020 -	02/2023	64.91	36
35	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	06/2019	371.00 -	427.10	99.98	09/2022 -	03/2023	15.12	6
36	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	05/2016	348.00 -	437.00	271.34	01/2021 -	12/2022	25.57	23
37	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	543.00	291.80	09/2021 -	12/2022	17.46	15
38	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	753.89	602.73	02/2020 -	12/2022	26.07	34
39	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	684.72	10/2017 -	12/2022	103.60	62
40	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	05/2016	1,945.00 -	2,145.00	1,801.97	02/2022 -	12/2022	10.28	10
41	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,446.06	03/2021 -	10/2022	66.09	19
42	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	3,250.17	12/2020 -	12/2022	43.82	24
43	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	4,938.92	12/2018 -	11/2023	33.98	59
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
44	DEVANGONTHI MARKETING TERMINAL - [N16000401]	06/2020	200.00 -	304.00	41.00	06/2023 -	01/2024	52.00	7
	<u>Oil & Natural Gas Corporation Limited</u>								
45	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	05/2019	763.92 -	829.58	830.87	12/2020 -	12/2022	8.60	24
46	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.34	1,680.76	05/2013 -	12/2022	132.23	115
47	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,911.17	04/2018 -	05/2023	5.80	61
48	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	2,816.87	03/2022 -	05/2023	23.16	14
	<u>Oil India Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	423.10	02/2020 -	12/2022	17.41	34
	Total		52,886.08 -	70,624.95	53,216.11				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
50	KALPI SOLAR POWER PROJECT - [N18000323]	07/2020	314.64 -	337.77	218.26	03/2022 -	12/2022	7.35	9
51	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	10,463.03	10,010.30	09/2009 -	12/2023	166.94	171
52	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	16,222.78	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								
53	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	243.32	10/2021 -	08/2022	11.93	10
54	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 -	524.83	506.75	09/2021 -	09/2022	4.70	12
55	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	679.00	549.68	11/2018 -	12/2022	28.19	49
56	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 -	852.90	637.22	09/2021 -	09/2022	6.85	12
57	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	809.11	09/2019 -	07/2025	30.48	70
58	NOKHRA - [N18000282]	03/2020	1,722.14 -	1,803.19	1,193.45	09/2021 -	01/2023	4.71	16
59	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	7,103.00	5,489.00	03/2013 -	12/2024	138.48	141
60	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	9,540.00	11/2020 -	06/2023	3.76	31
61	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	13,203.00	06/2019 -	12/2024	18.38	66
62	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	20,184.00	10/2011 -	03/2024	145.16	149
	<u>Power Grid Corporation Of India Limited</u>								
63	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	172.19	07/2019 -	12/2022	17.99	41
64	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]	10/2019	1,031.00 -	1,143.00	985.61	08/2021 -	10/2022	10.86	14
65	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 -	2,635.55	1,891.34	02/2020 -	04/2023	36.46	38

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
66	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,160.77	07/2020 -	08/2022	14.11	25
67	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	4,097.84	12/2018 -	01/2024	31.08	61
68	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	4,251.79	12/2018 -	03/2024	92.02	63
	<u>Satluj Jal Vidyut Nigam Limited</u>								
69	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	915.31	12/2021 -	12/2022	46.20	12
	<u>Thdc India Limited</u>								
70	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,640.57	06/2013 -	03/2025	54.94	141
71	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,755.19	02/2016 -	10/2023	191.23	92
	Total		73,662.78 -	1,26,624.66	101,677.48				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
72	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,384.72	629.92	03/2022 -	03/2024	8.85	24
73	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	464.66	03/2021 -	03/2025	75.00	48
74	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	881.45	03/2023 -	03/2025	10.94	24
75	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	1,543.90	03/2023 -	03/2024	8.75	12
76	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,805.17	3,140.43	03/2021 -	03/2025	111.54	48
	<u>East Central Railways</u>								
77	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	783.83	540.74	03/2020 -	03/2025	43.03	60
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,110.00	1,112.02	03/2012 -	06/2023	241.82	135
79	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	624.19	03/2021 -	03/2024	62.06	36
80	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	685.28	03/2021 -	12/2024	63.37	45
	<u>East Coast Railway</u>								
81	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	179.43	11/2018 -	03/2025	15.45	76

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
82	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	1,095.89	03/2020 -	03/2024	.07	48
83	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	1,027.78	06/2021 -	03/2025	137.80	45
84	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	2,027.20	03/2009 -	12/2025	29.71	201
	<u>Eastern Railways</u>								
85	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	525.35	03/2017 -	10/2022	20.30	67
86	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	906.01	03/2019 12/2009	03/2025	36.22	72
87	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	558.15	03/2022 -	03/2023	133.39	12
	<u>Indian Railway Construction Company Limited</u>								
88	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,500.00	2,945.30	09/2018 -	12/2023	14.57	63
89	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	1,509.87	03/2022 -	12/2024	117.23	33
	<u>Metropolitan Rapid Transport Projects</u>								
90	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	774.51	552.70	06/2013 -	12/2022	56.23	114
91	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,991.80	03/2004 -	03/2023	501.57	228
	<u>North Central Railway</u>								
92	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	799.75	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
93	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	77.45	03/2020 -	03/2024	94.45	48
94	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	708.73	380.92	03/2020 -	09/2022	24.42	30
95	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	983.55	344.80	03/2020 -	10/2024	137.09	55
96	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,145.79	990.86	03/2019 -	03/2024	197.45	60
97	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,047.51	1,050.40	03/2019 -	12/2023	13.88	57
98	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,650.00	1,255.18	03/2019 -	12/2023	397.31	57
99	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	4,059.65	2,380.05	03/2022 -	03/2025	81.86	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
100	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	6,527.45	5,330.91	03/2014 -	12/2023	172.72	117
101	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,663.00	1,781.77	03/2015 -	03/2026	186.39	132
102	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	7,876.92	3,408.77	12/2015 -	12/2023	488.06	96
103	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.79	12,817.81	03/2011 -	12/2023	221.56	153
	<u>North Eastern Railway</u>								
104	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	0.74	04/2017 -	10/2022	127.77	66
	<u>North Western Railway</u>								
105	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	476.01	03/2020 -	10/2022	16.97	31
	<u>Northern Railway</u>								
106	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.09	03/2023 -	12/2025	369.35	33
107	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024	348.44	148
108	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	37,012.26	30,671.82	11/2002 -	06/2023	1,380.49	247
	<u>Rail Vikas Nigam Ltd.</u>								
109	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	455.39	03/2009 03/2009	12/2022	224.56	165
110	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	626.34	03/2016 -	09/2022	50.15	78
111	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,457.79	1,408.80	03/2019 -	03/2023	57.26	48
112	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,500.00	1,127.95	03/2022 -	12/2022	58.97	9
113	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,536.00	1,664.15	03/2020 -	12/2022	102.11	33
114	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,552.26	1,445.70	03/2019 -	03/2023	64.62	48
115	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	2,340.59	12/2020 -	09/2022	23.55	21
116	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	2,350.49	03/2020 -	09/2022	111.91	30
117	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413]	03/2012	1,183.25 -	2,203.53	2,075.59	12/2020 -	09/2022	86.23	21
118	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	2,202.65	02/2015 -	09/2022	102.92	91

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
119	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	2,538.01	2,375.23	12/2021 -	12/2022	63.88	12
120	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	305.05	03/2014 -	12/2025	18.95	141
121	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	2,712.78	12/2024 -	12/2026	42.47	24
122	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	3,496.68	03/2016 -	03/2026	7.78	120
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,834.54	1,839.89	03/2016 -	07/2025	65.94	112
124	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	24,659.00	8,453.89	12/2024 -	03/2025	52.07	3
	<u>South Central Railway</u>								
125	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	918.80	03/2023 -	03/2025	5.16	24
126	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,095.80	03/2009 -	03/2027	102.85	216
127	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	2,250.00	784.26	03/2010 -	03/2025	93.89	180
128	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	2,206.22	03/2000 -	03/2023	98.57	276
129	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,755.92	03/2022 -	03/2025	7.06	36
	<u>South East Central Railway</u>								
130	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	88.40	12/2021 -	12/2024	378.60	36
131	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	918.24	12/2021 -	12/2023	.07	24
132	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	1,106.76	03/2021 -	12/2023	8.23	33
133	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,176.60	1,902.75	03/2023 -	12/2023	66.44	9
	<u>South Eastern Railway</u>								
134	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 -	393.83	34.60	06/2022 -	12/2023	16.52	18
135	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 -	472.50	6.00	06/2022 -	12/2025	10.23	42
136	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39 -	511.75	259.72	12/2021 -	01/2023	31.09	13
137	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.97	1,264.07	03/2020 -	10/2022	35.38	31
	<u>South Western Railway</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
138	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	826.18	499.13	03/2017 -	03/2026	28.13	108
139	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	332.27	03/2016 -	12/2026	55.13	129
140	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	1,611.28	03/2019 -	02/2024	16.31	59
141	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,954.21	1,381.52	03/2020 -	12/2022	68.91	33
	<u>Southern Railway</u>								
142	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,084.48	321.37	03/2019 -	12/2027	1,626.99	105
143	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	3,081.20	1,774.56	02/2019 -	03/2025	325.17	73
	<u>West Central Railway</u>								
144	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	704.97	03/2022 -	09/2024	114.32	30
145	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,445.30	1,720.50	03/2020 -	10/2024	38.63	55
146	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,658.34	03/2021 -	03/2024	585.35	36
147	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,938.00	1,450.69	03/2022 -	03/2024	18.55	24
148	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
149	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	04/2018	537.31 -	584.31	2.44	03/2024 -	12/2024	8.75	9
150	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]	04/2017	692.25 -	692.26	8.51	03/2020 -	12/2024	.00	57
151	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	1,083.17	252.70	03/2012 -	03/2024	240.36	144
152	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,119.12	962.02	03/2021 -	12/2022	11.65	21
153	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,394.02	1,300.17	03/2021 -	12/2022	34.41	21
154	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	1,063.17	03/2022 -	12/2024	13.17	33
155	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) [N22000139]	04/2007	1,640.04 -	1,873.10	908.51	03/2022 -	03/2025	14.21	36
156	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,448.99	2,142.58	03/2020 -	03/2024	195.15	48
157	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,383.82	2,529.21	03/2022 -	03/2026	82.20	48

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		1,26,859.22 -	2,63,046.48	156,070.61				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
158	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	108.00	06/2016 -	09/2022	.02	75
159	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	174.90	154.26	08/2018 -	10/2022	5.23	50
160	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	47.17	08/2019 -	03/2023	33.51	43
161	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576	02/2016	178.85 -	225.06	212.91	05/2016 -	11/2022	25.84	78
162	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	206.89	08/2018 -	10/2022	4.45	50
163	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	94.55	11/2019 -	10/2022	.08	35
164	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157	08/2016	175.50 -	241.60	164.41	02/2017 -	08/2022	37.66	66
165	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158	03/2018	159.97 -	242.61	94.29	06/2019 -	03/2023	51.66	45
166	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	91.29	08/2019 -	03/2023	11.18	43
167	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	125.25	11/2018 -	03/2023	7.39	52
168	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208	03/2018	288.30 -	323.36	237.25	08/2020 -	10/2022	12.16	26
169	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	404.69	03/2018 -	10/2022	9.23	55
170	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	452.11	09/2016 -	03/2023	14.24	78
171	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	572.66	280.46	08/2016 -	12/2022	15.19	76

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
172	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578	02/2016	553.30 -	587.41	553.81	05/2016 -	11/2022	6.16	78
173	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	01/2017	576.48 -	686.13	503.77	01/2018 -	12/2022	19.02	59
174	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	471.29	10/2016 -	12/2022	17.04	74
175	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922	12/2017	867.97 -	913.49	700.54	11/2018 -	09/2022	5.24	46
176	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	03/2016	877.79 -	949.54	807.22	06/2019 -	09/2022	8.17	39
177	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579	01/2014	1,408.85 -	2,138.16	1,412.08	10/2016 -	03/2023	51.77	77
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
178	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	171.06	04/2017 -	08/2022	27.16	64
179	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	180.00	04/2017 -	11/2022	29.48	67
180	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	03/2015	168.39 -	259.79	158.07	11/2018 -	08/2022	54.28	45
181	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	172.68	04/2017 -	10/2022	29.48	66
182	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583	01/2016	252.00 -	330.30	141.13	01/2016 -	12/2022	31.07	83
183	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320	06/2015	463.49 -	801.54	185.26	06/2018 -	03/2023	72.94	57
184	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	873.91	559.13	11/2018 -	09/2022	48.38	46
185	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823	03/2015	829.00 -	1,307.50	411.51	01/2016 -	06/2023	57.72	89
	<u>National Highways Authority Of India</u>								
186	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	410.81	11/2019 -	12/2022	2.02	37

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
187	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 -	732.34	530.71	11/2019 -	12/2022	.06	37
188	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	777.03	766.05	05/2018 -	12/2022	46.30	55
189	FOUR LANING OF SIMGA - SARAGAON - [N24000495	12/2015	596.67 -	819.35	439.27	05/2018 -	08/2022	37.32	51
190	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	830.31	31.82	03/2020 -	03/2023	23.39	36
191	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV [N24000691	04/2017	894.00 -	929.32	880.00	04/2020 -	12/2022	3.95	32
192	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	-	03/2020 -	07/2024	31.88	52
193	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138	09/2010	946.00 -	1,046.56	822.13	06/2018 -	12/2022	10.63	54
194	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	08/2017	950.64 -	1,168.33	503.74	08/2017 -	08/2023	22.90	72
195	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,309.79	1,162.72	09/2017 -	03/2023	16.52	66
196	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	1,309.30	03/2020 -	09/2022	10.58	30
197	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 -	1,321.60	678.20	02/2021 -	02/2023	7.72	24
198	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	09/2011	1,250.00 -	1,380.73	1,354.65	12/2013 -	05/2024	10.46	125
199	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	03/2017	1,373.28 -	1,405.27	1,401.96	03/2020 -	08/2022	2.33	29
200	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,414.01	1,000.57	06/2018 -	01/2023	30.56	55
201	FOUR LANING OF PARWANOO -SOLAN - [N24000479	09/2015	934.46 -	1,543.51	1,472.50	03/2018 -	12/2022	65.18	57
202	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	1,827.00	1,306.69	03/2021 -	08/2022	19.21	17
203	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	01/2016	815.28 -	2,323.88	2,223.06	06/2018 -	12/2022	185.04	54
204	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	06/2016	667.00 -	2,328.27	2,126.16	07/2018 -	09/2022	249.07	50

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
205	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]	07/2015	2,128.72 -	2,408.72	1,865.00	04/2019 -	09/2022	13.15	41
206	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	05/2014	1,655.01 -	2,639.00	1,710.83	08/2016 -	12/2022	59.46	76
207	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	3,006.53	2,989.89	06/2018 -	12/2022	350.75	54
208	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	3,063.99	2,904.36	04/2019 -	09/2022	93.01	41
209	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66	105
	Total		38,177.88 -	53,059.21	40,370.95				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
210	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	21,019.89	05/2015 -	03/2023	41.32	94
	Total		15,525.00 -	21,940.00	21,019.89				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
211	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]	03/2020	431.16 431.00	461.42	107.44	06/2021 -	11/2022	7.02	17
	Total		431.16 -	461.42	107.44				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
212	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,925.22	10,816.18	12/2018 -	09/2022	19.98	45
	<u>Mumbai Metro Rail Corporation Ltd</u>								
213	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	22,064.15	03/2020 -	12/2023	44.39	45
	Total		33,909.00 -	46,331.22	32,880.33				
	<u>WATER RESOURCES</u>								
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
214	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	413.29	0.07	09/2020 -	03/2024	62.63	42

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Kolkata Metropolitan Development Authority</u>								
215	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	03/2024	13.23	25
	<u>Polavaram Project Authority</u>								
216	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	20,538.05	03/2020 -	03/2024	447.22	48
	<u>Uttar Pradesh Jal Nigam</u>								
217	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	28.37	12/2021 -	06/2023	.97	18
218	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	04/2024	22.24	25
219	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	1.31	22
	Total		11,730.79 -	57,372.71	20,566.49				
	Grand Total		4,18,548.39	7,28,434.96	491,844.35				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 12/2021	12/2021
	Total		438.28 -		
	<u>COAL</u>				
	<u>Eastern Coal Fields Limited</u>				
2	HURA - C OC (3 MTY) - [N06000143]ECL, JHARKHAND	10/2015	359.69 -	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>				
3	ANANTA OCP EXPANSION PH III - [N06000225]MCL, ODISHA	08/2008	228.08 -	03/2012 -	-
4	SUBHADRA OCP - [N06000249]MCL, ODISHA	05/2021	1,693.81 -	03/2027 03/2029	-
	<u>Neyveli Lignite Corporation</u>				
5	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	12/2015 -	02/2021
6	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
8	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
9	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
	<u>South-Eastern Coal Fields Limited</u>				
10	BATURA HIGHWALL PROJECT - [N06000134]SECL, MADHYA PRADESH	07/2015	231.92 -	03/2022 -	03/2022
11	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL, CHHATISGARH	07/2016	459.49 -	03/2020 -	03/2022
	<u>Western Coal Fields Limited</u>				
12	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	03/2022
13	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL, MULTI STATE	08/2016	319.76 319.76	03/2022 -	03/2022
	Total		14,840.40 -		
	<u>FINANCE</u>				
	<u>Cpwd For Finance</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (August 2022)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU	11/2017	348.77 -	11/2021 -	-
	<u>National Projects Construction Corporation Limited</u>				
15	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA - [N07000001]NPCC,DELHI	07/2018	228.50 220.27	04/2022 -	04/2022
	Total		577.27 -		
	<u>PETROLEUM</u>				
	<u>Hindustan Petroleum Corporation Limited</u>				
16	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	07/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
17	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	Total		907.26 -		
	<u>POWER</u>				
	<u>National Thermal Power Corporation</u>				
18	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
	<u>Power Grid Corporation Of India Limited</u>				
19	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	04/2022
20	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315]PGCIL,MULTI STATE	07/2020	239.89 -	06/2021 -	04/2022
	Total		2,289.18 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Cpwd For Health</u>				
21	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29 -	03/2020 -	03/2020
22	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	06/2021
23	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	-
24	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00 -	09/2020 -	-
	<u>HII Infra Tech Services Limited</u>				
25	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
26	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
27	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 890.14	05/2021 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
28	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
29	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
30	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	04/2020
31	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	01/2021
32	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
33	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	02/2021
34	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	04/2021
35	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	05/2021
36	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2021
37	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	06/2021
38	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021
39	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	12/2021
40	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	12/2021
41	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	12/2021
42	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	12/2021
43	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	01/2022
44	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	06/2022
45	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	07/2022
	Total		9,113.26 -		
	<u>RAILWAYS</u>				
	<u>Container Corporation Of India</u>				
46	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	03/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
47	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
48	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
49	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
50	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 3,020.95	- -	07/2022
51	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	678.54 678.54	03/2019 -	07/2022
	<u>East Coast Railway</u>				
52	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	1,111.99 -	02/2019 -	-
	<u>Eastern Railways</u>				
53	BANDEL-BOINCHI 3RD LINE - [N22000221]ER, MULTI STATE	04/2011	288.35 -	- 09/2021	05/2022
	<u>Kolkata Metro Rail Corporation Limited</u>				
54	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
55	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
56	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
	<u>North East Frontier Railway</u>				
57	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
	<u>North Eastern Railway</u>				
58	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER, UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022
59	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER, UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022
60	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	01/2019 -	-
61	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	04/2016 -	-
62	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	-
	<u>North Western Railway</u>				
63	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	02/2019 -	06/2022
	<u>Northern Railway</u>				
64	ROHTAK-MEHAM HANSI - [N22000272]NR, HARYANA	04/2012	287.00 -	12/2011 -	12/2011
	<u>National High Speed Rail Corporation Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
65	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	-
	<u>Rail India Technical And Economic Service</u>				
66	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 998.06	03/2021 12/2022	-
	<u>Rail Vikas Nigam Ltd.</u>				
67	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	06/2022
68	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	07/2022
	<u>South Central Railway</u>				
69	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
70	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	-
	Total		1,61,524.20 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
71	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2014
72	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 - [N24000422]MoRTH,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	09/2015
73	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	06/2019
74	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	06/2019
75	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	07/2019
76	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 08/2019	08/2019
77	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 09/2019	09/2019
78	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	09/2019
79	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 10/2019	10/2019
80	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	11/2019
81	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	11/2019
82	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 12/2019	12/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
83	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	12/2019
84	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	12/2019
85	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019
86	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- 02/2019	01/2020
87	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	01/2020
88	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	01/2020
89	AMDJ TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	02/2020
90	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	03/2020
91	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	03/2020
92	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 2,617.44	03/2020 -	03/2020
93	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 07/2020	07/2020
94	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	08/2020
95	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	09/2020
96	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	09/2020
97	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	09/2020
98	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	09/2020
99	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020
100	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 10/2020	10/2020
101	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	10/2020
102	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 1,428.09	03/2020 -	10/2020
103	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 11/2020	11/2020
104	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	11/2020
105	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	11/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	11/2020
107	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	11/2020
108	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	11/2020
109	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	11/2020
110	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	11/2020
111	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2020
112	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	12/2020
113	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	12/2020
114	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	12/2020
115	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	12/2020
116	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	12/2020
117	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	12/2020
118	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 01/2021	01/2021
119	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 01/2021	01/2021
120	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	01/2021
121	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	01/2021
122	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 01/2021	01/2021
123	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	03/2021
124	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	03/2021
125	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	03/2021
126	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	04/2021
127	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 04/2021	04/2021
128	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 04/2021	04/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
129	REHABILITATION AND UPGADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	06/2021
130	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 06/2021	06/2021
131	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	06/2021
132	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	06/2021
133	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	07/2021
134	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 07/2021	07/2021
135	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	07/2021
136	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	07/2021
137	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	07/2021
138	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	08/2021
139	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 09/2021	09/2021
140	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	09/2021
141	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	11/2021
142	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021
143	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	12/2021
144	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2021
145	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 12/2021	12/2021
146	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	12/2021
147	REHABILITATION AND UPGADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 01/2022	01/2022
148	REHABILITATION AND UPGADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 386.99	08/2018 01/2022	01/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
149	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 02/2022	02/2022
150	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	02/2022
151	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	02/2022
152	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	02/2022
153	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	02/2022
154	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH - [N24001448]MoRTH,MAHARASHTRA	11/2021	223.35 -	02/2022 -	02/2022
155	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 354.43	- 12/2021	03/2022
156	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	03/2022
157	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	03/2022
158	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 03/2022	03/2022
159	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- 03/2022	03/2022
160	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	03/2022
161	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	03/2022
162	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	03/2022
163	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	03/2022
164	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	03/2022
165	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	03/2022
166	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	03/2022
167	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	03/2022
168	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	03/2022
169	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	03/2022
170	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	03/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
171	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	03/2022
172	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	03/2022
173	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	03/2022
174	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	03/2022
175	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	03/2022
176	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	03/2022
177	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	03/2022
178	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	03/2022
179	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	03/2022
180	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	03/2022
181	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	03/2022
182	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	03/2022
183	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	03/2022
184	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	03/2022
185	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	03/2022
186	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	03/2022
187	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	03/2022
188	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	04/2022
189	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	04/2022
190	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	01/2021 -	04/2022
191	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	03/2021 04/2022	04/2022
192	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 06/2022	05/2022
193	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 394.44	05/2019 -	05/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
194	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 06/2022	06/2022
195	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 06/2022	06/2022
196	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 698.82	07/2016 06/2022	06/2022
197	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 11/2021	06/2022
198	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 06/2022	06/2022
199	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 06/2022	06/2022
200	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 06/2022	06/2022
201	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 06/2022	06/2022
202	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 06/2022	06/2022
203	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 06/2022	06/2022
204	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 06/2022	06/2022
205	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	06/2022
206	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	06/2022
207	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	06/2022
208	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	06/2022
209	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	06/2022
210	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	06/2022
211	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	06/2022
212	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	06/2022
213	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	06/2022
214	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	06/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
215	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	06/2022
216	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	06/2022
217	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	06/2022
218	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	06/2022
219	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	06/2022
220	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	06/2022
221	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	06/2022
222	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	06/2022
223	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	06/2022
224	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	06/2022
225	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	06/2022
226	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	06/2022
227	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	06/2022
228	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	06/2022
229	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	06/2022
230	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	06/2022
231	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	06/2022
232	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	06/2022
233	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	06/2022
234	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 03/2021	06/2022
235	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 03/2021	06/2022
236	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 270.00	06/2021 -	06/2022
237	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	07/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
238	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	07/2022
239	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 07/2022	07/2022
240	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 07/2022	07/2022
241	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 07/2022	07/2022
242	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	07/2022
243	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 07/2021	07/2022
244	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 07/2022	07/2022
245	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 01/2021	07/2022
246	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	07/2022
247	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
248	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
249	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-
250	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-
251	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
252	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
253	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-
254	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
255	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
256	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
258	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
259	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
260	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
261	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
262	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
263	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 11/2022	-
264	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 11/2022	-
265	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
266	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
267	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
268	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
269	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
270	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	-
271	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	-
272	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	-
273	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 10/2022	-
274	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
275	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	01/2021 -	-
276	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 06/2022	-
277	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
278	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 212.74	06/2019 -	-
279	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-
280	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-
281	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
282	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 296.53	08/2017 03/2022	-
283	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 372.87	09/2017 01/2022	-
284	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
285	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
286	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
287	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-
288	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	-
289	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
290	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-
291	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-
292	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
293	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-
294	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 - [N24001441]MoRTH,MEGHALAYA	08/2020	302.88 -	02/2022 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
295	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2016
296	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	04/2017
297	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	06/2018
298	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	09/2018
299	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	10/2018
300	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	12/2021
301	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	03/2022
302	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	03/2022
303	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND	09/2020	257.15 -	04/2022 -	04/2022
304	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	05/2022
305	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	05/2022
306	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 447.37	10/2017 06/2022	06/2022
307	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	06/2022
308	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	06/2022
309	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND	03/2020	320.97 -	06/2022 -	06/2022
310	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND	03/2020	355.79 -	06/2022 -	06/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
311	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND	03/2020	361.53 -	06/2022 -	06/2022
312	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]NHIDCL,ASSAM	03/2020	217.50 -	06/2022 -	06/2022
313	4-LANING OF DERGAON TOWN - [N24001435]NHIDCL,ASSAM	03/2020	287.63 -	06/2022 -	06/2022
314	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	07/2022
315	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	07/2022
316	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	07/2022
317	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]NHIDCL,TRIPURA	03/2020	154.51 -	07/2022 03/2023	07/2022
318	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM	03/2020	206.88 -	07/2022 -	07/2022
319	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM	03/2020	216.49 -	07/2022 -	07/2022
320	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM	03/2020	292.24 -	07/2022 -	07/2022
321	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM	03/2020	281.78 -	07/2022 -	07/2022
322	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]NHIDCL,TRIPURA	11/2020	206.78 -	07/2022 02/2023	07/2022
323	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	-
324	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	-
325	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
326	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
327	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
328	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
329	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
330	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
331	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
332	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA	06/2020	277.50 -	01/2022 -	-
333	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL,MANIPUR	08/2020	268.98 -	04/2022 -	-
334	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL,MANIPUR	08/2020	228.97 -	04/2022 -	-
335	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND	03/2020	330.78 -	12/2021 -	-
336	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND	04/2020	330.80 -	12/2021 -	-
<u>National Highways Authority Of India</u>					
337	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	07/2013
338	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2013
339	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	01/2016
340	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 11/2018	11/2018
341	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 503.36	09/2016 -	11/2018
342	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 589.04	01/2016 -	01/2019
343	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 2,262.00	01/2019 -	01/2019
344	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	03/2019
345	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 839.00	05/2017 -	05/2019
346	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	05/2019
347	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2019
348	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019
349	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019
350	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	10/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
351	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 480.31	01/2014 -	12/2019
352	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- 01/2020	01/2020
353	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	03/2020
354	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 414.00	05/2018 11/2020	11/2020
355	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	01/2021
356	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 416.00	- -	02/2021
357	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI, UTTAR PRADESH	12/2017	1,232.21 -	- -	03/2021
358	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 -	- -	05/2021
359	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	08/2021
360	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	09/2021
361	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 2,047.39	06/2020 -	10/2021
362	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	10/2021
363	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	10/2021
364	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 1,103.55	04/2018 -	12/2021
365	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 2,421.37	- 12/2021	12/2021
366	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	12/2021
367	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	12/2021
368	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	02/2022
369	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	- -	02/2022
370	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI, MAHARASHTRA	03/2018	289.21 -	- 02/2022	02/2022
371	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	03/2022
372	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	03/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
373	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 1,082.40	10/2013 03/2022	03/2022
374	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	05/2018 -	03/2022
375	MEERUT-BULANDSHAHR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	03/2022
376	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2022
377	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	07/2018 -	03/2022
378	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 2,330.79	- 03/2022	03/2022
379	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 05/2022	03/2022
380	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	03/2022
381	REHABILITATION AND UPGRADE TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	03/2022
382	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI, RAJASTHAN	12/2016	1,031.95 -	- -	03/2022
383	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	02/2020 03/2022	03/2022
384	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI, ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	03/2022
385	REHABILITATION AND UPGRADE BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	03/2020 -	03/2022
386	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	07/2016 -	03/2022
387	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA	01/2018	668.86 -	- -	03/2022
388	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI, MAHARASHTRA	03/2018	291.53 -	- 02/2022	03/2022
389	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI, HARYANA	01/2019	1,033.19 1,044.32	- 03/2022	03/2022
390	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI, HARYANA	03/2018	795.50 -	- -	04/2022
391	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI, HARYANA	01/2019	1,243.45 1,407.35	- 04/2022	04/2022
392	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	05/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
393	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	05/2022
394	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2022
395	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	05/2022
396	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 05/2022	05/2022
397	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	05/2022
398	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- 03/2022	05/2022
399	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	05/2022
400	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	05/2022
401	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 1,023.23	07/2018 02/2022	05/2022
402	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2022
403	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 1,140.64	10/2017 -	05/2022
404	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	05/2022
405	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	05/2022
406	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	05/2022
407	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	05/2022
408	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 1,118.07	- 05/2022	05/2022
409	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 986.10	- 05/2022	05/2022
410	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 1,072.08	- 05/2022	05/2022
411	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 1,173.65	- 05/2022	05/2022
412	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 655.64	02/2019 04/2021	05/2022
413	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	06/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
414	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 12/2022	06/2022
415	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	06/2022
416	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	06/2022
417	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,950.04	06/2018 12/2022	06/2022
418	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	06/2022
419	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 1,376.86	04/2019 06/2022	06/2022
420	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	06/2022
421	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	06/2022
422	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	06/2022
423	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	06/2022
424	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2022
425	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2022
426	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	06/2022
427	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 595.00	- 06/2022	06/2022
428	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2022
429	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2022
430	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	06/2022
431	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	06/2022
432	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	06/2022
433	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 1,238.29	- 06/2022	06/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
434	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	07/2022
435	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 1,330.02	- 07/2022	07/2022
436	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 12/2021	07/2022
437	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	07/2022
438	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022
439	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 373.10	10/2017 -	07/2022
440	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022
441	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	07/2022
442	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	07/2022
443	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 1,632.70	- 07/2022	07/2022
444	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 1,206.48	- 07/2022	07/2022
445	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 570.98	01/2020 08/2021	07/2022
446	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
447	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
448	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 12/2022	-
449	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	-
450	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
451	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
452	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
453	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
454	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
455	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.92	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
456	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 416.07	- 07/2021	-
457	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
458	4-laning of Khammam-Ashwaraopet section of NH-365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
459	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
460	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
461	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
462	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
463	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	-
	Total		2,15,614.95 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Department Of Telecommunication</u>				
464	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	06/2022
	Total		13,334.00 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
465	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	04/2019 -	04/2022
466	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	03/2021 -	-
467	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	08/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
468	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
469	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	-
	<u>Delhi Metro Rail Corporation</u>				
470	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
471	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
472	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
473	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2022
	Total		72,393.12 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
474	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 12/2022	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
475	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 -	05/2022
476	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 398.90	03/2020 -	06/2022
477	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 431.21	01/2021 -	06/2022
	<u>Delhi Jal Board</u>				
478	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	03/2022
479	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
480	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 -	06/2022
481	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	06/2022
	<u>Uttar Pradesh Jal Nigam</u>				
482	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	06/2022
	<u>Uttarakhand Pey Jal Nigam</u>				
483	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]JUKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	02/2022
	Total		2,945.00 -		
	<u>COMMERCE</u>				
	<u>Nbcc For Commerce</u>				
484	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (August 2022)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Cpwd Of Higher Education</u>				
485	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23 -	10/2012 -	10/2012
486	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA	01/2018	223.37 -	07/2020 -	07/2020
487	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND	09/2012	171.86 171.86	03/2016 07/2022	07/2022
	Total		560.46 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
488	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
	Total		151.33 -		
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				
489	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		4,95,263.25		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
1	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	130.21	- 03/2023	03/2023	0(R3)	18/26
2	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	730.20	303.77	- 03/2023	03/2023	0(R3)	14/17
	Total		818.00 -	960.00	433.98				32/43
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
3	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	4,287.59	793.45	- 08/2024	07/2025	11(R3)	0/0
	Total		4,287.59 -	4,287.59	793.45				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
4	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	1,136.40	- -	03/2024	-	0/0
5	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,700.00	1,758.02	- -	03/2024	-	0/0
6	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	1,510.00	1,547.42	- -	03/2024	-	0/0
7	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,661.76	- -	12/2024	-	0/0
8	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	413.53	- -	12/2024	-	0/0
9	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	346.79	- -	12/2024	-	0/0
10	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	360.11	- -	03/2025	-	0/0
11	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	213.88	- -	12/2025	-	0/0
	<u>Eastern Railways</u>								
12	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	376.37	- -	09/2022	-	0/0
13	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	272.20	328.63	- -	12/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	470.90	- -	03/2023	-	0/0
	<u>North Central Railway</u>								
15	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 746.83	746.83	22.79	- 03/2026	12/2027	21(R3)	0/0
	<u>North East Frontier Railway</u>								
16	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	401.65	342.82	- -	03/2023	-	0/0
	<u>North Eastern Railway</u>								
17	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	800.00	185.52	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
18	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	791.39	572.99	- -	09/2023	-	0/0
19	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	133.78	- -	09/2023	-	0/0
	<u>South Western Railway</u>								
20	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	2,000.97	104.48	- -	03/2025	-	0/0
21	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,404.03	1,108.14	- -	12/2025	-	2/2
22	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	5,174.30	158.25	- -	03/2028	-	0/0
	<u>Southern Railway</u>								
23	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	591.00	464.44	- 09/2022	09/2022	0(R3)	0/0
24	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	1,431.90	1,019.34	- -	03/2024	-	0/0
25	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 1,281.63	1,339.00	.91	- -	03/2025	-	0/0
26	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	3,500.79	622.53	- -	12/2025	-	0/0
	<u>Western Railway</u>								
27	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	311.36	-	- -	03/2024	-	0/0
28	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	393.62	219.72	- -	03/2024	-	0/0
29	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	528.49	127.92	- -	03/2024	-	0/0
30	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	390.14	- 10/2025	10/2025	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		19,285.68	33,133.23	14,087.58				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
31	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81	225.81	114.55	-	09/2022	-	0/0
32	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51	390.51	314.69	-	03/2021	18(R3)	0/0
33	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66	356.66	162.29	-	09/2022	-	0/4
34	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45	319.96	202.69	-	09/2022	-	0/0
35	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68	293.68	185.08	-	10/2022	0(R3)	0/0
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68	404.10	400.67	-	11/2022	0(R3)	0/0
37	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40	936.40	611.47	-	09/2022	3(R3)	0/0
38	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19	249.72	184.91	-	01/2023	0(R3)	0/0
39	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00	780.77	453.21	-	06/2022	9(R3)	0/0
40	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58	1,101.58	395.64	-	03/2023	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
41	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79	245.79	224.65	-	09/2022	-	3/4

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	520.01	214.57	- -	11/2022	-	3/4
43	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL, MEGHALAYA	04/2017	553.51 -	553.51	232.58	- -	11/2022	-	2/4
44	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL, ARUNACHAL PRADESH	12/2016	200.44 -	200.44	135.92	- -	12/2022	-	3/4
45	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL, ARUNACHAL PRADESH	12/2016	188.78 -	188.78	142.23	- -	12/2022	-	3/4
46	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL, ARUNACHAL PRADESH	09/2016	568.92 -	568.92	390.60	- -	03/2023	-	0/0
47	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL, SIKKIM	03/2017	375.80 -	375.80	96.70	- -	04/2023	-	2/4
48	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL, ASSAM	10/2017	818.00 -	818.00	350.68	- -	04/2023	-	2/4
49	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL, ARUNACHAL PRADESH	03/2017	1,718.59 -	1,718.59	543.26	- -	03/2024	-	2/4
50	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL, ARUNACHAL PRADESH	01/2017	256.66 -	256.66	-	- -	03/2024	-	1/4
<u>National Highways Authority Of India</u>									
51	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	1,282.94	705.46	- -	08/2022	-	0/0
52	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	723.64	528.22	- -	08/2022	-	2/2
53	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH	02/2018	670.50 1,248.00	670.50	1,147.08	- -	08/2022	-	0/0
54	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI, ANDHRA PRADESH	02/2018	1,959.00 2,909.00	1,959.00	1,412.01	- 11/2021	08/2022	9(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
55	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	721.00	- -	08/2022	-	1/3
56	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	1,097.00	- -	08/2022	-	3/4
57	FOUR LANNING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	1,018.46	- -	09/2022	-	3/4
58	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 4,041.80	1,396.74	3,704.91	- -	09/2022	-	0/0
59	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 793.63	793.63	326.96	- 09/2022	09/2022	0(R3)	2/4
60	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	1,251.13	- 12/2021	09/2022	9(R3)	3/4
61	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	359.60	339.75	- 05/2017	09/2022	64(R3)	3/4
62	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG V)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,361.00	503.77	- 06/2021	09/2022	15(R3)	1/4
63	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	950.49	539.74	- -	09/2022	-	0/0
64	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	2,450.00	2,691.86	- -	09/2022	-	0/0
65	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	1,361.00	503.77	- 06/2021	09/2022	15(R3)	2/4
66	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,673.32	- -	09/2022	-	0/0
67	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	448.26	- -	09/2022	-	0/0
68	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	665.33	- -	09/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
69	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	856.21	- -	10/2022	-	0/0
70	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	320.13	- -	10/2022	-	0/0
71	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	440.00	- -	10/2022	-	0/0
72	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	452.72	- -	10/2022	-	0/1
73	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,568.04	- -	10/2022	-	0/0
74	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	84.10	- -	10/2022	-	0/0
75	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	857.62	561.95	- -	10/2022	-	0/0
76	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	884.00	797.00	- -	10/2022	-	3/4
77	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	379.01	- -	11/2022	-	0/1
78	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	627.92	- 08/2022	11/2022	3(R3)	2/4
79	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	1,135.08	905.95	- 11/2022	11/2022	0(R3)	0/0
80	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	689.00	- -	11/2022	-	2/4
81	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	681.67	673.94	- -	12/2022	-	3/4
82	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	408.37	- -	12/2022	-	2/2

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
83	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	329.71	- -	12/2022	-	0/0
84	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	261.83	- -	12/2022	-	0/0
85	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 1,296.93	1,422.13	444.08	- -	12/2022	-	0/0
86	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 1,065.70	1,065.70	1,049.98	- -	12/2022	-	0/0
87	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 649.00	649.00	185.59	- 10/2021	12/2022	14(R3)	0/0
88	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	255.05	- -	12/2022	-	0/0
89	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 1,282.30	1,308.88	492.86	- -	12/2022	-	0/0
90	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 1,140.50	828.29	287.90	- 03/2021	02/2023	23(R3)	0/0
91	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	1,005.08	-	- 02/2023	02/2023	0(R3)	0/0
92	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 479.00	479.00	456.80	- 03/2023	03/2023	0(R3)	3/4
93	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,182.94	399.40	- -	03/2023	-	0/0
94	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	1,092.03	- -	03/2023	-	0/0
95	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	454.01	- -	03/2023	-	4/4
96	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	276.17	175.09	- -	03/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
97	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	633.68	320.00	- -	03/2023	-	0/1
98	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	309.51	- -	03/2023	-	0/0
99	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,603.94	1,441.00	494.71	- -	03/2023	-	0/0
100	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	316.00	- -	06/2023	-	0/0
101	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 644.50	726.99	222.51	- 12/2019	06/2023	42(R3)	0/0
102	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	254.00	- -	06/2023	-	0/0
103	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	159.77	- -	06/2023	-	0/0
104	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	537.17	156.46	- -	06/2023	-	0/0
105	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 664.10	736.33	68.39	- 08/2023	08/2023	0(R3)	0/0
106	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	1,484.30	889.47	- -	08/2023	-	0/0
107	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	1,182.87	84.54	- -	10/2023	-	0/0
108	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	2,360.65	4,521.55	- -	12/2023	-	0/0
109	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWA (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	221.14	- -	12/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
110	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	486.78	171.98	- -	12/2023	-	3/3
111	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 1,862.77	1,862.77	192.01	- -	01/2024	-	0/0
112	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	2,169.00	-	- -	01/2024	-	0/0
113	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	1,339.00	1,236.41	- 10/2018	03/2024	65(R3)	2/3
114	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	895.39	1,369.90	- -	04/2024	-	0/0
115	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	2,145.96	199.05	- -	06/2024	-	0/0
116	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	781.17	- -	08/2024	-	2/2
117	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	1,962.50	689.57	- -	10/2024	-	0/0
	Total		75,260.45 -	80,934.90	53,941.23				67/110
	URBAN DEVELOPMENT								
	National Building Construcion Corporation Ltd								
118	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	1,292.02	- -	03/2023	-	0/9
	Total		2,694.00 -	2,694.00	1,292.02				0/9
	Grand Total		1,02,345.72	1,22,009.72	70,548.26				101/164

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	04/2020 12/2022	12/2022	0/0
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					
2	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	03/2017 -	12/2022	0/0
3	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	04/2018 -	06/2023	0/0
	<u>Central Coal Fields Limited</u>					
4	EPR PUNDI OCP - [N06000242]CCL, JHARKHAND	11/2020	713.35 -	03/2024 -	03/2024	0/0
5	SIRKA OCP - [N06000239]CCL, JHARKHAND	05/2020	222.82 -	03/2025 -	03/2025	0/0
6	EPR TAPIN SOUTH OCP - [N06000241]CCL, JHARKHAND	11/2020	230.41 -	03/2025 -	03/2025	0/0
7	EPR ROHINI KARKATA OCP - [N06000243]CCL, JHARKHAND	01/2021	1,020.42 -	03/2025 -	03/2025	0/0
8	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]CCL, JHARKHAND	07/2021	778.80 -	03/2026 -	03/2026	0/0
9	EXPANSION OF KARO OCP - [N06000246]CCL, JHARKHAND	01/2022	908.47 -	03/2026 -	03/2026	0/0
10	EXPANSION OF ASHOK OCP - [N06000247]CCL, JHARKHAND	05/2021	2,898.28 -	03/2026 -	03/2026	0/0
11	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]CCL, JHARKHAND	08/2020	7,254.37 -	03/2028 -	03/2028	0/0
12	EXPANSION PROJECT AMRAPALI OCP - [N06000217]CCL, JHARKHAND	08/2020	5,136.15 -	03/2028 -	03/2028	0/0
13	JHARKHAND LAIYO OCP - [N06000240]CCL, JHARKHAND	08/2020	764.57 -	03/2031 -	03/2031	0/0
14	KOTRE BASANTPUR PACHMO OCP - [N06000237]CCL, JHARKHAND	08/2020	861.06 -	03/2032 -	03/2032	0/0
15	CHANDRAGUPT OCP - [N06000238]CCL, JHARKHAND	08/2020	973.50 -	03/2032 -	03/2032	0/0
16	EXPANSION OF KONAR OCP - [N06000245]CCL, JHARKHAND	01/2022	799.34 -	03/2032 -	03/2032	0/0
	<u>Eastern Coal Fields Limited</u>					
17	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL, WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
18	MOHANPUR EXPANSION OC PHASE II - [N06000236]ECL, WEST BENGAL	11/2020	888.99 -	03/2025 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
19	BONJEME HARI EXPANSION OCP - [N06000244]ECL, WEST BENGAL	08/2021	570.12 -	03/2025 -	03/2025	0/0
20	SONEPUR BAZARI EXPANSION OC - [N06000220]ECL, WEST BENGAL	07/2021	5,365.88 5,366.00	03/2029 -	03/2029	0/0
21	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]ECL, WEST BENGAL	04/2020	1,210.12 -	03/2029 -	03/2029	0/0
	<u>Mahanadi Coal Fields Limited</u>					
22	KULDA EXPANSION OCP- 15 MTY - [N06000248]MCL, ODISHA	06/2014	348.16 -	03/2018 -	03/2026	0/0
23	GOPALJI-KANIHA OCP - [N06000229]MCL, ODISHA	08/2020	8,416.19 -	03/2028 -	03/2028	0/0
24	BALARAM EXPANSION OCP - [N06000230]MCL, ODISHA	08/2020	3,504.21 -	03/2029 -	03/2029	0/0
25	BHUBANESWARI EXPANSION OCP - [N06000227]MCL, ODISHA	08/2020	3,145.45 -	03/2031 -	03/2031	0/0
26	ANANTA OCP EXPANSION PH III - [N06000225]MCL, ODISHA	08/2008	228.08 -	03/2012 -	-	0/0
27	SUBHADRA OCP - [N06000249]MCL, ODISHA	05/2021	1,693.81 -	03/2027 03/2029	-	0/0
	<u>Neyveli Lignite Corporation</u>					
28	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
29	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
30	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
31	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
	<u>South-Eastern Coal Fields Limited</u>					
32	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL, CHHATISGARH	07/2016	459.49 -	03/2020 -	03/2022	0/0
33	JAMPALI OCP RCE - [N06000198]SECL, CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0
34	RAMPUR BATURA OC (4.0 MTY) - [N06000233]SECL, MADHYA PRADESH	07/2019	1,248.93 -	03/2026 -	03/2026	0/0
35	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]SECL, MADHYA PRADESH	03/2021	496.28 -	03/2028 -	03/2028	0/0
36	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL, CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
37	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]SECL, CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
38	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL, CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>Western Coal Fields Limited</u>					
39	MAKARDHOKDA I EXPANSION OC - [N06000253]WCL, MAHARASHTRA	06/2022	497.06 -	03/2026 -	03/2026	0/0
40	BHATADI EXPANSION OC - [N06000254]WCL, MAHARASHTRA	02/2020	729.86 -	03/2028 -	03/2028	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
41	SINGHORI DEEP OC - [N06000252]WCL,MAHARASHTRA	05/2022	421.84 -	03/2029 -	03/2029	0/0
	<u>FERTILISERS</u>					
	<u>Rashtriya Chemical & Fertiliser Limited</u>					
42	AN MELT PROJECT AT RCF TROMBAY - [N08000019]RCF,MAHARASHTRA	05/2022	187.27 -	09/2024 -	07/2024	0/0
	<u>MINES</u>					
	<u>National Aluminum Company Limited (Nalco)</u>					
43	POTTANGI BAUXITE MINES - [N10000016]NALCO,ODISHA	05/2018	1,437.00 1,381.00	12/2024 12/2024	12/2024	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					
44	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0
45	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT - [N12000126]SAIL,JHARKHAND	02/2022	207.74 -	06/2024 -	06/2024	0/0
46	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125]SAIL,ODISHA	01/2022	970.18 -	05/2025 -	05/2025	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
47	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	09/2022	0/0
48	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI - [N16000452]BPCL,MAHARASHTRA	05/2022	423.39 -	03/2024 -	03/2024	0/0
49	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442]BPCL,MAHARASHTRA	04/2021	1,164.69 -	06/2024 -	06/2024	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
50	BHATINDA SANGRUR PIPELINE - [N16000440]HPCL,PUNJAB	11/2021	367.00 -	04/2024 -	04/2024	0/0
	<u>Indian Iron Steel Company</u>					
51	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI - [N16000438]IISCO,TAMIL NADU	01/2022	827.00 -	07/2024 -	07/2024	0/0
	<u>Indian Oil Corporation Limited</u>					
52	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 09/2022	09/2022	0/0
53	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 09/2022	09/2022	0/0
54	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	01/2021 -	12/2022	0/0
55	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
56	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
57	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 03/2023	03/2023	0/0
58	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0
59	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	08/2023	0/0
60	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY - [N16000446]IOCL,MAHARASHTRA	09/2021	378.00 -	10/2023 -	10/2023	0/0
61	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	02/2024	0/0
62	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	02/2024	0/0
63	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI - [N16000453]IOCL,BIHAR	01/2022	389.00 -	09/2024 -	09/2024	0/0
64	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT - [N16000454]IOCL,GUJARAT	01/2022	328.00 -	09/2024 -	09/2024	0/0
65	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]IOCL,RAJASTHAN	12/2021	9,028.00 -	10/2024 -	10/2024	0/0
66	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE - [N16000451]IOCL,TAMIL NADU	03/2022	564.00 -	11/2024 -	11/2024	0/0
67	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE - [N16000437]IOCL,KARNATAKA	01/2022	463.00 -	07/2025 -	07/2025	0/0
68	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM - [N16000441]IOCL,ASSAM	03/2022	277.00 -	07/2026 -	07/2026	0/0
69	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE	06/2019	303.00 -	02/2028 -	02/2028	0/0
70	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH	10/2018	177.00 -	02/2027 09/2028	09/2028	0/0
71	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR	10/2018	176.00 -	08/2027 02/2029	02/2029	0/0
72	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR	06/2019	439.00 -	02/2028 08/2029	08/2029	0/0
73	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR	06/2019	347.00 -	02/2028 08/2029	08/2029	0/0
74	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	02/2028 08/2029	08/2029	0/0
75	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND	10/2018	613.00 -	12/2029 03/2030	03/2030	0/0
76	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU	10/2018	2,998.00 -	03/2030 -	03/2030	0/0
77	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU	10/2018	1,304.00 -	03/2030 -	03/2030	0/0
78	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	08/2027 03/2030	03/2030	0/0
79	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR	06/2019	988.00 -	12/2029 03/2030	03/2030	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
80	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR	06/2019	163.00 -	12/2029 03/2030	03/2030	0/0
81	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE	06/2019	169.00 -	12/2029 03/2030	03/2030	0/0
82	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
	<u>Oil India Limited</u>					
83	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING - [N16000450]OIL,ASSAM	12/2020	430.76 -	07/2024 -	07/2024	0/0
84	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT - [N16000449]OIL,ASSAM	06/2021	860.00 -	12/2024 -	12/2024	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
85	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 07/2025	07/2025	0/0
86	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	- 08/2024	07/2025	0/0
	<u>National Hydro-Electric Power Corporation</u>					
87	KALPI SOLAR POWER PROJECT - [N18000323]NHPC,UTTAR PRADESH	07/2020	314.64 335.36	03/2022 12/2022	12/2022	0/0
88	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
89	RANGIT IV HE PROJECT - [N18000326]NHPC,SIKKIM	03/2021	938.29 938.29	05/2024 08/2024	08/2024	0/0
90	TEESTA VI HE PROJECT - [N18000325]NHPC,SIKKIM	03/2019	5,748.04 -	03/2024 -	07/2025	0/0
91	RATLE HE PROJECT - [N18000324]NHPC,JAMMU AND KASHMIR	02/2021	5,281.94 5,281.94	02/2026 02/2026	02/2026	0/0
	<u>National Thermal Power Corporation</u>					
92	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	10/2021 01/2023	08/2022	0/0
93	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	09/2021 01/2023	09/2022	0/0
94	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	09/2021 11/2022	09/2022	0/0
95	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	09/2021 11/2022	10/2022	0/0
96	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	09/2021 01/2023	01/2023	0/0
97	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	09/2021 01/2023	01/2023	0/0
98	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	03/2022 12/2023	03/2023	0/0
99	DAYAPAR WIND ENERGY PROJECT 150MW - [N18000319]NTPC,GUJARAT	11/2021	937.80 -	05/2023 -	05/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	BHENSARA 320 MW - [N18000293]NTPC, RAJASTHAN	01/2021	1,221.73 -	07/2022 -	08/2023	0/0
101	CHHATTARGARH 150 MW - [N18000294]NTPC, RAJASTHAN	02/2021	599.99 -	07/2022 -	08/2023	0/0
102	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC, GUJARAT	01/2021	842.27 -	07/2022 10/2022	08/2023	0/0
103	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]NTPC, GUJARAT	05/2021	674.92 -	09/2022 -	08/2023	0/0
104	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320]NTPC, RAJASTHAN	03/2022	1,352.71 -	08/2023 10/2023	10/2023	0/0
105	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321]NTPC, RAJASTHAN	03/2022	1,409.52 -	08/2023 10/2023	10/2023	0/0
106	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322]NTPC, RAJASTHAN	03/2022	1,426.94 -	08/2023 10/2023	10/2023	0/0
<u>Power Grid Corporation Of India Limited</u>						
107	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315]PGCIL, MULTI STATE	07/2020	239.89 -	06/2021 -	04/2022	0/0
108	EASTERN REGION STRENGTHENING SCHEME - XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	08/2022	0/0
109	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION - [N18000339]PGCIL, MULTI STATE	11/2018	173.94 -	11/2021 -	09/2022	0/0
110	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]PGCIL, GUJARAT	10/2019	1,031.00 -	08/2021 -	10/2022	0/0
111	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	12/2019 -	11/2022	0/0
112	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302]PGCIL, HARYANA	01/2019	267.33 -	03/2022 -	11/2022	0/0
113	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	03/2018 -	12/2022	0/0
114	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 -	12/2022	0/0
115	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	06/2019 -	12/2022	0/0
116	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 -	07/2019 -	12/2022	0/0
117	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]PGCIL, RAJASTHAN	03/2021	1,340.81 -	12/2022 -	12/2022	0/0
118	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL, MULTI STATE	09/2015	167.31 -	12/2017 -	12/2022	0/0
119	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD - [N18000314]PGCIL, RAJASTHAN	01/2020	562.86 -	01/2021 -	12/2022	0/0
120	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL, MULTI STATE	11/2018	241.38 -	11/2021 -	12/2022	0/0
121	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL, RAJASTHAN	05/2021	1,184.88 -	09/2022 -	01/2023	0/0
122	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308]PGCIL, MULTI STATE	02/2019	572.98 -	12/2020 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
123	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316]PGCIL,MULTI STATE	05/2021	576.42 -	03/2023 -	03/2023	0/0
124	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327]PGCIL,ASSAM	03/2019	1,326.00 -	03/2023 -	03/2023	0/0
125	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. - [N18000329]PGCIL,MULTI STATE	03/2022	176.22 -	03/2023 -	03/2023	0/0
126	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	04/2023	0/0
127	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299]PGCIL,BIHAR	05/2021	179.29 -	04/2023 -	04/2023	0/0
128	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B - [N18000337]PGCIL,MULTI STATE	07/2022	4,546.26 -	06/2023 -	06/2023	0/0
129	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN	06/2021	1,562.00 -	12/2022 -	08/2023	0/0
130	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN	06/2021	1,006.00 -	12/2022 -	08/2023	0/0
131	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303]PGCIL,RAJASTHAN	03/2021	353.85 -	12/2022 -	09/2023	0/0
132	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000331]PGCIL,MULTI STATE	02/2022	359.47 -	09/2023 -	09/2023	0/0
133	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332]PGCIL,MULTI STATE	05/2022	1,666.00 -	11/2023 -	11/2023	0/0
134	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305]PGCIL,RAJASTHAN	06/2021	713.82 -	12/2022 -	12/2023	0/0
135	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	01/2024	0/0
136	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	03/2024	0/0
137	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM - [N18000330]PGCIL,MULTI STATE	03/2022	288.71 -	12/2024 -	12/2024	0/0
138	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C - [N18000338]PGCIL,MULTI STATE	07/2022	186.19 -	03/2025 -	03/2025	0/0
139	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM - [N18000328]PGCIL,MULTI STATE	02/2022	318.12 -	04/2025 -	04/2025	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
140	GURHAH SOLAR POWER PROJECT - [N18000334]SJVN,UTTAR PRADESH	05/2022	466.82 -	08/2023 -	08/2023	0/0
141	GUJRAI SOLAR POWER PROJECT - [N18000336]SJVN,UTTAR PRADESH	06/2022	279.94 -	08/2023 -	08/2023	0/0
142	BIKANER SOLAR POWER PROJECT - [N18000335]SJVN,MAHARASHTRA	04/2022	5,491.89 532.00	05/2024 -	05/2024	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Cpwd For Health</u>					
143	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
144	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
145	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
	<u>HII Infra Tech Services Limited</u>					
146	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-	0/0
147	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-	0/0
148	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 890.14	05/2021 -	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
149	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
150	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
151	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	02/2021	0/0
152	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	05/2021	0/0
153	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2021	0/0
154	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021	0/0
155	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	12/2021	0/0
156	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	12/2021	0/0
157	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	12/2021	0/0
158	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	12/2021	0/0
159	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	01/2022	0/0
160	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	06/2022	0/0
161	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	07/2022	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
162	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2024	0/0
163	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
164	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
165	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
166	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2024	0/0
167	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
168	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
169	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2025	0/0
170	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2025	0/0
171	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2025	0/0
	<u>Container Corporation Of India</u>					
172	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
173	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
174	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
175	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
	<u>East Central Railways</u>					
176	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	- -	07/2022	0/0
177	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2023	0/0
178	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	03/2012 -	06/2023	0/0
179	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	- -	03/2024	0/0
180	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2024	0/0
181	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2024	0/0
182	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	03/2021 -	03/2024	0/0
183	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	- -	03/2024	0/0
184	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- -	12/2024	0/0
185	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	12/2024	0/0
186	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	- -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
187	SAGULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	03/2021 -	12/2024	0/0
188	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	- -	03/2025	0/0
189	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 548.00	03/2020 -	03/2025	0/0
190	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	- -	12/2025	0/0
<u>East Coast Railway</u>						
191	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 -	03/2024	0/0
192	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2022 -	03/2024	0/0
193	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 -	03/2025	0/0
194	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2025	0/0
195	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2025	0/0
196	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 12/2025	12/2025	0/0
197	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	03/2026	0/0
198	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
199	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	-	0/0
<u>Eastern Railways</u>						
200	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- 09/2021	05/2022	0/0
201	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	09/2022	0/0
202	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	10/2022	0/0
203	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	12/2022	0/0
204	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2023	0/0
205	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2023	0/0
206	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
<u>Indian Railway Construction Company Limited</u>						
207	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	12/2025	0/0
<u>Kolkata Metro Rail Corporation Limited</u>						
208	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Metropolitan Rapid Transport Projects</u>					
209	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	03/2004 -	03/2023	0/0
210	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-	0/0
211	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
	<u>North Central Railway</u>					
212	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2026	0/0
213	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 746.83	- 03/2026	12/2027	0/0
	<u>North East Frontier Railway</u>					
214	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	03/2023	0/0
215	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	03/2011 -	12/2023	0/0
216	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	03/2019 -	12/2023	0/0
217	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	03/2014 -	12/2023	0/0
218	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	12/2023	0/0
219	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	12/2023	0/0
220	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	03/2019 -	03/2024	0/0
221	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	03/2024	0/0
222	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	10/2024	0/0
223	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2025	0/0
224	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	03/2026	0/0
225	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-	0/0
	<u>North Eastern Railway</u>					
226	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
227	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022	0/0
228	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
229	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
230	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
231	INDARA - DOHRGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	-	0/0
232	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	-	0/0
	<u>North Western Railway</u>					
233	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	06/2022	0/0
234	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	10/2022	0/0
235	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	11/2022	0/0
	<u>Northern Railway</u>					
236	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	12/2011	0/0
237	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 37,012.26	11/2002 06/2023	06/2023	0/0
238	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	09/2023	0/0
239	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0
240	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	11/2024	0/0
241	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	08/2016 -	08/2025	0/0
242	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	12/2025	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
243	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	06/2022	0/0
244	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	07/2022	0/0
245	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	09/2022	0/0
246	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	09/2022	0/0
247	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	09/2022	0/0
248	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	09/2022	0/0
249	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	09/2022	0/0
250	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	09/2022	0/0
251	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2022	0/0
252	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
253	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	03/2020 -	12/2022	0/0
254	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2023	0/0
255	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2023	0/0
256	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	05/2023	0/0
257	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
258	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76 -	12/2023 -	12/2023	0/0
259	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
260	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	03/2025	0/0
261	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
262	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	07/2025	0/0
263	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
264	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2026	0/0
265	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2026	0/0
<u>South Central Railway</u>						
266	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2023	0/0
267	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
268	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2025	0/0
269	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2025	0/0
270	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2027	0/0
271	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	-	0/0
<u>South East Central Railway</u>						
272	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 12/2023	12/2023	0/0
<u>South Eastern Railway</u>						
273	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	10/2022	0/0
274	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	12/2021 -	01/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
275	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	06/2022 -	12/2023	0/0
276	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2024	0/0
277	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	05/2023 -	12/2024	0/0
278	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	06/2022 -	12/2025	0/0
	<u>South Western Railway</u>					
279	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	02/2024	0/0
280	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	03/2024	0/0
281	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	03/2025	0/0
282	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	06/2025	0/0
283	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2026	0/0
284	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	03/2017 -	03/2026	0/0
285	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	03/2028	0/0
	<u>Southern Railway</u>					
286	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- 09/2022	09/2022	0/0
287	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	03/2024	0/0
288	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
289	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 1,281.63	- -	03/2025	0/0
290	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
291	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0
	<u>Western Railway</u>					
292	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,125.53	03/2021 12/2022	12/2022	0/0
293	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,042.12	03/2021 12/2022	12/2022	0/0
294	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 03/2023	03/2023	0/0
295	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,631.75	03/2020 03/2024	03/2024	0/0
296	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 322.19	03/2012 03/2024	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
297	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	03/2024	0/0
298	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	03/2024	0/0
299	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	03/2024	0/0
300	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,524.68	03/2022 12/2024	12/2024	0/0
301	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 692.26	03/2020 12/2024	12/2024	0/0
302	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT	04/2018	537.31 537.31	03/2024 12/2024	12/2024	0/0
303	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,873.10	03/2022 03/2025	03/2025	0/0
304	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 10/2025	10/2025	0/0
305	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	03/2022 03/2026	03/2026	0/0
306	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 495.18	03/2022 03/2026	03/2026	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
307	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 - [N24000422]MoRTH,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	09/2015	0/0
308	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	06/2019	0/0
309	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 08/2019	08/2019	0/0
310	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	09/2019	0/0
311	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 10/2019	10/2019	0/0
312	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	11/2019	0/0
313	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 12/2019	12/2019	0/0
314	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	12/2019	0/0
315	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	12/2019	0/0
316	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0
317	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	03/2020	0/0
318	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 07/2020	07/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
319	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020	0/0
320	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 10/2020	10/2020	0/0
321	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 11/2020	11/2020	0/0
322	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	11/2020	0/0
323	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	11/2020	0/0
324	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2020	0/0
325	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	12/2020	0/0
326	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 01/2021	01/2021	0/0
327	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 01/2021	01/2021	0/0
328	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 04/2021	04/2021	0/0
329	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 04/2021	04/2021	0/0
330	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 06/2021	06/2021	0/0
331	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	07/2021	0/0
332	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 07/2021	07/2021	0/0
333	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 09/2021	09/2021	0/0
334	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	11/2021	0/0
335	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021	0/0
336	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2021	0/0
337	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 12/2021	12/2021	0/0
338	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	12/2021	0/0
339	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH - [N24001448]MoRTH,MAHARASHTRA	11/2021	223.35 -	02/2022 -	02/2022	0/0
340	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	03/2022	0/0
341	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
342	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 03/2022	03/2022	0/0
343	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- 03/2022	03/2022	0/0
344	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	03/2022	0/0
345	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	03/2022	0/0
346	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	03/2022	0/0
347	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	03/2022	0/0
348	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	03/2022	0/0
349	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	03/2022	0/0
350	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	03/2022	0/0
351	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	04/2022	0/0
352	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	04/2022	0/0
353	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	01/2021 -	04/2022	0/0
354	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 06/2022	05/2022	0/0
355	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 06/2022	06/2022	0/0
356	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 06/2022	06/2022	0/0
357	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 698.82	07/2016 06/2022	06/2022	0/0
358	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 11/2021	06/2022	0/0
359	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 06/2022	06/2022	0/0
360	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 06/2022	06/2022	0/0
361	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 06/2022	06/2022	0/0
362	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 06/2022	06/2022	0/0
363	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	06/2022	0/0
364	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	06/2022	0/0
365	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 03/2021	06/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
366	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 03/2021	06/2022	0/0
367	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	07/2022	0/0
368	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	07/2022	0/0
369	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	07/2022	0/0
370	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 07/2021	07/2022	0/0
371	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 07/2022	07/2022	0/0
372	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 01/2021	07/2022	0/0
373	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	07/2022	0/0
374	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 241.60	02/2017 12/2020	08/2022	0/0
375	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	08/2022	0/0
376	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR - [N24001454]MoRTH,TAMIL NADU	02/2022	184.15 -	08/2022 -	08/2022	0/0
377	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 - [N24001455]MoRTH,TAMIL NADU	02/2022	191.33 -	08/2022 -	08/2022	0/0
378	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	09/2022	0/0
379	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- 03/2021	09/2022	0/0
380	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 06/2021	09/2022	0/0
381	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 08/2021	09/2022	0/0
382	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 09/2022	09/2022	0/0
383	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	09/2022	0/0
384	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 04/2021	09/2022	0/0
385	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	09/2022	0/0
386	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 03/2021	09/2022	0/0
387	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 12/2021	09/2022	0/0
388	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	09/2022	0/0
389	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 -	09/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
390	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 12/2021	10/2022	0/0
391	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 10/2022	10/2022	0/0
392	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 10/2022	10/2022	0/0
393	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- 10/2022	10/2022	0/0
394	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 10/2022	10/2022	0/0
395	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	10/2022	0/0
396	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 10/2021	10/2022	0/0
397	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 08/2021	10/2022	0/0
398	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	08/2018 09/2021	10/2022	0/0
399	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 10/2021	10/2022	0/0
400	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 08/2021	10/2022	0/0
401	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2022	10/2022	0/0
402	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 10/2022	10/2022	0/0
403	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	10/2022	0/0
404	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	03/2018 06/2021	10/2022	0/0
405	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	10/2022	0/0
406	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 -	10/2022	0/0
407	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 404.10	- 11/2022	11/2022	0/0
408	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 225.06	05/2016 06/2022	11/2022	0/0
409	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 587.41	05/2016 03/2022	11/2022	0/0
410	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 09/2021	11/2022	0/0
411	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 12/2021	11/2022	0/0
412	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 11/2022	11/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
413	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 11/2022	11/2022	0/0
414	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 11/2022	11/2022	0/0
415	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- 09/2022	12/2022	0/0
416	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	12/2022	0/0
417	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 -	09/2019 03/2022	12/2022	0/0
418	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 09/2021	12/2022	0/0
419	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 12/2022	12/2022	0/0
420	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 12/2022	12/2022	0/0
421	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
422	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 11/2021	12/2022	0/0
423	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	08/2016 -	12/2022	0/0
424	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 -	12/2022	0/0
425	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	10/2016 -	12/2022	0/0
426	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	07/2016 -	12/2022	0/0
427	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
428	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 04/2021	12/2022	0/0
429	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 249.72	- 01/2023	01/2023	0/0
430	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- 06/2022	03/2023	0/0
431	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 03/2022	03/2023	0/0
432	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	03/2023	0/0
433	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	11/2018 03/2022	03/2023	0/0
434	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 -	09/2020 03/2022	03/2023	0/0
435	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 -	10/2020 03/2022	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
436	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885])MoRTH, WEST BENGAL	03/2016	160.27 -	08/2019 11/2022	03/2023	0/0
437	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887])MoRTH, WEST BENGAL	06/2016	236.78 -	08/2019 08/2022	03/2023	0/0
438	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158])MoRTH, KARNATAKA	03/2018	159.97 -	06/2019 01/2022	03/2023	0/0
439	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219])MoRTH, CHHATISGARH	01/2016	476.20 544.00	09/2016 -	03/2023	0/0
440	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226])MoRTH, CHHATISGARH	12/2014	496.02 -	03/2015 -	03/2023	0/0
441	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981])MoRTH, TELANGANA	10/2016	248.83 -	03/2019 04/2023	04/2023	0/0
442	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875])MoRTH, MADHYA PRADESH	02/2018	169.63 -	03/2018 03/2022	05/2023	0/0
443	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994])MoRTH, TELANGANA	03/2018	626.76 -	07/2020 05/2023	05/2023	0/0
444	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173])MoRTH, KARNATAKA	02/2017	157.32 187.61	05/2019 05/2023	05/2023	0/0
445	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT - [N24001423])MoRTH, UTTAR PRADESH	04/2021	309.48 -	03/2022 -	09/2023	0/0
446	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W - [N24001424])MoRTH, UTTAR PRADESH	03/2021	185.09 -	03/2022 -	09/2023	0/0
447	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388])MoRTH, KARNATAKA	03/2019	423.15 -	12/2019 12/2022	12/2023	0/0
448	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373])MoRTH, ARUNACHAL PRADESH	01/2020	358.26 -	02/2024 -	02/2024	0/0
449	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421])MoRTH, UTTAR PRADESH	07/2018	1,948.25 -	02/2024 -	02/2024	0/0
450	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372])MoRTH, ARUNACHAL PRADESH	02/2021	588.09 -	03/2024 -	03/2024	0/0
451	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) - [N24001442])MoRTH, SIKKIM	10/2021	385.15 -	05/2024 -	05/2024	0/0
452	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K - [N24001447])MoRTH, HIMACHAL PRADESH	08/2020	371.93 -	12/2024 -	12/2024	0/0
453	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408])MoRTH, ASSAM	02/2021	925.47 -	07/2025 -	07/2025	0/0
454	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289])MoRTH, ARUNACHAL PRADESH	03/2019	403.68 -	03/2027 -	03/2027	0/0
455	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290])MoRTH, ARUNACHAL PRADESH	03/2019	342.55 -	03/2027 -	03/2027	0/0
456	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291])MoRTH, ARUNACHAL PRADESH	03/2019	421.48 -	03/2027 -	03/2027	0/0
457	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292])MoRTH, ARUNACHAL PRADESH	03/2019	543.05 -	03/2027 -	03/2027	0/0
458	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293])MoRTH, ARUNACHAL PRADESH	03/2019	486.70 -	03/2027 -	03/2027	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
459	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	03/2027 -	03/2027	0/0
460	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	03/2027 -	03/2027	0/0
461	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	03/2027 -	03/2027	0/0
462	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	03/2027 -	03/2027	0/0
463	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	03/2027 -	03/2027	0/0
464	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	03/2027 -	03/2027	0/0
465	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	03/2027 -	03/2027	0/0
466	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
467	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-	0/0
468	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-	0/0
469	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-	0/0
470	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-	0/0
471	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
472	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
473	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-	0/0
474	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-	0/0
475	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-	0/0
476	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-	0/0
477	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-	0/0
478	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
479	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-	0/0
480	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 11/2022	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
481	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 11/2022	-	0/0
482	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
483	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	-	0/0
484	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	-	0/0
485	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	-	0/0
486	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 10/2022	-	0/0
487	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
488	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	01/2021 -	-	0/0
489	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-	0/0
490	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 296.53	08/2017 03/2022	-	0/0
491	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 372.87	09/2017 01/2022	-	0/0
492	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-	0/0
493	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-	0/0
494	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-	0/0
495	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-	0/0
496	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-	0/0
497	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	-	0/0
498	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-	0/0
499	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 - [N24001441]MoRTH,MEGHALAYA	08/2020	302.88 -	02/2022 -	-	0/0
500	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 12/2022	09/2022	0/0
National Highways And Infrastructure Development Corporation Ltd.						
501	4-LANING OF DERGAON TOWN - [N24001435]NHIDCL,ASSAM	03/2020	287.63 -	06/2022 -	06/2022	0/0
502	IMPHAL – MOREH (PACKAGE 4) - [N24001399]NHIDCL,MANIPUR	03/2021	277.99 -	01/2023 -	01/2023	0/0
503	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR	07/2021	512.43 -	02/2023 -	02/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
504	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR	07/2021	497.09 -	02/2023 -	02/2023	0/0
505	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	03/2023	0/0
506	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR	02/2021	431.28 -	03/2023 -	03/2023	0/0
507	MARIAM - PEREN (PKG 2A) - [N24001398]NHIDCL,MANIPUR	07/2021	204.58 -	03/2023 -	03/2023	0/0
508	TAMENGLONG - MAHUR PKG-1 - [N24001402]NHIDCL,MANIPUR	07/2021	185.80 -	03/2023 -	03/2023	0/0
509	TAMENGLONG - MAHUR PKG-2 - [N24001403]NHIDCL,MANIPUR	07/2021	483.87 -	03/2023 -	03/2023	0/0
510	TAMENGLONG - MAHUR PKG-4 - [N24001404]NHIDCL,MANIPUR	07/2021	198.77 -	03/2023 -	03/2023	0/0
511	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]NHIDCL,NAGALAND	07/2021	258.52 -	03/2023 -	03/2023	0/0
512	PEREN-DIMAPUR PKG-5 - [N24001407]NHIDCL,NAGALAND	02/2021	207.33 -	03/2023 -	03/2023	0/0
513	TAMENGLONG - MAHUR PKG-5 - [N24001436]NHIDCL,MANIPUR	08/2021	477.86 -	05/2023 -	05/2023	0/0
514	TAMENGLONG - MAHUR PKG-6 - [N24001437]NHIDCL,MANIPUR	09/2021	311.18 -	05/2023 -	05/2023	0/0
515	KEIFANG - TUVAI PKG-1 - [N24001440]NHIDCL,MIZORAM	09/2021	492.94 -	05/2023 -	05/2023	0/0
516	REHABILITATION OF SECTION FROM KM 298.00 TO KM 330.662 PKG-8 - [N24001433]NHIDCL,A & N ISLANDS	04/2021	154.61 -	07/2023 -	07/2023	0/0
517	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL,JAMMU AND KASHMIR	07/2021	859.67 -	08/2023 -	08/2023	0/0
518	CHURACHANPUR TUVAI PKG-3 - [N24001405]NHIDCL,MANIPUR	07/2021	673.27 -	10/2023 -	08/2023	0/0
519	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR	07/2021	467.00 -	03/2023 -	09/2023	0/0
520	MARAM - PEREN PKG-3 - [N24001439]NHIDCL,MANIPUR	08/2021	467.41 -	05/2023 -	11/2023	0/0
521	MERANGKONG-TAMLU-MON (MTM) PKG-5 - [N24001438]NHIDCL,NAGALAND	07/2021	161.73 -	12/2023 -	12/2023	0/0
522	IMPHAL - KHONGSANG PKG-4 - [N24001453]NHIDCL,MANIPUR	08/2021	579.63 -	12/2023 -	12/2023	0/0
523	DABOKA KATHKATI PACKAGE-6 - [N24001450]NHIDCL,ASSAM	09/2021	625.64 -	07/2024 -	07/2024	0/0
524	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 - [N24001451]NHIDCL,ASSAM	03/2022	215.27 -	07/2024 -	07/2024	0/0
525	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 - [N24001452]NHIDCL,ASSAM	04/2022	170.95 -	07/2024 -	07/2024	0/0
526	JOGIGHOPA BRIDGE - [N24001434]NHIDCL,ASSAM	08/2021	746.76 -	11/2024 -	11/2024	0/0
	National Highways Authority Of India					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
527	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	07/2013	0/0
528	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
529	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	01/2016	0/0
530	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 589.00	01/2016 -	01/2019	0/0
531	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 2,262.00	01/2019 -	01/2019	0/0
532	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	03/2019	0/0
533	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 839.00	05/2017 -	05/2019	0/0
534	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	05/2019	0/0
535	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	07/2019	0/0
536	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019	0/0
537	4 LANING OF SOLAPUR - YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	10/2019	0/0
538	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 480.31	01/2014 -	12/2019	0/0
539	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- 01/2020	01/2020	0/0
540	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	03/2020	0/0
541	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 416.00	- -	02/2021	0/0
542	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI, UTTAR PRADESH	12/2017	1,232.21 -	- -	03/2021	0/0
543	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 -	- -	05/2021	0/0
544	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	08/2021	0/0
545	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	09/2021	0/0
546	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	10/2021	0/0
547	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	10/2021	0/0
548	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 1,103.55	04/2018 -	12/2021	0/0
549	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	12/2021	0/0
550	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
551	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	02/2022	0/0
552	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	02/2022	0/0
553	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2022	0/0
554	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 1,082.40	10/2013 03/2022	03/2022	0/0
555	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2022	0/0
556	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	03/2022	0/0
557	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 05/2022	03/2022	0/0
558	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	03/2022	0/0
559	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	03/2022	0/0
560	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	03/2022	0/0
561	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 03/2022	03/2022	0/0
562	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	03/2022	0/0
563	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2022	0/0
564	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	03/2022	0/0
565	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	03/2022	0/0
566	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	04/2022	0/0
567	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	05/2022	0/0
568	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2022	0/0
569	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	05/2022	0/0
570	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	05/2022	0/0
571	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DSIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	05/2022	0/0
572	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	05/2022	0/0
573	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2022	0/0
574	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 1,140.64	10/2017 -	05/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
575	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	05/2022	0/0
576	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	05/2022	0/0
577	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	05/2022	0/0
578	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	05/2022	0/0
579	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 655.64	02/2019 04/2021	05/2022	0/0
580	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	06/2022	0/0
581	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	06/2022	0/0
582	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	06/2022	0/0
583	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	06/2022	0/0
584	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	06/2022	0/0
585	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	06/2022	0/0
586	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	06/2022	0/0
587	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	06/2022	0/0
588	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2022	0/0
589	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2022	0/0
590	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	06/2022	0/0
591	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2022	0/0
592	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2022	0/0
593	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	06/2022	0/0
594	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	06/2022	0/0
595	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	06/2022	0/0
596	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	07/2022	0/0
597	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 12/2021	07/2022	0/0
598	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	07/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
599	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022	0/0
600	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 373.10	10/2017 -	07/2022	0/0
601	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022	0/0
602	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	07/2022	0/0
603	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	07/2022	0/0
604	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 1,632.70	- 07/2022	07/2022	0/0
605	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 570.98	01/2020 08/2021	07/2022	0/0
606	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	08/2022	0/0
607	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 819.35	05/2018 03/2022	08/2022	0/0
608	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 1,248.00	- -	08/2022	0/0
609	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 2,909.00	- 11/2021	08/2022	0/0
610	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	09/2022	0/0
611	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	09/2022	0/0
612	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 2,408.72	04/2019 -	09/2022	0/0
613	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 4,041.80	- -	09/2022	0/0
614	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 3,150.00	04/2019 12/2021	09/2022	0/0
615	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	09/2022	0/0
616	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	09/2022	0/0
617	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2022	0/0
618	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	09/2022	0/0
619	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	09/2022	0/0
620	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	10/2022	0/0
621	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	10/2022	0/0
622	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	10/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
623	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	10/2022	0/0
624	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	10/2022	0/0
625	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	10/2022	0/0
626	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	10/2022	0/0
627	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	11/2022	0/0
628	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	11/2022	0/0
629	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- 11/2022	11/2022	0/0
630	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	11/2022	0/0
631	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	11/2022	0/0
632	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
633	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	12/2022	0/0
634	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 480.35	05/2018 -	12/2022	0/0
635	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	12/2022	0/0
636	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 03/2021	12/2022	0/0
637	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 567.00	04/2019 07/2022	12/2022	0/0
638	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,603.99	06/2018 12/2021	12/2022	0/0
639	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,192.10	06/2018 12/2021	12/2022	0/0
640	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	12/2022	0/0
641	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	12/2022	0/0
642	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	12/2022	0/0
643	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	12/2022	0/0
644	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	12/2022	0/0
645	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 1,296.93	- -	12/2022	0/0
646	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 1,065.70	- -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
647	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 649.00	- 10/2021	12/2022	0/0
648	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	12/2022	0/0
649	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 1,282.30	- -	12/2022	0/0
650	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	12/2022	0/0
651	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	11/2019 01/2022	12/2022	0/0
652	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	11/2019 -	12/2022	0/0
653	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	11/2019 -	12/2022	0/0
654	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 1,414.01	06/2018 -	01/2023	0/0
655	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	02/2023	0/0
656	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 1,140.50	- 03/2021	02/2023	0/0
657	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- 02/2023	02/2023	0/0
658	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 1,240.13	02/2021 04/2021	02/2023	0/0
659	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 526.09	04/2014 -	03/2023	0/0
660	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	03/2023	0/0
661	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	03/2023	0/0
662	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARS-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 736.01	03/2020 12/2018	03/2023	0/0
663	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 05/2021	03/2023	0/0
664	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	03/2023	0/0
665	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	03/2023	0/0
666	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,603.94	- -	03/2023	0/0
667	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	05/2023	0/0
668	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	06/2023	0/0
669	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2023	0/0
670	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	06/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
671	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 644.50	- 12/2019	06/2023	0/0
672	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	06/2023	0/0
673	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2023	0/0
674	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	06/2023	0/0
675	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	07/2023	0/0
676	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	08/2017 08/2023	08/2023	0/0
677	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 664.10	- 08/2023	08/2023	0/0
678	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	08/2023	0/0
679	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 10/2023	10/2023	0/0
680	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	- -	10/2023	0/0
681	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428]NHAI,TAMIL NADU	03/2018	998.70 -	11/2021 -	11/2023	0/0
682	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429]NHAI,TAMIL NADU	03/2018	1,294.47 -	11/2021 -	11/2023	0/0
683	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2023	0/0
684	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	12/2023	0/0
685	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2023	0/0
686	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431]NHAI,TAMIL NADU	03/2018	1,872.68 -	10/2020 -	12/2023	0/0
687	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 1,862.77	- -	01/2024	0/0
688	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	01/2024	0/0
689	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRA ROAD (SH-1 - [N24001414]NHAI,PUNJAB	12/2020	733.00 -	01/2024 04/2024	01/2024	0/0
690	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430]NHAI,TAMIL NADU	03/2018	2,120.40 -	01/2022 -	01/2024	0/0
691	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	04/2024	0/0
692	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB	12/2020	881.00 -	04/2024 -	04/2024	0/0
693	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	01/2024 -	04/2024	0/0
694	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB	12/2020	1,234.40 -	04/2024 -	04/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
695	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB	12/2020	1,094.46 -	04/2024 -	04/2024	0/0
696	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- [N24001419]NHAI,PUNJAB	02/2021	1,269.96 -	04/2024 -	04/2024	0/0
697	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420]NHAI,PUNJAB	02/2021	853.66 -	04/2024 -	04/2024	0/0
698	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 1,380.73	12/2013 05/2024	05/2024	0/0
699	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	- -	06/2024	0/0
700	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 07/2022	07/2024	0/0
701	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	07/2024	0/0
702	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 - [N24001432]NHAI,ASSAM	12/2021	300.00 -	08/2024 -	08/2024	0/0
703	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	09/2024	0/0
704	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	10/2024	0/0
705	DEVELOPMENT OF MULTIMODAL LOGISTICS PARK AT BANGALORE AND EXTERNAL CONNECTIVITY TO THE MULTI MODEL L - [N24001449]NHAI,KARNATAKA	06/2022	1,769.70 -	03/2025 -	03/2025	0/0
706	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
707	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
708	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
709	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
710	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
711	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
712	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.92	- -	-	0/0
713	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 416.07	- 07/2021	-	0/0
714	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
715	4-laning of Khammam-Ashwaraopet section of NH-365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
716	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
717	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
718	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
719	FOUR LANEING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
720	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
721	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 461.42	06/2021 11/2021	11/2022	0/0
	<u>Department Of Telecommunication</u>					
722	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	06/2022	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
723	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 06/2024	06/2024	0/0
724	CONSTRUCTION OF NEW NACIN CAMPUS, PALASAMIDRAM, ANDHRA PRADESH - [N28000152]CPWD,ANDHRA PRADESH	02/2022	702.47 -	08/2024 -	08/2024	0/0
725	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	03/2021 -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
726	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	-	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
727	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	11/2024	0/0
728	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	12/2025	0/0
	<u>Maharastra Metro Rail Corporation Ltd.</u>					
729	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 03/2023	03/2023	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
730	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	03/2020 -	12/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
731	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 05/2025	05/2025	0/0
732	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 07/2025	07/2025	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
733	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2022	0/0
	<u>Patna Metro Rail Corporation</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
734	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL, BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
735	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB, MAHARASHTRA	03/2017	233.57 -	12/2019 12/2022	-	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					
736	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR	05/2017	191.62 -	11/2020 -	05/2022	0/0
737	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR	12/2014	225.77 398.90	03/2020 -	06/2022	0/0
738	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR	04/2015	268.63 431.21	01/2021 -	06/2022	0/0
739	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO, BIHAR	05/2017	356.37 -	04/2021 -	09/2022	0/0
740	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO, BIHAR	11/2018	236.15 -	12/2020 -	10/2022	0/0
741	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO, BIHAR	03/2017	277.42 -	05/2021 -	10/2022	0/0
742	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO, BIHAR	08/2017	578.89 -	06/2022 -	12/2022	0/0
743	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO, BIHAR	08/2017	824.00 -	06/2022 -	12/2022	0/0
744	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO, BIHAR	03/2018	230.06 -	07/2021 -	03/2023	0/0
745	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19 -	08/2021 -	08/2023	0/0
746	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO, BIHAR	03/2018	294.02 -	10/2021 -	12/2023	0/0
747	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 413.29	09/2020 -	03/2024	0/0
	<u>Delhi Jal Board</u>					
748	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB, DELHI	12/2018	515.07 -	01/2021 -	03/2022	0/0
749	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD - 10MG/L - [N30000014]DJB, DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
750	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
751	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
752	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB, DELHI	05/2017	344.81 -	05/2020 -	-	0/0
	<u>Kolkata Metropolitan Development Authority</u>					
753	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 -	06/2022	0/0

Costing Rs. 150 Crore and Above (August 2022)						
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
754	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	06/2022	0/0
755	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA,WEST BENGAL	08/2017	185.22 -	12/2021 -	09/2023	0/0
756	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA,WEST BENGAL	01/2018	172.10 -	12/2021 -	09/2023	0/0
757	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA,WEST BENGAL	10/2017	164.93 -	12/2021 -	09/2023	0/0
758	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA,WEST BENGAL	05/2018	198.43 224.69	02/2022 -	03/2024	0/0
759	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA,WEST BENGAL	03/2018	165.16 -	06/2022 -	03/2024	0/0
760	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA,WEST BENGAL	05/2018	160.00 154.73	02/2022 -	03/2024	0/0
761	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA,WEST BENGAL	01/2019	384.96 -	04/2022 -	12/2024	0/0
762	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA,WEST BENGAL	03/2019	287.53 -	04/2022 -	12/2024	0/0
763	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA,WEST BENGAL	12/2018	234.31 -	04/2022 -	12/2024	0/0
764	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA,WEST BENGAL	08/2017	307.12 -	09/2022 -	12/2024	0/0
	<u>Uttar Pradesh Jal Nigam</u>					
765	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	06/2022	0/0
766	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH	01/2019	206.05 -	10/2021 -	08/2022	0/0
767	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2022	0/0
768	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH	05/2017	767.59 -	09/2021 -	12/2022	0/0
769	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH	01/2019	231.79 234.03	12/2021 -	06/2023	0/0
770	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH	03/2019	271.39 -	08/2021 -	03/2024	0/0
771	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH	10/2017	213.62 261.12	03/2022 -	04/2024	0/0
772	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 690.71	06/2022 -	04/2024	0/0
773	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	07/2021 -	04/2024	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
774	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	02/2022	0/0
	<u>COMMERCE</u>					
	<u>Nbcc For Commerce</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
775	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-	0/0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>					
	<u>Cpwd Of Higher Education</u>					
776	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	07/2022 -	10/2022	0/0
	<u>Rites Of Higher Education</u>					
777	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 429.70	09/2014 12/2022	12/2022	0/0
	<u>DPIIT</u>					
	<u>Dmic For Dpiit</u>					
778	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	20,084.00 20,084.00	03/2027 03/2027	03/2027	0/0
	<u>Iicc For Dpiit</u>					
779	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	12/2019 -	01/2023	0/0
	<u>RENEWABLE ENERGY</u>					
	<u>Cpwd For Renewable Energy</u>					
780	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-	0/0
	Total		8,65,129.10 -			0/0
	Grand Total		8,65,129.10			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
1	AN MELT PROJECT AT RCF TROMBAY - [N08000019	5/2022	187.27	187.27	0.80	09/2024	07/2024
	Total		187.27	187.27	.80		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150	3/2019	1,828.00	1,828.00	303.17	09/2025	05/2024
	Total		1,828.00	1,828.00	303.17		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 3,338.00	3,338.00	3,250.17	12/2020 02/2023	12/2022
4	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409	9/2020	18,936.00	18,936.00	1,433.13	09/2024	08/2024
	Total		21,257.00	22,274.00	4,683.30		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
5	DEVIKOT SOLAR 90MW - [N18000280	3/2020	501.29	524.83	506.75	09/2021 01/2023	09/2022
6	DEVIKOT SOLAR 150MW - [N18000281	1/2020	798.24	852.90	637.22	09/2021 11/2022	09/2022
7	ANTA SOLAR 90 MW - [N18000292	1/2021	382.22	382.22	36.61	03/2022 12/2023	03/2023
8	ETTAYAPURAM SOLAR 230MW - [N18000290	3/2020	1,316.22	1,316.22	1,059.63	09/2021 11/2022	10/2022
9	KAWAS SOLAR 56 MW - [N18000283	8/2020	261.80	293.03	243.32	10/2021 01/2023	08/2022
	Total		3,259.77	3,369.20	2,483.53		
	<u>RAILWAYS</u>						
	<u>Rail Vikas Nigam Ltd.</u>						

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
10	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99 -	6,753.42	2,374.44	12/2026 -	03/2025
	Total		2,966.99 -	6,753.42	2,374.44		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
11	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179	3/2017	217.35 -	217.35	173.98	11/2020 12/2022	09/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
12	DABOKA KATHKATI PACKAGE-2 - [N24001364	3/2021	335.88 -	335.88	70.36	01/2024 -	01/2023
13	DABOKA KATHKATI PACKAGE-4 - [N24001365	2/2021	260.07 -	260.07	109.24	12/2023 -	12/2022
14	CHURACHANPUR TUIVAI PKG-3 - [N24001405	7/2021	673.27 -	673.27	106.28	10/2023 -	08/2023
	<u>National Highways Authority Of India</u>						
15	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 04/2024	01/2024
	Total		2,219.57 -	2,219.57	459.86		
	Grand Total		31,718.60	36,631.46	10,305.10		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	6,216.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	6,216.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	570.11	09/2018 10/2022	10/2022
3	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]	6/2018	2,467.00 -	2,467.00	1,048.18	02/2022 12/2024	12/2024
4	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	660.06	10/2021 04/2023	04/2023
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	475.39 -	475.39	248.29	04/2021 08/2023	08/2023
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	192.21	09/2021 12/2023	12/2023
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]	11/2016	303.80 -	351.21	247.98	04/2020 12/2022	12/2022
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB I AIRPORT KOLKATA - [N04000080]	1/2016	458.00 -	458.00	190.85	03/2020 03/2024	03/2024
9	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,216.90 -	1,216.90	333.86	10/2022 03/2024	03/2024
10	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	456.86 -	456.86	376.59	09/2020 12/2022	12/2022
11	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 - [N04000098]	10/2021	446.12 -	446.12	40.91	08/2023 -	08/2023
12	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 - [N04000094]	3/2021	242.14 -	242.14	57.40	12/2022 -	12/2022
13	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]	2/2019	645.63 -	645.63	519.30	08/2022 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
14	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]	8/2017	177.10 -	177.10	137.92	02/2020 12/2022	12/2022
15	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]	1/2018	1,405.00 -	1,405.00	681.21	08/2022 08/2023	08/2023
16	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24 -	412.24	284.51	06/2021 03/2023	03/2023
17	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	175.15	05/2022 03/2023	03/2023
18	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71 -	389.71	325.34	11/2021 04/2023	04/2023
	Total		11,164.28 -	11,636.25	6,089.87		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
19	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	48.22	03/2023 -	03/2023
20	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]	8/2020	7,254.37 -	7,254.37	782.87	03/2028 -	03/2028
21	EXPANSION OF ASHOK OCP - [N06000247]	5/2021	2,898.28 -	2,898.28	186.45	03/2026 -	03/2026
22	EXPANSION OF KARO OCP - [N06000246]	1/2022	908.47 -	908.47	99.05	03/2026 -	03/2026
23	EXPANSION OF KONAR OCP - [N06000245]	1/2022	799.34 -	799.34	263.19	03/2032 -	03/2032
24	EPR ROHINI KARKATA OCP - [N06000243]	1/2021	1,020.42 -	1,020.42	81.23	03/2025 -	03/2025
25	EPR PUNDI OCP - [N06000242]	11/2020	713.35 -	713.35	233.94	03/2024 -	03/2024
26	EPR TAPIN SOUTH OCP - [N06000241]	11/2020	230.41 -	230.41	18.14	03/2025 -	03/2025
27	JHARKHAND LAIYO OCP - [N06000240]	8/2020	764.57 -	764.57	152.91	03/2031 -	03/2031
28	SIRKA OCP - [N06000239]	5/2020	222.82 -	222.82	136.52	03/2025 -	03/2025
29	CHANDRAGUPT OCP - [N06000238]	8/2020	973.50 -	973.50	204.84	03/2032 -	03/2032
30	KOTRE BASANTPUR PACHMO OCP - [N06000237]	8/2020	861.06 -	861.06	137.75	03/2032 -	03/2032
31	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]	7/2021	778.80 -	778.80	508.97	03/2026 -	03/2026
32	EXPANSION PROJECT AMRAPALI OCP - [N06000217]	8/2020	5,136.15 -	5,136.15	331.85	03/2028 -	03/2028
	<u>Eastern Coal Fields Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
33	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	2.00	03/2026 -	03/2026
34	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	168.07	03/2024 -	03/2024
35	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	11.09	03/2025 -	03/2025
36	BONJEMEHARI EXPANSION OCP - [N06000244]	8/2021	570.12 -	570.12	.23	03/2025 -	03/2025
37	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]	4/2020	1,210.12 -	1,210.12	152.04	03/2029 -	03/2029
38	MOHANPUR EXPANSION OC PHASE II - [N06000236]	11/2020	888.99 -	888.99	13.41	03/2025 -	03/2025
39	SONEPUR BAZARI EXPANSION OC - [N06000220]	7/2021	5,365.88 5,366.00	5,365.88	170.95	03/2029 -	03/2029
40	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	2.14	03/2027 -	03/2027
41	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	37.77	03/2029 -	03/2029
42	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	6.04	03/2027 -	03/2027
	<u>Mahanadi Coal Fields Limited</u>						
43	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,803.48	03/2026 -	03/2026
44	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	934.50	03/2027 -	03/2027
45	BALARAM EXPANSION OCP - [N06000230]	8/2020	3,504.21 -	3,504.21	620.60	03/2029 -	03/2029
46	GOPALJI-KANIHA OCP - [N06000229]	8/2020	8,416.19 -	8,416.19	1,280.15	03/2028 -	03/2028
47	BHUBANESWARI EXPANSION OCP - [N06000227]	8/2020	3,145.45 -	3,145.45	840.23	03/2031 -	03/2031
48	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,355.67	03/2029 -	03/2029
	<u>Neyveli Lignite Corporation</u>						
49	TALABIRA II AND III OCP - [N06000189]	7/2017	2,401.07 -	2,401.07	918.18	01/2027 -	01/2027
50	PACHWARA SOUTH COAL BLOCK - [N06000193]	7/2013	1,795.01 -	1,795.01	40.80	09/2028 -	09/2028
	<u>Northern Coal Fields Limited</u>						
51	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	6.55	03/2023 -	03/2023
52	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	138.51	03/2024 -	03/2024
53	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	6.16	03/2025 -	03/2025
54	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	36.27	03/2025 -	03/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Singareni Colliers Company Limited</u>						
55	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	123.02	03/2023 -	03/2023
56	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210]	11/2015	489.62 -	489.62	341.71	03/2023 -	03/2023
57	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	282.84	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
58	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	11.18	03/2023 -	03/2023
59	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	234.80	03/2022 03/2025	03/2025
60	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	13.24	03/2023 -	03/2023
61	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
62	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
63	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,646.22	03/2023 -	03/2023
64	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	5,180.64	03/2023 -	03/2023
65	RAMPUR BATURA OC (4.0 MTY) - [N06000233]	7/2019	1,248.93 -	1,248.93	297.19	03/2026 -	03/2026
66	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
67	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,990.07	03/2029 -	03/2029
68	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
69	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	182.09	03/2024 -	03/2024
70	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	446.28	03/2029 -	03/2029
71	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	2.67	03/2026 -	03/2026
72	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	79.53	03/2026 -	03/2026
73	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	87.36	03/2026 -	03/2026
74	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	163.63	03/2021 03/2025	03/2025
	<u>Western Coal Fields Limited</u>						
75	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	465.37	03/2025 -	03/2025
76	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	108.78	03/2021 09/2022	09/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	21.89	03/2026 -	03/2026
78	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
79	GAURI PAUNI EXPANSION OC - [N06000235]	8/2020	337.38 -	337.38	48.04	03/2029 -	03/2029
80	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231]	11/2020	826.80 -	826.80	314.10	03/2026 -	03/2026
81	RPR FOR JAMUNIA UG - [N06000228]	8/2020	281.25 -	281.25	22.91	03/2026 -	03/2026
82	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226]	9/2018	313.34 -	313.34	169.46	03/2024 -	03/2024
83	DHANKASA UG (RECAST) (1 MTY) - [N06000224]	2/2020	289.30 -	289.30	40.60	03/2025 -	03/2025
84	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]	2/2020	1,184.33 -	1,184.33	511.36	03/2027 -	03/2027
85	BHANEAGAON OC (1MTY) - [N06000221]	2/2017	409.68 -	409.68	93.68	03/2023 -	03/2023
86	ADASA UG TO OC (1.50 MTY) - [N06000219]	11/2018	333.43 -	333.43	173.40	03/2024 -	03/2024
87	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	131.28	03/2028 -	03/2028
88	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
89	BHATADI EXPANSION OC - [N06000254]	2/2020	729.86 -	729.86	149.25	03/2028 -	03/2028
90	MAKARDHOKDA I EXPANSION OC - [N06000253]	6/2022	497.06 -	497.06	135.18	03/2026 -	03/2026
91	SINGHORI DEEP OC - [N06000252]	5/2022	421.84 -	421.84	86.08	03/2029 -	03/2029
92	SAONER UG MINE I EXPANSION - [N06000251]	1/2022	253.51 -	253.51	24.86	03/2028 -	03/2028
93	TAWA III UG MINE - [N06000250]	12/2021	324.25 -	324.25	10.20	03/2027 -	03/2027
94	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
	Total		1,16,984.82 -	1,16,984.82	28,432.17		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Central Public Works Department</u>						
95	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL - [N42000010]	8/2021	316.25 -	316.25	-	02/2024 -	02/2024
	<u>Cpwd Of Higher Education</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
96	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	424.93 -	424.93	209.30	07/2022 10/2022	10/2022
97	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	.15	04/2023 -	04/2023
98	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]	7/2019	851.00 851.00	851.00	466.32	03/2022 10/2022	10/2022
99	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	106.00	06/2022 04/2023	04/2023
	<u>Rites Of Higher Education</u>						
100	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	9/2013	484.32 -	429.70	242.25	09/2014 12/2022	12/2022
	Total		3,145.01 -	3,090.39	1,024.02		
	<u>DPIIT</u>						
	<u>Dmic For Dpiit</u>						
101	NATIONAL INDUSTRIAL CORRIDOR PROJECT - [N40000001]	9/2011	20,084.00 -	20,084.00	9,680.31	03/2027 03/2027	03/2027
	Total		20,084.00 -	20,084.00	9,680.31		
	<u>FINANCE</u>						
	<u>Cpwd For Finance</u>						
102	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	262.00	208.93	10/2019 10/2022	10/2022
	Total		209.00 -	262.00	208.93		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
103	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	667.78	09/2023 -	09/2023
	Total		1,404.00 -	1,404.00	667.78		
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
104	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" - [N28000147]	1/2020	166.98 167.00	166.98	17.41	10/2023 03/2024	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003	5/2019	199.31 -	199.31	98.57	01/2022 03/2023	03/2023
	Total		366.29 -	366.29	115.98		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
106	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	4,103.00 5,055.00	5,055.00	1,486.31	04/2021 01/2024	01/2024
107	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	581.00	96.18	11/2020 12/2023	12/2023
108	UTKAL D AND E COAL BLOCK - [N10000011	5/2016	534.00 -	667.23	497.21	01/2020 11/2023	11/2023
109	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	59.47	04/2021 12/2023	12/2023
110	POTTANGI BAUXITE MINES - [N10000016	5/2018	1,437.00 -	1,381.00	334.32	12/2024 12/2024	12/2024
111	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014	9/2017	166.62 -	163.17	135.00	06/2019 12/2022	12/2022
	Total		7,078.62 -	8,330.40	2,608.49		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
112	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	972.00	06/2019 02/2023	02/2023
113	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373	11/2018	248.55 -	248.55	180.31	06/2022 03/2023	03/2023
114	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374	8/2019	1,607.00 -	1,607.00	507.46	08/2022 06/2023	06/2023
115	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410	8/2020	697.00 -	697.00	486.80	03/2023 -	03/2023
116	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI - [N16000452	5/2022	423.39 -	423.39	36.46	03/2024 -	03/2024
117	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL - [N16000442	4/2021	1,164.69 -	1,164.69	58.88	06/2024 -	06/2024
	<u>Chennai Petroleum Corporation Limited</u>						
118	CBR 9 MMTPA PROJECT - [N16000434	1/2021	31,580.00 -	31,580.00	698.40	06/2025 -	06/2025
	<u>Gas Authority Of India Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
119	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	2,105.70	1,811.30	12/2020 11/2022	11/2022
120	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,048.00	2,444.60	12/2020 11/2022	11/2022
121	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,570.80	12/2012 02/2025	02/2025
122	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]	8/2018	217.92 -	217.92	126.20	04/2021 12/2022	12/2022
123	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]	5/2019	8,797.00 -	8,797.00	397.00	04/2025 -	04/2025
124	60 KTA POLYPROPYLENE PROJECT - [N16000429]	3/2019	910.56 -	910.56	213.00	04/2024 -	04/2024
125	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	2,903.70	05/2023 -	05/2023
126	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	448.70	11/2022 06/2023	06/2023
127	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	918.30	07/2022 07/2023	07/2023
128	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	2,819.70	12/2021 06/2023	06/2023
129	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	1,084.40	12/2020 06/2023	06/2023
	<u>Hindustan Petroleum Corporation Limited</u>						
130	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	3,185.00	2,943.70	06/2021 08/2022	08/2022
131	NEW LPG PLANT AT VARANASI - [N16000447]	8/2017	194.62 -	194.62	61.25	05/2024 -	05/2024
132	BHATINDA SANGRUR PIPELINE - [N16000440]	11/2021	367.00 -	367.00	7.07	04/2024 -	04/2024
133	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	567.76	11/2022 -	11/2022
134	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	235.86	12/2022 12/2023	12/2023
135	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	113.39	03/2024 -	03/2024
136	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]	9/2021	160.00 -	160.00	.13	06/2024 -	06/2024
137	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	502.70	02/2023 -	02/2023
	<u>Indian Iron Steel Company</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI - [N16000438] <u>Indian Oil Corporation Limited</u>	1/2022	827.00 -	827.00	63.86	07/2024 -	07/2024
139	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	6,025.00	4,938.92	12/2018 11/2023	11/2023
140	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	2,638.70	09/2022 02/2023	02/2023
141	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT - [N16000454]	1/2022	328.00 -	328.00	1.55	09/2024 -	09/2024
142	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI - [N16000453]	1/2022	389.00 -	389.00	-	09/2024 -	09/2024
143	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE - [N16000451]	3/2022	564.00 -	564.00	-	11/2024 -	11/2024
144	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY - [N16000446]	9/2021	378.00 -	378.00	60.31	10/2023 -	10/2023
145	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM - [N16000441]	3/2022	277.00 -	277.00	-	07/2026 -	07/2026
146	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	82.58	02/2027 09/2028	09/2028
147	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]	10/2018	613.00 -	613.00	191.24	12/2029 03/2030	03/2030
148	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]	10/2018	176.00 -	176.00	110.40	08/2027 02/2029	02/2029
149	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	49.33	10/2023 -	10/2023
150	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	818.04	09/2024 -	09/2024
151	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	173.85	08/2023 -	08/2023
152	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	441.50	12/2022 -	12/2022
153	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	1,266.59	01/2024 -	01/2024
154	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	309.35	01/2023 -	01/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE - [N16000437]	1/2022	463.00 -	463.00	19.27	07/2025 -	07/2025
156	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]	12/2021	9,028.00 -	9,028.00	58.89	10/2024 -	10/2024
157	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	48.73	12/2029 03/2030	03/2030
158	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]	6/2019	2,996.00 -	2,996.00	395.60	02/2028 08/2029	08/2029
159	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]	6/2019	347.00 -	347.00	125.47	02/2028 08/2029	08/2029
160	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	42.34	12/2029 03/2030	03/2030
161	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]	6/2019	439.00 -	439.00	147.85	02/2028 08/2029	08/2029
162	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	57.14	12/2029 03/2030	03/2030
163	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]	6/2019	2,880.00 -	2,880.00	139.21	08/2027 03/2030	03/2030
164	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	65.64	03/2030 -	03/2030
165	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	234.49	03/2030 -	03/2030
166	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	154.30	02/2028 -	02/2028
167	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	661.56	12/2021 01/2023	01/2023
168	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	804.64	12/2022 07/2023	07/2023
169	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	427.10	99.98	09/2022 03/2023	03/2023
170	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	543.00	291.80	09/2021 12/2022	12/2022
171	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	183.14	10/2021 09/2022	09/2022
172	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]	8/2018	466.00 -	466.00	343.45	04/2021 09/2022	09/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
173	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	303.77	- 03/2023	03/2023
174	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	614.47	08/2022 -	08/2022
175	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	1,472.17	05/2023 -	05/2023
176	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	47.33	07/2022 06/2023	06/2023
177	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	188.28	08/2020 11/2022	11/2022
178	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	115.53	02/2020 10/2022	10/2022
179	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	207.36	152.03	04/2020 10/2022	10/2022
180	LPG BP PROJECT JODHPUR - [N16000318]	3/2018	229.80 -	229.80	130.21	- 03/2023	03/2023
181	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	340.76	220.01	02/2020 02/2023	02/2023
182	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	210.47	08/2021 03/2023	03/2023
183	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	101.66	12/2019 01/2023	01/2023
	<u>Indradhanush Gas Grid Ltd</u>						
184	NORTH EAST GAS GRID - [N16000439]	11/2020	9,265.00 -	9,265.00	2,431.15	03/2024 03/2024	03/2024
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
185	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	304.00	41.00	06/2023 01/2024	01/2024
	<u>Numaligarh Refinery Limited</u>						
186	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY [N16000379]	1/2019	12,366.00 -	18,968.00	1,929.71	10/2024 -	10/2024
187	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	3,273.73	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
188	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	2,001.34	1,680.76	05/2013 12/2022	12/2022
189	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) - [N16000445]	11/2019	431.00 -	431.00	29.95	01/2024 -	01/2024
190	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD [N16000444]	1/2022	621.40 -	621.40	72.69	11/2024 -	11/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
191	CREATION OF GAS DEHYDRATION FACILITIES - [N16000443]	3/2022	209.33 -	209.33	-	05/2024 -	05/2024
192	PIPELINE REPLACEMENT PROJECT - VII - [N16000436]	1/2022	3,183.58 -	3,183.58	123.40	05/2024 -	05/2024
193	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON - [N16000433]	8/2021	218.38 -	218.38	35.16	02/2023 -	02/2023
194	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]	8/2021	885.63 -	885.63	231.36	02/2026 -	02/2026
195	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	212.55	03/2025 -	03/2025
196	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	338.56	08/2022 02/2023	02/2023
197	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	829.58	830.87	12/2020 12/2022	12/2022
198	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,494.68	2,141.49	03/2022 03/2023	03/2023
199	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	2,816.87	03/2022 05/2023	05/2023
200	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	2,311.32	05/2021 12/2022	12/2022
201	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	915.64	03/2026 -	03/2026
202	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,911.17	04/2018 05/2023	05/2023
203	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	31,040.00	19,243.11	06/2020 05/2023	05/2023
	<u>Oil India Limited</u>						
204	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	638.60	423.10	02/2020 12/2022	12/2022
205	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION, PROCESSING - [N16000450]	12/2020	430.76 -	430.76	8.66	07/2024 -	07/2024
206	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT - [N16000449]	6/2021	860.00 -	860.00	20.10	12/2024 -	12/2024
	Total		2,67,257.20 -	2,77,704.39	84,707.87		
	<u>POWER</u>						
	<u>Chenab Valley Power Projects [P] Limited</u>						
207	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	2,449.04	04/2020 07/2025	07/2025
	<u>National Hydro-Electric Power Corporation</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
208	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	9/2002	3,919.59 -	10,463.03	10,010.30	09/2009 12/2023	12/2023
209	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	9/2003	6,285.33 -	19,992.43	16,222.78	09/2010 08/2023	08/2023
210	RANGIT IV HE PROJECT - [N18000326]	3/2021	938.29 -	938.29	315.06	05/2024 08/2024	08/2024
211	RATLE HE PROJECT - [N18000324]	2/2021	5,281.94 -	5,281.94	43.55	02/2026 02/2026	02/2026
212	KALPI SOLAR POWER PROJECT - [N18000323]	7/2020	314.64 -	337.77	218.26	03/2022 12/2022	12/2022
	<u>National Thermal Power Corporation</u>						
213	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	679.00	549.68	11/2018 12/2022	12/2022
214	NOKH PLOT-1 SOLAR PV PROJECT 245MW - [N18000320]	3/2022	1,352.71 -	1,352.71	41.85	08/2023 10/2023	10/2023
215	NOKH PLOT-3 SOLAR PV PROJECT 245MW - [N18000322]	3/2022	1,426.94 -	1,426.94	49.14	08/2023 10/2023	10/2023
216	NOKH PLOT-2 SOLAR PV PROJECT 245MW - [N18000321]	3/2022	1,409.52 -	1,409.52	50.84	08/2023 10/2023	10/2023
217	DAYAPAR WIND ENERGY PROJECT 150MW - [N18000319]	11/2021	937.80 -	937.80	102.21	05/2023 -	05/2023
218	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]	3/2020	1,782.00 -	1,782.00	1,146.84	09/2021 01/2023	01/2023
219	NOKHRA - [N18000282]	3/2020	1,722.14 -	1,803.19	1,193.45	09/2021 01/2023	01/2023
	<u>Power Grid Corporation Of India Limited</u>						
220	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299]	5/2021	179.29 -	179.29	79.99	04/2023 -	04/2023
221	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316]	5/2021	576.42 -	576.42	54.00	03/2023 -	03/2023
222	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C [N18000338]	7/2022	186.19 -	186.19	-	03/2025 -	03/2025
223	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B [N18000337]	7/2022	4,546.26 -	4,546.26	21.50	06/2023 -	06/2023
224	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000332]	5/2022	1,666.00 -	1,666.00	-	11/2023 -	11/2023
225	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000331]	2/2022	359.47 -	359.47	9.29	09/2023 -	09/2023
226	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM - [N18000330]	3/2022	288.71 -	288.71	-	12/2024 -	12/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
227	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. - [N18000329]	3/2022	176.22 -	176.22	2.28	03/2023 -	03/2023
228	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM - [N18000328]	2/2022	318.12 -	318.12	45.42	04/2025 -	04/2025
229	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - [N18000327]	3/2019	1,326.00 -	1,326.00	1,054.46	03/2023 -	03/2023
230	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]	3/2021	1,340.81 -	1,340.81	626.81	12/2022 -	12/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						
231	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	5,935.72	01/2024 -	01/2024
232	GUJRAI SOLAR POWER PROJECT - [N18000336]	6/2022	279.94 -	279.94	28.39	08/2023 -	08/2023
233	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	810.74	01/2026 -	01/2026
234	Bagodara Solar Power Project - [N18000297]	5/2021	339.35 -	339.35	45.45	10/2022 -	10/2022
235	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	392.30 -	392.30	397.04	12/2022 -	12/2022
236	BIKANER SOLAR POWER PROJECT - [N18000335]	4/2022	5,491.89 532.00	6,023.89	791.28	05/2024 -	05/2024
237	GURHAH SOLAR POWER PROJECT - [N18000334]	5/2022	466.82 -	466.82	42.58	08/2023 -	08/2023
238	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	285.25	11/2025 -	11/2025
	Total		64,884.11 -	85,920.15	42,623.20		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
239	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	4,670.00	2,229.23	03/2024 -	03/2024
	<u>East Coast Railway</u>						
240	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	2,923.13 -	3,791.66	2,027.20	03/2009 12/2025	12/2025
241	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	729.38	03/2022 03/2026	03/2026
	<u>Northern Railway</u>						
242	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	37,012.26	30,671.82	11/2002 06/2023	06/2023
	<u>Rail Vikas Nigam Ltd.</u>						
243	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,300.00	2,799.96	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
244	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	3,492.37	12/2023 -	12/2023
245	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	4,099.98	12/2023 -	12/2023
	<u>South East Central Railway</u>						
246	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	3,176.60	1,902.75	03/2023 12/2023	12/2023
247	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	2,135.34	1,106.76	03/2021 12/2023	12/2023
248	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.94	918.24	12/2021 12/2023	12/2023
	<u>Southern Railway</u>						
249	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	591.00	464.44	- 09/2022	09/2022
	<u>West Central Railway</u>						
250	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,658.34	03/2021 03/2024	03/2024
251	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,938.00	1,450.69	03/2022 03/2024	03/2024
	<u>Western Railway</u>						
252	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	6,383.82	2,529.21	03/2022 03/2026	03/2026
253	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	1,083.17	252.70	03/2012 03/2024	03/2024
254	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,524.68	1,063.17	03/2022 12/2024	12/2024
255	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	390.14	- 10/2025	10/2025
256	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	4/2018	537.31 -	584.31	2.44	03/2024 12/2024	12/2024
257	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]	4/2017	692.25 -	692.26	8.51	03/2020 12/2024	12/2024
258	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]	4/2017	495.18 -	495.18	1.01	03/2022 03/2026	03/2026
259	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	640.75	497.73	06/2020 03/2023	03/2023
260	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,119.12	962.02	03/2021 12/2022	12/2022
261	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,394.02	1,300.17	03/2021 12/2022	12/2022
262	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,873.10	908.51	03/2022 03/2025	03/2025
263	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	2,448.99	2,142.58	03/2020 03/2024	03/2024
	Total		41,729.46 -	90,567.47	63,609.35		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
264	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	295.47	214.36	02/2017 12/2022	12/2022
265	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	206.46	06/2019 10/2022	10/2022
266	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780	2/2018	293.68 -	293.68	185.08	- 10/2022	10/2022
267	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K - [N24001447	8/2020	371.93 -	371.93	-	12/2024 -	12/2024
268	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOL TO BURTUK (L=23.316KM) - [N24001442	10/2021	385.15 -	385.15	8.95	05/2024 -	05/2024
269	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT - [N24001427	6/2020	166.21 -	166.21	53.63	04/2023 -	04/2023
270	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408	2/2021	925.47 -	925.47	2.54	07/2025 -	07/2025
271	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386	8/2020	222.61 -	222.61	42.15	03/2021 03/2023	03/2023
272	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385	6/2020	221.40 -	221.40	90.53	05/2021 12/2022	12/2022
273	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376	3/2021	182.55 -	182.55	24.82	03/2027 -	03/2027
274	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375	6/2020	496.47 -	496.47	32.23	03/2027 -	03/2027
275	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374	6/2020	437.60 -	437.60	41.92	03/2027 -	03/2027
276	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373	1/2020	358.26 -	358.26	141.82	02/2024 -	02/2024
277	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372	2/2021	588.09 -	588.09	176.69	03/2024 -	03/2024
278	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964	8/2016	350.61 -	350.61	325.56	01/2017 12/2022	12/2022
279	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHMAU ALLAHABAD ON EPC MODE - [N24001421	7/2018	1,948.25 -	1,948.25	509.41	02/2024 -	02/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
280	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09 995.00	995.09	643.29	05/2016 11/2022	11/2022
281	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]	3/2018	289.67 290.00	234.73	262.20	08/2018 08/2022	08/2022
282	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]	1/2017	319.28 -	319.28	241.94	08/2017 08/2022	08/2022
283	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]	11/2016	290.15 -	290.15	188.56	05/2017 08/2022	08/2022
284	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]	3/2018	199.16 -	199.16	101.34	08/2018 10/2022	10/2022
285	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]	3/2018	214.23 -	214.23	138.74	08/2018 11/2022	11/2022
286	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]	12/2016	206.88 -	206.88	134.11	04/2018 11/2022	11/2022
287	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]	12/2016	223.50 -	223.50	132.37	08/2018 11/2022	11/2022
288	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 - [N24001455]	2/2022	191.33 -	191.33	-	08/2022 -	08/2022
289	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR - [N24001454]	2/2022	184.15 -	184.15	-	08/2022 -	08/2022
290	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51 -	237.51	174.77	12/2022 -	12/2022
291	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]	2/2017	157.32 188.00	157.32	24.20	05/2019 05/2023	05/2023
292	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	138.51	09/2021 12/2022	12/2022
293	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]	1/2019	193.19 -	249.72	184.91	- 01/2023	01/2023
294	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]	3/2018	626.76 -	626.76	227.71	07/2020 05/2023	05/2023
295	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]	1/2018	283.15 -	283.15	201.27	05/2020 12/2022	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
296	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981	10/2016	248.83 -	248.83	149.11	03/2019 04/2023	04/2023
297	REHABILITATION AND UPGRADE OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	1/2017	576.48 -	686.13	503.77	01/2018 12/2022	12/2022
298	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	127.85	09/2017 12/2022	12/2022
299	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	236.18	107.81	12/2022 -	12/2022
300	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297	3/2019	450.65 -	450.65	117.78	03/2027 -	03/2027
301	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAGE - [N24001296	3/2019	394.27 -	394.27	158.24	03/2027 -	03/2027
302	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295	3/2019	347.78 -	347.78	223.07	03/2027 -	03/2027
303	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294	3/2019	560.39 -	560.39	307.44	03/2027 -	03/2027
304	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293	3/2019	486.70 -	486.70	201.16	03/2027 -	03/2027
305	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292	3/2019	543.05 -	543.05	241.22	03/2027 -	03/2027
306	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291	3/2019	421.48 -	421.48	147.23	03/2027 -	03/2027
307	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290	3/2019	342.55 -	342.55	264.65	03/2027 -	03/2027
308	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289	3/2019	403.68 -	403.68	224.20	03/2027 -	03/2027
309	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	111.85	05/2020 10/2022	10/2022
310	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	264.67	02/2020 10/2022	10/2022
311	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	1/1991	319.68 -	404.10	400.67	- 11/2022	11/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
312	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	8/2013	171.96 172.00	172.00	108.00	06/2016 09/2022	09/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
313	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683	2/2017	180.57 -	180.57	18.01	04/2017 11/2023	11/2023
314	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	550.00	12/2023 -	12/2023
315	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261	8/2020	311.00 -	311.00	50.95	04/2023 -	04/2023
316	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	28.82	07/2022 03/2023	03/2023
317	IMPHAL - KHONGSANG PKG-4 - [N24001453	8/2021	579.63 -	579.63	-	12/2023 -	12/2023
318	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 - [N24001452	4/2022	170.95 -	170.95	-	07/2024 -	07/2024
319	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 - [N24001451	3/2022	215.27 -	215.27	-	07/2024 -	07/2024
320	DABOKA KATHKATI PACKAGE-6 - [N24001450	9/2021	625.64 -	625.64	-	07/2024 -	07/2024
321	KEIFANG - TUVAI PKG-1 - [N24001440	9/2021	492.94 -	492.94	19.53	05/2023 -	05/2023
322	MERANGKONG-TAMLU-MON (MTM) PKG-5 - [N24001438	7/2021	161.73 -	161.73	11.38	12/2023 -	12/2023
323	TAMENGLONG - MAHUR PKG-6 - [N24001437	9/2021	311.18 -	311.18	22.84	05/2023 -	05/2023
324	TAMENGLONG - MAHUR PKG-5 - [N24001436	8/2021	477.86 -	477.86	14.26	05/2023 -	05/2023
325	JOGIGHOPA BRIDGE - [N24001434	8/2021	746.76 -	746.76	9.76	11/2024 -	11/2024
326	REHABILITATION OF SECTION FROM KM 298.00 TO KM 330.662 PKG-8 - [N24001433	4/2021	154.61 -	154.61	-	07/2023 -	07/2023
327	PEREN-DIMAPUR PKG-5 - [N24001407	2/2021	207.33 -	207.33	-	03/2023 -	03/2023
328	PEREN-DIMAPUR SECTION PKG-2 - [N24001406	7/2021	258.52 -	258.52	52.94	03/2023 -	03/2023
329	TAMENGLONG - MAHUR PKG-4 - [N24001404	7/2021	198.77 -	198.77	16.45	03/2023 -	03/2023
330	TAMENGLONG - MAHUR PKG-2 - [N24001403	7/2021	483.87 -	483.87	58.46	03/2023 -	03/2023
331	TAMENGLONG - MAHUR PKG-1 - [N24001402	7/2021	185.80 -	185.80	14.79	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
332	SENAPATI- IMPHAL PKG-5B - [N24001400	3/2021	211.70 -	211.70	-	01/2023 -	01/2023
333	IMPHAL – MOREH (PACKAGE 4) - [N24001399	3/2021	277.99 -	277.99	46.79	01/2023 -	01/2023
334	MARIAM - PEREN (PKG 2A) - [N24001398	7/2021	204.58 -	204.58	68.82	03/2023 -	03/2023
335	GOHA-KHELLANI PKG-3 - [N24001397	2/2021	431.28 -	431.28	43.78	03/2023 -	03/2023
336	KHELLANI-KHANABAL PKG-5 - [N24001396	7/2021	497.09 -	497.09	25.62	02/2023 -	02/2023
337	KHELLANI-KHANABAL PKG-4 - [N24001395	7/2021	859.67 -	859.67	25.50	08/2023 -	08/2023
338	KHELLANI-KHANABAL PKG-2 - [N24001394	7/2021	512.43 -	512.43	9.78	02/2023 -	02/2023
339	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) [N24001393	8/2020	184.88 -	184.88	57.76	04/2022 12/2022	12/2022
340	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) [N24001392	8/2020	199.03 -	199.03	70.58	04/2022 12/2022	12/2022
341	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391	8/2020	294.04 -	294.04	109.59	04/2022 12/2022	12/2022
342	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
343	DABOKA KATHKATI PACKAGE-5 - [N24001366	3/2021	288.85 -	288.85	8.28	01/2023 -	01/2023
344	MANU-SIMLUNG (PKG 4) - [N24001363	3/2021	354.79 -	354.79	24.72	12/2022 -	12/2022
345	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362	12/2020	410.60 -	410.60	21.94	02/2024 02/2024	02/2024
346	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361	1/2021	332.20 -	332.20	19.69	09/2023 -	09/2023
347	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360	3/2021	260.21 -	260.21	87.95	12/2022 -	12/2022
348	TLABUNG - LUNGLEI PKG-B - [N24001359	3/2021	740.58 -	740.58	33.38	01/2023 -	01/2023
349	TLABUNG - LUNGLEI PKG-A - [N24001358	3/2021	698.44 -	698.44	36.21	12/2022 -	12/2022
350	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357	3/2021	674.71 -	674.71	163.89	06/2023 -	06/2023
351	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356	3/2021	233.25 -	233.25	52.09	12/2022 -	12/2022
352	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355	3/2021	374.39 -	374.39	129.85	12/2022 -	12/2022
353	IMPHAL - KHONGSANG PKG-2 - [N24001353	3/2021	195.14 -	195.14	21.30	12/2022 -	12/2022
354	IMPHAL – MOREH PACKAGE- 3 - [N24001352	3/2021	259.31 -	259.31	112.33	12/2022 -	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
355	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]	12/2020	804.00 -	804.00	188.31	08/2023 -	08/2023
356	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]	11/2020	4,997.04 -	4,997.04	364.26	09/2028 -	09/2028
357	KHELLANI-KHANABAL PKG-6 - [N24001324]	2/2021	285.28 -	285.28	70.27	09/2022 -	09/2022
358	KHELLANI-KHANABAL PKG-1 - [N24001323]	3/2021	486.45 -	486.45	15.88	09/2022 -	09/2022
359	DEMBUEN - BRUNI - [N24001321]	12/2020	606.63 -	606.63	167.37	03/2023 -	03/2023
360	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	24.48	03/2023 -	03/2023
361	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	327.61	12/2023 -	12/2023
362	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	171.79	12/2023 -	12/2023
363	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	60.68	10/2022 -	10/2022
364	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	27.58	12/2022 -	12/2022
365	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	45.41	12/2022 -	12/2022
366	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	13.88	12/2022 -	12/2022
367	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	28.25	01/2023 -	01/2023
368	KARGIL-ZANSKR PACKAGE-7 - [N24001347]	1/2021	308.86 -	308.86	80.00	06/2024 -	06/2024
369	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	81.30	05/2024 -	05/2024
370	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	16.77	01/2023 -	01/2023
371	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	1.98	01/2023 -	01/2023
372	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	21.95	01/2023 -	01/2023
373	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]	3/2021	260.40 -	260.40	8.26	12/2022 -	12/2022
374	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	24.74	12/2022 -	12/2022
375	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	15.85	12/2023 11/2024	11/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
376	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336	8/2020	230.45 -	230.45	32.58	04/2023 09/2023	09/2023
377	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335	11/2020	284.21 -	284.21	44.52	12/2023 -	12/2023
378	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334	11/2020	445.51 -	445.51	175.18	12/2023 -	12/2023
379	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333	9/2019	761.54 -	761.54	256.92	05/2023 -	05/2023
380	KARGIL-ZANSKR PACKAGE-5 - [N24001330	8/2020	169.79 -	169.79	103.72	12/2023 -	12/2023
381	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262	7/2020	345.38 -	345.38	115.75	04/2023 -	04/2023
382	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	678.90	09/2026 -	09/2026
383	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	84.58	04/2023 -	04/2023
384	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	52.00	12/2022 -	12/2022
385	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249	6/2020	347.36 -	347.36	154.53	01/2022 08/2022	08/2022
	<u>National Highways Authority Of India</u>						
386	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138	9/2010	946.00 -	1,046.56	822.13	06/2018 12/2022	12/2022
387	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552	3/2016	701.40 -	701.40	156.33	03/2019 03/2023	03/2023
388	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559	3/2016	720.00 -	793.63	326.96	- 09/2022	09/2022
389	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854	3/2018	1,005.08 -	1,005.08	-	- 02/2023	02/2023
390	FOUR LANING OF SOLAN-KAITHLIGHT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	3/2018	478.74 -	1,135.08	905.95	- 11/2022	11/2022
391	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828	3/2018	633.55 -	736.33	68.39	- 08/2023	08/2023
392	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	8/2017	950.64 -	1,168.33	503.74	08/2017 08/2023	08/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
393	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	665.19	528.73	03/2020 03/2023	03/2023
394	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603	8/2016	1,167.42 -	870.00	380.24	03/2019 06/2023	06/2023
395	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	332.33	07/2019 10/2023	10/2023
396	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	347.64	07/2019 07/2023	07/2023
397	DEVELOPMENT OF MULTIMODAL LOGISTICS PARK AT BANGALORE AND EXTERNAL CONNECTIVITY TO THE MULTI MODEL L - [N24001449	6/2022	1,769.70 -	1,769.70	4.20	03/2025 -	03/2025
398	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAGE - [N24001446	5/2020	894.00 -	894.00	213.55	12/2023 -	12/2023
399	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDABAD - [N24001445	5/2020	691.52 -	691.52	113.57	07/2023 -	07/2023
400	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION - [N24001444	5/2020	882.00 -	882.00	.02	01/2024 -	01/2024
401	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 - [N24001443	5/2020	690.30 -	690.30	62.72	03/2024 -	03/2024
402	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
403	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- [N24001419	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
404	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
405	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
406	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
407	FOUR LANNING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	1,921.25	12/2018 12/2022	12/2022
408	FOUR LANNING OF LUDHIANA- TALWANDI SECTION - [N24000483	9/2014	479.00 -	479.00	456.80	- 03/2023	03/2023
409	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,380.73	1,354.65	12/2013 05/2024	05/2024
410	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 - [N24001432	12/2021	300.00 -	300.00	29.81	08/2024 -	08/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
411	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442	12/2015	649.50 -	649.50	277.75	03/2019 12/2022	12/2022
412	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	2,639.00	1,710.83	08/2016 12/2022	12/2022
	Total		84,352.95 -	86,466.11	24,519.72		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
413	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	2,160.50	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	2,160.50		
	<u>SOCIAL JUSTICE</u>						
	<u>Central Public Works Department</u>						
414	CENTRE FOR DISABILITY SPORTS - [N38000001	2/2019	170.99 -	170.99	73.80	03/2024 -	03/2024
	Total		170.99 -	170.99	73.80		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
415	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	21,940.00	21,019.89	05/2015 03/2023	03/2023
416	SCREENING PLANT-III AT KIRANDUL - [N12000127	3/2021	2,092.97 -	2,092.97	396.60	08/2024 -	08/2024
	<u>Steel Authority Of India Limited (Sail)</u>						
417	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	128.30	05/2023 -	05/2023
418	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125	1/2022	970.18 -	970.18	76.33	05/2025 -	05/2025
419	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT - [N12000126	2/2022	207.74 -	207.74	8.71	06/2024 -	06/2024
420	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	123.14	12/2023 -	12/2023
	Total		19,715.31 -	26,130.31	21,752.97		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
421	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137 <u>Bangalore Metro Rail Corporation Limited</u>	3/2019	5,384.17 -	5,384.17	763.91	03/2024 -	03/2024
422	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151 <u>Central Public Works Department</u>	6/2021	14,788.10 -	14,788.10	2,942.84	06/2026 -	06/2026
423	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129	10/2016	1,128.00 -	1,128.00	69.28	03/2022 06/2024	06/2024
424	CONSTRUCTION OF NEW NACIN CAMPUS, PALASAMIDRAM, ANDHRA PRADESH - [N28000152 <u>Maharastra Metro Rail Corporation Ltd.</u>	2/2022	702.47 -	702.47	1.16	08/2024 -	08/2024
425	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121 <u>Madhya Pradesh Metro Rail Co Limited</u>	12/2016	11,420.00 -	11,420.00	9,009.34	11/2021 03/2023	03/2023
426	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	244.26	02/2023 05/2025	05/2025
427	INDORE METRO RAIL - [N28000125 <u>National Capital Region Transport Corp</u>	11/2018	7,500.80 -	7,500.80	261.39	02/2023 07/2025	07/2025
428	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134 <u>Patna Metro Rail Corporation</u>	3/2019	30,274.00 -	30,274.00	9,900.05	06/2025 -	06/2025
429	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	2/2019	13,365.77 -	13,925.50	437.20	06/2024 -	06/2024
	Total		91,504.71 -	92,064.44	23,629.43		
	<u>WATER RESOURCES</u>						
	<u>Delhi Jal Board</u>						
430	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014 <u>Polavaram Project Authority</u>	3/2017	665.78 -	665.78	372.23	12/2022 -	12/2022
431	POLAVARAM IRRIGATION PROJECT - [N30000002	2/2009	10,151.04 -	55,548.87	20,538.05	03/2020 03/2024	03/2024
	Total		10,816.82 -	56,214.65	20,910.28		
	Grand Total		7,95,857.75	9,31,651.47	3,39,030.67		

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 6,840.00	7,500.00	09/2010 -	09/2024	114.78
	Total		3,492.00 - 6,840.00	7,500.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 - 1,383.00	2,445.00	09/2021 -	09/2023	76.79
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	12/2023	38.72
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2025	7.88
	Total		2,871.27 - 2,871.27	4,157.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
5	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>						
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 - 479.53	868.37	03/2013 -	03/2024	81.09
7	ANANTA OCP EXPANSION PH III - [N06000225]	08/2008	228.08 - 228.08	314.71	03/2012 -	-	37.98
	<u>Neyveli Lignite Corporation</u>						
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 - 5,907.11	7,980.79	12/2015 -	02/2021	35.10
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	11/2023	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		26,513.45 .00 26,513.45	31,548.15			
	<u>DPIIT</u>						
	<u>licc For Dpiit</u>						
10	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	01/2023	8.49
	Total		4,773.00 .00 4,773.00	5,178.00			
	<u>FINANCE</u>						
	<u>Cpwd For Finance</u>						
11	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089	12/2015	209.00 - 209.00	262.00	10/2019 -	10/2022	25.36
	Total		209.00 .00 209.00	262.00			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
12	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 - 414.11	586.50	11/2013 -	09/2021	41.63
13	LGBRIMH-TEZPUR, ASSAM - [N21000007	07/2012	175.57 - 175.57	179.15	12/2014 -	03/2018	2.04
14	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 - 204.44	285.00	05/2017 -	06/2021	39.41
15	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
16	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 - 168.90	191.20	05/2017 -	01/2021	13.20
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 - 505.58	586.96	03/2018 -	04/2020	16.10
18	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 - 152.95	177.92	02/2018 -	04/2021	16.33

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
19	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 - 244.00	248.00	09/2018 -	12/2021	1.64
20	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 - 272.19	280.00	03/2019 -	02/2021	2.87
21	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 - 156.56	205.00	- -	01/2022	30.94
22	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]	03/2018	268.84 - 268.84	284.67	- -	05/2021	5.89
23	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 - 249.01	249.07	- -	05/2021	.02
	<u>Nbcc For Health</u>						
24	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 - 1,351.00	1,471.04	09/2021 -	08/2022	8.89
	Total		4,456.80 .00 4,456.80	5,069.51			
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
25	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 - 1,219.21	1,679.02	10/2019 -	12/2022	37.71
26	NSG AT KOLKATA - [N28000104]	10/2014	162.88 - 162.88	210.83	04/2018 -	09/2023	29.44
27	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]	06/2019	277.35 - 277.35	290.33	07/2022 -	06/2023	4.68
	Total		1,659.44 .00 1,659.44	2,180.18			
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
28	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 - 225.54	247.90	02/2021 -	10/2022	9.91
29	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 - 327.00	327.01	08/2020 -	12/2022	14.17
	<u>Hindustan Petroleum Corporation Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
30	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 - 20,928.00	26,264.00	07/2020 -	03/2023	25.50
	<u>Indian Oil Corporation Limited</u>						
31	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT [N16000336]	03/2018	588.20 - 588.20	730.20	- -	03/2023	24.14
	<u>Numaligarh Refinery Limited</u>						
32	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY [N16000379]	01/2019	12,366.00 - 12,366.00	18,968.00	10/2024 -	10/2024	53.39
	<u>Oil & Natural Gas Corporation Limited</u>						
33	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	05/2019	763.92 - 763.92	829.58	12/2020 -	12/2022	8.60
	<u>Oil India Limited</u>						
34	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 - 543.91	638.60	02/2020 -	12/2022	17.41
	Total		35,701.99 .00 35,742.57	48,005.29			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
35	KALPI SOLAR POWER PROJECT - [N18000323]	07/2020	314.64 - 335.36	337.77	03/2022 -	12/2022	7.35
	<u>National Thermal Power Corporation</u>						
36	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 - 5,867.38	7,103.00	03/2013 -	12/2024	138.48
37	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 - 14,366.58	17,007.00	06/2019 -	12/2024	18.38
38	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 - 1,381.84	1,803.00	09/2019 -	07/2025	30.48
39	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 - 10,598.98	10,998.00	11/2020 -	06/2023	3.76
40	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 - 633.80	679.00	11/2018 -	12/2022	28.19
41	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 - 501.29	524.83	09/2021 -	09/2022	4.70

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
42	DEVIKOT SOLAR 150MW - [N18000281	01/2020	798.24 - 798.24	852.90	09/2021 -	09/2022	6.85
43	NOKHRA - [N18000282	03/2020	1,722.14 - 1,722.14	1,803.19	09/2021 -	01/2023	4.71
44	KAWAS SOLAR 56 MW - [N18000283	08/2020	261.80 - 261.80	293.03	10/2021 -	08/2022	11.93
	<u>Power Grid Corporation Of India Limited</u>						
45	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 - 522.29	546.36	11/2016 -	04/2022	4.61
46	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 - 4,754.42	9,129.32	12/2018 -	03/2024	92.02
47	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 - 5,111.33	6,700.00	12/2018 -	01/2024	31.08
48	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	08/2022	14.11
49	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262	05/2017	186.17 - 186.17	219.66	07/2019 -	12/2022	17.99
50	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	08/2017	1,931.39 - 1,931.39	2,635.55	02/2020 -	04/2023	36.46
51	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301	10/2019	1,031.00 - 1,031.00	1,143.00	08/2021 -	10/2022	10.86
	<u>Satluj Jal Vidyut Nigam Limited</u>						
52	NAITWAR MORI HEP - [N18000265	10/2017	648.33 - 648.33	947.89	12/2021 -	12/2022	46.20
53	BIKANER SOLAR POWER PROJECT - [N18000335	04/2022	5,491.89 532.00 532.00	6,023.89	05/2024 -	05/2024	1,032.31
	<u>Thdc India Limited</u>						
54	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 - 1,657.00	4,825.60	02/2016 -	10/2023	191.23
	Total		58,287.49 4,032.00 56,341.34	77,566.99			
	<u>RAILWAYS</u>						
	Central Railways						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 - 3,168.29	3,445.48	03/2023 -	03/2024	8.75
56	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	1,387.52	03/2021 -	03/2025	75.00
57	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,805.17	03/2021 -	03/2025	111.54
58	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,384.72	03/2022 -	03/2024	8.85
59	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	4,670.00	03/2024 -	03/2024	28.76
60	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2025	10.94
	<u>Container Corporation Of India</u>						
61	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	03/2019	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
62	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00 30,357.00	51,219.00	- - -	-	68.72
	<u>East Central Railways</u>						
63	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 - 3,020.95	3,800.00	- -	07/2022	267.84
64	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 - 967.29	1,110.00	03/2012 -	06/2023	241.82
65	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 - 678.54	1,010.00	03/2019 -	07/2022	48.85
66	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) [N22000180]	04/2004	372.14 - 1,470.50	1,700.00	- -	03/2024	356.82
67	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 - 548.00	783.83	03/2020 -	03/2025	43.03
68	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 - 1,483.14	1,510.00	- -	03/2024	358.42
	<u>East Coast Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
69	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 - 2,923.13	3,791.66	03/2009 -	12/2025	29.71
70	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 - 1,111.99	1,539.28	02/2019 -	-	38.43
71	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 - 1,160.00	1,160.83	03/2020 -	03/2024	.07
72	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2025	15.45
<u>Eastern Railways</u>							
73	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
74	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 - 365.17	439.30	03/2017 -	10/2022	20.30
75	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 - 175.80	495.10	- -	09/2022	181.63
76	MONIGRAM- NIMITTA - [N22000301	04/2012	250.93 - 250.93	310.70	- -	03/2023	23.82
77	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 - 255.64	272.20	- -	12/2022	6.48
78	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2023	133.39
79	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 - 288.35	402.48	- -	05/2022	39.58
<u>Indian Railway Construction Company Limited</u>							
80	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	12/2024	117.23
81	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 - 3,055.00	3,500.00	09/2018 -	12/2023	14.57
<u>Metropolitan Rapid Transport Projects</u>							
82	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 - 495.44	2,980.41	03/2004 -	03/2023	501.57
83	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 - 495.74	774.51	06/2013 -	12/2022	56.23

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
84	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	-	75.91
	<u>North Central Railway</u>						
85	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>						
86	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 2,393.47	6,527.45	03/2014 -	12/2023	172.72
87	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 4,454.17	14,322.79	03/2011 -	12/2023	221.56
88	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,145.79	03/2019 -	03/2024	197.45
89	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 - 532.87	2,650.00	03/2019 -	12/2023	397.31
90	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 - 2,326.52	6,663.00	03/2015 -	03/2026	186.39
91	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 1,339.48	7,876.92	12/2015 -	12/2023	488.06
92	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 - 1,798.00	2,047.51	03/2019 -	12/2023	13.88
93	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 569.63	708.73	03/2020 -	09/2022	24.42
94	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	8,324.28	03/2021 -	-	818.33
95	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	03/2024	94.45
96	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	401.65	- -	03/2023	66.30
97	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	983.55	03/2020 -	10/2024	137.09
98	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	4,059.65	03/2022 -	03/2025	81.86
	<u>North Eastern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
99	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	800.00	01/2019 -	-	171.19
100	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 - 1,295.42	2,000.00	03/2022 -	03/2022	54.39
101	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	-	.16
102	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 - 150.00	341.66	04/2017 -	10/2022	127.77
103	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	800.00	- -	12/2023	32.78
	<u>North Western Railway</u>						
104	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	06/2022	109.82
105	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	10/2022	16.97
	<u>Northern Railway</u>						
106	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	12/2011	211.31
107	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 - 336.91	791.39	- -	09/2023	134.90
108	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
109	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,017.96	07/2012 -	11/2024	348.44
110	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 - 328.14	1,540.13	03/2023 -	12/2025	369.35
	<u>Rail Vikas Nigam Ltd.</u>						
111	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	09/2022	102.92
112	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	433.00	03/2009 03/2009	12/2022	109.18
113	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,834.54	03/2016 -	07/2025	65.94

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
114	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	03/2025	127.62
115	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,300.00	03/2023 -	03/2023	55.15
116	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,259.48	03/2016 -	03/2026	7.78
117	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
118	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	3,633.12	03/2020 -	06/2022	141.61
119	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 - 1,548.66	2,538.01	12/2021 -	12/2022	63.88
120	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	950.00	03/2016 -	09/2022	50.15
121	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32
122	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,500.00	03/2022 -	12/2022	58.97
123	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,457.79	03/2019 -	03/2023	57.26
124	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	24,659.00	12/2024 -	03/2025	52.07
125	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,725.00	03/2020 -	07/2022	281.93
126	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
127	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	09/2022	111.91
128	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,552.26	03/2019 -	03/2023	64.62
129	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	2,203.53	12/2020 -	09/2022	86.23

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
130	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	09/2022	23.55
131	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	12/2022	102.11
	<u>South Central Railway</u>						
132	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2027	102.85
133	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 - 1,160.48	2,250.00	03/2010 -	03/2025	93.89
134	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2025	5.16
135	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
136	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2025	7.06
137	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 185.00	242.28	03/2022 -	-	30.96
	<u>South East Central Railway</u>						
138	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 - 1,908.51	3,176.60	03/2023 -	12/2023	66.44
139	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 - 229.00	1,096.00	12/2021 -	12/2024	378.60
140	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 - 1,370.00	1,370.94	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>						
141	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 - 969.83	1,312.97	03/2020 -	10/2022	35.38
142	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 - 428.65	472.50	06/2022 -	12/2025	10.23
143	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39 - 390.39	511.75	12/2021 -	01/2023	31.09
144	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 - 338.00	393.83	06/2022 -	12/2023	16.52

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>South Western Railway</u>						
145	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 - 1,801.01	2,000.97	- -	03/2025	11.10
146	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 - 1,378.00	1,530.09	03/2016 -	12/2026	55.13
147	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,404.03	- -	12/2025	16.57
148	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	5,174.30	- -	03/2028	123.51
149	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,954.21	03/2020 -	12/2022	68.91
150	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,614.59	1,878.00	03/2019 -	02/2024	16.31
	<u>Southern Railway</u>						
151	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 - 724.69	3,081.20	02/2019 -	03/2025	325.17
152	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 - 582.83	3,500.79	- -	12/2025	500.65
153	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	591.00	- -	09/2022	259.47
154	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,084.48	03/2019 -	12/2027	1,626.99
155	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,281.63	1,339.00	- -	03/2025	33.90
	<u>West Central Railway</u>						
156	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2024	585.35
157	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
158	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 - 582.13	1,247.64	03/2022 -	09/2024	114.32
	<u>Western Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
159	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 - 5,839.02	6,383.82	03/2022 -	03/2026	82.20
160	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 - 322.19	1,083.17	03/2012 -	03/2024	240.36
161	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 - 1,631.75	2,448.99	03/2020 -	03/2024	195.15
162	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 - 1,125.53	1,394.02	03/2021 -	12/2022	34.41
163	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 - 1,042.12	1,119.12	03/2021 -	12/2022	11.65
164	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM [N22000434]	03/2010	265.88 - 265.88	311.36	- -	03/2024	17.11
165	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]	03/2012	217.38 - 217.38	393.62	- -	03/2024	81.07
166	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]	03/2012	248.26 - 248.26	528.49	- -	03/2024	112.88
167	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	04/2016	700.00 - 603.69	640.75	06/2020 -	03/2023	-8.46
168	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	04/2018	537.31 - 537.31	584.31	03/2024 -	12/2024	8.75
	Total		1,61,272.48 34,377.00 1,87,481.71	3,37,599.09			
	<u>RENEWABLE ENERGY</u>						
	<u>Cpwd For Renewable Energy</u>						
169	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI [N28000118]	10/2017	271.90 - 271.90	365.00	11/2019 -	-	34.24
	Total		271.90 .00 271.90	365.00			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
170	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B [N24000331]	01/2014	282.41 - 282.41	319.96	03/2016 -	07/2022	13.30

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
171	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 - 280.16	290.59	- -	01/2020	3.72
172	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 - 268.08	390.73	05/2017 -	06/2022	45.75
173	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 - 889.24	904.82	- -	-	1.75
174	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 - 460.73	461.00	- -	-	.06
175	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 - 237.80	238.00	11/2019 -	10/2022	.08
176	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 - 166.21	174.90	08/2018 -	10/2022	5.23
177	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 - 160.27	213.97	08/2019 -	03/2023	33.51
178	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 - 236.78	263.26	08/2019 -	03/2023	11.18
179	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 - 217.22	226.88	08/2018 -	10/2022	4.45
180	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	03/2016	877.79 - 877.79	949.54	06/2019 -	09/2022	8.17
181	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 - 333.21	353.43	12/2015 -	01/2021	6.07
182	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00 504.00	504.19	11/2018 - -	01/2022	.04
183	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00 995.00	995.09	05/2016 -	11/2022	.01
184	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00 203.00	203.21	05/2019 -	09/2019	.10
185	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00 373.00	373.10	05/2019 -	11/2020	.03
186	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00 322.00	322.48	05/2019 -	03/2020	.15

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
187	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00 548.00	548.03	06/2019 -	01/2020	.01
188	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00 391.00	391.06	06/2019 -	03/2022	.02
189	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	12/2020	.05
190	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	03/2022	40.76
191	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00 257.00	257.38	12/2019 -	03/2022	.15
192	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	03/2022	.00
193	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	09/2022	.05
194	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	03/2022	.08
195	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	06/2022	.24
196	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	03/2022	.06
197	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	01/2021	.12
198	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	06/2021	.06
199	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	03/2022	.08
200	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	12/2020	.14
201	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	09/2021	.01
202	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	09/2022	.13

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
203	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	06/2022	.07
204	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	12/2020	.11
205	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	06/2022	.01
206	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	12/2020	.03
207	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	02/2022	.06
208	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	11/2020	.47
209	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	10/2020	.08
210	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	12/2021	.02
211	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	03/2022	.16
212	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	12/2022	.08
213	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	12/2022	26.19
214	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	06/2022	2.47
215	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	11/2020	.31
216	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	09/2022	.03
217	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	12/2022	.00
218	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	-	.13

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
219	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 - 392.33	428.55	03/2018 -	10/2022	9.23
220	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156	01/2017	166.67 - 166.67	264.34	09/2017 -	07/2022	58.60
221	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158	03/2018	159.97 - 159.97	242.61	06/2019 -	03/2023	51.66
222	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 - 297.30	318.28	01/2019 -	07/2022	7.06
223	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 - 325.86	386.41	10/2018 -	04/2021	18.58
224	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 - 336.25	369.96	09/2019 -	11/2020	10.03
225	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 - 186.96	322.24	09/2014 -	-	72.36
226	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 - 1,979.00	2,036.90	- -	12/2021	2.93
227	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J - [N24001208	03/2018	288.30 - 288.30	323.36	08/2020 -	10/2022	12.16
228	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 - 281.45	319.96	- -	09/2022	13.68
229	REHABILITATION AND UPGRADE OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 - 497.14	572.66	08/2016 -	12/2022	15.19
230	REHABILITATION AND UPGRADE OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 - 624.98	731.50	10/2016 -	12/2022	17.04
231	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239	03/2018	240.38 - 212.74	240.38	06/2019 -	-	.00
232	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 - 197.67	236.18	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
233	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	05/2015	454.89 - 454.89	814.56	05/2018 -	07/2022	79.07

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
234	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320	06/2015	463.49 - 463.49	801.54	06/2018 -	03/2023	72.94
235	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	03/2015	168.39 - 168.39	259.79	11/2018 -	08/2022	54.28
236	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 - 588.95	873.91	11/2018 -	09/2022	48.38
237	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582	01/2016	294.17 - 294.17	385.57	01/2016 -	07/2022	31.07
238	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583	01/2016	252.00 - 252.00	330.30	01/2016 -	12/2022	31.07
239	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 - 195.23	252.79	04/2017 -	11/2022	29.48
240	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 - 203.36	263.31	04/2017 -	10/2022	29.48
241	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 - 373.07	387.00	08/2016 -	-	3.73
242	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 - 198.22	252.05	04/2017 -	08/2022	27.16
243	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 - 447.37	530.67	10/2017 -	06/2022	36.77
244	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823	03/2015	829.00 - 829.00	1,307.50	01/2016 -	06/2023	57.72
<u>National Highways Authority Of India</u>							
245	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
246	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
247	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 - 511.54	591.00	11/2013 -	05/2022	15.53
248	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 - 480.35	777.03	05/2018 -	12/2022	46.30
249	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 - 593.26	717.24	05/2018 -	06/2022	20.90

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
250	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
251	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	09/2015	934.46 - 934.46	1,543.51	03/2018 -	12/2022	65.18
252	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 - 567.00	639.58	04/2019 -	12/2022	-38.57
253	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	09/2022	1.37
254	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	12/2022	6.11
255	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	03/2023	1.33
256	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	12/2023	41.78
257	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	05/2022	21.50
258	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	01/2021	25.80
259	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	03/2022	44.60
260	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 - 458.03	486.00	- -	06/2022	6.11
261	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	1,588.29	09/2019 -	05/2022	14.40
262	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 - 1,169.61	2,280.00	- -	05/2021	94.94
263	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 - 323.72	355.24	08/2018 -	05/2022	9.74
264	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 - 950.69	1,108.00	08/2019 -	06/2022	16.55
265	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 - 290.73	359.60	- -	09/2022	23.69

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
266	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	01/2017	1,251.11 - 1,251.11	1,361.00	- -	09/2022	8.78
267	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	03/2017	1,373.28 - 1,373.28	1,405.27	03/2020 -	08/2022	2.33
268	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	09/2022	10.58
269	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 - 744.64	982.00	03/2020 -	07/2024	31.88
270	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	06/2022	1.06
271	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 - 736.01	830.31	03/2020 -	03/2023	23.39
272	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	03/2022	13.97
273	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	03/2022	10.24
274	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	06/2022	41.54
275	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	06/2022	44.39
276	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	12/2022	3.95
277	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	08/2017	950.64 - 1,161.00	1,168.33	08/2017 -	08/2023	22.90
278	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703	10/2017	964.17 - 1,140.64	1,198.64	10/2017 -	05/2022	24.32
279	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 - 1,124.11	1,309.79	09/2017 -	03/2023	16.52
280	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG -I - [N24000723	01/2018	573.70 - 644.50	726.99	- -	06/2023	26.72
281	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 - 273.46	276.17	- -	03/2023	.99

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
282	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 - 1,296.93	1,422.13	- -	12/2022	21.94
283	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 - 1,995.34	2,400.00	- -	10/2022	20.28
284	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 - 2,177.80	2,450.00	- -	09/2022	12.50
285	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
286	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 - 1,052.21	1,361.00	- -	09/2022	29.35
287	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 - 1,532.62	1,827.00	03/2021 -	08/2022	19.21
288	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 - 496.20	537.17	- -	06/2023	8.26
289	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 - 1,632.70	16,732.70	- -	07/2022	1,524.60
290	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]	03/2018	633.55 - 664.10	736.33	- -	08/2023	16.22
291	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 - 1,282.30	1,308.88	- -	12/2022	28.71
292	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96 - 2,065.96	2,169.00	- -	01/2024	4.99
293	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
294	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 - 634.70	925.96	- -	02/2022	45.89
295	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 - 795.50	922.64	- -	04/2022	15.98
296	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]	03/2018	478.74 - 478.74	1,135.08	- -	11/2022	137.10
297	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	03/2018	642.13 - 642.13	807.00	- -	06/2022	25.68

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
298	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]	10/2019	743.88 - 743.88	743.89	- -	08/2022	.00
299	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]	12/2017	656.98 - 656.98	840.00	- -	11/2022	27.86
300	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]	12/2017	217.96 - 217.96	884.00	- -	10/2022	305.58
301	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]	09/2018	617.41 - 655.64	668.45	02/2019 -	05/2022	8.27
302	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]	11/2019	1,226.88 - 1,240.13	1,321.60	02/2021 -	02/2023	7.72
303	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]	07/2020	3,426.00 - 3,426.00	5,852.00	12/2021 -	-	70.81
304	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]	02/2019	731.89 - 731.89	732.34	11/2019 -	12/2022	.06
305	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]	02/2019	594.75 - 594.75	606.75	11/2019 -	12/2022	2.02
	Total		89,831.29 14,395.00 90,714.91	1,22,721.17			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
306	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 - 10,773.00	12,925.22	12/2018 -	09/2022	19.98
	<u>Central Public Works Department</u>						
307	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33 - 197.33	220.00	04/2019 -	-	11.49
	<u>Chennai Metro Rail Ltd</u>						
308	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 - 14,600.00	18,380.00	12/2015 -	-	25.89
	<u>Delhi Metro Rail Corporation</u>						
309	DELHI MRTS PHASE-III - [N28000056]	09/2011	38,585.00 - 38,585.00	40,180.91	03/2016 -	-	4.14
	<u>Kochi Metro Rail Corporation Ltd</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
310	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 - 5,181.79	6,218.14	07/2017 -	-	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>						
311	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 - 23,136.00	33,406.00	03/2020 -	12/2023	44.39
	<u>Nagpur Metro Rail Corporation Ltd</u>						
312	NAGPUR METRO RAIL - [N28000085]	08/2014	8,680.00 - 8,680.00	9,759.79	03/2018 -	03/2022	12.44
	<u>Patna Metro Rail Corporation</u>						
313	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 - 13,365.77	13,925.50	06/2024 -	06/2024	4.19
	Total		1,14,518.89 .00 1,14,518.89	1,35,015.56			
	Grand Total		5,03,859.00 52,804.00 5,32,394.28	7,77,168.27			

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	12320	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2023	11459	90
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2024	3492	168
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM	AAI	06/2017	12/2020	09/2023	255.68	33
6	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	AAI	02/2019	08/2022	03/2023	645.63	7
7	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	12/2022	177.1	34
8	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	03/2024	380.87	24
9	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	AAI	05/2020	05/2022	03/2023	353.61	10
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2025	1142	48
11	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	04/2023	389.71	17
12	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	AAI	03/2017	04/2021	08/2023	475.39	28
13	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	09/2023	1383	24
14	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT.	AAI	08/2018	02/2021	12/2022	353.25	22
15	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT.	AAI	11/2017	09/2021	09/2023	255.69	24
16	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	10/2022	417.23	49
17	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	12/2024	2467	34
18	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	AAI	08/2018	10/2021	04/2023	951.28	18
19	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	12/2022	303.8	32
20	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2023	346.27	27
21	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	03/2024	458	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
22	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	AAI	05/2018	10/2022	03/2024	1216.9	17
23	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	12/2022	456.86	27
24	UPGRADATION OF JABALPUR AIRPORT	AAI	06/2016	06/2021	03/2023	412.24	21
25	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	AAI	01/2018	08/2022	08/2023	1405	12

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
26	KULDA EXPANSION OCP- 15 MTY	MCL	06/2014	03/2018	03/2026	348.16	96
27	RCE OF KISTARAM OPENCAST PROJECT	SCCL	03/2017	03/2021	03/2023	164.04	24
28	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
29	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	09/2022	289.45	100
30	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
31	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2023	510.85	84
32	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	132
33	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2025	339.88	138
34	MOONIDIH XV SEAM UG	BCCL	08/2011	03/2019	04/2024	1230.27	61
35	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2025	869.44	48
36	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	11/2023	17237	24
37	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	09/2023	328	30
38	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2022	03/2024	413.84	24
39	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12
40	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
41	SRP OC-II EXPANSION PROJECT	SCCL	11/2016	03/2018	03/2024	272.73	72
42	UKNI DEEP OC	WCL	11/2018	03/2021	09/2022	318.14	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	BELLORA-NAIGAON DEEP OC	WCL	11/2018	03/2021	09/2022	252.71	18
44	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	06/2023	243	62
45	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2023	162.46	108
46	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2026	178.44	144
47	CHHAL OC SEAM -III (6.00 MTY)	SECL	12/2013	03/2022	03/2025	610.63	36
48	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2027	1458.17	147
49	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	BCCL	02/2014	03/2021	03/2023	555.52	24
50	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
51	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2026	1375.38	60
52	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
53	RAJNAGAR OCP RPR (1.70 MTY)	SECL	12/2014	03/2021	03/2024	357.8	36
54	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2023	1783.09	24
55	BHATADI EXPASION OC (0.975 MTY)	WCL	02/2016	03/2019	09/2026	327.41	90
56	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2023	163.51	144
57	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	12/2022	304.13	69
58	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II	SCCL	03/2019	03/2021	03/2023	473.22	24
59	VENKATESH KHANI COAL MINE	SCCL	10/2020	03/2023	03/2024	484.51	12
60	RCE OF KALYANIKHANI OPENCAST PROJECT	SCCL	03/2016	03/2020	03/2023	384.32	36
61	RCE OF KAKATHIYAKHANI OC - 2 PROJECT	SCCL	08/2017	03/2020	03/2024	442.42	48
62	RCE OF INDARAM OPENCAST PROJECT	SCCL	08/2017	03/2021	03/2023	349.28	24

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
63	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD FOR DEFEN	12/2016	02/2020	10/2022	246.31	32

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
64	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD EDUCATION	09/2018	09/2020	11/2022	375	26
65	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD EDUCATION	07/2019	03/2021	03/2023	753.63	24
66	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD EDUCATION	07/2019	03/2022	10/2022	851	7
67	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH 6 PLUS 8 STOREYED	CPWD EDUCATION	03/2020	06/2020	12/2022	193.83	30
68	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD EDUCATION	02/2016	06/2017	12/2022	496.18	66
69	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD EDUCATION	01/2018	05/2020	12/2022	430	31
70	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	CPWD EDUCATION	01/2019	03/2022	01/2023	790.79	10
71	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	CPWD EDUCATION	02/2019	06/2020	11/2022	655.34	29
72	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	CPWD EDUCATION	10/2019	05/2022	03/2023	348.24	10
73	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	CPWD EDUCATION	09/2019	09/2022	07/2023	588.72	10
74	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	MITES OF HIGH	09/2013	09/2014	12/2022	484.32	99
75	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	CPWD EDUCATION	05/2019	03/2020	02/2023	303.9	35
76	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	CPWD EDUCATION	09/2018	06/2022	04/2023	392.51	10

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
77	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	01/2023	4773	37

FINANCE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
78	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD FOR FINANCE	12/2015	10/2019	10/2022	209	36

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	08/2022	1351	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
80	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI	CPWD FOR MHA	05/2019	01/2022	03/2023	199.31	14
81	NSG AT KOLKATA	CPWD FOR MHA	10/2014	04/2018	09/2023	162.88	65
82	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	CPWD FOR MHA	06/2019	07/2022	06/2023	277.35	11
83	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MHA	10/2013	10/2019	12/2022	1219.21	38

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
84	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	NALCO	09/2017	06/2019	12/2022	166.62	42
85	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	12/2023	483	32
86	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	11/2023	534	46
87	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	CPWD	04/2019	04/2022	10/2024	255.37	30
88	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	01/2024	4103	33
89	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	12/2023	355	37

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
90	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	IOCL	06/2019	02/2028	08/2029	2996	18
91	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	IOCL	06/2019	02/2028	08/2029	439	18
92	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	IOCL	06/2019	08/2027	03/2030	2880	31
93	CGD PROJECT AT REWA DISTRICT	IOCL	10/2018	02/2027	09/2028	177	19
94	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFI	06/2020	06/2023	01/2024	200	7
95	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	GAIL	08/2018	04/2021	12/2022	217.92	20
96	SRIKAKULAM ANGUL PIPELINE PROJECT	GAIL	09/2019	07/2022	07/2023	2658.34	12
97	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	06/2023	164.69	23
98	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	12/2022	1636	28

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
99	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	IOCL	08/2018	04/2021	09/2022	466	17
100	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
101	PARADIP SOMNATHPUR HALDIA PIPELINE	IOCL	10/2018	10/2021	12/2022	1297.5	14
102	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	10/2022	225.54	20
103	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	IOCL	10/2018	10/2021	09/2022	316.2	11
104	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
105	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	11/2022	909	22
106	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	12/2022	598	34
107	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2023	3190.69	61
108	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2022	160.1	32
109	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	01/2023	161.59	37
110	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2025	2915	146
111	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	GAIL	07/2017	07/2022	08/2023	243.53	13
112	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	IOCL	01/2020	07/2022	03/2023	202.16	8
113	SULPHUR FORMING UNIT IN SRU	HPCL	10/2020	08/2021	12/2022	210.94	16
114	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	12/2022	607.06	62
115	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	10/2022	1823	19
116	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	12/2022	2321	24
117	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	09/2022	678	67
118	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	03/2023	20928	32
119	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	12/2022	650.82	45
120	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	05/2023	34012	35
121	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	11/2022	1933	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
122	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	11/2022	3437	23
123	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2023	1740	30
124	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677	14
125	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	10/2022	163.02	30
126	REVAMPING OF EXISTING FACILITIES/AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	IOCL	08/2017	08/2021	03/2023	318.8	19
127	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2023	1112	44
128	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2022	249.26	27
129	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	02/2023	206.63	36
130	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2022	861.79	115
131	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	02/2022	12/2022	1945	10
132	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	11/2023	4497	59
133	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	12/2022	348	23
134	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	11/2022	255.4	27
135	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	08/2023	199.36	34
136	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	09/2022	906	31
137	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	GAIL	10/2017	10/2022	10/2023	359.25	12
138	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	GAIL	07/2017	07/2022	08/2023	182.2	13
139	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	12/2022	543.91	34
140	BARAUNI-GUWAHATI PIPELINE	GAIL	06/2018	12/2021	06/2023	3308	18
141	ETHYLENE GLYCOL PROJECT AT PARADIP	IOCL	04/2018	10/2021	12/2022	5654	14
142	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	12/2022	286.42	28
143	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	ONGC	02/2019	05/2021	12/2022	2292.46	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
144	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14
145	HEERA REDEVELOPMENT - PHASE III	ONGC	06/2019	03/2022	03/2023	2494.68	12
146	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	12/2022	462.3	15
147	Fuel Quality Upgradation Project at Paradip Refinery	IOCL	05/2019	08/2021	03/2024	3361	31
148	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	03/2023	278.6	21
149	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	BPCL	07/2017	02/2021	03/2023	580.2	25
150	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2023	371	6
151	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	HPCL	12/2018	12/2022	12/2023	854	12
152	PIPELINE REPLACEMENT PROJECT (PRP-VI)	ONGC	05/2019	12/2020	12/2022	763.92	24
153	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	BPCL	11/2018	06/2022	03/2023	248.55	9
154	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha	BPCL	08/2019	08/2022	06/2023	1607	10
155	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2023	2281.94	7
156	PX-PTA REVAMP AT PANIPAT REFINERY	IOCL	08/2019	12/2021	01/2023	1255	13
157	LPG BP PROJECT CHITT00R	IOCL	07/2019	07/2022	06/2023	167	11
158	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	IOCL	01/2020	04/2023	07/2024	14810	15
159	CITY GAS DISTRIBUTION, JAMSHEDPUR	GAIL	10/2017	10/2022	08/2023	221.45	10
160	DHAMRA HALDIA PIPELINE PROJECT	GAIL	03/2020	11/2022	06/2023	1030.65	7
161	REDEVELOPMENT OF NANDASAN FIELD	ONGC	02/2020	08/2022	02/2023	444.87	6
162	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	IOCL	10/2018	08/2027	02/2029	176	18
163	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	IOCL	06/2019	02/2028	08/2029	347	18

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
164	TEESTA VI HE PROJECT	NHPC	03/2019	03/2024	07/2025	5748.04	16
165	TRANSMISSION SYSTEM STRENGTHENING	PGCIL	06/2021	12/2022	08/2023	1006	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA						
166	AMELIA COAL MINE	THDCIL	01/2017	09/2020	09/2022	2104.21	24
167	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	08/2022	3500	25
168	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	12/2022	186.17	41
169	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	04/2023	1931.39	38
170	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION	PGCIL	11/2018	11/2021	09/2022	173.94	10
171	DEVIKOT SOLAR 90MW	NTPC	03/2020	09/2021	09/2022	501.29	12
172	DEVIKOT SOLAR 150MW	NTPC	01/2020	09/2021	09/2022	798.24	12
173	NOKHRA	NTPC	03/2020	09/2021	01/2023	1722.14	16
174	KAWAS SOLAR 56 MW	NTPC	08/2020	10/2021	08/2022	261.8	10
175	SAMBHU KI BHURJ-II SOLAR 300MW	NTPC	03/2020	09/2021	01/2023	1782	16
176	ETTAYAPURAM SOLAR 230MW	NTPC	03/2020	09/2021	10/2022	1316.22	13
177	ANTA SOLAR 90 MW	NTPC	01/2021	03/2022	03/2023	382.22	12
178	BHENSARA 320 MW	NTPC	01/2021	07/2022	08/2023	1221.73	13
179	CHHATTARGARH 150 MW	NTPC	02/2021	07/2022	08/2023	599.99	13
180	GUJARAT 200 MW (GUVNL TENDER)	NTPC	01/2021	07/2022	08/2023	842.27	13
181	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR)	NTPC	05/2021	09/2022	08/2023	674.92	11
182	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	12/2022	197.4	57
183	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	03/2025	2491.58	141
184	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	10/2023	1657	92
185	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	03/2024	8692.97	149
186	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11
187	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT	PGCIL	10/2019	08/2021	10/2022	1031	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
188	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA	PGCIL	01/2019	03/2022	11/2022	267.33	8
189	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	03/2021	12/2022	09/2023	353.85	9
190	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	06/2021	12/2022	12/2023	713.82	12
191	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	PGCIL	06/2021	12/2022	08/2023	1562	8
192	NORTHERN REGION SYSTEM STRENGTHENING - XL	PGCIL	02/2019	12/2020	03/2023	572.98	27
193	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION	PGCIL	11/2018	11/2021	12/2022	241.38	13
194	NORTH EASTERN REGION STRENGTHENING SCHEME - III	PGCIL	09/2015	12/2017	12/2022	167.31	60
195	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD	PGCIL	01/2020	01/2021	12/2022	562.86	23
196	KALPI SOLAR POWER PROJECT	NHPC	07/2020	03/2022	12/2022	314.64	9
197	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2023	3919.59	171
198	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
199	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2024	2978.48	141
200	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
201	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	12/2024	14366.58	66
202	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	07/2025	1381.84	70
203	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	06/2023	10598.98	31
204	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	12/2022	322.3	46
205	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	12/2022	235.53	42
206	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	11/2022	379.95	35
207	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	63
208	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	01/2024	5111.33	61
209	NAITWAR MORI HEP	SJVN	10/2017	12/2021	12/2022	648.33	12
210	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	03/2025	18668	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
211	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	12/2022	529.68	49

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
212	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	SER	04/2018	06/2022	12/2023	338	18
213	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM)	SER	04/2018	06/2022	12/2025	428.65	42
214	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	SER	03/2019	05/2023	12/2024	1866.31	19
215	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	01/2023	390.39	13
216	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS	WR	04/2018	03/2024	12/2024	537.31	9
217	NIMACH BADI SADRI NEW LINE PROJECT	WR	04/2017	03/2022	03/2026	495.18	48
218	MANSABHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108
219	ANAND GODHRA DOUBLING PROJECT 79 KMS	WR	04/2017	03/2020	12/2024	692.25	57
220	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2025	2923.13	201
221	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
222	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2022	495.74	114
223	NEW B.G. LINE FROM TETELIA TO BYRNihat (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2024	385.2	60
224	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	12/2023	532.87	57
225	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	132
226	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	96
227	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450	148
228	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	06/2023	2500	247
229	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2026	3951.98	120
230	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
231	MUNEERABAD-MAHABOOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
232	BHUJ-NALIYA(GC) WITH EXTENSION FROM	WR	04/2008	03/2012	03/2024	318.24	144

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NALIYA TO VAYOR (WR)						
233	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	48
234	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
235	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2024	1160	48
236	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	12/2022	1156.94	33
237	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600	31
238	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	02/2024	1614.59	59
239	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	12/2024	1347.26	33
240	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2025	1640.04	36
241	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	12/2022	1548.66	12
242	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	21
243	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
244	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2025	548	60
245	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798	57
246	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2022	569.63	30
247	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	03/2024	242.22	48
248	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	10/2024	414.84	55
249	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	09/2022	632.68	78
250	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
251	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2023	915.98	12
252	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36
253	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2023	1491.47	45
254	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2024	1763.93	55
255	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2024	1272.19	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
256	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
257	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	03/2025	1876	24
258	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
259	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
260	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2025	3631	36
261	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	1547.38	24
262	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2026	2499.71	48
263	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
264	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2025	701.61	76
265	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2025	1172.92	75
266	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2025	2232.32	36
267	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
268	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
269	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	10/2022	969.83	31
270	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	03/2024	1724.2	36
271	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2022	943.6	9
272	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2023	927.01	48
273	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
274	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
275	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	09/2022	948.04	30
276	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	09/2022	1402.02	30
277	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2023	942.95	48
278	BHIMSEN - JHANSI DOUBLING WITH	RVNL	03/2012	12/2020	09/2022	1183.25	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	ELECTRIFICATION						
279	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	09/2022	1485.85	21
280	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2024	2478.23	24
281	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2024	582.13	30
282	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
283	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	12/2025	5200	69
284	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2023	528.57	48
285	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
286	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	RVNL	02/2015	03/2022	05/2023	1700	14
287	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	12/2022	760	33
288	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
289	CHANDIGARH-BADDI	NR	04/2007	03/2023	12/2025	328.14	33
290	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	12/2024	744.04	45
291	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	36
292	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
293	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2027	1045.2	216
294	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
295	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2024	424.6	36
296	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	09/2022	1202.7	91
297	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2022	133.41	165
298	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
299	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI- THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
300	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	117
301	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2025	1160.48	180

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
302	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	07/2025	2913.51	112
303	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2026	3503.69	48
304	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	10/2022	365.17	67
305	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	03/2024	3168.29	12
306	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2025	792.89	48
307	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
308	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.3	129
309	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2025	1856.95	24
310	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2026	832.47	120
311	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2026	2288.7	60
312	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
313	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	03/2024	279.54	96
314	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2025	2271.5	48
315	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2023	495.44	228
316	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
317	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	06/2023	324.73	135
318	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
319	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
320	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2026	644.78	108
321	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2024	2288	33
322	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2023	3055	63
323	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
324	JHANSI MANIKPUR AND KHAIRAR BHIMSEN	NCR	03/2018	03/2023	03/2026	4329.53	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DOUBLING						
325	JHANSI BINA DOUBLING	NCR	09/2016	03/2021	12/2023	2001	33

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
326	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN	NHAI	03/2018	10/2020	12/2023	1872.68	38
327	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM	NHAI	03/2018	01/2022	01/2024	2120.4	24
328	JORAM - KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	NHIDCL	08/2020	04/2022	12/2022	228.71	8
329	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	NHAI	02/2019	03/2020	08/2022	996.27	29
330	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	08/2022	847	29
331	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	08/2022	990.97	32
332	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	NHAI	03/2019	05/2020	08/2022	1047	27
333	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER	NHAI	03/2018	11/2021	11/2023	1294.47	24
334	SHIRUR TO KHARDA	MoRTH	02/2017	06/2019	09/2022	381.77	39
335	BHOGAN KHURD TO KASHEDI	MoRTH	09/2017	06/2021	09/2022	743.21	15
336	PARSHURAM GHAT TO ARAWALI	MoRTH	04/2016	12/2019	09/2022	983.14	33
337	KANTE TO WAKED	MoRTH	03/2016	11/2019	12/2022	1230.02	37
338	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	10/2022	392.33	55
339	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	MoRTH	09/2018	09/2021	12/2022	160	15
340	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	MoRTH	08/2016	02/2017	08/2022	175.5	66
341	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	MoRTH	03/2018	06/2019	03/2023	159.97	45
342	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	MoRTH	11/2016	03/2017	09/2022	314.9	66
343	NILAJPHATA TO BHANDARA	MoRTH	01/2018	05/2020	09/2022	420.63	28
344	KARAD TO TAGAON	MoRTH	01/2017	06/2019	12/2022	537.81	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
345	KARAD PATAN CHIPLUN GUHAGAR	MoRTH	02/2017	06/2019	09/2022	407.19	39
346	KOTHARI TO DHANORA	MoRTH	09/2018	08/2020	09/2022	301.38	25
347	SATARA TO MHASWAD	MoRTH	01/2017	07/2019	09/2022	653.46	38
348	SELDOH TO PANVAR	MoRTH	07/2018	05/2020	12/2022	404.33	31
349	MHASWAD TO TEMBHURNI	MoRTH	01/2017	07/2019	09/2022	488.6	38
350	PANCHARAL TO MANDANGHAR	MoRTH	07/2018	05/2020	12/2022	381.08	31
351	PAITHAN TO SHIRUR	MoRTH	03/2017	06/2019	12/2022	341.8	42
352	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MoRTH	01/2016	08/2016	12/2022	497.14	76
353	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MoRTH	11/2015	06/2017	12/2022	335.32	66
354	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MoRTH	01/2016	09/2016	03/2023	476.2	78
355	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	12/2022	624.98	74
356	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	12/2022	452.94	77
357	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	MoRTH	03/2017	01/2018	10/2022	423.79	57
358	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	03/2023	496.02	96
359	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	09/2022	188.8	40
360	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	MoRTH	10/2016	03/2019	04/2023	248.83	49
361	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	MoRTH	01/2018	05/2020	12/2022	283.15	31
362	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	MoRTH	03/2018	07/2020	05/2023	626.76	34
363	SARSAM TO KOTHARI	MoRTH	02/2016	07/2019	09/2022	545.64	38
364	AKOLA TO AKOT	MoRTH	01/2017	06/2019	09/2022	313.95	39
365	WADI TO ASOLA	MoRTH	01/2017	09/2019	12/2022	363.82	39
366	WAKAN PALI KHOPOLI	MoRTH	01/2017	05/2019	09/2022	376.19	40
367	MAHAD TO RAIGAD FORT	MoRTH	07/2018	05/2020	12/2022	237.4	31

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
368	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	MoRTH	03/2015	01/2016	09/2022	159.12	80
369	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	NHIDCL	03/2019	05/2019	09/2022	306.28	40
370	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	MoRTH	01/2017	03/2019	10/2022	247.25	43
371	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	MoRTH	03/2018	08/2020	12/2022	293.1	28
372	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	12/2022	1069.59	38
373	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	12/2022	170.57	25
374	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	MoRTH	12/2016	08/2018	11/2022	223.5	51
375	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	MoRTH	12/2016	04/2018	11/2022	206.88	55
376	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	MoRTH	03/2018	08/2018	11/2022	214.23	51
377	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	MoRTH	03/2018	08/2018	10/2022	199.16	50
378	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	10/2022	166.21	50
379	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	MoRTH	03/2016	11/2018	03/2023	271.17	52
380	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	05/2023	169.63	62
381	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	MoRTH	01/2017	09/2019	12/2022	396.86	39
382	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	03/2023	426.18	30
383	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	11/2022	184.62	57
384	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	MoRTH	03/2018	10/2020	03/2023	254.3	29
385	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	03/2023	160.27	43
386	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	03/2023	236.78	43
387	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN	NHAI	03/2021	11/2021	11/2023	1100.88	24
388	4L OF ADDAHOLE TO BANTWAL CROSS SECTION	NHAI	03/2021	10/2021	09/2023	317.9	23
389	MARAM - PEREN PKG-3	NHIDCL	08/2021	05/2023	11/2023	467.41	6
390	6-LANING OF VIJAYAWADA BYPASS FROM	NHAI	11/2019	02/2021	07/2024	1601.1	41

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)						
391	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	NHAI	11/2019	07/2021	07/2023	716	24
392	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	03/2023	671.3	121
393	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	09/2022	1100.7	99
394	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM)	NHAI	04/2012	04/2014	03/2023	624	107
395	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	10/2022	1348.2	104
396	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	09/2022	1724.55	114
397	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	12/2022	1175	116
398	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	05/2024	1250	125
399	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105
400	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	12/2022	574	105
401	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	06/2023	998.79	118
402	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	02/2023	1047	104
403	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	09/2022	822.9	53
404	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	09/2022	2128.72	41
405	4-LANING OF SOLAPUR - MAHARASHTRA/KARNATAKA SECTION	NHAI	06/2014	11/2016	12/2022	923.04	73
406	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2022	1655.01	76
407	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	NHAI	11/2019	02/2021	02/2023	1226.88	24
408	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	12/2022	946	54
409	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	11/2022	375.09	103
410	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	05/2023	563.92	65
411	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	12/2022	531.13	55
412	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	12/2022	649.5	45

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
413	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	01/2023	1083	55
414	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2023	2168.66	54
415	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	12/2022	934.46	57
416	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	NHAI	12/2015	04/2019	12/2022	1041.1	44
417	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	12/2022	2136.97	48
418	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	12/2022	815.28	54
419	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	08/2022	596.67	51
420	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	09/2022	667	50
421	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	12/2022	667	54
422	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	09/2022	1587.49	41
423	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2023	701.4	48
424	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	07/2023	546	48
425	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	10/2023	591.66	51
426	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MoRTH	02/2016	05/2016	11/2022	178.85	78
427	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MoRTH	02/2016	05/2016	11/2022	553.3	78
428	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MoRTH	01/2014	10/2016	03/2023	1408.85	77
429	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ	NHAI	05/2015	05/2017	09/2024	581.84	88
430	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	NHAI	08/2016	04/2020	08/2022	1664.2	28
431	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	06/2023	1167.42	51
432	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	06/2023	2510.04	46
433	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	12/2022	446.17	45
434	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	MoRTH	08/2013	06/2016	09/2022	171.96	75
435	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM	NHAI	03/2017	03/2020	12/2022	848.45	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.						
436	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	08/2022	1373.28	29
437	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	09/2022	1184.71	30
438	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	NHAI	03/2017	03/2020	11/2022	247.02	32
439	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	07/2024	744.64	52
440	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	03/2023	754.54	36
441	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	03/2023	672.89	36
442	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	12/2022	284.09	68
443	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	NHIDCL	02/2017	04/2017	11/2022	195.23	67
444	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	NHIDCL	02/2017	04/2017	10/2022	203.36	66
445	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	11/2023	180.57	79
446	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	NHIDCL	01/2017	04/2017	08/2022	198.22	64
447	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	12/2022	894	32
448	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	06/2023	2485.93	36
449	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	NHIDCL	03/2018	05/2018	12/2022	274.31	55
450	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	NHIDCL	03/2018	06/2018	12/2022	403.36	54
451	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	NHIDCL	03/2018	05/2018	12/2022	417.24	55
452	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	NHIDCL	03/2015	10/2018	03/2023	262.97	53
453	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	NHIDCL	02/2018	10/2018	12/2022	391	50
454	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
455	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
456	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2022	215.79	51
457	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	06/2023	272.89	57
458	CONSTRUCTION OF 2-LANE WITH PAVED	NHIDCL	11/2017	11/2017	09/2022	290.05	58

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5						
459	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MORTH	06/2017	06/2019	10/2022	282.08	40
460	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	08/2023	950.64	72
461	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	10/2022	476.56	63
462	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	03/2023	1124.11	66
463	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	03/2023	463.49	57
464	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	NHIDCL	03/2015	11/2018	08/2022	168.39	45
465	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	09/2022	588.95	46
466	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	MORTH	10/2014	02/2017	12/2022	295.47	70
467	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	10/2022	165.67	83
468	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	NHIDCL	12/2015	12/2018	12/2022	289.99	48
469	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MORTH	11/2015	01/2020	09/2022	628.45	32
470	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MORTH	12/2015	02/2020	09/2022	957.54	31
471	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MORTH	03/2015	08/2017	12/2022	511.83	64
472	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	12/2022	252	83
473	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	MORTH	12/2017	11/2018	09/2022	867.97	46
474	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	MORTH	08/2017	03/2018	12/2022	962.43	57
475	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	NHIDCL	08/2020	04/2022	01/2023	301.06	9
476	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	NHIDCL	09/2020	05/2022	01/2023	353.9	8
477	2-LANING FROM MANU-SIMLUNG (PKG I)	NHIDCL	03/2020	01/2022	10/2022	247.76	9
478	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	NHIDCL	08/2020	04/2022	04/2023	208.84	12
479	2-LANING FROM MANU-SIMLUNG (PKG III)	NHIDCL	06/2020	01/2022	08/2022	347.36	7
480	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	NHIDCL	08/2020	03/2022	11/2022	278.46	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
481	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	NHIDCL	03/2019	04/2022	05/2023	402.94	13
482	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	NHIDCL	03/2020	06/2022	12/2022	242.97	6
483	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	NHIDCL	09/2020	10/2022	12/2023	277.44	14
484	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	NHIDCL	08/2020	04/2022	06/2023	202.36	14
485	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	NHIDCL	09/2020	04/2022	03/2023	315.63	11
486	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	NHIDCL	07/2020	04/2022	12/2022	228.39	8
487	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	NHIDCL	07/2020	04/2022	12/2022	210.79	8
488	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	NHIDCL	03/2020	07/2022	03/2023	178.43	8
489	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	NHIDCL	03/2019	07/2022	03/2023	471	8
490	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	NHIDCL	03/2020	03/2022	12/2022	216.49	9
491	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	NHIDCL	03/2020	06/2022	12/2022	292.24	6
492	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	NHIDCL	03/2020	06/2022	12/2022	167.95	6
493	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	NHIDCL	08/2020	04/2022	02/2023	379.39	10
494	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	NHAI	10/2013	12/2020	12/2022	649.9	24
495	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	NHAI	10/2013	11/2020	11/2022	446.97	24
496	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	NHAI	10/2013	11/2020	11/2022	464.09	24
497	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	NHAI	10/2020	03/2023	01/2024	724.6	10
498	KAILASHAHAR TO KHOWAI PKG-4	NHIDCL	11/2020	06/2022	12/2022	159.13	6
499	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	NHIDCL	03/2020	06/2022	12/2022	167.95	6
500	LADDA - BASAI	NHIDCL	02/2021	04/2023	02/2024	445.96	10
501	2-LANING FROM JOLAIBARI - BELONIA	NHIDCL	06/2020	01/2022	12/2022	201.99	11
502	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	NHIDCL	09/2020	04/2022	10/2022	173.17	6
503	DOGINALA - GAU	NHIDCL	12/2020	09/2022	04/2023	242.3	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
504	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	NHIDCL	09/2020	05/2022	12/2022	183.31	7
505	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	NHIDCL	09/2020	05/2023	01/2024	262.84	8
506	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	NHIDCL	08/2020	05/2022	12/2022	292.8	7
507	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	NHIDCL	03/2020	07/2022	01/2023	165.54	6
508	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	NHIDCL	03/2020	06/2022	03/2023	261.13	9
509	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	NHIDCL	10/2020	11/2023	05/2024	493.42	6
510	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	NHIDCL	10/2020	12/2023	11/2024	816.79	11
511	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	NHIDCL	10/2020	04/2022	04/2023	157.86	12
512	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	NHAI	10/2019	02/2020	08/2023	1101.99	42
513	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	NHAI	02/2019	11/2019	12/2022	731.89	37
514	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	NHAI	02/2019	11/2019	12/2022	362.46	37
515	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	NHAI	02/2019	11/2019	12/2022	594.75	37
516	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	MORTH	06/2020	05/2021	12/2022	221.4	19
517	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	MORTH	08/2020	03/2021	03/2023	222.61	24
518	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT	MORTH	01/2017	09/2017	12/2022	264.34	63
519	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	MORTH	03/2019	12/2019	12/2023	423.15	48
520	CHANGTONGYA TO LONGLENG ROAD PKG-2	NHIDCL	03/2020	06/2022	12/2022	206.53	6
521	JORAM - KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	NHIDCL	08/2020	04/2022	12/2022	294.04	8
522	JORAM - KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	NHIDCL	08/2020	04/2022	12/2022	199.03	8
523	JORAM - KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	NHIDCL	08/2020	04/2022	12/2022	184.88	8
524	IMPHAL - KHONGSANG PKG-3	NHIDCL	07/2021	03/2023	09/2023	467	6
525	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT	MORTH	04/2021	03/2022	09/2023	309.48	18
526	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON	MORTH	03/2021	03/2022	09/2023	185.09	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NH-24A INCLUDING RETAINING W						
527	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	MoRTH	02/2018	02/2020	10/2022	418.88	32
528	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	MoRTH	05/2018	05/2020	10/2022	248	29
529	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	08/2022	1532.62	17
530	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	MoRTH	11/2017	11/2019	10/2022	237.8	35
531	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	NHIDCL	03/2015	01/2016	06/2023	829	89
532	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	NHIDCL	03/2018	07/2018	03/2024	1383.78	68
533	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
534	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	07/2023	640.07	46
535	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
536	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
537	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
538	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
539	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
540	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	09/2023	428.11	48
541	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	NHIDCL	03/2018	07/2019	12/2022	253.44	41
542	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	10/2022	162.56	55
543	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	11/2022	205.05	68
544	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	12/2022	214.69	57
545	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	10/2022	217.22	50
546	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	10/2022	233.04	55
547	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	10/2022	249.05	51
548	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	10/2022	254.17	56

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
549	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	09/2022	809.16	50
550	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	09/2022	877.79	39
551	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MoRTH	11/2016	05/2017	08/2022	290.15	63
552	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MoRTH	01/2017	08/2017	08/2022	319.28	60
553	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MoRTH	03/2018	08/2018	08/2022	289.67	48
554	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 0	MoRTH	03/2016	05/2016	11/2022	995.09	78
555	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	MoRTH	03/2018	08/2020	10/2022	293.64	26
556	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MoRTH	08/2016	01/2017	12/2022	350.61	71
557	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	12/2022	263.45	63
558	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MoRTH	01/2017	01/2018	12/2022	576.48	59
559	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	MoRTH	02/2017	05/2019	05/2023	157.32	48
560	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	MoRTH	03/2017	11/2020	09/2022	217.35	22
561	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	MoRTH	01/2019	03/2021	12/2022	264.5	21
562	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MoRTH	03/2018	04/2020	08/2022	263.89	28
563	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	MoRTH	03/2018	08/2020	10/2022	288.3	26
564	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON	NHAI	03/2018	11/2021	11/2023	998.7	24

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
565	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	09/2022	262.87	39
566	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2023	1034.01	74
567	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	03/2023	15525	94
568	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	NMDC	11/2015	06/2023	07/2024	2907	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
569	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD FOR TELECOM	10/2014	03/2018	11/2022	248.2	56
570	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	BSNL	03/2020	06/2021	11/2022	431.16	17

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
571	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	CPWD	05/2019	09/2020	11/2023	299.97	38
572	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	06/2024	1180	35
573	KANPUR METRO RAIL PROJECT	LMRCL	05/2019	03/2024	11/2024	11076.48	8
574	AGRA METRO RAIL PROJECT	LMRCL	05/2019	03/2024	12/2025	8379.62	21
575	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2021	03/2025	26405.14	49
576	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	12/2023	23136	45
577	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	03/2023	11420	16
578	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	09/2022	10773	45
579	BHOPAL METRO RAIL	MPMRCL	11/2018	02/2023	05/2025	6941.4	27
580	INDORE METRO RAIL	MPMRCL	11/2018	02/2023	07/2025	7500.8	29
581	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	CPWD	10/2016	03/2022	06/2024	1128	27
582	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	DMRC	07/2019	03/2025	09/2025	24948.65	6

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
583	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	BUIDCO	08/2017	06/2022	12/2022	824	6
584	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	BUIDCO	08/2017	06/2022	12/2022	578.89	6
585	INTERCEPTION AND DIVERSION WITH STP AT BALLY	KMDA	10/2017	12/2021	09/2023	164.93	21
586	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	KMDA	01/2018	12/2021	09/2023	172.1	21
587	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	KMDA	08/2017	12/2021	09/2023	185.22	21
588	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	BUIDCO	03/2017	05/2021	10/2022	277.42	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
589	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	03/2024	10151.04	48
590	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	KMDA	05/2018	02/2022	03/2024	160	25
591	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	BUIDCO	05/2017	04/2021	09/2022	356.37	17
592	SEWER NETWORKS, SPS AND STP, MUNGER	BUIDCO	03/2018	10/2021	12/2023	294.02	26
593	SEWER NETWORKS SPS AND STP HAJIPUR	BUIDCO	03/2018	08/2021	08/2023	305.19	24
594	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	KMDA	08/2017	09/2022	12/2024	307.12	27
595	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	KMDA	03/2018	06/2022	03/2024	165.16	21
596	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	KMDA	05/2018	02/2022	03/2024	198.43	25
597	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	KMDA	12/2018	04/2022	12/2024	234.31	32
598	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR	KMDA	03/2019	04/2022	12/2024	287.53	32
599	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	KMDA	01/2019	04/2022	12/2024	384.96	32
600	I AND D AND STP AT CHAPPRA	BUIDCO	11/2018	12/2020	10/2022	236.15	22
601	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	42
602	SEWER NETWORK SPS AND STP BEGUSARAI	BUIDCO	03/2018	07/2021	03/2023	230.06	20
603	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	04/2024	298.12	33
604	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	UPJalNigam	02/2019	06/2022	04/2024	681.78	22
605	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	UPJalNigam	01/2019	10/2021	08/2022	206.05	10
606	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	UPJalNigam	01/2019	12/2021	06/2023	231.79	18
607	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
608	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12
609	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	UPJalNigam	03/2019	08/2021	03/2024	271.39	31
610	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	UPJalNigam	03/2018	09/2021	09/2022	967.23	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
611	FARRUKHABAD I AND D AND STP WORKS HAM	UPJaNigam	10/2017	03/2022	04/2024	213.62	25
612	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	UPJaNigam	05/2017	09/2021	12/2022	767.59	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(AUGUST 2022)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	7500	4008
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	19220	7761
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	417.23	707.73	290.5
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	1383	2445	1062

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	479.53	868.37	388.84
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	414.11	586.5	172.39
12	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	1351	1471.04	120.04

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
13	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MH	10/2013	10/2019	1219.21	1679.02	459.81

MINES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	4103	5055	952

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	355	581	226
16	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	534	667.23	133.23
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
17	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	1236	628.94
18	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
19	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3185	508
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
21	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	1933	2105.7	172.7
22	ENNORE THIRUVALUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
23	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	02/2022	1945	2145	200
24	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
25	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
26	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
27	DEVANGONTHI MARKETING TERMINAL	MANGALORE RE	06/2020	06/2023	200	304	104
28	NUMALIGARH REFINERY EXPANSION PROJECT 6 MTPA REFINARY	NRL	01/2019	10/2024	12366	18968	6602
29	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
30	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	598	753.89	155.89
31	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MTPA TO 2.5 MTPA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
32	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	206.63	340.76	134.13
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	2001.34	1139.55
34	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
35	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
36	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
37	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	10463.03	6543.44
38	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	7103	4124.52
39	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
40	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	17007	2640.42
41	BIKANER SOLAR POWER PROJECT	SJVN	04/2022	05/2024	5491.89	6023.89	532
42	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT	PGCIL	10/2019	08/2021	1031	1143	112
43	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	529.68	679	149.32
44	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	947.89	299.56
45	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	1931.39	2635.55	704.16
46	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	3500	3994	494
47	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
48	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
49	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10998	399.02
50	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
51	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4825.6	3168.6
52	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
53	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1803	421.16
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
54	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3800	2766.93
55	KOTLIPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
56	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
57	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
58	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	433	299.59
60	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
61	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	3081.2	2356.51
62	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	3500.79	2917.96
63	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	6527.45	4133.98
64	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
65	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	1160.48	2250	1089.52
66	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4834.54	1921.03
67	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	6383.82	2880.13
68	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	3168.29	3445.48	277.19
69	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	450	2017.96	1567.96
70	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
71	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	7876.92	6537.44
72	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6663	4336.48
73	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2650	2117.13
74	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1145.79	760.59
75	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTTP	04/2006	06/2013	495.74	774.51	278.77
76	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	14322.79	9868.62
77	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
78	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	1010	331.46

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
79	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1878	263.41
80	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
81	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
82	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1954.21	797.27
83	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
84	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3633.12	2129.41
85	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	2448.99	1619.25
86	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	318.24	1083.17	764.93
87	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	2315	5174.3	2859.3
88	MUNEERABAD-MAHABOONNAGAR(NL),SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
89	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
91	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	2500	37012.26	34512.26
92	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	401.65	160.13
93	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
94	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	8324.28	7417.82
95	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	591	426.59
96	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	708.73	139.1
97	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2047.51	249.51
98	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	783.83	235.83
99	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1700	1327.86
100	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
101	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	402.48	114.13
102	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
103	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	120.7	2084.48	1963.78
104	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
105	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	983.55	568.71
106	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
107	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1394.02	356.87
108	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	2538.01	989.35
109	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	1640.04	1873.1	233.06
110	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	1347.26	1524.68	177.42
111	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
112	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	800	505
113	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
114	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
115	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
116	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
117	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
118	PUNE-MIRAJ-LONDA (467 KM)	CR	02/2015	03/2024	3627.47	4670	1042.53
119	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	1272.19	1384.72	112.53
120	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	1763.93	2445.3	681.37
121	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	1295.42	2000	704.58
122	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	51219	39630
123	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	390.39	511.75	121.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
124	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	3055	3500	445
125	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
126	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	826.18	181.4
127	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
128	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
129	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1510	1180.61
130	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
131	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
132	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	800	197.5
133	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
134	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
135	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	150	341.66	191.66
136	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	760	1536	776
137	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	WR	03/2012	N.A.	248.26	528.49	280.23
138	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	WR	03/2012	N.A.	217.38	393.62	176.24
139	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	242.28	122.55
140	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3176.6	1268.09
141	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
142	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	2478.23	2938	459.77
143	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
144	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	2203.53	1020.28
145	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1552.26	609.31
146	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
147	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
148	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2725	2011.52
149	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	24659	8443
150	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1457.79	530.78
151	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	943.6	1500	556.4
152	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1339	339
153	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.97	343.14
154	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	MITES	03/2015	03/2021	636.38	998.06	361.68
155	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	1002.39	1119.12	116.73
156	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	4059.65	1827.33
157	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
158	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1110	785.27
159	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
160	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTF	03/1996	03/2004	495.44	2980.41	2484.97
161	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4805.17	2533.67
162	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1387.52	594.63
163	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
164	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	2000.97	199.96
165	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	986.3	1530.09	543.79
166	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
167	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
168	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
169	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2404.03	341.73

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
170	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
171	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3300	1173
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
172	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	454.89	814.56	359.67
173	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	596.67	819.35	222.68
174	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	NHAI	01/2016	06/2018	1027.53	2628.31	1600.78
175	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	815.28	2323.88	1508.6
176	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	934.46	1543.51	609.05
177	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1414.01	331.01
178	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	1655.01	2639	983.99
179	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	2128.72	2408.72	280
180	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	593.26	717.24	123.98
181	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	777.03	245.9
182	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
183	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	NHAI	03/2018	N.A.	478.74	1135.08	656.34
184	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	NHAI	03/2018	N.A.	795.5	922.64	127.14
185	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	925.96	291.26
186	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
187	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	NHAI	03/2018	N.A.	1016.92	1308.88	291.96
188	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	NHAI	03/2018	N.A.	633.55	736.33	102.78
189	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	NHIDCL	03/2015	01/2016	829	1307.5	478.5
190	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1309.79	185.68
191	PREPATION OF FEASIBILITY/DPR OF	NHAI	07/2020	12/2021	3426	5852	2426

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA						
192	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	624.98	731.5	106.52
193	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
194	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
195	ISMAILABAD-NARNAUL PKG-1	NHAI	01/2019	N.A.	996.65	1173.65	177
196	ISMAILABAD-NARNAUL PKG-2	NHAI	01/2019	N.A.	1243.45	1407.35	163.9
197	ISMAILABAD-NARNAUL PKG-7	NHAI	01/2019	N.A.	1137.42	1238.29	100.87
198	SIX LANEING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	NHAI	11/2017	01/2019	2159	2262	103
199	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	186.96	322.24	135.28
200	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MoRTH	01/2017	01/2018	576.48	686.13	109.65
201	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	964.17	1198.64	234.47
202	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	950.64	1168.33	217.69
203	RHENOK-RORATHANG-PAKYONG ON NH 717A	NHIDCL	04/2017	10/2017	388	530.67	142.67
204	SIX LANEING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
205	SIX LANEING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
206	REHABILITATION AND UPGRADATION BY 4-LANEING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
207	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
208	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	672.89	830.31	157.42
209	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	16732.7	15702.74
210	FOUR LANEING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	1827	294.38
211	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	NHAI	02/2018	N.A.	972.77	1441	468.23
212	SIX LANEING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1361	308.79
213	4-LANEING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
214	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	NHAI	03/2018	N.A.	809.07	1065.7	256.63
215	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	2145.96	883.98
216	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
217	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
218	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	NHAI	02/2018	N.A.	1166.26	1422.13	255.87
219	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1862.77	438
220	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	NHAI	01/2018	N.A.	573.7	726.99	153.29
221	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
222	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
223	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	N.A.	1251.11	1361	109.89
224	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	1023.23	417.39
225	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
226	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
227	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	1588.29	199.95
228	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	899	1376.86	477.86
229	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	3063.99	1476.5
230	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
231	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
232	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
233	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
234	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	726.67	1096.52	369.85
235	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	667	3006.53	2339.53
236	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	667	2328.27	1661.27

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
237	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MORTH	01/2014	10/2016	1408.85	2138.16	729.31
238	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	NHAI	03/2016	N.A.	1737	2421.37	684.37
239	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	NHAI	03/2016	N.A.	1443	2330.79	887.79
240	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
241	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	268.08	390.73	122.65
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	MORTH	01/1991	N.A.	675	780.77	105.77
243	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	478.51	1082.4	603.89
244	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
245	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
246	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	1250	1380.73	130.73
247	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	946	1046.56	100.56
248	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
249	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
250	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
251	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	463.49	801.54	338.05
252	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	588.95	873.91	284.96

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
253	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
254	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
255	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	18380	3780
256	PATNA METRO RAIL CORPORATION LIMITED	PATNA METRO	02/2019	06/2024	13365.77	13925.5	559.73

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
257	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12925.22	2152.22
258	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	38585	40180.91	1595.91
259	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	8680	9759.79	1079.79
260	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	23136	33406	10270

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
261	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83
262	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	254.13	413.29	159.16
263	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	225.77	398.9	173.13
264	SAIDPUR SEWER NETWORK PATNA	BUIDCO	04/2015	01/2021	268.63	431.21	162.58

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	1,2320.00	1,7079.00	4759	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2023	1,1459.00	1,9220.00	7761	90
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2024	3492.00	7500.00	4008	168

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2023	346.27	480.33	134.06	27
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	10/2022	417.23	707.73	290.5	49
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	09/2023	1383.00	2445.00	1062	24

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5146.48	2484.75	60
8	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	868.37	388.84	132

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	01/2023	4773.00	5178.00	405	37

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	08/2022	1351.00	1471.04	120.04	11

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
11	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT	CPWD FOR MHA	10/2013	10/2019	12/2022	1219.21	1679.02	459.81	38

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	NEW DELHI								

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	11/2023	534.00	667.23	133.23	46
13	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	12/2023	355.00	581.00	226	37
14	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	01/2024	4103.00	5055.00	952	33

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFIN	06/2020	06/2023	01/2024	200.00	304.00	104	7
16	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677.00	3185.00	508	14
17	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	11/2023	4497.00	6025.00	1528	59
18	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2023	3190.69	3375.90	185.21	61
19	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2025	2915.00	5909.00	2994	146
20	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	12/2022	607.06	1236.00	628.94	62
21	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	10/2022	1823.00	3027.90	1204.9	19
22	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	12/2022	2321.00	3338.00	1017	24
23	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2022	861.79	2001.34	1139.55	115
24	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	09/2022	678.00	1472.00	794	67
25	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	03/2023	2,0928.00	2,6264.00	5336	32

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
26	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	05/2016	02/2022	12/2022	1945.00	2145.00	200	10
27	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	11/2022	1933.00	2105.70	172.7	23
28	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2023	1112.00	1507.24	395.24	44
29	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14
30	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	12/2022	598.00	753.89	155.89	34
31	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	02/2023	206.63	340.76	134.13	36

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
32	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT	PGCIL	10/2019	08/2021	10/2022	1031.00	1143.00	112	14
33	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	12/2022	529.68	679.00	149.32	49
34	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	08/2022	3500.00	3994.00	494	25
35	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	04/2023	1931.39	2635.55	704.16	38
36	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2023	3919.59	1,0463.03	6543.44	171
37	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
38	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	12/2024	1,4366.58	1,7007.00	2640.42	66
39	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	07/2025	1381.84	1803.00	421.16	70
40	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	03/2025	2491.58	3860.35	1368.77	141
41	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	10/2023	1657.00	4825.60	3168.6	92

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
42	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	03/2024	8692.97	2,1312.11	12619.1	149
43	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	06/2023	1,0598.98	1,0998.00	399.02	31
44	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	9129.32	4374.9	63
45	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	01/2024	5111.33	6700.00	1588.67	61
46	NAITWAR MORI HEP	SJVN	10/2017	12/2021	12/2022	648.33	947.89	299.56	12
47	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2024	2978.48	7103.00	4124.52	141

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
48	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	01/2023	390.39	511.75	121.36	13
49	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2023	3055.00	3500.00	445	63
50	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33
51	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2026	644.78	826.18	181.4	108
52	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2024	2288.00	4970.11	2682.11	33
53	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
54	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	12/2024	744.04	1215.54	471.5	45
55	CHANDIGARH-BADDI	NR	04/2007	03/2023	12/2025	328.14	1540.13	1211.99	33
56	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2024	1763.93	2445.30	681.37	55
57	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2024	1272.19	1384.72	112.53	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
58	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	03/2025	1876.00	2081.27	205.27	24
59	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2025	3631.00	3887.48	256.48	36
60	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2025	701.61	810.02	108.41	76
61	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2025	2232.32	4059.65	1827.33	36
62	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	1119.12	116.73	21
63	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	10/2022	969.83	1312.97	343.14	31
64	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2022	943.60	1500.00	556.4	9
65	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2023	927.01	1457.79	530.78	48
66	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
67	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	09/2022	948.04	2009.00	1060.96	30
68	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2023	942.95	1552.26	609.31	48
69	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	09/2022	1183.25	2203.53	1020.28	21
70	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	09/2022	1485.85	1835.83	349.98	21
71	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	6663.00	4336.48	132
72	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	7876.92	6537.44	96
73	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	11/2024	450.00	2017.96	1567.96	148
74	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	06/2023	2500.00	3,7012.26	34512.3	247
75	NEW WORK FOR CONSTRUCTION OF	RVNL	04/2010	03/2016	03/2026	3951.98	4259.48	307.5	120

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)								
76	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
77	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
78	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2024	318.24	1083.17	764.93	144
79	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	2448.99	1619.25	48
80	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	3081.20	2356.51	73
81	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	6527.45	4133.98	117
82	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2025	1160.48	2250.00	1089.52	180
83	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	07/2025	2913.51	4834.54	1921.03	112
84	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2026	3503.69	6383.82	2880.13	48
85	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	03/2024	3168.29	3445.48	277.19	12
86	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2025	792.89	1387.52	594.63	48
87	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.30	1530.09	543.79	129
88	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2025	2271.50	4805.17	2533.67	48
89	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2027	1045.20	2120.16	1074.96	216
90	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
91	RAMGANJMONDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2024	424.60	2909.99	2485.39	36
92	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	09/2022	1202.70	2440.53	1237.83	91

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
93	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2022	133.41	433.00	299.59	165
94	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
95	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2023	495.44	2980.41	2484.97	228
96	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
97	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	06/2023	324.73	1110.00	785.27	135
98	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2025	2923.13	3791.66	868.53	201
99	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,4322.79	9868.62	153
100	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTP	04/2006	06/2013	12/2022	495.74	774.51	278.77	114
101	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2024	385.20	1145.79	760.59	60
102	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	12/2023	532.87	2650.00	2117.13	57
103	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	12/2022	1156.94	1954.21	797.27	33
104	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600.00	701.81	101.81	31
105	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	02/2024	1614.59	1878.00	263.41	59
106	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	12/2024	1347.26	1524.68	177.42	33
107	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2025	1640.04	1873.10	233.06	36
108	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	12/2022	1548.66	2538.01	989.35	12
109	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	1394.02	356.87	21

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
110	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
111	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2025	548.00	783.83	235.83	60
112	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798.00	2047.51	249.51	57
113	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2022	569.63	708.73	139.1	30
114	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	03/2024	242.22	471.00	228.78	48
115	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	10/2024	414.84	983.55	568.71	55
116	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	09/2022	632.68	950.00	317.32	78
117	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2084.48	1963.78	105
118	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2023	915.98	2137.81	1221.83	12
119	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2024	2478.23	2938.00	459.77	24
120	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2024	582.13	1247.64	665.51	30
121	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3176.60	1268.09	9
122	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	12/2022	760.00	1536.00	776	33
123	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150.00	341.66	191.66	66
124	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	1185.73	454.09	36

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
125	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO	MORTH	01/2016	10/2016	12/2022	624.98	731.50	106.52	74

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	PATHALGAON SECTION								
126	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	NHIDCL	03/2015	01/2016	06/2023	829.00	1307.50	478.5	89
127	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	08/2023	950.64	1168.33	217.69	72
128	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	12/2022	946.00	1046.56	100.56	54
129	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	12/2022	531.13	777.03	245.9	55
130	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	01/2023	1083.00	1414.01	331.01	55
131	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	12/2022	934.46	1543.51	609.05	57
132	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	12/2022	815.28	2323.88	1508.6	54
133	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	08/2022	596.67	819.35	222.68	51
134	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	09/2022	667.00	2328.27	1661.27	50
135	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	12/2022	667.00	3006.53	2339.53	54
136	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	09/2022	1587.49	3063.99	1476.5	41
137	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MORTH	01/2014	10/2016	03/2023	1408.85	2138.16	729.31	77
138	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	03/2023	1124.11	1309.79	185.68	66
139	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	03/2023	463.49	801.54	338.05	57
140	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	09/2022	588.95	873.91	284.96	46
141	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	05/2024	1250.00	1380.73	130.73	125
142	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
143	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	09/2022	2128.72	2408.72	280	41
144	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2022	1655.01	2639.00	983.99	76
145	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	07/2024	744.64	982.00	237.36	52
146	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	09/2022	1184.71	1310.00	125.29	30
147	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	03/2023	672.89	830.31	157.42	36
148	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MoRTH	01/2017	01/2018	12/2022	576.48	686.13	109.65	59
149	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	08/2022	1532.62	1827.00	294.38	17

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
150	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	03/2023	1,5525.00	2,1940.00	6415	94

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
151	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	09/2022	1,0773.00	1,2925.22	2152.22	45
152	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	12/2023	2,3136.00	3,3406.00	10270	45

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
153	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	413.29	159.16	42
154	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	03/2024	1,0151.04	5,5548.87	45397.8	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(August 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>POWER</u>							
	<u>Power Grid Corporation Of India Limited</u>							
1	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION. - PPP (BOT) - [N18000329]	03/2022	176.22 -	176.22	03/2023 -	03/2023	.00	0
2	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM - PPP (BOT) - [N18000330]	03/2022	288.71 -	288.71	12/2024 -	12/2024	.00	0
3	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM - PPP (BOT) - [N18000328]	02/2022	318.12 -	318.12	04/2025 -	04/2025	.00	0
4	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - PPP (BOT) - [N18000331]	02/2022	359.47 -	359.47	09/2023 -	09/2023	.00	0
5	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD - PPP (BOT) - [N18000314]	01/2020	562.86 -	562.86	01/2021 -	12/2022	.00	23
6	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C - PPP (BOT) - [N18000327]	03/2019	1,326.00 -	1,326.00	03/2023 -	03/2023	.00	0
	Total		3,031.38 -	3,031.38				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
7	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	166.90	05/2013 -	05/2022	-55.37	108
8	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	469.31	01/2014 -	12/2019	61.08	71
9	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
10	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	07/2022	.00	107
11	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2020	.00	118
12	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
13	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	526.09	04/2014 -	03/2023	-15.69	107

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(August 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
14	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07	530.07	08/2016	05/2022	.00	69
15	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00	571.00	10/2013	-	.00	0
16	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00	574.00	03/2014	12/2022	.00	105
17	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00	575.00	07/2013	-	.00	0
18	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54	591.00	11/2013	05/2022	15.53	102
19	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00	617.00	08/2012	03/2022	.00	115
20	PATNA-MUZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	03/2023	.00	121
21	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16	702.16	07/2014	-	.00	0
22	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - PPP BOT (Hybrid Annuity) - [N24001340]	11/2019	716.00	716.00	07/2021	07/2023	.00	24
23	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	09/2022	.00	53
24	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	12/2022	.00	73
25	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	07/2013	.00	0
26	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	10/2019	.00	27
27	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	06/2023	.00	118
28	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	02/2023	.00	104
29	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	03/2022	.00	103
30	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	09/2022	.00	99
31	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	08/2013	.00	0
32	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	12/2022	.00	116
33	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88	1,321.60	02/2021	02/2023	7.72	24

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(August 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
34	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	10/2022	.00	104
35	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,380.73	12/2013	05/2024	10.46	125
36	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	06/2022	.00	46
37	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	08/2021	.00	83
38	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	06/2022	.00	93
39	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	05/2022	.00	96
40	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	01/2016	.00	4
41	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10	1,601.10	02/2021	07/2024	.00	41
42	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	06/2022	.00	128
43	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	09/2022	.00	114
44	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
45	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	05/2022	.00	85
46	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	05/2022	.00	82
47	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	11/2018	.00	35
48	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,262.00	01/2019	01/2019	4.77	0
49	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	2,360.65	-	12/2023	41.78	0
50	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,408.72	04/2019	09/2022	13.15	41
51	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	2,639.00	08/2016	12/2022	59.46	76
52	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00	3,379.45	03/2014	12/2022	18.66	105
	Total		53,322.67	56,244.61				

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (August 2022)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Grand Total		56,354.05	59,275.99				

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2022)
					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 12/2021	12/2021
	Total		438.28 -		
	<u>COAL</u>				
	<u>Eastern Coal Fields Limited</u>				
2	HURA - C OC (3 MTY) - [N06000143]ECL, JHARKHAND	10/2015	359.69 -	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>				
3	ANANTA OCP EXPANSION PH III - [N06000225]MCL, ODISHA	08/2008	228.08 -	03/2012 -	-
4	SUBHADRA OCP - [N06000249]MCL, ODISHA	05/2021	1,693.81 -	03/2027 03/2029	-
	<u>Neyveli Lignite Corporation</u>				
5	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	12/2015 -	02/2021
6	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
8	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
9	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
	<u>South-Eastern Coal Fields Limited</u>				
10	BATURA HIGHWALL PROJECT - [N06000134]SECL, MADHYA PRADESH	07/2015	231.92 -	03/2022 -	03/2022
11	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL, CHHATISGARH	07/2016	459.49 -	03/2020 -	03/2022
	<u>Western Coal Fields Limited</u>				
12	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	03/2022
13	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL, MULTI STATE	08/2016	319.76 319.76	03/2022 -	03/2022
	Total		14,840.40 -		
	<u>FINANCE</u>				

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Cpwd For Finance</u>				
14	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU	11/2017	348.77 -	11/2021 -	-
	<u>National Projects Construction Corporation Limited</u>				
15	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA - [N07000001]NPCC,DELHI	07/2018	228.50 220.27	04/2022 -	04/2022
	Total		577.27 -		
	<u>PETROLEUM</u>				
	<u>Hindustan Petroleum Corporation Limited</u>				
16	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	07/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
17	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	Total		907.26 -		
	<u>POWER</u>				
	<u>National Thermal Power Corporation</u>				
18	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
	<u>Power Grid Corporation Of India Limited</u>				
19	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	04/2022
20	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315]PGCIL,MULTI STATE	07/2020	239.89 -	06/2021 -	04/2022
	Total		2,289.18 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Cpwd For Health</u>				
21	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29 -	03/2020 -	03/2020
22	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	06/2021
23	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	-
24	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00 -	09/2020 -	-
	<u>Hll Infra Tech Services Limited</u>				

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
25	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-
26	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
27	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 890.14	05/2021 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
28	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
29	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
30	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	04/2020
31	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	01/2021
32	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
33	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	02/2021
34	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	04/2021
35	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	05/2021
36	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2021
37	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	06/2021
38	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021
39	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	12/2021
40	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	12/2021
41	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	12/2021
42	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	12/2021
43	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	01/2022
44	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	06/2022
45	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	07/2022
	Total		9,113.26 -		
	<u>RAILWAYS</u>				
	<u>Container Corporation Of India</u>				

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
46	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	03/2019
47	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
48	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
49	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
50	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	- -	07/2022
51	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	03/2019 -	07/2022
	<u>East Coast Railway</u>				
52	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	-
	<u>Eastern Railways</u>				
53	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- 09/2021	05/2022
	<u>Kolkata Metro Rail Corporation Limited</u>				
54	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
55	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
56	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
	<u>North East Frontier Railway</u>				
57	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
	<u>North Eastern Railway</u>				
58	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022
59	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022
60	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	-
61	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	-
62	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	-
	<u>North Western Railway</u>				
63	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	06/2022
	<u>Northern Railway</u>				

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
64	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	12/2011
	<u>National High Speed Rail Corporation Limited</u>				
65	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	-
	<u>Rail India Technical And Economic Service</u>				
66	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 998.06	03/2021 12/2022	-
	<u>Rail Vikas Nigam Ltd.</u>				
67	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	06/2022
68	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	07/2022
	<u>South Central Railway</u>				
69	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
70	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	-
	Total		1,61,524.20 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
71	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2014
72	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 - [N24000422]MoRTH,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	09/2015
73	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	06/2019
74	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	06/2019
75	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	07/2019
76	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 08/2019	08/2019
77	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 09/2019	09/2019
78	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	09/2019
79	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 10/2019	10/2019
80	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	11/2019

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
81	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	11/2019
82	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 12/2019	12/2019
83	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	12/2019
84	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	12/2019
85	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019
86	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- 02/2019	01/2020
87	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	01/2020
88	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	01/2020
89	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	02/2020
90	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	03/2020
91	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	03/2020
92	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 2,617.44	03/2020 -	03/2020
93	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 07/2020	07/2020
94	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	08/2020
95	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	09/2020
96	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	09/2020
97	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	09/2020
98	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	09/2020
99	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020
100	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 10/2020	10/2020
101	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	10/2020
102	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 1,428.09	03/2020 -	10/2020
103	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 11/2020	11/2020

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
104	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	11/2020
105	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	11/2020
106	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	11/2020
107	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	11/2020
108	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	11/2020
109	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	11/2020
110	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	11/2020
111	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2020
112	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	12/2020
113	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	12/2020
114	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	12/2020
115	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	12/2020
116	KUNDRA TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	12/2020
117	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	12/2020
118	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 01/2021	01/2021
119	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 01/2021	01/2021
120	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	01/2021
121	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	01/2021
122	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 01/2021	01/2021
123	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	03/2021
124	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	03/2021
125	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	03/2021
126	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	04/2021

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
127	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 04/2021	04/2021
128	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 04/2021	04/2021
129	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	06/2021
130	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 06/2021	06/2021
131	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	06/2021
132	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	06/2021
133	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	07/2021
134	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 07/2021	07/2021
135	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	07/2021
136	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	07/2021
137	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	07/2021
138	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	08/2021
139	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 09/2021	09/2021
140	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	09/2021
141	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	11/2021
142	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021
143	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	12/2021
144	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2021
145	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 12/2021	12/2021
146	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	12/2021
147	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 01/2022	01/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
148	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 386.99	08/2018 01/2022	01/2022
149	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 02/2022	02/2022
150	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	02/2022
151	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	02/2022
152	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	02/2022
153	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	02/2022
154	UPGRADATION OF ADHALGAON-JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH - [N24001448]MoRTH,MAHARASHTRA	11/2021	223.35 -	02/2022 -	02/2022
155	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 354.43	- 12/2021	03/2022
156	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	03/2022
157	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	03/2022
158	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 03/2022	03/2022
159	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- 03/2022	03/2022
160	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	03/2022
161	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	03/2022
162	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	03/2022
163	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	03/2022
164	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	03/2022
165	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	03/2022
166	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	03/2022
167	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	03/2022
168	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	03/2022
169	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	03/2022
170	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	03/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
171	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	03/2022
172	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	03/2022
173	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	03/2022
174	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	03/2022
175	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	03/2022
176	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	03/2022
177	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	03/2022
178	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	03/2022
179	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	03/2022
180	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	03/2022
181	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	03/2022
182	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	03/2022
183	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	03/2022
184	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	03/2022
185	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	03/2022
186	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	03/2022
187	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	03/2022
188	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	04/2022
189	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	04/2022
190	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	01/2021 -	04/2022
191	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	03/2021 04/2022	04/2022
192	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 06/2022	05/2022
193	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 394.44	05/2019 -	05/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
194	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 06/2022	06/2022
195	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 06/2022	06/2022
196	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 698.82	07/2016 06/2022	06/2022
197	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 11/2021	06/2022
198	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 06/2022	06/2022
199	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 06/2022	06/2022
200	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 06/2022	06/2022
201	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 06/2022	06/2022
202	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 06/2022	06/2022
203	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 06/2022	06/2022
204	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 06/2022	06/2022
205	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	06/2022
206	SHAHUPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	06/2022
207	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	06/2022
208	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	06/2022
209	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	06/2022
210	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	06/2022
211	KAJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	06/2022
212	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	06/2022
213	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	06/2022
214	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	06/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
215	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	06/2022
216	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	06/2022
217	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	06/2022
218	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	06/2022
219	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	06/2022
220	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	06/2022
221	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	06/2022
222	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	06/2022
223	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	06/2022
224	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	06/2022
225	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	06/2022
226	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	06/2022
227	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	06/2022
228	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	06/2022
229	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	06/2022
230	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	06/2022
231	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	06/2022
232	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	06/2022
233	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	06/2022
234	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 03/2021	06/2022
235	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 03/2021	06/2022
236	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 270.00	06/2021 -	06/2022
237	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	07/2022
238	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	07/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
239	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 07/2022	07/2022
240	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 07/2022	07/2022
241	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 07/2022	07/2022
242	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	07/2022
243	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 07/2021	07/2022
244	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 07/2022	07/2022
245	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 01/2021	07/2022
246	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	07/2022
247	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
248	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
249	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-
250	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-
251	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
252	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
253	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-
254	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
255	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
256	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
257	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
259	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
260	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
261	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
262	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
263	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 11/2022	-
264	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 11/2022	-
265	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
266	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
267	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
268	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
269	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
270	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	-
271	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	-
272	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	-
273	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 10/2022	-
274	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
275	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	01/2021 -	-
276	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 06/2022	-

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
277	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
278	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 212.74	06/2019 -	-
279	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-
280	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-
281	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
282	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 296.53	08/2017 03/2022	-
283	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 372.87	09/2017 01/2022	-
284	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
285	REHABILITATION AND UPGADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
286	REHABILITATION AND UPGADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
287	REHABILITATION AND UPGADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-
288	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	-
289	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
290	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-
291	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-
292	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	-
293	REHABILITATION AND UPGADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-
294	REHABILITATION AND UPGADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 - [N24001441]MoRTH,MEGHALAYA	08/2020	302.88 -	02/2022 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
295	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2016
296	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	04/2017
297	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	06/2018
298	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	09/2018
299	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	10/2018
300	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	12/2021
301	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	03/2022
302	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	03/2022
303	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND	09/2020	257.15 -	04/2022 -	04/2022
304	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	05/2022
305	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	05/2022
306	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 447.37	10/2017 06/2022	06/2022
307	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	06/2022
308	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	06/2022
309	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND	03/2020	320.97 -	06/2022 -	06/2022
310	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND	03/2020	355.79 -	06/2022 -	06/2022
311	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND	03/2020	361.53 -	06/2022 -	06/2022
312	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]NHIDCL,ASSAM	03/2020	217.50 -	06/2022 -	06/2022
313	4-LANING OF DERGAON TOWN - [N24001435]NHIDCL,ASSAM	03/2020	287.63 -	06/2022 -	06/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
314	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	07/2022
315	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	07/2022
316	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	07/2022
317	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]NHIDCL,TRIPURA	03/2020	154.51 -	07/2022 03/2023	07/2022
318	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM	03/2020	206.88 -	07/2022 -	07/2022
319	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM	03/2020	216.49 -	07/2022 -	07/2022
320	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM	03/2020	292.24 -	07/2022 -	07/2022
321	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM	03/2020	281.78 -	07/2022 -	07/2022
322	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]NHIDCL,TRIPURA	11/2020	206.78 -	07/2022 02/2023	07/2022
323	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	-
324	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	-
325	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
326	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
327	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
328	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
329	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
330	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
331	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
332	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA	06/2020	277.50 -	01/2022 -	-

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
333	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL,MANIPUR	08/2020	268.98 -	04/2022 -	-
334	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL,MANIPUR	08/2020	228.97 -	04/2022 -	-
335	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND	03/2020	330.78 -	12/2021 -	-
336	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND	04/2020	330.80 -	12/2021 -	-
	<u>National Highways Authority Of India</u>				
337	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	07/2013
338	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2013
339	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	01/2016
340	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 11/2018	11/2018
341	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 503.36	09/2016 -	11/2018
342	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 589.04	01/2016 -	01/2019
343	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 2,262.00	01/2019 -	01/2019
344	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	03/2019
345	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 839.00	05/2017 -	05/2019
346	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	05/2019
347	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2019
348	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019
349	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019
350	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	10/2019
351	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 480.31	01/2014 -	12/2019
352	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
353	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2020
354	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 414.00	05/2018 11/2020	11/2020

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
355	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	01/2021
356	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 416.00	- -	02/2021
357	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	03/2021
358	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	05/2021
359	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	08/2021
360	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	09/2021
361	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 2,047.39	06/2020 -	10/2021
362	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	10/2021
363	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	10/2021
364	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 1,103.55	04/2018 -	12/2021
365	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 2,421.37	- 12/2021	12/2021
366	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	12/2021
367	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	12/2021
368	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	02/2022
369	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	02/2022
370	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- 02/2022	02/2022
371	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2022
372	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	03/2022
373	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 1,082.40	10/2013 03/2022	03/2022
374	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	03/2022
375	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	03/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
376	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2022
377	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	03/2022
378	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 2,330.79	- 03/2022	03/2022
379	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 05/2022	03/2022
380	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	03/2022
381	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	03/2022
382	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	03/2022
383	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 03/2022	03/2022
384	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	03/2022
385	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2022
386	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	03/2022
387	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	03/2022
388	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 02/2022	03/2022
389	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 1,044.32	- 03/2022	03/2022
390	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	04/2022
391	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 1,407.35	- 04/2022	04/2022
392	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	05/2022
393	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	05/2022
394	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2022
395	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	05/2022
396	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 05/2022	05/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
397	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	05/2022
398	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- 03/2022	05/2022
399	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	05/2022
400	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	05/2022
401	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 1,023.23	07/2018 02/2022	05/2022
402	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2022
403	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 1,140.64	10/2017 -	05/2022
404	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	05/2022
405	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	05/2022
406	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	05/2022
407	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	05/2022
408	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 1,118.07	- 05/2022	05/2022
409	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 986.10	- 05/2022	05/2022
410	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 1,072.08	- 05/2022	05/2022
411	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 1,173.65	- 05/2022	05/2022
412	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 655.64	02/2019 04/2021	05/2022
413	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	06/2022
414	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 12/2022	06/2022
415	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	06/2022
416	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	06/2022
417	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,950.04	06/2018 12/2022	06/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
418	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	06/2022
419	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 1,376.86	04/2019 06/2022	06/2022
420	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	06/2022
421	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	06/2022
422	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	06/2022
423	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	06/2022
424	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2022
425	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2022
426	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	06/2022
427	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 595.00	- 06/2022	06/2022
428	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2022
429	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2022
430	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	06/2022
431	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	06/2022
432	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	06/2022
433	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 1,238.29	- 06/2022	06/2022
434	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	07/2022
435	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 1,330.02	- 07/2022	07/2022
436	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 12/2021	07/2022
437	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	07/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
438	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022
439	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 373.10	10/2017 -	07/2022
440	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022
441	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	07/2022
442	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	07/2022
443	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 1,632.70	- 07/2022	07/2022
444	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 1,206.48	- 07/2022	07/2022
445	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 570.98	01/2020 08/2021	07/2022
446	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
447	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
448	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 12/2022	-
449	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	-
450	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
451	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
452	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
453	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
454	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
455	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.92	- -	-
456	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 416.07	- 07/2021	-
457	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
458	4-laning of Khammam-Ashwaraopet section of NH-365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
459	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
460	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
461	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
462	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
463	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	-
	Total		2,15,614.95 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Department Of Telecommunication</u>				
464	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	06/2022
	Total		13,334.00 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
465	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	04/2019 -	04/2022
466	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	03/2021 -	-
467	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	08/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
468	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
469	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	-
	<u>Delhi Metro Rail Corporation</u>				
470	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	-
471	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
472	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
473	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2022
	Total		72,393.12 -		

Costing Rs. 150 Crore and above				(August 2022)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
474	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 12/2022	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
475	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 -	05/2022
476	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 398.90	03/2020 -	06/2022
477	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 431.21	01/2021 -	06/2022
	<u>Delhi Jal Board</u>				
478	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	03/2022
479	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
480	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 -	06/2022
481	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	06/2022
	<u>Uttar Pradesh Jal Nigam</u>				
482	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	06/2022
	<u>Uttarakhand Pey Jal Nigam</u>				
483	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	02/2022
	Total		2,945.00 -		
	<u>COMMERCE</u>				
	<u>Nbcc For Commerce</u>				
484	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Cpwd Of Higher Education</u>				
485	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23 -	10/2012 -	10/2012
486	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA	01/2018	223.37 -	07/2020 -	07/2020
487	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND	09/2012	171.86 171.86	03/2016 07/2022	07/2022

Costing Rs. 150 Crore and above					(August 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		560.46 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
488	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
	Total		151.33 -		
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				
489	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		4,95,263.25		

List of projects original without Date of Commissioning

Costing Rs. 150 Crore and above						(August 2022)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
1	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	1,136.40	-	03/2024	-	0/0
2	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,700.00	1,758.02	-	03/2024	-	0/0
3	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	1,510.00	1,547.42	-	03/2024	-	0/0
4	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,661.76	-	12/2024	-	0/0
5	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	413.53	-	12/2024	-	0/0
6	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	346.79	-	12/2024	-	0/0
7	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	360.11	-	03/2025	-	0/0
8	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	213.88	-	12/2025	-	0/0
	<u>Eastern Railways</u>								
9	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	376.37	-	09/2022	-	0/0
10	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	272.20	328.63	-	12/2022	-	0/0
11	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	470.90	-	03/2023	-	0/0
	<u>North East Frontier Railway</u>								
12	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	401.65	342.82	-	03/2023	-	0/0
	<u>North Eastern Railway</u>								
13	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	800.00	185.52	-	12/2023	-	0/0
	<u>Northern Railway</u>								
14	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	791.39	572.99	-	09/2023	-	0/0
15	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	133.78	-	09/2023	-	0/0
	<u>South Western Railway</u>								
16	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	2,000.97	104.48	-	03/2025	-	0/0
17	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,404.03	1,108.14	-	12/2025	-	2/2

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA <u>Southern Railway</u>	04/1997	2,315.00 -	5,174.30	158.25	- -	03/2028	-	0/0
19	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	1,431.90	1,019.34	- -	03/2024	-	0/0
20	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 1,281.63	1,339.00	.91	- -	03/2025	-	0/0
21	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU <u>Western Railway</u>	09/2006	582.83 -	3,500.79	622.53	- -	12/2025	-	0/0
22	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	311.36	-	- -	03/2024	-	0/0
23	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	393.62	219.72	- -	03/2024	-	0/0
24	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	528.49	127.92	- -	03/2024	-	0/0
	Total		16,246.67 -	30,951.30	13,210.21				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
25	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	225.81	114.55	- -	09/2022	-	0/0
26	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	356.66	162.29	- -	09/2022	-	0/4
27	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	319.96	202.69	- -	09/2022	-	0/0
28	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA <u>National Highways And Infrastructure Development Corporation Ltd.</u>	03/2016	1,101.58 -	1,101.58	395.64	- -	03/2023	-	0/0
29	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	224.65	- -	09/2022	-	3/4
30	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	520.01	214.57	- -	11/2022	-	3/4

Costing Rs. 150 Crore and above (August 2022)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
31	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	232.58	- -	11/2022	-	2/4
32	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	200.44	135.92	- -	12/2022	-	3/4
33	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	188.78	142.23	- -	12/2022	-	3/4
34	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	568.92	390.60	- -	03/2023	-	0/4
35	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	375.80	96.70	- -	04/2023	-	2/4
36	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	350.68	- -	04/2023	-	2/4
37	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	1,718.59	543.26	- -	03/2024	-	2/4
38	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	256.66	-	- -	03/2024	-	1/4
National Highways Authority Of India									
39	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	705.46	- -	08/2022	-	0/0
40	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	528.22	- -	08/2022	-	2/2
41	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 1,248.00	670.50	1,147.08	- -	08/2022	-	0/0
42	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	721.00	- -	08/2022	-	1/3

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANU VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	1,097.00	- -	08/2022	-	3/4
44	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	1,018.46	- -	09/2022	-	3/4
45	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 4,041.80	1,396.74	3,704.91	- -	09/2022	-	0/0
46	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	950.49	539.74	- -	09/2022	-	0/0
47	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	2,450.00	2,691.86	- -	09/2022	-	0/0
48	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,673.32	- -	09/2022	-	0/0
49	FOUR LANING OF MADURAI-CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	448.26	- -	09/2022	-	0/0
50	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	665.33	- -	09/2022	-	0/0
51	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	856.21	- -	10/2022	-	0/0
52	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	320.13	- -	10/2022	-	0/0
53	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	440.00	- -	10/2022	-	0/0
54	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	452.72	- -	10/2022	-	0/1
55	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,568.04	- -	10/2022	-	0/0
56	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	84.10	- -	10/2022	-	0/0

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
57	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	857.62	561.95	- -	10/2022	-	0/0
58	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	884.00	797.00	- -	10/2022	-	3/4
59	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	379.01	- -	11/2022	-	0/1
60	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	689.00	- -	11/2022	-	2/4
61	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	681.67	673.94	- -	12/2022	-	3/4
62	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	408.37	- -	12/2022	-	2/2
63	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	329.71	- -	12/2022	-	0/0
64	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	261.83	- -	12/2022	-	0/0
65	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 1,296.93	1,422.13	444.08	- -	12/2022	-	0/0
66	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 1,065.70	1,065.70	1,049.98	- -	12/2022	-	0/0
67	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	255.05	- -	12/2022	-	0/0
68	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 1,282.30	1,308.88	492.86	- -	12/2022	-	0/0
69	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,182.94	399.40	- -	03/2023	-	0/0
70	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	1,092.03	- -	03/2023	-	0/0
71	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	454.01	- -	03/2023	-	4/4

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
72	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	276.17	175.09	- -	03/2023	-	0/0
73	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	633.68	320.00	- -	03/2023	-	0/1
74	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	309.51	- -	03/2023	-	0/0
75	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,603.94	1,441.00	494.71	- -	03/2023	-	0/0
76	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	316.00	- -	06/2023	-	0/0
77	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	254.00	- -	06/2023	-	0/0
78	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	159.77	- -	06/2023	-	0/0
79	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	537.17	156.46	- -	06/2023	-	0/0
80	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	1,484.30	889.47	- -	08/2023	-	0/0
81	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	1,182.87	84.54	- -	10/2023	-	0/0
82	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	2,360.65	4,521.55	- -	12/2023	-	0/0
83	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	221.14	- -	12/2023	-	0/0
84	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	486.78	171.98	- -	12/2023	-	3/3
85	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 1,862.77	1,862.77	192.01	- -	01/2024	-	0/0

Costing Rs. 150 Crore and above (August 2022)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
86	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	2,169.00	-	- -	01/2024	-	0/0
87	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	895.39	1,369.90	- -	04/2024	-	0/0
88	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	2,145.96	199.05	- -	06/2024	-	0/0
89	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	781.17	- -	08/2024	-	2/2
90	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	1,962.50	689.57	- -	10/2024	-	0/0
	Total		58,830.48 -	63,077.62	43,462.34				49/83
	<u>URBAN DEVELOPMENT</u> <u>National Building Construcion</u> <u>Corporation Ltd</u>								
91	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	1,292.02	- -	03/2023	-	0/9
	Total		2,694.00 -	2,694.00	1,292.02				0/9
	Grand Total		77,771.15	96,722.92	57,964.57				51/94

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2022)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 6,840.00	7,500.00	6,433.54	09/2010 10/2022	09/2024	168	23
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 19,220.00	19,220.00	18,523.00	12/2015 -	06/2023	90	-
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	31,955.00	11/2020 -	11/2023	36	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	14,876.00	12/2016 -	12/2023	84	-
	Total		67,120.00 -	83,648.00	71,787.54				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. - [N04000093]AAI,GUJARAT	08/2018	353.25 -	353.25	143.30	02/2021 -	12/2022	22	-
6	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH	04/2020	611.80 -	611.80	167.35	03/2023 -	07/2023	4	-
7	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	2,445.00	797.96	09/2021 -	09/2023	24	-
8	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. - [N04000095]AAI,GOA	11/2017	255.69 -	255.69	27.32	09/2021 -	09/2023	24	-
9	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM - [N04000096]AAI,MAHARASHTRA	06/2017	255.68 -	255.68	202.60	12/2020 -	09/2023	33	-
10	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	68.90	03/2022 12/2023	03/2024	24	3
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	426.51	03/2021 -	03/2025	48	-
	Total		4,382.29 -	5,534.29	1,833.94				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
12	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 302.00	302.00	296.38	05/2014 -	09/2022	100	-
13	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	139.20	03/2017 -	12/2022	69	-
14	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	20.01	03/2021 -	03/2023	24	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	44.58	04/2018 -	06/2023	62	-
16	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	538.38	03/2019 -	04/2024	61	-
17	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	130.52	04/2014 -	10/2025	138	-
	<u>Central Coal Fields Limited</u>								
18	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	133.41	03/2011 -	03/2023	144	-
19	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	487.40	03/2016 -	03/2023	84	-
20	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	93.61	03/2014 -	03/2023	108	-
	<u>Eastern Coal Fields Limited</u>								
21	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	5,146.48	648.15	08/2019 -	08/2024	60	-
	<u>Mahanadi Coal Fields Limited</u>								
22	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	868.37	874.49	03/2013 -	03/2024	132	-
23	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	251.54	03/2019 -	03/2024	60	-
24	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	734.15	03/2021 -	03/2026	60	-
25	KULDA EXPANSION OCP- 15 MTY - [N06000248]MCL,ODISHA	06/2014	348.16 -	348.16	162.94	03/2018 -	03/2026	96	-
	<u>Neyveli Lignite Corporation</u>								
26	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	13,965.29	11/2021 -	11/2023	24	-
27	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	709.06	526.60	06/2015 -	09/2027	147	-
	<u>Northern Coal Fields Limited</u>								
28	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	1,197.65	03/2021 -	03/2023	24	-
29	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	846.30	03/2022 -	03/2023	12	-
	<u>Singareni Colliers Company Limited</u>								
30	RCE OF INDARAM OPENCAST PROJECT - [N06000211]SCCL,TELANGANA	08/2017	349.28 -	349.28	323.72	03/2021 -	03/2023	24	-
31	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II - [N06000212]SCCL,TELANGANA	03/2019	473.22 -	473.22	392.38	03/2021 -	03/2023	24	-
32	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213]SCCL,TELANGANA	03/2016	384.32 -	384.32	171.52	03/2020 -	03/2023	36	-
33	RCE OF KISTARAM OPENCAST PROJECT - [N06000215]SCCL,TELANGANA	03/2017	164.04 -	164.04	143.08	03/2021 -	03/2023	24	-
34	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	346.68	03/2022 -	03/2024	24	-
35	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	153.75	03/2018 -	03/2024	72	-
36	VENKATESH KHANI COAL MINE - [N06000204]SCCL,TELANGANA	10/2020	484.51 -	484.51	36.25	03/2023 -	03/2024	12	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214]SCCL, TELANGANA	08/2017	442.42 -	442.42	129.91	03/2020 -	03/2024	48	-
	<u>South-Eastern Coal Fields Limited</u>								
38	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	48.55	03/2018 -	03/2023	60	-
39	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH	07/2015	316.10 -	316.10	154.35	03/2020 -	03/2023	36	-
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL, MADHYA PRADESH	12/2014	357.80 -	357.80	86.97	03/2021 -	03/2024	36	-
41	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	87.70	03/2021 -	03/2024	36	-
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	16.13	03/2014 -	03/2026	144	-
	<u>Western Coal Fields Limited</u>								
43	UKNI DEEP OC - [N06000179]WCL, MAHARASHTRA	11/2018	318.14 -	318.14	237.84	03/2021 -	09/2022	18	-
44	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL, MULTI STATE	02/2017	328.00 -	328.00	302.91	03/2021 -	09/2023	30	-
45	BHATADI EXPASION OC (0.975 MTY) - [N06000234]WCL, MAHARASHTRA	02/2016	327.41 -	327.41	176.39	03/2019 -	09/2026	90	-
	Total		36,393.71 -	38,659.90	23,898.73				
	<u>MINES</u>								
	<u>Central Public Works Department</u>								
46	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]CPWD, WEST BENGAL	04/2019	255.37 -	255.37	26.26	04/2022 -	10/2024	30	-
	Total		255.37 -	255.37	26.26				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmhc)</u>								
47	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC, CHHATISGARH	11/2015	2,907.00 -	2,907.00	908.39	06/2023 -	07/2024	13	-
	<u>Steel Authority Of India Limited (Sail)</u>								
48	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	272.19	06/2019 06/2022	09/2022	39	3
49	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	782.72	10/2017 12/2021	12/2023	74	24
	Total		4,203.88 -	4,203.88	1,963.30				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
50	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	19.51	02/2017 08/2022	09/2022	67	1
51	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH	07/2017	580.20 -	580.20	393.95	02/2021 -	03/2023	25	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Gas Authority Of India Limited</u>								
52	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	247.90	154.74	02/2021 -	10/2022	20	-
53	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.00	327.01	255.10	08/2020 06/2022	12/2022	28	6
54	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]GAIL,JHARKHAND	10/2017	226.45 -	226.45	179.25	10/2022 -	03/2023	5	-
55	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 -	243.53	195.96	07/2022 -	08/2023	13	-
56	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20 -	182.20	115.16	07/2022 -	08/2023	13	-
57	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]GAIL,JHARKHAND	10/2017	221.45 -	221.45	129.91	10/2022 -	08/2023	10	-
58	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	359.25	228.18	10/2022 -	10/2023	12	-
	<u>Hindustan Petroleum Corporation Limited</u>								
59	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	249.10	06/2020 -	09/2022	27	-
60	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA	06/2019	2,166.38 -	2,166.38	1,762.67	06/2022 -	10/2022	4	-
61	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	210.94	139.97	08/2021 -	12/2022	16	-
62	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 -	26,264.00	20,025.46	07/2020 -	03/2023	32	-
63	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH	10/2020	332.61 -	332.61	32.33	11/2022 -	03/2023	4	-
64	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	275.43	09/2026 -	02/2027	5	-
65	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	763.70	03/2029 -	08/2029	5	-
66	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL	03/2019	5,830.20 -	5,830.20	301.79	03/2031 -	08/2031	5	-
	<u>Indian Oil Corporation Limited</u>								
67	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	423.21	02/2020 07/2022	09/2022	31	2
68	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,446.06	03/2021 06/2022	10/2022	19	4
69	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	680.30	01/2021 08/2022	11/2022	22	3
70	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	684.72	10/2017 03/2022	12/2022	62	9
71	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 2,145.00	2,145.00	1,801.97	02/2022 08/2022	12/2022	10	4

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
72	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	271.34	01/2021 -	12/2022	23	-
73	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA	04/2018	5,654.00 -	5,654.00	3,885.24	10/2021 07/2022	12/2022	14	5
74	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	1,097.83	08/2020 04/2022	12/2022	28	8
75	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	1,004.24	10/2021 07/2022	12/2022	14	5
76	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 753.89	753.89	602.73	02/2020 07/2022	12/2022	34	5
77	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	403.00	213.43	08/2022 -	12/2022	4	-
78	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	150.41	04/2022 -	02/2023	10	-
79	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	160.73	06/2021 07/2022	03/2023	21	8
80	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	202.16	129.65	07/2022 -	03/2023	8	-
81	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	81.34	07/2021 03/2022	06/2023	23	15
82	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	118.68	10/2020 08/2022	08/2023	34	12
83	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	193.17	04/2022 -	08/2023	16	-
84	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	61.75	09/2023 -	02/2024	5	-
85	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	1,398.00	290.30	12/2023 -	02/2024	2	-
86	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA	05/2019	3,361.00 -	3,361.00	2,258.02	08/2021 09/2022	03/2024	31	18
87	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR	01/2020	14,810.00 -	14,810.00	3,834.49	04/2023 -	07/2024	15	-
	<u>Oil & Natural Gas Corporation Limited</u>								
88	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	462.08	03/2019 09/2021	12/2022	45	15
89	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND	12/2015	823.27 1,137.79	1,137.79	848.08	03/2023 03/2022	03/2023	0	12
	Total		76,592.09 -	85,378.29	46,921.98				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	4,287.59	793.45	- 08/2024	07/2025	-	11
	<u>National Hydro-Electric Power Corporation</u>								
91	TEESTA VI HE PROJECT - [N18000325]NHPC,SIKKIM	03/2019	5,748.04 -	5,748.04	1,748.06	03/2024 -	07/2025	16	-
	<u>National Thermal Power Corporation</u>								
92	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,998.00	9,540.00	11/2020 07/2022	06/2023	31	11
93	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	1,221.73	146.13	07/2022 -	08/2023	13	-
94	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	599.99	170.95	07/2022 -	08/2023	13	-
95	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	842.27	92.08	07/2022 10/2022	08/2023	13	10
96	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]NTPC,GUJARAT	05/2021	674.92 -	674.92	76.91	09/2022 -	08/2023	11	-
97	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	20,184.00	10/2011 07/2023	03/2024	149	8
98	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	7,103.00	5,489.00	03/2013 12/2021	12/2024	141	36
99	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	17,007.00	13,203.00	06/2019 10/2022	12/2024	66	26
100	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	18,668.00	8,846.25	03/2023 -	03/2025	24	-
101	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,803.00	809.11	09/2019 12/2024	07/2025	70	7
	<u>Power Grid Corporation Of India Limited</u>								
102	EASTERN REGION STRENGTHENING SCHEME- XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,160.77	07/2020 -	08/2022	25	-
103	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION - [N18000339]PGCIL,MULTI STATE	11/2018	173.94 -	173.94	114.48	11/2021 -	09/2022	10	-
104	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]PGCIL,GUJARAT	10/2019	1,031.00 -	1,143.00	985.61	08/2021 -	10/2022	14	-
105	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	266.47	12/2019 -	11/2022	35	-
106	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302]PGCIL,HARYANA	01/2019	267.33 -	267.33	86.32	03/2022 -	11/2022	8	-
107	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	195.47	03/2018 -	12/2022	57	-
108	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	210.54	02/2019 -	12/2022	46	-
109	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	164.87	06/2019 -	12/2022	42	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	219.66	172.19	07/2019 -	12/2022	41	-
111	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL,MULTI STATE	09/2015	167.31 -	167.31	129.26	12/2017 -	12/2022	60	-
112	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD - [N18000314]PGCIL,RAJASTHAN	01/2020	562.86 -	562.86	374.60	01/2021 -	12/2022	23	-
113	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL,MULTI STATE	11/2018	241.38 -	241.38	223.80	11/2021 -	12/2022	13	-
114	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL,RAJASTHAN	05/2021	1,184.88 -	1,184.88	80.70	09/2022 -	01/2023	4	-
115	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308]PGCIL,MULTI STATE	02/2019	572.98 -	572.98	293.86	12/2020 -	03/2023	27	-
116	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	2,635.55	1,891.34	02/2020 -	04/2023	38	-
117	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN	06/2021	1,562.00 -	1,562.00	500.90	12/2022 -	08/2023	8	-
118	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN	06/2021	1,006.00 -	1,006.00	660.83	12/2022 -	08/2023	8	-
119	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303]PGCIL,RAJASTHAN	03/2021	353.85 -	353.85	134.19	12/2022 -	09/2023	9	-
120	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305]PGCIL,RAJASTHAN	06/2021	713.82 -	713.82	323.37	12/2022 -	12/2023	12	-
121	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,700.00	4,097.84	12/2018 -	01/2024	61	-
122	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	4,251.79	12/2018 -	03/2024	63	-
	<u>Satluj Jal Vidyut Nigam Limited</u>								
123	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	947.89	915.31	12/2021 -	12/2022	12	-
	<u>Thdc India Limited</u>								
124	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 -	1,587.16	742.49	09/2020 -	09/2022	24	-
125	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	4,825.60	4,755.19	02/2016 06/2022	10/2023	92	16

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
126	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42	11,089.42	5,031.01	09/2023	08/2024	11	-
127	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	2,640.57	06/2013	03/2025	141	-
	Total		1,12,507.77	1,44,339.13	93,502.71				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Nbcc For Health</u>								
128	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH	04/2018	1,351.00	1,471.04	1,162.76	09/2021	08/2022	11	-
	Total		1,351.00	1,471.04	1,162.76				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
129	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29	3,445.48	1,543.90	03/2023	03/2024	12	-
130	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02	540.02	365.59	03/2022	03/2024	24	-
131	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19	1,384.72	629.92	03/2022	03/2024	24	-
132	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91	2,449.91	657.66	03/2023	03/2024	12	-
133	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16	1,035.16	542.40	03/2022	03/2024	24	-
134	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95	637.95	313.34	03/2023	03/2024	12	-
135	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50	4,805.17	3,140.43	03/2021	03/2025	48	-
136	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89	1,387.52	464.66	03/2021	03/2025	48	-
137	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00	2,081.27	881.45	03/2023	03/2025	24	-
	<u>East Central Railways</u>								
138	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	1,153.56	03/2020	03/2023	36	-
139	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57	528.57	436.16	03/2019	03/2023	48	-
140	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	1,110.00	1,112.02	03/2012	06/2023	135	-
141	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47	1,491.47	660.90	03/2020	12/2023	45	-
142	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21	2,436.21	1,953.80	03/2020	03/2024	48	-
143	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	624.19	03/2021	03/2024	36	-
144	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	685.28	03/2021	12/2024	45	-
145	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 548.00	783.83	540.74	03/2020	03/2025	60	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>East Coast Railway</u>								
146	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	439.50	10/2020 -	03/2024	41	-
147	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	1,095.89	03/2020 -	03/2024	48	-
148	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	834.54	03/2022 -	03/2024	24	-
149	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	1,027.78	06/2021 -	03/2025	45	-
150	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	179.43	11/2018 -	03/2025	76	-
151	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	825.47	12/2018 -	03/2025	75	-
152	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	992.84	03/2022 -	03/2026	48	-
	<u>Eastern Railways</u>								
153	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	525.35	03/2017 -	10/2022	67	-
154	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	558.15	03/2022 -	03/2023	12	-
155	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	906.01	03/2019 12/2009	03/2025	72	183
	<u>Indian Railway Construction Company Limited</u>								
156	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,500.00	2,945.30	09/2018 -	12/2023	63	-
157	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	1,509.87	03/2022 -	12/2024	33	-
158	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	5,200.00	-	03/2020 -	12/2025	69	-
	<u>Metropolitan Rapid Transport Projects</u>								
159	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	774.51	552.70	06/2013 -	12/2022	114	-
160	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,991.80	03/2004 -	03/2023	228	-
	<u>North Central Railway</u>								
161	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 2,001.00	2,001.00	1,043.73	03/2021 -	12/2023	33	-
162	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	799.75	03/2022 -	12/2024	33	-
163	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	109.37	03/2023 -	03/2026	36	-
164	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 746.83	746.83	22.79	- 03/2026	12/2027	-	21
	<u>North East Frontier Railway</u>								

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
165	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	708.73	380.92	03/2020 -	09/2022	30	-
166	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	14,322.79	12,817.81	03/2011 -	12/2023	153	-
167	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,650.00	1,255.18	03/2019 -	12/2023	57	-
168	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	6,527.45	5,330.91	03/2014 -	12/2023	117	-
169	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	7,876.92	3,408.77	12/2015 -	12/2023	96	-
170	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	2,047.51	1,050.40	03/2019 -	12/2023	57	-
171	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,145.79	990.86	03/2019 -	03/2024	60	-
172	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	471.00	77.45	03/2020 -	03/2024	48	-
173	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	983.55	344.80	03/2020 -	10/2024	55	-
174	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	4,059.65	2,380.05	03/2022 -	03/2025	36	-
175	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,663.00	1,781.77	03/2015 -	03/2026	132	-
	<u>North Eastern Railway</u>								
176	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	341.66	.74	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
177	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	476.01	03/2020 -	10/2022	31	-
178	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	638.86	08/2022 -	11/2022	3	-
	<u>Northern Railway</u>								
179	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,017.96	845.23	07/2012 -	11/2024	148	-
180	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	-
181	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	1,540.13	242.09	03/2023 -	12/2025	33	-
	<u>Rail Vikas Nigam Ltd.</u>								
182	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	2,202.65	02/2015 -	09/2022	91	-
183	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	626.34	03/2016 -	09/2022	78	-
184	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	2,350.49	03/2020 -	09/2022	30	-
185	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,405.40	03/2020 -	09/2022	30	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	2,203.53	2,075.59	12/2020 -	09/2022	21	-
187	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	2,340.59	12/2020 -	09/2022	21	-
188	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	433.00	455.39	03/2009 03/2009	12/2022	165	165
189	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	2,538.01	2,375.23	12/2021 -	12/2022	12	-
190	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,500.00	1,127.95	03/2022 -	12/2022	9	-
191	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,664.15	03/2020 -	12/2022	33	-
192	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,457.79	1,408.80	03/2019 -	03/2023	48	-
193	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,552.26	1,445.70	03/2019 -	03/2023	48	-
194	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,284.85	03/2022 -	05/2023	14	-
195	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,267.55	03/2023 -	12/2024	21	-
196	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	24,659.00	8,453.89	12/2024 -	03/2025	3	-
197	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,834.54	1,839.89	03/2016 -	07/2025	112	-
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	305.05	03/2014 -	12/2025	141	-
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	3,496.68	03/2016 -	03/2026	120	-
200	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	2,712.78	12/2024 -	12/2026	24	-
	<u>South Central Railway</u>								
201	MUNEERABAD-MAHA BOOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,206.22	03/2000 -	03/2023	276	-
202	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,875.71	03/2021 -	03/2024	36	-
203	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	2,250.00	784.26	03/2010 -	03/2025	180	-
204	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	918.80	03/2023 -	03/2025	24	-
205	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,755.92	03/2022 -	03/2025	36	-
206	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	1,274.68	03/2021 -	03/2026	60	-
207	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,095.80	03/2009 -	03/2027	216	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>South East Central Railway</u>								
208	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	88.40	12/2021 -	12/2024	36	-
	<u>South Eastern Railway</u>								
209	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.97	1,264.07	03/2020 -	10/2022	31	-
210	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	511.75	259.72	12/2021 -	01/2023	13	-
211	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	393.83	34.60	06/2022 -	12/2023	18	-
212	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	1,358.49	03/2021 -	03/2024	36	-
213	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	1,866.31	610.05	05/2023 -	12/2024	19	-
214	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	472.50	6.00	06/2022 -	12/2025	42	-
	<u>South Western Railway</u>								
215	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,954.21	1,381.52	03/2020 -	12/2022	33	-
216	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,878.00	1,611.28	03/2019 -	02/2024	59	-
217	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	36.45	03/2016 -	03/2024	96	-
218	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	490.24	12/2018 -	06/2025	78	-
219	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2026	120	-
220	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	826.18	499.13	03/2017 -	03/2026	108	-
221	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 1,378.00	1,530.09	332.27	03/2016 -	12/2026	129	-
	<u>Southern Railway</u>								
222	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,081.20	1,774.56	02/2019 -	03/2025	73	-
223	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,084.48	321.37	03/2019 -	12/2027	105	-
	<u>West Central Railway</u>								
224	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	704.97	03/2022 -	09/2024	30	-
225	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	1,720.50	03/2020 -	10/2024	55	-
226	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,427.33	05/2008 -	03/2025	202	-
	Total		1,50,294.13 -	2,38,747.98	1,27,950.37				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
227	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 241.60	241.60	164.41	02/2017 12/2020	08/2022	66	20
228	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	190.01	04/2020 -	08/2022	28	-
229	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	314.69	- 03/2021	09/2022	-	18
230	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	467.04	01/2020 06/2021	09/2022	32	15
231	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	927.73	784.39	02/2020 08/2021	09/2022	31	13
232	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	635.00	07/2018 05/2021	09/2022	50	16
233	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	949.54	807.22	06/2019 04/2021	09/2022	39	17
234	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 913.49	913.49	700.54	11/2018 06/2021	09/2022	46	15
235	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	545.64	216.28	07/2019 -	09/2022	38	-
236	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	313.95	142.29	06/2019 -	09/2022	39	-
237	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	376.19	113.66	05/2019 -	09/2022	40	-
238	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	420.63	209.61	05/2020 -	09/2022	28	-
239	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	323.02	06/2019 -	09/2022	39	-
240	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	301.38	195.29	08/2020 -	09/2022	25	-
241	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	653.46	287.45	07/2019 -	09/2022	38	-
242	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	488.60	240.92	07/2019 -	09/2022	38	-
243	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	381.77	186.62	06/2019 -	09/2022	39	-
244	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	743.21	475.80	06/2021 -	09/2022	15	-
245	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 2,226.11	983.14	806.99	12/2019 -	09/2022	33	-
246	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	314.90	206.30	03/2017 03/2021	09/2022	66	18

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
247	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	159.12	123.72	01/2016 12/2021	09/2022	80	9
248	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	125.56	05/2019 -	09/2022	40	-
249	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	165.67	124.52	11/2015 12/2021	10/2022	83	10
250	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	238.00	94.55	11/2019 -	10/2022	35	-
251	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	10/2022	55	12
252	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	174.90	154.26	08/2018 08/2021	10/2022	50	14
253	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	206.89	08/2018 09/2021	10/2022	50	13
254	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	184.37	03/2018 10/2021	10/2022	55	12
255	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	219.86	07/2018 08/2021	10/2022	51	14
256	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	197.45	02/2018 03/2022	10/2022	56	7
257	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	195.15	03/2019 -	10/2022	43	-
258	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	293.64	283.78	08/2020 -	10/2022	26	-
259	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	428.55	404.69	03/2018 06/2021	10/2022	55	16
260	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	323.36	237.25	08/2020 -	10/2022	26	-
261	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	302.65	01/2018 -	10/2022	57	-
262	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 225.06	225.06	212.91	05/2016 06/2022	11/2022	78	5
263	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 587.41	587.41	553.81	05/2016 03/2022	11/2022	78	8

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
264	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	141.48	02/2018 09/2021	11/2022	57	14
265	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	137.88	03/2017 12/2021	11/2022	68	11
266	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	936.40	611.47	- 09/2022	12/2022	-	3
267	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	432.54	08/2017 06/2021	12/2022	64	18
268	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 -	396.86	282.77	09/2019 03/2022	12/2022	39	9
269	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	90.24	03/2018 09/2021	12/2022	57	15
270	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	293.10	256.89	08/2020 -	12/2022	28	-
271	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	739.08	10/2019 -	12/2022	38	-
272	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	87.84	11/2020 -	12/2022	25	-
273	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	962.43	594.81	03/2018 -	12/2022	57	-
274	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	363.82	109.56	09/2019 -	12/2022	39	-
275	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	237.40	31.41	05/2020 -	12/2022	31	-
276	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	237.00	06/2019 -	12/2022	42	-
277	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	404.33	114.51	05/2020 -	12/2022	31	-
278	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	381.08	21.02	05/2020 -	12/2022	31	-
279	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	341.80	203.09	06/2019 -	12/2022	42	-
280	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	1,230.02	664.06	11/2019 -	12/2022	37	-
281	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	179.94	03/2021 11/2021	12/2022	21	13

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
282	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	572.66	280.46	08/2016 -	12/2022	76	-
283	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	277.98	06/2017 -	12/2022	66	-
284	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	731.50	471.29	10/2016 -	12/2022	74	-
285	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	435.61	126.17	07/2016 -	12/2022	77	-
286	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	264.34	181.38	09/2017 04/2021	12/2022	63	20
287	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	780.77	453.21	- 06/2022	03/2023	-	9
288	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	2,138.16	1,412.08	10/2016 03/2022	03/2023	77	12
289	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	125.25	11/2018 03/2022	03/2023	52	12
290	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 -	426.18	284.89	09/2020 03/2022	03/2023	30	12
291	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO) - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 -	254.30	130.87	10/2020 03/2022	03/2023	29	12
292	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 -	213.97	47.17	08/2019 11/2022	03/2023	43	4
293	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 -	263.26	91.29	08/2019 08/2022	03/2023	43	7
294	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	242.61	94.29	06/2019 01/2022	03/2023	45	14
295	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	544.00	452.11	09/2016 -	03/2023	78	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
296	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	240.11	03/2015 -	03/2023	96	-
297	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	89.32	03/2018 03/2022	05/2023	62	14
298	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT - [N24001423]MoRTH,UTTAR PRADESH	04/2021	309.48 -	309.48	27.13	03/2022 -	09/2023	18	-
299	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W - [N24001424]MoRTH,UTTAR PRADESH	03/2021	185.09 -	185.09	3.58	03/2022 -	09/2023	18	-
300	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	423.15	216.18	12/2019 12/2022	12/2023	48	12
<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
301	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	259.79	158.07	11/2018 -	08/2022	45	-
302	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	252.05	171.06	04/2017 -	08/2022	64	-
303	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	873.91	559.13	11/2018 -	09/2022	46	-
304	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	119.22	09/2018 -	09/2022	48	-
305	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	175.49	11/2017 -	09/2022	58	-
306	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	165.99	05/2019 -	09/2022	40	-
307	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	263.31	172.68	04/2017 -	10/2022	66	-
308	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA	03/2020	247.76 -	247.76	67.01	01/2022 -	10/2022	9	-
309	2-LANING OF CHANGTONGGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND	03/2020	278.95 -	278.95	128.23	06/2022 -	10/2022	4	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
310	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]NHIDCL,TRIPURA	09/2020	173.17 -	173.17	21.34	04/2022 -	10/2022	6	-
311	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	252.79	180.00	04/2017 -	11/2022	67	-
312	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	199.63	09/2018 -	11/2022	50	-
313	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM	08/2020	278.46 -	278.46	120.18	03/2022 -	11/2022	8	-
314	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL,MANIPUR	07/2020	177.76 -	177.76	70.23	08/2022 -	11/2022	3	-
315	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	289.99	120.17	12/2018 -	12/2022	48	-
316	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	330.30	141.13	01/2016 -	12/2022	83	-
317	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	284.09	188.40	04/2017 -	12/2022	68	-
318	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	274.31	143.41	05/2018 -	12/2022	55	-
319	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	403.36	230.60	06/2018 -	12/2022	54	-
320	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	417.24	295.36	05/2018 -	12/2022	55	-
321	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	391.00	22.17	10/2018 -	12/2022	50	-
322	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	86.37	09/2018 -	12/2022	51	-
323	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	253.44	112.59	07/2019 -	12/2022	41	-
324	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM	03/2020	242.97 -	242.97	68.35	06/2022 -	12/2022	6	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
325	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR	07/2020	228.39 -	228.39	14.76	04/2022 -	12/2022	8	-
326	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR	07/2020	210.79 -	210.79	20.59	04/2022 -	12/2022	8	-
327	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 1B) - [N24001269]NHIDCL,ASSAM	03/2020	216.49 -	216.49	65.59	03/2022 -	12/2022	9	-
328	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL,MANIPUR	03/2020	292.24 -	292.24	98.42	06/2022 -	12/2022	6	-
329	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL,MANIPUR	06/2020	365.53 -	365.53	118.82	08/2022 -	12/2022	4	-
330	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL,MANIPUR	03/2020	167.95 -	167.95	77.72	06/2022 -	12/2022	6	-
331	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]NHIDCL,TRIPURA	11/2020	332.14 -	332.14	56.56	07/2022 11/2022	12/2022	5	1
332	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]NHIDCL,TRIPURA	11/2020	159.13 -	159.13	30.58	06/2022 -	12/2022	6	-
333	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]NHIDCL,TRIPURA	11/2020	280.91 -	280.91	148.65	07/2022 -	12/2022	5	-
334	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]NHIDCL,MANIPUR	03/2020	167.95 -	167.95	77.77	06/2022 -	12/2022	6	-
335	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA	06/2020	201.99 -	201.99	49.65	01/2022 -	12/2022	11	-
336	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]NHIDCL,SIKKIM	09/2020	183.31 -	183.31	87.22	05/2022 -	12/2022	7	-
337	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]NHIDCL,SIKKIM	08/2020	292.80 -	292.80	52.83	05/2022 -	12/2022	7	-
338	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]NHIDCL,NAGALAND	03/2020	206.53 -	206.53	95.95	06/2022 -	12/2022	6	-
339	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390]NHIDCL,ARUNACHAL PRADESH	08/2020	228.71 -	228.71	67.40	04/2022 04/2022	12/2022	8	8
340	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH	08/2020	301.06 -	301.06	45.78	04/2022 -	01/2023	9	-
341	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH	09/2020	353.90 -	353.90	34.28	05/2022 -	01/2023	8	-
342	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]NHIDCL,TRIPURA	03/2020	165.54 -	165.54	37.19	07/2022 -	01/2023	6	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
343	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM	03/2021	636.42 -	418.49	96.45	12/2022 -	01/2023	1	-
344	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL,MANIPUR	08/2020	379.39 -	379.39	22.07	04/2022 -	02/2023	10	-
345	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	801.54	185.26	06/2018 -	03/2023	57	-
346	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	262.97	30.00	10/2018 -	03/2023	53	-
347	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND	09/2020	315.63 -	315.63	12.23	04/2022 -	03/2023	11	-
348	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL,MANIPUR	03/2019	471.00 -	471.00	251.05	07/2022 -	03/2023	8	-
349	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]NHIDCL,ASSAM	03/2020	261.13 -	261.13	45.67	06/2022 -	03/2023	9	-
350	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	220.92	09/2019 -	04/2023	43	-
351	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	201.83	09/2019 -	04/2023	43	-
352	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	237.48	09/2019 -	04/2023	43	-
353	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM	08/2020	208.84 -	208.84	27.93	04/2022 -	04/2023	12	-
354	DOGINALA - GAU - [N24001320]NHIDCL,ARUNACHAL PRADESH	12/2020	242.30 -	242.30	15.04	09/2022 -	04/2023	7	-
355	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]NHIDCL,MEGHALAYA	10/2020	157.86 -	157.86	81.82	04/2022 -	04/2023	12	-
356	TAMENGLONG - MAHUR PKG-3 - [N24001354]NHIDCL,MANIPUR	03/2021	234.08 -	234.08	32.64	12/2022 -	04/2023	4	-
357	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM	03/2019	402.94 -	402.94	118.12	04/2022 -	05/2023	13	-
358	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	103.64	09/2018 -	06/2023	57	-

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
359	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM	03/2015	829.00 -	1,307.50	411.51	01/2016 -	06/2023	89	-
360	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL, MIZORAM	04/2017	642.96 -	642.96	234.97	09/2019 -	06/2023	45	-
361	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL, MIZORAM	04/2017	518.53 -	518.53	234.73	09/2019 -	06/2023	45	-
362	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL, NAGALAND	08/2020	202.36 -	202.36	15.41	04/2022 -	06/2023	14	-
363	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL, MIZORAM	04/2017	640.07 -	640.07	271.82	09/2019 -	07/2023	46	-
364	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL, MIZORAM	04/2017	428.11 -	428.11	182.20	09/2019 -	09/2023	48	-
365	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL, MANIPUR	07/2021	467.00 -	467.00	50.90	03/2023 -	09/2023	6	-
366	MARAM - PEREN PKG-3 - [N24001439]NHIDCL, MANIPUR	08/2021	467.41 -	467.41	20.74	05/2023 -	11/2023	6	-
367	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL, NAGALAND	09/2020	277.44 -	277.44	55.34	10/2022 -	12/2023	14	-
368	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]NHIDCL, SIKKIM	09/2020	262.84 -	262.84	129.59	05/2023 -	01/2024	8	-
369	LADDA - BASAI - [N24001316]NHIDCL, ARUNACHAL PRADESH	02/2021	445.96 -	445.96	2.94	04/2023 -	02/2024	10	-
370	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL, UTTARAKHAND	03/2018	1,383.78 -	1,383.78	362.22	07/2018 -	03/2024	68	-
371	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL, MIZORAM	04/2017	404.29 -	404.29	145.96	09/2019 -	04/2024	55	-
372	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]NHIDCL, SIKKIM	10/2020	493.42 -	493.42	12.26	11/2023 -	05/2024	6	-
	<u>National Highways Authority Of India</u>								
373	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 819.35	819.35	439.27	05/2018 03/2022	08/2022	51	5
374	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	1,664.20	1,301.27	04/2020 -	08/2022	28	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
375	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,405.27	1,401.96	03/2020 -	08/2022	29	-
376	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 2,909.00	1,959.00	1,412.01	- 11/2021	08/2022	-	9
377	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,827.00	1,306.69	03/2021 -	08/2022	17	-
378	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	1,020.00	12/2019 -	08/2022	32	-
379	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	908.00	03/2020 -	08/2022	29	-
380	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	879.00	05/2020 -	08/2022	27	-
381	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	996.27	965.00	03/2020 -	08/2022	29	-
382	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,919.69	03/2013 -	09/2022	114	-
383	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,935.64	06/2014 -	09/2022	99	-
384	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	09/2022	53	-
385	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 2,408.72	2,408.72	1,865.00	04/2019 -	09/2022	41	-
386	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,405.30	2,328.27	2,126.16	07/2018 12/2021	09/2022	50	9
387	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 3,150.00	3,063.99	2,904.36	04/2019 12/2021	09/2022	41	9
388	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	1,251.13	- 12/2021	09/2022	-	9
389	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	359.60	339.75	- 05/2017	09/2022	-	64
390	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,361.00	503.77	- 06/2021	09/2022	-	15

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
391	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	1,309.30	03/2020 -	09/2022	30	-
392	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	1,361.00	503.77	- 06/2021	09/2022	-	15
393	WIDENING OF KHEDE-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	10/2022	104	-
394	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	275.93	07/2017 -	10/2022	63	-
395	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	494.33	04/2014 -	11/2022	103	-
396	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	627.92	- 08/2022	11/2022	-	3
397	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	157.49	31.97	03/2020 -	11/2022	32	-
398	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	446.97	170.57	11/2020 -	11/2022	24	-
399	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	464.09	174.53	11/2020 -	11/2022	24	-
400	INDORE-JHABUA-GUJARAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	12/2022	116	-
401	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	-
402	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	768.92	03/2014 -	12/2022	105	-
403	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 480.35	777.03	766.05	05/2018 -	12/2022	55	-
404	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	869.13	11/2016 -	12/2022	73	-
405	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	1,543.51	1,472.50	03/2018 03/2021	12/2022	57	21
406	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 567.00	639.58	492.38	04/2019 07/2022	12/2022	44	5
407	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,603.99	2,323.88	2,223.06	06/2018 12/2021	12/2022	54	12
408	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,192.10	3,006.53	2,989.89	06/2018 12/2021	12/2022	54	12

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
409	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	242.52	03/2019 -	12/2022	45	-
410	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	252.08	03/2020 -	12/2022	33	-
411	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	880.00	04/2020 -	12/2022	32	-
412	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 649.00	649.00	185.59	- 10/2021	12/2022	-	14
413	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	649.90	155.54	12/2020 -	12/2022	24	-
414	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	732.34	530.71	11/2019 01/2022	12/2022	37	11
415	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	361.70	304.45	11/2019 -	12/2022	37	-
416	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	606.75	410.81	11/2019 -	12/2022	37	-
417	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 1,414.01	1,414.01	1,000.57	06/2018 -	01/2023	55	-
418	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	1,855.00	06/2014 -	02/2023	104	-
419	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 1,140.50	828.29	287.90	- 03/2021	02/2023	-	23
420	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 1,240.13	1,321.60	678.20	02/2021 04/2021	02/2023	24	22
421	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	1,587.77	02/2013 12/2022	03/2023	121	3
422	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 526.09	526.09	189.10	04/2014 -	03/2023	107	-
423	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 736.01	830.31	31.82	03/2020 12/2018	03/2023	36	51
424	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,309.79	1,162.72	09/2017 05/2021	03/2023	66	22
425	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	63.30	12/2017 -	05/2023	65	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
426	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	2,004.66	08/2013 -	06/2023	118	-
427	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	2,510.04	658.95	08/2019 -	06/2023	46	-
428	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	1,208.03	06/2020 -	06/2023	36	-
429	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 644.50	726.99	222.51	- 12/2019	06/2023	-	42
430	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI, MADHYA PRADESH	11/2019	716.00 -	716.00	-	07/2021 -	07/2023	24	-
431	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI, BIHAR	10/2019	1,101.99 -	1,101.99	424.90	02/2020 -	08/2023	42	-
432	4L OF ADDAHOLE TO BANTWAL CROSS SECTION - [N24001426]NHAI, KARNATAKA	03/2021	317.90 317.90	317.90	127.41	10/2021 -	09/2023	23	-
433	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN - [N24001425]NHAI, KARNATAKA	03/2021	1,100.88 1,100.88	1,100.88	261.90	11/2021 -	11/2023	24	-
434	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON - [N24001428]NHAI, TAMIL NADU	03/2018	998.70 -	998.70	-	11/2021 -	11/2023	24	-
435	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER - [N24001429]NHAI, TAMIL NADU	03/2018	1,294.47 -	1,294.47	-	11/2021 -	11/2023	24	-
436	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	1,190.60	06/2019 -	12/2023	54	-
437	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN - [N24001431]NHAI, TAMIL NADU	03/2018	1,872.68 -	1,872.68	-	10/2020 -	12/2023	38	-
438	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI, UTTAR PRADESH	10/2020	724.60 -	724.60	680.12	03/2023 -	01/2024	10	-
439	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM - [N24001430]NHAI, TAMIL NADU	03/2018	2,120.40 -	2,120.40	-	01/2022 -	01/2024	24	-
440	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 -	1,339.00	1,236.41	- 10/2018	03/2024	-	65
441	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI, PUNJAB	12/2020	989.66 -	989.66	-	01/2024 -	04/2024	3	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
442	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	982.00	-	03/2020 07/2022	07/2024	52	24
443	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	1,601.10	612.83	02/2021 -	07/2024	41	-
444	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	-	05/2017 -	09/2024	88	-
	Total		1,31,723.94 -	1,44,639.59	93,497.87				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
445	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 461.42	461.42	107.44	06/2021 11/2021	11/2022	17	12
	<u>Cpwd For Telecom</u>								
446	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20 -	248.20	174.08	03/2018 -	11/2022	56	-
	Total		679.36 -	709.62	281.52				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
447	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,925.22	10,816.18	12/2018 -	09/2022	45	-
448	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	12,020.32	814.67	03/2024 -	06/2024	3	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
449	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	22,869.55	02/2021 -	03/2025	49	-
	<u>Central Public Works Department</u>								
450	CONSTRUCTION729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	299.97	69.08	09/2020 -	11/2023	38	-
451	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	36.69	07/2021 -	06/2024	35	-
	<u>Delhi Metro Rail Corporation</u>								
452	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65 -	24,948.65	4,071.69	03/2025 -	09/2025	6	-
	<u>Lucknow Metro Rail Corporation Limited</u>								
453	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	3,461.78	03/2024 -	11/2024	8	-
454	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	1,143.47	03/2024 -	12/2025	21	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								

Costing Rs. 150 Crore and above

(August 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
455	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	33,406.00	22,064.15	03/2020 -	12/2023	45	-
	Total		1,18,219.18 -	1,30,562.20	65,347.26				
	<u>WATER RESOURCES</u>								
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
456	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO, BIHAR	05/2017	356.37 -	356.37	215.30	04/2021 -	09/2022	17	-
457	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO, BIHAR	11/2018	236.15 -	236.15	80.59	12/2020 -	10/2022	22	-
458	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO, BIHAR	03/2017	277.42 -	277.42	298.55	05/2021 -	10/2022	17	-
459	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO, BIHAR	08/2017	578.89 -	578.89	16.55	06/2022 -	12/2022	6	-
460	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO, BIHAR	08/2017	824.00 -	824.00	140.17	06/2022 -	12/2022	6	-
461	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO, BIHAR	03/2018	230.06 -	230.06	137.93	07/2021 -	03/2023	20	-
462	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19 -	305.19	146.80	08/2021 -	08/2023	24	-
463	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO, BIHAR	03/2018	294.02 -	294.02	90.96	10/2021 -	12/2023	26	-
464	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 413.29	413.29	.07	09/2020 -	03/2024	42	-
	<u>Delhi Jal Board</u>								
465	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI	05/2016	211.79 -	211.79	136.75	12/2021 -	12/2022	12	-
466	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI	05/2016	239.11 -	239.11	205.76	02/2022 -	12/2022	10	-
	<u>Kolkata Metropolitan Development Authority</u>								
467	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	185.22	36.83	12/2021 -	09/2023	21	-
468	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	172.10	36.83	12/2021 -	09/2023	21	-
469	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	164.93	36.83	12/2021 -	09/2023	21	-
470	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022 -	03/2024	25	-
471	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	165.16	-	06/2022 -	03/2024	21	-
472	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	10.35	02/2022 -	03/2024	25	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
473	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	384.96	-	04/2022 -	12/2024	32	-
474	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	287.53	-	04/2022 -	12/2024	32	-
475	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	234.31	-	04/2022 -	12/2024	32	-
476	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	307.12	-	09/2022 -	12/2024	27	-
	<u>Uttar Pradesh Jal Nigam</u>								
477	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05 -	206.05	110.89	10/2021 -	08/2022	10	-
478	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 -	967.23	161.48	09/2021 -	09/2022	12	-
479	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59 -	767.59	198.68	09/2021 -	12/2022	15	-
480	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam, UTTAR PRADESH	01/2019	231.79 234.03	234.03	28.37	12/2021 -	06/2023	18	-
481	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	271.39	-	08/2021 -	03/2024	31	-
482	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam, UTTAR PRADESH	10/2017	213.62 261.12	261.12	-	03/2022 -	04/2024	25	-
483	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UP JalNigam, UTTAR PRADESH	02/2019	681.78 690.71	690.71	-	06/2022 -	04/2024	22	-
484	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	04/2024	33	-
	Total		9,704.46 -	9,859.07	2,089.69				
	<u>DEFENCE PRODUCTION</u>								
	<u>Cpwd For Defence</u>								
485	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD FOR DEFENC, KARNATAKA	12/2016	246.31 210.00	200.00	181.63	02/2020 08/2022	10/2022	32	2
	Total		246.31 -	200.00	181.63				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
486	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	808.62	536.84	07/2022 -	10/2022	3	-
487	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION,ANDHRA PRADESH	02/2019	655.34 -	655.34	469.33	06/2020 -	11/2022	29	-
488	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	375.00	175.10	09/2020 -	11/2022	26	-
489	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR	02/2016	496.18 496.00	460.00	342.91	06/2017 06/2022	12/2022	66	6
490	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB	01/2018	430.00 -	387.83	258.31	05/2020 -	12/2022	31	-
491	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83 -	193.83	64.30	06/2020 -	12/2022	30	-
492	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA	01/2019	790.79 -	790.79	394.21	03/2022 -	01/2023	10	-
493	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION,GOA	05/2019	303.90 334.45	334.45	140.00	03/2020 -	02/2023	35	-
494	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	291.95	03/2021 -	03/2023	24	-
495	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	81.58	05/2022 -	03/2023	10	-
496	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	588.72	281.71	09/2022 -	07/2023	10	-
	Total		5,744.25 -	5,696.45	3,036.24				
	HOME AFFAIRS								
	Cpwd For Mha								
497	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 -	1,679.02	1,036.04	10/2019 -	12/2022	38	-
498	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI	06/2019	277.35 -	290.33	63.23	07/2022 -	06/2023	11	-
499	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL	10/2014	162.88 -	210.83	176.16	04/2018 -	09/2023	65	-

Costing Rs. 150 Crore and above

(August 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		1,659.44 -	2,180.18	1,275.43				
	<u>DPIIT</u>								
	<u>Iicc For Dpiit</u>								
500	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	5,178.00	3,032.83	12/2019 -	01/2023	37	-
	Total		4,773.00 -	5,178.00	3,032.83				
	Grand Total		7,25,850.18	9,01,262.99	5,37,790.06				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(August 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	7,500.00	09/2010 -	09/2024	114.78	168
	Total		3,492.00 -	7,500.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
2	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	09/2021 -	12/2023	38.72	27
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	03/2021 -	03/2025	7.88	48
4	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 -	2,445.00	09/2021 -	09/2023	76.79	24
	Total		2,871.27 -	4,157.33				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
5	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	08/2019 -	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>							
6	ANANTA OCP EXPANSION PH III - [N06000225]	08/2008	228.08 -	314.71	03/2012 -	-	37.98	0
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	868.37	03/2013 -	03/2024	81.09	132
	<u>Neyveli Lignite Corporation</u>							
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	12/2015 -	02/2021	35.10	62
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2023	.00	24
	Total		26,513.45 -	31,548.15				
	<u>DPIIT</u>							
	<u>licc For Dpiit</u>							

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
10	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	01/2023	8.49	37
	Total		4,773.00 -	5,178.00				
	<u>FINANCE</u>							
	<u>Cpwd For Finance</u>							
11	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	262.00	10/2019 -	10/2022	25.36	36
	Total		209.00 -	262.00				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
12	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	04/2021	16.33	38
13	LGBRIMH-TEZPUR, ASSAM - [N21000007]	07/2012	175.57 -	179.15	12/2014 -	03/2018	2.04	39
14	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR [N21000010]	12/2014	168.90 -	191.20	05/2017 -	01/2021	13.20	44
15	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	205.00	- -	01/2022	30.94	0
16	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	12/2021	1.64	39
17	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	05/2021	.02	0
18	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	280.00	03/2019 -	02/2021	2.87	23
19	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI [N21000021]	03/2018	268.84 -	284.67	- -	05/2021	5.89	0
20	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	285.00	05/2017 -	06/2021	39.41	49
21	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32
22	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	586.50	11/2013 -	09/2021	41.63	94
23	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR [N21000011]	09/2014	505.58 -	586.96	03/2018 -	04/2020	16.10	25
	<u>Nbcc For Health</u>							
24	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.04	09/2021 -	08/2022	8.89	11
	Total		4,456.80 -	5,069.51				

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
25	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	210.83	04/2018 -	09/2023	29.44	65
26	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002	06/2019	277.35 -	290.33	07/2022 -	06/2023	4.68	11
27	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,679.02	10/2019 -	12/2022	37.71	38
	Total		1,659.44 -	2,180.18				
	<u>PETROLEUM</u>							
	<u>Gas Authority Of India Limited</u>							
28	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 -	247.90	02/2021 -	10/2022	9.91	20
29	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	08/2020 -	12/2022	14.17	28
	<u>Hindustan Petroleum Corporation Limited</u>							
30	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	07/2020 -	03/2023	25.50	32
	<u>Indian Oil Corporation Limited</u>							
31	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336	03/2018	588.20 -	730.20	- -	03/2023	24.14	0
	<u>Numaligarh Refinery Limited</u>							
32	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379	01/2019	12,366.00 -	18,968.00	10/2024 -	10/2024	53.39	0
	<u>Oil & Natural Gas Corporation Limited</u>							
33	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	05/2019	763.92 -	829.58	12/2020 -	12/2022	8.60	24
	<u>Oil India Limited</u>							
34	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	638.60	02/2020 -	12/2022	17.41	34
	Total		35,701.99 -	48,005.29				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
35	KALPI SOLAR POWER PROJECT - [N18000323	07/2020	314.64 -	337.77	03/2022 -	12/2022	7.35	9
	<u>National Thermal Power Corporation</u>							

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
36	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	10/2021 -	08/2022	11.93	10
37	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 -	524.83	09/2021 -	09/2022	4.70	12
38	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	679.00	11/2018 -	12/2022	28.19	49
39	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 -	852.90	09/2021 -	09/2022	6.85	12
40	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	09/2019 -	07/2025	30.48	70
41	NOKHRA - [N18000282]	03/2020	1,722.14 -	1,803.19	09/2021 -	01/2023	4.71	16
42	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	7,103.00	03/2013 -	12/2024	138.48	141
43	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	11/2020 -	06/2023	3.76	31
44	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	06/2019 -	12/2024	18.38	66
	<u>Power Grid Corporation Of India Limited</u>							
45	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	07/2019 -	12/2022	17.99	41
46	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	04/2022	4.61	65
47	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]	10/2019	1,031.00 -	1,143.00	08/2021 -	10/2022	10.86	14
48	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 -	2,635.55	02/2020 -	04/2023	36.46	38
49	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	07/2020 -	08/2022	14.11	25
50	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	12/2018 -	01/2024	31.08	61
51	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	12/2018 -	03/2024	92.02	63
	<u>Satluj Jal Vidyut Nigam Limited</u>							
52	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	12/2021 -	12/2022	46.20	12
53	BIKANER SOLAR POWER PROJECT - [N18000335]	04/2022	5,491.89 532.00	6,023.89	05/2024 -	05/2024	9.69	0
	<u>Thdc India Limited</u>							
54	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	02/2016 -	10/2023	191.23	92
	Total		58,287.49 -	77,566.99				

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
55	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,384.72	03/2022 -	03/2024	8.85	24
56	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	03/2021 -	03/2025	75.00	48
57	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2025	10.94	24
58	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	03/2023 -	03/2024	8.75	12
59	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	4,670.00	03/2024 -	03/2024	28.74	0
60	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,805.17	03/2021 -	03/2025	111.54	48
	<u>Container Corporation Of India</u>							
61	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	03/2019	.21	0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
62	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT [N22000346]	10/2006	11,589.00 30,357.00	51,219.00	- -	-	341.96	0
	<u>East Central Railways</u>							
63	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	783.83	03/2020 -	03/2025	43.03	60
64	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	1,010.00	03/2019 -	07/2022	48.85	40
65	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,110.00	03/2012 -	06/2023	241.82	135
66	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,510.00	- -	03/2024	358.42	0
67	SAKRI-NIRMALI AND JHANJHARPUR- LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,700.00	- -	03/2024	356.82	0
68	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,800.00	- -	07/2022	267.84	0
	<u>East Coast Railway</u>							
69	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2025	15.45	76
70	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2024	.07	48
71	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	-	38.43	0
72	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	12/2025	29.71	201
	<u>Eastern Railways</u>							

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	12/2022	6.48	0
74	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	- -	03/2023	23.82	0
75	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	402.48	- -	05/2022	39.58	0
76	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	03/2017 -	10/2022	20.30	67
77	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	- -	09/2022	181.63	0
78	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
79	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2023	133.39	12
	<u>Indian Railway Construction Company Limited</u>							
80	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,500.00	09/2018 -	12/2023	14.57	63
81	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2024	117.23	33
	<u>Metropolitan Rapid Transport Projects</u>							
82	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	774.51	06/2013 -	12/2022	56.23	114
83	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2023	501.57	228
84	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	-	75.91	0
	<u>North Central Railway</u>							
85	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
86	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	401.65	- -	03/2023	66.30	0
87	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	03/2020 -	03/2024	94.45	48
88	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	708.73	03/2020 -	09/2022	24.42	30
89	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	983.55	03/2020 -	10/2024	137.09	55
90	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,145.79	03/2019 -	03/2024	197.45	60
91	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,047.51	03/2019 -	12/2023	13.88	57

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
92	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,650.00	03/2019 -	12/2023	397.31	57
93	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	4,059.65	03/2022 -	03/2025	81.86	36
94	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	6,527.45	03/2014 -	12/2023	172.72	117
95	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,663.00	03/2015 -	03/2026	186.39	132
96	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	7,876.92	12/2015 -	12/2023	488.06	96
97	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	8,324.28	03/2021 -	-	818.33	0
98	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.79	03/2011 -	12/2023	221.56	153
	<u>North Eastern Railway</u>							
99	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	-	.16	0
100	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	04/2017 -	10/2022	127.77	66
101	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	800.00	01/2019 -	-	171.19	0
102	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	800.00	- -	12/2023	32.78	0
103	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	2,000.00	03/2022 -	03/2022	54.39	0
	<u>North Western Railway</u>							
104	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	03/2020 -	10/2022	16.97	31
105	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	06/2022	109.82	40
	<u>Northern Railway</u>							
106	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
107	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	- -	09/2023	134.90	0
108	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	12/2011	211.31	0
109	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	03/2023 -	12/2025	369.35	33
110	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	07/2012 -	11/2024	348.44	148
	<u>Rail Vikas Nigam Ltd.</u>							
111	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	03/2009 03/2009	12/2022	224.56	165
112	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	03/2016 -	09/2022	50.15	78

Costing Rs. 150 Crore and above (August 2022)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
113	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,457.79	03/2019 -	03/2023	57.26	48
114	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	943.60 -	1,500.00	03/2022 -	12/2022	58.97	9
115	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	03/2020 -	12/2022	102.11	33
116	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,552.26	03/2019 -	03/2023	64.62	48
117	BINA - KOTA DOUBLING WITH RE - [N22000414	04/2011	1,485.85 -	1,835.83	12/2020 -	09/2022	23.55	21
118	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	2,009.00	03/2020 -	09/2022	111.91	30
119	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	03/2012	1,183.25 -	2,203.53	12/2020 -	09/2022	86.23	21
120	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	1,202.70 -	2,440.53	02/2015 -	09/2022	102.92	91
121	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,548.66 -	2,538.01	12/2021 -	12/2022	63.88	12
122	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,725.00	03/2020 -	07/2022	281.93	28
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
124	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	3,300.00	03/2023 -	03/2023	55.15	0
125	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
126	VIJAYAWADA-GUDUR - [N22000369	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
127	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	3,633.12	03/2020 -	06/2022	141.61	27
128	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2026	7.78	120
129	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,834.54	03/2016 -	07/2025	65.94	112
130	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	6,753.42	12/2026 -	03/2025	127.62	-21
131	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	24,659.00	12/2024 -	03/2025	52.07	3
	<u>South Central Railway</u>							
132	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	242.28	03/2022 -	-	102.36	0

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
133	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2025	5.16	24
134	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2027	102.85	216
135	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	2,250.00	03/2010 -	03/2025	93.89	180
136	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
137	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2025	7.06	36
	<u>South East Central Railway</u>							
138	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
139	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	12/2021 -	12/2023	.07	24
140	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,176.60	03/2023 -	12/2023	66.44	9
	<u>South Eastern Railway</u>							
141	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 -	393.83	06/2022 -	12/2023	16.52	18
142	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 -	472.50	06/2022 -	12/2025	10.23	42
143	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39 -	511.75	12/2021 -	01/2023	31.09	13
144	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.97	03/2020 -	10/2022	35.38	31
	<u>South Western Railway</u>							
145	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	03/2016 -	12/2026	55.13	129
146	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	03/2019 -	02/2024	16.31	59
147	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,954.21	03/2020 -	12/2022	68.91	33
148	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	2,000.97	- -	03/2025	11.10	0
149	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,404.03	- -	12/2025	16.57	0
150	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	- -	03/2028	123.51	0
	<u>Southern Railway</u>							
151	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	591.00	- -	09/2022	259.47	0
152	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	- -	03/2025	33.90	0
153	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,084.48	03/2019 -	12/2027	1,626.99	105

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
154	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	3,081.20	02/2019 -	03/2025	325.17	73
155	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,500.79	- -	12/2025	500.65	0
	<u>West Central Railway</u>							
156	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2024	114.32	30
157	RAMGANJMUHDI-BHOPAL (NL), WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2024	585.35	36
158	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>							
159	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]	03/2010	265.88 -	311.36	- -	03/2024	17.11	0
160	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]	03/2012	217.38 -	393.62	- -	03/2024	81.07	0
161	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]	03/2012	248.26 -	528.49	- -	03/2024	112.88	0
162	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	04/2018	537.31 -	584.31	03/2024 -	12/2024	8.75	9
163	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	04/2016	700.00 -	640.75	06/2020 -	03/2023	-8.46	33
164	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	1,083.17	03/2012 -	03/2024	240.36	144
165	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,119.12	03/2021 -	12/2022	11.65	21
166	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,394.02	03/2021 -	12/2022	34.41	21
167	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,448.99	03/2020 -	03/2024	195.15	48
168	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,383.82	03/2022 -	03/2026	82.20	48
	Total		1,61,272.48 -	3,37,599.09				
	<u>RENEWABLE ENERGY</u>							
	<u>Cpwd For Renewable Energy</u>							
169	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	365.00	11/2019 -	-	34.24	0
	Total		271.90 -	365.00				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
170	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	174.90	08/2018 -	10/2022	5.23	50
171	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00	177.84	12/2019 -	11/2020	.00	11
172	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00	189.46	12/2019 -	06/2022	.00	30
173	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00	194.23	02/2020 -	01/2021	.00	11
174	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00	203.21	05/2019 -	09/2019	.00	4
175	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	08/2019 -	03/2023	33.51	43
176	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00	217.14	02/2020 -	06/2021	.00	16
177	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00	222.13	11/2019 -	02/2022	.00	27
178	KUNDRAI TO WAZAR - [N24001077]	01/2018	225.25 225.00	225.25	12/2019 -	12/2020	.00	12
179	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	08/2018 -	10/2022	4.45	50
180	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00	227.19	12/2019 -	03/2022	.00	27
181	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	01/2017	197.67 -	236.18	12/2022 -	12/2022	19.48	0
182	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	10/2022	.08	35
183	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00	238.19	12/2019 -	03/2022	.00	27
184	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00	240.30	01/2020 -	-	.00	0
185	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]	03/2018	240.38 -	240.38	06/2019 -	-	.00	0
186	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]	03/2018	159.97 -	242.61	06/2019 -	03/2023	51.66	45
187	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00	244.04	03/2019 -	12/2021	.00	33
188	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00	257.38	12/2019 -	03/2022	.00	27
189	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	08/2019 -	03/2023	11.18	43

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
190	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156	01/2017	166.67 -	264.34	09/2017 -	07/2022	58.60	58
191	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00	264.41	03/2019 -	03/2022	.00	36
192	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	09/2021	.00	21
193	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	01/2020	3.72	0
194	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	11/2020	.31	16
195	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	09/2022	.00	25
196	MALEGAON TO RISOD - [N24001089	02/2018	303.24 303.00	303.24	12/2019 -	10/2020	.00	10
197	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 -	318.28	01/2019 -	07/2022	7.06	42
198	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 -	319.96	- -	09/2022	13.68	0
199	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	01/2014	282.41 -	319.96	03/2016 -	07/2022	13.30	76
200	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	-	72.36	0
201	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	03/2020	.00	10
202	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J - [N24001208	03/2018	288.30 -	323.36	08/2020 -	10/2022	12.16	26
203	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	03/2022	.00	27
204	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	12/2020	.00	12
205	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	12/2020	.00	18
206	OSMANNAGAR TO KUNDRAL - [N24001075	09/2017	344.25 344.00	344.25	08/2020 -	06/2022	.00	22
207	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	03/2022	.00	27
208	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	12/2015 -	01/2021	6.07	61
209	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	369.96	09/2019 -	11/2020	10.03	14
210	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	11/2020	.00	18

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
211	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00	381.08	05/2020 -	12/2022	.00	31
212	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	03/2018	325.86 -	386.41	10/2018 -	04/2021	18.58	30
213	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	05/2017 -	06/2022	45.75	61
214	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00	391.06	06/2019 -	03/2022	.00	33
215	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00	393.10	12/2019 -	12/2020	.00	12
216	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00	404.33	05/2020 -	12/2022	.00	31
217	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00	407.19	06/2019 -	09/2022	.00	39
218	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI [N24001056]	02/2017	422.02 422.00	422.02	07/2019 -	03/2022	.00	32
219	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	06/2020 -	06/2022	.00	24
220	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	03/2018 -	10/2022	9.23	55
221	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06	0
222	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	03/2018	504.19 504.00	504.19	11/2018 -	01/2022	.00	38
223	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00	548.03	06/2019 -	01/2020	.00	7
224	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	08/2016 -	12/2022	15.19	76
225	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	10/2016 -	12/2022	17.04	74
226	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00	743.21	06/2021 -	09/2022	.00	15
227	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	- -	-	1.75	0
228	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]	03/2016	877.79 -	949.54	06/2019 -	09/2022	8.17	39
229	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00	995.09	05/2016 -	11/2022	.00	78
230	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	12/2022	.00	37

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
231	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	06/2022	.00	31
232	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	- -	12/2021	2.93	0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
233	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	04/2017 -	08/2022	27.16	64
234	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	04/2017 -	11/2022	29.48	67
235	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	03/2015	168.39 -	259.79	11/2018 -	08/2022	54.28	45
236	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	04/2017 -	10/2022	29.48	66
237	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583	01/2016	252.00 -	330.30	01/2016 -	12/2022	31.07	83
238	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582	01/2016	294.17 -	385.57	01/2016 -	07/2022	31.07	78
239	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	08/2016 -	-	3.73	0
240	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	530.67	10/2017 -	06/2022	36.77	56
241	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	06/2015	463.49 -	801.54	06/2018 -	03/2023	72.94	57
242	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	05/2015	454.89 -	814.56	05/2018 -	07/2022	79.07	50
243	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	873.91	11/2018 -	09/2022	48.38	46
244	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823	03/2015	829.00 -	1,307.50	01/2016 -	06/2023	57.72	89
	<u>National Highways Authority Of India</u>							
245	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	- -	03/2023	.99	0
246	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 -	355.24	08/2018 -	05/2022	9.74	45
247	SIX LANNING FROM EXISTING KM 494.410 (DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550 (DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	359.60	- -	09/2022	23.69	0
248	INDORE-DEWAS (NH-3) - [N24000159	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
249	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594	07/2016	458.03 -	486.00	- -	06/2022	6.11	0
250	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	- -	06/2023	8.26	0
251	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	11/2013 -	05/2022	15.53	102
252	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	11/2019 -	12/2022	2.02	37
253	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480	12/2015	1,041.10 -	639.58	04/2019 -	12/2022	-38.57	44
254	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	08/2015	516.13 -	649.27	04/2018 -	01/2021	25.80	33
255	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299	09/2018	617.41 -	668.45	02/2019 -	05/2022	8.27	39
256	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	- -	12/2022	6.11	0
257	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	717.24	05/2018 -	06/2022	20.90	49
258	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723	01/2018	573.70 -	726.99	- -	06/2023	26.72	0
259	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 -	732.34	11/2019 -	12/2022	.06	37
260	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828	03/2018	633.55 -	736.33	- -	08/2023	16.22	0
261	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	- -	08/2022	.00	0
262	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	777.03	05/2018 -	12/2022	46.30	55
263	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	- -	06/2022	25.68	0
264	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	- -	09/2022	1.37	0
265	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	830.31	03/2020 -	03/2023	23.39	36
266	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	- -	11/2022	27.86	0

Costing Rs. 150 Crore and above (August 2022)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
267	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	- -	10/2022	305.58	0
268	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	922.64	- -	04/2022	15.98	0
269	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	925.96	- -	02/2022	45.89	0
270	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	04/2020 -	12/2022	3.95	32
271	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	- -	01/2020	11.33	0
272	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	07/2024	31.88	52
273	MEERUT-BULANDSHAHAH - [N24000539	01/2016	683.24 -	987.94	- -	03/2022	44.60	0
274	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521	08/2015	854.80 -	1,038.56	- -	05/2022	21.50	0
275	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	06/2022	1.06	63
276	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	08/2019 -	06/2022	16.55	34
277	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	03/2018	478.74 -	1,135.08	- -	11/2022	137.10	0
278	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	08/2017	950.64 -	1,168.33	08/2017 -	08/2023	22.90	72
279	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2022	41.54	27
280	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507	12/2015	1,167.45 -	1,182.94	- -	03/2023	1.33	0
281	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2022	13.97	24
282	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703	10/2017	964.17 -	1,198.64	10/2017 -	05/2022	24.32	55
283	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12	0
284	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,308.88	- -	12/2022	28.71	0

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
285	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,309.79	09/2017 -	03/2023	16.52	66
286	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	09/2022	10.58	30
287	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 -	1,321.60	02/2021 -	02/2023	7.72	24
288	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
289	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	01/2017	1,251.11 -	1,361.00	- -	09/2022	8.78	0
290	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,361.00	- -	09/2022	29.35	0
291	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	03/2017	1,373.28 -	1,405.27	03/2020 -	08/2022	2.33	29
292	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2022	10.24	24
293	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,422.13	- -	12/2022	21.94	0
294	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2022	44.39	27
295	FOUR LANING OF PARWANOO -SOLAN - [N24000479	09/2015	934.46 -	1,543.51	03/2018 -	12/2022	65.18	57
296	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	1,588.29	09/2019 -	05/2022	14.40	32
297	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	1,827.00	03/2021 -	08/2022	19.21	17
298	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	01/2024	4.99	0
299	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 -	2,280.00	- -	05/2021	94.94	0
300	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 -	2,360.65	- -	12/2023	41.78	0
301	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	10/2022	20.28	0
302	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	09/2022	12.50	0
303	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105

Costing Rs. 150 Crore and above

(August 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
304	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	07/2020	3,426.00 -	5,852.00	12/2021 -	-	70.81	0
305	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	16,732.70	- -	07/2022	1,524.60	0
	Total		89,831.29 -	1,22,721.17				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
306	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,925.22	12/2018 -	09/2022	19.98	45
	<u>Central Public Works Department</u>							
307	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	06/2015	197.33 -	220.00	04/2019 -	-	11.49	36
	<u>Chennai Metro Rail Ltd</u>							
308	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	18,380.00	12/2015 -	-	25.89	0
	<u>Delhi Metro Rail Corporation</u>							
309	DELHI MRTS PHASE-III - [N28000056	09/2011	38,585.00 -	40,180.91	03/2016 -	-	4.14	0
	<u>Kochi Metro Rail Corporation Ltd</u>							
310	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	6,218.14	07/2017 -	-	20.00	0
	<u>Mumbai Metro Rail Corporation Ltd</u>							
311	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	33,406.00	03/2020 -	12/2023	44.39	45
	<u>Nagpur Metro Rail Corporation Ltd</u>							
312	NAGPUR METRO RAIL - [N28000085	08/2014	8,680.00 -	9,759.79	03/2018 -	03/2022	12.44	48
	<u>Patna Metro Rail Corporation</u>							
313	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	02/2019	13,365.77 -	13,925.50	06/2024 -	06/2024	4.19	0
	Total		1,14,518.89 -	1,35,015.56				
	Grand Total		5,03,859.00	7,77,168.27				

North East Projects Costing Rs.150 crore and above (as on					31.08.2022)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (3/2023) [3/2023]	645.63 (-) [645.63]	519.30 (0.00) [7]
	<u>Power</u>				
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	16,222.78 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
3	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	3/2027 (-) [3/2027]	496.47 (-) [496.47]	32.23 (0.00) [0]
4	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [3/2022]	243.89 (-) [243.89]	232.72 (0.00) [0]
5	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	3/2027 (-) [3/2027]	437.60 (-) [437.60]	41.92 (0.00) [0]
6	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	176.69 (0.00) [0]
7	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	141.82 (0.00) [0]
8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	3/2027 (-) [3/2027]	403.68 (-) [403.68]	224.20 (0.00) [0]
9	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	3/2027 (-) [3/2027]	543.05 (-) [543.05]	241.22 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	3/2027 (-) [3/2027]	450.65 (-) [450.65]	117.78 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	3/2027 (-) [3/2027]	486.70 (-) [486.70]	201.16 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	3/2027 (-) [3/2027]	560.39 (-) [560.39]	307.44 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	3/2027 (-) [3/2027]	347.78 (-) [347.78]	223.07 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	3/2027 (-) [3/2027]	394.27 (-) [394.27]	158.24 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95	3/2019	3/2027 (-)	342.55 (-)	264.65 (0.00)

	(PACKAGE 2		[3/2027]	[342.55]	[0]
16	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	3/2027 (-) [3/2027]	421.48 (-) [421.48]	147.23 (0.00) [0]
17	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [12/2022]	200.44 (-) [200.44]	135.92 (0.00) [-]
18	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [3/2023]	568.92 (-) [568.92]	390.60 (0.00) [-]
19	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [12/2022]	188.78 (-) [188.78]	142.23 (0.00) [-]
20	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [9/2022]	245.79 (-) [245.79]	224.65 (0.00) [-]
21	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	0.00 (0.00) [0]
22	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [3/2024]	1,718.59 (-) [1,718.59]	543.26 (0.00) [-]
23	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [1/2023]	301.06 (-) [301.06]	45.78 (0.00) [9]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [1/2023]	353.90 (-) [353.90]	34.28 (0.00) [8]
25	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [4/2017]	167.28 (-) [167.28]	0.00 (0.00) [0]
26	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	167.37 (0.00) [0]
27	DOGINALA - GAU	12/2020	9/2022 (-) [4/2023]	242.30 (-) [242.30]	15.04 (0.00) [7]
28	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
29	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (4/2022) [12/2022]	228.71 (-) [228.71]	67.40 (0.00) [8]
30	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (12/2022) [12/2022]	294.04 (-) [294.04]	109.59 (0.00) [8]
31	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (12/2022) [12/2022]	199.03 (-) [199.03]	70.58 (0.00) [8]
32	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (12/2022) [12/2022]	184.88 (-) [184.88]	57.76 (0.00) [8]
33	LADDA - BASAI	2/2021	4/2023 (-) [2/2024]	445.96 (-) [445.96]	2.94 (0.00) [10]
34	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	24.48 (0.00) [0]
35	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [12/2022]	284.09 (-) [284.09]	188.40 (0.00) [68]

36	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [11/2022]	195.23 (-) [252.79]	180.00 (57.56) [67]
37	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST]	2/2017	4/2017 (-) [10/2022]	203.36 (-) [263.31]	172.68 (59.95) [66]
38	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [8/2022]	198.22 (-) [252.05]	171.06 (53.83) [64]
39	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX]	2/2017	4/2017 (11/2023) [11/2023]	180.57 (244.10) [180.57]	18.01 (0.00) [79]
40	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [3/2024]	256.66 (-) [256.66]	0.00 (0.00) [-]
41	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (12/2021) [12/2021]	1,979.00 (-) [2,036.90]	1,251.08 (57.90) [0]
42	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	3/2027 (-) [3/2027]	182.55 (-) [182.55]	24.82 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
43	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2025]	1,142.00 (-) [1,232.00]	426.51 (90.00) [48]
	<u>Health And Family Welfare</u>				
44	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (890.14) [860.00]	528.81 (-15.00) [0]
45	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [179.15]	179.15 (3.58) [0]
	<u>Petroleum</u>				
46	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (12/2022) [12/2022]	543.91 (-) [638.60]	423.10 (94.69) [34]
47	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	49.33 (0.00) [0]
48	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [2/2023]	218.38 (-) [218.38]	35.16 (0.00) [0]
49	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	1,929.71 (6,602.00) [0]
50	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	3,273.73 (-1,170.00) [0]
51	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING	12/2020	7/2024 (-) [7/2024]	430.76 (-) [430.76]	8.66 (0.00) [0]
52	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM	3/2022	7/2026 (-) [7/2026]	277.00 (-) [277.00]	0.00 (0.00) [0]
53	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT	6/2021	12/2024 (-) [12/2024]	860.00 (-) [860.00]	20.10 (0.00) [0]
	<u>Power</u>				
54	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C	3/2019	3/2023 (-)	1,326.00 (-)	1,054.46 (0.00)

			[3/2023]	[1,326.00]	[0]
	Railways				
55	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2025]	2,232.32 (-) [4,059.65]	2,380.05 (1,827.33) [36]
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2024]	385.20 (-) [1,145.79]	990.86 (760.59) [60]
	Road Transport And Highways				
57	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (6/2022) [6/2022]	268.08 (-) [390.73]	386.57 (122.65) [0]
58	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [3/2023]	261.13 (-) [261.13]	45.67 (0.00) [9]
59	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	46.43 (0.00) [0]
60	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [12/2022]	216.49 (-) [216.49]	65.59 (0.00) [9]
61	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [11/2022]	520.01 (-) [520.01]	214.57 (0.00) [-]
62	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [9/2022]	588.95 (-) [873.91]	559.13 (284.96) [46]
63	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2022]	289.99 (-) [289.99]	120.17 (0.00) [48]
64	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [12/2022]	252.00 (-) [330.30]	141.13 (78.30) [83]
65	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [6/2018]	437.39 (-) [437.39]	0.00 (0.00) [0]
66	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [7/2022]	294.17 (-) [385.57]	229.26 (91.40) [0]
67	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	364.26 (0.00) [0]
68	4-LANING OF DERGAON TOWN	3/2020	6/2022 (-) [6/2022]	287.63 (-) [287.63]	89.55 (0.00) [0]
69	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	52.00 (0.00) [0]
70	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146	12/2021	8/2024 (-) [8/2024]	300.00 (-) [300.00]	29.81 (0.00) [0]
71	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	93.86 (0.00) [0]
72	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	2.54 (0.00) [0]
73	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2023]	335.88 (-) [335.88]	70.36 (0.00) [-12]
74	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023	260.07	109.24

			(-) [12/2022]	(-) [260.07]	(0.00) [-12]
75	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	8.28 (0.00) [0]
76	DABOKA KATHKATI PACKAGE-6	9/2021	7/2024 (-) [7/2024]	625.64 (-) [625.64]	0.00 (0.00) [0]
77	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1	3/2022	7/2024 (-) [7/2024]	215.27 (-) [215.27]	0.00 (0.00) [0]
78	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2	4/2022	7/2024 (-) [7/2024]	170.95 (-) [170.95]	0.00 (0.00) [0]
79	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [8/2022]	168.39 (-) [259.79]	158.07 (91.40) [45]
80	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [4/2023]	818.00 (-) [818.00]	350.68 (0.00) [-]
81	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [3/2023]	463.49 (-) [801.54]	185.26 (338.05) [57]
82	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [6/2023]	829.00 (-) [1,307.50]	411.51 (478.50) [89]
83	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [7/2022]	454.89 (-) [814.56]	391.87 (359.67) [0]
84	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	188.31 (0.00) [0]
85	JOGIGHOPA BRIDGE	8/2021	11/2024 (-) [11/2024]	746.76 (-) [746.76]	9.76 (0.00) [0]
86	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	98.01 (0.00) [0]
87	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (12/2022) [12/2022]	160.00 (-) [160.00]	138.51 (0.00) [15]
88	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [1/2023]	636.42 (-) [418.49]	96.45 (-217.93) [1]
89	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
90	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	256.92 (0.00) [0]
91	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2023]	208.84 (-) [208.84]	27.93 (0.00) [12]
92	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [11/2022]	278.46 (-) [278.46]	120.18 (0.00) [8]
	<u>MANIPUR</u>				
	<u>Railways</u>				
93	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [14,322.79]	12,817.81 (9,868.62) [153]

	Road Transport And Highways				
94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [12/2022]	167.95 (-) [167.95]	77.77 (0.00) [6]
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [12/2022]	292.24 (-) [292.24]	98.42 (0.00) [6]
96	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [12/2022]	365.53 (-) [365.53]	118.82 (0.00) [4]
97	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [12/2022]	167.95 (-) [167.95]	77.72 (0.00) [6]
98	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [11/2022]	177.76 (-) [177.76]	70.23 (0.00) [3]
99	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [8/2023]	673.27 (-) [673.27]	106.28 (0.00) [-2]
100	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	21.30 (0.00) [0]
101	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [9/2023]	467.00 (-) [467.00]	50.90 (0.00) [6]
102	IMPHAL - KHONGSANG PKG-4	8/2021	12/2023 (-) [12/2023]	579.63 (-) [579.63]	0.00 (0.00) [0]
103	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	46.79 (0.00) [0]
104	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	112.33 (0.00) [0]
105	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [0/0]	268.98 (-) [268.98]	22.08 (0.00) [0]
106	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [0/0]	228.97 (-) [228.97]	0.00 (0.00) [0]
107	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [2/2023]	379.39 (-) [379.39]	22.07 (0.00) [10]
108	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [3/2023]	471.00 (-) [471.00]	251.05 (0.00) [8]
109	MARAM - PEREN PKG-3	8/2021	5/2023 (-) [11/2023]	467.41 (-) [467.41]	20.74 (0.00) [6]
110	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	45.41 (0.00) [0]
111	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	68.82 (0.00) [0]
112	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	13.88 (0.00) [0]
113	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	27.58 (0.00) [0]

114	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]
115	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	14.79 (0.00) [0]
116	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	58.46 (0.00) [0]
117	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [4/2023]	234.08 (-) [234.08]	32.64 (0.00) [4]
118	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	16.45 (0.00) [0]
119	TAMENGLONG - MAHUR PKG-5	8/2021	5/2023 (-) [5/2023]	477.86 (-) [477.86]	14.26 (0.00) [0]
120	TAMENGLONG - MAHUR PKG-6	9/2021	5/2023 (-) [5/2023]	311.18 (-) [311.18]	22.84 (0.00) [0]
	<u>MEGHALAYA</u>				
	<u>Department Of Higher Education</u>				
121	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (12/2022) [12/2022]	484.32 (429.70) [429.70]	242.25 (-54.62) [99]
	<u>Doner</u>				
122	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	148.33 (0.00) [0]
	<u>Health And Family Welfare</u>				
123	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [6/2022]	363.99 (-) [363.99]	299.13 (0.00) [0]
	<u>Railways</u>				
124	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [8,324.28]	266.07 (7,417.82) [0]
	<u>Road Transport And Highways</u>				
125	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.79 (0.00) [0]
126	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [9/2022]	306.28 (-) [306.28]	165.99 (0.00) [40]
127	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	44.52 (0.00) [0]
128	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	327.61 (0.00) [0]
129	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	175.18 (0.00) [0]
130	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	87.95 (0.00) [0]
131	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2023]	157.86 (-) [157.86]	81.82 (0.00) [12]
132	REHABILITATION AND UPGRADATION OF NONGSTOIN	8/2020	2/2022	302.88	9.20

	TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06		(-) [0/0]	(-) [302.88]	(0.00) [0]
133	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [11/2022]	553.51 (-) [553.51]	232.58 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
134	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [12/2023]	2,393.47 (-) [6,527.45]	5,330.91 (4,133.98) [117]
	<u>Road Transport And Highways</u>				
135	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [4/2022]	205.95 (-) [205.95]	164.98 (0.00) [0]
136	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2022) [0/0]	195.04 (434.65) [377.99]	400.65 (182.95) [0]
137	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (10/2022) [0/0]	186.96 (-) [322.24]	312.50 (135.28) [0]
138	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2022) [0/0]	193.69 (374.59) [327.92]	347.48 (134.23) [0]
139	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	60.68 (0.00) [0]
140	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	81.09 (0.00) [0]
141	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	134.55 (0.00) [0]
142	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	98.32 (0.00) [0]
143	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	163.52 (0.00) [0]
144	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	129.85 (0.00) [0]
145	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	52.09 (0.00) [0]
146	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	163.89 (0.00) [0]
147	KEIFANG - TUVAI PKG-1	9/2021	5/2023 (-) [5/2023]	492.94 (-) [492.94]	19.53 (0.00) [0]
148	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	36.21 (0.00) [0]
149	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	33.38 (0.00) [0]
150	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	220.92 (0.00) [43]
151	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC	4/2017	9/2019 (-)	473.18 (-)	201.83 (0.00)

	IMPROVEMENTS FRO		[4/2023]	[473.18]	[43]
152	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	237.48 (0.00) [43]
153	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	145.96 (0.00) [55]
154	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	182.20 (0.00) [48]
155	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	234.73 (0.00) [45]
156	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	271.82 (0.00) [46]
157	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	234.97 (0.00) [45]
158	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2022) [0/0]	624.41 (1,109.88) [992.67]	1,021.46 (368.26) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
159	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	1,781.77 (4,336.48) [132]
	<u>Road Transport And Highways</u>				
160	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	137.74 (0.00) [0]
161	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	119.22 (0.00) [48]
162	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	195.15 (0.00) [0]
163	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	365.94 (0.00) [0]
164	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	199.63 (0.00) [50]
165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	94.03 (0.00) [0]
166	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	96.39 (0.00) [0]
167	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	64.96 (0.00) [0]
168	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [0/0]	330.78 (-) [330.78]	98.59 (0.00) [0]
169	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [0/0]	330.80 (-) [330.80]	63.26 (0.00) [0]
170	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [10/2022]	278.95 (-) [278.95]	128.23 (0.00) [4]

171	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [12/2022]	206.53 (-) [206.53]	95.95 (0.00) [6]
172	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (12/2022) [9/2022]	217.35 (-) [217.35]	173.98 (0.00) [22]
173	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	84.56 (0.00) [0]
174	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [6/2023]	202.36 (-) [202.36]	15.41 (0.00) [14]
175	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [12/2023]	277.44 (-) [277.44]	55.34 (0.00) [14]
176	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	212.37 (0.00) [0]
177	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	141.12 (0.00) [0]
178	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	136.85 (0.00) [0]
179	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [6/2022]	215.12 (-) [215.12]	127.87 (0.00) [0]
180	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2022]	215.79 (-) [215.79]	86.37 (0.00) [51]
181	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [6/2023]	272.89 (-) [272.89]	103.64 (0.00) [57]
182	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [9/2018]	323.98 (-) [323.98]	0.00 (0.00) [0]
183	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	157.06 (0.00) [0]
184	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	134.89 (0.00) [0]
185	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [0/0]	373.07 (-) [387.00]	364.31 (13.93) [0]
186	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [0/0]	396.52 (-) [396.52]	321.87 (0.00) [0]
187	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2016]	429.52 (-) [429.52]	0.00 (0.00) [0]
188	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [11/2020]	336.25 (-) [369.96]	309.98 (33.71) [0]
189	MERANGKONG-TAMLU-MON (MTM) PKG-5	7/2021	12/2023 (-) [12/2023]	161.73 (-) [161.73]	11.38 (0.00) [0]
190	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	0.00 (0.00) [0]
191	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023	258.52	52.94

			(-) [3/2023]	(-) [258.52]	(0.00) [0]
192	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	167.62 (-) [167.62]	142.40 (0.00) [0]
193	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]
194	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [3/2023]	315.63 (-) [315.63]	12.23 (0.00) [11]
195	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	174.77 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Power</u>				
196	RANGIT IV HE PROJECT	3/2021	5/2024 (8/2024) [8/2024]	938.29 (938.29) [938.29]	315.06 (0.00) [3]
197	TEESTA VI HE PROJECT	3/2019	3/2024 (-) [7/2025]	5,748.04 (-) [5,748.04]	1,748.06 (0.00) [16]
	<u>Railways</u>				
198	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [7,876.92]	3,408.77 (6,537.44) [96]
	<u>Road Transport And Highways</u>				
199	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (9/2023) [9/2023]	230.45 (-) [230.45]	32.58 (0.00) [5]
200	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [5/2024]	493.42 (-) [493.42]	12.26 (0.00) [6]
201	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	50.95 (0.00) [0]
202	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	115.75 (0.00) [0]
203	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [12/2022]	183.31 (-) [183.31]	87.22 (0.00) [7]
204	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [1/2024]	262.84 (-) [262.84]	129.59 (0.00) [8]
205	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM)	10/2021	5/2024 (-) [5/2024]	385.15 (-) [385.15]	8.95 (0.00) [0]
206	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [4/2023]	375.80 (-) [375.80]	96.70 (0.00) [-]
207	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [9/2022]	290.05 (-) [290.05]	175.49 (0.00) [58]
208	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (11/2024) [11/2024]	816.79 (-) [816.79]	15.85 (0.00) [11]
209	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	62.92 (0.00) [0]
210	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY	3/2019	4/2022	402.94	118.12

	TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N		(-) [5/2023]	(-) [402.94]	(0.00) [13]
211	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	84.58 (0.00) [0]
212	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [12/2022]	242.97 (-) [242.97]	68.35 (0.00) [6]
213	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [12/2022]	292.80 (-) [292.80]	52.83 (0.00) [7]
214	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (6/2022) [6/2022]	388.00 (447.37) [530.67]	316.99 (142.67) [0]
215	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	19.69 (0.00) [0]
216	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (2/2024) [2/2024]	410.60 (-) [410.60]	21.94 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
217	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2021) [12/2021]	438.28 (-) [402.00]	405.76 (-36.28) [0]
	<u>Petroleum</u>				
218	CREATION OF GAS DEHYDRATION FACILITIES	3/2022	5/2024 (-) [5/2024]	209.33 (-) [209.33]	0.00 (0.00) [0]
	<u>Railways</u>				
219	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [9/2022]	569.63 (-) [708.73]	380.92 (139.10) [30]
	<u>Road Transport And Highways</u>				
220	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [12/2022]	201.99 (-) [201.99]	49.65 (0.00) [11]
221	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [10/2022]	247.76 (-) [247.76]	67.01 (0.00) [9]
222	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (8/2022) [8/2022]	347.36 (-) [347.36]	154.53 (0.00) [7]
223	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [10/2022]	173.17 (-) [173.17]	21.34 (0.00) [6]
224	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [1/2023]	165.54 (-) [165.54]	37.19 (0.00) [6]
225	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (2/2023) [7/2022]	206.78 (-) [206.78]	43.98 (0.00) [0]
226	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [12/2022]	280.91 (-) [280.91]	148.65 (0.00) [5]
227	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [12/2022]	159.13 (-) [159.13]	30.58 (0.00) [6]
228	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (11/2022) [12/2022]	332.14 (-) [332.14]	56.56 (0.00) [5]

229	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	24.72 (0.00) [0]
230	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (3/2023) [3/2023]	178.43 (-) [178.43]	28.82 (0.00) [8]
231	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (3/2023) [7/2022]	154.51 (-) [154.51]	11.92 (0.00) [0]
232	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [0/0]	277.50 (-) [277.50]	140.76 (0.00) [0]
233	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	107.81 (38.51) [0]
234	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	136.98 (0.00) [0]
	Total			1,36,889.35 (26,063.48) [1,94,037.96]	81,597.21 (57,148.61)

State Wise Projects Costing Rs.150 crore and above (as on					31.08.2022)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (10/2022) [10/2022]	417.23 (707.73) [707.73]	570.11 (290.50) [49]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [3/2022]	409.85 (-) [409.85]	70.00 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	260.08 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	159.49 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [3/2023]	262.97 (-) [262.97]	30.00 (0.00) [53]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	257.34 (-) [238.00]	214.90 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [12/2022]	391.00 (-) [391.00]	22.17 (0.00) [50]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [6/2022]	234.27 (-) [234.27]	11.03 (0.00) [0]
9	REHABILITATION OF SECTION FROM KM 298.00 TO KM 330.662 PKG-8	4/2021	7/2023 (-) [7/2023]	154.61 (-) [154.61]	0.00 (0.00) [0]
10	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [10/2022]	237.80 (-) [238.00]	94.55 (0.20) [35]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
11	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [7/2023]	611.80 (-) [611.80]	167.35 (0.00) [4]
12	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (12/2022) [12/2022]	177.10 (-) [177.10]	137.92 (0.00) [34]
	<u>Department Of Higher Education</u>				
13	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC	9/2019	9/2022 (-) [7/2023]	588.72 (-) [588.72]	281.71 (0.00) [10]
14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [11/2022]	655.34 (-) [655.34]	469.33 (0.00) [29]

	<u>Health And Family Welfare</u>				
15	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [7/2022]	601.02 (-) [601.02]	578.84 (0.00) [0]
16	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [2/2021]	272.19 (-) [280.00]	268.59 (7.81) [0]
	<u>Petroleum</u>				
17	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	8/2027 (3/2030) [3/2030]	2,880.00 (-) [2,880.00]	139.21 (0.00) [31]
18	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (9/2022) [9/2022]	466.00 (-) [466.00]	343.45 (0.00) [17]
19	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [3/2023]	580.20 (-) [580.20]	393.95 (0.00) [25]
20	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY	9/2021	6/2024 (-) [6/2024]	160.00 (-) [160.00]	0.13 (0.00) [0]
21	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (5/2023) [5/2023]	34,012.00 (-) [31,040.00]	19,243.11 (-2,972.00) [35]
22	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (6/2023) [6/2023]	167.00 (-) [167.00]	47.33 (0.00) [11]
23	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	150.41 (0.00) [10]
24	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (9/2022) [9/2022]	316.20 (-) [316.20]	183.14 (0.00) [11]
25	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [3/2023]	332.61 (-) [332.61]	32.33 (0.00) [4]
26	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [12/2022]	210.94 (-) [210.94]	139.97 (0.00) [16]
27	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [0/0]	196.26 (-) [196.26]	125.93 (0.00) [0]
28	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [3/2023]	20,928.00 (-) [26,264.00]	20,025.46 (5,336.00) [32]
	<u>Railways</u>				
29	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2025]	3,631.00 (-) [3,887.48]	1,755.92 (256.48) [36]
30	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2027]	1,045.20 (-) [2,120.16]	1,095.80 (1,074.96) [216]
31	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2026]	2,499.71 (-) [2,499.71]	992.84 (0.00) [48]
32	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [3/2019]	234.50 (-) [235.00]	14.14 (0.50) [0]
33	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2026]	2,288.70 (-) [2,288.70]	1,274.68 (0.00) [60]
34	VIJAYAWADA-GUDUR	4/2015	12/2023	3,246.26	4,099.98

			(-) [12/2023]	(-) [3,548.68]	(302.42) [0]
35	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [6/2022]	1,503.71 (-) [3,633.12]	4,271.59 (2,129.41) [0]
	<u>Road Transport And Highways</u>				
36	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (7/2021) [0/0]	328.67 (416.07) [416.07]	330.31 (87.40) [0]
37	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (4/2021) [2/2023]	1,226.88 (1,240.13) [1,321.60]	678.20 (94.72) [24]
38	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021 (-) [7/2024]	1,601.10 (-) [1,601.10]	612.83 (0.00) [41]
39	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [5/2022]	357.00 (-) [357.00]	0.00 (0.00) [0]
40	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [5/2022]	557.30 (-) [557.30]	460.93 (0.00) [0]
41	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (12/2022) [12/2022]	263.45 (263.45) [263.45]	127.85 (0.00) [63]
42	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (6/2022) [6/2022]	429.43 (373.05) [373.05]	338.66 (-56.38) [0]
43	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [6/2022]	314.43 (-) [314.43]	85.61 (0.00) [0]
44	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (12/2022) [12/2022]	350.61 (-) [350.61]	325.56 (0.00) [71]
45	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (1/2021) [1/2021]	333.21 (-) [353.43]	341.76 (20.22) [0]
46	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [8/2022]	1,532.62 (-) [1,827.00]	1,306.69 (294.38) [17]
47	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (12/2022) [12/2022]	576.48 (686.13) [686.13]	503.77 (109.65) [59]
48	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (6/2022) [6/2022]	348.95 (-) [348.95]	274.08 (0.00) [0]
49	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	3/2020	3/2021 (4/2022) [4/2022]	207.79 (-) [207.79]	134.98 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (7/2022) [7/2022]	386.09 (316.06) [316.06]	224.62 (-70.03) [0]
51	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (8/2022) [8/2022]	290.15 (290.15) [290.15]	188.56 (0.00) [63]
52	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [11/2014]	195.45 (-) [195.45]	0.00 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [5/2022]	565.09 (-) [565.09]	713.85 (0.00) [0]
54	REHABILITATION AND UPGRADATION OF	3/2016	5/2016	995.09	643.29

	KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O		(11/2022) [11/2022]	(995.00) [995.09]	(0.00) [78]
55	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (7/2022) [7/2022]	444.84 (-) [444.84]	396.31 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (6/2022) [6/2022]	376.25 (-) [376.25]	365.44 (0.00) [0]
57	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (8/2022) [8/2022]	289.67 (234.73) [234.73]	262.20 (-54.94) [48]
58	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (1/2022) [1/2022]	504.19 (504.00) [504.19]	495.73 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (6/2021) [6/2021]	271.45 (-) [271.45]	234.26 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (8/2022) [8/2022]	319.28 (319.28) [319.28]	241.94 (0.00) [60]
61	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600	3/2015	9/2015 (-) [9/2015]	309.01 (-) [309.01]	0.00 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (2/2022) [2/2022]	372.68 (309.37) [309.37]	274.73 (-63.31) [0]
63	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (7/2022) [7/2022]	228.32 (202.83) [202.83]	170.97 (-25.49) [0]
64	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (1/2022) [1/2022]	418.03 (386.99) [386.99]	361.50 (-31.04) [0]
65	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	8/2020	3/2021 (3/2023) [3/2023]	222.61 (-) [222.61]	42.15 (0.00) [24]
66	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (11/2021) [8/2022]	1,959.00 (2,909.00) [1,959.00]	1,412.01 (0.00) [-]
67	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (8/2021) [7/2022]	597.67 (570.98) [570.98]	509.41 (-26.69) [0]
68	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN	9/2018	2/2019 (4/2021) [5/2022]	617.41 (655.64) [668.45]	562.93 (51.04) [0]
69	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [6/2022]	1,323.15 (-) [1,323.15]	1,254.88 (0.00) [0]
70	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [9/2022]	1,550.98 (-) [1,550.98]	1,673.32 (0.00) [-]
71	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [5/2022]	1,535.00 (-) [1,535.00]	3,287.35 (0.00) [0]
72	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [3/2022]	1,041.62 (-) [1,187.10]	975.08 (145.48) [0]
73	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
74	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF	6/2020	5/2021 (12/2022)	221.40 (-)	90.53 (0.00)

	RAIPUR		[12/2022]	[221.40]	[19]
	<u>Urban Development</u>				
75	CONSTRUCTION OF NEW NACIN CAMPUS, PALASAMIDRAM, ANDHRA PRADESH	2/2022	8/2024 (-) [8/2024]	702.47 (-) [702.47]	1.16 (0.00) [0]
	<u>Water Resources</u>				
76	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (3/2024) [3/2024]	10,151.04 (55,548.87) [55,548.87]	20,538.05 (45,397.83) [48]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
77	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (3/2023) [3/2023]	645.63 (-) [645.63]	519.30 (0.00) [7]
	<u>Power</u>				
78	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	16,222.78 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
79	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	3/2027 (-) [3/2027]	496.47 (-) [496.47]	32.23 (0.00) [0]
80	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [3/2022]	243.89 (-) [243.89]	232.72 (0.00) [0]
81	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	3/2027 (-) [3/2027]	437.60 (-) [437.60]	41.92 (0.00) [0]
82	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	176.69 (0.00) [0]
83	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	141.82 (0.00) [0]
84	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	3/2027 (-) [3/2027]	403.68 (-) [403.68]	224.20 (0.00) [0]
85	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	3/2027 (-) [3/2027]	543.05 (-) [543.05]	241.22 (0.00) [0]
86	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	3/2027 (-) [3/2027]	450.65 (-) [450.65]	117.78 (0.00) [0]
87	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	3/2027 (-) [3/2027]	486.70 (-) [486.70]	201.16 (0.00) [0]
88	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	3/2027 (-) [3/2027]	560.39 (-) [560.39]	307.44 (0.00) [0]
89	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	3/2027 (-) [3/2027]	347.78 (-) [347.78]	223.07 (0.00) [0]
90	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	3/2027 (-) [3/2027]	394.27 (-) [394.27]	158.24 (0.00) [0]
91	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	3/2027 (-) [3/2027]	342.55 (-) [342.55]	264.65 (0.00) [0]
92	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	3/2027 (-) [3/2027]	421.48 (-) [421.48]	147.23 (0.00) [0]

93	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [12/2022]	200.44 (-) [200.44]	135.92 (0.00) [-]
94	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [3/2023]	568.92 (-) [568.92]	390.60 (0.00) [-]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [12/2022]	188.78 (-) [188.78]	142.23 (0.00) [-]
96	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [9/2022]	245.79 (-) [245.79]	224.65 (0.00) [-]
97	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	0.00 (0.00) [0]
98	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [3/2024]	1,718.59 (-) [1,718.59]	543.26 (0.00) [-]
99	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [1/2023]	301.06 (-) [301.06]	45.78 (0.00) [9]
100	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [1/2023]	353.90 (-) [353.90]	34.28 (0.00) [8]
101	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [4/2017]	167.28 (-) [167.28]	0.00 (0.00) [0]
102	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	167.37 (0.00) [0]
103	DOGINALA - GAU	12/2020	9/2022 (-) [4/2023]	242.30 (-) [242.30]	15.04 (0.00) [7]
104	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
105	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (4/2022) [12/2022]	228.71 (-) [228.71]	67.40 (0.00) [8]
106	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (12/2022) [12/2022]	294.04 (-) [294.04]	109.59 (0.00) [8]
107	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (12/2022) [12/2022]	199.03 (-) [199.03]	70.58 (0.00) [8]
108	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (12/2022) [12/2022]	184.88 (-) [184.88]	57.76 (0.00) [8]
109	LADDA - BASAI	2/2021	4/2023 (-) [2/2024]	445.96 (-) [445.96]	2.94 (0.00) [10]
110	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	24.48 (0.00) [0]
111	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [12/2022]	284.09 (-) [284.09]	188.40 (0.00) [68]
112	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [11/2022]	195.23 (-) [252.79]	180.00 (57.56) [67]
113	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON	2/2017	4/2017	203.36	172.68

	EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST]		(-) [10/2022]	(-) [263.31]	(59.95) [66]
114	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [8/2022]	198.22 (-) [252.05]	171.06 (53.83) [64]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (11/2023) [11/2023]	180.57 (244.10) [180.57]	18.01 (0.00) [79]
116	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [3/2024]	256.66 (-) [256.66]	0.00 (0.00) [-]
117	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (12/2021) [12/2021]	1,979.00 (-) [2,036.90]	1,251.08 (57.90) [0]
118	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	3/2027 (-) [3/2027]	182.55 (-) [182.55]	24.82 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
119	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2025]	1,142.00 (-) [1,232.00]	426.51 (90.00) [48]
	<u>Health And Family Welfare</u>				
120	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (890.14) [860.00]	528.81 (-15.00) [0]
121	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [179.15]	179.15 (3.58) [0]
	<u>Petroleum</u>				
122	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (12/2022) [12/2022]	543.91 (-) [638.60]	423.10 (94.69) [34]
123	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	49.33 (0.00) [0]
124	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [2/2023]	218.38 (-) [218.38]	35.16 (0.00) [0]
125	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	1,929.71 (6,602.00) [0]
126	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	3,273.73 (-1,170.00) [0]
127	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING	12/2020	7/2024 (-) [7/2024]	430.76 (-) [430.76]	8.66 (0.00) [0]
128	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM	3/2022	7/2026 (-) [7/2026]	277.00 (-) [277.00]	0.00 (0.00) [0]
129	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT	6/2021	12/2024 (-) [12/2024]	860.00 (-) [860.00]	20.10 (0.00) [0]
	<u>Power</u>				
130	NORTH EAST-NORTHERN/ WESTERN INTERCONNECTOR-I, PART-C	3/2019	3/2023 (-) [3/2023]	1,326.00 (-) [1,326.00]	1,054.46 (0.00) [0]
	<u>Railways</u>				
131	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-)	2,232.32 (-)	2,380.05 (1,827.33)

			[3/2025]	[4,059.65]	[36]
132	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2024]	385.20 (-) [1,145.79]	990.86 (760.59) [60]
	Road Transport And Highways				
133	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (6/2022) [6/2022]	268.08 (-) [390.73]	386.57 (122.65) [0]
134	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [3/2023]	261.13 (-) [261.13]	45.67 (0.00) [9]
135	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	46.43 (0.00) [0]
136	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [12/2022]	216.49 (-) [216.49]	65.59 (0.00) [9]
137	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [11/2022]	520.01 (-) [520.01]	214.57 (0.00) [-]
138	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [9/2022]	588.95 (-) [873.91]	559.13 (284.96) [46]
139	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2022]	289.99 (-) [289.99]	120.17 (0.00) [48]
140	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [12/2022]	252.00 (-) [330.30]	141.13 (78.30) [83]
141	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [6/2018]	437.39 (-) [437.39]	0.00 (0.00) [0]
142	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [7/2022]	294.17 (-) [385.57]	229.26 (91.40) [0]
143	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	364.26 (0.00) [0]
144	4-LANING OF DERGAON TOWN	3/2020	6/2022 (-) [6/2022]	287.63 (-) [287.63]	89.55 (0.00) [0]
145	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	52.00 (0.00) [0]
146	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146	12/2021	8/2024 (-) [8/2024]	300.00 (-) [300.00]	29.81 (0.00) [0]
147	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	93.86 (0.00) [0]
148	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	2.54 (0.00) [0]
149	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2023]	335.88 (-) [335.88]	70.36 (0.00) [-12]
150	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2022]	260.07 (-) [260.07]	109.24 (0.00) [-12]
151	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-)	288.85 (-)	8.28 (0.00)

			[1/2023]	[288.85]	[0]
152	DABOKA KATHKATI PACKAGE-6	9/2021	7/2024 (-) [7/2024]	625.64 (-) [625.64]	0.00 (0.00) [0]
153	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1	3/2022	7/2024 (-) [7/2024]	215.27 (-) [215.27]	0.00 (0.00) [0]
154	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2	4/2022	7/2024 (-) [7/2024]	170.95 (-) [170.95]	0.00 (0.00) [0]
155	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [8/2022]	168.39 (-) [259.79]	158.07 (91.40) [45]
156	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [4/2023]	818.00 (-) [818.00]	350.68 (0.00) [-]
157	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [3/2023]	463.49 (-) [801.54]	185.26 (338.05) [57]
158	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [6/2023]	829.00 (-) [1,307.50]	411.51 (478.50) [89]
159	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [7/2022]	454.89 (-) [814.56]	391.87 (359.67) [0]
160	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	188.31 (0.00) [0]
161	JOGIGHOPA BRIDGE	8/2021	11/2024 (-) [11/2024]	746.76 (-) [746.76]	9.76 (0.00) [0]
162	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	98.01 (0.00) [0]
163	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (12/2022) [12/2022]	160.00 (-) [160.00]	138.51 (0.00) [15]
164	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [1/2023]	636.42 (-) [418.49]	96.45 (-217.93) [1]
165	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
166	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	256.92 (0.00) [0]
167	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2023]	208.84 (-) [208.84]	27.93 (0.00) [12]
168	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [11/2022]	278.46 (-) [278.46]	120.18 (0.00) [8]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
169	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (3/2024) [3/2024]	1,216.90 (-) [1,216.90]	333.86 (0.00) [17]
	<u>Department Of Higher Education</u>				
170	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (6/2022) [12/2022]	496.18 (496.00) [460.00]	342.91 (-36.18) [66]

171	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (-) [375.00]	175.10 (0.00) [26]
	<u>Petroleum</u>				
172	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [7/2024]	14,810.00 (-) [14,810.00]	3,834.49 (0.00) [15]
173	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS	6/2019	12/2029 (3/2030) [3/2030]	988.00 (-) [988.00]	57.14 (0.00) [3]
174	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	6/2019	2/2028 (8/2029) [8/2029]	439.00 (-) [439.00]	147.85 (0.00) [18]
175	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	10/2018	8/2027 (2/2029) [2/2029]	176.00 (-) [176.00]	110.40 (0.00) [18]
176	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA	6/2019	12/2029 (3/2030) [3/2030]	163.00 (-) [163.00]	42.34 (0.00) [3]
177	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	6/2019	2/2028 (8/2029) [8/2029]	347.00 (-) [347.00]	125.47 (0.00) [18]
178	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2/2028 (8/2029) [8/2029]	2,996.00 (-) [2,996.00]	395.60 (0.00) [18]
179	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2023]	359.25 (-) [359.25]	228.18 (0.00) [12]
180	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (8/2022) [8/2023]	199.36 (-) [199.36]	118.68 (0.00) [34]
181	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI	1/2022	9/2024 (-) [9/2024]	389.00 (-) [389.00]	0.00 (0.00) [0]
182	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [12/2022]	403.00 (-) [403.00]	213.43 (0.00) [4]
	<u>Power</u>				
183	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [3/2024]	8,692.97 (21,312.11) [21,312.11]	20,184.00 (12,619.14) [149]
184	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (-) [10,439.09]	5,935.72 (0.00) [0]
185	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION	5/2021	4/2023 (-) [4/2023]	179.29 (-) [179.29]	79.99 (0.00) [0]
	<u>Railways</u>				
186	ARARIA-SUPAUL (NL)	4/2008	/ (-) [12/2025]	1,605.17 (1,605.17) [1,605.17]	213.88 (0.00) [-]
187	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [3/2024]	329.39 (1,483.14) [1,510.00]	1,547.42 (1,180.61) [-]
188	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [12/2024]	528.65 (2,066.78) [2,066.78]	1,661.76 (1,538.13) [-]
189	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [6/2023]	324.73 (967.29) [1,110.00]	1,112.02 (785.27) [135]
190	JAYNAGAR-BIJALPURA INCLUDING EXTENSION	4/2009	3/2020	548.00	540.74

	BIJALPURA-BARDIBAS(NEPAL) GC		(-) [3/2025]	(548.00) [783.83]	(235.83) [60]
191	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	360.11
			(-) [3/2025]	(614.45) [614.45]	(451.58) [-]
192	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	1,153.56 (0.00) [36]
193	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021 (-) [3/2024]	731.64 (1,185.73) [1,185.73]	624.19 (454.09) [36]
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [12/2023]	532.87 (-) [2,650.00]	1,255.18 (2,117.13) [57]
195	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [12/2023]	1,491.47 (-) [1,491.47]	660.90 (0.00) [45]
196	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [12/2024]	744.04 (1,215.54) [1,215.54]	685.28 (471.50) [45]
197	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	413.53
			(-) [12/2024]	(735.20) [735.20]	(410.20) [-]
198	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	1,758.02
			(-) [3/2024]	(1,470.50) [1,700.00]	(1,327.86) [-]
199	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	346.79
			(-) [12/2024]	(519.33) [519.33]	(139.33) [-]
	Road Transport And Highways				
200	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [5/2022]	511.54 (-) [591.00]	576.99 (79.46) [0]
201	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [11/2022]	375.09 (-) [375.09]	494.33 (0.00) [103]
202	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (12/2022) [0/0]	575.00 (-) [575.00]	517.32 (0.00) [0]
203	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [9/2024]	581.84 (-) [581.84]	0.00 (0.00) [88]
204	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [11/2022]	464.09 (-) [464.09]	174.53 (0.00) [24]
205	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [12/2022]	649.90 (-) [649.90]	155.54 (0.00) [24]
206	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [11/2022]	446.97 (-) [446.97]	170.57 (0.00) [24]
207	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	10/2019	2/2020 (-) [8/2023]	1,101.99 (-) [1,101.99]	424.90 (0.00) [42]
208	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/	2,926.42	535.86
			(-) [0/0]	(-) [2,926.42]	(0.00) [0]
209	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/	1,478.40	234.43
			(-) [0/0]	(-) [1,478.40]	(0.00) [0]
210	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00	12/2017	/	2,598.00	689.57

	(KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15		(-) [10/2024]	(-) [1,962.50]	(-635.50) [-]
211	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2022]	235.48 (-) [227.77]	11.00 (-7.71) [0]
212	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [6/2023]	496.20 (-) [537.17]	156.46 (40.97) [-]
213	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (6/2022) [6/2022]	683.83 (698.82) [698.82]	717.89 (14.99) [0]
214	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (6/2022) [11/2022]	178.85 (225.06) [225.06]	212.91 (46.21) [78]
215	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (3/2022) [11/2022]	553.30 (587.41) [587.41]	553.81 (34.11) [78]
216	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [3/2023]	1,167.45 (-) [1,182.94]	399.40 (15.49) [-]
217	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [12/2022]	642.41 (-) [681.67]	673.94 (39.26) [-]
218	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [6/2022]	322.09 (-) [322.09]	181.18 (0.00) [0]
219	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (3/2022) [3/2023]	1,408.85 (2,138.16) [2,138.16]	1,412.08 (729.31) [77]
220	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [9/2022]	814.04 (-) [825.17]	1,018.46 (11.13) [-]
221	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
222	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (7/2022) [12/2022]	1,041.10 (567.00) [639.58]	492.38 (-401.52) [44]
223	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [12/2022]	574.00 (-) [574.00]	768.92 (0.00) [105]
224	PATNA-MUZZAFFARPUR	8/2010	2/2013 (12/2022) [3/2023]	671.30 (-) [671.30]	1,587.77 (0.00) [121]
225	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (6/2022) [5/2022]	1,742.01 (-) [1,742.01]	1,845.15 (0.00) [0]
226	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (12/2019) [6/2023]	573.70 (644.50) [726.99]	222.51 (153.29) [-]
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (11/2022) [11/2022]	319.68 (404.10) [404.10]	400.67 (84.42) [-]
228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (6/2022) [3/2023]	675.00 (780.77) [780.77]	453.21 (105.77) [-]
229	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [4/2024]	895.39 (-) [895.39]	1,369.90 (0.00) [-]
230	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (8/2023)	950.64 (1,161.00)	503.74 (217.69)

			[8/2023]	[1,168.33]	[72]
231	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (3/2022) [3/2022]	153.24 (-) [153.24]	115.69 (0.00) [0]
232	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (3/2022) [5/2022]	854.80 (-) [1,038.56]	1,065.19 (183.76) [0]
233	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [1/2021]	516.13 (-) [649.27]	638.53 (133.14) [0]
234	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (12/2018) [3/2023]	672.89 (736.01) [830.31]	31.82 (157.42) [36]
	<u>Urban Development</u>				
235	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [6/2024]	13,365.77 (-) [13,925.50]	437.20 (559.73) [0]
	<u>Water Resources</u>				
236	I AND D AND STP AT CHAPPRA	11/2018	12/2020 (-) [10/2022]	236.15 (-) [236.15]	80.59 (0.00) [22]
237	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [3/2024]	254.13 (413.29) [413.29]	0.07 (159.16) [42]
238	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [6/2022]	268.63 (431.21) [431.21]	432.61 (162.58) [0]
239	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [3/2023]	230.06 (-) [230.06]	137.93 (0.00) [20]
240	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [8/2023]	305.19 (-) [305.19]	146.80 (0.00) [24]
241	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [12/2023]	294.02 (-) [294.02]	90.96 (0.00) [26]
242	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [9/2022]	356.37 (-) [356.37]	215.30 (0.00) [17]
243	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [12/2022]	824.00 (-) [824.00]	140.17 (0.00) [6]
244	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [12/2022]	578.89 (-) [578.89]	16.55 (0.00) [6]
245	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [6/2022]	225.77 (398.90) [398.90]	332.70 (173.13) [0]
246	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [10/2022]	277.42 (-) [277.42]	298.55 (0.00) [17]
247	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (-) [5/2022]	191.62 (-) [191.62]	94.08 (0.00) [0]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
248	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	48.55 (0.00) [60]
249	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-)	316.10 (-)	154.35 (0.00)

			[3/2023]	[316.10]	[36]
250	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	446.28 (0.00) [0]
251	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (3/2025) [3/2025]	610.63 (-) [610.63]	234.80 (0.00) [36]
252	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	1,990.07 (0.00) [0]
253	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	13.24 (0.00) [0]
254	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	5,180.64 (0.00) [0]
255	JAGANNATHPUR OC RCE (3.0 MTY)	7/2016	3/2020 (-) [3/2022]	459.49 (-) [459.49]	215.67 (0.00) [0]
256	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	182.09 (0.00) [0]
257	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	2.67 (0.00) [0]
258	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	16.13 (0.00) [144]
259	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	3,646.22 (0.00) [0]
260	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
261	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	79.53 (0.00) [0]
262	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	11.18 (0.00) [0]
263	PORDA CHIMTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
264	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	87.36 (0.00) [0]
	<u>Department Of Higher Education</u>				
265	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [10/2022]	808.62 (-) [808.62]	536.84 (0.00) [3]
	<u>Petroleum</u>				
266	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT	3/2021	3/2024 (-) [3/2024]	456.00 (-) [456.00]	113.39 (0.00) [0]
	<u>Railways</u>				
267	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [12/2024]	2,288.00 (-) [4,970.11]	1,509.87 (2,682.11) [33]
268	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2023) [12/2023]	1,973.00 (2,135.34) [2,135.34]	1,106.76 (162.34) [33]

269	KHARSIA DHARAMJAGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [12/2023]	3,055.00 (-) [3,500.00]	2,945.30 (445.00) [63]
270	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2024]	1,160.00 (-) [1,160.83]	1,095.89 (0.83) [48]
271	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [9/2022]	1,402.02 (-) [1,300.00]	1,405.40 (-102.02) [30]
	<u>Road Transport And Highways</u>				
272	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (7/2022) [7/2022]	1,029.96 (1,632.70) [16,732.70]	468.76 (15,702.74) [0]
273	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [12/2021]	726.67 (1,103.55) [1,096.52]	538.73 (369.85) [0]
274	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (3/2022) [8/2022]	596.67 (819.35) [819.35]	439.27 (222.68) [51]
275	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (-) [12/2022]	335.32 (-) [335.32]	277.98 (0.00) [66]
276	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (-) [3/2023]	476.20 (544.00) [544.00]	452.11 (67.80) [78]
277	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (-) [3/2023]	496.02 (-) [496.02]	240.11 (0.00) [96]
278	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (-) [12/2022]	497.14 (-) [572.66]	280.46 (75.52) [76]
279	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (-) [12/2022]	624.98 (-) [731.50]	471.29 (106.52) [74]
280	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (-) [12/2022]	452.94 (-) [435.61]	126.17 (-17.33) [77]
281	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (-) [10/2022]	423.79 (-) [423.79]	302.65 (0.00) [57]
282	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (-) [9/2022]	188.80 (-) [188.80]	125.56 (0.00) [40]
	<u>Steel</u>				
283	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (3/2023) [3/2023]	15,525.00 (21,940.00) [21,940.00]	21,019.89 (6,415.00) [94]
284	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (-) [7/2024]	2,907.00 (-) [2,907.00]	908.39 (0.00) [13]
285	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	123.14 (0.00) [0]
286	SCREENING PLANT-III AT KIRANDUL	3/2021	8/2024 (-) [8/2024]	2,092.97 (-) [2,092.97]	396.60 (0.00) [0]
	<u>Urban Development</u>				
287	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	5/2019	9/2020 (-) [11/2023]	299.97 (-) [299.97]	69.08 (0.00) [38]
	<u>DELHI</u>				

	<u>Civil Aviation</u>				
288	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (12/2022) [12/2022]	303.80 (351.21) [351.21]	247.98 (47.41) [32]
	<u>Commerce</u>				
289	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [0/0]	302.64 (-) [302.64]	30.00 (0.00) [0]
	<u>Dpiit</u>				
290	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [1/2023]	4,773.00 (-) [5,178.00]	3,032.83 (405.00) [37]
	<u>Finance</u>				
291	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA	7/2018	4/2022 (-) [4/2022]	228.50 (220.27) [220.27]	182.43 (-8.23) [0]
	<u>Health And Family Welfare</u>				
292	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [6/2021]	204.44 (-) [285.00]	285.00 (80.56) [0]
293	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
294	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [1/2022]	156.56 (-) [205.00]	145.94 (48.44) [0]
295	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [9/2021]	414.11 (-) [586.50]	586.50 (172.39) [0]
	<u>Home Affairs</u>				
296	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	6/2019	7/2022 (-) [6/2023]	277.35 (-) [290.33]	63.23 (12.98) [11]
297	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [12/2022]	1,219.21 (-) [1,679.02]	1,036.04 (459.81) [38]
	<u>Railways</u>				
298	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	133.78 (123.32) [-]
	<u>Renewable Energy</u>				
299	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [0/0]	271.90 (-) [365.00]	249.96 (93.10) [0]
	<u>Telecommunications</u>				
300	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	3/2018 (-) [11/2022]	248.20 (-) [248.20]	174.08 (0.00) [56]
	<u>Urban Development</u>				
301	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (-) [4/2022]	197.33 (-) [220.00]	113.34 (22.67) [0]
302	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [9/2025]	24,948.65 (-) [24,948.65]	4,071.69 (0.00) [6]
303	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (9/2021) [0/0]	565.00 (-) [565.00]	514.44 (0.00) [0]
304	DELHI MRTS PHASE-III	9/2011	3/2016 (8/2021) [0/0]	38,585.00 (-) [40,180.91]	39,907.57 (1,595.91) [0]

305	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [6/2024]	1,180.00 (-) [1,100.80]	36.69 (-79.20) [35]
306	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (-) [0/0]	392.00 (-) [392.00]	242.43 (0.00) [0]
307	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (6/2024) [6/2024]	1,128.00 (-) [1,128.00]	69.28 (0.00) [27]
308	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (-) [0/0]	422.00 (-) [422.00]	221.22 (0.00) [0]
309	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [3/2023]	2,694.00 (-) [2,694.00]	1,292.02 (0.00) [-]
	<u>Water Resources</u>				
310	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
311	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [3/2022]	515.07 (-) [515.07]	388.08 (0.00) [0]
312	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	372.23 (0.00) [0]
313	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	136.75 (0.00) [12]
314	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	205.76 (0.00) [10]
	<u>GOA</u>				
	<u>Civil Aviation</u>				
315	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT.	11/2017	9/2021 (-) [9/2023]	255.69 (-) [255.69]	27.32 (0.00) [24]
	<u>Department Of Higher Education</u>				
316	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [2/2023]	303.90 (334.45) [334.45]	140.00 (30.55) [35]
	<u>Health And Family Welfare</u>				
317	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [5/2021]	249.01 (-) [249.07]	244.64 (0.06) [0]
	<u>Road Transport And Highways</u>				
318	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (2/2019) [1/2020]	280.16 (-) [290.59]	243.00 (10.43) [0]
319	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [12/2021]	184.05 (-) [184.05]	118.37 (0.00) [0]
320	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (9/2022) [12/2022]	936.40 (-) [936.40]	611.47 (0.00) [-]
321	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (12/2021) [3/2022]	298.33 (354.43) [298.33]	349.92 (0.00) [0]
322	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [3/2022]	852.67 (-) [852.67]	234.18 (0.00) [0]
323	PATRADEVI TO KARASWADA 4L	3/2017	5/2020	634.32	347.93

			(-) [6/2022]	(-) [634.32]	(0.00) [0]
324	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/	773.98	413.42
			(-) [3/2022]	(-) [773.98]	(0.00) [0]
325	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/	819.95	423.47
			(-) [3/2022]	(-) [819.95]	(0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
326	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11,459.00	18,523.00
			(-) [6/2023]	(19,220.00) [19,220.00]	(7,761.00) [90]
	<u>Civil Aviation</u>				
327	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022	1,405.00	681.21
			(8/2023) [8/2023]	(-) [1,405.00]	(0.00) [12]
328	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT.	8/2018	2/2021	353.25	143.30
			(-) [12/2022]	(-) [353.25]	(0.00) [22]
	<u>Petroleum</u>				
329	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023	5,251.00	1,472.17
			(-) [5/2023]	(-) [5,251.00]	(0.00) [0]
330	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/	588.20	303.77
			(3/2023) [3/2023]	(-) [730.20]	(142.00) [-]
331	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023	1,614.00	173.85
			(-) [8/2023]	(-) [1,614.00]	(0.00) [0]
332	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD	1/2022	11/2024	621.40	72.69
			(-) [11/2024]	(-) [621.40]	(0.00) [0]
333	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020	906.00	423.21
			(7/2022) [9/2022]	(-) [906.00]	(0.00) [31]
334	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT	1/2022	9/2024	328.00	1.55
			(-) [9/2024]	(-) [328.00]	(0.00) [0]
335	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024	18,936.00	1,433.13
			(-) [8/2024]	(-) [18,936.00]	(0.00) [-1]
336	REDEVELOPMENT OF LINCH FIELD	4/2021	3/2025	631.03	212.55
			(-) [3/2025]	(-) [631.03]	(0.00) [0]
337	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022	444.87	338.56
			(2/2023) [2/2023]	(-) [444.87]	(0.00) [6]
338	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026	1,162.56	915.64
			(-) [3/2026]	(-) [1,162.56]	(0.00) [0]
339	REDEVELOPMENT OF SOBHASAN COMPLEX	8/2021	2/2026	885.63	231.36
			(-) [2/2026]	(-) [885.63]	(0.00) [0]
340	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022	1,378.00	441.50
			(-) [12/2022]	(-) [1,378.00]	(0.00) [0]
341	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021	225.54	154.74
			(-) [10/2022]	(-) [247.90]	(22.36) [20]
	<u>Power</u>				

342	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR)	5/2021	9/2022 (-) [8/2023]	674.92 (-) [674.92]	76.91 (0.00) [11]
343	Bagodara Solar Power Project	5/2021	10/2022 (-) [10/2022]	339.35 (-) [339.35]	45.45 (0.00) [0]
344	DAYAPAR WIND ENERGY PROJECT 150MW	11/2021	5/2023 (-) [5/2023]	937.80 (-) [937.80]	102.21 (0.00) [0]
345	GUJARAT 200 MW (GUVNL TENDER)	1/2021	7/2022 (10/2022) [8/2023]	842.27 (-) [842.27]	92.08 (0.00) [13]
346	KAWAS SOLAR 56 MW	8/2020	10/2021 (1/2023) [8/2022]	261.80 (-) [293.03]	243.32 (31.23) [10]
347	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT	10/2019	8/2021 (-) [10/2022]	1,031.00 (-) [1,143.00]	985.61 (112.00) [14]
	<u>Railways</u>				
348	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2024) [3/2024]	829.74 (1,631.75) [2,448.99]	2,142.58 (1,619.25) [48]
349	ANAND GODHRA DOUBLING PROJECT 79 KMS	4/2017	3/2020 (12/2024) [12/2024]	692.25 (692.26) [692.26]	8.51 (0.01) [57]
350	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2024) [3/2024]	318.24 (322.19) [1,083.17]	252.70 (764.93) [144]
351	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS	4/2018	3/2024 (12/2024) [12/2024]	537.31 (537.31) [584.31]	2.44 (47.00) [9]
352	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (10/2025) [10/2025]	844.10 (844.10) [844.10]	390.14 (0.00) [-]
353	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [3/2019]	343.00 (-) [343.00]	222.83 (0.00) [0]
354	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2022]	1,548.66 (-) [2,538.01]	2,375.23 (989.35) [12]
355	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,042.12) [1,119.12]	962.02 (116.73) [21]
356	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (12/2022) [12/2022]	1,037.15 (1,125.53) [1,394.02]	1,300.17 (356.87) [21]
357	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [3/2024]	248.26 (-) [528.49]	127.92 (280.23) [-]
	<u>Road Transport And Highways</u>				
358	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	199.86 (0.00) [0]
359	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [12/2022]	829.97 (-) [829.97]	329.71 (0.00) [-]
360	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [10/2021]	1,958.88 (2,047.39) [1,993.81]	1,116.85 (34.93) [0]
361	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (11/2018)	2,125.24 (-)	437.87 (0.00)

			[11/2018]	[2,125.24]	[0]
362	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [6/2022]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
363	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [6/2022]	1,437.64 (-) [1,437.64]	564.11 (0.00) [0]
364	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [6/2022]	2,702.05 (-) [2,043.00]	2,043.00 (-659.05) [0]
365	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG	5/2020	12/2023 (-) [12/2023]	894.00 (-) [894.00]	213.55 (0.00) [0]
366	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0	5/2020	3/2024 (-) [3/2024]	690.30 (-) [690.30]	62.72 (0.00) [0]
367	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION	5/2020	1/2024 (-) [1/2024]	882.00 (-) [882.00]	0.02 (0.00) [0]
368	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB	5/2020	7/2023 (-) [7/2023]	691.52 (-) [691.52]	113.57 (0.00) [0]
369	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [5/2022]	400.76 (394.44) [394.44]	215.03 (-6.32) [0]
370	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT	6/2020	4/2023 (-) [4/2023]	166.21 (-) [166.21]	53.63 (0.00) [0]
371	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [12/2022]	962.43 (-) [962.43]	594.81 (0.00) [57]
372	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (6/2021) [9/2022]	867.97 (913.49) [913.49]	700.54 (45.52) [46]
373	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [8/2024]	998.18 (-) [998.18]	781.17 (0.00) [-]
374	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [8/2022]	723.64 (-) [723.64]	528.22 (0.00) [-]
375	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [12/2022]	763.08 (-) [763.08]	408.37 (0.00) [-]
376	JUNAGADH BYPASS	10/2017	10/2017 (-) [7/2022]	232.49 (373.10) [232.49]	228.82 (0.00) [0]
377	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [7/2013]	953.88 (-) [953.88]	91.63 (0.00) [0]
378	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (6/2021) [9/2022]	1,052.21 (-) [1,361.00]	503.77 (308.79) [-]
379	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (6/2021) [9/2022]	1,251.11 (-) [1,361.00]	503.77 (109.89) [-]
380	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
381	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2022]	351.00 (270.00) [270.00]	197.00 (-81.00) [0]

	<u>Urban Development</u>				
382	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [9/2022]	10,773.00 (-) [12,925.22]	10,816.18 (2,152.22) [45]
383	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	763.91 (0.00) [0]
384	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [6/2024]	12,020.32 (-) [12,020.32]	814.67 (0.00) [3]
	<u>HARYANA</u>				
	<u>Health And Family Welfare</u>				
385	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [4/2020]	505.58 (-) [586.96]	586.96 (81.38) [0]
	<u>Home Affairs</u>				
386	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)"	1/2020	10/2023 (3/2024) [3/2024]	166.98 (166.98) [166.98]	17.41 (0.00) [5]
	<u>Petroleum</u>				
387	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	818.04 (0.00) [0]
388	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (8/2022) [11/2022]	909.00 (-) [909.00]	680.30 (0.00) [22]
389	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (2/2023) [2/2023]	206.63 (340.76) [340.76]	220.01 (134.13) [36]
390	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (-) [2/2027]	520.00 (-) [520.00]	275.43 (0.00) [5]
391	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [6/2023]	164.69 (-) [164.69]	81.34 (0.00) [23]
392	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (7/2022) [12/2022]	598.00 (753.89) [753.89]	602.73 (155.89) [34]
393	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [3/2023]	278.60 (-) [278.60]	160.73 (0.00) [21]
394	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (4/2022) [12/2022]	1,636.00 (-) [1,636.00]	1,097.83 (0.00) [28]
395	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	12/2021 (1/2023) [1/2023]	1,255.00 (-) [1,255.00]	661.56 (0.00) [13]
396	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (3,219.94) [2,281.94]	804.64 (0.00) [7]
397	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (6/2022) [12/2022]	286.42 (327.00) [327.01]	255.10 (40.59) [28]
	<u>Power</u>				
398	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA	1/2019	3/2022 (-) [11/2022]	267.33 (-) [267.33]	86.32 (0.00) [8]
	<u>Railways</u>				
399	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [12/2011]	287.00 (-) [893.45]	686.20 (606.45) [0]

	Road Transport And Highways				
400	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [7/2019]	574.28 (-) [537.16]	485.00 (-37.12) [0]
401	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [9/2022]	2,128.72 (2,408.72) [2,408.72]	1,865.00 (280.00) [41]
402	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [10/2022]	247.25 (-) [247.25]	195.15 (0.00) [43]
403	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [8/2023]	1,484.30 (-) [1,484.30]	889.47 (0.00) [-]
404	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [0]
405	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (5/2022) [5/2022]	996.65 (1,173.65) [1,173.65]	1,115.31 (177.00) [0]
406	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (4/2022) [4/2022]	1,243.45 (1,407.35) [1,407.35]	1,355.53 (163.90) [0]
407	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (5/2022) [5/2022]	889.36 (986.10) [986.10]	949.40 (96.74) [0]
408	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (5/2022) [5/2022]	1,018.79 (1,072.08) [1,072.08]	1,023.71 (53.29) [0]
409	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (5/2022) [5/2022]	1,051.91 (1,118.07) [1,118.07]	1,031.96 (66.16) [0]
410	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (7/2022) [7/2022]	1,120.06 (1,206.48) [1,206.48]	1,127.92 (86.42) [0]
411	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (6/2022) [6/2022]	1,137.42 (1,238.29) [1,238.29]	1,185.04 (100.87) [0]
412	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (3/2022) [3/2022]	1,033.19 (1,044.32) [1,044.32]	911.58 (11.13) [0]
413	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [4/2022]	795.50 (-) [922.64]	820.70 (127.14) [0]
414	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [2/2022]	634.70 (-) [925.96]	823.04 (291.26) [0]
	HIMACHAL PRADESH				
	Department Of Higher Education				
415	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022 (4/2023) [4/2023]	392.51 (-) [392.51]	106.00 (0.00) [10]
	Health And Family Welfare				
416	AIIMS BILASPUR	4/2018	9/2021 (-) [8/2022]	1,351.00 (-) [1,471.04]	1,162.76 (120.04) [11]
417	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [6/2021]	260.00 (-) [260.00]	25.38 (0.00) [0]
	Power				
418	DHAULASIDH HYDROELECTRIC PROJECT (66 MW)	10/2020	11/2025 (-)	687.97 (-)	285.25 (0.00)

			[11/2025]	[687.97]	[0]
419	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	810.74 (0.00) [0]
420	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (12/2023) [12/2023]	3,919.59 (10,463.03) [10,463.03]	10,010.30 (6,543.44) [171]
	<u>Railways</u>				
421	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [3/2025]	2,966.99 (-) [6,753.42]	2,374.44 (3,786.43) [-21]
	<u>Road Transport And Highways</u>				
422	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [6/2023]	2,485.93 (-) [2,485.93]	1,208.03 (0.00) [36]
423	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,660.92 (0.00) [0]
424	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (3/2021) [12/2022]	934.46 (-) [1,543.51]	1,472.50 (609.05) [57]
425	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (11/2022) [11/2022]	478.74 (-) [1,135.08]	905.95 (656.34) [-]
426	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [3/2023]	1,273.71 (-) [1,273.71]	1,092.03 (0.00) [-]
427	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [7/2022]	447.75 (-) [447.75]	1,402.07 (0.00) [0]
428	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K	2/2021	9/2021 (-) [0/0]	345.89 (-) [345.89]	88.41 (0.00) [0]
429	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K	8/2020	12/2024 (-) [12/2024]	371.93 (-) [371.93]	0.00 (0.00) [0]
430	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50.	8/2020	3/2021 (-) [0/0]	242.80 (-) [242.80]	41.61 (0.00) [0]
431	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA	8/2020	4/2021 (-) [0/0]	272.98 (-) [272.98]	57.24 (0.00) [0]
432	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75	8/2020	4/2021 (-) [0/0]	349.20 (-) [349.20]	206.92 (0.00) [0]
433	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	0.00 (0.00) [0]
	<u>JAMMU AND KASHMIR</u>				
	<u>Department Of Higher Education</u>				
434	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (-) [676.00]	0.15 (0.00) [0]
435	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (10/2022) [10/2022]	424.93 (-) [424.93]	209.30 (0.00) [3]
	<u>Health And Family Welfare</u>				
436	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	303.17 (0.00) [-16]
437	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA	3/2019	9/2023	1,404.00	667.78

	JAMMU AND KASHMIR		(-) [9/2023]	(-) [1,404.00]	(0.00) [0]
	<u>Power</u>				
438	KIRU HYDRO ELECTRIC PROJECT	3/2019	/ (8/2024) [7/2025]	4,287.59 (-) [4,287.59]	793.45 (0.00) [-]
439	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (7/2025) [7/2025]	8,112.12 (-) [8,112.12]	2,449.04 (0.00) [63]
440	RATLE HE PROJECT	2/2021	2/2026 (2/2026) [2/2026]	5,281.94 (5,281.94) [5,281.94]	43.55 (0.00) [0]
	<u>Railways</u>				
441	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (6/2023) [6/2023]	2,500.00 (37,012.26) [37,012.26]	30,671.82 (34,512.26) [247]
	<u>Road Transport And Highways</u>				
442	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	678.90 (0.00) [0]
443	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (10/2018) [3/2024]	1,471.75 (-) [1,339.00]	1,236.41 (-132.75) [-]
444	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	550.00 (0.00) [0]
445	DONIPAWA TO ASHAJIPORA BYPASS PKG-7	3/2021	12/2022 (-) [12/2022]	260.40 (-) [260.40]	8.26 (0.00) [0]
446	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2023]	2,168.66 (-) [2,168.66]	1,190.60 (0.00) [54]
447	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (12/2022) [12/2022]	2,136.97 (2,288.97) [2,136.97]	1,921.25 (0.00) [48]
448	GOHA-KHELLANI PKG-3	2/2021	3/2023 (-) [3/2023]	431.28 (-) [431.28]	43.78 (0.00) [0]
449	KHELLANI-KHANABAL PKG-1	3/2021	9/2022 (-) [9/2022]	486.45 (-) [486.45]	15.88 (0.00) [0]
450	KHELLANI-KHANABAL PKG-2	7/2021	2/2023 (-) [2/2023]	512.43 (-) [512.43]	9.78 (0.00) [0]
451	KHELLANI-KHANABAL PKG-3	3/2021	12/2022 (-) [12/2022]	398.51 (-) [398.51]	24.74 (0.00) [0]
452	KHELLANI-KHANABAL PKG-4	7/2021	8/2023 (-) [8/2023]	859.67 (-) [859.67]	25.50 (0.00) [0]
453	KHELLANI-KHANABAL PKG-5	7/2021	2/2023 (-) [2/2023]	497.09 (-) [497.09]	25.62 (0.00) [0]
454	KHELLANI-KHANABAL PKG-6	2/2021	9/2022 (-) [9/2022]	285.28 (-) [285.28]	70.27 (0.00) [0]
455	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [5/2022]	1,987.00 (-) [1,987.00]	3,116.66 (0.00) [0]
456	SRINAGAR TO BANIHAL	6/2011	6/2014 (-)	1,100.70 (-)	2,935.64 (0.00)

			[9/2022]	[1,100.70]	[99]
457	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [12/2022]	228.39 (-) [228.39]	14.76 (0.00) [8]
458	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (-) [12/2022]	210.79 (-) [210.79]	20.59 (0.00) [8]
459	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [12/2022]	253.44 (-) [253.44]	112.59 (0.00) [41]
460	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [5/2022]	404.17 (-) [404.17]	296.31 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
461	CHANDRAGUPT OCP	8/2020	3/2032 (-) [3/2032]	973.50 (-) [973.50]	204.84 (0.00) [0]
462	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	168.07 (0.00) [0]
463	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2023]	163.51 (-) [163.51]	133.41 (0.00) [144]
464	EPR PUNDI OCP	11/2020	3/2024 (-) [3/2024]	713.35 (-) [713.35]	233.94 (0.00) [0]
465	EPR ROHINI KARKATA OCP	1/2021	3/2025 (-) [3/2025]	1,020.42 (-) [1,020.42]	81.23 (0.00) [0]
466	EPR TAPIN SOUTH OCP	11/2020	3/2025 (-) [3/2025]	230.41 (-) [230.41]	18.14 (0.00) [0]
467	EXPANSION OF ASHOK OCP	5/2021	3/2026 (-) [3/2026]	2,898.28 (-) [2,898.28]	186.45 (0.00) [0]
468	EXPANSION OF KARO OCP	1/2022	3/2026 (-) [3/2026]	908.47 (-) [908.47]	99.05 (0.00) [0]
469	EXPANSION OF KONAR OCP	1/2022	3/2032 (-) [3/2032]	799.34 (-) [799.34]	263.19 (0.00) [0]
470	EXPANSION PROJECT AMRAPALI OCP	8/2020	3/2028 (-) [3/2028]	5,136.15 (-) [5,136.15]	331.85 (0.00) [0]
471	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	263.24 (0.00) [0]
472	JHARKHAND LAIYO OCP	8/2020	3/2031 (-) [3/2031]	764.57 (-) [764.57]	152.91 (0.00) [0]
473	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2023]	162.46 (-) [162.46]	93.61 (0.00) [108]
474	KOTRE BASANTPUR PACHMO OCP	8/2020	3/2032 (-) [3/2032]	861.06 (-) [861.06]	137.75 (0.00) [0]
475	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [9/2022]	289.45 (302.00) [302.00]	296.38 (12.55) [100]
476	MOONIDIH XV SEAM UG	8/2011	3/2019	1,230.27	538.38

			(-) [4/2024]	(-) [1,230.27]	(0.00) [61]
477	MURAIIDH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2025]	339.88 (-) [339.88]	130.52 (0.00) [138]
478	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2023]	555.52 (-) [555.52]	20.01 (0.00) [24]
479	PACHWARA SOUTH COAL BLOCK	7/2013	9/2028 (-) [9/2028]	1,795.01 (-) [1,795.01]	40.80 (0.00) [0]
480	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [6/2023]	243.00 (334.27) [334.27]	44.58 (91.27) [62]
481	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2023]	510.85 (-) [510.85]	487.40 (0.00) [84]
482	REVISED PROJECT REPORT MAGADH EXPANSION OCP	8/2020	3/2028 (-) [3/2028]	7,254.37 (-) [7,254.37]	782.87 (0.00) [0]
483	SIRKA OCP	5/2020	3/2025 (-) [3/2025]	222.82 (-) [222.82]	136.52 (0.00) [0]
484	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	48.22 (0.00) [0]
485	UCE OF EPR OF NORTH URIMARI OCP	7/2021	3/2026 (-) [3/2026]	778.80 (-) [778.80]	508.97 (0.00) [0]
	<u>Department Of Higher Education</u>				
486	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (7/2022) [7/2022]	171.86 (171.86) [171.86]	151.07 (0.00) [0]
	<u>Petroleum</u>				
487	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS	10/2018	12/2029 (3/2030) [3/2030]	613.00 (-) [613.00]	191.24 (0.00) [3]
488	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [3/2023]	226.45 (-) [226.45]	179.25 (0.00) [5]
489	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [8/2023]	221.45 (-) [221.45]	129.91 (0.00) [10]
490	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1)	11/2019	1/2024 (-) [1/2024]	431.00 (-) [431.00]	29.95 (0.00) [0]
491	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2023]	823.27 (1,137.79) [1,137.79]	848.08 (314.52) [0]
492	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (3/2023) [3/2023]	248.55 (-) [248.55]	180.31 (0.00) [9]
	<u>Power</u>				
493	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [12/2024]	14,366.58 (-) [17,007.00]	13,203.00 (2,640.42) [66]
494	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2025]	18,668.00 (-) [18,668.00]	8,846.25 (0.00) [24]
	<u>Railways</u>				
495	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021	1,724.20	1,358.49

			(-) [3/2024]	(-) [1,724.20]	(0.00) [36]
496	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/	1,033.07	3,787.71
			(-) [7/2022]	(3,020.95) [3,800.00]	(2,766.93) [0]
497	KODERMA-TILAIYA (NL), ECR	4/2002	/	459.91	1,136.40
			(-) [3/2024]	(1,625.87) [1,625.87]	(1,165.96) [-]
498	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM)	4/2018	6/2022	428.65	6.00
			(-) [12/2025]	(-) [472.50]	(43.85) [42]
499	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	4/2018	12/2021	390.39	259.72
			(-) [1/2023]	(-) [511.75]	(121.36) [13]
	Road Transport And Highways				
500	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/	1,005.08	0.00
			(2/2023) [2/2023]	(-) [1,005.08]	(0.00) [-]
501	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/	273.46	175.09
			(-) [3/2023]	(-) [276.17]	(2.71) [-]
502	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018	323.72	327.54
			(-) [5/2022]	(-) [355.24]	(31.52) [0]
503	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/	1,155.16	539.74
			(-) [9/2022]	(-) [950.49]	(-204.67) [-]
504	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/	458.03	487.99
			(-) [6/2022]	(-) [486.00]	(27.97) [0]
505	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021	196.00	141.64
			(6/2022) [0/0]	(-) [196.00]	(0.00) [0]
	Steel				
506	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017	1,034.01	782.72
			(12/2021) [12/2023]	(-) [1,034.01]	(0.00) [74]
507	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019	262.87	272.19
			(6/2022) [9/2022]	(-) [262.87]	(0.00) [39]
508	UP GRADATION OF AUTOMATION SYSTEM OF HOT STRIP MILL AT BOKARO STEEL PLANT	2/2022	6/2024	207.74	8.71
			(-) [6/2024]	(-) [207.74]	(0.00) [0]
	KARNATAKA				
	Defence Production				
509	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020	246.31	181.63
			(8/2022) [10/2022]	(210.00) [200.00]	(-46.31) [32]
	Department Of Higher Education				
510	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL	8/2021	2/2024	316.25	0.00
			(-) [2/2024]	(-) [316.25]	(0.00) [0]
511	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022	851.00	466.32
			(10/2022) [10/2022]	(851.00) [851.00]	(0.00) [7]
	Petroleum				
512	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022	854.00	235.86
			(12/2023) [12/2023]	(-) [854.00]	(0.00) [12]
513	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023	200.00	41.00
			(1/2024)	(304.00)	(104.00)

			[1/2024]	[304.00]	[7]
514	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [10/2022]	2,166.38 (-) [2,166.38]	1,762.67 (0.00) [4]
515	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE	1/2022	7/2025 (-) [7/2025]	463.00 (-) [463.00]	19.27 (0.00) [0]
	<u>Railways</u>				
516	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2026]	986.30 (1,378.00) [1,530.09]	332.27 (543.79) [129]
517	GADAG-WADI NL	4/2013	12/2018 (-) [6/2025]	2,841.84 (-) [2,841.84]	490.24 (0.00) [78]
518	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [3,300.00]	2,799.96 (1,173.00) [0]
519	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [12/2022]	1,156.94 (-) [1,954.21]	1,381.52 (797.27) [33]
520	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [3/2028]	2,315.00 (-) [5,174.30]	158.25 (2,859.30) [-]
521	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2026]	644.78 (889.00) [826.18]	499.13 (181.40) [108]
522	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [3/2024]	279.54 (-) [279.54]	36.45 (0.00) [96]
523	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2026]	832.47 (-) [832.47]	0.94 (0.00) [120]
524	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [3/2025]	1,801.01 (-) [2,000.97]	104.48 (199.96) [-]
	<u>Road Transport And Highways</u>				
525	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (6/2023) [6/2023]	1,167.42 (-) [870.00]	380.24 (-297.42) [51]
526	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [12/2023]	486.78 (-) [486.78]	171.98 (0.00) [-]
527	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (12/2022) [12/2022]	1,655.01 (2,639.00) [2,639.00]	1,710.83 (983.99) [76]
528	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (3/2023) [3/2023]	701.40 (-) [701.40]	156.33 (0.00) [48]
529	4L OF ADDAHOLE TO BANTWAL CROSS SECTION	3/2021	10/2021 (-) [9/2023]	317.90 (317.90) [317.90]	127.41 (0.00) [23]
530	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN	3/2021	11/2021 (-) [11/2023]	1,100.88 (1,100.88) [1,100.88]	261.90 (0.00) [24]
531	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	3/2019	12/2019 (12/2022) [12/2023]	423.15 (-) [423.15]	216.18 (0.00) [48]
532	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (5/2023) [5/2023]	157.32 (187.61) [157.32]	24.20 (0.00) [48]
533	DEVELOPMENT OF MULTIMODAL LOGISTICS PARK AT	6/2022	3/2025	1,769.70	4.20

	BANGALORE AND EXTERNAL CONNECTIVITY TO THE MULTI MODEL L		(-) [3/2025]	(-) [1,769.70]	(0.00) [0]
534	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (7/2022) [7/2022]	171.60 (-) [171.60]	82.13 (0.00) [0]
535	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [6/2022]	1,388.00 (-) [1,388.00]	1,255.00 (0.00) [0]
536	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [8/2022]	1,664.20 (-) [1,664.20]	1,301.27 (0.00) [28]
537	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (12/2022) [12/2022]	946.00 (1,046.56) [1,046.56]	822.13 (100.56) [54]
538	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (4/2021) [4/2021]	325.86 (-) [386.41]	347.42 (60.55) [0]
539	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (12/2020) [8/2022]	175.50 (241.60) [241.60]	164.41 (66.10) [66]
540	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (1/2022) [3/2023]	159.97 (-) [242.61]	94.29 (82.64) [45]
541	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2022]	993.16 (-) [1,434.00]	1,319.54 (440.84) [0]
542	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [6/2022]	831.58 (-) [1,177.00]	912.41 (345.42) [0]
543	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [9/2022]	2,177.80 (-) [2,450.00]	2,691.86 (272.20) [-]
544	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [10/2022]	1,995.34 (-) [2,400.00]	3,568.04 (404.66) [-]
545	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (12/2021) [10/2022]	165.67 (-) [165.67]	124.52 (0.00) [83]
546	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [9/2019]	709.00 (-) [709.00]	541.35 (0.00) [0]
547	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [6/2022]	950.69 (-) [1,108.00]	1,529.21 (157.31) [0]
548	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (3/2021) [6/2022]	396.96 (-) [396.96]	272.96 (0.00) [0]
549	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (3/2021) [9/2022]	314.90 (-) [314.90]	206.30 (0.00) [66]
550	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT	1/2017	9/2017 (4/2021) [12/2022]	264.34 (-) [264.34]	181.38 (0.00) [63]
551	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (4/2021) [4/2021]	191.60 (-) [191.60]	108.94 (0.00) [0]
552	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (1/2021) [7/2022]	291.49 (-) [291.49]	217.77 (0.00) [0]
553	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE	1/2017	9/2017 (-)	166.67 (-)	181.38 (97.67)

	CROSS – PA		[7/2022]	[264.34]	[0]
554	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (7/2021) [7/2022]	297.30 (-) [318.28]	246.53 (20.98) [0]
555	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (3/2021) [6/2022]	159.70 (-) [159.70]	122.11 (0.00) [0]
556	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (12/2021) [9/2022]	159.12 (-) [159.12]	123.72 (0.00) [80]
	<u>Urban Development</u>				
557	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B	6/2021	6/2026 (-) [6/2026]	14,788.10 (-) [14,788.10]	2,942.84 (0.00) [0]
558	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2021 (-) [3/2025]	26,405.14 (-) [26,405.14]	22,869.55 (0.00) [49]
	<u>KERALA</u>				
	<u>Department Of Higher Education</u>				
559	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [3/2023]	753.63 (-) [753.63]	291.95 (0.00) [24]
560	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [10/2012]	165.23 (-) [165.23]	136.31 (0.00) [0]
	<u>Health And Family Welfare</u>				
561	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	88.39 (0.00) [0]
	<u>Petroleum</u>				
562	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (2/2023) [2/2023]	1,112.00 (1,507.24) [1,507.24]	972.00 (395.24) [44]
563	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [12/2022]	607.06 (1,236.00) [1,236.00]	684.72 (628.94) [62]
	<u>Railways</u>				
564	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [3/2024]	1,431.90 (-) [1,431.90]	1,019.34 (0.00) [-]
565	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [3/2025]	1,000.00 (1,281.63) [1,339.00]	0.91 (339.00) [-]
	<u>Road Transport And Highways</u>				
566	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (1/2020) [1/2020]	845.24 (-) [941.00]	910.78 (95.76) [0]
567	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (12/2021) [7/2022]	804.97 (-) [804.97]	615.73 (0.00) [0]
568	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (5/2021) [3/2023]	1,124.11 (-) [1,309.79]	1,162.72 (185.68) [66]
569	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [1/2024]	1,424.77 (1,862.77) [1,862.77]	192.01 (438.00) [-]
570	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [3/2022]	617.00 (-) [617.00]	0.00 (0.00) [0]
571	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN	2/2017	8/2017 (3/2022)	294.28 (296.53)	211.30 (2.25)

	PALAKK		[0/0]	[296.53]	[0]
572	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49)	2/2017	9/2017 (1/2022) [0/0]	380.76 (372.87) [372.87]	312.49 (-7.89) [0]
	<u>Urban Development</u>				
573	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (9/2020) [0/0]	5,181.79 (-) [6,218.14]	6,065.85 (1,036.35) [0]
	<u>LADAKH</u>				
	<u>Civil Aviation</u>				
574	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (12/2023) [12/2023]	346.27 (-) [480.33]	192.21 (134.06) [27]
	<u>Road Transport And Highways</u>				
575	KARGIL-ZANSKR PACKAGE-1	3/2021	1/2023 (-) [1/2023]	384.23 (-) [384.23]	21.95 (0.00) [0]
576	KARGIL-ZANSKR PACKAGE-2	3/2021	1/2023 (-) [1/2023]	404.89 (-) [404.89]	1.98 (0.00) [0]
577	KARGIL-ZANSKR PACKAGE-3	8/2020	1/2023 (-) [1/2023]	381.01 (-) [381.01]	16.77 (0.00) [0]
578	KARGIL-ZANSKR PACKAGE-5	8/2020	12/2023 (-) [12/2023]	169.79 (-) [169.79]	103.72 (0.00) [0]
579	KARGIL-ZANSKR PACKAGE-6	1/2021	5/2024 (-) [5/2024]	239.81 (-) [239.81]	81.30 (0.00) [0]
580	KARGIL-ZANSKR PACKAGE-7	1/2021	6/2024 (-) [6/2024]	308.86 (-) [308.86]	80.00 (0.00) [0]
581	KARGIL-ZANSKR PACKAGE-8	3/2021	1/2023 (-) [1/2023]	398.37 (-) [398.37]	28.25 (0.00) [0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
582	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01	10/2021	8/2023 (-) [8/2023]	446.12 (-) [446.12]	40.91 (0.00) [0]
583	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021 (3/2023) [3/2023]	412.24 (-) [412.24]	284.51 (0.00) [21]
	<u>Coal</u>				
584	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021 (3/2025) [3/2025]	869.44 (-) [869.44]	163.63 (0.00) [48]
585	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
586	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	2.24 (0.00) [0]
587	BATURA WEST OC PROJECT (0.80 MTY)	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]
588	BLOCK-B EXPANSION OPENCASE PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	6.55 (0.00) [0]
589	DHANKASA UG (RECAST) (1 MTY)	2/2020	3/2025 (-)	289.30 (-)	40.60 (0.00)

			[3/2025]	[289.30]	[0]
590	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2023]	1,255.17 (-) [1,255.17]	846.30 (0.00) [12]
591	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	21.89 (0.00) [0]
592	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2023]	1,783.09 (-) [1,783.09]	1,197.65 (0.00) [24]
593	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	87.70 (0.00) [36]
594	NIGAH EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	36.27 (0.00) [0]
595	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2024]	357.80 (-) [357.80]	86.97 (0.00) [36]
596	RAMPUR BATURA OC (4.0 MTY)	7/2019	3/2026 (-) [3/2026]	1,248.93 (-) [1,248.93]	297.19 (0.00) [0]
597	RPR FOR JAMUNIA UG	8/2020	3/2026 (-) [3/2026]	281.25 (-) [281.25]	22.91 (0.00) [0]
598	TAWA III UG MINE	12/2021	3/2027 (-) [3/2027]	324.25 (-) [324.25]	10.20 (0.00) [0]
599	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
600	CGD PROJECT AT REWA DISTRICT	10/2018	2/2027 (9/2028) [9/2028]	177.00 (-) [177.00]	82.58 (0.00) [19]
	<u>Power</u>				
601	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2022]	2,104.21 (-) [1,587.16]	742.49 (-517.05) [24]
	<u>Railways</u>				
602	ANUPPUR-KATNI	4/2015	12/2021 (12/2023) [12/2023]	1,370.00 (-) [1,370.94]	918.24 (0.94) [24]
603	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [9/2022]	1,485.85 (-) [1,835.83]	2,340.59 (349.98) [21]
604	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [640.75]	497.73 (-59.25) [33]
605	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [10/2024]	1,763.93 (2,445.30) [2,445.30]	1,720.50 (681.37) [55]
606	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [9/2024]	582.13 (-) [1,247.64]	704.97 (665.51) [30]
607	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (3/2024) [3/2024]	2,478.23 (2,938.00) [2,938.00]	1,450.69 (459.77) [24]
608	NIMACH BADI SADRI NEW LINE PROJECT	4/2017	3/2022 (3/2026) [3/2026]	495.18 (495.18) [495.18]	1.01 (0.00) [48]

609	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2024) [3/2024]	424.60 (-) [2,909.99]	1,658.34 (2,485.39) [36]
610	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2026) [3/2026]	3,503.69 (5,839.02) [6,383.82]	2,529.21 (2,880.13) [48]
	Road Transport And Highways				
611	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (8/2021) [10/2022]	249.05 (-) [249.05]	219.86 (0.00) [51]
612	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	11/2019	7/2021 (-) [7/2023]	716.00 (-) [716.00]	0.00 (0.00) [24]
613	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	326.56 (0.00) [0]
614	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [3/2023]	950.27 (-) [950.27]	454.01 (0.00) [-]
615	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [10/2022]	392.33 (-) [428.55]	404.69 (36.22) [55]
616	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (3/2021) [9/2022]	390.51 (-) [390.51]	314.69 (0.00) [-]
617	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	689.00 (183.02) [-]
618	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [8/2022]	743.88 (-) [743.89]	721.00 (0.01) [-]
619	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [8/2022]	1,094.97 (-) [1,094.97]	1,097.00 (0.00) [-]
620	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [10/2022]	217.96 (-) [884.00]	797.00 (666.04) [-]
621	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (12/2021) [11/2022]	205.05 (-) [205.05]	137.88 (0.00) [68]
622	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (11/2021) [12/2022]	264.50 (-) [264.50]	179.94 (0.00) [21]
623	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	538.44 (0.00) [0]
624	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (8/2021) [9/2022]	957.54 (-) [927.73]	784.39 (-29.81) [31]
625	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
626	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [12/2022]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [116]
627	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (6/2021) [9/2022]	628.45 (-) [628.45]	467.04 (0.00) [32]
628	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	410.72 (-) [410.72]	392.45 (0.00) [0]

629	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [8/2022]	990.97 (-) [990.97]	1,020.00 (0.00) [32]
630	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [8/2022]	1,047.00 (-) [1,047.00]	879.00 (0.00) [27]
631	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [8/2022]	847.00 (-) [847.00]	908.00 (0.00) [29]
632	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [8/2022]	996.27 (-) [996.27]	965.00 (0.00) [29]
633	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (3/2022) [5/2023]	169.63 (-) [169.63]	89.32 (0.00) [62]
634	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (4/2021) [9/2022]	877.79 (-) [949.54]	807.22 (71.75) [39]
635	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (5/2021) [9/2022]	809.16 (-) [809.16]	635.00 (0.00) [50]
636	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (6/2021) [12/2022]	511.83 (-) [511.83]	432.54 (0.00) [64]
637	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (3/2022) [10/2022]	254.17 (-) [254.17]	197.45 (0.00) [56]
638	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [10/2022]	233.04 (-) [233.04]	184.37 (0.00) [55]
639	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (11/2021) [6/2022]	279.44 (-) [279.44]	231.61 (0.00) [0]
640	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (8/2021) [10/2022]	166.21 (-) [174.90]	154.26 (8.69) [50]
641	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (9/2021) [11/2022]	184.62 (-) [184.62]	141.48 (0.00) [57]
642	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (9/2021) [12/2022]	214.69 (-) [214.69]	90.24 (0.00) [57]
643	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (9/2021) [10/2022]	217.22 (-) [226.88]	206.89 (9.66) [50]
644	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [10/2022]	162.56 (-) [162.56]	137.52 (0.00) [55]
645	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (9/2021) [9/2021]	373.82 (-) [373.82]	244.81 (0.00) [0]
<u>Social Justice</u>					
646	CENTRE FOR DISABILITY SPORTS	2/2019	3/2024 (-) [3/2024]	170.99 (-) [170.99]	73.80 (0.00) [0]
<u>Urban Development</u>					
647	BHOPAL METRO RAIL	11/2018	2/2023 (5/2025) [5/2025]	6,941.40 (-) [6,941.40]	244.26 (0.00) [27]
648	INDORE METRO RAIL	11/2018	2/2023 (7/2025)	7,500.80 (-)	261.39 (0.00)

			[7/2025]	[7,500.80]	[29]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
649	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (8/2023) [8/2023]	475.39 (-) [475.39]	248.29 (0.00) [28]
650	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM	6/2017	12/2020 (-) [9/2023]	255.68 (-) [255.68]	202.60 (0.00) [33]
	<u>Coal</u>				
651	DINESH (MAKARDHOKDA-III) OC (8.0 MTY)	2/2020	3/2027 (-) [3/2027]	1,184.33 (-) [1,184.33]	511.36 (0.00) [0]
652	ADASA UG TO OC (1.50 MTY)	11/2018	3/2024 (-) [3/2024]	333.43 (-) [333.43]	173.40 (0.00) [0]
653	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY)	9/2018	3/2024 (-) [3/2024]	313.34 (-) [313.34]	169.46 (0.00) [0]
654	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	465.37 (0.00) [0]
655	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (9/2022) [9/2022]	252.71 (-) [252.71]	108.78 (0.00) [18]
656	BHANEGAON OC (1MTY)	2/2017	3/2023 (-) [3/2023]	409.68 (-) [409.68]	93.68 (0.00) [0]
657	BHATADI EXPANSION OC	2/2020	3/2028 (-) [3/2028]	729.86 (-) [729.86]	149.25 (0.00) [0]
658	BHATADI EXPASION OC (0.975 MTY)	2/2016	3/2019 (-) [9/2026]	327.41 (-) [327.41]	176.39 (0.00) [90]
659	DHUPTALA OC(SASTI UG TO OC)	2/2019	3/2028 (-) [3/2028]	720.87 (-) [720.87]	131.28 (0.00) [0]
660	GAURI PAUNI EXPANSION OC	8/2020	3/2029 (-) [3/2029]	337.38 (-) [337.38]	48.04 (0.00) [0]
661	GHONSA EXPANSION DEEP OC	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	57.00 (0.00) [0]
662	MAKARDHOKDA I EXPANSION OC	6/2022	3/2026 (-) [3/2026]	497.06 (-) [497.06]	135.18 (0.00) [0]
663	MUNGOLI NIRGUDA EXTENSION (DEEP) OC	11/2020	3/2026 (-) [3/2026]	826.80 (-) [826.80]	314.10 (0.00) [0]
664	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2022]	295.56 (-) [295.56]	220.94 (0.00) [0]
665	SAONER UG MINE I EXPANSION	1/2022	3/2028 (-) [3/2028]	253.51 (-) [253.51]	24.86 (0.00) [0]
666	SASTI EXPANSION OC	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	52.55 (0.00) [0]
667	SINGHORI DEEP OC	5/2022	3/2029 (-) [3/2029]	421.84 (-) [421.84]	86.08 (0.00) [0]

668	UKNI DEEP OC	11/2018	3/2021 (-) [9/2022]	318.14 (-) [318.14]	237.84 (0.00) [18]
	<u>Department Of Higher Education</u>				
669	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [7/2020]	223.37 (-) [223.37]	61.35 (0.00) [0]
	<u>Fertilisers</u>				
670	AN MELT PROJECT AT RCF TROMBAY	5/2022	9/2024 (-) [7/2024]	187.27 (-) [187.27]	0.80 (0.00) [-2]
	<u>Health And Family Welfare</u>				
671	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [12/2021]	582.99 (-) [582.99]	562.03 (0.00) [0]
672	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	259.46 (0.00) [0]
	<u>Petroleum</u>				
673	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [9/2022]	249.26 (-) [249.26]	249.10 (0.00) [27]
674	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [12/2022]	348.00 (437.00) [437.00]	271.34 (89.00) [23]
675	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI	5/2022	3/2024 (-) [3/2024]	423.39 (-) [423.39]	36.46 (0.00) [0]
676	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2022) [12/2022]	861.79 (2,001.34) [2,001.34]	1,680.76 (1,139.55) [115]
677	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL	4/2021	6/2024 (-) [6/2024]	1,164.69 (-) [1,164.69]	58.88 (0.00) [0]
678	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (12/2022) [12/2022]	2,292.46 (-) [2,292.46]	2,311.32 (0.00) [19]
679	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY	9/2021	10/2023 (-) [10/2023]	378.00 (-) [378.00]	60.31 (0.00) [0]
680	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (3/2023) [3/2023]	2,494.68 (-) [2,494.68]	2,141.49 (0.00) [12]
681	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R	8/2020	3/2023 (-) [3/2023]	697.00 (-) [697.00]	486.80 (0.00) [0]
682	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (8/2022) [12/2022]	1,945.00 (2,145.00) [2,145.00]	1,801.97 (200.00) [10]
683	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2023) [5/2023]	3,190.69 (3,375.90) [3,375.90]	2,911.17 (185.21) [61]
684	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	2,816.87 (747.87) [14]
685	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (12/2022) [12/2022]	763.92 (-) [829.58]	830.87 (65.66) [24]
686	PIPELINE REPLACEMENT PROJECT - VII	1/2022	5/2024 (-) [5/2024]	3,183.58 (-) [3,183.58]	123.40 (0.00) [0]

687	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND	5/2019	4/2025 (-) [4/2025]	8,797.00 (-) [8,797.00]	397.00 (0.00) [0]
	Power				
688	BIKANER SOLAR POWER PROJECT	4/2022	5/2024 (-) [5/2024]	5,491.89 (532.00) [6,023.89]	791.28 (532.00) [0]
	Railways				
689	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2025]	2,271.50 (-) [4,805.17]	3,140.43 (2,533.67) [48]
690	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2023]	495.44 (-) [2,980.41]	1,991.80 (2,484.97) [228]
691	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2025]	1,876.00 (-) [2,081.27]	881.45 (205.27) [24]
692	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [7/2022]	713.48 (-) [2,725.00]	3,066.34 (2,011.52) [0]
693	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	657.66 (0.00) [12]
694	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2025]	792.89 (-) [1,387.52]	464.66 (594.63) [48]
695	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	542.40 (0.00) [24]
696	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [3/2024]	265.88 (-) [311.36]	0.00 (45.48) [-]
697	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [0/0]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]
698	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2024]	3,627.47 (3,627.00) [4,670.00]	2,229.23 (1,042.53) [0]
699	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (-) [3,176.60]	1,902.75 (1,268.09) [9]
700	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [3/2024]	217.38 (-) [393.62]	219.72 (176.24) [-]
701	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2024]	229.00 (-) [1,096.00]	88.40 (867.00) [36]
702	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	313.34 (0.00) [12]
703	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2024]	1,272.19 (-) [1,384.72]	629.92 (112.53) [24]
704	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2024]	3,168.29 (-) [3,445.48]	1,543.90 (277.19) [12]
705	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	365.59 (0.00) [24]
	Road Transport And Highways				
706	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017	972.50	1,492.00

			(-) [10/2019]	(-) [972.50]	(0.00) [0]
707	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (6/2022) [6/2022]	621.00 (595.00) [595.00]	595.00 (-26.00) [0]
708	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [12/2022]	923.04 (-) [923.04]	869.13 (0.00) [73]
709	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (7/2022) [7/2024]	744.64 (-) [982.00]	0.00 (237.36) [52]
710	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (12/2021) [9/2022]	1,071.61 (-) [1,048.10]	1,251.13 (-23.51) [-]
711	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [12/2022]	446.17 (-) [446.17]	242.52 (0.00) [45]
712	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [7/2021]	1,142.62 (1,907.03) [1,142.62]	978.04 (0.00) [0]
713	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [3/2023]	1,101.58 (-) [1,101.58]	395.64 (0.00) [-]
714	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [6/2022]	400.25 (-) [400.25]	259.11 (0.00) [0]
715	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (8/2022) [11/2022]	1,064.88 (-) [1,021.00]	627.92 (-43.88) [-]
716	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [6/2022]	1,059.73 (-) [1,071.00]	0.00 (11.27) [0]
717	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (-) [3/2022]	505.00 (-) [504.00]	550.48 (-1.00) [0]
718	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [6/2022]	422.38 (-) [422.38]	243.81 (0.00) [0]
719	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [8/2021]	955.40 (-) [955.40]	492.20 (0.00) [0]
720	AKOLA TO AKOT	1/2017	6/2019 (-) [9/2022]	313.95 (-) [313.95]	142.29 (0.00) [39]
721	AKOT TO ANJANGAON	1/2017	6/2019 (-) [11/2020]	245.77 (246.00) [245.77]	220.54 (0.00) [0]
722	AMD I TO SAONER	1/2017	6/2019 (-) [2/2020]	396.91 (397.00) [396.91]	289.79 (0.00) [0]
723	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2022]	426.06 (426.00) [426.06]	247.48 (0.00) [0]
724	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [6/2022]	309.94 (310.00) [309.94]	207.17 (0.00) [0]
725	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [6/2022]	456.32 (-) [456.32]	341.63 (0.00) [0]
726	BAMNI TO NAVAEGAON	9/2017	4/2020 (-)	241.69 (242.00)	172.01 (0.00)

			[3/2021]	[241.69]	[0]
727	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [3/2022]	289.11 (290.00) [289.11]	144.69 (0.00) [0]
728	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [12/2020]	259.55 (260.00) [259.55]	215.68 (0.00) [0]
729	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [12/2019]	392.83 (393.00) [392.83]	274.75 (0.00) [0]
730	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [9/2022]	743.21 (743.00) [743.21]	475.80 (0.00) [15]
731	BHOKAR TO SARSAM	2/2017	7/2019 (-) [11/2020]	295.09 (-) [295.99]	186.27 (0.90) [0]
732	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [11/2020]	178.26 (-) [178.26]	159.96 (0.00) [0]
733	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [3/2021]	206.97 (207.00) [206.97]	145.87 (0.00) [0]
734	CHIKALI TO DHAD	3/2018	12/2019 (-) [6/2022]	189.46 (189.00) [189.46]	111.73 (0.00) [0]
735	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [1/2020]	548.03 (548.00) [548.03]	406.13 (0.00) [0]
736	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2020]	393.10 (393.00) [393.10]	253.71 (0.00) [0]
737	CHIMUR TO WARORA	11/2016	3/2019 (-) [6/2022]	467.70 (-) [467.70]	223.35 (0.00) [0]
738	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [10/2023]	1,162.92 (1,182.87) [1,182.87]	84.54 (19.95) [-]
739	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2022) [12/2022]	649.50 (-) [649.50]	277.75 (0.00) [45]
740	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (2/2022) [3/2022]	291.53 (-) [291.53]	264.99 (0.00) [0]
741	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH- 53 (OLD NH-6)	3/2018	/ (2/2022) [2/2022]	289.21 (-) [289.21]	240.40 (0.00) [0]
742	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (12/2022) [6/2022]	593.26 (-) [717.24]	662.98 (123.98) [0]
743	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [12/2022]	531.13 (480.35) [777.03]	766.05 (245.90) [55]
744	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [6/2019]	168.30 (-) [168.30]	100.56 (0.00) [0]
745	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [11/2022]	247.02 (-) [157.49]	31.97 (-89.53) [32]
746	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (414.00) [414.00]	399.23 (-0.51) [0]

747	DAHEGAON TO KUHI	1/2017	6/2019 (-) [9/2020]	228.89 (229.00) [228.89]	154.82 (0.00) [0]
748	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [9/2020]	182.63 (-) [182.63]	137.99 (0.00) [0]
749	DEORI TO AMGAON	1/2017	5/2019 (-) [6/2022]	409.62 (410.00) [409.62]	290.44 (0.00) [0]
750	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	146.73 (0.00) [0]
751	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [3/2022]	336.21 (336.00) [336.21]	234.29 (0.00) [0]
752	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [6/2021]	217.14 (217.00) [217.14]	153.92 (0.00) [0]
753	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [3/2022]	391.06 (391.00) [391.06]	256.99 (0.00) [0]
754	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [6/2022]	456.45 (-) [456.45]	425.07 (0.00) [0]
755	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [6/2022]	642.13 (-) [807.00]	760.42 (164.87) [0]
756	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (3/2022) [3/2022]	904.16 (-) [904.16]	0.00 (0.00) [0]
757	GADCHIROLI TO MUL	12/2016	6/2019 (-) [3/2022]	484.15 (-) [484.15]	349.78 (0.00) [0]
758	HELWAK TO KARAD	2/2017	7/2019 (-) [7/2021]	416.99 (-) [416.99]	225.83 (0.00) [0]
759	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [6/2022]	294.87 (295.00) [294.87]	163.51 (0.00) [0]
760	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [2/2022]	355.17 (-) [355.17]	270.78 (0.00) [0]
761	INDAPUR TO VADPALE	1/2017	12/2019 (-) [6/2022]	1,202.52 (1,203.00) [1,202.52]	929.67 (0.00) [0]
762	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [3/2022]	461.96 (-) [461.96]	329.59 (0.00) [0]
763	JALGAON TO BHADGAON	1/2018	11/2019 (-) [1/2021]	307.54 (308.00) [307.54]	221.49 (0.00) [0]
764	JALGAON TO NANDURA	3/2018	12/2019 (-) [11/2020]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
765	JALKOT TO TOGRI	7/2018	8/2020 (-) [3/2022]	299.92 (300.00) [299.92]	186.89 (0.00) [0]
766	JINTUR TO PARBHANI	1/2017	/ (-) [9/2022]	356.66 (-) [356.66]	162.29 (0.00) [-]
767	KAIJ TO KUSALAM	1/2017	7/2019	554.78	317.29

			(-) [6/2022]	(-) [554.78]	(0.00) [0]
768	KALMAB TO RALEGAON	1/2017	6/2019 (-) [8/2020]	467.78 (-) [467.78]	467.78 (0.00) [0]
769	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (2,617.44) [1,338.13]	1,346.39 (0.00) [0]
770	KANTE TO WAKED	3/2016	11/2019 (-) [12/2022]	1,230.02 (1,230.00) [1,230.02]	664.06 (0.00) [37]
771	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [9/2022]	407.19 (407.00) [407.19]	323.02 (0.00) [39]
772	KARAD TO TAGAON	1/2017	6/2019 (-) [12/2022]	537.81 (538.00) [537.81]	237.00 (0.00) [42]
773	KARAD TO VITA	1/2018	12/2019 (-) [3/2022]	344.85 (245.00) [344.85]	260.80 (0.00) [0]
774	KARWANDI TO RAJURI	3/2018	12/2019 (-) [6/2022]	276.95 (277.00) [276.95]	160.17 (0.00) [0]
775	KATOL TO WARUD	1/2017	6/2019 (-) [1/2020]	463.62 (664.00) [463.62]	265.78 (0.00) [0]
776	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [3/2020]	249.29 (-) [249.29]	146.41 (0.00) [0]
777	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [9/2019]	203.21 (203.00) [203.21]	163.81 (0.00) [0]
778	KHERDA TO NAGZARI	3/2018	12/2019 (-) [9/2020]	181.30 (-) [181.30]	137.37 (0.00) [0]
779	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [12/2022]	594.75 (594.75) [606.75]	410.81 (12.00) [37]
780	KOLDE TO KHETIYA	1/2017	7/2019 (-) [3/2022]	509.18 (-) [509.18]	283.13 (0.00) [0]
781	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [6/2022]	281.78 (282.00) [281.78]	73.92 (0.00) [0]
782	KOTHARI TO DHANORA	9/2018	8/2020 (-) [9/2022]	301.38 (301.00) [301.38]	195.29 (0.00) [25]
783	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [6/2019]	406.51 (-) [406.51]	340.26 (0.00) [0]
784	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [12/2020]	225.25 (225.00) [225.25]	199.34 (0.00) [0]
785	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [3/2022]	307.63 (-) [307.63]	197.27 (0.00) [0]
786	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [7/2021]	243.45 (244.00) [243.45]	170.25 (0.00) [0]
787	LATUR TO PANGAON	3/2018	12/2019 (-)	336.47 (336.00)	203.39 (0.00)

			[12/2020]	[336.47]	[0]
788	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [12/2022]	237.40 (-) [237.40]	31.41 (0.00) [31]
789	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [4/2022]	256.15 (-) [256.15]	100.31 (0.00) [0]
790	MALEGAON TO RISOD	2/2018	12/2019 (-) [10/2020]	303.24 (303.00) [303.24]	198.53 (0.00) [0]
791	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2022]	322.55 (-) [322.55]	213.50 (0.00) [0]
792	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [3/2022]	457.52 (-) [457.52]	392.92 (0.00) [0]
793	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [2/2022]	222.13 (222.00) [222.13]	156.87 (0.00) [0]
794	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [3/2022]	228.54 (-) [228.54]	161.24 (0.00) [0]
795	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [6/2021]	418.36 (-) [418.36]	263.13 (0.00) [0]
796	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [3/2022]	486.19 (-) [486.19]	315.19 (0.00) [0]
797	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [3/2022]	232.77 (-) [232.77]	151.60 (0.00) [0]
798	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [3/2020]	322.48 (322.00) [322.48]	230.03 (0.00) [0]
799	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [9/2022]	488.60 (-) [488.60]	240.92 (0.00) [38]
800	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (1/2022) [12/2022]	731.89 (731.89) [732.34]	530.71 (0.45) [37]
801	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2020]	341.16 (341.00) [341.16]	247.86 (0.00) [0]
802	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [12/2019]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
803	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [6/2022]	162.34 (-) [162.34]	66.99 (0.00) [0]
804	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [12/2020]	376.72 (377.00) [376.72]	273.87 (0.00) [0]
805	NAGBHID TO ARMORI	9/2016	7/2019 (-) [11/2019]	269.05 (-) [269.05]	200.00 (0.00) [0]
806	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (7/2023) [7/2023]	546.00 (-) [546.00]	347.64 (0.00) [48]
807	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (10/2023) [10/2023]	591.66 (-) [591.66]	332.33 (0.00) [51]

808	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2021]	244.04 (244.00) [244.04]	177.32 (0.00) [0]
809	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2020]	274.50 (275.00) [274.50]	143.39 (0.00) [0]
810	NANDED TO JALKOT	12/2017	9/2019 (-) [6/2022]	456.93 (457.00) [456.93]	456.93 (0.00) [0]
811	NANDGAON TO MORSHI	1/2017	6/2019 (-) [11/2019]	385.87 (386.00) [385.87]	258.29 (0.00) [0]
812	NASHIK TO PETH	12/2015	11/2018 (-) [4/2021]	289.60 (-) [289.60]	210.10 (0.00) [0]
813	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [6/2022]	406.54 (407.00) [406.54]	193.70 (0.00) [0]
814	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [9/2022]	420.63 (421.00) [420.63]	209.61 (0.00) [28]
815	OMREGA TO AUSA	3/2018	12/2019 (-) [9/2021]	272.04 (272.00) [272.04]	272.04 (0.00) [0]
816	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [6/2022]	344.25 (344.00) [344.25]	177.10 (0.00) [0]
817	PAHUR TO BODHWAD	1/2017	5/2020 (-) [2/2022]	244.93 (-) [244.93]	167.44 (0.00) [0]
818	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [12/2022]	341.80 (-) [341.80]	203.09 (0.00) [42]
819	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [3/2022]	227.19 (227.00) [227.19]	141.92 (0.00) [0]
820	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [12/2022]	381.08 (302.00) [381.08]	21.02 (0.00) [31]
821	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [3/2022]	218.38 (-) [218.38]	175.69 (0.00) [0]
822	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [3/2022]	238.19 (238.00) [238.19]	190.37 (0.00) [0]
823	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2022]	205.72 (206.00) [205.72]	85.71 (0.00) [0]
824	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [9/2022]	983.14 (2,226.11) [983.14]	806.99 (0.00) [33]
825	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [6/2022]	420.57 (-) [420.57]	270.28 (0.00) [0]
826	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [3/2022]	170.00 (-) [170.00]	125.80 (0.00) [0]
827	PEN TO KHOPOLI	3/2018	3/2018 (-) [6/2022]	301.39 (302.00) [301.39]	147.64 (0.00) [0]
828	PIMPLA TO MANJARSUMBHA	1/2017	8/2019	595.77	332.72

			(-) [6/2022]	(-) [595.77]	(0.00) [0]
829	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [3/2022]	223.46 (-) [223.46]	68.00 (0.00) [0]
830	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [4/2022]	228.31 (-) [228.31]	100.97 (0.00) [0]
831	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [9/2022]	1,724.55 (-) [1,724.55]	2,919.69 (0.00) [114]
832	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [3/2022]	210.81 (-) [210.81]	210.81 (0.00) [0]
833	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	303.72 (0.00) [0]
834	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [9/2022]	225.81 (-) [225.81]	114.55 (0.00) [-]
835	RISOD TO HINGOLI	2/2018	12/2019 (-) [3/2022]	355.99 (-) [355.99]	247.60 (0.00) [0]
836	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [6/2022]	362.96 (-) [362.96]	215.12 (0.00) [0]
837	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [3/2022]	415.25 (415.25) [415.25]	273.34 (0.00) [0]
838	SANGOLA TO JATH	1/2018	12/2019 (-) [3/2022]	257.38 (257.00) [257.38]	166.31 (0.00) [0]
839	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [3/2021]	250.46 (-) [250.46]	174.16 (0.00) [0]
840	SARSAM TO KOTHARI	2/2016	7/2019 (-) [9/2022]	545.64 (-) [545.64]	216.28 (0.00) [38]
841	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [6/2022]	388.44 (-) [388.44]	213.91 (0.00) [0]
842	SATARA TO MHASWAD	1/2017	7/2019 (-) [9/2022]	653.46 (-) [653.46]	287.45 (0.00) [38]
843	SELDOH TO PANVAR	7/2018	5/2020 (-) [12/2022]	404.33 (404.00) [404.33]	114.51 (0.00) [31]
844	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [6/2022]	150.79 (-) [150.79]	59.88 (0.00) [0]
845	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [11/2020]	373.10 (373.00) [373.10]	320.45 (0.00) [0]
846	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [2/2022]	211.34 (-) [211.34]	136.33 (0.00) [0]
847	SHIRUR TO KHARDA	2/2017	6/2019 (-) [9/2022]	381.77 (-) [381.77]	186.62 (0.00) [39]
848	SHIVUR TO YEOLA	3/2018	12/2019 (-)	181.08 (-)	97.86 (0.00)

			[3/2022]	[181.08]	[0]
849	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [6/2022]	337.46 (-) [337.46]	262.43 (0.00) [0]
850	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [0/0]	404.94 (495.92) [404.94]	427.22 (0.00) [0]
851	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (5/2017) [9/2022]	290.73 (-) [359.60]	339.75 (68.87) [-]
852	TAKARKHED TO JALNA	9/2017	6/2019 (-) [11/2020]	417.90 (418.00) [417.90]	275.39 (0.00) [0]
853	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [3/2022]	264.41 (264.00) [264.41]	189.64 (0.00) [0]
854	TALGAON TO KALMATH	10/2016	3/2020 (-) [10/2020]	904.70 (1,428.09) [904.70]	969.90 (0.00) [0]
855	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [7/2019]	195.64 (196.00) [195.64]	116.92 (0.00) [0]
856	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [3/2022]	422.02 (422.00) [422.02]	302.13 (0.00) [0]
857	UPGRADATION OF ADHALGAON-JAMKHED SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH	11/2021	2/2022 (-) [2/2022]	223.35 (-) [223.35]	0.00 (0.00) [0]
858	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [6/2022]	1,598.47 (1,560.00) [1,598.47]	1,246.19 (0.00) [0]
859	VITA TO NAGAJ	3/2018	12/2019 (-) [6/2022]	304.58 (305.00) [304.58]	142.11 (0.00) [0]
860	WADI TO ASOLA	1/2017	9/2019 (-) [12/2022]	363.82 (364.00) [363.82]	109.56 (0.00) [39]
861	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [1/2021]	194.23 (194.00) [194.23]	134.91 (0.00) [0]
862	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [9/2022]	376.19 (-) [376.19]	113.66 (0.00) [40]
863	WAKED TO TALEGAON	2/2016	2/2019 (-) [11/2021]	1,244.75 (1,245.00) [1,244.75]	911.66 (0.00) [0]
864	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [12/2022]	362.46 (362.46) [361.70]	304.45 (-0.76) [37]
865	WARDHA TO ARVI	2/2018	4/2020 (-) [3/2022]	313.58 (-) [313.58]	229.05 (0.00) [0]
866	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [7/2021]	216.90 (217.00) [216.90]	160.37 (0.00) [0]
867	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [9/2020]	165.51 (-) [165.51]	133.93 (0.00) [0]
868	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [10/2022]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [104]

	<u>Urban Development</u>				
869	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	3/2020 (-) [12/2023]	23,136.00 (-) [33,406.00]	22,064.15 (10,270.00) [45]
870	NAGPUR METRO RAIL	8/2014	3/2018 (-) [3/2022]	8,680.00 (-) [9,759.79]	8,524.81 (1,079.79) [0]
871	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (3/2023) [3/2023]	11,420.00 (-) [11,420.00]	9,009.34 (0.00) [16]
	<u>Water Resources</u>				
872	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (12/2022) [0/0]	233.57 (-) [233.57]	196.88 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
873	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [14,322.79]	12,817.81 (9,868.62) [153]
	<u>Road Transport And Highways</u>				
874	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [12/2022]	167.95 (-) [167.95]	77.77 (0.00) [6]
875	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [12/2022]	292.24 (-) [292.24]	98.42 (0.00) [6]
876	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [12/2022]	365.53 (-) [365.53]	118.82 (0.00) [4]
877	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [12/2022]	167.95 (-) [167.95]	77.72 (0.00) [6]
878	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [11/2022]	177.76 (-) [177.76]	70.23 (0.00) [3]
879	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [8/2023]	673.27 (-) [673.27]	106.28 (0.00) [-2]
880	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	21.30 (0.00) [0]
881	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [9/2023]	467.00 (-) [467.00]	50.90 (0.00) [6]
882	IMPHAL - KHONGSANG PKG-4	8/2021	12/2023 (-) [12/2023]	579.63 (-) [579.63]	0.00 (0.00) [0]
883	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	46.79 (0.00) [0]
884	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	112.33 (0.00) [0]
885	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [0/0]	268.98 (-) [268.98]	22.08 (0.00) [0]
886	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [0/0]	228.97 (-) [228.97]	0.00 (0.00) [0]
887	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI	8/2020	4/2022 (-)	379.39 (-)	22.07 (0.00)

	SECTI		[2/2023]	[379.39]	[10]
888	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [3/2023]	471.00 (-) [471.00]	251.05 (0.00) [8]
889	MARAM - PEREN PKG-3	8/2021	5/2023 (-) [11/2023]	467.41 (-) [467.41]	20.74 (0.00) [6]
890	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	45.41 (0.00) [0]
891	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	68.82 (0.00) [0]
892	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	13.88 (0.00) [0]
893	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	27.58 (0.00) [0]
894	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]
895	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	14.79 (0.00) [0]
896	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	58.46 (0.00) [0]
897	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [4/2023]	234.08 (-) [234.08]	32.64 (0.00) [4]
898	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	16.45 (0.00) [0]
899	TAMENGLONG - MAHUR PKG-5	8/2021	5/2023 (-) [5/2023]	477.86 (-) [477.86]	14.26 (0.00) [0]
900	TAMENGLONG - MAHUR PKG-6	9/2021	5/2023 (-) [5/2023]	311.18 (-) [311.18]	22.84 (0.00) [0]
	<u>MEGHALAYA</u>				
	<u>Department Of Higher Education</u>				
901	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (12/2022) [12/2022]	484.32 (429.70) [429.70]	242.25 (-54.62) [99]
	<u>Doner</u>				
902	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	148.33 (0.00) [0]
	<u>Health And Family Welfare</u>				
903	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [6/2022]	363.99 (-) [363.99]	299.13 (0.00) [0]
	<u>Railways</u>				
904	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [8,324.28]	266.07 (7,417.82) [0]
	<u>Road Transport And Highways</u>				
905	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.79 (0.00) [0]

906	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [9/2022]	306.28 (-) [306.28]	165.99 (0.00) [40]
907	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	44.52 (0.00) [0]
908	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	327.61 (0.00) [0]
909	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	175.18 (0.00) [0]
910	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	87.95 (0.00) [0]
911	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2023]	157.86 (-) [157.86]	81.82 (0.00) [12]
912	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06	8/2020	2/2022 (-) [0/0]	302.88 (-) [302.88]	9.20 (0.00) [0]
913	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [11/2022]	553.51 (-) [553.51]	232.58 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
914	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [12/2023]	2,393.47 (-) [6,527.45]	5,330.91 (4,133.98) [117]
	<u>Road Transport And Highways</u>				
915	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [4/2022]	205.95 (-) [205.95]	164.98 (0.00) [0]
916	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2022) [0/0]	195.04 (434.65) [377.99]	400.65 (182.95) [0]
917	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (10/2022) [0/0]	186.96 (-) [322.24]	312.50 (135.28) [0]
918	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2022) [0/0]	193.69 (374.59) [327.92]	347.48 (134.23) [0]
919	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	60.68 (0.00) [0]
920	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	81.09 (0.00) [0]
921	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	134.55 (0.00) [0]
922	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	98.32 (0.00) [0]
923	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	163.52 (0.00) [0]
924	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	129.85 (0.00) [0]
925	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022	233.25	52.09

			(-) [12/2022]	(-) [233.25]	(0.00) [0]
926	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	163.89 (0.00) [0]
927	KEIFANG - TUVAI PKG-1	9/2021	5/2023 (-) [5/2023]	492.94 (-) [492.94]	19.53 (0.00) [0]
928	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	36.21 (0.00) [0]
929	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	33.38 (0.00) [0]
930	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	220.92 (0.00) [43]
931	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	234.97 (0.00) [45]
932	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	234.73 (0.00) [45]
933	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	237.48 (0.00) [43]
934	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	145.96 (0.00) [55]
935	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	182.20 (0.00) [48]
936	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	201.83 (0.00) [43]
937	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	271.82 (0.00) [46]
938	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2022) [0/0]	624.41 (1,109.88) [992.67]	1,021.46 (368.26) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
939	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	138.51 (0.00) [0]
940	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [9/2023]	328.00 (-) [328.00]	302.91 (0.00) [30]
941	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (319.76) [319.76]	259.10 (0.00) [0]
	<u>Dpiit</u>				
942	NATIONAL INDUSTRIAL CORRIDOR PROJECT	9/2011	3/2027 (3/2027) [3/2027]	20,084.00 (20,084.00) [20,084.00]	9,680.31 (0.00) [0]
	<u>Petroleum</u>				
943	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	3/2021 (6/2022) [10/2022]	1,823.00 (3,027.90) [3,027.90]	2,446.06 (1,204.90) [19]
944	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021	3,308.00	2,819.70

			(6/2023) [6/2023]	(-) [3,308.00]	(0.00) [18]
945	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	567.76 (0.00) [0]
946	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (11/2022) [11/2022]	3,437.00 (-) [3,048.00]	2,444.60 (-389.00) [23]
947	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS	6/2019	12/2029 (3/2030) [3/2030]	169.00 (-) [169.00]	48.73 (0.00) [3]
948	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	154.30 (0.00) [0]
949	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (6/2023) [6/2023]	1,030.65 (-) [1,030.65]	448.70 (0.00) [7]
950	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (8/2022) [8/2022]	2,677.00 (3,185.00) [3,185.00]	2,943.70 (508.00) [14]
951	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2025) [2/2025]	2,915.00 (5,909.00) [5,909.00]	3,570.80 (2,994.00) [146]
952	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	2,903.70 (0.00) [0]
953	NORTH EAST GAS GRID	11/2020	3/2024 (3/2024) [3/2024]	9,265.00 (9,265.00) [9,265.00]	2,431.15 (0.00) [0]
954	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (2/2023) [12/2022]	2,321.00 (3,338.00) [3,338.00]	3,250.17 (1,017.00) [24]
955	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (7/2023) [7/2023]	2,658.34 (-) [2,658.34]	918.30 (0.00) [12]
	Power				
956	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION.	3/2022	3/2023 (-) [3/2023]	176.22 (-) [176.22]	2.28 (0.00) [0]
957	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [3/2024]	4,754.42 (-) [9,129.32]	4,251.79 (4,374.90) [63]
958	EASTERN REGION STRENGTHENING SCHEME - XXIII	7/2020	6/2021 (-) [4/2022]	239.89 (-) [239.89]	163.02 (0.00) [0]
959	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (-) [4/2022]	522.29 (-) [546.36]	481.89 (24.07) [0]
960	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [8/2022]	3,500.00 (3,500.00) [3,994.00]	3,160.77 (494.00) [25]
961	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [12/2022]	235.53 (-) [235.53]	164.87 (0.00) [42]
962	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [12/2022]	322.30 (-) [322.30]	210.54 (0.00) [46]
963	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [12/2022]	197.40 (-) [197.40]	195.47 (0.00) [57]
964	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH	8/2017	2/2020	1,931.39	1,891.34

	TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN		(-) [4/2023]	(-) [2,635.55]	(704.16) [38]
965	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [1/2024]	5,111.33 (-) [6,700.00]	4,097.84 (1,588.67) [61]
966	NORTH EASTERN REGION STRENGTHENING SCHEME - III	9/2015	12/2017 (-) [12/2022]	167.31 (-) [167.31]	129.26 (0.00) [60]
967	NORTH EASTERN REGION STRENGTHENING SCHEME-XII	5/2021	3/2023 (-) [3/2023]	576.42 (-) [576.42]	54.00 (0.00) [0]
968	NORTHERN REGION SYSTEM STRENGTHENING - XL	2/2019	12/2020 (-) [3/2023]	572.98 (-) [572.98]	293.86 (0.00) [27]
969	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION	11/2018	11/2021 (-) [12/2022]	241.38 (-) [241.38]	223.80 (0.00) [13]
970	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR SOUTHERN REGION	11/2018	11/2021 (-) [9/2022]	173.94 (-) [173.94]	114.48 (0.00) [10]
971	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [11/2022]	379.95 (-) [379.95]	266.47 (0.00) [35]
972	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B	7/2022	6/2023 (-) [6/2023]	4,546.26 (-) [4,546.26]	21.50 (0.00) [0]
973	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C	7/2022	3/2025 (-) [3/2025]	186.19 (-) [186.19]	0.00 (0.00) [0]
974	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM	3/2022	12/2024 (-) [12/2024]	288.71 (-) [288.71]	0.00 (0.00) [0]
975	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	2/2022	9/2023 (-) [9/2023]	359.47 (-) [359.47]	9.29 (0.00) [0]
976	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	5/2022	11/2023 (-) [11/2023]	1,666.00 (-) [1,666.00]	0.00 (0.00) [0]
977	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM	2/2022	4/2025 (-) [4/2025]	318.12 (-) [318.12]	45.42 (0.00) [0]
	<u>Railways</u>				
978	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [0/0]	1,08,000.00 (-) [1,08,000.00]	30,489.68 (0.00) [0]
979	BANDEL-BOINCHI 3RD LINE	4/2011	/ (9/2021) [5/2022]	288.35 (-) [402.48]	548.37 (114.13) [0]
980	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [923.23]	2.46 (0.00) [0]
981	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [9/2022]	175.80 (-) [495.10]	376.37 (319.30) [-]
982	CHANDIGARH-BADDI	4/2007	3/2023 (-) [12/2025]	328.14 (-) [1,540.13]	242.09 (1,211.99) [33]
983	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [0/0]	295.00 (-) [800.00]	687.13 (505.00) [0]
984	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022	1,347.26	1,063.17

			(12/2024) [12/2024]	(1,524.68) [1,524.68]	(177.42) [33]
985	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2025) [3/2025]	1,640.04 (1,873.10) [1,873.10]	908.51 (233.06) [36]
986	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [10/2022]	365.17 (-) [439.30]	525.35 (74.13) [67]
987	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [9/2023]	336.91 (-) [791.39]	572.99 (454.48) [-]
988	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (3/2026) [12/2027]	2,030.50 (746.83) [746.83]	22.79 (-1,283.67) [-]
989	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [51,219.00]	31,304.00 (39,630.00) [0]
990	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	799.75 (932.64) [33]
991	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [7/2022]	678.54 (678.54) [1,010.00]	1,038.66 (331.46) [0]
992	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [2/2024]	1,614.59 (-) [1,878.00]	1,611.28 (263.41) [59]
993	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,875.71 (0.00) [36]
994	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2025]	1,856.95 (-) [1,952.68]	918.80 (95.73) [24]
995	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,427.33 (8,000.84) [202]
996	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2027]	120.70 (-) [2,084.48]	321.37 (1,963.78) [105]
997	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2023]	250.93 (-) [310.70]	470.90 (59.77) [-]
998	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2023]	1,723.00 (1.00) [3,421.35]	2,206.22 (1,698.35) [276]
999	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [10/2024]	414.84 (-) [983.55]	344.80 (568.71) [55]
1000	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [11/2024]	450.00 (-) [2,017.96]	845.23 (1,567.96) [148]
1001	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	3/2019	5/2023 (-) [12/2024]	1,866.31 (-) [1,866.31]	610.05 (0.00) [19]
1002	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2024]	242.22 (-) [471.00]	77.45 (228.78) [48]
1003	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [3/2023]	241.52 (-) [401.65]	342.82 (160.13) [-]
1004	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-)	1,798.00 (-)	1,050.40 (249.51)

			[12/2023]	[2,047.51]	[57]
1005	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [10/2022]	600.00 (-) [701.81]	476.01 (101.81) [31]
1006	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2023]	915.98 (-) [2,137.81]	558.15 (1,221.83) [12]
1007	RAYADURGA-TUMKUR NL	4/2007	/ (-) [12/2025]	2,062.30 (-) [2,404.03]	1,108.14 (341.73) [-]
1008	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [0/0]	16,592.00 (51,101.00) [51,101.00]	47,476.00 (34,509.00) [0]
	<u>Road Transport And Highways</u>				
1009	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (5/2022) [5/2022]	1,928.22 (-) [1,928.22]	1,890.04 (0.00) [0]
1010	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1011	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [962.00]	0.00 (-36.70) [0]
1012	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	3,379.45 (531.45) [105]
	<u>Shipping And Ports</u>				
1013	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	5,369.18 (4,633.81) [4,633.81]	2,160.50 (-735.37) [0]
	<u>Telecommunications</u>				
1014	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [6/2022]	13,334.00 (-) [13,334.00]	21,545.00 (0.00) [0]
1015	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021 (11/2021) [11/2022]	431.16 (461.42) [461.42]	107.44 (30.26) [17]
	<u>Urban Development</u>				
1016	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	9,900.05 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1017	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	1,781.77 (4,336.48) [132]
	<u>Road Transport And Highways</u>				
1018	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	137.74 (0.00) [0]
1019	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	119.22 (0.00) [48]
1020	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	195.15 (0.00) [0]
1021	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	365.94 (0.00) [0]
1022	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM	3/2018	9/2018 (-)	500.09 (-)	199.63 (0.00)

	EXISTING		[11/2022]	[500.09]	[50]
1023	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	94.03 (0.00) [0]
1024	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	96.39 (0.00) [0]
1025	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	64.96 (0.00) [0]
1026	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [0/0]	330.78 (-) [330.78]	98.59 (0.00) [0]
1027	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [0/0]	330.80 (-) [330.80]	63.26 (0.00) [0]
1028	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [10/2022]	278.95 (-) [278.95]	128.23 (0.00) [4]
1029	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [12/2022]	206.53 (-) [206.53]	95.95 (0.00) [6]
1030	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (12/2022) [9/2022]	217.35 (-) [217.35]	173.98 (0.00) [22]
1031	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	84.56 (0.00) [0]
1032	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [6/2023]	202.36 (-) [202.36]	15.41 (0.00) [14]
1033	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [12/2023]	277.44 (-) [277.44]	55.34 (0.00) [14]
1034	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	212.37 (0.00) [0]
1035	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	141.12 (0.00) [0]
1036	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	136.85 (0.00) [0]
1037	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [6/2022]	215.12 (-) [215.12]	127.87 (0.00) [0]
1038	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2022]	215.79 (-) [215.79]	86.37 (0.00) [51]
1039	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [6/2023]	272.89 (-) [272.89]	103.64 (0.00) [57]
1040	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [9/2018]	323.98 (-) [323.98]	0.00 (0.00) [0]
1041	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	157.06 (0.00) [0]
1042	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	134.89 (0.00) [0]

1043	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [0/0]	373.07 (-) [387.00]	364.31 (13.93) [0]
1044	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [0/0]	396.52 (-) [396.52]	321.87 (0.00) [0]
1045	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2016]	429.52 (-) [429.52]	0.00 (0.00) [0]
1046	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [11/2020]	336.25 (-) [369.96]	309.98 (33.71) [0]
1047	MERANGKONG-TAMLU-MON (MTM) PKG-5	7/2021	12/2023 (-) [12/2023]	161.73 (-) [161.73]	11.38 (0.00) [0]
1048	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	0.00 (0.00) [0]
1049	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	52.94 (0.00) [0]
1050	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	167.62 (-) [167.62]	142.40 (0.00) [0]
1051	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]
1052	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [3/2023]	315.63 (-) [315.63]	12.23 (0.00) [11]
1053	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	174.77 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1054	ANANTA OCP EXPANSION PH III	8/2008	3/2012 (-) [0/0]	228.08 (-) [314.71]	323.51 (86.63) [0]
1055	BALARAM EXPANSION OCP	8/2020	3/2029 (-) [3/2029]	3,504.21 (-) [3,504.21]	620.60 (0.00) [0]
1056	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	251.54 (0.00) [60]
1057	BHUBANESWARI EXPANSION OCP	8/2020	3/2031 (-) [3/2031]	3,145.45 (-) [3,145.45]	840.23 (0.00) [0]
1058	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2026]	1,375.38 (-) [1,375.38]	734.15 (0.00) [60]
1059	GOPALJI-KANIHA OCP	8/2020	3/2028 (-) [3/2028]	8,416.19 (-) [8,416.19]	1,280.15 (0.00) [0]
1060	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2024]	479.53 (-) [868.37]	874.49 (388.84) [132]
1061	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	934.50 (0.00) [0]
1062	KULDA EXPANSION OCP- 15 MTY	6/2014	3/2018 (-)	348.16 (-)	162.94 (0.00)

			[3/2026]	[348.16]	[96]
1063	NAINI COAL MINE	3/2020	3/2024 (-) [3/2024]	494.30 (-) [494.30]	282.84 (0.00) [0]
1064	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,355.67 (0.00) [0]
1065	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	2,803.48 (0.00) [0]
1066	SUBHADRA OCP	5/2021	3/2027 (3/2029) [0/0]	1,693.81 (-) [1,693.81]	543.47 (0.00) [0]
1067	TALABIRA II AND III OCP	7/2017	1/2027 (-) [1/2027]	2,401.07 (-) [2,401.07]	918.18 (0.00) [0]
	<u>Department Of Higher Education</u>				
1068	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [1/2023]	790.79 (-) [790.79]	394.21 (0.00) [10]
	<u>Mines</u>				
1069	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (1/2024) [1/2024]	4,103.00 (5,055.00) [5,055.00]	1,486.31 (952.00) [33]
1070	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (12/2023) [12/2023]	355.00 (581.00) [581.00]	96.18 (226.00) [37]
1071	POTTANGI BAUXITE MINES	5/2018	12/2024 (12/2024) [12/2024]	1,437.00 (1,381.00) [1,381.00]	334.32 (-56.00) [0]
1072	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (12/2023) [12/2023]	483.00 (483.00) [483.00]	59.47 (0.00) [32]
1073	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (11/2023) [11/2023]	534.00 (667.23) [667.23]	497.21 (133.23) [46]
	<u>Petroleum</u>				
1074	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (12/2022) [12/2022]	462.30 (543.00) [543.00]	291.80 (80.70) [15]
1075	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [8/2023]	243.53 (-) [243.53]	195.96 (0.00) [13]
1076	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [8/2023]	182.20 (-) [182.20]	115.16 (0.00) [13]
1077	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (11/2022) [11/2022]	1,933.00 (2,105.70) [2,105.70]	1,811.30 (172.70) [23]
1078	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (7/2022) [12/2022]	5,654.00 (-) [5,654.00]	3,885.24 (0.00) [14]
1079	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (9/2022) [3/2024]	3,361.00 (-) [3,361.00]	2,258.02 (0.00) [31]
1080	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [3/2023]	202.16 (-) [202.16]	129.65 (0.00) [8]
1081	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2023) [3/2023]	371.00 (427.10) [427.10]	99.98 (56.10) [6]

1082	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	1,266.59 (0.00) [0]
1083	LPG BP PROJECT KHORDHA	12/2016	12/2019 (1/2023) [1/2023]	161.59 (-) [161.59]	101.66 (0.00) [37]
1084	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (7/2022) [12/2022]	1,297.50 (-) [1,297.50]	1,004.24 (0.00) [14]
1085	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha	8/2019	8/2022 (6/2023) [6/2023]	1,607.00 (-) [1,607.00]	507.46 (0.00) [10]
	<u>Railways</u>				
1086	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2023]	942.95 (-) [1,552.26]	1,445.70 (609.31) [48]
1087	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2024]	843.04 (-) [843.04]	439.50 (0.00) [41]
1088	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2025]	1,172.92 (-) [1,172.92]	825.47 (0.00) [75]
1089	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [12/2025]	5,200.00 (-) [5,200.00]	0.00 (0.00) [69]
1090	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2024]	1,547.38 (-) [1,547.38]	834.54 (0.00) [24]
1091	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2025]	701.61 (-) [810.02]	179.43 (108.41) [76]
1092	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2022]	133.41 (207.00) [433.00]	455.39 (299.59) [165]
1093	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (12/2025) [12/2025]	2,923.13 (-) [3,791.66]	2,027.20 (868.53) [201]
1094	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	729.38 (0.00) [48]
1095	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [10/2022]	969.83 (-) [1,312.97]	1,264.07 (343.14) [31]
1096	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [9/2022]	948.04 (-) [2,009.00]	2,350.49 (1,060.96) [30]
1097	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [0/0]	1,111.99 (-) [1,539.28]	1,152.38 (427.29) [0]
1098	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [9/2022]	1,202.70 (-) [2,440.53]	2,202.65 (1,237.83) [91]
1099	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2025]	810.78 (1,928.07) [1,928.07]	1,027.78 (1,117.29) [45]
1100	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	2,712.78 (992.05) [24]
	<u>Road Transport And Highways</u>				
1101	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-)	1,282.94 (-)	705.46 (0.00)

			[8/2022]	[1,282.94]	[-]
1102	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [6/2023]	2,510.04 (-) [2,510.04]	658.95 (0.00) [46]
1103	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2022]	752.28 (-) [752.28]	379.01 (0.00) [-]
1104	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [10/2022]	1,069.65 (-) [1,069.65]	856.21 (0.00) [-]
1105	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [6/2022]	1,410.00 (-) [1,410.00]	0.00 (0.00) [0]
1106	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [3/2022]	1,008.96 (-) [1,008.96]	1,148.36 (0.00) [0]
1107	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [10/2022]	564.66 (-) [564.66]	452.72 (0.00) [-]
1108	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [10/2022]	476.56 (-) [476.56]	275.93 (0.00) [63]
1109	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [3/2023]	633.68 (-) [633.68]	320.00 (0.00) [-]
1110	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [7/2022]	953.09 (-) [953.09]	664.48 (0.00) [0]
1111	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [3/2022]	668.86 (-) [668.86]	505.36 (0.00) [0]
1112	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [10/2022]	614.48 (-) [614.48]	440.00 (0.00) [-]
1113	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2023]	503.88 (-) [503.88]	159.77 (0.00) [-]
1114	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2022]	1,288.07 (-) [1,420.00]	1,105.15 (131.93) [0]
1115	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [6/2023]	686.65 (-) [686.65]	316.00 (0.00) [-]
1116	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [6/2023]	686.65 (-) [686.65]	254.00 (0.00) [-]
1117	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [10/2022]	417.51 (-) [417.51]	320.13 (0.00) [-]
1118	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [3/2023]	999.00 (-) [999.00]	309.51 (0.00) [-]
1119	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (9/2022) [9/2022]	171.96 (172.00) [172.00]	108.00 (0.04) [75]
1120	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (-) [7/2022]	1,522.00 (-) [1,522.00]	636.05 (0.00) [0]
1121	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [2/2023]	1,047.00 (-) [1,047.00]	1,855.00 (0.00) [104]

1122	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [9/2022]	806.11 (-) [806.11]	665.33 (0.00) [-]
1123	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	183.94 (0.50) [0]
1124	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (6/2022) [6/2022]	191.08 (-) [191.08]	182.41 (0.00) [0]
1125	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (11/2022) [0/0]	287.70 (-) [287.70]	229.52 (0.00) [0]
1126	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (11/2022) [11/2022]	214.23 (-) [214.23]	138.74 (0.00) [51]
1127	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (11/2022) [11/2022]	223.50 (-) [223.50]	132.37 (0.00) [51]
1128	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (10/2022) [10/2022]	199.16 (-) [199.16]	101.34 (0.00) [50]
1129	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (11/2022) [0/0]	295.67 (-) [295.67]	203.61 (0.00) [0]
1130	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (11/2022) [11/2022]	206.88 (-) [206.88]	134.11 (0.00) [55]
	<u>Steel</u>				
1131	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP	1/2022	5/2025 (-) [5/2025]	970.18 (-) [970.18]	76.33 (0.00) [0]
1132	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023 (-) [5/2023]	377.18 (-) [377.18]	128.30 (0.00) [0]
	<u>PONDICHERRY</u>				
	<u>Health And Family Welfare</u>				
1133	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020 (-) [0/0]	195.00 (-) [195.00]	16.41 (0.00) [0]
	<u>PUNJAB</u>				
	<u>Department Of Higher Education</u>				
1134	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022 (-) [3/2023]	348.24 (-) [348.24]	81.58 (0.00) [10]
1135	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [12/2022]	430.00 (-) [387.83]	258.31 (-42.17) [31]
	<u>Health And Family Welfare</u>				
1136	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [0/0]	703.00 (-) [635.00]	575.00 (-68.00) [0]
1137	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [4/2021]	152.95 (-) [177.92]	171.90 (24.97) [0]
	<u>Petroleum</u>				
1138	BHATINDA SANGRUR PIPELINE	11/2021	4/2024 (-) [4/2024]	367.00 (-) [367.00]	7.07 (0.00) [0]
1139	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,421.46]	502.70 (0.00) [0]

	<u>Railways</u>				
1140	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	190.00 (0.00) [108]
	<u>Road Transport And Highways</u>				
1141	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [5/2021]	1,169.61 (-) [2,280.00]	1,330.39 (1,110.39) [0]
1142	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [904.82]	849.98 (15.58) [0]
1143	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [5/2022]	1,388.34 (-) [1,588.29]	739.00 (199.95) [0]
1144	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (3/2023) [3/2023]	754.54 (756.27) [665.19]	528.73 (-89.35) [36]
1145	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1	12/2020	1/2024 (4/2024) [1/2024]	733.00 (-) [733.00]	0.00 (0.00) [0]
1146	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH-	2/2021	4/2024 (-) [4/2024]	1,269.96 (-) [1,269.96]	0.00 (0.00) [0]
1147	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR-	2/2021	4/2024 (-) [4/2024]	853.66 (-) [853.66]	0.00 (0.00) [0]
1148	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO	12/2020	4/2024 (-) [4/2024]	1,094.46 (-) [1,094.46]	0.00 (0.00) [0]
1149	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI	12/2020	1/2024 (-) [4/2024]	989.66 (-) [989.66]	0.00 (0.00) [3]
1150	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO	12/2020	4/2024 (-) [4/2024]	1,234.40 (-) [1,234.40]	0.00 (0.00) [0]
1151	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO	12/2020	4/2024 (-) [4/2024]	881.00 (-) [881.00]	0.00 (0.00) [0]
1152	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (3/2023) [3/2023]	479.00 (479.00) [479.00]	456.80 (0.00) [-]
1153	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [12/2022]	1,069.59 (-) [1,069.59]	739.08 (0.00) [38]
1154	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [12/2022]	170.57 (192.48) [170.57]	87.84 (0.00) [25]
1155	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [10/2022]	293.64 (-) [293.64]	283.78 (0.00) [26]
1156	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [12/2022]	293.10 (-) [293.10]	256.89 (0.00) [28]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1157	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2023]	12,320.00 (17,079.00) [17,079.00]	14,876.00 (4,759.00) [84]
	<u>Coal</u>				
1158	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020 (-)	2,112.60 (-)	93.05 (0.00)

			[0/0]	[2,112.60]	[0]
1159	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]
1160	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020 (-) [0/0]	2,196.30 (-) [2,196.30]	112.92 (0.00) [0]
1161	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Petroleum</u>				
1162	LPG BP PROJECT JODHPUR	3/2018	/ (3/2023) [3/2023]	229.80 (-) [229.80]	130.21 (0.00) [-]
1163	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE	12/2021	10/2024 (-) [10/2024]	9,028.00 (-) [9,028.00]	58.89 (0.00) [0]
	<u>Power</u>				
1164	ANTA SOLAR 90 MW	1/2021	3/2022 (12/2023) [3/2023]	382.22 (-) [382.22]	36.61 (0.00) [12]
1165	BHENSARA 320 MW	1/2021	7/2022 (-) [8/2023]	1,221.73 (-) [1,221.73]	146.13 (0.00) [13]
1166	CHHATTARGARH 150 MW	2/2021	7/2022 (-) [8/2023]	599.99 (-) [599.99]	170.95 (0.00) [13]
1167	NOKH PLOT-1 SOLAR PV PROJECT 245MW	3/2022	8/2023 (10/2023) [10/2023]	1,352.71 (-) [1,352.71]	41.85 (0.00) [2]
1168	NOKH PLOT-2 SOLAR PV PROJECT 245MW	3/2022	8/2023 (10/2023) [10/2023]	1,409.52 (-) [1,409.52]	50.84 (0.00) [2]
1169	NOKH PLOT-3 SOLAR PV PROJECT 245MW	3/2022	8/2023 (10/2023) [10/2023]	1,426.94 (-) [1,426.94]	49.14 (0.00) [2]
1170	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (1/2023) [1/2023]	1,782.00 (-) [1,782.00]	1,146.84 (0.00) [16]
1171	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II AND BHAD	1/2020	1/2021 (-) [12/2022]	562.86 (-) [562.86]	374.60 (0.00) [23]
1172	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	12/2022 (-) [9/2023]	353.85 (-) [353.85]	134.19 (0.00) [9]
1173	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [12/2023]	713.82 (-) [713.82]	323.37 (0.00) [12]
1174	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [8/2023]	1,562.00 (-) [1,562.00]	500.90 (0.00) [8]
1175	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	5/2021	9/2022 (-) [1/2023]	1,184.88 (-) [1,184.88]	80.70 (0.00) [4]
1176	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [8/2023]	1,006.00 (-) [1,006.00]	660.83 (0.00) [8]
1177	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	12/2022 (-) [12/2022]	1,340.81 (-) [1,340.81]	626.81 (0.00) [0]
	<u>Railways</u>				

1178	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [6/2022]	410.08 (-) [860.41]	837.18 (450.33) [0]
1179	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [11/2022]	808.85 (-) [808.85]	638.86 (0.00) [3]
	Road Transport And Highways				
1180	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [5/2022]	530.07 (-) [530.07]	558.12 (0.00) [0]
1181	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG-	2/2021	11/2021 (-) [0/0]	240.99 (-) [240.99]	12.16 (0.00) [0]
1182	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II	8/2020	12/2020 (-) [0/0]	216.72 (-) [216.72]	81.28 (0.00) [0]
1183	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II.	12/2020	10/2021 (-) [0/0]	339.65 (-) [339.65]	63.00 (0.00) [0]
1184	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I.	12/2020	10/2021 (-) [0/0]	379.23 (-) [379.23]	46.00 (0.00) [0]
1185	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I.	7/2020	9/2021 (-) [0/0]	319.09 (-) [319.09]	15.53 (0.00) [0]
1186	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [3/2022]	1,031.95 (-) [1,031.95]	1,518.41 (0.00) [0]
1187	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [9/2022]	822.90 (-) [822.90]	844.08 (0.00) [53]
1188	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (10/2021) [12/2022]	741.86 (649.00) [649.00]	185.59 (-92.86) [-]
1189	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [12/2023]	1,308.73 (-) [1,308.73]	221.14 (0.00) [-]
1190	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (5/2022) [3/2022]	649.00 (-) [649.00]	724.30 (0.00) [0]
1191	FOUR LANNING OF DARAH JHALWAR TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [5/2022]	964.17 (1,140.64) [1,198.64]	1,053.15 (234.47) [0]
1192	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [6/2022]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1193	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020 (-) [0/0]	196.23 (-) [196.00]	84.00 (-0.23) [0]
1194	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [12/2022]	894.00 (-) [929.32]	880.00 (35.32) [32]
1195	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO	3/2020	8/2020 (-) [0/0]	255.23 (-) [255.23]	89.00 (0.00) [0]
1196	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	330.30 (0.00) [0]
1197	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	147.79 (0.00) [0]

	<u>SIKKIM</u>				
	<u>Power</u>				
1198	RANGIT IV HE PROJECT	3/2021	5/2024 (8/2024) [8/2024]	938.29 (938.29) [938.29]	315.06 (0.00) [3]
1199	TEESTA VI HE PROJECT	3/2019	3/2024 (-) [7/2025]	5,748.04 (-) [5,748.04]	1,748.06 (0.00) [16]
	<u>Railways</u>				
1200	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [7,876.92]	3,408.77 (6,537.44) [96]
	<u>Road Transport And Highways</u>				
1201	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (9/2023) [9/2023]	230.45 (-) [230.45]	32.58 (0.00) [5]
1202	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [5/2024]	493.42 (-) [493.42]	12.26 (0.00) [6]
1203	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	50.95 (0.00) [0]
1204	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	115.75 (0.00) [0]
1205	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [12/2022]	183.31 (-) [183.31]	87.22 (0.00) [7]
1206	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [1/2024]	262.84 (-) [262.84]	129.59 (0.00) [8]
1207	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM)	10/2021	5/2024 (-) [5/2024]	385.15 (-) [385.15]	8.95 (0.00) [0]
1208	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [4/2023]	375.80 (-) [375.80]	96.70 (0.00) [-]
1209	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [9/2022]	290.05 (-) [290.05]	175.49 (0.00) [58]
1210	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (11/2024) [11/2024]	816.79 (-) [816.79]	15.85 (0.00) [11]
1211	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	62.92 (0.00) [0]
1212	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [5/2023]	402.94 (-) [402.94]	118.12 (0.00) [13]
1213	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	84.58 (0.00) [0]
1214	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [12/2022]	242.97 (-) [242.97]	68.35 (0.00) [6]
1215	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [12/2022]	292.80 (-) [292.80]	52.83 (0.00) [7]
1216	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (6/2022) [6/2022]	388.00 (447.37) [530.67]	316.99 (142.67) [0]

1217	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	19.69 (0.00) [0]
1218	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (2/2024) [2/2024]	410.60 (-) [410.60]	21.94 (0.00) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1219	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6	6/2017	9/2027 (-) [9/2027]	49,621.00 (-) [49,621.00]	6,216.00 (0.00) [0]
1220	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	31,955.00 (0.00) [36]
1221	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (10/2022) [9/2024]	3,492.00 (6,840.00) [7,500.00]	6,433.54 (4,008.00) [168]
	<u>Civil Aviation</u>				
1222	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (12/2023) [3/2024]	380.87 (-) [380.87]	68.90 (0.00) [24]
1223	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (12/2024) [12/2024]	2,467.00 (-) [2,467.00]	1,048.18 (0.00) [34]
1224	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (4/2023) [4/2023]	951.28 (-) [951.28]	660.06 (0.00) [18]
	<u>Coal</u>				
1225	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [9/2027]	1,458.17 (-) [709.06]	526.60 (-749.11) [147]
1226	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (-) [7,980.79]	7,457.04 (2,073.68) [0]
	<u>Finance</u>				
1227	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (10/2022) [10/2022]	209.00 (-) [262.00]	208.93 (53.00) [36]
1228	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [0/0]	348.77 (-) [348.77]	270.69 (0.00) [0]
	<u>Mines</u>				
1229	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (12/2022) [12/2022]	166.62 (163.17) [163.17]	135.00 (-3.45) [42]
	<u>Petroleum</u>				
1230	CBR 9 MMTPA PROJECT	1/2021	6/2025 (-) [6/2025]	31,580.00 (-) [31,580.00]	698.40 (0.00) [0]
1231	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE	3/2022	11/2024 (-) [11/2024]	564.00 (-) [564.00]	0.00 (0.00) [0]
1232	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	234.49 (0.00) [0]
1233	CGD PROJECT AT SALEM DISTRICT	10/2018	3/2030 (-) [3/2030]	1,304.00 (-) [1,304.00]	65.64 (0.00) [0]
1234	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [2/2024]	921.00 (-) [921.00]	61.75 (0.00) [5]

1235	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (11/2023) [11/2023]	4,497.00 (6,025.00) [6,025.00]	4,938.92 (1,528.00) [59]
1236	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1237	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (9/2021) [12/2022]	650.82 (-) [650.82]	462.08 (0.00) [45]
1238	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI	1/2022	7/2024 (-) [7/2024]	827.00 (-) [827.00]	63.86 (0.00) [0]
1239	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [9/2022]	678.00 (1,472.00) [1,472.00]	19.51 (794.00) [67]
1240	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [2/2024]	1,398.00 (-) [1,398.00]	290.30 (0.00) [2]
	<u>Power</u>				
1241	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (11/2022) [10/2022]	1,316.22 (-) [1,316.22]	1,059.63 (0.00) [13]
1242	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [12/2022]	186.17 (-) [219.66]	172.19 (33.49) [41]
	<u>Railways</u>				
1243	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [12/2022]	495.74 (-) [774.51]	552.70 (278.77) [114]
1244	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [12/2022]	760.00 (-) [1,536.00]	1,664.15 (776.00) [33]
1245	MADURAI-BODINAYAKKANUR	4/2008	/ (9/2022) [9/2022]	164.41 (-) [591.00]	464.44 (426.59) [-]
1246	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [5/2023]	1,700.00 (-) [1,305.00]	1,284.85 (-395.00) [14]
1247	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [3,081.20]	1,774.56 (2,356.51) [73]
1248	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [12/2025]	582.83 (-) [3,500.79]	622.53 (2,917.96) [-]
	<u>Road Transport And Highways</u>				
1249	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [7/2022]	485.00 (-) [485.00]	293.45 (0.00) [0]
1250	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [3/2023]	624.00 (526.09) [526.09]	189.10 (-97.91) [107]
1251	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	929.50 (0.00) [0]
1252	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6	2/2022	8/2022 (-) [8/2022]	191.33 (-) [191.33]	0.00 (0.00) [0]
1253	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [2/2022]	600.00 (-) [600.00]	2.98 (0.00) [0]
1254	FOUR LANING OF KALAGAM TO KARUPPUR FROM	3/2018	/	1,016.92	492.86

	KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS		(-) [12/2022]	(1,282.30) [1,308.88]	(291.96) [-]
1255	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [9/2022]	628.71 (-) [628.71]	448.26 (0.00) [-]
1256	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM	3/2018	1/2022 (-) [1/2024]	2,120.40 (-) [2,120.40]	0.00 (0.00) [24]
1257	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [1/2024]	2,065.96 (-) [2,169.00]	0.00 (103.04) [-]
1258	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN	3/2018	10/2020 (-) [12/2023]	1,872.68 (-) [1,872.68]	0.00 (0.00) [38]
1259	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [12/2022]	1,166.26 (1,296.93) [1,422.13]	444.08 (255.87) [-]
1260	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [3/2022]	641.17 (-) [641.17]	430.39 (0.00) [0]
1261	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON	3/2018	11/2021 (-) [11/2023]	998.70 (-) [998.70]	0.00 (0.00) [24]
1262	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [12/2022]	505.35 (-) [505.35]	255.05 (0.00) [-]
1263	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	742.16 (0.00) [0]
1264	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2022]	707.82 (-) [707.82]	449.52 (0.00) [0]
1265	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [12/2022]	848.45 (-) [848.45]	252.08 (0.00) [33]
1266	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [3/2022]	641.17 (-) [641.17]	430.39 (0.00) [0]
1267	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER	3/2018	11/2021 (-) [11/2023]	1,294.47 (-) [1,294.47]	0.00 (0.00) [24]
1268	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	7/2020	12/2021 (-) [0/0]	3,426.00 (-) [5,852.00]	0.00 (2,426.00) [0]
1269	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [12/2022]	379.90 (-) [379.90]	261.83 (0.00) [-]
1270	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (5/2024) [5/2024]	1,250.00 (1,380.73) [1,380.73]	1,354.65 (130.73) [125]
1271	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1272	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [5/2022]	374.00 (-) [166.90]	98.45 (-207.10) [0]
1273	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (8/2023) [8/2023]	633.55 (664.10) [736.33]	68.39 (102.78) [-]
1274	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-)	563.92 (-)	63.30 (0.00)

			[5/2023]	[563.92]	[65]
1275	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (212.74) [240.38]	171.85 (0.00) [0]
1276	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8	8/2020	2/2021 (-) [0/0]	302.62 (-) [302.62]	166.72 (0.00) [0]
1277	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	276.41 (0.00) [0]
1278	WIDENING FROM TWO LANE TO TWO LANE WITH PAVED SHOULDER FROM KM 34/000 TO 49/000 AND TWO LANE TO FOUR	2/2022	8/2022 (-) [8/2022]	184.15 (-) [184.15]	0.00 (0.00) [0]
	<u>Urban Development</u>				
1279	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (2/2021) [0/0]	3,770.00 (-) [3,770.00]	2,549.19 (0.00) [0]
1280	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [18,380.00]	17,629.68 (3,780.00) [0]
	<u>TELANGANA</u>				
	<u>Civil Aviation</u>				
1281	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (3/2023) [3/2023]	353.61 (-) [353.61]	175.15 (0.00) [10]
	<u>Coal</u>				
1282	GODAVARIKHANI COAL MINE	7/2019	3/2023 (-) [3/2023]	438.98 (-) [438.98]	123.02 (0.00) [0]
1283	KAKATHIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2022 (-) [3/2024]	413.84 (-) [413.84]	346.68 (0.00) [24]
1284	RCE OF INDARAM OPENCAST PROJECT	8/2017	3/2021 (-) [3/2023]	349.28 (-) [349.28]	323.72 (0.00) [24]
1285	RCE OF KAKATHIYAKHANI OC - 2 PROJECT	8/2017	3/2020 (-) [3/2024]	442.42 (-) [442.42]	129.91 (0.00) [48]
1286	RCE OF KALYANIKHANI OPENCAST PROJECT	3/2016	3/2020 (-) [3/2023]	384.32 (-) [384.32]	171.52 (0.00) [36]
1287	RCE OF KISTARAM OPENCAST PROJECT	3/2017	3/2021 (-) [3/2023]	164.04 (-) [164.04]	143.08 (0.00) [24]
1288	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT	11/2015	3/2023 (-) [3/2023]	489.62 (-) [489.62]	341.71 (0.00) [0]
1289	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II	3/2019	3/2021 (-) [3/2023]	473.22 (-) [473.22]	392.38 (0.00) [24]
1290	SRP OC-II EXPANSION PROJECT	11/2016	3/2018 (-) [3/2024]	272.73 (-) [272.73]	153.75 (0.00) [72]
1291	VENKATESH KHANI COAL MINE	10/2020	3/2023 (-) [3/2024]	484.51 (-) [484.51]	36.25 (0.00) [12]
	<u>Health And Family Welfare</u>				
1292	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [0/0]	209.84 (-) [209.84]	228.52 (0.00) [0]
	<u>Petroleum</u>				

1293	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	193.17 (0.00) [16]
	<u>Power</u>				
1294	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [6/2023]	10,598.98 (-) [10,998.00]	9,540.00 (399.02) [31]
	<u>Railways</u>				
1295	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [9/2022]	632.68 (-) [950.00]	626.34 (317.32) [78]
1296	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (12/2022) [0/0]	636.38 (998.06) [998.06]	900.29 (361.68) [0]
1297	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [0/0]	119.73 (185.00) [242.28]	56.14 (122.55) [0]
1298	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2025]	1,160.48 (-) [2,250.00]	784.26 (1,089.52) [180]
	<u>Road Transport And Highways</u>				
1299	4-laning of Khammam-Ashwaraopet section of NH-365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1300	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (12/2022) [12/2022]	283.15 (-) [283.15]	201.27 (0.00) [31]
1301	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (5/2023) [5/2023]	626.76 (-) [626.76]	227.71 (0.00) [34]
1302	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.96 (0.00) [0]
1303	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [10/2022]	857.62 (-) [857.62]	561.95 (0.00) [-]
1304	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/ (-) [12/2021]	802.65 (-) [802.65]	527.89 (0.00) [0]
1305	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [10/2021]	950.63 (-) [950.63]	764.27 (0.00) [0]
1306	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (3/2021) [2/2023]	828.29 (1,140.50) [828.29]	287.90 (0.00) [-]
1307	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (6/2022) [6/2022]	192.67 (-) [192.67]	171.04 (0.00) [0]
1308	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (6/2021) [6/2021]	605.08 (-) [605.08]	411.93 (0.00) [0]
1309	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (7/2020) [7/2020]	426.52 (-) [426.52]	398.81 (0.00) [0]
1310	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (9/2019) [9/2019]	270.00 (-) [270.00]	7.65 (0.00) [0]
1311	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (3/2022) [3/2022]	294.13 (-) [294.13]	174.27 (0.00) [0]
1312	REHABILITATION AND UPGRADATION OF NH-167 FROM	2/2018	11/2019	220.28	193.45

	DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS		(6/2022) [6/2022]	(-) [220.28]	(0.00) [0]
1313	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (6/2022) [6/2022]	322.81 (-) [322.81]	294.69 (0.00) [0]
1314	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (12/2022) [12/2022]	295.47 (-) [295.47]	214.36 (0.00) [70]
1315	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (4/2023) [4/2023]	248.83 (-) [248.83]	149.11 (0.00) [49]
1316	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (6/2022) [6/2022]	298.32 (-) [298.32]	142.58 (0.00) [0]
1317	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (11/2020) [11/2020]	230.03 (-) [230.03]	222.85 (0.00) [0]
1318	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (1/2021) [1/2021]	206.13 (-) [206.13]	185.75 (0.00) [0]
1319	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (1/2023) [1/2023]	193.19 (249.72) [249.72]	184.91 (56.53) [-]
1320	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (10/2019) [10/2019]	196.52 (-) [196.52]	121.70 (0.00) [0]
1321	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019 (12/2019) [12/2019]	283.00 (-) [283.00]	250.42 (0.00) [0]
1322	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (8/2019) [8/2019]	244.54 (-) [244.54]	169.89 (0.00) [0]
1323	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT	1/2017	5/2019 (10/2020) [10/2020]	359.27 (-) [359.27]	311.81 (0.00) [0]
1324	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (7/2021) [7/2021]	300.00 (-) [300.00]	217.68 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1325	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2021) [12/2021]	438.28 (-) [402.00]	405.76 (-36.28) [0]
	<u>Petroleum</u>				
1326	CREATION OF GAS DEHYDRATION FACILITIES	3/2022	5/2024 (-) [5/2024]	209.33 (-) [209.33]	0.00 (0.00) [0]
	<u>Railways</u>				
1327	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [9/2022]	569.63 (-) [708.73]	380.92 (139.10) [30]
	<u>Road Transport And Highways</u>				
1328	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [12/2022]	201.99 (-) [201.99]	49.65 (0.00) [11]
1329	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [10/2022]	247.76 (-) [247.76]	67.01 (0.00) [9]
1330	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (8/2022) [8/2022]	347.36 (-) [347.36]	154.53 (0.00) [7]

1331	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [10/2022]	173.17 (-) [173.17]	21.34 (0.00) [6]
1332	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [1/2023]	165.54 (-) [165.54]	37.19 (0.00) [6]
1333	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (2/2023) [7/2022]	206.78 (-) [206.78]	43.98 (0.00) [0]
1334	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [12/2022]	280.91 (-) [280.91]	148.65 (0.00) [5]
1335	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [12/2022]	159.13 (-) [159.13]	30.58 (0.00) [6]
1336	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (11/2022) [12/2022]	332.14 (-) [332.14]	56.56 (0.00) [5]
1337	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	24.72 (0.00) [0]
1338	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (3/2023) [3/2023]	178.43 (-) [178.43]	28.82 (0.00) [8]
1339	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (3/2023) [7/2022]	154.51 (-) [154.51]	11.92 (0.00) [0]
1340	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [0/0]	277.50 (-) [277.50]	140.76 (0.00) [0]
1341	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	107.81 (38.51) [0]
1342	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	136.98 (0.00) [0]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1343	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2023]	1,383.00 (-) [2,445.00]	797.96 (1,062.00) [24]
1344	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01	3/2021	12/2022 (-) [12/2022]	242.14 (-) [242.14]	57.40 (0.00) [0]
	<u>Coal</u>				
1345	KHADIA EXPANSION OCP	6/2021	3/2025 (-) [3/2025]	491.67 (-) [491.67]	6.16 (0.00) [0]
1346	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2023]	17,237.00 (-) [17,237.80]	13,965.29 (0.80) [24]
	<u>Health And Family Welfare</u>				
1347	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [0/0]	785.00 (-) [760.00]	672.98 (-25.00) [0]
1348	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [5/2021]	268.84 (-) [284.67]	269.92 (15.83) [0]
	<u>Home Affairs</u>				
1349	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI	5/2019	1/2022 (3/2023)	199.31 (-)	98.57 (0.00)

			[3/2023]	[199.31]	[14]
	<u>Petroleum</u>				
1350	60 KTA POLYPROPYLENE PROJECT	3/2019	4/2024 (-) [4/2024]	910.56 (-) [910.56]	213.00 (0.00) [0]
1351	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	614.47 (0.00) [0]
1352	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (-) [8/2029]	3,450.20 (-) [3,450.20]	763.70 (0.00) [5]
1353	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (12/2022) [12/2022]	217.92 (-) [217.92]	126.20 (0.00) [20]
1354	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (11/2022) [11/2022]	255.40 (-) [255.40]	188.28 (0.00) [27]
1355	NEW LPG PLANT AT VARANASI	8/2017	5/2024 (-) [5/2024]	194.62 (-) [194.62]	61.25 (0.00) [0]
1356	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (3/2023) [3/2023]	318.80 (-) [318.80]	210.47 (0.00) [19]
	<u>Power</u>				
1357	DEVIKOT SOLAR 150MW	1/2020	9/2021 (11/2022) [9/2022]	798.24 (-) [852.90]	637.22 (54.66) [12]
1358	DEVIKOT SOLAR 90MW	3/2020	9/2021 (1/2023) [9/2022]	501.29 (-) [524.83]	506.75 (23.54) [12]
1359	GUJRAI SOLAR POWER PROJECT	6/2022	8/2023 (-) [8/2023]	279.94 (-) [279.94]	28.39 (0.00) [0]
1360	GURHAH SOLAR POWER PROJECT	5/2022	8/2023 (-) [8/2023]	466.82 (-) [466.82]	42.58 (0.00) [0]
1361	KALPI SOLAR POWER PROJECT	7/2020	3/2022 (12/2022) [12/2022]	314.64 (335.36) [337.77]	218.26 (23.13) [9]
1362	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	5,031.01 (0.00) [11]
1363	NOKHRA	3/2020	9/2021 (1/2023) [1/2023]	1,722.14 (-) [1,803.19]	1,193.45 (81.05) [16]
1364	PARASAN SOLAR POWER PROJECT	8/2021	12/2022 (-) [12/2022]	392.30 (-) [392.30]	397.04 (0.00) [0]
	<u>Railways</u>				
1365	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	362.14 (-233.29) [0]
1366	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [9/2022]	1,183.25 (-) [2,203.53]	2,075.59 (1,020.28) [21]
1367	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [12/2023]	602.50 (-) [800.00]	185.52 (197.50) [-]
1368	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [0/0]	213.00 (-) [213.35]	141.72 (0.35) [0]

1369	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [12/2023]	2,001.00 (2,001.00) [2,001.00]	1,043.73 (0.00) [33]
1370	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2026]	4,329.53 (-) [4,329.53]	109.37 (0.00) [36]
1371	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2023]	528.57 (-) [528.57]	436.16 (0.00) [48]
1372	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2023]	927.01 (-) [1,457.79]	1,408.80 (530.78) [48]
1373	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	3,492.37 (0.00) [0]
1374	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	1,267.55 (0.00) [21]
1375	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [341.66]	0.74 (191.66) [66]
1376	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,953.80 (0.00) [48]
1377	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [2,000.00]	1,832.40 (704.58) [0]
1378	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [0/0]	1,177.96 (-) [1,028.95]	866.28 (-149.01) [0]
1379	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2022]	943.60 (-) [1,500.00]	1,127.95 (556.40) [9]
Road Transport And Highways					
1380	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [11/2018]	368.73 (503.36) [368.73]	488.83 (0.00) [0]
1381	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [1/2019]	351.34 (589.04) [417.68]	545.12 (66.34) [0]
1382	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [12/2019]	291.36 (480.31) [469.31]	470.89 (177.95) [0]
1383	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,228.92 (211.43) [0]
1384	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (7/2022) [7/2022]	1,408.00 (1,330.02) [1,330.02]	679.90 (-77.98) [0]
1385	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (12/2021) [12/2021]	1,737.00 (2,421.37) [2,421.37]	1,877.96 (684.37) [0]
1386	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (12/2021) [9/2022]	1,587.49 (3,150.00) [3,063.99]	2,904.36 (1,476.50) [41]
1387	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [9/2022]	1,396.74 (4,041.80) [1,396.74]	3,704.91 (0.00) [-]
1388	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [9/2021]	207.00 (-) [207.00]	0.00 (0.00) [0]

1389	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [3/2019]	676.73 (-) [676.73]	986.47 (0.00) [0]
1390	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [3/2023]	972.77 (1,603.94) [1,441.00]	494.71 (468.23) [-]
1391	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD	7/2018	2/2024 (-) [2/2024]	1,948.25 (-) [1,948.25]	509.41 (0.00) [0]
1392	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT	4/2021	3/2022 (-) [9/2023]	309.48 (-) [309.48]	27.13 (0.00) [18]
1393	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W	3/2021	3/2022 (-) [9/2023]	185.09 (-) [185.09]	3.58 (0.00) [18]
1394	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [5/2019]	305.00 (-) [305.00]	0.00 (0.00) [0]
1395	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [10/2022]	1,117.84 (-) [1,117.84]	84.10 (0.00) [-]
1396	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [7/2022]	282.41 (-) [319.96]	218.75 (37.55) [0]
1397	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [3/2021]	1,232.21 (-) [1,087.00]	1,084.94 (-145.21) [0]
1398	ETAWAH CHAKERI	3/2013	9/2015 (-) [1/2016]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]
1399	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [8/2022]	670.50 (1,248.00) [670.50]	1,147.08 (0.00) [-]
1400	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [12/2022]	809.07 (1,065.70) [1,065.70]	1,049.98 (256.63) [-]
1401	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (12/2021) [12/2022]	667.00 (3,192.10) [3,006.53]	2,989.89 (2,339.53) [54]
1402	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (12/2021) [9/2022]	667.00 (2,405.30) [2,328.27]	2,126.16 (1,661.27) [50]
1403	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (12/2022) [6/2022]	1,027.53 (2,950.04) [2,628.31]	2,588.02 (1,600.78) [0]
1404	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (12/2021) [12/2022]	815.28 (2,603.99) [2,323.88]	2,223.06 (1,508.60) [54]
1405	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [5/2019]	261.09 (839.00) [261.09]	240.96 (0.00) [0]
1406	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	3/2018	8/2020 (-) [10/2022]	288.30 (-) [323.36]	237.25 (35.06) [26]
1407	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [8/2022]	1,373.28 (-) [1,405.27]	1,401.96 (31.99) [29]
1408	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [9/2022]	1,184.71 (-) [1,310.00]	1,309.30 (125.29) [30]
1409	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF	3/2016	4/2019	899.00	909.36

	NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791		(6/2022) [6/2022]	(1,376.86) [1,376.86]	(477.86) [0]
1410	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [8/2013]	1,141.00 (-) [1,141.00]	1,715.00 (0.00) [0]
1411	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [9/2022]	281.45 (-) [319.96]	202.69 (38.51) [-]
1412	MEERUT-BULANDSHAHR	1/2016	/ (-) [3/2022]	683.24 (-) [987.94]	0.00 (304.70) [0]
1413	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [7/2022]	326.99 (327.00) [326.99]	281.05 (0.00) [0]
1414	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [12/2021]	296.50 (-) [296.50]	259.77 (0.00) [0]
1415	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [12/2021]	1,025.80 (-) [677.07]	222.94 (-348.73) [0]
1416	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [10/2021]	1,115.28 (-) [770.04]	332.69 (-345.24) [0]
1417	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [8/2022]	263.89 (-) [242.05]	190.01 (-21.84) [28]
1418	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	1/2021 (-) [0/0]	185.18 (-) [185.18]	84.07 (0.00) [0]
1419	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [7/2022]	306.59 (-) [306.59]	218.06 (0.00) [0]
1420	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [0/0]	240.30 (240.00) [240.30]	200.00 (0.00) [0]
1421	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019 (-) [1/2019]	2,159.00 (2,262.00) [2,262.00]	1,978.74 (103.00) [0]
1422	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [5/2022]	2,140.93 (-) [2,140.93]	1,877.63 (0.00) [0]
1423	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [1/2024]	724.60 (-) [724.60]	680.12 (0.00) [10]
1424	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	141.33 (0.00) [0]
	<u>Urban Development</u>				
1425	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [12/2025]	8,379.62 (-) [8,379.62]	1,143.47 (0.00) [21]
1426	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [11/2024]	11,076.48 (-) [11,076.48]	3,461.78 (0.00) [8]
	<u>Water Resources</u>				
1427	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [4/2024]	213.62 (261.12) [261.12]	0.00 (47.50) [25]
1428	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [8/2022]	206.05 (-) [206.05]	110.89 (0.00) [10]

1429	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [6/2023]	231.79 (234.03) [234.03]	28.37 (2.24) [18]
1430	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [3/2024]	271.39 (-) [271.39]	0.00 (0.00) [31]
1431	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [4/2024]	298.12 (213.91) [213.91]	0.00 (-84.21) [33]
1432	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [12/2022]	767.59 (-) [767.59]	198.68 (0.00) [15]
1433	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [6/2022]	460.45 (-) [460.45]	278.49 (0.00) [0]
1434	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [4/2024]	681.78 (690.71) [690.71]	0.00 (8.93) [22]
1435	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2022]	967.23 (-) [967.23]	161.48 (0.00) [12]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1436	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (12/2022) [12/2022]	456.86 (-) [456.86]	376.59 (0.00) [27]
	<u>Petroleum</u>				
1437	SITARGANJ LPG PROJECT	2/2017	2/2020 (10/2022) [10/2022]	160.10 (-) [160.10]	115.53 (0.00) [32]
	<u>Power</u>				
1438	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,527.00]	149.93 (0.00) [0]
1439	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2022]	648.33 (-) [947.89]	915.31 (299.56) [12]
1440	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [12/2024]	2,978.48 (5,867.38) [7,103.00]	5,489.00 (4,124.52) [141]
1441	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (6/2022) [10/2023]	1,657.00 (-) [4,825.60]	4,755.19 (3,168.60) [92]
1442	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [3/2025]	2,491.58 (3,860.35) [3,860.35]	2,640.57 (1,368.77) [141]
	<u>Railways</u>				
1443	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [24,659.00]	8,453.89 (8,443.00) [3]
	<u>Road Transport And Highways</u>				
1444	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [12/2022]	403.36 (-) [403.36]	230.60 (0.00) [54]
1445	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [12/2022]	417.24 (-) [417.24]	295.36 (0.00) [55]
1446	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (2/2022) [5/2022]	605.84 (1,023.23) [1,023.23]	981.05 (417.39) [0]
1447	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF	3/2016	/	1,443.00	1,246.85

	NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900		(3/2022) [3/2022]	(2,330.79) [2,330.79]	(887.79) [0]
1448	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [12/2022]	274.31 (-) [274.31]	143.41 (0.00) [55]
1449	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [3/2024]	1,383.78 (-) [1,383.78]	362.22 (0.00) [68]
1450	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (10/2022) [10/2022]	248.00 (-) [248.00]	111.85 (0.00) [29]
1451	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (9/2022) [9/2022]	720.00 (793.63) [793.63]	326.96 (73.63) [-]
1452	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (3/2022) [3/2022]	478.51 (1,082.40) [1,082.40]	315.11 (603.89) [0]
1453	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	151.70 (0.00) [0]
1454	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [0/0]	283.51 (-) [283.51]	196.03 (0.00) [0]
1455	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	257.34 (-) [257.34]	156.63 (0.00) [0]
1456	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (10/2022) [10/2022]	282.08 (-) [282.08]	206.46 (0.00) [40]
1457	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	200.34 (-) [200.34]	141.39 (0.00) [0]
1458	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (10/2022) [10/2022]	418.88 (-) [418.88]	264.67 (0.00) [32]
1459	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (10/2020) [10/2020]	266.52 (-) [266.52]	153.44 (0.00) [0]
1460	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (1/2021) [1/2021]	234.88 (-) [234.88]	174.51 (0.00) [0]
1461	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (10/2022) [10/2022]	293.68 (-) [293.68]	185.08 (0.00) [-]
1462	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1463	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [0/0]	248.22 (-) [248.22]	146.17 (0.00) [0]
	<u>Water Resources</u>				
1464	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (-) [2/2022]	158.00 (-) [158.00]	91.30 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1465	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (4/2023) [4/2023]	389.71 (-) [389.71]	325.34 (0.00) [17]
1466	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (3/2024)	458.00 (-)	190.85 (0.00)

			[3/2024]	[458.00]	[48]
	<u>Coal</u>				
1467	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [12/2022]	304.13 (341.22) [341.22]	139.20 (37.09) [69]
1468	BONJEME HARI EXPANSION OCP	8/2021	3/2025 (-) [3/2025]	570.12 (-) [570.12]	0.23 (0.00) [0]
1469	EXPANSION PR OF JHANJRA UG (5.00 MTY)	4/2020	3/2029 (-) [3/2029]	1,210.12 (-) [1,210.12]	152.04 (0.00) [0]
1470	MOHANPUR EXPANSION OC PHASE II	11/2020	3/2025 (-) [3/2025]	888.99 (-) [888.99]	13.41 (0.00) [0]
1471	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	37.77 (0.00) [0]
1472	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	2.14 (0.00) [0]
1473	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	648.15 (2,484.75) [60]
1474	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	11.09 (0.00) [0]
1475	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	2.00 (0.00) [0]
1476	SONEPUR BAZARI EXPANSION OC	7/2021	3/2029 (-) [3/2029]	5,365.88 (5,366.00) [5,365.88]	170.95 (0.00) [0]
1477	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	6.04 (0.00) [0]
	<u>Department Of Higher Education</u>				
1478	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [12/2022]	193.83 (-) [193.83]	64.30 (0.00) [30]
	<u>Health And Family Welfare</u>				
1479	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [12/2021]	244.00 (-) [248.00]	224.92 (4.00) [0]
1480	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [1/2021]	168.90 (-) [191.20]	182.10 (22.30) [0]
1481	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [12/2021]	651.99 (-) [651.99]	622.18 (0.00) [0]
1482	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [12/2021]	355.15 (-) [355.15]	321.31 (0.00) [0]
	<u>Home Affairs</u>				
1483	NSG AT KOLKATA	10/2014	4/2018 (-) [9/2023]	162.88 (-) [210.83]	176.16 (47.95) [65]
	<u>Mines</u>				
1484	CONSTRUCTION OF BASEMENT G FLOOR 10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	4/2019	4/2022 (-) [10/2024]	255.37 (-) [255.37]	26.26 (0.00) [30]
	<u>Petroleum</u>				

1485	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (2/2023) [2/2023]	3,712.00 (3,696.00) [3,696.00]	2,638.70 (-16.00) [5]
1486	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (-) [8/2031]	5,830.20 (-) [5,830.20]	301.79 (0.00) [5]
1487	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (6/2023) [6/2023]	1,740.00 (-) [1,740.00]	1,084.40 (0.00) [30]
1488	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	309.35 (0.00) [0]
1489	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2022) [10/2022]	163.02 (207.36) [207.36]	152.03 (44.34) [30]
	Power				
1490	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (12/2022) [12/2022]	529.68 (633.80) [679.00]	549.68 (149.32) [49]
1491	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [7/2025]	1,381.84 (-) [1,803.00]	809.11 (421.16) [70]
	Railways				
1492	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [12/2022]	255.64 (-) [272.20]	328.63 (16.56) [-]
1493	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [0]
1494	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	305.05 (435.44) [141]
1495	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [7/2025]	2,913.51 (-) [4,834.54]	1,839.89 (1,921.03) [112]
1496	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1497	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2026]	3,951.98 (-) [4,259.48]	3,496.68 (307.50) [120]
1498	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	4/2018	6/2022 (-) [12/2023]	338.00 (-) [393.83]	34.60 (55.83) [18]
1499	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	906.01 (430.57) [72]
	Road Transport And Highways				
1500	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [1/2023]	1,083.00 (1,414.01) [1,414.01]	1,000.57 (331.01) [55]
1501	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2023]	998.79 (-) [998.79]	2,004.66 (0.00) [118]
1502	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [3/2022]	1,078.84 (-) [1,078.84]	2,301.82 (0.00) [0]
1503	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [8/2021]	1,396.18 (-) [1,396.18]	1,396.18 (0.00) [0]
1504	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/	361.15	276.71

			(-) [2/2021]	(416.00) [363.93]	(2.78) [0]
1505	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (3/2022) [3/2023]	271.17 (291.20) [291.20]	125.25 (20.03) [52]
1506	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (11/2022) [3/2023]	160.27 (-) [213.97]	47.17 (53.70) [43]
1507	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (8/2022) [3/2023]	236.78 (-) [263.26]	91.29 (26.48) [43]
1508	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (3/2022) [3/2023]	254.30 (-) [254.30]	130.87 (0.00) [29]
1509	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [3/2022]	767.03 (-) [767.03]	613.08 (0.00) [0]
1510	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [0/0]	702.16 (-) [702.16]	0.00 (0.00) [0]
1511	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [6/2024]	1,261.98 (2,145.96) [2,145.96]	199.05 (883.98) [-]
1512	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (3/2022) [12/2022]	396.86 (-) [396.86]	282.77 (0.00) [39]
1513	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [12/2023]	1,665.00 (-) [2,360.65]	4,521.55 (695.65) [-]
1514	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (3/2022) [3/2023]	426.18 (-) [426.18]	284.89 (0.00) [30]
	<u>Water Resources</u>				
1515	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (-) [6/2022]	274.76 (-) [274.76]	238.21 (0.00) [0]
1516	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [12/2024]	384.96 (-) [384.96]	0.00 (0.00) [32]
1517	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [12/2024]	234.31 (-) [234.31]	0.00 (0.00) [32]
1518	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [3/2024]	165.16 (-) [165.16]	0.00 (0.00) [21]
1519	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [3/2024]	160.00 (154.73) [154.73]	10.35 (-5.27) [25]
1520	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [12/2024]	287.53 (-) [287.53]	0.00 (0.00) [32]
1521	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [9/2023]	164.93 (-) [164.93]	36.83 (0.00) [21]
1522	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [3/2024]	198.43 (224.69) [224.69]	0.00 (26.26) [25]
1523	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [12/2024]	307.12 (-) [307.12]	0.00 (0.00) [27]
1524	INTERCEPTION, DIVERSION AND TREATMENT WORKS	1/2018	12/2021	172.10	36.83

	AT BARANAGAR AND KAMARAHATI		(-) [9/2023]	(-) [172.10]	(0.00) [21]
1525	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [9/2023]	185.22 (-) [185.22]	36.83 (0.00) [21]
1526	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [6/2022]	272.32 (-) [272.32]	276.10 (0.00) [0]
	Total			21,26,460.93 (6,23,756.33) [25,91,823.45]	13,60,645.94 (4,65,362.52)
